

JAN 12 2016

Form C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☐ AMENDED REPORT

District I
1625 N. French Dr., Hobbs, NM 88240
Phone (575) 393-6161 Fax (575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone (575) 748-1283 Fax (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone (505) 334-6178 Fax (505) 334-6179

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone (505) 476-3460 Fax (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505
AS-DRILLED PLAT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-045-31431	² Pool Code 71629	³ Pool Name Basin Fruitland Coal
⁴ Property Code 001158	⁵ Property Name Tank Mountain B	⁶ Well Number 001S
⁷ OGRID No. 000778	⁸ Operator Name BP America Production Company	⁹ Elevation 6815

¹⁰ Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
P (Lot 16)	29	32N	09W		840	South	741	East	San Juan

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
P (Lot 16)	29	32N	09W		852	South	784	East	San Juan

¹² Dedicated Acres 317.666	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
--	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

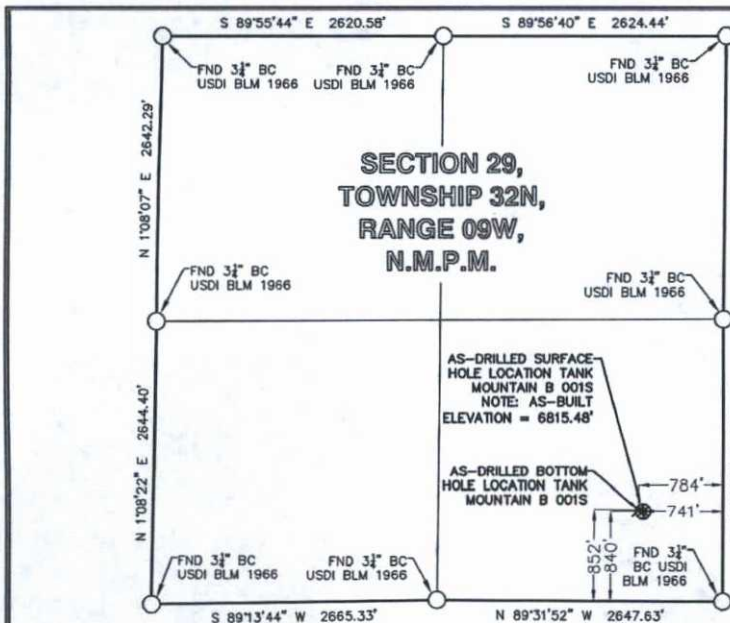

LEGEND
FOUND MONUMENT ○
AS-DRILLED SURFACE HOLE LOCATION ●
AS-DRILLED BOTTOM HOLE LOCATION ×

TANK MOUNTAIN B 001S	NW1/4 NAD'83	NAD'83	TIES
AS-DRILLED SURFACE HOLE LOCATION (SHL)	N (Y) = 2,165,414.83' E (X) = 2,733,846.67'	LAT. = 36.95077801°N LON. = 107.79652587°W	FSL = 840' FEL = 741'
AS-DRILLED BOTTOM HOLE LOCATION (BHL)	N (Y) = 2,165,427.90' E (X) = 2,733,804.01'	LAT. = 36.95081395°N LON. = 107.79667185°W	FSL = 852' FEL = 784'

¹⁷ OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or undivided mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order previously entered by the division.

Signature: *Toya Colvin* Date: 12/10/15

Toya Colvin
Printed Name

Toya.Colvin@bp.com
E-mail Address

¹⁸ SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

9-22-15
Date of Survey

Signature and Seal of Professional Surveyor

17078
Certificate Number



FV



B.P.

San Juan County, NM NAD83

Tank Mountain B


Tank Mountain B 001S

OH

Design: OH

Standard Survey Report


07 December, 2015



www.scientificdrilling.com



Survey Report



Company:	B.P.	Local Co-ordinate Reference:	Well Tank Mountain B 001S
Project:	San Juan County, NM NAD83	TVD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Site:	Tank Mountain B	MD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Well:	Tank Mountain B 001S	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Grand Junction District

Project	San Juan County, NM NAD83		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Western Zone		

Site	Tank Mountain B		
Site Position:		Northing:	2,165,414.83 usft
From:	Map	Easting:	2,733,846.67 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13.20 in
		Latitude:	36.9507780
		Longitude:	-107.7965259
		Grid Convergence:	0.02 °

Well	Tank Mountain B 001S		
Well Position	+N/-S	0.00 usft	Northing:
	+E/-W	0.00 usft	Easting:
Position Uncertainty	0.00 usft	Wellhead Elevation:	0.00 usft
		Latitude:	36.9507780
		Longitude:	-107.7965259
		Ground Level:	6,816.00 usft

Wellbore	OH		
Magnetics	Model Name	Sample Date	Declination
			(°)
	HDGM	12/4/2015	9.28
			Dip Angle
			(°)
			63.57
			Field Strength
			(nT)
			50,218


Design	OH		
Audit Notes:			
Version:	1.0	Phase:	ACTUAL
		Tie On Depth:	
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W
	(usft)	(usft)	(usft)
	0.00	0.00	0.00
			Direction
			(°)
			287.03

Survey Program	Date 12/4/2015		
From	To	Survey (Wellbore)	Tool Name
(usft)	(usft)		
99.11	3,761.48	Survey #1 - Gyro Survey (OH)	Standard Keeper 104
			Description
			Standard Wireline Keeper ver 1.0.4

Survey										
Measured	Inclination	Azimuth	Vertical	+N/-S	+E/-W	Vertical	Dogleg	Build	Turn	
Depth	(°)	(°)	Depth	(usft)	(usft)	Section	Rate	Rate	Rate	
(usft)			(usft)			(usft)	(°/100usft)	(°/100usft)	(°/100usft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
99.11	0.57	326.67	99.11	0.41	-0.27	0.38	0.58	0.58	0.00	
124.22	0.37	280.87	124.22	0.53	-0.42	0.56	1.63	-0.80	-182.40	
149.98	0.41	275.02	149.98	0.56	-0.59	0.73	0.22	0.16	-22.71	
174.71	0.40	253.32	174.71	0.54	-0.76	0.89	0.62	-0.04	-87.75	
198.63	0.50	254.55	198.63	0.49	-0.94	1.05	0.42	0.42	5.14	
224.94	0.57	244.24	224.93	0.40	-1.17	1.24	0.45	0.27	-39.19	
249.28	0.52	227.04	249.27	0.27	-1.36	1.38	0.70	-0.21	-70.67	
274.48	0.61	211.06	274.47	0.08	-1.52	1.47	0.72	0.36	-63.41	
299.62	0.65	206.57	299.61	-0.16	-1.65	1.53	0.25	0.16	-17.86	



Survey Report




Company:	B.P.	Local Co-ordinate Reference:	Well Tank Mountain B 001S
Project:	San Juan County, NM NAD83	TVD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Site:	Tank Mountain B	MD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Well:	Tank Mountain B 001S	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Grand Junction District

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
324.28	0.64	192.31	324.27	-0.42	-1.74	1.54	0.65	-0.04	-57.83	
348.91	0.59	187.15	348.90	-0.68	-1.79	1.51	0.30	-0.20	-20.95	
374.11	0.49	193.48	374.10	-0.92	-1.83	1.48	0.46	-0.40	25.12	
399.33	0.39	199.55	399.32	-1.10	-1.88	1.47	0.44	-0.40	24.07	
424.07	0.29	219.92	424.06	-1.23	-1.95	1.50	0.63	-0.40	82.34	
448.72	0.29	214.24	448.71	-1.33	-2.02	1.55	0.12	0.00	-23.04	
474.93	0.31	222.04	474.91	-1.44	-2.11	1.60	0.17	0.08	29.76	
499.57	0.44	235.03	499.55	-1.54	-2.23	1.68	0.63	0.53	52.72	
523.78	0.41	223.26	523.76	-1.66	-2.37	1.78	0.38	-0.12	-48.62	
549.96	0.48	228.15	549.94	-1.80	-2.51	1.88	0.30	0.27	18.68	
574.63	0.40	228.66	574.61	-1.92	-2.65	1.97	0.32	-0.32	2.07	
599.28	0.37	228.68	599.26	-2.03	-2.78	2.06	0.12	-0.12	0.08	
624.94	0.46	245.82	624.92	-2.13	-2.93	2.18	0.59	0.35	66.80	
649.57	0.57	264.84	649.55	-2.18	-3.15	2.37	0.82	0.45	77.22	
674.28	0.69	269.48	674.26	-2.19	-3.42	2.63	0.53	0.49	18.78	
699.91	0.74	265.06	699.89	-2.21	-3.74	2.93	0.29	0.20	-17.25	
723.99	0.87	272.32	723.96	-2.22	-4.07	3.25	0.69	0.54	30.15	
749.18	0.79	276.57	749.15	-2.19	-4.44	3.60	0.40	-0.32	16.87	
774.78	0.72	277.23	774.75	-2.15	-4.77	3.93	0.28	-0.27	2.58	
799.36	0.74	297.00	799.33	-2.06	-5.07	4.24	1.02	0.08	80.43	
824.46	0.69	313.67	824.43	-1.88	-5.32	4.54	0.85	-0.20	66.41	
849.60	0.76	316.78	849.56	-1.65	-5.55	4.82	0.32	0.28	12.37	
874.29	0.78	320.74	874.25	-1.40	-5.76	5.10	0.23	0.08	16.04	
899.92	0.80	312.19	899.88	-1.15	-6.01	5.41	0.47	0.08	-33.36	
924.57	0.87	313.09	924.53	-0.90	-6.27	5.73	0.29	0.28	3.65	
949.78	0.84	297.80	949.73	-0.69	-6.57	6.08	0.91	-0.12	-60.65	
974.91	0.92	285.98	974.86	-0.55	-6.93	6.47	0.79	0.32	-47.04	
999.55	0.86	289.76	999.50	-0.43	-7.30	6.85	0.34	-0.24	15.34	
1,024.21	0.83	290.06	1,024.15	-0.30	-7.64	7.21	0.12	-0.12	1.22	
1,048.90	0.93	291.17	1,048.84	-0.17	-7.99	7.59	0.41	0.41	4.50	
1,074.10	0.85	294.50	1,074.04	-0.02	-8.35	7.98	0.38	-0.32	13.21	
1,099.78	1.00	291.42	1,099.72	0.14	-8.73	8.39	0.62	0.58	-11.99	
1,124.99	1.03	293.58	1,124.92	0.31	-9.15	8.84	0.19	0.12	8.57	
1,149.77	1.08	287.07	1,149.70	0.47	-9.57	9.29	0.52	0.20	-26.27	
1,174.43	1.07	284.26	1,174.35	0.59	-10.02	9.75	0.22	-0.04	-11.39	
1,198.69	1.06	279.79	1,198.61	0.69	-10.46	10.20	0.34	-0.04	-18.43	
1,224.88	0.91	282.24	1,224.79	0.77	-10.90	10.65	0.59	-0.57	9.35	
1,249.08	0.79	275.82	1,248.99	0.83	-11.26	11.01	0.63	-0.50	-26.53	
1,274.75	0.77	277.76	1,274.66	0.87	-11.60	11.35	0.13	-0.08	7.56	
1,298.92	0.73	278.60	1,298.83	0.92	-11.92	11.66	0.17	-0.17	3.48	
1,323.70	0.71	280.22	1,323.61	0.97	-12.22	11.97	0.12	-0.08	6.54	
1,349.87	0.78	268.01	1,349.77	0.99	-12.56	12.30	0.66	0.27	-46.66	
1,374.15	0.90	267.08	1,374.05	0.98	-12.92	12.64	0.50	0.49	-3.83	
1,398.84	0.94	257.19	1,398.74	0.92	-13.31	12.99	0.66	0.16	-40.06	



Survey Report




Company:	B.P.	Local Co-ordinate Reference:	Well Tank Mountain B 001S
Project:	San Juan County, NM NAD83	TVD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Site:	Tank Mountain B	MD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Well:	Tank Mountain B 001S	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Grand Junction District

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
1,424.51	0.95	256.82	1,424.40	0.83	-13.72	13.36	0.05	0.04	-1.44
1,448.72	0.90	258.84	1,448.61	0.74	-14.10	13.70	0.25	-0.21	8.34
1,474.50	0.84	252.22	1,474.39	0.65	-14.48	14.04	0.45	-0.23	-25.68
1,499.63	0.71	260.14	1,499.52	0.56	-14.81	14.33	0.67	-0.52	31.52
1,524.75	0.67	273.25	1,524.63	0.55	-15.11	14.61	0.65	-0.16	52.19
1,549.64	0.64	283.09	1,549.52	0.59	-15.39	14.89	0.47	-0.12	39.53
1,573.95	0.65	295.62	1,573.83	0.68	-15.65	15.16	0.58	0.04	51.54
1,599.67	0.70	295.79	1,599.55	0.81	-15.92	15.46	0.19	0.19	0.66
1,624.39	0.81	284.85	1,624.27	0.92	-16.22	15.78	0.73	0.44	-44.26
1,649.15	1.06	275.90	1,649.02	0.99	-16.62	16.18	1.17	1.01	-36.15
1,674.90	1.12	273.21	1,674.77	1.02	-17.11	16.66	0.31	0.23	-10.45
1,699.17	1.18	272.32	1,699.03	1.05	-17.60	17.13	0.26	0.25	-3.67
1,724.53	1.20	261.74	1,724.39	1.02	-18.12	17.62	0.87	0.08	-41.72
1,749.80	1.26	251.05	1,749.65	0.89	-18.64	18.09	0.94	0.24	-42.30
1,774.93	1.23	244.84	1,774.78	0.69	-19.15	18.51	0.55	-0.12	-24.71
1,799.29	1.14	242.81	1,799.13	0.47	-19.60	18.88	0.41	-0.37	-8.33
1,823.54	1.04	236.05	1,823.38	0.23	-20.00	19.19	0.67	-0.41	-27.88
1,848.80	1.07	237.42	1,848.63	-0.02	-20.39	19.49	0.16	0.12	5.42
1,873.77	1.01	233.66	1,873.60	-0.28	-20.76	19.77	0.36	-0.24	-15.06
1,899.09	0.97	232.06	1,898.92	-0.54	-21.11	20.03	0.19	-0.16	-6.32
1,923.91	0.90	226.41	1,923.73	-0.81	-21.42	20.24	0.47	-0.28	-22.76
1,949.24	1.07	225.67	1,949.06	-1.11	-21.73	20.45	0.67	0.67	-2.92
1,974.97	1.12	217.20	1,974.78	-1.48	-22.06	20.66	0.66	0.19	-32.92
1,998.88	1.21	222.94	1,998.69	-1.85	-22.37	20.85	0.62	0.38	24.01
2,024.26	1.24	224.02	2,024.06	-2.24	-22.74	21.09	0.15	0.12	4.26
2,049.47	1.25	220.73	2,049.27	-2.64	-23.11	21.32	0.29	0.04	-13.05
2,073.83	1.25	222.57	2,073.62	-3.04	-23.46	21.54	0.16	0.00	7.55
2,099.60	1.12	219.99	2,099.39	-3.44	-23.82	21.76	0.55	-0.50	-10.01
2,124.93	0.94	223.80	2,124.71	-3.78	-24.12	21.95	0.76	-0.71	15.04
2,149.15	0.88	230.85	2,148.93	-4.04	-24.40	22.15	0.52	-0.25	29.11
2,174.01	0.92	234.36	2,173.79	-4.28	-24.71	22.37	0.27	0.16	14.12
2,199.78	0.90	241.10	2,199.55	-4.50	-25.06	22.64	0.42	-0.08	26.15
2,223.57	0.79	248.27	2,223.34	-4.65	-25.37	22.90	0.64	-0.46	30.14
2,249.95	0.90	244.13	2,249.72	-4.81	-25.73	23.19	0.48	0.42	-15.69
2,274.74	0.77	251.88	2,274.50	-4.94	-26.06	23.47	0.69	-0.52	31.26
2,299.55	0.81	248.15	2,299.31	-5.06	-26.38	23.74	0.26	0.16	-15.03
2,323.93	0.74	248.49	2,323.69	-5.18	-26.69	24.00	0.29	-0.29	1.39
2,349.21	0.80	239.11	2,348.97	-5.33	-26.99	24.25	0.55	0.24	-37.10
2,374.89	0.83	234.36	2,374.64	-5.53	-27.30	24.48	0.29	0.12	-18.50
2,399.89	0.91	228.89	2,399.64	-5.77	-27.59	24.69	0.46	0.32	-21.88
2,424.72	0.88	229.28	2,424.47	-6.02	-27.89	24.90	0.12	-0.12	1.57
2,448.62	0.94	229.02	2,448.37	-6.27	-28.17	25.10	0.25	0.25	-1.09
2,474.05	0.91	231.17	2,473.79	-6.53	-28.49	25.33	0.18	-0.12	8.45



Survey Report




Company:	B.P.	Local Co-ordinate Reference:	Well Tank Mountain B 001S
Project:	San Juan County, NM NAD83	TVD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Site:	Tank Mountain B	MD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Well:	Tank Mountain B 001S	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Grand Junction District

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
2,499.70	0.88	230.28	2,499.44	-6.79	-28.80	25.55	0.13	-0.12	-3.47
2,524.13	0.93	228.71	2,523.87	-7.04	-29.09	25.75	0.23	0.20	-6.43
2,549.48	0.91	231.13	2,549.21	-7.30	-29.40	25.98	0.17	-0.08	9.55
2,574.87	0.83	226.22	2,574.60	-7.55	-29.69	26.18	0.43	-0.32	-19.34
2,598.40	0.88	217.15	2,598.13	-7.82	-29.93	26.32	0.61	0.21	-38.55
2,624.10	0.94	213.60	2,623.82	-8.15	-30.16	26.45	0.32	0.23	-13.81
2,648.47	1.01	216.77	2,648.19	-8.49	-30.40	26.58	0.36	0.29	13.01
2,674.39	0.91	220.14	2,674.11	-8.83	-30.67	26.74	0.44	-0.39	13.00
2,699.31	0.94	216.77	2,699.02	-9.14	-30.92	26.89	0.25	0.12	-13.52
2,724.20	0.91	226.61	2,723.91	-9.44	-31.19	27.05	0.65	-0.12	39.53
2,748.98	0.88	227.17	2,748.69	-9.71	-31.47	27.25	0.13	-0.12	2.26
2,774.43	0.85	235.20	2,774.13	-9.95	-31.77	27.46	0.49	-0.12	31.55
2,799.74	1.00	235.74	2,799.44	-10.18	-32.10	27.71	0.59	0.59	2.13
2,824.33	0.84	242.01	2,824.03	-10.38	-32.44	27.98	0.77	-0.65	25.50
2,849.76	1.07	243.60	2,849.45	-10.58	-32.82	28.28	0.91	0.90	6.25
2,874.69	1.05	236.71	2,874.38	-10.81	-33.22	28.60	0.52	-0.08	-27.64
2,899.65	1.13	247.87	2,899.34	-11.02	-33.64	28.93	0.91	0.32	44.71
2,923.68	1.21	244.83	2,923.36	-11.22	-34.09	29.30	0.42	0.33	-12.65
2,948.68	1.14	250.45	2,948.36	-11.42	-34.56	29.70	0.54	-0.28	22.48
2,974.19	1.18	250.27	2,973.86	-11.59	-35.04	30.11	0.16	0.16	-0.71
2,999.21	1.10	247.36	2,998.88	-11.77	-35.51	30.50	0.39	-0.32	-11.63
3,023.74	1.04	244.61	3,023.40	-11.96	-35.93	30.85	0.32	-0.24	-11.21
3,049.76	1.02	246.99	3,049.42	-12.15	-36.35	31.20	0.18	-0.08	9.15
3,074.40	0.89	249.51	3,074.05	-12.30	-36.74	31.52	0.55	-0.53	10.23
3,099.89	0.79	254.33	3,099.54	-12.42	-37.09	31.83	0.48	-0.39	18.91
3,124.88	0.79	255.23	3,124.53	-12.51	-37.42	32.12	0.05	0.00	3.60
3,148.67	0.80	253.35	3,148.32	-12.60	-37.74	32.40	0.12	0.04	-7.90
3,173.78	0.77	256.58	3,173.42	-12.69	-38.07	32.69	0.21	-0.12	12.86
3,199.28	1.27	344.27	3,198.92	-12.45	-38.32	32.99	5.72	1.96	343.88
3,223.87	2.15	6.64	3,223.50	-11.73	-38.34	33.22	4.43	3.58	90.97
3,248.92	1.97	10.80	3,248.53	-10.84	-38.20	33.35	0.93	-0.72	16.61
3,274.63	1.96	10.10	3,274.23	-9.98	-38.04	33.45	0.10	-0.04	-2.72
3,299.85	2.03	6.45	3,299.43	-9.11	-37.91	33.58	0.58	0.28	-14.47
3,324.52	1.93	2.04	3,324.09	-8.26	-37.85	33.77	0.74	-0.41	-17.88
3,349.51	1.92	353.14	3,349.06	-7.42	-37.89	34.05	1.20	-0.04	-35.61
3,374.35	1.80	342.74	3,373.89	-6.64	-38.05	34.44	1.44	-0.48	-41.87
3,399.91	1.77	338.79	3,399.44	-5.89	-38.31	34.91	0.50	-0.12	-15.45
3,424.66	1.64	340.02	3,424.18	-5.20	-38.57	35.36	0.55	-0.53	4.97
3,448.90	1.99	4.64	3,448.41	-4.45	-38.66	35.66	3.49	1.44	101.57
3,474.59	1.87	3.32	3,474.08	-3.59	-38.60	35.85	0.50	-0.47	-5.14
3,499.81	1.74	347.02	3,499.29	-2.80	-38.66	36.14	2.09	-0.52	-64.63
3,524.55	1.96	337.98	3,524.02	-2.05	-38.90	36.60	1.47	0.89	-36.54
3,548.93	2.18	344.33	3,548.38	-1.21	-39.18	37.11	1.30	0.90	26.05



Survey Report



Company:	B.P.	Local Co-ordinate Reference:	Well Tank Mountain B 001S
Project:	San Juan County, NM NAD83	TVD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Site:	Tank Mountain B	MD Reference:	GL 6816' & RKB 12' @ 6828.00usft
Well:	Tank Mountain B 001S	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	Grand Junction District

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
3,574.14	2.29	352.34	3,573.57	-0.25	-39.38	37.58	1.31	0.44	31.77
3,600.24	1.88	351.82	3,599.65	0.69	-39.51	37.98	1.57	-1.57	-1.99
3,624.13	2.74	345.54	3,623.52	1.63	-39.71	38.44	3.75	3.60	-26.29
3,649.03	5.02	350.72	3,648.37	3.28	-40.03	39.24	9.25	9.16	20.80
3,674.73	5.70	350.93	3,673.95	5.65	-40.41	40.30	2.65	2.65	0.82
3,699.63	5.54	346.03	3,698.73	8.04	-40.90	41.46	2.03	-0.64	-19.68
3,724.08	5.22	339.81	3,723.08	10.23	-41.57	42.74	2.72	-1.31	-25.44
3,749.53	4.44	338.31	3,748.44	12.23	-42.33	44.06	3.10	-3.06	-5.89
3,761.48	4.21	338.75	3,760.35	13.07	-42.66	44.62	1.94	-1.92	3.68

Checked By: _____ Approved By: _____ Date: _____
