

W LYBROOK UNIT #711H

Lybrook Mancos W

(page 1)

CONTINUED FROM TUBING EXTENSION

Spud: 12/15/16

Completed: 60 day
tubing extension
requested 4/12/17-
granted until 5/27/17

COMPLETED: 5/10/17

SHL: 1205' FSL & 1327' FWL
SE/4 SW/4 Section 8 (N), T23N, R8W


BHL: 1004' FSL & 803' FWL
SW/4 SW/4 Section 17 (M), T23N, R8W

San Juan, NM

Elevation: 6823'

API: 30-045-35809

Formation	MD	TVD
OJO ALAMO	867	867
KIRTLAND	1069	1069
PICTURED CLIFFS	1402	1402
LEWIS	1592	1592
CHACRA	1806	1806
CLIFF HOUSE	2919	2885
MENEFEE	2961	2924
POINT LOOKOUT	3954	3839
MANCOS	4146	4015
GALLUP	4521	4371

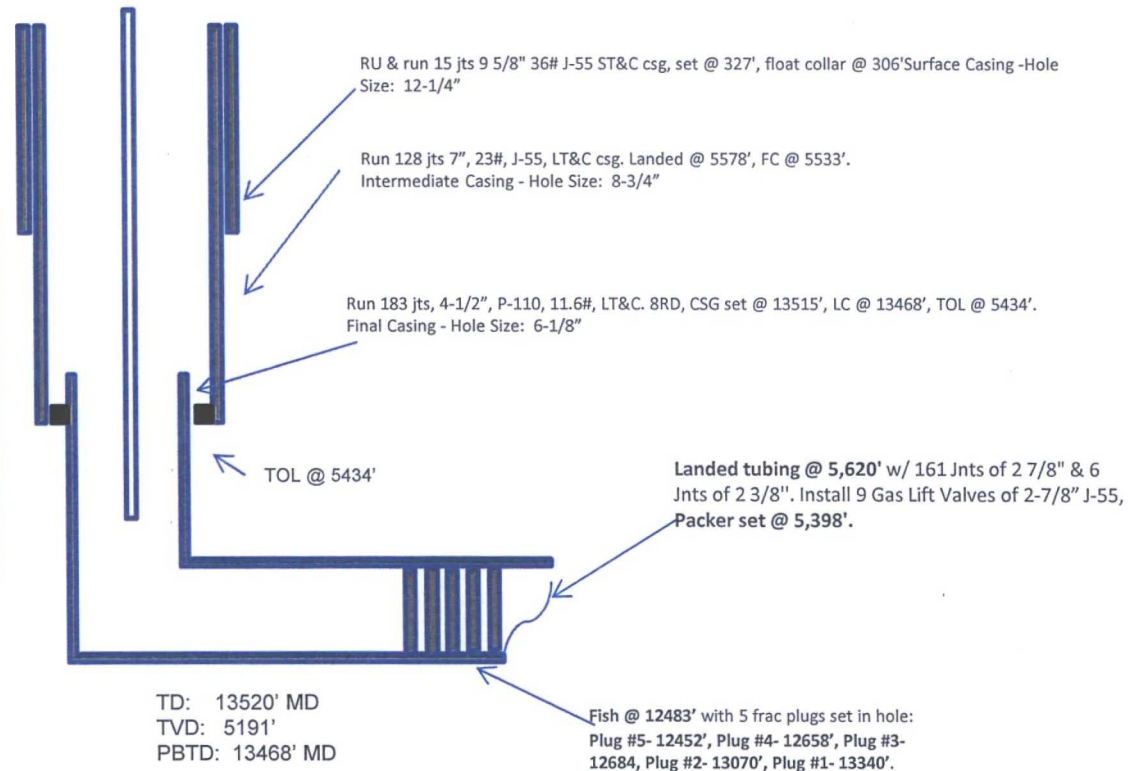

Mancos Frac-

5599'-13457'/.32"

diameter- 20 spf total of

755 holes. w/ 38 stages

20/40 sand total of

7,797,585#

LG 5/11/17

HOLE SIZE	CASING	CEMENT	VOLUME	CMT TOP
12-1/4"	9-5/8"	101sx	162cu.ft.	Surface
8-3/4"	7"	955 sx	1544cu. ft.	Surface
6-1/8"	4-1/2"	730sx	993 cu. ft.	TOL 5434'

CONFIDENTIAL
