

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☒ DRILL ☐ REENTER 1b. Type of Well: ☐ Oil Well ☒ Gas Well ☐ Other 1c. Type of Completion: ☐ Hydraulic Fracturing ☒ Single Zone ☐ Multiple Zone		5. Lease Serial No. NMNM138866 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No. VONI FED COM 204H 9. API Well No. 30-015-47312
2. Name of Operator MATADOR PRODUCTION COMPANY 3a. Address 5400 LBJ Freeway, Suite 1500, Dallas, TX 75240 3b. Phone No. (include area code) (972) 371-5200		10. Field and Pool, or Exploratory Purple Sage; Wolfcamp (Gas)/PURPLE S/ 11. Sec., T, R, M, or Blk. and Survey or Area SEC 21/T26S/R31E/NMP
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NENE / 260 FNL / 1128 FEL / LAT 32.0347522 / LONG -103.778314 At proposed prod. zone LOT 1 / 240 FSL / 990 FEL / LAT 32.0008423 / LONG -103.7777509		12. County or Parish EDDY 13. State NM
14. Distance in miles and direction from nearest town or post office* 15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 260 feet	16. No of acres in lease 640 17. Spacing Unit dedicated to this well 770.49	18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 30 feet 19. Proposed Depth 11386 feet / 23705 feet 20. BLM/BIA Bond No. in file FED: NMB001079
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3191 feet	22. Approximate date work will start* 12/01/2019	23. Estimated duration 60 days
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature (Electronic Submission) Title Project Manager	Name (Printed/Typed) LARA THOMPSON / Ph: (972) 371-5200 Date 08/20/2019	
Approved by (Signature) (Electronic Submission) Title Assistant Field Manager Lands & Minerals	Name (Printed/Typed) Cody Layton / Ph: (575) 234-5959 Date 07/29/2020	Office Carlsbad Field Office

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

APPROVED WITH CONDITIONS

Approval Date: 07/29/2020

(Continued on page 2)

*(Instructions on page 2)

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources
Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

FORM C-102

Revised August 1, 2011

Submit one copy to appropriate

District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-47312	² Pool Code 98220	³ Pool Name Purple Sage; Wolfcamp (Gas)
⁴ Property Code 328098	⁵ Property Name VONI FED COM	
⁶ Well Number 204H	⁷ Elevation 3191'	
⁸ OGRID No. 228937	⁹ Operator Name MATADOR PRODUCTION COMPANY	

¹⁰Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	21	26-S	31-E	-	260'	NORTH	1128'	EAST	EDDY

¹¹Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
1	33	26-S	31-E	-	240'	SOUTH	990'	EAST	EDDY

¹² Dedicated Acres 770.49	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
--	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

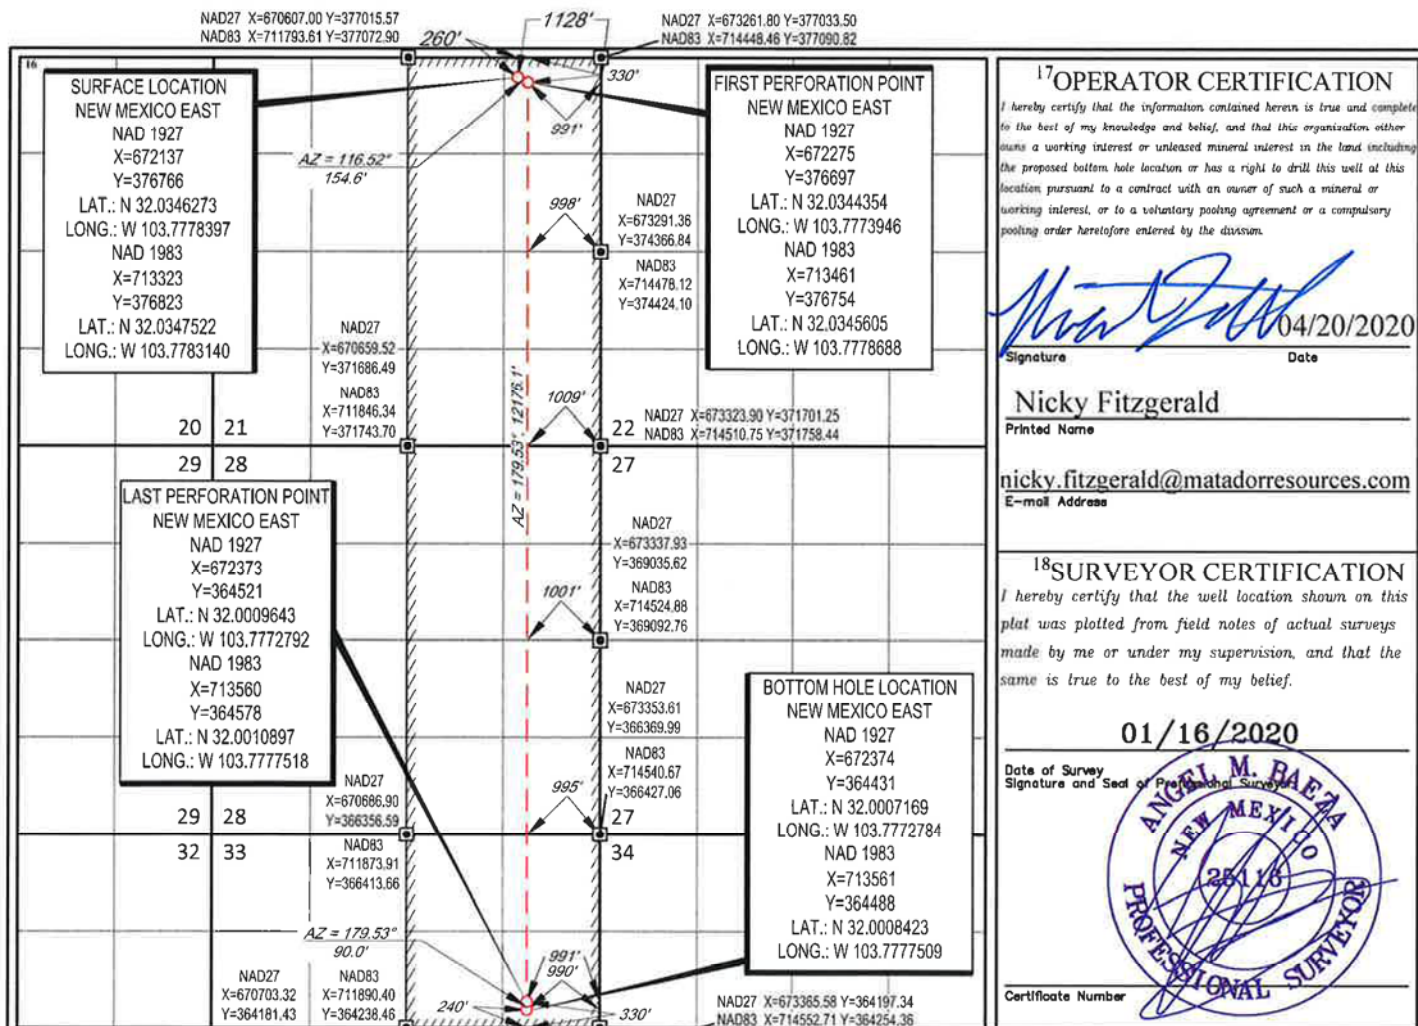



Application for Permit to Drill

U.S. Department of the Interior
Bureau of Land Management

APD Package Report

Date Printed: 07/31/2020 05:55 PM

APD ID: 10400045433

Well Status: AAPD

APD Received Date: 08/20/2019 12:46 PM

Well Name: VONI FED COM

Operator: MATADOR PRODUCTION COMPAN Well Number: 204H

APD Package Report Contents

- Form 3160-3
- Operator Certification Report
- Application Report
- Application Attachments
 - Well Plat: 1 file(s)
- Drilling Plan Report
- Drilling Plan Attachments
 - Blowout Prevention Choke Diagram Attachment: 1 file(s)
 - Blowout Prevention BOP Diagram Attachment: 3 file(s)
 - Casing Spec Documents: 2 file(s)
 - Casing Taperd String Specs: 2 file(s)
 - Casing Design Assumptions and Worksheet(s): 4 file(s)
 - Proposed horizontal/directional/multi-lateral plan submission: 2 file(s)
 - Other Facets: 6 file(s)
- SUPO Report
- SUPO Attachments
 - Existing Road Map: 10 file(s)
 - New Road Map: 2 file(s)
 - Attach Well map: 2 file(s)
 - Production Facilities map: 4 file(s)
 - Water source and transportation map: 1 file(s)
 - Construction Materials source location attachment: 1 file(s)
 - Well Site Layout Diagram: 2 file(s)
 - Recontouring attachment: 1 file(s)
 - Other SUPO Attachment: 4 file(s)
- PWD Report
- PWD Attachments
 - None

- Bond Report
- Bond Attachments
 - None

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM 1: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

0. SHL: NENE / 260 FNL / 1128 FEL / TWSP: 26S / RANGE: 31E / SECTION: 21 / LAT: 32.0347522 / LONG: -103.778314 (TVD: 0 feet, MD: 0 feet)

PPP: NENE / 330 FNL / 991 FEL / TWSP: 26S / RANGE: 31E / SECTION: 21 / LAT: 32.0345605 / LONG: -103.7778688 (TVD: 11237 feet, MD: 11305 feet)

PPP: NENE / 0 FNL / 1009 FEL / TWSP: 26S / RANGE: 31E / SECTION: 28 / LAT: 32.0208275 / LONG: -103.776754 (TVD: 11386 feet, MD: 16730 feet)

BHL: LOT 1 / 240 FSL / 990 FEL / TWSP: 26S / RANGE: 31E / SECTION: 33 / LAT: 32.0008423 / LONG: -103.7777509 (TVD: 11386 feet, MD: 23705 feet)

BLM Point of Contact

Name: Sophia Cwiklinski

Title: LIE

Phone: (575) 234-5972

Email: scwiklinski@blm.gov

CONFIDENTIAL

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL

**PECOS DISTRICT
SURFACE USE
CONDITIONS OF APPROVAL**

OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE LOCATION: COUNTY:	Matador Production Company Voni Federal 021H 400'/N & 624'/W 100'/S & 660'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE LOCATION: COUNTY:	Matador Production Company Voni Federal 101H 300'/N & 374'/W 100'/S & 339'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE LOCATION: COUNTY:	Matador Production Company Voni Federal 105H 350'/N & 484'/W 100'/S & 990'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE LOCATION: COUNTY:	Matador Production Company Voni Federal 111H 350'/N & 454'/W 100'/S & 339'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE LOCATION: COUNTY:	Matador Production Company Voni Federal 121H 320'/N & 454'/W 100'/S & 660'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE LOCATION: COUNTY:	Matador Production Company Voni Federal 131H 350'/N & 564'/W 100'/S & 660'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE LOCATION: COUNTY:	Matador Production Company Voni Federal 201H 350'/N & 344'/W 240'/S & 338'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico

Approval Date: 07/29/2020

OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 215H 320'/N & 374'/W 240'/S & 990'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 221H 320'/N & 344'/W 240'/S & 338'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 225H 350'/N & 594'/W 240'/S & 990'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 241H 320'/N & 564'/W 240'/S & 660'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 022H 350'/N & 2240'/W 100'/S & 1980'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 102H 350'/N & 2130'/W 100'/S & 1650'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 106H 320'/N & 2240'/W 100'/S & 2310'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico

OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 112H 350'/N & 2210'/W 100'/S & 1650'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 122H 320'/N & 2210'/W 100'/S & 1980'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 132H 350'/N & 2320'/W 100'/S & 1980'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 202H 350'/N & 2100'/W 240'/S & 1650'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 216H 320'/N & 2130'/W 240'/S & 2310'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 222H 320'/N & 2100'/W 240'/S & 1650'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 226H 350'/N & 2350'/W 240'/S & 2310'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico

OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 242H 320'/N & 2320'/W 240'/S & 1980'/W Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 023H 320'/N & 2056'/E 100'/S & 1980'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 103H 350'/N & 2166'/E 100'/S & 2310'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 107H 350'/N & 2056'/E 100'/S & 1661'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 113H 350'/N & 2086'/E 100'/S & 2310'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 106H 320'/N & 2086'/E 100'/S & 1980'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 133H 350'/N & 1976'/E 100'/S & 1980'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico

OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 203H 350'/N & 2196'/E 240'/S & 2310'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 217H 320'/N & 2166'/E 240'/S & 1650'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 223H 320'/N & 2196'/E 240'/S & 2310'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 227H 350'/N & 1946'/E 240'/S & 1650'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 243H 320'/N & 1976'/E 240'/S & 1980'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 024H 260'/N & 1238'/E 100'/S & 660'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 104H 260'/N & 1128'/E 100'/S & 990'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico

OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 108H 290'/N & 1238'/E 100'/S & 330'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 114H 290'/N & 1208'/E 100'/S & 990'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 124H 260'/N & 1208'/E 100'/S & 660'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 134H 260'/N & 1318'/E 100'/S & 660'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 204H 260'/N & 1098'/E 240'/S & 990'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico
OPERATOR'S NAME: WELL NAME & NO.: SURFACE HOLE FOOTAGE: BOTTOM HOLE FOOTAGE: LOCATION: COUNTY:	Matador Production Company Voni Federal 218H 290'/N & 1098'/E 240'/S & 330'/E Section 21, T.26 S., R.31 E., NMPM Eddy County, New Mexico

TABLE OF CONTENTS

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ General Provisions
☐ Permit Expiration

Approval Date: 07/29/2020

☐ **Archaeology, Paleontology, and Historical Sites**

☐ **Noxious Weeds**

☒ **Special Requirements**

Hydrological Features

Phantom Banks SMA

Karst Features

Range Stipulations

Special Status Plant Species

☒ **Construction**

Notification

Topsoil

Closed Loop System

Federal Mineral Material Pits

Well Pads

Roads

☐ **Road Section Diagram**

☒ **Production (Post Drilling)**

Well Structures & Facilities

Pipelines

Electric Lines

Access Roads

Frac Pond

☒ **Interim Reclamation**

☐ **Final Abandonment & Reclamation**

I. GENERAL PROVISIONS

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

II. PERMIT EXPIRATION

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

The flowlines/facility pad and road/flowline that go to the flare-pad were analyzed but were not approved for construction by archaeology until new files are submitted via Sundry to confirm their proposed location.

Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. Only If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during

construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 6 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

IV. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

V. SPECIAL REQUIREMENT(S)

Phantom Banks SMA

Surface disturbance will not be allowed within 660 feet of active heronries or by delaying activity for up to 120 days, or a combination of both. Exhaust noise from engines must be muffled or otherwise controlled so as not to exceed 75 decibels measured at 30 feet from the source of the noise.

Hydrology Stipulations / Conditions of Approval

The entire well pad(s) will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. The compacted berm shall be constructed at a minimum of 12 inches with impermeable mineral material (e.g. caliche). Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The integrity of the berm shall be maintained around the surfaced pad throughout the life of the well and around the downsized pad after interim reclamation has been completed. Any water erosion that may occur due to the construction of the well pad during the life of the well will be quickly corrected and proper measures will be taken to prevent future erosion. Stockpiling of topsoil is required. The top soil shall be stockpiled in an appropriate location to prevent loss of soil due to water or wind erosion and not used for berming or erosion control. If fluid collects within the bermed area, the fluid must be vacuumed into a safe container and disposed of properly at a state approved facility.

Tank battery locations will be lined and bermed. A 20 mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Tank battery berms must be large enough to contain 1 ½ times the content of the largest tank or 24 hour production, whichever is greater. Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

Any water erosion that may occur due to the construction of overhead electric line and during the life of the power line will be quickly corrected and proper measures will be taken to prevent future erosion. A power pole should not be placed in drainages, playas, wetlands, riparian areas, or floodplains and must span across the features at a distance away that would not promote further erosion.


Hydrology – Fresh Water Frac Pond:

Energy dissipation and filtration devices (e.g., certified weed-free hay/straw bales and silt fence) will be used to reduce the velocity of the discharged water and thereby reduce potential for erosion.

Matador agreed to place straw wattles around the perimeter of the proposed frac pond to minimize the risk of erosion and runoff. Matador also agreed to take additional measures to protect the heronry habitat located south of the proposed frac pond by meeting with a BLM Resource Representative prior to construction of the frac pond to place hay wattles

along the draw to the southeast. BLM and Matador agree that the frac pond's current dimension are not to exceed 800x800 feet. Furthermore, a request for expansion will not be granted due to maintaining the relevance, importance and functionality of the nearby resources.

Matador agrees to protect the critical habitat located south of the proposed Frac Pond throughout the life on the proposed project until finalization of the reclamation. To best protect this resource Matador proposes to meet with a BLM Resource Representative at the proposed site prior to construction of the Frac Pond to accurately place hay wattles along the draw at the BLM Resource Representative's direction. This will provide for the most effective protection of the resource. Please see the map below.

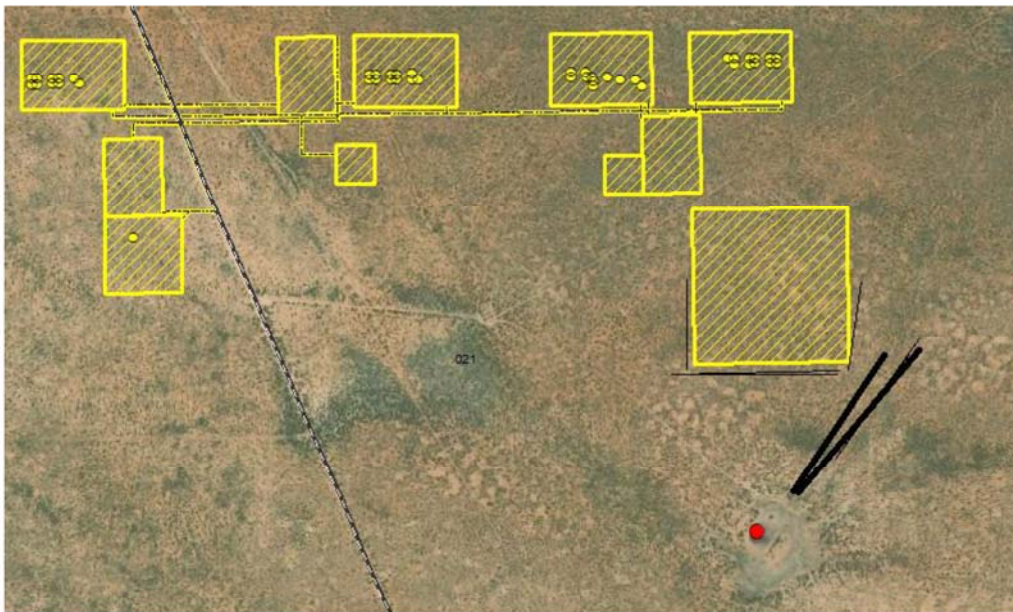

Range Stipulations / Conditions of Approval

Cattleguards

Where a permanent cattlegaurd is approved, an appropriately sized cattleguard(s) sufficient to carry out the project shall be installed and maintained at fence crossing(s). Any existing cattleguard(s) on the access road shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattleguard(s) that are in place and are utilized during lease operations. A gate shall be constructed on one side of the cattleguard and fastened securely to H-braces.

Fence Requirement

Where entry granted across a fence line, the fence must be braced and tied off on both sides of the passageway prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fence(s).

Livestock Watering Requirement

Structures that provide water to livestock, such as windmills, pipelines, drinking troughs, and earthen reservoirs, will be avoided by moving the proposed action. Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

Karst Stipulations / Conditions of Approval

CONSTRUCTION IMPACT ANALYSIS

The construction of roads, pipelines, compressor station pads and utilities can impact bedrock integrity and reroute, impede, focus, or erode natural surface drainage systems. Increased silting and sedimentation from construction can plug downstream sinkholes, caves, springs, and other components of aquifer recharge systems and result in adverse impacts to aquifer quality and cave environments. Any contaminants released into the environment during or after construction can impact aquifers and cave systems. A possibility exists for slow subsidence or sudden surface collapse during construction operations due to collapse of underlying cave passages and voids. This would cause associated safety hazards to the operator and the potential for increased environmental impact. Subsidence processes can be triggered by blasting, intense vibrations, rerouting of surface drainages, focusing of surface drainage, and general surface disturbance.

Blasting fractures in bedrock can serve as direct conduits for transfer of contaminants into cave and groundwater systems. Blasting also creates an expanded volume of rock rubble that cannot be reclaimed to natural contours, soil condition, or native vegetative condition. As such, surface and subsurface disruptions from blasting procedures can lead to permanent changes in vegetation, rainfall percolation, silting/erosion factors, aquifer recharge, and freshwater quality and can increase the risk of contaminant migration from drilling/production facilities built atop the blast area. Additional or special Conditions of Approval may apply at that time.

CONSTRUCTION MITIGATION

In order to mitigate the impacts from construction activities on cave and karst resources, the following Conditions of Approval will apply to this APD or project:

- In the event that any underground voids are encountered during construction activities, construction activities will be halted and the BLM will be notified immediately.
- No Blasting to prevent geologic structure instabilities.
- Pad Berming to minimize effects of any spilled contaminants.

DRILLING IMPACT ANALYSIS

During drilling, previously unknown cave and karst features could be encountered. If a void is encountered while drilling and a loss of circulation occurs, lost drilling fluids can directly contaminate groundwater recharge areas, aquifers, and groundwater quality. Drilling operations can also lead to sudden collapse of underground voids. Cementing operations may plug or alter groundwater flow, potentially reducing the water quantity at springs and water wells. Inadequate subsurface cementing, casing, and cave/aquifer protection measures can lead to the migration of oil, gas, drilling fluids, and produced saltwater into cave systems and freshwater aquifers.

DRILLING MITIGATION

Federal regulations and standard Conditions of Approval applied to all APDs require that adequate measures are taken to prevent contamination to the environment. Due to the extreme sensitivity of the cave and karst resources in this project area, the following additional Conditions of Approval will be added to this APD.

To prevent cave and karst resource contamination the following will be required.

- Closed Mud System Using Steel Tanks with All Fluids and Cuttings Hauled Off.
- Rotary drilling with fresh water where cave or karst features are expected to prevent contamination of freshwater aquifers.
- Directional Drilling allowed after at least 100 feet below the cave occurrence zone to prevent additional impacts resulting from directional drilling.
- Lost Circulation zones logged and reported in the drilling report so BLM can assess the situation and work with the operator on corrective actions.
- Additional drilling, casing, and cementing procedures to protect cave zones and fresh water aquifers. See Drilling COAs.

PRODUCTION IMPACT ANALYSIS

Production facilities such as tank batteries, pump-jacks, compressors, transfer stations, and pipe may fail and allow contaminants to enter caves and freshwater systems. Downhole casing and cementing failures can allow migration of fluids and/or gas between formations and aquifers. Facilities may also be subject to slow subsidence or sudden collapse of the underlying bedrock.

PRODUCTION MITIGATION

In order to mitigate the impacts from production activities and due to the nature of karst terrain, the following Conditions of Approval will apply to this APD:

- Tank battery liners and berms to minimize the impact resulting from leaks.
- Leak detection system to provide an early alert to operators when a leak has occurred.
- Automatic shut off, check valves, or similar systems will be installed for pipelines and tanks to minimize the effects of line failures used in production or drilling.

RESIDUAL AND CUMULATIVE IMPACT ANALYSIS

Any industrial activities that take place upon or within karst terrains or freshwater aquifer zones have the potential to create both short-term and long-term negative impacts to freshwater aquifers and cave systems. While a number of mitigation measures can be implemented to mitigate many impacts, it is still possible for impacts to occur from containment failures, well blowouts, accidents, spills, and structural collapses. It is therefore necessary to implement long-term monitoring studies to determine if current mitigations measures are sufficient enough to prevent long-term or cumulative impacts.

RESIDUAL AND CUMULATIVE MITIGATION

- Nontoxic fluorescent dyes will be added to the drilling fluid when the hole is spudded and will be circulated to the bottom of the karst layers. This provides data as part of a long-term monitoring study.

- Annual pressure monitoring will be performed by the operator. If the test results indicate a casing failure has occurred, remedial action will be undertaken to correct the problem to the BLM's approval.

PLUGGING AND ABANDONMENT IMPACT ANALYSIS

Failure of a plugged and abandoned well can lead to migration of contaminants to karst resources and fresh water aquifers. While this action does not specifically approve plugging and abandonment procedures, the operator should be made aware that additional or special Conditions of Approval may apply at that time.

PLUGGING AND ABANDONMENT MITIGATION

Abandonment Cementing: Upon well abandonment in high cave karst areas additional plugging conditions of approval may be required. The BLM will assess the situation and work with the operator to ensure proper plugging of the wellbore.

MITIGATING MEASURES for ROADS:

- Roads will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize changes to runoff or possible leaks and spills from entering karst systems.
- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, cave passages, or voids are penetrated during construction and no further construction will be done until clearance has been issued by the Authorized Officer.
- Turnout ditches and drainage leadoffs will not be constructed in such a manner as to increase or decrease the natural flow of water into or out of cave or karst features.
- Special restoration stipulations or realignment may be required.

MITIGATING MEASURES FOR POWERLINES:

- Smaller powerlines will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize changes to runoff or possible leaks and spills from entering karst systems. Larger powerlines will adjust their pole spacing to avoid cave and karst features.
- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, cave passages, or voids are penetrated during construction.
- No further construction will be done until clearance has been issued by the Authorized Officer.
- Special restoration stipulations or realignment may be required.

MITIGATING MEASURES for BURIED PIPELINES AND CABLES:

- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, passages, or voids are intersected by trenching, and no pipe will be laid in the trench at that point until clearance has been issued by the Authorized Officer.
- If a void is encountered alignments may be rerouted to avoid the karst feature and lessen; the potential of subsidence or collapse of karst features, buildup of toxic or combustible gas, or other possible impacts to cave and karst resources from the buried pipeline.

- Special restoration stipulations or realignment may be required at such intersections, if any.
- A leak detection plan **will be submitted to the BLM Carlsbad Field Office for approval** prior to pipeline installation. The method could incorporate gauges to detect pressure drops, siting valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.
- Regular monitoring is required to quickly identify leaks for their immediate and proper treatment.

MITIGATING MEASURES for SURFACE FLOWLINES:

- Flowlines will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize the possibility of leaks and spills from entering karst systems.
- If a void is encountered alignments may be rerouted to avoid the karst feature and lessen; the potential of subsidence or collapse of karst features, buildup of toxic or combustible gas, or other possible impacts to cave and karst resources from the buried pipeline.
- Regular monitoring is required to quickly identify leaks for their immediate and proper treatment.
- All spills or leaks will be reported to the BLM immediately for their immediate and proper treatment.

Special Status Plans Species Stipulations

For projects with potential for direct impacts but not direct displacement

No blading would be authorized within proposed project. Occupied habitat areas at high risk for habitat degradation and/or displacement of special status plant species individuals would be barricaded from project-related activities, as specified in the Conditions of Approval or by a BLM Authorized Officer. All surface disturbance within 50 meters of known special status plant species locations will be mulched after construction, as specified in the Conditions of Approval or by a BLM Authorized Officer.

To prevent direct impacts to the Tharp's Blue Star individuals that were observed during field surveys, the individuals will be visibly marked and barricaded to impede accidental pedestrian, vehicle or equipment travel over the individual. Project participants will be briefed about the avoidance area and trained in Tharp's Blue Star identification prior to initiating any ground disturbing activities, including vehicle travel. Upon project completion, the barricade and visible markings will be removed, and the condition of the individual will be documented and reported to the Authorized Officer and BLM Botanist.

To limit any impacts to vegetation and to protect any special status plant species that were not observed during field surveys, vehicles and equipment would be kept on existing roads and approved surfaces and would avoid travel across undisturbed surfaces;

workers would be instructed not to park off roads or in undisturbed areas more than 20 meters from fenceline.

Blading of vegetation within undisturbed areas will not be allowed: maximum width of blading operations will not exceed 0 feet. The fenceline is included in this area. (Blading is defined as the complete removal of brush and ground vegetation).

BLM special status plant surveys would be required for subsequent actions tiered from this analysis when the impacts effects zones of the proposed actions intersect SSPS potential habitat that has not been surveyed within three years prior to the notice of application for the proposed action. If occupied habitat is observed within the impacts effects zones for the proposed action(s), the proposed action(s) would avoid occupied habitat and mitigate anticipated impacts as determined appropriate for the conservation of the species by the Authorized Officer in coordination with a BLM biologist.

Vehicles and equipment will be kept on existing roads and approved surfaces only, and will avoid travel across undisturbed surfaces; workers will be instructed not to park off the roads or in undisturbed areas. Alterations to project design and additions of project components will require SSPS surveys and re-analysis of impacts if those project elements intersect SSPS suitable habitat.

VI. CONSTRUCTION

A. NOTIFICATION

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

B. TOPSOIL

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

C. CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

D. FEDERAL MINERAL MATERIALS PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

E. WELL PAD SURFACING

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

F. EXCLOSURE FENCING (CELLARS & PITS)

Exclosure Fencing

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

G. ON LEASE ACCESS ROADS

Road Width

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

Surfacing

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

Crowning

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

Ditching

Ditching shall be required on both sides of the road.

Turnouts


Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

Drainage

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outsloping and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

Cross Section of a Typical Lead-off Ditch



All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

Formula for Spacing Interval of Lead-off Ditches

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

Cattle guards

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

Fence Requirement

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

Public Access

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes

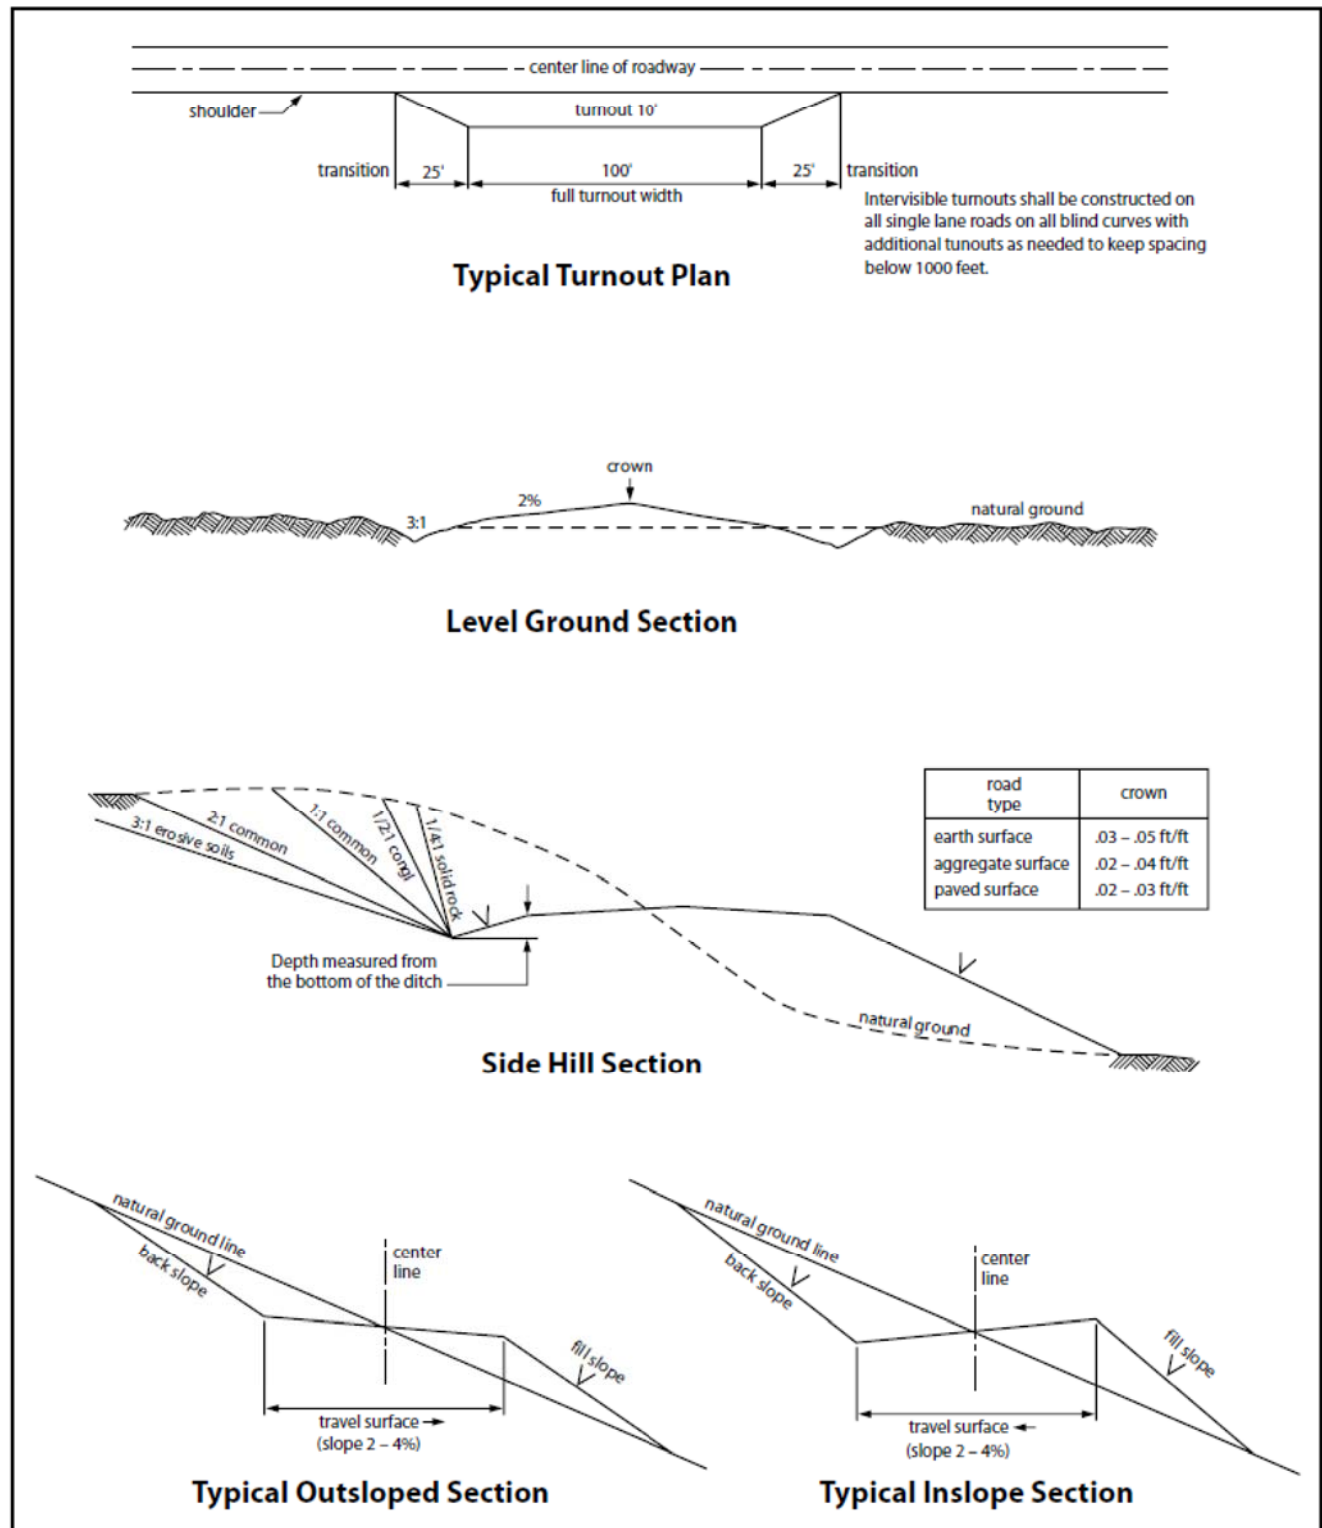


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

VII. PRODUCTION (POST DRILLING)

A. WELL STRUCTURES & FACILITIES

Placement of Production Facilities

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

Exclosure Netting (Open-top Tanks)

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

Chemical and Fuel Secondary Containment and Exclosure Screening

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

Open-Vent Exhaust Stack Exclosures

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

Containment Structures

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

Painting Requirement

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

B. PIPELINES

BURIED PIPELINE STIPULATIONS

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.
5. All construction and maintenance activity will be confined to the authorized right-of-way.
6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.
7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:
- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 20 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
 - Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
 - The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)
8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.
9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.

11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.

12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

☐ seed mixture 1	☒ seed mixture 3
☒ seed mixture 2	☐ seed mixture 4
☐ seed mixture 2/LPC	☐ Aplomado Falcon Mixture

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural and/or paleontological resources (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

17. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

18. Escape Ramps - The operator will construct and maintain pipeline/utility trenches that are not otherwise fenced, screened, or netted to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.
- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

19. Special Stipulations:

Hydrology Stipulations / Conditions of Approval

When crossing ephemeral drainages the pipeline(s) will be buried to a minimum depth of 48 inches from the top of pipe to ground level. Erosion control methods such as gabions and/or rock aprons should be placed on both up and downstream sides of the pipeline crossing. In addition, curled (weed free) wood/straw fiber wattles/logs and/or silt fences should be placed on the downstream side for sediment control during construction and maintained until soils and vegetation have stabilized. Water bars should be placed within the ROW to divert and dissipate surface runoff. A pipeline access road is not permitted to cross these ephemeral drainages. Traffic should be diverted to a preexisting route. Additional seeding may be required in floodplains and drainages to restore energy dissipating vegetation.

Prior to pipeline installation/construction a leak detection plan will be developed. The method(s) could incorporate gauges to detect pressure drops, situating valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.

Karst Stipulations / Conditions of Approval

The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, passages, or voids are intersected by trenching, and no pipe will be laid in the trench at that point until clearance has been issued by the Authorized Officer.

If a void is encountered alignments may be rerouted to avoid the karst feature and lessen; the potential of subsidence or collapse of karst features, buildup of toxic or combustible gas, or other possible impacts to cave and karst resources from the buried pipeline.

Special restoration stipulations or realignment may be required at such intersections, if any.

A leak detection plan **will be submitted to the BLM Carlsbad Field Office for approval** prior to pipeline installation. The method could incorporate gauges to detect pressure drops, siting valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.

Regular monitoring is required to quickly identify leaks for their immediate and proper treatment.

C. ELECTRIC LINES

STANDARD STIPULATIONS FOR OVERHEAD ELECTRIC DISTRIBUTION LINES

A copy of the grant and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the

release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. There will be no clearing or blading of the right-of-way unless otherwise agreed to in writing by the Authorized Officer.

5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the holder without liability or expense to the United States.

Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.

6. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

7. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.

8. Upon cancellation, relinquishment, or expiration of this grant, the holder shall comply with those abandonment procedures as prescribed by the Authorized Officer.

9. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this grant, whichever comes first. This will not apply where the power line extends

service to an active, adjoining facility or facilities.

10. Any cultural and/or paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

11. Special Stipulations:

- For reclamation remove poles, lines, transformer, etc. and dispose of properly.
- Fill in any holes from the poles removed.

Hydrology Stipulations / Conditions of Approval

Any water erosion that may occur due to the construction of overhead electric line and during the life of the power line will be quickly corrected and proper measures will be taken to prevent future erosion. A power pole should not be placed in drainages, playas, wetlands, riparian areas, or floodplains and must span across the features at a distance away that would not promote further erosion.

Karst Stipulations / Conditions of Approval

MITIGATING MEASURES FOR POWERLINES:

Smaller powerlines will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize changes to runoff or possible leaks and spills from entering karst systems. Larger powerlines will adjust their pole spacing to avoid cave and karst features.

The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, cave passages, or voids are penetrated during construction.

No further construction will be done until clearance has been issued by the Authorized Officer.

D. FRAC POND STIPULATIONS

FRAC POND CONDITIONS OF APPROVAL

A copy of the Right-of-Way Request, and attachments, including stipulations, survey plat and diagram, will be on location during construction. BLM personnel may request to see a copy of your permit during construction to ensure compliance with all conditions of approval.

Holder agrees to comply with the following conditions of approval to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this permit.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated.
3. Required Standard Conditions of Approval:
 - Contact the Supervisory Environmental Protection Specialist, Jim Amos, at 575-234-5909 at least 24 hours prior to starting construction.
 - The frac pond will only be authorized to contain freshwater and testing of water quality is required. Additives are not allowed without consent of the authorized officer.
 - If at any time the water in the frac pond becomes polluted with salts or other contaminants, use of the frac pond will cease and desist, and all liquids will be removed from the frac pond and disposed of properly.
 - Confine all construction and maintenance activity to the authorized area.
 - Temporary pipelines flowing from the frac pond to the target well will be laid along existing roadways unless an exception has been granted by the authorized officer.
 - Mineral materials extracted during construction of the frac pond will be stored on-location and/or used for constructing the frac pond.
 - The frac pond will be lined.
 - The operator shall stockpile topsoil approximately 25 feet outside the bermed perimeter of the pond in a low profile manner, reasonably protected from wind and water erosion
 - Topsoil shall not be used for constructing the frac pond. The topsoil will be used for final reclamation purposes only.
 - The frac pond shall be fenced on all sides.

- Install earthen erosion-control structures as are suitable for the specific terrain and soil conditions.
- The plastic lining will be removed prior to final abandonment
- Reclamation efforts will commence immediately after the frac pond is no longer needed for the purpose of completing wells.
- Within 3 months of completion of frac operations on associated wells, all earthwork and final reclamation must be completed. This includes reclaiming and/or removal of:

Any roads approved for use with the pond

Surface water lines

Tanks, pumps, fencing etc.

- Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Requirements for Operations and Final Reclamation:

4. If, during any phase of the construction, operation, maintenance, or termination of the frac pond, any pollutant should be released from the contaminated frac pond, the control and total removal, disposal, and cleaning up of such pollutant, wherever found, shall be the responsibility of holder, regardless of fault.

5. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

6. Any cultural and/or paleontological resources (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized

Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

7. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

8. After all disturbed areas have been satisfactorily contoured and prepared for seeding the location needs to be revegetated with the seed mixture provided. Seeding may need to be repeated until revegetation is successful. Operators shall contact Jim Amos, Supervisor, Environmental Protection – (575)234-5909, **prior** to beginning surface reclamation operations.

9. Seeding is required: Use the following seed mix.

☐ seed mixture 1	☒ seed mixture 3
☒ seed mixture 2	☐ seed mixture 4
☐ LPC mixture	☐ Aplomado Falcon mix

10. Special Stipulations:

11. Upon failure of holder to control, dispose of, or clean up such discharge, or to repair all damages resulting there-from, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.

E. OIL AND GAS RELATES SITES

STANDARD STIPULATIONS FOR OIL AND GAS RELATED SITES

A copy of the application (Grant/Sundry Notice) and attachments, including stipulations and map, will be on location during construction. BLM personnel may request to view a copy of your permit during construction to ensure compliance with all stipulations.

The holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer, BLM.

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant and for all response costs, penalties, damages, claims, and other costs arising from the provisions of the Resource Conservation and Recovery Act (RCRA), 42 U.S.C. Chap. 82, Section 6901 et. seq., from the Comprehensive Environmental Response, Compensation and Liability Act (CERCLA), 42 U.S.C. Chap. 109, Section 9601 et. seq., and from other applicable environmental statutes.

2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976, as amended (15 U.S.C. 2601, et. seq.) with regard to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized by this grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation and Liability Act, Section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the Authorized Officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et. seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et. seq.) on the right-of-way (unless the release or threatened release is wholly unrelated to the right-of-way holder's activity on the right-of-way). This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. If, during any phase of the construction, operation, maintenance, or termination of the site or related pipeline(s), any oil or other pollutant should be discharged from site facilities, the pipeline(s) or from containers or vehicles impacting Federal lands, the control and total removal, disposal, and cleanup of such oil or other pollutant, wherever found, shall be the responsibility of the holder, regardless of fault. Upon failure of the holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages to Federal lands resulting therefrom, the Authorized Officer may take such measures as deemed necessary to control and cleanup the discharge and restore the area, including, where appropriate, the aquatic environment and fish and wildlife

habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve the holder of any liability or responsibility.

5. Sites shall be maintained in an orderly, sanitary condition at all times. Waste materials, both liquid and solid, shall be disposed of promptly at an appropriate, authorized waste disposal facility in accordance with all applicable State and Federal laws. "Waste" means all discarded matter including, but not limited to, human waste, trash, garbage, refuse, petroleum products, brines, chemicals, oil drums, ashes, and equipment.

6. The operator will notify the Bureau of Land Management (BLM) authorized officer and nearest Fish and Wildlife Service (FWS) Law Enforcement office within 24 hours, if the operator discovers a dead or injured federally protected species (i.e., migratory bird species, bald or golden eagle, or species listed by the FWS as threatened or endangered) in or adjacent to a pit, trench, tank, exhaust stack, or fence. (If the operator is unable to contact the FWS Law Enforcement office, the operator must contact the nearest FWS Ecological Services office.)

7. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be a color which simulates "Standard Environmental Colors" designated by the Rocky Mountain Five-State Interagency Committee. The color selected for this project is **Shale Green**, Munsell Soil Color Chart Number 5Y 4/2.

8. Any cultural and/or paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

9. A sales contract for removal of mineral material (caliche, sand, gravel, fill dirt) from an authorized pit, site, or on location must be obtained from the BLM prior to commencing construction. There are several options available for purchasing mineral material: contact the BLM office (575-234-5972).

10. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

11. Once the site is no longer in service or use, the site must undergo final abandonment. At final abandonment, the site and access roads must undergo "final" reclamation so that the character and productivity of the land are restored. Earthwork for final reclamation must be completed within six (6) months of the abandonment of the site. All pads and facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact. After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

12. The holder shall stockpile an adequate amount of topsoil where blading occurs. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles. The topsoil will be used for final reclamation.

13. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- | | |
|--|--|
| ☐ seed mixture 1 | ☒ seed mixture 3 |
| ☒ seed mixture 2 | ☐ seed mixture 4 |
| ☐ seed mixture 2/LPC | ☐ Aplomado Falcon Mixture |

14. In those areas where erosion control structures are required to stabilize soil conditions, the holder shall install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound management practices. Any earth work will require prior approval by the Authorized Officer.

15. Open-topped Tanks - The operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps

16. The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an

impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclusion systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

17. Open-Vent Exhaust Stack Enclosures – The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (Recommended enclosure structures on open-vent exhaust stacks are in the shape of a cone.) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

18. Containment Structures - Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

19. Special Stipulations:

- The entire well pad will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The berm shall be maintained through the life of the well and after interim reclamation has been completed.
- Any water erosion that may occur due to the construction of the well pad during the life of the well will be corrected within two weeks and proper measures will be taken to prevent future erosion.

SPECIAL STATUS PLANT SPECIES (SSPS) HABITAT

Vehicles and equipment will be kept on existing roads and approved surfaces only, and will avoid travel across undisturbed surfaces; workers will be instructed not to park off the roads or in undisturbed areas. Alterations to project design and additions of project components will require SSPS surveys and re-analysis of impacts if those design project elements intersect SSPS suitable habitat. Blading, mowing, and chemical control of vegetation within undisturbed areas will not be allowed.

Sub Pad and Final Pad Stipulations / Conditions of Approval

Only the sub pad will be built for beginning production. The 400'x400' sub pad may be extended to the full 600'x600' length when needed to advance production. Only the 400'x400' sub pad may be graded until the additional 200' expansion is needed to advance production.

Hydrology Stipulations / Conditions of Approval

The entire well pad(s) will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. The compacted berm shall be constructed at a minimum of 12 inches with impermeable mineral material (e.g. caliche). Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The integrity of the berm shall be maintained around the surfaced pad throughout the life of the well and around the downsized pad after interim reclamation has been completed. Any water erosion that may occur due to the construction of the well pad during the life of the well will be quickly corrected and proper measures will be taken to prevent future erosion. Stockpiling of topsoil is required. The top soil shall be stockpiled in an appropriate location to prevent loss of soil due to water or wind erosion and not used for berming or erosion control. If fluid collects within the bermed area, the fluid must be vacuumed into a safe container and disposed of properly at a state approved facility.

Tank battery locations will be lined and bermed. A 20 mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Tank battery berms must be large enough to contain 1 ½ times the content of the largest tank or 24 hour production, whichever is greater. Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

Karst Stipulations / Conditions of Approval

CONSTRUCTION IMPACT ANALYSIS

The construction of roads, pipelines, compressor station pads and utilities can impact bedrock integrity and reroute, impede, focus, or erode natural surface drainage systems. Increased silting and sedimentation from construction can plug downstream sinkholes, caves, springs, and other components of aquifer recharge systems and result in adverse impacts to aquifer quality and cave environments. Any contaminants released into the environment during or after construction can impact aquifers and cave systems. A possibility exists for slow subsidence or sudden surface collapse during construction operations due to collapse of underlying cave passages and voids. This would cause associated safety hazards to the operator and the potential for increased environmental impact. Subsidence processes can be triggered by blasting, intense vibrations, rerouting of surface drainages, focusing of surface drainage, and general surface disturbance.

Blasting fractures in bedrock can serve as direct conduits for transfer of contaminants into cave and groundwater systems. Blasting also creates an expanded volume of rock rubble that cannot be reclaimed to natural contours, soil condition, or native vegetative condition. As such, surface and subsurface disruptions from blasting procedures can lead to permanent changes in vegetation, rainfall percolation, silting/erosion factors, aquifer recharge, and freshwater quality

and can increase the risk of contaminant migration from drilling/production facilities built atop the blast are additional or special Conditions of Approval may apply at that time.

CONSTRUCTION MITIGATION

In order to mitigate the impacts from construction activities on cave and karst resources, the following Conditions of Approval will apply to this APD or project:

- In the event that any underground voids are encountered during construction activities, construction activities will be halted and the BLM will be notified immediately.
- No Blasting to prevent geologic structure instabilities.
- Pad Berming to minimize effects of any spilled contaminants.

DRILLING IMPACT ANALYSIS

During drilling, previously unknown cave and karst features could be encountered. If a void is encountered while drilling and a loss of circulation occurs, lost drilling fluids can directly contaminate groundwater recharge areas, aquifers, and groundwater quality. Drilling operations can also lead to sudden collapse of underground voids. Cementing operations may plug or alter groundwater flow, potentially reducing the water quantity at springs and water wells. Inadequate subsurface cementing, casing, and cave/aquifer protection measures can lead to the migration of oil, gas, drilling fluids, and produced saltwater into cave systems and freshwater aquifers.

DRILLING MITIGATION

Federal regulations and standard Conditions of Approval applied to all APDs require that adequate measures are taken to prevent contamination to the environment. Due to the extreme sensitivity of the cave and karst resources in this project area, the following additional Conditions of Approval will be added to this APD.

To prevent cave and karst resource contamination the following will be required.

- Closed Mud System Using Steel Tanks with All Fluids and Cuttings Hauled Off.
- Rotary drilling with fresh water where cave or karst features are expected to prevent contamination of freshwater aquifers.
- Directional Drilling allowed after at least 100 feet below the cave occurrence zone to prevent additional impacts resulting from directional drilling.
- Lost Circulation zones logged and reported in the drilling report so BLM can assess the situation and work with the operator on corrective actions.
- Additional drilling, casing, and cementing procedures to protect cave zones and fresh water aquifers. See Drilling COAs.

PRODUCTION IMPACT ANALYSIS

Production facilities such as tank batteries, pump-jacks, compressors, transfer stations, and pipe may fail and allow contaminants to enter caves and freshwater systems. Downhole casing and cementing failures can allow migration of fluids and/or gas between formations and aquifers. Facilities may also be subject to slow subsidence or sudden collapse of the underlying bedrock.

PRODUCTION MITIGATION

In order to mitigate the impacts from production activities and due to the nature of karst terrain, the following Conditions of Approval will apply to this APD:

- Tank battery liners and berms to minimize the impact resulting from leaks.
- Leak detection system to provide an early alert to operators when a leak has occurred.
- Automatic shut off, check valves, or similar systems will be installed for pipelines and tanks to minimize the effects of line failures used in production or drilling.

RESIDUAL AND CUMULATIVE IMPACT ANALYSIS

Any industrial activities that take place upon or within karst terrains or freshwater aquifer zones have the potential to create both short-term and long-term negative impacts to freshwater aquifers and cave systems. While a number of mitigation measures can be implemented to mitigate many impacts, it is still possible for impacts to occur from containment failures, well blowouts, accidents, spills, and structural collapses. It is therefore necessary to implement long-term monitoring studies to determine if current mitigations measures are sufficient enough to prevent long-term or cumulative impacts.

RESIDUAL AND CUMULATIVE MITIGATION

- Nontoxic fluorescent dyes will be added to the drilling fluid when the hole is spudded and will be circulated to the bottom of the karst layers. This provides data as part of a long-term monitoring study.
- Annual pressure monitoring will be performed by the operator. If the test results indicate a casing failure has occurred, remedial action will be undertaken to correct the problem to the BLM's approval.

PLUGGING AND ABANDONMENT IMPACT ANALYSIS

Failure of a plugged and abandoned well can lead to migration of contaminants to karst resources and fresh water aquifers. While this action does not specifically approve plugging and abandonment procedures, the operator should be made aware that additional or special Conditions of Approval may apply at that time.

PLUGGING AND ABANDONMENT MITIGATION

Abandonment Cementing: Upon well abandonment in high cave karst areas additional plugging conditions of approval may be required. The BLM will assess the situation and work with the operator to ensure proper plugging of the wellbore.

MITIGATING MEASURES for ROADS:

- Roads will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize changes to runoff or possible leaks and spills from entering karst systems.
- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, cave passages, or voids are penetrated during construction and no further construction will be done until clearance has been issued by the Authorized Officer.
- Turnout ditches and drainage leadoffs will not be constructed in such a manner as to increase or decrease the natural flow of water into or out of cave or karst features.
- Special restoration stipulations or realignment may be required.

VIII. INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

IX. FINAL ABANDONMENT & RECLAMATION

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Ground-level Abandoned Well Marker to avoid raptor perching: Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well.

Seed Mixture 2, for Sandy Sites

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law (s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed* per acre:

<u>Species</u>	<u>lb/acre</u>
Sand dropseed (<i>Sporobolus cryptandrus</i>)	1.0
Sand love grass (<i>Eragrostis trichodes</i>)	1.0
Plains bristlegrass (<i>Setaria macrostachya</i>)	2.0

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed

Seed Mixture 3, for Shallow Sites

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law(s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed* per acre:

<u>Species</u>	<u>lb/acre</u>
Plains Bristlegrass (<i>Setaria macrostachya</i>)	1.0
Green Sprangletop (<i>Leptochloa dubia</i>)	2.0
Sideoats Grama (<i>Bouteloua curtipendula</i>)	5.0

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed

PECOS DISTRICT

DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	MATADOR PRODUCTION COMPANY
LEASE NO.:	NMNM138866
WELL NAME & NO.:	VONI FED COM / 204H
SURFACE HOLE FOOTAGE:	260'/N & 1098'/E
BOTTOM HOLE FOOTAGE:	240'/S & 990'/E
LOCATION:	Section 21, T.26 S., R.31 E., NMPM
COUNTY:	Eddy County, New Mexico

COA

H2S	☐ Yes	☒ No	
Potash	☒ None	☐ Secretary	☐ R-111-P
Cave/Karst Potential	☐ Low	☐ Medium	☒ High
Cave/Karst Potential	☐ Critical		
Variance	☐ None	☒ Flex Hose	☐ Other
Wellhead	☐ Conventional	☐ Multibowl	☒ Both
Other	☐ 4 String Area	☐ Capitan Reef	☐ WIPP
Other	☐ Fluid Filled	☐ Cement Squeeze	☐ Pilot Hole
Special Requirements	☐ Water Disposal	☒ COM	☐ Unit

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

Casing Design:

1. The 13-3/8 inch surface casing shall be set at approximately **1092 feet** (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after

- completing the cement job.
- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **7-5/8** inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
 - b. Second stage above DV tool:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office.
Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.
- ❖ In **High Cave/Karst Areas** if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
3. The minimum required fill of cement behind the **5-1/2** inch production casing is:

Option 1 (Single Stage):

- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
- b. Second stage above DV tool:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
- 2.

Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi**.
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **10,000 (10M) psi**. **Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**

Option 2:

1. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi**. **Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.

- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including

lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

NMK07222020



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Operator Certification Data Report

07/31/2020

Operator Certification

I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.

NAME: Lara Thompson

Signed on: 08/05/2019

Title: Project Manager

Street Address: 5647 Jefferson Street NE

City: Albuquerque

State: NM

Zip: 87109

Phone: (505)431-2678

Email address: Lara.Thompson@swca.com

Field Representative

Representative Name:

Street Address:

City:

State:

Zip:

Phone:

Email address:



APD ID: 10400045433

Submission Date: 08/20/2019

Highlighted data
reflects the most
recent changes

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

[Show Final Text](#)

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

Section 1 - General

APD ID: 10400045433

Tie to previous NOS? N

Submission Date: 08/20/2019

BLM Office: CARLSBAD

User: Lara Thompson

Title: Project Manager

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMNM138866

Lease Acres: 640

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? NO

Federal or Indian agreement:

Agreement number:

Agreement name:

Keep application confidential? Y

Permitting Agent? NO

APD Operator: MATADOR PRODUCTION COMPANY

Operator letter of designation:

Operator Info

Operator Organization Name: MATADOR PRODUCTION COMPANY

Operator Address: 5400 LBJ Freeway, Suite 1500

Zip: 75240

Operator PO Box:

Operator City: Dallas

State: TX

Operator Phone: (972)371-5200

Operator Internet Address: amonroe@matadorresources.com

Section 2 - Well Information

Well in Master Development Plan? NO

Master Development Plan name:

Well in Master SUPO? EXISTING

Master SUPO name: Voni Federal Master SUPO

Well in Master Drilling Plan? NO

Master Drilling Plan name:

Well Name: VONI FED COM

Well Number: 204H

Well API Number:

Field/Pool or Exploratory? Field and Pool

Field Name: Purple
Sage; Wolfcamp (Gas)

Pool Name: PURPLE SAGE;
WOLFCAMP (GAS)

Is the proposed well in an area containing other mineral resources? NATURAL GAS,OIL

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

Is the proposed well in an area containing other mineral resources? NATURAL GAS,OIL

Is the proposed well in a Helium production area? N Use Existing Well Pad? N New surface disturbance?

Type of Well Pad: MULTIPLE WELL

Multiple Well Pad Name: Slot 4 Number: 11

Well Class: HORIZONTAL

Number of Legs: 1

Well Work Type: Drill

Well Type: CONVENTIONAL GAS WELL

Describe Well Type:

Well sub-Type: EXPLORATORY (WILDCAT)

Describe sub-type:

Distance to town:

Distance to nearest well: 30 FT

Distance to lease line: 260 FT

Reservoir well spacing assigned acres Measurement: 770.49 Acres

Well plat: Voni_Fed_Com_204H_signed_C_102_20200420094700.pdf

Well work start Date: 12/01/2019

Duration: 60 DAYS

Section 3 - Well Location Table

Survey Type: RECTANGULAR

Describe Survey Type:

Datum: NAD83

Vertical Datum: NAVD88

Survey number:

Reference Datum: GROUND LEVEL

Wellbore	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD	Will this well produce from this lease?
SHL Leg #1	260	FNL	1128	FEL	26S	31E	21	Aliquot NENE	32.0347522	-103.778314	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 138866	3191	0	0	Y
KOP Leg #1	260	FNL	1128	FEL	26S	31E	21	Aliquot NENE	32.0347522	-103.778314	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 138866	-7622	10831	10813	Y
PPP Leg #1-1	0	FNL	1009	FEL	26S	31E	28	Aliquot NENE	32.0208275	-103.776754	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 138867	-8195	16730	11386	Y


Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

Wellbore	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD	Will this well produce from this lease?
PPP Leg #1-2	330	FNL	991	FEL	26S	31E	21	Aliquot NENE	32.0345605	- 103.7778688	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 138866	- 8046	11305	11237	Y
EXIT Leg #1	330	FSL	991	FEL	26S	31E	33	Lot 1	32.0010897	- 103.7777518	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 138867	- 8195	23615	11386	Y
BHL Leg #1	240	FSL	990	FEL	26S	31E	33	Lot 1	32.0008423	- 103.7777509	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 138867	- 8195	23705	11386	Y

LOCATION & ELEVATION VERIFICATION MAP

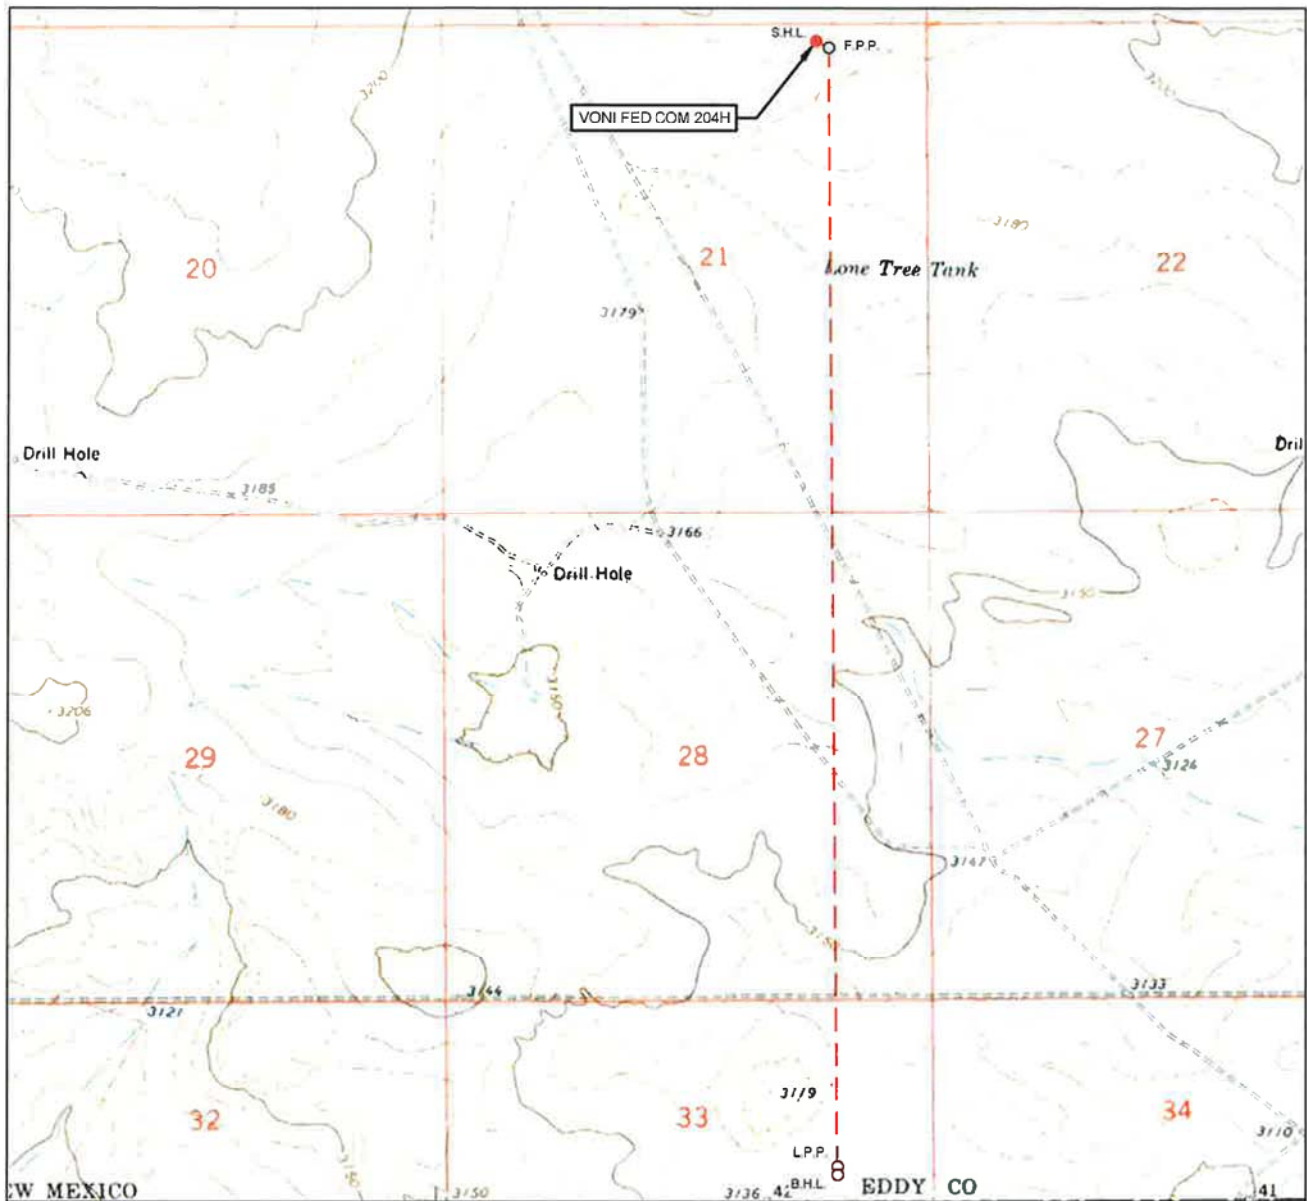

LEASE NAME & WELL NO.: VONI FED COM 204H

SECTION 21 TWP 26-S RGE 31-E SURVEY N.M.P.M.
 COUNTY EDDY STATE NM ELEVATION 3191'
 DESCRIPTION 260' FNL & 1128' FEL

LATITUDE N 32.0347522 LONGITUDE W 103.7783140



SCALE: 1" = 2000'
 0' 1000' 2000'

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY MATADOR PRODUCTION COMPANY. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.


ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.



TOPOGRAPHIC
 LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705
 TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743
 WWW.TOPOGRAPHIC.COM

VICINITY MAP

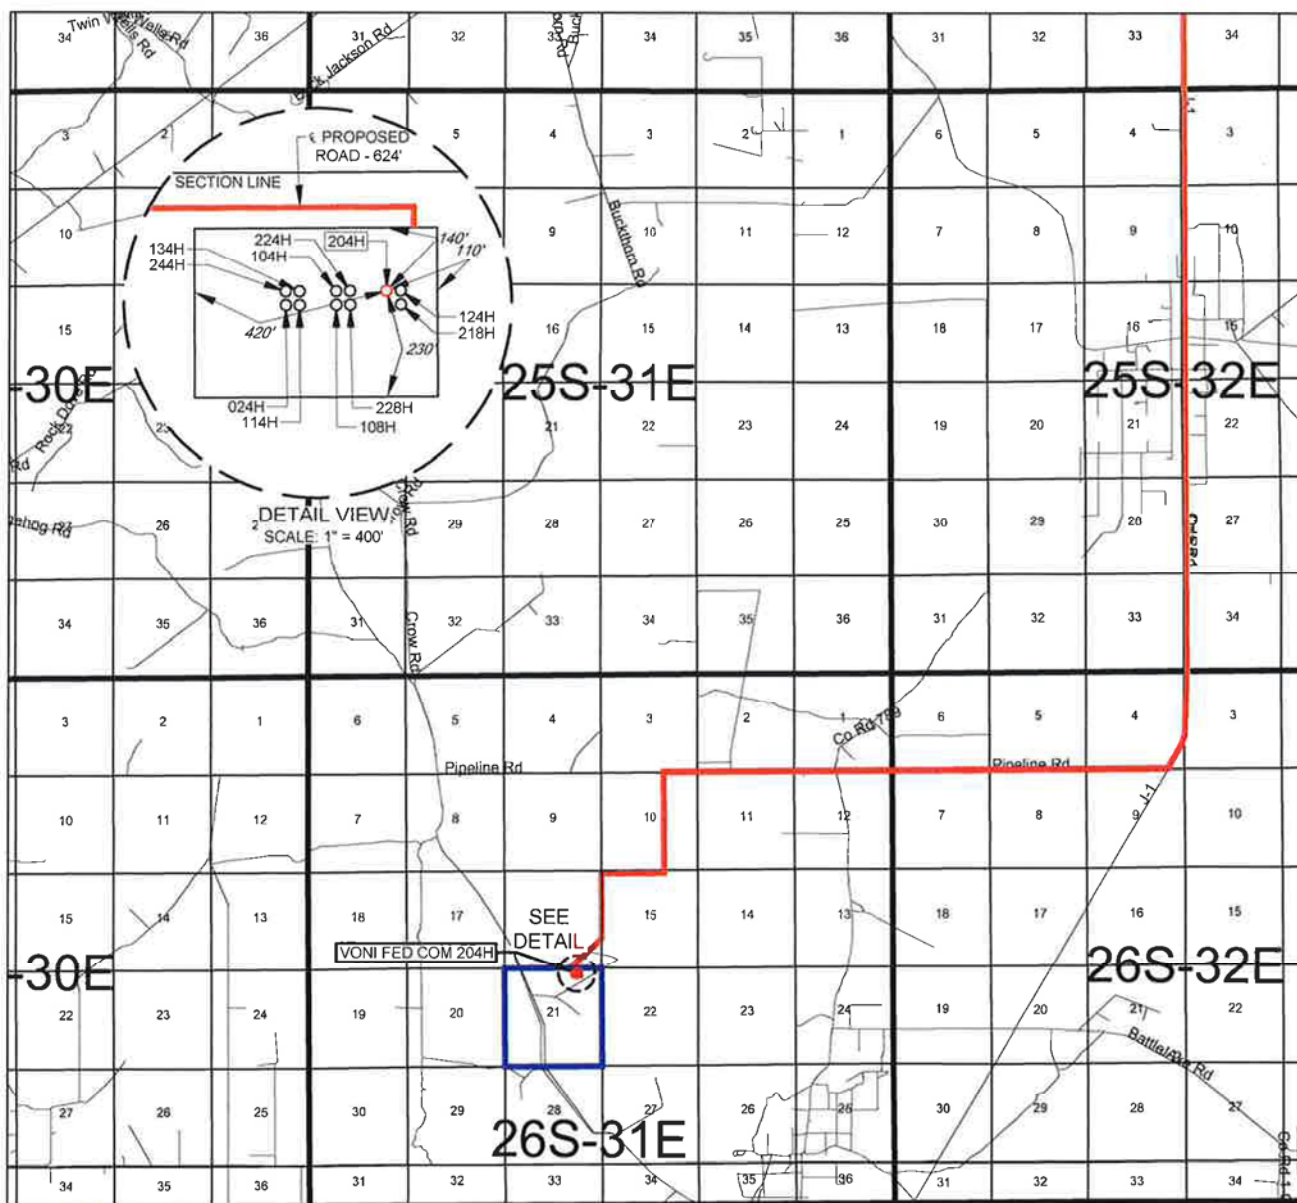

LEASE NAME & WELL NO.: _____ VONI FED COM 204H

SECTION 21 TWP 26-S RGE 31-E SURVEY N.M.P.M.
 COUNTY EDDY STATE NM
 DESCRIPTION 260' FNL & 1128' FEL

DISTANCE & DIRECTION

FROM INT. OF NM128 & J-1/ORLA RD., GO SOUTH ON J-1/ORLA RD. ± 10.5 MILES, THENCE WEST (RIGHT) ON PIPELINE RD ± 5.2 MILES, THENCE SOUTH (LEFT) ON PROPOSED RD. ± 1.0 MILES, THENCE WEST (RIGHT) ON PROPOSED RD. ± 1.8 MILES, THENCE EAST (LEFT) ON PROPOSED RD. ± 624 FEET, TO A POINT ± 144 FEET NORTHEAST OF THE LOCATION.

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY MATADOR PRODUCTION COMPANY. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.



SCALE: 1" = 10000'
 0' 5000' 10000'




TOPOGRAPHIC
 LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705
 TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743
 WWW.TOPOGRAPHIC.COM

SCALE: 1" = 2000'

SECTION 21, TOWNSHIP 26-S, RANGE 31-E, N.M.P.M.
EDDY COUNTY, NEW MEXICO

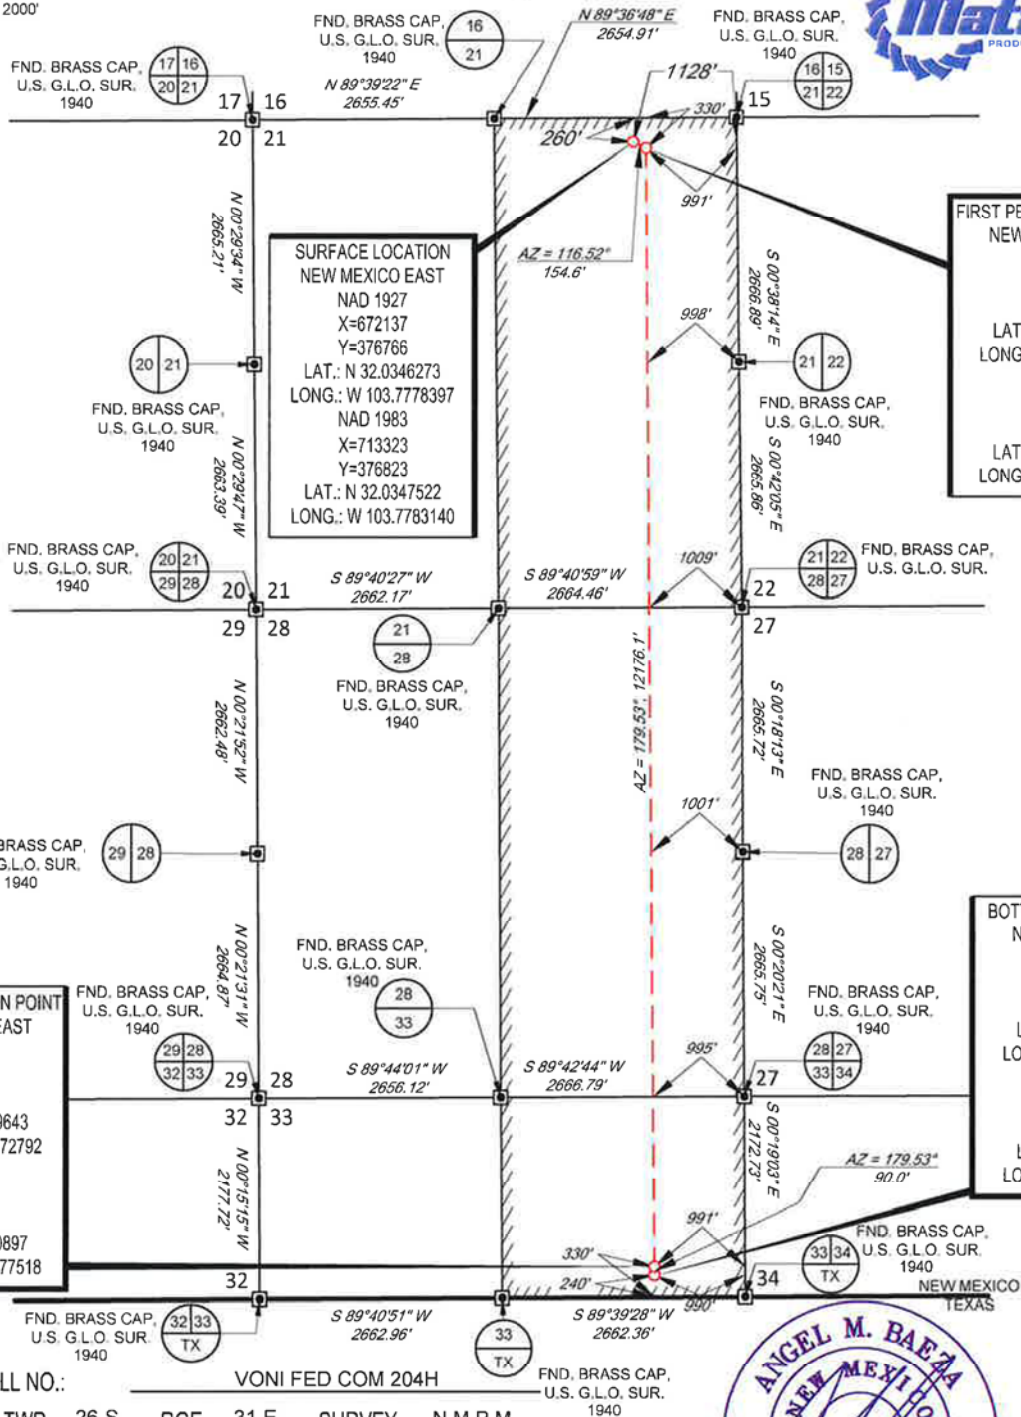

FIRST PERFORATION POINT
NEW MEXICO EAST
NAD 1927
X=672275
Y=376697
LAT.: N 32.0344354
LONG.: W 103.7773946
NAD 1983
X=713461
Y=376754
LAT.: N 32.0345605
LONG.: W 103.7778688

LAST PERFORATION POINT
NEW MEXICO EAST
NAD 1927
X=672373
Y=364521
LAT.: N 32.0009643
LONG.: W 103.7772792
NAD 1983
X=713560
Y=364578
LAT.: N 32.0010897
LONG.: W 103.777518

BOTTOM HOLE LOCATION
NEW MEXICO EAST
NAD 1927
X=672374
Y=364431
LAT.: N 32.0007169
LONG.: W 103.7772784
NAD 1983
X=713561
Y=364488
LAT.: N 32.0008423
LONG.: W 103.777509



Angel M. Baeza, P.S. No. 25116
January 24, 2020

TOPOGRAPHIC
LOYALTY INNOVATION LEGACY
1400 EVERMAN PARKWAY, Ste. 146 - FT. WORTH, TEXAS 76140
TELEPHONE: (817) 744-7512 - FAX (817) 744-7554
2803 NORTH BIG SPRING - MIDLAND, TEXAS 79705
TELEPHONE: (432) 682-1653 OR (800) 767-1653 - FAX (432) 682-1743
WWW.TOPOGRAPHIC.COM

LEASE NAME & WELL NO.: VONI FED COM 204H
SECTION 21 TWP 26-S RGE 31-E SURVEY N.M.P.M.
COUNTY EDDY STATE NM
DESCRIPTION 260' FNL & 1128' FEL

DISTANCE & DIRECTION
FROM INT. OF NM128. & J-1/ORLA RD. GO SOUTH ON J-1/ORLA RD. ±10.5 MILES.
THENCE WEST (RIGHT) ON PIPELINE RD ±5.2 MILES. THENCE SOUTH (LEFT) ON
PROPOSED RD. ±1.0 MILES. THENCE WEST (RIGHT) ON PROPOSED RD. ±1.8 MILES.
THENCE EAST (LEFT) ON PROPOSED RD. ±624 FEET, TO A POINT ±144 FEET
NORTHEAST OF THE LOCATION.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET
THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY MATADOR PRODUCTION COMPANY. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.
AS OF THE DATE OF SURVEY, ALL ABOVE GROUND APPURTENANCES WITHIN 300' OF THE STAKED LOCATION ARE SHOWN HEREON.

LEGEND


SECTION LINE
PROPOSED ROAD



SECTION 21, TOWNSHIP 26-S, RANGE 31-E, N.M.P.M.
EDDY COUNTY, NEW MEXICO

DETAIL VIEW
SCALE: 1" = 100'

SCALE: 1" = 100'
0' 50' 100'

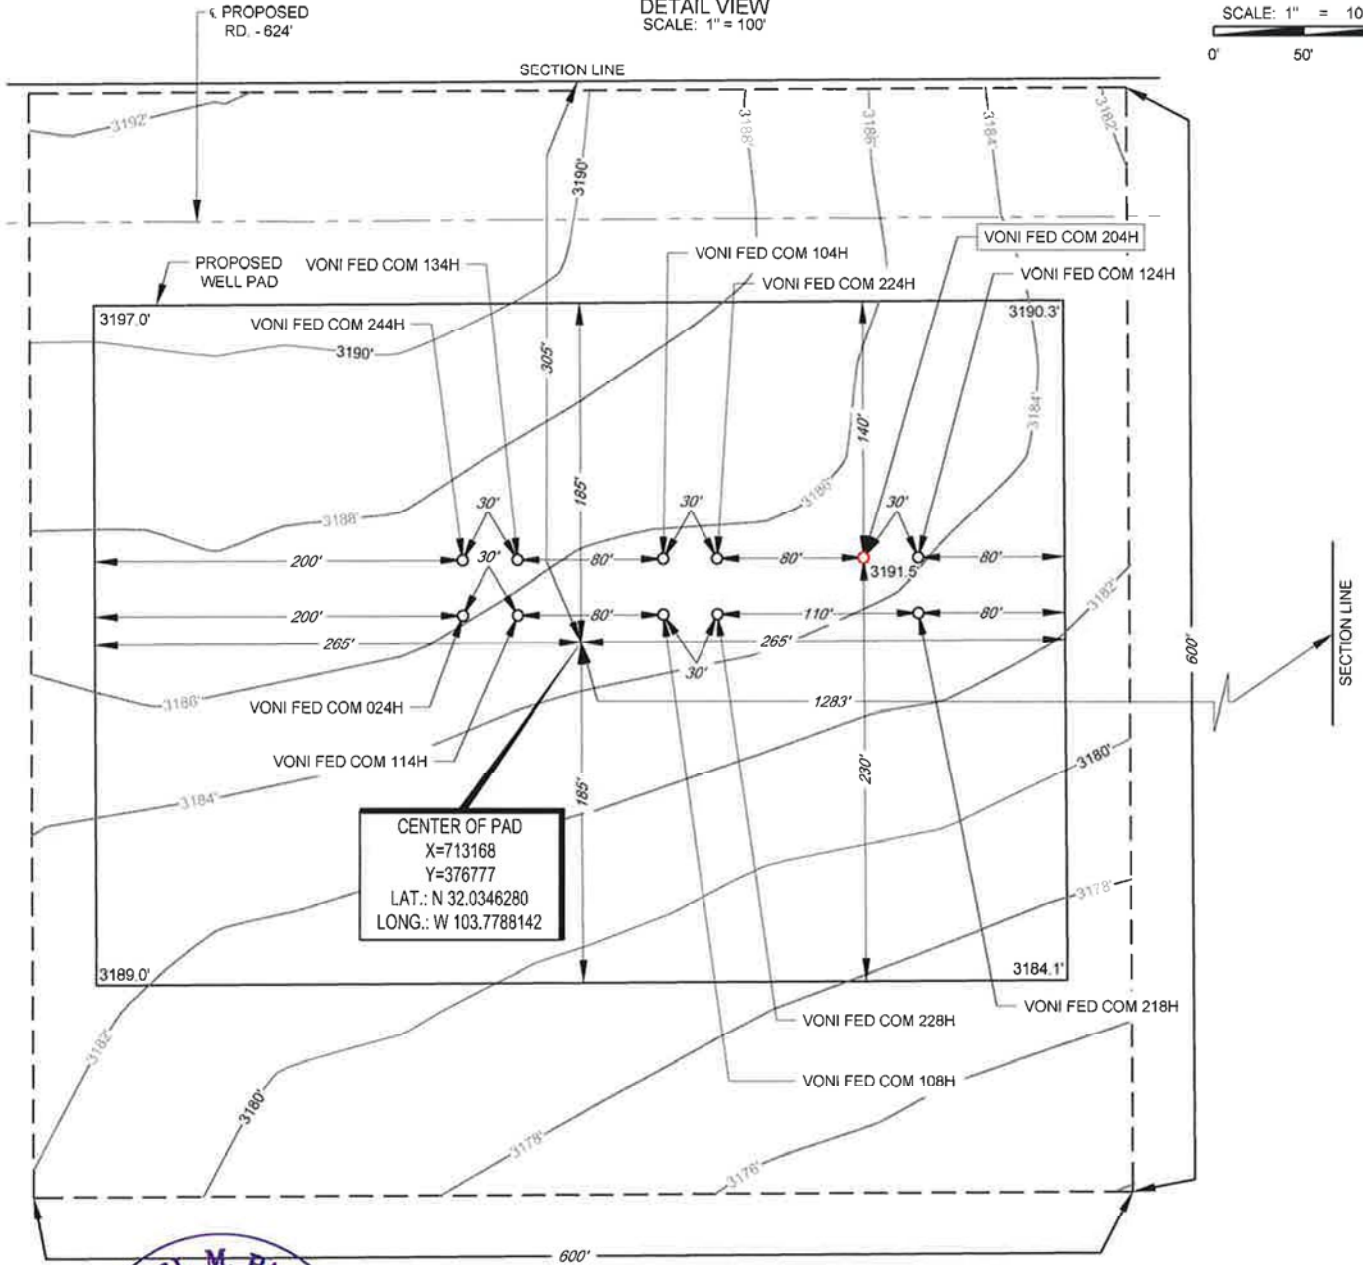

Angel M. Baeza, P.S. No. 25116

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET. ELEVATIONS USED ARE NAVD83, OBTAINED THROUGH AN OPUS SOLUTION. THIS PROPOSED PAD SITE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY MATADOR PRODUCTION COMPANY. ONLY THE DATA SHOWN ABOVE IS BEING CERTIFIED TO. ALL OTHER INFORMATION WAS INTENTIONALLY OMITTED. THIS PLAT IS ONLY INTENDED TO BE USED FOR A PERMIT AND IS NOT A BOUNDARY SURVEY. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION

ORIGINAL DOCUMENT SIZE: 8.5" X 11"

S:\SURVEY\MATADOR_RESOURCES\VONI_FEDERAL_21-26S-31E\FINAL_PRODUCTS\SILO_VONI_FED_COM_204H_REV4.DWG 1/27/2020 11:18:09 AM adisabella

LEASE NAME & WELL NO.: VONI FED COM 204H
204H LATITUDE N 32.0347522 204H LONGITUDE W 103.7783140

CENTER OF PAD IS 305' FNL & 1283' FEL




TOPOGRAPHIC
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
2803 NORTH BIG SPRING • MIDLAND, TEXAS 79705
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743
WWW.TOPOGRAPHIC.COM

SCALE: 1" = 300'
0' 150' 300'

SECTION 21, TOWNSHIP 26-S, RANGE 31-E, N.M.P.M.
EDDY COUNTY, NEW MEXICO

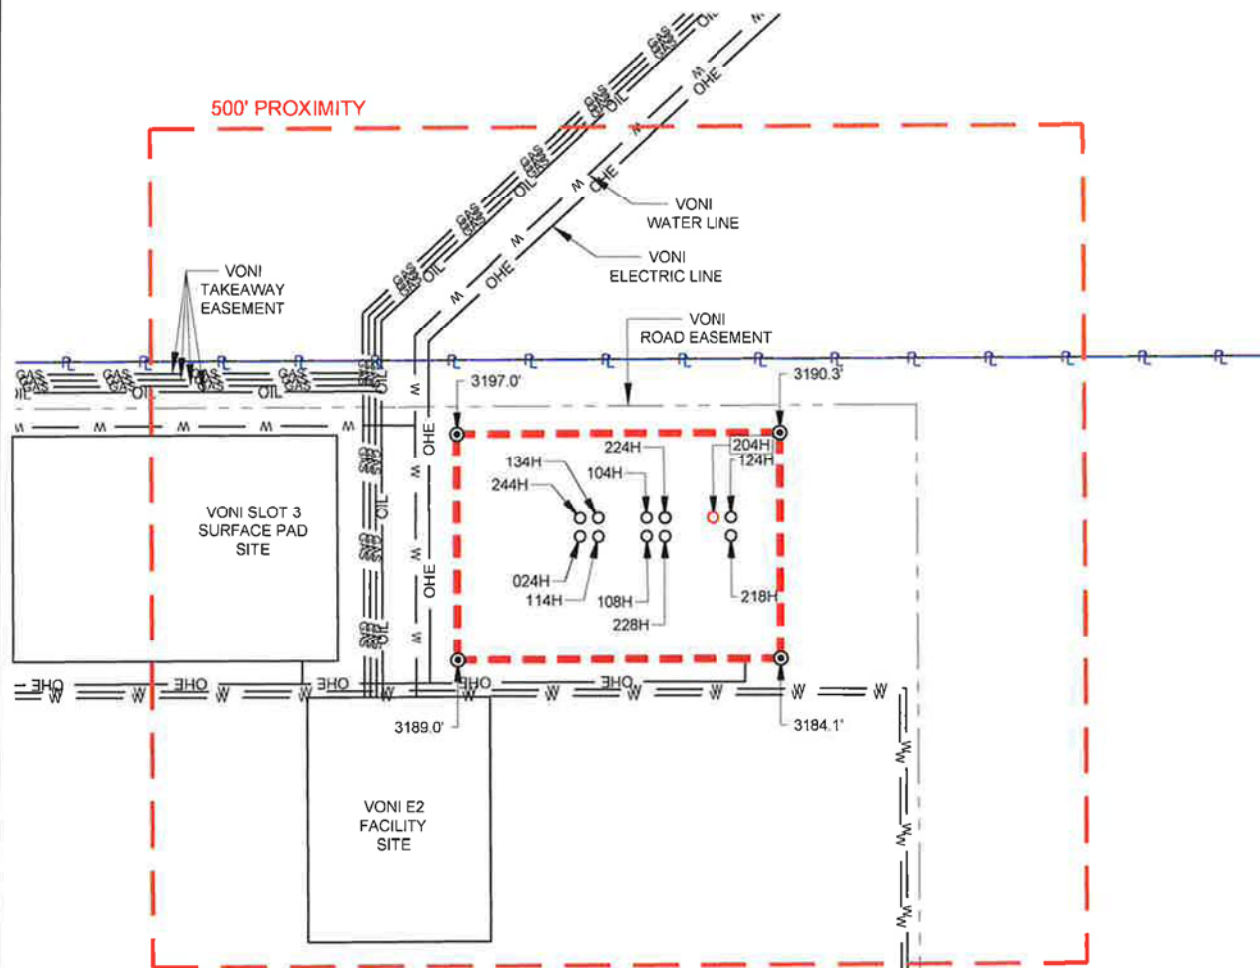

LEGEND

- PROPOSED SITE
- 500' PROXIMITY
- TRACT BORDER
- PROPOSED ROAD
- PROPOSED GAS TAKEAWAY
- OHE PROPOSED ELECTRIC
- W PROPOSED WATERLINE
- SECTION LINE
- IRON ROD SET



TOPOGRAPHIC
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 140 • FT. WORTH, TEXAS 76140
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743
WWW.TOPOGRAPHIC.COM



Angel M. Baeza, P.S. No. 25116
January 23, 2020

VONI FED COM 204H PROXIMITY MAP	REVISION:		NOTES: 1. ORIGINAL DOCUMENT SIZE: 8.5" X 11" 2. ALL BEARINGS, DISTANCES AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET. 3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER MY SUPERVISION, AND USING DOCUMENTATION PROVIDED BY MATADOR PRODUCTION COMPANY. ONLY UTILITIES/EASEMENTS THAT WERE VISIBLE ON THE DATE OF THIS SURVEY, WITHIN/ADJOINING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREON OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY. 4. ADJOINER INFORMATION SHOWN FOR INFORMATIONAL PURPOSES ONLY.
	EAH	02/04/19	
DATE: 01/28/19	EAH	03/06/19	
FILE: LO_VONI_FED_COM_204H_REV4	AMD	03/28/19	
DRAWN BY: EAH	IMU	01/24/20	
SHEET: 6 OF 6			

APD ID: 10400045433

Submission Date: 08/20/2019

Highlighted data
reflects the most
recent changes

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

[Show Final Text](#)

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
508843	RUSTLER	3191	893	893	ANHYDRITE	NONE	N
508844	SALADO	1617	1574	1574	SALT	NONE	N
508856	CASTILE	-200	3391	3391	SALT	NONE	N
508845	LAMAR	-834	4025	4025	SALT	NONE	N
508846	BELL CANYON	-861	4052	4052	SANDSTONE	NATURAL GAS	N
508847	CHERRY CANYON	-1951	5142	5142	SANDSTONE	NATURAL GAS, OIL	N
508848	BRUSHY CANYON	-3100	6291	6291	SANDSTONE	NATURAL GAS, OIL	N
508849	BONE SPRING LIME	-4753	7944	7944	LIMESTONE	NATURAL GAS, OIL	N
508850	BONE SPRING 1ST	-5739	8930	8930	SANDSTONE	NATURAL GAS, OIL	N
519382	BONE SPRING 2ND	-6164	9355	9355	OTHER : Carbonate	NATURAL GAS, OIL	N
508853	BONE SPRING 3RD	-6920	10111	10111	OTHER : Carbonate	NATURAL GAS, OIL	N
508855	WOLFCAMP	-8046	11237	11305	SHALE	NATURAL GAS, OIL	Y

Section 2 - Blowout Prevention

Pressure Rating (PSI): 10M

Rating Depth: 18000

Equipment: A 18,000' 10,000-psi BOP stack consisting of 3 rams with 2 pipe rams, 1 blind ram, and one annular preventer will be utilized below surface casing to TD. See attachments for BOP and choke manifold diagrams. An accumulator complying with Onshore Order #2 requirements for the pressure rating of the BOP stack will be present. A rotating head will also be installed as needed.

Requesting Variance? YES

Variance request: Matador requests a variance to have the option of running a multi-bowl wellhead assembly for setting the Intermediate 1, Intermediate 2, and Production Strings. The BOPs will not be tested again unless any flanges are separated. Matador requests a variance to drill this well using a co-flex line between the BOP and choke manifold. Certification for

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

proposed co-flex hose is attached. The hose is not required by the manufacturer to be anchored. If the specific hose is not available, then one of equal or higher rating will be used. Matador requests a variance to have the option of batch drilling this well with other wells on the same pad. In the event that this well is batch drilled, the wellbore will be secured with a blind flange of like pressure. When the rig returns to this well and BOPs are installed, the operator will perform a full BOP test. Matador requests a variance to drill this well using a 5M annular preventer with a 10M BOP ram stack. The "Well Control Plan For 10M MASP Section of Wellbore" is attached. Matador request a variance to wave the centralizer requirement for the 7-5/8" flush casing in the last 800' of 8-3/4" hole and the 5-1/2" SF/Flush casing in the 6-3/4" hole. If a DV tool is used, depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above the current shoe. Lab reports with the 500 psi compressive strength time for the cement will be onsite for review. 9-7/8" hole depth may fluctuate, but 7-5/8" BUTT will only be run inside of 9-7/8" OH and Flush joint will be run in 8-3/4" OH. Cement volumes will be adjusted proportionally. Option to drill the entire Intermediate I hole section in 9-7/8" hole size. Matador request option to perform a bradenhead cement squeeze on Intermediate 1 string. Matador request a variance to utilize a surface setting rig. If this is used, Matador request the option to drill either 17.5" or 20" surface hole.

Testing Procedure: BOP will be inspected and operated as required in Onshore Order #2. Kelly cock and sub equipped with a full opening valve sized to fit the drill pipe and collars will be available on the rig floor in the open position. A third party company will test the BOPs. After setting surface casing, a minimum 10M BOPE system will be installed. Test pressures will be 250 psi low and 10,000 psi high with the annular preventer being tested to 250 psi low and 5000 psi high before drilling below surface shoe. In the event that the rig drills multiple wells on the pad and any seal subject to test pressures are broken, a full BOP test will be performed when the rig returns and the 10M BOPE system is re-installed.

Choke Diagram Attachment:

Voni_Fed_Com_204H_10M_Choke_Manifold_Arrangement_20200420112144.pdf

BOP Diagram Attachment:

Voni_Fed_Com_204H_10M_Well_Control_Plan_20200420112200.pdf

Voni_Fed_Com_204H_10M_BOP_20200420112200.pdf

Voni_Fed_Com_204H_Co_Flex_Certs_20200420112203.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	918	0	918	3191	2273	918	J-55	54.5	BUTT	1.125	1.125	BUOY	1.8	BUOY	1.8
2	INTERMEDIATE	9.875	7.625	NEW	API	N	0	9500	0	9500	3194	-6309	9500	P-110	29.7	BUTT	1.125	1.125	BUOY	1.8	BUOY	1.8
3	INTERMEDIATE	8.75	7.625	NEW	NON API	Y	9500	10681	9500	10663	-6309	-7472	1181	P-110	29.7	OTHER - VAM HTF-NR	1.125	1.125	BUOY	1.8	BUOY	1.8
4	PRODUCTION	6.75	5.5	NEW	NON API	Y	0	23705	0	11386	3194	-8195	23705	P-110	20	OTHER - Hunting TLW	1.125	1.125	BUOY	1.8	BUOY	1.8

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

Casing Attachments

Casing ID: 1 **String Type:** SURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Voni_Fed_Com_204H_BLM_Casing_Design_Assumptions_4_string_20200420133717.pdf

Casing ID: 2 **String Type:** INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Voni_Fed_Com_204H_BLM_Casing_Design_Assumptions_4_string_20200420134139.pdf

Casing ID: 3 **String Type:** INTERMEDIATE

Inspection Document:

Spec Document:

Voni_Fed_Com_204H_Casing_Specs_7.625in_29.7lb_VAM_HTF_NR_20200420134618.pdf

Tapered String Spec:

Voni_Fed_Com_204H_Tapered_String_Spec_20200420134635.pdf

Casing Design Assumptions and Worksheet(s):

Voni_Fed_Com_204H_BLM_Casing_Design_Assumptions_4_string_20200420134707.pdf

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

Casing Attachments

Casing ID: 4 String Type: PRODUCTION

Inspection Document:

Spec Document:

Voni_Fed_Com_204H_Casing_Specs_5.5in_20lb_Hunting_TLW_SC_20200420135006.pdf

Tapered String Spec:

Voni_Fed_Com_204H_Tapered_String_Spec_20200420135019.pdf

Casing Design Assumptions and Worksheet(s):

Voni_Fed_Com_204H_BLM_Casing_Design_Assumptions_4_string_20200420135054.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	618	420	1.72	12.5	716	50	C	5% NaCl + LCM
SURFACE	Tail		618	918	250	1.38	14.8	347	50	C	5% NaCl + LCM
INTERMEDIATE	Lead	4200	0	4200	400	3.66	10.3	1457	35	A/C	Stage 2: Tuned light blend

INTERMEDIATE	Lead		0	9681	770	3.66	10.3	2807	35	A/C	Tuned Light Blend
INTERMEDIATE	Tail		9681	10681	110	1.43	13.2	156	35	A/C	Stage 1: Fluid Loss + Dispersant + Retarder
INTERMEDIATE	Lead	4200	4200	9681	430	3.66	10.3	1589	35	A/C	Stage 1: Fluid Loss + Dispersant + Retarder + LCM
INTERMEDIATE	Tail		9681	10681	110	1.46	13.2	156	35	A/C	Stage 1: Fluid Loss + Dispersant + Retarder
INTERMEDIATE	Lead		0	10681	1000	1.46	14.2	1460	35	C	Bradenhead Contingency: Class C Cement + LCM

PRODUCTION	Lead		10481	23705	1050	1.17	14.5	1227	10	H	Fluid Loss + Dispersant + Retarder
------------	------	--	-------	-------	------	------	------	------	----	---	------------------------------------

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
-------------	-----------	------------------	--------	-----------	--------------	-------	---------	-------	---------	-------------	-----------

Section 5 - Circulating Medium

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

Describe what will be on location to control well or mitigate other conditions: All necessary mud products (barite, bentonite, LCM) for weight addition and fluid loss control will be on location at all times. Mud program is subject to change due to hole conditions.

Describe the mud monitoring system utilized: An electronic Pason mud monitoring system complying with Onshore Order 2 will be used.

Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	918	SPUD MUD	8.4	8.8							
918	1066 3	OTHER : Diesel Brine Emulsion	8.4	9.4							
1066 3	1138 6	OIL-BASED MUD	11.5	12.5							

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

A 2-person mud logging program will be used from Intermediate 2 Casing shoe to TD.

No electric logs are planned at this time. GR will be collected through the MWD tools from Intermediate casing to TD. CBL with CCL will be run as far as gravity will let it fall to top of curve

List of open and cased hole logs run in the well:

CEMENT BOND LOG, GAMMA RAY LOG, MUD LOG/GEOLOGICAL LITHOLOGY LOG,

Coring operation description for the well:

No core or drill stem test is planned.

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 7401

Anticipated Surface Pressure: 4896

Anticipated Bottom Hole Temperature(F): 187

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards attachment:

Hydrogen Sulfide drilling operations plan required? NO

Hydrogen sulfide drilling operations plan:

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

Voni_Fed_Com_204H_Directional_AC_Report_v2_20200420150458.pdf

Voni_Fed_Com_204H_Directional_Well_Plan_v2_20200420150459.pdf

Other proposed operations facets description:

Other proposed operations facets attachment:

Gas_Capture_Plan___Voni_Federal_Com_Slot_4_20200420150655.pdf

Voni_Fed_Com_204H_10M_Well_Control_Plan_20200420150655.pdf

Voni_Fed_Com_204H_Closed_Loop_System_20200420150655.pdf

H2S_Plan_20200420150656.pdf

Voni_Fed_Com_204H_4_String_Wellhead_Diagram_20200420150656.pdf

Voni_Fed_Com_204H_Drill_Plan___Revised_20200717132103.pdf

Other Variance attachment:

Operator Name: MATADOR PRODUCTION COMPANY

Well Name: VONI FED COM

Well Number: 204H

CONFIDENTIAL



Well Control Plan For 10M MASP Section of Wellbore

Component and Preventer Compatibility Table:

The table below covers the drilling and casing of the 10M MASP portion of the well and outlines the tubulars and the compatible preventers in use. This table, combined with the mud program, documents that two barriers to flow can be maintained at all times, independent of the rating of the annular preventer.

Component	OD	Preventer	RWP
Drill pipe	4"	Lower 3.5-5.5" VBR Upper 3.5-5.5" VBR	10M
HWDP	4"		
Jars/Agitator	4.75-5"		
Drill collars and MWD tools	4.75-5.25"		
Mud Motor	4.75-5.25"		
Production casing	4.5-5.5"		
ALL	0-13.625"	Annular	5M
Open-hole	-	Blind Rams	10M

VBR = Variable Bore Ram with compatible range listed in chart

HWDP = Heavy Weight Drill Pipe

MWD = Measurement While Drilling

Well Control Procedures

Well control procedures are specific to the rig equipment and the operation at the time the kick occurs. Below are the minimal high-level tasks prescribed to assure a proper shut-in while drilling, tripping, running casing, pipe out of the hole (open hole), and moving the Bottom Hole Assembly (BHA) through the Blowout Preventers (BOP). The maximum pressure at which well control is transferred from the annular to another compatible ram is 3,000 psi.

General Procedure While Drilling

1. Sound alarm (alert crew)
2. Space out drill string
3. Shut down pumps and stop rotary
4. Shut-in well with the annular preventer (The Hydraulic Control Remote (HCR) valve and choke will already be in the closed position)
5. Confirm shut-in
6. Notify tool pusher and company representative
7. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
8. Regroup and identify forward plan
9. If pressure has increased or is anticipated to increase above 3,000 psi, confirm spacing and close the upper pipe rams

General Procedure While Tripping

1. Sound alarm (alert crew)
2. Stab full opening safety valve and close
3. Space out drill string



Well Control Plan For 10M MASP Section of Wellbore

4. Shut-in well with annular preventer (The HCR valve and choke will already be in the closed position)
5. Confirm shut-in
6. Notify tool pusher and company representative
7. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
8. Regroup and identify forward plan
9. If pressure has increased or is anticipated to increase above 3,000 psi, confirm spacing and close the upper pipe rams

General Procedure While Running Casing

1. Sound alarm (alert crew)
2. Stab crossover and full opening safety valve and close
3. Space out string
4. Shut-in well with annular preventer (The HCR valve and choke will already be in the closed position)
5. Confirm shut-in
6. Notify tool pusher and company representative
7. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
8. Regroup and identify forward plan
9. If pressure has increased or is anticipated to increase above 3,000 psi, confirm spacing and close the upper pipe rams

General Procedure with No Pipe In Hole

1. At any point when the BOP stack is clear of pipe or BHA, the well will be shut in with blind rams, the HCR valve will be open, and choke will be closed. If pressure increase is observed:
2. Sound alarm (alert crew)
3. Confirm shut-in
4. Notify tool pusher and company representative
5. Read and record the following:
 - SICP
 - Time of shut in
6. Regroup and identify forward plan

General Procedure While Pulling BHA through Stack

1. Prior to pulling last joint/stand of drill pipe through the stack, perform flow check. If flowing:
 - a. Sound alarm (alert crew)
 - b. Stab full opening safety valve and close
 - c. Space out drill string
 - d. Shut-in well with annular preventer (The HCR valve and choke will already be in the closed position)
 - e. Confirm shut-in
 - f. Notify tool pusher and company representative
 - g. Read and record the following:
 - SIDPP and SICP



Well Control Plan For 10M MASP Section of Wellbore

- Pit gain
 - Time of shut in
 - h. Regroup and identify forward plan
2. With BHA in the stack and compatible ram preventer and pipe combo immediately available:
- a. Sound alarm (alert crew)
 - b. Stab crossover and full opening safety valve and close
 - c. Space out drill string with the upset just beneath the compatible pipe ram
 - d. Shut-in well using compatible pipe rams (The HCR valve and choke will already be in the closed position)
 - e. Confirm shut-in
 - f. Notify tool pusher and company representative
 - g. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
 - h. Regroup and identify forward plan
3. With BHA in the stack and no compatible ram preventer and pipe combo immediately available:
- a. Sound alarm (alert crew)
 - b. If possible to pick up high enough, pull BHA clear of the stack
 - i. Follow "No Pipe in Hole" procedure above
 - c. If impossible to pick up high enough to pull string clear of the stack:
 - i. Stab crossover, make up one joint/stand of drill pipe, and full opening safety valve and close
 - ii. Space out drill string with the upset just beneath the compatible pipe ram
 - iii. Shut-in well using compatible pipe rams (The HCR valve and choke will already be in the closed position)
 - iv. Confirm shut-in
 - v. Notify tool pusher and company representative
 - vi. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
 - vii. Regroup and identify forward plan

Well Control Drills


Well control drills are specific to the rig equipment, personnel, and operations. Each crew will execute one drill weekly relevant to ongoing operations, but will make a reasonable attempt to vary the type of drills. The drills will be recorded in the daily drilling log.



PATTERSON-UTI

Well Control

RIG: 297

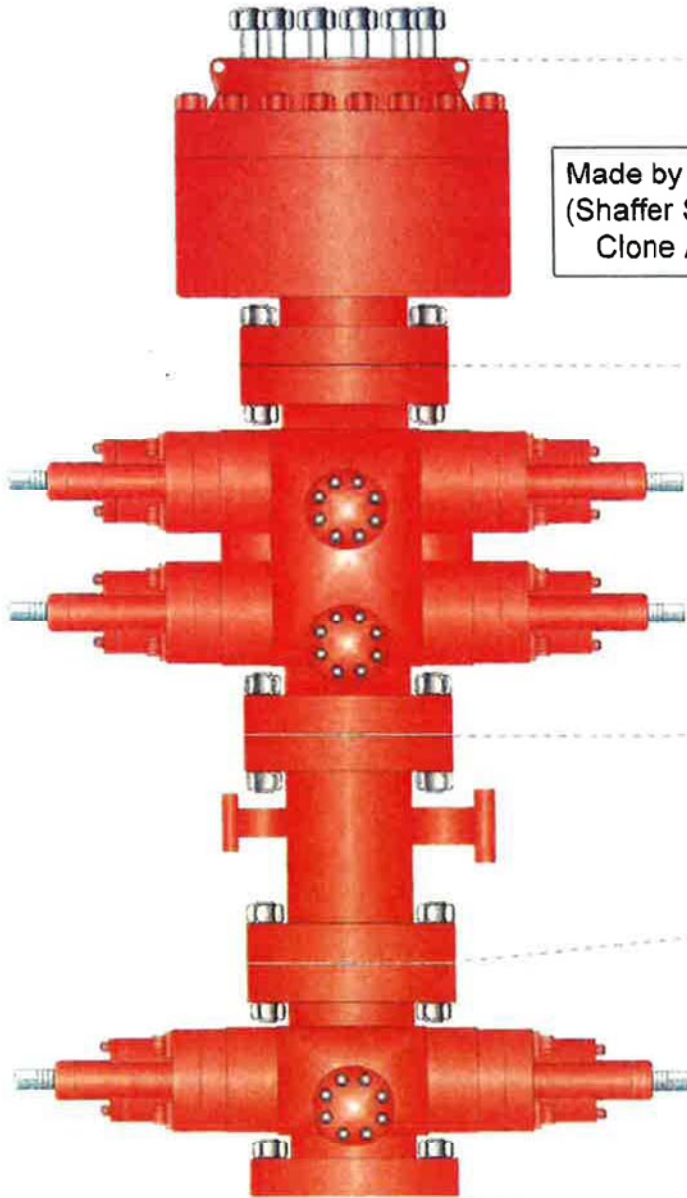

Made by Cameron
(Shaffer Spherical)
Clone Annular


PATTERSON-UTI # PS2-628
STYLE: New Shaffer Spherical
BORE 13 5/8" PRESSURE 5,000
HEIGHT: 48 1/2" WEIGHT: 13,800 lbs

PATTERSON-UTI # PC2-128
STYLE: New Cameron Type U
BORE 13 5/8" PRESSURE 10,000
RAMS: TOP 5" Pipe BTM Blinds
HEIGHT: 66 5/8" WEIGHT: 24,000 lbs

Length 40" Outlets 4" 10M
DSA 4" 10M x 2" 10M

PATTERSON-UTI # PC2-228
STYLE: New Cameron Type U
BORE 13 5/8" PRESSURE 10,000
RAMS: 5" Pipe
HEIGHT: 41 5/8" WEIGHT: 13,000 lbs

WING VALVES

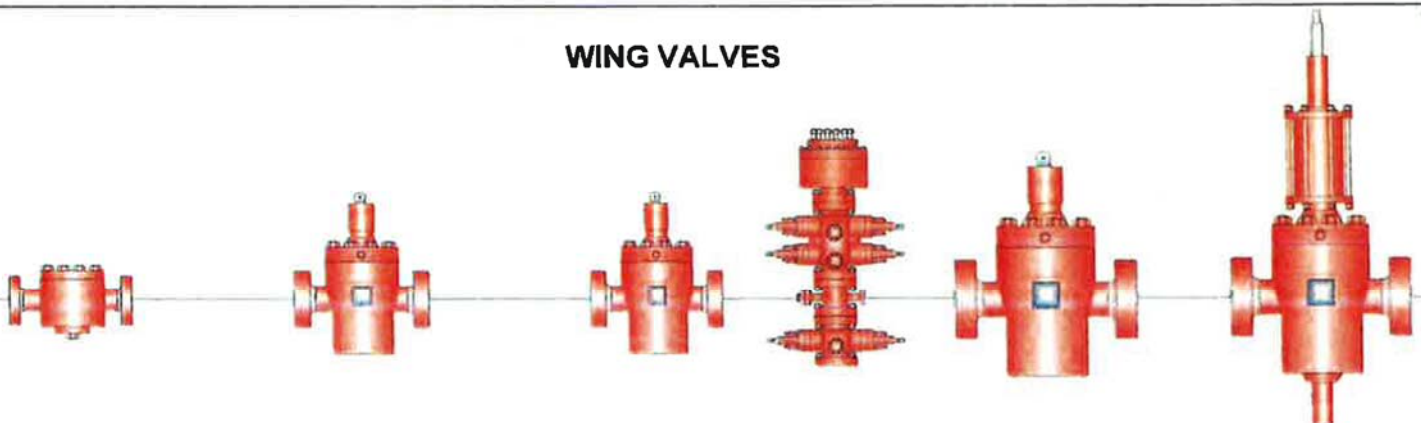

2" Check Valve

2" Manual Valve

2" Manual Valve

4" Manual Valve

4" Hydraulic Valve

December 8, 2014

Internal Hydrostatic Test Graph



Midwest Hose
& Specialty, Inc.

Customer: Patterson

Pick Ticket #: 284918

Hose Specifications

Hose Type

Ck

I.D.

3"

Length

10'

O.D.

4.79"

Verification

Type of Fitting

4-1/16 10K

Die Size

5.37"

Coupling Method

Swage

Final O.D.

5.37"

Working Pressure

10000 PSI

Burst Pressure

Standard Safety Multiplier Applies


Hose Serial

10490

Hose Assembly Serial

284918-2

Pressure Test

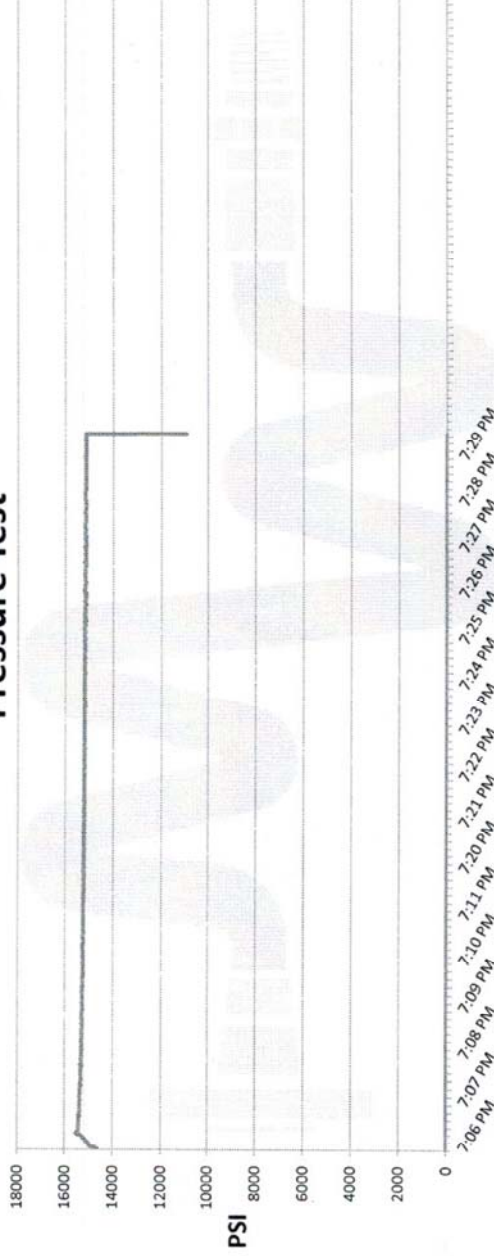

Test Pressure
15000 PSI

Time Held at Test Pressure
15 2/4 Minutes

Actual Burst Pressure

Peak Pressure
15732 PSI

Comments: Hose assembly pressure tested with water at ambient temperature.

Tested By: Tyler Hill

Approved By: Ryan Adams



Midwest Hose
& Specialty, Inc.

Internal Hydrostatic Test Certificate

General Information		Hose Specifications	
Customer	PATTERSON B&E	Hose Assembly Type	Choke & Kill
MWH Sales Representative	AMY WHITE	Certification	API 7K
Date Assembled	12/8/2014	Hose Grade	MUD
Location Assembled	OKC	Hose Working Pressure	10000
Sales Order #	236404	Hose Lot # and Date Code	10490-01/13
Customer Purchase Order #	260471	Hose I.D. (Inches)	3"
Assembly Serial # (Pick Ticket #)	287918-2	Hose O.D. (Inches)	5.30"
Hose Assembly Length	10'	Armor (yes/no)	YES
Fittings			
End A		End B	
Stem (Part and Revision #)	R3.0X64WB	Stem (Part and Revision #)	R3.0X64WB
Stem (Heat #)	91996	Stem (Heat #)	91996
Ferrule (Part and Revision #)	RF3.0	Ferrule (Part and Revision #)	RF3.0
Ferrule (Heat #)	37DA5631	Ferrule (Heat #)	37DA5631
Connection (Part #)	4 1/16 10K	Connection (Part #)	4 1/16 10K
Connection (Heat #)		Connection (Heat #)	
Dies Used	5.37	Dies Used	5.37
Hydrostatic Test Requirements			
Test Pressure (psi)	15,000	Hose assembly was tested with ambient water temperature.	
Test Pressure Hold Time (minutes)	15 1/2		
Date Tested	Tested By		Approved By
12/8/2014			



Midwest Hose
& Specialty, Inc.

Certificate of Conformity

Customer: **PATTERSON B&E**

Customer P.O.# **260471**

Sales Order # **236404**

Date Assembled: **12/8/2014**

Specifications

Hose Assembly Type: **Choke & Kill**

Assembly Serial # **287918-2**

Hose Lot # and Date Code **10490-01/13**

Hose Working Pressure (psi) **10000**

Test Pressure (psi) **15000**

We hereby certify that the above material supplied for the referenced purchase order to be true according to the requirements of the purchase order and current industry standards.

Supplier:

Midwest Hose & Specialty, Inc.

3312 S I-35 Service Rd

Oklahoma City, OK 73129

Comments:

Approved By

Date

12/9/2014

December 9, 2014



Midwest Hose
& Specialty, Inc.

Internal Hydrostatic Test Graph

Customer: Patterson

Pick Ticket #: 284918

Midwest Hose
& Specialty, Inc.

Hose Specifications

Hose Type

Ck

Length

20'

Type of Fitting

4-1/16 10K

Verification

Coupling Method

Swage

Die Size

5.37"

Final O.D.

5.40"

Hose Serial #

10490

Hose Assembly Serial #

284918-1

Working Pressure

10000 PSI

Burst Pressure

4.77"

Hose Serial #

10490

Hose Assembly Serial #

284918-1

Working Pressure

10000 PSI

Burst Pressure

4.77"


Hose Serial #

10490

Hose Assembly Serial #

284918-1

Pressure Test

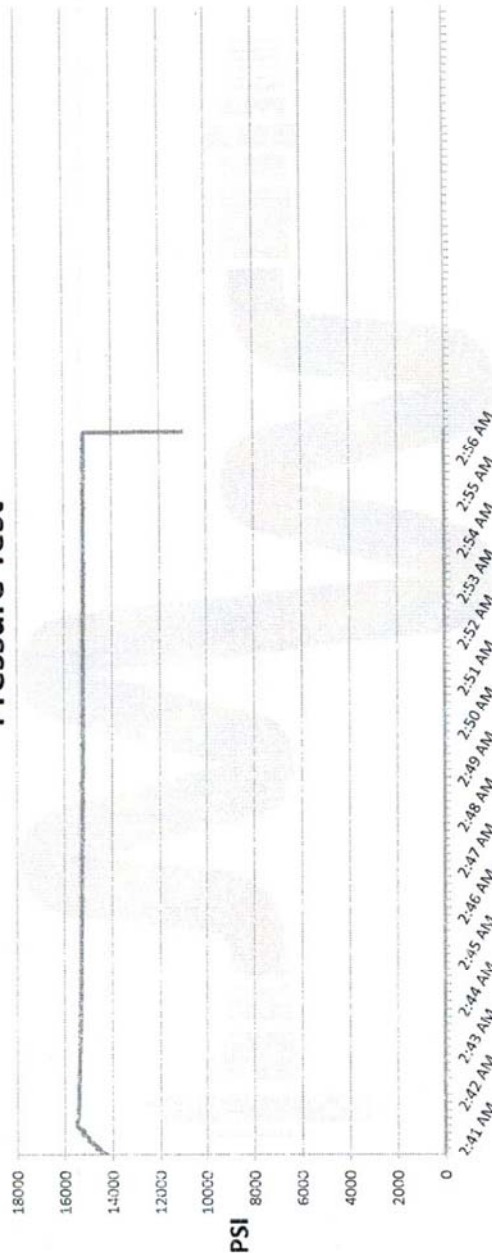

Test Pressure
15000 PSI

Time Held at Test Pressure
15 2/4 Minutes

Actual Burst Pressure

Peak Pressure
15893 PSI

Comments: Hose assembly pressure tested with water at ambient temperature.



Tested By: Tyler Hill

Approved By: Ryan Adams



Midwest Hose
& Specialty, Inc.

Internal Hydrostatic Test Certificate

General Information		Hose Specifications	
Customer	PATTERSON B&E	Hose Assembly Type	Choke & Kill
MWH Sales Representative	AMY WHITE	Certification	API 7K
Date Assembled	12/8/2014	Hose Grade	MUD
Location Assembled	OKC	Hose Working Pressure	10000
Sales Order #	236404	Hose Lot # and Date Code	10490-01/13
Customer Purchase Order #	260471	Hose I.D. (Inches)	3"
Assembly Serial # (Pick Ticket #)	287918-1	Hose O.D. (Inches)	5.30"
Hose Assembly Length	20'	Armor (yes/no)	YES
Fittings			
End A		End B	
Stem (Part and Revision #)	R3.0X64WB	Stem (Part and Revision #)	R3.0X64WB
Stem (Heat #)	A141420	Stem (Heat #)	A141420
Ferrule (Part and Revision #)	RF3.0	Ferrule (Part and Revision #)	RF3.0
Ferrule (Heat #)	37DA5631	Ferrule (Heat #)	37DA5631
Connection (Part #)	4 1/16 10K	Connection (Part #)	4 1/16 10K
Connection (Heat #)	V3579	Connection (Heat #)	V3579
Dies Used	5.37	Dies Used	5.37
Hydrostatic Test Requirements			
Test Pressure (psi)	15,000	Hose assembly was tested with ambient water temperature.	
Test Pressure Hold Time (minutes)	15 1/2		
Date Tested	Tested By	Approved By	
12/9/2014			



Midwest Hose
& Specialty, Inc.

Certificate of Conformity

Customer: **PATTERSON B&E**

Customer P.O.# **260471**

Sales Order # **236404**

Date Assembled: **12/8/2014**

Specifications

Hose Assembly Type: **Choke & Kill**

Assembly Serial # **287918-1**

Hose Lot # and Date Code **10490-01/13**

Hose Working Pressure (psi) **10000**

Test Pressure (psi) **15000**

We hereby certify that the above material supplied for the referenced purchase order to be true according to the requirements of the purchase order and current industry standards.

Supplier:

Midwest Hose & Specialty, Inc.

3312 S I-35 Service Rd

Oklahoma City, OK 73129

Comments:

Approved By

Date

12/9/2014

December 9, 2014

Internal Hydrostatic Test Graph



Midwest Hose
& Specialty, Inc.

Customer: Patterson

Pick Ticket #: 284918

Hose Specifications

Hose Type

Mud

I.D.

3"

Length

70'

O.D.

4.79"

Verification

Type of Fitting

4 1/16 10K

Die Size

5.37"

Coupling Method

Swage

Final O.D.

5.37"

Working Pressure

10000 PSI

Burst Pressure


Standard Safety Multiplier Applies

Hose Serial

10490

Hose Assembly Serial

284918-3

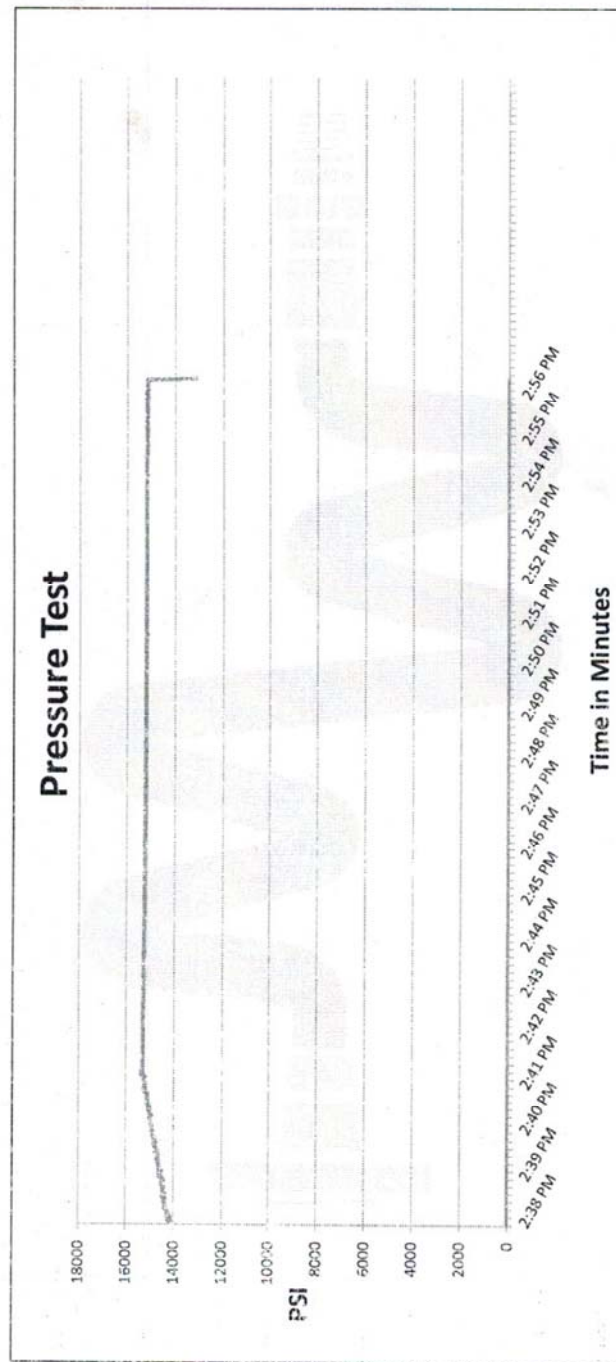

Test Pressure

15000 PSI

Time Held at Test Pressure

16 3/4 Minutes

Actual Burst Pressure

Peak Pressure

15410 PSI

Comments: Hose assembly pressure tested with water at ambient temperature.

Tested By: Tyler Hill

Approved By: Ryan Adams



Midwest Hose
& Specialty, Inc.

Internal Hydrostatic Test Certificate

General Information		Hose Specifications	
Customer	PATTERSON B&E	Hose Assembly Type	Choke & Kill
MWH Sales Representative	AMY WHITE	Certification	API 7K
Date Assembled	12/8/2014	Hose Grade	MUD
Location Assembled	OKC	Hose Working Pressure	10000
Sales Order #	236404	Hose Lot # and Date Code	10490-01/13
Customer Purchase Order #	260471	Hose I.D. (Inches)	3"
Assembly Serial # (Pick Ticket #)	287918-3	Hose O.D. (Inches)	5.23"
Hose Assembly Length	70'	Aarmor (yes/no)	YES
Fittings			
End A		End B	
Stem (Part and Revision #)	R3.0X64WB	Stem (Part and Revision #)	R3.0X64WB
Stem (Heat #)	A141420	Stem (Heat #)	A141420
Ferrule (Part and Revision #)	RF3.0	Ferrule (Part and Revision #)	RF3.0
Ferrule (Heat #)	37DA5631	Ferrule (Heat #)	37DA5631
Connection (Part #)	4 1/16 10K	Connection (Part #)	4 1/16 10K
Connection (Heat #)		Connection (Heat #)	
Dies Used	5.37	Dies Used	5.37
Hydrostatic Test Requirements			
Test Pressure (psi)	15,000	Hose assembly was tested with ambient water temperature.	
Test Pressure Hold Time (minutes)	16 3/4		
Date Tested	Tested By		Approved By
12/9/2014			



Midwest Hose
& Specialty, Inc.

Certificate of Conformity

Customer: PATTERSON B&E	Customer P.O.# 260471
Sales Order # 236404	Date Assembled: 12/8/2014

Specifications


Hose Assembly Type:	Choke & Kill		
Assembly Serial #	287918-3	Hose Lot # and Date Code	10490-01/13
Hose Working Pressure (psi)	10000	Test Pressure (psi)	15000

We hereby certify that the above material supplied for the referenced purchase order to be true according to the requirements of the purchase order and current industry standards.

Supplier:

Midwest Hose & Specialty, Inc.
3312 S I-35 Service Rd
Oklahoma City, OK 73129

Comments:

Approved By	Date
	12/9/2014

**DATA ARE INFORMATIVE ONLY.
BASED ON SI_PD-101836 P&B**



Connection Data Sheet

OD	Weight	Wall Th.	Grade	API Drift	Connection
7 5/8 in.	29.70 lb/ft	0.375 in.	P110 EC	6.750 in.	VAM® HTF NR

PIPE PROPERTIES	
Nominal OD	7.625 in.
Nominal ID	6.875 in.
Nominal Cross Section Area	8.541 sqin.
Grade Type	Enhanced API
Min. Yield Strength	125 ksi
Max. Yield Strength	140 ksi
Min. Ultimate Tensile Strength	135 ksi
Tensile Yield Strength	1 068 klb
Internal Yield Pressure	10 760 psi
Collapse pressure	7 360 psi

CONNECTION PROPERTIES	
Connection Type	Premium Integral Flush
Connection OD (nom)	7.701 in.
Connection ID (nom)	6.782 in.
Make-Up Loss	4.657 in.
Critical Cross Section	4.971 sqin.
Tension Efficiency	58 % of pipe
Compression Efficiency	72.7 % of pipe
Compression Efficiency with Sealability	34.8 % of pipe
Internal Pressure Efficiency	100 % of pipe
External Pressure Efficiency	100 % of pipe

CONNECTION PERFORMANCES	
Tensile Yield Strength	619 klb
Compression Resistance	778 klb
Compression with Sealability	372 klb
Internal Yield Pressure	10 760 psi
External Pressure Resistance	7 360 psi
Max. Bending	44 °/100ft
Max. Bending with Sealability	17 °/100ft

TORQUE VALUES	
Min. Make-up torque	9 600 ft.lb
Opti. Make-up torque	11 300 ft.lb
Max. Make-up torque	13 000 ft.lb
Max. Torque with Sealability	58 500 ft.lb
Max. Torsional Value	73 000 ft.lb

VAM® HTF™ (High Torque Flush) is a flush OD integral connection providing maximum clearance along with torque strength for challenging applications such as extended reach and slim hole wells, drilling liner / casing, liner rotation to achieve better cementation in highly deviated and critical High Pressure / High Temperature wells.

Looking ahead on the outcoming testing industry standards, VAM® decided to create an upgraded design and launch on the market the VAM® HTF-NR as the new standard version of VAM® extreme high torque flush connection. The VAM® HTF-NR has extensive tests as per API RP 5C5:2015 CAL II which include the gas sealability having load points with bending, internal pressure and high temperature at 135°C.

Do you need help on this product? - Remember no one knows VAM® like VAM®

canada@vamfieldservice.com
usa@vamfieldservice.com
mexico@vamfieldservice.com
brazil@vamfieldservice.com

uk@vamfieldservice.com
dubai@vamfieldservice.com
nigeria@vamfieldservice.com
angola@vamfieldservice.com

china@vamfieldservice.com
baku@vamfieldservice.com
singapore@vamfieldservice.com
australia@vamfieldservice.com

Over 180 VAM® Specialists available worldwide 24/7 for Rig Site Assistance

Other Connection Data Sheets are available at www.vamservices.com

Vallourec Group





TEC-LOCK WEDGE

5.500" 20 LB/FT (.361"Wall) with 5.875" SPECIAL CLEARANCE OD
BEN P110 CY

Pipe Body Data

Nominal OD:	5.500	in
Nominal Wall:	.361	in
Nominal Weight:	20.00	lb/ft
Plain End Weight:	19.83	lb/ft
Material Grade:	P110 CY	
Mill/Specification:	BEN	
Yield Strength:	125,000	psi
Tensile Strength:	135,000	psi
Nominal ID:	4.778	in
API Drift Diameter:	4.653	in
Special Drift Diameter:	None	in
RBW:	87.5 %	
Body Yield:	729,000	lbf
Burst:	14,360	psi
Collapse:	13,010	psi

Connection Data

Standard OD:	5.875	in
Pin Bored ID:	4.778	in
Critical Section Area:	5.656	in ²
Tensile Efficiency:	97 %	
Compressive Efficiency:	100 %	
Longitudinal Yield Strength:	707,000	lbf
Compressive Limit:	729,000	lbf
Internal Pressure Rating:	14,360	psi
External Pressure Rating:	13,010	psi
Maximum Bend:	101.2	°/100ft

Operational Data

Minimum Makeup Torque:	15,000	ft*lbf
Optimum Makeup Torque:	18,700	ft*lbf
Maximum Makeup Torque:	41,200	ft*lbf
Minimum Yield:	45,800	ft*lbf
Makeup Loss:	5.97	in

Notes Operational Torque is equivalent to the Maximum Make-Up Torque

Tapered String Specification Sheet

Voni Fed Com #204H
SHL: 260' FNL & 1128' FEL Section 21
BHL: 240' FSL & 990' FEL Section 33
Township/Range: 26S 31E
Elevation Above Sea Level: 3191

String	Hole Size (in)	Set MD (ft)	Set TVD (ft)	Casing Size (in)	Wt. (lb/ft)	Grade	Joint	Collapse	Burst	Tension
Surface	17.5	0 - 918	0 - 918	13.375	54.5	J-55	BUTT	1.125	1.125	1.8
Intermediate 1 Top	9.875	0 - 9500	0 - 9500	7.625	29.7	P-110	BUTT	1.125	1.125	1.8
Intermediate 1 Bottom	8.75	9500 - 10681	9500 - 10663	7.625	29.7	P-110	VAM HTF-NR	1.125	1.125	1.8
Production	6.75	0 - 23705	0 - 11386	5.5	20	P-110	Hunting TLW	1.125	1.125	1.8

Tapered String Specification Sheet

Voni Fed Com #204H
SHL: 260' FNL & 1128' FEL Section 21
BHL: 240' FSL & 990' FEL Section 33
Township/Range: 26S 31E
Elevation Above Sea Level: 3191

String	Hole Size (in)	Set MD (ft)	Set TVD (ft)	Casing Size (in)	Wt. (lb/ft)	Grade	Joint	Collapse	Burst	Tension
Surface	17.5	0 - 918	0 - 918	13.375	54.5	J-55	BUTT	1.125	1.125	1.8
Intermediate 1 Top	9.875	0 - 9500	0 - 9500	7.625	29.7	P-110	BUTT	1.125	1.125	1.8
Intermediate 1 Bottom	8.75	9500 - 10681	9500 - 10663	7.625	29.7	P-110	VAM HTF-NR	1.125	1.125	1.8
Production	6.75	0 - 23705	0 - 11386	5.5	20	P-110	Hunting TLW	1.125	1.125	1.8

Casing Design Criteria and Load Case Assumptions

Surface Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.43 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.52 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.43 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (8.3 ppg).

Intermediate #1 Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.52 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 50 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.47 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (10.0 ppg).

Intermediate #2 Casing

Collapse: $DF_c=1.125$

- Partial Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.47 psi/ft). The effects of axial load on collapse will be considered. Internal force equal to gas gradient over half of setting depth and mud gradient with which the next hole section will be run below that (0.65 psi/ft).

- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.47 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 100 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.65 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (9.0 ppg).

Production Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.65 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.65 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: 8000 psi casing test with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.
- Injection Down Casing: 9500 psi surface injection pressure plus an internal pressure gradient of 0.65 psi/ft with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (12.5 ppg).

Casing Design Criteria and Load Case Assumptions

Surface Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.43 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.52 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.43 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (8.3 ppg).

Intermediate #1 Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.52 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 50 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.47 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (10.0 ppg).

Intermediate #2 Casing

Collapse: $DF_c=1.125$

- Partial Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.47 psi/ft). The effects of axial load on collapse will be considered. Internal force equal to gas gradient over half of setting depth and mud gradient with which the next hole section will be run below that (0.65 psi/ft).

- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.47 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 100 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.65 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (9.0 ppg).

Production Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.65 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.65 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: 8000 psi casing test with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.
- Injection Down Casing: 9500 psi surface injection pressure plus an internal pressure gradient of 0.65 psi/ft with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (12.5 ppg).

Casing Design Criteria and Load Case Assumptions

Surface Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.43 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.52 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.43 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (8.3 ppg).

Intermediate #1 Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.52 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 50 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.47 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (10.0 ppg).

Intermediate #2 Casing

Collapse: $DF_c=1.125$

- Partial Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.47 psi/ft). The effects of axial load on collapse will be considered. Internal force equal to gas gradient over half of setting depth and mud gradient with which the next hole section will be run below that (0.65 psi/ft).

- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.47 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 100 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.65 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (9.0 ppg).

Production Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.65 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.65 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: 8000 psi casing test with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.
- Injection Down Casing: 9500 psi surface injection pressure plus an internal pressure gradient of 0.65 psi/ft with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (12.5 ppg).

Casing Design Criteria and Load Case Assumptions

Surface Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.43 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.52 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.43 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (8.3 ppg).

Intermediate #1 Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.52 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 50 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.47 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.52 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (10.0 ppg).

Intermediate #2 Casing

Collapse: $DF_c=1.125$

- Partial Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.47 psi/ft). The effects of axial load on collapse will be considered. Internal force equal to gas gradient over half of setting depth and mud gradient with which the next hole section will be run below that (0.65 psi/ft).

- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.47 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: Casing test per Onshore Oil and Gas Order No. 2 with an external force equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Gas Kick Profile: Internal burst force at the shoe will be Fracture Pressure at that depth. Surface burst pressure will be fracture gradient at setting depth less a gas gradient to equivalent height of 100 bbl kick with Drill Pipe inside casing and mud gradient with which the next hole section will be run above that (0.65 psi/ft). External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft), which is a more conservative backup force than pore pressure.
- Fracture at Shoe with 1/3 BHP at Surface: Internal burst force at the shoe will be Fracture Pressure at setting depth. Internal burst force at surface will be 1/3 of pore pressure at setting depth. External force will be equal to the mud gradient in which the casing will be run (0.47 psi/ft) which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (9.0 ppg).

Production Casing

Collapse: $DF_c=1.125$

- Full Internal Evacuation: Collapse force equal to the mud gradient in which the casing will be run (0.65 psi/ft). The effects of axial load on collapse will be considered.
- Cementing: Collapse force equal to the gradient of planned cement slurries to planned depths and mud gradient in which the casing will be run above that (0.65 psi/ft) and an internal force equal to mud gradient of displacement fluid (0.43 psi/ft).

Burst: $DF_b=1.125$

- Pressure Test: 8000 psi casing test with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.
- Injection Down Casing: 9500 psi surface injection pressure plus an internal pressure gradient of 0.65 psi/ft with an external force equal to the mud gradient in which the casing will be run (0.65 psi/ft), which is a more conservative backup force than pore pressure.

Tensile: $DF_t=1.8$

- Overpull: A downward force of 100,000 lbs is applied at the shoe along with the weight of the casing string utilizing the effects of buoyancy (12.5 ppg).

Matador Production Company

Rustler Breaks

Voni

Voni Fed Com #204H

Wellbore #1

BLM Plan #1

Anticollision Report

21 January, 2020

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Reference	BLM Plan #1		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	Stations	Error Model:	ISCWSA
Depth Range:	Unlimited	Scan Method:	Closest Approach 3D
Results Limited by:	Maximum center-center distance of 10,000.0 usft	Error Surface:	Pedal Curve
Warning Levels Evaluated at:	2.00 Sigma	Casing Method:	Not applied

Survey Tool Program	Date	1/21/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
0.0	23,705.7	BLM Plan #1 (Wellbore #1)	MWD	OWSG MWD - Standard

Summary						
Site Name	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
Voni						
Voni Fed Com #024H - Wellbore #1 - BLM Plan #1	4,333.2	4,350.2	86.4	53.5	2.630	CC
Voni Fed Com #024H - Wellbore #1 - BLM Plan #1	4,400.0	4,416.3	86.9	53.5	2.605	ES, SF
Voni Fed Com #104H - Wellbore #1 - BLM Plan #1	7,609.2	7,612.0	77.0	22.9	1.422	Level 3, CC, ES, SF
Voni Fed Com #108H - Wellbore #1 - BLM Plan #1	1,577.7	1,605.7	93.5	82.5	8.473	CC
Voni Fed Com #108H - Wellbore #1 - BLM Plan #1	1,700.0	1,716.2	94.1	82.2	7.868	ES
Voni Fed Com #108H - Wellbore #1 - BLM Plan #1	3,400.0	3,407.1	159.2	133.0	6.089	SF
Voni Fed Com #114H - Wellbore #1 - BLM Plan #1	500.0	500.0	192.4	189.3	61.590	CC
Voni Fed Com #114H - Wellbore #1 - BLM Plan #1	8,754.2	8,761.1	241.3	179.2	3.887	ES, SF
Voni Fed Com #124H - Wellbore #1 - BLM Plan #1	500.0	501.0	30.1	26.9	9.611	CC
Voni Fed Com #124H - Wellbore #1 - BLM Plan #1	700.0	700.0	30.9	26.3	6.802	ES
Voni Fed Com #124H - Wellbore #1 - BLM Plan #1	9,500.0	9,526.4	331.8	264.3	4.913	SF
Voni Fed Com #218H - Wellbore #1 - BLM Plan #1	500.0	501.0	42.4	39.3	13.557	CC
Voni Fed Com #218H - Wellbore #1 - BLM Plan #1	800.0	801.1	43.2	38.0	8.197	ES
Voni Fed Com #218H - Wellbore #1 - BLM Plan #1	23,705.7	23,956.7	695.9	297.6	1.747	SF
Voni Fed Com #224H - Wellbore #1 - BLM Plan #1	500.0	501.0	80.0	76.9	25.584	CC
Voni Fed Com #224H - Wellbore #1 - BLM Plan #1	600.0	601.0	80.6	76.8	20.986	ES
Voni Fed Com #224H - Wellbore #1 - BLM Plan #1	11,000.0	11,004.8	159.7	81.4	2.040	SF
Voni Fed Com #228H - Wellbore #1 - BLM Plan #1	500.0	501.0	85.4	82.3	27.313	CC
Voni Fed Com #228H - Wellbore #1 - BLM Plan #1	8,400.0	8,405.5	135.5	75.3	2.251	ES
Voni Fed Com #228H - Wellbore #1 - BLM Plan #1	8,500.0	8,504.5	136.4	75.5	2.239	SF
Voni Fed Com #244H - Wellbore #1 - BLM Plan #1	11,173.3	11,171.5	86.9	8.0	1.102	Level 2, CC, ES, SF

Offset Design												Offset Site Error:		0.0 usft
Voni - Voni Fed Com #024H - Wellbore #1 - BLM Plan #1												Offset Well Error:		0.0 usft
Survey Program: 0-MWD														
Reference		Offset		Semi Major Axis			Distance					Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)		Separation Factor	
0.0	0.0	3.0	3.0	0.0	0.0	-98.15	-31.5	-219.9	222.1					
100.0	100.0	103.0	103.0	0.1	0.1	-98.15	-31.5	-219.9	222.1	221.8	0.27	831.701		
200.0	200.0	203.0	203.0	0.5	0.5	-98.15	-31.5	-219.9	222.1	221.1	0.98	225.726		
300.0	300.0	303.0	303.0	0.8	0.9	-98.15	-31.5	-219.9	222.1	220.4	1.70	130.583		
400.0	400.0	403.0	403.0	1.2	1.2	-98.15	-31.5	-219.9	222.1	219.7	2.42	91.863		
500.0	500.0	503.1	503.1	1.6	1.6	-98.15	-31.5	-219.9	222.1	219.0	3.14	70.848		
600.0	600.0	607.1	607.1	1.9	1.9	-142.19	-31.1	-218.9	221.9	218.0	3.86	57.489		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #024H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
700.0	700.0	711.0	711.0	2.3	2.3	-142.48	-30.2	-216.2	221.2	216.6	4.58	48.303		
800.0	799.9	814.9	814.8	2.6	2.7	-142.97	-28.6	-211.7	220.2	214.9	5.30	41.517		
900.0	899.7	918.8	918.4	3.0	3.0	-143.65	-26.3	-205.5	218.8	212.7	6.03	36.287		
1,000.0	999.4	1,022.6	1,021.9	3.4	3.4	-144.55	-23.5	-197.4	217.0	210.3	6.76	32.123		
1,100.0	1,098.9	1,126.4	1,125.1	3.7	3.8	-145.67	-20.0	-187.7	215.0	207.5	7.48	28.727		
1,200.0	1,198.3	1,230.1	1,228.1	4.1	4.2	-147.01	-15.9	-176.1	212.7	204.5	8.21	25.892		
1,300.0	1,297.4	1,332.5	1,329.5	4.5	4.6	-148.57	-11.2	-163.1	210.3	201.3	8.94	23.511		
1,400.0	1,396.4	1,432.3	1,428.4	4.9	5.0	-150.23	-6.6	-150.0	208.3	198.7	9.67	21.541		
1,500.0	1,495.5	1,532.0	1,527.2	5.3	5.4	-151.92	-1.9	-136.9	206.6	196.2	10.40	19.860		
1,600.0	1,594.5	1,631.8	1,626.0	5.7	5.8	-153.63	2.7	-123.8	205.0	193.9	11.14	18.413		
1,700.0	1,693.5	1,731.6	1,724.8	6.1	6.2	-155.37	7.4	-110.8	203.7	191.8	11.87	17.159		
1,800.0	1,792.5	1,831.4	1,823.7	6.5	6.6	-157.13	12.1	-97.7	202.5	189.9	12.61	16.064		
1,900.0	1,891.6	1,931.2	1,922.5	6.9	7.0	-158.91	16.7	-84.6	201.5	188.2	13.34	15.103		
2,000.0	1,990.6	2,031.0	2,021.3	7.3	7.4	-160.70	21.4	-71.5	200.7	186.6	14.08	14.256		
2,100.0	2,089.6	2,130.8	2,120.2	7.7	7.8	-162.51	26.1	-58.4	200.1	185.3	14.82	13.504		
2,200.0	2,188.6	2,230.6	2,219.0	8.1	8.2	-164.33	30.7	-45.3	199.8	184.2	15.56	12.836		
2,300.0	2,287.7	2,330.4	2,317.8	8.5	8.7	-166.15	35.4	-32.3	199.6	183.3	16.31	12.239		
2,341.6	2,328.9	2,372.0	2,359.0	8.7	8.8	-166.91	37.3	-26.8	199.5	182.9	16.62	12.009		
2,400.0	2,386.7	2,430.2	2,416.6	8.9	9.1	-167.97	40.0	-19.2	199.6	182.5	17.05	11.704		
2,500.0	2,485.7	2,530.0	2,515.5	9.3	9.5	-169.79	44.7	-6.1	199.8	182.0	17.80	11.223		
2,600.0	2,584.8	2,629.8	2,614.3	9.8	9.9	-171.61	49.4	7.0	200.2	181.7	18.56	10.790		
2,700.0	2,683.8	2,729.6	2,713.1	10.2	10.3	-173.41	54.0	20.1	200.8	181.5	19.31	10.400		
2,739.3	2,722.7	2,768.8	2,751.9	10.3	10.5	-174.12	55.9	25.2	201.1	181.5	19.61	10.257		
2,800.0	2,782.9	2,829.4	2,811.9	10.6	10.7	-175.19	58.7	33.2	201.2	181.1	20.07	10.023		
2,900.0	2,882.3	2,929.2	2,910.8	11.0	11.1	-176.93	63.4	46.2	199.3	178.5	20.83	9.567		
3,000.0	2,981.9	3,028.9	3,009.5	11.4	11.6	-178.68	68.0	59.3	195.0	173.4	21.60	9.030		
3,100.0	3,081.7	3,128.5	3,108.1	11.7	12.0	179.49	72.7	72.4	188.3	165.9	22.36	8.421		
3,200.0	3,181.7	3,227.9	3,206.5	12.1	12.4	177.48	77.3	85.4	179.1	156.0	23.12	7.747		
3,272.6	3,254.3	3,300.1	3,277.8	12.3	12.7	-140.20	80.7	94.8	171.0	147.3	23.68	7.222		
3,300.0	3,281.7	3,327.0	3,304.7	12.4	12.8	-140.86	81.9	98.4	167.8	143.9	23.89	7.021		
3,400.0	3,381.7	3,426.0	3,402.7	12.7	13.2	-143.50	86.6	111.4	156.0	131.3	24.67	6.322		
3,500.0	3,481.7	3,525.1	3,500.8	13.1	13.6	-146.57	91.2	124.4	144.6	119.1	25.47	5.677		
3,600.0	3,581.7	3,624.1	3,598.9	13.4	14.0	-150.14	95.8	137.3	133.7	107.4	26.29	5.085		
3,700.0	3,681.7	3,723.1	3,696.9	13.7	14.5	-154.32	100.4	150.3	123.4	96.3	27.14	4.547		
3,800.0	3,781.7	3,822.1	3,795.0	14.1	14.9	-159.23	105.1	163.3	113.9	85.9	28.02	4.065		
3,900.0	3,881.7	3,921.2	3,893.1	14.4	15.3	-164.96	109.7	176.3	105.4	76.4	28.93	3.642		
4,000.0	3,981.7	4,020.2	3,991.1	14.7	15.7	-171.62	114.3	189.3	98.1	68.2	29.86	3.284		
4,100.0	4,081.7	4,119.2	4,089.2	15.1	16.1	-179.20	118.9	202.2	92.3	61.5	30.80	2.996		
4,200.0	4,181.7	4,218.2	4,187.2	15.4	16.5	172.39	123.6	215.2	88.4	56.6	31.72	2.785		
4,300.0	4,281.7	4,317.3	4,285.3	15.8	16.9	163.42	128.2	228.2	86.5	53.9	32.59	2.655		
4,333.2	4,314.9	4,350.2	4,317.9	15.9	17.1	160.39	129.7	232.5	86.4	53.5	32.86	2.630 CC		
4,400.0	4,381.7	4,416.3	4,383.4	16.1	17.3	154.31	132.8	241.2	86.9	53.5	33.36	2.605 ES, SF		
4,500.0	4,481.7	4,515.3	4,481.4	16.4	17.8	145.49	137.4	254.2	89.5	55.4	34.04	2.628		
4,600.0	4,581.7	4,614.3	4,579.5	16.8	18.2	137.34	142.1	267.2	94.0	59.4	34.65	2.714		
4,700.0	4,681.7	4,713.4	4,677.6	17.1	18.6	130.06	146.7	280.1	100.3	65.1	35.21	2.850		
4,800.0	4,781.7	4,812.4	4,775.6	17.5	19.0	123.72	151.3	293.1	108.1	72.3	35.75	3.024		
4,900.0	4,881.7	4,911.4	4,873.7	17.8	19.4	118.27	155.9	306.1	117.0	80.7	36.30	3.223		
5,000.0	4,981.7	5,010.5	4,971.7	18.2	19.8	113.62	160.6	319.1	126.8	89.9	36.86	3.440		
5,100.0	5,081.7	5,109.5	5,069.8	18.5	20.3	109.66	165.2	332.1	137.3	99.9	37.44	3.667		
5,200.0	5,181.7	5,208.5	5,167.9	18.8	20.7	106.26	169.8	345.1	148.4	110.3	38.04	3.900		
5,300.0	5,281.7	5,307.5	5,265.9	19.2	21.1	103.35	174.5	358.0	159.9	121.2	38.66	4.136		
5,400.0	5,381.7	5,406.6	5,364.0	19.5	21.5	100.83	179.1	371.0	171.8	132.5	39.29	4.371		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #024H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,500.0	5,481.7	5,505.6	5,462.1	19.9	21.9	98.64	183.7	384.0	183.9	144.0	39.94	4.605		
5,600.0	5,581.7	5,604.6	5,560.1	20.2	22.3	96.72	188.3	397.0	196.3	155.7	40.60	4.836		
5,700.0	5,681.7	5,703.6	5,658.2	20.6	22.7	95.03	193.0	410.0	208.9	167.7	41.26	5.063		
5,800.0	5,781.7	5,802.7	5,756.3	20.9	23.2	93.53	197.6	422.9	221.7	179.7	41.93	5.286		
5,900.0	5,881.7	5,903.7	5,856.3	21.3	23.6	92.18	202.2	436.0	234.4	191.8	42.64	5.497		
6,000.0	5,981.7	6,009.2	5,961.1	21.6	24.0	91.11	206.4	447.6	245.3	201.9	43.39	5.653		
6,100.0	6,081.7	6,115.3	6,066.8	22.0	24.4	90.36	209.5	456.5	253.6	209.5	44.12	5.748		
6,200.0	6,181.7	6,221.9	6,173.2	22.3	24.8	89.87	211.7	462.6	259.3	214.5	44.82	5.786		
6,300.0	6,281.7	6,328.7	6,279.9	22.7	25.2	89.61	212.9	465.9	262.5	217.0	45.49	5.769		
6,400.0	6,381.7	6,433.5	6,384.7	23.0	25.5	89.56	213.1	466.6	263.1	216.9	46.15	5.700		
6,500.0	6,481.7	6,533.5	6,484.7	23.4	25.8	89.56	213.1	466.6	263.1	216.2	46.84	5.617		
6,600.0	6,581.7	6,633.5	6,584.7	23.7	26.1	89.56	213.1	466.6	263.1	215.5	47.53	5.535		
6,700.0	6,681.7	6,733.5	6,684.7	24.1	26.4	89.56	213.1	466.6	263.1	214.9	48.22	5.456		
6,800.0	6,781.7	6,833.5	6,784.7	24.4	26.7	89.56	213.1	466.6	263.1	214.2	48.91	5.379		
6,900.0	6,881.7	6,933.5	6,884.7	24.8	27.1	89.56	213.1	466.6	263.1	213.5	49.60	5.304		
7,000.0	6,981.7	7,033.5	6,984.7	25.1	27.4	89.56	213.1	466.6	263.1	212.8	50.29	5.231		
7,100.0	7,081.7	7,133.5	7,084.7	25.5	27.7	89.57	213.1	466.6	263.1	212.1	50.98	5.161		
7,127.8	7,109.5	7,161.3	7,112.5	25.6	27.8	89.80	212.0	466.6	263.1	211.9	51.17	5.141		
7,200.0	7,181.7	7,232.4	7,183.0	25.8	28.0	91.71	203.2	466.6	263.2	211.5	51.71	5.091		
7,300.0	7,281.7	7,325.4	7,272.6	26.2	28.2	97.02	178.7	466.7	265.4	212.9	52.52	5.054		
7,400.0	7,381.7	7,408.6	7,348.5	26.5	28.4	104.15	144.7	466.8	273.9	220.8	53.11	5.158		
7,500.0	7,481.7	7,480.6	7,409.6	26.9	28.5	111.62	106.7	467.0	293.1	240.3	52.86	5.545		
7,600.0	7,581.7	7,541.8	7,457.4	27.2	28.6	118.39	68.7	467.1	325.5	274.1	51.39	6.335		
7,700.0	7,681.7	7,593.2	7,494.2	27.6	28.6	124.06	32.8	467.2	370.9	322.0	48.93	7.580		
7,800.0	7,781.7	7,636.4	7,522.6	28.0	28.7	128.63	0.3	467.3	427.4	381.4	46.03	9.286		
7,900.0	7,881.7	7,672.8	7,544.6	28.3	28.7	132.27	-28.7	467.4	492.8	449.6	43.11	11.430		
8,000.0	7,981.7	7,700.0	7,559.8	28.7	28.8	134.83	-51.3	467.5	564.9	524.6	40.24	14.037		
8,100.0	8,081.7	7,730.0	7,575.3	29.0	28.8	137.50	-77.0	467.6	642.0	604.0	38.07	16.863		
8,200.0	8,181.7	7,750.0	7,584.9	29.4	28.8	139.17	-94.6	467.7	723.2	687.3	35.89	20.151		
8,300.0	8,281.7	7,772.4	7,594.8	29.7	28.8	140.95	-114.6	467.7	807.3	773.1	34.26	23.565		
8,400.0	8,381.7	7,800.0	7,606.0	30.1	28.9	143.02	-139.8	467.8	894.0	860.9	33.16	26.959		
8,500.0	8,481.7	7,800.0	7,606.0	30.4	28.9	143.02	-139.8	467.8	982.3	951.0	31.34	31.341		
8,600.0	8,581.7	7,818.1	7,612.7	30.8	28.9	144.29	-156.6	467.9	1,072.3	1,041.8	30.44	35.224		
8,700.0	8,681.7	7,830.0	7,616.8	31.1	28.9	145.09	-167.8	467.9	1,163.5	1,134.0	29.54	39.386		
8,800.0	8,781.7	7,850.0	7,623.2	31.5	28.9	146.39	-186.8	468.0	1,255.9	1,226.8	29.04	43.248		
8,900.0	8,881.7	7,850.0	7,623.2	31.8	28.9	146.39	-186.8	468.0	1,348.9	1,320.8	28.14	47.941		
9,000.0	8,981.7	7,850.0	7,623.2	32.2	28.9	146.39	-186.8	468.0	1,442.9	1,415.5	27.40	52.662		
9,100.0	9,081.7	7,866.8	7,628.0	32.6	29.0	147.42	-202.9	468.0	1,537.2	1,510.1	27.17	56.582		
9,200.0	9,181.7	7,874.0	7,630.0	32.9	29.0	147.85	-209.8	468.1	1,632.2	1,605.4	26.80	60.897		
9,300.0	9,281.7	7,880.6	7,631.7	33.3	29.0	148.23	-216.1	468.1	1,727.7	1,701.2	26.51	65.180		
9,400.0	9,381.7	7,900.0	7,636.2	33.6	29.0	149.33	-235.0	468.2	1,823.8	1,797.3	26.52	68.782		
9,500.0	9,481.7	7,900.0	7,636.2	34.0	29.0	149.33	-235.0	468.2	1,919.9	1,893.6	26.22	73.225		
9,600.0	9,581.7	7,900.0	7,636.2	34.3	29.0	149.33	-235.0	468.2	2,016.3	1,990.3	25.99	77.589		
9,700.0	9,681.7	7,900.0	7,636.2	34.7	29.0	149.33	-235.0	468.2	2,113.1	2,087.3	25.81	81.864		
9,800.0	9,781.7	7,900.0	7,636.2	35.0	29.0	149.33	-235.0	468.2	2,210.2	2,184.5	25.69	86.043		
9,900.0	9,881.7	7,900.0	7,636.2	35.4	29.0	149.33	-235.0	468.2	2,307.5	2,281.9	25.60	90.121		
10,000.0	9,981.7	7,900.0	7,636.2	35.7	29.0	149.33	-235.0	468.2	2,405.1	2,379.5	25.56	94.094		
10,100.0	10,081.7	7,900.0	7,636.2	36.1	29.0	149.33	-235.0	468.2	2,502.8	2,477.3	25.55	97.960		
10,200.0	10,181.7	7,921.5	7,640.5	36.5	29.1	150.47	-256.1	468.2	2,600.2	2,574.4	25.83	100.680		
10,300.0	10,281.7	7,924.7	7,641.1	36.8	29.1	150.63	-259.3	468.2	2,698.1	2,672.2	25.90	104.189		
10,400.0	10,381.7	7,927.7	7,641.6	37.2	29.1	150.78	-262.2	468.3	2,796.2	2,770.2	25.99	107.603		
10,500.0	10,481.7	7,950.0	7,645.0	37.5	29.1	151.87	-284.3	468.3	2,894.7	2,868.4	26.30	110.051		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #024H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,600.0	10,581.7	7,950.0	7,645.0	37.9	29.1	151.87	-284.3	468.3	2,992.9	2,966.5	26.39	113.406		
10,700.0	10,681.7	7,950.0	7,645.0	38.2	29.1	151.87	-284.3	468.3	3,091.2	3,064.7	26.50	116.659		
10,800.0	10,781.7	7,950.0	7,645.0	38.6	29.1	151.87	-284.3	468.3	3,189.6	3,162.9	26.62	119.812		
10,831.3	10,813.0	7,950.0	7,645.0	38.7	29.1	151.87	-284.3	468.3	3,220.4	3,193.7	26.66	120.779		
10,850.0	10,831.7	7,950.0	7,645.0	38.8	29.1	-28.23	-284.3	468.3	3,238.7	3,212.1	26.69	121.361		
10,900.0	10,881.5	7,950.0	7,645.0	38.9	29.1	-19.91	-284.3	468.3	3,287.3	3,260.6	26.73	122.960		
10,950.0	10,930.8	7,950.0	7,645.0	39.1	29.1	-15.31	-284.3	468.3	3,334.8	3,308.0	26.76	124.606		
11,000.0	10,979.2	7,950.0	7,645.0	39.2	29.1	-12.45	-284.3	468.3	3,380.9	3,354.1	26.77	126.276		
11,050.0	11,026.4	7,950.0	7,645.0	39.3	29.1	-10.51	-284.3	468.3	3,425.3	3,398.6	26.77	127.952		
11,100.0	11,071.9	7,950.0	7,645.0	39.5	29.1	-9.14	-284.3	468.3	3,467.8	3,441.1	26.76	129.611		
11,150.0	11,115.5	7,950.0	7,645.0	39.6	29.1	-8.11	-284.3	468.3	3,508.2	3,481.4	26.73	131.233		
11,200.0	11,156.7	7,950.0	7,645.0	39.7	29.1	-7.33	-284.3	468.3	3,546.1	3,519.4	26.70	132.793		
11,250.0	11,195.4	7,950.0	7,645.0	39.8	29.1	-6.72	-284.3	468.3	3,581.4	3,554.7	26.67	134.264		
11,300.0	11,231.1	7,972.0	7,647.4	39.9	29.2	-6.25	-306.1	468.4	3,613.4	3,586.6	26.80	134.830		
11,350.0	11,263.7	7,977.5	7,647.9	39.9	29.2	-5.87	-311.6	468.4	3,642.6	3,615.8	26.81	135.884		
11,400.0	11,292.8	8,000.0	7,649.4	40.0	29.2	-5.58	-334.0	468.5	3,669.0	3,642.0	26.93	136.253		
11,450.0	11,318.3	8,000.0	7,649.4	40.1	29.2	-5.34	-334.0	468.5	3,691.5	3,664.6	26.91	137.171		
11,500.0	11,339.9	8,000.0	7,649.4	40.2	29.2	-5.15	-334.0	468.5	3,710.7	3,683.8	26.91	137.867		
11,550.0	11,357.5	8,000.0	7,649.4	40.3	29.2	-5.01	-334.0	468.5	3,726.3	3,699.4	26.94	138.317		
11,600.0	11,371.0	8,000.0	7,649.4	40.4	29.2	-4.90	-334.0	468.5	3,738.5	3,711.5	26.99	138.499		
11,650.0	11,380.2	8,014.9	7,649.9	40.5	29.3	-4.84	-348.9	468.6	3,746.7	3,719.6	27.14	138.075		
11,700.0	11,385.1	8,025.8	7,650.0	40.7	29.3	-4.82	-359.8	468.6	3,751.4	3,724.1	27.28	137.510		
11,731.3	11,386.0	8,025.8	7,650.0	40.7	29.3	-4.81	-359.8	468.6	3,752.3	3,725.0	27.36	137.154		
11,800.0	11,386.0	8,091.4	7,650.0	40.9	29.6	-4.91	-425.4	469.1	3,752.8	3,725.0	27.79	135.035		
11,900.0	11,386.0	8,191.2	7,650.0	41.3	30.0	-5.00	-525.2	469.9	3,753.3	3,724.8	28.48	131.767		
12,009.9	11,386.0	8,301.0	7,650.0	41.7	30.6	-5.04	-635.1	470.8	3,753.5	3,724.2	29.30	128.097		
12,100.0	11,386.0	8,408.8	7,650.0	42.1	31.3	-5.04	-725.2	471.6	3,753.5	3,723.4	30.12	124.629		
12,200.0	11,386.0	8,508.8	7,650.0	42.6	32.0	-5.04	-825.2	472.4	3,753.5	3,722.5	30.98	121.166		
12,300.0	11,386.0	8,608.8	7,650.0	43.2	32.8	-5.04	-925.2	473.2	3,753.5	3,721.6	31.89	117.692		
12,400.0	11,386.0	8,708.8	7,650.0	43.8	33.6	-5.04	-1,025.2	474.1	3,753.5	3,720.6	32.86	114.240		
12,500.0	11,386.0	8,808.8	7,650.0	44.5	34.5	-5.04	-1,125.2	474.9	3,753.5	3,719.6	33.86	110.838		
12,600.0	11,386.0	8,908.8	7,650.0	45.2	35.5	-5.04	-1,225.2	475.7	3,753.5	3,718.6	34.91	107.507		
12,700.0	11,386.0	9,008.8	7,650.0	46.0	36.5	-5.04	-1,325.2	476.5	3,753.5	3,717.5	36.00	104.262		
12,800.0	11,386.0	9,108.8	7,650.0	46.8	37.5	-5.04	-1,425.2	477.4	3,753.5	3,716.4	37.12	101.115		
12,900.0	11,386.0	9,208.8	7,650.0	47.7	38.6	-5.04	-1,525.2	478.2	3,753.5	3,715.2	38.27	98.073		
13,000.0	11,386.0	9,308.8	7,650.0	48.6	39.7	-5.04	-1,625.2	479.0	3,753.5	3,714.0	39.45	95.139		
13,100.0	11,386.0	9,408.8	7,650.0	49.5	40.9	-5.04	-1,725.2	479.8	3,753.5	3,712.8	40.66	92.317		
13,200.0	11,386.0	9,508.8	7,650.0	50.5	42.1	-5.04	-1,825.2	480.7	3,753.5	3,711.6	41.89	89.606		
13,300.0	11,386.0	9,608.8	7,650.0	51.5	43.3	-5.04	-1,925.2	481.5	3,753.5	3,710.4	43.14	87.005		
13,400.0	11,386.0	9,708.8	7,650.0	52.6	44.6	-5.04	-2,025.1	482.3	3,753.5	3,709.1	44.41	84.512		
13,500.0	11,386.0	9,808.8	7,650.0	53.6	45.9	-5.04	-2,125.1	483.1	3,753.5	3,707.8	45.71	82.124		
13,600.0	11,386.0	9,908.8	7,650.0	54.7	47.2	-5.04	-2,225.1	484.0	3,753.5	3,706.5	47.01	79.839		
13,700.0	11,386.0	10,008.8	7,650.0	55.9	48.5	-5.04	-2,325.1	484.8	3,753.5	3,705.2	48.34	77.651		
13,800.0	11,386.0	10,108.8	7,650.0	57.0	49.8	-5.04	-2,425.1	485.6	3,753.5	3,703.8	49.68	75.558		
13,900.0	11,386.0	10,208.8	7,650.0	58.2	51.2	-5.04	-2,525.1	486.4	3,753.5	3,702.5	51.03	73.554		
14,000.0	11,386.0	10,308.8	7,650.0	59.4	52.6	-5.04	-2,625.1	487.3	3,753.5	3,701.1	52.40	71.637		
14,100.0	11,386.0	10,408.8	7,650.0	60.6	54.0	-5.04	-2,725.1	488.1	3,753.5	3,699.7	53.77	69.803		
14,200.0	11,386.0	10,508.8	7,650.0	61.9	55.4	-5.04	-2,825.1	488.9	3,753.5	3,698.3	55.16	68.046		
14,300.0	11,386.0	10,608.8	7,650.0	63.1	56.8	-5.04	-2,925.1	489.7	3,753.5	3,696.9	56.56	66.363		
14,400.0	11,386.0	10,708.8	7,650.0	64.4	58.2	-5.04	-3,025.1	490.6	3,753.5	3,695.5	57.97	64.752		
14,500.0	11,386.0	10,808.8	7,650.0	65.7	59.7	-5.04	-3,125.1	491.4	3,753.5	3,694.1	59.38	63.207		
14,600.0	11,386.0	10,908.8	7,650.0	67.0	61.1	-5.04	-3,225.1	492.2	3,753.5	3,692.7	60.81	61.726		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #024H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,700.0	11,386.0	11,008.8	7,650.0	68.4	62.6	-5.04	-3,325.1	493.0	3,753.5	3,691.3	62.24	60.305		
14,800.0	11,386.0	11,108.8	7,650.0	69.7	64.1	-5.04	-3,425.1	493.9	3,753.5	3,689.8	63.68	58.941		
14,900.0	11,386.0	11,208.8	7,650.0	71.1	65.6	-5.04	-3,525.1	494.7	3,753.5	3,688.4	65.13	57.632		
15,000.0	11,386.0	11,308.8	7,650.0	72.4	67.0	-5.04	-3,625.1	495.5	3,753.5	3,686.9	66.58	56.374		
15,100.0	11,386.0	11,408.8	7,650.0	73.8	68.5	-5.04	-3,725.1	496.3	3,753.5	3,685.5	68.04	55.166		
15,200.0	11,386.0	11,508.8	7,650.0	75.2	70.1	-5.04	-3,825.1	497.2	3,753.5	3,684.0	69.51	54.003		
15,300.0	11,386.0	11,608.8	7,650.0	76.6	71.6	-5.04	-3,925.1	498.0	3,753.5	3,682.5	70.97	52.885		
15,400.0	11,386.0	11,691.2	7,650.0	78.0	72.8	-5.04	-4,025.1	498.8	3,753.5	3,681.2	72.31	51.906		
15,500.0	11,386.0	11,808.8	7,650.0	79.4	74.6	-5.04	-4,125.1	499.6	3,753.5	3,679.6	73.93	50.772		
15,600.0	11,386.0	11,908.8	7,650.0	80.9	76.1	-5.04	-4,225.1	500.5	3,753.5	3,678.1	75.41	49.773		
15,700.0	11,386.0	11,991.2	7,650.0	82.3	77.4	-5.04	-4,325.1	501.3	3,753.5	3,676.7	76.76	48.896		
15,800.0	11,386.0	12,108.8	7,650.0	83.7	79.2	-5.04	-4,425.1	502.1	3,753.5	3,675.1	78.39	47.881		
15,900.0	11,386.0	12,208.8	7,650.0	85.2	80.7	-5.04	-4,525.1	502.9	3,753.5	3,673.6	79.89	46.984		
16,000.0	11,386.0	12,308.8	7,650.0	86.7	82.3	-5.04	-4,625.1	503.8	3,753.5	3,672.1	81.39	46.119		
16,100.0	11,386.0	12,408.8	7,650.0	88.1	83.8	-5.04	-4,725.1	504.6	3,753.5	3,670.6	82.89	45.283		
16,200.0	11,386.0	12,508.8	7,650.0	89.6	85.4	-5.04	-4,825.1	505.4	3,753.5	3,669.1	84.40	44.475		
16,300.0	11,386.0	12,608.8	7,650.0	91.1	87.0	-5.04	-4,925.0	506.2	3,753.5	3,667.6	85.90	43.694		
16,400.0	11,386.0	12,708.8	7,650.0	92.6	88.5	-5.04	-5,025.0	507.1	3,753.5	3,666.1	87.42	42.938		
16,500.0	11,386.0	12,808.8	7,650.0	94.0	90.1	-5.04	-5,125.0	507.9	3,753.5	3,664.6	88.93	42.207		
16,600.0	11,386.0	12,908.8	7,650.0	95.5	91.6	-5.04	-5,225.0	508.7	3,753.5	3,663.1	90.45	41.500		
16,700.0	11,386.0	13,008.8	7,650.0	97.0	93.2	-5.04	-5,325.0	509.5	3,753.5	3,661.5	91.97	40.814		
16,800.0	11,386.0	13,108.8	7,650.0	98.5	94.8	-5.04	-5,425.0	510.4	3,753.5	3,660.0	93.49	40.150		
16,900.0	11,386.0	13,208.8	7,650.0	100.1	96.4	-5.04	-5,525.0	511.2	3,753.5	3,658.5	95.01	39.506		
17,000.0	11,386.0	13,308.8	7,650.0	101.6	97.9	-5.04	-5,625.0	512.0	3,753.5	3,657.0	96.54	38.881		
17,100.0	11,386.0	13,408.8	7,650.0	103.1	99.5	-5.04	-5,725.0	512.9	3,753.5	3,655.4	98.07	38.276		
17,200.0	11,386.0	13,508.8	7,650.0	104.6	101.1	-5.04	-5,825.0	513.7	3,753.5	3,653.9	99.60	37.688		
17,300.0	11,386.0	13,608.8	7,650.0	106.1	102.7	-5.04	-5,925.0	514.5	3,753.5	3,652.4	101.13	37.117		
17,400.0	11,386.0	13,708.8	7,650.0	107.7	104.3	-5.04	-6,025.0	515.3	3,753.5	3,650.8	102.66	36.562		
17,500.0	11,386.0	13,808.8	7,650.0	109.2	105.9	-5.04	-6,125.0	516.2	3,753.5	3,649.3	104.20	36.024		
17,600.0	11,386.0	13,908.8	7,650.0	110.7	107.5	-5.04	-6,225.0	517.0	3,753.5	3,647.8	105.73	35.500		
17,700.0	11,386.0	14,008.8	7,650.0	112.3	109.1	-5.04	-6,325.0	517.8	3,753.5	3,646.2	107.27	34.991		
17,800.0	11,386.0	14,108.8	7,650.0	113.8	110.7	-5.04	-6,425.0	518.6	3,753.5	3,644.7	108.81	34.496		
17,900.0	11,386.0	14,208.8	7,650.0	115.4	112.3	-5.04	-6,525.0	519.5	3,753.5	3,643.2	110.35	34.014		
18,000.0	11,386.0	14,308.8	7,650.0	116.9	113.9	-5.04	-6,625.0	520.3	3,753.5	3,641.6	111.89	33.545		
18,100.0	11,386.0	14,408.8	7,650.0	118.5	115.5	-5.04	-6,725.0	521.1	3,753.5	3,640.1	113.44	33.089		
18,200.0	11,386.0	14,508.8	7,650.0	120.0	117.1	-5.04	-6,825.0	521.9	3,753.5	3,638.5	114.98	32.644		
18,300.0	11,386.0	14,608.8	7,650.0	121.6	118.7	-5.04	-6,925.0	522.8	3,753.5	3,637.0	116.53	32.211		
18,400.0	11,386.0	14,708.8	7,650.0	123.2	120.3	-5.04	-7,025.0	523.6	3,753.5	3,635.4	118.08	31.789		
18,500.0	11,386.0	14,808.8	7,650.0	124.7	121.9	-5.04	-7,125.0	524.4	3,753.5	3,633.9	119.63	31.377		
18,600.0	11,386.0	14,908.8	7,650.0	126.3	123.5	-5.04	-7,225.0	525.2	3,753.5	3,632.3	121.18	30.976		
18,700.0	11,386.0	15,008.8	7,650.0	127.9	125.1	-5.04	-7,325.0	526.1	3,753.5	3,630.8	122.73	30.584		
18,800.0	11,386.0	15,108.8	7,650.0	129.4	126.7	-5.04	-7,425.0	526.9	3,753.5	3,629.2	124.28	30.202		
18,900.0	11,386.0	15,208.8	7,650.0	131.0	128.3	-5.04	-7,525.0	527.7	3,753.5	3,627.7	125.83	29.830		
19,000.0	11,386.0	15,308.8	7,650.0	132.6	129.9	-5.04	-7,625.0	528.5	3,753.5	3,626.1	127.39	29.466		
19,100.0	11,386.0	15,408.8	7,650.0	134.1	131.5	-5.04	-7,725.0	529.4	3,753.5	3,624.6	128.94	29.111		
19,200.0	11,386.0	15,508.8	7,650.0	135.7	133.1	-5.04	-7,824.9	530.2	3,753.5	3,623.0	130.50	28.764		
19,300.0	11,386.0	15,608.8	7,650.0	137.3	134.8	-5.04	-7,924.9	531.0	3,753.5	3,621.5	132.05	28.425		
19,400.0	11,386.0	15,708.8	7,650.0	138.9	136.4	-5.04	-8,024.9	531.8	3,753.5	3,619.9	133.61	28.093		
19,500.0	11,386.0	15,808.8	7,650.0	140.5	138.0	-5.04	-8,124.9	532.7	3,753.5	3,618.4	135.17	27.770		
19,600.0	11,386.0	15,908.8	7,650.0	142.0	139.6	-5.04	-8,224.9	533.5	3,753.5	3,616.8	136.72	27.453		
19,700.0	11,386.0	16,008.8	7,650.0	143.6	141.2	-5.04	-8,324.9	534.3	3,753.5	3,615.2	138.28	27.144		
19,800.0	11,386.0	16,108.8	7,650.0	145.2	142.8	-5.04	-8,424.9	535.1	3,753.5	3,613.7	139.84	26.841		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #024H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,900.0	11,386.0	16,208.8	7,650.0	146.8	144.5	-5.04	-8,524.9	536.0	3,753.5	3,612.1	141.40	26.544		
20,000.0	11,386.0	16,308.8	7,650.0	148.4	146.1	-5.04	-8,624.9	536.8	3,753.5	3,610.6	142.97	26.255		
20,100.0	11,386.0	16,408.8	7,650.0	150.0	147.7	-5.04	-8,724.9	537.6	3,753.5	3,609.0	144.53	25.971		
20,200.0	11,386.0	16,508.8	7,650.0	151.6	149.3	-5.04	-8,824.9	538.4	3,753.5	3,607.4	146.09	25.693		
20,300.0	11,386.0	16,608.8	7,650.0	153.2	150.9	-5.04	-8,924.9	539.3	3,753.5	3,605.9	147.65	25.421		
20,400.0	11,386.0	16,708.8	7,650.0	154.8	152.6	-5.04	-9,024.9	540.1	3,753.5	3,604.3	149.22	25.155		
20,500.0	11,386.0	16,808.8	7,650.0	156.4	154.2	-5.04	-9,124.9	540.9	3,753.5	3,602.7	150.78	24.894		
20,600.0	11,386.0	16,908.8	7,650.0	158.0	155.8	-5.04	-9,224.9	541.7	3,753.5	3,601.2	152.35	24.638		
20,700.0	11,386.0	17,008.8	7,650.0	159.6	157.4	-5.04	-9,324.9	542.6	3,753.5	3,599.6	153.91	24.387		
20,800.0	11,386.0	17,108.8	7,650.0	161.2	159.1	-5.04	-9,424.9	543.4	3,753.5	3,598.0	155.48	24.142		
20,900.0	11,386.0	17,208.8	7,650.0	162.8	160.7	-5.04	-9,524.9	544.2	3,753.5	3,596.5	157.04	23.901		
21,000.0	11,386.0	17,308.8	7,650.0	164.4	162.3	-5.04	-9,624.9	545.0	3,753.5	3,594.9	158.61	23.665		
21,100.0	11,386.0	17,408.8	7,650.0	166.0	163.9	-5.04	-9,724.9	545.9	3,753.5	3,593.3	160.18	23.433		
21,200.0	11,386.0	17,508.8	7,650.0	167.6	165.6	-5.04	-9,824.9	546.7	3,753.5	3,591.8	161.75	23.206		
21,300.0	11,386.0	17,608.8	7,650.0	169.2	167.2	-5.04	-9,924.9	547.5	3,753.5	3,590.2	163.32	22.983		
21,400.0	11,386.0	17,708.8	7,650.0	170.8	168.8	-5.04	-10,024.9	548.3	3,753.5	3,588.6	164.88	22.765		
21,500.0	11,386.0	17,791.2	7,650.0	172.4	170.2	-5.04	-10,124.9	549.2	3,753.5	3,587.2	166.31	22.569		
21,600.0	11,386.0	17,908.8	7,650.0	174.0	172.1	-5.04	-10,224.9	550.0	3,753.5	3,585.5	168.02	22.339		
21,700.0	11,386.0	18,008.8	7,650.0	175.6	173.7	-5.04	-10,324.9	550.8	3,753.5	3,583.9	169.59	22.133		
21,800.0	11,386.0	18,091.2	7,650.0	177.2	175.0	-5.04	-10,424.9	551.7	3,753.5	3,582.5	171.02	21.948		
21,900.0	11,386.0	18,208.8	7,650.0	178.8	177.0	-5.04	-10,524.9	552.5	3,753.5	3,580.8	172.73	21.730		
22,000.0	11,386.0	18,308.8	7,650.0	180.4	178.6	-5.04	-10,624.9	553.3	3,753.5	3,579.2	174.30	21.534		
22,100.0	11,386.0	18,408.8	7,650.0	182.0	180.2	-5.04	-10,724.9	554.1	3,753.5	3,577.7	175.88	21.342		
22,200.0	11,386.0	18,508.8	7,650.0	183.7	181.9	-5.04	-10,824.8	555.0	3,753.5	3,576.1	177.45	21.153		
22,300.0	11,386.0	18,608.8	7,650.0	185.3	183.5	-5.04	-10,924.8	555.8	3,753.5	3,574.5	179.02	20.967		
22,400.0	11,386.0	18,708.8	7,650.0	186.9	185.1	-5.04	-11,024.8	556.6	3,753.5	3,572.9	180.59	20.785		
22,500.0	11,386.0	18,808.8	7,650.0	188.5	186.8	-5.04	-11,124.8	557.4	3,753.5	3,571.4	182.16	20.605		
22,600.0	11,386.0	18,908.8	7,650.0	190.1	188.4	-5.04	-11,224.8	558.3	3,753.5	3,569.8	183.74	20.429		
22,700.0	11,386.0	19,008.8	7,650.0	191.7	190.0	-5.04	-11,324.8	559.1	3,753.5	3,568.2	185.31	20.255		
22,800.0	11,386.0	19,108.8	7,650.0	193.3	191.7	-5.04	-11,424.8	559.9	3,753.5	3,566.6	186.88	20.085		
22,900.0	11,386.0	19,208.8	7,650.0	195.0	193.3	-5.04	-11,524.8	560.7	3,753.5	3,565.1	188.46	19.917		
23,000.0	11,386.0	19,308.8	7,650.0	196.6	194.9	-5.04	-11,624.8	561.6	3,753.5	3,563.5	190.03	19.752		
23,100.0	11,386.0	19,408.8	7,650.0	198.2	196.6	-5.04	-11,724.8	562.4	3,753.5	3,561.9	191.61	19.590		
23,200.0	11,386.0	19,508.8	7,650.0	199.8	198.2	-5.04	-11,824.8	563.2	3,753.5	3,560.3	193.18	19.430		
23,300.0	11,386.0	19,608.8	7,650.0	201.4	199.8	-5.04	-11,924.8	564.0	3,753.5	3,558.8	194.76	19.273		
23,400.0	11,386.0	19,708.8	7,650.0	203.0	201.5	-5.04	-12,024.8	564.9	3,753.5	3,557.2	196.33	19.118		
23,500.0	11,386.0	19,808.8	7,650.0	204.7	203.1	-5.04	-12,124.8	565.7	3,753.5	3,555.6	197.91	18.966		
23,600.0	11,386.0	19,908.8	7,650.0	206.3	204.7	-5.04	-12,224.8	566.5	3,753.5	3,554.0	199.48	18.816		
23,705.7	11,386.0	20,003.1	7,650.0	208.0	206.3	-5.04	-12,330.5	567.4	3,753.5	3,552.5	201.06	18.669		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #104H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	1.0	1.0	0.0	0.0	-90.43	-0.8	-110.0	110.0					
100.0	100.0	101.0	101.0	0.1	0.1	-90.43	-0.8	-110.0	110.0	109.7	0.26	423.079		
200.0	200.0	201.0	201.0	0.5	0.5	-90.43	-0.8	-110.0	110.0	109.0	0.98	112.563		
300.0	300.0	301.0	301.0	0.8	0.8	-90.43	-0.8	-110.0	110.0	108.3	1.69	64.917		
400.0	400.0	401.0	401.0	1.2	1.2	-90.43	-0.8	-110.0	110.0	107.5	2.41	45.611		
500.0	500.0	501.0	501.0	1.6	1.6	-90.43	-0.8	-110.0	110.0	106.8	3.13	35.156		
600.0	600.0	601.0	601.0	1.9	1.9	-134.70	-0.8	-110.0	110.6	106.7	3.84	28.777		
700.0	700.0	701.0	701.0	2.3	2.3	-135.63	-0.8	-110.0	112.4	107.9	4.56	24.678		
800.0	799.9	800.9	800.9	2.6	2.6	-137.12	-0.8	-110.0	115.6	110.3	5.27	21.931		
900.0	899.7	900.7	900.7	3.0	3.0	-139.07	-0.8	-110.0	120.1	114.1	5.99	20.067		
1,000.0	999.4	1,000.4	1,000.4	3.4	3.4	-141.37	-0.8	-110.0	126.2	119.5	6.70	18.820		
1,100.0	1,098.9	1,100.1	1,099.9	3.7	3.7	-143.88	-0.8	-110.0	133.8	126.4	7.42	18.024		
1,200.0	1,198.3	1,199.3	1,199.3	4.1	4.1	-146.50	-0.8	-110.0	143.1	135.0	8.14	17.576		
1,300.0	1,297.4	1,300.8	1,300.8	4.5	4.4	-149.03	-0.2	-109.3	153.4	144.5	8.87	17.297		
1,400.0	1,396.4	1,402.7	1,402.7	4.9	4.8	-151.18	1.6	-107.3	163.1	153.5	9.60	17.002		
1,500.0	1,495.5	1,505.0	1,504.9	5.3	5.2	-152.85	4.6	-103.9	171.4	161.1	10.32	16.606		
1,600.0	1,594.5	1,607.6	1,607.3	5.7	5.5	-154.15	8.9	-99.2	178.1	167.1	11.05	16.123		
1,700.0	1,693.5	1,710.4	1,709.8	6.1	5.9	-155.16	14.3	-93.0	183.3	171.5	11.78	15.562		
1,800.0	1,792.5	1,813.5	1,812.3	6.5	6.3	-155.92	21.1	-85.5	186.8	174.3	12.51	14.937		
1,900.0	1,891.6	1,916.6	1,914.8	6.9	6.6	-156.46	29.1	-76.6	188.6	175.4	13.23	14.255		
2,000.0	1,990.6	2,019.2	2,016.4	7.3	7.0	-156.82	38.2	-66.4	188.8	174.9	13.96	13.525		
2,100.0	2,089.6	2,119.2	2,115.5	7.7	7.4	-157.11	47.5	-56.1	188.5	173.8	14.69	12.826		
2,200.0	2,188.6	2,219.2	2,214.5	8.1	7.8	-157.40	56.8	-45.7	188.1	172.7	15.43	12.192		
2,300.0	2,287.7	2,319.2	2,313.5	8.5	8.2	-157.69	66.0	-35.3	187.8	171.6	16.16	11.615		
2,400.0	2,386.7	2,419.2	2,412.5	8.9	8.6	-157.98	75.3	-25.0	187.4	170.5	16.90	11.088		
2,500.0	2,485.7	2,519.2	2,511.5	9.3	9.0	-158.27	84.6	-14.6	187.1	169.4	17.64	10.605		
2,600.0	2,584.8	2,619.2	2,610.6	9.8	9.4	-158.56	93.9	-4.3	186.7	168.3	18.38	10.161		
2,700.0	2,683.8	2,719.2	2,709.6	10.2	9.8	-158.86	103.2	6.1	186.4	167.3	19.12	9.750		
2,739.3	2,722.7	2,758.5	2,748.5	10.3	9.9	-158.97	106.8	10.2	186.3	166.9	19.41	9.598		
2,800.0	2,782.9	2,819.2	2,808.6	10.6	10.2	-159.10	112.5	16.5	185.6	165.8	19.86	9.348		
2,900.0	2,882.3	2,919.1	2,907.6	11.0	10.6	-159.06	121.8	26.8	182.6	162.0	20.59	8.866		
3,000.0	2,981.9	3,019.0	3,006.5	11.4	11.0	-158.70	131.0	37.2	177.1	155.8	21.33	8.304		
3,100.0	3,081.7	3,118.6	3,105.1	11.7	11.4	-157.98	140.3	47.5	169.2	147.1	22.06	7.670		
3,200.0	3,181.7	3,218.0	3,203.6	12.1	11.8	-156.82	149.5	57.8	158.9	136.1	22.80	6.972		
3,272.6	3,254.3	3,309.9	3,274.9	12.3	12.1	-111.66	156.2	65.3	150.0	126.6	23.40	6.411		
3,300.0	3,281.7	3,317.2	3,301.8	12.4	12.2	-111.14	158.7	68.1	146.5	122.9	23.53	6.225		
3,400.0	3,381.7	3,416.2	3,399.8	12.7	12.6	-109.03	167.9	78.3	133.5	109.3	24.27	5.502		
3,500.0	3,481.7	3,515.2	3,497.9	13.1	13.0	-106.47	177.1	88.6	120.8	95.8	25.02	4.829		
3,600.0	3,581.7	3,614.2	3,595.9	13.4	13.4	-103.32	186.3	98.9	108.4	82.6	25.78	4.203		
3,700.0	3,681.7	3,711.2	3,692.1	13.7	13.8	-99.85	194.5	108.0	97.4	70.8	26.58	3.665		
3,800.0	3,781.7	3,808.7	3,789.1	14.1	14.1	-96.47	201.1	115.4	89.0	61.6	27.36	3.252		
3,900.0	3,881.7	3,906.6	3,886.8	14.4	14.5	-93.50	206.1	120.9	82.9	54.8	28.12	2.948		
4,000.0	3,981.7	4,004.9	3,984.9	14.7	14.9	-91.28	209.4	124.6	79.0	50.2	28.86	2.738		
4,100.0	4,081.7	4,103.4	4,083.3	15.1	15.2	-90.11	211.0	126.4	77.2	47.6	29.55	2.611		
4,160.3	4,141.9	4,163.0	4,142.9	15.3	15.4	-89.99	211.1	126.5	77.0	47.0	29.96	2.570		
4,200.0	4,181.7	4,202.7	4,182.7	15.4	15.5	-89.99	211.1	126.5	77.0	46.8	30.23	2.547		
4,300.0	4,281.7	4,302.7	4,282.7	15.8	15.9	-89.99	211.1	126.5	77.0	46.1	30.92	2.490		
4,400.0	4,381.7	4,402.7	4,382.7	16.1	16.2	-89.99	211.1	126.5	77.0	45.4	31.61	2.435		
4,500.0	4,481.7	4,502.7	4,482.7	16.4	16.6	-89.99	211.1	126.5	77.0	44.7	32.30	2.383		
4,600.0	4,581.7	4,602.7	4,582.7	16.8	16.9	-89.99	211.1	126.5	77.0	44.0	33.00	2.333		
4,700.0	4,681.7	4,702.7	4,682.7	17.1	17.2	-89.99	211.1	126.5	77.0	43.3	33.69	2.285		
4,800.0	4,781.7	4,802.7	4,782.7	17.5	17.6	-89.99	211.1	126.5	77.0	42.6	34.38	2.239		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #104H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
4,900.0	4,881.7	4,902.7	4,882.7	17.8	17.9	-89.99	211.1	126.5	77.0	41.9	35.08	2.195		
5,000.0	4,981.7	5,002.7	4,982.7	18.2	18.3	-89.99	211.1	126.5	77.0	41.2	35.78	2.152		
5,100.0	5,081.7	5,102.7	5,082.7	18.5	18.6	-89.99	211.1	126.5	77.0	40.5	36.47	2.111		
5,200.0	5,181.7	5,202.7	5,182.7	18.8	19.0	-89.99	211.1	126.5	77.0	39.8	37.17	2.071		
5,300.0	5,281.7	5,302.7	5,282.7	19.2	19.3	-89.99	211.1	126.5	77.0	39.1	37.87	2.033		
5,400.0	5,381.7	5,402.7	5,382.7	19.5	19.6	-89.99	211.1	126.5	77.0	38.4	38.57	1.996		
5,500.0	5,481.7	5,502.7	5,482.7	19.9	20.0	-89.99	211.1	126.5	77.0	37.7	39.27	1.960		
5,600.0	5,581.7	5,602.7	5,582.7	20.2	20.3	-89.99	211.1	126.5	77.0	37.0	39.97	1.926		
5,700.0	5,681.7	5,702.7	5,682.7	20.6	20.7	-89.99	211.1	126.5	77.0	36.3	40.67	1.893		
5,800.0	5,781.7	5,802.7	5,782.7	20.9	21.0	-89.99	211.1	126.5	77.0	35.6	41.37	1.861		
5,900.0	5,881.7	5,902.7	5,882.7	21.3	21.4	-89.99	211.1	126.5	77.0	34.9	42.07	1.830		
6,000.0	5,981.7	6,002.7	5,982.7	21.6	21.7	-89.99	211.1	126.5	77.0	34.2	42.78	1.800		
6,100.0	6,081.7	6,102.7	6,082.7	22.0	22.1	-89.99	211.1	126.5	77.0	33.5	43.48	1.771		
6,200.0	6,181.7	6,202.7	6,182.7	22.3	22.4	-89.99	211.1	126.5	77.0	32.8	44.18	1.742		
6,300.0	6,281.7	6,302.7	6,282.7	22.7	22.8	-89.99	211.1	126.5	77.0	32.1	44.89	1.715		
6,400.0	6,381.7	6,402.7	6,382.7	23.0	23.1	-89.99	211.1	126.5	77.0	31.4	45.59	1.689		
6,500.0	6,481.7	6,502.7	6,482.7	23.4	23.5	-89.99	211.1	126.5	77.0	30.7	46.30	1.663		
6,600.0	6,581.7	6,602.7	6,582.7	23.7	23.8	-89.99	211.1	126.5	77.0	30.0	47.00	1.638		
6,700.0	6,681.7	6,702.7	6,682.7	24.1	24.2	-89.99	211.1	126.5	77.0	29.3	47.71	1.614		
6,800.0	6,781.7	6,802.7	6,782.7	24.4	24.5	-89.99	211.1	126.5	77.0	28.6	48.41	1.590		
6,900.0	6,881.7	6,902.7	6,882.7	24.8	24.9	-89.99	211.1	126.5	77.0	27.9	49.12	1.567		
7,000.0	6,981.7	7,002.7	6,982.7	25.1	25.2	-89.99	211.1	126.5	77.0	27.2	49.83	1.545		
7,100.0	7,081.7	7,102.7	7,082.7	25.5	25.6	-89.99	211.1	126.5	77.0	26.5	50.53	1.523		
7,200.0	7,181.7	7,202.7	7,182.7	25.8	25.9	-89.99	211.1	126.5	77.0	25.7	51.24	1.502		
7,300.0	7,281.7	7,302.7	7,282.7	26.2	26.3	-89.99	211.1	126.5	77.0	25.0	51.95	1.482 Level 3		
7,400.0	7,381.7	7,402.7	7,382.7	26.5	26.6	-89.99	211.1	126.5	77.0	24.3	52.66	1.462 Level 3		
7,500.0	7,481.7	7,502.7	7,482.7	26.9	27.0	-89.99	211.1	126.5	77.0	23.6	53.36	1.443 Level 3		
7,600.0	7,581.7	7,602.8	7,582.7	27.2	27.3	-90.82	210.0	126.6	77.0	22.9	54.05	1.424 Level 3		
7,609.2	7,590.9	7,612.0	7,591.9	27.3	27.3	-91.30	209.4	126.6	77.0	22.9	54.11	1.422 Level 3, CC, ES, SF		
7,700.0	7,681.7	7,700.6	7,679.4	27.6	27.6	-101.43	195.6	126.9	78.3	23.8	54.46	1.437 Level 3		
7,800.0	7,781.7	7,791.2	7,765.5	28.0	27.8	-119.66	167.8	127.5	89.1	35.4	53.74	1.658		
7,900.0	7,881.7	7,871.4	7,837.3	28.3	28.0	-136.39	132.2	128.3	118.1	67.1	50.99	2.316		
8,000.0	7,981.7	7,940.4	7,894.5	28.7	28.1	-147.65	93.8	129.2	164.5	117.2	47.32	3.477		
8,100.0	8,081.7	8,000.0	7,939.9	29.0	28.2	-154.77	55.2	130.1	223.8	179.8	43.96	5.091		
8,200.0	8,181.7	8,050.0	7,974.8	29.4	28.3	-159.25	19.4	130.9	292.0	251.1	40.92	7.136		
8,300.0	8,281.7	8,088.8	7,999.6	29.7	28.4	-162.00	-10.4	131.6	366.6	328.7	37.93	9.666		
8,400.0	8,381.7	8,123.5	8,020.0	30.1	28.4	-164.05	-38.4	132.2	446.0	410.3	35.65	12.510		
8,500.0	8,481.7	8,150.0	8,034.5	30.4	28.4	-165.39	-60.7	132.7	528.9	495.4	33.49	15.793		
8,600.0	8,581.7	8,178.3	8,048.7	30.8	28.5	-166.65	-85.0	133.3	614.6	582.5	32.12	19.136		
8,700.0	8,681.7	8,200.0	8,058.8	31.1	28.5	-167.52	-104.3	133.7	702.5	671.7	30.78	22.826		
8,800.0	8,781.7	8,218.9	8,067.1	31.5	28.6	-168.20	-121.3	134.1	792.1	762.4	29.66	26.707		
8,900.0	8,881.7	8,235.5	8,073.8	31.8	28.6	-168.76	-136.4	134.4	883.1	854.3	28.73	30.738		
9,000.0	8,981.7	8,250.0	8,079.3	32.2	28.7	-169.21	-149.8	134.7	975.2	947.2	27.96	34.884		
9,100.0	9,081.7	8,250.0	8,079.3	32.6	28.7	-169.21	-149.8	134.7	1,068.5	1,041.7	26.83	39.827		
9,200.0	9,181.7	8,274.5	8,087.9	32.9	28.8	-169.92	-172.8	135.3	1,162.1	1,135.3	26.81	43.350		
9,300.0	9,281.7	8,300.0	8,095.8	33.3	28.8	-170.58	-197.0	135.8	1,256.9	1,230.1	26.87	46.777		
9,400.0	9,381.7	8,300.0	8,095.8	33.6	28.8	-170.58	-197.0	135.8	1,351.8	1,325.5	26.22	51.551		
9,500.0	9,481.7	8,300.0	8,095.8	34.0	28.8	-170.58	-197.0	135.8	1,447.3	1,421.6	25.72	56.271		
9,600.0	9,581.7	8,300.0	8,095.8	34.3	28.8	-170.58	-197.0	135.8	1,543.4	1,518.0	25.34	60.910		
9,700.0	9,681.7	8,317.3	8,100.5	34.7	28.9	-170.99	-213.7	136.2	1,639.6	1,614.1	25.45	64.433		
9,800.0	9,781.7	8,323.7	8,102.1	35.0	28.9	-171.14	-219.9	136.3	1,736.2	1,710.9	25.35	68.493		
9,900.0	9,881.7	8,329.6	8,103.6	35.4	28.9	-171.27	-225.6	136.5	1,833.2	1,807.9	25.29	72.477		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #104H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,000.0	9,981.7	8,350.0	8,108.0	35.7	29.0	-171.70	-245.5	136.9	1,930.6	1,905.0	25.55	75.562		
10,100.0	10,081.7	8,350.0	8,108.0	36.1	29.0	-171.70	-245.5	136.9	2,027.8	2,002.4	25.46	79.657		
10,200.0	10,181.7	8,350.0	8,108.0	36.5	29.0	-171.70	-245.5	136.9	2,125.3	2,099.9	25.41	83.636		
10,300.0	10,281.7	8,350.0	8,108.0	36.8	29.0	-171.70	-245.5	136.9	2,223.0	2,197.6	25.41	87.497		
10,400.0	10,381.7	8,350.0	8,108.0	37.2	29.0	-171.70	-245.5	136.9	2,321.0	2,295.5	25.44	91.241		
10,500.0	10,481.7	8,350.0	8,108.0	37.5	29.0	-171.70	-245.5	136.9	2,419.0	2,393.5	25.50	94.868		
10,600.0	10,581.7	8,350.0	8,108.0	37.9	29.0	-171.70	-245.5	136.9	2,517.3	2,491.7	25.59	98.380		
10,700.0	10,681.7	8,350.0	8,108.0	38.2	29.0	-171.70	-245.5	136.9	2,615.6	2,589.9	25.70	101.780		
10,800.0	10,781.7	8,350.0	8,108.0	38.6	29.0	-171.70	-245.5	136.9	2,714.1	2,688.3	25.83	105.070		
10,831.3	10,813.0	8,350.0	8,108.0	38.7	29.0	-171.70	-245.5	136.9	2,745.0	2,719.1	25.88	106.079		
10,850.0	10,831.7	8,350.0	8,108.0	38.8	29.0	2.69	-245.5	136.9	2,763.4	2,737.5	25.90	106.687		
10,900.0	10,881.5	8,370.5	8,111.9	38.9	29.1	1.67	-265.7	137.4	2,811.5	2,785.3	26.17	107.418		
10,950.0	10,930.8	8,373.3	8,112.3	39.1	29.1	1.28	-268.3	137.4	2,858.7	2,832.5	26.21	109.067		
11,000.0	10,979.2	8,376.6	8,112.8	39.2	29.1	1.03	-271.6	137.5	2,904.5	2,878.3	26.23	110.742		
11,050.0	11,026.4	8,400.0	8,116.0	39.3	29.2	0.76	-294.8	138.0	2,948.9	2,922.5	26.43	111.592		
11,100.0	11,071.9	8,400.0	8,116.0	39.5	29.2	0.67	-294.8	138.0	2,990.7	2,964.3	26.36	113.465		
11,150.0	11,115.5	8,400.0	8,116.0	39.6	29.2	0.60	-294.8	138.0	3,030.2	3,004.0	26.28	115.321		
11,200.0	11,156.7	8,400.0	8,116.0	39.7	29.2	0.54	-294.8	138.0	3,067.3	3,041.1	26.19	117.132		
11,250.0	11,195.4	8,400.0	8,116.0	39.8	29.2	0.50	-294.8	138.0	3,101.8	3,075.7	26.09	118.870		
11,300.0	11,231.1	8,400.0	8,116.0	39.9	29.2	0.46	-294.8	138.0	3,133.4	3,107.4	26.00	120.503		
11,350.0	11,263.7	8,400.0	8,116.0	39.9	29.2	0.44	-294.8	138.0	3,162.1	3,136.2	25.92	121.999		
11,400.0	11,292.8	8,400.0	8,116.0	40.0	29.2	0.42	-294.8	138.0	3,187.6	3,161.8	25.85	123.322		
11,450.0	11,318.3	8,426.1	8,118.5	40.1	29.3	0.34	-320.7	138.6	3,209.3	3,183.3	25.96	123.635		
11,500.0	11,339.9	8,450.0	8,119.7	40.2	29.4	0.28	-344.6	139.2	3,228.1	3,202.1	26.05	123.911		
11,550.0	11,357.5	8,450.0	8,119.7	40.3	29.4	0.27	-344.6	139.2	3,243.0	3,217.0	26.02	124.648		
11,600.0	11,371.0	8,450.0	8,119.7	40.4	29.4	0.26	-344.6	139.2	3,254.4	3,228.4	26.01	125.100		
11,650.0	11,380.2	8,450.0	8,119.7	40.5	29.4	0.26	-344.6	139.2	3,262.2	3,236.2	26.05	125.244		
11,700.0	11,385.1	8,467.0	8,120.0	40.7	29.4	0.23	-361.7	139.5	3,266.4	3,240.2	26.18	124.781		
11,731.3	11,386.0	8,467.0	8,120.0	40.7	29.4	0.22	-361.7	139.5	3,267.0	3,240.8	26.23	124.538		
11,800.0	11,386.0	8,533.5	8,120.0	40.9	29.7	0.12	-428.1	140.4	3,267.0	3,240.4	26.61	122.787		
11,900.0	11,386.0	8,633.3	8,120.0	41.3	30.2	0.02	-527.9	141.2	3,267.0	3,239.8	27.22	120.008		
11,949.4	11,386.0	8,682.7	8,120.0	41.4	30.5	0.00	-577.3	141.6	3,267.0	3,239.4	27.56	118.553		
12,009.9	11,386.0	8,743.1	8,120.0	41.7	30.8	-0.01	-637.8	142.1	3,267.0	3,239.0	27.98	116.749		
12,100.0	11,386.0	8,833.3	8,120.0	42.1	31.4	-0.01	-727.9	142.8	3,267.0	3,238.3	28.67	113.966		
12,200.0	11,386.0	8,933.3	8,120.0	42.6	32.1	-0.01	-827.9	143.6	3,267.0	3,237.5	29.49	110.798		
12,300.0	11,386.0	9,033.3	8,120.0	43.2	32.9	-0.01	-927.9	144.5	3,267.0	3,236.6	30.36	107.595		
12,400.0	11,386.0	9,133.3	8,120.0	43.8	33.7	-0.01	-1,027.9	145.3	3,267.0	3,235.7	31.29	104.395		
12,500.0	11,386.0	9,233.3	8,120.0	44.5	34.6	-0.01	-1,127.9	146.1	3,267.0	3,234.7	32.27	101.231		
12,600.0	11,386.0	9,333.3	8,120.0	45.2	35.6	-0.01	-1,227.9	146.9	3,267.0	3,233.7	33.29	98.125		
12,700.0	11,386.0	9,433.3	8,120.0	46.0	36.6	-0.01	-1,327.9	147.7	3,267.0	3,232.6	34.36	95.095		
12,800.0	11,386.0	9,533.3	8,120.0	46.8	37.6	-0.01	-1,427.9	148.5	3,267.0	3,231.5	35.45	92.154		
12,900.0	11,386.0	9,633.3	8,120.0	47.7	38.7	-0.01	-1,527.9	149.3	3,267.0	3,230.4	36.58	89.309		
13,000.0	11,386.0	9,733.3	8,120.0	48.6	39.8	-0.01	-1,627.9	150.2	3,267.0	3,229.3	37.74	86.568		
13,100.0	11,386.0	9,833.3	8,120.0	49.5	41.0	-0.01	-1,727.9	151.0	3,267.0	3,228.1	38.92	83.931		
13,200.0	11,386.0	9,933.3	8,120.0	50.5	42.2	-0.01	-1,827.9	151.8	3,267.0	3,226.9	40.14	81.400		
13,300.0	11,386.0	10,033.3	8,120.0	51.5	43.4	-0.01	-1,927.9	152.6	3,267.0	3,225.6	41.37	78.974		
13,400.0	11,386.0	10,133.3	8,120.0	52.6	44.6	-0.01	-2,027.9	153.4	3,267.0	3,224.4	42.62	76.651		
13,500.0	11,386.0	10,233.3	8,120.0	53.6	45.9	-0.01	-2,127.9	154.2	3,267.0	3,223.1	43.89	74.428		
13,600.0	11,386.0	10,333.3	8,120.0	54.7	47.2	-0.01	-2,227.9	155.1	3,267.0	3,221.8	45.18	72.303		
13,700.0	11,386.0	10,433.3	8,120.0	55.9	48.5	-0.01	-2,327.9	155.9	3,267.0	3,220.5	46.49	70.271		
13,800.0	11,386.0	10,533.3	8,120.0	57.0	49.9	-0.01	-2,427.8	156.7	3,267.0	3,219.2	47.81	68.329		
13,900.0	11,386.0	10,633.3	8,120.0	58.2	51.2	-0.01	-2,527.8	157.5	3,267.0	3,217.9	49.15	66.473		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #104H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,000.0	11,386.0	10,733.3	8,120.0	59.4	52.6	-0.01	-2,627.8	158.3	3,267.0	3,216.5	50.50	64.698		
14,100.0	11,386.0	10,833.3	8,120.0	60.6	54.0	-0.01	-2,727.8	159.1	3,267.0	3,215.1	51.86	63.002		
14,200.0	11,386.0	10,933.3	8,120.0	61.9	55.4	-0.01	-2,827.8	159.9	3,267.0	3,213.8	53.23	61.379		
14,300.0	11,386.0	11,033.3	8,120.0	63.1	56.8	-0.01	-2,927.8	160.8	3,267.0	3,212.4	54.61	59.827		
14,400.0	11,386.0	11,133.3	8,120.0	64.4	58.3	-0.01	-3,027.8	161.6	3,267.0	3,211.0	56.00	58.342		
14,500.0	11,386.0	11,233.3	8,120.0	65.7	59.7	-0.01	-3,127.8	162.4	3,267.0	3,209.6	57.40	56.920		
14,600.0	11,386.0	11,333.3	8,120.0	67.0	61.2	-0.01	-3,227.8	163.2	3,267.0	3,208.2	58.80	55.558		
14,700.0	11,386.0	11,433.3	8,120.0	68.4	62.6	-0.01	-3,327.8	164.0	3,267.0	3,206.8	60.22	54.252		
14,800.0	11,386.0	11,533.3	8,120.0	69.7	64.1	-0.01	-3,427.8	164.8	3,267.0	3,205.4	61.64	53.000		
14,900.0	11,386.0	11,633.3	8,120.0	71.1	65.6	-0.01	-3,527.8	165.6	3,267.0	3,203.9	63.07	51.800		
15,000.0	11,386.0	11,733.3	8,120.0	72.4	67.1	-0.01	-3,627.8	166.5	3,267.0	3,202.5	64.51	50.647		
15,100.0	11,386.0	11,833.3	8,120.0	73.8	68.6	-0.01	-3,727.8	167.3	3,267.0	3,201.1	65.95	49.540		
15,200.0	11,386.0	11,933.3	8,120.0	75.2	70.1	-0.01	-3,827.8	168.1	3,267.0	3,199.6	67.39	48.477		
15,300.0	11,386.0	12,033.3	8,120.0	76.6	71.6	-0.01	-3,927.8	168.9	3,267.0	3,198.2	68.84	47.455		
15,400.0	11,386.0	12,133.3	8,120.0	78.0	73.1	-0.01	-4,027.8	169.7	3,267.0	3,196.7	70.30	46.471		
15,500.0	11,386.0	12,233.3	8,120.0	79.4	74.6	-0.01	-4,127.8	170.5	3,267.0	3,195.2	71.76	45.525		
15,600.0	11,386.0	12,333.3	8,120.0	80.9	76.1	-0.01	-4,227.8	171.3	3,267.0	3,193.8	73.23	44.614		
15,700.0	11,386.0	12,433.3	8,120.0	82.3	77.7	-0.01	-4,327.8	172.2	3,267.0	3,192.3	74.70	43.736		
15,800.0	11,386.0	12,533.3	8,120.0	83.7	79.2	-0.01	-4,427.8	173.0	3,267.0	3,190.8	76.17	42.890		
15,900.0	11,386.0	12,633.3	8,120.0	85.2	80.8	-0.01	-4,527.8	173.8	3,267.0	3,189.4	77.65	42.074		
16,000.0	11,386.0	12,733.3	8,120.0	86.7	82.3	-0.01	-4,627.8	174.6	3,267.0	3,187.9	79.13	41.287		
16,100.0	11,386.0	12,833.3	8,120.0	88.1	83.8	-0.01	-4,727.8	175.4	3,267.0	3,186.4	80.61	40.527		
16,200.0	11,386.0	12,933.3	8,120.0	89.6	85.4	-0.01	-4,827.8	176.2	3,267.0	3,184.9	82.10	39.793		
16,300.0	11,386.0	13,033.3	8,120.0	91.1	87.0	-0.01	-4,927.8	177.1	3,267.0	3,183.4	83.59	39.083		
16,400.0	11,386.0	13,133.3	8,120.0	92.6	88.5	-0.01	-5,027.8	177.9	3,267.0	3,181.9	85.08	38.398		
16,500.0	11,386.0	13,233.3	8,120.0	94.0	90.1	-0.01	-5,127.8	178.7	3,267.0	3,180.4	86.58	37.735		
16,600.0	11,386.0	13,333.3	8,120.0	95.5	91.7	-0.01	-5,227.8	179.5	3,267.0	3,178.9	88.08	37.093		
16,700.0	11,386.0	13,433.3	8,120.0	97.0	93.2	-0.01	-5,327.8	180.3	3,267.0	3,177.4	89.58	36.471		
16,800.0	11,386.0	13,533.3	8,120.0	98.5	94.8	-0.01	-5,427.7	181.1	3,267.0	3,175.9	91.08	35.870		
16,900.0	11,386.0	13,633.3	8,120.0	100.1	96.4	-0.01	-5,527.7	181.9	3,267.0	3,174.4	92.58	35.287		
17,000.0	11,386.0	13,733.3	8,120.0	101.6	98.0	-0.01	-5,627.7	182.8	3,267.0	3,172.9	94.09	34.722		
17,100.0	11,386.0	13,833.3	8,120.0	103.1	99.5	-0.01	-5,727.7	183.6	3,267.0	3,171.4	95.60	34.174		
17,200.0	11,386.0	13,933.3	8,120.0	104.6	101.1	-0.01	-5,827.7	184.4	3,267.0	3,169.9	97.11	33.642		
17,300.0	11,386.0	14,033.3	8,120.0	106.1	102.7	-0.01	-5,927.7	185.2	3,267.0	3,168.4	98.62	33.126		
17,400.0	11,386.0	14,133.3	8,120.0	107.7	104.3	-0.01	-6,027.7	186.0	3,267.0	3,166.9	100.14	32.625		
17,500.0	11,386.0	14,233.3	8,120.0	109.2	105.9	-0.01	-6,127.7	186.8	3,267.0	3,165.3	101.65	32.139		
17,600.0	11,386.0	14,333.3	8,120.0	110.7	107.5	-0.01	-6,227.7	187.6	3,267.0	3,163.8	103.17	31.666		
17,700.0	11,386.0	14,433.3	8,120.0	112.3	109.1	-0.01	-6,327.7	188.5	3,267.0	3,162.3	104.69	31.206		
17,800.0	11,386.0	14,533.3	8,120.0	113.8	110.7	-0.01	-6,427.7	189.3	3,267.0	3,160.8	106.21	30.760		
17,900.0	11,386.0	14,633.3	8,120.0	115.4	112.3	-0.01	-6,527.7	190.1	3,267.0	3,159.3	107.73	30.325		
18,000.0	11,386.0	14,733.3	8,120.0	116.9	113.9	-0.01	-6,627.7	190.9	3,267.0	3,157.7	109.26	29.902		
18,100.0	11,386.0	14,833.3	8,120.0	118.5	115.5	-0.01	-6,727.7	191.7	3,267.0	3,156.2	110.78	29.491		
18,200.0	11,386.0	14,933.3	8,120.0	120.0	117.1	-0.01	-6,827.7	192.5	3,267.0	3,154.7	112.31	29.090		
18,300.0	11,386.0	15,033.3	8,120.0	121.6	118.7	-0.01	-6,927.7	193.4	3,267.0	3,153.2	113.83	28.700		
18,400.0	11,386.0	15,133.3	8,120.0	123.2	120.3	-0.01	-7,027.7	194.2	3,267.0	3,151.6	115.36	28.320		
18,500.0	11,386.0	15,233.3	8,120.0	124.7	121.9	-0.01	-7,127.7	195.0	3,267.0	3,150.1	116.89	27.949		
18,600.0	11,386.0	15,333.3	8,120.0	126.3	123.5	-0.01	-7,227.7	195.8	3,267.0	3,148.6	118.42	27.588		
18,700.0	11,386.0	15,433.3	8,120.0	127.9	125.1	-0.01	-7,327.7	196.6	3,267.0	3,147.0	119.95	27.236		
18,800.0	11,386.0	15,533.3	8,120.0	129.4	126.7	-0.01	-7,427.7	197.4	3,267.0	3,145.5	121.48	26.893		
18,900.0	11,386.0	15,633.3	8,120.0	131.0	128.3	-0.01	-7,527.7	198.2	3,267.0	3,144.0	123.02	26.558		
19,000.0	11,386.0	15,733.3	8,120.0	132.6	129.9	-0.01	-7,627.7	199.1	3,267.0	3,142.5	124.55	26.230		
19,100.0	11,386.0	15,833.3	8,120.0	134.1	131.5	-0.01	-7,727.7	199.9	3,267.0	3,140.9	126.08	25.911		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #104H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,200.0	11,386.0	15,933.3	8,120.0	135.7	133.1	0.00	-7,827.7	200.7	3,267.0	3,139.4	127.62	25.599		
19,300.0	11,386.0	16,033.3	8,120.0	137.3	134.7	0.00	-7,927.7	201.5	3,267.0	3,137.8	129.16	25.295		
19,400.0	11,386.0	16,133.3	8,120.0	138.9	136.4	0.00	-8,027.7	202.3	3,267.0	3,136.3	130.69	24.997		
19,500.0	11,386.0	16,233.3	8,120.0	140.5	138.0	0.00	-8,127.7	203.1	3,267.0	3,134.8	132.23	24.707		
19,600.0	11,386.0	16,333.3	8,120.0	142.0	139.6	0.00	-8,227.7	203.9	3,267.0	3,133.2	133.77	24.422		
19,700.0	11,386.0	16,433.3	8,120.0	143.6	141.2	0.00	-8,327.7	204.8	3,267.0	3,131.7	135.31	24.145		
19,800.0	11,386.0	16,533.3	8,120.0	145.2	142.8	0.00	-8,427.6	205.6	3,267.0	3,130.2	136.85	23.873		
19,900.0	11,386.0	16,633.3	8,120.0	146.8	144.5	0.00	-8,527.6	206.4	3,267.0	3,128.6	138.39	23.607		
20,000.0	11,386.0	16,733.3	8,120.0	148.4	146.1	0.00	-8,627.6	207.2	3,267.0	3,127.1	139.93	23.347		
20,100.0	11,386.0	16,833.3	8,120.0	150.0	147.7	0.00	-8,727.6	208.0	3,267.0	3,125.5	141.47	23.093		
20,200.0	11,386.0	16,933.3	8,120.0	151.6	149.3	0.00	-8,827.6	208.8	3,267.0	3,124.0	143.02	22.844		
20,300.0	11,386.0	17,033.3	8,120.0	153.2	150.9	0.00	-8,927.6	209.7	3,267.0	3,122.4	144.56	22.600		
20,400.0	11,386.0	17,133.3	8,120.0	154.8	152.6	0.00	-9,027.6	210.5	3,267.0	3,120.9	146.10	22.361		
20,500.0	11,386.0	17,233.3	8,120.0	156.4	154.2	0.00	-9,127.6	211.3	3,267.0	3,119.4	147.65	22.127		
20,600.0	11,386.0	17,333.3	8,120.0	158.0	155.8	0.00	-9,227.6	212.1	3,267.0	3,117.8	149.19	21.898		
20,700.0	11,386.0	17,433.3	8,120.0	159.6	157.4	0.00	-9,327.6	212.9	3,267.0	3,116.3	150.74	21.673		
20,800.0	11,386.0	17,533.3	8,120.0	161.2	159.1	0.00	-9,427.6	213.7	3,267.0	3,114.7	152.28	21.453		
20,900.0	11,386.0	17,633.3	8,120.0	162.8	160.7	0.00	-9,527.6	214.5	3,267.0	3,113.2	153.83	21.238		
21,000.0	11,386.0	17,733.3	8,120.0	164.4	162.3	0.00	-9,627.6	215.4	3,267.0	3,111.6	155.38	21.026		
21,100.0	11,386.0	17,833.3	8,120.0	166.0	163.9	0.00	-9,727.6	216.2	3,267.0	3,110.1	156.92	20.819		
21,200.0	11,386.0	17,933.3	8,120.0	167.6	165.6	0.00	-9,827.6	217.0	3,267.0	3,108.5	158.47	20.616		
21,300.0	11,386.0	18,033.3	8,120.0	169.2	167.2	0.00	-9,927.6	217.8	3,267.0	3,107.0	160.02	20.416		
21,400.0	11,386.0	18,133.3	8,120.0	170.8	168.8	0.00	-10,027.6	218.6	3,267.0	3,105.4	161.57	20.221		
21,500.0	11,386.0	18,233.3	8,120.0	172.4	170.4	0.00	-10,127.6	219.4	3,267.0	3,103.9	163.12	20.029		
21,600.0	11,386.0	18,333.3	8,120.0	174.0	172.1	0.00	-10,227.6	220.2	3,267.0	3,102.3	164.67	19.840		
21,700.0	11,386.0	18,433.3	8,120.0	175.6	173.7	0.00	-10,327.6	221.1	3,267.0	3,100.8	166.22	19.655		
21,800.0	11,386.0	18,533.3	8,120.0	177.2	175.3	0.00	-10,427.6	221.9	3,267.0	3,099.2	167.76	19.474		
21,900.0	11,386.0	18,633.3	8,120.0	178.8	177.0	0.00	-10,527.6	222.7	3,267.0	3,097.7	169.32	19.295		
22,000.0	11,386.0	18,733.3	8,120.0	180.4	178.6	0.00	-10,627.6	223.5	3,267.0	3,096.1	170.87	19.120		
22,100.0	11,386.0	18,833.3	8,120.0	182.0	180.2	0.00	-10,727.6	224.3	3,267.0	3,094.6	172.42	18.948		
22,200.0	11,386.0	18,933.3	8,120.0	183.7	181.9	0.00	-10,827.6	225.1	3,267.0	3,093.0	173.97	18.779		
22,300.0	11,386.0	19,033.3	8,120.0	185.3	183.5	0.00	-10,927.6	226.0	3,267.0	3,091.5	175.52	18.613		
22,400.0	11,386.0	19,133.3	8,120.0	186.9	185.1	0.00	-11,027.6	226.8	3,267.0	3,089.9	177.07	18.450		
22,500.0	11,386.0	19,233.3	8,120.0	188.5	186.8	0.00	-11,127.6	227.6	3,267.0	3,088.4	178.62	18.290		
22,600.0	11,386.0	19,333.3	8,120.0	190.1	188.4	0.00	-11,227.6	228.4	3,267.0	3,086.8	180.18	18.132		
22,700.0	11,386.0	19,433.3	8,120.0	191.7	190.0	0.00	-11,327.6	229.2	3,267.0	3,085.3	181.73	17.977		
22,800.0	11,386.0	19,533.3	8,120.0	193.3	191.7	0.00	-11,427.5	230.0	3,267.0	3,083.7	183.28	17.825		
22,900.0	11,386.0	19,633.3	8,120.0	195.0	193.3	0.00	-11,527.5	230.8	3,267.0	3,082.2	184.84	17.675		
23,000.0	11,386.0	19,733.3	8,120.0	196.6	194.9	0.00	-11,627.5	231.7	3,267.0	3,080.6	186.39	17.528		
23,100.0	11,386.0	19,833.3	8,120.0	198.2	196.6	0.00	-11,727.5	232.5	3,267.0	3,079.1	187.94	17.383		
23,200.0	11,386.0	19,933.3	8,120.0	199.8	198.2	0.00	-11,827.5	233.3	3,267.0	3,077.5	189.50	17.240		
23,300.0	11,386.0	20,033.3	8,120.0	201.4	199.8	0.00	-11,927.5	234.1	3,267.0	3,075.9	191.05	17.100		
23,400.0	11,386.0	20,133.3	8,120.0	203.0	201.5	0.00	-12,027.5	234.9	3,267.0	3,074.4	192.61	16.962		
23,500.0	11,386.0	20,233.3	8,120.0	204.7	203.1	0.00	-12,127.5	235.7	3,267.0	3,072.8	194.16	16.826		
23,600.0	11,386.0	20,333.3	8,120.0	206.3	204.7	0.00	-12,227.5	236.5	3,267.0	3,071.3	195.72	16.692		
23,705.7	11,386.0	20,439.0	8,120.0	208.0	206.5	0.00	-12,333.2	237.4	3,267.0	3,069.6	197.36	16.553		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #108H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	1.0	1.0	0.0	0.0	-105.72	-30.9	-109.8	114.1					
100.0	100.0	101.0	101.0	0.1	0.1	-105.72	-30.9	-109.8	114.1	113.8	0.26	438.889		
200.0	200.0	201.0	201.0	0.5	0.5	-105.72	-30.9	-109.8	114.1	113.1	0.98	116.769		
300.0	300.0	301.0	301.0	0.8	0.8	-105.72	-30.9	-109.8	114.1	112.4	1.69	67.343		
400.0	400.0	401.0	401.0	1.2	1.2	-105.72	-30.9	-109.8	114.1	111.7	2.41	47.315		
500.0	500.0	501.0	501.0	1.6	1.6	-105.72	-30.9	-109.8	114.1	110.9	3.13	36.469		
600.0	600.0	603.5	603.5	1.9	1.9	-149.91	-30.6	-108.7	113.7	109.8	3.85	29.555		
700.0	700.0	706.0	705.9	2.3	2.3	-150.62	-29.7	-105.4	112.6	108.1	4.56	24.688		
800.0	799.9	808.4	808.2	2.6	2.7	-151.84	-28.2	-99.9	110.9	105.7	5.28	21.006		
900.0	899.7	910.8	910.2	3.0	3.0	-153.60	-26.2	-92.3	108.6	102.6	6.00	18.104		
1,000.0	999.4	1,013.0	1,011.9	3.4	3.4	-155.97	-23.5	-82.5	105.9	99.1	6.72	15.749		
1,100.0	1,098.9	1,115.1	1,113.3	3.7	3.8	-159.02	-20.3	-70.6	102.7	95.3	7.44	13.802		
1,200.0	1,198.3	1,217.0	1,214.1	4.1	4.2	-162.85	-16.5	-56.6	99.4	91.2	8.17	12.172		
1,300.0	1,297.4	1,317.6	1,313.4	4.5	4.6	-167.44	-12.2	-40.9	96.4	87.5	8.90	10.839		
1,400.0	1,396.4	1,417.2	1,411.7	4.9	5.0	-172.37	-7.9	-25.1	94.7	85.1	9.64	9.827		
1,500.0	1,495.5	1,516.9	1,510.0	5.3	5.4	-177.43	-3.6	-9.3	93.8	83.4	10.40	9.019		
1,577.7	1,572.4	1,605.7	1,586.4	5.6	5.8	178.58	-0.3	2.9	93.5	82.5	11.04	8.473 CC		
1,600.0	1,594.5	1,616.5	1,608.3	5.7	5.8	177.44	0.6	6.4	93.6	82.4	11.17	8.376		
1,700.0	1,693.5	1,716.2	1,706.6	6.1	6.3	172.33	4.9	22.2	94.1	82.2	11.96	7.868 ES		
1,800.0	1,792.5	1,815.8	1,804.9	6.5	6.7	167.32	9.2	38.0	95.4	82.6	12.77	7.472		
1,900.0	1,891.6	1,915.5	1,903.2	6.9	7.1	162.47	13.5	53.7	97.4	83.8	13.59	7.167		
2,000.0	1,990.6	2,015.1	2,001.5	7.3	7.5	157.85	17.8	69.5	100.1	85.6	14.43	6.936		
2,100.0	2,089.6	2,114.8	2,099.8	7.7	8.0	153.50	22.0	85.3	103.4	88.1	15.27	6.767		
2,200.0	2,188.6	2,214.4	2,198.1	8.1	8.4	149.44	26.3	101.0	107.2	91.1	16.13	6.646		
2,300.0	2,287.7	2,314.1	2,296.4	8.5	8.8	145.67	30.6	116.8	111.6	94.6	16.99	6.565		
2,400.0	2,386.7	2,413.7	2,394.7	8.9	9.3	142.20	34.9	132.6	116.4	98.5	17.86	6.516		
2,500.0	2,485.7	2,513.3	2,493.0	9.3	9.7	139.01	39.2	148.3	121.5	102.8	18.72	6.492		
2,600.0	2,584.8	2,613.0	2,591.3	9.8	10.1	136.09	43.4	164.1	127.1	107.5	19.59	6.487		
2,700.0	2,683.8	2,712.6	2,689.6	10.2	10.6	133.42	47.7	179.9	132.9	112.5	20.46	6.497		
2,739.3	2,722.7	2,751.8	2,728.2	10.3	10.7	132.43	49.4	186.1	135.3	114.5	20.80	6.505		
2,800.0	2,782.9	2,812.3	2,787.9	10.6	11.0	130.87	52.0	195.6	138.7	117.4	21.32	6.505		
2,900.0	2,882.3	2,911.9	2,886.1	11.0	11.4	127.79	56.3	211.4	143.3	121.1	22.19	6.457		
3,000.0	2,981.9	3,011.4	2,984.3	11.4	11.9	124.08	60.6	227.1	146.7	123.7	23.04	6.369		
3,100.0	3,081.7	3,110.7	3,082.2	11.7	12.3	119.69	64.8	242.8	149.5	125.6	23.88	6.262		
3,200.0	3,181.7	3,209.7	3,179.9	12.1	12.7	114.63	69.1	258.5	152.1	127.4	24.68	6.161		
3,272.6	3,254.3	3,281.4	3,250.7	12.3	13.1	154.48	72.2	269.9	154.1	128.8	25.23	6.105		
3,300.0	3,281.7	3,308.4	3,277.3	12.4	13.2	152.87	73.3	274.1	154.9	129.5	25.43	6.092		
3,400.0	3,381.7	3,407.1	3,374.7	12.7	13.6	147.16	77.5	289.7	159.2	133.0	26.14	6.089 SF		
3,500.0	3,481.7	3,505.7	3,472.0	13.1	14.1	141.79	81.8	305.4	165.0	138.1	26.81	6.152		
3,600.0	3,581.7	3,604.4	3,569.3	13.4	14.5	136.81	86.0	321.0	172.1	144.6	27.46	6.267		
3,700.0	3,681.7	3,703.0	3,666.6	13.7	14.9	132.25	90.3	336.6	180.5	152.4	28.09	6.424		
3,800.0	3,781.7	3,801.7	3,763.9	14.1	15.4	128.12	94.5	352.2	189.9	161.2	28.71	6.613		
3,900.0	3,881.7	3,900.3	3,861.2	14.4	15.8	124.38	98.7	367.8	200.2	170.9	29.33	6.826		
4,000.0	3,981.7	4,001.0	3,958.5	14.7	16.2	121.02	103.0	383.4	211.3	181.3	29.95	7.053		
4,100.0	4,081.7	4,102.4	4,055.8	15.1	16.7	117.99	107.2	399.0	223.0	192.4	30.59	7.291		
4,200.0	4,181.7	4,203.7	4,153.1	15.4	17.1	115.28	111.4	414.6	235.3	204.1	31.22	7.536		
4,300.0	4,281.7	4,305.1	4,250.5	15.8	17.6	112.83	115.7	430.2	248.1	216.2	31.87	7.784		
4,400.0	4,381.7	4,406.4	4,347.8	16.1	18.0	110.63	119.9	445.8	261.2	228.7	32.52	8.033		
4,500.0	4,481.7	4,492.2	4,445.1	16.4	18.4	108.63	124.2	461.4	274.8	241.6	33.12	8.297		
4,600.0	4,581.7	4,609.2	4,542.4	16.8	18.9	106.83	128.4	477.0	288.6	254.7	33.84	8.527		
4,700.0	4,681.7	4,689.5	4,639.7	17.1	19.3	105.19	132.6	492.7	302.7	268.2	34.43	8.790		
4,800.0	4,781.7	4,788.1	4,737.0	17.5	19.7	103.69	136.9	508.3	317.0	281.9	35.10	9.031		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #108H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
4,900.0	4,881.7	4,886.8	4,834.3	17.8	20.1	102.33	141.1	523.9	331.5	295.7	35.77	9.267		
5,000.0	4,981.7	4,985.4	4,931.6	18.2	20.6	101.08	145.3	539.5	346.1	309.7	36.44	9.498		
5,100.0	5,081.7	5,084.1	5,029.0	18.5	21.0	99.93	149.6	555.1	360.9	323.8	37.12	9.723		
5,200.0	5,181.7	5,184.6	5,128.2	18.8	21.5	98.87	153.8	570.7	375.6	337.8	37.82	9.931		
5,300.0	5,281.7	5,285.3	5,227.6	19.2	21.9	97.92	157.9	585.9	389.9	351.4	38.53	10.121		
5,400.0	5,381.7	5,386.1	5,327.3	19.5	22.3	97.07	161.9	600.5	403.9	364.6	39.24	10.292		
5,500.0	5,481.7	5,487.2	5,427.3	19.9	22.8	96.30	165.7	614.7	417.3	377.4	39.95	10.447		
5,600.0	5,581.7	5,588.4	5,527.5	20.2	23.2	95.60	169.5	628.3	430.4	389.7	40.66	10.585		
5,700.0	5,681.7	5,689.7	5,627.9	20.6	23.6	94.97	173.0	641.5	443.0	401.6	41.38	10.706		
5,800.0	5,781.7	5,791.2	5,728.5	20.9	24.0	94.40	176.4	654.1	455.1	413.0	42.09	10.813		
5,900.0	5,881.7	5,892.8	5,829.4	21.3	24.4	93.88	179.7	666.2	466.8	424.0	42.81	10.904		
6,000.0	5,981.7	5,994.6	5,930.4	21.6	24.8	93.41	182.9	677.8	477.9	434.4	43.52	10.982		
6,100.0	6,081.7	6,096.5	6,031.7	22.0	25.2	92.98	185.9	688.8	488.6	444.4	44.24	11.045		
6,200.0	6,181.7	6,198.5	6,133.1	22.3	25.7	92.58	188.7	699.4	498.8	453.8	44.95	11.096		
6,300.0	6,281.7	6,300.6	6,234.7	22.7	26.0	92.23	191.4	709.4	508.5	462.8	45.67	11.134		
6,400.0	6,381.7	6,402.9	6,336.5	23.0	26.4	91.90	194.0	718.8	517.7	471.3	46.39	11.160		
6,500.0	6,481.7	6,505.2	6,438.4	23.4	26.8	91.60	196.4	727.8	526.3	479.2	47.10	11.174		
6,600.0	6,581.7	6,607.7	6,540.5	23.7	27.2	91.33	198.7	736.2	534.5	486.6	47.81	11.178		
6,700.0	6,681.7	6,710.2	6,642.7	24.1	27.6	91.09	200.9	744.0	542.1	493.6	48.53	11.171		
6,800.0	6,781.7	6,812.9	6,745.1	24.4	28.0	90.86	202.8	751.4	549.2	499.9	49.24	11.154		
6,900.0	6,881.7	6,915.6	6,847.6	24.8	28.3	90.66	204.7	758.1	555.8	505.8	49.95	11.127		
7,000.0	6,981.7	7,018.4	6,950.2	25.1	28.7	90.48	206.4	764.4	561.8	511.1	50.66	11.090		
7,100.0	7,081.7	7,121.2	7,052.9	25.5	29.1	90.32	207.9	770.1	567.3	516.0	51.37	11.045		
7,200.0	7,181.7	7,224.2	7,155.6	25.8	29.4	90.18	209.3	775.2	572.3	520.2	52.07	10.991		
7,300.0	7,281.7	7,327.1	7,258.5	26.2	29.8	90.05	210.6	779.8	576.8	524.0	52.78	10.928		
7,400.0	7,381.7	7,430.2	7,361.5	26.5	30.1	89.95	211.7	783.8	580.7	527.2	53.48	10.858		
7,500.0	7,481.7	7,533.2	7,464.5	26.9	30.5	89.85	212.6	787.3	584.1	529.9	54.18	10.780		
7,600.0	7,581.7	7,636.4	7,567.5	27.2	30.8	89.78	213.4	790.2	586.9	532.0	54.88	10.694		
7,700.0	7,681.7	7,739.5	7,670.6	27.6	31.2	89.71	214.0	792.6	589.2	533.6	55.58	10.601		
7,800.0	7,781.7	7,842.7	7,773.8	28.0	31.5	89.67	214.5	794.4	591.0	534.7	56.28	10.501		
7,900.0	7,881.7	7,945.8	7,877.0	28.3	31.8	89.63	214.9	795.7	592.2	535.3	56.97	10.395		
8,000.0	7,981.7	8,049.0	7,980.2	28.7	32.2	89.62	215.1	796.4	592.9	535.3	57.66	10.282		
8,100.0	8,081.7	8,151.6	8,082.7	29.0	32.5	89.65	214.7	796.6	593.1	534.7	58.35	10.164		
8,125.5	8,107.1	8,177.1	8,108.1	29.1	32.6	89.80	213.2	796.6	593.1	534.6	58.53	10.134		
8,200.0	8,181.7	8,250.2	8,180.4	29.4	32.8	90.83	202.5	796.6	593.2	534.1	59.05	10.045		
8,300.0	8,281.7	8,342.0	8,268.3	29.7	33.0	93.36	176.3	796.7	594.4	534.6	59.78	9.943		
8,400.0	8,381.7	8,423.8	8,342.2	30.1	33.1	96.70	141.4	796.9	598.8	538.3	60.47	9.902		
8,500.0	8,481.7	8,494.3	8,401.4	30.4	33.3	100.32	103.1	797.0	608.7	547.7	60.93	9.989		
8,600.0	8,581.7	8,554.0	8,447.5	30.8	33.4	103.81	65.2	797.1	626.0	565.1	60.96	10.270		
8,700.0	8,681.7	8,600.0	8,480.1	31.1	33.4	106.71	32.8	797.2	652.1	591.8	60.32	10.811		
8,800.0	8,781.7	8,650.0	8,512.6	31.5	33.5	110.01	-5.2	797.4	687.3	628.0	59.33	11.584		
8,900.0	8,881.7	8,681.9	8,531.5	31.8	33.5	112.17	-30.9	797.5	731.2	673.6	57.63	12.688		
9,000.0	8,981.7	8,712.1	8,548.1	32.2	33.5	114.22	-56.1	797.5	783.0	727.3	55.72	14.052		
9,100.0	9,081.7	8,737.9	8,561.1	32.6	33.6	115.97	-78.3	797.6	841.8	788.2	53.65	15.690		
9,200.0	9,181.7	8,750.0	8,566.9	32.9	33.6	116.80	-88.9	797.7	906.7	855.4	51.30	17.676		
9,300.0	9,281.7	8,779.4	8,580.1	33.3	33.6	118.77	-115.2	797.8	976.3	926.8	49.54	19.707		
9,400.0	9,381.7	8,800.0	8,588.5	33.6	33.6	120.15	-134.1	797.8	1,050.3	1,002.5	47.75	21.997		
9,500.0	9,481.7	8,800.0	8,588.5	34.0	33.6	120.15	-134.1	797.8	1,127.8	1,082.1	45.67	24.693		
9,600.0	9,581.7	8,824.2	8,597.4	34.3	33.6	121.74	-156.5	797.9	1,207.9	1,163.6	44.37	27.227		
9,700.0	9,681.7	8,850.0	8,606.0	34.7	33.7	123.40	-180.9	798.0	1,290.9	1,247.6	43.26	29.841		
9,800.0	9,781.7	8,850.0	8,606.0	35.0	33.7	123.40	-180.9	798.0	1,375.4	1,333.6	41.79	32.912		
9,900.0	9,881.7	8,850.0	8,606.0	35.4	33.7	123.40	-180.9	798.0	1,461.9	1,421.4	40.51	36.090		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #108H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,000.0	9,981.7	8,850.0	8,606.0	35.7	33.7	123.40	-180.9	798.0	1,550.0	1,510.6	39.39	39.351		
10,100.0	10,081.7	8,872.2	8,612.4	36.1	33.7	124.80	-202.1	798.1	1,638.9	1,600.1	38.80	42.239		
10,200.0	10,181.7	8,879.2	8,614.3	36.5	33.7	125.24	-208.9	798.1	1,729.1	1,691.0	38.06	45.432		
10,300.0	10,281.7	8,900.0	8,619.3	36.8	33.7	126.51	-229.1	798.1	1,820.5	1,782.8	37.64	48.369		
10,400.0	10,381.7	8,900.0	8,619.3	37.2	33.7	126.51	-229.1	798.1	1,912.3	1,875.3	36.98	51.709		
10,500.0	10,481.7	8,900.0	8,619.3	37.5	33.7	126.51	-229.1	798.1	2,004.9	1,968.4	36.42	55.049		
10,600.0	10,581.7	8,900.0	8,619.3	37.9	33.7	126.51	-229.1	798.1	2,098.1	2,062.2	35.94	58.377		
10,700.0	10,681.7	8,900.0	8,619.3	38.2	33.7	126.51	-229.1	798.1	2,192.0	2,156.4	35.54	61.681		
10,800.0	10,781.7	8,900.0	8,619.3	38.6	33.7	126.51	-229.1	798.1	2,286.4	2,251.2	35.20	64.954		
10,831.3	10,813.0	8,900.0	8,619.3	38.7	33.7	126.51	-229.1	798.1	2,316.0	2,280.9	35.11	65.972		
10,850.0	10,831.7	8,900.0	8,619.3	38.8	33.7	-54.09	-229.1	798.1	2,333.7	2,298.6	35.05	66.581		
10,900.0	10,881.5	8,900.0	8,619.3	38.9	33.7	-44.20	-229.1	798.1	2,380.4	2,345.5	34.89	68.231		
10,950.0	10,930.8	8,919.7	8,623.4	39.1	33.8	-36.40	-248.4	798.2	2,425.7	2,390.7	34.94	69.432		
11,000.0	10,979.2	8,923.8	8,624.2	39.2	33.8	-31.08	-252.4	798.2	2,469.8	2,435.0	34.79	70.995		
11,050.0	11,026.4	8,928.6	8,625.0	39.3	33.8	-27.08	-257.1	798.2	2,512.3	2,477.7	34.64	72.528		
11,100.0	11,071.9	8,950.0	8,628.4	39.5	33.8	-23.87	-278.2	798.3	2,553.2	2,518.6	34.66	73.672		
11,150.0	11,115.5	8,950.0	8,628.4	39.6	33.8	-21.56	-278.2	798.3	2,591.6	2,557.1	34.45	75.228		
11,200.0	11,156.7	8,950.0	8,628.4	39.7	33.8	-19.73	-278.2	798.3	2,627.6	2,593.4	34.25	76.716		
11,250.0	11,195.4	8,950.0	8,628.4	39.8	33.8	-18.25	-278.2	798.3	2,661.2	2,627.1	34.07	78.115		
11,300.0	11,231.1	8,950.0	8,628.4	39.9	33.8	-17.05	-278.2	798.3	2,692.2	2,658.3	33.91	79.403		
11,350.0	11,263.7	8,950.0	8,628.4	39.9	33.8	-16.08	-278.2	798.3	2,720.4	2,686.7	33.77	80.560		
11,400.0	11,292.8	8,974.7	8,631.3	40.0	33.9	-15.27	-302.7	798.4	2,745.1	2,711.3	33.84	81.132		
11,450.0	11,318.3	9,000.0	8,633.2	40.1	33.9	-14.63	-328.0	798.5	2,767.3	2,733.4	33.92	81.596		
11,500.0	11,339.9	9,000.0	8,633.2	40.2	33.9	-14.14	-328.0	798.5	2,785.8	2,751.9	33.86	82.283		
11,550.0	11,357.5	9,000.0	8,633.2	40.3	33.9	-13.75	-328.0	798.5	2,801.0	2,767.2	33.84	82.766		
11,600.0	11,371.0	9,000.0	8,633.2	40.4	33.9	-13.46	-328.0	798.5	2,813.0	2,779.1	33.88	83.030		
11,650.0	11,380.2	9,015.9	8,633.8	40.5	34.0	-13.28	-343.8	798.5	2,821.4	2,787.4	34.03	82.909		
11,700.0	11,385.1	9,029.9	8,634.0	40.7	34.0	-13.18	-357.8	798.6	2,826.5	2,792.3	34.21	82.624		
11,731.3	11,386.0	9,029.9	8,634.0	40.7	34.0	-13.15	-357.8	798.6	2,827.8	2,793.5	34.31	82.408		
11,800.0	11,386.0	9,105.3	8,634.0	40.9	34.2	-13.29	-422.7	799.1	2,829.1	2,794.3	34.81	81.281		
11,900.0	11,386.0	9,205.4	8,634.0	41.3	34.6	-13.42	-522.5	799.9	2,830.4	2,794.9	35.51	79.709		
12,009.9	11,386.0	9,304.4	8,634.0	41.7	35.0	-13.47	-632.3	800.8	2,830.9	2,794.6	36.26	78.078		
12,100.0	11,386.0	9,405.5	8,634.0	42.1	35.6	-13.47	-722.5	801.6	2,830.9	2,793.9	37.00	76.518		
12,200.0	11,386.0	9,494.5	8,634.0	42.6	36.1	-13.47	-822.5	802.4	2,830.9	2,793.1	37.76	74.964		
12,300.0	11,386.0	9,605.5	8,634.0	43.2	36.8	-13.47	-922.5	803.2	2,830.9	2,792.2	38.70	73.151		
12,400.0	11,386.0	9,705.5	8,634.0	43.8	37.6	-13.47	-1,022.5	804.1	2,830.9	2,791.3	39.63	71.428		
12,500.0	11,386.0	9,805.5	8,634.0	44.5	38.4	-13.47	-1,122.5	804.9	2,830.9	2,790.3	40.62	69.699		
12,600.0	11,386.0	9,905.5	8,634.0	45.2	39.2	-13.47	-1,222.4	805.7	2,830.9	2,789.3	41.64	67.977		
12,700.0	11,386.0	10,005.5	8,634.0	46.0	40.1	-13.47	-1,322.4	806.5	2,830.9	2,788.2	42.72	66.271		
12,800.0	11,386.0	10,105.5	8,634.0	46.8	41.1	-13.47	-1,422.4	807.4	2,830.9	2,787.1	43.83	64.591		
12,900.0	11,386.0	10,194.5	8,634.0	47.7	42.0	-13.47	-1,522.4	808.2	2,830.9	2,786.0	44.91	63.042		
13,000.0	11,386.0	10,305.5	8,634.0	48.6	43.1	-13.47	-1,622.4	809.0	2,830.9	2,784.7	46.16	61.329		
13,100.0	11,386.0	10,405.5	8,634.0	49.5	44.2	-13.47	-1,722.4	809.8	2,830.9	2,783.5	47.37	59.758		
13,200.0	11,386.0	10,505.5	8,634.0	50.5	45.3	-13.47	-1,822.4	810.7	2,830.9	2,782.3	48.62	58.230		
13,300.0	11,386.0	10,605.5	8,634.0	51.5	46.4	-13.47	-1,922.4	811.5	2,830.9	2,781.0	49.89	56.747		
13,400.0	11,386.0	10,705.5	8,634.0	52.6	47.6	-13.47	-2,022.4	812.3	2,830.9	2,779.7	51.18	55.311		
13,500.0	11,386.0	10,805.5	8,634.0	53.6	48.8	-13.47	-2,122.4	813.1	2,830.9	2,778.4	52.50	53.922		
13,600.0	11,386.0	10,894.5	8,634.0	54.7	49.9	-13.47	-2,222.4	814.0	2,830.9	2,777.1	53.76	52.657		
13,700.0	11,386.0	11,005.5	8,634.0	55.9	51.3	-13.47	-2,322.4	814.8	2,830.9	2,775.7	55.20	51.284		
13,800.0	11,386.0	11,105.5	8,634.0	57.0	52.5	-13.47	-2,422.4	815.6	2,830.9	2,774.3	56.58	50.034		
13,900.0	11,386.0	11,205.5	8,634.0	58.2	53.8	-13.47	-2,522.4	816.4	2,830.9	2,772.9	57.98	48.828		
14,000.0	11,386.0	11,305.5	8,634.0	59.4	55.1	-13.47	-2,622.4	817.3	2,830.9	2,771.5	59.39	47.667		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #108H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,100.0	11,386.0	11,405.5	8,634.0	60.6	56.5	-13.47	-2,722.4	818.1	2,830.9	2,770.1	60.82	46.548		
14,200.0	11,386.0	11,505.5	8,634.0	61.9	57.8	-13.47	-2,822.4	818.9	2,830.9	2,768.7	62.26	45.470		
14,300.0	11,386.0	11,605.5	8,634.0	63.1	59.2	-13.47	-2,922.4	819.7	2,830.9	2,767.2	63.71	44.432		
14,400.0	11,386.0	11,705.5	8,634.0	64.4	60.6	-13.47	-3,022.4	820.6	2,830.9	2,765.7	65.18	43.432		
14,500.0	11,386.0	11,805.5	8,634.0	65.7	61.9	-13.47	-3,122.4	821.4	2,830.9	2,764.3	66.66	42.468		
14,600.0	11,386.0	11,905.5	8,634.0	67.0	63.3	-13.47	-3,222.4	822.2	2,830.9	2,762.8	68.15	41.540		
14,700.0	11,386.0	12,005.5	8,634.0	68.4	64.8	-13.47	-3,322.4	823.0	2,830.9	2,761.3	69.65	40.646		
14,800.0	11,386.0	12,105.5	8,634.0	69.7	66.2	-13.47	-3,422.4	823.9	2,830.9	2,759.8	71.16	39.784		
14,900.0	11,386.0	12,194.5	8,634.0	71.1	67.5	-13.47	-3,522.4	824.7	2,830.9	2,758.3	72.59	39.000		
15,000.0	11,386.0	12,305.5	8,634.0	72.4	69.1	-13.47	-3,622.4	825.5	2,830.9	2,756.7	74.20	38.152		
15,100.0	11,386.0	12,405.5	8,634.0	73.8	70.5	-13.47	-3,722.4	826.3	2,830.9	2,755.2	75.73	37.380		
15,200.0	11,386.0	12,505.5	8,634.0	75.2	72.0	-13.47	-3,822.4	827.2	2,830.9	2,753.6	77.28	36.634		
15,300.0	11,386.0	12,605.5	8,634.0	76.6	73.4	-13.47	-3,922.4	828.0	2,830.9	2,752.1	78.82	35.915		
15,400.0	11,386.0	12,705.5	8,634.0	78.0	74.9	-13.47	-4,022.4	828.8	2,830.9	2,750.5	80.38	35.220		
15,500.0	11,386.0	12,805.5	8,634.0	79.4	76.4	-13.47	-4,122.4	829.6	2,830.9	2,749.0	81.94	34.549		
15,600.0	11,386.0	12,905.5	8,634.0	80.9	77.9	-13.47	-4,222.3	830.5	2,830.9	2,747.4	83.51	33.901		
15,700.0	11,386.0	13,005.5	8,634.0	82.3	79.4	-13.47	-4,322.3	831.3	2,830.9	2,745.8	85.08	33.275		
15,800.0	11,386.0	13,105.5	8,634.0	83.7	80.9	-13.47	-4,422.3	832.1	2,830.9	2,744.3	86.65	32.669		
15,900.0	11,386.0	13,205.5	8,634.0	85.2	82.4	-13.47	-4,522.3	832.9	2,830.9	2,742.7	88.24	32.083		
16,000.0	11,386.0	13,305.5	8,634.0	86.7	83.9	-13.47	-4,622.3	833.8	2,830.9	2,741.1	89.82	31.516		
16,100.0	11,386.0	13,405.5	8,634.0	88.1	85.4	-13.47	-4,722.3	834.6	2,830.9	2,739.5	91.42	30.968		
16,200.0	11,386.0	13,505.5	8,634.0	89.6	87.0	-13.48	-4,822.3	835.4	2,830.9	2,737.9	93.01	30.436		
16,300.0	11,386.0	13,605.5	8,634.0	91.1	88.5	-13.48	-4,922.3	836.2	2,830.9	2,736.3	94.61	29.922		
16,400.0	11,386.0	13,705.5	8,634.0	92.6	90.0	-13.48	-5,022.3	837.1	2,830.9	2,734.7	96.21	29.423		
16,500.0	11,386.0	13,805.5	8,634.0	94.0	91.6	-13.48	-5,122.3	837.9	2,830.9	2,733.1	97.82	28.940		
16,600.0	11,386.0	13,905.5	8,634.0	95.5	93.1	-13.48	-5,222.3	838.7	2,830.9	2,731.5	99.43	28.471		
16,700.0	11,386.0	14,005.5	8,634.0	97.0	94.6	-13.48	-5,322.3	839.5	2,830.9	2,729.9	101.05	28.016		
16,800.0	11,386.0	14,105.5	8,634.0	98.5	96.2	-13.48	-5,422.3	840.4	2,830.9	2,728.3	102.66	27.575		
16,900.0	11,386.0	14,205.5	8,634.0	100.1	97.7	-13.48	-5,522.3	841.2	2,830.9	2,726.7	104.28	27.147		
17,000.0	11,386.0	14,305.5	8,634.0	101.6	99.3	-13.48	-5,622.3	842.0	2,830.9	2,725.0	105.90	26.731		
17,100.0	11,386.0	14,405.5	8,634.0	103.1	100.9	-13.48	-5,722.3	842.8	2,830.9	2,723.4	107.53	26.327		
17,200.0	11,386.0	14,505.5	8,634.0	104.6	102.4	-13.48	-5,822.3	843.7	2,830.9	2,721.8	109.16	25.934		
17,300.0	11,386.0	14,605.5	8,634.0	106.1	104.0	-13.48	-5,922.3	844.5	2,830.9	2,720.2	110.79	25.553		
17,400.0	11,386.0	14,705.5	8,634.0	107.7	105.5	-13.48	-6,022.3	845.3	2,830.9	2,718.5	112.42	25.181		
17,500.0	11,386.0	14,805.5	8,634.0	109.2	107.1	-13.48	-6,122.3	846.1	2,830.9	2,716.9	114.06	24.820		
17,600.0	11,386.0	14,905.5	8,634.0	110.7	108.7	-13.48	-6,222.3	847.0	2,830.9	2,715.2	115.69	24.469		
17,700.0	11,386.0	15,005.5	8,634.0	112.3	110.3	-13.48	-6,322.3	847.8	2,830.9	2,713.6	117.33	24.127		
17,800.0	11,386.0	15,105.5	8,634.0	113.8	111.8	-13.48	-6,422.3	848.6	2,830.9	2,712.0	118.97	23.794		
17,900.0	11,386.0	15,205.5	8,634.0	115.4	113.4	-13.48	-6,522.3	849.4	2,830.9	2,710.3	120.62	23.470		
18,000.0	11,386.0	15,305.5	8,634.0	116.9	115.0	-13.48	-6,622.3	850.3	2,830.9	2,708.7	122.26	23.154		
18,100.0	11,386.0	15,405.5	8,634.0	118.5	116.6	-13.48	-6,722.3	851.1	2,830.9	2,707.0	123.91	22.847		
18,200.0	11,386.0	15,505.5	8,634.0	120.0	118.2	-13.48	-6,822.3	851.9	2,830.9	2,705.4	125.56	22.547		
18,300.0	11,386.0	15,605.5	8,634.0	121.6	119.8	-13.48	-6,922.3	852.7	2,830.9	2,703.7	127.21	22.254		
18,400.0	11,386.0	15,694.5	8,634.0	123.2	121.2	-13.48	-7,022.3	853.6	2,831.0	2,702.2	128.77	21.985		
18,500.0	11,386.0	15,805.5	8,634.0	124.7	122.9	-13.48	-7,122.2	854.4	2,831.0	2,700.4	130.51	21.691		
18,600.0	11,386.0	15,905.5	8,634.0	126.3	124.5	-13.48	-7,222.2	855.2	2,831.0	2,698.8	132.17	21.419		
18,700.0	11,386.0	16,005.5	8,634.0	127.9	126.1	-13.48	-7,322.2	856.0	2,831.0	2,697.1	133.83	21.154		
18,800.0	11,386.0	16,105.5	8,634.0	129.4	127.7	-13.48	-7,422.2	856.9	2,831.0	2,695.5	135.48	20.895		
18,900.0	11,386.0	16,205.5	8,634.0	131.0	129.3	-13.48	-7,522.2	857.7	2,831.0	2,693.8	137.14	20.642		
19,000.0	11,386.0	16,305.5	8,634.0	132.6	130.9	-13.48	-7,622.2	858.5	2,831.0	2,692.2	138.80	20.396		
19,100.0	11,386.0	16,405.5	8,634.0	134.1	132.5	-13.48	-7,722.2	859.3	2,831.0	2,690.5	140.46	20.154		
19,200.0	11,386.0	16,505.5	8,634.0	135.7	134.1	-13.48	-7,822.2	860.2	2,831.0	2,688.8	142.13	19.919		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #108H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,300.0	11,386.0	16,605.5	8,634.0	137.3	135.7	-13.48	-7,922.2	861.0	2,831.0	2,687.2	143.79	19.688		
19,400.0	11,386.0	16,705.5	8,634.0	138.9	137.3	-13.48	-8,022.2	861.8	2,831.0	2,685.5	145.45	19.463		
19,500.0	11,386.0	16,805.5	8,634.0	140.5	138.9	-13.48	-8,122.2	862.6	2,831.0	2,683.8	147.12	19.242		
19,600.0	11,386.0	16,905.5	8,634.0	142.0	140.5	-13.48	-8,222.2	863.5	2,831.0	2,682.2	148.79	19.027		
19,700.0	11,386.0	17,005.5	8,634.0	143.6	142.1	-13.48	-8,322.2	864.3	2,831.0	2,680.5	150.46	18.816		
19,800.0	11,386.0	17,105.5	8,634.0	145.2	143.7	-13.48	-8,422.2	865.1	2,831.0	2,678.8	152.12	18.610		
19,900.0	11,386.0	17,205.5	8,634.0	146.8	145.3	-13.48	-8,522.2	865.9	2,831.0	2,677.2	153.79	18.408		
20,000.0	11,386.0	17,305.5	8,634.0	148.4	146.9	-13.48	-8,622.2	866.8	2,831.0	2,675.5	155.46	18.210		
20,100.0	11,386.0	17,405.5	8,634.0	150.0	148.6	-13.48	-8,722.2	867.6	2,831.0	2,673.8	157.14	18.016		
20,200.0	11,386.0	17,505.5	8,634.0	151.6	150.2	-13.48	-8,822.2	868.4	2,831.0	2,672.2	158.81	17.826		
20,300.0	11,386.0	17,605.5	8,634.0	153.2	151.8	-13.48	-8,922.2	869.2	2,831.0	2,670.5	160.48	17.641		
20,400.0	11,386.0	17,705.5	8,634.0	154.8	153.4	-13.48	-9,022.2	870.1	2,831.0	2,668.8	162.15	17.458		
20,500.0	11,386.0	17,805.5	8,634.0	156.4	155.0	-13.48	-9,122.2	870.9	2,831.0	2,667.1	163.83	17.280		
20,600.0	11,386.0	17,905.5	8,634.0	158.0	156.6	-13.48	-9,222.2	871.7	2,831.0	2,665.5	165.50	17.105		
20,700.0	11,386.0	18,005.5	8,634.0	159.6	158.2	-13.48	-9,322.2	872.5	2,831.0	2,663.8	167.18	16.934		
20,800.0	11,386.0	18,105.5	8,634.0	161.2	159.9	-13.48	-9,422.2	873.4	2,831.0	2,662.1	168.86	16.765		
20,900.0	11,386.0	18,205.5	8,634.0	162.8	161.5	-13.48	-9,522.2	874.2	2,831.0	2,660.4	170.54	16.601		
21,000.0	11,386.0	18,305.5	8,634.0	164.4	163.1	-13.48	-9,622.2	875.0	2,831.0	2,658.8	172.21	16.439		
21,100.0	11,386.0	18,405.5	8,634.0	166.0	164.7	-13.48	-9,722.2	875.8	2,831.0	2,657.1	173.89	16.280		
21,200.0	11,386.0	18,505.5	8,634.0	167.6	166.3	-13.48	-9,822.2	876.7	2,831.0	2,655.4	175.57	16.124		
21,300.0	11,386.0	18,605.5	8,634.0	169.2	167.9	-13.48	-9,922.2	877.5	2,831.0	2,653.7	177.25	15.972		
21,400.0	11,386.0	18,705.5	8,634.0	170.8	169.6	-13.48	-10,022.1	878.3	2,831.0	2,652.0	178.93	15.822		
21,500.0	11,386.0	18,805.5	8,634.0	172.4	171.2	-13.48	-10,122.1	879.1	2,831.0	2,650.4	180.61	15.674		
21,600.0	11,386.0	18,905.5	8,634.0	174.0	172.8	-13.48	-10,222.1	880.0	2,831.0	2,648.7	182.29	15.530		
21,700.0	11,386.0	19,005.5	8,634.0	175.6	174.4	-13.48	-10,322.1	880.8	2,831.0	2,647.0	183.98	15.388		
21,800.0	11,386.0	19,105.5	8,634.0	177.2	176.0	-13.48	-10,422.1	881.6	2,831.0	2,645.3	185.66	15.248		
21,900.0	11,386.0	19,205.5	8,634.0	178.8	177.7	-13.48	-10,522.1	882.4	2,831.0	2,643.6	187.34	15.111		
22,000.0	11,386.0	19,305.5	8,634.0	180.4	179.3	-13.48	-10,622.1	883.3	2,831.0	2,642.0	189.03	14.977		
22,100.0	11,386.0	19,405.5	8,634.0	182.0	180.9	-13.48	-10,722.1	884.1	2,831.0	2,640.3	190.71	14.844		
22,200.0	11,386.0	19,505.5	8,634.0	183.7	182.5	-13.48	-10,822.1	884.9	2,831.0	2,638.6	192.40	14.714		
22,300.0	11,386.0	19,605.5	8,634.0	185.3	184.2	-13.48	-10,922.1	885.8	2,831.0	2,636.9	194.08	14.587		
22,400.0	11,386.0	19,705.5	8,634.0	186.9	185.8	-13.48	-11,022.1	886.6	2,831.0	2,635.2	195.77	14.461		
22,500.0	11,386.0	19,805.5	8,634.0	188.5	187.4	-13.48	-11,122.1	887.4	2,831.0	2,633.5	197.45	14.338		
22,600.0	11,386.0	19,905.5	8,634.0	190.1	189.0	-13.48	-11,222.1	888.2	2,831.0	2,631.8	199.14	14.216		
22,700.0	11,386.0	20,005.5	8,634.0	191.7	190.7	-13.48	-11,322.1	889.1	2,831.0	2,630.2	200.83	14.097		
22,800.0	11,386.0	20,105.5	8,634.0	193.3	192.3	-13.48	-11,422.1	889.9	2,831.0	2,628.5	202.51	13.979		
22,900.0	11,386.0	20,205.5	8,634.0	195.0	193.9	-13.48	-11,522.1	890.7	2,831.0	2,626.8	204.20	13.864		
23,000.0	11,386.0	20,305.5	8,634.0	196.6	195.6	-13.48	-11,622.1	891.5	2,831.0	2,625.1	205.89	13.750		
23,100.0	11,386.0	20,405.5	8,634.0	198.2	197.2	-13.48	-11,722.1	892.4	2,831.0	2,623.4	207.58	13.638		
23,200.0	11,386.0	20,505.5	8,634.0	199.8	198.8	-13.48	-11,822.1	893.2	2,831.0	2,621.7	209.27	13.528		
23,300.0	11,386.0	20,605.5	8,634.0	201.4	200.4	-13.48	-11,922.1	894.0	2,831.0	2,620.0	210.96	13.420		
23,400.0	11,386.0	20,705.5	8,634.0	203.0	202.1	-13.48	-12,022.1	894.8	2,831.0	2,618.4	212.64	13.313		
23,500.0	11,386.0	20,805.5	8,634.0	204.7	203.7	-13.48	-12,122.1	895.7	2,831.0	2,616.7	214.33	13.208		
23,600.0	11,386.0	20,905.5	8,634.0	206.3	205.3	-13.48	-12,222.1	896.5	2,831.0	2,615.0	216.02	13.105		
23,705.7	11,386.0	21,000.2	8,634.0	208.0	206.9	-13.48	-12,327.8	897.4	2,831.0	2,613.3	217.72	13.003		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #114H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis		Distance								
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
0.0	0.0	0.0	0.0	0.0	0.0	-99.37	-31.3	-189.8	192.4					
100.0	100.0	100.0	100.0	0.1	0.1	-99.37	-31.3	-189.8	192.4	192.2	0.26	750.703		
200.0	200.0	200.0	200.0	0.5	0.5	-99.37	-31.3	-189.8	192.4	191.4	0.97	197.699		
300.0	300.0	300.0	300.0	0.8	0.8	-99.37	-31.3	-189.8	192.4	190.7	1.69	113.839		
400.0	400.0	400.0	400.0	1.2	1.2	-99.37	-31.3	-189.8	192.4	190.0	2.41	79.933		
500.0	500.0	500.0	500.0	1.6	1.6	-99.37	-31.3	-189.8	192.4	189.3	3.12	61.590 CC		
600.0	600.0	600.0	600.0	1.9	1.9	-143.47	-31.3	-189.8	193.1	189.3	3.84	50.307		
700.0	700.0	700.0	700.0	2.3	2.3	-143.91	-31.3	-189.8	195.2	190.7	4.55	42.882		
800.0	799.9	800.1	799.9	2.6	2.6	-144.63	-31.3	-189.8	198.8	193.5	5.27	37.731		
900.0	899.7	900.3	899.7	3.0	3.0	-145.60	-31.3	-189.8	203.8	197.8	5.99	34.046		
1,000.0	999.4	1,000.6	999.4	3.4	3.4	-146.77	-31.3	-189.8	210.3	203.6	6.70	31.367		
1,100.0	1,098.9	1,101.1	1,098.9	3.7	3.7	-148.10	-31.3	-189.8	218.4	211.0	7.43	29.408		
1,200.0	1,198.3	1,201.7	1,198.3	4.1	4.1	-149.55	-31.3	-189.8	228.1	219.9	8.15	27.986		
1,300.0	1,297.4	1,302.6	1,297.4	4.5	4.4	-151.08	-31.3	-189.8	239.5	230.6	8.88	26.975		
1,400.0	1,396.4	1,403.6	1,396.4	4.9	4.8	-152.61	-31.3	-189.8	251.8	242.1	9.60	26.212		
1,500.0	1,495.5	1,495.5	1,495.5	5.3	5.1	-153.99	-31.3	-189.8	264.2	253.9	10.30	25.654		
1,600.0	1,594.5	1,598.2	1,598.2	5.7	5.5	-155.19	-30.6	-189.4	276.2	265.1	11.03	25.028		
1,700.0	1,693.5	1,701.7	1,701.6	6.1	5.9	-156.08	-28.3	-188.0	286.8	275.0	11.77	24.364		
1,800.0	1,792.5	1,805.4	1,805.3	6.5	6.2	-156.68	-24.3	-185.6	296.0	283.5	12.51	23.664		
1,900.0	1,891.6	1,909.5	1,909.2	6.9	6.6	-157.04	-18.8	-182.3	303.8	290.5	13.25	22.931		
2,000.0	1,990.6	2,013.9	2,013.2	7.3	7.0	-157.19	-11.6	-177.9	310.1	296.1	13.99	22.170		
2,100.0	2,089.6	2,118.4	2,117.2	7.7	7.4	-157.12	-2.8	-172.6	314.9	300.2	14.73	21.383		
2,200.0	2,188.6	2,223.0	2,221.1	8.1	7.7	-156.86	7.7	-166.3	318.3	302.8	15.47	20.575		
2,300.0	2,287.7	2,326.4	2,323.6	8.5	8.1	-156.41	19.6	-159.1	320.2	304.0	16.21	19.752		
2,400.0	2,386.7	2,426.4	2,422.6	8.9	8.5	-155.93	31.5	-151.9	321.8	304.9	16.96	18.978		
2,500.0	2,485.7	2,526.3	2,521.5	9.3	8.9	-155.46	43.4	-144.7	323.4	305.7	17.70	18.268		
2,600.0	2,584.8	2,626.3	2,620.5	9.8	9.3	-154.99	55.3	-137.6	325.0	306.6	18.45	17.613		
2,700.0	2,683.8	2,726.2	2,719.5	10.2	9.7	-154.52	67.2	-130.4	326.6	307.4	19.20	17.009		
2,739.3	2,722.7	2,765.5	2,758.4	10.3	9.8	-154.34	71.9	-127.5	327.3	307.8	19.50	16.783		
2,800.0	2,782.9	2,826.2	2,818.5	10.6	10.0	-154.03	79.1	-123.2	327.9	307.9	19.96	16.427		
2,900.0	2,882.3	2,926.1	2,917.4	11.0	10.4	-153.34	91.0	-116.0	326.9	306.2	20.71	15.786		
3,000.0	2,981.9	3,025.9	3,016.3	11.4	10.8	-152.42	102.9	-108.8	323.7	302.3	21.46	15.083		
3,100.0	3,081.7	3,125.6	3,114.9	11.7	11.2	-151.24	114.8	-101.6	318.3	296.1	22.21	14.330		
3,200.0	3,181.7	3,225.0	3,213.4	12.1	11.6	-149.77	126.6	-94.5	310.8	287.8	22.96	13.533		
3,272.6	3,254.3	3,303.0	3,284.7	12.3	11.9	-104.53	135.2	-89.3	304.0	280.5	23.53	12.921		
3,300.0	3,281.7	3,324.1	3,311.5	12.4	12.0	-104.03	138.4	-87.4	301.3	277.6	23.71	12.707		
3,400.0	3,381.7	3,423.1	3,409.6	12.7	12.4	-102.11	150.2	-80.2	291.6	267.1	24.46	11.918		
3,500.0	3,481.7	3,522.2	3,507.7	13.1	12.8	-100.06	162.0	-73.1	282.2	256.9	25.22	11.188		
3,600.0	3,581.7	3,621.2	3,605.7	13.4	13.2	-97.88	173.8	-66.0	273.2	247.2	25.98	10.513		
3,700.0	3,681.7	3,718.1	3,701.7	13.7	13.6	-95.66	185.1	-59.2	264.8	238.0	26.75	9.900		
3,800.0	3,781.7	3,813.6	3,796.6	14.1	14.0	-93.73	194.4	-53.6	258.1	230.6	27.49	9.387		
3,900.0	3,881.7	3,909.6	3,892.2	14.4	14.3	-92.14	201.7	-49.2	253.1	224.9	28.23	8.967		
4,000.0	3,981.7	4,006.0	3,988.4	14.7	14.7	-90.97	206.9	-46.0	249.7	220.7	28.94	8.627		
4,100.0	4,081.7	4,102.6	4,085.0	15.1	15.0	-90.25	210.1	-44.1	247.7	218.0	29.64	8.357		
4,200.0	4,181.7	4,201.6	4,181.7	15.4	15.4	-90.00	211.1	-43.5	247.0	216.7	30.32	8.147		
4,300.0	4,281.7	4,300.7	4,281.7	15.8	15.7	-90.00	211.1	-43.5	247.0	216.0	31.01	7.966		
4,400.0	4,381.7	4,400.7	4,381.7	16.1	16.1	-90.00	211.1	-43.5	247.0	215.3	31.70	7.793		
4,500.0	4,481.7	4,500.7	4,481.7	16.4	16.4	-90.00	211.1	-43.5	247.0	214.6	32.39	7.626		
4,600.0	4,581.7	4,600.7	4,581.7	16.8	16.7	-90.00	211.1	-43.5	247.0	213.9	33.08	7.466		
4,700.0	4,681.7	4,700.7	4,681.7	17.1	17.1	-90.00	211.1	-43.5	247.0	213.2	33.78	7.313		
4,800.0	4,781.7	4,800.7	4,781.7	17.5	17.4	-90.00	211.1	-43.5	247.0	212.5	34.47	7.165		
4,900.0	4,881.7	4,900.7	4,881.7	17.8	17.8	-90.00	211.1	-43.5	247.0	211.8	35.17	7.024		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #114H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,000.0	4,981.7	5,000.7	4,981.7	18.2	18.1	-90.00	211.1	-43.5	247.0	211.1	35.87	6.887		
5,100.0	5,081.7	5,100.7	5,081.7	18.5	18.5	-90.00	211.1	-43.5	247.0	210.4	36.56	6.756		
5,200.0	5,181.7	5,200.7	5,181.7	18.8	18.8	-90.00	211.1	-43.5	247.0	209.7	37.26	6.629		
5,300.0	5,281.7	5,300.7	5,281.7	19.2	19.2	-90.00	211.1	-43.5	247.0	209.0	37.96	6.507		
5,400.0	5,381.7	5,400.7	5,381.7	19.5	19.5	-90.00	211.1	-43.5	247.0	208.3	38.66	6.389		
5,500.0	5,481.7	5,500.7	5,481.7	19.9	19.9	-90.00	211.1	-43.5	247.0	207.6	39.36	6.275		
5,600.0	5,581.7	5,600.7	5,581.7	20.2	20.2	-90.00	211.1	-43.5	247.0	206.9	40.06	6.166		
5,700.0	5,681.7	5,700.7	5,681.7	20.6	20.6	-90.00	211.1	-43.5	247.0	206.2	40.76	6.060		
5,800.0	5,781.7	5,800.7	5,781.7	20.9	20.9	-90.00	211.1	-43.5	247.0	205.5	41.46	5.957		
5,900.0	5,881.7	5,900.7	5,881.7	21.3	21.3	-90.00	211.1	-43.5	247.0	204.8	42.17	5.858		
6,000.0	5,981.7	6,000.7	5,981.7	21.6	21.6	-90.00	211.1	-43.5	247.0	204.1	42.87	5.762		
6,100.0	6,081.7	6,100.7	6,081.7	22.0	22.0	-90.00	211.1	-43.5	247.0	203.4	43.57	5.669		
6,200.0	6,181.7	6,200.7	6,181.7	22.3	22.3	-90.00	211.1	-43.5	247.0	202.7	44.28	5.579		
6,300.0	6,281.7	6,300.7	6,281.7	22.7	22.7	-90.00	211.1	-43.5	247.0	202.0	44.98	5.491		
6,400.0	6,381.7	6,400.7	6,381.7	23.0	23.0	-90.00	211.1	-43.5	247.0	201.3	45.69	5.406		
6,500.0	6,481.7	6,500.7	6,481.7	23.4	23.4	-90.00	211.1	-43.5	247.0	200.6	46.39	5.324		
6,600.0	6,581.7	6,600.7	6,581.7	23.7	23.7	-90.00	211.1	-43.5	247.0	199.9	47.10	5.245		
6,700.0	6,681.7	6,700.7	6,681.7	24.1	24.1	-90.00	211.1	-43.5	247.0	199.2	47.80	5.167		
6,800.0	6,781.7	6,800.7	6,781.7	24.4	24.4	-90.00	211.1	-43.5	247.0	198.5	48.51	5.092		
6,900.0	6,881.7	6,900.7	6,881.7	24.8	24.8	-90.00	211.1	-43.5	247.0	197.8	49.22	5.019		
7,000.0	6,981.7	7,000.7	6,981.7	25.1	25.1	-90.00	211.1	-43.5	247.0	197.1	49.92	4.948		
7,100.0	7,081.7	7,100.7	7,081.7	25.5	25.5	-90.00	211.1	-43.5	247.0	196.4	50.63	4.879		
7,200.0	7,181.7	7,200.7	7,181.7	25.8	25.8	-90.00	211.1	-43.5	247.0	195.7	51.34	4.811		
7,300.0	7,281.7	7,300.7	7,281.7	26.2	26.2	-90.00	211.1	-43.5	247.0	195.0	52.04	4.746		
7,400.0	7,381.7	7,400.7	7,381.7	26.5	26.5	-90.00	211.1	-43.5	247.0	194.3	52.75	4.682		
7,500.0	7,481.7	7,500.7	7,481.7	26.9	26.9	-90.00	211.1	-43.5	247.0	193.5	53.46	4.620		
7,600.0	7,581.7	7,600.7	7,581.7	27.2	27.2	-90.00	211.1	-43.5	247.0	192.8	54.17	4.560		
7,700.0	7,681.7	7,700.7	7,681.7	27.6	27.6	-90.00	211.1	-43.5	247.0	192.1	54.88	4.501		
7,800.0	7,781.7	7,800.7	7,781.7	28.0	27.9	-90.00	211.1	-43.5	247.0	191.4	55.59	4.444		
7,900.0	7,881.7	7,900.7	7,881.7	28.3	28.3	-90.00	211.1	-43.5	247.0	190.7	56.29	4.388		
8,000.0	7,981.7	8,000.7	7,981.7	28.7	28.7	-90.00	211.1	-43.5	247.0	190.0	57.00	4.333		
8,100.0	8,081.7	8,100.7	8,081.7	29.0	29.0	-90.00	211.1	-43.5	247.0	189.3	57.71	4.280		
8,200.0	8,181.7	8,200.7	8,181.7	29.4	29.4	-90.00	211.1	-43.5	247.0	188.6	58.42	4.228		
8,300.0	8,281.7	8,300.7	8,281.7	29.7	29.7	-90.00	211.1	-43.5	247.0	187.9	59.13	4.177		
8,400.0	8,381.7	8,400.7	8,381.7	30.1	30.1	-90.00	211.1	-43.5	247.0	187.2	59.84	4.128		
8,500.0	8,481.7	8,500.7	8,481.7	30.4	30.4	-90.00	211.1	-43.5	247.0	186.5	60.55	4.079		
8,600.0	8,581.7	8,601.7	8,589.1	30.8	30.8	-91.73	203.7	-41.9	245.6	184.4	61.24	4.011		
8,700.0	8,681.7	8,710.0	8,688.6	31.1	31.0	-97.73	178.6	-36.4	242.2	180.4	61.82	3.918		
8,754.2	8,735.9	8,761.1	8,735.9	31.3	31.2	-102.30	159.7	-32.3	241.3	179.2	62.09	3.887 ES, SF		
8,800.0	8,781.7	8,801.3	8,771.7	31.5	31.3	-106.58	142.0	-28.4	242.2	180.0	62.21	3.893		
8,900.0	8,881.7	8,879.1	8,837.2	31.8	31.4	-116.27	101.1	-19.5	252.6	191.0	61.65	4.098		
9,000.0	8,981.7	8,943.9	8,887.0	32.2	31.5	-125.11	60.6	-10.7	278.4	219.0	59.36	4.690		
9,100.0	9,081.7	9,000.0	8,926.0	32.6	31.6	-132.72	21.3	-2.1	320.2	264.4	55.85	5.734		
9,200.0	9,181.7	9,041.7	8,952.4	32.9	31.7	-138.09	-10.3	4.8	375.6	324.1	51.52	7.290		
9,300.0	9,281.7	9,078.5	8,973.7	33.3	31.8	-142.50	-39.6	11.2	441.2	393.6	47.60	9.269		
9,400.0	9,381.7	9,109.3	8,990.0	33.6	31.9	-145.93	-65.1	16.8	514.4	470.1	44.23	11.630		
9,500.0	9,481.7	9,135.3	9,002.7	34.0	31.9	-148.63	-87.3	21.6	592.9	551.5	41.41	14.317		
9,600.0	9,581.7	9,150.0	9,009.4	34.3	32.0	-150.07	-100.1	24.4	675.6	636.9	38.70	17.460		
9,700.0	9,681.7	9,176.7	9,020.7	34.7	32.0	-152.54	-123.7	29.5	761.1	723.9	37.23	20.443		
9,800.0	9,781.7	9,200.0	9,029.6	35.0	32.1	-154.54	-144.8	34.1	849.1	813.1	36.01	23.582		
9,900.0	9,881.7	9,200.0	9,029.6	35.4	32.1	-154.54	-144.8	34.1	938.8	904.7	34.15	27.487		
10,000.0	9,981.7	9,220.6	9,036.8	35.7	32.2	-156.20	-163.6	38.2	1,029.9	996.4	33.47	30.774		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #114H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,100.0	10,081.7	9,232.0	9,040.4	36.1	32.2	-157.07	-174.1	40.5	1,122.2	1,089.5	32.66	34.362		
10,200.0	10,181.7	9,250.0	9,045.7	36.5	32.3	-158.38	-191.0	44.2	1,215.5	1,183.2	32.25	37.693		
10,300.0	10,281.7	9,250.0	9,045.7	36.8	32.3	-158.38	-191.0	44.2	1,309.4	1,277.9	31.46	41.627		
10,400.0	10,381.7	9,250.0	9,045.7	37.2	32.3	-158.38	-191.0	44.2	1,404.2	1,373.3	30.85	45.524		
10,500.0	10,481.7	9,266.8	9,050.2	37.5	32.3	-159.54	-206.8	47.6	1,499.3	1,468.5	30.77	48.731		
10,600.0	10,581.7	9,273.6	9,051.9	37.9	32.3	-159.99	-213.2	49.0	1,595.0	1,564.5	30.53	52.241		
10,700.0	10,681.7	9,279.7	9,053.4	38.2	32.4	-160.39	-219.0	50.3	1,691.1	1,660.7	30.36	55.697		
10,800.0	10,781.7	9,300.0	9,057.7	38.6	32.4	-161.66	-238.4	54.5	1,787.8	1,757.3	30.52	58.568		
10,831.3	10,813.0	9,300.0	9,057.7	38.7	32.4	-161.66	-238.4	54.5	1,818.0	1,787.6	30.46	59.679		
10,850.0	10,831.7	9,300.0	9,057.7	38.8	32.4	11.82	-238.4	54.5	1,836.0	1,805.6	30.42	60.347		
10,900.0	10,881.5	9,300.0	9,057.7	38.9	32.4	9.17	-238.4	54.5	1,883.2	1,853.0	30.28	62.193		
10,950.0	10,930.8	9,300.0	9,057.7	39.1	32.4	7.50	-238.4	54.5	1,929.1	1,899.0	30.09	64.106		
11,000.0	10,979.2	9,300.0	9,057.7	39.2	32.4	6.35	-238.4	54.5	1,973.4	1,943.5	29.87	66.065		
11,050.0	11,026.4	9,300.0	9,057.7	39.3	32.4	5.52	-238.4	54.5	2,015.8	1,986.2	29.62	68.051		
11,100.0	11,071.9	9,300.0	9,057.7	39.5	32.4	4.90	-238.4	54.5	2,056.2	2,026.9	29.36	70.043		
11,150.0	11,115.5	9,318.7	9,061.1	39.6	32.5	4.15	-256.4	58.5	2,094.0	2,064.7	29.33	71.398		
11,200.0	11,156.7	9,325.8	9,062.2	39.7	32.5	3.72	-263.2	59.9	2,129.4	2,100.3	29.12	73.117		
11,250.0	11,195.4	9,350.0	9,065.4	39.8	32.6	3.17	-286.6	65.1	2,162.5	2,133.4	29.12	74.272		
11,300.0	11,231.1	9,350.0	9,065.4	39.9	32.6	2.97	-286.6	65.1	2,192.2	2,163.4	28.81	76.080		
11,350.0	11,263.7	9,350.0	9,065.4	39.9	32.6	2.81	-286.6	65.1	2,219.1	2,190.6	28.54	77.756		
11,400.0	11,292.8	9,350.0	9,065.4	40.0	32.6	2.68	-286.6	65.1	2,243.1	2,214.8	28.30	79.264		
11,450.0	11,318.3	9,350.0	9,065.4	40.1	32.6	2.57	-286.6	65.1	2,264.1	2,236.0	28.10	80.564		
11,500.0	11,339.9	9,375.7	9,067.7	40.2	32.7	2.28	-311.7	70.5	2,281.3	2,253.2	28.13	81.109		
11,550.0	11,357.5	9,400.0	9,068.8	40.3	32.8	2.03	-335.4	75.7	2,295.7	2,267.6	28.15	81.550		
11,600.0	11,371.0	9,400.0	9,068.8	40.4	32.8	1.99	-335.4	75.7	2,306.3	2,278.2	28.07	82.173		
11,650.0	11,380.2	9,400.0	9,068.8	40.5	32.8	1.96	-335.4	75.7	2,313.6	2,285.6	28.05	82.475		
11,700.0	11,385.1	9,413.6	9,069.0	40.7	32.8	1.85	-348.7	78.6	2,317.5	2,289.4	28.15	82.340		
11,731.3	11,386.0	9,439.4	9,069.0	40.7	32.9	1.66	-373.9	84.0	2,318.1	2,289.8	28.27	81.998		
11,800.0	11,386.0	9,504.2	9,069.0	40.9	33.2	1.24	-437.4	96.5	2,317.6	2,289.0	28.59	81.076		
11,900.0	11,386.0	9,600.5	9,069.0	41.3	33.7	0.74	-532.5	112.4	2,317.2	2,288.1	29.13	79.539		
12,009.9	11,386.0	9,708.4	9,069.0	41.7	34.3	0.37	-639.4	126.5	2,317.0	2,287.2	29.83	77.670		
12,100.0	11,386.0	9,797.9	9,069.0	42.1	34.8	0.17	-728.5	135.1	2,317.0	2,286.5	30.47	76.053		
12,200.0	11,386.0	9,897.6	9,069.0	42.6	35.5	0.04	-828.0	141.3	2,317.0	2,285.8	31.23	74.196		
12,254.7	11,386.0	9,952.3	9,069.0	42.9	35.9	0.00	-882.6	143.3	2,317.0	2,285.3	31.68	73.148		
12,300.0	11,386.0	9,997.6	9,069.0	43.2	36.2	-0.01	-927.9	144.2	2,317.0	2,285.0	32.05	72.303		
12,400.0	11,386.0	10,102.4	9,069.0	43.8	37.0	-0.01	-1,027.9	145.0	2,317.0	2,284.1	32.94	70.345		
12,500.0	11,386.0	10,202.4	9,069.0	44.5	37.8	-0.01	-1,127.9	145.8	2,317.0	2,283.1	33.86	68.437		
12,600.0	11,386.0	10,302.4	9,069.0	45.2	38.7	-0.01	-1,227.9	146.6	2,317.0	2,282.2	34.82	66.541		
12,700.0	11,386.0	10,402.4	9,069.0	46.0	39.6	-0.01	-1,327.9	147.4	2,317.0	2,281.2	35.83	64.672		
12,800.0	11,386.0	10,502.4	9,069.0	46.8	40.5	-0.01	-1,427.9	148.3	2,317.0	2,280.1	36.87	62.840		
12,900.0	11,386.0	10,602.4	9,069.0	47.7	41.6	-0.01	-1,527.9	149.1	2,317.0	2,279.0	37.95	61.052		
13,000.0	11,386.0	10,702.4	9,069.0	48.6	42.6	-0.01	-1,627.9	149.9	2,317.0	2,277.9	39.06	59.314		
13,100.0	11,386.0	10,802.4	9,069.0	49.5	43.7	-0.01	-1,727.9	150.7	2,317.0	2,276.8	40.21	57.629		
13,200.0	11,386.0	10,902.4	9,069.0	50.5	44.8	-0.01	-1,827.9	151.5	2,317.0	2,275.6	41.37	56.001		
13,300.0	11,386.0	11,002.4	9,069.0	51.5	46.0	-0.01	-1,927.9	152.4	2,317.0	2,274.4	42.57	54.430		
13,400.0	11,386.0	11,102.4	9,069.0	52.6	47.1	-0.01	-2,027.9	153.2	2,317.0	2,273.2	43.79	52.917		
13,500.0	11,386.0	11,202.4	9,069.0	53.6	48.4	-0.01	-2,127.9	154.0	2,317.0	2,272.0	45.02	51.462		
13,600.0	11,386.0	11,302.4	9,069.0	54.7	49.6	-0.01	-2,227.9	154.8	2,317.0	2,270.7	46.28	50.063		
13,700.0	11,386.0	11,402.4	9,069.0	55.9	50.8	-0.01	-2,327.9	155.6	2,317.0	2,269.4	47.56	48.721		
13,800.0	11,386.0	11,502.4	9,069.0	57.0	52.1	-0.01	-2,427.8	156.4	2,317.0	2,268.2	48.85	47.432		
13,900.0	11,386.0	11,602.4	9,069.0	58.2	53.4	-0.01	-2,527.8	157.3	2,317.0	2,266.8	50.16	46.195		
14,000.0	11,386.0	11,702.4	9,069.0	59.4	54.7	-0.01	-2,627.8	158.1	2,317.0	2,265.5	51.48	45.009		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #114H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)						
14,100.0	11,386.0	11,802.4	9,069.0	60.6	56.1	-0.01	-2,727.8	158.9	2,317.0	2,264.2	52.81	43.871		
14,200.0	11,386.0	11,902.4	9,069.0	61.9	57.4	-0.01	-2,827.8	159.7	2,317.0	2,262.8	54.16	42.780		
14,300.0	11,386.0	12,002.4	9,069.0	63.1	58.8	-0.01	-2,927.8	160.5	2,317.0	2,261.5	55.52	41.733		
14,400.0	11,386.0	12,102.4	9,069.0	64.4	60.2	-0.01	-3,027.8	161.3	2,317.0	2,260.1	56.89	40.729		
14,500.0	11,386.0	12,202.4	9,069.0	65.7	61.6	-0.01	-3,127.8	162.2	2,317.0	2,258.7	58.27	39.765		
14,600.0	11,386.0	12,302.4	9,069.0	67.0	63.0	-0.01	-3,227.8	163.0	2,317.0	2,257.3	59.66	38.839		
14,700.0	11,386.0	12,402.4	9,069.0	68.4	64.4	-0.01	-3,327.8	163.8	2,317.0	2,255.9	61.05	37.951		
14,800.0	11,386.0	12,502.4	9,069.0	69.7	65.9	-0.01	-3,427.8	164.6	2,317.0	2,254.5	62.46	37.097		
14,900.0	11,386.0	12,602.4	9,069.0	71.1	67.3	-0.01	-3,527.8	165.4	2,317.0	2,253.1	63.87	36.277		
15,000.0	11,386.0	12,702.4	9,069.0	72.4	68.7	-0.01	-3,627.8	166.2	2,317.0	2,251.7	65.29	35.488		
15,100.0	11,386.0	12,802.4	9,069.0	73.8	70.2	-0.01	-3,727.8	167.1	2,317.0	2,250.3	66.72	34.729		
15,200.0	11,386.0	12,902.4	9,069.0	75.2	71.7	-0.01	-3,827.8	167.9	2,317.0	2,248.9	68.15	34.000		
15,300.0	11,386.0	13,002.4	9,069.0	76.6	73.2	-0.01	-3,927.8	168.7	2,317.0	2,247.4	69.59	33.297		
15,400.0	11,386.0	13,102.4	9,069.0	78.0	74.6	-0.01	-4,027.8	169.5	2,317.0	2,246.0	71.03	32.620		
15,500.0	11,386.0	13,202.4	9,069.0	79.4	76.1	-0.01	-4,127.8	170.3	2,317.0	2,244.5	72.48	31.968		
15,600.0	11,386.0	13,302.4	9,069.0	80.9	77.6	-0.01	-4,227.8	171.1	2,317.0	2,243.1	73.93	31.340		
15,700.0	11,386.0	13,402.4	9,069.0	82.3	79.1	-0.01	-4,327.8	172.0	2,317.0	2,241.6	75.39	30.734		
15,800.0	11,386.0	13,502.4	9,069.0	83.7	80.6	-0.01	-4,427.8	172.8	2,317.0	2,240.1	76.85	30.149		
15,900.0	11,386.0	13,602.4	9,069.0	85.2	82.1	-0.01	-4,527.8	173.6	2,317.0	2,238.7	78.32	29.584		
16,000.0	11,386.0	13,702.4	9,069.0	86.7	83.7	-0.01	-4,627.8	174.4	2,317.0	2,237.2	79.79	29.039		
16,100.0	11,386.0	13,802.4	9,069.0	88.1	85.2	-0.01	-4,727.8	175.2	2,317.0	2,235.7	81.26	28.513		
16,200.0	11,386.0	13,902.4	9,069.0	89.6	86.7	-0.01	-4,827.8	176.1	2,317.0	2,234.3	82.74	28.003		
16,300.0	11,386.0	14,002.4	9,069.0	91.1	88.3	-0.01	-4,927.8	176.9	2,317.0	2,232.8	84.22	27.511		
16,400.0	11,386.0	14,102.4	9,069.0	92.6	89.8	-0.01	-5,027.8	177.7	2,317.0	2,231.3	85.70	27.035		
16,500.0	11,386.0	14,202.4	9,069.0	94.0	91.3	-0.01	-5,127.8	178.5	2,317.0	2,229.8	87.19	26.574		
16,600.0	11,386.0	14,302.4	9,069.0	95.5	92.9	-0.01	-5,227.8	179.3	2,317.0	2,228.3	88.68	26.127		
16,700.0	11,386.0	14,402.4	9,069.0	97.0	94.4	-0.01	-5,327.7	180.1	2,317.0	2,226.8	90.17	25.695		
16,800.0	11,386.0	14,502.4	9,069.0	98.5	96.0	-0.01	-5,427.7	181.0	2,317.0	2,225.3	91.67	25.276		
16,900.0	11,386.0	14,602.4	9,069.0	100.1	97.5	-0.01	-5,527.7	181.8	2,317.0	2,223.8	93.17	24.870		
17,000.0	11,386.0	14,702.4	9,069.0	101.6	99.1	-0.01	-5,627.7	182.6	2,317.0	2,222.3	94.66	24.476		
17,100.0	11,386.0	14,802.4	9,069.0	103.1	100.7	-0.01	-5,727.7	183.4	2,317.0	2,220.8	96.17	24.094		
17,200.0	11,386.0	14,902.4	9,069.0	104.6	102.2	-0.01	-5,827.7	184.2	2,317.0	2,219.3	97.67	23.723		
17,300.0	11,386.0	15,002.4	9,069.0	106.1	103.8	-0.01	-5,927.7	185.0	2,317.0	2,217.8	99.18	23.362		
17,400.0	11,386.0	15,102.4	9,069.0	107.7	105.4	-0.01	-6,027.7	185.9	2,317.0	2,216.3	100.68	23.013		
17,500.0	11,386.0	15,202.4	9,069.0	109.2	106.9	-0.01	-6,127.7	186.7	2,317.0	2,214.8	102.19	22.673		
17,600.0	11,386.0	15,302.4	9,069.0	110.7	108.5	-0.01	-6,227.7	187.5	2,317.0	2,213.3	103.71	22.342		
17,700.0	11,386.0	15,402.4	9,069.0	112.3	110.1	-0.01	-6,327.7	188.3	2,317.0	2,211.8	105.22	22.021		
17,800.0	11,386.0	15,502.4	9,069.0	113.8	111.7	-0.01	-6,427.7	189.1	2,317.0	2,210.3	106.73	21.708		
17,900.0	11,386.0	15,602.4	9,069.0	115.4	113.3	-0.01	-6,527.7	189.9	2,317.0	2,208.8	108.25	21.404		
18,000.0	11,386.0	15,702.4	9,069.0	116.9	114.8	-0.01	-6,627.7	190.8	2,317.0	2,207.2	109.77	21.108		
18,100.0	11,386.0	15,802.4	9,069.0	118.5	116.4	-0.01	-6,727.7	191.6	2,317.0	2,205.7	111.29	20.820		
18,200.0	11,386.0	15,902.4	9,069.0	120.0	118.0	0.00	-6,827.7	192.4	2,317.0	2,204.2	112.81	20.539		
18,300.0	11,386.0	16,002.4	9,069.0	121.6	119.6	0.00	-6,927.7	193.2	2,317.0	2,202.7	114.33	20.266		
18,400.0	11,386.0	16,102.4	9,069.0	123.2	121.2	0.00	-7,027.7	194.0	2,317.0	2,201.1	115.85	20.000		
18,500.0	11,386.0	16,202.4	9,069.0	124.7	122.8	0.00	-7,127.7	194.8	2,317.0	2,199.6	117.38	19.740		
18,600.0	11,386.0	16,302.4	9,069.0	126.3	124.4	0.00	-7,227.7	195.7	2,317.0	2,198.1	118.90	19.487		
18,700.0	11,386.0	16,402.4	9,069.0	127.9	126.0	0.00	-7,327.7	196.5	2,317.0	2,196.6	120.43	19.240		
18,800.0	11,386.0	16,502.4	9,069.0	129.4	127.6	0.00	-7,427.7	197.3	2,317.0	2,195.0	121.96	18.999		
18,900.0	11,386.0	16,602.4	9,069.0	131.0	129.2	0.00	-7,527.7	198.1	2,317.0	2,193.5	123.49	18.763		
19,000.0	11,386.0	16,702.4	9,069.0	132.6	130.8	0.00	-7,627.7	198.9	2,317.0	2,192.0	125.02	18.534		
19,100.0	11,386.0	16,802.4	9,069.0	134.1	132.4	0.00	-7,727.7	199.8	2,317.0	2,190.5	126.55	18.310		
19,200.0	11,386.0	16,902.4	9,069.0	135.7	134.0	0.00	-7,827.7	200.6	2,317.0	2,188.9	128.08	18.091		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #114H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)						
19,300.0	11,386.0	17,002.4	9,069.0	137.3	135.6	0.00	-7,927.7	201.4	2,317.0	2,187.4	129.61	17.877		
19,400.0	11,386.0	17,102.4	9,069.0	138.9	137.2	0.00	-8,027.7	202.2	2,317.0	2,185.9	131.14	17.668		
19,500.0	11,386.0	17,202.4	9,069.0	140.5	138.8	0.00	-8,127.7	203.0	2,317.0	2,184.3	132.68	17.463		
19,600.0	11,386.0	17,302.4	9,069.0	142.0	140.4	0.00	-8,227.7	203.8	2,317.0	2,182.8	134.21	17.264		
19,700.0	11,386.0	17,402.4	9,069.0	143.6	142.0	0.00	-8,327.6	204.7	2,317.0	2,181.3	135.75	17.068		
19,800.0	11,386.0	17,502.4	9,069.0	145.2	143.6	0.00	-8,427.6	205.5	2,317.0	2,179.7	137.29	16.877		
19,900.0	11,386.0	17,602.4	9,069.0	146.8	145.2	0.00	-8,527.6	206.3	2,317.0	2,178.2	138.82	16.690		
20,000.0	11,386.0	17,702.4	9,069.0	148.4	146.8	0.00	-8,627.6	207.1	2,317.0	2,176.6	140.36	16.507		
20,100.0	11,386.0	17,802.4	9,069.0	150.0	148.5	0.00	-8,727.6	207.9	2,317.0	2,175.1	141.90	16.328		
20,200.0	11,386.0	17,902.4	9,069.0	151.6	150.1	0.00	-8,827.6	208.7	2,317.0	2,173.6	143.44	16.153		
20,300.0	11,386.0	18,002.4	9,069.0	153.2	151.7	0.00	-8,927.6	209.6	2,317.0	2,172.0	144.98	15.982		
20,400.0	11,386.0	18,102.4	9,069.0	154.8	153.3	0.00	-9,027.6	210.4	2,317.0	2,170.5	146.52	15.814		
20,500.0	11,386.0	18,202.4	9,069.0	156.4	154.9	0.00	-9,127.6	211.2	2,317.0	2,168.9	148.06	15.649		
20,600.0	11,386.0	18,302.4	9,069.0	158.0	156.5	0.00	-9,227.6	212.0	2,317.0	2,167.4	149.60	15.488		
20,700.0	11,386.0	18,402.4	9,069.0	159.6	158.1	0.00	-9,327.6	212.8	2,317.0	2,165.9	151.15	15.330		
20,800.0	11,386.0	18,502.4	9,069.0	161.2	159.8	0.00	-9,427.6	213.6	2,317.0	2,164.3	152.69	15.175		
20,900.0	11,386.0	18,602.4	9,069.0	162.8	161.4	0.00	-9,527.6	214.5	2,317.0	2,162.8	154.23	15.023		
21,000.0	11,386.0	18,702.4	9,069.0	164.4	163.0	0.00	-9,627.6	215.3	2,317.0	2,161.2	155.78	14.874		
21,100.0	11,386.0	18,802.4	9,069.0	166.0	164.6	0.00	-9,727.6	216.1	2,317.0	2,159.7	157.32	14.728		
21,200.0	11,386.0	18,902.4	9,069.0	167.6	166.2	0.00	-9,827.6	216.9	2,317.0	2,158.1	158.87	14.585		
21,300.0	11,386.0	19,002.4	9,069.0	169.2	167.9	0.00	-9,927.6	217.7	2,317.0	2,156.6	160.41	14.444		
21,400.0	11,386.0	19,102.4	9,069.0	170.8	169.5	0.00	-10,027.6	218.5	2,317.0	2,155.0	161.96	14.306		
21,500.0	11,386.0	19,202.4	9,069.0	172.4	171.1	0.00	-10,127.6	219.4	2,317.0	2,153.5	163.50	14.171		
21,600.0	11,386.0	19,302.4	9,069.0	174.0	172.7	0.00	-10,227.6	220.2	2,317.0	2,151.9	165.05	14.038		
21,700.0	11,386.0	19,402.4	9,069.0	175.6	174.3	0.00	-10,327.6	221.0	2,317.0	2,150.4	166.60	13.908		
21,800.0	11,386.0	19,502.4	9,069.0	177.2	176.0	0.00	-10,427.6	221.8	2,317.0	2,148.9	168.15	13.780		
21,900.0	11,386.0	19,602.4	9,069.0	178.8	177.6	0.00	-10,527.6	222.6	2,317.0	2,147.3	169.69	13.654		
22,000.0	11,386.0	19,702.4	9,069.0	180.4	179.2	0.00	-10,627.6	223.4	2,317.0	2,145.8	171.24	13.531		
22,100.0	11,386.0	19,802.4	9,069.0	182.0	180.8	0.00	-10,727.6	224.3	2,317.0	2,144.2	172.79	13.409		
22,200.0	11,386.0	19,902.4	9,069.0	183.7	182.5	0.00	-10,827.6	225.1	2,317.0	2,142.7	174.34	13.290		
22,300.0	11,386.0	20,002.4	9,069.0	185.3	184.1	0.00	-10,927.6	225.9	2,317.0	2,141.1	175.89	13.173		
22,400.0	11,386.0	20,102.4	9,069.0	186.9	185.7	0.00	-11,027.6	226.7	2,317.0	2,139.6	177.44	13.058		
22,500.0	11,386.0	20,202.4	9,069.0	188.5	187.4	0.00	-11,127.6	227.5	2,317.0	2,138.0	178.99	12.945		
22,600.0	11,386.0	20,302.4	9,069.0	190.1	189.0	0.00	-11,227.6	228.4	2,317.0	2,136.5	180.54	12.834		
22,700.0	11,386.0	20,402.4	9,069.0	191.7	190.6	0.00	-11,327.5	229.2	2,317.0	2,134.9	182.09	12.724		
22,800.0	11,386.0	20,502.4	9,069.0	193.3	192.2	0.00	-11,427.5	230.0	2,317.0	2,133.4	183.64	12.617		
22,805.6	11,386.0	20,503.1	9,069.0	193.4	192.2	0.00	-11,433.1	230.0	2,317.0	2,133.3	183.69	12.614		
22,900.0	11,386.0	20,602.4	9,069.0	195.0	193.9	0.00	-11,527.5	230.8	2,317.0	2,131.8	185.19	12.511		
23,000.0	11,386.0	20,702.4	9,069.0	196.6	195.5	0.00	-11,627.5	231.6	2,317.0	2,130.3	186.75	12.407		
23,100.0	11,386.0	20,802.4	9,069.0	198.2	197.1	0.00	-11,727.5	232.4	2,317.0	2,128.7	188.30	12.305		
23,200.0	11,386.0	20,902.4	9,069.0	199.8	198.8	0.00	-11,827.5	233.3	2,317.0	2,127.1	189.85	12.204		
23,300.0	11,386.0	21,002.4	9,069.0	201.4	200.4	0.00	-11,927.5	234.1	2,317.0	2,125.6	191.40	12.105		
23,400.0	11,386.0	21,102.4	9,069.0	203.0	202.0	0.00	-12,027.5	234.9	2,317.0	2,124.0	192.96	12.008		
23,500.0	11,386.0	21,202.4	9,069.0	204.7	203.6	0.00	-12,127.5	235.7	2,317.0	2,122.5	194.51	11.912		
23,600.0	11,386.0	21,302.4	9,069.0	206.3	205.3	0.00	-12,227.5	236.5	2,317.0	2,120.9	196.06	11.818		
23,705.7	11,386.0	21,403.3	9,069.0	208.0	206.9	0.00	-12,333.2	237.4	2,317.0	2,119.3	197.67	11.722		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #124H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	1.0	1.0	0.0	0.0	89.71	0.2	30.1	30.1					
100.0	100.0	101.0	101.0	0.1	0.1	89.71	0.2	30.1	30.1	29.8	0.26	115.667		
200.0	200.0	201.0	201.0	0.5	0.5	89.71	0.2	30.1	30.1	29.1	0.98	30.774		
300.0	300.0	301.0	301.0	0.8	0.8	89.71	0.2	30.1	30.1	28.4	1.69	17.748		
400.0	400.0	401.0	401.0	1.2	1.2	89.71	0.2	30.1	30.1	27.7	2.41	12.470		
500.0	500.0	501.0	501.0	1.6	1.6	89.71	0.2	30.1	30.1	26.9	3.13	9.611 CC		
600.0	600.0	600.5	600.5	1.9	1.9	46.29	0.5	30.9	30.3	26.4	3.84	7.891		
700.0	700.0	700.0	700.0	2.3	2.3	47.88	1.5	33.3	30.9	26.3	4.54	6.802 ES		
800.0	799.9	799.5	799.4	2.6	2.6	50.41	3.2	37.3	32.0	26.7	5.25	6.087		
900.0	899.7	899.0	898.7	3.0	3.0	53.67	5.5	42.9	33.5	27.6	5.96	5.626		
1,000.0	999.4	998.4	997.8	3.4	3.3	57.41	8.6	50.0	35.7	29.0	6.68	5.348		
1,100.0	1,098.9	1,097.8	1,096.8	3.7	3.7	61.39	12.2	58.8	38.6	31.2	7.40	5.208		
1,200.0	1,198.3	1,197.2	1,195.5	4.1	4.1	65.38	16.6	69.1	42.1	34.0	8.14	5.174		
1,300.0	1,297.4	1,296.5	1,294.0	4.5	4.5	69.20	21.6	81.0	46.4	37.5	8.89	5.221		
1,400.0	1,396.4	1,395.8	1,392.1	4.9	4.9	71.86	27.2	94.5	51.8	42.1	9.66	5.360		
1,500.0	1,495.5	1,505.1	1,489.9	5.3	5.3	72.70	33.6	109.5	58.3	47.8	10.47	5.569		
1,600.0	1,594.5	1,605.4	1,588.1	5.7	5.7	72.73	40.3	125.5	65.5	54.2	11.26	5.815		
1,700.0	1,693.5	1,694.4	1,686.4	6.1	6.1	72.76	47.0	141.4	72.6	60.6	12.01	6.048		
1,800.0	1,792.5	1,805.9	1,784.6	6.5	6.6	72.78	53.7	157.4	79.8	67.0	12.86	6.208		
1,900.0	1,891.6	1,893.9	1,882.8	6.9	7.0	72.80	60.4	173.4	87.0	73.4	13.61	6.390		
2,000.0	1,990.6	2,006.4	1,981.0	7.3	7.4	72.82	67.1	189.3	94.1	79.7	14.47	6.506		
2,100.0	2,089.6	2,106.6	2,079.3	7.7	7.9	72.83	73.8	205.3	101.3	86.0	15.28	6.629		
2,200.0	2,188.6	2,206.9	2,177.5	8.1	8.3	72.84	80.5	221.2	108.5	92.4	16.10	6.740		
2,300.0	2,287.7	2,292.8	2,275.7	8.5	8.7	72.85	87.3	237.2	115.6	98.8	16.85	6.862		
2,400.0	2,386.7	2,407.4	2,374.0	8.9	9.2	72.86	94.0	253.2	122.8	105.1	17.73	6.927		
2,500.0	2,485.7	2,507.7	2,472.2	9.3	9.6	72.87	100.7	269.1	130.0	111.4	18.55	7.007		
2,600.0	2,584.8	2,607.9	2,570.4	9.8	10.1	72.88	107.4	285.1	137.1	117.8	19.37	7.081		
2,700.0	2,683.8	2,691.8	2,668.6	10.2	10.5	72.88	114.1	301.1	144.3	124.2	20.12	7.171		
2,739.3	2,722.7	2,731.0	2,707.2	10.3	10.6	72.88	116.7	307.4	147.1	126.7	20.44	7.196		
2,800.0	2,782.9	2,791.5	2,766.9	10.6	10.9	72.78	120.8	317.0	151.6	130.7	20.94	7.242		
2,900.0	2,882.3	2,908.8	2,865.0	11.0	11.4	71.91	127.5	333.0	159.7	137.9	21.79	7.328		
3,000.0	2,981.9	3,009.3	2,962.9	11.4	11.9	70.31	134.2	348.9	168.6	146.1	22.53	7.483		
3,100.0	3,081.7	3,089.9	3,060.7	11.7	12.2	68.11	140.9	364.8	178.7	155.5	23.15	7.716		
3,200.0	3,181.7	3,188.8	3,158.1	12.1	12.7	65.47	147.6	380.6	190.0	166.2	23.82	7.979		
3,272.6	3,254.3	3,260.5	3,228.7	12.3	13.0	107.30	152.4	392.1	199.3	175.0	24.28	8.208		
3,300.0	3,281.7	3,287.4	3,255.2	12.4	13.1	106.44	154.2	396.4	203.0	178.5	24.45	8.302		
3,400.0	3,381.7	3,385.9	3,352.2	12.7	13.5	103.55	160.8	412.2	216.8	191.7	25.08	8.644		
3,500.0	3,481.7	3,484.4	3,449.2	13.1	14.0	101.01	167.5	427.9	231.1	205.4	25.72	8.984		
3,600.0	3,581.7	3,582.9	3,546.2	13.4	14.4	98.76	174.1	443.7	245.8	219.4	26.37	9.321		
3,700.0	3,681.7	3,681.3	3,643.1	13.7	14.9	96.77	180.7	459.5	260.8	233.7	27.02	9.650		
3,800.0	3,781.7	3,779.8	3,740.1	14.1	15.3	95.00	187.3	475.2	276.1	248.4	27.68	9.972		
3,900.0	3,881.7	3,882.0	3,840.8	14.4	15.8	93.39	194.1	491.3	291.3	262.9	28.39	10.260		
4,000.0	3,981.7	3,988.4	3,946.1	14.7	16.2	92.09	200.1	505.6	304.5	275.3	29.13	10.453		
4,100.0	4,081.7	4,095.6	4,052.5	15.1	16.6	91.11	205.0	517.3	315.3	285.4	29.86	10.560		
4,200.0	4,181.7	4,203.5	4,160.0	15.4	17.1	90.41	208.8	526.3	323.6	293.0	30.57	10.584		
4,300.0	4,281.7	4,311.8	4,268.1	15.8	17.4	89.95	211.4	532.5	329.3	298.0	31.27	10.532		
4,400.0	4,381.7	4,420.5	4,376.6	16.1	17.8	89.70	212.8	535.9	332.4	300.5	31.94	10.407		
4,500.0	4,481.7	4,526.5	4,482.7	16.4	18.1	89.65	213.1	536.6	333.0	300.4	32.60	10.215		
4,600.0	4,581.7	4,626.5	4,582.7	16.8	18.4	89.65	213.1	536.6	333.0	299.8	33.28	10.007		
4,700.0	4,681.7	4,726.5	4,682.7	17.1	18.8	89.65	213.1	536.6	333.0	299.1	33.96	9.806		
4,800.0	4,781.7	4,826.5	4,782.7	17.5	19.1	89.65	213.1	536.6	333.0	298.4	34.64	9.613		
4,900.0	4,881.7	4,926.5	4,882.7	17.8	19.4	89.65	213.1	536.6	333.0	297.7	35.33	9.427		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #124H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)						
5,000.0	4,981.7	5,026.5	4,982.7	18.2	19.7	89.65	213.1	536.6	333.0	297.0	36.01	9.248		
5,100.0	5,081.7	5,126.5	5,082.7	18.5	20.0	89.65	213.1	536.6	333.0	296.3	36.70	9.075		
5,200.0	5,181.7	5,226.5	5,182.7	18.8	20.3	89.65	213.1	536.6	333.0	295.7	37.39	8.908		
5,300.0	5,281.7	5,326.5	5,282.7	19.2	20.6	89.65	213.1	536.6	333.0	295.0	38.08	8.747		
5,400.0	5,381.7	5,426.5	5,382.7	19.5	21.0	89.65	213.1	536.6	333.0	294.3	38.77	8.591		
5,500.0	5,481.7	5,526.5	5,482.7	19.9	21.3	89.65	213.1	536.6	333.0	293.6	39.46	8.441		
5,600.0	5,581.7	5,626.5	5,582.7	20.2	21.6	89.65	213.1	536.6	333.0	292.9	40.15	8.295		
5,700.0	5,681.7	5,726.5	5,682.7	20.6	21.9	89.65	213.1	536.6	333.0	292.2	40.84	8.155		
5,800.0	5,781.7	5,826.5	5,782.7	20.9	22.3	89.65	213.1	536.6	333.0	291.5	41.53	8.019		
5,900.0	5,881.7	5,926.5	5,882.7	21.3	22.6	89.65	213.1	536.6	333.0	290.8	42.23	7.887		
6,000.0	5,981.7	6,026.5	5,982.7	21.6	22.9	89.65	213.1	536.6	333.0	290.1	42.92	7.759		
6,100.0	6,081.7	6,126.5	6,082.7	22.0	23.2	89.65	213.1	536.6	333.0	289.4	43.62	7.636		
6,200.0	6,181.7	6,226.5	6,182.7	22.3	23.6	89.65	213.1	536.6	333.0	288.7	44.31	7.516		
6,300.0	6,281.7	6,326.5	6,282.7	22.7	23.9	89.65	213.1	536.6	333.0	288.0	45.01	7.399		
6,400.0	6,381.7	6,426.5	6,382.7	23.0	24.2	89.65	213.1	536.6	333.0	287.3	45.71	7.286		
6,500.0	6,481.7	6,526.5	6,482.7	23.4	24.5	89.65	213.1	536.6	333.0	286.6	46.40	7.177		
6,600.0	6,581.7	6,626.5	6,582.7	23.7	24.9	89.65	213.1	536.6	333.0	285.9	47.10	7.070		
6,700.0	6,681.7	6,726.5	6,682.7	24.1	25.2	89.65	213.1	536.6	333.0	285.2	47.80	6.967		
6,800.0	6,781.7	6,826.5	6,782.7	24.4	25.5	89.65	213.1	536.6	333.0	284.5	48.50	6.866		
6,900.0	6,881.7	6,926.5	6,882.7	24.8	25.9	89.65	213.1	536.6	333.0	283.8	49.20	6.769		
7,000.0	6,981.7	7,026.5	6,982.7	25.1	26.2	89.65	213.1	536.6	333.0	283.1	49.90	6.674		
7,100.0	7,081.7	7,126.5	7,082.7	25.5	26.5	89.65	213.1	536.6	333.0	282.4	50.60	6.581		
7,200.0	7,181.7	7,226.5	7,182.7	25.8	26.9	89.65	213.1	536.6	333.0	281.7	51.30	6.491		
7,300.0	7,281.7	7,326.5	7,282.7	26.2	27.2	89.65	213.1	536.6	333.0	281.0	52.01	6.404		
7,400.0	7,381.7	7,426.5	7,382.7	26.5	27.6	89.65	213.1	536.6	333.0	280.3	52.71	6.318		
7,500.0	7,481.7	7,526.5	7,482.7	26.9	27.9	89.65	213.1	536.6	333.0	279.6	53.41	6.235		
7,600.0	7,581.7	7,626.5	7,582.7	27.2	28.2	89.65	213.1	536.6	333.0	278.9	54.11	6.154		
7,700.0	7,681.7	7,726.5	7,682.7	27.6	28.6	89.65	213.1	536.6	333.0	278.2	54.82	6.075		
7,800.0	7,781.7	7,826.5	7,782.7	28.0	28.9	89.65	213.1	536.6	333.0	277.5	55.52	5.998		
7,900.0	7,881.7	7,926.5	7,882.7	28.3	29.2	89.65	213.1	536.6	333.0	276.8	56.23	5.923		
8,000.0	7,981.7	8,026.5	7,982.7	28.7	29.6	89.65	213.1	536.6	333.0	276.1	56.93	5.850		
8,100.0	8,081.7	8,126.5	8,082.7	29.0	29.9	89.65	213.1	536.6	333.0	275.4	57.64	5.778		
8,200.0	8,181.7	8,226.5	8,182.7	29.4	30.3	89.65	213.1	536.6	333.0	274.7	58.34	5.709		
8,300.0	8,281.7	8,326.5	8,282.7	29.7	30.6	89.65	213.1	536.6	333.0	274.0	59.05	5.640		
8,400.0	8,381.7	8,426.5	8,382.7	30.1	31.0	89.65	213.1	536.6	333.0	273.3	59.75	5.574		
8,500.0	8,481.7	8,526.5	8,482.7	30.4	31.3	89.65	213.1	536.6	333.0	272.6	60.46	5.509		
8,600.0	8,581.7	8,626.5	8,582.7	30.8	31.6	89.65	213.1	536.6	333.0	271.9	61.16	5.445		
8,700.0	8,681.7	8,726.5	8,682.7	31.1	32.0	89.65	213.1	536.6	333.0	271.2	61.87	5.383		
8,800.0	8,781.7	8,826.5	8,782.7	31.5	32.3	89.65	213.1	536.6	333.0	270.5	62.58	5.322		
8,900.0	8,881.7	8,926.5	8,882.7	31.8	32.7	89.65	213.1	536.6	333.0	269.8	63.28	5.263		
9,000.0	8,981.7	9,026.5	8,982.7	32.2	33.0	89.65	213.1	536.6	333.0	269.0	63.99	5.205		
9,100.0	9,081.7	9,126.5	9,082.7	32.6	33.4	89.65	213.1	536.6	333.0	268.3	64.70	5.148		
9,200.0	9,181.7	9,226.5	9,182.7	32.9	33.7	89.65	213.1	536.6	333.0	267.6	65.40	5.092		
9,300.0	9,281.7	9,328.7	9,284.8	33.3	34.0	89.88	211.8	536.4	332.9	266.8	66.10	5.037		
9,400.0	9,381.7	9,431.8	9,386.5	33.6	34.3	92.66	195.7	534.9	331.8	265.0	66.79	4.968		
9,454.3	9,436.0	9,484.5	9,437.0	33.8	34.5	95.30	180.5	533.5	331.4	264.2	67.20	4.932		
9,500.0	9,481.7	9,526.4	9,475.9	34.0	34.6	97.96	165.2	532.1	331.8	264.3	67.55	4.913 SF		
9,600.0	9,581.7	9,609.1	9,549.0	34.3	34.7	104.54	126.8	528.5	337.5	269.4	68.08	4.957		
9,700.0	9,681.7	9,679.3	9,606.2	34.7	34.9	111.23	86.3	524.8	353.0	285.3	67.75	5.211		
9,800.0	9,781.7	9,737.9	9,649.8	35.0	34.9	117.27	47.3	521.2	381.3	315.2	66.11	5.767		
9,900.0	9,881.7	9,786.7	9,682.9	35.4	35.0	122.39	11.7	517.9	422.5	359.1	63.33	6.670		
10,000.0	9,981.7	9,827.3	9,708.0	35.7	35.0	126.58	-20.0	514.9	475.2	415.3	59.95	7.927		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #124H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,100.0	10,081.7	9,861.3	9,727.3	36.1	35.1	129.99	-47.9	512.3	537.3	480.9	56.46	9.516		
10,200.0	10,181.7	9,890.1	9,742.3	36.5	35.1	132.76	-72.4	510.1	606.8	553.6	53.21	11.404		
10,300.0	10,281.7	9,914.6	9,754.1	36.8	35.1	135.03	-93.7	508.1	682.0	631.6	50.33	13.549		
10,400.0	10,381.7	9,935.6	9,763.5	37.2	35.1	136.90	-112.5	506.4	761.5	713.6	47.85	15.913		
10,500.0	10,481.7	9,950.0	9,769.5	37.5	35.1	138.14	-125.5	505.1	844.3	798.7	45.59	18.521		
10,600.0	10,581.7	9,969.8	9,777.2	37.9	35.1	139.78	-143.6	503.5	929.8	885.8	43.97	21.147		
10,700.0	10,681.7	9,983.8	9,782.3	38.2	35.1	140.91	-156.6	502.3	1,017.4	974.9	42.49	23.945		
10,800.0	10,781.7	10,000.0	9,787.8	38.6	35.2	142.17	-171.8	500.8	1,106.7	1,065.3	41.37	26.749		
10,831.3	10,813.0	10,000.0	9,787.8	38.7	35.2	142.17	-171.8	500.8	1,135.0	1,094.0	40.92	27.734		
10,850.0	10,831.7	10,000.0	9,787.8	38.8	35.2	-40.36	-171.8	500.8	1,151.8	1,111.1	40.66	28.327		
10,900.0	10,881.5	10,000.0	9,787.8	38.9	35.2	-34.57	-171.8	500.8	1,196.0	1,156.1	39.94	29.949		
10,950.0	10,930.8	10,015.9	9,792.8	39.1	35.2	-29.46	-186.9	499.4	1,238.7	1,199.1	39.62	31.268		
11,000.0	10,979.2	10,024.3	9,795.2	39.2	35.2	-25.83	-194.8	498.7	1,279.9	1,240.9	39.06	32.766		
11,050.0	11,026.4	10,033.3	9,797.7	39.3	35.2	-22.97	-203.5	497.9	1,319.3	1,280.8	38.51	34.258		
11,100.0	11,071.9	10,050.0	9,802.0	39.5	35.2	-20.59	-219.5	496.4	1,356.7	1,318.5	38.12	35.589		
11,150.0	11,115.5	10,050.0	9,802.0	39.6	35.2	-18.92	-219.5	496.4	1,391.8	1,354.4	37.37	37.248		
11,200.0	11,156.7	10,050.0	9,802.0	39.7	35.2	-17.54	-219.5	496.4	1,424.8	1,388.2	36.66	38.870		
11,250.0	11,195.4	10,075.6	9,807.6	39.8	35.2	-16.19	-244.4	494.1	1,454.9	1,418.5	36.45	39.918		
11,300.0	11,231.1	10,100.0	9,811.9	39.9	35.3	-15.11	-268.3	491.9	1,482.9	1,446.7	36.21	40.954		
11,350.0	11,263.7	10,100.0	9,811.9	39.9	35.3	-14.38	-268.3	491.9	1,507.8	1,472.2	35.61	42.338		
11,400.0	11,292.8	10,100.0	9,811.9	40.0	35.3	-13.77	-268.3	491.9	1,530.2	1,495.1	35.11	43.582		
11,450.0	11,318.3	10,124.5	9,815.2	40.1	35.3	-13.18	-292.5	489.7	1,549.5	1,514.5	34.97	44.306		
11,500.0	11,339.9	10,150.0	9,817.6	40.2	35.4	-12.71	-317.8	487.3	1,566.1	1,531.3	34.87	44.913		
11,550.0	11,357.5	10,150.0	9,817.6	40.3	35.4	-12.41	-317.8	487.3	1,579.4	1,544.8	34.61	45.638		
11,600.0	11,371.0	10,163.6	9,818.4	40.4	35.4	-12.16	-331.3	486.1	1,589.8	1,555.3	34.55	46.018		
11,650.0	11,380.2	10,189.8	9,819.0	40.5	35.5	-11.98	-357.4	483.6	1,597.4	1,562.8	34.62	46.143		
11,700.0	11,385.1	10,191.1	9,819.0	40.7	35.5	-11.89	-358.7	483.5	1,601.4	1,566.7	34.68	46.171		
11,731.3	11,386.0	10,219.2	9,819.0	40.7	35.6	-11.87	-386.7	481.1	1,602.3	1,567.4	34.82	46.013		
11,800.0	11,386.0	10,280.8	9,819.0	40.9	35.8	-11.88	-448.1	476.7	1,602.3	1,567.2	35.15	45.582		
11,900.0	11,386.0	10,370.4	9,819.0	41.3	36.1	-11.89	-537.6	472.6	1,602.4	1,566.7	35.68	44.905		
12,009.9	11,386.0	10,469.0	9,819.0	41.7	36.6	-11.89	-636.1	471.4	1,602.4	1,566.0	36.33	44.106		
12,044.0	11,386.0	10,502.0	9,819.0	41.8	36.7	-11.89	-669.2	471.7	1,602.4	1,565.8	36.55	43.835		
12,100.0	11,386.0	10,558.0	9,819.0	42.1	37.0	-11.89	-725.2	472.1	1,602.4	1,565.4	36.94	43.375		
12,200.0	11,386.0	10,658.0	9,819.0	42.6	37.6	-11.89	-825.2	473.0	1,602.4	1,564.7	37.68	42.526		
12,300.0	11,386.0	10,758.0	9,819.0	43.2	38.3	-11.89	-925.2	473.8	1,602.4	1,563.9	38.48	41.644		
12,400.0	11,386.0	10,858.0	9,819.0	43.8	39.0	-11.89	-1,025.2	474.6	1,602.4	1,563.0	39.33	40.741		
12,500.0	11,386.0	10,958.0	9,819.0	44.5	39.8	-11.89	-1,125.2	475.4	1,602.4	1,562.1	40.23	39.825		
12,600.0	11,386.0	11,058.0	9,819.0	45.2	40.6	-11.89	-1,225.2	476.2	1,602.4	1,561.2	41.19	38.904		
12,700.0	11,386.0	11,158.0	9,819.0	46.0	41.5	-11.89	-1,325.2	477.1	1,602.4	1,560.2	42.19	37.983		
12,800.0	11,386.0	11,258.0	9,819.0	46.8	42.4	-11.89	-1,425.2	477.9	1,602.4	1,559.1	43.23	37.069		
12,900.0	11,386.0	11,358.0	9,819.0	47.7	43.3	-11.89	-1,525.2	478.7	1,602.4	1,558.1	44.31	36.166		
13,000.0	11,386.0	11,458.0	9,819.0	48.6	44.3	-11.89	-1,625.2	479.5	1,602.4	1,556.9	45.42	35.278		
13,100.0	11,386.0	11,558.0	9,819.0	49.5	45.4	-11.89	-1,725.2	480.3	1,602.4	1,555.8	46.57	34.407		
13,200.0	11,386.0	11,658.0	9,819.0	50.5	46.4	-11.89	-1,825.2	481.2	1,602.4	1,554.6	47.75	33.557		
13,300.0	11,386.0	11,758.0	9,819.0	51.5	47.5	-11.89	-1,925.2	482.0	1,602.4	1,553.4	48.96	32.728		
13,400.0	11,386.0	11,858.0	9,819.0	52.6	48.7	-11.89	-2,025.2	482.8	1,602.4	1,552.2	50.20	31.921		
13,500.0	11,386.0	11,958.0	9,819.0	53.6	49.8	-11.89	-2,125.1	483.6	1,602.4	1,550.9	51.46	31.139		
13,600.0	11,386.0	12,058.0	9,819.0	54.7	51.0	-11.89	-2,225.1	484.4	1,602.4	1,549.6	52.74	30.381		
13,700.0	11,386.0	12,158.0	9,819.0	55.9	52.3	-11.89	-2,325.1	485.3	1,602.4	1,548.3	54.05	29.646		
13,800.0	11,386.0	12,258.0	9,819.0	57.0	53.5	-11.89	-2,425.1	486.1	1,602.4	1,547.0	55.38	28.936		
13,900.0	11,386.0	12,358.0	9,819.0	58.2	54.8	-11.89	-2,525.1	486.9	1,602.4	1,545.6	56.72	28.250		
14,000.0	11,386.0	12,458.0	9,819.0	59.4	56.0	-11.89	-2,625.1	487.7	1,602.4	1,544.3	58.08	27.588		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #124H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,100.0	11,386.0	12,558.0	9,819.0	60.6	57.3	-11.89	-2,725.1	488.5	1,602.4	1,542.9	59.46	26.948		
14,200.0	11,386.0	12,658.0	9,819.0	61.9	58.7	-11.89	-2,825.1	489.4	1,602.4	1,541.5	60.85	26.331		
14,300.0	11,386.0	12,758.0	9,819.0	63.1	60.0	-11.89	-2,925.1	490.2	1,602.4	1,540.1	62.26	25.736		
14,400.0	11,386.0	12,858.0	9,819.0	64.4	61.3	-11.89	-3,025.1	491.0	1,602.4	1,538.7	63.68	25.162		
14,500.0	11,386.0	12,958.0	9,819.0	65.7	62.7	-11.89	-3,125.1	491.8	1,602.4	1,537.2	65.12	24.608		
14,600.0	11,386.0	13,058.0	9,819.0	67.0	64.1	-11.89	-3,225.1	492.7	1,602.4	1,535.8	66.56	24.074		
14,700.0	11,386.0	13,158.0	9,819.0	68.4	65.5	-11.89	-3,325.1	493.5	1,602.4	1,534.3	68.01	23.559		
14,800.0	11,386.0	13,258.0	9,819.0	69.7	66.9	-11.89	-3,425.1	494.3	1,602.4	1,532.9	69.48	23.062		
14,900.0	11,386.0	13,358.0	9,819.0	71.1	68.3	-11.89	-3,525.1	495.1	1,602.4	1,531.4	70.96	22.583		
15,000.0	11,386.0	13,458.0	9,819.0	72.4	69.7	-11.89	-3,625.1	495.9	1,602.4	1,529.9	72.44	22.120		
15,100.0	11,386.0	13,558.0	9,819.0	73.8	71.1	-11.89	-3,725.1	496.8	1,602.4	1,528.4	73.93	21.674		
15,200.0	11,386.0	13,658.0	9,819.0	75.2	72.6	-11.89	-3,825.1	497.6	1,602.4	1,526.9	75.43	21.243		
15,300.0	11,386.0	13,758.0	9,819.0	76.6	74.0	-11.89	-3,925.1	498.4	1,602.4	1,525.4	76.94	20.826		
15,400.0	11,386.0	13,858.0	9,819.0	78.0	75.5	-11.89	-4,025.1	499.2	1,602.4	1,523.9	78.45	20.424		
15,500.0	11,386.0	13,958.0	9,819.0	79.4	77.0	-11.89	-4,125.1	500.0	1,602.4	1,522.4	79.97	20.036		
15,600.0	11,386.0	14,058.0	9,819.0	80.9	78.4	-11.89	-4,225.1	500.9	1,602.4	1,520.9	81.50	19.660		
15,700.0	11,386.0	14,158.0	9,819.0	82.3	79.9	-11.89	-4,325.1	501.7	1,602.4	1,519.3	83.04	19.297		
15,800.0	11,386.0	14,258.0	9,819.0	83.7	81.4	-11.89	-4,425.1	502.5	1,602.4	1,517.8	84.57	18.946		
15,900.0	11,386.0	14,358.0	9,819.0	85.2	82.9	-11.89	-4,525.1	503.3	1,602.4	1,516.2	86.12	18.606		
16,000.0	11,386.0	14,458.0	9,819.0	86.7	84.4	-11.89	-4,625.1	504.1	1,602.4	1,514.7	87.67	18.278		
16,100.0	11,386.0	14,558.0	9,819.0	88.1	85.9	-11.89	-4,725.1	505.0	1,602.4	1,513.1	89.22	17.959		
16,200.0	11,386.0	14,658.0	9,819.0	89.6	87.4	-11.89	-4,825.1	505.8	1,602.4	1,511.6	90.78	17.651		
16,300.0	11,386.0	14,758.0	9,819.0	91.1	88.9	-11.89	-4,925.1	506.6	1,602.4	1,510.0	92.34	17.352		
16,400.0	11,386.0	14,858.0	9,819.0	92.6	90.5	-11.89	-5,025.1	507.4	1,602.4	1,508.4	93.91	17.063		
16,500.0	11,386.0	14,958.0	9,819.0	94.0	92.0	-11.89	-5,125.0	508.2	1,602.4	1,506.9	95.48	16.782		
16,600.0	11,386.0	15,058.0	9,819.0	95.5	93.5	-11.89	-5,225.0	509.1	1,602.4	1,505.3	97.05	16.510		
16,700.0	11,386.0	15,158.0	9,819.0	97.0	95.1	-11.89	-5,325.0	509.9	1,602.4	1,503.7	98.63	16.246		
16,800.0	11,386.0	15,258.0	9,819.0	98.5	96.6	-11.89	-5,425.0	510.7	1,602.4	1,502.1	100.21	15.990		
16,900.0	11,386.0	15,358.0	9,819.0	100.1	98.1	-11.89	-5,525.0	511.5	1,602.4	1,500.6	101.80	15.741		
17,000.0	11,386.0	15,458.0	9,819.0	101.6	99.7	-11.89	-5,625.0	512.3	1,602.4	1,499.0	103.38	15.499		
17,100.0	11,386.0	15,558.0	9,819.0	103.1	101.2	-11.89	-5,725.0	513.2	1,602.4	1,497.4	104.97	15.264		
17,200.0	11,386.0	15,658.0	9,819.0	104.6	102.8	-11.89	-5,825.0	514.0	1,602.4	1,495.8	106.57	15.036		
17,300.0	11,386.0	15,758.0	9,819.0	106.1	104.3	-11.89	-5,925.0	514.8	1,602.4	1,494.2	108.16	14.814		
17,400.0	11,386.0	15,858.0	9,819.0	107.7	105.9	-11.89	-6,025.0	515.6	1,602.4	1,492.6	109.76	14.599		
17,500.0	11,386.0	15,958.0	9,819.0	109.2	107.5	-11.89	-6,125.0	516.4	1,602.4	1,491.0	111.36	14.389		
17,600.0	11,386.0	16,058.0	9,819.0	110.7	109.0	-11.89	-6,225.0	517.3	1,602.4	1,489.4	112.96	14.185		
17,700.0	11,386.0	16,158.0	9,819.0	112.3	110.6	-11.89	-6,325.0	518.1	1,602.4	1,487.8	114.57	13.986		
17,800.0	11,386.0	16,258.0	9,819.0	113.8	112.2	-11.89	-6,425.0	518.9	1,602.4	1,486.2	116.18	13.792		
17,900.0	11,386.0	16,358.0	9,819.0	115.4	113.7	-11.89	-6,525.0	519.7	1,602.4	1,484.6	117.79	13.604		
18,000.0	11,386.0	16,458.0	9,819.0	116.9	115.3	-11.89	-6,625.0	520.6	1,602.4	1,483.0	119.40	13.420		
18,100.0	11,386.0	16,558.0	9,819.0	118.5	116.9	-11.89	-6,725.0	521.4	1,602.4	1,481.3	121.01	13.241		
18,200.0	11,386.0	16,658.0	9,819.0	120.0	118.5	-11.89	-6,825.0	522.2	1,602.4	1,479.7	122.63	13.067		
18,300.0	11,386.0	16,758.0	9,819.0	121.6	120.0	-11.89	-6,925.0	523.0	1,602.4	1,478.1	124.24	12.897		
18,400.0	11,386.0	16,858.0	9,819.0	123.2	121.6	-11.89	-7,025.0	523.8	1,602.4	1,476.5	125.86	12.731		
18,500.0	11,386.0	16,958.0	9,819.0	124.7	123.2	-11.89	-7,125.0	524.7	1,602.4	1,474.9	127.48	12.569		
18,600.0	11,386.0	17,058.0	9,819.0	126.3	124.8	-11.89	-7,225.0	525.5	1,602.4	1,473.2	129.10	12.411		
18,700.0	11,386.0	17,158.0	9,819.0	127.9	126.4	-11.89	-7,325.0	526.3	1,602.4	1,471.6	130.73	12.257		
18,800.0	11,386.0	17,258.0	9,819.0	129.4	128.0	-11.89	-7,425.0	527.1	1,602.4	1,470.0	132.35	12.107		
18,900.0	11,386.0	17,358.0	9,819.0	131.0	129.6	-11.89	-7,525.0	527.9	1,602.4	1,468.4	133.98	11.960		
19,000.0	11,386.0	17,458.0	9,819.0	132.6	131.1	-11.89	-7,625.0	528.8	1,602.4	1,466.7	135.60	11.816		
19,100.0	11,386.0	17,558.0	9,819.0	134.1	132.7	-11.89	-7,725.0	529.6	1,602.4	1,465.1	137.23	11.676		
19,200.0	11,386.0	17,658.0	9,819.0	135.7	134.3	-11.88	-7,825.0	530.4	1,602.3	1,463.5	138.86	11.539		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #124H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,300.0	11,386.0	17,758.0	9,819.0	137.3	135.9	-11.88	-7,925.0	531.2	1,602.3	1,461.9	140.49	11.405		
19,400.0	11,386.0	17,858.0	9,819.0	138.9	137.5	-11.88	-8,025.0	532.0	1,602.3	1,460.2	142.12	11.274		
19,500.0	11,386.0	17,958.0	9,819.0	140.5	139.1	-11.88	-8,124.9	532.9	1,602.3	1,458.6	143.76	11.146		
19,600.0	11,386.0	18,058.0	9,819.0	142.0	140.7	-11.88	-8,224.9	533.7	1,602.3	1,457.0	145.39	11.021		
19,700.0	11,386.0	18,158.0	9,819.0	143.6	142.3	-11.88	-8,324.9	534.5	1,602.3	1,455.3	147.03	10.898		
19,800.0	11,386.0	18,258.0	9,819.0	145.2	143.9	-11.88	-8,424.9	535.3	1,602.3	1,453.7	148.66	10.778		
19,900.0	11,386.0	18,358.0	9,819.0	146.8	145.5	-11.88	-8,524.9	536.1	1,602.3	1,452.0	150.30	10.661		
20,000.0	11,386.0	18,458.0	9,819.0	148.4	147.1	-11.88	-8,624.9	537.0	1,602.3	1,450.4	151.94	10.546		
20,100.0	11,386.0	18,558.0	9,819.0	150.0	148.7	-11.88	-8,724.9	537.8	1,602.3	1,448.8	153.58	10.433		
20,200.0	11,386.0	18,658.0	9,819.0	151.6	150.4	-11.88	-8,824.9	538.6	1,602.3	1,447.1	155.22	10.323		
20,300.0	11,386.0	18,758.0	9,819.0	153.2	152.0	-11.88	-8,924.9	539.4	1,602.3	1,445.5	156.86	10.215		
20,400.0	11,386.0	18,858.0	9,819.0	154.8	153.6	-11.88	-9,024.9	540.2	1,602.3	1,443.8	158.50	10.109		
20,500.0	11,386.0	18,958.0	9,819.0	156.4	155.2	-11.88	-9,124.9	541.1	1,602.3	1,442.2	160.14	10.006		
20,600.0	11,386.0	19,058.0	9,819.0	158.0	156.8	-11.88	-9,224.9	541.9	1,602.3	1,440.6	161.79	9.904		
20,700.0	11,386.0	19,158.0	9,819.0	159.6	158.4	-11.88	-9,324.9	542.7	1,602.3	1,438.9	163.43	9.804		
20,800.0	11,386.0	19,258.0	9,819.0	161.2	160.0	-11.88	-9,424.9	543.5	1,602.3	1,437.3	165.07	9.707		
20,900.0	11,386.0	19,358.0	9,819.0	162.8	161.6	-11.88	-9,524.9	544.3	1,602.3	1,435.6	166.72	9.611		
21,000.0	11,386.0	19,458.0	9,819.0	164.4	163.2	-11.88	-9,624.9	545.2	1,602.3	1,434.0	168.37	9.517		
21,100.0	11,386.0	19,558.0	9,819.0	166.0	164.9	-11.88	-9,724.9	546.0	1,602.3	1,432.3	170.01	9.425		
21,200.0	11,386.0	19,658.0	9,819.0	167.6	166.5	-11.88	-9,824.9	546.8	1,602.3	1,430.7	171.66	9.334		
21,300.0	11,386.0	19,758.0	9,819.0	169.2	168.1	-11.88	-9,924.9	547.6	1,602.3	1,429.0	173.31	9.246		
21,400.0	11,386.0	19,858.0	9,819.0	170.8	169.7	-11.88	-10,024.9	548.4	1,602.3	1,427.4	174.96	9.158		
21,500.0	11,386.0	19,958.0	9,819.0	172.4	171.3	-11.88	-10,124.9	549.3	1,602.3	1,425.7	176.61	9.073		
21,600.0	11,386.0	20,058.0	9,819.0	174.0	172.9	-11.88	-10,224.9	550.1	1,602.3	1,424.1	178.26	8.989		
21,700.0	11,386.0	20,158.0	9,819.0	175.6	174.6	-11.88	-10,324.9	550.9	1,602.3	1,422.4	179.91	8.906		
21,800.0	11,386.0	20,258.0	9,819.0	177.2	176.2	-11.88	-10,424.9	551.7	1,602.3	1,420.8	181.56	8.825		
21,900.0	11,386.0	20,358.0	9,819.0	178.8	177.8	-11.88	-10,524.9	552.6	1,602.3	1,419.1	183.21	8.746		
22,000.0	11,386.0	20,458.0	9,819.0	180.4	179.4	-11.88	-10,624.9	553.4	1,602.3	1,417.5	184.86	8.668		
22,100.0	11,386.0	20,558.0	9,819.0	182.0	181.0	-11.88	-10,724.9	554.2	1,602.3	1,415.8	186.52	8.591		
22,200.0	11,386.0	20,658.0	9,819.0	183.7	182.7	-11.88	-10,824.9	555.0	1,602.3	1,414.2	188.17	8.515		
22,300.0	11,386.0	20,758.0	9,819.0	185.3	184.3	-11.88	-10,924.9	555.8	1,602.3	1,412.5	189.82	8.441		
22,400.0	11,386.0	20,858.0	9,819.0	186.9	185.9	-11.88	-11,024.8	556.7	1,602.3	1,410.9	191.48	8.368		
22,500.0	11,386.0	20,958.0	9,819.0	188.5	187.5	-11.88	-11,124.8	557.5	1,602.3	1,409.2	193.13	8.297		
22,600.0	11,386.0	21,058.0	9,819.0	190.1	189.1	-11.88	-11,224.8	558.3	1,602.3	1,407.6	194.79	8.226		
22,700.0	11,386.0	21,158.0	9,819.0	191.7	190.8	-11.88	-11,324.8	559.1	1,602.3	1,405.9	196.44	8.157		
22,800.0	11,386.0	21,258.0	9,819.0	193.3	192.4	-11.88	-11,424.8	559.9	1,602.3	1,404.2	198.10	8.089		
22,900.0	11,386.0	21,358.0	9,819.0	195.0	194.0	-11.88	-11,524.8	560.8	1,602.3	1,402.6	199.75	8.022		
23,000.0	11,386.0	21,458.0	9,819.0	196.6	195.6	-11.88	-11,624.8	561.6	1,602.3	1,400.9	201.41	7.956		
23,100.0	11,386.0	21,558.0	9,819.0	198.2	197.3	-11.88	-11,724.8	562.4	1,602.3	1,399.3	203.07	7.891		
23,200.0	11,386.0	21,658.0	9,819.0	199.8	198.9	-11.88	-11,824.8	563.2	1,602.3	1,397.6	204.72	7.827		
23,300.0	11,386.0	21,758.0	9,819.0	201.4	200.5	-11.88	-11,924.8	564.0	1,602.3	1,396.0	206.38	7.764		
23,400.0	11,386.0	21,858.0	9,819.0	203.0	202.2	-11.88	-12,024.8	564.9	1,602.3	1,394.3	208.04	7.702		
23,500.0	11,386.0	21,958.0	9,819.0	204.7	203.8	-11.88	-12,124.8	565.7	1,602.3	1,392.6	209.70	7.641		
23,600.0	11,386.0	22,058.0	9,819.0	206.3	205.4	-11.88	-12,224.8	566.5	1,602.3	1,391.0	211.36	7.581		
23,705.7	11,386.0	22,163.7	9,819.0	208.0	207.1	-11.88	-12,330.5	567.4	1,602.3	1,389.2	213.11	7.519		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #218H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	1.0	-1.0	0.0	0.0	134.59	-29.8	30.2	42.4					
100.0	100.0	101.0	99.0	0.1	0.1	134.59	-29.8	30.2	42.4	42.2	0.26	162.131		
200.0	200.0	201.0	199.0	0.5	0.5	134.59	-29.8	30.2	42.4	41.4	0.98	43.354		
300.0	300.0	301.0	299.0	0.8	0.9	134.59	-29.8	30.2	42.4	40.7	1.70	25.022		
400.0	400.0	401.0	399.0	1.2	1.2	134.59	-29.8	30.2	42.4	40.0	2.41	17.586		
500.0	500.0	501.0	499.0	1.6	1.6	134.59	-29.8	30.2	42.4	39.3	3.13	13.557 CC		
600.0	600.0	601.0	599.0	1.9	1.9	91.82	-29.8	30.2	42.4	38.6	3.84	11.042		
700.0	700.0	701.0	699.0	2.3	2.3	95.33	-29.8	30.2	42.6	38.1	4.56	9.348		
800.0	799.9	801.1	798.9	2.6	2.6	101.09	-29.8	30.2	43.2	38.0	5.27	8.197 ES		
900.0	899.7	901.3	898.7	3.0	3.0	108.74	-29.8	30.2	44.8	38.8	5.99	7.475		
1,000.0	999.4	1,001.6	998.4	3.4	3.4	117.61	-29.8	30.2	47.9	41.2	6.72	7.132		
1,100.0	1,098.9	1,102.1	1,097.9	3.7	3.7	126.75	-29.8	30.2	53.1	45.6	7.45	7.126		
1,200.0	1,198.3	1,202.7	1,197.3	4.1	4.1	135.29	-29.8	30.2	60.5	52.4	8.17	7.406		
1,300.0	1,297.4	1,303.6	1,296.4	4.5	4.4	142.70	-29.8	30.2	70.4	61.5	8.90	7.913		
1,400.0	1,396.4	1,404.6	1,395.4	4.9	4.8	148.59	-29.8	30.2	82.0	72.4	9.63	8.514		
1,500.0	1,495.5	1,505.5	1,494.5	5.3	5.2	153.00	-29.8	30.2	94.2	83.8	10.35	9.094		
1,600.0	1,594.5	1,606.5	1,593.5	5.7	5.5	156.38	-29.8	30.2	106.8	95.7	11.08	9.638		
1,700.0	1,693.5	1,707.5	1,692.5	6.1	5.9	159.05	-29.8	30.2	119.7	107.9	11.80	10.139		
1,800.0	1,792.5	1,808.5	1,791.5	6.5	6.3	161.20	-29.8	30.2	132.8	120.3	12.53	10.598		
1,900.0	1,891.6	1,909.4	1,890.6	6.9	6.6	162.96	-29.8	30.2	146.0	132.8	13.25	11.018		
2,000.0	1,990.6	1,989.6	1,989.6	7.3	6.9	164.42	-29.8	30.2	159.4	145.5	13.91	11.464		
2,100.0	2,089.6	2,088.6	2,088.6	7.7	7.3	165.66	-29.8	30.2	172.9	158.2	14.62	11.820		
2,200.0	2,188.6	2,187.6	2,187.6	8.1	7.6	166.72	-29.8	30.2	186.4	171.0	15.34	12.147		
2,300.0	2,287.7	2,286.7	2,286.7	8.5	8.0	167.63	-29.8	30.2	200.0	183.9	16.06	12.448		
2,400.0	2,386.7	2,385.7	2,385.7	8.9	8.3	168.43	-29.8	30.2	213.6	196.8	16.78	12.725		
2,500.0	2,485.7	2,484.7	2,484.7	9.3	8.7	169.14	-29.8	30.2	227.2	209.7	17.50	12.982		
2,600.0	2,584.8	2,583.8	2,583.8	9.8	9.0	169.76	-29.8	30.2	240.9	222.7	18.22	13.220		
2,700.0	2,683.8	2,682.8	2,682.8	10.2	9.4	170.32	-29.8	30.2	254.6	235.7	18.95	13.440		
2,739.3	2,722.7	2,721.7	2,721.7	10.3	9.5	170.52	-29.8	30.2	260.0	240.8	19.23	13.523		
2,800.0	2,782.9	2,781.9	2,781.9	10.6	9.7	170.82	-29.8	30.2	267.9	248.2	19.67	13.622		
2,900.0	2,882.3	2,881.3	2,881.3	11.0	10.1	171.21	-29.8	30.2	278.8	258.4	20.38	13.677		
3,000.0	2,981.9	2,980.9	2,980.9	11.4	10.5	171.48	-29.8	30.2	287.1	266.0	21.10	13.607		
3,100.0	3,081.7	3,084.3	3,084.3	11.7	10.8	171.60	-29.6	30.8	292.4	270.6	21.84	13.391		
3,200.0	3,181.7	3,188.6	3,188.6	12.1	11.2	171.42	-28.7	33.1	293.6	271.1	22.56	13.013		
3,272.6	3,254.3	3,264.4	3,264.3	12.3	11.5	-144.95	-27.7	36.0	292.0	268.9	23.09	12.646		
3,300.0	3,281.7	3,292.9	3,292.8	12.4	11.6	-145.10	-27.3	37.3	290.9	267.6	23.28	12.493		
3,400.0	3,381.7	3,397.0	3,396.7	12.7	11.9	-145.83	-25.1	43.2	286.0	262.0	24.00	11.918		
3,500.0	3,481.7	3,500.8	3,500.2	13.1	12.3	-146.82	-22.4	50.8	279.7	255.0	24.71	11.320		
3,600.0	3,581.7	3,604.3	3,603.2	13.4	12.6	-148.09	-19.0	60.2	272.1	246.7	25.42	10.704		
3,700.0	3,681.7	3,707.4	3,705.6	13.7	13.0	-149.68	-15.1	71.3	263.2	237.1	26.13	10.074		
3,800.0	3,781.7	3,810.0	3,807.3	14.1	13.4	-151.67	-10.5	84.0	253.2	226.3	26.84	9.434		
3,900.0	3,881.7	3,908.7	3,905.1	14.4	13.7	-153.84	-5.9	96.9	243.0	215.4	27.56	8.815		
4,000.0	3,981.7	4,007.7	4,003.1	14.7	14.1	-156.21	-1.2	109.9	233.1	204.8	28.30	8.239		
4,100.0	4,081.7	4,106.8	4,101.2	15.1	14.5	-158.78	3.4	122.9	223.7	194.7	29.03	7.706		
4,200.0	4,181.7	4,205.8	4,199.2	15.4	14.9	-161.57	8.1	135.9	214.8	185.0	29.78	7.214		
4,300.0	4,281.7	4,304.8	4,297.3	15.8	15.2	-164.59	12.7	148.8	206.5	175.9	30.53	6.762		
4,400.0	4,381.7	4,403.8	4,395.4	16.1	15.6	-167.85	17.4	161.8	198.7	167.4	31.29	6.351		
4,500.0	4,481.7	4,502.9	4,493.4	16.4	16.0	-171.36	22.0	174.8	191.7	159.6	32.06	5.979		
4,600.0	4,581.7	4,601.9	4,591.5	16.8	16.4	-175.12	26.7	187.8	185.4	152.6	32.83	5.648		
4,700.0	4,681.7	4,700.9	4,689.6	17.1	16.7	-179.11	31.3	200.7	180.0	146.4	33.60	5.357		
4,800.0	4,781.7	4,800.1	4,787.6	17.5	17.1	176.67	36.0	213.7	175.6	141.2	34.38	5.106		
4,900.0	4,881.7	4,901.0	4,885.7	17.8	17.5	172.26	40.6	226.7	172.1	137.0	35.17	4.895		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #218H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,000.0	4,981.7	5,002.0	4,983.7	18.2	17.9	167.71	45.3	239.7	169.8	133.8	35.94	4.723		
5,100.0	5,081.7	5,103.0	5,081.8	18.5	18.3	163.06	49.9	252.6	168.5	131.8	36.72	4.589		
5,159.2	5,140.8	5,155.6	5,139.8	18.7	18.5	160.28	52.7	260.3	168.3	131.2	37.14	4.532		
5,200.0	5,181.7	5,203.9	5,179.9	18.8	18.7	158.37	54.6	265.6	168.4	130.9	37.48	4.493		
5,300.0	5,281.7	5,304.9	5,277.9	19.2	19.1	153.70	59.2	278.6	169.4	131.2	38.23	4.432		
5,400.0	5,381.7	5,405.9	5,376.0	19.5	19.5	149.13	63.9	291.6	171.6	132.6	38.96	4.404		
5,500.0	5,481.7	5,506.9	5,474.1	19.9	19.9	144.69	68.5	304.5	174.9	135.2	39.69	4.406		
5,600.0	5,581.7	5,607.8	5,572.1	20.2	20.3	140.43	73.2	317.5	179.1	138.7	40.40	4.434		
5,700.0	5,681.7	5,691.2	5,670.2	20.6	20.6	136.40	77.8	330.5	184.4	143.3	41.03	4.494		
5,800.0	5,781.7	5,790.2	5,768.3	20.9	21.0	132.59	82.5	343.5	190.5	148.8	41.71	4.566		
5,900.0	5,881.7	5,889.2	5,866.3	21.3	21.4	129.04	87.1	356.4	197.4	155.0	42.39	4.656		
6,000.0	5,981.7	5,988.3	5,964.4	21.6	21.8	125.73	91.8	369.4	205.0	161.9	43.07	4.760		
6,100.0	6,081.7	6,087.3	6,062.4	22.0	22.2	122.67	96.4	382.4	213.2	169.5	43.74	4.875		
6,200.0	6,181.7	6,186.3	6,160.5	22.3	22.6	119.84	101.1	395.3	222.1	177.6	44.42	5.000		
6,300.0	6,281.7	6,285.4	6,258.6	22.7	23.0	117.23	105.7	408.3	231.4	186.3	45.09	5.132		
6,400.0	6,381.7	6,384.4	6,356.6	23.0	23.4	114.83	110.4	421.3	241.1	195.4	45.76	5.269		
6,500.0	6,481.7	6,483.4	6,454.7	23.4	23.8	112.61	115.0	434.3	251.3	204.9	46.44	5.411		
6,600.0	6,581.7	6,582.4	6,552.8	23.7	24.2	110.57	119.7	447.2	261.8	214.7	47.12	5.556		
6,700.0	6,681.7	6,681.5	6,650.8	24.1	24.6	108.68	124.3	460.2	272.6	224.8	47.80	5.703		
6,800.0	6,781.7	6,780.5	6,748.9	24.4	25.0	106.94	129.0	473.2	283.7	235.2	48.48	5.852		
6,900.0	6,881.7	6,879.5	6,846.9	24.8	25.4	105.33	133.6	486.2	295.0	245.8	49.16	6.000		
7,000.0	6,981.7	6,978.5	6,945.0	25.1	25.8	103.84	138.3	499.1	306.5	256.7	49.85	6.149		
7,100.0	7,081.7	7,077.6	7,043.1	25.5	26.2	102.46	142.9	512.1	318.3	267.7	50.54	6.297		
7,200.0	7,181.7	7,176.6	7,141.1	25.8	26.6	101.18	147.6	525.1	330.2	278.9	51.23	6.444		
7,300.0	7,281.7	7,275.6	7,239.2	26.2	27.0	99.98	152.2	538.1	342.2	290.3	51.92	6.590		
7,400.0	7,381.7	7,374.6	7,337.3	26.5	27.4	98.87	156.9	551.0	354.4	301.8	52.62	6.735		
7,500.0	7,481.7	7,473.7	7,435.3	26.9	27.8	97.83	161.5	564.0	366.7	313.4	53.32	6.878		
7,600.0	7,581.7	7,572.7	7,533.4	27.2	28.2	96.86	166.2	577.0	379.1	325.1	54.01	7.019		
7,700.0	7,681.7	7,671.7	7,631.5	27.6	28.6	95.95	170.8	590.0	391.6	336.9	54.71	7.158		
7,800.0	7,781.7	7,770.8	7,729.5	28.0	29.0	95.10	175.5	602.9	404.2	348.8	55.41	7.295		
7,900.0	7,881.7	7,869.8	7,827.6	28.3	29.4	94.30	180.1	615.9	416.9	360.8	56.11	7.430		
8,000.0	7,981.7	7,968.8	7,925.6	28.7	29.8	93.54	184.8	628.9	429.7	372.9	56.82	7.563		
8,100.0	8,081.7	8,067.8	8,023.7	29.0	30.2	92.83	189.4	641.8	442.5	385.0	57.52	7.693		
8,200.0	8,181.7	8,166.9	8,121.8	29.4	30.6	92.16	194.1	654.8	455.4	397.2	58.23	7.822		
8,300.0	8,281.7	8,265.9	8,219.8	29.7	31.1	91.53	198.7	667.8	468.4	409.5	58.93	7.948		
8,400.0	8,381.7	8,367.2	8,320.1	30.1	31.5	90.92	203.5	681.0	481.4	421.7	59.67	8.068		
8,500.0	8,481.7	8,480.0	8,432.1	30.4	31.9	90.36	208.0	693.7	492.6	432.1	60.52	8.139		
8,600.0	8,581.7	8,593.5	8,545.1	30.8	32.4	89.96	211.5	703.3	501.1	439.7	61.33	8.170		
8,700.0	8,681.7	8,707.4	8,658.9	31.1	32.8	89.70	213.8	709.8	506.8	444.7	62.10	8.160		
8,800.0	8,781.7	8,821.8	8,773.2	31.5	33.2	89.57	215.0	713.1	509.6	446.8	62.83	8.112		
8,900.0	8,881.7	8,929.3	8,880.7	31.8	33.5	89.55	215.1	713.5	510.0	446.5	63.52	8.029		
9,000.0	8,981.7	9,029.3	8,980.7	32.2	33.9	89.55	215.1	713.5	510.0	445.8	64.22	7.942		
9,100.0	9,081.7	9,129.3	9,080.7	32.6	34.2	89.55	215.1	713.5	510.0	445.1	64.92	7.856		
9,200.0	9,181.7	9,229.3	9,180.7	32.9	34.5	89.55	215.1	713.5	510.0	444.4	65.63	7.772		
9,300.0	9,281.7	9,329.3	9,280.7	33.3	34.9	89.55	215.1	713.5	510.0	443.7	66.33	7.689		
9,400.0	9,381.7	9,429.3	9,380.7	33.6	35.2	89.55	215.1	713.5	510.0	443.0	67.03	7.609		
9,500.0	9,481.7	9,529.3	9,480.7	34.0	35.5	89.55	215.1	713.5	510.0	442.3	67.73	7.530		
9,600.0	9,581.7	9,629.3	9,580.7	34.3	35.9	89.55	215.1	713.5	510.0	441.6	68.44	7.453		
9,700.0	9,681.7	9,729.3	9,680.7	34.7	36.2	89.55	215.1	713.5	510.0	440.9	69.14	7.377		
9,800.0	9,781.7	9,829.3	9,780.7	35.0	36.5	89.55	215.1	713.5	510.0	440.2	69.84	7.302		
9,900.0	9,881.7	9,929.3	9,880.7	35.4	36.9	89.55	215.1	713.5	510.0	439.5	70.55	7.230		
10,000.0	9,981.7	10,029.3	9,980.7	35.7	37.2	89.55	215.1	713.5	510.0	438.8	71.25	7.158		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #218H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,100.0	10,081.7	10,129.3	10,080.7	36.1	37.6	89.55	215.1	713.5	510.0	438.1	71.96	7.088		
10,200.0	10,181.7	10,229.3	10,180.7	36.5	37.9	89.55	215.1	713.5	510.0	437.4	72.66	7.019		
10,300.0	10,281.7	10,329.3	10,280.7	36.8	38.2	89.55	215.1	713.5	510.0	436.7	73.37	6.952		
10,400.0	10,381.7	10,429.3	10,380.7	37.2	38.6	89.55	215.1	713.5	510.0	436.0	74.07	6.886		
10,500.0	10,481.7	10,529.3	10,480.7	37.5	38.9	89.55	215.1	713.5	510.0	435.3	74.78	6.821		
10,600.0	10,581.7	10,629.3	10,580.7	37.9	39.2	89.55	215.1	713.5	510.0	434.5	75.48	6.757		
10,700.0	10,681.7	10,729.3	10,680.7	38.2	39.6	89.55	215.1	713.5	510.0	433.8	76.19	6.694		
10,800.0	10,781.7	10,829.3	10,780.7	38.6	39.9	89.55	215.1	713.5	510.0	433.1	76.89	6.633		
10,831.3	10,813.0	10,860.6	10,812.0	38.7	40.0	89.55	215.1	713.5	510.0	432.9	77.11	6.614		
10,850.0	10,831.7	10,879.2	10,830.7	38.8	40.1	-95.58	215.1	713.5	510.1	432.8	77.24	6.603		
10,900.0	10,881.5	10,929.1	10,880.5	38.9	40.3	-95.97	215.1	713.5	510.4	432.9	77.56	6.581		
10,950.0	10,930.8	10,978.4	10,929.8	39.1	40.4	-96.77	215.1	713.5	511.4	433.5	77.87	6.567		
11,000.0	10,979.2	11,026.8	10,978.2	39.2	40.6	-97.94	215.1	713.5	513.0	434.8	78.16	6.564		
11,050.0	11,026.4	11,074.0	11,025.4	39.3	40.8	-99.40	215.1	713.5	515.6	437.2	78.43	6.575		
11,100.0	11,071.9	11,119.7	11,071.1	39.5	40.9	-100.94	213.9	713.7	519.7	441.0	78.68	6.605		
11,150.0	11,115.5	11,166.6	11,117.7	39.6	41.0	-102.38	208.9	714.3	525.2	446.3	78.92	6.655		
11,200.0	11,156.7	11,215.1	11,165.3	39.7	41.2	-103.72	199.7	715.4	532.1	453.0	79.13	6.725		
11,250.0	11,195.4	11,265.2	11,213.5	39.8	41.3	-104.95	186.1	717.0	540.5	461.2	79.30	6.815		
11,300.0	11,231.1	11,317.2	11,262.0	39.9	41.5	-106.06	167.7	719.2	550.1	470.7	79.43	6.926		
11,350.0	11,263.7	11,371.2	11,310.5	39.9	41.6	-107.04	143.9	722.0	560.8	481.4	79.48	7.056		
11,400.0	11,292.8	11,427.6	11,358.3	40.0	41.7	-107.88	114.5	725.5	572.6	493.1	79.46	7.206		
11,450.0	11,318.3	11,486.4	11,404.9	40.1	41.8	-108.57	78.9	729.8	585.1	505.8	79.34	7.375		
11,500.0	11,339.9	11,547.9	11,449.5	40.2	41.9	-109.11	36.9	734.8	598.3	519.2	79.12	7.562		
11,550.0	11,357.5	11,612.2	11,491.0	40.3	42.0	-109.49	-11.9	740.6	611.9	533.0	78.82	7.762		
11,600.0	11,371.0	11,679.6	11,528.2	40.4	42.1	-109.68	-67.6	747.3	625.6	547.1	78.46	7.974		
11,650.0	11,380.2	11,750.0	11,559.8	40.5	42.2	-109.68	-130.1	754.7	639.3	561.1	78.12	8.183		
11,700.0	11,385.1	11,823.5	11,584.3	40.7	42.4	-109.47	-198.9	762.9	652.6	574.8	77.83	8.386		
11,731.3	11,386.0	11,871.1	11,595.3	40.7	42.5	-109.23	-244.8	768.4	660.8	583.1	77.71	8.503		
11,800.0	11,386.0	11,979.3	11,606.0	40.9	42.7	-109.40	-351.6	781.1	675.6	597.7	77.87	8.675		
11,900.0	11,386.0	12,107.6	11,606.0	41.3	43.1	-108.80	-479.2	793.5	689.2	610.5	78.65	8.762		
12,009.9	11,386.0	12,249.8	11,606.0	41.7	43.6	-108.53	-621.2	800.6	695.5	616.0	79.56	8.742		
12,100.0	11,386.0	12,351.0	11,606.0	42.1	44.1	-108.52	-722.5	801.9	695.8	615.5	80.33	8.662		
12,200.0	11,386.0	12,451.0	11,606.0	42.6	44.6	-108.52	-822.5	802.7	695.8	614.6	81.28	8.561		
12,300.0	11,386.0	12,551.0	11,606.0	43.2	45.1	-108.52	-922.5	803.5	695.8	613.5	82.34	8.451		
12,400.0	11,386.0	12,651.0	11,606.0	43.8	45.7	-108.52	-1,022.5	804.3	695.8	612.3	83.51	8.333		
12,500.0	11,386.0	12,751.0	11,606.0	44.5	46.4	-108.52	-1,122.5	805.2	695.8	611.1	84.78	8.208		
12,600.0	11,386.0	12,851.0	11,606.0	45.2	47.1	-108.52	-1,222.5	806.0	695.8	609.7	86.15	8.077		
12,700.0	11,386.0	12,951.0	11,606.0	46.0	47.8	-108.52	-1,322.5	806.8	695.8	608.2	87.61	7.943		
12,800.0	11,386.0	13,051.0	11,606.0	46.8	48.6	-108.52	-1,422.4	807.6	695.8	606.7	89.16	7.804		
12,900.0	11,386.0	13,151.0	11,606.0	47.7	49.4	-108.52	-1,522.4	808.5	695.8	605.0	90.80	7.664		
13,000.0	11,386.0	13,251.0	11,606.0	48.6	50.3	-108.52	-1,622.4	809.3	695.8	603.3	92.51	7.522		
13,100.0	11,386.0	13,351.0	11,606.0	49.5	51.2	-108.52	-1,722.4	810.1	695.8	601.5	94.30	7.379		
13,200.0	11,386.0	13,451.0	11,606.0	50.5	52.2	-108.52	-1,822.4	810.9	695.8	599.7	96.17	7.236		
13,300.0	11,386.0	13,551.0	11,606.0	51.5	53.1	-108.52	-1,922.4	811.7	695.8	597.7	98.09	7.094		
13,400.0	11,386.0	13,651.0	11,606.0	52.6	54.2	-108.52	-2,022.4	812.6	695.8	595.8	100.09	6.952		
13,500.0	11,386.0	13,751.0	11,606.0	53.6	55.2	-108.52	-2,122.4	813.4	695.8	593.7	102.14	6.813		
13,600.0	11,386.0	13,851.0	11,606.0	54.7	56.3	-108.52	-2,222.4	814.2	695.8	591.6	104.25	6.675		
13,700.0	11,386.0	13,951.0	11,606.0	55.9	57.4	-108.52	-2,322.4	815.0	695.8	589.4	106.41	6.539		
13,800.0	11,386.0	14,051.0	11,606.0	57.0	58.5	-108.52	-2,422.4	815.9	695.8	587.2	108.62	6.406		
13,900.0	11,386.0	14,151.0	11,606.0	58.2	59.7	-108.52	-2,522.4	816.7	695.9	585.0	110.88	6.276		
14,000.0	11,386.0	14,251.0	11,606.0	59.4	60.8	-108.52	-2,622.4	817.5	695.9	582.7	113.18	6.148		
14,100.0	11,386.0	14,351.0	11,606.0	60.6	62.0	-108.52	-2,722.4	818.3	695.9	580.3	115.53	6.023		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #218H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,200.0	11,386.0	14,451.0	11,606.0	61.9	63.2	-108.52	-2,822.4	819.1	695.9	577.9	117.91	5.902		
14,300.0	11,386.0	14,551.0	11,606.0	63.1	64.5	-108.52	-2,922.4	820.0	695.9	575.5	120.33	5.783		
14,400.0	11,386.0	14,651.0	11,606.0	64.4	65.7	-108.52	-3,022.4	820.8	695.9	573.1	122.78	5.667		
14,500.0	11,386.0	14,751.0	11,606.0	65.7	67.0	-108.52	-3,122.4	821.6	695.9	570.6	125.27	5.555		
14,600.0	11,386.0	14,851.0	11,606.0	67.0	68.3	-108.52	-3,222.4	822.4	695.9	568.1	127.78	5.446		
14,700.0	11,386.0	14,951.0	11,606.0	68.4	69.6	-108.52	-3,322.4	823.3	695.9	565.5	130.33	5.339		
14,800.0	11,386.0	15,051.0	11,606.0	69.7	70.9	-108.52	-3,422.4	824.1	695.9	563.0	132.90	5.236		
14,900.0	11,386.0	15,151.0	11,606.0	71.1	72.2	-108.52	-3,522.4	824.9	695.9	560.4	135.50	5.136		
15,000.0	11,386.0	15,251.0	11,606.0	72.4	73.6	-108.52	-3,622.4	825.7	695.9	557.7	138.12	5.038		
15,100.0	11,386.0	15,351.0	11,606.0	73.8	75.0	-108.52	-3,722.4	826.5	695.9	555.1	140.76	4.943		
15,200.0	11,386.0	15,451.0	11,606.0	75.2	76.3	-108.52	-3,822.4	827.4	695.9	552.4	143.43	4.852		
15,300.0	11,386.0	15,551.0	11,606.0	76.6	77.7	-108.52	-3,922.4	828.2	695.9	549.7	146.11	4.762		
15,400.0	11,386.0	15,651.0	11,606.0	78.0	79.1	-108.52	-4,022.4	829.0	695.9	547.0	148.82	4.676		
15,500.0	11,386.0	15,751.0	11,606.0	79.4	80.5	-108.52	-4,122.4	829.8	695.9	544.3	151.54	4.592		
15,600.0	11,386.0	15,851.0	11,606.0	80.9	81.9	-108.52	-4,222.4	830.7	695.9	541.6	154.28	4.510		
15,700.0	11,386.0	15,951.0	11,606.0	82.3	83.3	-108.52	-4,322.3	831.5	695.9	538.8	157.04	4.431		
15,800.0	11,386.0	16,051.0	11,606.0	83.7	84.7	-108.52	-4,422.3	832.3	695.9	536.1	159.81	4.354		
15,900.0	11,386.0	16,151.0	11,606.0	85.2	86.2	-108.52	-4,522.3	833.1	695.9	533.3	162.60	4.280		
16,000.0	11,386.0	16,251.0	11,606.0	86.7	87.6	-108.52	-4,622.3	833.9	695.9	530.5	165.40	4.207		
16,100.0	11,386.0	16,351.0	11,606.0	88.1	89.1	-108.52	-4,722.3	834.8	695.9	527.7	168.21	4.137		
16,200.0	11,386.0	16,451.0	11,606.0	89.6	90.5	-108.52	-4,822.3	835.6	695.9	524.8	171.04	4.068		
16,300.0	11,386.0	16,551.0	11,606.0	91.1	92.0	-108.52	-4,922.3	836.4	695.9	522.0	173.88	4.002		
16,400.0	11,386.0	16,651.0	11,606.0	92.6	93.5	-108.52	-5,022.3	837.2	695.9	519.1	176.73	3.938		
16,500.0	11,386.0	16,751.0	11,606.0	94.0	94.9	-108.52	-5,122.3	838.1	695.9	516.3	179.59	3.875		
16,600.0	11,386.0	16,851.0	11,606.0	95.5	96.4	-108.52	-5,222.3	838.9	695.9	513.4	182.46	3.814		
16,700.0	11,386.0	16,951.0	11,606.0	97.0	97.9	-108.52	-5,322.3	839.7	695.9	510.5	185.34	3.755		
16,800.0	11,386.0	17,051.0	11,606.0	98.5	99.4	-108.52	-5,422.3	840.5	695.9	507.6	188.23	3.697		
16,900.0	11,386.0	17,151.0	11,606.0	100.1	100.9	-108.52	-5,522.3	841.3	695.9	504.8	191.13	3.641		
17,000.0	11,386.0	17,251.0	11,606.0	101.6	102.4	-108.52	-5,622.3	842.2	695.9	501.8	194.04	3.586		
17,100.0	11,386.0	17,351.0	11,606.0	103.1	103.9	-108.52	-5,722.3	843.0	695.9	498.9	196.95	3.533		
17,200.0	11,386.0	17,451.0	11,606.0	104.6	105.4	-108.52	-5,822.3	843.8	695.9	496.0	199.88	3.482		
17,300.0	11,386.0	17,551.0	11,606.0	106.1	106.9	-108.52	-5,922.3	844.6	695.9	493.1	202.81	3.431		
17,400.0	11,386.0	17,651.0	11,606.0	107.7	108.5	-108.52	-6,022.3	845.5	695.9	490.1	205.75	3.382		
17,500.0	11,386.0	17,751.0	11,606.0	109.2	110.0	-108.52	-6,122.3	846.3	695.9	487.2	208.69	3.335		
17,600.0	11,386.0	17,851.0	11,606.0	110.7	111.5	-108.52	-6,222.3	847.1	695.9	484.2	211.64	3.288		
17,700.0	11,386.0	17,951.0	11,606.0	112.3	113.0	-108.52	-6,322.3	847.9	695.9	481.3	214.60	3.243		
17,800.0	11,386.0	18,051.0	11,606.0	113.8	114.6	-108.52	-6,422.3	848.7	695.9	478.3	217.57	3.199		
17,900.0	11,386.0	18,151.0	11,606.0	115.4	116.1	-108.52	-6,522.3	849.6	695.9	475.4	220.54	3.155		
18,000.0	11,386.0	18,251.0	11,606.0	116.9	117.6	-108.52	-6,622.3	850.4	695.9	472.4	223.51	3.113		
18,100.0	11,386.0	18,351.0	11,606.0	118.5	119.2	-108.52	-6,722.3	851.2	695.9	469.4	226.49	3.072		
18,200.0	11,386.0	18,451.0	11,606.0	120.0	120.7	-108.52	-6,822.3	852.0	695.9	466.4	229.48	3.032		
18,300.0	11,386.0	18,551.0	11,606.0	121.6	122.3	-108.52	-6,922.3	852.9	695.9	463.4	232.47	2.993		
18,400.0	11,386.0	18,651.0	11,606.0	123.2	123.8	-108.52	-7,022.3	853.7	695.9	460.4	235.47	2.955		
18,500.0	11,386.0	18,751.0	11,606.0	124.7	125.4	-108.52	-7,122.3	854.5	695.9	457.4	238.47	2.918		
18,600.0	11,386.0	18,851.0	11,606.0	126.3	126.9	-108.52	-7,222.3	855.3	695.9	454.4	241.47	2.882		
18,700.0	11,386.0	18,951.0	11,606.0	127.9	128.5	-108.52	-7,322.2	856.2	695.9	451.4	244.48	2.846		
18,800.0	11,386.0	19,051.0	11,606.0	129.4	130.1	-108.52	-7,422.2	857.0	695.9	448.4	247.49	2.812		
18,900.0	11,386.0	19,151.0	11,606.0	131.0	131.6	-108.52	-7,522.2	857.8	695.9	445.4	250.51	2.778		
19,000.0	11,386.0	19,251.0	11,606.0	132.6	133.2	-108.52	-7,622.2	858.6	695.9	442.4	253.53	2.745		
19,100.0	11,386.0	19,351.0	11,606.0	134.1	134.8	-108.52	-7,722.2	859.4	695.9	439.3	256.56	2.712		
19,200.0	11,386.0	19,451.0	11,606.0	135.7	136.3	-108.52	-7,822.2	860.3	695.9	436.3	259.59	2.681		
19,300.0	11,386.0	19,551.0	11,606.0	137.3	137.9	-108.52	-7,922.2	861.1	695.9	433.3	262.62	2.650		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #218H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,400.0	11,386.0	19,651.0	11,606.0	138.9	139.5	-108.52	-8,022.2	861.9	695.9	430.3	265.65	2.620		
19,500.0	11,386.0	19,751.0	11,606.0	140.5	141.1	-108.52	-8,122.2	862.7	695.9	427.2	268.69	2.590		
19,600.0	11,386.0	19,851.0	11,606.0	142.0	142.6	-108.52	-8,222.2	863.6	695.9	424.2	271.73	2.561		
19,700.0	11,386.0	19,951.0	11,606.0	143.6	144.2	-108.52	-8,322.2	864.4	695.9	421.1	274.78	2.533		
19,800.0	11,386.0	20,051.0	11,606.0	145.2	145.8	-108.52	-8,422.2	865.2	695.9	418.1	277.82	2.505		
19,900.0	11,386.0	20,151.0	11,606.0	146.8	147.4	-108.52	-8,522.2	866.0	695.9	415.0	280.87	2.478		
20,000.0	11,386.0	20,251.0	11,606.0	148.4	149.0	-108.52	-8,622.2	866.8	695.9	412.0	283.93	2.451		
20,100.0	11,386.0	20,351.0	11,606.0	150.0	150.5	-108.52	-8,722.2	867.7	695.9	408.9	286.98	2.425		
20,200.0	11,386.0	20,451.0	11,606.0	151.6	152.1	-108.52	-8,822.2	868.5	695.9	405.9	290.04	2.399		
20,300.0	11,386.0	20,551.0	11,606.0	153.2	153.7	-108.52	-8,922.2	869.3	695.9	402.8	293.10	2.374		
20,400.0	11,386.0	20,651.0	11,606.0	154.8	155.3	-108.52	-9,022.2	870.1	695.9	399.8	296.16	2.350		
20,500.0	11,386.0	20,751.0	11,606.0	156.4	156.9	-108.52	-9,122.2	871.0	695.9	396.7	299.23	2.326		
20,600.0	11,386.0	20,851.0	11,606.0	158.0	158.5	-108.52	-9,222.2	871.8	695.9	393.6	302.29	2.302		
20,700.0	11,386.0	20,951.0	11,606.0	159.6	160.1	-108.52	-9,322.2	872.6	695.9	390.6	305.36	2.279		
20,800.0	11,386.0	21,051.0	11,606.0	161.2	161.7	-108.52	-9,422.2	873.4	695.9	387.5	308.43	2.256		
20,900.0	11,386.0	21,151.0	11,606.0	162.8	163.3	-108.52	-9,522.2	874.2	695.9	384.4	311.51	2.234		
21,000.0	11,386.0	21,251.0	11,606.0	164.4	164.9	-108.52	-9,622.2	875.1	695.9	381.3	314.58	2.212		
21,100.0	11,386.0	21,351.0	11,606.0	166.0	166.5	-108.52	-9,722.2	875.9	695.9	378.3	317.66	2.191		
21,200.0	11,386.0	21,451.0	11,606.0	167.6	168.1	-108.52	-9,822.2	876.7	695.9	375.2	320.74	2.170		
21,300.0	11,386.0	21,551.0	11,606.0	169.2	169.7	-108.52	-9,922.2	877.5	695.9	372.1	323.82	2.149		
21,400.0	11,386.0	21,651.0	11,606.0	170.8	171.3	-108.52	-10,022.2	878.4	695.9	369.0	326.90	2.129		
21,500.0	11,386.0	21,751.0	11,606.0	172.4	172.9	-108.52	-10,122.2	879.2	695.9	365.9	329.99	2.109		
21,600.0	11,386.0	21,851.0	11,606.0	174.0	174.5	-108.52	-10,222.2	880.0	695.9	362.9	333.07	2.089		
21,700.0	11,386.0	21,951.0	11,606.0	175.6	176.1	-108.52	-10,322.1	880.8	695.9	359.8	336.16	2.070		
21,800.0	11,386.0	22,051.0	11,606.0	177.2	177.7	-108.52	-10,422.1	881.6	695.9	356.7	339.25	2.051		
21,900.0	11,386.0	22,151.0	11,606.0	178.8	179.3	-108.52	-10,522.1	882.5	695.9	353.6	342.34	2.033		
22,000.0	11,386.0	22,251.0	11,606.0	180.4	180.9	-108.52	-10,622.1	883.3	695.9	350.5	345.43	2.015		
22,100.0	11,386.0	22,351.0	11,606.0	182.0	182.5	-108.52	-10,722.1	884.1	695.9	347.4	348.53	1.997		
22,200.0	11,386.0	22,451.0	11,606.0	183.7	184.1	-108.52	-10,822.1	884.9	695.9	344.3	351.62	1.979		
22,300.0	11,386.0	22,551.0	11,606.0	185.3	185.7	-108.52	-10,922.1	885.8	695.9	341.2	354.72	1.962		
22,400.0	11,386.0	22,651.0	11,606.0	186.9	187.3	-108.52	-11,022.1	886.6	695.9	338.1	357.82	1.945		
22,500.0	11,386.0	22,751.0	11,606.0	188.5	188.9	-108.52	-11,122.1	887.4	695.9	335.0	360.92	1.928		
22,600.0	11,386.0	22,851.0	11,606.0	190.1	190.5	-108.52	-11,222.1	888.2	695.9	331.9	364.02	1.912		
22,700.0	11,386.0	22,951.0	11,606.0	191.7	192.1	-108.52	-11,322.1	889.0	695.9	328.8	367.12	1.896		
22,800.0	11,386.0	23,051.0	11,606.0	193.3	193.8	-108.52	-11,422.1	889.9	695.9	325.7	370.22	1.880		
22,900.0	11,386.0	23,151.0	11,606.0	195.0	195.4	-108.52	-11,522.1	890.7	695.9	322.6	373.33	1.864		
23,000.0	11,386.0	23,251.0	11,606.0	196.6	197.0	-108.52	-11,622.1	891.5	695.9	319.5	376.43	1.849		
23,100.0	11,386.0	23,351.0	11,606.0	198.2	198.6	-108.52	-11,722.1	892.3	695.9	316.4	379.54	1.834		
23,200.0	11,386.0	23,451.0	11,606.0	199.8	200.2	-108.52	-11,822.1	893.2	695.9	313.3	382.65	1.819		
23,300.0	11,386.0	23,551.0	11,606.0	201.4	201.8	-108.52	-11,922.1	894.0	695.9	310.2	385.75	1.804		
23,400.0	11,386.0	23,651.0	11,606.0	203.0	203.4	-108.52	-12,022.1	894.8	695.9	307.1	388.86	1.790		
23,500.0	11,386.0	23,751.0	11,606.0	204.7	205.1	-108.52	-12,122.1	895.6	695.9	304.0	391.97	1.775		
23,600.0	11,386.0	23,851.0	11,606.0	206.3	206.7	-108.52	-12,222.1	896.5	695.9	300.9	395.09	1.762		
23,705.7	11,386.0	23,956.7	11,606.0	208.0	208.4	-108.51	-12,327.8	897.3	695.9	297.6	398.38	1.747 SF		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #224H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	1.0	1.0	0.0	0.0	-90.42	-0.6	-80.0	80.0					
100.0	100.0	101.0	101.0	0.1	0.1	-90.42	-0.6	-80.0	80.0	79.8	0.26	307.889		
200.0	200.0	201.0	201.0	0.5	0.5	-90.42	-0.6	-80.0	80.0	79.0	0.98	81.916		
300.0	300.0	301.0	301.0	0.8	0.8	-90.42	-0.6	-80.0	80.0	78.3	1.69	47.242		
400.0	400.0	401.0	401.0	1.2	1.2	-90.42	-0.6	-80.0	80.0	77.6	2.41	33.193		
500.0	500.0	501.0	501.0	1.6	1.6	-90.42	-0.6	-80.0	80.0	76.9	3.13	25.584 CC		
600.0	600.0	601.0	601.0	1.9	1.9	-134.82	-0.6	-80.0	80.6	76.8	3.84	20.986 ES		
700.0	700.0	701.0	701.0	2.3	2.3	-136.09	-0.6	-80.0	82.5	77.9	4.56	18.109		
800.0	799.9	800.9	800.9	2.6	2.6	-138.09	-0.6	-80.0	85.7	80.4	5.27	16.259		
900.0	899.7	900.7	900.7	3.0	3.0	-140.65	-0.6	-80.0	90.3	84.3	5.99	15.089		
1,000.0	999.4	1,000.4	1,000.4	3.4	3.4	-143.56	-0.6	-80.0	96.5	89.8	6.70	14.399		
1,100.0	1,098.9	1,100.1	1,099.9	3.7	3.7	-146.64	-0.6	-80.0	104.4	97.0	7.42	14.066		
1,200.0	1,198.3	1,200.7	1,199.3	4.1	4.1	-149.71	-0.6	-80.0	114.0	105.9	8.15	13.999		
1,300.0	1,297.4	1,301.6	1,298.4	4.5	4.4	-152.66	-0.6	-80.0	125.5	116.6	8.87	14.146		
1,400.0	1,396.4	1,402.6	1,397.4	4.9	4.8	-155.31	-0.6	-80.0	138.0	128.4	9.60	14.383		
1,500.0	1,495.5	1,503.5	1,496.5	5.3	5.2	-157.52	-0.6	-80.0	150.8	140.5	10.32	14.610		
1,600.0	1,594.5	1,604.5	1,595.5	5.7	5.5	-159.38	-0.6	-80.0	163.8	152.7	11.05	14.824		
1,700.0	1,693.5	1,705.5	1,694.5	6.1	5.9	-160.96	-0.6	-80.0	176.9	165.1	11.77	15.024		
1,800.0	1,792.5	1,806.5	1,793.5	6.5	6.2	-162.33	-0.6	-80.0	190.1	177.6	12.50	15.209		
1,900.0	1,891.6	1,907.4	1,892.6	6.9	6.6	-163.52	-0.6	-80.0	203.4	190.2	13.23	15.381		
2,000.0	1,990.6	2,008.4	1,991.6	7.3	7.0	-164.56	-0.6	-80.0	216.8	202.9	13.95	15.540		
2,100.0	2,089.6	2,109.4	2,090.6	7.7	7.3	-165.48	-0.6	-80.0	230.3	215.6	14.68	15.687		
2,200.0	2,188.6	2,189.6	2,189.6	8.1	7.6	-166.30	-0.6	-80.0	243.8	228.4	15.33	15.900		
2,300.0	2,287.7	2,288.7	2,288.7	8.5	8.0	-167.04	-0.6	-80.0	257.3	241.3	16.05	16.030		
2,400.0	2,386.7	2,387.7	2,387.7	8.9	8.3	-167.70	-0.6	-80.0	270.9	254.1	16.77	16.152		
2,500.0	2,485.7	2,486.7	2,486.7	9.3	8.7	-168.29	-0.6	-80.0	284.5	267.0	17.49	16.265		
2,600.0	2,584.8	2,585.8	2,585.8	9.8	9.0	-168.84	-0.6	-80.0	298.2	280.0	18.21	16.370		
2,700.0	2,683.8	2,684.8	2,684.8	10.2	9.4	-169.33	-0.6	-80.0	311.9	292.9	18.94	16.469		
2,739.3	2,722.7	2,723.7	2,723.7	10.3	9.5	-169.51	-0.6	-80.0	317.2	298.0	19.22	16.506		
2,800.0	2,782.9	2,783.9	2,783.9	10.6	9.7	-169.79	-0.6	-80.0	325.1	305.4	19.66	16.538		
2,900.0	2,882.3	2,883.3	2,883.3	11.0	10.1	-170.15	-0.6	-80.0	335.9	315.6	20.38	16.488		
3,000.0	2,981.9	2,982.9	2,982.9	11.4	10.5	-170.41	-0.6	-80.0	344.3	323.2	21.09	16.322		
3,100.0	3,081.7	3,082.7	3,082.7	11.7	10.8	-170.59	-0.6	-80.0	350.0	328.2	21.81	16.050		
3,200.0	3,181.7	3,182.7	3,182.7	12.1	11.2	-170.68	-0.6	-80.0	353.2	330.7	22.52	15.682		
3,272.6	3,254.3	3,255.3	3,255.3	12.3	11.4	-126.75	-0.6	-80.0	353.9	330.8	23.04	15.362		
3,300.0	3,281.7	3,282.7	3,282.7	12.4	11.5	-126.75	-0.6	-80.0	353.9	330.6	23.23	15.234		
3,400.0	3,381.7	3,382.7	3,382.7	12.7	11.9	-126.75	-0.6	-80.0	353.9	329.9	23.93	14.785		
3,500.0	3,481.7	3,482.7	3,482.7	13.1	12.3	-126.75	-0.6	-80.0	353.9	329.2	24.64	14.361		
3,600.0	3,581.7	3,582.7	3,582.7	13.4	12.6	-126.75	-0.6	-80.0	353.9	328.5	25.35	13.960		
3,700.0	3,681.7	3,682.7	3,682.7	13.7	13.0	-126.75	-0.6	-80.0	353.9	327.8	26.06	13.581		
3,800.0	3,781.7	3,782.7	3,782.7	14.1	13.3	-126.75	-0.6	-80.0	353.9	327.1	26.76	13.222		
3,900.0	3,881.7	3,882.7	3,882.7	14.4	13.7	-126.75	-0.6	-80.0	353.9	326.4	27.47	12.881		
4,000.0	3,981.7	3,982.7	3,982.7	14.7	14.0	-126.75	-0.6	-80.0	353.9	325.7	28.18	12.557		
4,100.0	4,081.7	4,082.7	4,082.7	15.1	14.4	-126.70	0.0	-79.7	353.3	324.4	28.92	12.216		
4,200.0	4,181.7	4,193.6	4,193.6	15.4	14.8	-126.54	2.2	-78.4	351.0	321.4	29.65	11.837		
4,300.0	4,281.7	4,299.4	4,299.3	15.8	15.2	-126.24	6.2	-76.1	347.1	316.7	30.38	11.424		
4,400.0	4,381.7	4,405.1	4,404.7	16.1	15.6	-125.81	11.8	-72.8	341.4	310.3	31.10	10.980		
4,500.0	4,481.7	4,510.4	4,509.7	16.4	15.9	-125.22	19.0	-68.6	334.2	302.4	31.80	10.507		
4,600.0	4,581.7	4,615.4	4,614.2	16.8	16.3	-124.46	27.9	-63.4	325.3	292.8	32.50	10.008		
4,700.0	4,681.7	4,720.0	4,718.1	17.1	16.7	-123.51	38.4	-57.2	314.8	281.6	33.19	9.484		
4,800.0	4,781.7	4,823.0	4,820.2	17.5	17.1	-122.35	50.3	-50.3	302.8	268.9	33.88	8.938		
4,900.0	4,881.7	4,922.0	4,918.2	17.8	17.4	-121.09	62.2	-43.4	290.5	255.9	34.59	8.398		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #224H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,000.0	4,981.7	5,021.0	5,016.3	18.2	17.8	-119.72	74.1	-36.4	278.3	243.0	35.30	7.884		
5,100.0	5,081.7	5,120.1	5,114.3	18.5	18.1	-118.23	86.0	-29.5	266.3	230.3	36.02	7.394		
5,200.0	5,181.7	5,219.1	5,212.4	18.8	18.5	-116.60	97.9	-22.5	254.5	217.8	36.74	6.928		
5,300.0	5,281.7	5,318.1	5,310.5	19.2	18.9	-114.81	109.8	-15.6	243.0	205.5	37.46	6.486		
5,400.0	5,381.7	5,417.1	5,408.5	19.5	19.2	-112.84	121.8	-8.6	231.7	193.5	38.19	6.066		
5,500.0	5,481.7	5,516.2	5,506.6	19.9	19.6	-110.68	133.7	-1.7	220.6	181.7	38.92	5.669		
5,600.0	5,581.7	5,615.2	5,604.7	20.2	20.0	-108.30	145.6	5.3	210.0	170.3	39.66	5.294		
5,700.0	5,681.7	5,714.2	5,702.7	20.6	20.4	-105.67	157.5	12.2	199.7	159.3	40.41	4.942		
5,800.0	5,781.7	5,813.2	5,800.8	20.9	20.7	-102.76	169.4	19.2	189.9	148.7	41.16	4.614		
5,900.0	5,881.7	5,911.7	5,898.3	21.3	21.1	-99.58	181.2	26.0	180.7	138.7	41.92	4.309		
6,000.0	5,981.7	6,008.2	5,994.1	21.6	21.5	-96.58	191.3	32.0	173.1	130.4	42.70	4.053		
6,100.0	6,081.7	6,105.2	6,090.6	22.0	21.8	-94.01	199.4	36.7	167.4	124.0	43.46	3.853		
6,200.0	6,181.7	6,202.6	6,187.8	22.3	22.2	-91.99	205.4	40.2	163.5	119.3	44.20	3.699		
6,300.0	6,281.7	6,300.3	6,285.4	22.7	22.6	-90.64	209.3	42.5	161.1	116.2	44.92	3.587		
6,400.0	6,381.7	6,398.2	6,383.3	23.0	22.9	-90.03	211.0	43.5	160.1	114.4	45.62	3.509		
6,447.0	6,428.7	6,444.7	6,429.7	23.2	23.1	-90.00	211.1	43.5	160.0	114.1	45.94	3.483		
6,500.0	6,481.7	6,502.4	6,482.7	23.4	23.3	-90.00	211.1	43.5	160.0	113.7	46.34	3.453		
6,600.0	6,581.7	6,602.4	6,582.7	23.7	23.6	-90.00	211.1	43.5	160.0	113.0	47.04	3.401		
6,700.0	6,681.7	6,702.4	6,682.7	24.1	24.0	-90.00	211.1	43.5	160.0	112.3	47.75	3.351		
6,800.0	6,781.7	6,802.4	6,782.7	24.4	24.3	-90.00	211.1	43.5	160.0	111.6	48.46	3.302		
6,900.0	6,881.7	6,902.4	6,882.7	24.8	24.7	-90.00	211.1	43.5	160.0	110.8	49.16	3.255		
7,000.0	6,981.7	7,002.4	6,982.7	25.1	25.0	-90.00	211.1	43.5	160.0	110.1	49.87	3.208		
7,100.0	7,081.7	7,102.4	7,082.7	25.5	25.4	-90.00	211.1	43.5	160.0	109.4	50.58	3.163		
7,200.0	7,181.7	7,202.4	7,182.7	25.8	25.8	-90.00	211.1	43.5	160.0	108.7	51.29	3.120		
7,300.0	7,281.7	7,302.4	7,282.7	26.2	26.1	-90.00	211.1	43.5	160.0	108.0	52.00	3.077		
7,400.0	7,381.7	7,402.4	7,382.7	26.5	26.5	-90.00	211.1	43.5	160.0	107.3	52.71	3.036		
7,500.0	7,481.7	7,502.4	7,482.7	26.9	26.8	-90.00	211.1	43.5	160.0	106.6	53.42	2.996		
7,600.0	7,581.7	7,602.4	7,582.7	27.2	27.2	-90.00	211.1	43.5	160.0	105.9	54.13	2.956		
7,700.0	7,681.7	7,702.4	7,682.7	27.6	27.5	-90.00	211.1	43.5	160.0	105.2	54.84	2.918		
7,800.0	7,781.7	7,802.4	7,782.7	28.0	27.9	-90.00	211.1	43.5	160.0	104.5	55.54	2.881		
7,900.0	7,881.7	7,902.4	7,882.7	28.3	28.2	-90.00	211.1	43.5	160.0	103.8	56.25	2.844		
8,000.0	7,981.7	8,002.4	7,982.7	28.7	28.6	-90.00	211.1	43.5	160.0	103.0	56.96	2.809		
8,100.0	8,081.7	8,102.4	8,082.7	29.0	28.9	-90.00	211.1	43.5	160.0	102.3	57.68	2.774		
8,200.0	8,181.7	8,202.4	8,182.7	29.4	29.3	-90.00	211.1	43.5	160.0	101.6	58.39	2.741		
8,300.0	8,281.7	8,302.4	8,282.7	29.7	29.7	-90.00	211.1	43.5	160.0	100.9	59.10	2.708		
8,400.0	8,381.7	8,402.4	8,382.7	30.1	30.0	-90.00	211.1	43.5	160.0	100.2	59.81	2.675		
8,500.0	8,481.7	8,502.4	8,482.7	30.4	30.4	-90.00	211.1	43.5	160.0	99.5	60.52	2.644		
8,600.0	8,581.7	8,602.4	8,582.7	30.8	30.7	-90.00	211.1	43.5	160.0	98.8	61.23	2.613		
8,700.0	8,681.7	8,702.4	8,682.7	31.1	31.1	-90.00	211.1	43.5	160.0	98.1	61.94	2.583		
8,800.0	8,781.7	8,802.4	8,782.7	31.5	31.4	-90.00	211.1	43.5	160.0	97.4	62.65	2.554		
8,900.0	8,881.7	8,902.4	8,882.7	31.8	31.8	-90.00	211.1	43.5	160.0	96.6	63.36	2.525		
9,000.0	8,981.7	9,002.4	8,982.7	32.2	32.1	-90.00	211.1	43.5	160.0	95.9	64.07	2.497		
9,100.0	9,081.7	9,102.4	9,082.7	32.6	32.5	-90.00	211.1	43.5	160.0	95.2	64.79	2.470		
9,200.0	9,181.7	9,202.4	9,182.7	32.9	32.9	-90.00	211.1	43.5	160.0	94.5	65.50	2.443		
9,300.0	9,281.7	9,302.4	9,282.7	33.3	33.2	-90.00	211.1	43.5	160.0	93.8	66.21	2.417		
9,400.0	9,381.7	9,402.4	9,382.7	33.6	33.6	-90.00	211.1	43.5	160.0	93.1	66.92	2.391		
9,500.0	9,481.7	9,502.4	9,482.7	34.0	33.9	-90.00	211.1	43.5	160.0	92.4	67.63	2.366		
9,600.0	9,581.7	9,602.4	9,582.7	34.3	34.3	-90.00	211.1	43.5	160.0	91.7	68.35	2.341		
9,700.0	9,681.7	9,702.4	9,682.7	34.7	34.6	-90.00	211.1	43.5	160.0	91.0	69.06	2.317		
9,800.0	9,781.7	9,802.4	9,782.7	35.0	35.0	-90.00	211.1	43.5	160.0	90.2	69.77	2.293		
9,900.0	9,881.7	9,902.4	9,882.7	35.4	35.3	-90.00	211.1	43.5	160.0	89.5	70.48	2.270		
10,000.0	9,981.7	10,002.4	9,982.7	35.7	35.7	-90.00	211.1	43.5	160.0	88.8	71.20	2.247		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #224H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,100.0	10,081.7	10,102.4	10,082.7	36.1	36.1	-90.00	211.1	43.5	160.0	88.1	71.91	2.225		
10,200.0	10,181.7	10,202.4	10,182.7	36.5	36.4	-90.00	211.1	43.5	160.0	87.4	72.62	2.203		
10,300.0	10,281.7	10,302.4	10,282.7	36.8	36.8	-90.00	211.1	43.5	160.0	86.7	73.33	2.182		
10,400.0	10,381.7	10,402.4	10,382.7	37.2	37.1	-90.00	211.1	43.5	160.0	86.0	74.05	2.161		
10,500.0	10,481.7	10,502.4	10,482.7	37.5	37.5	-90.00	211.1	43.5	160.0	85.3	74.76	2.140		
10,600.0	10,581.7	10,602.4	10,582.7	37.9	37.8	-90.00	211.1	43.5	160.0	84.5	75.47	2.120		
10,700.0	10,681.7	10,702.4	10,682.7	38.2	38.2	-90.00	211.1	43.5	160.0	83.8	76.19	2.100		
10,800.0	10,781.7	10,802.4	10,782.7	38.6	38.6	-90.00	211.1	43.5	160.0	83.1	76.90	2.081		
10,831.3	10,813.0	10,829.0	10,814.0	38.7	38.6	-90.00	211.1	43.5	160.0	82.9	77.11	2.075		
10,850.0	10,831.7	10,847.6	10,832.7	38.8	38.7	85.01	211.1	43.5	160.0	82.7	77.24	2.071		
10,900.0	10,881.5	10,902.5	10,882.5	38.9	38.9	86.39	211.1	43.5	159.7	82.1	77.60	2.058		
10,950.0	10,930.8	10,946.8	10,931.8	39.1	39.1	89.30	211.1	43.5	159.4	81.5	77.93	2.045		
10,959.3	10,939.9	10,955.9	10,940.9	39.1	39.1	90.00	211.1	43.5	159.4	81.4	77.99	2.044		
11,000.0	10,979.2	11,004.8	10,980.2	39.2	39.3	93.58	211.1	43.5	159.7	81.4	78.30	2.040 SF		
11,050.0	11,026.4	11,042.4	11,027.4	39.3	39.4	98.93	211.1	43.5	161.6	83.0	78.61	2.056		
11,100.0	11,071.9	11,087.9	11,072.9	39.5	39.6	104.92	211.1	43.5	166.3	87.4	78.94	2.107		
11,150.0	11,115.5	11,131.5	11,116.5	39.6	39.7	111.02	211.1	43.5	174.9	95.7	79.24	2.208		
11,200.0	11,156.7	11,172.7	11,157.7	39.7	39.9	116.73	211.1	43.5	188.3	108.8	79.52	2.368		
11,250.0	11,195.4	11,211.4	11,196.4	39.8	40.0	121.67	211.1	43.5	207.0	127.2	79.77	2.595		
11,300.0	11,231.1	11,247.1	11,232.1	39.9	40.1	125.62	211.1	43.5	230.8	150.9	79.98	2.886		
11,350.0	11,263.7	11,279.6	11,264.7	39.9	40.3	128.45	211.1	43.5	259.6	179.4	80.16	3.238		
11,400.0	11,292.8	11,308.8	11,293.8	40.0	40.4	130.10	211.1	43.5	292.7	212.4	80.32	3.645		
11,450.0	11,318.3	11,334.2	11,319.3	40.1	40.4	130.49	211.1	43.5	329.7	249.2	80.44	4.098		
11,500.0	11,339.9	11,355.9	11,340.9	40.2	40.5	129.43	211.1	43.5	369.7	289.2	80.54	4.591		
11,550.0	11,357.5	11,373.5	11,358.5	40.3	40.6	126.61	211.1	43.5	412.4	331.8	80.62	5.116		
11,600.0	11,371.0	11,386.9	11,372.0	40.4	40.6	121.42	211.1	43.5	457.2	376.5	80.67	5.668		
11,650.0	11,380.2	11,403.8	11,381.2	40.5	40.7	112.98	211.1	43.5	503.6	422.8	80.73	6.238		
11,700.0	11,385.1	11,401.1	11,386.1	40.7	40.7	100.25	211.1	43.5	551.0	470.2	80.71	6.826		
11,731.3	11,386.0	11,401.9	11,387.0	40.7	40.7	90.00	211.1	43.5	581.0	500.3	80.71	7.198		
11,800.0	11,386.0	11,401.9	11,387.0	40.9	40.7	90.00	211.1	43.5	647.5	566.8	80.71	8.023		
11,900.0	11,386.0	11,401.9	11,387.0	41.3	40.7	90.00	211.1	43.5	745.6	664.9	80.70	9.239		
12,009.9	11,386.0	11,401.9	11,387.0	41.7	40.7	90.00	211.1	43.5	854.5	773.8	80.71	10.588		
12,100.0	11,386.0	11,401.9	11,387.0	42.1	40.7	90.00	211.1	43.5	944.2	863.5	80.71	11.698		
12,200.0	11,386.0	11,401.9	11,387.0	42.6	40.7	90.00	211.1	43.5	1,043.7	963.0	80.72	12.931		
12,300.0	11,386.0	13,428.0	12,514.0	43.2	47.2	-179.96	-927.9	144.5	1,127.0	1,086.3	40.71	27.681		
12,400.0	11,386.0	13,528.0	12,514.0	43.8	47.8	-179.96	-1,027.9	145.3	1,127.0	1,085.6	41.38	27.235		
12,500.0	11,386.0	13,628.0	12,514.0	44.5	48.4	-179.96	-1,127.9	146.1	1,127.0	1,084.9	42.10	26.773		
12,600.0	11,386.0	13,728.0	12,514.0	45.2	49.1	-179.96	-1,227.9	146.9	1,127.0	1,084.1	42.86	26.298		
12,700.0	11,386.0	13,828.0	12,514.0	46.0	49.8	-179.96	-1,327.9	147.8	1,127.0	1,083.3	43.66	25.814		
12,800.0	11,386.0	13,928.0	12,514.0	46.8	50.6	-179.96	-1,427.9	148.6	1,127.0	1,082.5	44.50	25.324		
12,900.0	11,386.0	14,028.0	12,514.0	47.7	51.4	-179.96	-1,527.9	149.4	1,127.0	1,081.6	45.39	24.831		
13,000.0	11,386.0	14,128.0	12,514.0	48.6	52.2	-179.96	-1,627.9	150.2	1,127.0	1,080.7	46.31	24.338		
13,100.0	11,386.0	14,228.0	12,514.0	49.5	53.1	-179.96	-1,727.9	151.0	1,127.0	1,079.7	47.26	23.847		
13,200.0	11,386.0	14,328.0	12,514.0	50.5	54.0	-179.96	-1,827.9	151.8	1,127.0	1,078.8	48.24	23.360		
13,300.0	11,386.0	14,428.0	12,514.0	51.5	55.0	-179.96	-1,927.8	152.7	1,127.0	1,077.7	49.26	22.879		
13,400.0	11,386.0	14,528.0	12,514.0	52.6	56.0	-179.96	-2,027.8	153.5	1,127.0	1,076.7	50.30	22.404		
13,500.0	11,386.0	14,628.0	12,514.0	53.6	57.0	-179.96	-2,127.8	154.3	1,127.0	1,075.6	51.37	21.937		
13,600.0	11,386.0	14,728.0	12,514.0	54.7	58.0	-179.97	-2,227.8	155.1	1,127.0	1,074.5	52.47	21.479		
13,700.0	11,386.0	14,828.0	12,514.0	55.9	59.1	-179.97	-2,327.8	155.9	1,127.0	1,073.4	53.59	21.030		
13,800.0	11,386.0	14,928.0	12,514.0	57.0	60.2	-179.97	-2,427.8	156.7	1,127.0	1,072.3	54.73	20.592		
13,900.0	11,386.0	15,028.0	12,514.0	58.2	61.4	-179.97	-2,527.8	157.5	1,127.0	1,071.1	55.89	20.164		
14,000.0	11,386.0	15,128.0	12,514.0	59.4	62.5	-179.97	-2,627.8	158.4	1,127.0	1,069.9	57.07	19.746		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #224H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,100.0	11,386.0	15,228.0	12,514.0	60.6	63.7	-179.97	-2,727.8	159.2	1,127.0	1,068.7	58.27	19.340		
14,200.0	11,386.0	15,328.0	12,514.0	61.9	64.9	-179.97	-2,827.8	160.0	1,127.0	1,067.5	59.49	18.944		
14,300.0	11,386.0	15,428.0	12,514.0	63.1	66.1	-179.97	-2,927.8	160.8	1,127.0	1,066.3	60.72	18.560		
14,400.0	11,386.0	15,528.0	12,514.0	64.4	67.3	-179.97	-3,027.8	161.6	1,127.0	1,065.0	61.97	18.186		
14,500.0	11,386.0	15,628.0	12,514.0	65.7	68.6	-179.97	-3,127.8	162.4	1,127.0	1,063.8	63.23	17.823		
14,600.0	11,386.0	15,728.0	12,514.0	67.0	69.8	-179.97	-3,227.8	163.2	1,127.0	1,062.5	64.51	17.471		
14,700.0	11,386.0	15,828.0	12,514.0	68.4	71.1	-179.97	-3,327.8	164.1	1,127.0	1,061.2	65.80	17.129		
14,800.0	11,386.0	15,928.0	12,514.0	69.7	72.4	-179.97	-3,427.8	164.9	1,127.0	1,059.9	67.10	16.797		
14,900.0	11,386.0	16,028.0	12,514.0	71.1	73.7	-179.97	-3,527.8	165.7	1,127.0	1,058.6	68.41	16.475		
15,000.0	11,386.0	16,128.0	12,514.0	72.4	75.0	-179.97	-3,627.8	166.5	1,127.0	1,057.3	69.73	16.162		
15,100.0	11,386.0	16,228.0	12,514.0	73.8	76.4	-179.97	-3,727.8	167.3	1,127.0	1,055.9	71.06	15.859		
15,200.0	11,386.0	16,328.0	12,514.0	75.2	77.7	-179.97	-3,827.8	168.1	1,127.0	1,054.6	72.40	15.566		
15,300.0	11,386.0	16,428.0	12,514.0	76.6	79.1	-179.97	-3,927.8	168.9	1,127.0	1,053.2	73.75	15.280		
15,400.0	11,386.0	16,528.0	12,514.0	78.0	80.5	-179.97	-4,027.8	169.8	1,127.0	1,051.9	75.11	15.004		
15,500.0	11,386.0	16,628.0	12,514.0	79.4	81.8	-179.97	-4,127.8	170.6	1,127.0	1,050.5	76.48	14.736		
15,600.0	11,386.0	16,728.0	12,514.0	80.9	83.2	-179.97	-4,227.8	171.4	1,127.0	1,049.1	77.85	14.476		
15,700.0	11,386.0	16,828.0	12,514.0	82.3	84.6	-179.97	-4,327.8	172.2	1,127.0	1,047.8	79.24	14.223		
15,800.0	11,386.0	16,928.0	12,514.0	83.7	86.0	-179.97	-4,427.8	173.0	1,127.0	1,046.4	80.63	13.978		
15,900.0	11,386.0	17,028.0	12,514.0	85.2	87.5	-179.97	-4,527.8	173.8	1,127.0	1,045.0	82.02	13.740		
16,000.0	11,386.0	17,128.0	12,514.0	86.7	88.9	-179.97	-4,627.8	174.6	1,127.0	1,043.6	83.42	13.510		
16,100.0	11,386.0	17,228.0	12,514.0	88.1	90.3	-179.97	-4,727.8	175.5	1,127.0	1,042.2	84.83	13.286		
16,200.0	11,386.0	17,328.0	12,514.0	89.6	91.8	-179.97	-4,827.8	176.3	1,127.0	1,040.8	86.24	13.068		
16,300.0	11,386.0	17,428.0	12,514.0	91.1	93.2	-179.97	-4,927.7	177.1	1,127.0	1,039.3	87.66	12.857		
16,400.0	11,386.0	17,528.0	12,514.0	92.6	94.7	-179.98	-5,027.7	177.9	1,127.0	1,037.9	89.08	12.651		
16,500.0	11,386.0	17,628.0	12,514.0	94.0	96.1	-179.98	-5,127.7	178.7	1,127.0	1,036.5	90.51	12.452		
16,600.0	11,386.0	17,728.0	12,514.0	95.5	97.6	-179.98	-5,227.7	179.5	1,127.0	1,035.1	91.94	12.258		
16,700.0	11,386.0	17,828.0	12,514.0	97.0	99.1	-179.98	-5,327.7	180.3	1,127.0	1,033.6	93.38	12.069		
16,800.0	11,386.0	17,928.0	12,514.0	98.5	100.6	-179.98	-5,427.7	181.2	1,127.0	1,032.2	94.82	11.885		
16,900.0	11,386.0	18,028.0	12,514.0	100.1	102.0	-179.98	-5,527.7	182.0	1,127.0	1,030.7	96.27	11.707		
17,000.0	11,386.0	18,128.0	12,514.0	101.6	103.5	-179.98	-5,627.7	182.8	1,127.0	1,029.3	97.72	11.533		
17,100.0	11,386.0	18,228.0	12,514.0	103.1	105.0	-179.98	-5,727.7	183.6	1,127.0	1,027.8	99.17	11.365		
17,200.0	11,386.0	18,328.0	12,514.0	104.6	106.5	-179.98	-5,827.7	184.4	1,127.0	1,026.4	100.62	11.200		
17,300.0	11,386.0	18,428.0	12,514.0	106.1	108.0	-179.98	-5,927.7	185.2	1,127.0	1,024.9	102.08	11.040		
17,400.0	11,386.0	18,528.0	12,514.0	107.7	109.5	-179.98	-6,027.7	186.0	1,127.0	1,023.5	103.55	10.884		
17,500.0	11,386.0	18,628.0	12,514.0	109.2	111.1	-179.98	-6,127.7	186.9	1,127.0	1,022.0	105.01	10.732		
17,600.0	11,386.0	18,728.0	12,514.0	110.7	112.6	-179.98	-6,227.7	187.7	1,127.0	1,020.5	106.48	10.584		
17,700.0	11,386.0	18,828.0	12,514.0	112.3	114.1	-179.98	-6,327.7	188.5	1,127.0	1,019.0	107.95	10.440		
17,800.0	11,386.0	18,928.0	12,514.0	113.8	115.6	-179.98	-6,427.7	189.3	1,127.0	1,017.6	109.43	10.299		
17,900.0	11,386.0	19,028.0	12,514.0	115.4	117.1	-179.98	-6,527.7	190.1	1,127.0	1,016.1	110.90	10.162		
18,000.0	11,386.0	19,128.0	12,514.0	116.9	118.7	-179.98	-6,627.7	190.9	1,127.0	1,014.6	112.38	10.028		
18,100.0	11,386.0	19,228.0	12,514.0	118.5	120.2	-179.98	-6,727.7	191.7	1,127.0	1,013.1	113.87	9.898		
18,200.0	11,386.0	19,328.0	12,514.0	120.0	121.7	-179.98	-6,827.7	192.6	1,127.0	1,011.7	115.35	9.770		
18,300.0	11,386.0	19,428.0	12,514.0	121.6	123.3	-179.98	-6,927.7	193.4	1,127.0	1,010.2	116.84	9.646		
18,400.0	11,386.0	19,528.0	12,514.0	123.2	124.8	-179.98	-7,027.7	194.2	1,127.0	1,008.7	118.32	9.525		
18,500.0	11,386.0	19,628.0	12,514.0	124.7	126.4	-179.98	-7,127.7	195.0	1,127.0	1,007.2	119.81	9.406		
18,600.0	11,386.0	19,728.0	12,514.0	126.3	127.9	-179.98	-7,227.7	195.8	1,127.0	1,005.7	121.31	9.290		
18,700.0	11,386.0	19,828.0	12,514.0	127.9	129.5	-179.98	-7,327.7	196.6	1,127.0	1,004.2	122.80	9.177		
18,800.0	11,386.0	19,928.0	12,514.0	129.4	131.0	-179.98	-7,427.7	197.4	1,127.0	1,002.7	124.30	9.067		
18,900.0	11,386.0	20,028.0	12,514.0	131.0	132.6	-179.98	-7,527.7	198.3	1,127.0	1,001.2	125.80	8.959		
19,000.0	11,386.0	20,128.0	12,514.0	132.6	134.1	-179.98	-7,627.7	199.1	1,127.0	999.7	127.30	8.853		
19,100.0	11,386.0	20,228.0	12,514.0	134.1	135.7	-179.98	-7,727.7	199.9	1,127.0	998.2	128.80	8.750		
19,200.0	11,386.0	20,328.0	12,514.0	135.7	137.3	-179.99	-7,827.7	200.7	1,127.0	996.7	130.30	8.649		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #224H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,300.0	11,386.0	20,428.0	12,514.0	137.3	138.8	-179.99	-7,927.6	201.5	1,127.0	995.2	131.81	8.550		
19,400.0	11,386.0	20,528.0	12,514.0	138.9	140.4	-179.99	-8,027.6	202.3	1,127.0	993.7	133.31	8.454		
19,500.0	11,386.0	20,628.0	12,514.0	140.5	142.0	-179.99	-8,127.6	203.1	1,127.0	992.2	134.82	8.359		
19,600.0	11,386.0	20,728.0	12,514.0	142.0	143.5	-179.99	-8,227.6	204.0	1,127.0	990.7	136.33	8.267		
19,700.0	11,386.0	20,828.0	12,514.0	143.6	145.1	-179.99	-8,327.6	204.8	1,127.0	989.2	137.84	8.176		
19,800.0	11,386.0	20,928.0	12,514.0	145.2	146.7	-179.99	-8,427.6	205.6	1,127.0	987.7	139.35	8.088		
19,900.0	11,386.0	21,028.0	12,514.0	146.8	148.2	-179.99	-8,527.6	206.4	1,127.0	986.1	140.86	8.001		
20,000.0	11,386.0	21,128.0	12,514.0	148.4	149.8	-179.99	-8,627.6	207.2	1,127.0	984.6	142.38	7.916		
20,100.0	11,386.0	21,228.0	12,514.0	150.0	151.4	-179.99	-8,727.6	208.0	1,127.0	983.1	143.89	7.832		
20,200.0	11,386.0	21,328.0	12,514.0	151.6	153.0	-179.99	-8,827.6	208.8	1,127.0	981.6	145.41	7.751		
20,300.0	11,386.0	21,428.0	12,514.0	153.2	154.6	-179.99	-8,927.6	209.7	1,127.0	980.1	146.93	7.671		
20,400.0	11,386.0	21,528.0	12,514.0	154.8	156.2	-179.99	-9,027.6	210.5	1,127.0	978.6	148.44	7.592		
20,500.0	11,386.0	21,628.0	12,514.0	156.4	157.7	-179.99	-9,127.6	211.3	1,127.0	977.0	149.96	7.515		
20,600.0	11,386.0	21,728.0	12,514.0	158.0	159.3	-179.99	-9,227.6	212.1	1,127.0	975.5	151.49	7.440		
20,700.0	11,386.0	21,828.0	12,514.0	159.6	160.9	-179.99	-9,327.6	212.9	1,127.0	974.0	153.01	7.366		
20,800.0	11,386.0	21,928.0	12,514.0	161.2	162.5	-179.99	-9,427.6	213.7	1,127.0	972.5	154.53	7.293		
20,900.0	11,386.0	22,028.0	12,514.0	162.8	164.1	-179.99	-9,527.6	214.5	1,127.0	970.9	156.05	7.222		
21,000.0	11,386.0	22,128.0	12,514.0	164.4	165.7	-179.99	-9,627.6	215.4	1,127.0	969.4	157.58	7.152		
21,068.3	11,386.0	22,203.7	12,514.0	165.5	166.9	-179.99	-9,695.9	215.9	1,127.0	968.3	158.68	7.103		
21,100.0	11,386.0	22,228.0	12,514.0	166.0	167.3	-179.99	-9,727.6	216.2	1,127.0	967.9	159.10	7.083		
21,200.0	11,386.0	22,328.0	12,514.0	167.6	168.9	-179.99	-9,827.6	217.0	1,127.0	966.4	160.63	7.016		
21,300.0	11,386.0	22,428.0	12,514.0	169.2	170.5	-179.99	-9,927.6	217.8	1,127.0	964.8	162.16	6.950		
21,400.0	11,386.0	22,528.0	12,514.0	170.8	172.1	-179.99	-10,027.6	218.6	1,127.0	963.3	163.68	6.885		
21,500.0	11,386.0	22,628.0	12,514.0	172.4	173.7	-179.99	-10,127.6	219.4	1,127.0	961.8	165.21	6.822		
21,600.0	11,386.0	22,728.0	12,514.0	174.0	175.3	-179.99	-10,227.6	220.2	1,127.0	960.3	166.74	6.759		
21,700.0	11,386.0	22,828.0	12,514.0	175.6	176.9	-179.99	-10,327.6	221.1	1,127.0	958.7	168.27	6.697		
21,800.0	11,386.0	22,928.0	12,514.0	177.2	178.5	-179.99	-10,427.6	221.9	1,127.0	957.2	169.80	6.637		
21,900.0	11,386.0	23,028.0	12,514.0	178.8	180.1	-179.99	-10,527.6	222.7	1,127.0	955.7	171.33	6.578		
22,000.0	11,386.0	23,128.0	12,514.0	180.4	181.7	-179.99	-10,627.6	223.5	1,127.0	954.1	172.87	6.519		
22,100.0	11,386.0	23,228.0	12,514.0	182.0	183.3	-180.00	-10,727.6	224.3	1,127.0	952.6	174.40	6.462		
22,200.0	11,386.0	23,328.0	12,514.0	183.7	184.9	-180.00	-10,827.6	225.1	1,127.0	951.1	175.93	6.406		
22,300.0	11,386.0	23,428.0	12,514.0	185.3	186.5	-180.00	-10,927.6	225.9	1,127.0	949.5	177.47	6.350		
22,400.0	11,386.0	23,528.0	12,514.0	186.9	188.1	-180.00	-11,027.5	226.8	1,127.0	948.0	179.00	6.296		
22,500.0	11,386.0	23,628.0	12,514.0	188.5	189.7	-180.00	-11,127.5	227.6	1,127.0	946.5	180.54	6.242		
22,600.0	11,386.0	23,728.0	12,514.0	190.1	191.3	-180.00	-11,227.5	228.4	1,127.0	944.9	182.07	6.190		
22,700.0	11,386.0	23,828.0	12,514.0	191.7	192.9	-180.00	-11,327.5	229.2	1,127.0	943.4	183.61	6.138		
22,800.0	11,386.0	23,928.0	12,514.0	193.3	194.5	-180.00	-11,427.5	230.0	1,127.0	941.9	185.15	6.087		
22,900.0	11,386.0	24,028.0	12,514.0	195.0	196.1	-180.00	-11,527.5	230.8	1,127.0	940.3	186.68	6.037		
23,000.0	11,386.0	24,128.0	12,514.0	196.6	197.7	-180.00	-11,627.5	231.6	1,127.0	938.8	188.22	5.988		
23,100.0	11,386.0	24,228.0	12,514.0	198.2	199.3	-180.00	-11,727.5	232.5	1,127.0	937.2	189.76	5.939		
23,200.0	11,386.0	24,328.0	12,514.0	199.8	200.9	-180.00	-11,827.5	233.3	1,127.0	935.7	191.30	5.891		
23,300.0	11,386.0	24,428.0	12,514.0	201.4	202.6	-180.00	-11,927.5	234.1	1,127.0	934.2	192.84	5.844		
23,400.0	11,386.0	24,528.0	12,514.0	203.0	204.2	-180.00	-12,027.5	234.9	1,127.0	932.6	194.38	5.798		
23,500.0	11,386.0	24,628.0	12,514.0	204.7	205.8	180.00	-12,127.5	235.7	1,127.0	931.1	195.92	5.752		
23,600.0	11,386.0	24,728.0	12,514.0	206.3	207.4	180.00	-12,227.5	236.5	1,127.0	929.5	197.46	5.707		
23,705.7	11,386.0	24,833.7	12,514.0	208.0	209.1	180.00	-12,333.2	237.4	1,127.0	927.9	199.09	5.661		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #228H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	1.0	1.0	0.0	0.0	-110.97	-30.6	-79.8	85.4					
100.0	100.0	101.0	101.0	0.1	0.1	-110.97	-30.6	-79.8	85.4	85.2	0.26	328.696		
200.0	200.0	201.0	201.0	0.5	0.5	-110.97	-30.6	-79.8	85.4	84.4	0.98	87.451		
300.0	300.0	301.0	301.0	0.8	0.8	-110.97	-30.6	-79.8	85.4	83.7	1.69	50.435		
400.0	400.0	401.0	401.0	1.2	1.2	-110.97	-30.6	-79.8	85.4	83.0	2.41	35.436		
500.0	500.0	501.0	501.0	1.6	1.6	-110.97	-30.6	-79.8	85.4	82.3	3.13	27.313 CC		
600.0	600.0	601.0	601.0	1.9	1.9	-155.16	-30.6	-79.8	86.2	82.4	3.84	22.439		
700.0	700.0	701.0	701.0	2.3	2.3	-155.86	-30.6	-79.8	88.6	84.0	4.56	19.447		
800.0	799.9	800.9	800.9	2.6	2.6	-156.95	-30.6	-79.8	92.6	87.3	5.27	17.568		
900.0	899.7	900.7	900.7	3.0	3.0	-158.32	-30.6	-79.8	98.2	92.3	5.99	16.411		
1,000.0	999.4	1,000.4	1,000.4	3.4	3.4	-159.87	-30.6	-79.8	105.6	98.9	6.70	15.751		
1,100.0	1,098.9	1,100.1	1,099.9	3.7	3.7	-161.49	-30.6	-79.8	114.6	107.2	7.42	15.448		
1,200.0	1,198.3	1,200.7	1,199.3	4.1	4.1	-163.10	-30.6	-79.8	125.4	117.3	8.14	15.403		
1,300.0	1,297.4	1,301.6	1,298.4	4.5	4.4	-164.64	-30.6	-79.8	138.0	129.1	8.87	15.561		
1,400.0	1,396.4	1,402.6	1,397.4	4.9	4.8	-166.04	-30.6	-79.8	151.4	141.9	9.59	15.792		
1,500.0	1,495.5	1,503.5	1,496.5	5.3	5.2	-167.20	-30.6	-79.8	165.0	154.7	10.31	15.997		
1,600.0	1,594.5	1,604.5	1,595.5	5.7	5.5	-168.19	-30.6	-79.8	178.6	167.6	11.04	16.180		
1,700.0	1,693.5	1,705.5	1,694.5	6.1	5.9	-169.04	-30.6	-79.8	192.2	180.5	11.76	16.343		
1,800.0	1,792.5	1,806.5	1,793.5	6.5	6.2	-169.77	-30.6	-79.8	205.9	193.4	12.49	16.489		
1,900.0	1,891.6	1,907.4	1,892.6	6.9	6.6	-170.42	-30.6	-79.8	219.6	206.4	13.21	16.621		
2,000.0	1,990.6	2,008.4	1,991.6	7.3	7.0	-170.99	-30.6	-79.8	233.4	219.4	13.94	16.740		
2,100.0	2,089.6	2,109.4	2,090.6	7.7	7.3	-171.49	-30.6	-79.8	247.1	232.5	14.67	16.849		
2,200.0	2,188.6	2,189.6	2,189.6	8.1	7.6	-171.94	-30.6	-79.8	260.9	245.6	15.32	17.030		
2,300.0	2,287.7	2,288.7	2,288.7	8.5	8.0	-172.35	-30.6	-79.8	274.7	258.7	16.04	17.125		
2,400.0	2,386.7	2,387.7	2,387.7	8.9	8.3	-172.72	-30.6	-79.8	288.5	271.7	16.76	17.212		
2,500.0	2,485.7	2,486.7	2,486.7	9.3	8.7	-173.05	-30.6	-79.8	302.3	284.8	17.48	17.292		
2,600.0	2,584.8	2,585.8	2,585.8	9.8	9.0	-173.36	-30.6	-79.8	316.1	297.9	18.20	17.366		
2,700.0	2,683.8	2,684.8	2,684.8	10.2	9.4	-173.64	-30.6	-79.8	330.0	311.0	18.93	17.435		
2,739.3	2,722.7	2,723.7	2,723.7	10.3	9.5	-173.74	-30.6	-79.8	335.4	316.2	19.21	17.461		
2,800.0	2,782.9	2,783.9	2,783.9	10.6	9.7	-173.90	-30.6	-79.8	343.3	323.7	19.65	17.475		
2,900.0	2,882.3	2,883.3	2,883.3	11.0	10.1	-174.11	-30.6	-79.8	354.3	333.9	20.37	17.398		
3,000.0	2,981.9	2,982.9	2,982.9	11.4	10.5	-174.26	-30.6	-79.8	362.7	341.6	21.08	17.203		
3,100.0	3,081.7	3,082.7	3,082.7	11.7	10.8	-174.35	-30.6	-79.8	368.5	346.7	21.80	16.904		
3,200.0	3,181.7	3,182.7	3,182.7	12.1	11.2	-174.41	-30.6	-79.8	371.7	349.2	22.51	16.511		
3,272.6	3,254.3	3,255.3	3,255.3	12.3	11.4	-130.47	-30.6	-79.8	372.4	349.4	23.03	16.172		
3,300.0	3,281.7	3,282.7	3,282.7	12.4	11.5	-130.47	-30.6	-79.8	372.4	349.2	23.22	16.037		
3,400.0	3,381.7	3,382.7	3,382.7	12.7	11.9	-130.47	-30.6	-79.8	372.4	348.5	23.93	15.564		
3,500.0	3,481.7	3,482.7	3,482.7	13.1	12.3	-130.47	-30.6	-79.8	372.4	347.7	24.63	15.117		
3,600.0	3,581.7	3,582.7	3,582.7	13.4	12.6	-130.47	-30.6	-79.8	372.4	347.0	25.34	14.695		
3,700.0	3,681.7	3,682.7	3,682.7	13.7	13.0	-130.47	-30.6	-79.8	372.4	346.3	26.05	14.296		
3,800.0	3,781.7	3,782.7	3,782.7	14.1	13.3	-130.47	-30.6	-79.8	372.4	345.6	26.76	13.917		
3,900.0	3,881.7	3,882.7	3,882.7	14.4	13.7	-130.47	-30.6	-79.8	372.4	344.9	27.47	13.558		
4,000.0	3,981.7	3,982.7	3,982.7	14.7	14.0	-130.47	-30.6	-79.8	372.4	344.2	28.17	13.217		
4,100.0	4,081.7	4,082.7	4,082.7	15.1	14.4	-130.47	-30.6	-79.8	372.4	343.5	28.88	12.892		
4,200.0	4,181.7	4,182.7	4,182.7	15.4	14.8	-130.47	-30.6	-79.8	372.4	342.8	29.59	12.583		
4,300.0	4,281.7	4,282.7	4,282.7	15.8	15.1	-130.47	-30.6	-79.8	372.4	342.1	30.30	12.288		
4,400.0	4,381.7	4,382.7	4,382.7	16.1	15.5	-130.47	-30.6	-79.8	372.4	341.4	31.01	12.006		
4,500.0	4,481.7	4,482.7	4,482.7	16.4	15.8	-130.47	-30.6	-79.8	372.4	340.7	31.73	11.737		
4,600.0	4,581.7	4,582.7	4,582.7	16.8	16.2	-130.47	-30.6	-79.8	372.4	339.9	32.44	11.480		
4,700.0	4,681.7	4,682.7	4,682.7	17.1	16.6	-130.47	-30.6	-79.8	372.4	339.2	33.15	11.234		
4,800.0	4,781.7	4,782.7	4,782.7	17.5	16.9	-130.47	-30.6	-79.8	372.4	338.5	33.86	10.998		
4,900.0	4,881.7	4,882.7	4,882.7	17.8	17.3	-130.47	-30.6	-79.8	372.4	337.8	34.57	10.771		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #228H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,000.0	4,981.7	4,982.7	4,982.7	18.2	17.6	-130.47	-30.6	-79.8	372.4	337.1	35.28	10.554		
5,100.0	5,081.7	5,082.7	5,082.7	18.5	18.0	-130.47	-30.6	-79.8	372.4	336.4	36.00	10.345		
5,200.0	5,181.7	5,182.7	5,182.7	18.8	18.3	-130.47	-30.6	-79.8	372.4	335.7	36.71	10.144		
5,300.0	5,281.7	5,282.7	5,282.7	19.2	18.7	-130.47	-30.6	-79.8	372.4	335.0	37.42	9.951		
5,400.0	5,381.7	5,382.7	5,382.7	19.5	19.1	-130.47	-30.6	-79.8	372.4	334.2	38.13	9.765		
5,500.0	5,481.7	5,482.7	5,482.7	19.9	19.4	-130.47	-30.6	-79.8	372.4	333.5	38.85	9.586		
5,600.0	5,581.7	5,588.0	5,588.0	20.2	19.8	-130.51	-30.3	-79.1	371.8	332.2	39.58	9.392		
5,700.0	5,681.7	5,694.4	5,694.3	20.6	20.2	-130.65	-29.5	-76.7	369.5	329.2	40.31	9.166		
5,800.0	5,781.7	5,800.6	5,800.5	20.9	20.5	-130.92	-28.0	-72.3	365.5	324.5	41.02	8.909		
5,900.0	5,881.7	5,906.6	5,906.3	21.3	20.9	-131.31	-25.8	-66.1	359.8	318.0	41.73	8.622		
6,000.0	5,981.7	6,012.4	6,011.7	21.6	21.3	-131.83	-23.1	-58.1	352.4	309.9	42.42	8.307		
6,100.0	6,081.7	6,117.8	6,116.6	22.0	21.6	-132.50	-19.7	-48.3	343.3	300.2	43.09	7.966		
6,200.0	6,181.7	6,222.8	6,220.9	22.3	22.0	-133.34	-15.6	-36.8	332.6	288.8	43.76	7.600		
6,300.0	6,281.7	6,325.9	6,323.1	22.7	22.4	-134.37	-11.1	-23.7	320.4	275.9	44.43	7.210		
6,400.0	6,381.7	6,424.9	6,421.1	23.0	22.7	-135.47	-6.6	-10.7	307.8	262.7	45.14	6.819		
6,500.0	6,481.7	6,524.0	6,519.2	23.4	23.1	-136.66	-2.1	2.4	295.4	249.5	45.85	6.442		
6,600.0	6,581.7	6,623.0	6,617.3	23.7	23.5	-137.96	2.4	15.4	283.1	236.5	46.56	6.080		
6,700.0	6,681.7	6,722.0	6,715.3	24.1	23.8	-139.38	7.0	28.4	271.0	223.7	47.28	5.731		
6,800.0	6,781.7	6,821.1	6,813.4	24.4	24.2	-140.93	11.5	41.4	259.0	211.0	48.00	5.396		
6,900.0	6,881.7	6,920.1	6,911.4	24.8	24.5	-142.62	16.0	54.4	247.2	198.5	48.72	5.074		
7,000.0	6,981.7	7,019.1	7,009.5	25.1	24.9	-144.48	20.5	67.5	235.7	186.3	49.45	4.767		
7,100.0	7,081.7	7,118.1	7,107.6	25.5	25.3	-146.53	25.0	80.5	224.5	174.3	50.19	4.473		
7,200.0	7,181.7	7,217.2	7,205.6	25.8	25.6	-148.79	29.5	93.5	213.6	162.6	50.93	4.193		
7,300.0	7,281.7	7,316.2	7,303.7	26.2	26.0	-151.29	34.0	106.5	203.0	151.3	51.67	3.928		
7,400.0	7,381.7	7,415.2	7,401.8	26.5	26.4	-154.05	38.6	119.5	192.8	140.4	52.43	3.678		
7,500.0	7,481.7	7,514.2	7,499.8	26.9	26.8	-157.11	43.1	132.6	183.2	130.0	53.19	3.444		
7,600.0	7,581.7	7,613.3	7,597.9	27.2	27.1	-160.49	47.6	145.6	174.1	120.2	53.96	3.227		
7,700.0	7,681.7	7,712.3	7,696.0	27.6	27.5	-164.23	52.1	158.6	165.8	111.0	54.74	3.028		
7,800.0	7,781.7	7,811.3	7,794.0	28.0	27.9	-168.34	56.6	171.6	158.1	102.6	55.52	2.848		
7,900.0	7,881.7	7,910.3	7,892.1	28.3	28.3	-172.83	61.1	184.7	151.4	95.1	56.31	2.689		
8,000.0	7,981.7	8,009.4	7,990.1	28.7	28.6	-177.70	65.7	197.7	145.8	88.7	57.11	2.552		
8,100.0	8,081.7	8,108.4	8,088.2	29.0	29.0	177.09	70.2	210.7	141.2	83.3	57.90	2.439		
8,200.0	8,181.7	8,207.4	8,186.3	29.4	29.4	171.58	74.7	223.7	138.0	79.3	58.68	2.351		
8,300.0	8,281.7	8,306.5	8,284.3	29.7	29.8	165.87	79.2	236.7	136.0	76.6	59.45	2.288		
8,386.0	8,367.6	8,391.6	8,368.6	30.0	30.1	160.87	83.1	247.9	135.5	75.4	60.10	2.255		
8,400.0	8,381.7	8,405.5	8,382.4	30.1	30.2	160.05	83.7	249.8	135.5	75.3	60.20	2.251 ES		
8,500.0	8,481.7	8,504.5	8,480.5	30.4	30.6	154.25	88.2	262.8	136.4	75.5	60.93	2.239 SF		
8,600.0	8,581.7	8,603.5	8,578.5	30.8	30.9	148.59	92.8	275.8	138.7	77.1	61.64	2.251		
8,700.0	8,681.7	8,702.6	8,676.6	31.1	31.3	143.16	97.3	288.8	142.4	80.1	62.32	2.284		
8,800.0	8,781.7	8,801.6	8,774.6	31.5	31.7	138.03	101.8	301.8	147.2	84.3	62.99	2.337		
8,900.0	8,881.7	8,900.6	8,872.7	31.8	32.1	133.27	106.3	314.9	153.2	89.6	63.65	2.407		
9,000.0	8,981.7	9,000.4	8,970.8	32.2	32.5	128.88	110.8	327.9	160.2	95.9	64.31	2.491		
9,100.0	9,081.7	9,098.7	9,068.8	32.6	32.9	124.88	115.3	340.9	168.0	103.1	64.96	2.587		
9,200.0	9,181.7	9,202.3	9,166.9	32.9	33.3	121.25	119.9	353.9	176.6	111.0	65.62	2.691		
9,300.0	9,281.7	9,303.3	9,265.0	33.3	33.7	117.96	124.4	366.9	185.9	119.6	66.28	2.804		
9,400.0	9,381.7	9,395.7	9,363.0	33.6	34.0	114.99	128.9	380.0	195.6	128.7	66.92	2.924		
9,500.0	9,481.7	9,505.2	9,461.1	34.0	34.5	112.30	133.4	393.0	205.9	138.3	67.62	3.045		
9,600.0	9,581.7	9,606.2	9,559.1	34.3	34.9	109.87	137.9	406.0	216.6	148.3	68.29	3.172		
9,700.0	9,681.7	9,707.2	9,657.2	34.7	35.3	107.68	142.4	419.0	227.6	158.6	68.96	3.300		
9,800.0	9,781.7	9,791.9	9,755.3	35.0	35.6	105.68	147.0	432.0	238.9	169.3	69.59	3.434		
9,900.0	9,881.7	9,909.1	9,853.3	35.4	36.1	103.87	151.5	445.1	250.5	180.2	70.33	3.562		
10,000.0	9,981.7	9,989.9	9,951.4	35.7	36.4	102.22	156.0	458.1	262.3	191.4	70.94	3.698		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #228H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,100.0	10,081.7	10,088.9	10,049.5	36.1	36.8	100.71	160.5	471.1	274.3	202.7	71.63	3.830		
10,200.0	10,181.7	10,188.0	10,147.5	36.5	37.2	99.33	165.0	484.1	286.5	214.2	72.32	3.962		
10,300.0	10,281.7	10,287.0	10,245.6	36.8	37.6	98.06	169.5	497.2	298.9	225.9	73.01	4.094		
10,400.0	10,381.7	10,386.0	10,343.7	37.2	38.0	96.89	174.1	510.2	311.3	237.6	73.70	4.224		
10,500.0	10,481.7	10,485.0	10,441.7	37.5	38.4	95.81	178.6	523.2	323.9	249.5	74.40	4.354		
10,600.0	10,581.7	10,584.1	10,539.8	37.9	38.8	94.82	183.1	536.2	336.6	261.5	75.09	4.483		
10,700.0	10,681.7	10,683.1	10,637.8	38.2	39.2	93.89	187.6	549.2	349.4	273.6	75.79	4.610		
10,800.0	10,781.7	10,782.1	10,735.9	38.6	39.6	93.03	192.1	562.3	362.3	285.8	76.49	4.736		
10,831.3	10,813.0	10,813.2	10,766.6	38.7	39.7	92.77	193.5	566.3	366.3	289.6	76.71	4.775		
10,850.0	10,831.7	10,831.6	10,784.9	38.8	39.8	-92.28	194.4	568.8	368.7	291.9	76.84	4.799		
10,900.0	10,881.5	10,880.8	10,833.6	38.9	40.0	-92.57	196.6	575.2	375.4	298.3	77.15	4.866		
10,950.0	10,930.8	10,929.1	10,881.5	39.1	40.1	-93.42	198.8	581.6	382.5	305.0	77.45	4.939		
11,000.0	10,979.2	10,976.4	10,928.3	39.2	40.3	-94.70	201.0	587.8	390.2	312.5	77.72	5.021		
11,050.0	11,026.4	11,022.5	10,973.9	39.3	40.5	-96.32	203.1	593.9	399.0	321.0	77.99	5.116		
11,100.0	11,071.9	11,071.5	11,022.6	39.5	40.7	-98.43	205.2	600.0	408.9	330.6	78.33	5.220		
11,150.0	11,115.5	11,118.6	11,069.3	39.6	40.9	-100.65	207.0	605.3	420.2	341.6	78.66	5.342		
11,200.0	11,156.7	11,163.4	11,113.8	39.7	41.1	-102.83	208.6	609.8	433.4	354.4	78.98	5.488		
11,250.0	11,195.4	11,205.4	11,155.7	39.8	41.2	-104.81	210.0	613.7	449.0	369.7	79.28	5.663		
11,300.0	11,231.1	11,244.5	11,194.6	39.9	41.4	-106.45	211.0	616.8	467.3	387.7	79.58	5.872		
11,350.0	11,263.7	11,280.2	11,230.2	39.9	41.5	-107.62	211.9	619.4	488.6	408.7	79.87	6.117		
11,400.0	11,292.8	11,312.3	11,262.2	40.0	41.6	-108.19	212.6	621.4	513.0	432.9	80.15	6.401		
11,450.0	11,318.3	11,340.5	11,290.3	40.1	41.7	-108.01	213.2	623.0	540.6	460.2	80.41	6.724		
11,500.0	11,339.9	11,364.4	11,314.3	40.2	41.8	-106.98	213.6	624.2	571.3	490.7	80.64	7.084		
11,550.0	11,357.5	11,384.0	11,333.8	40.3	41.9	-104.92	213.9	625.0	604.8	523.9	80.85	7.480		
11,600.0	11,371.0	11,398.8	11,348.6	40.4	42.0	-101.70	214.1	625.6	640.8	559.8	81.04	7.907		
11,650.0	11,380.2	11,408.8	11,358.6	40.5	42.0	-97.18	214.2	626.0	678.9	597.7	81.19	8.362		
11,700.0	11,385.1	11,413.7	11,363.5	40.7	42.0	-91.26	214.3	626.1	718.8	637.4	81.32	8.839		
11,731.3	11,386.0	11,414.2	11,364.0	40.7	42.0	-86.87	214.3	626.2	744.4	663.0	81.38	9.147		
11,800.0	11,386.0	11,413.0	11,362.8	40.9	42.0	-86.82	214.3	626.1	801.5	720.0	81.50	9.835		
11,900.0	11,386.0	11,411.3	11,361.1	41.3	42.0	-86.79	214.3	626.1	886.2	804.5	81.66	10.852		
12,009.9	11,386.0	11,409.6	11,359.4	41.7	42.0	-86.79	214.2	626.0	980.6	898.8	81.82	11.985		
12,100.0	11,386.0	12,882.1	12,178.0	42.1	46.3	-140.55	-669.1	792.6	1,025.8	965.3	60.54	16.944		
12,200.0	11,386.0	13,011.6	12,178.0	42.6	46.9	-140.22	-798.3	801.3	1,029.6	968.1	61.52	16.737		
12,300.0	11,386.0	13,135.9	12,178.0	43.2	47.5	-140.13	-922.5	804.3	1,030.6	968.1	62.41	16.512		
12,400.0	11,386.0	13,235.9	12,178.0	43.8	48.1	-140.13	-1,022.5	805.1	1,030.6	967.3	63.30	16.281		
12,500.0	11,386.0	13,335.9	12,178.0	44.5	48.7	-140.13	-1,122.5	805.9	1,030.6	966.3	64.26	16.037		
12,600.0	11,386.0	13,435.9	12,178.0	45.2	49.4	-140.13	-1,222.5	806.7	1,030.5	965.2	65.30	15.781		
12,700.0	11,386.0	13,535.9	12,178.0	46.0	50.1	-140.13	-1,322.5	807.6	1,030.5	964.1	66.42	15.517		
12,800.0	11,386.0	13,635.9	12,178.0	46.8	50.9	-140.14	-1,422.5	808.4	1,030.5	962.9	67.60	15.245		
12,900.0	11,386.0	13,735.9	12,178.0	47.7	51.7	-140.14	-1,522.5	809.2	1,030.5	961.7	68.85	14.968		
13,000.0	11,386.0	13,835.9	12,178.0	48.6	52.5	-140.14	-1,622.5	810.0	1,030.5	960.4	70.16	14.689		
13,100.0	11,386.0	13,935.9	12,178.0	49.5	53.4	-140.14	-1,722.5	810.8	1,030.5	959.0	71.53	14.407		
13,200.0	11,386.0	14,035.9	12,178.0	50.5	54.3	-140.14	-1,822.5	811.6	1,030.5	957.6	72.95	14.126		
13,300.0	11,386.0	14,135.9	12,178.0	51.5	55.2	-140.14	-1,922.5	812.4	1,030.5	956.1	74.43	13.845		
13,400.0	11,386.0	14,235.9	12,178.0	52.6	56.2	-140.14	-2,022.5	813.3	1,030.5	954.6	75.96	13.567		
13,500.0	11,386.0	14,335.9	12,178.0	53.6	57.2	-140.14	-2,122.5	814.1	1,030.5	953.0	77.53	13.291		
13,600.0	11,386.0	14,435.9	12,178.0	54.7	58.3	-140.14	-2,222.5	814.9	1,030.5	951.4	79.15	13.020		
13,700.0	11,386.0	14,535.9	12,178.0	55.9	59.3	-140.14	-2,322.5	815.7	1,030.5	949.7	80.81	12.752		
13,800.0	11,386.0	14,635.9	12,178.0	57.0	60.4	-140.14	-2,422.5	816.5	1,030.5	948.0	82.51	12.490		
13,900.0	11,386.0	14,735.9	12,178.0	58.2	61.5	-140.14	-2,522.5	817.3	1,030.5	946.3	84.24	12.233		
14,000.0	11,386.0	14,835.9	12,178.0	59.4	62.7	-140.14	-2,622.4	818.2	1,030.5	944.5	86.01	11.982		
14,100.0	11,386.0	14,935.9	12,178.0	60.6	63.9	-140.14	-2,722.4	819.0	1,030.5	942.7	87.81	11.736		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #228H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,200.0	11,386.0	15,035.9	12,178.0	61.9	65.0	-140.14	-2,822.4	819.8	1,030.5	940.9	89.63	11.497		
14,300.0	11,386.0	15,135.9	12,178.0	63.1	66.2	-140.14	-2,922.4	820.6	1,030.5	939.0	91.49	11.263		
14,400.0	11,386.0	15,235.9	12,178.0	64.4	67.5	-140.14	-3,022.4	821.4	1,030.5	937.1	93.38	11.036		
14,500.0	11,386.0	15,335.9	12,178.0	65.7	68.7	-140.14	-3,122.4	822.2	1,030.5	935.2	95.28	10.815		
14,600.0	11,386.0	15,435.9	12,178.0	67.0	70.0	-140.14	-3,222.4	823.0	1,030.5	933.3	97.22	10.600		
14,700.0	11,386.0	15,535.9	12,178.0	68.4	71.2	-140.14	-3,322.4	823.9	1,030.5	931.3	99.17	10.391		
14,800.0	11,386.0	15,635.9	12,178.0	69.7	72.5	-140.14	-3,422.4	824.7	1,030.5	929.3	101.15	10.188		
14,900.0	11,386.0	15,735.9	12,178.0	71.1	73.8	-140.14	-3,522.4	825.5	1,030.5	927.3	103.14	9.991		
15,000.0	11,386.0	15,835.9	12,178.0	72.4	75.2	-140.14	-3,622.4	826.3	1,030.5	925.3	105.16	9.799		
15,100.0	11,386.0	15,935.9	12,178.0	73.8	76.5	-140.14	-3,722.4	827.1	1,030.5	923.3	107.19	9.614		
15,200.0	11,386.0	16,035.9	12,178.0	75.2	77.8	-140.14	-3,822.4	827.9	1,030.4	921.2	109.24	9.433		
15,300.0	11,386.0	16,135.9	12,178.0	76.6	79.2	-140.14	-3,922.4	828.8	1,030.4	919.1	111.30	9.258		
15,400.0	11,386.0	16,235.9	12,178.0	78.0	80.6	-140.14	-4,022.4	829.6	1,030.4	917.1	113.38	9.089		
15,500.0	11,386.0	16,335.9	12,178.0	79.4	81.9	-140.14	-4,122.4	830.4	1,030.4	915.0	115.47	8.924		
15,600.0	11,386.0	16,435.9	12,178.0	80.9	83.3	-140.14	-4,222.4	831.2	1,030.4	912.9	117.57	8.764		
15,700.0	11,386.0	16,535.9	12,178.0	82.3	84.7	-140.14	-4,322.4	832.0	1,030.4	910.7	119.69	8.609		
15,800.0	11,386.0	16,635.9	12,178.0	83.7	86.1	-140.14	-4,422.4	832.8	1,030.4	908.6	121.82	8.458		
15,900.0	11,386.0	16,735.9	12,178.0	85.2	87.5	-140.14	-4,522.4	833.6	1,030.4	906.5	123.96	8.312		
16,000.0	11,386.0	16,835.9	12,178.0	86.7	89.0	-140.14	-4,622.4	834.5	1,030.4	904.3	126.11	8.171		
16,100.0	11,386.0	16,935.9	12,178.0	88.1	90.4	-140.14	-4,722.4	835.3	1,030.4	902.1	128.28	8.033		
16,200.0	11,386.0	17,035.9	12,178.0	89.6	91.8	-140.14	-4,822.4	836.1	1,030.4	900.0	130.45	7.899		
16,300.0	11,386.0	17,135.9	12,178.0	91.1	93.3	-140.14	-4,922.4	836.9	1,030.4	897.8	132.63	7.769		
16,400.0	11,386.0	17,235.9	12,178.0	92.6	94.7	-140.14	-5,022.4	837.7	1,030.4	895.6	134.82	7.643		
16,500.0	11,386.0	17,335.9	12,178.0	94.0	96.2	-140.14	-5,122.4	838.5	1,030.4	893.4	137.01	7.520		
16,600.0	11,386.0	17,435.9	12,178.0	95.5	97.7	-140.15	-5,222.4	839.4	1,030.4	891.2	139.22	7.401		
16,700.0	11,386.0	17,535.9	12,178.0	97.0	99.1	-140.15	-5,322.4	840.2	1,030.4	889.0	141.43	7.285		
16,800.0	11,386.0	17,635.9	12,178.0	98.5	100.6	-140.15	-5,422.4	841.0	1,030.4	886.7	143.65	7.173		
16,900.0	11,386.0	17,735.9	12,178.0	100.1	102.1	-140.15	-5,522.4	841.8	1,030.4	884.5	145.88	7.063		
17,000.0	11,386.0	17,835.9	12,178.0	101.6	103.6	-140.15	-5,622.3	842.6	1,030.4	882.3	148.11	6.957		
17,100.0	11,386.0	17,935.9	12,178.0	103.1	105.1	-140.15	-5,722.3	843.4	1,030.4	880.0	150.35	6.853		
17,200.0	11,386.0	18,035.9	12,178.0	104.6	106.6	-140.15	-5,822.3	844.2	1,030.4	877.8	152.60	6.752		
17,300.0	11,386.0	18,135.9	12,178.0	106.1	108.1	-140.15	-5,922.3	845.1	1,030.4	875.5	154.85	6.654		
17,400.0	11,386.0	18,235.9	12,178.0	107.7	109.6	-140.15	-6,022.3	845.9	1,030.4	873.3	157.11	6.558		
17,500.0	11,386.0	18,335.9	12,178.0	109.2	111.1	-140.15	-6,122.3	846.7	1,030.4	871.0	159.37	6.465		
17,600.0	11,386.0	18,435.9	12,178.0	110.7	112.6	-140.15	-6,222.3	847.5	1,030.4	868.7	161.64	6.375		
17,700.0	11,386.0	18,535.9	12,178.0	112.3	114.1	-140.15	-6,322.3	848.3	1,030.3	866.4	163.91	6.286		
17,800.0	11,386.0	18,635.9	12,178.0	113.8	115.6	-140.15	-6,422.3	849.1	1,030.3	864.2	166.18	6.200		
17,900.0	11,386.0	18,735.9	12,178.0	115.4	117.1	-140.15	-6,522.3	850.0	1,030.3	861.9	168.47	6.116		
18,000.0	11,386.0	18,835.9	12,178.0	116.9	118.7	-140.15	-6,622.3	850.8	1,030.3	859.6	170.75	6.034		
18,100.0	11,386.0	18,935.9	12,178.0	118.5	120.2	-140.15	-6,722.3	851.6	1,030.3	857.3	173.04	5.954		
18,200.0	11,386.0	19,035.9	12,178.0	120.0	121.7	-140.15	-6,822.3	852.4	1,030.3	855.0	175.33	5.876		
18,300.0	11,386.0	19,135.9	12,178.0	121.6	123.3	-140.15	-6,922.3	853.2	1,030.3	852.7	177.63	5.800		
18,400.0	11,386.0	19,235.9	12,178.0	123.2	124.8	-140.15	-7,022.3	854.0	1,030.3	850.4	179.93	5.726		
18,500.0	11,386.0	19,335.9	12,178.0	124.7	126.4	-140.15	-7,122.3	854.8	1,030.3	848.1	182.24	5.654		
18,600.0	11,386.0	19,435.9	12,178.0	126.3	127.9	-140.15	-7,222.3	855.7	1,030.3	845.8	184.54	5.583		
18,700.0	11,386.0	19,535.9	12,178.0	127.9	129.5	-140.15	-7,322.3	856.5	1,030.3	843.5	186.85	5.514		
18,800.0	11,386.0	19,635.9	12,178.0	129.4	131.0	-140.15	-7,422.3	857.3	1,030.3	841.1	189.17	5.447		
18,900.0	11,386.0	19,735.9	12,178.0	131.0	132.6	-140.15	-7,522.3	858.1	1,030.3	838.8	191.48	5.381		
19,000.0	11,386.0	19,835.9	12,178.0	132.6	134.1	-140.15	-7,622.3	858.9	1,030.3	836.5	193.80	5.316		
19,100.0	11,386.0	19,935.9	12,178.0	134.1	135.7	-140.15	-7,722.3	859.7	1,030.3	834.2	196.13	5.253		
19,200.0	11,386.0	20,035.9	12,178.0	135.7	137.2	-140.15	-7,822.3	860.6	1,030.3	831.8	198.45	5.192		
19,300.0	11,386.0	20,135.9	12,178.0	137.3	138.8	-140.15	-7,922.3	861.4	1,030.3	829.5	200.78	5.131		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #228H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,400.0	11,386.0	20,235.9	12,178.0	138.9	140.4	-140.15	-8,022.3	862.2	1,030.3	827.2	203.11	5.073		
19,500.0	11,386.0	20,335.9	12,178.0	140.5	141.9	-140.15	-8,122.3	863.0	1,030.3	824.8	205.44	5.015		
19,600.0	11,386.0	20,435.9	12,178.0	142.0	143.5	-140.15	-8,222.3	863.8	1,030.3	822.5	207.78	4.959		
19,700.0	11,386.0	20,535.9	12,178.0	143.6	145.1	-140.15	-8,322.3	864.6	1,030.3	820.2	210.11	4.903		
19,800.0	11,386.0	20,635.9	12,178.0	145.2	146.6	-140.15	-8,422.3	865.4	1,030.3	817.8	212.45	4.849		
19,900.0	11,386.0	20,735.9	12,178.0	146.8	148.2	-140.15	-8,522.3	866.3	1,030.3	815.5	214.80	4.796		
20,000.0	11,386.0	20,835.9	12,178.0	148.4	149.8	-140.15	-8,622.2	867.1	1,030.3	813.1	217.14	4.745		
20,100.0	11,386.0	20,935.9	12,178.0	150.0	151.4	-140.15	-8,722.2	867.9	1,030.3	810.8	219.48	4.694		
20,200.0	11,386.0	21,035.9	12,178.0	151.6	153.0	-140.15	-8,822.2	868.7	1,030.3	808.4	221.83	4.644		
20,300.0	11,386.0	21,135.9	12,178.0	153.2	154.5	-140.15	-8,922.2	869.5	1,030.2	806.1	224.18	4.596		
20,400.0	11,386.0	21,235.9	12,178.0	154.8	156.1	-140.15	-9,022.2	870.3	1,030.2	803.7	226.53	4.548		
20,500.0	11,386.0	21,335.9	12,178.0	156.4	157.7	-140.16	-9,122.2	871.2	1,030.2	801.4	228.89	4.501		
20,600.0	11,386.0	21,435.9	12,178.0	158.0	159.3	-140.16	-9,222.2	872.0	1,030.2	799.0	231.24	4.455		
20,700.0	11,386.0	21,535.9	12,178.0	159.6	160.9	-140.16	-9,322.2	872.8	1,030.2	796.6	233.60	4.410		
20,800.0	11,386.0	21,635.9	12,178.0	161.2	162.5	-140.16	-9,422.2	873.6	1,030.2	794.3	235.95	4.366		
20,900.0	11,386.0	21,735.9	12,178.0	162.8	164.0	-140.16	-9,522.2	874.4	1,030.2	791.9	238.31	4.323		
21,000.0	11,386.0	21,835.9	12,178.0	164.4	165.6	-140.16	-9,622.2	875.2	1,030.2	789.5	240.67	4.281		
21,100.0	11,386.0	21,935.9	12,178.0	166.0	167.2	-140.16	-9,722.2	876.0	1,030.2	787.2	243.04	4.239		
21,200.0	11,386.0	22,035.9	12,178.0	167.6	168.8	-140.16	-9,822.2	876.9	1,030.2	784.8	245.40	4.198		
21,300.0	11,386.0	22,135.9	12,178.0	169.2	170.4	-140.16	-9,922.2	877.7	1,030.2	782.4	247.76	4.158		
21,400.0	11,386.0	22,235.9	12,178.0	170.8	172.0	-140.16	-10,022.2	878.5	1,030.2	780.1	250.13	4.119		
21,500.0	11,386.0	22,335.9	12,178.0	172.4	173.6	-140.16	-10,122.2	879.3	1,030.2	777.7	252.50	4.080		
21,600.0	11,386.0	22,435.9	12,178.0	174.0	175.2	-140.16	-10,222.2	880.1	1,030.2	775.3	254.87	4.042		
21,700.0	11,386.0	22,535.9	12,178.0	175.6	176.8	-140.16	-10,322.2	880.9	1,030.2	773.0	257.24	4.005		
21,800.0	11,386.0	22,635.9	12,178.0	177.2	178.4	-140.16	-10,422.2	881.8	1,030.2	770.6	259.61	3.968		
21,900.0	11,386.0	22,735.9	12,178.0	178.8	180.0	-140.16	-10,522.2	882.6	1,030.2	768.2	261.98	3.932		
22,000.0	11,386.0	22,835.9	12,178.0	180.4	181.6	-140.16	-10,622.2	883.4	1,030.2	765.8	264.35	3.897		
22,100.0	11,386.0	22,935.9	12,178.0	182.0	183.2	-140.16	-10,722.2	884.2	1,030.2	763.5	266.73	3.862		
22,200.0	11,386.0	23,035.9	12,178.0	183.7	184.8	-140.16	-10,822.2	885.0	1,030.2	761.1	269.10	3.828		
22,300.0	11,386.0	23,135.9	12,178.0	185.3	186.4	-140.16	-10,922.2	885.8	1,030.2	758.7	271.48	3.795		
22,400.0	11,386.0	23,235.9	12,178.0	186.9	188.0	-140.16	-11,022.2	886.6	1,030.2	756.3	273.86	3.762		
22,500.0	11,386.0	23,335.9	12,178.0	188.5	189.6	-140.16	-11,122.2	887.5	1,030.2	753.9	276.24	3.729		
22,600.0	11,386.0	23,435.9	12,178.0	190.1	191.2	-140.16	-11,222.2	888.3	1,030.2	751.5	278.62	3.697		
22,700.0	11,386.0	23,535.9	12,178.0	191.7	192.8	-140.16	-11,322.2	889.1	1,030.2	749.2	281.00	3.666		
22,800.0	11,386.0	23,635.9	12,178.0	193.3	194.4	-140.16	-11,422.2	889.9	1,030.2	746.8	283.38	3.635		
22,900.0	11,386.0	23,735.9	12,178.0	195.0	196.0	-140.16	-11,522.2	890.7	1,030.1	744.4	285.76	3.605		
23,000.0	11,386.0	23,835.9	12,178.0	196.6	197.7	-140.16	-11,622.1	891.5	1,030.1	742.0	288.14	3.575		
23,100.0	11,386.0	23,935.9	12,178.0	198.2	199.3	-140.16	-11,722.1	892.3	1,030.1	739.6	290.53	3.546		
23,200.0	11,386.0	24,035.9	12,178.0	199.8	200.9	-140.16	-11,822.1	893.2	1,030.1	737.2	292.91	3.517		
23,300.0	11,386.0	24,135.9	12,178.0	201.4	202.5	-140.16	-11,922.1	894.0	1,030.1	734.8	295.30	3.488		
23,400.0	11,386.0	24,235.9	12,178.0	203.0	204.1	-140.16	-12,022.1	894.8	1,030.1	732.4	297.68	3.460		
23,500.0	11,386.0	24,335.9	12,178.0	204.7	205.7	-140.16	-12,122.1	895.6	1,030.1	730.1	300.07	3.433		
23,600.0	11,386.0	24,435.9	12,178.0	206.3	207.3	-140.16	-12,222.1	896.4	1,030.1	727.7	302.46	3.406		
23,705.7	11,386.0	24,541.6	12,178.0	208.0	209.0	-140.16	-12,327.8	897.3	1,030.1	725.1	304.98	3.378		

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #244H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	3.0	3.0	0.0	0.0	-90.42	-1.6	-220.0	220.0					
100.0	100.0	103.0	103.0	0.1	0.1	-90.42	-1.6	-220.0	220.0	219.8	0.27	823.907		
200.0	200.0	203.0	203.0	0.5	0.5	-90.42	-1.6	-220.0	220.0	219.0	0.98	223.611		
300.0	300.0	303.0	303.0	0.8	0.9	-90.42	-1.6	-220.0	220.0	218.3	1.70	129.360		
400.0	400.0	403.0	403.0	1.2	1.2	-90.42	-1.6	-220.0	220.0	217.6	2.42	91.002		
500.0	500.0	503.0	503.0	1.6	1.6	-90.42	-1.6	-220.0	220.0	216.9	3.13	70.190		
600.0	600.0	603.0	603.0	1.9	1.9	-134.53	-1.6	-220.0	220.6	216.8	3.85	57.320		
700.0	700.0	703.0	703.0	2.3	2.3	-134.99	-1.6	-220.0	222.5	217.9	4.56	48.762		
800.0	799.9	802.9	802.9	2.6	2.6	-135.76	-1.6	-220.0	225.6	220.3	5.28	42.746		
900.0	899.7	902.7	902.7	3.0	3.0	-136.79	-1.6	-220.0	230.0	224.0	5.99	38.375		
1,000.0	999.4	1,002.4	1,002.4	3.4	3.4	-138.05	-1.6	-220.0	235.8	229.1	6.71	35.132		
1,100.0	1,098.9	1,101.9	1,101.9	3.7	3.7	-139.51	-1.6	-220.0	243.0	235.6	7.43	32.702		
1,200.0	1,198.3	1,201.3	1,201.3	4.1	4.1	-141.12	-1.6	-220.0	251.8	243.6	8.15	30.879		
1,300.0	1,297.4	1,300.4	1,300.4	4.5	4.4	-142.85	-1.6	-220.0	262.1	253.2	8.88	29.526		
1,400.0	1,396.4	1,400.6	1,399.4	4.9	4.8	-144.60	-1.6	-220.0	273.3	263.7	9.60	28.461		
1,500.0	1,495.5	1,501.5	1,498.5	5.3	5.2	-146.22	-1.6	-220.0	284.8	274.5	10.33	27.562		
1,600.0	1,594.5	1,602.5	1,597.5	5.7	5.5	-147.71	-1.6	-220.0	296.5	285.5	11.06	26.799		
1,700.0	1,693.5	1,703.5	1,696.5	6.1	5.9	-149.09	-1.6	-220.0	308.4	296.6	11.80	26.147		
1,800.0	1,792.5	1,804.5	1,795.5	6.5	6.2	-150.37	-1.6	-220.0	320.5	307.9	12.53	25.584		
1,900.0	1,891.6	1,905.4	1,894.6	6.9	6.6	-151.55	-1.6	-220.0	332.7	319.4	13.26	25.094		
2,000.0	1,990.6	2,006.4	1,993.6	7.3	7.0	-152.65	-1.6	-220.0	345.0	331.0	13.99	24.666		
2,100.0	2,089.6	2,107.4	2,092.6	7.7	7.3	-153.67	-1.6	-220.0	357.4	342.7	14.72	24.287		
2,200.0	2,188.6	2,208.4	2,191.6	8.1	7.7	-154.62	-1.6	-220.0	370.0	354.5	15.45	23.952		
2,300.0	2,287.7	2,309.3	2,290.7	8.5	8.0	-155.52	-1.6	-220.0	382.6	366.4	16.18	23.653		
2,400.0	2,386.7	2,389.7	2,389.7	8.9	8.3	-156.35	-1.6	-220.0	395.4	378.5	16.83	23.488		
2,500.0	2,485.7	2,488.7	2,488.7	9.3	8.7	-157.13	-1.6	-220.0	408.2	390.6	17.55	23.251		
2,600.0	2,584.8	2,587.8	2,587.8	9.8	9.0	-157.87	-1.6	-220.0	421.0	402.8	18.28	23.036		
2,700.0	2,683.8	2,686.8	2,686.8	10.2	9.4	-158.56	-1.6	-220.0	434.0	415.0	19.00	22.842		
2,739.3	2,722.7	2,725.7	2,725.7	10.3	9.5	-158.82	-1.6	-220.0	439.1	419.8	19.28	22.770		
2,800.0	2,782.9	2,785.9	2,785.9	10.6	9.8	-159.23	-1.6	-220.0	446.5	426.8	19.72	22.643		
2,900.0	2,882.3	2,885.3	2,885.3	11.0	10.1	-159.77	-1.6	-220.0	456.9	436.4	20.44	22.353		
3,000.0	2,981.9	2,984.9	2,984.9	11.4	10.5	-160.17	-1.6	-220.0	464.8	443.7	21.16	21.970		
3,100.0	3,081.7	3,084.7	3,084.7	11.7	10.8	-160.44	-1.6	-220.0	470.3	448.4	21.87	21.503		
3,200.0	3,181.7	3,184.7	3,184.7	12.1	11.2	-160.59	-1.6	-220.0	473.3	450.7	22.58	20.960		
3,272.6	3,254.3	3,257.3	3,257.3	12.3	11.4	-116.67	-1.6	-220.0	474.0	450.9	23.10	20.522		
3,300.0	3,281.7	3,284.7	3,284.7	12.4	11.5	-116.67	-1.6	-220.0	474.0	450.7	23.29	20.353		
3,400.0	3,381.7	3,384.7	3,384.7	12.7	11.9	-116.67	-1.6	-220.0	474.0	450.0	23.99	19.755		
3,500.0	3,481.7	3,484.7	3,484.7	13.1	12.3	-116.67	-1.6	-220.0	474.0	449.3	24.70	19.192		
3,600.0	3,581.7	3,584.7	3,584.7	13.4	12.6	-116.67	-1.6	-220.0	474.0	448.6	25.40	18.659		
3,700.0	3,681.7	3,684.7	3,684.7	13.7	13.0	-116.67	-1.6	-220.0	474.0	447.9	26.11	18.154		
3,800.0	3,781.7	3,784.7	3,784.7	14.1	13.3	-116.67	-1.6	-220.0	474.0	447.2	26.81	17.676		
3,900.0	3,881.7	3,884.7	3,884.7	14.4	13.7	-116.67	-1.6	-220.0	474.0	446.4	27.52	17.222		
4,000.0	3,981.7	3,984.7	3,984.7	14.7	14.1	-116.67	-1.6	-220.0	474.0	445.7	28.23	16.790		
4,100.0	4,081.7	4,084.7	4,084.7	15.1	14.4	-116.67	-1.6	-220.0	474.0	445.0	28.94	16.379		
4,200.0	4,181.7	4,184.7	4,184.7	15.4	14.8	-116.67	-1.6	-220.0	474.0	444.3	29.65	15.988		
4,300.0	4,281.7	4,284.7	4,284.7	15.8	15.1	-116.67	-1.6	-220.0	474.0	443.6	30.35	15.614		
4,400.0	4,381.7	4,384.7	4,384.7	16.1	15.5	-116.67	-1.6	-220.0	474.0	442.9	31.06	15.258		
4,500.0	4,481.7	4,484.7	4,484.7	16.4	15.8	-116.67	-1.6	-220.0	474.0	442.2	31.77	14.917		
4,600.0	4,581.7	4,584.7	4,584.7	16.8	16.2	-116.67	-1.6	-220.0	474.0	441.5	32.48	14.591		
4,700.0	4,681.7	4,684.7	4,684.7	17.1	16.6	-116.67	-1.6	-220.0	474.0	440.8	33.19	14.279		
4,800.0	4,781.7	4,784.7	4,784.7	17.5	16.9	-116.67	-1.6	-220.0	474.0	440.1	33.90	13.980		
4,900.0	4,881.7	4,884.7	4,884.7	17.8	17.3	-116.67	-1.6	-220.0	474.0	439.4	34.62	13.693		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #244H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,000.0	4,981.7	4,984.7	4,984.7	18.2	17.6	-116.67	-1.6	-220.0	474.0	438.6	35.33	13.417		
5,100.0	5,081.7	5,084.7	5,084.7	18.5	18.0	-116.67	-1.6	-220.0	474.0	437.9	36.04	13.152		
5,200.0	5,181.7	5,184.7	5,184.7	18.8	18.4	-116.67	-1.6	-220.0	474.0	437.2	36.75	12.897		
5,300.0	5,281.7	5,284.7	5,284.7	19.2	18.7	-116.67	-1.6	-220.0	474.0	436.5	37.46	12.652		
5,400.0	5,381.7	5,384.7	5,384.7	19.5	19.1	-116.67	-1.6	-220.0	474.0	435.8	38.17	12.416		
5,500.0	5,481.7	5,484.7	5,484.7	19.9	19.4	-116.67	-1.6	-220.0	474.0	435.1	38.88	12.189		
5,600.0	5,581.7	5,584.7	5,584.7	20.2	19.8	-116.67	-1.6	-220.0	474.0	434.4	39.60	11.970		
5,700.0	5,681.7	5,684.7	5,684.7	20.6	20.1	-116.67	-1.6	-220.0	474.0	433.7	40.31	11.758		
5,800.0	5,781.7	5,784.7	5,784.7	20.9	20.5	-116.67	-1.6	-220.0	474.0	432.9	41.02	11.554		
5,900.0	5,881.7	5,884.7	5,884.7	21.3	20.9	-116.67	-1.6	-220.0	474.0	432.2	41.73	11.357		
6,000.0	5,981.7	5,984.7	5,984.7	21.6	21.2	-116.67	-1.6	-220.0	474.0	431.5	42.45	11.166		
6,100.0	6,081.7	6,084.7	6,084.7	22.0	21.6	-116.67	-1.6	-220.0	474.0	430.8	43.16	10.982		
6,200.0	6,181.7	6,184.7	6,184.7	22.3	21.9	-116.67	-1.6	-220.0	474.0	430.1	43.87	10.803		
6,300.0	6,281.7	6,284.7	6,284.7	22.7	22.3	-116.67	-1.6	-220.0	474.0	429.4	44.59	10.630		
6,400.0	6,381.7	6,384.7	6,384.7	23.0	22.7	-116.67	-1.6	-220.0	474.0	428.7	45.30	10.463		
6,500.0	6,481.7	6,484.7	6,484.7	23.4	23.0	-116.67	-1.6	-220.0	474.0	428.0	46.01	10.301		
6,600.0	6,581.7	6,584.7	6,584.7	23.7	23.4	-116.67	-1.6	-220.0	474.0	427.2	46.73	10.143		
6,700.0	6,681.7	6,684.7	6,684.7	24.1	23.7	-116.67	-1.6	-220.0	474.0	426.5	47.44	9.991		
6,800.0	6,781.7	6,784.7	6,784.7	24.4	24.1	-116.67	-1.6	-220.0	474.0	425.8	48.15	9.843		
6,900.0	6,881.7	6,884.7	6,884.7	24.8	24.4	-116.67	-1.6	-220.0	474.0	425.1	48.87	9.699		
7,000.0	6,981.7	6,984.7	6,984.7	25.1	24.8	-116.67	-1.6	-220.0	474.0	424.4	49.58	9.559		
7,100.0	7,081.7	7,084.7	7,084.7	25.5	25.2	-116.67	-1.6	-220.0	474.0	423.7	50.30	9.424		
7,200.0	7,181.7	7,184.7	7,184.7	25.8	25.5	-116.67	-1.6	-220.0	474.0	423.0	51.01	9.292		
7,300.0	7,281.7	7,284.7	7,284.7	26.2	25.9	-116.67	-1.6	-220.0	474.0	422.2	51.72	9.163		
7,400.0	7,381.7	7,384.7	7,384.7	26.5	26.2	-116.67	-1.6	-220.0	474.0	421.5	52.44	9.038		
7,500.0	7,481.7	7,484.7	7,484.7	26.9	26.6	-116.67	-1.6	-220.0	474.0	420.8	53.15	8.917		
7,600.0	7,581.7	7,584.7	7,584.7	27.2	27.0	-116.67	-1.6	-220.0	474.0	420.1	53.87	8.799		
7,700.0	7,681.7	7,684.7	7,684.7	27.6	27.3	-116.67	-1.6	-220.0	474.0	419.4	54.58	8.684		
7,800.0	7,781.7	7,784.7	7,784.7	28.0	27.7	-116.67	-1.6	-220.0	474.0	418.7	55.30	8.571		
7,900.0	7,881.7	7,884.7	7,884.7	28.3	28.0	-116.67	-1.6	-220.0	474.0	418.0	56.01	8.462		
8,000.0	7,981.7	7,984.7	7,984.7	28.7	28.4	-116.67	-1.6	-220.0	474.0	417.2	56.73	8.355		
8,100.0	8,081.7	8,084.7	8,084.7	29.0	28.8	-116.67	-1.6	-220.0	474.0	416.5	57.44	8.251		
8,200.0	8,181.7	8,184.7	8,184.7	29.4	29.1	-116.67	-1.6	-220.0	474.0	415.8	58.16	8.150		
8,300.0	8,281.7	8,292.3	8,292.3	29.7	29.5	-116.67	-1.3	-219.3	473.3	414.4	58.90	8.035		
8,400.0	8,381.7	8,401.2	8,401.1	30.1	29.9	-116.70	-0.3	-216.8	470.7	411.1	59.63	7.895		
8,500.0	8,481.7	8,510.0	8,509.8	30.4	30.2	-116.75	1.6	-212.3	466.3	406.0	60.33	7.729		
8,600.0	8,581.7	8,618.5	8,618.1	30.8	30.6	-116.81	4.2	-205.9	460.0	398.9	61.02	7.538		
8,700.0	8,681.7	8,726.7	8,726.0	31.1	31.0	-116.90	7.6	-197.6	451.7	390.1	61.68	7.324		
8,800.0	8,781.7	8,834.6	8,833.3	31.5	31.4	-117.02	11.7	-187.5	441.7	379.3	62.32	7.087		
8,900.0	8,881.7	8,942.0	8,940.0	31.8	31.8	-117.16	16.6	-175.6	429.7	366.8	62.94	6.827		
9,000.0	8,981.7	9,045.4	9,042.4	32.2	32.1	-117.32	22.0	-162.6	416.1	352.5	63.59	6.544		
9,100.0	9,081.7	9,144.4	9,140.4	32.6	32.5	-117.50	27.2	-149.8	402.3	338.0	64.29	6.257		
9,200.0	9,181.7	9,243.5	9,238.5	32.9	32.8	-117.68	32.4	-137.1	388.4	323.4	64.99	5.976		
9,300.0	9,281.7	9,342.5	9,336.5	33.3	33.2	-117.88	37.6	-124.3	374.5	308.9	65.69	5.702		
9,400.0	9,381.7	9,441.5	9,434.6	33.6	33.5	-118.10	42.9	-111.6	360.7	294.3	66.39	5.433		
9,500.0	9,481.7	9,540.5	9,532.7	34.0	33.9	-118.33	48.1	-98.8	346.8	279.8	67.09	5.170		
9,600.0	9,581.7	9,639.6	9,630.7	34.3	34.3	-118.58	53.3	-86.1	333.0	265.2	67.79	4.912		
9,700.0	9,681.7	9,738.6	9,728.8	34.7	34.6	-118.86	58.6	-73.3	319.2	250.7	68.50	4.660		
9,800.0	9,781.7	9,837.6	9,826.9	35.0	35.0	-119.15	63.8	-60.6	305.4	236.2	69.20	4.413		
9,900.0	9,881.7	9,936.6	9,924.9	35.4	35.3	-119.48	69.0	-47.8	291.5	221.6	69.90	4.171		
10,000.0	9,981.7	10,035.7	10,023.0	35.7	35.7	-119.84	74.2	-35.1	277.7	207.1	70.61	3.933		
10,100.0	10,081.7	10,134.7	10,121.1	36.1	36.1	-120.24	79.5	-22.3	263.9	192.6	71.31	3.701		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #244H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,200.0	10,181.7	10,233.7	10,219.1	36.5	36.4	-120.68	84.7	-9.6	250.2	178.1	72.02	3.473		
10,300.0	10,281.7	10,332.7	10,317.2	36.8	36.8	-121.17	89.9	3.2	236.4	163.7	72.73	3.250		
10,400.0	10,381.7	10,431.8	10,415.2	37.2	37.2	-121.72	95.2	15.9	222.7	149.2	73.44	3.032		
10,500.0	10,481.7	10,530.8	10,513.3	37.5	37.5	-122.34	100.4	28.7	208.9	134.8	74.15	2.818		
10,600.0	10,581.7	10,629.8	10,611.4	37.9	37.9	-123.06	105.6	41.4	195.2	120.4	74.86	2.608		
10,700.0	10,681.7	10,728.9	10,709.4	38.2	38.3	-123.87	110.9	54.2	181.6	106.0	75.57	2.403		
10,800.0	10,781.7	10,827.9	10,807.5	38.6	38.7	-124.83	116.1	66.9	168.0	91.7	76.28	2.202		
10,831.3	10,813.0	10,858.9	10,838.2	38.7	38.8	-125.16	117.7	70.9	163.7	87.2	76.51	2.140		
10,850.0	10,831.7	10,877.4	10,856.5	38.8	38.8	49.83	118.7	73.3	161.0	84.3	76.64	2.101		
10,900.0	10,881.5	10,926.5	10,905.1	38.9	39.0	51.08	121.3	79.6	151.8	74.8	76.97	1.972		
10,950.0	10,930.8	10,974.8	10,953.0	39.1	39.2	54.05	123.8	85.8	140.0	62.7	77.28	1.812		
11,000.0	10,979.2	11,022.0	10,999.7	39.2	39.4	59.25	126.3	91.9	126.1	48.5	77.57	1.626		
11,050.0	11,026.4	11,067.6	11,044.9	39.3	39.6	67.37	128.7	97.8	111.2	33.3	77.85	1.428 Level 3		
11,100.0	11,071.9	11,111.4	11,088.2	39.5	39.7	79.06	131.1	103.4	97.3	19.1	78.17	1.245 Level 2		
11,150.0	11,115.5	11,152.9	11,129.4	39.6	39.9	93.97	133.2	108.8	88.1	9.5	78.60	1.121 Level 2		
11,173.3	11,135.0	11,171.5	11,147.7	39.6	40.0	101.46	134.2	111.2	86.9	8.0	78.87	1.102 Level 2, CC, ES, SF		
11,200.0	11,156.7	11,192.0	11,168.0	39.7	40.0	109.87	135.3	113.8	88.7	9.5	79.20	1.120 Level 2		
11,250.0	11,195.4	11,228.2	11,203.9	39.8	40.2	123.74	137.2	118.5	101.9	22.1	79.75	1.277 Level 3		
11,300.0	11,231.1	11,261.4	11,236.8	39.9	40.3	134.11	139.0	122.7	126.2	46.1	80.11	1.576		
11,350.0	11,263.7	11,308.8	11,266.3	39.9	40.5	141.16	140.5	126.6	158.5	78.1	80.39	1.972		
11,400.0	11,292.8	11,317.4	11,292.2	40.0	40.5	145.53	141.9	130.0	196.2	115.7	80.47	2.438		
11,450.0	11,318.3	11,339.9	11,314.5	40.1	40.6	147.73	143.1	132.9	237.8	157.2	80.58	2.951		
11,500.0	11,339.9	11,358.4	11,332.8	40.2	40.7	147.87	144.1	135.2	282.1	201.5	80.66	3.498		
11,550.0	11,357.5	11,372.8	11,347.1	40.3	40.7	145.52	144.9	137.1	328.6	247.9	80.72	4.071		
11,600.0	11,371.0	11,383.1	11,357.3	40.4	40.8	139.13	145.4	138.4	376.6	295.8	80.76	4.663		
11,650.0	11,380.2	11,389.1	11,363.2	40.5	40.8	124.34	145.7	139.2	425.5	344.7	80.78	5.267		
11,700.0	11,385.1	11,409.2	11,364.9	40.7	40.9	92.53	145.8	139.4	475.0	394.2	80.86	5.875		
11,731.3	11,386.0	11,389.6	11,363.7	40.7	40.8	66.58	145.7	139.3	506.1	425.3	80.78	6.266		
11,800.0	11,386.0	11,385.3	11,359.5	40.9	40.8	57.28	145.5	138.7	574.4	493.6	80.76	7.112		
11,900.0	11,386.0	11,379.4	11,353.7	41.3	40.7	35.19	145.2	137.9	674.1	593.3	80.74	8.348		
12,009.9	11,386.0	11,373.5	11,347.8	41.7	40.7	-3.14	144.9	137.2	783.8	703.0	80.73	9.708		
12,100.0	11,386.0	11,368.8	11,343.1	42.1	40.7	-2.07	144.6	136.6	873.8	793.0	80.73	10.823		
12,200.0	11,386.0	11,363.6	11,338.0	42.6	40.7	-1.11	144.4	135.9	973.6	892.9	80.73	12.061		
12,300.0	11,386.0	11,358.4	11,332.9	43.2	40.7	-0.33	144.1	135.2	1,073.5	992.8	80.72	13.299		
12,400.0	11,386.0	11,353.3	11,327.8	43.8	40.6	0.33	143.8	134.6	1,173.4	1,092.6	80.72	14.536		
12,500.0	11,386.0	11,348.1	11,322.6	44.5	40.6	0.88	143.6	133.9	1,273.2	1,192.5	80.72	15.773		
12,600.0	11,386.0	11,342.9	11,317.5	45.2	40.6	1.35	143.3	133.2	1,373.1	1,292.4	80.72	17.010		
12,700.0	11,386.0	11,337.7	11,312.4	46.0	40.6	1.76	143.0	132.6	1,472.9	1,392.2	80.72	18.247		
12,800.0	11,386.0	11,332.6	11,307.3	46.8	40.6	2.12	142.7	131.9	1,572.8	1,492.1	80.72	19.484		
12,900.0	11,386.0	11,327.4	11,302.2	47.7	40.6	2.43	142.5	131.2	1,672.7	1,592.0	80.73	20.720		
13,000.0	11,386.0	11,322.2	11,297.0	48.6	40.5	2.71	142.2	130.6	1,772.5	1,691.8	80.73	21.956		
13,100.0	11,386.0	11,317.0	11,291.9	49.5	40.5	2.97	141.9	129.9	1,872.4	1,791.7	80.74	23.192		
13,200.0	11,386.0	11,311.9	11,286.8	50.5	40.5	3.19	141.6	129.2	1,972.3	1,891.5	80.74	24.427		
13,300.0	11,386.0	11,306.7	11,281.7	51.5	40.5	3.39	141.4	128.6	2,072.1	1,991.4	80.75	25.661		
13,400.0	11,386.0	11,301.5	11,276.5	52.6	40.5	3.58	141.1	127.9	2,172.0	2,091.2	80.76	26.895		
13,500.0	11,386.0	15,735.8	13,591.0	53.6	60.7	-171.48	-2,125.1	483.3	2,226.6	2,170.8	55.71	39.968		
13,600.0	11,386.0	15,835.8	13,591.0	54.7	61.7	-171.48	-2,225.1	484.1	2,226.6	2,169.8	56.79	39.209		
13,700.0	11,386.0	15,935.8	13,591.0	55.9	62.7	-171.48	-2,325.1	485.0	2,226.6	2,168.7	57.89	38.462		
13,800.0	11,386.0	16,035.8	13,591.0	57.0	63.7	-171.48	-2,425.1	485.8	2,226.6	2,167.5	59.02	37.728		
13,900.0	11,386.0	16,135.8	13,591.0	58.2	64.8	-171.48	-2,525.1	486.6	2,226.6	2,166.4	60.17	37.007		
14,000.0	11,386.0	16,235.8	13,591.0	59.4	65.9	-171.48	-2,625.1	487.4	2,226.6	2,165.2	61.34	36.301		
14,100.0	11,386.0	16,335.8	13,591.0	60.6	67.0	-171.48	-2,725.1	488.3	2,226.6	2,164.0	62.53	35.610		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #244H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,200.0	11,386.0	16,435.8	13,591.0	61.9	68.1	-171.48	-2,825.1	489.1	2,226.6	2,162.8	63.74	34.934		
14,300.0	11,386.0	16,535.8	13,591.0	63.1	69.3	-171.48	-2,925.1	489.9	2,226.6	2,161.6	64.96	34.274		
14,400.0	11,386.0	16,635.8	13,591.0	64.4	70.5	-171.48	-3,025.1	490.7	2,226.6	2,160.3	66.21	33.629		
14,500.0	11,386.0	16,735.8	13,591.0	65.7	71.7	-171.48	-3,125.1	491.5	2,226.6	2,159.1	67.47	33.001		
14,600.0	11,386.0	16,835.8	13,591.0	67.0	72.9	-171.48	-3,225.1	492.4	2,226.6	2,157.8	68.74	32.389		
14,700.0	11,386.0	16,935.8	13,591.0	68.4	74.1	-171.48	-3,325.1	493.2	2,226.6	2,156.5	70.03	31.792		
14,800.0	11,386.0	17,035.8	13,591.0	69.7	75.4	-171.48	-3,425.1	494.0	2,226.6	2,155.2	71.34	31.211		
14,900.0	11,386.0	17,135.8	13,591.0	71.1	76.6	-171.48	-3,525.1	494.8	2,226.6	2,153.9	72.65	30.646		
15,000.0	11,386.0	17,235.8	13,591.0	72.4	77.9	-171.48	-3,625.1	495.7	2,226.6	2,152.6	73.98	30.095		
15,100.0	11,386.0	17,335.8	13,591.0	73.8	79.2	-171.48	-3,725.1	496.5	2,226.6	2,151.2	75.32	29.560		
15,200.0	11,386.0	17,435.8	13,591.0	75.2	80.5	-171.48	-3,825.1	497.3	2,226.6	2,149.9	76.67	29.039		
15,300.0	11,386.0	17,535.8	13,591.0	76.6	81.8	-171.48	-3,925.1	498.1	2,226.6	2,148.5	78.04	28.532		
15,400.0	11,386.0	17,635.8	13,591.0	78.0	83.1	-171.48	-4,025.1	499.0	2,226.6	2,147.1	79.41	28.040		
15,500.0	11,386.0	17,735.8	13,591.0	79.4	84.5	-171.48	-4,125.1	499.8	2,226.6	2,145.8	80.79	27.560		
15,600.0	11,386.0	17,835.8	13,591.0	80.9	85.8	-171.48	-4,225.1	500.6	2,226.6	2,144.4	82.18	27.094		
15,700.0	11,386.0	17,935.8	13,591.0	82.3	87.2	-171.48	-4,325.1	501.4	2,226.6	2,143.0	83.58	26.641		
15,800.0	11,386.0	18,035.8	13,591.0	83.7	88.5	-171.48	-4,425.1	502.2	2,226.6	2,141.6	84.98	26.200		
15,900.0	11,386.0	18,135.8	13,591.0	85.2	89.9	-171.48	-4,525.0	503.1	2,226.6	2,140.2	86.40	25.772		
16,000.0	11,386.0	18,235.8	13,591.0	86.7	91.3	-171.48	-4,625.0	503.9	2,226.6	2,138.7	87.82	25.355		
16,100.0	11,386.0	18,335.8	13,591.0	88.1	92.7	-171.48	-4,725.0	504.7	2,226.6	2,137.3	89.24	24.949		
16,200.0	11,386.0	18,435.8	13,591.0	89.6	94.1	-171.48	-4,825.0	505.5	2,226.6	2,135.9	90.68	24.554		
16,300.0	11,386.0	18,535.8	13,591.0	91.1	95.5	-171.48	-4,925.0	506.4	2,226.6	2,134.4	92.12	24.170		
16,400.0	11,386.0	18,635.8	13,591.0	92.6	97.0	-171.48	-5,025.0	507.2	2,226.6	2,133.0	93.57	23.797		
16,500.0	11,386.0	18,735.8	13,591.0	94.0	98.4	-171.48	-5,125.0	508.0	2,226.6	2,131.5	95.02	23.433		
16,600.0	11,386.0	18,835.8	13,591.0	95.5	99.8	-171.48	-5,225.0	508.8	2,226.6	2,130.1	96.48	23.079		
16,700.0	11,386.0	18,935.8	13,591.0	97.0	101.3	-171.48	-5,325.0	509.6	2,226.6	2,128.6	97.94	22.734		
16,800.0	11,386.0	19,035.8	13,591.0	98.5	102.7	-171.48	-5,425.0	510.5	2,226.6	2,127.1	99.41	22.398		
16,900.0	11,386.0	19,135.8	13,591.0	100.1	104.2	-171.48	-5,525.0	511.3	2,226.6	2,125.7	100.88	22.071		
17,000.0	11,386.0	19,235.8	13,591.0	101.6	105.6	-171.48	-5,625.0	512.1	2,226.6	2,124.2	102.36	21.752		
17,100.0	11,386.0	19,335.8	13,591.0	103.1	107.1	-171.48	-5,725.0	512.9	2,226.6	2,122.7	103.84	21.442		
17,200.0	11,386.0	19,435.8	13,591.0	104.6	108.6	-171.48	-5,825.0	513.8	2,226.6	2,121.2	105.33	21.139		
17,300.0	11,386.0	19,535.8	13,591.0	106.1	110.0	-171.48	-5,925.0	514.6	2,226.6	2,119.7	106.82	20.844		
17,400.0	11,386.0	19,635.8	13,591.0	107.7	111.5	-171.48	-6,025.0	515.4	2,226.6	2,118.2	108.31	20.557		
17,500.0	11,386.0	19,735.8	13,591.0	109.2	113.0	-171.48	-6,125.0	516.2	2,226.6	2,116.7	109.81	20.276		
17,600.0	11,386.0	19,835.8	13,591.0	110.7	114.5	-171.48	-6,225.0	517.1	2,226.6	2,115.2	111.31	20.003		
17,700.0	11,386.0	19,935.8	13,591.0	112.3	116.0	-171.48	-6,325.0	517.9	2,226.6	2,113.7	112.82	19.736		
17,800.0	11,386.0	20,035.8	13,591.0	113.8	117.5	-171.48	-6,425.0	518.7	2,226.6	2,112.2	114.33	19.475		
17,900.0	11,386.0	20,135.8	13,591.0	115.4	119.0	-171.48	-6,525.0	519.5	2,226.6	2,110.7	115.84	19.221		
18,000.0	11,386.0	20,235.8	13,591.0	116.9	120.5	-171.48	-6,625.0	520.3	2,226.6	2,109.2	117.35	18.973		
18,100.0	11,386.0	20,335.8	13,591.0	118.5	122.0	-171.48	-6,725.0	521.2	2,226.6	2,107.7	118.87	18.731		
18,200.0	11,386.0	20,435.8	13,591.0	120.0	123.5	-171.48	-6,825.0	522.0	2,226.6	2,106.2	120.39	18.494		
18,300.0	11,386.0	20,535.8	13,591.0	121.6	125.1	-171.48	-6,925.0	522.8	2,226.6	2,104.6	121.92	18.263		
18,400.0	11,386.0	20,635.8	13,591.0	123.2	126.6	-171.48	-7,025.0	523.6	2,226.6	2,103.1	123.44	18.037		
18,500.0	11,386.0	20,735.8	13,591.0	124.7	128.1	-171.48	-7,125.0	524.5	2,226.6	2,101.6	124.97	17.817		
18,600.0	11,386.0	20,835.8	13,591.0	126.3	129.6	-171.48	-7,225.0	525.3	2,226.6	2,100.1	126.50	17.601		
18,700.0	11,386.0	20,935.8	13,591.0	127.9	131.2	-171.48	-7,325.0	526.1	2,226.6	2,098.5	128.03	17.390		
18,800.0	11,386.0	21,035.8	13,591.0	129.4	132.7	-171.48	-7,425.0	526.9	2,226.6	2,097.0	129.57	17.184		
18,900.0	11,386.0	21,135.8	13,591.0	131.0	134.2	-171.48	-7,524.9	527.7	2,226.6	2,095.5	131.11	16.983		
19,000.0	11,386.0	21,235.8	13,591.0	132.6	135.8	-171.48	-7,624.9	528.6	2,226.6	2,093.9	132.65	16.786		
19,100.0	11,386.0	21,335.8	13,591.0	134.1	137.3	-171.48	-7,724.9	529.4	2,226.6	2,092.4	134.19	16.593		
19,200.0	11,386.0	21,435.8	13,591.0	135.7	138.9	-171.48	-7,824.9	530.2	2,226.6	2,090.8	135.73	16.404		
19,300.0	11,386.0	21,535.8	13,591.0	137.3	140.4	-171.48	-7,924.9	531.0	2,226.6	2,089.3	137.28	16.219		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Voni - Voni Fed Com #244H - Wellbore #1 - BLM Plan #1													Offset Site Error:	0.0 usft
Survey Program: 0-MWD													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,400.0	11,386.0	21,635.8	13,591.0	138.9	142.0	-171.48	-8,024.9	531.9	2,226.6	2,087.7	138.83	16.039		
19,500.0	11,386.0	21,735.8	13,591.0	140.5	143.5	-171.48	-8,124.9	532.7	2,226.6	2,086.2	140.37	15.862		
19,600.0	11,386.0	21,835.8	13,591.0	142.0	145.1	-171.48	-8,224.9	533.5	2,226.6	2,084.6	141.93	15.688		
19,700.0	11,386.0	21,935.8	13,591.0	143.6	146.6	-171.48	-8,324.9	534.3	2,226.6	2,083.1	143.48	15.518		
19,800.0	11,386.0	22,035.8	13,591.0	145.2	148.2	-171.48	-8,424.9	535.2	2,226.6	2,081.5	145.03	15.352		
19,900.0	11,386.0	22,135.8	13,591.0	146.8	149.7	-171.48	-8,524.9	536.0	2,226.6	2,080.0	146.59	15.189		
20,000.0	11,386.0	22,235.8	13,591.0	148.4	151.3	-171.48	-8,624.9	536.8	2,226.6	2,078.4	148.15	15.029		
20,100.0	11,386.0	22,335.8	13,591.0	150.0	152.9	-171.48	-8,724.9	537.6	2,226.6	2,076.9	149.71	14.873		
20,200.0	11,386.0	22,435.8	13,591.0	151.6	154.4	-171.48	-8,824.9	538.4	2,226.6	2,075.3	151.27	14.720		
20,300.0	11,386.0	22,535.8	13,591.0	153.2	156.0	-171.48	-8,924.9	539.3	2,226.6	2,073.7	152.83	14.569		
20,400.0	11,386.0	22,635.8	13,591.0	154.8	157.6	-171.48	-9,024.9	540.1	2,226.6	2,072.2	154.39	14.422		
20,500.0	11,386.0	22,735.8	13,591.0	156.4	159.1	-171.48	-9,124.9	540.9	2,226.6	2,070.6	155.96	14.277		
20,600.0	11,386.0	22,835.8	13,591.0	158.0	160.7	-171.48	-9,224.9	541.7	2,226.6	2,069.0	157.52	14.135		
20,700.0	11,386.0	22,935.8	13,591.0	159.6	162.3	-171.48	-9,324.9	542.6	2,226.6	2,067.5	159.09	13.996		
20,800.0	11,386.0	23,035.8	13,591.0	161.2	163.9	-171.48	-9,424.9	543.4	2,226.6	2,065.9	160.66	13.859		
20,900.0	11,386.0	23,135.8	13,591.0	162.8	165.4	-171.48	-9,524.9	544.2	2,226.6	2,064.3	162.23	13.725		
21,000.0	11,386.0	23,235.8	13,591.0	164.4	167.0	-171.48	-9,624.9	545.0	2,226.6	2,062.8	163.80	13.594		
21,100.0	11,386.0	23,335.8	13,591.0	166.0	168.6	-171.48	-9,724.9	545.9	2,226.6	2,061.2	165.37	13.464		
21,200.0	11,386.0	23,435.8	13,591.0	167.6	170.2	-171.48	-9,824.9	546.7	2,226.6	2,059.6	166.94	13.338		
21,300.0	11,386.0	23,535.8	13,591.0	169.2	171.8	-171.48	-9,924.9	547.5	2,226.6	2,058.1	168.51	13.213		
21,400.0	11,386.0	23,635.8	13,591.0	170.8	173.3	-171.48	-10,024.9	548.3	2,226.6	2,056.5	170.09	13.091		
21,500.0	11,386.0	23,735.8	13,591.0	172.4	174.9	-171.48	-10,124.9	549.1	2,226.6	2,054.9	171.66	12.971		
21,600.0	11,386.0	23,835.8	13,591.0	174.0	176.5	-171.48	-10,224.9	550.0	2,226.6	2,053.3	173.24	12.852		
21,700.0	11,386.0	23,935.8	13,591.0	175.6	178.1	-171.48	-10,324.9	550.8	2,226.6	2,051.8	174.82	12.737		
21,800.0	11,386.0	24,035.8	13,591.0	177.2	179.7	-171.48	-10,424.8	551.6	2,226.6	2,050.2	176.40	12.623		
21,900.0	11,386.0	24,135.8	13,591.0	178.8	181.3	-171.48	-10,524.8	552.4	2,226.6	2,048.6	177.98	12.511		
22,000.0	11,386.0	24,235.8	13,591.0	180.4	182.9	-171.48	-10,624.8	553.3	2,226.6	2,047.0	179.56	12.400		
22,100.0	11,386.0	24,335.8	13,591.0	182.0	184.5	-171.48	-10,724.8	554.1	2,226.6	2,045.4	181.14	12.292		
22,200.0	11,386.0	24,435.8	13,591.0	183.7	186.1	-171.48	-10,824.8	554.9	2,226.6	2,043.9	182.72	12.186		
22,300.0	11,386.0	24,535.8	13,591.0	185.3	187.7	-171.48	-10,924.8	555.7	2,226.6	2,042.3	184.30	12.081		
22,400.0	11,386.0	24,635.8	13,591.0	186.9	189.3	-171.48	-11,024.8	556.5	2,226.6	2,040.7	185.88	11.978		
22,500.0	11,386.0	24,735.8	13,591.0	188.5	190.9	-171.48	-11,124.8	557.4	2,226.6	2,039.1	187.47	11.877		
22,600.0	11,386.0	24,835.8	13,591.0	190.1	192.5	-171.48	-11,224.8	558.2	2,226.6	2,037.5	189.05	11.778		
22,700.0	11,386.0	24,935.8	13,591.0	191.7	194.1	-171.48	-11,324.8	559.0	2,226.6	2,035.9	190.64	11.680		
22,800.0	11,386.0	25,035.8	13,591.0	193.3	195.7	-171.48	-11,424.8	559.8	2,226.6	2,034.3	192.22	11.583		
22,900.0	11,386.0	25,135.8	13,591.0	195.0	197.3	-171.48	-11,524.8	560.7	2,226.6	2,032.8	193.81	11.488		
23,000.0	11,386.0	25,235.8	13,591.0	196.6	198.9	-171.48	-11,624.8	561.5	2,226.6	2,031.2	195.40	11.395		
23,100.0	11,386.0	25,335.8	13,591.0	198.2	200.5	-171.48	-11,724.8	562.3	2,226.6	2,029.6	196.99	11.303		
23,200.0	11,386.0	25,435.8	13,591.0	199.8	202.1	-171.48	-11,824.8	563.1	2,226.6	2,028.0	198.58	11.213		
23,300.0	11,386.0	25,535.8	13,591.0	201.4	203.7	-171.48	-11,924.8	564.0	2,226.6	2,026.4	200.16	11.124		
23,400.0	11,386.0	25,635.8	13,591.0	203.0	205.3	-171.48	-12,024.8	564.8	2,226.6	2,024.8	201.75	11.036		
23,500.0	11,386.0	25,735.8	13,591.0	204.7	206.9	-171.48	-12,124.8	565.6	2,226.6	2,023.2	203.35	10.950		
23,600.0	11,386.0	25,835.8	13,591.0	206.3	208.5	-171.48	-12,224.8	566.4	2,226.6	2,021.6	204.94	10.865		
23,705.7	11,386.0	25,941.5	13,591.0	208.0	210.2	-171.48	-12,330.5	567.3	2,226.6	2,020.0	206.62	10.776		

Anticollision Report


Company: Matador Production Company
 Project: Rustler Breaks
 Reference Site: Voni
 Site Error: 0.0 usft
 Reference Well: Voni Fed Com #204H
 Well Error: 0.0 usft
 Reference Wellbore: Wellbore #1
 Reference Design: BLM Plan #1

Local Co-ordinate Reference: Well Voni Fed Com #204H
 TVD Reference: KB @ 3219.5usft
 MD Reference: KB @ 3219.5usft
 North Reference: Grid
 Survey Calculation Method: Minimum Curvature
 Output errors are at: 2.00 sigma
 Database: EDM 5000.14 Server
 Offset TVD Reference: Offset Datum

Reference Depths are relative to KB @ 3219.5usft
 Offset Depths are relative to Offset Datum
 Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: Voni Fed Com #204H
 Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30
 Grid Convergence at Surface is: 0.29°

Ladder Plot

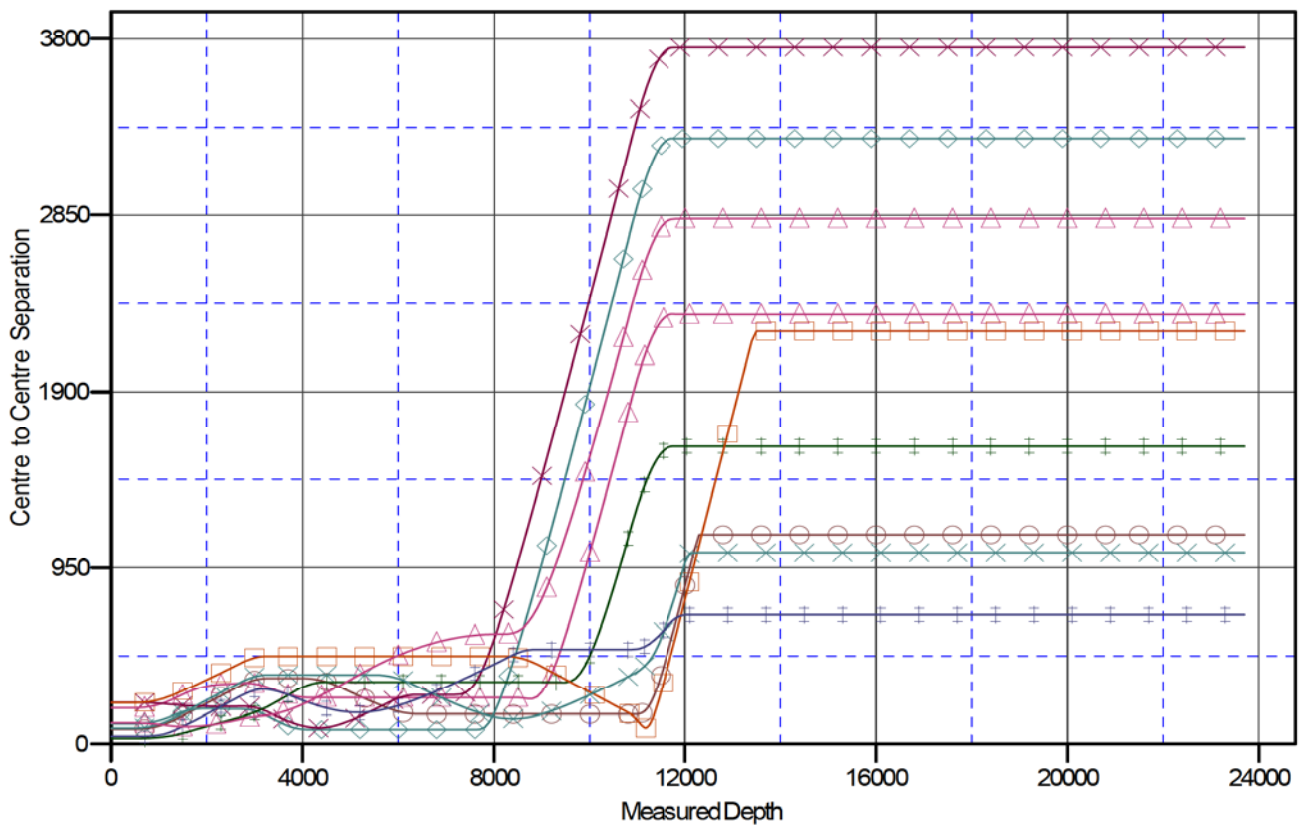

LEGEND

Voni Fed Can #204H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #14H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #104H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #204H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #124H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #204H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #208H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #218H, Wellbore #1, BLM Plan #1 V0
 Voni Fed Can #108H, Wellbore #1, BLM Plan #1 V0


Anticollision Report

Company:	Matador Production Company	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Project:	Rustler Breaks	TVD Reference:	KB @ 3219.5usft
Reference Site:	Voni	MD Reference:	KB @ 3219.5usft
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.14 Server
Reference Design:	BLM Plan #1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to KB @ 3219.5usft
 Offset Depths are relative to Offset Datum
 Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: Voni Fed Com #204H
 Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30
 Grid Convergence at Surface is: 0.29°

Separation Factor Plot

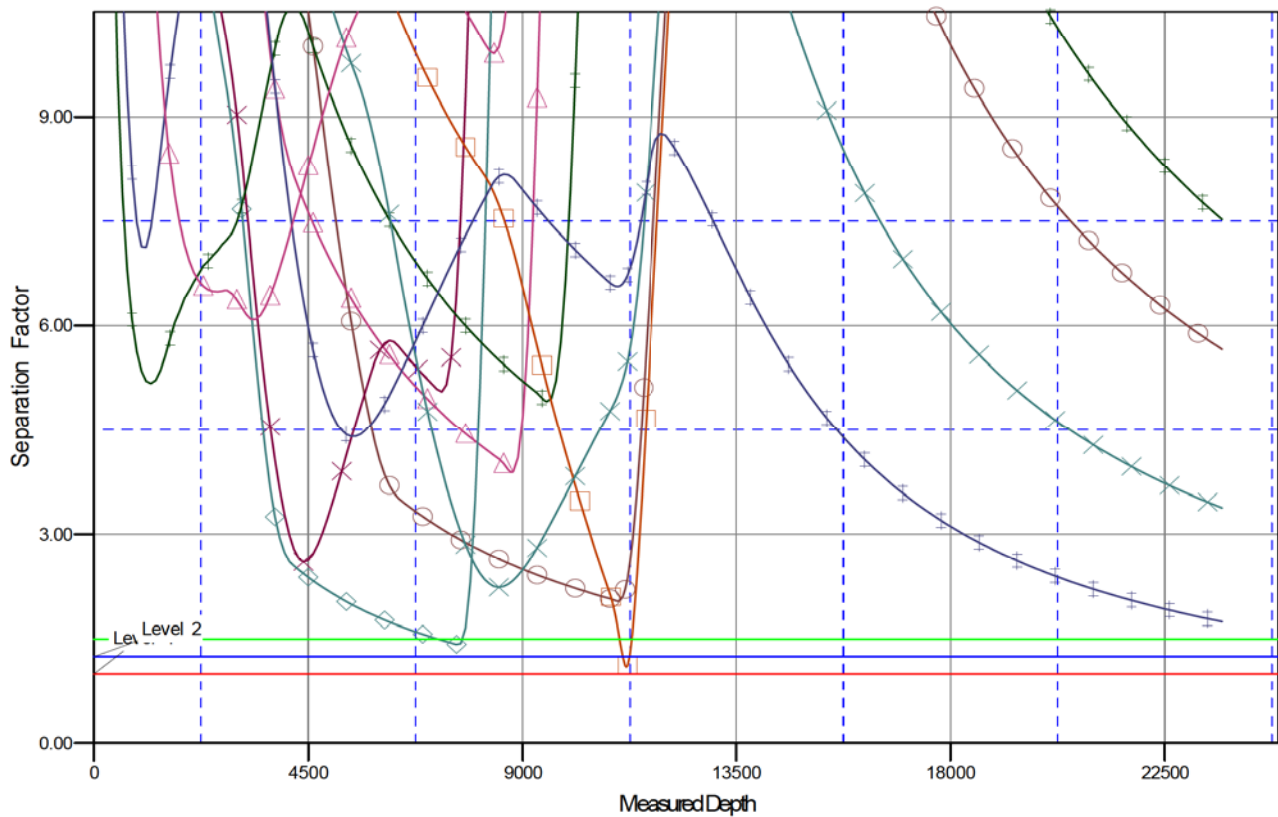

LEGEND

Voni Fed Can #204H, Wellbore #1, BLM Plan #1 V0	Voni Fed Can #124H, Wellbore #1, BLM Plan #1 V0	Voni Fed Can #204H, Wellbore #1, BLM Plan #1 V0
Voni Fed Can #124H, Wellbore #1, BLM Plan #1 V0	Voni Fed Can #104H, Wellbore #1, BLM Plan #1 V0	Voni Fed Can #124H, Wellbore #1, BLM Plan #1 V0
Voni Fed Can #104H, Wellbore #1, BLM Plan #1 V0	Voni Fed Can #204H, Wellbore #1, BLM Plan #1 V0	Voni Fed Can #104H, Wellbore #1, BLM Plan #1 V0



SURVEY PROGRAM

WELL DETAILS: Voni Fed Com #204H

Depth From	Depth To	Survey/Plan	Tool	+N/-S	+E/-W	Northing	GL @ 3191.0	KB @ 3219.5usft	Longitude	Slot
0.0	23705.7	BLM Plan #1 (Wellbore #1)	MWD	0.0	0.0	376765.89	Easting 672136.48	Latitude 32° 2' 4.658 N	103° 46' 40.223 W	

Company: Matador Production Company
Well: Voni Fed Com #204H
County: Eddy County, New Mexico
Wellbore: Wellbore #1
Plan: BLM Plan #1
Date: 1/23/20

Geodetic System: US State Plane 1927 (Exact solution)
Datum: NAD 1927 (NADCON CONUS)
Ellipsoid: Clarke 1866
Zone: New Mexico East 3001
System Datum: Mean Sea Level

To convert a Magnetic Direction to a Grid Direction, Add 6.46°
To convert a Magnetic Direction to a True Direction, Add 6.75° East
To convert a True Direction to a Grid Direction, Subtract 0.29°



Azimuths to Grid North
True North: -0.29°
Magnetic North: 6.46°

Magnetic Field
Strength: 47539.5snT
Dip Angle: 59.82°
Date: 1/21/2020
Model: IGRF2015







DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
VP - Voni Fed Com #204H	10813.0	211.1	203.5	376977.00	672340.00	32° 2' 6.737 N	103° 46' 37.846 W
BHL - Voni Fed Com #204H	11386.0	-12333.2	237.4	364431.42	672373.92	32° 0' 2.581 N	103° 46' 38.202 W

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VFace	Annotation
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
500.0	0.00	0.00	500.0	0.0	0.0	0.00	0.00	0.0	Start Build 1.00
1300.0	8.00	43.95	1297.4	40.1	38.7	1.00	43.95	-39.8	Start 1439.3 hold at 1300.0 MD
2739.3	8.00	43.95	2722.7	184.4	177.7	0.00	0.00	0.0	Start Drop -1.50
3272.6	0.00	0.00	3254.3	211.1	203.5	1.50	180.00	-209.4	Start 7558.7 hold at 3272.6 MD
10831.3	0.00	0.00	10813.0	211.1	203.5	0.00	0.00	-209.4	Start Build 10.00
11731.3	90.00	185.10	11386.0	-359.6	152.6	10.00	185.10	360.8	Start DLS 2.00 TFO -90.00
12009.9	90.00	179.53	11386.0	-637.8	141.3	2.00	-90.00	638.9	Start 11695.8 hold at 12009.9 MD
23705.7	90.00	179.53	11386.0	-12333.2	237.4	0.00	0.00	12334.7	TD at 23705.7

Vertical Section at 179.53° (500 usft/in)

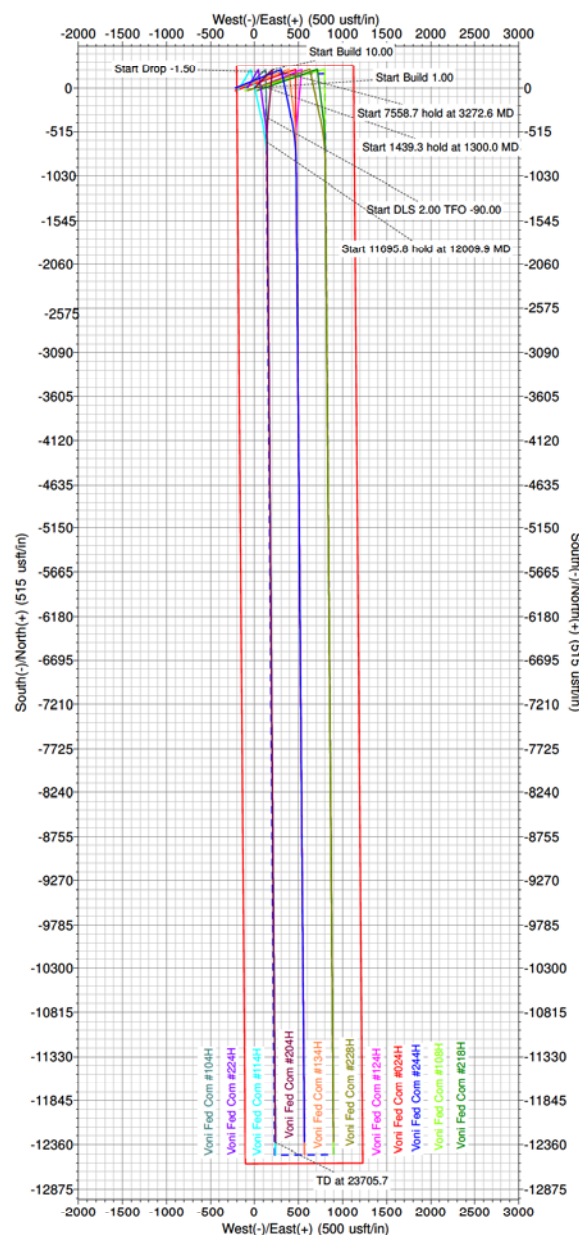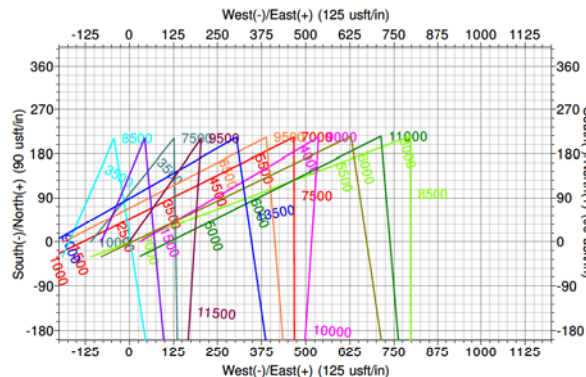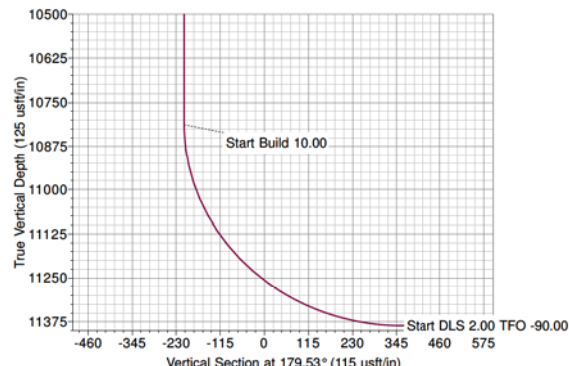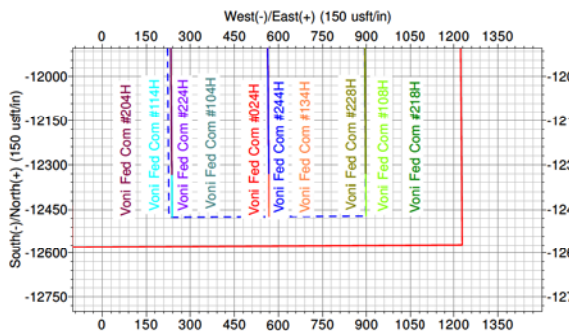

Matador Production Company

Rustler Breaks

Voni

Voni Fed Com #204H

Wellbore #1

Plan: BLM Plan #1

Standard Planning Report

21 January, 2020

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Project	Rustler Breaks		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		Using geodetic scale factor

Site	Voni					
Site Position:		Northing:	376,651.72 usft	Latitude:	32° 2' 3.721 N	
From:	Lat/Long	Easting:	668,298.64 usft	Longitude:	103° 47' 24.814 W	
Position Uncertainty:		0.0 usft	Slot Radius:	13-3/16 "	Grid Convergence:	0.29 °

Well	Voni Fed Com #204H					
Well Position	+N/-S	114.2 usft	Northing:	376,765.89 usft	Latitude:	32° 2' 4.658 N
	+E/-W	3,838.1 usft	Easting:	672,136.48 usft	Longitude:	103° 46' 40.223 W
Position Uncertainty		0.0 usft	Wellhead Elevation:		Ground Level:	3,191.0 usft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2015	1/21/2020	6.75	59.82	47,539.49739680

Design	BLM Plan #1			
Audit Notes:				
Version:	1	Phase:	PROTOTYPE	Tie On Depth: 0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	179.53

Plan Survey Tool Program	Date	1/21/2020			
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.0	23,705.7	BLM Plan #1 (Wellbore #1)	MWD	
				OWSG MWD - Standard	

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
500.0	0.00	0.00	500.0	0.0	0.0	0.00	0.00	0.00	0.00	
1,300.0	8.00	43.95	1,297.4	40.1	38.7	1.00	1.00	0.00	43.95	
2,739.3	8.00	43.95	2,722.7	184.4	177.7	0.00	0.00	0.00	0.00	
3,272.6	0.00	0.00	3,254.3	211.1	203.5	1.50	-1.50	0.00	180.00	
10,831.3	0.00	0.00	10,813.0	211.1	203.5	0.00	0.00	0.00	0.00	VP - Voni Fed Com #
11,731.3	90.00	185.10	11,386.0	-359.6	152.6	10.00	10.00	0.00	185.10	
12,009.9	90.00	179.53	11,386.0	-637.8	141.3	2.00	0.00	-2.00	-90.00	
23,705.7	90.00	179.53	11,386.0	-12,333.2	237.4	0.00	0.00	0.00	0.00	BHL - Voni Fed Com #

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
Start Build 1.00									
600.0	1.00	43.95	600.0	0.6	0.6	-0.6	1.00	1.00	0.00
700.0	2.00	43.95	700.0	2.5	2.4	-2.5	1.00	1.00	0.00
800.0	3.00	43.95	799.9	5.7	5.4	-5.6	1.00	1.00	0.00
893.9	3.94	43.95	893.6	9.7	9.4	-9.7	1.00	1.00	0.00
Rustler									
900.0	4.00	43.95	899.7	10.0	9.7	-10.0	1.00	1.00	0.00
1,000.0	5.00	43.95	999.4	15.7	15.1	-15.6	1.00	1.00	0.00
1,100.0	6.00	43.95	1,098.9	22.6	21.8	-22.4	1.00	1.00	0.00
1,200.0	7.00	43.95	1,198.3	30.7	29.6	-30.5	1.00	1.00	0.00
1,300.0	8.00	43.95	1,297.4	40.1	38.7	-39.8	1.00	1.00	0.00
Start 1439.3 hold at 1300.0 MD									
1,400.0	8.00	43.95	1,396.4	50.2	48.4	-49.8	0.00	0.00	0.00
1,500.0	8.00	43.95	1,495.5	60.2	58.0	-59.7	0.00	0.00	0.00
1,579.9	8.00	43.95	1,574.6	68.2	65.7	-67.7	0.00	0.00	0.00
Salado (Top Salt)									
1,600.0	8.00	43.95	1,594.5	70.2	67.7	-69.6	0.00	0.00	0.00
1,700.0	8.00	43.95	1,693.5	80.2	77.3	-79.6	0.00	0.00	0.00
1,800.0	8.00	43.95	1,792.5	90.2	87.0	-89.5	0.00	0.00	0.00
1,900.0	8.00	43.95	1,891.6	100.3	96.7	-99.5	0.00	0.00	0.00
2,000.0	8.00	43.95	1,990.6	110.3	106.3	-109.4	0.00	0.00	0.00
2,100.0	8.00	43.95	2,089.6	120.3	116.0	-119.3	0.00	0.00	0.00
2,200.0	8.00	43.95	2,188.6	130.3	125.6	-129.3	0.00	0.00	0.00
2,300.0	8.00	43.95	2,287.7	140.3	135.3	-139.2	0.00	0.00	0.00
2,400.0	8.00	43.95	2,386.7	150.4	145.0	-149.2	0.00	0.00	0.00
2,500.0	8.00	43.95	2,485.7	160.4	154.6	-159.1	0.00	0.00	0.00
2,600.0	8.00	43.95	2,584.8	170.4	164.3	-169.0	0.00	0.00	0.00
2,700.0	8.00	43.95	2,683.8	180.4	173.9	-179.0	0.00	0.00	0.00
2,739.3	8.00	43.95	2,722.7	184.4	177.7	-182.9	0.00	0.00	0.00
Start Drop -1.50									
2,800.0	7.09	43.95	2,782.9	190.1	183.3	-188.6	1.50	-1.50	0.00
2,900.0	5.59	43.95	2,882.3	198.0	190.9	-196.5	1.50	-1.50	0.00
3,000.0	4.09	43.95	2,981.9	204.1	196.8	-202.5	1.50	-1.50	0.00
3,100.0	2.59	43.95	3,081.7	208.3	200.8	-206.7	1.50	-1.50	0.00
3,200.0	1.09	43.95	3,181.7	210.6	203.0	-208.9	1.50	-1.50	0.00
3,272.6	0.00	0.00	3,254.3	211.1	203.5	-209.4	1.50	-1.50	0.00
Start 7558.7 hold at 3272.6 MD									
3,300.0	0.00	0.00	3,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
3,400.0	0.00	0.00	3,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
3,500.0	0.00	0.00	3,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
3,600.0	0.00	0.00	3,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
3,700.0	0.00	0.00	3,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
3,800.0	0.00	0.00	3,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
3,900.0	0.00	0.00	3,881.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,000.0	0.00	0.00	3,981.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,043.6	0.00	0.00	4,025.3	211.1	203.5	-209.4	0.00	0.00	0.00
Base Salt									

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,070.8	0.00	0.00	4,052.5	211.1	203.5	-209.4	0.00	0.00	0.00
Bell Canyon									
4,100.0	0.00	0.00	4,081.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,200.0	0.00	0.00	4,181.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,300.0	0.00	0.00	4,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,400.0	0.00	0.00	4,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,500.0	0.00	0.00	4,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,600.0	0.00	0.00	4,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,700.0	0.00	0.00	4,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,800.0	0.00	0.00	4,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
4,900.0	0.00	0.00	4,881.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,000.0	0.00	0.00	4,981.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,100.0	0.00	0.00	5,081.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,160.9	0.00	0.00	5,142.6	211.1	203.5	-209.4	0.00	0.00	0.00
Cherry Canyon									
5,200.0	0.00	0.00	5,181.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,300.0	0.00	0.00	5,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,400.0	0.00	0.00	5,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,500.0	0.00	0.00	5,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,600.0	0.00	0.00	5,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,700.0	0.00	0.00	5,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,800.0	0.00	0.00	5,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
5,900.0	0.00	0.00	5,881.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,000.0	0.00	0.00	5,981.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,100.0	0.00	0.00	6,081.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,200.0	0.00	0.00	6,181.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,300.0	0.00	0.00	6,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,310.3	0.00	0.00	6,292.0	211.1	203.5	-209.4	0.00	0.00	0.00
Brushy Canyon									
6,400.0	0.00	0.00	6,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,500.0	0.00	0.00	6,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,600.0	0.00	0.00	6,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,700.0	0.00	0.00	6,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,800.0	0.00	0.00	6,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
6,900.0	0.00	0.00	6,881.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,000.0	0.00	0.00	6,981.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,100.0	0.00	0.00	7,081.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,200.0	0.00	0.00	7,181.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,300.0	0.00	0.00	7,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,400.0	0.00	0.00	7,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,406.4	0.00	0.00	7,388.1	211.1	203.5	-209.4	0.00	0.00	0.00
L. Brushy Canyon									
7,500.0	0.00	0.00	7,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,600.0	0.00	0.00	7,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,700.0	0.00	0.00	7,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,800.0	0.00	0.00	7,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,900.0	0.00	0.00	7,881.7	211.1	203.5	-209.4	0.00	0.00	0.00
7,962.6	0.00	0.00	7,944.3	211.1	203.5	-209.4	0.00	0.00	0.00
BSGL									
8,000.0	0.00	0.00	7,981.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,100.0	0.00	0.00	8,081.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,111.5	0.00	0.00	8,093.1	211.1	203.5	-209.4	0.00	0.00	0.00
Avalon-SS									

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,200.0	0.00	0.00	8,181.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,300.0	0.00	0.00	8,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,400.0	0.00	0.00	8,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,500.0	0.00	0.00	8,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,600.0	0.00	0.00	8,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,700.0	0.00	0.00	8,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,800.0	0.00	0.00	8,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,900.0	0.00	0.00	8,881.7	211.1	203.5	-209.4	0.00	0.00	0.00
8,948.6	0.00	0.00	8,930.3	211.1	203.5	-209.4	0.00	0.00	0.00
FBSG									
9,000.0	0.00	0.00	8,981.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,100.0	0.00	0.00	9,081.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,200.0	0.00	0.00	9,181.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,300.0	0.00	0.00	9,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,373.8	0.00	0.00	9,355.5	211.1	203.5	-209.4	0.00	0.00	0.00
SBSC									
9,400.0	0.00	0.00	9,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,500.0	0.00	0.00	9,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,600.0	0.00	0.00	9,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,627.3	0.00	0.00	9,609.0	211.1	203.5	-209.4	0.00	0.00	0.00
SBSG									
9,700.0	0.00	0.00	9,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,800.0	0.00	0.00	9,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
9,900.0	0.00	0.00	9,881.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,000.0	0.00	0.00	9,981.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,100.0	0.00	0.00	10,081.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,130.3	0.00	0.00	10,112.0	211.1	203.5	-209.4	0.00	0.00	0.00
TBSC									
10,200.0	0.00	0.00	10,181.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,300.0	0.00	0.00	10,281.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,400.0	0.00	0.00	10,381.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,500.0	0.00	0.00	10,481.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,600.0	0.00	0.00	10,581.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,700.0	0.00	0.00	10,681.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,800.0	0.00	0.00	10,781.7	211.1	203.5	-209.4	0.00	0.00	0.00
10,831.3	0.00	0.00	10,813.0	211.1	203.5	-209.4	0.00	0.00	0.00
Start Build 10.00 - VP - Voni Fed Com #204H									
10,837.8	0.64	185.10	10,819.4	211.1	203.5	-209.4	10.00	10.00	0.00
TBSG									
10,900.0	6.87	185.10	10,881.5	207.0	203.2	-205.3	10.00	10.00	0.00
11,000.0	16.87	185.10	10,979.2	186.6	201.3	-184.9	10.00	10.00	0.00
11,100.0	26.87	185.10	11,071.9	149.5	198.0	-147.9	10.00	10.00	0.00
11,200.0	36.87	185.10	11,156.7	97.0	193.3	-95.4	10.00	10.00	0.00
11,203.0	37.16	185.10	11,159.1	95.2	193.2	-93.6	10.00	10.00	0.00
L. TBSG									
11,300.0	46.87	185.10	11,231.1	30.6	187.4	-29.1	10.00	10.00	0.00
11,306.6	47.53	185.10	11,235.6	25.8	187.0	-24.2	10.00	10.00	0.00
WFMP-A									
11,400.0	56.87	185.10	11,292.8	-47.6	180.4	49.1	10.00	10.00	0.00
11,500.0	66.87	185.10	11,339.9	-135.4	172.6	136.8	10.00	10.00	0.00
11,600.0	76.87	185.10	11,371.0	-229.9	164.2	231.2	10.00	10.00	0.00
11,700.0	86.87	185.10	11,385.1	-328.4	155.4	329.6	10.00	10.00	0.00
11,731.3	90.00	185.10	11,386.0	-359.6	152.6	360.8	10.00	10.00	0.00

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
Start DLS 2.00 TFO -90.00									
11,800.0	90.00	183.73	11,386.0	-428.0	147.3	429.2	2.00	0.00	-2.00
11,900.0	90.00	181.73	11,386.0	-527.9	142.6	529.1	2.00	0.00	-2.00
12,000.0	90.00	179.73	11,386.0	-627.9	141.3	629.0	2.00	0.00	-2.00
12,009.9	90.00	179.53	11,386.0	-637.8	141.3	638.9	2.00	0.00	-2.00
Start 11695.8 hold at 12009.9 MD									
12,100.0	90.00	179.53	11,386.0	-727.9	142.1	729.0	0.00	0.00	0.00
12,200.0	90.00	179.53	11,386.0	-827.9	142.9	829.0	0.00	0.00	0.00
12,300.0	90.00	179.53	11,386.0	-927.9	143.7	929.0	0.00	0.00	0.00
12,400.0	90.00	179.53	11,386.0	-1,027.9	144.6	1,029.0	0.00	0.00	0.00
12,500.0	90.00	179.53	11,386.0	-1,127.9	145.4	1,129.0	0.00	0.00	0.00
12,600.0	90.00	179.53	11,386.0	-1,227.9	146.2	1,229.0	0.00	0.00	0.00
12,700.0	90.00	179.53	11,386.0	-1,327.9	147.0	1,329.0	0.00	0.00	0.00
12,800.0	90.00	179.53	11,386.0	-1,427.9	147.8	1,429.0	0.00	0.00	0.00
12,900.0	90.00	179.53	11,386.0	-1,527.9	148.7	1,529.0	0.00	0.00	0.00
13,000.0	90.00	179.53	11,386.0	-1,627.9	149.5	1,629.0	0.00	0.00	0.00
13,100.0	90.00	179.53	11,386.0	-1,727.9	150.3	1,729.0	0.00	0.00	0.00
13,200.0	90.00	179.53	11,386.0	-1,827.9	151.1	1,829.0	0.00	0.00	0.00
13,300.0	90.00	179.53	11,386.0	-1,927.9	151.9	1,929.0	0.00	0.00	0.00
13,400.0	90.00	179.53	11,386.0	-2,027.9	152.8	2,029.0	0.00	0.00	0.00
13,500.0	90.00	179.53	11,386.0	-2,127.9	153.6	2,129.0	0.00	0.00	0.00
13,600.0	90.00	179.53	11,386.0	-2,227.8	154.4	2,229.0	0.00	0.00	0.00
13,700.0	90.00	179.53	11,386.0	-2,327.8	155.2	2,329.0	0.00	0.00	0.00
13,800.0	90.00	179.53	11,386.0	-2,427.8	156.1	2,429.0	0.00	0.00	0.00
13,900.0	90.00	179.53	11,386.0	-2,527.8	156.9	2,529.0	0.00	0.00	0.00
14,000.0	90.00	179.53	11,386.0	-2,627.8	157.7	2,629.0	0.00	0.00	0.00
14,100.0	90.00	179.53	11,386.0	-2,727.8	158.5	2,729.0	0.00	0.00	0.00
14,200.0	90.00	179.53	11,386.0	-2,827.8	159.3	2,829.0	0.00	0.00	0.00
14,300.0	90.00	179.53	11,386.0	-2,927.8	160.2	2,929.0	0.00	0.00	0.00
14,400.0	90.00	179.53	11,386.0	-3,027.8	161.0	3,029.0	0.00	0.00	0.00
14,500.0	90.00	179.53	11,386.0	-3,127.8	161.8	3,129.0	0.00	0.00	0.00
14,600.0	90.00	179.53	11,386.0	-3,227.8	162.6	3,229.0	0.00	0.00	0.00
14,700.0	90.00	179.53	11,386.0	-3,327.8	163.4	3,329.0	0.00	0.00	0.00
14,800.0	90.00	179.53	11,386.0	-3,427.8	164.3	3,429.0	0.00	0.00	0.00
14,900.0	90.00	179.53	11,386.0	-3,527.8	165.1	3,529.0	0.00	0.00	0.00
15,000.0	90.00	179.53	11,386.0	-3,627.8	165.9	3,629.0	0.00	0.00	0.00
15,100.0	90.00	179.53	11,386.0	-3,727.8	166.7	3,729.0	0.00	0.00	0.00
15,200.0	90.00	179.53	11,386.0	-3,827.8	167.6	3,829.0	0.00	0.00	0.00
15,300.0	90.00	179.53	11,386.0	-3,927.8	168.4	3,929.0	0.00	0.00	0.00
15,400.0	90.00	179.53	11,386.0	-4,027.8	169.2	4,029.0	0.00	0.00	0.00
15,500.0	90.00	179.53	11,386.0	-4,127.8	170.0	4,129.0	0.00	0.00	0.00
15,600.0	90.00	179.53	11,386.0	-4,227.8	170.8	4,229.0	0.00	0.00	0.00
15,700.0	90.00	179.53	11,386.0	-4,327.8	171.7	4,329.0	0.00	0.00	0.00
15,800.0	90.00	179.53	11,386.0	-4,427.8	172.5	4,429.0	0.00	0.00	0.00
15,900.0	90.00	179.53	11,386.0	-4,527.8	173.3	4,529.0	0.00	0.00	0.00
16,000.0	90.00	179.53	11,386.0	-4,627.8	174.1	4,629.0	0.00	0.00	0.00
16,100.0	90.00	179.53	11,386.0	-4,727.8	174.9	4,729.0	0.00	0.00	0.00
16,200.0	90.00	179.53	11,386.0	-4,827.8	175.8	4,829.0	0.00	0.00	0.00
16,300.0	90.00	179.53	11,386.0	-4,927.8	176.6	4,929.0	0.00	0.00	0.00
16,400.0	90.00	179.53	11,386.0	-5,027.8	177.4	5,029.0	0.00	0.00	0.00
16,500.0	90.00	179.53	11,386.0	-5,127.8	178.2	5,129.0	0.00	0.00	0.00
16,600.0	90.00	179.53	11,386.0	-5,227.7	179.1	5,229.0	0.00	0.00	0.00
16,700.0	90.00	179.53	11,386.0	-5,327.7	179.9	5,329.0	0.00	0.00	0.00
16,800.0	90.00	179.53	11,386.0	-5,427.7	180.7	5,429.0	0.00	0.00	0.00

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
16,900.0	90.00	179.53	11,386.0	-5,527.7	181.5	5,529.0	0.00	0.00	0.00
17,000.0	90.00	179.53	11,386.0	-5,627.7	182.3	5,629.0	0.00	0.00	0.00
17,100.0	90.00	179.53	11,386.0	-5,727.7	183.2	5,729.0	0.00	0.00	0.00
17,200.0	90.00	179.53	11,386.0	-5,827.7	184.0	5,829.0	0.00	0.00	0.00
17,300.0	90.00	179.53	11,386.0	-5,927.7	184.8	5,929.0	0.00	0.00	0.00
17,400.0	90.00	179.53	11,386.0	-6,027.7	185.6	6,029.0	0.00	0.00	0.00
17,500.0	90.00	179.53	11,386.0	-6,127.7	186.4	6,129.0	0.00	0.00	0.00
17,600.0	90.00	179.53	11,386.0	-6,227.7	187.3	6,229.0	0.00	0.00	0.00
17,700.0	90.00	179.53	11,386.0	-6,327.7	188.1	6,329.0	0.00	0.00	0.00
17,800.0	90.00	179.53	11,386.0	-6,427.7	188.9	6,429.0	0.00	0.00	0.00
17,900.0	90.00	179.53	11,386.0	-6,527.7	189.7	6,529.0	0.00	0.00	0.00
18,000.0	90.00	179.53	11,386.0	-6,627.7	190.6	6,629.0	0.00	0.00	0.00
18,100.0	90.00	179.53	11,386.0	-6,727.7	191.4	6,729.0	0.00	0.00	0.00
18,200.0	90.00	179.53	11,386.0	-6,827.7	192.2	6,829.0	0.00	0.00	0.00
18,300.0	90.00	179.53	11,386.0	-6,927.7	193.0	6,929.0	0.00	0.00	0.00
18,400.0	90.00	179.53	11,386.0	-7,027.7	193.8	7,029.0	0.00	0.00	0.00
18,500.0	90.00	179.53	11,386.0	-7,127.7	194.7	7,129.0	0.00	0.00	0.00
18,600.0	90.00	179.53	11,386.0	-7,227.7	195.5	7,229.0	0.00	0.00	0.00
18,700.0	90.00	179.53	11,386.0	-7,327.7	196.3	7,329.0	0.00	0.00	0.00
18,800.0	90.00	179.53	11,386.0	-7,427.7	197.1	7,429.0	0.00	0.00	0.00
18,900.0	90.00	179.53	11,386.0	-7,527.7	197.9	7,529.0	0.00	0.00	0.00
19,000.0	90.00	179.53	11,386.0	-7,627.7	198.8	7,629.0	0.00	0.00	0.00
19,100.0	90.00	179.53	11,386.0	-7,727.7	199.6	7,729.0	0.00	0.00	0.00
19,200.0	90.00	179.53	11,386.0	-7,827.7	200.4	7,829.0	0.00	0.00	0.00
19,300.0	90.00	179.53	11,386.0	-7,927.7	201.2	7,929.0	0.00	0.00	0.00
19,400.0	90.00	179.53	11,386.0	-8,027.7	202.1	8,029.0	0.00	0.00	0.00
19,500.0	90.00	179.53	11,386.0	-8,127.6	202.9	8,129.0	0.00	0.00	0.00
19,600.0	90.00	179.53	11,386.0	-8,227.6	203.7	8,229.0	0.00	0.00	0.00
19,700.0	90.00	179.53	11,386.0	-8,327.6	204.5	8,329.0	0.00	0.00	0.00
19,800.0	90.00	179.53	11,386.0	-8,427.6	205.3	8,429.0	0.00	0.00	0.00
19,900.0	90.00	179.53	11,386.0	-8,527.6	206.2	8,529.0	0.00	0.00	0.00
20,000.0	90.00	179.53	11,386.0	-8,627.6	207.0	8,629.0	0.00	0.00	0.00
20,100.0	90.00	179.53	11,386.0	-8,727.6	207.8	8,729.0	0.00	0.00	0.00
20,200.0	90.00	179.53	11,386.0	-8,827.6	208.6	8,829.0	0.00	0.00	0.00
20,300.0	90.00	179.53	11,386.0	-8,927.6	209.4	8,929.0	0.00	0.00	0.00
20,400.0	90.00	179.53	11,386.0	-9,027.6	210.3	9,029.0	0.00	0.00	0.00
20,500.0	90.00	179.53	11,386.0	-9,127.6	211.1	9,129.0	0.00	0.00	0.00
20,600.0	90.00	179.53	11,386.0	-9,227.6	211.9	9,229.0	0.00	0.00	0.00
20,700.0	90.00	179.53	11,386.0	-9,327.6	212.7	9,329.0	0.00	0.00	0.00
20,800.0	90.00	179.53	11,386.0	-9,427.6	213.5	9,429.0	0.00	0.00	0.00
20,900.0	90.00	179.53	11,386.0	-9,527.6	214.4	9,529.0	0.00	0.00	0.00
21,000.0	90.00	179.53	11,386.0	-9,627.6	215.2	9,629.0	0.00	0.00	0.00
21,100.0	90.00	179.53	11,386.0	-9,727.6	216.0	9,729.0	0.00	0.00	0.00
21,200.0	90.00	179.53	11,386.0	-9,827.6	216.8	9,829.0	0.00	0.00	0.00
21,300.0	90.00	179.53	11,386.0	-9,927.6	217.7	9,929.0	0.00	0.00	0.00
21,400.0	90.00	179.53	11,386.0	-10,027.6	218.5	10,029.0	0.00	0.00	0.00
21,500.0	90.00	179.53	11,386.0	-10,127.6	219.3	10,129.0	0.00	0.00	0.00
21,600.0	90.00	179.53	11,386.0	-10,227.6	220.1	10,229.0	0.00	0.00	0.00
21,700.0	90.00	179.53	11,386.0	-10,327.6	220.9	10,329.0	0.00	0.00	0.00
21,800.0	90.00	179.53	11,386.0	-10,427.6	221.8	10,429.0	0.00	0.00	0.00
21,900.0	90.00	179.53	11,386.0	-10,527.6	222.6	10,529.0	0.00	0.00	0.00
22,000.0	90.00	179.53	11,386.0	-10,627.6	223.4	10,629.0	0.00	0.00	0.00
22,100.0	90.00	179.53	11,386.0	-10,727.6	224.2	10,729.0	0.00	0.00	0.00
22,200.0	90.00	179.53	11,386.0	-10,827.6	225.0	10,829.0	0.00	0.00	0.00

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
22,300.0	90.00	179.53	11,386.0	-10,927.6	225.9	10,929.0	0.00	0.00	0.00	
22,400.0	90.00	179.53	11,386.0	-11,027.6	226.7	11,029.0	0.00	0.00	0.00	
22,500.0	90.00	179.53	11,386.0	-11,127.5	227.5	11,129.0	0.00	0.00	0.00	
22,600.0	90.00	179.53	11,386.0	-11,227.5	228.3	11,229.0	0.00	0.00	0.00	
22,700.0	90.00	179.53	11,386.0	-11,327.5	229.2	11,329.0	0.00	0.00	0.00	
22,800.0	90.00	179.53	11,386.0	-11,427.5	230.0	11,429.0	0.00	0.00	0.00	
22,900.0	90.00	179.53	11,386.0	-11,527.5	230.8	11,529.0	0.00	0.00	0.00	
23,000.0	90.00	179.53	11,386.0	-11,627.5	231.6	11,629.0	0.00	0.00	0.00	
23,100.0	90.00	179.53	11,386.0	-11,727.5	232.4	11,729.0	0.00	0.00	0.00	
23,200.0	90.00	179.53	11,386.0	-11,827.5	233.3	11,829.0	0.00	0.00	0.00	
23,300.0	90.00	179.53	11,386.0	-11,927.5	234.1	11,929.0	0.00	0.00	0.00	
23,400.0	90.00	179.53	11,386.0	-12,027.5	234.9	12,029.0	0.00	0.00	0.00	
23,500.0	90.00	179.53	11,386.0	-12,127.5	235.7	12,129.0	0.00	0.00	0.00	
23,600.0	90.00	179.53	11,386.0	-12,227.5	236.5	12,229.0	0.00	0.00	0.00	
23,700.0	90.00	179.53	11,386.0	-12,327.5	237.4	12,329.0	0.00	0.00	0.00	
23,705.7	90.00	179.53	11,386.0	-12,333.2	237.4	12,334.7	0.00	0.00	0.00	
TD at 23705.7 - BHL - Voni Fed Com #204H										

Design Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
VP - Voni Fed Com #204H - hit/miss target - Shape - Point	0.00	0.01	10,813.0	211.1	203.5	376,977.00	672,340.00	32° 2' 6.737 N	103° 46' 37.846 W	
BHL - Voni Fed Com #204H - plan hits target center - Point	0.00	0.00	11,386.0	-12,333.2	237.4	364,431.41	672,373.92	32° 0' 2.581 N	103° 46' 38.202 W	

Planning Report

Database:	EDM 5000.14 Server	Local Co-ordinate Reference:	Well Voni Fed Com #204H
Company:	Matador Production Company	TVD Reference:	KB @ 3219.5usft
Project:	Rustler Breaks	MD Reference:	KB @ 3219.5usft
Site:	Voni	North Reference:	Grid
Well:	Voni Fed Com #204H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	BLM Plan #1		

Formations						
Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)	
893.9	892.6	Rustler				
1,579.9	1,573.6	Salado (Top Salt)				
4,043.6	4,024.3	Base Salt				
4,070.8	4,051.5	Bell Canyon				
5,160.9	5,141.6	Cherry Canyon				
6,310.3	6,291.0	Brushy Canyon				
7,406.4	7,387.1	L. Brushy Canyon				
7,962.6	7,943.3	BSGL				
8,111.5	8,092.1	Avalon-SS				
8,948.6	8,929.3	FBSG				
9,373.8	9,354.5	SBSC				
9,627.3	9,608.0	SBSG				
10,130.3	10,111.0	TBSC				
10,837.8	10,818.4	TBSG				
11,203.0	11,158.1	L. TBSG				
11,306.6	11,234.6	WFMP-A				

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates			
		+N/-S (usft)	+E/-W (usft)	Comment	
500.0	500.0	0.0	0.0	Start Build 1.00	
1,300.0	1,297.4	40.1	38.7	Start 1439.3 hold at 1300.0 MD	
2,739.3	2,722.7	184.4	177.7	Start Drop -1.50	
3,272.6	3,254.3	211.1	203.5	Start 7558.7 hold at 3272.6 MD	
10,831.3	10,813.0	211.1	203.5	Start Build 10.00	
11,731.3	11,386.0	-359.6	152.6	Start DLS 2.00 TFO -90.00	
12,009.9	11,386.0	-637.8	141.3	Start 11695.8 hold at 12009.9 MD	
23,705.7	11,386.0	-12,333.2	237.4	TD at 23705.7	

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Road, Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit Original
to Appropriate
District Office

GAS CAPTURE PLAN

X Original

Operator & OGRID No.: Matador Production Company (228937)

☐ Amended

Date: 4/23/19

Reason for Amendment: _____

This Gas Capture Plan outlines actions to be taken by the Operator to reduce well/production facility flaring/venting for new completion (new drill, recomple to new zone, re-frac) activity.

Note: A C-129 must be submitted and approved prior to exceeding 60 days allowed by Rule 19.15.18.12.A

Well(s)/Production Facility – Name of facility

The wells that will be located at the production facility are shown in the table below.

Well Name	API	Well Location (ULSTR)	Footages	Expected MCF/D	Flared or Vented	Comments
Voni Fed Com 024H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 400	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well
Voni Fed Com 104H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 3,000	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well
Voni Fed Com 108H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 3,000	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup.
Voni Fed Com 114 H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 2,500	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup
Voni Fed Com 124H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 2,500	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup
Voni Fed Com 134H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 6,000	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup

Voni Fed Com 204H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 6,000	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup
Voni Fed Com 218H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 6,500	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup
Voni Fed Com 224H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/-5900	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup
Voni Fed Com 228H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 5900	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup
Voni Fed Com 244H	N/A	UL-A Sec 21 &16 T26S R31E	### FNL ### FEL	+/- 10,000	~30 days	Flare ~30 days on flowback before turn into TB. Time est. depends on sales connect and well cleanup

Gathering System and Pipeline Notification

The wells will be connected to a production facility after flowback operations are complete so long as the gas transporter system is in place. The gas produced from the production facility should be connected to Lucid Energy Delaware, LLC gathering system. It will require ~5,000' of pipeline to connect the facility to Lucid Energy Delaware, LLC gathering system. Matador Production Company periodically provides a drilling, completion and estimated first production date for wells that are scheduled to be drilled in the foreseeable future to Lucid Energy Delaware, LLC. If changes occur that will affect the drilling and completion schedule, Matador Production Company will notify Lucid Energy Delaware, LLC. Additionally, the gas produced from the well will be processed at a processing plant further downstream and, although unanticipated, any issues with downstream facilities could cause flaring at the wellhead. The actual flow of the gas will be based on compression operating parameters and gathering system pressures measured when the well starts producing.

Flowback Strategy

After the fracture treatment/completion operations (flowback), the well will be produced to temporary production tanks and the gas will be flared or vented. During flowback, the fluids and sand content will be monitored. If the produced fluids contain minimal sand, then the well will be turned to production facilities. The gas sales should start as soon as the well starts flowing through the production facilities, unless there are operational issues on the midstream system at that time. Based on current information, it is Matador's belief the system will be able to take the gas upon completion of the well.

Safety requirements during cleanout operations may necessitate that sand and non-pipeline quality gas be vented and/or flared rather than sold on a temporary basis.

Alternatives to Reduce Flaring

Below are alternatives considered from a conceptual standpoint to reduce the amount of gas flared.

- Power Generation – On lease
 - Operating a generator will only utilize a portion of the produced gas and the remainder of gas would still need to be flared.
 - Power Company has to be willing to purchase gas back and if they are willing they require a 5 year commitment to supply the agreed upon amount of power back to them. With gas decline rates and unpredictability of markets

it is impossible to agree to such long term demands. If the demands are not met then operator is burdened with penalty for not delivering.

- Compressed Natural Gas – On lease
 - Compressed Natural Gas is likely to be uneconomic to operate when the gas volume declines.
- NGL Removal – On lease
 - NGL Removal requires a plant and is expensive on such a small scale rendering it uneconomic and still requires residue gas to be flared.



Well Control Plan For 10M MASP Section of Wellbore

Component and Preventer Compatibility Table:

The table below covers the drilling and casing of the 10M MASP portion of the well and outlines the tubulars and the compatible preventers in use. This table, combined with the mud program, documents that two barriers to flow can be maintained at all times, independent of the rating of the annular preventer.

Component	OD	Preventer	RWP
Drill pipe	4"	Lower 3.5-5.5" VBR Upper 3.5-5.5" VBR	10M
HWDP	4"		
Jars/Agitator	4.75-5"		
Drill collars and MWD tools	4.75-5.25"		
Mud Motor	4.75-5.25"		
Production casing	4.5-5.5"		
ALL	0-13.625"	Annular	5M
Open-hole	-	Blind Rams	10M

VBR = Variable Bore Ram with compatible range listed in chart

HWDP = Heavy Weight Drill Pipe

MWD = Measurement While Drilling

Well Control Procedures

Well control procedures are specific to the rig equipment and the operation at the time the kick occurs. Below are the minimal high-level tasks prescribed to assure a proper shut-in while drilling, tripping, running casing, pipe out of the hole (open hole), and moving the Bottom Hole Assembly (BHA) through the Blowout Preventers (BOP). The maximum pressure at which well control is transferred from the annular to another compatible ram is 3,000 psi.

General Procedure While Drilling

1. Sound alarm (alert crew)
2. Space out drill string
3. Shut down pumps and stop rotary
4. Shut-in well with the annular preventer (The Hydraulic Control Remote (HCR) valve and choke will already be in the closed position)
5. Confirm shut-in
6. Notify tool pusher and company representative
7. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
8. Regroup and identify forward plan
9. If pressure has increased or is anticipated to increase above 3,000 psi, confirm spacing and close the upper pipe rams

General Procedure While Tripping

1. Sound alarm (alert crew)
2. Stab full opening safety valve and close
3. Space out drill string



Well Control Plan For 10M MASP Section of Wellbore

4. Shut-in well with annular preventer (The HCR valve and choke will already be in the closed position)
5. Confirm shut-in
6. Notify tool pusher and company representative
7. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
8. Regroup and identify forward plan
9. If pressure has increased or is anticipated to increase above 3,000 psi, confirm spacing and close the upper pipe rams

General Procedure While Running Casing

1. Sound alarm (alert crew)
2. Stab crossover and full opening safety valve and close
3. Space out string
4. Shut-in well with annular preventer (The HCR valve and choke will already be in the closed position)
5. Confirm shut-in
6. Notify tool pusher and company representative
7. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
8. Regroup and identify forward plan
9. If pressure has increased or is anticipated to increase above 3,000 psi, confirm spacing and close the upper pipe rams

General Procedure with No Pipe In Hole

1. At any point when the BOP stack is clear of pipe or BHA, the well will be shut in with blind rams, the HCR valve will be open, and choke will be closed. If pressure increase is observed:
2. Sound alarm (alert crew)
3. Confirm shut-in
4. Notify tool pusher and company representative
5. Read and record the following:
 - SICP
 - Time of shut in
6. Regroup and identify forward plan

General Procedure While Pulling BHA through Stack

1. Prior to pulling last joint/stand of drill pipe through the stack, perform flow check. If flowing:
 - a. Sound alarm (alert crew)
 - b. Stab full opening safety valve and close
 - c. Space out drill string
 - d. Shut-in well with annular preventer (The HCR valve and choke will already be in the closed position)
 - e. Confirm shut-in
 - f. Notify tool pusher and company representative
 - g. Read and record the following:
 - SIDPP and SICP




Well Control Plan For 10M MASP Section of Wellbore

- Pit gain
 - Time of shut in
 - h. Regroup and identify forward plan
2. With BHA in the stack and compatible ram preventer and pipe combo immediately available:
- a. Sound alarm (alert crew)
 - b. Stab crossover and full opening safety valve and close
 - c. Space out drill string with the upset just beneath the compatible pipe ram
 - d. Shut-in well using compatible pipe rams (The HCR valve and choke will already be in the closed position)
 - e. Confirm shut-in
 - f. Notify tool pusher and company representative
 - g. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
 - h. Regroup and identify forward plan
3. With BHA in the stack and no compatible ram preventer and pipe combo immediately available:
- a. Sound alarm (alert crew)
 - b. If possible to pick up high enough, pull BHA clear of the stack
 - i. Follow "No Pipe in Hole" procedure above
 - c. If impossible to pick up high enough to pull string clear of the stack:
 - i. Stab crossover, make up one joint/stand of drill pipe, and full opening safety valve and close
 - ii. Space out drill string with the upset just beneath the compatible pipe ram
 - iii. Shut-in well using compatible pipe rams (The HCR valve and choke will already be in the closed position)
 - iv. Confirm shut-in
 - v. Notify tool pusher and company representative
 - vi. Read and record the following:
 - SIDPP and SICP
 - Pit gain
 - Time of shut in
 - vii. Regroup and identify forward plan

Well Control Drills

Well control drills are specific to the rig equipment, personnel, and operations. Each crew will execute one drill weekly relevant to ongoing operations, but will make a reasonable attempt to vary the type of drills. The drills will be recorded in the daily drilling log.

Closed-Loop System

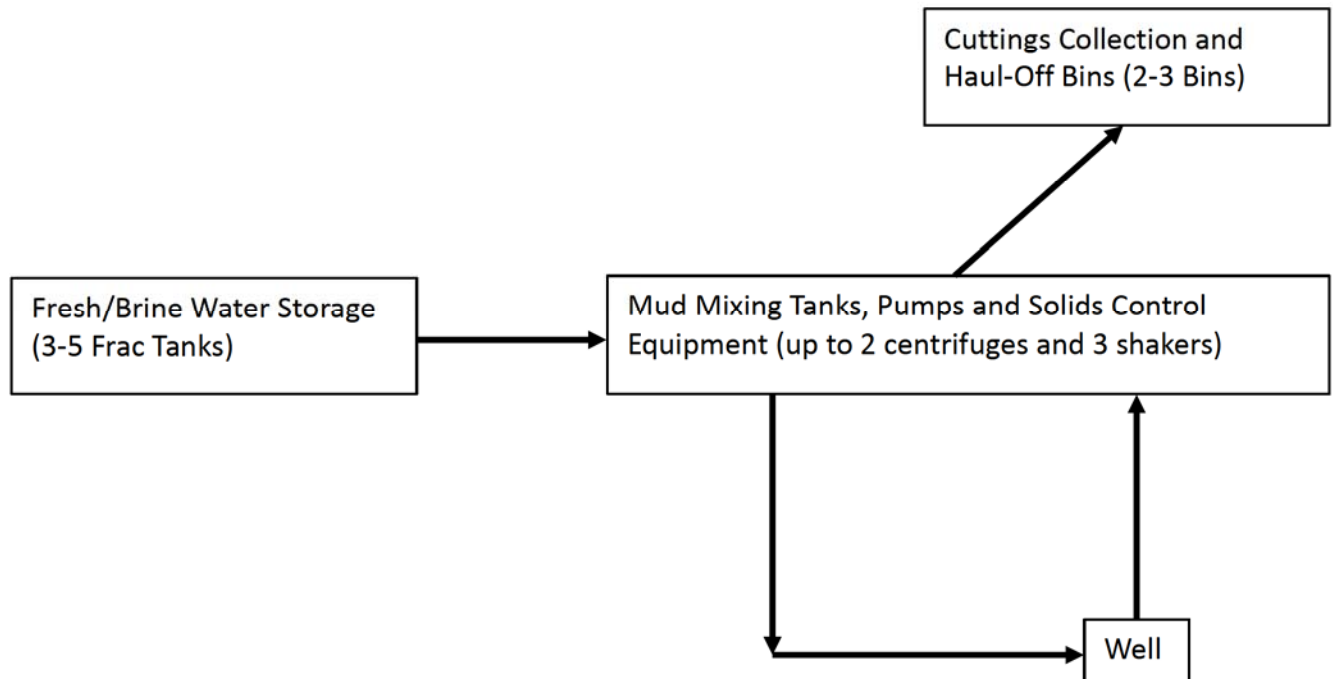

Operating and Maintenance Plan:

During drilling operations, third party service companies will utilize solids control equipment to remove cuttings from the drilling fluids and collect it in haul-off bins. Equipment will be closely monitored at all times while drilling by the derrick man and the service company employees.

Closure Plan:

During drilling operations, third party service companies will haul off drill solids and fluids to an approved disposal facility. At the end of the well, all closed loop equipment will be removed from the location.

Hydrogen Sulfide Drilling
Operations Plan
Matador Resources

1 H2S safety instructions to the following:

- Characteristics of H2S
- Physical effects and hazards
- Principal and operation of H2S detectors, warning system and briefing areas
- Evacuation procedures, routes and first aid
- Proper use of safety equipment & life support systems
- Essential personnel meeting medical evaluation criteria will receive additional training on the proper use of 30min pressure demand air packs

2 H2S Detection and Alarm Systems:

- H2S sensor/detectors to be located on the drilling rig floor, in the base of the sub structure / cellar area, on the mud pits in the shale shaker area. Additional H2S detectors may be placed as deemed necessary
- An audio alarm system will be installed on the derrick floor and in the doghouse

3 Windssocks and / Wind Streamers:

- Windssocks at mud pit area should be high enough to be visible
- Windssock on the rig floor and / top of doghouse should be high enough to be visible

4 Condition Flags and Signs:

- Warning sign on access road to location
- Flags to be displayed on sign at entrance to location
 - Green Flag – Normal Safe Operation Condition
 - Yellow Flag – Potential Pressure and Danger
 - Red Flag – Danger (H2S present in dangerous concentrations) Only H2S trained personnel admitted on location

5 Well Control Equipment:

- See Exhibit E-1

6 Communication:

- While working under masks chalkboards will be used for communications
- Hand signals will be used where chalk board is inappropriate
- Two way radio will be used to communicate off location in case of emergency help is required. In most cases cellular telephones will be available at most drilling foreman's trailer or living quarters.

7 Drilling Stem Testing:

- No DST cores are planned at this time

8 Drilling contractor supervisor will be required to be familiar with the effects H₂S has on tubulars good and other mechanical equipment

9 If H₂S is encountered, mud system will be altered if necessary to maintain control of formation. A mud gas separator will be brought into service along with H₂S scavengers if necessary

11 Emergency Contacts

- See exhibit E-6

HYDROGEN SULFIDE CONTINGENCY PLAN
Drilling, Testing, & Completion

MRC ENERGY CO.

Reviewers

----- Operations Manager
----- Operations Supt.
----- Staff RES
----- Field Supt.
Blake Hermes---Engineering

H2S Contingency Plan # 0165

Revision# 0

This H2S Contingency Plan is subject to updating

Effective date: July 8, 2015

TABLE OF CONTENTS

I.	INTRODUCTION	3
II.	PURPOSE	4
A.	Operating Procedures	5
B.	Procedures to be Initiated Prior to reaching H2S Contingency Plan Compliance	6
C.	Drilling Below Contingency Plan Depth	7
D.	Procedures program	7
III.	CONDITIONS & H₂S EMERGENCY PROCEDURES	10
A.	Definition of Operational “Conditions”	10
B.	H2S Emergency Procedures; In Scope Personnel	12
C.	Instructions for Igniting the Well	16
D.	Coring	17
E.	Normal Operations	18
IV.	SAFETY EQUIPMENT	21
V.	TOXICITY OF VARIOUS GASES	23
VI.	PROPERTIES OF GASES	24
VII.	TREATMENT PROCEDURES FOR H₂S POISONING	25
VIII.	BREATHING AIR EQUIPMENT DRILLS ON/OFF DUTY	26
IX.	HYDROGEN SULFIDE TRAINING CURRICULUM	27
X.	FIT TEST	29
XI.	H₂S EQUIPMENT LIST	30
XII.	EMERGENCY PHONE NUMBERS	32
XIII.	EVACUATION OF GENERAL PUBLIC	37
XIV.	SEPCO EMERGENCY PHONE NUMBERS AND DIRECTIONS TO WELL SITE	38
XV.	ROE MAP (RADIUS OF EXPOSURE)	39
XVI.	RESIDENCE LIST WITHIN ROE	40

INTRODUCTION

The H2S equipment will be rigged up 2 days prior to reaching a potential H2S containing zone. Drilling into any potential H2S zone shall not commence until the on-site MRC Drilling Supervisor has confirmed this plan in place.

The onsite Drilling Foreman will give Total Safety one week (7 days) notice to prepare for rig up of H2S equipment)

To be effective, the plan requires the cooperation and effort of each person participating in the drilling of an H₂S well. Each person must know his/her responsibilities and all emergency and safety procedures. He/she should thoroughly understand and be able to use with accuracy, all safety equipment while performing his/her normal duties, if the circumstance should arise. He/she should therefore familiarize himself/herself with the location of all safety equipment and check to see that it is properly stored, easily accessible at all times, and routinely maintained.

It is the intention of MRC ENERGY CO. and the Drilling Contractor to make every effort to provide adequate safeguards against harm to persons on the rig and in the immediate vicinity from the effects of hydrogen sulfide, which may be released into the atmosphere under emergency conditions. However, the initiative rests with the individual in utilizing the safeguards provided. The ideas and suggestions of the individuals involved in the drilling of this well are highly welcomed and act as a fundamental tool for providing the safest working conditions possible.

The drilling representative is required to enforce these procedures. They are set up for your safety and the safety of all others.

II. PURPOSE

It is MRC Energy Co.'s intent to provide a safe working place, not only for its employees, but also for other contractors who are aiding in the drilling of this well. The safety of the general public is of utmost concern. All precautions will be taken to keep a safe working environment and protect the public.

There is a possibility of encountering toxic hydrogen sulfide gas. Safety procedures must be adhered to in order to protect all personnel connected with the operations as well as people living within the area.

The MRC Energy Co. representative will enforce all aspects of the H₂S Contingency Plan. This job will become easier by a careful study of the following pages and training and informing all personnel that will be working on the well, their duties and responsibilities.

A. OPERATING PROCEDURES

DEFINITIONS:

For purpose of this plan, on-site personnel shall be referred to as “In Scope Personnel” or “Out of Scope Personnel”, per the following definitions:

In Scope Personnel – Personnel who will be working or otherwise present in potential H₂S release areas, including the rig floor, cellar, pits, and shaker areas.

Out of Scope Personnel – Personnel who will not be working or Otherwise present in potential H₂S areas. Such personnel include rig Site visitor, delivery and camp services personnel.

GENERAL:

Before this H₂S contingency plan becomes operational, all regularly assigned In Scope Personnel (primarily the MRC, drilling contractor, and certain service personnel,) shall be thoroughly trained in the use of breathing equipment, emergency procedures, and responsibilities. Total Safety Technician or a designee assigned by the MRC Drilling Foreman shall keep a list of all personnel who have been through the on-site H₂S training program at the drill site.

All In Scope Personnel shall be given H₂S training and the steps to be taken during H₂S conditions under which the well may be drilled. General information will be explained about toxic gases, as well as the physiological effects of H₂S and the various classified operating conditions. In addition, the reader will be informed his/her general responsibility concerning safety equipment and emergency procedures.

The Total Safety H₂S Safety Technician or MRC on-site RSE Technician shall make available the H₂S Contingency Plan for all personnel to review.

Without exception, all personnel that arrive on location must proceed directly to and sign-in with the on-site MRC RSE Technician. In Scope Personnel will be required to complete an on-site H₂S training and respirator fit testing before starting work, or produce evidence that they have received equivalent training. Out of Scope Personnel will be required to complete a site H₂S awareness and general safety briefing. This briefing will consist of a H₂S hazard overview, alarm review and required response to alarms.

B. PROCEDURES TO BE INITIATED PRIOR TO H₂S CONTINGENCY PLAN COMPLIANCE:

A list of emergency phone numbers and contacts will be on location and posted at the following locations:

1. MRC ENERGY CO.'S Representative's Office
2. Drilling Contractor's, Toolpusher Office
3. Living Quarters Area

All safety equipment and H₂S related hardware must be set up as required by MRC Energy Co. with regard to location of briefing areas, breathing equipment, etc. All safety equipment must be inspected periodically (at least weekly) with particular attention to resuscitators and breathing equipment.

In Scope Personnel working in the well site area will be assigned breathing apparatus. Operator and drilling contractor personnel required to work in the following areas will be provided with Self Contained Breathing Apparatus:

1. Rig Floor
2. Mud Pits
3. Derrick
4. Shale Shaker
5. Cellar

The Total Safety H₂S Safety Technician will be responsible for rigging up all H₂S continuous monitoring-type detectors. The Total Safety Technician will monitor and bump test the detector units periodically (at least at least once a week to test alarm function during drilling conditions. In the event H₂S is detected, or when drilling in a zone confirmed to contain H₂S, the units shall be bump tested at least once every 24 hours. A bump test/calibration log will be kept on location. All results will be reported to the MRC on-site Drilling Foreman.

All Total Safety H₂S equipment will be maintained and inspected by a Total Safety Technician on at least a Weekly basis.

C. DRILLING BELOW CONTINGENCY PLAN DEPTH

H₂S response drills will be held at least once per week if possible or as often as necessary to acquaint the crews and service company personnel of their responsibilities and the proper procedures to shut-in a well. Initial drills will be performed until crews demonstrate competency donning and working under mask. After the MRC Energy Co.'s representative is satisfied with initial blowout drill procedures, a drill will be conducted weekly with each crew, as necessary. The H₂S Safety Technician or designee will conduct safety talks and maintain the safety equipment, consult and carry out the instructions of the drilling supervisor. All personnel allowed in the well work area during drilling or testing operations will be instructed in the use of breathing equipment until supervisory personnel are satisfied that they are capable of using it.

After familiarization, each person must perform a drill with breathing equipment. The drill should include getting the breathing equipment, donning the breathing apparatus, and performing expected duties for a short period. A record shall be kept of all personnel drilled and the date of the drill. H₂S training records will be kept on location for all personnel.

Rig crews and service company personnel shall be made aware of the location of spare air bottles, resuscitation equipment, portable fire extinguishers, H₂S monitors and detectors. Knowledge of the location of the H₂S monitors and detectors are vital in determining as our gas location and the severity of the emergency conditions.

After any device has initially detected H₂S, all areas of poor ventilation shall be inspected periodically by means of a portable H₂S detector instrument. The buddy system will be utilized. (When an alarm sounds, personnel will don an SCBA, shut the well in, and proceed to SBA for roll call. The H₂S Technician or designee will mask up, with a buddy and will verify source of H₂S and report back to the on-site MRC Foreman.)

D. PROCEDURES PROGRAM

1. Drill Site
 - a. The drilling rig will be located to allow prevailing winds to blow across the reserve pit.
 - b. A Safe Briefing Area will be provided with a breathing air cascade trailer and or 30-minute SCBA's at the Primary Area. Personnel will assemble at the most up-wind station under alarm conditions, or when so ordered by the MRC Energy Co. representative, the Contractor representative, or

the Total Safety H₂S Safety Technician. Windssocks or streamers will be anchored to various strategic places on a pole about 10 feet high, so it is in easy view from the rig floor at all times.

- c. Warning signs will be posted on the perimeters. "No Smoking" signs will be posted by MRC Energy Co.as well.
- d. One multi-channel automatic H₂S monitor will be provided by Total Safety and the detector heads will be at the shale shaker, bell nipple, mud pits, rig floor, and quarter's area. The monitor will be located inside HSE or Company man trailer. Should the alarm be shut off to silence the sirens, the blinker light must continue to warn of H₂S presence. The Total Safety H₂S Safety Technician or designee will continuously monitor the detectors and will reactivate the alarm if H₂S concentrations increase to a dangerous level.
- e. A method of escape will be open at all times.
- f. If available, land line telephone service will be provided or cell phones provided. (Primary communications provided)
- g. A rig communication system will be provided, as needed.
- h. A gas trap, choke manifold, and degasser will be installed.
- i. A kill line, securely anchored and of ample strength, will be laid to the well-head from a safe location. This line is to be used only in an emergency.

General

- a. The MRC Energy Co. representative and/or the Contractor's Toolpusher will be available at all times. The drilling supervisor, while on duty, will have complete charge of the rig and location operations and will take whatever action is deemed necessary to insure personnel safety, to protect the well, and to prevent damage.
- b. A Mud Engineer will be on location at all times when drilling takes place at the depth H₂S may be expected. The mud engineer will be able to verify the presence or absence of H₂S.

III. CONDITIONS AND EMERGENCY PROCEDURES

A. DEFINITION OF OPERATIONAL "CONDITIONS"

CONDITION I	"POSSIBLE DANGER"
Warning Flags	Green
Alarms	No Alarm. Less than 10 ppm
Characterized By:	Drilling operations in zones that may contain hydrogen sulfide. This condition remains in effect unless H ₂ S is detected and it becomes necessary to go to Condition II.
General Action:	a. Be alert for a condition change b. Check all safety equipment for availability and proper functioning. c. Perform all drills for familiarization and proficiency.
CONDITION II	"MODERATE DANGER"
Warning Flags	Yellow
Alarms:	Actuates at 10 ppm. Continuous flashing light.
Characterized By:	Drilling operations in zones containing hydrogen sulfide. This condition will remain in effect until adding chemicals to the mud system neutralizes the hydrogen sulfide or it becomes necessary to go to Condition III.
General Action:	a. Be alert for a condition change b. WHEN DRILLING AHEAD - Driller and designated crewmember will don 30 min SCBA, shut-in the well and immediately proceed to the Safe Briefing Area. WHEN TRIPPING – Driller and two designated crewmembers will don 30 min SCBA, shut in the well and immediately proceed to the Safe Briefing Area. The Derrickman will

don a 5-minute escape pack, descend to the rig floor, don a 30-min SCBA (if necessary) and immediately proceed to the Safe Briefing Area.

- c. All In Scope Personnel will proceed directly to the appropriate Safe Briefing Area.
- d. Remain in safe briefing area, take roll call and wait for instructions
- e. Contact the Total H2S Technician if not on location.
- f. Personnel shall ensure that their breathing apparatus is properly fitted and operational before entering an H₂S contaminated area to provide assistance to anyone who may be injured or overcome by toxic gases.
- g. All Out of Scope Personnel will report to the appropriate Safe Briefing Area.

CONDITION III “EXTREME DANGER”
Warning Flags Red

Alarms Actuate at 15 ppm. Continuous Sirens and Flashing Lights

Characterized by: Critical well operations which pose an immediate threat of H₂S exposure to on-site personnel and a potential threat to the public.

- General Action:
- a. **WHEN DRILLING AHEAD -**
Driller and designated crewmember will don 30 min SCBA, shut-in the well and immediately proceed to the Safe Briefing Area.
 - WHEN TRIPPING –** Driller and two designated crewmembers will don 30

min SCBA, shut in the well and immediately proceed to the Safe Briefing Area. The Derrickman will don a 5-minute escape pack, descend to the rig floor, don a 30-min SCBA (if necessary) and immediately proceed to the Safe Briefing Area.

- b. All In Scope Personnel should don SCBA if nearby and immediately proceed to Safe Briefing Area. If SCBA is not nearby at time of alarm, DO NOT GO TOWARDS RIG AREA, but proceed directly to the Safe Briefing Area
- c. All out of Scope Personnel shall evacuate the location.
- d. Remain in the Safe Briefing Area, take roll call and wait for instructions.
- e. Contact the Total H2S Technician if not on location.
- f. Personnel shall ensure that their breathing apparatus is properly fitted and operational before entering an H₂S contaminated area to provide assistance to anyone who may be injured or overcome by toxic gases. Use the buddy system.
- g. Remain in safe briefing area, take roll call and wait for instructions.
- h. A cascade breathing air system shall be mobilized and utilized to conduct any additional on rig work required to correct the H₂S release condition.
- i. If well is ignited do not assume area is safe. SO₂ is hazardous and not all H₂S will burn.

H₂S EMERGENCY PROCEDURES; IN SCOPE PERSONNEL

A. Day To Day Drilling Operations

1. Upon discovering a release of H₂S gas in the ambient air by warning alarms or in any other way **Do Not Panic**.
2. Hold your breath donning the nearest Self Contained Breathing Apparatus and rapidly move up or across-wind away from the areas where H₂S sensing devices are in place, to the closest available safe briefing area. Continue to use breathing apparatus until it has been determined that the exposure of H₂S gas in the ambient air no longer exists. **Do Not Panic!**
3. Utilize the "Buddy System", i.e.; select and pair up each person participating in the drilling of an H₂S well prior to an emergency situation.
4. Help anyone who is overcome or affected by the H₂S gas by taking him/her up-wind out of the contaminated area. (This should be done utilizing an SCBA and with a buddy.)
5. Take necessary steps to confirm the release of the H₂S gas into the ambient air.
 - When an H₂S alarm activates, two designated personnel using the buddy system, while wearing their self contained breathing apparatus, will determine by the read-out on the fixed monitor which sensing device has detected the release of the H₂S gas.
 - They will utilize the hand-held sniffer type device at the particular sensing point disclosed on the fixed monitor to corroborate the fact that H₂S gas has actually been released. This will rule out the possibility of a false alarm. This will be done with a buddy and under mask after reporting to the Safe Briefing Area for roll call and instructions by on-site MRC Foreman.
6. Refer to the Emergency Phone Numbers and call emergency personnel.
7. Take the necessary steps to suppress the release of H₂S gas into the ambient air. Comply with the MRC Energy Co. Representative to physically suppress the release of H₂S gas at the actual release point.

8. Check all of MRC Energy Co.'s monitoring devices and increase gas-monitoring activities with the portable hand-operated H₂S and gas detector units.

Do Not Panic!

The MRC Energy Co. representative will assess the situation and with assistance of the Contractor's Representative and Total Safety's H₂S Safety Technician or on site designee, will assign duties to each person to bring the situation under control.

B. RESPONSIBILITIES OF WELL-SITE PERSONNEL

In the event of a release of potentially hazardous amounts of H₂S, all personnel will immediately don their protective breathing apparatus, the well will be shut in and personnel will proceed upwind to the nearest designated safe briefing area for roll call and instructions by MRC Foreman. Consideration will be given to evacuating Out of Scope Personnel, as situation warrants.

1. MRC ENERGY CO.'S Well-site Representatives

- a. If MRC Energy Co.'s well-site representative is incapacitated or not on location, this responsibility will fall to the Toolpusher/Driller.
- b. Immediately upon assessing the situation, set this plan into Action by initiating the proper procedures to contain the gas and notify the appropriate people and agencies.
- c. Ensure that the alarm area indicated by the fixed H₂S Monitor is checked and verified with a portable H₂S detector. (Safety Technician if on location or MRC assigned designee with a buddy utilizing SCBA's)
- d. Consult Pusher/driller of remedial actions as needed.
- e. Ensure that non-essential personnel proceed to the safe briefing area.
- f. Ensure location entrance barricades are positioned. Keep the number of persons on location to a minimum during hazardous operations.

- g. Consult each contractor, Service Company and all others allowed to enter the site, that H₂S gas may be encountered and the potential hazards that may exist.
- h. Authorize the evacuation of local residents if H₂S threatens Their safety.
- i. Non essential personnel should be evacuated from location if Situation warrants.

2. Toolpusher

- a. Toolpusher/Driller will assume responsibilities of MRC Energy Co.'s well-site representative if that person is incapacitated or not on location.
- b. Ensure that the alarm area indicated by the fixed H₂S monitor is checked and verified with a portable H₂S gas detector. (Alarm area indicated by the monitor will be Checked by the H₂S Technician and a buddy, under mask.) This will be done after checking in and roll call at the Upwind Safe Briefing Area.
- c. Confer with MRC Energy Co.'s well-site representative or superintendent and direct remedial action to suppress the H₂S and control the well.
- d. Ensure that personnel at the safe briefing area are instructed on emergency actions required.
- e. Ensure that personnel at the drill floor area are instructed on emergency actions required.
- f. Ensure that all personnel observe the appropriate safety and emergency procedures.
- g. Ensure that all persons are accounted for and provided emergency assistance as necessary.

3. Mud Engineer

- a. Run a sulfide check on the flowline mud.
- b. Take steps to determine the source of the H₂S and suppress it. Lime and H₂S scavenger shall be added to the mud as necessary.

4. Total H₂S Safety Technician, if on location, or MRC Designee

- a. H₂S Safety Technician or designee don nearest SCBA and report to Safe Briefing Area for roll call, take a buddy masked up and check monitor and verify with a portable H₂S detector the alarm area indicated by the fixed H₂S monitor. Advise the Toolpusher/Driller and MRC Energy Co.'s well-site representative of findings. Record all findings.
- b. If H₂S is flared, check for sulfur dioxide (SO₂) near the flare as necessary. Take hourly readings at different perimeters, log readings and record on location.
- c. Ensure that personnel at the safe briefing area are instructed on emergency actions required.
- d. Ensure that the appropriate warning flags are displayed.
- e. Ensure that all personnel are in S.C.B.A. as necessary.
- f. Ensure that all persons are accounted for and provide emergency assistance as necessary.
- g. Be prepared to evacuate rig if order is issued.

5. General Personnel & Visitors

- a. All In Scope Personnel, if not specifically designated to shut the well in or control the well, shall proceed to the (upwind) safe briefing area. All Out of Scope Personnel shall immediately proceed to the appropriate (upwind) safe briefing area or evacuate the site as conditions warrant.

- b. During any emergency, use the “buddy” system to prevent anyone from entering or being left in a gas area alone, even wearing breathing apparatus.
- c. Provide assistance to anyone who may be injured or overcome by toxic gases. Personnel shall ensure that their breathing apparatus is properly fitted and operational before entering a potentially H₂S contaminated area.
- d. Remain in safe briefing area and wait for instructions.

C. INSTRUCTIONS FOR IGNITING THE WELL

1. The Toolpusher/Driller will confer with MRC Energy Co.'s well-site representative who will secure the approval of the “Texas Wells Delivery Manager, prior to igniting the well, if at all possible.

The Toolpusher/Driller will be responsible for igniting the well in the event of severe well control problems. This decision should be made only as a last resort in situations where it is clear that:

- a. Human life and property are endangered, or
 - b. There is no hope of controlling the well under current conditions.
2. Once the decision has been made, the following procedures should be followed:
 - a. Two people wearing self-contained breathing apparatus will be needed for the actual lighting of the well. They must first establish the flammable perimeter by using an explosimeter. This should be established at 30% to 40% of the lower flammable limits.
 - b. After the flammable perimeter has been established and everyone removed from the area, the ignition team should select a site upwind of the well from which to ignite the well. This site should offer the maximum protection and have a clear path for retreat from the area.

- c. The ignition team should have safety belts and lifeline attached and manned before attempting ignition. If the leak is not ignited on the first attempt, move in 20 to 30 feet and fire again. Continue to monitor with the explosimeter and NEVER fire from an area with over 75% of the Lower Explosive Limit (LEL). If having trouble igniting the well, try firing 40 degrees to 90 degrees on either side of the well.
- d. If ignition is not possible due to the makeup of the gas, the toxic perimeter must be established and evacuation continued until the well is contained.
- e. All personnel must act only as directed by the person in charge of the operations.

NOTE: After the well is ignited, burning hydrogen sulfide (H_2S) will convert to sulfur dioxide (SO_2), which is also a highly toxic gas.

DO NOT ASSUME THE AREA IS SAFE AFTER THE WELL IS IGNITED

D. CORING PROCEDURES

Only essential personnel shall be on the rig floor. Ten (10) stands prior to retrieving core barrel; all personnel on drill floor and in derrick shall confirm self-Contained breathing apparatus available and ready for use.

A Total H₂S Technician will don a SCBA with a buddy assigned from the rig crew, and continuously monitor for H₂S at each connection. Any levels detected will require operations to be shut down and all involved personnel to don SCBAs. Precautions will remain in place until barrel is laid down.

All involved personnel will don SCBAs when removing the inner barrel from the outer barrel. SCBAs can be removed once the absence of H₂S is confirmed by the Total H₂S Technician.

Cores will be appropriately marked and sealed for transportation.

Normal Operations

1. Responsibilities of well-site personnel

a. Well-site Representative

1. Notify H₂S Technician of expected date to reach Contingency Plan implementation depth (Two (2) days prior to reaching suspected H₂S bearing zone) or prior to starting well work.
2. Ensure H₂S Safety Technician completes rig-up procedures prior to reaching Contingency Plan effective depth.
3. Restrict the number of personnel at the drilling rig or well site to a minimum while drilling, starting well work, testing or coring.
4. Ensure weekly H₂S drills/training are performed, if possible.

B. Toolpusher

1. Ensure that necessary H₂S safety equipment is provided on the rig, and that it is properly inspected and maintained.
2. Ensure that all personnel that work in the well area, are thoroughly trained in the use of H₂S safety equipment and periodic drills are held to maintain an adequate level of proficiency.

C. In Scope Personnel

1. Remain clean-shaven. Beards and long sideburns do not allow a proper facepiece seal.
2. Receive H₂S safety training on location, or confirm prior training by certification that is one year within date.
3. Familiarize yourself with the rig's Contingency Plan.
4. Inspect and practice putting on your breathing apparatus.

5. Know the location of the “safe briefing areas”.
6. Keep yourself “wind conscious”. Be prepared to quickly move upwind and away in the event of any emergency involving release of H₂S.

D. Total Safety H₂S Safety Technician or MRC Designee

1. Conduct training as necessary to ensure all personnel working in well area are familiar with the contingency procedures and the operation of emergency equipment.
2. Check all H₂S safety equipment to ensure that it is ready for emergency use:
 - Check pressure weekly for each shift on breathing apparatus (both 30-minute and hip-packs) to make sure they are charged to full volume.
 - Check pressure on cascade air bottles, if on location, to see that they are capable of recharging breathing apparatus.
 - Check oxygen resuscitator, if on location, to ensure that it is charged to full volume.
 - Check H₂S detectors weekly for each shift (fixed and portable), and explosimeter, to ensure they are working properly.
3. Provide a weekly report to MRC Energy Co.'s well-site representative documenting:
 - Calibrations performed on H₂S detectors.
 - Proper location and working order of H₂S safety equipment.
 - Attendance of all personnel, trained or retrained, and their company.
 - Weekly drills, if held and a list of personnel participating and summary of actions.

OUT OF SCOPE PERSONNEL

MRC Energy Co. policy will not require Out of Scope Personnel to be clean shaven, have processed medical questionnaires, fit testing, or have certified H2S Training.

SAFETY EQUIPMENT

All respirators will be designed, selected, used and maintained in conformance with ANSI Z88.2, American National Standard for respiratory protection.

Personal protective equipment must be provided and used. Those who are expected to use respiratory equipment in case of an emergency will be carefully instructed in the proper use and told why the equipment is being used. Careful attention will be given to the minute details in order to avoid possible misuse of the equipment during periods of extreme stress.

Self-contained breathing apparatus provides complete respiratory and eye protection in any concentration of toxic gases and under any condition of oxygen deficiency. The wearer is independent of the surrounding atmosphere because he/she is breathing with a system admitting no outside air. It consists of a full face mask, breathing tube, pressure demand regulator, air supply cylinder, and harness. Pure breathing air from the supply cylinder flows to the mask automatically through the pressure demand regulator which reduces the pressure to a breathing level. Upon inhalation, air flows into the mask at a rate precisely regulated to the user's demand. Upon exhalation, the flow to the mask stops and the exhaled breath passes through a valve in the face piece to the surrounding atmosphere. The apparatus includes an alarm & gauge which warns the wearer to leave the contaminated area for a new cylinder of air or cylinder refill.

The derrickman is provided with a full face piece unit attached to a 5-minute escape cylinder. He will also have his own self-contained 30-minute unit breathing apparatus located on the drilling floor. He will use the 5-minute unit to exit the derrick to the floor, donning the 30-minute unit located on the floor, if needed.

All respiratory protective equipment, when not in use, should be stored in a clean, cool, dry place, and out of direct sunlight to retard the deterioration of rubber parts. After each use, the mask assembly will be scrubbed with soap and water, rinsed thoroughly, and dried. Air cylinders can be recharged to a full condition from a cascade system.

Personnel in each crew will be trained in the proper techniques of bottle filling.

The primary piece of equipment to be utilized, should anyone be overcome by hydrogen sulfide, is the oxygen resuscitator, if on location.

When asphyxiation occurs, the victim must be moved to fresh air and immediately given artificial respiration. In order to assure readiness, the bottles of oxygen will be checked at regular intervals and an extra tank kept on hand.

Hand-operated pump-type detectors incorporating detector tubes will give more accurate readings of hydrogen sulfide. The pump-type draws air to be tested through the detector tube containing lead acetate-silica gel granules. Presence of hydrogen sulfide in the air sample is shown by the development of a dark brown stain on the granules, which is the

scale reading of the concentration of hydrogen sulfide. By changing the type of detector tube used, this detector may also be used for sulfur dioxide (SO₂) detection when hydrogen sulfide (H₂S) is being burned in the flare area.

Provisions must be made for the storage of all safety equipment as is evident from the foregoing discussion. All equipment must be stored in an available location so that anyone engaged in normal work situations is no more than "one breath away" from a mask.

V – TOXICITY OF VARIOUS GASES

Lethal Common Name ppm⁴	Chemical Formula	Specific Gravity¹	PEL (OSHA)²	STEL³
Hydrogen Cyanide 300	HCN	0.94	10	150
Hydrogen Sulfide 600	H ₂ S	1.18	20	Peak- 50ppm
Note: The ACGIH(7) recommends a TWA(6) value of 10ppm as the TLV(5) for H ₂ S and an STEL of 15ppm.				
Sulfur Dioxide 1000	SO ₂	2.21	2	5 ppm
Chlorine	CL ₂	2.45	1	
Carbon Monoxide 1000	CO	0.97	35	200/1 Hour
Carbon Dioxide 10%	CO ₂	1.52	5000	5%
Methane	CH ₄	0.55	90000	

¹ **Air = 1.0**

² **Permissible** - Concentration at which is believed that all workers may repeatedly be exposed, day after day, without adverse effect.

³ **STEL** - Short Term Exposure Limit. A 15-minute time weighted average.

⁴ **Lethal** - Concentration that will cause death with short-term exposure.

TLV – Threshold Limit Value; a concentration recommended by the American Conference of Governmental Industrial Hygienists (ACGIH)

TWA – Time Weighted Average; the average concentration of contaminant one can be exposed to over a given eight-hour period.

ACGIH – (American Conference of Governmental Industrial Hygienists) is an organization comprised of Occupational Health Professionals believed by many to be the top experts in the field of Industrial Hygiene. They are recognized as an expert resource by OSHA. The ACGIH releases a bi-annual publication "Threshold Limit Values and Biological Indices" that many safety professionals consider to be the authoritative document on airborne contaminants.

Reference: API RP-49, September 1974 - Reissued August 1978

VI. PROPERTIES OF GASES

A. CARBON DIOXIDE

1. Carbon Dioxide (CO₂) is usually considered inert and is commonly used to extinguish fires. It is 1.52 times heavier than air and will concentrate in low areas of still air. Humans cannot breathe air containing more than 10% CO₂ without losing conscience or becoming disorientation in a few minutes. Continued exposure to CO₂ after being affected will cause convulsions, coma, and respiratory failure.

2. The threshold limit of CO₂ is 5000 ppm. Short-term exposure to 50,000 ppm (5%) is reasonable. This gas is colorless, odorless, and can be tolerated in relatively high concentrations.

B. HYDROGEN SULFIDE

1. Hydrogen Sulfide (H₂S) is a colorless, transparent, flammable gas. It is heavier than air and, hence, may accumulate in low places.

2. Although the slightest presence of H₂S in the air is normally detectable by its characteristic "rotten egg" odor, it is dangerous to rely on the odor as a means of detecting excessive concentrations because the sense of smell is rapidly lost, allowing lethal concentrations to be accumulated without warning. The following table indicates the poisonous nature of H₂S.

CONCENTRATION			EFFECTS
% H ₂ S	PPM	GR/100 SCF ¹	
0.001	10	.65	Safe for 8 hours without respirator. Obvious and unpleasant odor.
0.0015	15	0.975	Safe for 15 minutes of exposure without respirator.
0.01	100	6.48	Kills smell in 3-15 minutes; may sting eyes and throat.
0.02	200	12.96	Kills smell quickly; stings eyes and throat.
0.05	500	32.96	Dizziness; breathing ceases in a few minutes; need prompt artificial respiration.
0.07	700	45.92	Rapid Unconsciousness; death will result if not rescued promptly.
0.1	1000	64.80	Instant unconsciousness, followed by death within minutes.

¹ Grains per 100 Cubic Feet

VII. Treatment Procedures for Hydrogen Sulfide Poisoning

- A. Remove the victim to fresh air.
- B. If breathing has ceased or is labored, begin resuscitation immediately.
Note: This is the quickest and preferred method of clearing victim's lungs of contaminated air; however, under disaster conditions, it may not be practical to move the victim to fresh air. In such instances, where those rendering first aid must continue to wear masks, a resuscitator should be used.
- C. Apply resuscitator to help purge H₂S from the blood stream.
- D. Keep the victim at rest and prevent chilling.
- E. Get victim under physician's care as soon as possible.

C. SULPHUR DIOXIDE

1. Sulfur Dioxide (SO₂) is a colorless, non-flammable, transparent gas.
2. SO₂ is produced during the burning of H₂S. Although SO₂ is heavier than air, it can be picked up by a breeze and carried downwind at elevated temperatures. Since SO₂ is extremely irritating to the eyes and mucous membranes of the upper respiratory tract, it has exceptionally good warning powers in this respect. The following table indicates the toxic nature of SO₂:

CONCENTRATION		EFFECTS
% SO ₂	PPM	
0.0005	3 to 5	Pungent odor, normally a person can detect SO ₂ in this range.
0.0012	12	Throat irritation, coughing, constriction of the chest, tearing and smarting of eyes.
0.015	150	So irritating that it can only be endured for a few minutes.
.05	500	Causes a sense of suffocation, event with the first breath.

VIII. BREATHING AIR EQUIPMENT DRILLS FOR ON & OFF DUTY PERSONNEL

An H₂S Drill and Training Session must be given once a week to ALL on-duty personnel with off duty personnel. On-duty and Off-duty personnel will reverse roles on alternate drills.

An H₂S drill and training session must be given once a week to all off-duty personnel in coincidence with on-duty personnel reversing roles on alternate drills.

The purpose of this drill is to instruct the crews in the operation and use of breathing air and H₂S related emergency equipment and to allow the personnel to become acquainted with using the equipment under working conditions. The crews should be trained to put on the breathing air equipment within one minute when required or requested to do so.

The following procedure should be used for weekly drills. The MRC supervisor must be satisfied that the crews are proficient with the equipment.

1. All personnel should be informed that a drill will be held.
2. The Total H₂S Safety Technician or a designee assigned by the MRC Drilling Foreman should initiate the drill by signaling as he/she would if H₂S was detected.
3. Personnel should don their breathing apparatus.
4. Once the breathing air equipment is on, the H₂S Technician should check all personnel to insure proper operation.

A training and information session will be conducted after each drill to answer any H₂S related questions and to cover any gaps identified from one of the following topics:

- Condition II, and III alerts and steps to be taken by all personnel.
- The importance of wind direction when dealing with H₂S.
- Proper use and storage of all types of breathing equipment.
- Proper use and storage of oxygen resuscitators.
- Proper use and storage of H₂S detectors (Mini Checks or equivalent).
- The "buddy system" and the procedure for rescuing a person overcome by H₂S.
- Responsibilities and duties.
- Location of H₂S safety equipment.
- Other parts of the "H₂S Contingency Plan" that should be reviewed.

NOTE: A record of attendance must be kept for weekly drills and training sessions.

IX. HYDROGEN SULFIDE TRAINING CURRICULUM

(FOR EMPLOYERS, VISITORS, AND CONTRACTORS)

EACH PERSON WILL BE INFORMED ON THE RESTRICTIONS OF HAVING BEARDS AND CONTACT LENS. THEY WILL ALSO BE INFORMED OF THE AVAILABILITY OF SPECTACLE KITS.

AFTER THE H₂S EQUIPMENT IS RIGGED UP, ALL IN SCOPE PERSONNEL WILL BE H₂S TRAINED AND PUT THROUGH A DRILL. ANY DEFICIENCIES WILL BE CORRECTED.

Training Completion cards are good for one year and will indicate date of completion or expiration. Personnel previously trained on another facility and visiting, must attend a "supplemental briefing" on H₂S equipment and procedures before beginning duty. Visitors who remain on the location more than 24 hours must receive full H₂S training given all crew members. A "supplemental briefing" will include but not be limited to: Location of respirators, familiarization with safe briefing areas, alarms with instruction on responsibilities in the event of a release and hazards of H₂S and (SO₂, if applicable). A training and drill log will be kept.

Topics for full H₂S training shall include the following equipment if on location, but not be limited to the following:

1. **Brief Introduction on H₂S**
 - A. Slide or Computer presentation (If Available)
 - B. H₂S material will be distributed
 - C. Re-emphasize the properties, toxicity, and hazards of H₂S
 - D. Source of SO₂ (if applicable)
2. **H₂S Detection**
 - A. Description of H₂S sensors
 - B. Description of warning system (how it works & it's location)
 - C. Actual location of H₂S sensors
 - D. Instruction on use of pump type detector (Gastec)
 - E. Use of card detectors, ampoules, or dosimeters
 - F. Use of combustible gas detector
 - G. Other personnel detectors used
 - H. Alarm conditions I & II,
 - I. SO₂ alarms (if applicable)

3. **H2S Protection**
 - A. Types of breathing apparatus provided (30-minute SCBA & 5-minute SCBA (with voice diaphragms for communication if supplied)
 - B. Principle of how breathing apparatus works
 - C. Demonstration on how to use breathing apparatus
 - D. Location of breathing apparatus
4. **Cascade System**
 - A. Description of cascade system
 - B. How system works
 - C. Cascade location of rig with reference to briefing areas
 - D. How to use cascade system (with 5-minute hose work line units & refill, if supplied)
 - E. Importance of wind direction and actual location of Windsocks
 - F. Purpose of compressor/function (if one is on site)
5. **H2S Rescue and First Aid**
 - A. Importance of wind direction
 - B. Safe briefing area
 - C. Buddy system
 - D. H2S symptoms
 - E. Methods of rescue
6. **Hands on Training**
 - A. Donning/familiarization of SCBA 30-minute unit
 - B. Donning/familiarization of SKADA 5- MIN. Packs
 - C. Familiarization of cascades
 - D. Use of O2 resuscitator
 - E. Alarm conditions - upwind briefing areas, etc...
 - F. Duties and responsibilities of all personnel
 - G. Procedures for evacuation
 - H. Search and Rescue teams
7. **Certification**
 - A. Testing on material covered

TOTAL SAFETY US INC., FIT TEST

X. EMPLOYEE INFORMATION

Employee Name: _____ Date: _____

Date of Employee Medical Evaluation: _____

Medical Status (circle): Unrestricted Limitations on Use Use Not
Authorized

RESPIRATOR INFORMATION

Respirator Type (Dustmask, SCBA, etc): _____

Brand: _____

Size: (circle): XS S M L XL

FIT TEST INFORMATION

Type of Fit Test Performed:

Quantitative

Porta Count
Fittester 3000

Fit Factor: _____

Fit Factor: _____

Qualitative

Irritant Smoke
Isoamyl Acetate (Banana Oil)
Saccharin
Bitrex

Passed / Failed

Passed / Failed

Passed / Failed

Passed / Failed

I hereby certify that this fittest was conducted in accordance with the OSHA Fit Testing Protocols found in Appendix A of 1910.134.

Fit Tester Name (Print): _____

Signature: _____ Date: _____

XI. H₂S SAFETY SERVICES

HYDROGEN SULFIDE SAFETY PACKAGE – Contained on location in Total Safety H₂S Equipment Trailer, unless otherwise noted:

RESPIRATORY SAFETY SYSTEMS

QTY DESCRIPTION

- 12 30-Minute Pressure Demand SCBA
(4-Primary Safe Briefing Area, 4-Secondary Safe Briefing Area, 4-floor with one of these for derrick man)
- 9 Hose Line 5-minute Work Unit w/Escapes Cylinder (1 in derrick, 6 on drill floor, 1 in mud pit wt area, 1 in shaker area)

The following shall be part of the package if requested by the MRC Foremen (at least one trailer with cascade system is required to be located in the MRC Magnolia asset for use as needed)

- 1 Breathing air cascade of 10 bottles w/regulator
- 2 Refill lines to refill 30-minute units on location
- 1 6-Man manifold that can be rigged up to work area on floor, if needed
- 6 25 foot hose lines
- 2 50 foot hose lines
- 100 Feet of hose line to rig cascade up to 12 man manifold on floor
- 12 30-minute Self Contained Breathing apparatus

DETECTION AND ALARM SAFETY SYSTEM

- 1 H₂S Fixed Monitor w/8Channels (Loc determined at rig up) suggested.
(Mud pit area, shaker area, bell nipple area, floor/driller area, & outside quarters)
- 5 H₂S Sensors
- 3 Explosion Proof Alarms (Light and Siren)
(1 on floor, 1 in work area, 1 in trailer area where quarters are located)
- 2 Personal H₂S monitors
- 1 Portable Tri-Gas Hand Held Meter (O₂, LEL, H₂S)
- 1 Sensidyne/Gastech Manual Pump Type Detector
- 8 Boxes H₂S Tubes Various Ranges
- 2 Boxes SO₂ Tubes Various Ranges
- 1 Calibration Gas
- 1 Set Paper Work for Records: Training, Cal, Inspection, other

ADDITIONAL SAFETY RELATED EQUIPMENT

QTY DESCRIPTION

2	Windssocks with Pole and Bracket
1	Set Well Condition Sign w/Green, Yellow, Red Flags
1	Primary Safe Briefing Area Sign
1	Secondary Safe Briefing Area Sign
6	Operating Condition Signs for Work Areas & Living Quarters

**TRAILER WITH BREATHING AIR CASCADE WILL
ALSO INCLUDE THE FOLLOWING:**

This equipment will be part of the H2S equipment stored in the trailer, when on location

1	First aid kit
1	Fire Blanket
1	Eye wash station
2	Safety Harness w/150' safety line

XII. EMERGENCY PHONE NUMBERS (Updated March 18, 2009)

EMERGENCY PHONE NUMBERS

MRC Energy Co. Emergency Phone #

MRC Energy Co. Permian Operations Phone-----

MRC Energy Co. Production

113 Daw Rd

Mansfield LA 71052

Title	Names	Phone	Cell
Operations Manager			
Operation Supt.			
Operations Supervisor			
Operations Supervisor			
Office Supervisor			
HSE			
Scheduler Planner			

Hydrogen Sulfide Safety Consultants

Total Safety W. Bender Blvd. Hobbs, NM	575-392-2973	After Hours 24 Hour Call Center Through Office Number
Tommy Throckmorton Operations Manager	575-392-2973	940-268-9614
Rodney Jourdan Sales Contact	575-392-2973	432-349-3928

MRC Energy Co. MEDICAL RESPONSE PLAN AND IT'S MEDICAL PROTOCOLS WILL BE FOLLOWED

MEDICAL COORDINATOR # -----

[Emergency Numbers & Directions](#)

Hospitals (911)

Artesia General Hospital 702 N. 13th St. Artesia, NM 88210	Main Phone Number	575-748-3333
Nor-Lea General Hospital 1600 N. Main Ave. Lovington, NM 88260	Main Phone Number	575-396-6611
Lea Regional Medical Center 5419 N. Lovington Hwy Hobbs, NM 88240	Main Phone Number	575-492-5260
Carlsbad General Hospital 2430 W. Pierce St. Carlsbad, NM	Main Phone Number	575-887-4100
Lovelace Regional Hospital 117 E. 19th St Roswell, NM 88201	Main Phone Number	575-627-7000
Winkler Co. Memorial Hospital 821 Jeffee Dr. Kermit, Texas 79745	Main Phone Number	432-586-8299
Reeves County Hospital 2323 Texas St. Pecos, Texas 79772	Main Phone Number	432-447-3551

State Police (911)

Texas DPS Loving co. 225 N.Pecos Mentone, Texas 79754	Office Number	432-377-2411
Texas DPS Winkler Co. 100 E Winkler Kermit, Texas 79745	Office Number	432-586-3465
Texas DPS Pecos Co. 148 N I-20 Frontage RD Pecos, Texas 79772	Office Number	432-447-3532
New Mexico State Police 3300 W. Main St Artesia, NM	Office Number	575-748-9718
New Mexico State Police 304 N. Canyon St Carlsbad, NM 88220	Office Number	575-885-3137
New Mexico State Police 5100 Jack Gomez Blvd. Hobbs, NM 88240	Office Number	575-392-5588

Local Law Enforcement (911) (Sheriff)

Reeves Co. Sheriff 500 N. Oak ST Pecos, Texas 79722	Office Number	432-445-4901
Winkler Co. Sheriff 1300 Bellaire St. Kermit, Texas 79745	Office Number	432-586-3461
Loving Co. Sheriff Courthouse Mentone, Texas	Office Number	432-377-2411
Lea Co. Sheriff 1417 S. Commercial St. Lovington, NM 88260	Office Number	
Eddy Co. Sheriff 305 N 7th St. Artesia, NM 88210	Office Number	575-766-9888
Eddy Co. Sheriff 305 N 7th St. Carlsbad, NM 88220	Office Number	575-746-9888

Federal & State Agencies

OSHA Lubbock Area Office 1205 Texas Av. Room 806 Lubbock, Texas 79401	Main Number	806-472-7681 EXT 7685
New Mexico Environment Department 400 N Pennsylvania Roswell, NM 88201	Joe Fresquez	575-623-3935
Texas Railroad Commission Midland, Texas	Main Number	844-773-0305
BLM Carlsbad, NM Field Office 620 E. Green ST Carlsbad, NM 88220	Main Number	575-234-5972
BLM Hobbs Field Station 414 W. Taylor Rd. Hobbs, NM 88240	Main Number	575-393-3612
BLM Roswell District Office 2909 W. Second St. Roswell, NM 88201	Main Number	575-627-0272
TECQ Texas Commission on Environmental Quality	Main Number	800-832-8224
New Mexico OCD		
U.S. Environmental Protection Agency Region 6 Texas/New Mexico	Main Number	214-655-2222
National Response Center Toxic Chemicals & Oil Spills	Main Number	800-424-8802

Rig Company

XIII. EVACUATION OF THE GENERAL PUBLIC

The procedure to be used in alerting nearby persons in the event of any occurrence that could pose a threat to life or property will be arranged and completed with public officials in detail, prior to drilling into the hydrogen sulfide formations.

In the event of an actual emergency, the following steps will be immediately taken:


1. The MRC Energy Co.'s representative will dispatch sufficient personnel to immediately warn each resident and transients down-wind within radius of exposure from the well site. Then warn all residence in the radius of exposure. Additional evacuation zones may be necessary as the situation warrants.
2. The MRC Energy Co.'s representative will immediately notify proper authorities, including the Sheriff's Office, Highway Patrol, and any other public officials as described above and will enlist their assistance in warning residents and transients in the calculated radius of exposure.
3. The MRC Energy Co.'s representative will dispatch sufficient personnel to divert traffic in the vicinity away from the potentially dangerous area. A guard to the entrance of the well site will be posted to monitor essential and non essential traffic.
4. General:
 - A. The area included within the radius of exposure is considered to be the zone of maximum potential hazard from a hydrogen sulfide gas escape. Immediate evacuation of public areas, in accordance with the provisions of this contingency plan, is imperative. When it is determined that conditions exist which create an additional area (beyond the initial zone of maximum potential hazard) vulnerable to possible hazard, public areas in the additional hazardous area will be evacuated in accordance with the contingency plan.
 - B. In the event of a disaster, after the public areas have been evacuated and traffic stopped, it is expected that local civil authorities will have arrived and within a few hours will have assumed direction of and control of the public, including all public areas. MRC Energy Co. will cooperate with these authorities to the fullest extent and will exert every effort by careful advice to such authorities to prevent panic or rumors.
 - C. MRC Energy Co. will dispatch appropriate management personnel at the disaster site as soon as possible. The company's personnel

will cooperate with and provide such information to civil authorities as they might require.

- D. One of the products of the combustion of hydrogen sulfide is sulfur dioxide (SO_2). Under certain conditions this gas may be equally as dangerous as H_2S . A pump type detector device, which determines the percent of SO_2 in air through concentrations in ppm, will be available. Although normal air movement is sufficient to dissipate this material to safe levels, the SO_2 detector should be utilized to check concentrations in the proximity of the well once every hour, or as necessary and the situation warrants. Also, if any low areas are suspected of having high concentrations, personnel should be made aware of these areas, and steps should be taken to determine whether or not these low areas are hazardous.

Exhibit E-6: H2S Contingency Plan Emergency Contacts
Matador Resources Company

Company Office			
Matador Resources Company		(972)-371-5200	
Key Personnel			
Name	Title	Office	Mobile
Billy Goodwin	Vice President Drilling	972-371-5210	817-522-2928
Gary Martin	Drilling Superintendent		601-669-1774
Dee Smith	Drilling Superintendent	972-371-5447	972-822-1010
Blake Hermes	Drilling Engineer	972-371-5485	713-876-8558
	Construction Superintendent		
Artesia			
Ambulance		911	
State Police		575-746-2703	
City Police		575-746-2703	
Sheriff's Office		575-746-9888	
Fire Department		575-746-2701	
Local Emergency Planning Committee		575-746-2122	
New Mexico Oil Conservation Division		575-748-1283	
Carlsbad			
Ambulance		911	
State Police		575-885-3137	
City Police		575-885-2111	
Sheriff's Office		575-887-7551	
Fire Department		575-887-3798	
Local Emergency Planning Committee		575-887-6544	
New Mexico Oil Conservation Division		575-887-6544	
Santa Fe			
New Mexico Emergency Response Comission (Santa Fe)		505-476-9600	
New Mexico Emergency Response Comission (Santa Fe) 24 hrs		505-827-9126	
New Mexico State Emergency Operations Center		505-476-9635	
National			
National Emegency Response Center (Washington, D.C.)		800-424-8802	
Medical			
Flight for Life- 4000 24th St.; Lubbock, TX		806-743-9911	
Aerocare- R3, Box 49F; Lubbock, TX		806-747-8923	
Med Flight Air Amb- 2301 Yale Blvd S.E., D3; Albuquerque, NM		505-842-4433	
SB Air Med Service- 2505 Clark Carr Loop S.E.; Albuquerque, NM		505-842-4949	
Other			
Boots & Coots IWC		800-256-9688	or 281-931-8884
Cudd Pressure Control		432-699-0139	or 432-563-3356
Haliburton		575-746-2757	
B.J. Services		575-746-3569	

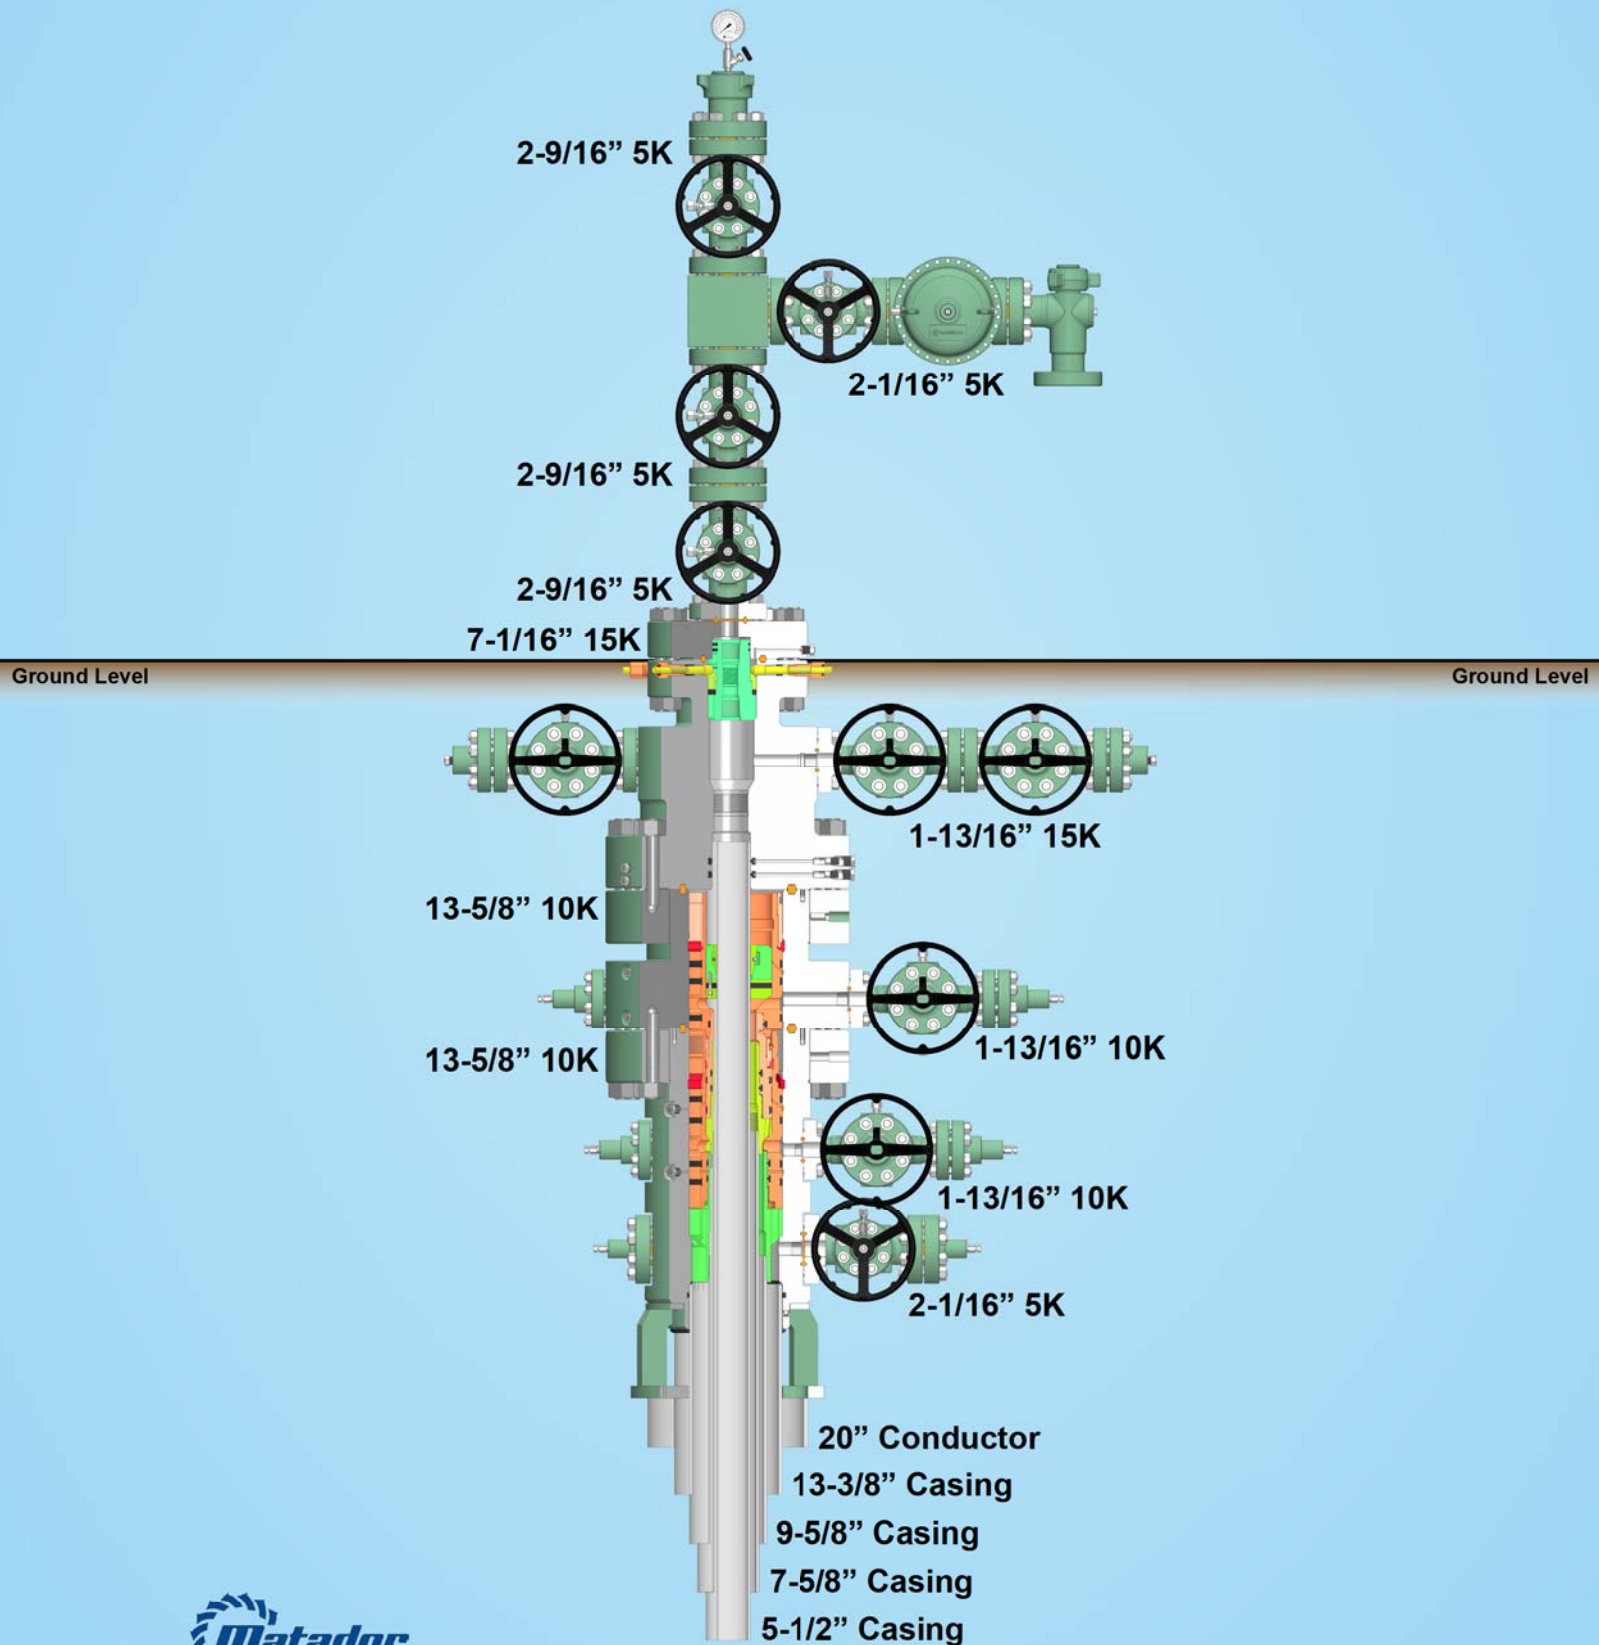

Voni Fed Com #204H
 SHL: 260' FNL & 1128' FEL Section 21
 BHL: 240' FSL & 990' FEL Section 33
 Township/Range: 26S 31E
 Elevation Above Sea Level: 3191

Drilling Operation Plan

Proposed Drilling Depth: 23705' MD / 11386' TVD

Type of well: Horizontal well, no pilot hole

Permitted Well Type: Gas

Geologic Name of Surface Formation Quaternary Deposits

KOP Lat/Long (NAD83): 32.0353297881 N / -103.7776539289 W

TD Lat/Long (NAD83): 32.0008422632 N / -103.7777515396 W

1. Estimated Tops

Formation	MD (ft)	TVD (ft)	Thickness (ft)	Lithology	Resource
Rustler	893	893	681	Anhydrite	Barren
Salado (Top of Salt)	1,574	1,574	1,817	Salt	Barren
Castile	3,391	3,391	634	Salt	Barren
Lamar (Base of Salt)	4,025	4,025	27	Salt	Barren
Bell Canyon	4,052	4,052	1,090	Sandstone	Oil/Natural Gas
Cherry Canyon	5,142	5,142	1,149	Sandstone	Oil/Natural Gas
Brushy Canyon	6,291	6,291	1,653	Sandstone	Oil/Natural Gas
Bone Spring Lime	7,944	7,944	986	Limestone	Oil/Natural Gas
1st Bone Spring Sand	8,930	8,930	425	Sandstone	Oil/Natural Gas
2nd Bone Spring Carbonate	9,355	9,355	253	Carbonate	Oil/Natural Gas
2nd Bone Spring Sand	9,608	9,608	503	Sandstone	Oil/Natural Gas
3rd Bone Spring Carbonate	10,111	10,111	708	Carbonate	Oil/Natural Gas
3rd Bone Spring Sand	10,819	10,819	418	Sandstone	Oil/Natural Gas
KOP	10,831	10,813	-	Shale	Oil/Natural Gas
Wolfcamp	11,305	11,237	-	Shale	Oil/Natural Gas
TD	23,705	11,386		Shale	Oil/Natural Gas

2. Notable Zones

Wolfcamp is the goal. All perforations will be within the setback requirements as prescribed or permitted by the New Mexico Oil Conservation Division. OSE estimated ground water depth at this location is 230'

3. Pressure Control

Equipment

A 18,000' 10,000-psi BOP stack consisting of 3 rams with 2 pipe rams, 1 blind ram, and one annular preventer will be utilized below surface casing to TD. See attachments for BOP and choke manifold diagrams.

An accumulator complying with Onshore Order #2 requirements for the pressure rating of the BOP stack will be present. A rotating head will also be installed as needed.

Testing Procedure

BOP will be inspected and operated as required in Onshore Order #2. Kelly cock and sub equipped with a full opening valve sized to fit the drill pipe and collars will be available on the rig floor in the open position.

A third party company will test the BOPs.

After setting surface casing, a minimum 10M BOPE system will be installed. Test pressures will be 250 psi low and 10,000 psi high with the annular preventer being tested to 250 psi low and 5000 psi high before drilling below surface shoe. In the event that the rig drills multiple wells on the pad and any seal subject to test pressures are broken, a full BOP test will be performed when the rig returns and the 10M BOPE system is re-installed.

Variance Request

Matador requests a variance to have the option of running a multi-bowl wellhead assembly for setting the Intermediate 1, Intermediate 2, and Production Strings. The BOPs will not be tested again unless any flanges are separated.

Matador requests a variance to drill this well using a co-flex line between the BOP and choke manifold. Certification for proposed co-flex hose is attached. The hose is not required by the manufacturer to be anchored. If the specific hose is not available, then one of equal or higher rating will be used.

Matador requests a variance to have the option of batch drilling this well with other wells on the same pad. In the event that this well is batch drilled, the wellbore will be secured with a blind flange of like pressure. When the rig returns to this well and BOPs are installed, the operator will perform a full BOP test.

Matador requests a variance to drill this well using a 5M annular preventer with a 10M BOP ram stack. The "Well Control Plan For 10M MASP Section of Wellbore" is attached.

4. Casing & Cement

All casing will be API and new. See attached casing assumption worksheet.

String	Hole Size (in)	Set MD (ft)	Set TVD (ft)	Casing Size (in)	Wt. (lb/ft)	Grade	Joint	Collapse	Burst	Tension
Surface	17.5	0 - 918	0 - 918	13.375	54.5	J-55	BUTT	1.125	1.125	1.8
Intermediate 1 Top	9.875	0 - 9500	0 - 9500	7.625	29.7	P-110	BUTT	1.125	1.125	1.8
Intermediate 1 Bottom	8.75	9500 - 10681	9500 - 10663	7.625	29.7	P-110	VAM HTF-NR	1.125	1.125	1.8
Production	6.75	0 - 23705	0 - 11386	5.5	20	P-110	Hunting TLW	1.125	1.125	1.8

- All casing strings will be tested in accordance with Onshore Order #2 - III.B.1.h
- Rustler top will be validated via drilling parameters (i.e. reduction in ROP) and surface casing setting depth revised accordingly if needed
- All non-API joint connections will be of like or greater quality, and as run specification sheets will be on location for review
- Request the option to deepen the Intermediate 1 casing set depth to 70° in curve, no changes in pipe grade or weight is necessary.

Variance Request

Matador request a variance to wave the centralizer requirement for the 7-5/8" flush casing in the last 800' of 8-3/4" hole and the 5-1/2" SF/Flush casing in the 6-3/4" hole.

If a DV tool is used, depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above the current shoe. Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

9-7/8" hole depth may fluctuate, but 7-5/8" BUTT will only be run inside of 9-7/8" OH and Flush joint will be run in 8-3/4" OH. Cement volumes will be adjusted proportionally. Option to drill the entire Intermediate 1 hole section in 9-7/8" hole size.

Matador request option to perform a bradenhead cement squeeze on Intermediate 1 string.

Matador request a variance to utilize a surface setting rig. If this is used, Matador request the option to drill either 17.5" or 20" surface hole.

String	Type	Sacks	Yield	Cu. Ft.	Weight	Percent Excess	Top of Cement	Class	Blend
Surface	Lead	420	1.72	716	12.5	50%	0	C	5% NaCl + LCM
	Tail	250	1.38	347	14.8	50%	618	C	5% NaCl + LCM
Intermediate 1 DV ~4,200'	Lead	400	3.66	1457	10.3	35%	0	A/C	Stage 2: Tuned light blend
	Lead	430	3.66	1589	10.3	35%	4200	A/C	Stage 1: Fluid Loss + Dispersant + Retarder + LCM
	Tail	110	1.46	156	13.2	35%	9681	A/C	Stage 1: Fluid Loss + Dispersant + Retarder
Intermediate 1 Alternate Design- Bradenhead Squeeze	Lead	770	3.66	2807	10.3	35%	0	A/C	Tuned light blend
	Tail	110	1.43	156	13.2	35%	9681	A/C	Stage 1: Fluid Loss + Dispersant + Retarder
	Tail	1000	1.46	1460	14.2	35%	0	C	Bradenhead Contingency: Clas C Cement + LCM
Production	Tail	1050	1.17	1227	14.5	10%	10481	H	Fluid Loss + Dispersant + Retarder

5. Mud Program

An electronic Pason mud monitoring system complying with Onshore Order 2 will be used. All necessary mud products (barite, bentonite, LCM) for weight addition and fluid loss control will be on location at all times. Mud program is subject to change due to hole conditions.

Hole Section	Hole Size (in)	Mud Type	Interval MD (ft)	Density (lb/gal)	Viscosity	Fluid Loss
Surface	17.5	Spud Mud	0 - 918	8.4 - 8.8	28-30	NC
Intermediate 1	9.875	Diesel Brine Emulsion	918 - 10681	8.4 - 9.4	28-30	NC
Production	6.75	OBM	10681 - 23705	11.5 - 12.5	50-65	<20

6. Cores, Test, & Logs

No core or drill stem test is planned.

No electric logs are planned at this time. GR will be collected through the MWD tools from Intermediate casing to TD. CBL with CCL will be run as far as gravity will let it fall to top of curve.

7. Down Hole Conditions

No abnormal pressure or temperature is expected. Maximum anticipated surface pressure is 4896 psi. Expected bottom hole temperature is 187 F.

In accordance with Onshore Order 6, Matador does not anticipate that there will be enough H₂S from the surface to the Bone Spring formations to meet the BLM's minimum requirements for the submission of an "H₂S Drilling Operation Plan" or "Public Protection Plan" for the drilling and completion of this well. Since we have an H₂S safety package on all wells, attached is an "H₂S Drilling Operations Plan". Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely. All personnel will be familiar with all aspects of safe operation of equipment being used.
