

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

N.M. Oil Cons. Div.-Dist. 2
1301 W. Grand Avenue
Artesia, NM 88210

FORM APPROVED
Budget Bureau No. 1004-0135
Expires July 31, 1996

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other instructions on reverse side

1. Type of Well

☐ Oil Well ☒ Gas Well ☐ Other

2. Name of Operator

OXY USA WTP Limited Partnership

3a. Address

P.O. Box 50250, Midland, TX 79710-0250

3b. Phone No. (include area code)
915-685-5717

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

1600 FSL 990 FWL NWSW(L) Sec 20 T17S R31E

6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.

8. Well Name and No.

OXY Chocolate 1

Moose Federal

9. API Well No.

30-015-32119

10. Field and Pool, or Exploratory Area

Undsg. Cedar Lake Morrow, N.

11. County or Parish, State

Eddy NM

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

☐ Notice of Intent
☒ Subsequent Report
☐ Final Abandonment Notice

TYPE OF ACTION

☐ Acidize ☐ Deepen ☐ Production (Start/Resume) ☐ Water Shut-Off
☐ Alter Casing ☐ Fracture Treat ☐ Reclamation ☐ Well Integrity
☐ Casing Repair ☐ New Construction ☐ Recomplete ☒ Other Spud, set
☐ Change Plans ☐ Plug and Abandon ☐ Temporarily Abandon ☐ CSG & CMT
☐ Convert to Injection ☐ Plug Back ☐ Water Disposal

3. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the final site is ready for final inspection.)

NOTIFIED BLM 12/18/01 OF SPUD. MIRU KEY #37, SPUD WELL @ 0900hrs 12/20/01. DRILL 17-1/2" HOLE TO TD @ 445', 12/11/01, PUMP SWEEP, CIRC. RIH W/ 13-3/8" 48# H40 CSG, SET @ 445'. M&P 300sx 65/35 C/POZ W/ 6% BENTONITE + 2% CaCl2 + 5#/sx GILSONITE FOLLOWED BY 200sx CL C W/ 2% CaCl2, DISP W/ FW, BUMP PLUG, 12/22/01, CIRC 100sx CMT TO PIT, WOC-6hrs. BLM NOTIFIED BUT DID NOT WITNESS. CUT OFF CASING, WELD ON STARTING HEAD, TEST TO 500#, OK. NU BOP & CHOKE MANIFOLD, TEST BLIND RAMS, PIPE RAMS, & HYDRIL TO 1000#, OK. TOTAL WOC-18hrs, RIH & TAG, DRILL OUT & DRILL AHEAD 12/22/01.

DRILL 12-1/4" HOLE TO TD @ 4550', 12/31/01, PUMP SWEEP, CIRC. RIH W/ 83 JTS 9-5/8" 40-36# N80-K55 CSG, AND PIPE GOT STUCK.

SEE ATTACHED FOR THE WORK DONE 1/1/02-1/8/02.

ACCEPTED FOR RECORD

JAN 15 2002

ALEXIS C. SWOBODA
PETROLEUM ENGINEER

14. I hereby certify that the foregoing is true and correct
Name (Printed/Typed)

David Stewart

Title

Sr. Regulatory Analyst

Date

1/1/02

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title


Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on reverse)



ATTACHMENT 3160-5

01/01/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)

Job:DRILL & EQUIP Flag:GREEN CMIC:MESSENGER

Days Since Spud: 11 Days on Location: 12

Total Depth (Md): 4503 Total Depth (Tvd):

Amt Drilled (Md): 53 Amt Drilled (Tvd): 0

P.B.T.D. (Mtd): P.B.T.D. (Tvd):

Perforations:

Formations:

Pres Oprs: WAIT ON FISHING TOOLS

Daily Cost: \$23424 CUM Cost: \$305132 AFE Cost: \$0

Daily Remarks:

DRILLING F/ 4550' TO 4503'. REACHED TD AT 8:45 AM MST. CIRCULATE FOR CASING. DROP TOTCO & TRIP FOR CASING. TRIPPING SLOW, PIPE VERY TIGHT. RIG UP LAYDOWN MACHINE & LAYDOWN 8" DRILL COLLARS. RIG UP CASING CREW & RUN 83 JTS 9 5/8" 40# & 36# NS-80 & K-55 CASING. WASHED DOWN 3 JOINTS & RAN IN 3 JOINTS. PICKED UP 83rd JPINT & WOULD NOT GO. PICKED UP TO STABBING BORAD TO INSTALL SWEDGE. PIPE WAS FREE AT THAT POINT. TRIED TO PUMP INTO CASING, PACKED OFF. WORK STUCK PIPE. LAYED DOWN LAST JOINT PICKED UP & CHANGED ELEVATORS. WORK STUCK PIPE & TRY TO PUMP INTO CASING. HELD 1500 PSI & WORK PIPE. NO MOVEMENT. BLEED OFF PRESSURE & WORK PIPE. PULLED UP TO 275,000lb. PIPE SEEMING TO MOVE UP SLIGHTLY. PULLED 250,000 & WT INDICATOR SEEMED TO INDICATE PIPE MOVEMENT. CASING PARTED 2 JTS BELOW ROTARY TABLE. WT. INDICATOR MALFUNCTIONED. PASON INDICATOR SHOULD A MAXIMUM PULL OF 405,000lb WHEN PIPE PARTED. CHECK CROWN & BLOCK SHEAVES FOR JUMPED LINE. EVERY THING OK. LAY DOWN 2 JOINTS CASING. WAIT ON FISHING TOOLS.

01/02/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)

Job:DRILL & EQUIP Flag:GREEN CMIC:MESSENGER

Days Since Spud: 12 Days on Location: 13

Total Depth (Md): 4503 Total Depth (Tvd):

Amt Drilled (Md): 0 Amt Drilled (Tvd): 0

P.B.T.D. (Mtd): P.B.T.D. (Tvd):

Perforations:

Formations:

Pres Oprs: WORK STUCK CASING

Daily Cost: \$15131 CUM Cost: \$320263 AFE Cost: \$0

Daily Remarks:

WAIT ON TOOLS. PICK UP TOOLS & SPEAR CASING. WORK CASING. RIG UP WIRLINE TRUCK & BACK OFF CASING. RIG UP CASERS & LAY DOWN TOP JOINT. PICK 3 JOINTS OF CASING & ATTEMPT TO SCREW INTO CASING. LAY DOWN 12 JOINTS CASING. TOP OF FISH AT +- 490' W/ PIN LOOKING UP. WAIT ON OVERSHOT. PICK UP TOOLS & TRIP IN HOLE W/ OVERSHOT. WORK TOOLS OVER FISH. WORK STUCK PIPE.

01/03/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)

Job:DRILL & EQUIP Flag:GREEN CMIC:MESSENGER

Days Since Spud: 13 Days on Location: 14

Total Depth (Md): 4503 Total Depth (Tvd):

Amt Drilled (Md): 0 Amt Drilled (Tvd): 0

P.B.T.D. (Mtd): P.B.T.D. (Tvd):

Perforations:


Formations:

Pres Oprs: WAIT ON CASING CREW

Daily Cost: \$22318 CUM Cost: \$361392 AFE Cost: \$0

Daily Remarks:

WORK STUCK PIPE. RUN IN HOLE W/ MAGNETIC FREE POINT TOOL. TORQUE READING GOOD AT 3338'. POOH W/ FP & RIH W/ PERF GUN & SHOT 4 HOLES @ 3378'. ATTEMPT TO CIRCULATE BUT COULD NOT. RIH W/ FP & CHECK FP READINGS. STILL ABLE TO GET TORQUE READINGS BUT NO GOOD STRETCH READINGS. PERFORATE PIPE AT 3333' & ATTEMPT TO CIRCULATE. COULD NOT BREAK CIRCULATION. RIH W/ BOW SPRING TYPE FP TOOL. GOOD TORQUE & STRETCH AT 2640', RESTRICTED @ 2650', 50% STUCK @ 2662'. POOH W/ FP & RIH W/ 300GRAIN SHOT & ATTEMPT TO BACK OFF AT 2633'. PIPE UNSCREWED @ 1407'. TRIP OUT OF HOLE & LAYDOWN FISHING TOOLS. WAIT ON CASING CREW.



01/04/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)

Job:DRILL & EQUIP Flag:GREEN CMIC:MESSENGER
Days Since Spud: 14 Days on Location: 15
Total Depth (Md): 4503 Total Depth (Tvd):
Amt Drilled (Md): 0 Amt Drilled (Tvd): 0
P.B.T.D. (Mtd): P.B.T.D. (Tvd):
Perforations:
Formations:
Pres Oprs: PU DRILL COLLARS
Daily Cost: \$35908 CUM Cost: \$378489 AFE Cost: \$0

Daily Remarks:

WAIT ON CASING CREW. RIG UP CASING CREW & LAYDOWN 22 JOINTS CASING.
RIG DOWN CASERS. TIH W/ OVERSHOT. CATCH FISH & RIG UP WIRELINE & ATTEMPT
TO BACK OFF AT 2650'. ATTEMPTED 3 SHOTS TO BACK OFF. NOT LOSING ANY
TORQUE. MANUALLY BACKED OFF CASING. TRIP OUT OF HOLE & LAY DOWN 7 JOINTS
OF CASING. TOP OF FISH NOW AT 1719'. MAKE UP INSIDE CUTTER & TRIP IN
HOLE & CUT CASING AT 2645'. MILLED UP 1' OF CASING. TRIP OUT OF HOLE
W/ CUTTER & LAYDOWN. PICK UP COLLARS.

01/05/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)

Job:DRILL & EQUIP Flag:GREEN CMIC:MESSENGER
Days Since Spud: 15 Days on Location: 16
Total Depth (Md): 4503 Total Depth (Tvd):
Amt Drilled (Md): 0 Amt Drilled (Tvd): 0
P.B.T.D. (Mtd): P.B.T.D. (Tvd):
Perforations:
Formations:
Pres Oprs: PICK UP FISHING TOOLS
Daily Cost: \$21666 CUM Cost: \$400155 AFE Cost: \$0

Daily Remarks:

PU 9 8" DRILL COLLARS & TRIP IN HOLE. WORK OVER FISH & JAR ON FISH.
OVERSHOT SLIPPED OFF OF FISH. CIRCULATE SWEEP. TOOH. PU NEW OVERSHOT
& TRIP IN HOLE. WORK OVERSHOT OVER FISH. FISH LOOSE. CIRCULATE SWEEP
OUT OF HOLE. TOOH. LAY DOWN FISHING TOOLS. COULD NOT GET OVERSHOT OFF
OF FISH. LAY DOWN 20 JOINTS OF CASING. TOP OF FISH 2584'. 19 JOINTS
LEFT IN HOLE. PICK UP FISHING TOOLS.

01/06/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)


Job:DRILL & EQUIP Flag:GREEN CMIC:MESSENGER
Days Since Spud: 16 Days on Location: 17
Total Depth (Md): 4503 Total Depth (Tvd):
Amt Drilled (Md): 0 Amt Drilled (Tvd): 0
P.B.T.D. (Mtd): P.B.T.D. (Tvd):
Perforations:
Formations:
Pres Oprs: JAR ON 9 5/8" CASING
Daily Cost: \$22925 CUM Cost: \$423080 AFE Cost: \$0

Daily Remarks:

TRIP IN HOLE & SPEAR INTO FISH. TRIP OUT OF HOLE W/ 60' OF FISH. LAY
DOWN FISH. TRIP IN HOLE & TAG FISH AT 1645'. CIRCULATE HOLE & PUMP 2
70 BBL 120+ VIS SWEEPS. DID NOT SEE ANY PART OF SWEEPS COME OUT OF HOLE.
ENGAGE FISH & JAR ON FISH W/ 175000' OVERPULL. MOVED FISH UP HOLE 5'.
WHILE JARRING, KEEPER HOLDING BAILS ON BLOCKS BROKE & ONE BAIL FELL TO
FLOOR. NO ONE ON FLOOR AT THE TIME.

01/07/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)

Job:DRILL & EQUIP Flag:GREEN CMIC:MESSENGER
Days Since Spud: 17 Days on Location: 18
Total Depth (Md): 4503 Total Depth (Tvd):
Amt Drilled (Md): 0 Amt Drilled (Tvd): 0
P.B.T.D. (Mtd): P.B.T.D. (Tvd):

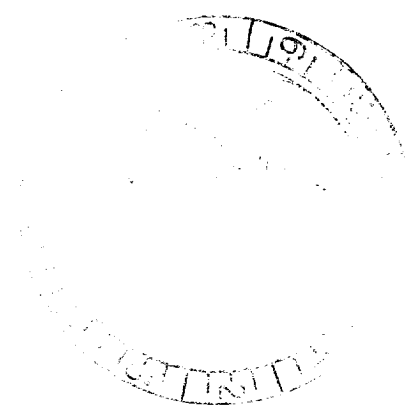

Perforations:

Formations:

Pres Oprs: TRIP IN HOLE W/ BIT TO MIX MUD

Daily Cost: \$18267 CUM Cost: \$441347 AFE Cost: \$0

Daily Remarks:

JAR ON FISH. WORK OVERSHOT OFF OF FISH. LAY DOWN 2 JOINTS & CIRCULATE
HOLE & WAIT ON BLOCKS. CHANGE OUT BLOCKS. TRIP OUT OF HOLE & LAYDOWN
FISHING TOOLS. TRIP IN HOLE W/ BIT. WORK INTO TOP OF FISH. MUD UP WELL BORE.

01/08/2002 OXY CHOCOLATE MOOSE FEDERAL NO. 1 (Drilling)

Job:DRILL & EQUIP CMIC:MESSENGER

Days Since Spud: 18 Days on Location: 19

Total Depth (Md): 4503 Total Depth (Tvd):

Amt Drilled (Md): 0 Amt Drilled (Tvd): 0

P.B.T.D. (Mtd): P.B.T.D. (Tvd):

Perforations:

Formations: DOLOMITE

Pres Oprs: CLEANING OUT CASING AT 2782'

Daily Cost: \$20693 CUM Cost: \$462040 AFE Cost: \$0

Daily Remarks:

CIRCULATED AND CONDITIONED MUD FOR 15 HOURS. TIH WITH BIT AND TAGGED
UP AT 2703'. CLEANING OUT CASING AT 2782' AT REPORT TIME.

