


Parkway West Unit #6
660' FSL & 1980' FEL
Sec. 21, T-19-S, R-29-E
Eddy Co., NM

Elevation: 3330' GL, 3347' KB

Current Completion

Spud Date: 8/10/79

Completion Date: 10/79

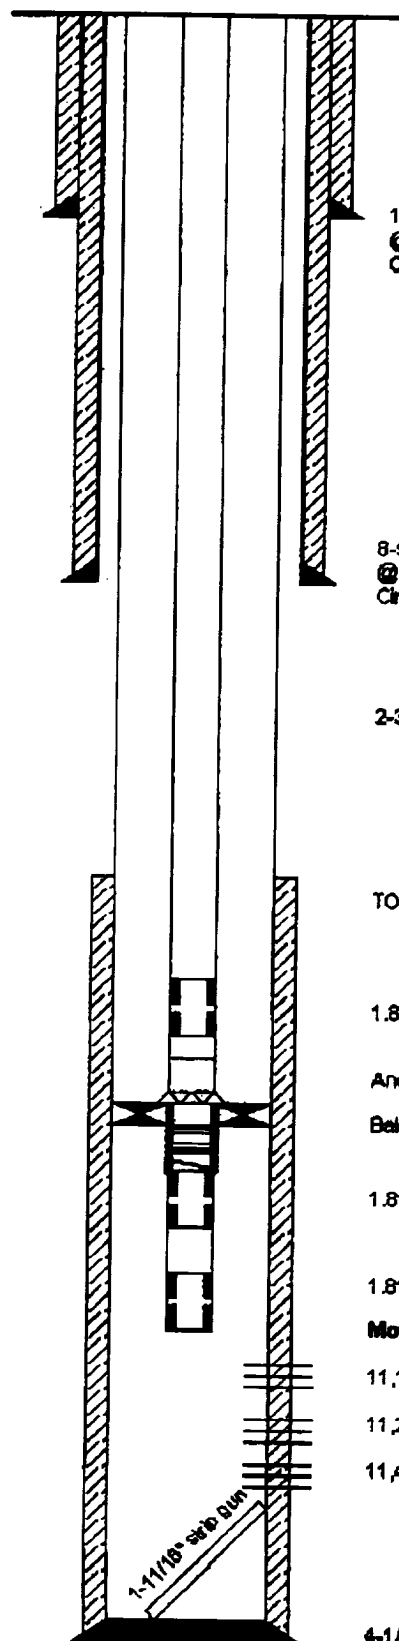

Completion

10/79: Perf'd Morrow 11,489-76' (1 spf) using 1-11/16" strip gun thru tog 20 min SITP - 3100 psi. IP 5.4 MMcf/d. SI well while w/o facilities.

2/88: Treated Morrow perfs w/2500 gals 7.5% MS acid w/1000 scf/bbl N2. Well would not unload. Swabbed back load w/no flow.

3/80: Perf'd Morrow 11,298-305', 11,308-11' & 11,316-20' (1 spf) using 1-11/16" thru tubing strip gun. Lost strip gun in the hole. Treated all perfs w/3000 gals 7.5% MS acid w/1000 scf/bbl N2. IP 950 Mcf/d.

12/84: Perf'd Morrow 11,170-92', 11,228-32', 11,246-54' (4 spf) using 1-11/16" strip gun. Lost strips in the hole after perfing.

Tubing Detail

Description	Depth (Top)
2-3/8" N-80 Landing fl	17.00'
2-3/8", 4.7# N-80 EUE 8rd 6' sub	47.65'
352 lbs 2-3/8", 4.7# N-80 EUE 8rd	53.74'
1.875" Baker "F" nipple	10,888.74'
1 ft 2-3/8", 4.7# N-80 EUE 8rd	10,990.67'
Baker Model DB packer (10' Millout ext?)	11,020.00'
10' pup fl 2-3/8" N80	11,033.00'
1.812" Baker "F" nipple	11,043.00'
10' pup fl 2-3/8" N80	11,044.00'
1.812" Baker "R" nipple	11,054.00'

1.875" Baker "F" nipple

Anchor seal assy

Baker Model DB @ 11,020'

1.812" Baker "F" nipple @ 11,043'

1.812" Baker "R" nipple @ 11,054'

Morrow Perfs

11,170-92', 11,228-32', 11,246-54' (4 spf)

11,298-305', 11,308-11', 11,316-20' (1 spf)

11,489-76' (1 spf)

4-1/2", 11.8# & 13.5# N-80 LT&C
@ 11,870' Cmt'd w/875 sx
