District I

1625 N. French Dr. Hobbs, NM 88240

District II

1301 W Grand Ave, Artesia, NM 88210

District III

1000 Rio Brazos Rd Aztec, NM 87410

State of New Mexico Energy Minerals and Natural Resources

> Department Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505

July 21, 2008 For temporary pits, closed-loop sytems, and below-grade

Form C-144

tanks, submit to the appropriate NMOCD District Office

For permanent pits and exceptions submit to the Santa Fe Environmental Bureau office and provide a copy to the appropriate NMOCD District Office

District IV 1220 S St Francis Dr , Santa Fe, NM 87505 Pit, Closed-Loop System, Below-Grade Tank, or Proposed Alternative Method Permit or Closure Plan Application Type of action: Permit of a pit, closed-loop system, below-grade tank, or proposed alternative method X Closure of a pit, closed-loop system, below-grade tank, or proposed alternative method Modification to an existing permit Closure plan only submitted for an existing permitted or non-permitted pit, closed-loop system, below-grade tank, or proposed alternative method Instructions: Please submit one application (Form C-144) per individual pit, closed-loop system, below-grade tank or alternative request Please be advised that approval of this request does not relieve the operator of liability should operations result in pollution of surface water, ground water or the environment. Nor does approval relieve the operator of its responsibility to comply with any other applicable governmental authority's rules, regulations or ordinances Operator Burlington Resources Oil & Gas Company, LP OGRID#: 14538 Address. P.O. Box 4289, Farmington, NM 87499 Facility or well name CANYON LARGO UNIT 239N API Number. 30-039-30883 OCD Permit Number U/L or Otr/Otr L(NW/SW) Section: 25N Township Range^{*} County. Rio Arriba 36.42675 °W NAD. ☐ 1927 🗓 1983 Center of Proposed Design. Latitude ٥N 107.42568 Longitude: Surface Owner: X Federal Private Tribal Trust or Indian Allotment X Pit: Subsection F or G of 19 15 17 11 NMAC X Drilling Workover Temporary Permanent Emergency Cavitation P&A Thickness 20 mil X LLDPE HDPE PVC Other X Lined Unlined Liner type X String-Reinforced X Welded X Factory Other Liner Seams 7700 bbl Dimensions L 120' x W 55' Volume Closed-loop System: Subsection H of 19 15 17 11 NMAC Type of Operation P&A Drilling a new well Workover or Drilling (Applies to activities which require prior approval of a permit or notice of intent) Above Ground Steel Tanks Haul-off Bins Other Lined Unlined LLDPE HDPE PVD Other Thickness mıl Liner Seams Welded Factory Other Below-grade tank: Subsection I of 19 15 17 11 NMAC Type of fluid Volume bbl Tank Construction material Secondary containment with leak detection Visible sidewalls, liner, 6-inch lift and automatic overflow shu Visible sidewalls and liner Visible sidewalls only Other □ HDPE **PVC** Other Thickness mıl Liner Type Alternative Method: Submittal of an exception request is required Exceptions must be submitted to the Santa Fe Environmental Bureau office for consideration of approval.

Form C-144

Oil Conservation Division

Page 1 of 5

| Fencing: Subsection D of 19 15 17 11 NMAC (Applies to permanent pit, temporary pits, and below-grade tanks) Chain link, six feet in height, two strands of barbed wire at top (Required if located within 1000 feet of a permanent residence, school, hospital, institution or church) Four foot height, four strands of barbed wire evenly spaced between one and four feet | | | | |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------|-------|--|--|
| Alternate Please specify | | | | |
| Netting: Subsection E of 19 15 17 11 NMAC (Applies to permanent pits and permanent open top tanks) Screen Netting Other Monthly inspections (If netting or screening is not physically feasible) | | | | |
| 8 Signs: Subsection C of 19 15 17 11 NMAC 12" X 24", 2" lettering, providing Operator's name, site location, and emergency telephone numbers X Signed in compliance with 19 15 3 103 NMAC | | | | |
| Administrative Approvals and Exceptions: Justifications and/or demonstrations of equivalency are required Please refer to 19 15 17 NMAC for guidance Please check a box if one or more of the following is requested, if not leave blank: Administrative approval(s) Requests must be submitted to the appropriate division district of the Santa Fe Environmental Bureau office for consideration of approval Exception(s) Requests must be submitted to the Santa Fe Environmental Bureau office for consideration of approval | leration of appi | roval | | |
| 10 | | | | |
| Siting Criteria (regarding permitting) 19.15.17.10 NMAC Instructions: The applicant must demonstrate compliance for each sting criteria below in the application. Recommendations of acceptable source material are provided below. Requests regarding changes to certain siting criteria may require administrative approval from the appropriate district office or may be considered an exception which must be submitted to the Santa Fe Environmental Bureau Office for consideration of approval. Applicant must attach justification for request. Please refer to 19.15.17.10 NMAC for guidance. Siting criteria does not apply to drying pads or above grade-tanks associated with a closed-loop system. | | | | |
| Ground water is less than 50 feet below the bottom of the temporary pit, permanent pit, or below-grade tank. - NM Office of the State Engineer - IWATERS database search, USGS, Data obtained from nearby wells | Yes | □No | | |
| Within 300 feet of a continuously flowing watercourse, or 200 feet of any other watercourse, lakebed, sinkhole, or playa lake (measured from the ordinary high-water mark). - Topographic map; Visual inspection (certification) of the proposed site | Yes | □No | | |
| Within 300 feet from a permanent residence, school, hospital, institution, or church in existence at the time of initial application. | Yes | □No | | |
| (Applies to temporary, emergency, or cavitation pits and below-grade tanks) - Visual inspection (certification) of the proposed site; Aerial photo, Satellite image | NA | | | |
| Within 1000 feet from a permanent residence, school, hospital, institution, or church in existence at the time of initial application. | Yes | □No | | |
| (Applied to permanent pits) - Visual inspection (certification) of the proposed site, Aerial photo, Satellite image | ∐NA | | | |
| Within 500 horizonal feet of a private, domestic fresh water well or spring that less than five households use for domestic or stock watering purposes, or within 1000 horizontal feet of any other fresh water well or spring, in existence at the time of initial application. | Yes | □No | | |
| - NM Office of the State Engineer - tWATERS database search, Visual inspection (certification) of the proposed site. | İ | | | |
| Within incorporated municipal boundaries or within a defined municipal fresh water well field covered under a municipal ordinance adopted pursuant to NMSA 1978, Section 3-27-3, as amended - Written confirmation or verification from the municipality, Written approval obtained from the municipality | Yes | □No | | |
| Within 500 feet of a wetland. - US Fish and Wildlife Wetland Identification map; Topographic map, Visual inspection (certification) of the proposed site | Yes | □No | | |
| Within the area overlying a subsurface mine. - Written confirmation or verification or map from the NM EMNRD - Mining and Mineral Division | Yes | □No | | |
| Within an unstable area. - Engineering measures incorporated into the design; NM Bureau of Geology & Mineral Resources; USGS; NM Geological | Yes | No | | |
| Society; Topographic map Within a 100-year floodplain - FEMA map | Yes | □No | | |

Form C-144 Oil Conservation Division Page 2 of 5

| Hydrogoologe Report (Below egade Tanks)- based upon the requirements of Panagraph (4) of Subrection B of 1915 17.9 NMAC Hydrogoologe Data (Temporary and Emergency Pus)- based upon the expurements of 1915 17.10 NMAC Dosgar Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of Subsection C of 1915 17.9 NMAC International Exact the following stams are be attached to the application of Plans understance the state of the following stams are be attached to the application of Plans understance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of Subsection C of 1915 17.9 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of Subsection C of 1915 17.9 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of Subsection C of 1915 17.9 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.10 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.11 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.11 NMAC Operating and Mannetance Plan - based upon the appropriate requirements of 1915 17.11 NMAC Operating and Mannetance Plan - based upon | Temporary Pits, Emergency Pits and Below-grade Tanks Permit Application Attachment Checklist Subsection B of 19 15 17 9 NMAC | | | |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------|--|--|--|
| Hydrogeologe Data (Temporary and Emergency Pis) - based upon the requirements of Pangraph (2) of Subsection B of 19 15 17 9 Sitting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19 15 17 11 NMAC Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 10 NMAC and 19 15 17 13 NMAC Instructions Euclidean Distriction Activation (Control of Previously Approved Design (auton close) of the depth of the following tensis must be attacked to the application Planta (activate the design of Planta (activate the Control of Planta (activate the Activate the A | Instructions Each of the following items must be attached to the application Please indicate, by a check mark in the box, that the documents are attached | | | |
| String Criteria Compilate Demonstrations - based upon the appropriate requirements of 19 15 17 10 NMAC | | | | |
| Design Plan - hased upon the appropriate requirements of 19 15.17.12 NMAC | | | | |
| Closure Telan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of 1915 179 NMAC and 1915 1713 NMAC Previously Approved Design (attach capy of design) | | | | |
| Closure Plan (Please complete Baxes 14 through, 18, if applicable) - based upon the appropriate requirements of Subsection C of 1915 17 9 NMAC and 1915 173 NMAC | | | | |
| 19 51 79 NMAC and 19 51 71 3 NMAC | Operating and Maintenance Plan - based upon the appropriate requirements of 19 15.17 12 NMAC | | | |
| Closed-loop Systems Permit Application Attachment Checklist: Solocoton B of 19 15 17.9 NMAC | | | | |
| Closed-loop Systems Permit Application Attachment Checklist:Subsection B of 19 15 179 NNAC Closed-loop Systems December 20 the application Pilos without the program of the pollurous miss must be attached to the application Pilos without the program of the program of the pollurous missed upon the appropriate requirements of 19 15 17 10 NMAC Design Pilos - based upon the appropriate requirements of 19 15.17.10 NMAC Design Pilos - based upon the appropriate requirements of 19 15.17.10 NMAC Design Pilos - based upon the appropriate requirements of 19 15.17.10 NMAC Design Pilos - based upon the appropriate power of the provisional power of the properties requirements of 19 15 17 11 NMAC Design based upon the appropriate requirements of 19 15 17 11 NMAC Design based upon the appropriate requirements of 19 15 17 11 NMAC Design based upon the appropriate requirements of 19 15 17 11 NMAC Design based upon the appropriate requirements of 19 15 17 11 NMAC Design based upon the appropriate requirements of 19 15 17 11 NMAC Design based upon the appropriate requirements | Previously Approved Design (attach copy of design) API or Permit | | | |
| Instructions: Each of the following term must be attached to the application Please indicate, by a check mark in the bas, that the documents are attached | | | | |
| Situng Criteria Compilance Demonstrations (only for on-site closure) - based upon the appropriate requirements of 19 15.17.10 NMAC Design Plan - based upon the appropriate requirements of 19 15.17.12 NMAC Operating and Maintenance Plan - based upon the appropriate requirements of 19 15.17.13 NMAC Closure Plan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of 19 15.17.9 NMAC and 19 15.17.13 NMAC Trevolusly Approved Design dataths copy of design) API Previously Approved Design dataths copy of design) API Previously Approved Operating and Maintenance Plan Previously Approved Operating and United Plan Previously Approved Operating and United Plan Previously Approved Operating Api Previously Approved Operating | Instructions Each of the following items must be attached to the application Please indicate, by a check mark in the box, that the documents are attached | | | |
| Design Plan - based upon the appropriate requirements of 19 15 17 11 NMAC | | | | |
| Closure Plan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of 19 15 17 9 NNAC and 19 15 17 13 NMAC | | | | |
| Closure Plan (Please complete Boxes 14 through 18, if applicable) - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC | | | | |
| NMAC and 19 15 17 13 NMAC Previously Approved Design (attach copy of design) API | | | | |
| Previously Approved Operating and Maintenance Plan API | NMAC and 19 15 17 13 NMAC | | | |
| Permanent Pits Permit Application Checklist: Subsection B of 19 15 17 9 NMAC Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached. Hydrogeologic Report - based upon the requirements of Paragraph (1) of Subsection B of 19 15 17 10 NMAC Climatological Factors Assessment String Criteria Compliance Demonstrations - based upon the appropriate requirements of 19 15 17 11 NMAC Cimitatological Factors Assessment Caestricide Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC Dike Protection and Structural Integrity Design based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Precboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Responses Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emergency Responses Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emergency Carlotine Plan - based upon the appropriate requirements of Subsection C of 19 15 17 13 NMAC Instructions: Please complete the applicable bases, Bases 14 through 18, in regards to the proposed closure plan. Type Online Workover Emergency Carvatation P&A Permanent Pit Below-grade Tank Closed-loop System In-place Burial On-site Closure Method (Only for temporary pits and closed-loop systems) On-site Closure Removal (Closed-loop systems only) On-site Closure Method (Only for temporary pits and closed-loop systems) On-site Closure Method (Only for temporary | Previously Approved Design (attach copy of design) API | | | |
| Permanent Pits Permit Application Checklist: Subsection B of 19 15 17 9 NMAC Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached. Hydrogeologic Report - based upon the requirements of Paragraph (1) of Subsection B of 19 15 17 10 NMAC Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19 15 17 10 NMAC Climatological Factors Assessment Centrified Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emosponse October 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type Dirilling Workover Emergency Cavitation P&A Permanent Pit Below-grade Tank Closed-loop System Alternative Proposed Closure Method Waste Excavation and Removal On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) Passed Indicate, by a check mark in the box, that the documents are attached. Proposed Closure Method (Engelia Conference and Engineering Plan (if applicable) - based upon the appropriate requirements of Subsect | Previously Approved Operating and Maintenance Plan API | | | |
| Permanent Pits Permit Application Checklist: Subsection B of 19 15 17 9 NMAC Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached. Hydrogeologic Report - based upon the requirements of Paragraph (1) of Subsection B of 19 15 17 10 NMAC Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19 15 17 10 NMAC Climatological Factors Assessment Centrified Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emosponse October 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type Dirilling Workover Emergency Cavitation P&A Permanent Pit Below-grade Tank Closed-loop System Alternative Proposed Closure Method Waste Excavation and Removal On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) Passed Indicate, by a check mark in the box, that the documents are attached. Proposed Closure Method (Engelia Conference and Engineering Plan (if applicable) - based upon the appropriate requirements of Subsect | | | | |
| Hydrogeologic Report - based upon the requirements of Paragraph (1) of Subsection B of 19 15 17 9 NMAC Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19 15 17 10 NMAC Clambdogical Factor Assessment Certified Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC Dike Protection and Structural Integrity Design based upon the appropriate requirements of 19 15 17 11 NMAC Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Emospection Plan Em | | | | |
| Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19 15 17 10 NMAC Climatological Factors Assessment Certified Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC Dike Protection and Structural Integrity Design based upon the appropriate requirements of 19 15 17 11 NMAC Lanc Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Lanc Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overlopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Montitoring and Inspection Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type Drilling Workover Emergency Cavitation P&A Permanent Pit Below-grade Tank Closed-loop System Alternative Proposed Closure Method Waste Excavation and Removal Maste Excavation and Removal Closure Method (Closed-loop systems only) On-site Closure Method (only for temporary pits and closed-loop systems) In-place Burial On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) Is Waste Excavation and Removal Closure Plan Checklist(19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Protocols and Procedures - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (fo | Instructions: Each of the following items must be attached to the application. Please indicate, by a check mark in the box, that the documents are attached. | | | |
| Climatological Factors Assessment Certified Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC Dike Protection and Structural Integrity Design based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Limer Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Engrency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type Drilling Workover Emergency Cavitation P&A Permanent Pit Below-grade Tank Closed-loop System Alternative Proposed Closure Method Waste Excavation and Removal Waste Removal (Closed-loop systems only) On-site Closure Method (folly for temporary pits and closed-loop systems) In-place Burial On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) 15 Waste Excavation and Removal Closure Plan Checklist(19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please Indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-veg | Hydrogeologic Report - based upon the requirements of Paragraph (I) of Subsection B of 19 15 17 9 NMAC | | | |
| Climatological Factors Assessment Certified Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC Dike Protection and Structural Integrity Design based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Limer Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Engrency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type Drilling Workover Emergency Cavitation P&A Permanent Pit Below-grade Tank Closed-loop System Alternative Proposed Closure Method Waste Excavation and Removal Waste Removal (Closed-loop systems only) On-site Closure Method (folly for temporary pits and closed-loop systems) In-place Burial On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) 15 Waste Excavation and Removal Closure Plan Checklist(19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please Indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-veg | Siting Criteria Compliance Demonstrations - based upon the appropriate requirements of 19 15 17 10 NMAC | | | |
| Dike Protection and Structural Integrity Design based upon the appropriate requirements of 19 15 17 11 NMAC Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assessment - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type | | | | |
| Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Erosion Control Plan Erosion Control Plan Erosion Control Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Oil Field Waste Stream Characterization Oil Field Waste Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Oil Field Closure: 20 15 17 13 NMAC Oil Field Closu | Certified Engineering Design Plans - based upon the appropriate requirements of 19 15 17 11 NMAC | | | |
| Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. | Dike Protection and Structural Integrity Design based upon the appropriate requirements of 19 15 17 11 NMAC | | | |
| Quality Control/Quality Assurance Construction and Installation Plan Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Errosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC | Leak Detection Design - based upon the appropriate requirements of 19 15 17 11 NMAC | | | |
| Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type | Liner Specifications and Compatibility Assessment - based upon the appropriate requirements of 19 15 17 11 NMAC | | | |
| Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type | Quality Control/Quality Assurance Construction and Installation Plan | | | |
| Nuisance or Hazardous Odors, including H2S, Prevention Plan Emergency Response Plan Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC | Operating and Maintenance Plan - based upon the appropriate requirements of 19 15 17 12 NMAC | | | |
| Emergency Response Plan | Freeboard and Overtopping Prevention Plan - based upon the appropriate requirements of 19 15 17 11 NMAC | | | |
| Oil Field Waste Stream Characterization Monitoring and Inspection Plan Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC | Nuisance or Hazardous Odors, including H2S, Prevention Plan | | | |
| Monitoring and Inspection Plan Erosion Control Plan Erosion E | Emergency Response Plan | | | |
| Erosion Control Plan Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC | Oil Field Waste Stream Characterization | | | |
| Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type | Monitoring and Inspection Plan | | | |
| 14 Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type | Erosion Control Plan | | | |
| Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type | Closure Plan - based upon the appropriate requirements of Subsection C of 19 15 17 9 NMAC and 19 15 17 13 NMAC | | | |
| Proposed Closure: 19 15 17 13 NMAC Instructions: Please complete the applicable boxes, Boxes 14 through 18, in regards to the proposed closure plan. Type | 14 | | | |
| Type Drilling Workover Emergency Cavitation P&A Permanent Pit Below-grade Tank Closed-loop System Alternative | Proposed Closure: 19 15 17 13 NMAC | | | |
| Alternative | | | | |
| Proposed Closure Method Waste Excavation and Removal Waste Removal (Closed-loop systems only) Waste Removal (Closed-loop systems only) On-site Closure Method (only for temporary pits and closed-loop systems) In-place Burial On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) 15 Waste Excavation and Removal Closure Plan Checklist (19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Waste Removal (Closed-loop systems only) On-site Closure Method (only for temporary pits and closed-loop systems) In-place Burial | | | | |
| In-place Burial On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) 15 Waste Excavation and Removal Closure Plan Checklist(19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | Waste Removal (Closed-loop systems only) | | | |
| In-place Burial On-site Trench Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) 15 Waste Excavation and Removal Closure Plan Checklist(19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | On-site Closure Method (only for temporary pits and closed-loop systems) | | | |
| Alternative Closure Method (Exceptions must be submitted to the Santa Fe Environmental Bureau for consideration) Maste Excavation and Removal Closure Plan Checklist (19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Waste Excavation and Removal Closure Plan Checklist (19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Waste Excavation and Removal Closure Plan Checklist (19 15 17 13 NMAC) Instructions: Each of the following items must be attached to the closure plan. Please indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Please indicate, by a check mark in the box, that the documents are attached. Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Protocols and Procedures - based upon the appropriate requirements of 19 15 17.13 NMAC Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings) Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Soil Backfill and Cover Design Specifications - based upon the appropriate requirements of Subsection H of 19 15 17 13 NMAC Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | | |
| | Re-vegetation Plan - based upon the appropriate requirements of Subsection I of 19 15 17 13 NMAC | | | |
| Site Reciamation Plan - based upon the appropriate requirements of Subsection G of 19 13 17 13 NMAC | Site Reclamation Plan - based upon the appropriate requirements of Subsection G of 19 15 17 13 NMAC | | | |

Form C-144 Oil Conservation Division Page 3 of 5

| 16 Weste Demoved Cleans For Cleand Ion Systems That Hillian Abo | ove Ground Steel Tanks or Haul-off Bins Only:(19 15 17 13 D NMAC) | | |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------|--|
| Instructions Please identify the facility or facilities for the disposal of | fliquids, drilling fluids and drill cuttings. Use attachment if more than two | | |
| facilities are required | D 15 1 D 11 | | |
| Disposal Facility Name | | | |
| Disposal Facility Name | Disposal Facility Permit # | | |
| Yes (If yes, please provide the information N | | e service and | |
| Required for impacted areas which will not be used for future service. | - | SIN A C | |
| Re-vegetation Plan - based upon the appropriate requirem | on the appropriate requirements of Subsection H of 19 15 17 13 Nept. of Subsection Lof 19 15 17 13 NMAC | NMAC | |
| Site Reclamation Plan - based upon the appropriate requi | | | |
| | | | |
| | e closure plan Recommendations of acceptable source material are provided belov te district office or may be considered an exception which must be submitted to the . | | |
| Ground water is less than 50 feet below the bottom of the burie | ed waste | Yes No | |
| - NM Office of the State Engineer - IWATERS database search, | USGS Data obtained from nearby wells | ∐N/A | |
| Ground water is between 50 and 100 feet below the bottom of | the buried waste | Yes No | |
| - NM Office of the State Engineer - tWATERS database search, U | JSGS, Data obtained from nearby wells | N/A | |
| Ground water is more than 100 feet below the bottom of the bi | uried waste | Yes No | |
| - NM Office of the State Engineer - (WATERS database search, U | | | |
| Within 200 feet of a continuously flavour victoriours, or 200 feet of | ony other constituent waterscopes or letraked evaluate as along late. | | |
| Within 300 feet of a continuously flowing watercourse, or 200 feet of (measured from the ordinary high-water mark) | • | YesNo | |
| - Topographic map, Visual inspection (certification) of the propos | | | |
| Within 300 feet from a permanent residence, school, hospital, institution - Visual inspection (certification) of the proposed site, Aerial phot | •• | ∐Yes ∐No | |
| - visual hispection (certification) of the proposed site, Aerial phot | o, satemic mage | Yes No | |
| Within 500 horizontal feet of a private, domestic fresh water well or sp purposes, or within 1000 horizontal fee of any other fresh water well of NM Office of the State Engineer - iWATERS database, Visual in | or spring, in existence at the time of the initial application | | |
| Within incorporated municipal boundaries or within a defined municipal pursuant to NMSA 1978. Section 3-27-3, as amended | | Yes No | |
| - Written confirmation or verification from the municipality, Writ | ten approval obtained from the municipality | | |
| Within 500 feet of a wetland - US Fish and Wildlife Wetland Identification map, Topographic | man. Visual inspection (certification) of the proposed site | Yes No | |
| Within the area overlying a subsurface mine | | □Yes □No | |
| - Written confiramtion or verification or map from the NM EMNR | tD-Mining and Mineral Division | | |
| Within an unstable area | | Yes No | |
| | of Geology & Mineral Resources, USGS, NM Geological Society, | | |
| Topographic map Within a 100-year floodplain | | Yes No | |
| - FEMA map | | | |
| On-Site Closure Plan Checklist: (19 15 17 13 NMAC) Instr. by a check mark in the box, that the documents are attached. | uctions: Each of the following items must bee attached to the cl | osure plan. Please indicate, | |
| Siting Criteria Compliance Demonstrations - based upo | | | |
| Proof of Surface Owner Notice - based upon the appropriate requirements of Subsection F of 19.15 17 13 NMAC | | | |
| Construction/Design Plan of Burial Trench (if applicable) based upon the appropriate requirements of 19 15 17 11 NMAC | | | |
| Construction/Design Plan of Temporary Pit (for in place burial of a drying pad) - based upon the appropriate requirements of 19 15 17 11 NMAC | | | |
| Protocols and Procedures - based upon the appropriate requirements of 19.15.17 13 NMAC | | | |
| Confirmation Sampling Plan (if applicable) - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC | | | |
| Waste Material Sampling Plan - based upon the appropriate requirements of Subsection F of 19 15 17 13 NMAC | | | |
| Disposal Facility Name and Permit Number (for liquids, drilling fluids and drill cuttings or in case on-site closure standards cannot be achieved) | | | |
| Soil Cover Design - based upon the appropriate requirements of Subsection H of 19.15 17 13 NMAC | | | |
| Re-vegetation Plan - based upon the appropriate require | | | |
| Site Reclamation Plan - based upon the appropriate requirements of Subsection G of 19.15.17.13 NMAC | | | |

| Operator Application Certification: I hereby certify that the information submitted with this application is true, accurate and complete to the best of my knowledge and belief |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Name (Print) Title |
| Signature Date |
| e-mail address Telephone |
| |
| OCD Approval: Permit Application (including closure plan) Closure Plan (only) OCD Conditions (see attachment) OCD Representative Signature: Approval Date: OCD Permit Number: |
| The state of the s |
| Closure Report (required within 60 days of closure completion): Instructions Operators are required to obtain an approved closure plan prior to implementing any closure activities and submitting the closure report. The closure report is required to be submitted to the division within 60 days of the completion of the closure activities. Please do not complete this section of the form until an approved closure plan has been obtained and the closure activities have been completed. X Closure Completion Date: July 29, 2011 |
| 22 |
| Closure Method: Waste Excavation and Removal X On-site Closure Method Alternative Closure Method Waste Removal (Closed-loop systems only) If different from approved plan, please explain |
| 23 |
| Closure Report Regarding Waste Removal Closure For Closed-loop Systems That Utilize Above Ground Steel Tanks or Haul-off Bins Only: Instructions: Please identify the facility or facilities for where the liquids, drilling fluids and drill cuttings were disposed. Use attachment if more than two facilities |
| were utilized. |
| Disposal Facility Name Disposal Facility Permit Number |
| Disposal Facility Name Disposal Facility Permit Number |
| Were the closed-loop system operations and associated activities performed on or in areas that will not be used for future service and operations? Yes (If yes, please demonstrate compliane to the items below) No |
| Required for impacted areas which will not be used for future service and operations |
| Site Reclamation (Photo Documentation) |
| Soil Backfilling and Cover Installation |
| Re-vegetation Application Rates and Seeding Technique |
| 24 |
| Closure Report Attachment Checklist: Instructions: Each of the following items must be attached to the closure report. Please indicate, by a check mark in |
| the box, that the documents are attached. |
| X Proof of Closure Notice (surface owner and division) X Proof of Deed Notice (required for on-site closure) |
| X Plot Plan (for on-site closures and temporary pits) |
| X Confirmation Sampling Analytical Results (if applicable) |
| Waste Material Sampling Analytical Results (if applicable) |
| X Disposal Facility Name and Permit Number |
| X Soil Backfilling and Cover Installation |
| X Re-vegetation Application Rates and Seeding Technique |
| X Site Reclamation (Photo Documentation) |
| On-site Closure Location Latitude 36.42699 °N Longitude 107.42583 °W NAD 1927 X 1983 |
| |
| Oneseton Clauma Contification |
| Operator Closure Certification: I hereby certify that the information and attachments submitted with this closure report is ture, accurate and complete to the best of my knowledge and belief. I also certify that |
| the closure complies with all applicable closure requirements and conditions specified in the approved closure plan |
| Name (Print) Jamie Goodwin, Title Regulatory Tech |
| Signature (MCGIVI) Date 91311 |
| e-mail address |

Burlington Resources Oil Gas Company, LP San Juan Basin Closure Report

Lease Name: CANYON LARGO UNIT 239N

API No.: 30-039-30883

In accordance with Rule 19.15.17.13 NMAC the following information describes the closure of the temporary pit referenced above. All proper documentation regarding closure activities is being included with the C-144. The temporary pit for this location was constructed and location drilled before June 16, 2008 (effective date for Rule 19.15.17). While closure of the temporary pit did fall within the rule some dates for submittals are after the rig release date.

- Details on Capping and Covering, where applicable (See report)
- Plot Plan (Pit Diagram) (Included as an attachment)
- Inspection Reports (Included as an attachment)
- Sampling Results (Included as an attachment)
- C-105 (Included as an attachment)
- Copy of Deed Notice will be filed with County Clerk (Not required on Federal, State, or Tribal land as stated by FAQ dated October 30, 2008)

General Plan:

 All free standing liquids will be removed at the start of the pit closure process from the pit and disposed of in a division—approved facility or recycle, reuse or reclaim the liquids in a manner that the appropriate division district office approves.

All recovered liquids were disposed of at Basin Disposal (Permit #NM-01-005) and any sludge or soil required to be removed to facilitate closure was hauled to Envirotech Land Farm (Permit #NM-01-011) and JFJ Landfarm % IEI (Permit #NM-01-0010B).

2. The preferred method of closure for all temporary pits will be on-site burial, assuming that all the criteria listed in sub-section (B) of 19.15.17 13 are met.

The pit was closed using onsite burial.

3. The surface owner shall be notified of BR's closing of the temporary pit as per the approved closure plan using certified mail, return receipt requested.

The closure process notification to the landowner was sent via email. (See Attached)(Well located on Federal Land, certified mail is not required for Federal Land per BLM/OCD MOU.)

4. Within 6 months of the Rig Off status occurring BR will ensure that temporary pits are closed, re-contoured, and reseeded.

Provision 4 of the closure plan requirements were not met due to rig move off date as noted on C-105 which was prior to pit rule change. Burlington will ensure compliance with this rule in the future.

- 5. Notice of Closure will be given to the Aztec Division office between 72 hours and one week of closure via email, or verbally. The notification of closure will include the following:
 - i. Operator's name
 - ii. Location by Unit Letter, Section, Township, and Range. Well name and API number.

Notification is attached.

6. Liner of temporary pit shall be removed above "mud level" after stabilization. Removal of liner will consist of manually or mechanically cutting liner at mud level and removing all remaining liner. Care will be taken to remove "All" of the liner i.e., edges of liner entrenched or buried. All excessive liner will be disposed of at a licensed disposal facility.

Liner of temporary pit was removed above "mud level" after stabilization. Removal of the liner consisted of manually cutting liner at mud level and removing all remaining liner. Care was taken to remove "ALL" of the liner i.e., edges of liner entrenched or buried. All excessive liner was disposed of at a licensed disposal facility, (San Juan County Landfill).

7. Pit contents shall be mixed with non-waste containing, earthen material in order to achieve the solidification process. The solidification process will be accomplished using a combination of natural drying and mechanically mixing. Pit contents will be mixed with non-waste, earthen material to a consistency that is deemed a safe and stable. The mixing ratio shall not exceed 3 parts clean soil to 1 part pit contents.

Burlington mixed the Pit contents with non-waste containing, earthen material in order to achieve the solidification process. The solidification process was accomplished by using a combination of natural drying and mechanically mixing. Pit contents were mixed with non-waste, earthen material to a consistency that is deemed as safe and stable. The mixing ratio consisted of approximately 3 parts clean soil to 1 part pit contents.

8. A five point composite sample will be taken of the pit using sampling tools and all samples tested per Subsection B of 19.15.17.13(B)(1)(b). In the event that the criteria are not met, all contents will be handled per Subparagraph (a) of Paragraph (1) of Subsection B of 19.15.17.13 i.e., Dig and haul.

A five point composite sample was taken of the pit using sampling tools and all samples tested per Subsection B of 19.15.17.1 3(B)(1)(b). (Sample results attached).

| Components | Tests Method | Limit (mg/Kg) | Results |
|------------|---------------------------|---------------|------------|
| Benzene | EPA SW-846 8021B or 8260B | 0.2 | ND ug/kg |
| BTEX | EPA SW-846 8021B or 8260B | 50 | 60.0 ug/kG |
| TPH | EPA SW-846 418.1 | 2500 | 261mg/kg |
| GRO/DRO | EPA SW-846 8015M | 500 | 39.4 mg/Kg |
| Chlorides | EPA 300.1 | 1000/500 | 100 mg/L |

9. Upon completion of solidification and testing standards being passed, the pit area will be backfilled with compacted, non-waste containing, earthen material. A minimum of four feet of cover shall be achieved and the cover shall include one foot of suitable material to establish vegetation at the site, or the background thickness of topsoil, whichever is greater. If standard testing fails BR will dig and haul all contents pursuant to 19.15.17.13.i.a. After doing such, confirmation sampling will be conducted to ensure a release has not occurred.

The pit material passed solidification and testing standards. The pit area was then backfilled with compacted, non-waste containing, earthen material. More than four feet of cover was achieved and the cover included one foot of suitable material to establish vegetation at the site.

10. During the stabilization process if the liner is ripped by equipment the Aztec OCD office will be notified within 48 hours and the liner will be repaired if possible. If the liner can not be repaired then all contents will be excavated and removed.

The integrity of the liner was not damaged in the pit closure process.

11. Dig and Haul Material will be transported to the Envirotech Land Farm located 16 miles south of Bloomfield on Angel Peak Road, CR 7175. Permit # NM010011

Dig and Haul was not required.

12. Re-contouring of location will match fit, shape, line, form and texture of the surrounding. Re-shaping will include drainage control, prevent ponding, and prevent erosion. Natural drainages will be unimpeded and water bars and/or silt traps will be place in areas where needed to prevent erosion on a large scale. Final recontour shall have a uniform appearance with smooth surface, fitting the natural landscape.

The pit area was re-contoured to match fit, shape, line, form and texture of the surrounding area. Reshaping included drainage control, to prevent ponding and erosion. Natural drainages were unimpeded and water bars and/or silt traps were placed in areas where needed to prevent erosion on a large scale. Final recontour has a uniform appearance with smooth surface, fitting the natural landscape.

13. Notification will be sent to OCD when the reclaimed area is seeded.

Provision 13 was accomplished through complying with BLM seeding requirements as allowed by the BLM/OCD MOU.

14. BR shall seed the disturbed areas the first growing season after the operator closes the pit. Seeding will be accomplished via drilling on the contour whenever practical or by other division-approved methods. BLM or Forest Service stipulated seed mixes will used on federal lands. Vegetative cover will equal 70% of the native perennial vegetative cover (un-impacted) consisting of at least three native plant species, including at least one grass, but not including noxious weeds, and maintain that cover through two successive growing seasons. Repeat seeding or planting will be continued until successful vegetative growth occurs.

Provision 14 was accomplished through complying with BLM seeding requirements as allowed by the BLM/OCD MOU.

15. The temporary pit will be located with a steel marker, no less than four inches in diameter, cemented in a hole three feet deep in the center of the onsite burial upon the abandonment of all the wells on the pad. The marker will be flush with the ground to allow access of the active well pad and for safety concerns. The marker will include a threaded collar to be used for future abandonment. The top of the marker will contain a welded steel 12" square plate that indicates the onsite burial of the temporary pit. The plate will be easily removable and a four foot tall riser will be threaded into the top of the collar marker and welded around the base with the operator's information at the time of all wells on the pad are abandoned. The operator's information will include the following: Operator Name, Lease Name, Well Name and number, Unit Number, Section, Township, Range and an indicator that the marker is an onsite burial location.

Provision 15 was accomplished by installing a steel marker in the temporary pit, no less than four inches in diameter, cemented in a hole three feet deep in the center of the onsite burial. The marker is flush with the ground to allow access of the active well pad and for safety concerns. The top of the marker contains a welded steel 12" square plate that indicates the onsite burial of the temporary pit. The plate contains the following: Operator Name, Lease Name, Well Name and number, Unit Number, Section, Township, Range and an indicator that the marker is an onsite burial location.

The plate will be easily removable and a four foot tall riser will be threaded into the top of the collar marker and welded around the base with the following operator's information at the time of all wells on the pad are abandoned. The riser will be labeled: BR, BLM, CANYON LARGO UNIT 239N, UL-L, Sec. 1, T 25N, R 6W, API # 30-039-30883

Jaramillo, Marie E

From:

Jaramillo, Marie E

Sent:

Wednesday, December 09, 2009 10:26 AM

To:

Subject:

'mark_kelly@nm.blm.gov' SURFACE OWNER NOTIFICATION 12/09/09

Importance:

High

The subject well will have a temporary pit that will be closed on site. Please let me know if you have any questions. Thanks

FLORANCE 41M FLORANCE 41N SAN JUAN 28-6 UNIT 466S REESE MESA 101 LATERAL CANYON LARGO UNIT 239N **DELHI TURNER 1B**

Marie Jaramillo Staff Regulatory Tech. ConocoPhillips Office # (505) 326-9865 Fax # (505) 599-4062 mailto:marie e jaramillo@conocophillips com DISTRICT I 1625 N. French Dr., Hobbs, N.M. 88240

State of New Mexico Energy, Minerals & Natural Resources Department

Form C-102 Revised October 12, 2005

DISTRICT II 1301 W. Grand Avenue, Artesia, N.M. 88210

DISTRICT III 1000 Rio Brazos Rd., Aztec, N.M. 87410

1220 S. St. Francis Dr., Santa Fe, NM 87505

DISTRICT IV

OIL CONSERVATION DIVISION 1220 South St. Francis Dr. Santa Fe, NM 87505 Submit to Appropriate District Office State Lease - 4 Copies Fee Lease - 3 Copies

☐ AMENDED REPORT


WELL LOCATION AND ACREAGE DEDICATION PLAT

| ¹ API Number | Pool Code Pool Name CHACRA/BASIN DAKOTA/BLANCO ME | | |
|-------------------------|---------------------------------------------------|--------------|-------------|
| Property Code | Property Name | | Well Number |
| | CANYO | N LARGO UNIT | 239 N |
| OGRID No. | Operator Name | | * Elevation |
| | BURLINGTON RESOURCES OIL & GAS COMPANY LP | | 6749' |

10 Surface Location

| UL or lot no. | Section 1 | Township 25N | Range 6W | Lot Idn | Feet from the 1930' | North/South Line SOUTH | Feet from the 670' | East/West line WEST | County RIO ARRIBA |
|-----------------------------------------------|--------------|--------------------|-------------|---------|-------------------------------|---------------------------|-------------------------|------------------------|----------------------|
| | | | 11 Bott | om Hole | Location I | f Different Fr | om Surface | | |
| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
| Dedicated Acres 160.0 Acres 320.6 Acres | - (SW/ | /4) CH 2) MV/DK | 18 Joint or | Infill | ¹⁴ Consolidation C | Code | ¹⁵ Order No. | | |

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED

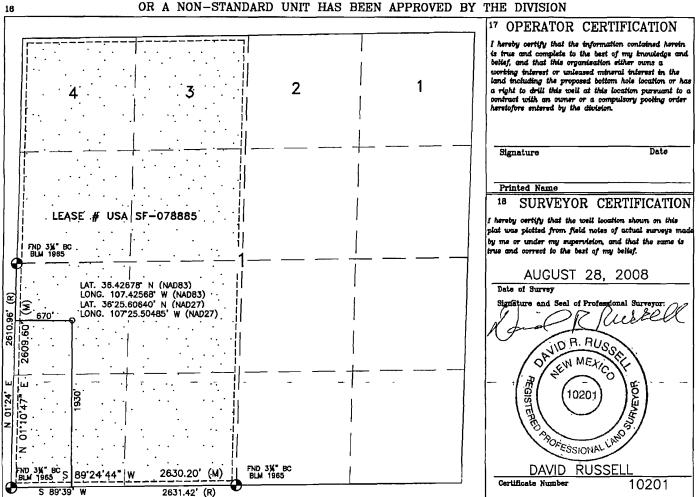

WELL FLAG

LATITUDE 36 42678°N LONGITUDE: 107 42568°W

CENTER OF PIT

LATITUDE. 36 42699° N LONGITUDE[.] 107 42583° W

ELEVATION 6738.7' DATUM: NAD83 & NAVD88

BURLINGTON RESOURCES OIL & GAS COMPANY LP


CANYON LARGO UNIT #239N 1930' FSL & 670' FWL


LOCATED IN THE NW/4 SW/4 OF SECTION 1,

T25N, R6W, N M.P.M.,

RIO ARRIBA COUNTY, NEW MEXICO GROUND ELEVATION: 6749', NAVD 88

FINISHED PAD ELEVATION 6750.7', NAVD 88



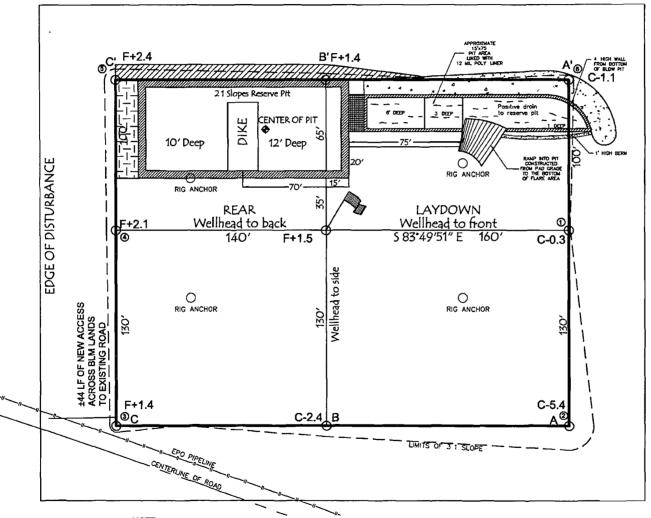

SLOPES TO BE CONSTRUCTED TO MATCH THE ORIGINAL CONTOURS AS CLOSE AS POSSIBLE.

330' x 400' = 3.03 ACRES OF DISTURBANCE

SCALE: 1" = 60' JOB No.: COPC235 DATE: 09/02/08 RESERVE PIT DIKE: TO BE 8' ABOVE DEEP SIDE (OVERFLOW - 3' WIDE AND 1' ABOVE SHALLOW SIDE).
RUSSELL SURVEYING, INC. IS NOT LIABLE FOR UNDERGROUND UTILITIES OR PIPELINES.
CONTRACTOR SHOULD CALL ONE-CALL FOR LOCATION OF ANY MARKED OR UNMARKED, BURIED PIPELINES OR
CABLES ON WELL PAD, IN CONSTRUCTION ZONE AND/OR ACCESS ROAD AT LEAST TWO (2) WORKING DAYS PRIOR
TO CONSTRUCTION.



Russell Surveying 1409 W. Aztec Blvd. #2 Aztec, New Mexico 87410 (505) 334-8637



EPA METHOD 8015 Modified Nonhalogenated Volatile Organics Total Petroleum Hydrocarbons

| Client: | Burlington | Project #: | 92115-1271 |
|----------------------|-------------|---------------------|------------|
| Sample ID: | Reserve Pit | Date Reported: | 07-08-11 |
| Laboratory Number: | 58815 | Sampled: | 07-06-11 |
| Chain of Custody No: | 11990 | Date Received: | 07-06-11 |
| Sample Matrix: | Soil | Date Extracted: | 07-07-11 |
| Preservative: | Cool | Date Analyzed: | 07-07-11 |
| Condition: | Intact | Analysis Requested: | 8015 TPH |

| Parameter | Concentration (mg/Kg) | Det. Limit (mg/Kg) |
|------------------------------|-----------------------|--------------------------|
| Gasoline Range (C5 - C10) | 39.4 | 0.2 |
| Diesel Range (C10 - C28) | ND | 0.1 |
| Total Petroleum Hydrocarbons | 39.4 | |

ND - Parameter not detected at the stated detection limit.

References:

Method 8015B, Nonhalogenated Volatile Organics, Test Methods for Evaluating Solid

Waste, SW-846, USEPA, December 1996.

Comments:

Canyon Largo Unit 239N

Analyst



EPA METHOD 8015 Modified Nonhalogenated Volatile Organics Total Petroleum Hydrocarbons

| Client: | Burlington | Project #: | 92115-1271 |
|----------------------|-------------|---------------------|------------|
| Sample ID: | Back Ground | Date Reported: | 07-08-11 |
| Laboratory Number: | 58816 | Sampled: | 07-06-11 |
| Chain of Custody No: | 11990 | Date Received: | 07-06-11 |
| Sample Matrix: | Soil | Date Extracted: | 07-07-11 |
| Preservative: | Cool | Date Analyzed: | 07-07-11 |
| Condition: | Intact | Analysis Requested: | 8015 TPH |

| Parameter | Concentration (mg/Kg) | Det. Limit (mg/Kg) |
|------------------------------|--------------------------|--------------------------|
| Gasoline Range (C5 - C10) | 17.3 | 0.2 |
| Diesel Range (C10 - C28) | ND | 0.1 |
| Total Petroleum Hydrocarbons | 17.3 | |

ND - Parameter not detected at the stated detection limit.

References:

Method 8015B, Nonhalogenated Volatile Organics, Test Methods for Evaluating Solid

Waste, SW-846, USEPA, December 1996.

Comments:

Canyon Largo Unit 239N

Analyst



EPA Method 8015 Modified Nonhalogenated Volatile Organics Total Petroleum Hydrocarbons

Quality Assurance Report

| Client: | QA/QC | Project #: | N/A |
|--------------------|--------------------|---------------------|----------|
| Sample ID: | 07-07-11 QA/QC | Date Reported: | 07-08-11 |
| Laboratory Number: | 58813 | Date Sampled: | N/A |
| Sample Matrix: | Methylene Chloride | Date Received: | N/A |
| Preservative: | N/A | Date Analyzed: | 07-07-11 |
| Condition: | N/A | Analysis Requested: | TPH |

| | l-Cal Date | I-Cal RF: | C-Cal RF. | Difference | Accept. Range |
|-------------------------|------------|-----------|-----------|------------|---------------|
| Gasoline Range C5 - C10 | 07/07/11 | 9.996E+02 | 1.000E+03 | 0.04% | 0 - 15% |
| Diesel Range C10 - C28 | 07/07/11 | 9.996E+02 | 1.000E+03 | 0.04% | 0 - 15% |

| Blank Conc. (mg/l== mg/Kg) | Concentration | Detection Limit |
|----------------------------|---------------|-----------------|
| Gasoline Range C5 - C10 | 20.0 | 0.2 |
| Diesel Range C10 - C28 | 34.2 | 0.1 |

| Duplicate Conc. (mg/Kg) | Sample | Duplicate 4 | % Difference | Range |
|-------------------------|--------|-------------|--------------|---------|
| Gasoline Range C5 - C10 | ND | ND | 0.00% | 0 - 30% |
| Diesel Range C10 - C28 | ND | ND | 0.00% | 0 - 30% |

| Spike Conc. (mg/Kg) | Sample | Spike Added | Spike Result | % Recovery | Accept. Range |
|-------------------------|--------|-------------|--------------|------------|---------------|
| Gasoline Range C5 - C10 | ND | 250 | 254 | 101% | 75 - 125% |
| Diesel Range C10 - C28 | ND | 250 | 245 | 98.0% | 75 - 125% |

ND - Parameter not detected at the stated detection limit.

References:

Method 8015B, Nonhalogenated Volatile Organics, Test Methods for Evaluating Solid

Waste,

SW-846, USEPA, December 1996.

Comments:

QA/QC for Samples 58813-58816, 58821-58828, 58830-58831

Analyst



EPA METHOD 8021 AROMATIC VOLATILE ORGANICS

| Client: | Burlington | Project #: | 92115-1271 |
|--------------------|-------------|---------------------|------------|
| Sample ID: | Reserve Pit | Date Reported: | 07-08-11 |
| Laboratory Number: | 58815 | Date Sampled: | 07-06-11 |
| Chain of Custody: | 11990 | Date Received: | 07-06-11 |
| Sample Matrix: | Soil | Date Analyzed: | 07-07-11 |
| Preservative: | Cool | Date Extracted: | 07-07-11 |
| Condition: | Intact | Analysis Requested: | BTEX |
| • | | Dilution: | 10 |

| Parameter | Concentration (ug/Kg) | Det. Limit (ug/Kg) | |
|--------------|-----------------------|---------------------------------------|--|
| | • | , , , , , , , , , , , , , , , , , , , | |
| Benzene | ND | 0.9 | |
| Toluene | 12.6 | 1.0 | |
| Ethylbenzene | 5.3 | 1.0 | |
| p,m-Xylene | 30.7 | 1.2 | |
| o-Xylene | 11.4 | 0.9 | |
| Total BTEX | 60.0 | | |

ND - Parameter not detected at the stated detection limit.

| Surrogate Recoveries: | Parameter | Percent Recovery |
|-----------------------|---------------------|------------------|
| | Fluorobenzene | 85.6 % |
| | 1,4-difluorobenzene | 91.6 % |
| | Bromochlorobenzene | 103 % |

References:

Method 5030B, Purge-and-Trap, Test Methods for Evaluating Solid Waste, SW-846, USEPA,

December 1996.

Method 8021B, Aromatic Volatile Organics, Test Methods for Evaluating Solid Waste, SW-846,

USEPA, December 1996.

Comments:

Canyon Largo Unit 239N

Analyst

Review



EPA METHOD 8021 AROMATIC VOLATILE ORGANICS

| Client: | Burlington | Project #: | 92115-1271 |
|--------------------|-------------|---------------------|------------|
| Sample ID: | Back Ground | Date Reported: | 07-08-11 |
| Laboratory Number: | 58816 | Date Sampled: | 07-06-11 |
| Chain of Custody: | 11990 | Date Received: | 07-06-11 |
| Sample Matrix: | Soil | Date Analyzed: | 07-07-11 |
| Preservative: | Cool | Date Extracted: | 07-07-11 |
| Condition: | Intact | Analysis Requested: | BTEX |
| | | Dilution: | 10 |

| | Dilution: | 10 | |
|--------------------|--------------------------|--------------------------|--|
| Parameter | Concentration (ug/Kg) | Det. Limit (ug/Kg) | |
| Panera | ND | 0.0 | |
| Benzene Toluene | ND 4.9 | 0.9 1.0 | |
| Ethylbenzene | ND | 1.0 | |
| p,m-Xylene | 2.2 | 1.2 | |
| o-Xylene | 1.9 | 0.9 | |
| Total BTEX | 9.0 | | |
| | | | |

ND - Parameter not detected at the stated detection limit.

| Surrogate Recoveries: | Parameter | Percent Recovery |
|-----------------------|---------------------|------------------|
| | Fluorobenzene | 87.2 % |
| | 1,4-difluorobenzene | 94.0 % |
| | Bromochlorobenzene | 91.6 % |

References:

Method 5030B, Purge-and-Trap, Test Methods for Evaluating Solid Waste, SW-846, USEPA,

December 1996.

Method 8021B, Aromatic Volatile Organics, Test Methods for Evaluating Solid Waste, SW-846,

USEPA, December 1996.

Comments:

Canyon Largo Unit 239N

Analyst



EPA METHOD 8021 AROMATIC VOLATILE ORGANICS

| Client: | N/A | F | Project#: | | N/A | |
|----------------------------------------------------------------------------------------------------------------|----------------------------|--------------------------------------------|-----------------------------------|------------------|--------------------------------|------|
| Sample ID: | 0707BBLK QA/QC |) C | Date Reported: | | 07-07-11 | |
| Laboratory Number: | 58821 | [| Date Sampled: | | N/A | |
| Sample Matrix: | Soil | ſ | Date Received: | | N/A | |
| Preservative: | N/A | ĺ | Date Analyzed: | | 07-07-11 | |
| Condition: | N/A | , | Analysis: | | BTEX | |
| | | , | Dilution: | | 10 | |
| Calibration and | I-Cal RF | 1 C-Cal RF: | | Blank | Detect: | |
| Calibration and Detection Limits (ug/L) | | | ? - %Diff e 0 ≩ 15% | Blank Conc | Detect: | |
| 。1.100 (1) 11 (1) 11 (1) 11 (1) 11 (1) 12 (1) 12 (1) 13 (1) 13 (1) 13 (1) 13 (1) 13 (1) 13 (1) 13 (1) 13 (1) 1 | | C-Cal RF: | %Diff | の。これでは多いは金融の | Detect. | |
| Detection Limits (ug/L) | | C-Cal RE | ? - %Diff e 0 ≩ 15% | Conc | Detect. | |
| Detection Limits (ug/L) | 3.9998E+006 | Accept. Rang 4.0078E+006 | %Diff e 0 ≩ 15% 0.2% | Conc | Detect. Limit | |
| Detection Limits (ug/L) Benzene Toluene | 3.9998E+006 4.2167E+006 | Accept. Rang 4.0078E+006 4.2251E+006 | %Diff e 0 ≩15% 0.2% 0.2% | Conc ND ND | Detect. Limit 0.1 0.1 | 5.00 |

| Duplicate Conc. (ug/Kg) | Sample Du | plicate 😘 | %Diff. | Accept Range | Detect, Limit |
|-------------------------|-----------|-----------|--------|--------------|---------------|
| Benzene | 3.6 | 2.6 | 27.8% | 0 - 30% | 0.9 |
| Toluene | 36.0 | 35.6 | 1.1% | 0 - 30% | 1.0 |
| Ethylbenzene | 2.5 | 2.4 | 4.0% | 0 - 30% | 1.0 |
| p,m-Xylene | 18.9 | 17.4 | 7.9% | 0 - 30% | 1.2 |
| o-Xylene | 6.4 | 5.5 | 14.1% | 0 - 30% | 0.9 |

| Spike Conc. (ug/Kg) | Sample Amo | unt Spiked Spil | ked Sample % | Recovery | Accept Range |
|---------------------|------------|-----------------|--------------|----------|--------------|
| Benzene | 3.6 | 500 | 473 | 93.8% | 39 - 150 |
| Toluene | 36.0 | 500 | 539 | 101% | 46 - 148 |
| Ethylbenzene | 2.5 | 500 | 501 | 100% | 32 - 160 |
| p,m-Xylene | 18.9 | 1000 | 1,020 | 100% | 46 - 148 |
| o-Xylene | 6.4 | 500 | 508 | 100% | 46 - 148 |

ND - Parameter not detected at the stated detection limit.

Dilution: Spike and spiked sample concentration represent a dilution proportional to sample dilution.

References:

Method 5030B, Purge-and-Trap, Test Methods for Evaluating Solid Waste, SW-846, USEPA,

December 1996.

Method 8021B, Aromatic and Halogenated Volatiles by Gas Chromatography Using Photoionization and/or Electrolytic Conductivity Detectors, SW-846, USEPA December 1996.

Comments:

QA/QC for Samples 58813-58816, 58821-58824

Analyst



EPA METHOD 418.1 TOTAL PETROLEUM HYDROCARBONS

| Client: | Burlington | Project #: | 92115-1271 |
|----------------------|-------------|------------------|------------|
| Sample ID: | Reserve Pit | Date Reported: | 07/07/11 |
| Laboratory Number: | 58815 | Date Sampled: | 07/06/11 |
| Chain of Custody No: | 11990 | Date Received: | 07/06/11 |
| Sample Matrix: | Soil | Date Extracted: | 07/07/11 |
| Preservative: | Cool | Date Analyzed: | 07/07/11 |
| Condition: | Intact | Analysis Needed: | TPH-418.1 |

| | | Det. |
|-----------|---------------|---------|
| | Concentration | Limit |
| Parameter | (mg/kg) | (mg/kg) |

Total Petroleum Hydrocarbons

261

5.0

ND = Parameter not detected at the stated detection limit.

References:

Method 418.1, Petroleum Hydrocarbons, Total Recoverable, Chemical Analysis of Water

and Waste, USEPA Storet No. 4551, 1978.

Comments:

Canyon Largo Unit 239N

Analyst



EPA METHOD 418.1 TOTAL PETROLEUM HYDROCARBONS

| Client: | Burlington | Project #: | 92115-1271 |
|----------------------|-------------|------------------|------------|
| Sample ID: | Back Ground | Date Reported: | 07/07/11 |
| Laboratory Number: | 58816 | Date Sampled: | 07/06/11 |
| Chain of Custody No: | 11990 | Date Received: | 07/06/11 |
| Sample Matrix: | Soil | Date Extracted: | 07/07/11 |
| Preservative: | Cool | Date Analyzed: | 07/07/11 |
| Condition: | Intact | Analysis Needed: | TPH-418.1 |

| | | Det. |
|-----------|---------------|---------|
| | Concentration | Limit |
| Parameter | (mg/kg) | (mg/kg) |

Total Petroleum Hydrocarbons

28.2

5.0

ND = Parameter not detected at the stated detection limit.

References:

Method 418.1, Petroleum Hydrocarbons, Total Recoverable, Chemical Analysis of Water

and Waste, USEPA Storet No. 4551, 1978.

Canyon Largo Unit 239N Comments:

Analyst



EPA METHOD 418.1 TOTAL PETROLEUM HYDROCARBONS QUALITY ASSURANCE REPORT

Client:

QA/QC

Project #:

N/A

Sample ID:

QA/QC

Date Reported:

07/07/11

Laboratory Number:

Freon-113

Date Sampled: Date Analyzed: N/A

Sample Matrix: Preservative:

N/A

Date Extracted:

07/07/11 07/07/11

Condition:

N/A

Analysis Needed:

TPH

Calibration

I-Cal Date

C-Cal Date

07-07-TPH.QA/QC 58813

I-Cal RF:

C-Cal RF: % Difference

Accept. Range

06/14/11

07/07/11

1,760

1,610

8.5%

+/- 10%

Blank Conc. (mg/Kg)

Detection Limit

TPH

TPH

8.5

5.0

Duplicate Conc. (mg/Kg) **TPH**

Sample -458

Concentration

Duplicate 522

% Difference 13.8% +/- 30%

Accept. Range

Spike Conc. (mg/Kg

Sample 458

Spike Added Spike Result % Recovery 2,000

2,260

91.9%

Accept Range 80 - 120%

ND = Parameter not detected at the stated detection limit.

References:

Method 418.1, Petroleum Hydrocarbons, Total Recoverable, Chemical Analysis of Water

and Waste, USEPA Storet No. 4551, 1978.

Comments:

QA/QC for Samples 58813-58816, 58821-58825

Analyst



Chloride

Client:

Burlington

Project #:

92115-1271

Sample ID:

Reserve Pit

Date Reported:

07/07/11

Lab ID#:

58815

Date Sampled:

07/06/11

Sample Matrix:

Soil

Date Received:

Preservative:

Cool

07/06/11

Date Analyzed:

07/07/11

Condition:

Intact

Chain of Custody:

11990

Parameter

Concentration (mg/Kg)

Total Chloride

100

Reference:

U.S.E.P.A., 4500B, "Methods for Chemical Analysis of Water and Wastes", 1983.

Standard Methods For The Examination of Water And Waste Water", 18th ed., 1992.

Comments:

Canyon Largo Unit 239N

Analyst



Chloride

Client: Sample ID: Burlington

Project #:

92115-1271

Back Ground

Date Reported:

07/07/11

Lab ID#:

58816 Soil

Date Sampled:

07/06/11

Sample Matrix: Preservative:

Cool

Date Received:

07/06/11

Condition:

Intact

Date Analyzed:

07/07/11

Chain of Custody:

11990

Parameter

Concentration (mg/Kg)

Total Chloride

70

Reference:

U.S.E.P.A., 4500B, "Methods for Chemical Analysis of Water and Wastes", 1983.

Standard Methods For The Examination of Water And Waste Water", 18th ed., 1992.

Comments:

Canyon Largo Unit 239N

Analyst

| Submit To Appropr Two Copies | | State of New Mexico | | | | | Form C-105 | | | | | | | | | | | | |
|-------------------------------------------------------------------------------|---------------------------------|---------------------|-----------------------------------|---------------------------|--------------|----------------------------------------|-------------|--------------|-------------|---------------------------------|--------------------------------|--------------------------------------------------|-----------------|------------|----------|-----------|---------------------------------------|--|--|
| District I 1625 N French Dr District II | 625 N French Dr Hobbs, NM 88240 | | | | | Energy, Minerals and Natural Resources | | | | | July 17, 2008 1. WELL API NO. | | | | | | | | |
| 1301 W Grand Ave | enue, Artes | ıa, NM 8821 | 0 | Oil Conservation Division | | | | | | 30-039-30883 2 Type of Lease | | | | | | | | | |
| 1000 Rio Brazos Ro | | | . | | | 20 South S Santa Fe, N | | | | r . | | STATE FEE FED/INDIAN 3 State Oil & Gas Lease No | | | | | | | |
| 1220 S St Francis | | | | | | | | | | | | SF - 078885 | | | | | | | |
| WELL (| | LETION | I OR I | RECC | MPL | ETION RE | POF | RT A | ND | LOG | | 5 Lease Name or Unit Agreement Name | | | | | | | |
| COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) | | | | | | | | | | CANYON | LAF | | | | | | | | |
| ☐ C-144 CLOS | | | | | | | | | | nd #32 and | /or | 6 Well Numb 239N | er | | | | | | |
| #33, attach this ar | nd the plat | | | | | | | | | | | | | | | | | | |
| | WELL [|] worko | VER [|] DEEPE | ENING | □PLUGBAC | < 🗆 : | DIFFE | EREN | T RESERV | OIR | OTHER 9 OGRID | | | | | | | |
| Burlington R | esource | s Oil G | as Con | ıpany, | LP | | | | | | | 14538 | | | | | | | |
| 10 Address of Op PO Box 4298, Far | | NM 87499 |) | | | | | | | | | 11 Pool name | or W | ıldcat | | | | | |
| 12.Location | Unit Ltr | Section | n | Towns | hıp | Range | Lot | | | Feet from t | he | N/S Line | Feet | from the | E/W | Line | County | | |
| Surface: | | | | | | | | | | | | | | | | | | | |
| BH: | I II Da | ate T D Re | | 115 5 |)-4- D | Dalasad | | - | 16 | Dir. C. 1 | | (D. 1 . D. | | [12 | | · (DE | LDVD | | |
| 13 Date Spudded | | | acned | 3/27/ | 2011 | Released | | | | | | (Ready to Prod | • | R7 | Γ, GR, 6 | etc) | and RKB, | | |
| 18 Total Measure | ed Depth of | of Well | | 19 P | 'lug Bac | k Measured Dep | oth | | 20 | Was Direct | iona | l Survey Made? | i | 21 Туре | e Electr | rc and Ot | her Logs Run | | |
| 22 Producing Int | erval(s), o | f this comp | oletion - | Top, Bot | tom, Na | ame | | 1 | | | | | | | | | | | |
| 23 | | | | | CAS | ING REC | ORI |) (R | epo | rt all str | ring | gs set in we | ell) | | | | | | |
| CASING SIZ | ZE | WEIG | HT LB / | | | DEPTH SET | | ` | | E SIZE | | CEMENTIN | | CORD | Al | MOUNT | PULLED | | |
| | | | | | | | | | | | | | | | | | | | |
| | | | | | | | _ | | | | | | | | | | | | |
| | | · | | | | | | | | | | | | | | | | | |
| SIZE | ТОР | | BO' | ТТОМ | LINI | ER RECORD SACKS CEM | ENT | SCR | REEN | | 25 SIZ | | | NG RECO | | PACKI | ER SET | | |
| | | | | | | | | | 1 | | | | | | | | | | |
| 26 Perforation | record (ın | iterval, size | , and nu | mber) | | <u> </u> | | 27 | ACI | D, SHOT, | FR | ACTURE, CE | <u> </u> MEN | T, SQUE | EEZE, | ETC | | | |
| | | | | | | | | DEP | TH I | NTERVAL | | AMOUNT A | ND K | IND MAT | ΓERIAI | L USED | | | |
| i | | | | | | | | | | | | | | · | | | | | |
| 28 | | | | | | | PR | | CT | ION | | | | | | | · · · · · · · · · · · · · · · · · · · | | |
| Date First Produc | tion | - | Product | ion Meti | nod (Flo | owing, gas lift, p | | | | |) | Well Status | (Proc | d or Shut- | ın) | | | | |
| Data effect | 11 | Total | Lou | -1 - C | | D., #. F. | | 0.1 | Dist | | - | MOF | 137 | . Dil | | To o | N. D. | | |
| Date of Test | Hours | Tested | Che | oke Size | | Prod'n For Test Period | | O:1 - | - Bbi | 1 | Gas | s - MCF | Wa | ater - Bbl | | Gas - C | Oil Ratio | | |
| Flow Tubing Press | Casing | g Pressure | | culated 2 ur Rate | 24- | Oıl - Bbl | | | Gas - | MCF | 1 | Water - Bbl | | Oil Grav | vity - A | PI - (Cor | r) | | |
| 29 Disposition of | Gas (Sold | d, used for | | | ; | | | | | | | | 30 T | est Witnes | ssed By | , | | | |
| 31 List Attachme | | | | | | | | | | | | | | | | | | | |
| 32 If a temporary | pit was u | sed at the v | vell, atta | ch a plat | with the | e location of the | tempo | rary p | oit | · | | | | | | | | | |
| 33. If an on-site b | urial was | | | | | | | | _ | | | · | | | | | | | |
| I hereby certif | y that th | | <u>de 36.4?</u> ation s | | n both | gitude 107.4258 i sides of this | 3°W form | NAD is tr | ∐19 ue a | 27 ⊠1983 nd compl | ete | to the best o | f my | knowled | lge an | d belief | 6 | | |
| Signature | mi | L GO | box | Wi. | Prin _Nan | ited ne Jamie Go | odwi | n ′ | Tıtle | : Regula | ator | y Tech, | Date | : 9/13/20 | 011 | , | | | |
| E-mail Address jamie.l.goodwin@conocophillips.com | | | | | | | | | | | | | | | | | | | |

ConocoPhillips

| Pit Closure Form: | |
|----------------------------------------------------------------------------|---|
| Date: 7/29 /11 | |
| Well Name: Caryon Largo Vnit 39N | |
| Footages: 1930 FSL 670 FWL Unit Letter: | |
| Section: 1, T-25-N, R-6 -W, County: Rio Acab. State: 12 | _ |
| Contractor Closing Pit: | _ |
| | |
| Construction Inspector: 5. M-Glasson Date: 729/11 | - |
| Construction Inspector: 5. M-Glasson Date: 729/11 nspector Signature: 912 | |
| • | |
| | |
| | |
| evised 11/4/10 | |
| ffice Use Only: ubtask SM | |
| older | |

Goodwin, Jamie L

From:

Payne, Wendy F

Sent:

Thursday, July 28, 2011 9:00 AM

To:

(Brandon.Powell@state nm.us); GRP:SJBU Regulatory; Eli (Cimarron)

(eliv@qwestoffice.net); James (Cimarron) (jwood@cimarronsvc.com); Mark Kelly; Randy

McKee, Robert Switzer, Sherrie Landon; Bassing, Kendal R.; Berenz

(mxberenz@yahoo.com); Chavez Darrell (dchavez0330@yahoo.com), Crawford, Lea A: Elmer Perry: Faver Norman, Fred Martinez: Jared Chavez: Lowe, Terry: McDonald Johnny (ir mcdonald@msn.com); Payne, Wendy F; Smith, Mike W; Spearman, Bobby E; Steve McGlasson; Tally, Ethel, Becker, Joey W; Bowker, Terry D; Frost, Ryan M; Goosey, Paul P, Gordon Chenault; Green, Cary J; GRP SJBU Production Leads, Hockett, Christy R, Johnson. Kirk L; Bassing, Kendal R.; Kennedy, Jim R; Lopez, Richard A; Nelson, Garry D; O'Nan, Mike J.: Peace, James T; Pierce, Richard M; Poulson, Mark E; Schaaphok, Bill; Smith, Randall O, Souther, Tappan G; Spearman, Bobby E, Stamets, Steve A; Thacker, LARRY; Thibodeaux,

Gordon A; Work, Jim A; Corey Alfandre; 'isaiah@crossfire-llc com', Jerid Cabot

(jerid@crossfire-llc com); Blair, Maxwell O; Blakley, Mac; Farrell, Juanita R; Gillette, Steven L (PAC); Hines, Derek J; Maxwell, Mary Alice; McWilliams, Peggy L; Saiz, Kooper (Finney Land

Co.); Seabolt, Elmo F; Thayer, Ashley A; Thompson, Trey E (Finney Land Co.)

Cc:

Ace Services

Subject:

Reclamation Notice: Canyon Largo Unit 239N (Area 26 * Run 652)

Importance:

High

Attachments:

Canyon Largo Unit 239N.pdf

ACE Services will move a tractor to the **Canyon Largo Unit 239N** to start the reclamation process on Tuesday, August 2, 2011. Please contact Steve McGlasson (716-3285) if you have guestions or need further assistance.



Canyon Largo Unit 239N.pdf (2...

Burlington Resources Well - Network # 10256439 - Activity Code D250 (reclamation) & D260 (pit closure) (PO: Kaitlw)

Rio Arriba County, NM

Canyon Largo Unit 239N - BLM surface/BLM minerals

Onsited: Mike Flaniken 10-8-08

Twin: n/a

1930' FSL, 670' FWL Sec.1, T25N, R6W Unit Letter " L " Lease #: SF-078885 Unit # NMNM78383D

Latitude: 36° 25' 36" N (NAD 83) Longitude: 107° 25' 32" W (NAD 83)

Elevation: 6749'

Total Acres Disturbed, 3.07 acres

Access Road: 44 feet API # 30-039-30883 Within City Limits: No Pit Lined. YES

NOTE: Arch Monitoring is NOT required on this location.

Wendy Payne ConocoPhillips-SJBU


505-326-9533 Wendy.F.Payne@conocophillips.com


ConocoPhillips


| Reclamation Form: |
|---------------------------------------------------------------------------------------------------|
| Date: 9/7/11 |
| Well Name: Canyon Lago Unit 239W |
| Footages: 1936 FSL 670 FWL Unit Letter: |
| Section:, T-25-N, R-6-W, County: Rodon L. State: |
| Reclamation Contractor: |
| Reclamation Date: 8/5/11 |
| Road Completion Date: $\frac{8/9}{11}$ |
| Seeding Date: 8/7/// |
| **PIT MARKER STATUS (When Required): Picture of Marker set needed MARKER PLACED: $8/9/11$ (DATE) |
| LATATUDE: 36. 42694 |
| LONGITUDE: 107, 42579 |
| Pit Manifold removed 7/29/11 (DATE) |
| Construction Inspector: $\frac{5 M^{5} l_{950}}{100}$ Date: $\frac{9/7}{11}$ |
| Inspector Signature: |
| Office Use Only: Subtask DSM Folder Pictures Revised 11/4/10 |

BURLINGTON

CANYON LARGO UNIT #239N
1571' FNL 1396' FWL
UNIT F SEC 1 T25N R06W / LEASE# SF-078885
BH: NWNW SEC 1 T25N R06W
API #30-039-30882 ELEV. 6682'
UNIT # NMNM78383D
LATITUDE 36° 25 MIN. 53 SEC. N (NAD 83)
LONGITUDE 107° 25 MIN. 23 SEC. W (NAD 83)
RIO ARRIBA COUNTY, NEW MEXICO
EMERGENCY CONTACT: 1-505-324-5170

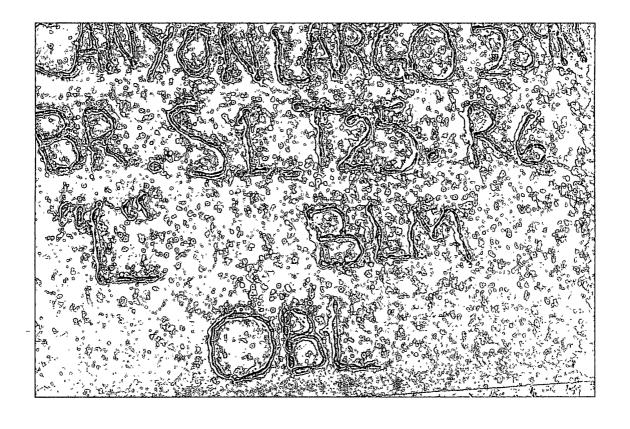



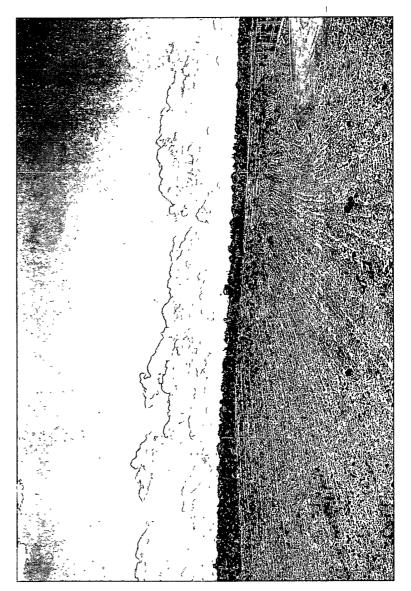

| | WELL NAME: | OPEN D | PIT INSPE | CTION | FORM | | | | | :::: |
|---------------|---------------------------------------------------------------------------------------------------|-------------------------------------|-------------------------------------|-------------------------------------|-------------------------------------|-------------------------------------|-------------------------------------|---------------------------|------------------------------------------------|------------------------------------------------|
| | CANYON LARGO 239N | | | ConocoPhillips | | | | | | |
| | | | JARED CHAVEZ | | | | JARED CHAVEZ | | | |
| _ | DATE | | 02/16/11 | 02/22/11 | 03/01/11 | 03/07/11 | 03/14/11 | 03/21/11 | 03/29/11 | 04/05/11 |
| | *Please request for pit extention after 26 weeks | Week 1 | Week 2 | Week 3 | Week 4 | Week 5 | Week 6 | Week 7 | Week 8 | Week 9 |
| | DIP 47 4 7114 | Drilled | ☐ Drilled☐ Completed☐ | ☐ Drilled☐ Completed | Drilled | ☐ Drilled☐ Completed | ☐ Drilled | ☑ Drilled | ☐ Drilled☐ Completed | ✓ Drilled ☐ Completed |
| | PIT STATUS | Completed | Clean-Up | Clean-Up | ☐ Completed☐ Clean-Up | | Completed | Completed | ☐ Clean-Up | Clean-Up |
| | | Clean-Up | ☐ Clean-Up | ☐ Clean-Up | □ Clean-Up | Clean-Up | Clean-Up | Clean-Up | Crean-Up | Clean-up |
| LOCATION | Is the location marked with the proper flagging? (Const. Zone, poles, pipelines, etc.) | ☑ Yes ☐ No | ✓ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☐ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No |
| /201 | Is the temporary well sign on location and visible from access road? | ☑ Yes ☐ No | ✓ Yes ☐ No | ✓ Yes 🗌 No | ✓ Yes □ No | ✓ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes ☐ No |
| | Is the access road in good driving condition? (deep ruts, bladed) | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes □ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No |
| | Are the culverts free from debris or any object preventing flow? | ☑ Yes ☐ No | ✓ Yes 🗌 No | ✓ Yes 🗌 No | ✓ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | Yes No | ☑ Yes ☐ No | ✓ Yes □ No |
| | Is the top of the location bladed and in good operating condition? | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No |
| NCE | Is the fence stock-proof? (fences tight, barbed wire, fence clips in place? | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ✓ Yes 🗌 No | ☑ Yes ☐ No | Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No |
| COMPLIANCE | Is the pit liner in good operating condition? (no tears, up-rooting corners, etc.) | ☑ Yes ☐ No | ☑ Yes 🗌 No | Yes No | ☑ Yes ☐ No | ☑ Yes ☐ No |
| | is the the location free from trash, oil stains and other materials? (cables, pipe threads, etc.) | ☑ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes 🗌 No | Yes No | ☑ Yes ☐ No | ☑ Yes ☐ No |
| ENVIRONMENTAL | Does the pit contain two feet of free board? (check the water levels) | ✓ Yes 🗌 No | ☑ Yes 🗌 No | ☑ Yes ☐ No | Yes No | ✓ Yes ☐ No | ☑ Yes ☐ No |
| RON | Is there any standing water on the blow pit? | ☐ Yes ☑ No | ☐ Yes ☐ No | ☐ Yes ☑ No | ☐ Yes ☑ No |
| ENV | Are the pits free of trash and oil? | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗋 No | ☐ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No |
| | Are there diversion ditches around the pits for natural drainage? | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☐ Yes ☐ No | ✓ Yes ☐ No | ☑ Yes ☐ No |
| | Is there a Manifold on location? | ☑ Yes ☐ No | ✓ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ✓ Yes □ No | ✓ Yes 🗌 No | ☐ Yes ☐ No | ✓ Yes □ No | ☑ Yes ☐ No |
| | Is the Manifold free of leaks? Are the hoses in good condition? | ✓ Yes 🗌 No | ✓ Yes □ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes □ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ✓ Yes □ No | ✓ Yes 🗌 No |
| ٥ م | Was the OCD contacted? | ☐ Yes ☑ No | Yes No | ☐ Yes ☑ No | ☐ Yes ☑ No |
| | PICTURE TAKEN | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | Yes 🗸 No | ☐ Yes ☑ No | ☐ Yes ☑ No | Yes No | ☐ Yes ☑ No | ☐ Yes ☑ No |
| | COMMENTS | LOCATION IS IN GOOD CONDITION | AWS 673 IS ON LOCATION | PIT AND LOCATION IS IN GOOD CONDITION | PIT AND LOCATION IS IN GOOD CONDITION |

WELL NAME: CANYON LARGO 239N INSPECTOR JARED CHAVEZ JARED CHAVEZ E. Perry E. Perry E. Perrv E. Perry E. Perry E. Perry DATE 04/12/11 04/27/11 05/04/11 05/10/11 06/07/11 05/13/11 05/24/11 06/01/11 *Please request for pit extention after 26 weeks Week 10 Week 11 Week 12 Week 13 Week 14 Week 15 Week 16 Week 17 Week 18 ✓ Drilled ✓ Drilled Drilled ✓ Drilled ✓ Drilled ✓ Drilled ✓ Drilled ✓ Drilled ✓ Drilled ☐ Completed ☐ Completed ☐ Completed Completed Completed ☐ Completed Completed Completed Completed PIT STATUS Clean-Up Clean-Up Clean-Up Clean-Up Clean-Up Clean-Up Clean-Up Clean-Up Clean-Up is the location marked with the proper flagging? ☑ Yes ☐ No ☐ Yes ☐ No ✓ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No ☑ Yes ☐ No (Const. Zone, poles, pipelines, etc.) Is the temporary well sign on location and visible ✓ Yes 🖺 No ✓ Yes ☐ No ✓ Yes ☐ No. ☐ Yes ☐ No. ✓ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No. ✓ Yes ☐ No. ✓ Yes ☐ No Ŏ from access road? Is the access road in good driving condition? ☑ Yes ☐ No. ☐ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No. ✓ Yes 🗌 No ✓ Yes ☐ No ✓ Yes ☐ No. ✓ Yes ☐ No. ✓ Yes ☐ No. (deep ruts, bladed) Are the culverts free from debris or any object ✓ Yes 🗌 No ☐ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No ✓ Yes 🗀 No ✓ Yes ☐ No ✓ Yes No ☑ Yes ☐ No preventing flow? is the top of the location bladed and in good ✓ Yes □ No ☐ Yes ☐ No ✓ Yes □ No ☑ Yes ☐ No ✓ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No operating condition? Is the fence stock-proof? (fences tight, barbed ✓ Yes 🗌 No ☐ Yes ☐ No ✓ Yes ☐ No ☐ Yes 🗸 No ☑ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No Yes V No Yes 🗹 No wire, fence clips in place? Is the pit liner in good operating condition? (no ✓ Yes ☐ No ☐ Yes ☐ No. ✓ Yes ☐ No. ✓ Yes ☐ No. ☑ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No ✓ Yes ☐ No. ✓ Yes ☐ No tears, up-rooting corners, etc.) Is the the location free from trash, oil stains and ☑ Yes ☐ No Yes No. ✓ Yes ☐ No. ☑ Yes ☐ No ☑ Yes ☐ No ✓ Yes ☐ No ✓ Yes 🗆 No ✓ Yes ☐ No ☑ Yes ☐ No other materials? (cables, pipe threads, etc.) Does the pit contain two feet of free board? (check ENVIRONMENT ✓ Yes □ No ☐ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No. ✓ Yes ☐ No ✓ Yes ☐ No ✓ Yes 🗀 No ✓ Yes No ✓ Yes ☐ No the water levels) Is there any standing water on the blow pit? ☐ Yes ☑ No Yes No ☐ Yes ☑ No ☐ Yes ☑ No Yes V No ☐ Yes ☑ No Yes V No ☐ Yes ☑ No Yes V No Are the pits free of trash and oil? ☐ Yes ☐ No ✓ Yes □ No ✓ Yes ☐ No ☐ Yes ☑ No ☑ Yes ☐ No ☑ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No Are there diversion ditches around the pits for ☑ Yes ☐ No Yes No ☑ Yes 🗌 No ☑ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No ✓ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No natural drainaae? Is there a Manifold on location? ✓ Yes ☐ No ☐ Yes ☐ No ☑ Yes ☐ No ☑ Yes ☐ No ✓ Yes ☐ No is the Manifold free of leaks? Are the hoses in ☑ Yes ☐ No ☐ Yes ☐ No ✓ Yes ☐ No ✓ Yes 🗌 No ✓ Yes ☐ No ✓ Yes 🗆 No ✓ Yes No ☑ Yes ☐ No ☑ Yes ☐ No acod condition? ○ △Was the OCD contacted? ☐ Yes ☑ No Yes No Yes V No ☐ Yes ☑ No ☐ Yes ☑ No ☐ Yes ☑ No Yes 🗸 No ☐ Yes ✓ No ☐ Yes ✓ No ☐ Yes ☑ No Yes No ☐ Yes ☑ No PICTURE TAKEN Yes V No Yes V No Yes 🗹 No ☐ Yes ☑ No Yes No Yes V No PIT AND PIT AND COMMENTS LOCATION IS IN LOCATION IS IN GOOD GOOD Fence in Bad Fence Loose CONDITION CONDITION OK Fence Loose Stains on Loc Contion Oil in Pit Frac on Loc Pit cleaned up

| | WELL NAME: CANYON LARGO 239N | | | | | | | | | |
|---------------|---------------------------------------------------------------------------------------------------|----------------------------------------|---------------------------------|-------------------------------------------|----------------------------------|----------------------------------|---------------------------------|------------------------------------|----------------------------|--------------------------------|
| | INSPECTOR DATE | | E. Perry 06/21/11 | E. Perry 06/29/11 | E. Perry 07/06/11 | E. Perry 07/11/11 | JON BERENZ 07/18/11 | E. Perry 07/26/11 | E. Perry 08/02/11 | CLOSED 08/09/11 |
| | *Please request for pit extention after 26 weeks | Week 19 | Week 20 | Week 21 | Week 22 | Week 23 | Week 24 | Week 25 | *Week 26* | Week 27 |
| | PIT STATUS | ☑ Drilled ☐ Completed ☐ Clean-Up | ☑ Dniled ☐ Completed ☐ Clean-Up | ☑ Drilled ☑ Completed ☐ Clean-Up | ☑ Drilled ☑ Completed ☐ Clean-Up | ✓ Drilled ✓ Completed ☐ Clean-Up | ✓ Dniled ✓ Completed ☐ Clean-Up | ✓ Drilled ✓ Completed ☐ Clean-Up | Drilled Completed Clean-Up | ☐ Drilled☐ Completed☐ Clean-Up |
| CATION | Is the location marked with the proper flagging? (Const. Zone, poles, pipelines, etc.) | ✓ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes ☐ No | ✓ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| 10C/ | Is the temporary well sign on location and visible from access road? | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☐ Yes ☑ No | Yes No | ☐ Yes ☐ No |
| | Is the access road in good driving condition? (deep ruts, bladed) | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ✓ Yes □ No | ☑ Yes 🗌 No | ✓ Yes ☐ No | Yes No | ☐ Yes ☐ No |
| | Are the culverts free from debris or any object preventing flow? | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | Yes No | ☐ Yes ☐ No |
| | Is the top of the location bladed and in good operating condition? | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | Yes No | ☐ Yes ☐ No |
| NCE | Is the fence stock-proof? (fences tight, barbed wire, fence clips in place? | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ✓ Yes ☐ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| OMPLIAN | Is the pit liner in good operating condition? (no tears, up-rooting corners, etc.) | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| Ŭ | Is the the location free from trash, oil stains and other materials? (cables, pipe threads, etc.) | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| MENT/ | Does the pit contain two feet of free board? (check the water levels) | ✓ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| ENVIRONMENTAL | Is there any standing water on the blow pit? | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| S | Are the pits free of trash and oil? | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| | Are there diversion ditches around the pits for natural drainage? | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| | Is there a Manifold on location? | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes ☐ No | ☑ Yes ☐ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| | Is the Manifold free of leaks? Are the hoses in good condition? | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☑ Yes ☐ No | ✓ Yes 🗌 No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| ၁၀ ဝ | Was the OCD contacted? | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☐ No | ☐ Yes ☐ No |
| | PICTURE TAKEN | Yes No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | ☐ Yes ☑ No | Yes V No | ☐ Yes ☑ No | ☐ Yes ☐ No | ✓ Yes 🗌 No |
| | COMMENTS | Stains on Loc | Staimns on Loc | Stains on Loc Completion Rig on Loc | GOOD | Fence Loose | Fence loose | Sign on Facility Fence Repaired | PIT CLOSED | PIT CLOSED |
