


BAKER PACKERS DIVISION

DATE 11-16-81 WELL NO. 123E LEASE Breech B COUNTY Dakota

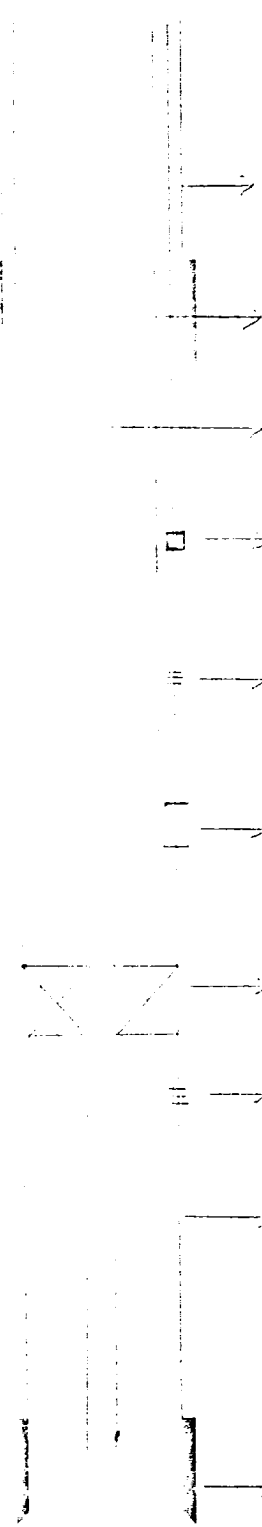

9 5/8" 32.3# H-40 surface casing set at 283'. Cemented with 250 sacks Neat cement, 2% CaCl. Cement circulated to surface.

1 1/4" 2.33# V-55 IJ tubing set at 5378'.

1 1/4" 2.33# V-55 IJ tubing set at 7352'.

Stage tool set at 3832'. Cemented thru tool with 538 sacks 50 50 Poz, 6% Gel followed by 100 sacks Neat. Cement circulated to surface.

Mesa Verde perforations 5366 to 5178.

Stage tool set at 5393'. Cemented thru tool with 250 sacks 50-50 Poz, 6% Gel followed by 100 sacks Neat. Cement circulated to stage tool set at 3832'.

5 1/2" Baker Packers Model "R" Double Grip packer set at 5508'.

Dakota perforations 7370 to 7216.

5 1/2" 15.5# & 17# casing set at 7512'. Cemented thru shoe with 250 sacks Class B cement, 50-50 Poz, 6% Gel followed by 100 sacks Latex. Cement circulated to stage tool set at 5393'.

TD 7512'

