

Step Rate Injection Test Report

for


Texaco E&P


CVU 14

9/21/01

E-30-17s-35e
2630/N 4 1238/W

30-025-25811





COMPANY : Texaco E&P
WELL: CVU 14
COMPANY REP: Steve Guillot
PERFORATIONS: N/A


SERVICE DATES : 9/21/01
TEST TYPE : Step Rate Injection
PPS TECHNICIANS : D. Ginanni
BHP GAUGE DEPTH: N/A

	TIME	PRESSURE (PSI)	INTEGRITY (PSI)	INJECTION RATE (GPM)	INTEGRITY RATE (GPM)	INTEGRITY PRESSURE (PSI)
	9:30	953.9				
	9:35	979.7	1.7	487.6	14.22	
	9:40	1009.1	3.4	489.7	14.28	
1	9:45	1036.0	5.0	477.1	13.91	
	9:50	1185.0	8.4	959.8	27.99	
	9:55	1225.4	11.8	989.1	28.85	
2	10:00	1357.5	15.2	974.4	28.42	
	10:05	1476.4	20.3	1475.8	43.05	
	10:10	1566.2	25.5	1500.1	43.75	
3	10:15	1687.9	30.5	1435.9	41.88	
	10:20	1813.7	37.2	1923.6	56.10	
	10:25	1888.8	43.8	1895.2	55.28	
4	10:30	1985.2	51.0	2074.0	60.49	
	10:35	2153.7	59.5	2455.2	71.61	
	10:40	2218.7	67.9	2420.1	70.59	
5	10:45	2230.3	76.7	2518.3	73.45	
	10:50	2341.9	86.6	2868.0	83.65	
	10:55	2349.7	96.8	2937.0	85.66	
6	11:00	2398.8	106.9	2894.4	84.42	
	11:05	2541.2	118.4	3325.5	96.99	
	11:10	2563.4	129.9	3322.2	96.90	
7	11:15	2748.6	142.0	3460.7	100.94	
	11:20	2768.0	155.5	3895.7	113.62	
	11:25	2727.2	168.8	3845.2	112.15	
8	11:30	1877.8	182.2	3857.0	112.50	
FALLOFF	11:31	1796.1				
	11:32	1788.8				
	11:33	1781.1				
	11:34	1774.3				
	11:35	1767.8				
	11:40	1737.7				
	11:45	1712.2				

Pacific PROCESS SYSTEMS, INC.

TEXACO BUCKEYE CVU 14

Step Rate Injection Test

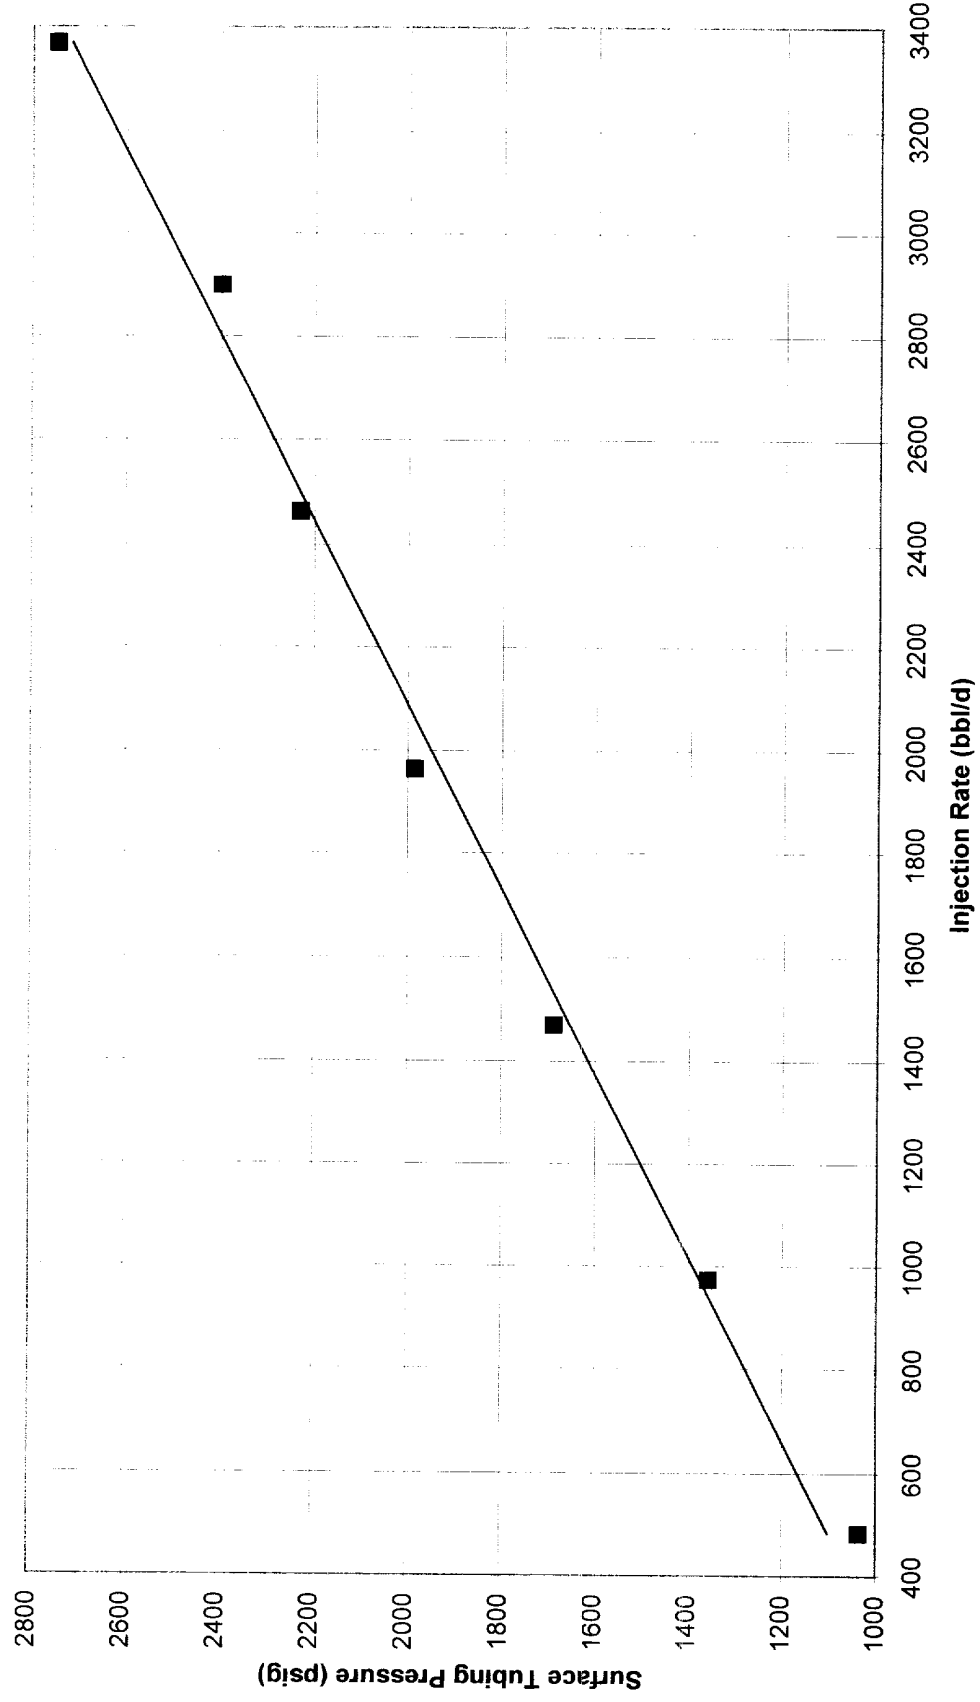

Phone: (505) 392-8813

Fax: (505) 392-6612

3406 Lovington Hwy.

Hobbs, NM 88240

TABLE OF CONTENTS

SECTION I	CONTENTS
SECTION II	SEQUENCE OF EVENTS
SECTION III	DATA REPORT
SECTION IV	CHART



COMPANY : Texaco E&P
WELL: CVU 14
COMPANY REP: Steve Guillot
PERFORATIONS: N/A

SERVICE DATES : 9/21/01
TEST TYPE : Step Rate Injection
PPS TECHNICIANS : D. Ginanni
BHP GAUGE DEPTH: N/A

		REMARKS
09/21/01	9:30	Start Pumping @ 500 BPD
09/21/01	9:35	
09/21/01	9:40	
09/21/01	9:45	Increase to 1000 BPD
09/21/01	9:50	
09/21/01	9:55	
09/21/01	10:00	Increase to 1500 BPD
09/21/01	10:05	
09/21/01	10:10	
09/21/01	10:15	Increase to 2000 BPD
09/21/01	10:20	
09/21/01	10:25	
09/21/01	10:30	Increase to 2500 BPD
09/21/01	10:35	
09/21/01	10:40	
09/21/01	10:45	Increase to 3000 BPD
09/21/01	10:50	
09/21/01	10:55	
09/21/01	11:00	Increase to 3500 BPD
09/21/01	11:05	
09/21/01	11:10	
09/21/01	11:15	Increase to 4000 BPD
09/21/01	11:20	
09/21/01	11:25	
09/21/01	11:30	Cease pumping, start falloff
09/21/01	11:31	
09/21/01	11:32	
09/21/01	11:33	
09/21/01	11:34	
09/21/01	11:35	
09/21/01	11:40	
09/21/01	11:45	End of test
