




Tubing Summary

15-42671

Well Name	Lease	Field Name	Business Unit
RUSTLER BLUFF 34-24-29 FED COM 002H	Rustler Bluffs Unit	Bone Spring	Mid-Continent
Ground Elevation (ft)	Original RKB Elevation (ft)	Current RKB Elevation	Mud Line Elevation (ft)
2,979.00	3,010.00	3,010.00, 12/18/2014	Water Depth (ft)
Current KB to Ground (ft)	Current KB to Mud Line (ft)	Current KB to Csg Flange (ft)	Current KB to Tubing Head (ft)
31.00			

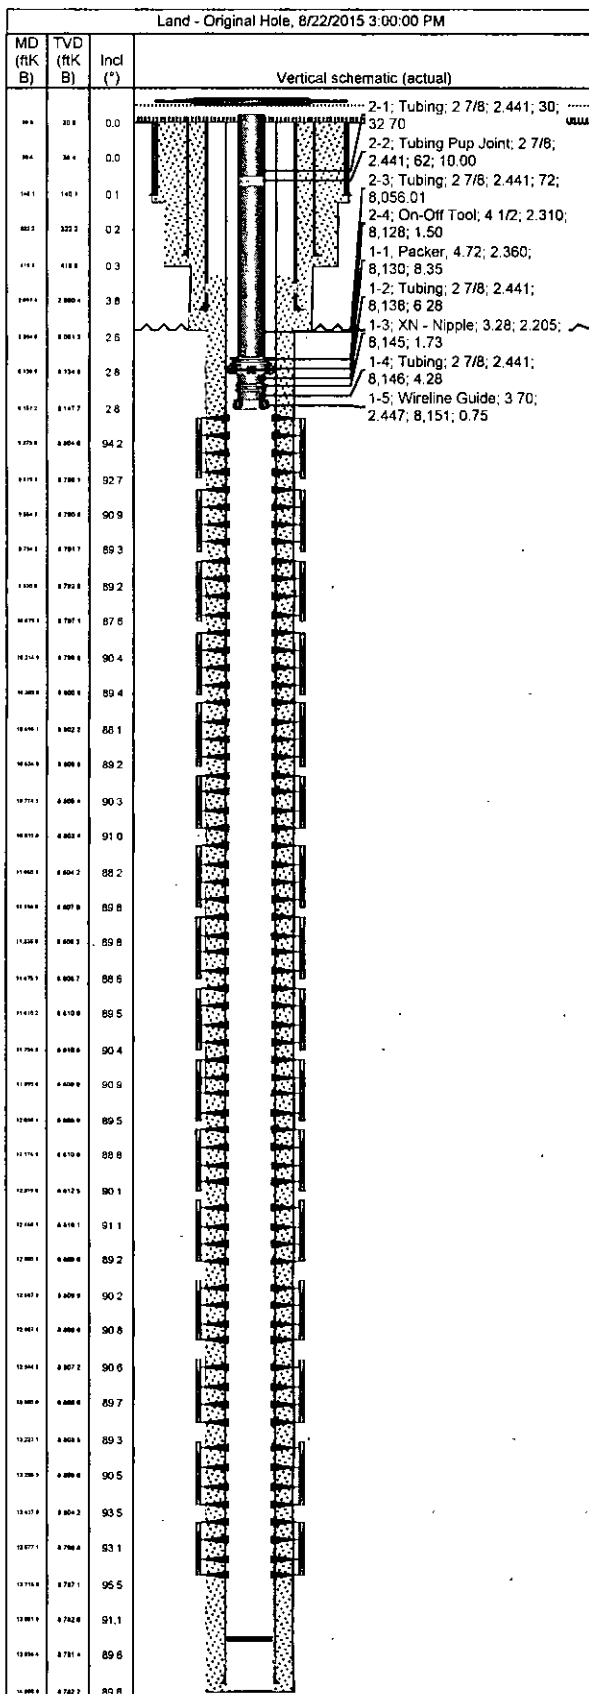

Tubing Strings

Tubing Description	Planned Run?	Set Depth (MD) (ftKB)	Set Depth (TVD) (ftKB)
Tubing - Production	N	8,130.0	8,126.4
Run Date	Run Job	Pull Date	Pull Job
8/22/2015	Complete, 3/11/2015 13:00		
Jts	Item Des	OD (in)	ID (in)
1	Tubing	2 7/8	2.441
1	Tubing Pup Joint	2 7/8	2.441
247	Tubing	2 7/8	2.441
1	On-Off Tool	4 1/2	2.310
Wt (lb/ft)	Grade	Top Thread	Len (ft)
6.50	L-80		32.70
6.50	L-80		10.00
6.50	L-80		8,056.0
			1
			1.50
Top (ftKB)	Botm (ftKB)		
29.8	62.5		
62.5	72.5		
72.5	8,128.5		
8,128.5	8,130.0		

Rod Strings

Rod Description	Planned Run?	Set Depth (ftKB)	Set Depth (TVD) (ftKB)
Run Date	Run Job	Pull Date	Pull Job


Rod Components

Jts	Item Des	OD (in)	Grade	Model	Len (ft)	Top (ftKB)	Botm (ftKB)



Wellbore Schematic

Well Name RUSTLER BLUFF 34-24-29 FED COM 002H	Lease Rustler Bluffs Unit	Field Name Bone Spring	Business Unit Mid-Continent
--	------------------------------	---------------------------	--------------------------------

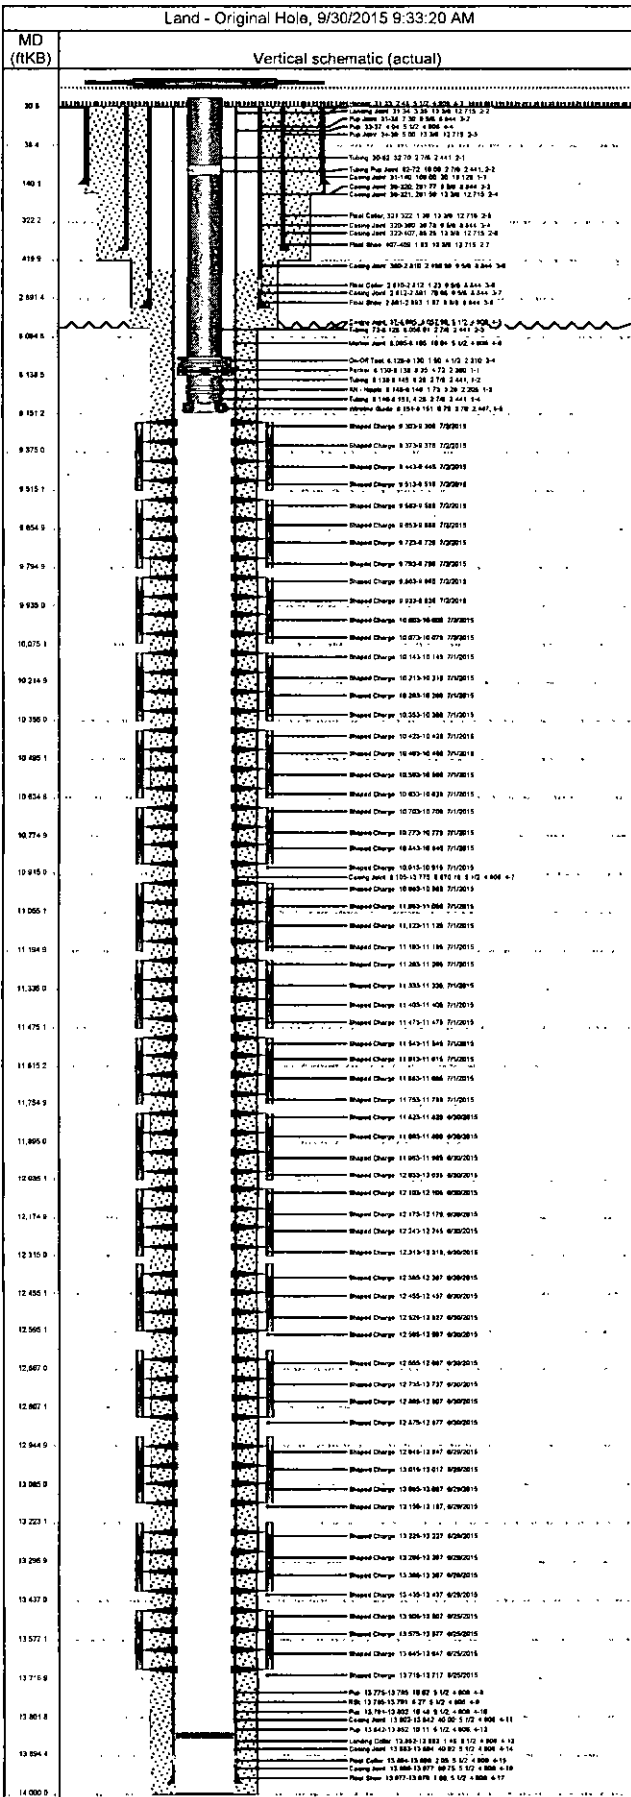


Job Details						
Job Category			Start Date		Rig/Unit End Date	
Completion			3/11/2015		3/14/2015	
Completion			6/25/2015		6/25/2015	
Completion			6/27/2015		7/2/2015	
Completion			7/2/2015		7/4/2015	
Completion			7/6/2015			
Completion			8/21/2015		8/24/2015	
Casing Strings						
Csg Des	OD (in)	Wt/Len (lb/ft)	Grade	Top Thread	Set Depth (MD) (ftKB)	
Conductor	20	94.00	K-55		140	
Surface	13 3/8	48.00	H-40		409	
Intermediate Casing 1	9 5/8	40.00	K-55		2,893	
Production Casing	5 1/2	17.00	P-110		13,979	
Tubing Strings						
Baker Hornet Pkr set at 8,151.4ftKB on 7/6/2015 00:00						
Tubing Description		Run Date		String Length (ft)		Set Depth (MD) (ftKB)
Baker Hornet Pkr		7/6/2015		21.39		8,151.4
Item Des	Jts	OD (in)	Wt (lb/ft)	Grade	Len (ft)	Btm (ftKB)
Packer	1	4.72			8.35	8,138.4
Tubing	1	2 7/8	6.50	L-80	6.28	8,144.6
XN - Nipple	1	3.28			1.73	8,146.4
Tubing	1	2 7/8	6.50	L-80	4.28	8,150.6
Wireline Guide	1	3.7			0.75	8,151.4
Tubing - Production set at 8,130.0ftKB on 8/22/2015 15:00						
Tubing Description		Run Date		String Length (ft)		Set Depth (MD) (ftKB)
Tubing - Production		8/22/2015		8,100.21		8,130.0
Item Des	Jts	OD (in)	Wt (lb/ft)	Grade	Len (ft)	Btm (ftKB)
Tubing	1	2 7/8	6.50	L-80	32.70	62.5
Tubing Pup Joint	1	2 7/8	6.50	L-80	10.00	72.5
Tubing	247	2 7/8	6.50	L-80	8,056.01	8,128.5
On-Off Tool	1	4 1/2			1.50	8,130.0
Perforations						
Date	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Entered Shot Total	Zone & Completion	
7/2/2015	9,303.0	9,305.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,373.0	9,375.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,443.0	9,445.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,513.0	9,515.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,583.0	9,585.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,653.0	9,655.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,723.0	9,725.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,793.0	9,795.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,863.0	9,865.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	9,933.0	9,935.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	10,003.0	10,005.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/2/2015	10,073.0	10,075.0	6.0	12	2ND BONE SPRINGS, Original Hole	
7/1/2015	10,143.0	10,145.0	6.0	12	2ND BONE SPRINGS, Original Hole	



Wellbore Schematic

Well Name RUSTLER BLUFF 34-24-29 FED COM 002H	Lease Rustler Bluffs Unit	Field Name Bone Spring	Business Unit Mid-Continent
--	------------------------------	---------------------------	--------------------------------

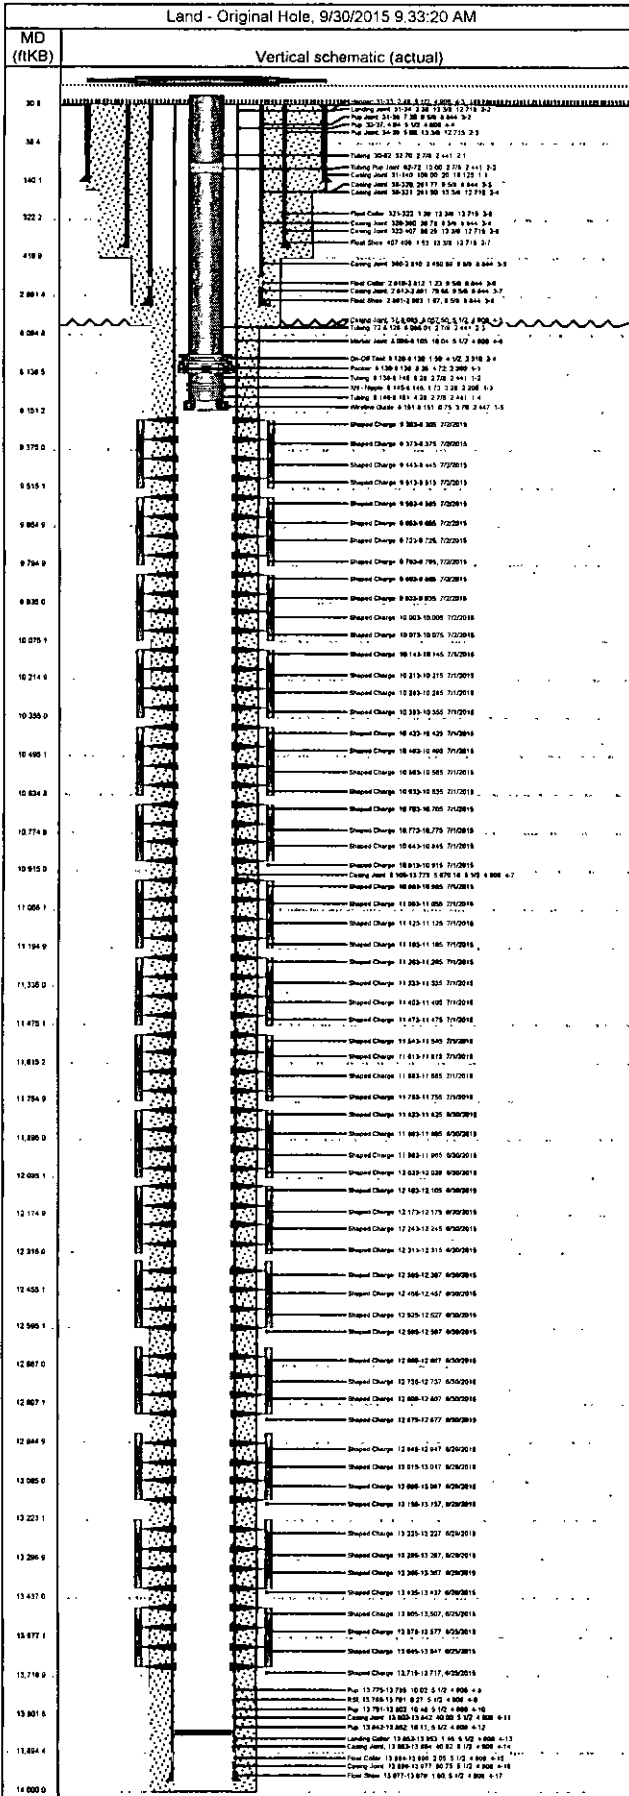


Perforations					
Date	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Entered Shot Total	Zone & Completion
7/1/2015	10,213.0	10,215.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,283.0	10,285.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,353.0	10,355.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,423.0	10,425.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,493.0	10,495.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,563.0	10,565.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,633.0	10,635.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,703.0	10,705.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,773.0	10,775.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,843.0	10,845.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,913.0	10,915.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	10,983.0	10,985.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,053.0	11,055.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,123.0	11,125.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,193.0	11,195.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,263.0	11,265.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,333.0	11,335.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,403.0	11,405.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,473.0	11,475.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,543.0	11,545.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,613.0	11,615.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,683.0	11,685.0	6.0	12	2ND BONE SPRINGS, Original Hole
7/1/2015	11,753.0	11,755.0	6.0	12	2ND BONE SPRINGS, Original Hole
6/30/2015	11,823.0	11,825.0	6.0	12	2ND BONE SPRINGS, Original Hole
6/30/2015	11,893.0	11,895.0	6.0	12	2ND BONE SPRINGS, Original Hole
6/30/2015	11,963.0	11,965.0	6.0	12	2ND BONE SPRINGS, Original Hole
6/30/2015	12,033.0	12,035.0	6.0	12	2ND BONE SPRINGS, Original Hole
6/30/2015	12,103.0	12,105.0	6.0	12	2ND BONE SPRINGS, Original Hole
6/30/2015	12,173.0	12,175.0	6.0	12	2ND BONE SPRINGS, Original Hole
6/30/2015	12,243.0	12,245.0	6.0	12	2ND BONE SPRINGS, Original Hole



Wellbore Schematic


Well Name RUSTLER BLUFF 34-24-29 FED COM 002H	Lease Rustler Bluffs Unit	Field Name Bone Spring	Business Unit Mid-Continent
--	------------------------------	---------------------------	--------------------------------

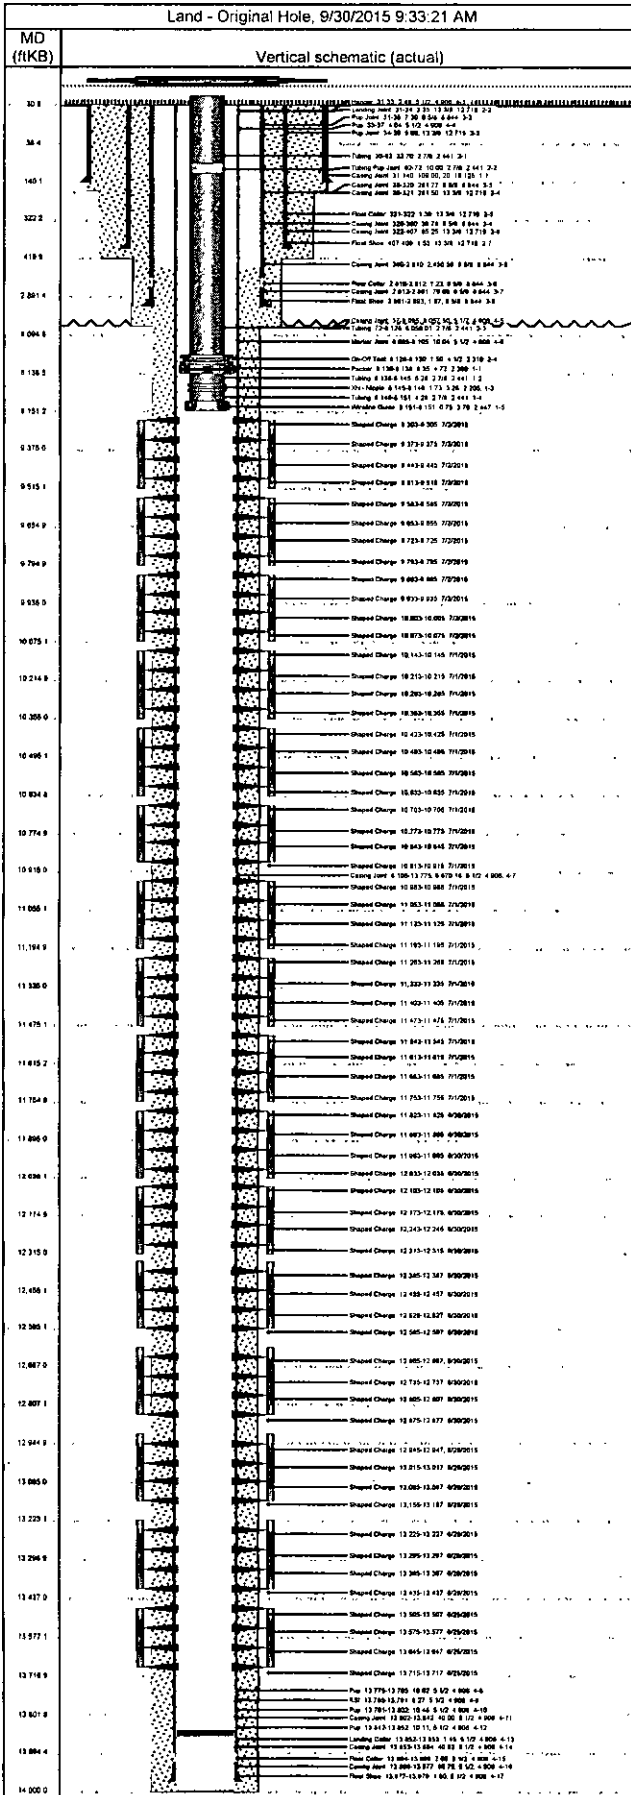



Wellbore Schematic

Well Name RUSTLER BLUFF 34-24-29 FED COM 002H	Lease Rustler Bluffs Unit	Field Name Bone Spring	Business Unit Mid-Continent
--	------------------------------	---------------------------	--------------------------------

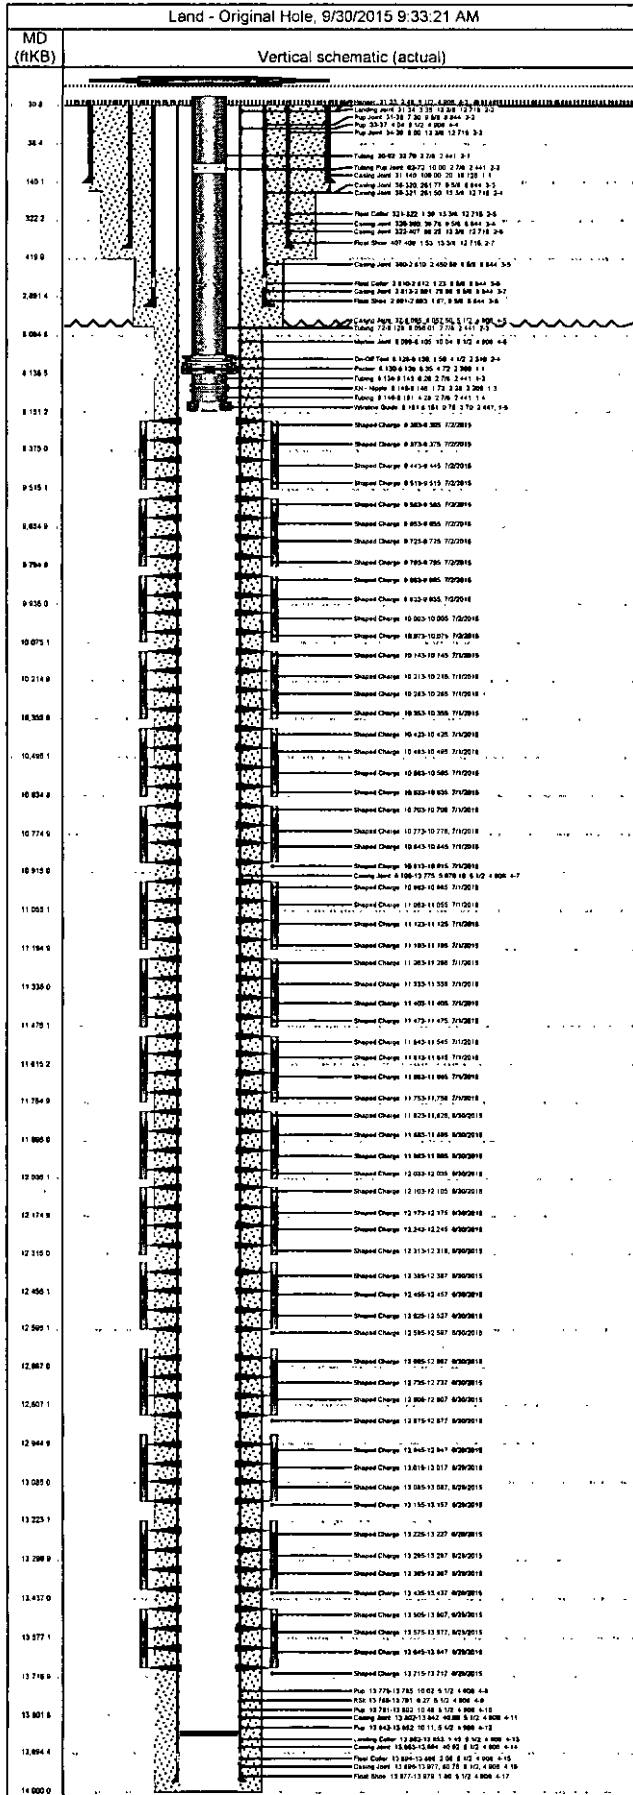

Other In Hole					
Des	Top (ftKB)	Btm (ftKB)	Run Date	Pull Date	Com
Composite Frac Plug (drop ball)	11,500.0	11,502.0	7/1/2015	7/3/2015	Stage 9
Composite Frac Plug (drop ball)	11,800.0	11,802.0	7/1/2015	7/3/2015	Stage 8
Composite Frac Plug (drop ball)	12,075.0	12,077.0	6/30/2015	7/3/2015	Stage 7
Composite Frac Plug (drop ball)	12,356.0	12,358.0	6/30/2015	7/3/2015	Stage 6
Composite Frac Plug (drop ball)	12,634.0	12,636.0	6/30/2015	7/3/2015	Stage 5
Composite Frac Plug (drop ball)	12,910.0	12,912.0	6/30/2015	7/3/2015	Stage 4
Composite Frac Plug (drop ball)	13,190.0	13,192.0	6/29/2015	7/3/2015	Stage 3
Composite Frac Plug (drop ball)	13,470.0	13,472.0	6/29/2015	7/3/2015	Stage 2

HALLIBURTON

3950 Interwood S. Pkwy • Houston, TX 77032

PHONE 281.986.4400 • FAX 281.986.4499

State of New Mexico, Eddy County

I, Kevin Stolarski certify that I am employed by Halliburton Energy Services, Inc. (aka Sperry Drilling) and that on the dates of 11-January-2015 through 3-February-2015, I did conduct or supervise the taking of MWD directional surveys for the well Rustler Bluff 34 24 29 Fed #2H from a depth of 427' MD to a depth of 13938' MD. This data is true, correct, complete and within the limitations of the tools as set forth by Halliburton Energy Services, Inc. (aka Sperry Drilling). I am authorized and qualified to make this report and these surveys were conducted at the request of Chevron USA, Inc. for the well Rustler Bluff 34 24 29 Fed #2H, API No. 30-015-42671-0000 in Eddy County, New Mexico. I have reviewed this report and find that it conforms to the principles and procedures as set forth by Halliburton Energy Services, Inc. (aka Sperry Drilling).



K. Stolarski
Field Engineer
