

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

NM OIL CONSERVATION

ARTESIA DISTRICT

FORM APPROVED
OMB NO. 1004-0137
Expires: January 31, 2018**SUNDRY NOTICES AND REPORTS ON WELLS**
Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.

APR 18 2018

RECEIVED

SUBMIT IN TRIPLICATE - Other instructions on page 2

1. Type of Well <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other	5. Lease Serial No. NMNM147554-77018
2. Name of Operator MEWBOURNE OIL COMPANY	6. If Indian, Allottee or Tribe Name
3a. Address PO BOX 5270 HOBBS, NM 88241	7. If Unit or CA/Agreement, Name and/or No. 320703
3b. Location of Well (Footage, Sec., T., R., M., or Survey Description) Sec 6 T24S R29E Mer NMP NENE 10FNL 890FEL	8. Well Name and No. HARROUN TRUST 6 FED COM 1H
Contact: JACKIE LATHAN E-Mail: jlathan@mewbourne.com Carlsbad Field Office OCD Artesia Ph: 575-393-5905	9. API Well No. 30-025-42714
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) Sec 6 T24S R29E Mer NMP NENE 10FNL 890FEL	10. Field and Pool or Exploratory Area 42940
	11. County or Parish, State EDDY COUNTY, NM

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize <input type="checkbox"/> Deepen <input type="checkbox"/> Production (Start/Resume) <input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Reclamation <input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair <input type="checkbox"/> New Construction <input type="checkbox"/> Recomplete <input checked="" type="checkbox"/> Other
	<input type="checkbox"/> Change Plans <input type="checkbox"/> Plug and Abandon <input type="checkbox"/> Temporarily Abandon Change to Original APD
	<input type="checkbox"/> Convert to Injection <input type="checkbox"/> Plug Back <input type="checkbox"/> Water Disposal

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.

Mewbourne Oil Company has an approved APD for the above well. Mewbourne requests approval to make the following changes:

- 1) Change well name to Pecos Valley 6/7 W2AH Fed Com #2H. - 321207 - effective 4.1.2018
- 2) Change pool to 98220.
- 3) Change target zone to Wolfcamp & TVD to 10,927' ✓
- 4) Change BHL to 2310' FNL & 330' FEL, Sec 7.
- 5) Change csg depth and cement to suit new plan.
- 6) Change wellhead to multi-bowl type wellhead.
- 7) Change well type to gas ✓
- 8) Change spacing to 480 acres ✓

**SEE ATTACHED FOR
CONDITIONS OF APPROVAL**

14. I hereby certify that the foregoing is true and correct. Electronic Submission #403235 verified by the BLM Well Information System For MEWBOURNE OIL COMPANY, sent to the Carlsbad Committed to AFMSS for processing by PRISCILLA PEREZ on 02/06/2018 ()	
Name (Printed/Typed) ROBERT TALLEY	Title ENGINEER
Signature (Electronic Submission)	Date 02/05/2018
THIS SPACE FOR FEDERAL OR STATE OFFICE USE	
Approved By _____	Title PETROLEUM ENGINEER
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Date _____
Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.	Office BUREAU OF LAND MANAGEMENT CARLSBAD FIELD OFFICE

(Instructions on page 2)

**** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ****

NSP.

RW 4-18-18.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate District Office

APR 27 2018 AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION RECEIVED

¹ API Number 30-015-42714		² Pool Code 98220		³ Pool Name Purple Sage; Wolfcamp (Gas)	
⁴ Property Code 313284		⁵ Property Name PECOS VALLEY 6/7 W2AH FEDERAL COM			⁶ Well Number 2H
⁷ OGRID NO. 14744		⁸ Operator Name MEWBOURNE OIL COMPANY			⁹ Elevation


¹⁰ Surface Location

UL or lot no. 1	Section 6	Township 24S	Range 29E	Lot Idn	Feet from the 10	North/South line NORTH	Feet From the 890	East/West line EAST	County EDDY
--------------------	--------------	-----------------	--------------	---------	---------------------	---------------------------	----------------------	------------------------	----------------

¹¹ Bottom Hole Location If Different From Surface

UL or lot no. H	Section 7	Township 24S	Range 29E	Lot Idn	Feet from the 2310	North/South line NORTH	Feet from the 330	East/West line EAST	County EDDY
¹² Dedicated Acres 480		¹³ Joint or Infill		¹⁴ Consolidation Code		¹⁵ Order No.			

No allowable will be assigned to this completion until all interest have been consolidated or a non-standard unit has been approved by the division.

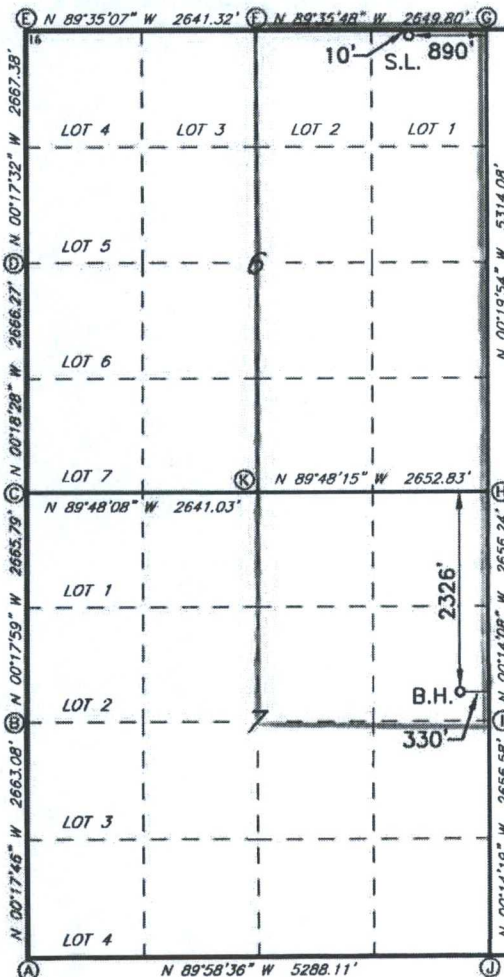

GEODETIC DATA
NAD 83 GRID - NM EAST
SURFACE LOCATION
N 456344.9 - E 638780.9
LAT: 32.2541742° N
LONG: 104.0181158° W
BOTTOM HOLE
N 448711.5 - E 639380.9
LAT: 32.2331862° N
LONG: 104.0162477° W

CORNER DATA
NAD 83 GRID - NM EAST
A: FOUND 1\" BAR
N 445726.4 - E 634436.4
B: FOUND BRASS CAP \"1942\"
N 448388.8 - E 634422.6
C: FOUND BRASS CAP \"1942\"
N 451054.0 - E 634408.7
D: FOUND BRASS CAP \"1942\"
N 453719.6 - E 634394.4
E: FOUND BRASS CAP \"1942\"
N 456386.4 - E 634380.8
F: FOUND 1/2\" REBAR
N 456367.3 - E 637021.4
G: FOUND 1/2\" REBAR
N 458348.8 - E 639670.8
H: FOUND BRASS CAP \"1942\"
N 451035.8 - E 639701.3
I: FOUND BRASS CAP \"1942\"
N 448380.2 - E 639712.3
J: FOUND BRASS CAP \"1942\"
N 445724.2 - E 639723.3
K: FOUND BRASS CAP \"1942\"
N 451044.9 - E 637049.1

¹⁷ OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Signature: Jackie Lathan Date: 4/19/18
Printed Name: Jackie Lathan

E-mail Address

¹⁸ SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

12-18-2017

Date of Survey

Signature and Seal of Professional Surveyor

19680
Certificate Number



Job No.: LS1712837

NSP required

Mewbourne Oil Company, Pecos Valley 6/7 W2AH Fed Com #2H
Sec 6, T24S, R29E
SL: 10' FNL & 890' FEL
BHL: 2310' FNL & 330' FEL

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Jt Tension	SF Body Tension
	From	To								
17.5"	0'	340'	13.375"	48	H40	STC	4.84	10.87	19.73	33.15
12.25"	0'	2635'	9.625"	36	J55	LTC	1.47	2.57	4.78	5.95
8.75"	0'	11229'	7"	26	HCP110	LTC	1.45	1.85	2.20	2.84
6.125"	10333'	18290'	4.5"	13.5	P110	LTC	1.88	2.18	3.15	3.93
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h
Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Is casing API approved? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Mewbourne Oil Company, Pecos Valley 6/7 W2AH Fed Com #2H

Sec 6, T24S, R29E

SL: 10' FNL & 890' FEL

BHL: 2310' FNL & 330' FEL

3. Cementing Program

Casing	# Sks	Wt. lb/ gal	Yld ft3/ sack	H ₂ O gal/ sk	500# Comp. Strength (hours)	Slurry Description
Surf.	100	12.5	2.12	11	10	Lead: Class C + Salt + Gel + Extender + LCM
	200	14.8	1.34	6.3	8	Tail: Class C + Retarder
Inter.	380	12.5	2.12	11	10	Lead: Class C + Salt + Gel + Extender + LCM
	200	14.8	1.34	6.3	8	Tail: Class C + Retarder
Prod. Stg 1	440	12.5	2.12	11	9	Lead: Class C + Gel + Retarder + Defoamer + Extender
	400	15.6	1.18	5.2	10	Tail: Class H + Retarder + Fluid Loss + Defoamer
ECP/DV Tool @ 3782'						
Prod. Stg 2	60	12.5	2.12	11	9	Lead: Class C + Gel + Retarder + Defoamer + Extender
	100	14.8	1.34	6.3	8	Tail: Class C + Retarder
Liner	325	11.2	2.97	18	16	Class C + Salt + Gel + Fluid Loss + Retarder + Dispersant + Defoamer + Anti-Settling Agent

A copy of cement test will be available on location at time of cement job providing pump times & compressive strengths.

Casing String	TOC	% Excess
Surface	0'	100%
Intermediate	0'	25%
Production	2435'	25%
Liner	10333'	25%

Mewbourne Oil Company, Pecos Valley 6/7 W2AH Fed Com #2H

Sec 6, T24S, R29E

SL: 10' FNL & 890' FEL

BHL: 2310' FNL & 330' FEL

4. Pressure Control Equipment

BOP installed and tested before drilling which hole?	Size?	System Rated WP	Type	✓	Tested to:
12-1/4"	13-5/8"	5M	Annular	X	2500#
			Blind Ram	X	5000#
			Pipe Ram	X	
			Double Ram		
			Other*		

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

X	Formation integrity test will be performed per Onshore Order #2. On exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
N	Are anchors required by manufacturer?
Y	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. • Provide description here: See attached schematic.

Mewbourne Oil Company, Pecos Valley 6/7 W2AH Fed Com #2H
Sec 6, T24S, R29E
SL: 10' FNL & 890' FEL
BHL: 2310' FNL & 330' FEL

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0'	340'	FW Gel	8.6-8.8	28-34	N/C
340'	2635'	Saturated Brine	10.0	28-34	N/C
2635'	10333'	Cut Brine	8.6-9.5	28-34	N/C
10333'	18290'	OBM	10.0-13.0	30-40	<10cc

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times. Mud wieght up to 13.0 ppg may be required for shale control. The highest mud weight needed to balance formation is expected to be 12.0 ppg.

What will be used to monitor the loss or gain of fluid?	Pason/PVT/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
X	Will run GR/CNL from KOP (10333') to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No Logs are planned based on well control or offset log information.
	Drill stem test? If yes, explain
	Coring? If yes, explain

Additional logs planned		Interval
X	Gamma Ray	10333' (KOP) to TD
	Density	
	CBL	
	Mud log	
	PEX	

Mewbourne Oil Company, Pecos Valley 6/7 W2AH Fed Com #2H
Sec 6, T24S, R29E
SL: 10' FNL & 890' FEL
BHL: 2310' FNL & 330' FEL

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	6448 psi
Abnormal Temperature	No

Mitigation measure for abnormal conditions. Describe. **Lost circulation material/sweeps/mud scavengers in surface hole.**

Hydrogen Sulfide (H2S) monitors will be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

<input type="checkbox"/>	H2S is present
X	H2S Plan attached

8. Other facets of operation

Is this a walking operation? If yes, describe.

Will be pre-setting casing? If yes, describe.

Attachments

☐ Directional Plan

☐ Other, describe

NM OIL CONSERVATION
ARTESIA DISTRICT

APR 18 2018

RECEIVED

Mewbourne Oil Company

Eddy County, New Mexico NAD 83

Pecos Valley 6/7 W2AH Fed Com #2H

Sec 6, T24S, R29E

SL: 10' FNL & 890' FEL, Sec 6

BHL: 2326' FNL & 330' FEL, Sec 7

Plan: Design #1

Standard Planning Report

13 December, 2017

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Pecos Valley 6/7 W2AH Fed Com #2H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2992.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 2992.0usft (Original Well Elev)
Site:	Pecos Valley 6/7 W2AH Fed Com #2H	North Reference:	Grid
Well:	Sec 6, T24S, R29E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 2326' FNL & 330' FEL, Sec 7		
Design:	Design #1		

Project	Eddy County, New Mexico NAD 83		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Pecos Valley 6/7 W2AH Fed Com #2H			
Site Position:		Northing:	456,345.00 usft	Latitude: 32° 15' 15.028 N
From:	Map	Easting:	638,781.00 usft	Longitude: 104° 1' 5.215 W
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "	Grid Convergence: 0.17 °

Well	Sec 6, T24S, R29E			
Well Position	+N/-S	0.0 usft	Northing:	456,345.00 usft
	+E/-W	0.0 usft	Easting:	638,781.00 usft
Position Uncertainty	0.0 usft		Wellhead Elevation:	2,992.0 usft
			Ground Level:	2,965.0 usft

Wellbore	BHL: 2326' FNL & 330' FEL, Sec 7				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	12/13/2017	6.99	59.98	47,942

Design	Design #1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	175.51

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,710.0	0.00	0.00	2,710.0	0.0	0.0	0.00	0.00	0.00	0.00	
3,002.1	4.38	90.41	3,001.8	-0.1	11.2	1.50	1.50	0.00	90.41	
10,041.1	4.38	90.41	10,020.3	-3.9	548.8	0.00	0.00	0.00	0.00	
10,333.2	0.00	0.00	10,312.0	-4.0	560.0	1.50	-1.50	0.00	180.00	KOP @ 10,312'
11,229.8	89.66	179.70	10,885.0	-573.6	563.0	10.00	10.00	0.00	179.70	
18,290.5	89.66	179.70	10,927.0	-7,634.0	600.0	0.00	0.00	0.00	0.00	BHL: 2326' FNL & 330'

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Pecos Valley 6/7 W2AH Fed Com #2H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2992.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 2992.0usft (Original Well Elev)
Site:	Pecos Valley 6/7 W2AH Fed Com #2H	North Reference:	Grid
Well:	Sec 6, T24S, R29E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 2326' FNL & 330' FEL, Sec 7		
Design:	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
SL: 10' FNL & 890' FEL, Sec 6									
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,710.0	0.00	0.00	2,710.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	1.35	90.41	2,800.0	0.0	1.1	0.1	1.50	1.50	0.00
2,900.0	2.85	90.41	2,899.9	0.0	4.7	0.4	1.50	1.50	0.00
3,000.0	4.35	90.41	2,999.7	-0.1	11.0	0.9	1.50	1.50	0.00
3,002.1	4.38	90.41	3,001.8	-0.1	11.2	1.0	1.50	1.50	0.00
3,100.0	4.38	90.41	3,099.4	-0.1	18.6	1.6	0.00	0.00	0.00
3,200.0	4.38	90.41	3,199.1	-0.2	26.3	2.2	0.00	0.00	0.00
3,300.0	4.38	90.41	3,298.8	-0.2	33.9	2.9	0.00	0.00	0.00
3,400.0	4.38	90.41	3,398.6	-0.3	41.6	3.6	0.00	0.00	0.00
3,500.0	4.38	90.41	3,498.3	-0.4	49.2	4.2	0.00	0.00	0.00
3,600.0	4.38	90.41	3,598.0	-0.4	56.8	4.9	0.00	0.00	0.00
3,700.0	4.38	90.41	3,697.7	-0.5	64.5	5.5	0.00	0.00	0.00
3,800.0	4.38	90.41	3,797.4	-0.5	72.1	6.2	0.00	0.00	0.00
3,900.0	4.38	90.41	3,897.1	-0.6	79.7	6.8	0.00	0.00	0.00
4,000.0	4.38	90.41	3,996.8	-0.6	87.4	7.5	0.00	0.00	0.00
4,100.0	4.38	90.41	4,096.5	-0.7	95.0	8.1	0.00	0.00	0.00
4,200.0	4.38	90.41	4,196.2	-0.7	102.7	8.8	0.00	0.00	0.00
4,300.0	4.38	90.41	4,295.9	-0.8	110.3	9.4	0.00	0.00	0.00
4,400.0	4.38	90.41	4,395.6	-0.8	117.9	10.1	0.00	0.00	0.00
4,500.0	4.38	90.41	4,495.3	-0.9	125.6	10.7	0.00	0.00	0.00
4,600.0	4.38	90.41	4,595.0	-1.0	133.2	11.4	0.00	0.00	0.00
4,700.0	4.38	90.41	4,694.8	-1.0	140.9	12.0	0.00	0.00	0.00
4,800.0	4.38	90.41	4,794.5	-1.1	148.5	12.7	0.00	0.00	0.00
4,900.0	4.38	90.41	4,894.2	-1.1	156.1	13.3	0.00	0.00	0.00
5,000.0	4.38	90.41	4,993.9	-1.2	163.8	14.0	0.00	0.00	0.00

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Pecos Valley 6/7 W2AH Fed Com #2H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2992.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 2992.0usft (Original Well Elev)
Site:	Pecos Valley 6/7 W2AH Fed Com #2H	North Reference:	Grid
Well:	Sec 6, T24S, R29E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 2326' FNL & 330' FEL, Sec 7		
Design:	Design #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,100.0	4.38	90.41	5,093.6	-1.2	171.4	14.7	0.00	0.00	0.00	
5,200.0	4.38	90.41	5,193.3	-1.3	179.1	15.3	0.00	0.00	0.00	
5,300.0	4.38	90.41	5,293.0	-1.3	186.7	16.0	0.00	0.00	0.00	
5,400.0	4.38	90.41	5,392.7	-1.4	194.3	16.6	0.00	0.00	0.00	
5,500.0	4.38	90.41	5,492.4	-1.4	202.0	17.3	0.00	0.00	0.00	
5,600.0	4.38	90.41	5,592.1	-1.5	209.6	17.9	0.00	0.00	0.00	
5,700.0	4.38	90.41	5,691.8	-1.6	217.2	18.6	0.00	0.00	0.00	
5,800.0	4.38	90.41	5,791.5	-1.6	224.9	19.2	0.00	0.00	0.00	
5,900.0	4.38	90.41	5,891.2	-1.7	232.5	19.9	0.00	0.00	0.00	
6,000.0	4.38	90.41	5,991.0	-1.7	240.2	20.5	0.00	0.00	0.00	
6,100.0	4.38	90.41	6,090.7	-1.8	247.8	21.2	0.00	0.00	0.00	
6,200.0	4.38	90.41	6,190.4	-1.8	255.4	21.8	0.00	0.00	0.00	
6,300.0	4.38	90.41	6,290.1	-1.9	263.1	22.5	0.00	0.00	0.00	
6,400.0	4.38	90.41	6,389.8	-1.9	270.7	23.1	0.00	0.00	0.00	
6,500.0	4.38	90.41	6,489.5	-2.0	278.4	23.8	0.00	0.00	0.00	
6,600.0	4.38	90.41	6,589.2	-2.0	286.0	24.4	0.00	0.00	0.00	
6,700.0	4.38	90.41	6,688.9	-2.1	293.6	25.1	0.00	0.00	0.00	
6,800.0	4.38	90.41	6,788.6	-2.2	301.3	25.8	0.00	0.00	0.00	
6,900.0	4.38	90.41	6,888.3	-2.2	308.9	26.4	0.00	0.00	0.00	
7,000.0	4.38	90.41	6,988.0	-2.3	316.5	27.1	0.00	0.00	0.00	
7,100.0	4.38	90.41	7,087.7	-2.3	324.2	27.7	0.00	0.00	0.00	
7,200.0	4.38	90.41	7,187.4	-2.4	331.8	28.4	0.00	0.00	0.00	
7,300.0	4.38	90.41	7,287.2	-2.4	339.5	29.0	0.00	0.00	0.00	
7,400.0	4.38	90.41	7,386.9	-2.5	347.1	29.7	0.00	0.00	0.00	
7,500.0	4.38	90.41	7,486.6	-2.5	354.7	30.3	0.00	0.00	0.00	
7,600.0	4.38	90.41	7,586.3	-2.6	362.4	31.0	0.00	0.00	0.00	
7,700.0	4.38	90.41	7,686.0	-2.6	370.0	31.6	0.00	0.00	0.00	
7,800.0	4.38	90.41	7,785.7	-2.7	377.7	32.3	0.00	0.00	0.00	
7,900.0	4.38	90.41	7,885.4	-2.8	385.3	32.9	0.00	0.00	0.00	
8,000.0	4.38	90.41	7,985.1	-2.8	392.9	33.6	0.00	0.00	0.00	
8,100.0	4.38	90.41	8,084.8	-2.9	400.6	34.2	0.00	0.00	0.00	
8,200.0	4.38	90.41	8,184.5	-2.9	408.2	34.9	0.00	0.00	0.00	
8,300.0	4.38	90.41	8,284.2	-3.0	415.8	35.5	0.00	0.00	0.00	
8,400.0	4.38	90.41	8,383.9	-3.0	423.5	36.2	0.00	0.00	0.00	
8,500.0	4.38	90.41	8,483.7	-3.1	431.1	36.9	0.00	0.00	0.00	
8,600.0	4.38	90.41	8,583.4	-3.1	438.8	37.5	0.00	0.00	0.00	
8,700.0	4.38	90.41	8,683.1	-3.2	446.4	38.2	0.00	0.00	0.00	
8,800.0	4.38	90.41	8,782.8	-3.2	454.0	38.8	0.00	0.00	0.00	
8,900.0	4.38	90.41	8,882.5	-3.3	461.7	39.5	0.00	0.00	0.00	
9,000.0	4.38	90.41	8,982.2	-3.4	469.3	40.1	0.00	0.00	0.00	
9,100.0	4.38	90.41	9,081.9	-3.4	477.0	40.8	0.00	0.00	0.00	
9,200.0	4.38	90.41	9,181.6	-3.5	484.6	41.4	0.00	0.00	0.00	
9,300.0	4.38	90.41	9,281.3	-3.5	492.2	42.1	0.00	0.00	0.00	
9,400.0	4.38	90.41	9,381.0	-3.6	499.9	42.7	0.00	0.00	0.00	
9,500.0	4.38	90.41	9,480.7	-3.6	507.5	43.4	0.00	0.00	0.00	
9,600.0	4.38	90.41	9,580.4	-3.7	515.1	44.0	0.00	0.00	0.00	
9,700.0	4.38	90.41	9,680.1	-3.7	522.8	44.7	0.00	0.00	0.00	
9,800.0	4.38	90.41	9,779.9	-3.8	530.4	45.3	0.00	0.00	0.00	
9,900.0	4.38	90.41	9,879.6	-3.8	538.1	46.0	0.00	0.00	0.00	
10,000.0	4.38	90.41	9,979.3	-3.9	545.7	46.6	0.00	0.00	0.00	
10,041.1	4.38	90.41	10,020.3	-3.9	548.8	46.9	0.00	0.00	0.00	
10,100.0	3.50	90.41	10,079.0	-3.9	552.9	47.3	1.50	-1.50	0.00	
10,200.0	2.00	90.41	10,178.9	-4.0	557.7	47.7	1.50	-1.50	0.00	
10,300.0	0.50	90.41	10,278.9	-4.0	559.9	47.9	1.50	-1.50	0.00	

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Pecos Valley 6/7 W2AH Fed Com #2H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2992.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 2992.0usft (Original Well Elev)
Site:	Pecos Valley 6/7 W2AH Fed Com #2H	North Reference:	Grid
Well:	Sec 6, T24S, R29E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 2326' FNL & 330' FEL, Sec 7		
Design:	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
10,333.2	0.00	0.00	10,312.0	-4.0	560.0	47.9	1.50	-1.50	0.00
KOP @ 10,312'									
10,400.0	6.68	179.70	10,378.7	-7.9	560.0	51.7	10.00	10.00	0.00
10,500.0	16.68	179.70	10,476.5	-28.1	560.1	71.9	10.00	10.00	0.00
10,600.0	26.68	179.70	10,569.3	-65.0	560.3	108.7	10.00	10.00	0.00
10,700.0	36.68	179.70	10,654.3	-117.5	560.6	161.0	10.00	10.00	0.00
10,800.0	46.68	179.70	10,728.9	-183.9	560.9	227.3	10.00	10.00	0.00
10,900.0	56.68	179.70	10,790.8	-262.2	561.4	305.4	10.00	10.00	0.00
10,982.3	64.91	179.70	10,831.0	-334.0	561.7	377.0	10.00	10.00	0.00
FTP: 330' FNL & 330' FEL, Sec 6									
11,000.0	66.68	179.70	10,838.2	-350.2	561.8	393.1	10.00	10.00	0.00
11,100.0	76.68	179.70	10,869.6	-445.0	562.3	487.7	10.00	10.00	0.00
11,200.0	86.68	179.70	10,884.0	-543.8	562.8	586.2	10.00	10.00	0.00
11,229.8	89.66	179.70	10,885.0	-573.6	563.0	615.9	9.98	9.98	0.00
LP: 580' FNL & 330' FEL, Sec 6									
11,300.0	89.66	179.70	10,885.4	-643.8	563.4	685.9	0.00	0.00	0.00
11,400.0	89.66	179.70	10,886.0	-743.8	563.9	785.7	0.00	0.00	0.00
11,500.0	89.66	179.70	10,886.6	-843.8	564.4	885.4	0.00	0.00	0.00
11,600.0	89.66	179.70	10,887.2	-943.8	564.9	985.1	0.00	0.00	0.00
11,700.0	89.66	179.70	10,887.8	-1,043.8	565.5	1,084.8	0.00	0.00	0.00
11,800.0	89.66	179.70	10,888.4	-1,143.7	566.0	1,184.6	0.00	0.00	0.00
11,900.0	89.66	179.70	10,889.0	-1,243.7	566.5	1,284.3	0.00	0.00	0.00
12,000.0	89.66	179.70	10,889.6	-1,343.7	567.0	1,384.0	0.00	0.00	0.00
12,100.0	89.66	179.70	10,890.2	-1,443.7	567.5	1,483.8	0.00	0.00	0.00
12,200.0	89.66	179.70	10,890.8	-1,543.7	568.1	1,583.5	0.00	0.00	0.00
12,300.0	89.66	179.70	10,891.4	-1,643.7	568.6	1,683.2	0.00	0.00	0.00
12,400.0	89.66	179.70	10,892.0	-1,743.7	569.1	1,783.0	0.00	0.00	0.00
12,500.0	89.66	179.70	10,892.6	-1,843.7	569.6	1,882.7	0.00	0.00	0.00
12,600.0	89.66	179.70	10,893.2	-1,943.7	570.2	1,982.4	0.00	0.00	0.00
12,700.0	89.66	179.70	10,893.7	-2,043.7	570.7	2,082.2	0.00	0.00	0.00
12,800.0	89.66	179.70	10,894.3	-2,143.7	571.2	2,181.9	0.00	0.00	0.00
12,900.0	89.66	179.70	10,894.9	-2,243.7	571.7	2,281.6	0.00	0.00	0.00
13,000.0	89.66	179.70	10,895.5	-2,343.7	572.3	2,381.3	0.00	0.00	0.00
13,100.0	89.66	179.70	10,896.1	-2,443.7	572.8	2,481.1	0.00	0.00	0.00
13,200.0	89.66	179.70	10,896.7	-2,543.7	573.3	2,580.8	0.00	0.00	0.00
13,300.0	89.66	179.70	10,897.3	-2,643.7	573.8	2,680.5	0.00	0.00	0.00
13,400.0	89.66	179.70	10,897.9	-2,743.7	574.4	2,780.3	0.00	0.00	0.00
13,500.0	89.66	179.70	10,898.5	-2,843.7	574.9	2,880.0	0.00	0.00	0.00
13,600.0	89.66	179.70	10,899.1	-2,943.7	575.4	2,979.7	0.00	0.00	0.00
13,700.0	89.66	179.70	10,899.7	-3,043.7	575.9	3,079.5	0.00	0.00	0.00
13,800.0	89.66	179.70	10,900.3	-3,143.7	576.5	3,179.2	0.00	0.00	0.00
13,900.0	89.66	179.70	10,900.9	-3,243.7	577.0	3,278.9	0.00	0.00	0.00
14,000.0	89.66	179.70	10,901.5	-3,343.7	577.5	3,378.7	0.00	0.00	0.00
14,100.0	89.66	179.70	10,902.1	-3,443.7	578.0	3,478.4	0.00	0.00	0.00
14,200.0	89.66	179.70	10,902.7	-3,543.7	578.6	3,578.1	0.00	0.00	0.00
14,300.0	89.66	179.70	10,903.3	-3,643.7	579.1	3,677.8	0.00	0.00	0.00
14,400.0	89.66	179.70	10,903.9	-3,743.7	579.6	3,777.6	0.00	0.00	0.00
14,500.0	89.66	179.70	10,904.5	-3,843.7	580.1	3,877.3	0.00	0.00	0.00
14,600.0	89.66	179.70	10,905.0	-3,943.7	580.7	3,977.0	0.00	0.00	0.00
14,700.0	89.66	179.70	10,905.6	-4,043.7	581.2	4,076.8	0.00	0.00	0.00
14,800.0	89.66	179.70	10,906.2	-4,143.7	581.7	4,176.5	0.00	0.00	0.00
14,900.0	89.66	179.70	10,906.8	-4,243.7	582.2	4,276.2	0.00	0.00	0.00
15,000.0	89.66	179.70	10,907.4	-4,343.6	582.8	4,376.0	0.00	0.00	0.00

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Pecos Valley 6/7 W2AH Fed Com #2H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2992.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 2992.0usft (Original Well Elev)
Site:	Pecos Valley 6/7 W2AH Fed Com #2H	North Reference:	Grid
Well:	Sec 6, T24S, R29E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 2326' FNL & 330' FEL, Sec 7		
Design:	Design #1		

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
15,100.0	89.66	179.70	10,908.0	-4,443.6	583.3	4,475.7	0.00	0.00	0.00
15,200.0	89.66	179.70	10,908.6	-4,543.6	583.8	4,575.4	0.00	0.00	0.00
15,300.0	89.66	179.70	10,909.2	-4,643.6	584.3	4,675.1	0.00	0.00	0.00
15,400.0	89.66	179.70	10,909.8	-4,743.6	584.8	4,774.9	0.00	0.00	0.00
15,500.0	89.66	179.70	10,910.4	-4,843.6	585.4	4,874.6	0.00	0.00	0.00
15,600.0	89.66	179.70	10,911.0	-4,943.6	585.9	4,974.3	0.00	0.00	0.00
15,700.0	89.66	179.70	10,911.6	-5,043.6	586.4	5,074.1	0.00	0.00	0.00
15,800.0	89.66	179.70	10,912.2	-5,143.6	586.9	5,173.8	0.00	0.00	0.00
15,900.0	89.66	179.70	10,912.8	-5,243.6	587.5	5,273.5	0.00	0.00	0.00
16,000.0	89.66	179.70	10,913.4	-5,343.6	588.0	5,373.3	0.00	0.00	0.00
16,100.0	89.66	179.70	10,914.0	-5,443.6	588.5	5,473.0	0.00	0.00	0.00
16,200.0	89.66	179.70	10,914.6	-5,543.6	589.0	5,572.7	0.00	0.00	0.00
16,300.0	89.66	179.70	10,915.2	-5,643.6	589.6	5,672.5	0.00	0.00	0.00
16,400.0	89.66	179.70	10,915.8	-5,743.6	590.1	5,772.2	0.00	0.00	0.00
16,500.0	89.66	179.70	10,916.3	-5,843.6	590.6	5,871.9	0.00	0.00	0.00
16,600.0	89.66	179.70	10,916.9	-5,943.6	591.1	5,971.6	0.00	0.00	0.00
16,700.0	89.66	179.70	10,917.5	-6,043.6	591.7	6,071.4	0.00	0.00	0.00
16,800.0	89.66	179.70	10,918.1	-6,143.6	592.2	6,171.1	0.00	0.00	0.00
16,900.0	89.66	179.70	10,918.7	-6,243.6	592.7	6,270.8	0.00	0.00	0.00
17,000.0	89.66	179.70	10,919.3	-6,343.6	593.2	6,370.6	0.00	0.00	0.00
17,100.0	89.66	179.70	10,919.9	-6,443.6	593.8	6,470.3	0.00	0.00	0.00
17,200.0	89.66	179.70	10,920.5	-6,543.6	594.3	6,570.0	0.00	0.00	0.00
17,300.0	89.66	179.70	10,921.1	-6,643.6	594.8	6,669.8	0.00	0.00	0.00
17,400.0	89.66	179.70	10,921.7	-6,743.6	595.3	6,769.5	0.00	0.00	0.00
17,500.0	89.66	179.70	10,922.3	-6,843.6	595.9	6,869.2	0.00	0.00	0.00
17,600.0	89.66	179.70	10,922.9	-6,943.6	596.4	6,968.9	0.00	0.00	0.00
17,700.0	89.66	179.70	10,923.5	-7,043.6	596.9	7,068.7	0.00	0.00	0.00
17,800.0	89.66	179.70	10,924.1	-7,143.6	597.4	7,168.4	0.00	0.00	0.00
17,900.0	89.66	179.70	10,924.7	-7,243.6	598.0	7,268.1	0.00	0.00	0.00
18,000.0	89.66	179.70	10,925.3	-7,343.6	598.5	7,367.9	0.00	0.00	0.00
18,100.0	89.66	179.70	10,925.9	-7,443.6	599.0	7,467.6	0.00	0.00	0.00
18,200.0	89.66	179.70	10,926.5	-7,543.5	599.5	7,567.3	0.00	0.00	0.00
18,290.5	89.66	179.70	10,927.0	-7,634.0	600.0	7,657.5	0.00	0.00	0.00



BHL: 2326' FNL & 330' FEL, Sec 7

Planning Report

Database:	Hobbs	Local Co-ordinate Reference:	Site Pecos Valley 6/7 W2AH Fed Com #2H
Company:	Mewbourne Oil Company	TVD Reference:	WELL @ 2992.0usft (Original Well Elev)
Project:	Eddy County, New Mexico NAD 83	MD Reference:	WELL @ 2992.0usft (Original Well Elev)
Site:	Pecos Valley 6/7 W2AH Fed Com #2H	North Reference:	Grid
Well:	Sec 6, T24S, R29E	Survey Calculation Method:	Minimum Curvature
Wellbore:	BHL: 2326' FNL & 330' FEL, Sec 7		
Design:	Design #1		

Design Targets									
Target Name	Dip Angle	Dip Dir.	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
- hit/miss target	(°)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)		
- Shape									
SL: 10' FNL & 890' FEL, - plan hits target center - Point	0.00	0.00	0.0	0.0	0.0	456,345.00	638,781.00	32° 15' 15.028 N	104° 1' 5.215 W
KOP @ 10,312' - plan hits target center - Point	0.00	0.00	10,312.0	-4.0	560.0	456,341.00	639,341.00	32° 15' 14.972 N	104° 0' 58.694 W
FTP: 330' FNL & 330' FE - plan hits target center - Point	0.00	0.00	10,830.9	-334.0	561.7	456,011.00	639,342.73	32° 15' 11.707 N	104° 0' 58.685 W
LP: 580' FNL & 330' FEL - plan hits target center - Point	0.00	0.00	10,885.0	-573.6	563.0	455,771.40	639,344.00	32° 15' 9.335 N	104° 0' 58.679 W
BHL: 2326' FNL & 330' F - plan hits target center - Point	0.00	0.00	10,927.0	-7,634.0	600.0	448,711.00	639,381.00	32° 13' 59.465 N	104° 0' 58.491 W

Pecos Valley 6/7 W2AH Fed Com

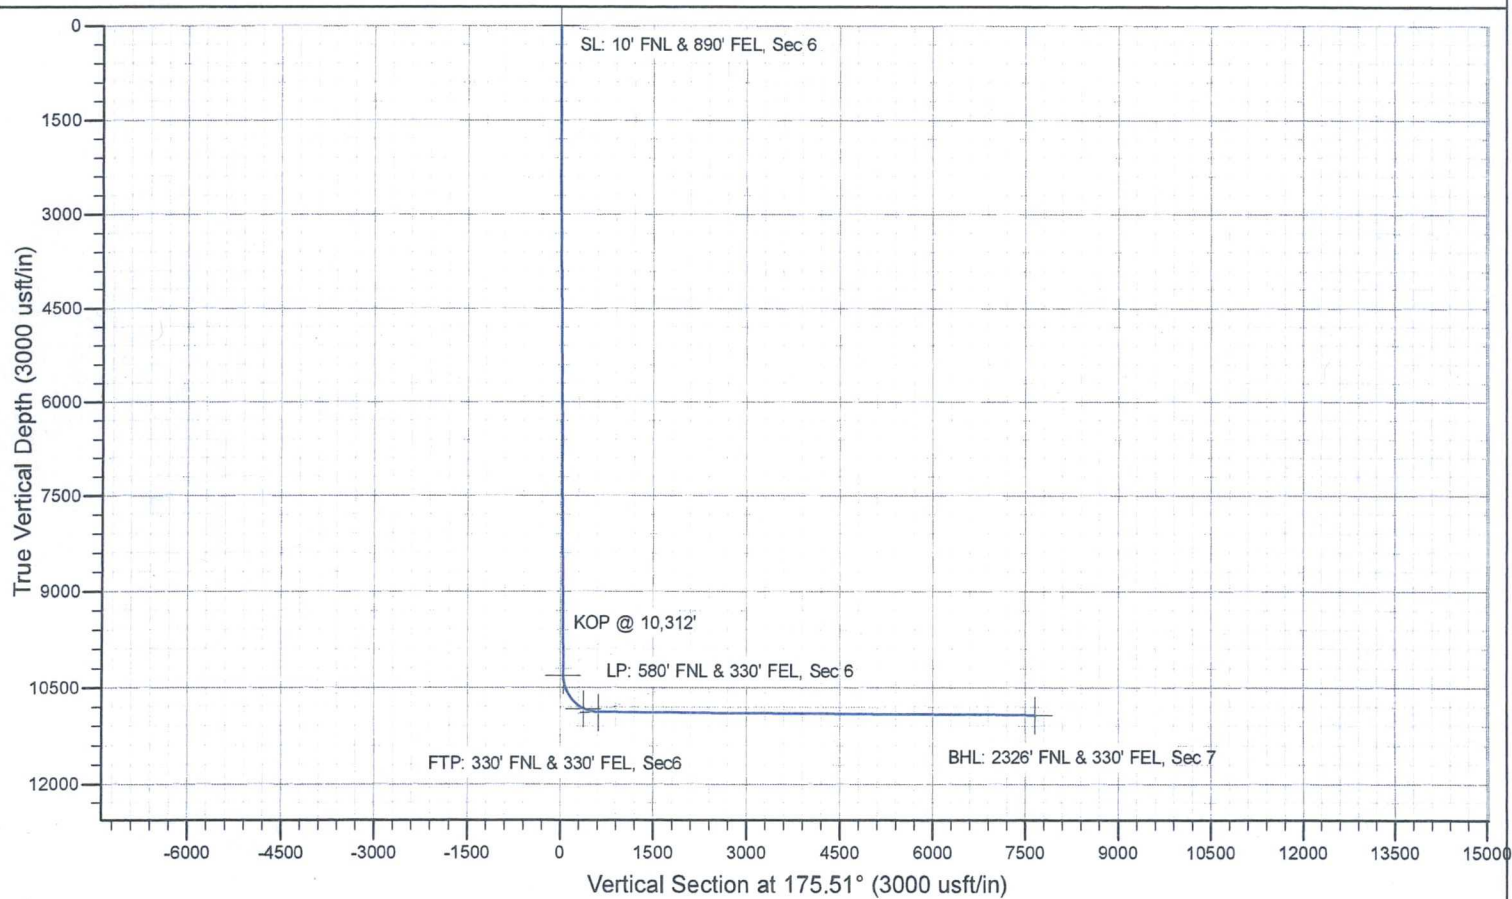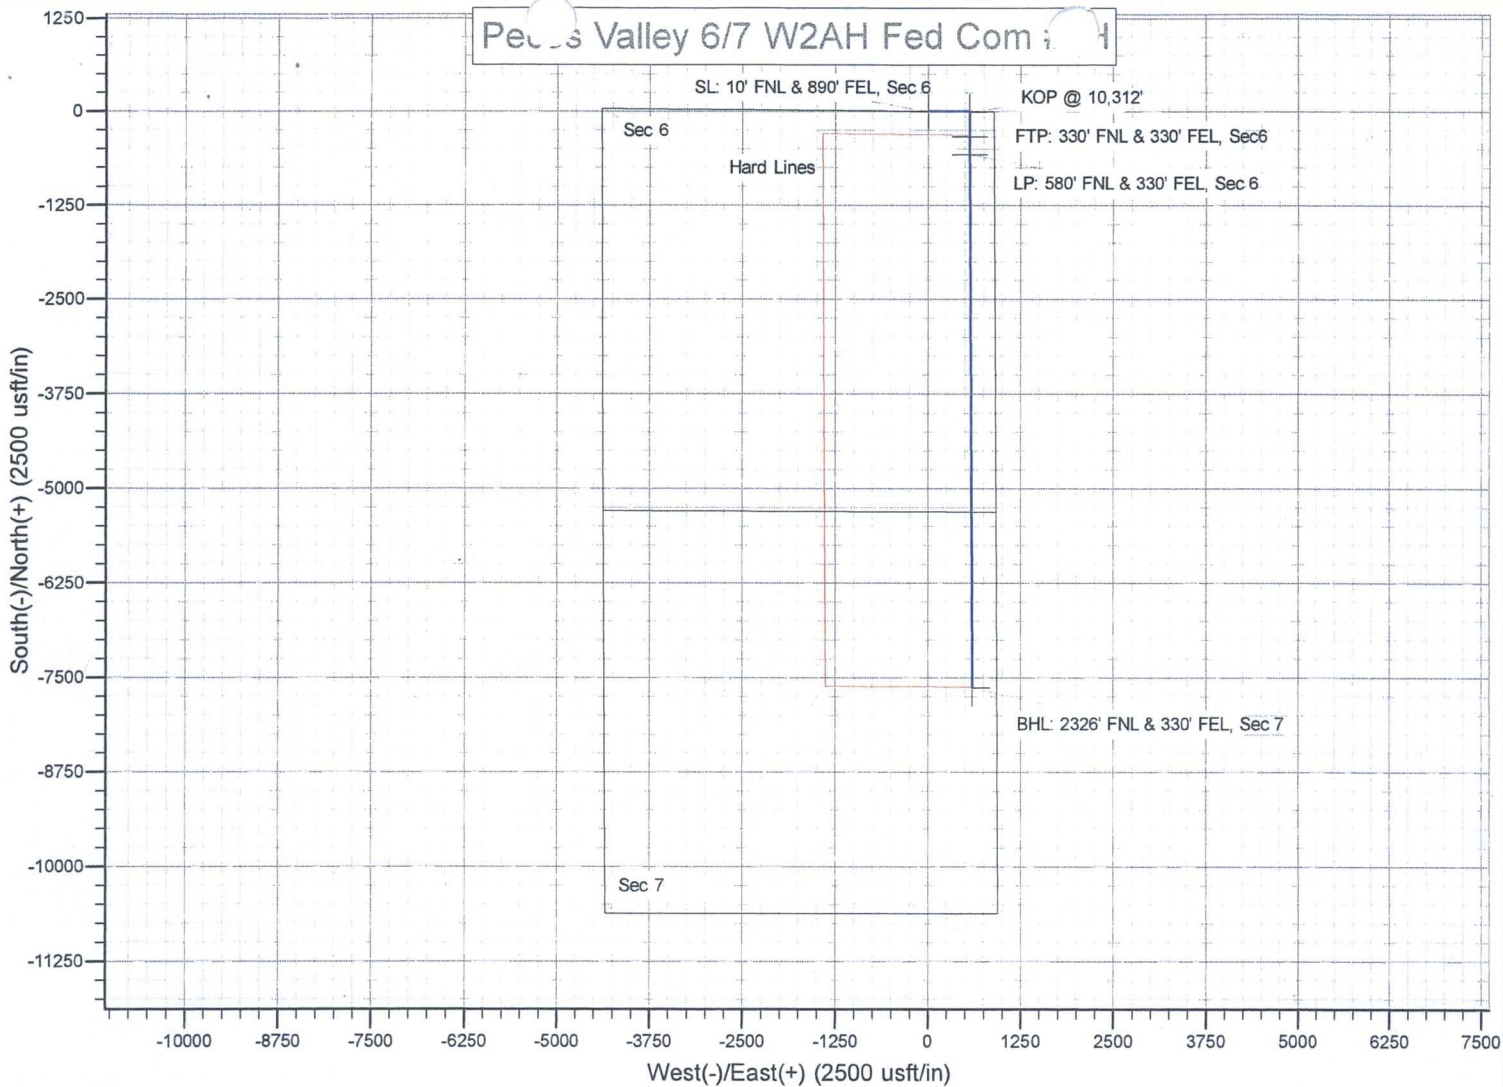

Hydril "GK"
13 5/8" 5M




Hydril "GK"


Cameron Type U
13 5/8" 5M



4 1/2" x 5 7/8" VBR




BLIND RAMS



MUD CROSS

H.C.R.





7" RAMS


13 5/8" 5M

13 5/8" 5M

13 5/8" 5M

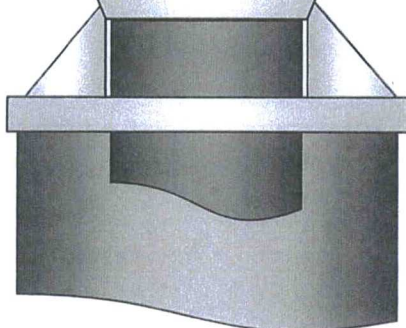

5M BOPE & Closed Loop Equipment Schematic

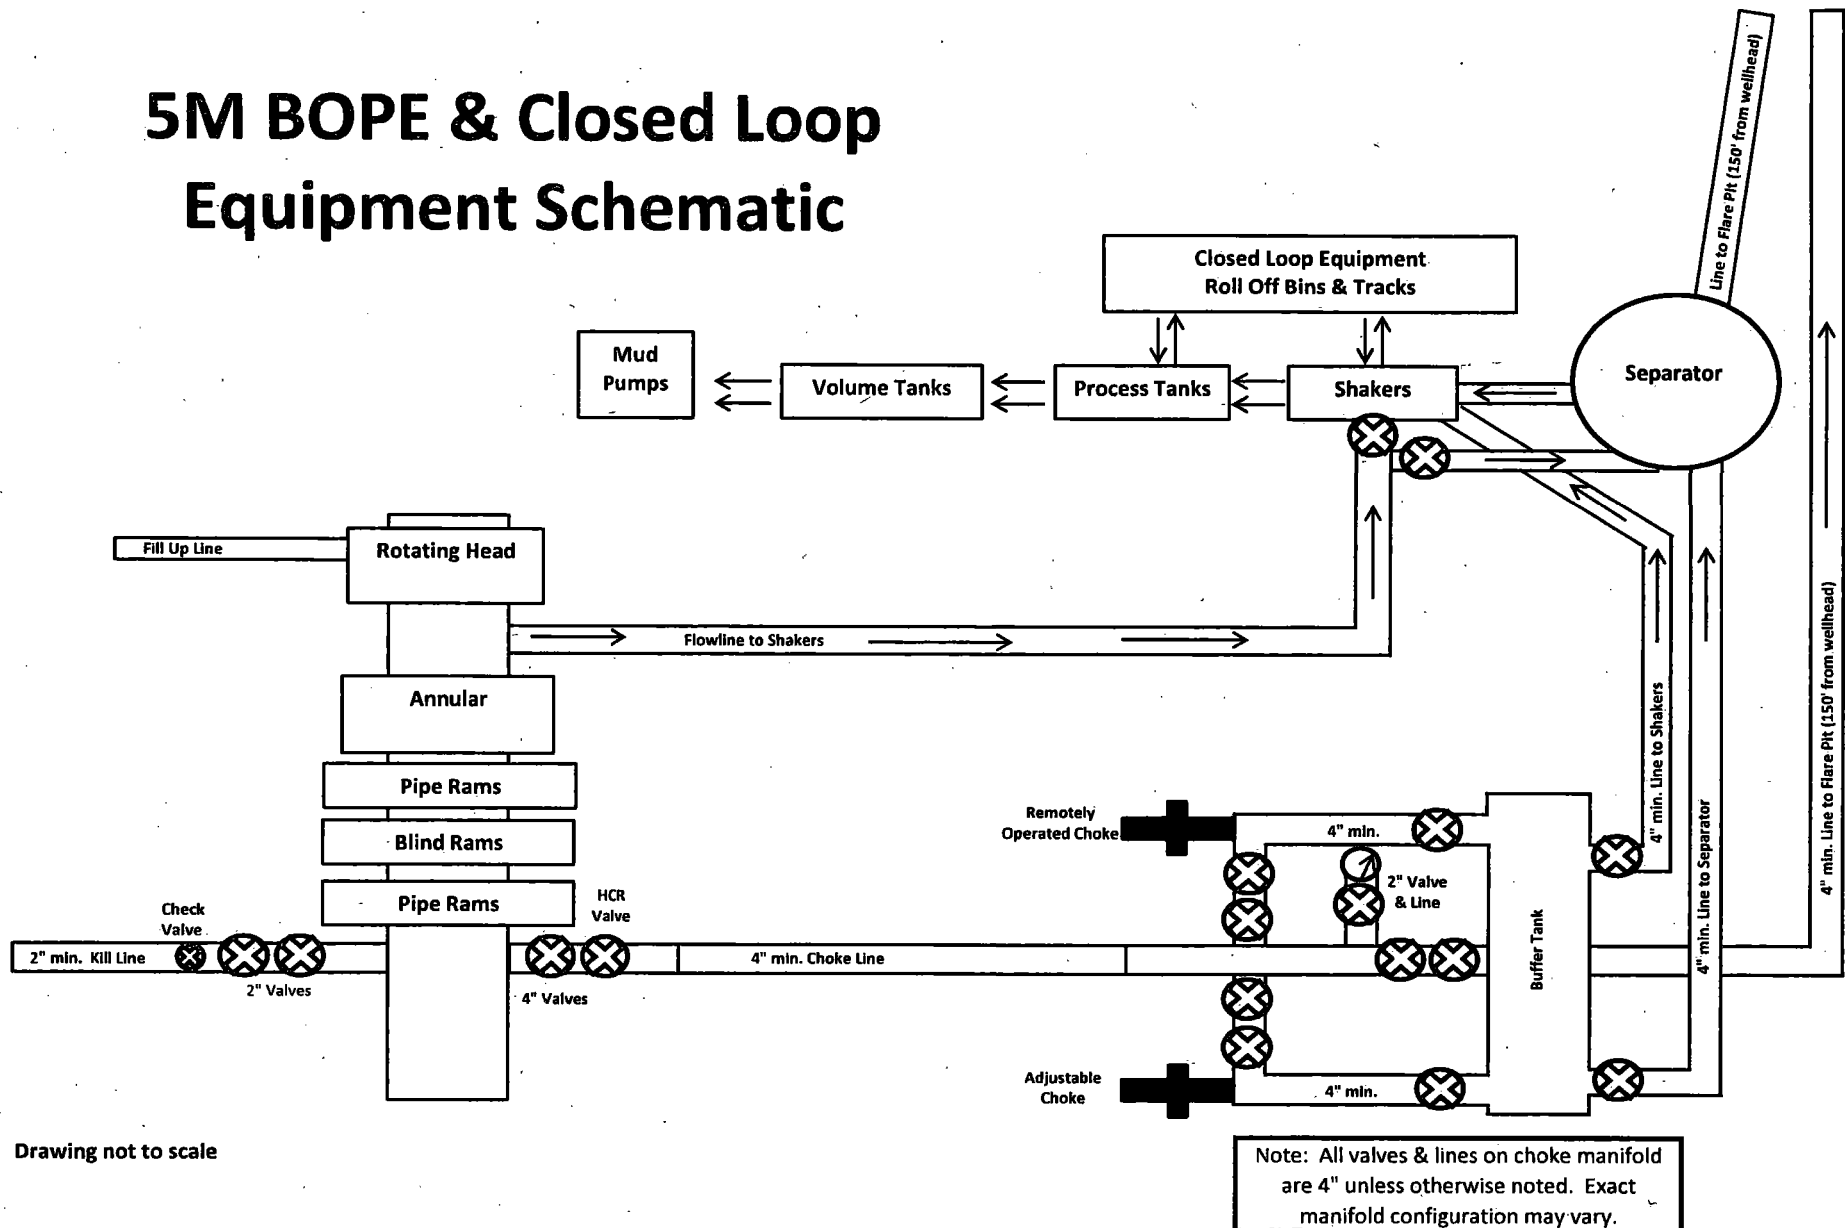



GATES E & S NORTH AMERICA, INC.
134 44TH STREET
CORPUS CHRISTI, TEXAS 78405

PHONE: 361-887-9807
FAX: 361-887-0812
EMAIL: Tim.Cantu@gates.com
WEB: www.gates.com

10K CEMENTING ASSEMBLY PRESSURE TEST CERTIFICATE

Customer :	AUSTIN DISTRIBUTING	Test Date:	4/30/2015
Customer Ref. :	4060578	Hose Serial No.:	D-043015-7
Invoice No. :	500506	Created By:	JUSTIN CROPPER
Product Description:	10K3.548.0CK4.1/1610KFLGE/E LE		
End Fitting 1 :	4 1/16 10K FLG	End Fitting 2 :	4 1/16 10K FLG
Gates Part No. :	4773-6290	Assembly Code :	L36554102914D-043015-7
Working Pressure :	10,000 PSI	Test Pressure :	15,000 PSI

Gates E & S North America, Inc. certifies that the following hose assembly has been tested to the Gates Oilfield Roughneck Agreement/Specification requirements and passed the 15 minute hydrostatic test per API Spec 7K/Q1, Fifth Edition, June 2010, Test pressure 9.6.7 and per Table 9 to 15,000 psi in accordance with this product number. Hose burst pressure 9.6.7.2 exceeds the minimum of 2.5 times the working pressure per Table 9.

Quality Manager :
Date :
Signature :


QUALITY
4/30/2015
<i>Justin Cropper</i>

Production:
Date :
Signature :

PRODUCTION
4/30/2015
<i>Justin Cropper</i>

Form PTC - 01 Rev.02



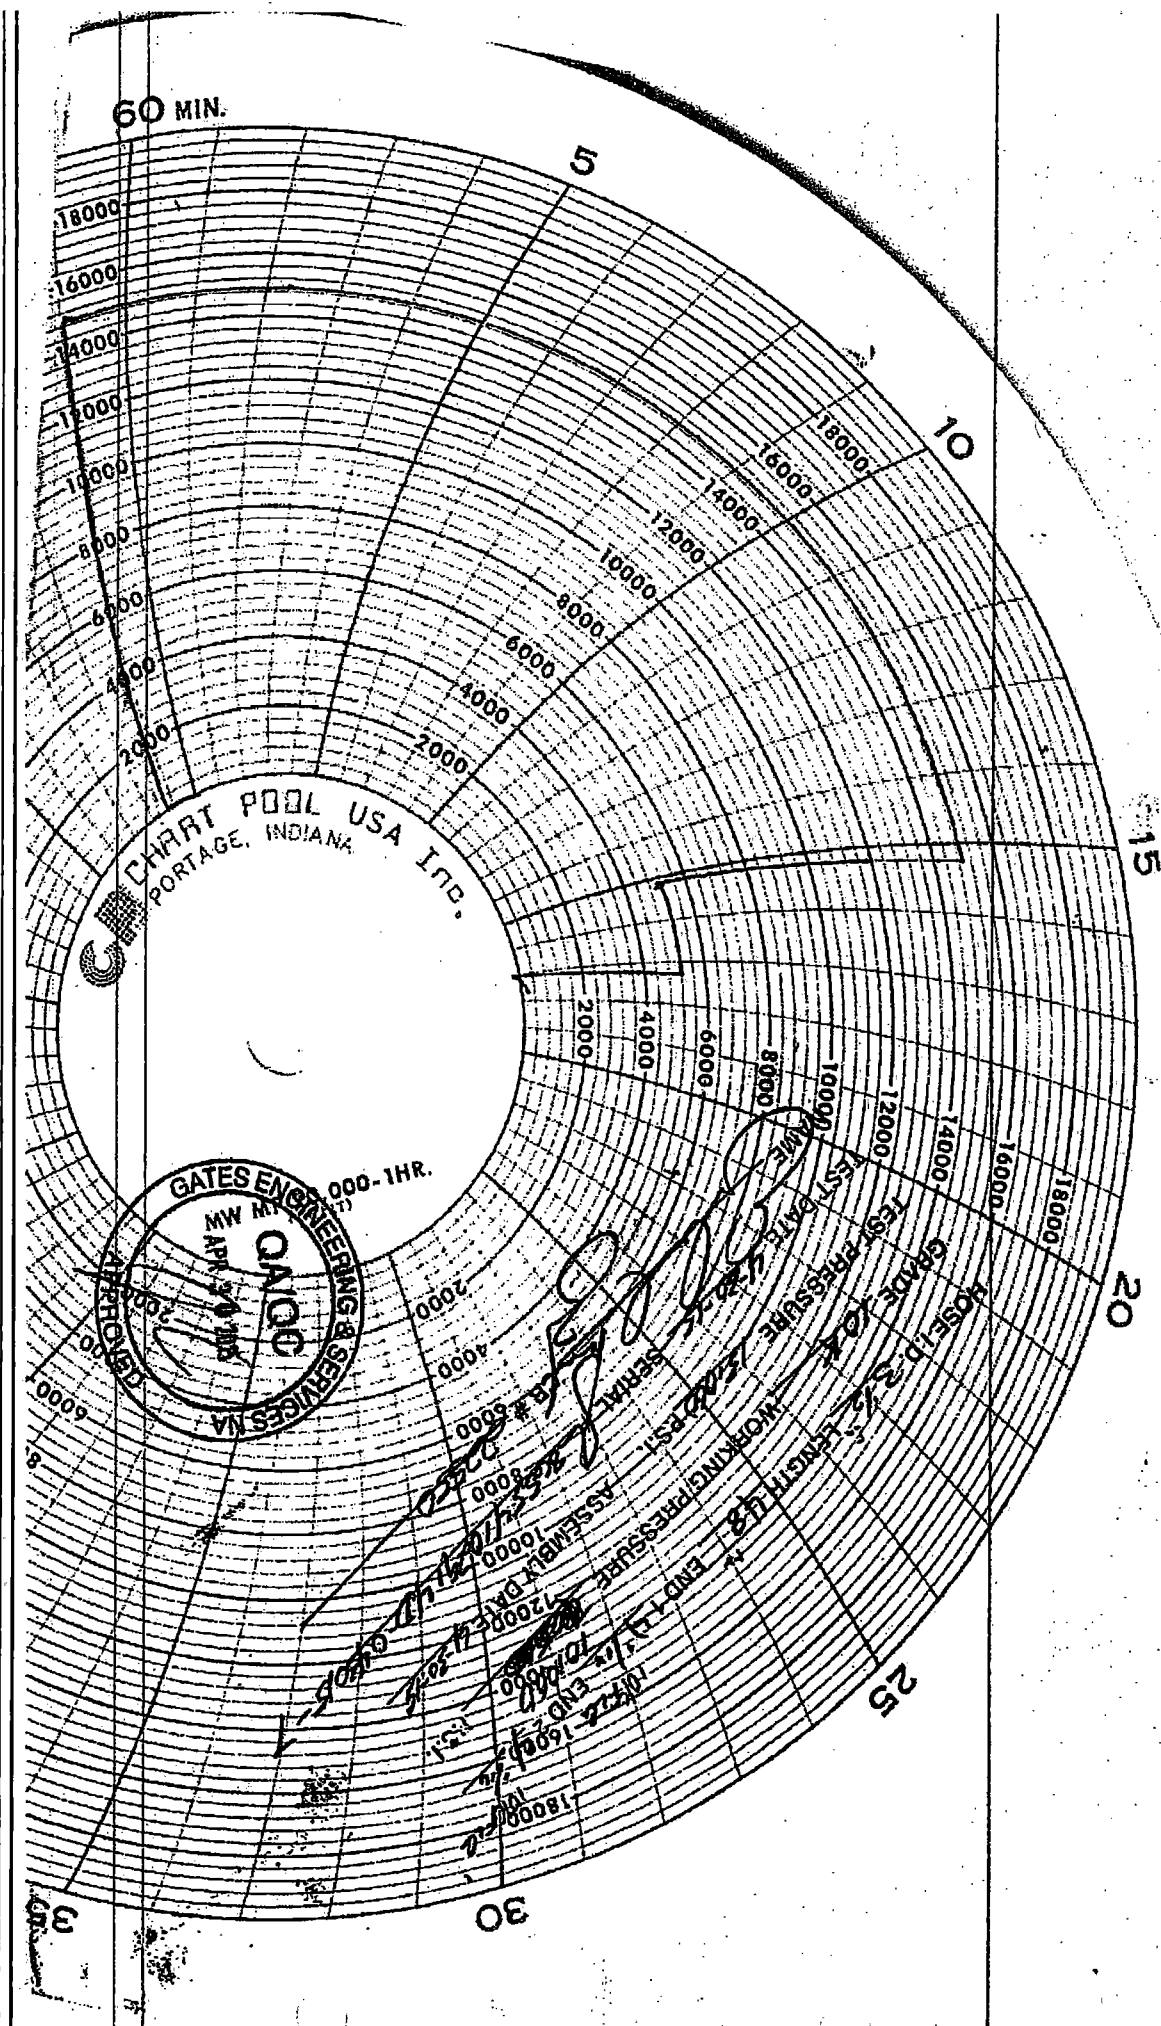

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

NM OIL CONSERVATION
ARTESIA DISTRICT

APR 18 2018

RECEIVED

OPERATOR'S NAME:	MEWBOURNE OIL CO
LEASE NO.:	NMNM77018
WELL NAME & NO.:	PECOS VALLEY 6/7 W2AH FED COM 2H
SURFACE HOLE FOOTAGE:	10' FNL & 890' FEL
BOTTOM HOLE FOOTAGE:	2310' FNL & 330' FEL
LOCATION:	Section 6, T. 24 S., R 29 E., NMPM
COUNTY:	Eddy County, New Mexico

COA

All previous COA still apply expect the following:

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input type="radio"/> Low	<input checked="" type="radio"/> Medium	<input type="radio"/> High
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP

A. Hydrogen Sulfide

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The 13-3/8 inch surface casing shall be set at approximately 340 feet (a minimum of 25 feet into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of 8 hours or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)

- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the 9-5/8 inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.

Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

 - ❖ In Medium Cave/Karst Areas if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
3. The minimum required fill of cement behind the 7 inch production casing is:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

 - a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job. **Additional cement maybe required. Excess calculates to 24%.**
 - b. Second stage above DV tool: Cement should tie-back at least 200 feet into previous casing string. Operator shall provide method of verification.
4. The minimum required fill of cement behind the 4-1/2 inch production liner is:
 - Cement should tie-back 100' into the previous casing. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
2. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Chaves and Roosevelt Counties

Call the Roswell Field Office, 2909 West Second St., Roswell NM 88201.

During office hours call (575) 627-0272.

After office hours call (575)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as

well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a

larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.

- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except, the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
- c. The tests shall be done by an independent service company utilizing a test plug. The results of the test shall be reported to the appropriate BLM office.
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes. This test shall be performed prior to the test at full stack pressure.
- g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Waste Minimization Plan (WMP)

In the interest of resource development, submission of additional well gas capture development plan information is deferred but may be required by the BLM Authorized Officer at a later date.

ZS 041118

Medium Cave Karst: two casing strings, both to circulate cement to surface.

13 3/8	surface csg in a	17 1/2	inch hole.	Design Factors			SURFACE	
Segment	#/ft	Grade	Coupling	Joint	Collapse	Burst	Length	
"A"	48.00	H 40	ST&C	19.73	4.95	1.26	340	
"B"							0	
w/8.4#/g mud, 30min Sfc Csg Test psig: 1,063			Tail Cmt	does	circ to sfc.	Totals:	340	
Comparison of Proposed to Minimum Required Cement Volumes								
Hole	Annular	1 Stage	1 Stage	Min	1 Stage	Drilling	Calc	Req'd
Size	Volume	Cmt Sx	CuFt Cmt	Cu Ft	% Excess	Mud Wt	MASP	BOPE
17 1/2	0.6946	300	480	291	65	8.80	789	2M

9 5/8	casing inside the	13 3/8	Design Factors				INTERMEDIATE	
Segment	#/ft	Grade	Coupling	Joint	Collapse	Burst	Length	
"A"	36.00	J 55	LT&C	4.78	1.48	0.66	2,635	
"B"							0	
w/8.4#/g mud, 30min Sfc Csg Test psig: 1,314						Totals:	2,635	
The cement volume(s) are intended to achieve a top of				0	ft from surface or a		340	
Hole	Annular	1 Stage	1 Stage	Min	1 Stage	Drilling	Calc	Req'd
Size	Volume	Cmt Sx	CuFt Cmt	Cu Ft	% Excess	Mud Wt	MASP	BOPE
12 1/4	0.3132	600	1100	866	27	10.00	2977	3M
Setting Depths for D V Tool(s):			2160				sum of sx	Σ CuFt
excess cmt by stage % :		119	59				880	1479
Class 'C' tail cmt yld > 1.35								
Burst Frac Gradient(s) for Segment(s): A, B, C, D = 1.34, b, c, d All > 0.70, OK.								

7	casing inside the		9 5/8	Design Factors			PRODUCTION	
Segment	#/ft	Grade	Coupling	Body	Collapse	Burst	Length	
"A"	26.00	HCP 110	LT&C	2.09	1.34	1.35	11,229	
"B"							0	
w/8.4#/g mud, 30min Sfc Csg Test psig: 2,395						Totals:	11,229	
A	Segment Design Factors would be:			2.93	1.45	if it were a vertical well		
No Pilot Hole Planned			MTD	Max VTD	Csg VD	Curve KOP	Dogleg°	Severity°
			11229	10885	10885	10333	90	10
The cement volume(s) are intended to achieve a top of				2435	ft from surface or a		200	
Hole	Annular	1 Stage	1 Stage	Min	1 Stage	Drilling	Calc	Req'd
Size	Volume	Cmt Sx	CuFt Cmt	Cu Ft	% Excess	Mud Wt	MASP	BOPE
8 3/4	0.1503	look ↘	0	1335		9.50	4975	5M
Setting Depths for D V Tool(s):			3782				sum of sx	Σ CuFt
% excess cmt by stage:			24	27			1000	1666
MASP is within 10% of 5000psig, need exrta equip?								

Tail cmt proposed for the csg below could overlap the previous csg shoe.

4 1/2	Liner w/top @ 10333				Design Factors		LINER	
Segment	#/ft	Grade	Coupling	Joint	Collapse	Burst	Length	
"A"	13.50	P 110	LT&C	2.39	1.34	1.68	896	
"B"	13.50	P 110	LT&C	2.50	1.45	1.68	7,061	
w/8.4#/g mud, 30min Sfc Csg Test psig: 2,404						Totals:	7,957	
A	Segment	Design	Factors	would be:	2.29	1.45	if it were a vertical wellbore	
No Pilot Hole Planned		MTD	Max VTD	Csg VD	Curve KOP	Dogleg°	Severity°	
		18290	10927	10927	10333	90	10	
The cement volume(s) are intended to achieve a top of					10333	ft from surface or a	896	
Hole	Annular	1 Stage	1 Stage	Min	1 Stage	Drilling	Calc	Req'd
Size	Volume	Cmt Sx	CuFt Cmt	Cu Ft	% Excess	Mud Wt	MASP	BOPE
6 1/8	0.0942	325	965	679	42	13.00		
Class 'H' tail cmt yld > 1.20				Capitan Reef est top XXXX.		MASP is within 10% of 5000psig, need		
