

RECEIVED

APR 24 2019

Form 3160-3  
(June 2015)FORM APPROVED  
OMB No. 1004-0137  
Expires: January 31, 2018UNITED STATES DISTRICT II-ARTESIA O.C.D.  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

## APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☒ DRILL ☐ REENTER  
 1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other  
 1c. Type of Completion: ☐ Hydraulic Fracturing ☒ Single Zone ☐ Multiple Zone

5. Lease Serial No.  
NMNM0544986

6. If Indian, Allottee or Tribe Name

7. If Unit or CA Agreement, Name and No.

8. Lease Name and Well No.

TODD 36-25 STATE FED COM  
235H 325/417

9. API Well No.

6137 30-015-45910

2. Name of Operator

DEVON ENERGY PRODUCTION COMPANY LP

3a. Address

333 West Sheridan Avenue Oklahoma City OK 73102

3b. Phone No. (include area code)

(800)583-3866

10. Field and Pool, or Exploratory

Wildcat

SAND. Dunes BSPG 53805

4. Location of Well (Report location clearly and in accordance with any State requirements. \*)

At surface SWSE / 330 FSL / 1636 FEL / LAT 32.254575 / LONG -103.7282716

At proposed prod. zone NENE / 20 FNL / 400 FEL / LAT 32.2826299 / LONG -103.7242618

11. Sec., T., R., M. or Blk. and Survey or Area  
SEC 36, T23S, R31E / NMP

14. Distance in miles and direction from nearest town or post office\*

12. County or Parish  
EDDY13. State  
NM15. Distance from proposed\*  
location to nearest  
property or lease line, ft.  
(Also to nearest drig. unit line, if any)

330 feet

16. No of acres in lease

600

17. Spacing, Unit dedicated to this well

320

18. Distance from proposed location\*  
to nearest well, drilling, completed,  
applied for, on this lease, ft.

5950 feet

19. Proposed Depth

10570 feet / 20908 feet

20. BLM/BIA Bond No. in file

FED: CO1104

21. Elevations (Show whether DF, KDB, RT, GL, etc.)  
3508 feet22. Approximate date work will start\*  
06/24/201923. Estimated duration  
30 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

1. Well plat certified by a registered surveyor.

2. A Drilling Plan.

3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).

4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).

5. Operator certification.

6. Such other site specific information and/or plans as may be requested by the BLM.

25. Signature  
(Electronic Submission)

Name (Printed/Typed)

Jenny Harms / Ph: (405)552-6560

Date

10/10/2018

Title

Regulatory Compliance Professional

Approved by (Signature)  
(Electronic Submission)

Name (Printed/Typed)

Cody Layton / Ph: (575)234-5959

Date

04/18/2019

Title

Assistant Field Manager Lands &amp; Minerals

Office

CARLSBAD

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

APPROVED WITH CONDITIONS

(Continued on page 2)

\*(Instructions on page 2)

Approval Date: 04/18/2019

KUP 4-24-19



## INSTRUCTIONS

**GENERAL:** This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

**ITEM 1:** If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

**ITEM 4:** Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

**ITEM 14:** Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

**ITEMS 15 AND 18:** If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

**ITEM 22:** Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

**ITEM 24:** If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

## NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

**AUTHORITY:** 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

**PRINCIPAL PURPOSES:** The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

**ROUTINE USE:** Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

**EFFECT OF NOT PROVIDING INFORMATION:** Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

**BURDEN HOURS STATEMENT:** Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.



## Additional Operator Remarks

### Location of Well

1. SHL: SWSE / 330 FSL / 1636 FEL / TWSP: 23S / RANGE: 31E / SECTION: 36 / LAT: 32.254575 / LONG: -103.7282716 ( TVD: 0 feet, MD: 0 feet )  
PPP: SESE / 100 FSL / 400 FEL / TWSP: 23S / RANGE: 31E / SECTION: 36 / LAT: 32.2539422 / LONG: -103.7242735 ( TVD: 10203 feet, MD: 10306 feet )  
BHL: NENE / 20 FNL / 400 FEL / TWSP: 23S / RANGE: 31E / SECTION: 25 / LAT: 32.2826299 / LONG: -103.7242618 ( TVD: 10570 feet, MD: 20908 feet )

### BLM Point of Contact

Name: Candy Vigil

Title: Admin Support Assistant

Phone: 5752345982

Email: cvigil@blm.gov

CONFIDENTIAL



### **Review and Appeal Rights**

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL



## PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

<b>OPERATOR'S NAME:</b>	Devon Energy Production Company LP
<b>LEASE NO.:</b>	Todd 36-25 State Fed Com 235H
<b>WELL NAME &amp; NO.:</b>	330'S & 1636'E
<b>SURFACE HOLE FOOTAGE:</b>	20'/N & 400'E
<b>BOTTOM HOLE FOOTAGE</b>	Section 36, T.23 S., R.31 E., NMPM
<b>LOCATION:</b>	Eddy County, New Mexico
<b>COUNTY:</b>	Devon Energy Production Company LP

COA

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input type="radio"/> None	<input checked="" type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input type="radio"/> Multibowl	<input checked="" type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input checked="" type="checkbox"/> Fluid Filled	<input checked="" type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit

### A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

### B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **837 feet** (a minimum of 25 feet into the Rustler Anhydrite and above the salt) and cemented to the surface.
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **24 hours in the Potash Area** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)



- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

**Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.**

- 2. The minimum required fill of cement behind the 9-5/8 inch intermediate casing shall be set at approximately **4490 feet** is:

**Option 1 (Single Stage):**

- Cement to surface. If cement does not circulate see B.1.a, c-d above.  
**Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.**

**Option 2:**

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
- b. Second stage above DV tool:
  - Cement to surface. If cement does not circulate, contact the appropriate BLM office.  
**Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.**

**Operator has proposed to pump down 13-3/8" X 9-5/8" annulus. Operator must run a CBL from TD of the 9-5/8" casing to surface. Submit results to BLM.**

- 3. The minimum required fill of cement behind the 5-1/2 inch production casing is:
  - Cement should tie-back at least **500 feet** into previous casing string. Operator shall provide method of verification.  
**Cement excess is less than 25%, more cement might be required.**



### **C. PRESSURE CONTROL**

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
- 2.

#### **Option 1:**

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **5000 (5M)** psi.

#### **Option 2:**

1. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
  - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

### **D. SPECIAL REQUIREMENT (S)**

#### **Communitization Agreement**

- The operator will submit a Communitization Agreement to the Carlsbad Field Office, 620 E Greene St. Carlsbad, New Mexico 88220, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases



subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.

- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.



## GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Chaves and Roosevelt Counties

Call the Roswell Field Office, 2909 West Second St., Roswell NM 88201.  
During office hours call (575) 627-0272.  
After office hours call (575)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,  
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)  
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig
    - Notify the BLM when moving in and removing the Spudder Rig.
    - Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
    - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.



3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.



8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

**B. PRESSURE CONTROL**

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
  - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
  - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the



plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time.
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

#### C. DRILLING MUD



Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

**D. WASTE MATERIAL AND FLUIDS**

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.



**PECOS DISTRICT  
SURFACE USE  
CONDITIONS OF APPROVAL**

OPERATOR'S NAME:	Devon Energy Production Company LP
WELL NAME & NO.:	Todd 36-25 State Fed Com 235H
SURFACE HOLE FOOTAGE:	330'/S & 1636'/E
BOTTOM HOLE FOOTAGE	20'/N & 400'/E
LOCATION:	Section 36, T.23 S., R.31 E., NMPM
COUNTY:	Eddy County, New Mexico

**TABLE OF CONTENTS**

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
  - Lesser Prairie-Chicken Timing Stipulations
  - Ground-level Abandoned Well Marker
  - Range
- ☐ **Construction**
  - Notification
  - Topsoil
  - Closed Loop System
  - Federal Mineral Material Pits
  - Well Pads
  - Roads
- ☐ **Road Section Diagram**
- ☒ **Production (Post Drilling)**
  - Well Structures & Facilities
  - Pipelines
  - Electric Lines
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**



## **I. GENERAL PROVISIONS**

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

## **II. PERMIT EXPIRATION**

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

## **III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES**

Any cultural and/or paleontological resource discovered by the operator or by any person working on the operator's behalf shall immediately report such findings to the Authorized Officer. The operator is fully accountable for the actions of their contractors and subcontractors. The operator shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery shall be made by the Authorized Officer to determine the appropriate actions that shall be required to prevent the loss of significant cultural or scientific values of the discovery. The operator shall be held responsible for the cost of the proper mitigation measures that the Authorized Officer assesses after consultation with the operator on the evaluation and decisions of the discovery. Any unauthorized collection or disturbance of cultural or paleontological resources may result in a shutdown order by the Authorized Officer.

## **IV. NOXIOUS WEEDS**

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.



## V. SPECIAL REQUIREMENT(S)

In May 2008, the Pecos District Special Status Species Resource Management Plan Amendment (RMPA) was approved and is being implemented. In addition to the standard practices that minimize impacts, as listed above, the following COA will apply:

- Timing Limitation Stipulation / Condition of Approval for lesser prairie-chicken, to minimize noise associated impacts which could disrupt breeding and nesting activities.
- Upon abandonment, a low profile abandoned well marker will be installed to prevent raptor perching.
- Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006. The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all power line structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. The holder without liability or expense shall make such modifications and/or additions to the United States.

### Livestock Watering Requirement

Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

### Fence Requirement

Where entry is granted across a fence line, the fence must be braced and tied off on both sides of the passageway with H-braces prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fence(s).

The operator must contact the allotment holder prior to construction to identify the location of the pipeline. The operator must take measures to protect the pipeline from compression or other damages. If the pipeline is damaged or compromised in any way near the proposed project as a result of oil and gas activity, the operator is responsible for repairing the pipeline immediately. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

During construction, the proponent shall minimize disturbance to existing fences, water lines, troughs, windmills, and other improvements on public lands. The proponent is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the grazing permittee/allottee prior to disturbing any range improvement projects. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

Lessees must comply with the 2012 Secretarial Potash Order. The Order is designed to manage the efficient development of oil, gas, and potash resources. Section 6 of the Order provides



general provisions which must be followed to minimize conflict between the industries and ensure the safety of operations.

To minimize impacts to potash resources, the proposed well is confined within the boundaries of the established Todd 36-25's Drill Island (See Potash Memo and Map in attached file for Drill Island description).



## **VI. CONSTRUCTION**

### **A. NOTIFICATION**

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

### **B. TOPSOIL**

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

### **C. CLOSED LOOP SYSTEM**

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

### **D. FEDERAL MINERAL MATERIALS PIT**

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

### **E. WELL PAD SURFACING**

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

### **F. EXCLOSURE FENCING (CELLARS & PITS)**



**Exclosure Fencing**

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

**G. ON LEASE ACCESS ROADS****Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

**Surfacing**

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

**Crowning**

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

**Ditching**

Ditching shall be required on both sides of the road.

**Turnouts**

Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.


**Drainage**



Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outslowing and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

#### **Cross Section of a Typical Lead-off Ditch**



All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

#### **Formula for Spacing Interval of Lead-off Ditches**

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

#### **Cattle guards**

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

#### **Fence Requirement**

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

#### **Public Access**

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.



### Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes

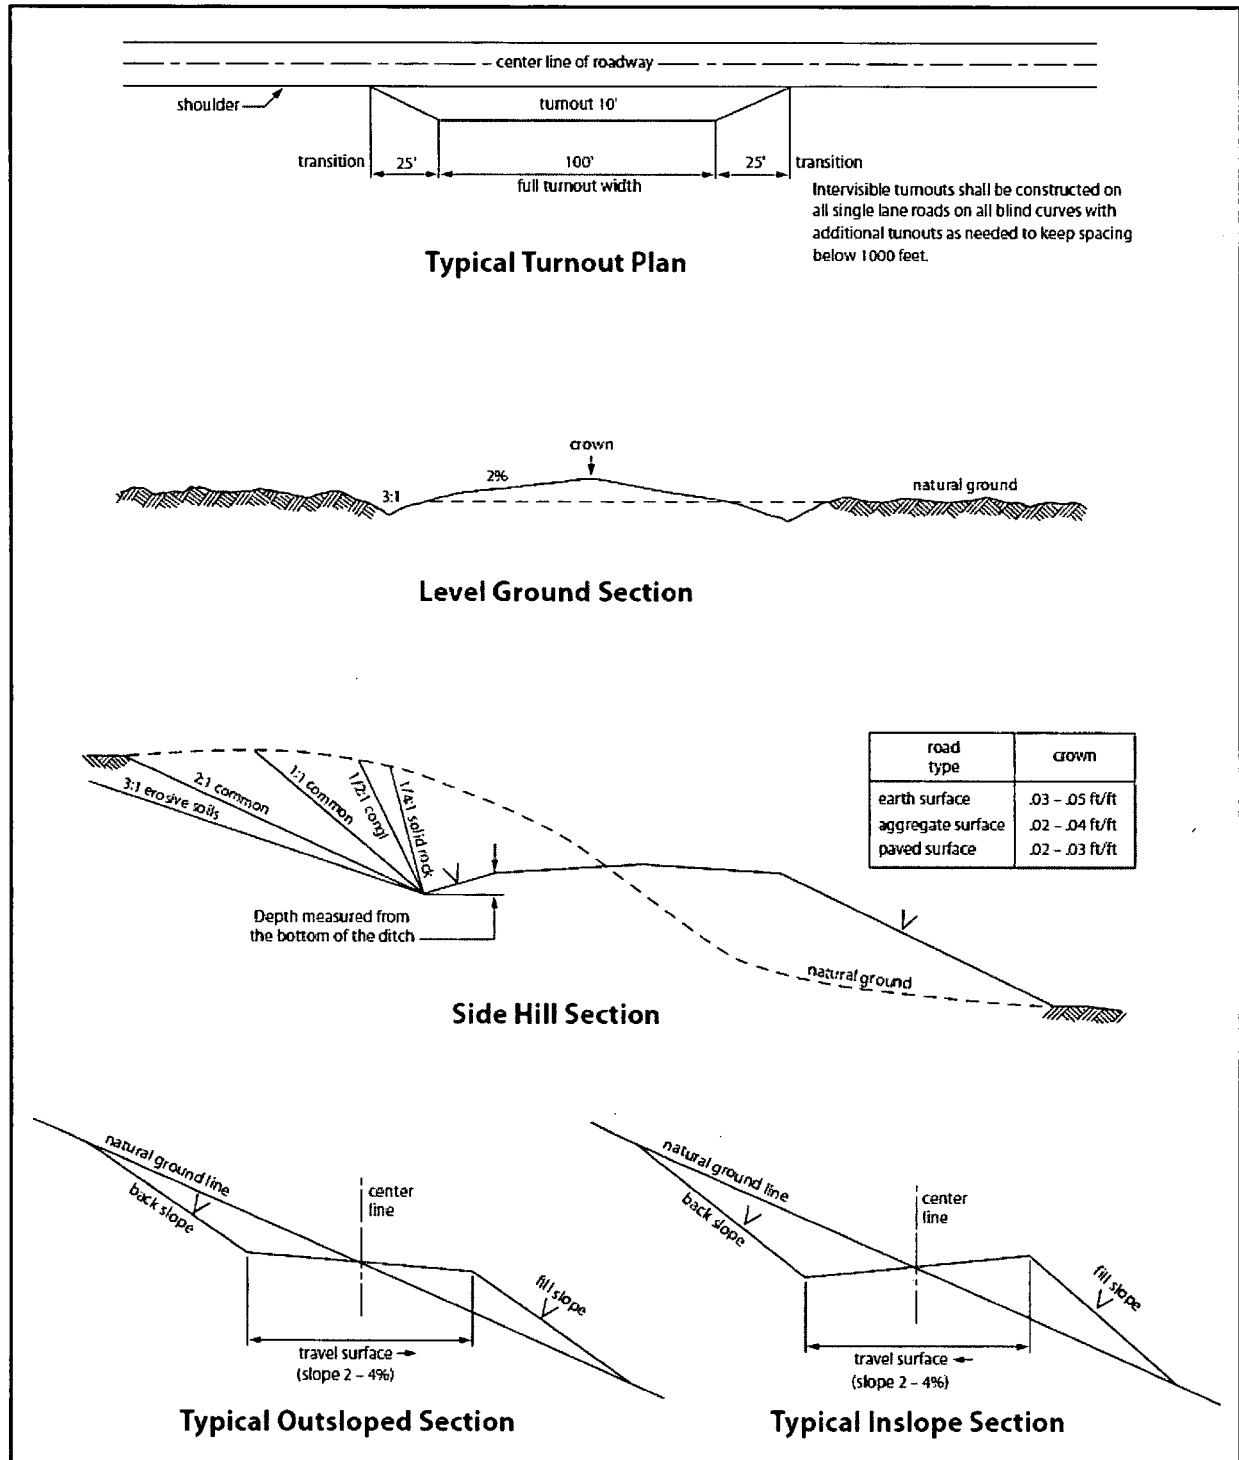


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.



## **VII. PRODUCTION (POST DRILLING)**

### **A. WELL STRUCTURES & FACILITIES**

#### **Placement of Production Facilities**

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

#### **Exclosure Netting (Open-top Tanks)**

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

#### **Chemical and Fuel Secondary Containment and Exclosure Screening**

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

#### **Open-Vent Exhaust Stack Exclosures**

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

#### **Containment Structures**

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus



freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

#### **Painting Requirement**

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

#### **STANDARD STIPULATIONS FOR OIL AND GAS RELATED SITES**

A copy of the application (Grant/Sundry Notice) and attachments, including stipulations and map, will be on location during construction. BLM personnel may request to view a copy of your permit during construction to ensure compliance with all stipulations.

The holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer, BLM.

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant and for all response costs, penalties, damages, claims, and other costs arising from the provisions of the Resource Conservation and Recovery Act (RCRA), 42 U.S.C. Chap. 82, Section 6901 et. seq., from the Comprehensive Environmental Response, Compensation and Liability Act (CERCLA), 42 U.S.C. Chap. 109, Section 9601 et. seq., and from other applicable environmental statutes.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976, as amended (15 U.S.C. 2601, et. seq.) with regard to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized by this grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation and Liability Act, Section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the Authorized Officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et. seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et. seq.) on the right-of-way (unless the release or threatened release is wholly unrelated to the right-of-way holder's activity on the right-of-way). This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.



4. If, during any phase of the construction, operation, maintenance, or termination of the site or related pipeline(s), any oil or other pollutant should be discharged from site facilities, the pipeline(s) or from containers or vehicles impacting Federal lands, the control and total removal, disposal, and cleanup of such oil or other pollutant, wherever found, shall be the responsibility of the holder, regardless of fault. Upon failure of the holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages to Federal lands resulting therefrom, the Authorized Officer may take such measures as deemed necessary to control and cleanup the discharge and restore the area, including, where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve the holder of any liability or responsibility.
5. Sites shall be maintained in an orderly, sanitary condition at all times. Waste materials, both liquid and solid, shall be disposed of promptly at an appropriate, authorized waste disposal facility in accordance with all applicable State and Federal laws. "Waste" means all discarded matter including, but not limited to, human waste, trash, garbage, refuse, petroleum products, brines, chemicals, oil drums, ashes, and equipment.
6. The operator will notify the Bureau of Land Management (BLM) authorized officer and nearest Fish and Wildlife Service (FWS) Law Enforcement office within 24 hours, if the operator discovers a dead or injured federally protected species (i.e., migratory bird species, bald or golden eagle, or species listed by the FWS as threatened or endangered) in or adjacent to a pit, trench, tank, exhaust stack, or fence. (If the operator is unable to contact the FWS Law Enforcement office, the operator must contact the nearest FWS Ecological Services office.)
7. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be a color which simulates "Standard Environmental Colors" designated by the Rocky Mountain Five-State Interagency Committee. The color selected for this project is **Shale Green**, Munsell Soil Color Chart Number 5Y 4/2.
8. Any cultural and/or paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.
9. A sales contract for removal of mineral material (caliche, sand, gravel, fill dirt) from an authorized pit, site, or on location must be obtained from the BLM prior to commencing construction. There are several options available for purchasing mineral material: contact the BLM office (575-234-5972).



10. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.



11. Once the site is no longer in service or use, the site must undergo final abandonment. At final abandonment, the site and access roads must undergo "final" reclamation so that the character and productivity of the land are restored. Earthwork for final reclamation must be completed within six (6) months of the abandonment of the site. All pads and facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact. After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

12. The holder shall stockpile an adequate amount of topsoil where blading occurs. The topsoil to be stripped is approximately   6   inches in depth. The topsoil will be segregated from other spoil piles. The topsoil will be used for final reclamation.

13. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- |  |  |
|--|--|
| <input type="checkbox"/> seed mixture 1                | <input type="checkbox"/> seed mixture 3          |
| <input type="checkbox"/> seed mixture 2                | <input type="checkbox"/> seed mixture 4          |
| <input checked="" type="checkbox"/> seed mixture 2/LPC | <input type="checkbox"/> Aplomado Falcon Mixture |

14. In those areas where erosion control structures are required to stabilize soil conditions, the holder shall install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound management practices. Any earth work will require prior approval by the Authorized Officer.

15. Open-topped Tanks - The operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps



16. The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an

impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S.

Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock enclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

17. Open-Vent Exhaust Stack Enclosures – The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (Recommended enclosure structures on open-vent exhaust stacks are in the shape of a cone.) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

18. Containment Structures - Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

19. Special Stipulations:

- The entire well pad will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The berm shall be maintained through the life of the well and after interim reclamation has been completed.
- Any water erosion that may occur due to the construction of the well pad during the life of the well will be corrected within two weeks and proper measures will be taken to prevent future erosion.

#### **Lesser Prairie-Chicken**

Oil and gas activities will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except



between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Normal vehicle use on existing roads will not be restricted. Exhaust noise from permanent engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

## **B. PIPELINES**

### **BURIED PIPELINE STIPULATIONS**

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C.6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.
4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure



of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.



5. All construction and maintenance activity will be confined to the authorized right-of-way.
6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.
7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:
- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 20 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
  - Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
  - The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)
8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.
9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.
10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.
11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.



12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- |  |  |
|--|--|
| <input type="checkbox"/> seed mixture 1                | <input type="checkbox"/> seed mixture 3          |
| <input type="checkbox"/> seed mixture 2                | <input type="checkbox"/> seed mixture 4          |
| <input checked="" type="checkbox"/> seed mixture 2/LPC | <input type="checkbox"/> Aplomado Falcon Mixture |

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural and/or paleontological resources (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

17. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

18. Escape Ramps - The operator will construct and maintain pipeline/utility trenches that are not otherwise fenced, screened, or netted to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or



other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.
- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

19. Special Stipulations:

**Lesser Prairie-Chicken**

Oil and gas activities will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

**C. ELECTRIC LINES**

**STANDARD STIPULATIONS FOR OVERHEAD ELECTRIC DISTRIBUTION LINES**

**A copy of the grant and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.**

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b.



A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. There will be no clearing or blading of the right-of-way unless otherwise agreed to in writing by the Authorized Officer.

5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the holder without liability or expense to the United States.

Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.

6. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

7. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.

8. Upon cancellation, relinquishment, or expiration of this grant, the holder shall comply



with those abandonment procedures as prescribed by the Authorized Officer.

9. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this grant, whichever comes first. This will not apply where the power line extends service to an active, adjoining facility or facilities.

10. Any cultural and/or paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

11. Special Stipulations:

- For reclamation remove poles, lines, transformer, etc. and dispose of properly.
- Fill in any holes from the poles removed.

**Timing Limitation Stipulation/Condition of Approval for Lesser Prairie-Chicken:**

Oil and gas activities including 3-D geophysical exploration, and drilling will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Additionally, no new drilling will be allowed within up to 200 meters of leks known at the time of permitting. Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

## **VIII. INTERIM RECLAMATION**

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce



the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

## **IX. FINAL ABANDONMENT & RECLAMATION**

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Below Ground-level Abandoned Well Marker to avoid raptor perching: Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well.



## Seed Mixture for LPC Sand/Shinnery Sites

Holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)\* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed shall be done in accordance with State law(s) and within nine (9) months prior to purchase. Commercial seed shall be either certified or registered seed. The seed container shall be tagged in accordance with State law(s) and available for inspection by the Authorized Officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). Holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. Seeding shall be repeated until a satisfactory stand is established as determined by the Authorized Officer. Evaluation of growth may not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed\* per acre:

<u>Species</u>	<u>lb/acre</u>
Plains Bristlegrass	5lbs/A
Sand Bluestem	5lbs/A
Little Bluestem	3lbs/A
Big Bluestem	6lbs/A
Plains Coreopsis	2lbs/A
Sand Dropseed	1lbs/A

\*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed





U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## Operator Certification Data Report

04/18/2019

### Operator Certification

*I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.*

**NAME:** Jenny Harms

**Signed on:** 10/10/2018

**Title:** Regulatory Compliance Professional

**Street Address:** 333 W Sheridan Ave

**City:** Oklahoma City

**State:** OK

**Zip:** 73102

**Phone:** (405)552-6560

**Email address:** jenny.harms@dnv.com

### Field Representative

**Representative Name:** RAY VAZ

**Street Address:** 333 WEST SHERIDAN AVENUE

**City:** OKLAHOMA CITY

**State:** OK

**Zip:** 73102-5015

**Phone:** (575)748-1871

**Email address:** RAY.VAZ@DVN.COM





U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## Application Data Report

04/18/2019

APD ID: 10400035068

Submission Date: 10/10/2018

Highlighted data  
reflects the most  
recent changes

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: TODD 36-25 STATE FED COM

Well Number: 235H

[Show Final Text](#)

Well Type: OIL WELL

Well Work Type: Drill

### Section 1 - General

APD ID: 10400035068

Tie to previous NOS?

Submission Date: 10/10/2018

BLM Office: CARLSBAD

User: Jenny Harms

Title: Regulatory Compliance  
Professional

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMNM0544986

Lease Acres: 600

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? NO

Federal or Indian agreement:

Agreement number:

Agreement name:

Keep application confidential? YES

Permitting Agent? NO

APD Operator: DEVON ENERGY PRODUCTION COMPANY LP

Operator letter of designation:

### Operator Info

Operator Organization Name: DEVON ENERGY PRODUCTION COMPANY LP

Operator Address: 333 West Sheridan Avenue

Zip: 73102

Operator PO Box:

Operator City: Oklahoma City State: OK

Operator Phone: (800)583-3866

Operator Internet Address:

### Section 2 - Well Information

Well in Master Development Plan? NO

Master Development Plan name:

Well in Master SUPO? NO

Master SUPO name:

Well in Master Drilling Plan? NO

Master Drilling Plan name:

Well Name: TODD 36-25 STATE FED COM

Well Number: 235H

Well API Number:

Field/Pool or Exploratory? Exploratory

Field Name: WILDCAT

Pool Name:

Is the proposed well in an area containing other mineral resources? POTASH



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

**Describe other minerals:**

**Is the proposed well in a Helium production area?** N **Use Existing Well Pad?** NO **New surface disturbance?**

**Type of Well Pad:** MULTIPLE WELL

**Multiple Well Pad Name:** TODD **Number:** 3

**Well Class:** HORIZONTAL

36 WELLPAD

**Number of Legs:** 1

**Well Work Type:** Drill

**Well Type:** OIL WELL

**Describe Well Type:**

**Well sub-Type:** INFILL

**Describe sub-type:**

**Distance to town:**

**Distance to nearest well:** 5950 FT

**Distance to lease line:** 330 FT

**Reservoir well spacing assigned acres Measurement:** 320 Acres

**Well plat:** TODD\_36\_25\_STATE\_FED\_COM\_235H\_C102\_9\_23\_2018\_1\_20181010090322.pdf

**Well work start Date:** 06/24/2019

**Duration:** 30 DAYS

### Section 3 - Well Location Table

**Survey Type:** RECTANGULAR

**Describe Survey Type:**

**Datum:** NAD83

**Vertical Datum:** NAVD88

**Survey number:**

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
SHL Leg #1	330	FSL	163 6	FEL	23S	31E	36	Aliquot SWSE	32.25457 5	- 103.7282 716	EDD Y	NEW MEXI CO	NEW MEXI CO	S	STATE	350 8	0	0
KOP Leg #1	50	FSL	498	FEL	23S	31E	36	Aliquot SESE	32.25382 1	- 103.7245 79	EDD Y	NEW MEXI CO	NEW MEXI CO	S	STATE	- 647 4	100 78	998 2
PPP Leg #1	100	FSL	400	FEL	23S	31E	36	Aliquot SESE	32.25394 22	- 103.7242 735	EDD Y	NEW MEXI CO	NEW MEXI CO	S	STATE	- 669 5	103 06	102 03



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP


**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
EXIT Leg #1	100	FNL	400	FEL	23S	31E	25	Aliquot NENE	32.28241	- 103.7242 619	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 054498 6	- 706 2	208 28	105 70
BHL Leg #1	20	FNL	400	FEL	23S	31E	25	Aliquot NENE	32.28262 99	- 103.7242 618	EDD Y	NEW MEXI CO	NEW MEXI CO	F	NMNM 054498 6	- 706 2	209 08	105 70



§

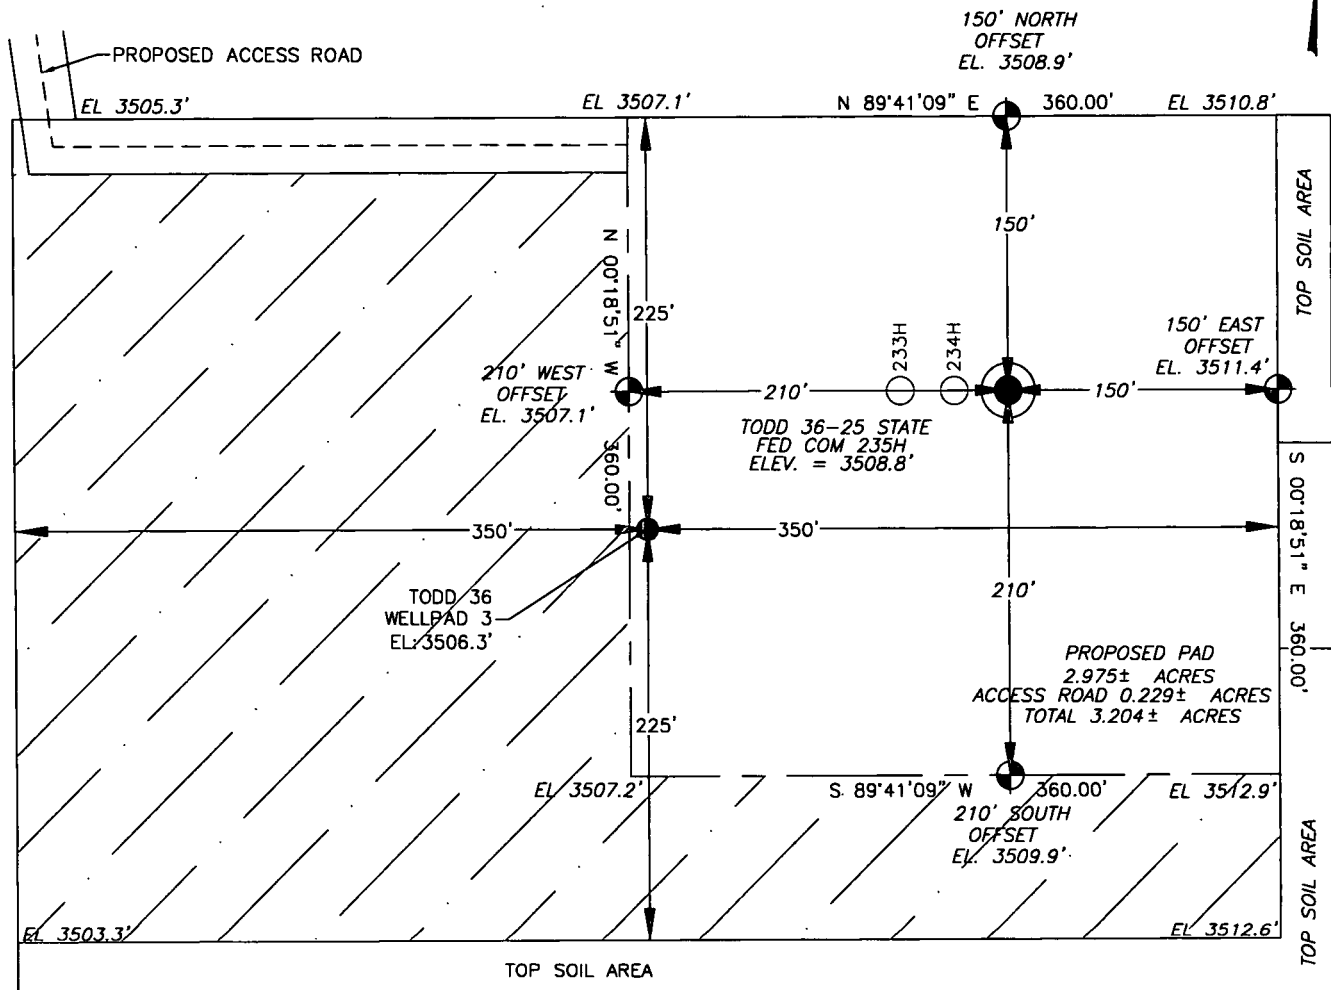

*Note: All bearings recited herein are based on the New Mexico State Plane Coordinate System, NAD 83, New Mexico East Zone 3001, US Survey Feet, all distances are grid.*

DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO

100	200
-----	-----

**DIRECTIONS TO LOCATION**

FROM THE INTERSECTION OF NM-128 AND RED ROAD HEAD NORTH ON RED ROAD FOR 0.09 MILES. TURN RIGHT ONTO AN ACCESS ROAD AND HEAD NORTHEAST FOR 0.07 MILES TO THE POINT OF BEGINNING OF THE PROPOSED TODD 36 WELLPAD 1 ACCESS ROAD. LEAVE THE EXISTING ACCESS ROAD AND HEAD NORTH AND EAST ON THE PROPOSED TODD 36 WELLPAD 1 ACCESS ROAD FOR 0.19 MILES TO THE SAME EXISTING ACCESS ROAD AND THEN HEAD EAST FOR 0.50 MILES TO THE POINT OF BEGINNING OF THE PROPOSED TODD 36 WELLPAD 3 ACCESS ROAD. HEAD SOUTH ALONG THE PROPOSED TODD 36 WELLPAD 3 ACCESS ROAD FOR 46 FEET TO THE TO THE NORTHWEST CORNER OF THE TODD 36 WELLPAD 3.

*HORIZON ROW LLC*

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
**CHRIS MAAS**


Date: 09/20/2018

Drawn for:






SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
INTERIM SITE BUILD PLAN

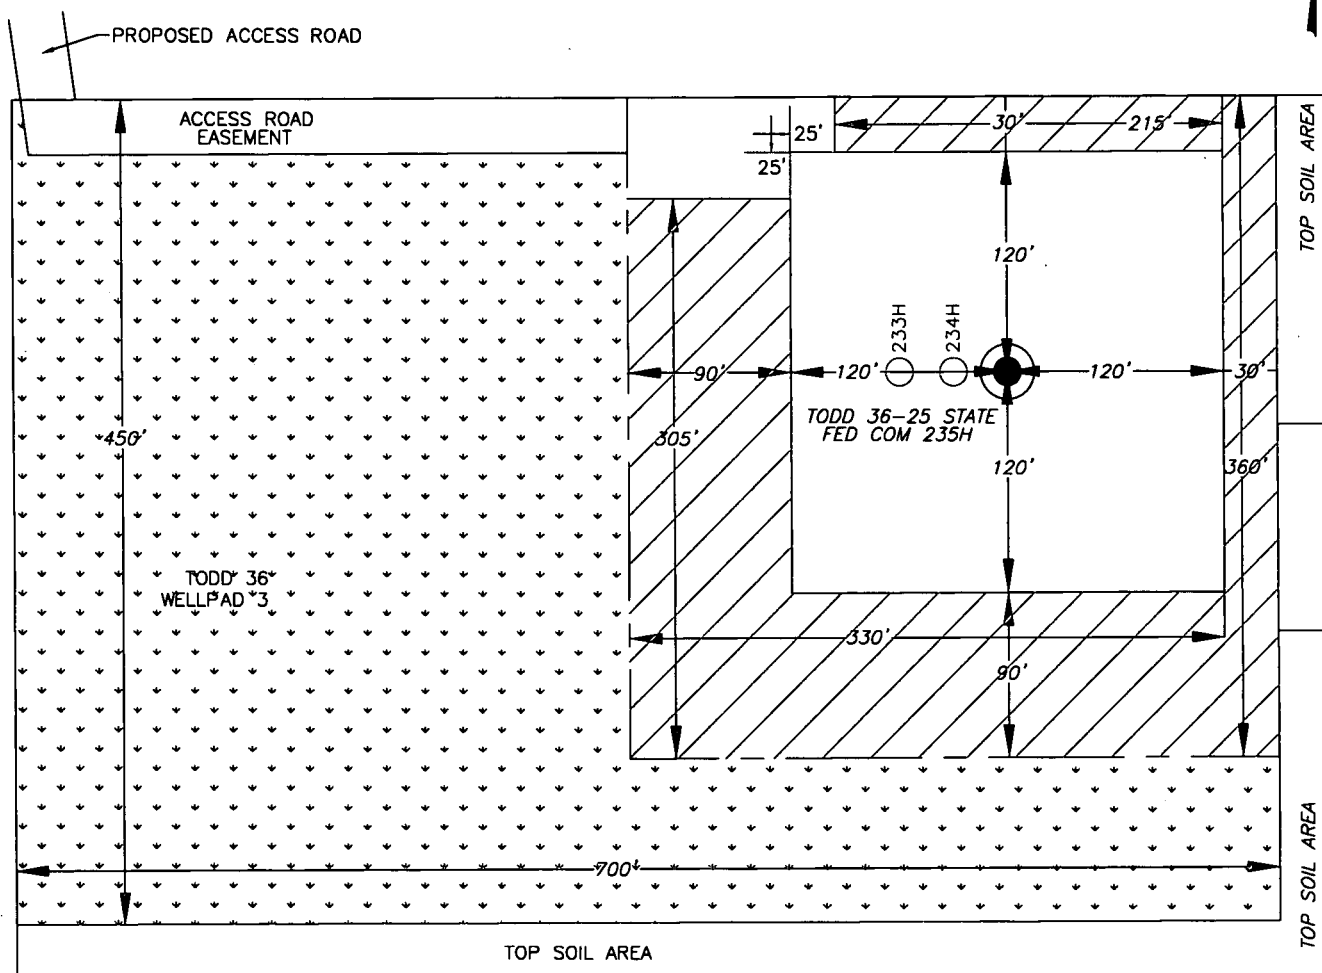

- DENOTES INTERIM PAD RECLAMATION AREA
- DENOTES GRADING SITE RECLAMATION AREA

1.522± ACRES INTERIM PAD RECLAMATION AREA  
4.026± ACRES GRADING SITE RECLAMATION AREA  
1.683± ACRES NON-RECLAIMED AREA  
7.231± ACRES GRADING SITE RECLAMATION AREA



DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO

**HORIZON ROW LLC**

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
CHRIS MAAS


Date: 09/20/2018

Drawn for:






SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
VICINITY MAP

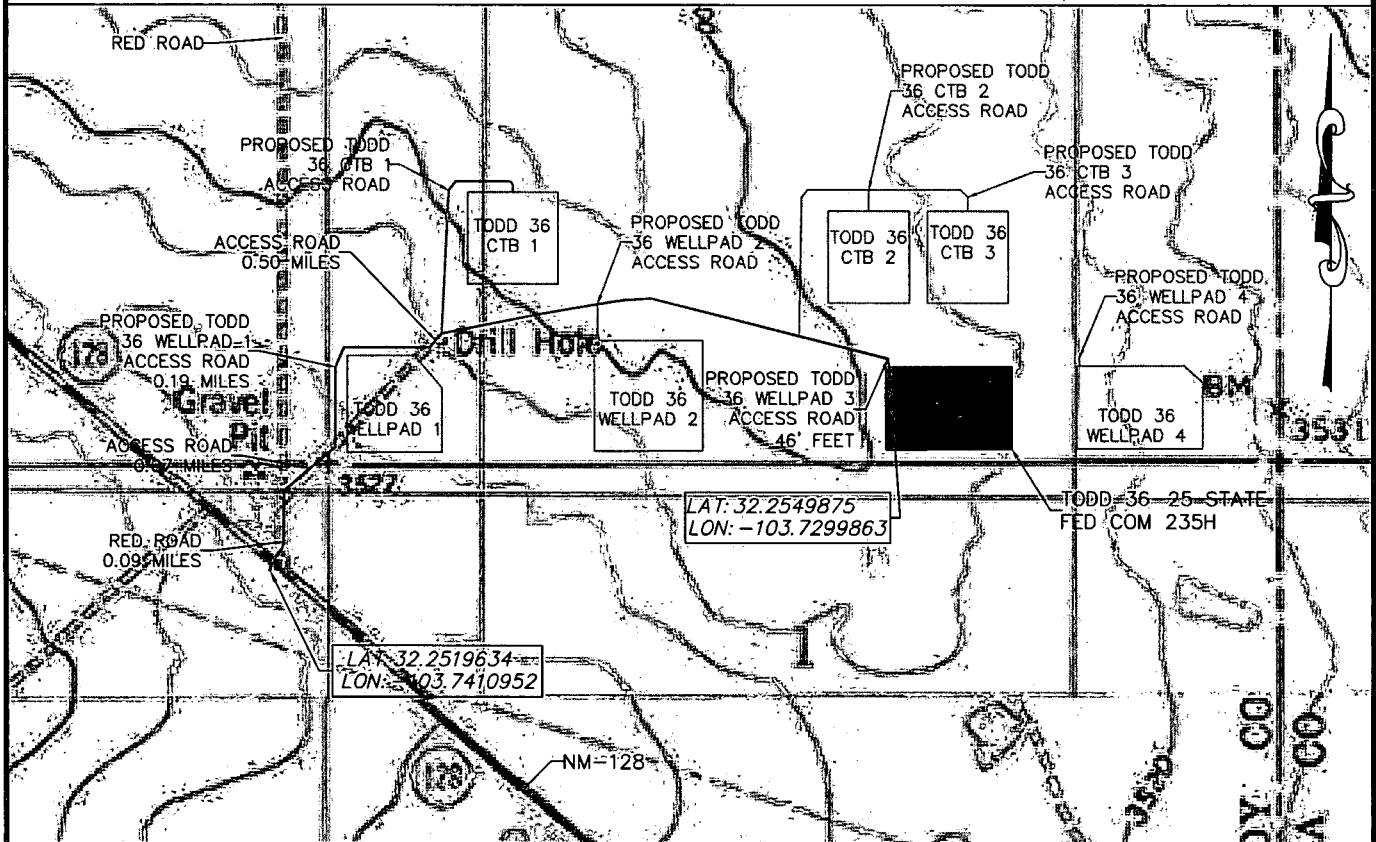

DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO

**DIRECTIONS TO LOCATION**

FROM THE INTERSECTION OF NM-128 AND RED ROAD HEAD NORTH ON RED ROAD FOR 0.09 MILES. TURN RIGHT ONTO AN ACCESS ROAD AND HEAD NORTHEAST FOR 0.07 MILES TO THE POINT OF BEGINNING OF THE PROPOSED TODD 36 WELLPAD 1 ACCESS ROAD. LEAVE THE EXISTING ACCESS ROAD AND HEAD NORTH AND EAST ON THE PROPOSED TODD 36 WELLPAD 1 ACCESS ROAD FOR 0.19 MILES TO THE SAME EXISTING ACCESS ROAD AND THEN HEAD EAST FOR 0.50 MILES TO THE POINT OF BEGINNING OF THE PROPOSED TODD 36 WELLPAD 3 ACCESS ROAD. HEAD SOUTH ALONG THE PROPOSED TODD 36 WELLPAD 3 ACCESS ROAD FOR 46 FEET TO THE TO THE NORTHWEST CORNER OF THE TODD 36 WELLPAD 3.



**HORIZON ROW LLC**

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
CHRIS MAAS


Date: 09/20/2018

Drawn for:


**devon**



SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
 EDDY COUNTY, STATE OF NEW MEXICO  
 LOCATION VERIFICATION MAP

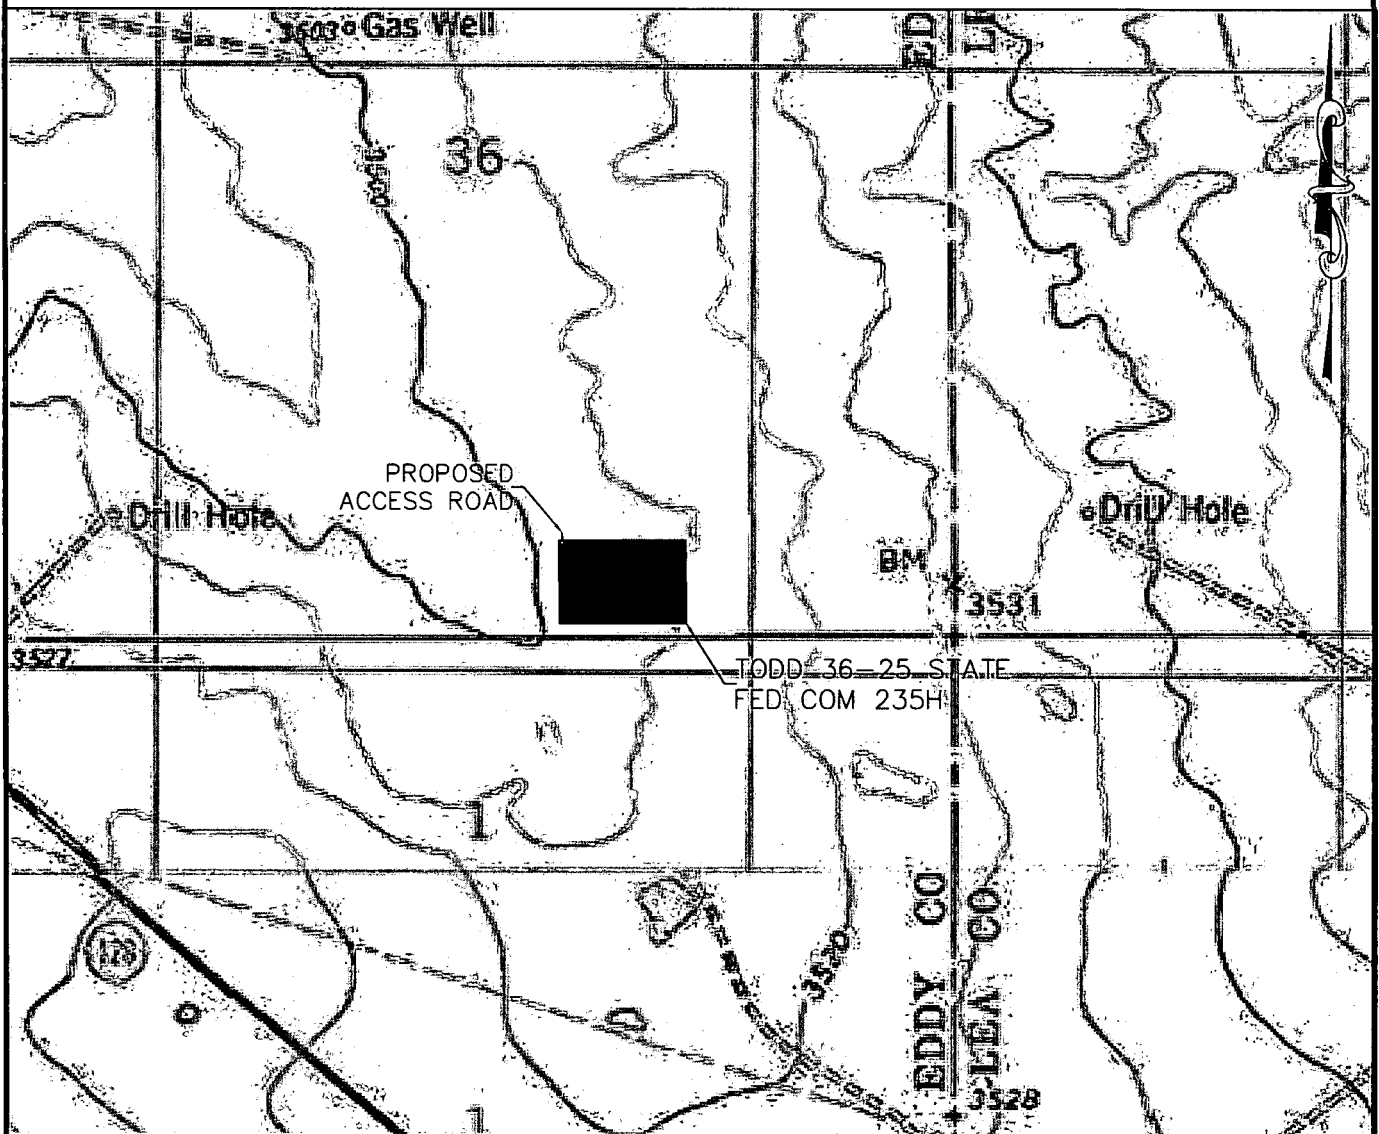

DEVON ENERGY PRODUCTION COMPANY, L.P.  
 TODD 36-25 STATE FED COM 235H  
 LOCATED 330 FT. FROM THE SOUTH LINE  
 AND 1636 FT. FROM THE EAST LINE OF  
 SECTION 36, TOWNSHIP 23 SOUTH,  
 RANGE 31 EAST, N.M.P.M.  
 EDDY COUNTY, STATE OF NEW MEXICO



HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
 CHRIS MAAS


Date: 09/20/2018

Drawn for:


devon



SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
AERIAL PHOTO

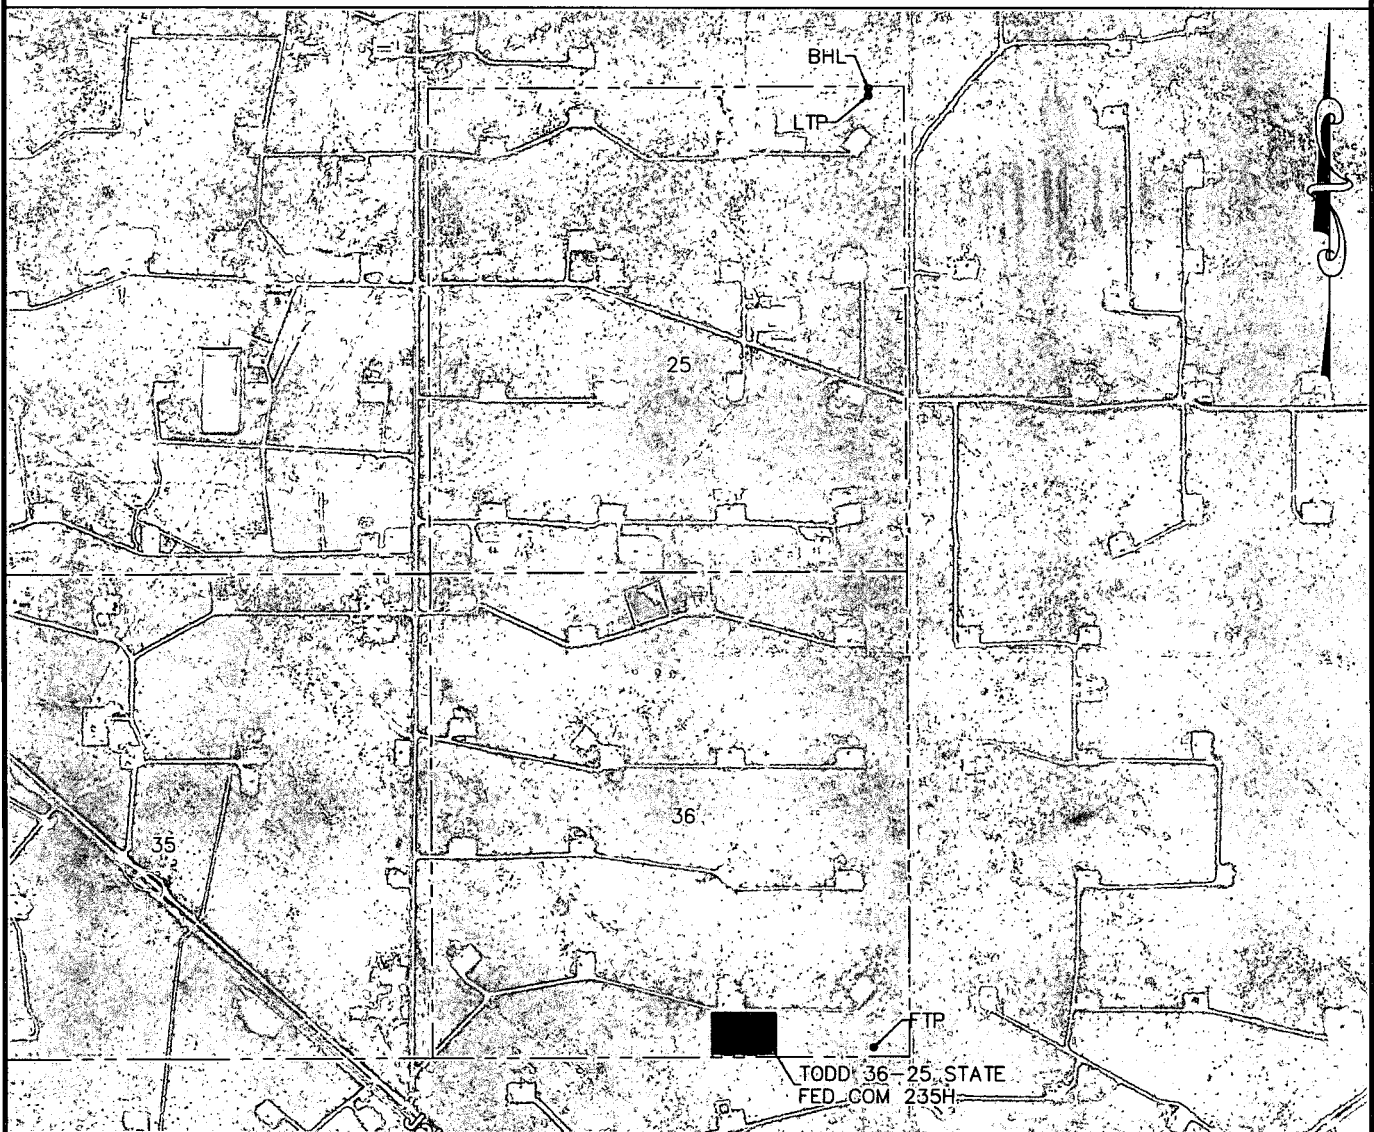

DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO



**HORIZON ROW LLC**

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
CHRIS MAAS

Date: 09/20/2018

Drawn for:


**devon**



SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
AERIAL ACCESS ROUTE MAP



DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO



HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
CHRIS MAAS


Date: 09/20/2018

Drawn for:

devon



EXHIBIT "A"  
ACCESS ROAD PLAT  
SECTION 36, T23S-R31E, N.M.P.M.  
EDDY COUNTY, NEW MEXICO

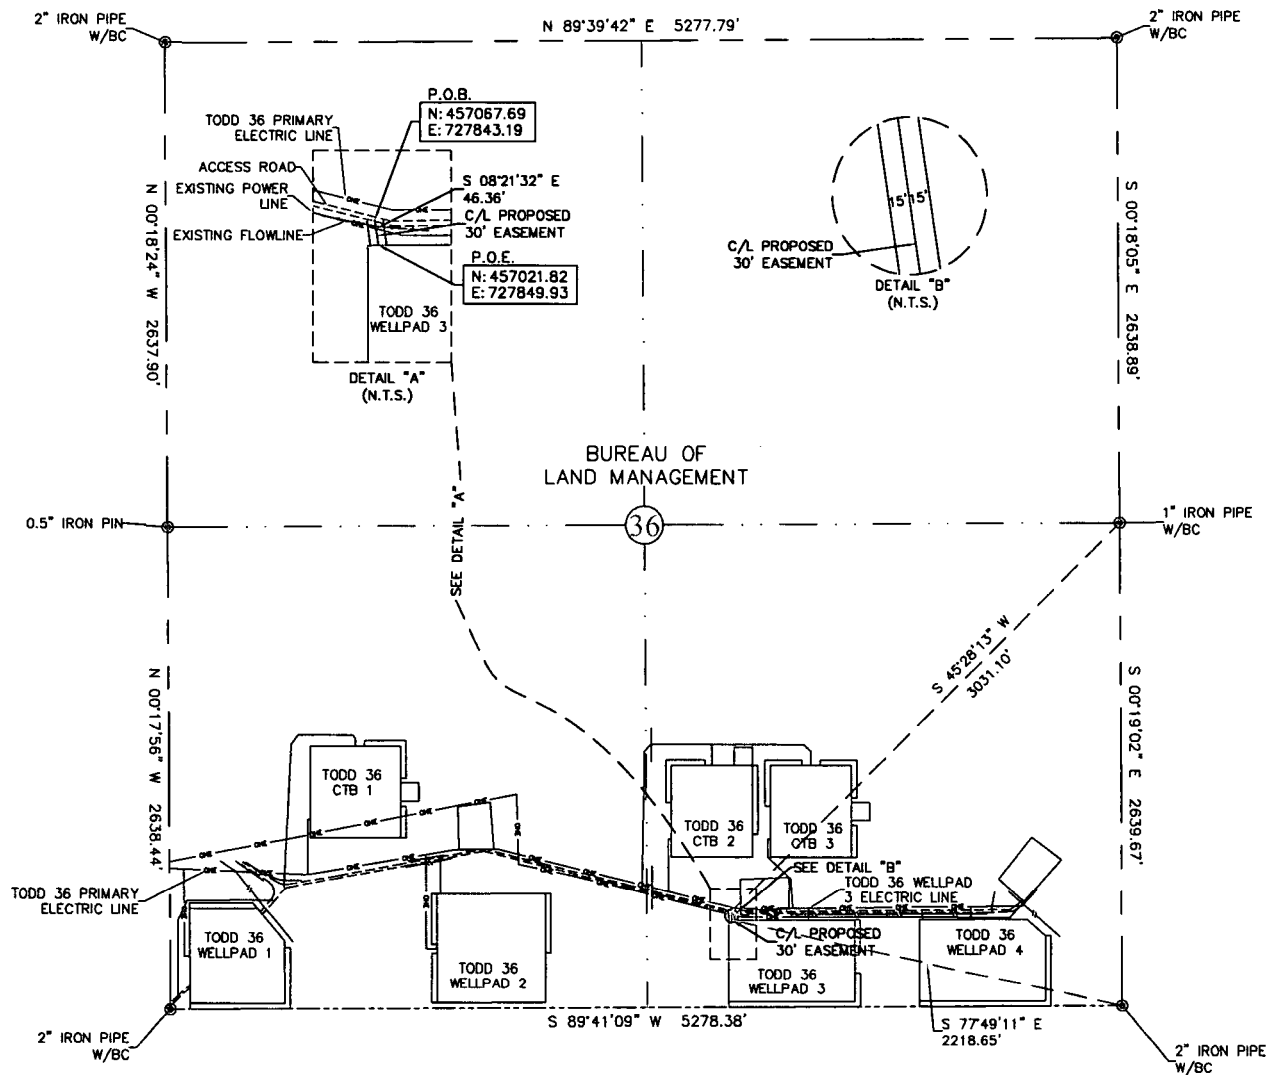

30' EASEMENT AREA = 0.032 ACRE(S)  
46.36 FEET OR 2.81 RODS


0+00.0 P.O.B./EXISTING ACCESS ROAD  
0+03.9 EDGE OF ROAD  
0+11.6 EXISTING FLOW LINE  
0+16.3 POWER LINE  
0+46.3 P.O.E./TODD 36 WELLPAD 3

SEE THE ATTACHED LEGAL DESCRIPTION

Note: All bearings recited herein are based on the New Mexico State Plane Coordinate System, NAD 83, New Mexico East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.

B.L. Laman PLS #22404  
Date Signed: 09-23-2018  
P.O. Box 548, Dry Creek, La.  
(903) 388-3045 70637  
Employee of Horizonrow, LLC



HORIZON ROW LLC

Drawn for:

devon

Drawn by:  
CHRIS MAAS

Date: 07/07/2018

DEVON ENERGY PRODUCTION COMPANY, L.P.

TODD 36  
WELLPAD 3 ACCESS ROAD

PROPOSED 30' EASEMENT  
ON THE PROPERTY OF  
BUREAU OF LAND MANAGEMENT  
SECTION 36, T23S-R31E, N.M.P.M.


LINE NUMBER:

WBS NUMBER:

SCALE:  
1" = 1000'

REVISIONS:

SURVEY DATE:  
6/30/18





**SECTION 36, T23S-R31E, N.M.P.M.,  
EDDY COUNTY, NEW MEXICO**

**ACCESS ROAD PLAT**

**LEGAL DESCRIPTION**

**FOR**

**DEVON ENERGY PRODUCTION COMPANY, L.P.**

**BUREAU OF LAND MANAGEMENT**

**30' EASEMENT DESCRIPTION:**

**BEING** an easement thirty (30) feet in width lying fifteen (15) feet on the right side and fifteen (15) feet on the left side of the survey centerline described below, being out of the southeast quarter (SE  $\frac{1}{4}$ ) of Section 36, Township 23 South, Range 31 East, N.M.P.M., Eddy County, New Mexico, and being out of a parcel of land owned by the Bureau of Land Management. Said centerline of easement being more particularly described as follows:

Commencing from a 1" iron pipe w/BC for the east quarter corner of Section 36, T23S-R31E, N.M.P.M., Eddy County, New Mexico;


Thence S 45°28'13" W a distance of 3031.10' to the **Point of Beginning** of this easement having coordinates of Northing=457067.69, Easting=727843.19 feet and continuing the following course;

Thence S 08°21'32" E a distance of 46.36' to the **Point of Ending** having coordinates of Northing=457021.82, Easting=727849.93 feet from said point a 2" iron pipe w/BC for the southeast corner of Section 36, T23S-R31E bears S 77°49'11" E a distance of 2218.65', covering **46.36' or 2.81 rods** and having an area of **0.032 acres**.

**NOTES:**

Bearings, distances and coordinates shown herein are based on New Mexico State Plane Coordinate System, NAD 83, East Zone 3001, US Survey Feet, all distances are grid.


I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.

  
B.L. Laman PLS 22404  
Date Signed: 09/23/2018  
Horizon Row, LLC  
P.O. Box 548, Dry Creek, La.  
(903) 388-3045 70637  
Employee of Horizon Row, LLC






SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
PLAN VIEW

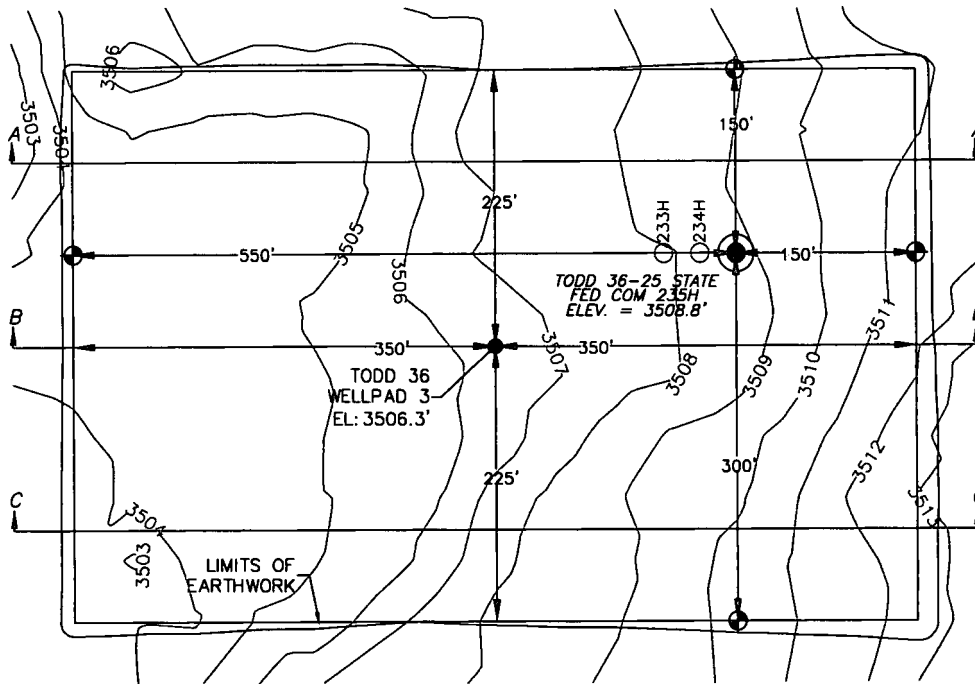

DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO



EARTHWORK QUANTITIES FOR  
TODD 36 WELLPAD 3

CUT	FILL	NET
12,929 CY	12,929 CY	0 CY

EARTHWORK QUANTITIES ARE ESTIMATED

HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
CHRIS MAAS




Date: 09/20/2018

Drawn for:





SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
CROSS SECTIONS

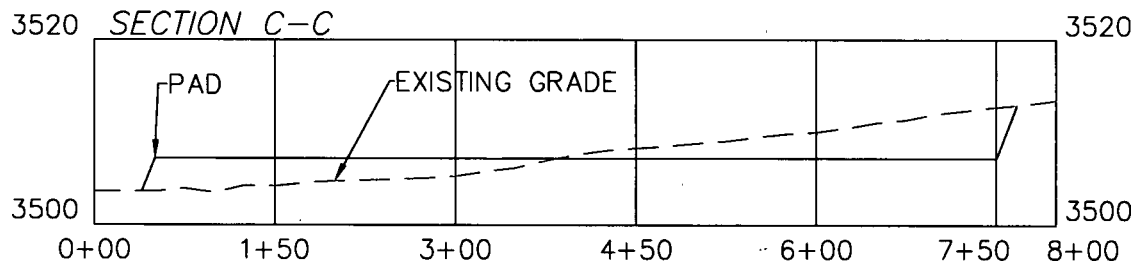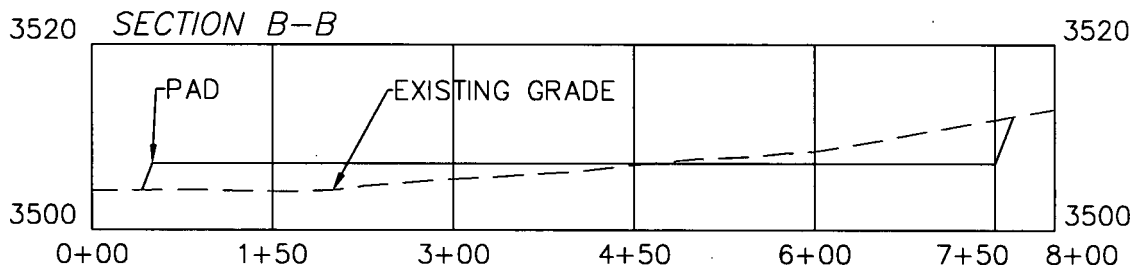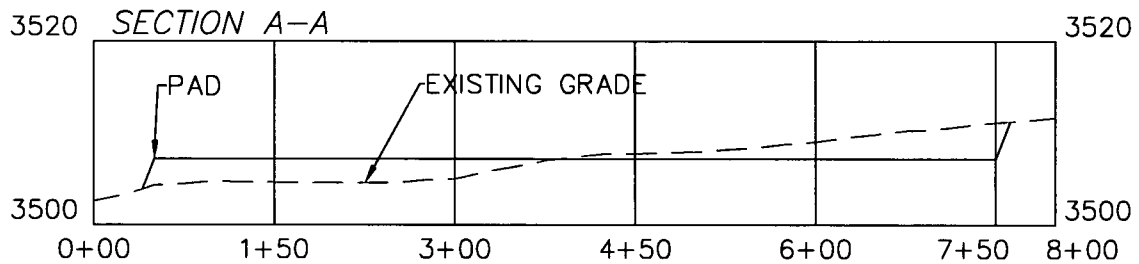

DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO

SCALE 1" = 150' HORIZONTAL  
SCALE 1" = 20' VERTICAL

EARTHWORK QUANTITIES FOR  
TODD 36 WELLPAD 3

CUT	FILL	NET
12,929 CY	12,929 CY	0 CY

EARTHWORK QUANTITIES ARE ESTIMATED

HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
CHRIS MAAS

Date: 09/20/2018

Drawn for:







U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## Drilling Plan Data Report

04/18/2019

APD ID: 10400035068

Submission Date: 10/10/2018

Highlighted data  
reflects the most  
recent changes

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: TODD 36-25 STATE FED COM

Well Number: 235H

[Show Final Text](#)

Well Type: OIL WELL

Well Work Type: Drill

### Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
1	UNKNOWN	3508	0	0	ALLUVIUM	NONE	No
2	RUSTLER	2711	797	797	SALT	NONE	No
3	SALADO	2375	1133	1133	SALT	NONE	No
4	BASE OF SALT	-924	4432	4432	SALT	NONE	No
5	DELAWARE	-984	4492	4492	SANDSTONE	NONE	No
6	BONE SPRING LIME	-4849	8357	8357	LIMESTONE	NONE	No
7	BONE SPRING 1ST	-6141	9649	9649	SANDSTONE	NATURAL GAS,OIL	No
8	2ND BONE SPRING LIME	-6215	9723	9723	LIMESTONE	NATURAL GAS,OIL	No
9	BONE SPRING 2ND	-7042	10550	20555	SANDSTONE	NATURAL GAS,OIL	Yes

### Section 2 - Blowout Prevention

Pressure Rating (PSI): 5M

Rating Depth: 6000

**Equipment:** BOP/BOPE will be installed per Onshore Oil & Gas Order #2 requirements prior to drilling below surface casing, a BOP/BOPE system with the minimum rating listed above will be installed on the wellhead system. BOP/BOPE will be tested by an independent service company per Onshore Oil & Gas Order #2 requirements and MASP (Maximum Anticipated Surface Pressure) calculations. If the system is upgraded, all the components installed will be functional and tested.

**Requesting Variance?** YES

**Variance request:** A variance is requested for the use of a flexible choke line from the BOP stack to the choke manifold. See attached for specs for hydrostatic test chart.

**Testing Procedure:** A multibowl wellhead may be used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

**Choke Diagram Attachment:**

5M\_BOPE\_\_CK\_20190225085247.pdf



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

5M\_BOPE\_\_CK\_20190225085247.pdf

**BOP Diagram Attachment:**

5M\_BOPE\_\_CK\_20190225085257.pdf

**Pressure Rating (PSI):** 5M

**Rating Depth:** 10550

**Equipment:** BOP/BOPE will be installed per Onshore Oil & Gas Order #2 requirements prior to drilling below surface casing, a BOP/BOPE system with the minimum rating listed above will be installed on the wellhead system. BOP/BOPE will be tested by an independent service company per Onshore Oil & Gas Order #2 requirements and MASP (Maximum Anticipated Surface Pressure) calculations. If the system is upgraded, all the components installed will be functional and tested.

**Requesting Variance?** YES

**Variance request:** A variance is requested for the use of a flexible choke line from the BOP stack to the choke manifold. See attached for specs for hydrostatic test chart.

**Testing Procedure:** A multibowl wellhead may be used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

**Choke Diagram Attachment:**

5M\_BOPE\_\_CK\_20190225085355.pdf

**BOP Diagram Attachment:**

5M\_BOPE\_\_CK\_20190225085405.pdf

### Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	836	0	836			836	H-40	48	STC	1.125	1	BUOY	1.6	BUOY	1.6
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	6000	0	6000			6000	J-55	40	OTHER - BTC	1.125	1	BUOY	1.6	BUOY	1.6
3	PRODUCTION	8.75	5.5	NEW	API	N	0	20908	0	10570			20908	P-110	17	OTHER - BTC	1.125	1	BUOY	1.6	BUOY	1.6

**Casing Attachments**



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

#### Casing Attachments

---

**Casing ID:** 1      **String Type:** SURFACE

**Inspection Document:**

**Spec Document:**

**Tapered String Spec:**

**Casing Design Assumptions and Worksheet(s):**

Surf\_Csg\_Ass\_20181010091239.pdf

---

**Casing ID:** 2      **String Type:** INTERMEDIATE

**Inspection Document:**

**Spec Document:**

**Tapered String Spec:**

**Casing Design Assumptions and Worksheet(s):**

Int\_Csg\_Ass\_20181010091256.pdf

---

**Casing ID:** 3      **String Type:** PRODUCTION

**Inspection Document:**

**Spec Document:**

**Tapered String Spec:**

**Casing Design Assumptions and Worksheet(s):**

Prod\_Csg\_Ass\_20181010091311.pdf

---

#### Section 4 - Cement



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	836	873	1.33	13.2	1162	100	c	Class C + adds

INTERMEDIATE	Lead		0	5500	1095	1.94	9	2124	50	C	Class C + Adds
INTERMEDIATE	Tail		5500	6000	196	1.33	13.2	261	50	C	Class C + Adds
PRODUCTION	Lead		4107	1007 8	357	3.57	9	1663	10	TUNED	Class C + adds
PRODUCTION	Tail		1007 8	2090 8	1885	1.46	13.2	2752	10	H	(50:50) Clas H Cement: Poz (Fly Ash) + 0.5% bwoc HALAD-344 + 0.4% bwoc CFR-3 + 0.2% BWOC HR-601 + 2% bwoc Bentonite

### Section 5 - Circulating Medium

**Mud System Type:** Closed

**Will an air or gas system be Used?** NO

**Description of the equipment for the circulating system in accordance with Onshore Order #2:**

**Diagram of the equipment for the circulating system in accordance with Onshore Order #2:**

**Describe what will be on location to control well or mitigate other conditions:** Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

**Describe the mud monitoring system utilized:** Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

### Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
6000	1057 0	WATER-BASED MUD	8.5	9							



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	837	OTHER : FRESH WATER	8.5	9							
837	6000	OTHER : BRINE	10	10.5							

### Section 6 - Test, Logging, Coring

**List of production tests including testing procedures, equipment and safety measures:**

Will run GRMWD from TD to from KOP. Cement bond logs will be run in vertical to determine top of cement. Stated logs run will be in the Completion Report and submitted to the BLM.

**List of open and cased hole logs run in the well:**

CALIPER,CBL,DS,GR,MUDLOG

**Coring operation description for the well:**

N/A

### Section 7 - Pressure

**Anticipated Bottom Hole Pressure:** 4947

**Anticipated Surface Pressure:** 2621.6

**Anticipated Bottom Hole Temperature(F):** 169

**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO

**Describe:**

**Contingency Plans geohazards description:**

**Contingency Plans geohazards attachment:**

**Hydrogen Sulfide drilling operations plan required?** YES

**Hydrogen sulfide drilling operations plan:**

Todd\_36\_25\_State\_Fed\_Com\_235H\_H2S\_20181010091713.pdf



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

## Section 8 - Other Information

### **Proposed horizontal/directional/multi-lateral plan submission:**

Devon\_Todd\_36\_25\_State\_Fed\_Com\_235H\_AC\_Report\_Permit\_Plan\_1\_20181010091743.pdf

Devon\_Todd\_36\_25\_State\_Fed\_Com\_235H\_Permit\_Plan\_1\_20181010091743.pdf

Devon\_Todd\_36\_25\_State\_Fed\_Com\_235H\_Plot\_Permit\_Plan\_1\_20181010091744.pdf

### **Other proposed operations facets description:**

DRILLING PLAN-revised intermediate casing to 6000' , 5M; 2/12/2019

BOP 5M- UPDATED 2-25-2019

Formations added - 3-19-2019

### **Other proposed operations facets attachment:**

Clsd\_Loop\_20181009090953.pdf

Todd\_36\_25\_Fed\_Com\_235H\_Drilling\_Plan\_Rev1\_20190214100304.pdf

MB\_Wellhd\_5M\_20190225085436.pdf

MB\_Verb\_5M\_20190225085437.pdf

Spudder\_Rig\_Info\_20190319130445.pdf


TODD\_36\_Fed\_Com\_GasCapturePlan\_10\_4\_2018\_20190319130514.pdf

### **Other Variance attachment:**

Co\_flex\_20181009090519.pdf




# 13-5/8" 5M BOPE & Closed Loop Equipment Schematic

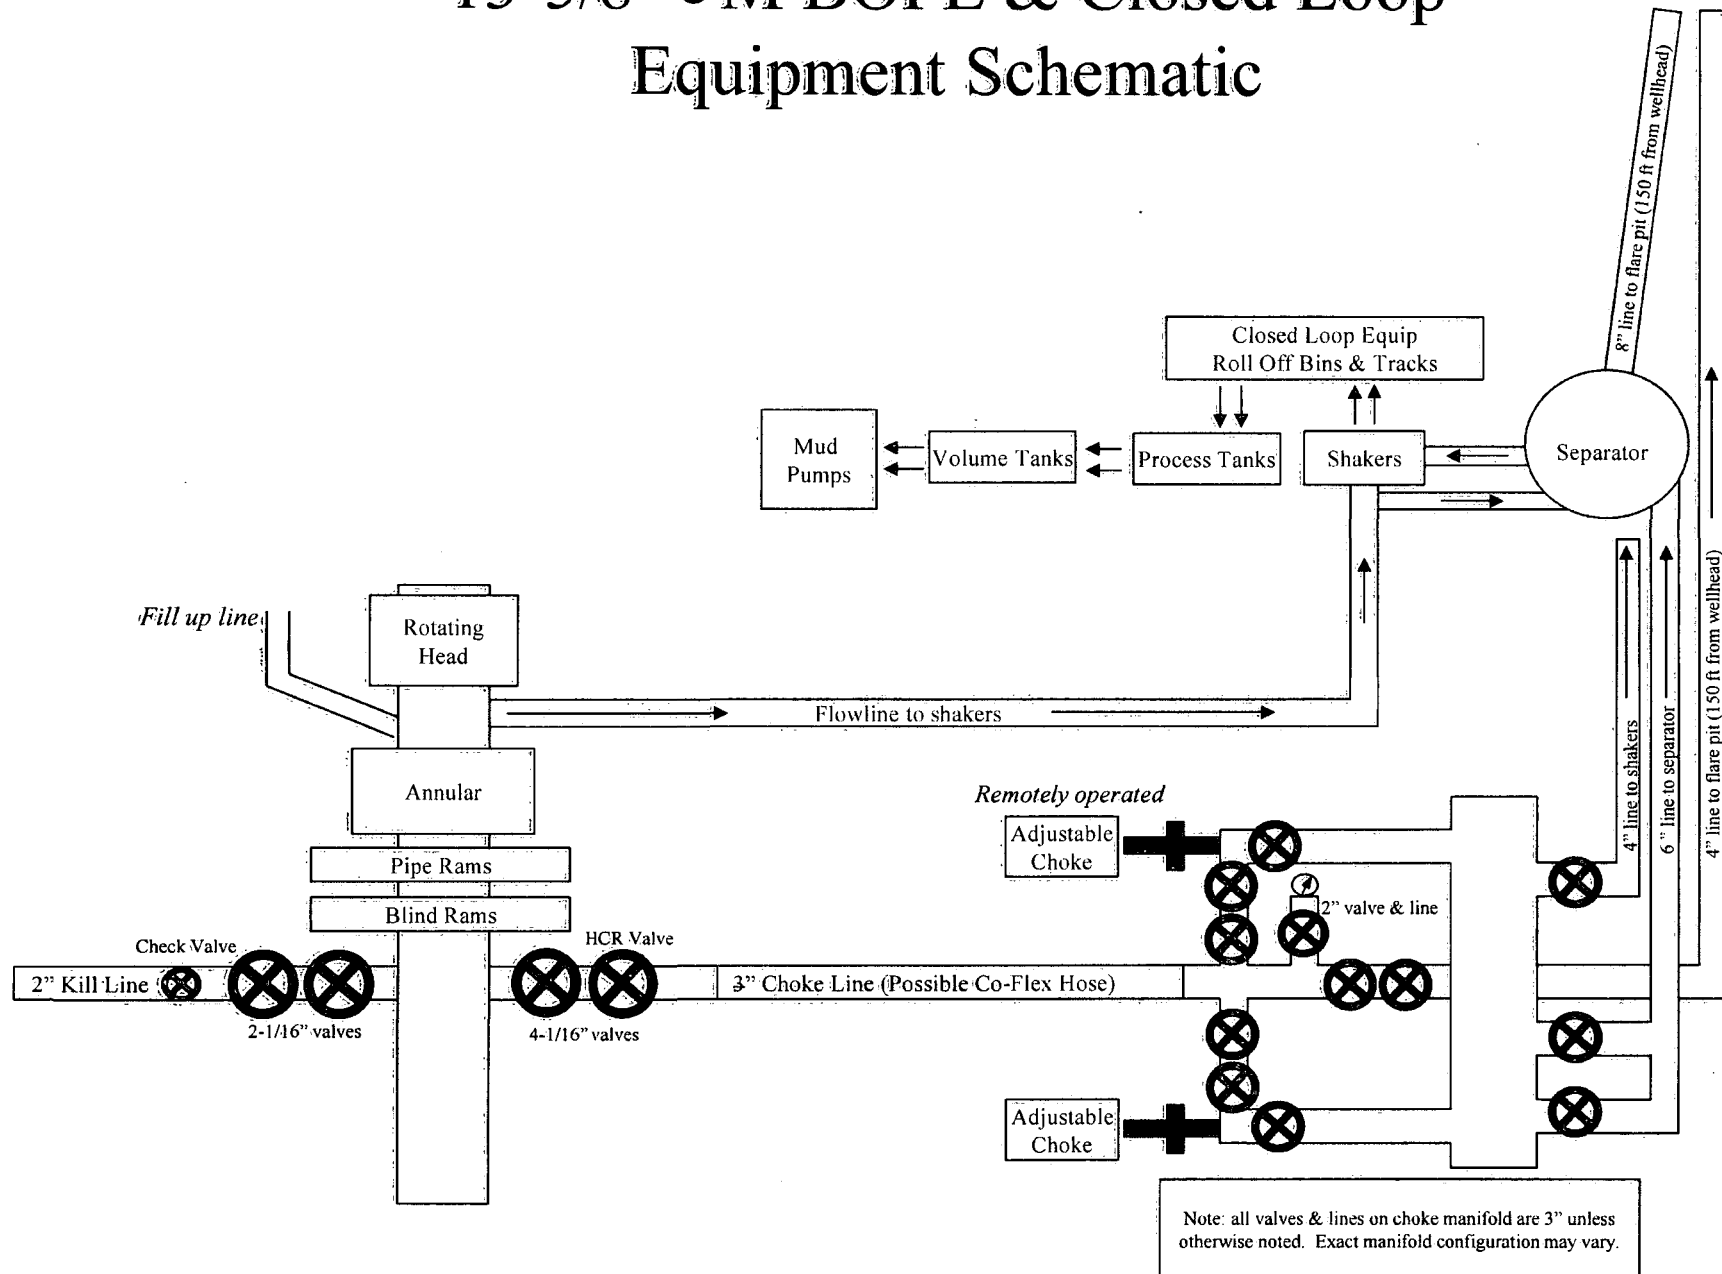




# 13-5/8" 5M BOPE & Closed Loop Equipment Schematic

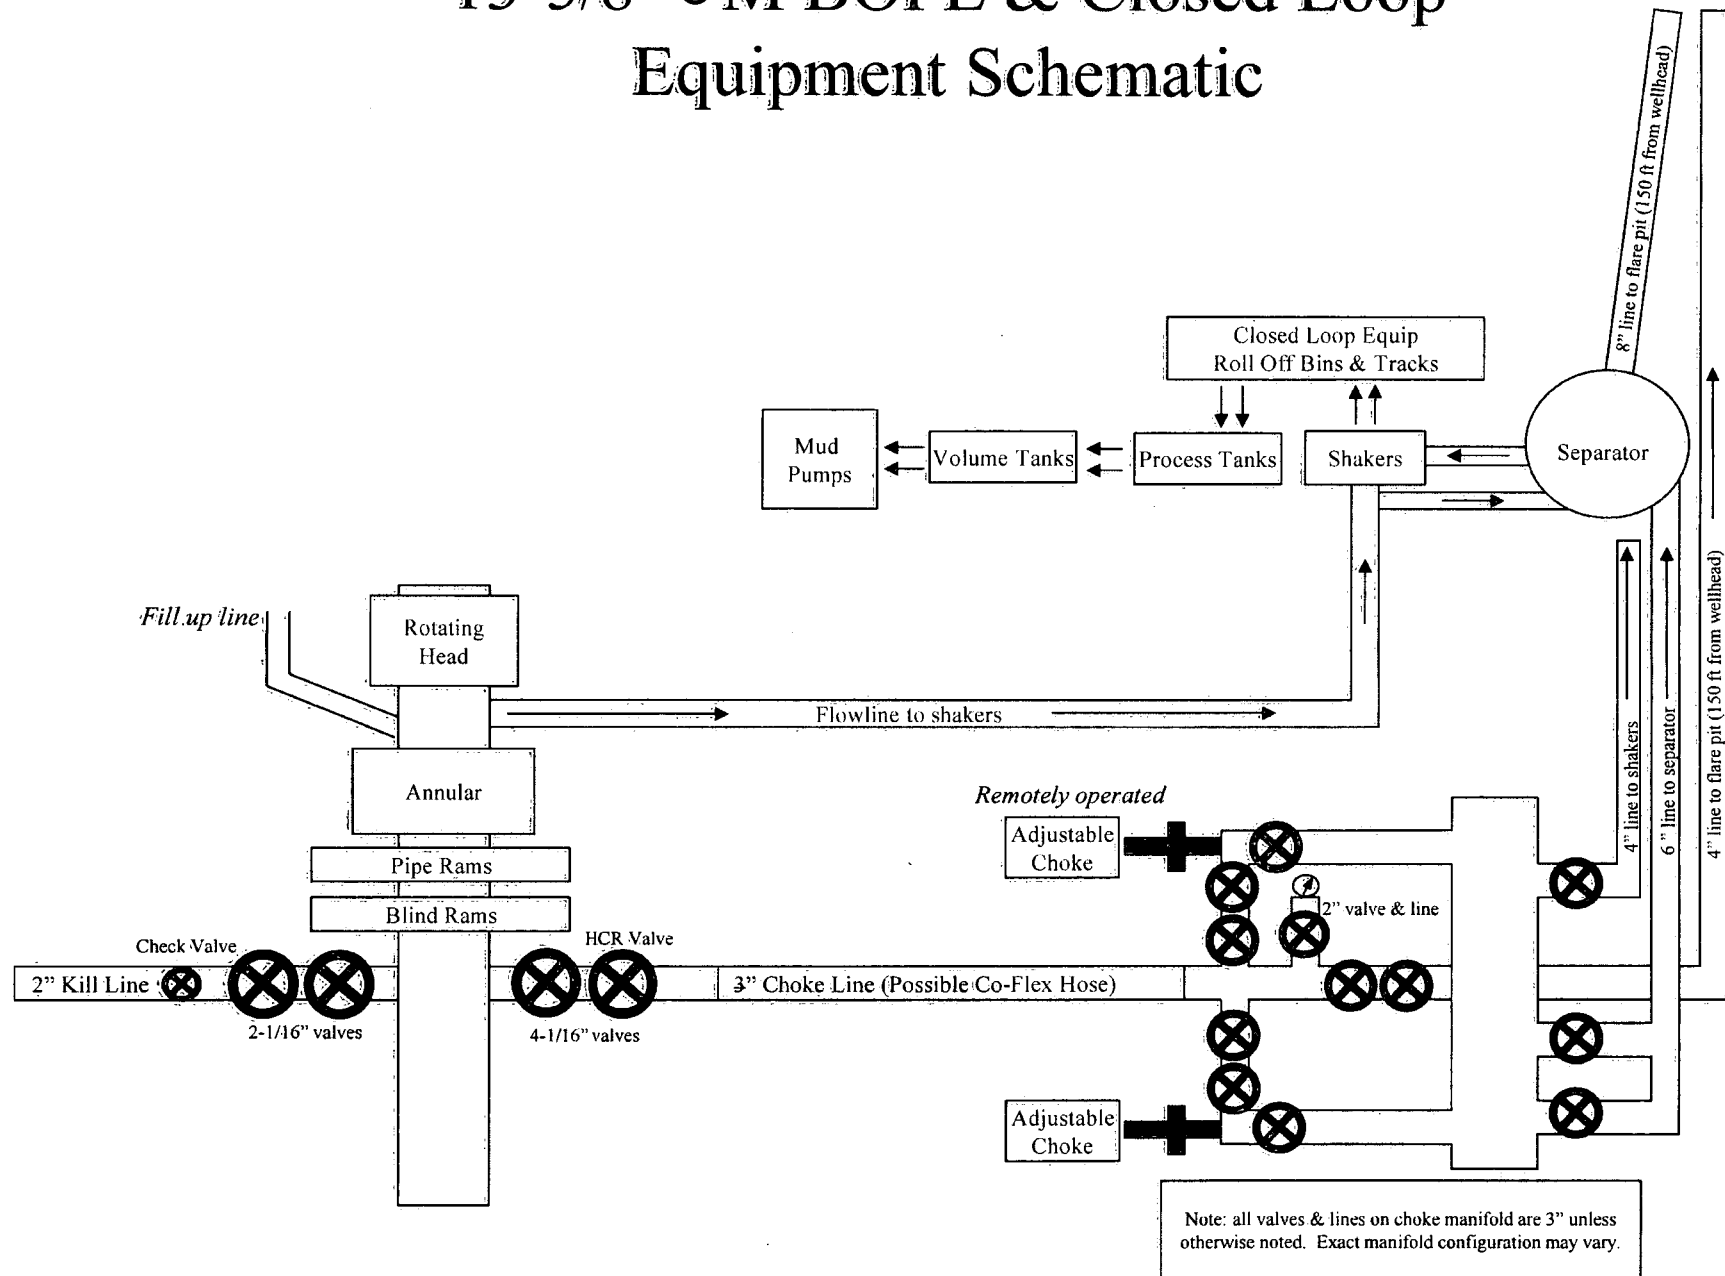




# 13-5/8" 5M BOPE & Closed Loop Equipment Schematic

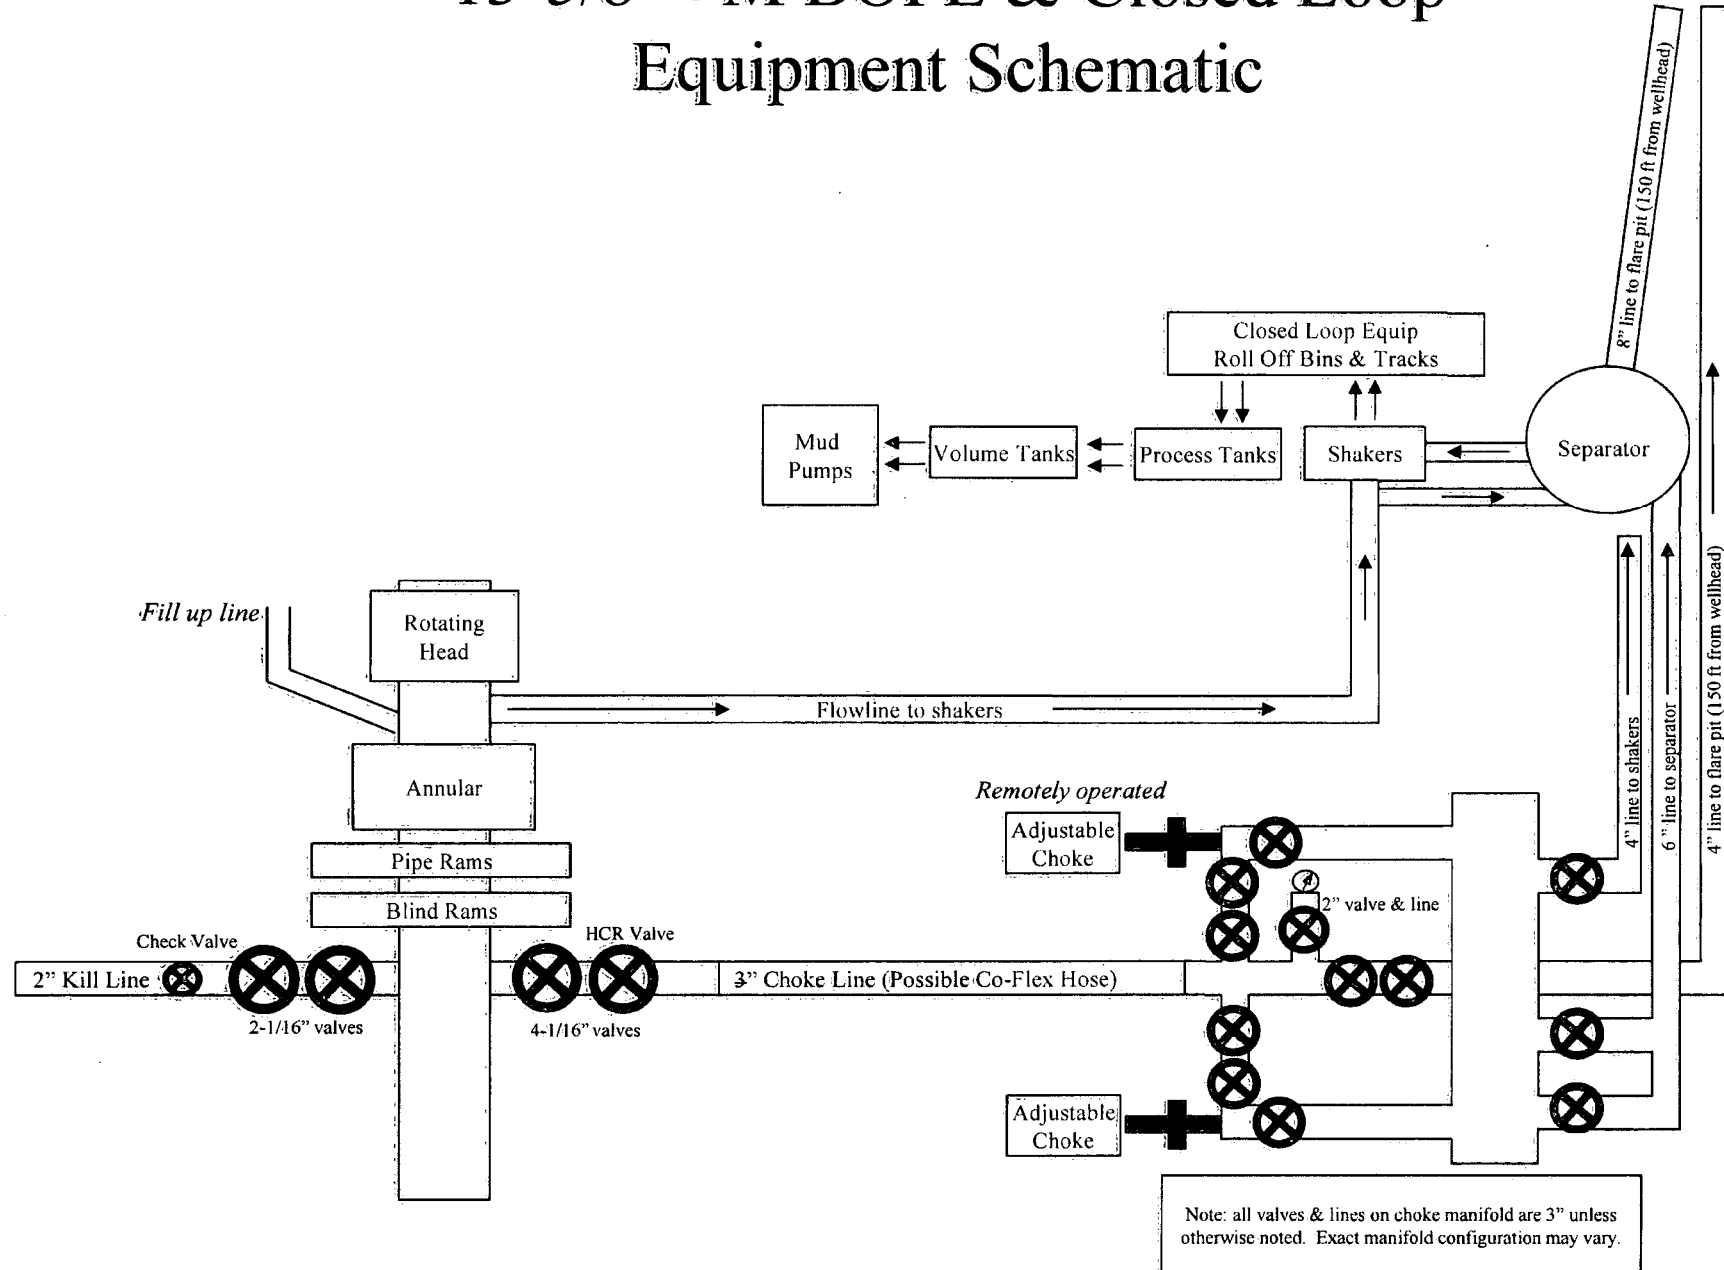



# 13-5/8" 5M BOPE & Closed Loop Equipment Schematic

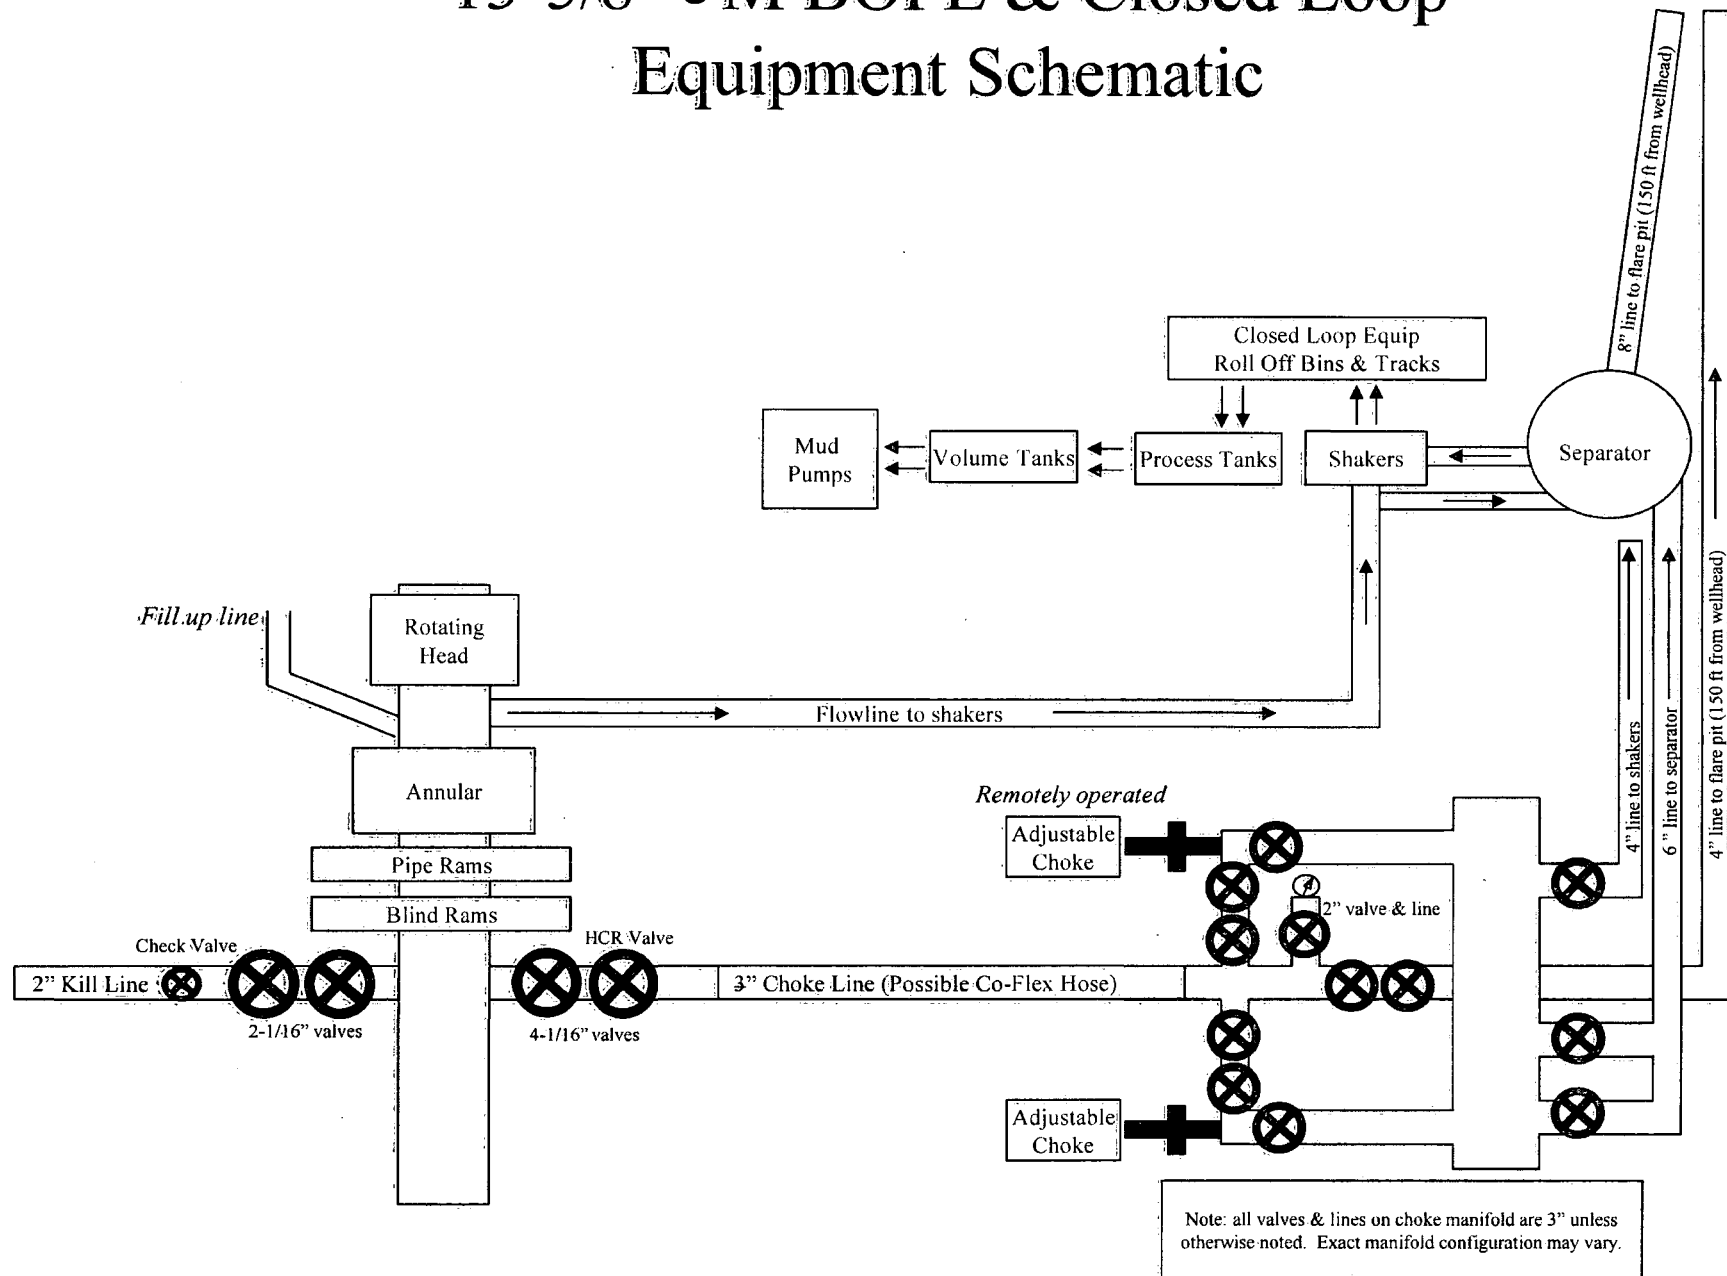



## Casing Assumptions and Load Cases

### Production

All casing design assumptions were ran in Stress Check to determine safety factor which meet or exceed both Devon Energy and BLM minimum requirements. All casing strings will be filled while running in hole in order to not exceed collapse rating of the pipe.

Production Casing Burst Design		
Load Case	External Pressure	Internal Pressure
Pressure Test	Formation Pore Pressure	Fluid in hole (water or produced water) + test psi
Tubing Leak	Formation Pore Pressure	Packer @ KOP, leak below surface 8.6 ppg packer fluid
Stimulation	Formation Pore Pressure	Max frac pressure with heaviest frac fluid

Production Casing Collapse Design		
Load Case	External Pressure	Internal Pressure
Full Evacuation	Water gradient in cement, mud above TOC.	None
Cementing	Wet cement weight	Water (8.33ppg)

Production Casing Tension Design	
Load Case	Assumptions
Overpull	100kips
Runing in hole	2 ft/s
Service Loads	N/A



## Casing Assumptions and Load Cases

### Surface

All casing design assumptions were ran in Stress Check to determine safety factor which meet or exceed both Devon Energy and BLM minimum requirements. All casing strings will be filled while running in hole in order to not exceed collapse rating of the pipe.

Surface Casing Burst Design		
Load Case	External Pressure	Internal Pressure
Pressure Test	Formation Pore Pressure	Max mud weight of next hole-section plus Test psi
Drill Ahead	Formation Pore Pressure	Max mud weight of next hole section
Displace to Gas	Formation Pore Pressure	Dry gas from next casing point

Surface Casing Collapse Design		
Load Case	External Pressure	Internal Pressure
Full Evacuation	Water gradient in cement, mud above TOC	None
Cementing	Wet cement weight	Water (8.33ppg)

Surface Casing Tension Design	
Load Case	Assumptions
Overpull	100kips
Runing in hole	3 ft/s
Service Loads	N/A



## Casing Assumptions and Load Cases

### Intermediate

All casing design assumptions were ran in Stress Check to determine safety factor which meet or exceed both Devon Energy and BLM minimum requirements. All casing strings will be filled while running in hole in order to not exceed collapse rating of the pipe.

Intermediate Casing Burst Design		
Load Case	External Pressure	Internal Pressure
Pressure Test	Formation Pore Pressure	Max mud weight of next hole-section plus Test psi
Drill Ahead	Formation Pore Pressure	Max mud weight of next hole section
Fracture @ Shoe	Formation Pore Pressure	Dry gas

Intermediate Casing Collapse Design		
Load Case	External Pressure	Internal Pressure
Full Evacuation	Water gradient in cement, mud above TOC	None
Cementing	Wet cement weight	Water (8.33ppg)

Intermediate Casing Tension Design	
Load Case	Assumptions
Overpull	100kips
Runing in hole	2 ft/s
Service Loads	N/A





**Devon Energy Center  
333 West Sheridan Avenue  
Oklahoma City, Oklahoma 73102-5015**

# **Hydrogen Sulfide (H<sub>2</sub>S) Contingency Plan**

**For**

**Todd 36-25 State Fed Com 235H**



**Sec-36 T-23S R-31E  
330' FSL & 1636' FEL  
LAT. = 32.2545750' N (NAD83)  
LONG = 103.7282716' W**

**Eddy County NM**



## Todd 36-25 State Fed Com 235H

This is an open drilling site. H<sub>2</sub>S monitoring equipment and emergency response equipment will be used within 500' of zones known to contain H<sub>2</sub>S, including warning signs, wind indicators and H<sub>2</sub>S monitor.

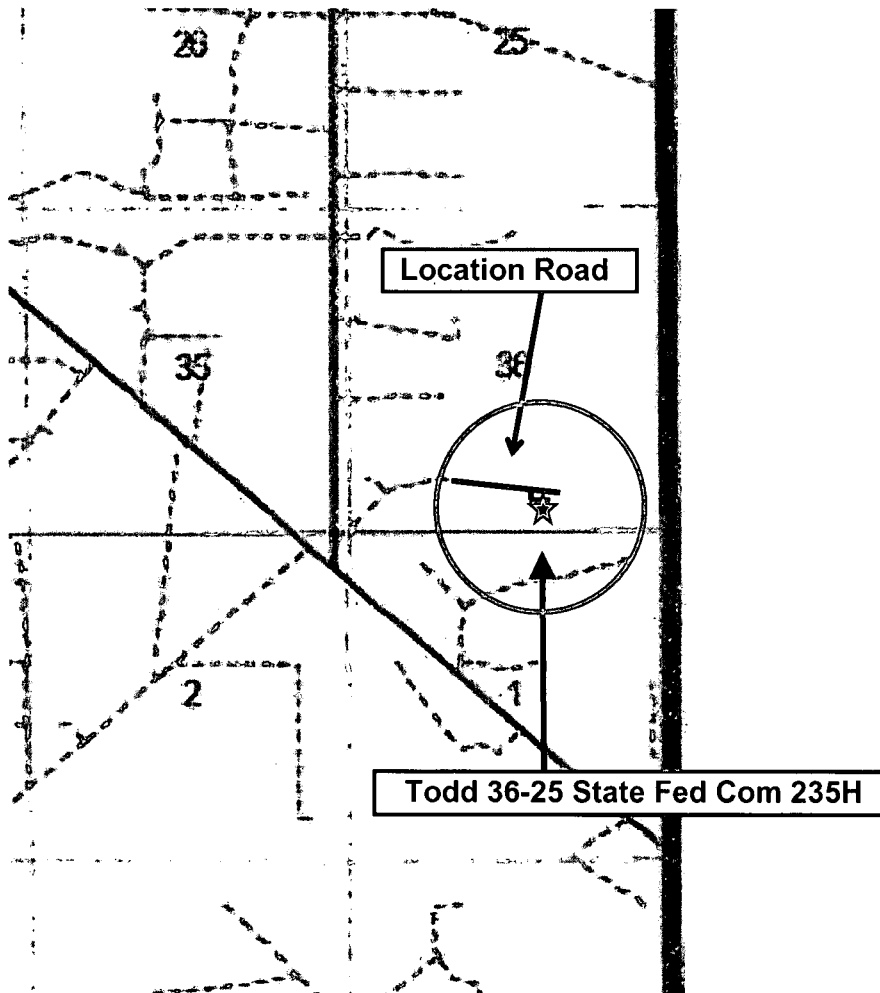

Assumed 100 ppm ROE = 3000' (Radius of Exposure)  
100 ppm H<sub>2</sub>S concentration shall trigger activation of this plan.

### Escape

Crews shall escape upwind of escaping gas in the event of an emergency release of gas. Escape can be facilitated from the location entrance road. Crews should then block the entrance to the location from the lease road so as not to allow anyone traversing into a hazardous area. The blockade should be at a safe distance outside of the ROE. There are no homes or buildings in or near the ROE.

**Assumed 100 ppm ROE = 3000'**



**100 ppm H<sub>2</sub>S concentration shall trigger activation of this plan.**

### **Emergency Procedures**

**In the event of a release of gas containing H<sub>2</sub>S, the first responder(s) must**

- **Isolate the area and prevent entry by other persons into the 100 ppm ROE.**
- **Evacuate any public places encompassed by the 100 ppm ROE.**
- **Be equipped with H<sub>2</sub>S monitors and air packs in order to control the release.**
- **Use the “buddy system” to ensure no injuries occur during the response**
- **Take precautions to avoid personal injury during this operation.**
- **Contact operator and/or local officials to aid in operation. See list of phone numbers attached.**
- **Have received training in the**
  - **Detection of H<sub>2</sub>S, and**
  - **Measures for protection against the gas,**
  - **Equipment used for protection and emergency response.**

### **Ignition of Gas Source**

Should control of the well be considered lost and ignition considered, take care to protect against exposure to Sulfur Dioxide (SO<sub>2</sub>). Intentional ignition must be coordinated with the NMOCD and local officials. Additionally the NM State Police may become involved. NM State Police shall be the Incident Command on scene of any major release. Take care to protect downwind whenever there is an ignition of the gas

### **Characteristics of H<sub>2</sub>S and SO<sub>2</sub>**

<b>Common Name</b>	<b>Chemical Formula</b>	<b>Specific Gravity</b>	<b>Threshold Limit</b>	<b>Hazardous Limit</b>	<b>Lethal Concentration</b>
<b>Hydrogen Sulfide</b>	<b>H<sub>2</sub>S</b>	<b>1.189 Air = 1</b>	<b>10 ppm</b>	<b>100 ppm/hr</b>	<b>600 ppm</b>
<b>Sulfur Dioxide</b>	<b>SO<sub>2</sub></b>	<b>2.21 Air = 1</b>	<b>2 ppm</b>	<b>N/A</b>	<b>1000 ppm</b>

### **Contacting Authorities**

Devon Energy Corp. personnel must liaison with local and state agencies to ensure a proper response to a major release. Additionally, the OCD must be notified of the release as soon as possible but no later than 4 hours. Agencies will ask for information such as type and volume of release, wind direction, location of release, etc. Be prepared with all information available. The following call list of essential and potential responders has been prepared for use during a release. Devon Energy Corp. Company response must be in coordination with the State of New Mexico's 'Hazardous Materials Emergency Response Plan' (HMER)



## **Hydrogen Sulfide Drilling Operation Plan**

### **I. HYDROGEN SULFIDE (H<sub>2</sub>S) TRAINING**

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

1. The hazards and characteristics of hydrogen sulfide (H<sub>2</sub>S)
2. The proper use and maintenance of personal protective equipment and life support systems.
3. The proper use of H<sub>2</sub>S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
4. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

1. The effects of H<sub>2</sub>S metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
2. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
3. The contents and requirements of the H<sub>2</sub>S Drilling Operations Plan and Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H<sub>2</sub>S zone (within 3 days or 500 feet) and weekly H<sub>2</sub>S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H<sub>2</sub>S Drilling Operations Plan and the Public Protection Plan.

### **II. HYDROGEN SULFIDE TRAINING**

Note: All H<sub>2</sub>S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H<sub>2</sub>S.



## **1. Well Control Equipment**

- A. Flare line
- B. Choke manifold – Remotely Operated
- C. Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit
- D. Auxiliary equipment may include if applicable: annular preventer and rotating head.
- E. Mud/Gas Separator

## **2. Protective equipment for essential personnel:**

30-minute SCBA units located at briefing areas, as indicated on well site diagram, with escape units available in the top doghouse. As it may be difficult to communicate audibly while wearing these units, hand signals shall be utilized.

## **3. H<sub>2</sub>S detection and monitoring equipment:**

Portable H<sub>2</sub>S monitors positioned on location for best coverage and response. These units have warning lights which activate when H<sub>2</sub>S levels reach 10 ppm and audible sirens which activate at 15 ppm. Sensor locations:

- Bell nipple
- Possum Belly/Shale shaker
- Rig floor
- Choke manifold
- Cellar

### **Visual warning systems:**

- A. Wind direction indicators as shown on well site diagram
- B. Caution/ Danger signs shall be posted on roads providing direct access to locations. Signs will be painted a high visibility yellow with black lettering of sufficient size to be reasonable distance from the immediate location. Bilingual signs will be used when appropriate.



**4. Mud program:**

The mud program has been designed to minimize the volume of H<sub>2</sub>S circulated to surface. Proper mud weight, safe drilling practices and the use of H<sub>2</sub>S scavengers will minimize hazards when penetrating H<sub>2</sub>S bearing zones.

**5. Metallurgy:**

- A. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold lines, and valves shall be H<sub>2</sub>S trim.
- B. All elastomers used for packing and seals shall be H<sub>2</sub>S trim.

**6. Communication:**

- A. Company personnel have/use cellular telephones in the field.
- B. Land line (telephone) communications at Office

**7. Well testing:**

- A. Drill stem testing will be performed with a minimum number of personnel in the immediate vicinity, which are necessary to safety and adequately conduct the test. The drill stem testing will be conducted during daylight hours and formation fluids will not be flowed to the surface. All drill-stem-testing operations conducted in an H<sub>2</sub>S environment will use the closed chamber method of testing.
- B. There will be no drill stem testing.



<b>Devon Energy Corp. Company Call List</b>		
Drilling Supervisor – Basin – Mark Kramer		405-823-4796
EHS Professional – Laura Wright		405-439-8129
<b>Agency Call List</b>		
<b>Lea County (575)</b>	<b>Hobbs</b>	
	Lea County Communication Authority	393-3981
	State Police	392-5588
	City Police	397-9265
	Sheriff's Office	393-2515
	<b>Ambulance</b>	<b>911</b>
	Fire Department	397-9308
	LEPC (Local Emergency Planning Committee)	393-2870
	NMOCD	393-6161
	US Bureau of Land Management	393-3612
<b>Eddy County (575)</b>	<b>Carlsbad</b>	
	State Police	885-3137
	City Police	885-2111
	Sheriff's Office	887-7551
	<b>Ambulance</b>	<b>911</b>
	Fire Department	885-3125
	LEPC (Local Emergency Planning Committee)	887-3798
	US Bureau of Land Management	887-6544
	NM Emergency Response Commission (Santa Fe)	(505) 476-9600
	24 HR	(505) 827-9126
	National Emergency Response Center	(800) 424-8802
	National Pollution Control Center: Direct	(703) 872-6000
	For Oil Spills	(800) 280-7118
	<b>Emergency Services</b>	
	Wild Well Control	(281) 784-4700
	Cudd Pressure Control	(915) 699-0139 (915) 563-3356
	Halliburton	(575) 746-2757
	B. J. Services	(575) 746-3569
<b>Give GPS position:</b>	Native Air – Emergency Helicopter – Hobbs	(575) 392-6429
	Flight For Life - Lubbock, TX	(806) 743-9911
	Aerocare - Lubbock, TX	(806) 747-8923
	Med Flight Air Amb - Albuquerque, NM	(575) 842-4433
	Lifeguard Air Med Svc. Albuquerque, NM	(800) 222-1222
	Poison Control (24/7)	(575) 272-3115
	Oil & Gas Pipeline 24 Hour Service	(800) 364-4366
	NOAA – Website - <a href="http://www.nhc.noaa.gov">www.nhc.noaa.gov</a>	



# **WCDSC Permian NM**

Eddy County (NAD 83 NM Eastern)

Sec. 36-T23S-R31E

Todd 36\_25 State Fed Com 235H

Wellbore #1

Permit Plan 1

## **Anticollision Report**

04 October, 2018



# Anticollision Report

Company:	WCDSC Permian NM	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Project:	Eddy County (NAD 83 NM Eastern)	TVD Reference:	RKB @ 3533.80ft
Reference Site:	Sec. 36-T23S-R31E	MD Reference:	RKB @ 3533.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore:	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

Reference	Permit Plan 1		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	MD Interval 50.00ft	Error Model:	ISCWSA
Depth Range:	Unlimited	Scan Method:	Closest Approach 3D
Results Limited by:	Maximum center-center distance of 1,500.00 ft	Error Surface:	Pedal Curve
Warning Levels Evaluated at:	2.00 Sigma	Casing Method:	Not applied

Survey Tool Program		Date	10/4/2018		
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description	
0.00	20,908.38	Permit Plan 1 (Wellbore #1)	MWD+HDGM	OWSG MWD + HDGM	

Summary						
Site Name	Reference Measured Depth (ft)	Offset Measured Depth (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
Sec. 25-T23S-R31E						
Aldabra 25 Fed 3H - Wellbore #1 - Wellbore #1						Out of range
Aldabra 25 Fed 6H - Wellbore #1 - Wellbore #1						Out of range
Aldabra 25 Fed 7H - Wellbore #1 - Wellbore #1						Out of range
Aldabra 25 Fed Com 1H - Wellbore #1 - Wellbore #1						Out of range
Aldabra 25 Fed Com 2H - Wellbore #1 - Wellbore #1						Out of range
Todd 25 Fed 001Z SWD (Offset) - Wellbore #1 - Wellbor						Out of range
Sec. 36-T23S-R31E						
Todd 36 State 01 SWD - Wellbore #1 - Wellbore #1						Out of range
Todd 36 State 231H - Wellbore #1 - Permit Plan 1						Out of range
Todd 36_25 State Fed Com 232H - Wellbore #1 - Origina						Out of range
Todd 36_25 State Fed Com 232H - Wellbore #1 - Permit						Out of range
Todd 36_25 State Fed Com 233H - Wellbore #1 - Permit	2,500.00	2,499.20	60.00	42.50	3.429	Alert, CC, ES
Todd 36_25 State Fed Com 233H - Wellbore #1 - Permit	2,550.00	2,548.76	60.40	42.55	3.385	Alert, SF
Todd 36-25 State Fed Com 230H - Wellbore #1 - Permit						Out of range
Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit	2,500.00	2,500.30	30.02	12.51	1.715	Minor Risk, CC
Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit	2,550.00	2,549.70	30.23	12.37	1.693	Minor Risk, ES, SF
Todd 36B State 20H (Offset) - Wellbore #1 - Wellbore #1	9,143.88	13,975.00	412.76	263.11	2.758	Alert, CC, ES, SF

Offset Design		Sec. 36-T23S-R31E - Todd 36_25 State Fed Com 233H - Wellbore #1 - Permit Plan 1										Offset Site Error:		0.00 ft
Survey Program:		0-MWD+HDGM										Offset Well Error:		0.50 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth	Vertical Depth	Measured Depth	Vertical Depth	Reference	Offset	Highside Toolface	Offset Wellbore Centre		Between Centres	Between Ellipses	Minimum Separation	Separation Factor		
(ft)	(ft)	(ft)	(ft)	(ft)	(ft)	(°)	+N-S (ft)	+E/-W (ft)	(ft)	(ft)	(ft)			
0.00	0.00	0.80	-0.80	0.50	0.50	-90.32	-0.34	-60.00	60.00					
50.00	50.00	49.20	49.20	0.50	0.50	-90.32	-0.34	-60.00	60.00	59.00	1.01	59.625		
100.00	100.00	100.80	99.20	0.52	0.52	-90.32	-0.34	-60.00	60.00	58.97	1.04	57.905		
150.00	150.00	149.20	149.20	0.59	0.59	-90.32	-0.34	-60.00	60.00	58.83	1.18	50.896		
200.00	200.00	200.80	199.20	0.70	0.70	-90.32	-0.34	-60.00	60.00	58.60	1.41	42.671		
250.00	250.00	249.20	249.20	0.84	0.84	-90.32	-0.34	-60.00	60.00	58.33	1.67	35.864		
300.00	300.00	300.80	299.20	0.99	0.99	-90.32	-0.34	-60.00	60.00	58.03	1.98	30.349		
350.00	350.00	349.20	349.20	1.15	1.14	-90.32	-0.34	-60.00	60.00	57.72	2.29	26.221		
400.00	400.00	400.80	399.20	1.31	1.31	-90.32	-0.34	-60.00	60.00	57.38	2.82	22.895		
450.00	450.00	449.20	449.20	1.48	1.47	-90.32	-0.34	-60.00	60.00	57.05	2.95	20.341		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design												Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM												Offset Well Error:	0.50 ft
Sec. 36-T23S-R31E - Todd 36_25 State Fed Com 233H - Wellbore #1 - Permit Plan 1													
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		Minimum Separation (ft)	Separation Factor	Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)		+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)			
500.00	500.00	500.80	499.20	1.65	1.65	-90.32	-0.34	-60.00	60.00	56.71	3.29	18.211	
550.00	550.00	549.20	549.20	1.82	1.81	-90.32	-0.34	-60.00	60.00	56.37	3.63	16.518	
600.00	600.00	600.80	599.20	1.99	1.99	-90.32	-0.34	-60.00	60.00	56.02	3.98	15.061	
650.00	650.00	649.20	649.20	2.16	2.16	-90.32	-0.34	-60.00	60.00	55.68	4.33	13.870	
700.00	700.00	700.80	699.20	2.34	2.34	-90.32	-0.34	-60.00	60.00	55.32	4.68	12.818	
750.00	750.00	749.20	749.20	2.51	2.51	-90.32	-0.34	-60.00	60.00	54.98	5.03	11.937	
800.00	800.00	800.80	799.20	2.69	2.69	-90.32	-0.34	-60.00	60.00	54.62	5.38	11.145	
850.00	850.00	849.20	849.20	2.87	2.86	-90.32	-0.34	-60.00	60.00	54.27	5.73	10.470	
900.00	900.00	900.80	899.20	3.04	3.05	-90.32	-0.34	-60.00	60.00	53.91	6.09	9.853	
950.00	950.00	949.20	949.20	3.22	3.22	-90.32	-0.34	-60.00	60.00	53.57	6.44	9.320	
1,000.00	1,000.00	1,000.80	999.20	3.40	3.40	-90.32	-0.34	-60.00	60.00	53.21	6.80	8.827	
1,050.00	1,050.00	1,049.20	1,049.20	3.58	3.57	-90.32	-0.34	-60.00	60.00	52.86	7.15	8.395	
1,100.00	1,100.00	1,100.80	1,099.20	3.75	3.76	-90.32	-0.34	-60.00	60.00	52.50	7.51	7.992	
1,150.00	1,150.00	1,149.20	1,149.20	3.93	3.93	-90.32	-0.34	-60.00	60.00	52.15	7.86	7.636	
1,200.00	1,200.00	1,200.80	1,199.20	4.11	4.11	-90.32	-0.34	-60.00	60.00	51.79	8.22	7.301	
1,250.00	1,250.00	1,249.20	1,249.20	4.29	4.28	-90.32	-0.34	-60.00	60.00	51.43	8.57	7.002	
1,300.00	1,300.00	1,300.80	1,299.20	4.46	4.47	-90.32	-0.34	-60.00	60.00	51.07	8.93	6.719	
1,350.00	1,350.00	1,349.20	1,349.20	4.64	4.64	-90.32	-0.34	-60.00	60.00	50.72	9.28	6.465	
1,400.00	1,400.00	1,400.80	1,399.20	4.82	4.82	-90.32	-0.34	-60.00	60.00	50.36	9.64	6.222	
1,450.00	1,450.00	1,449.20	1,449.20	5.00	5.00	-90.32	-0.34	-60.00	60.00	50.01	9.99	6.004	
1,500.00	1,500.00	1,500.80	1,499.20	5.18	5.18	-90.32	-0.34	-60.00	60.00	49.65	10.36	5.793	
1,550.00	1,550.00	1,549.20	1,549.20	5.36	5.35	-90.32	-0.34	-60.00	60.00	49.30	10.71	5.603	
1,600.00	1,600.00	1,600.80	1,599.20	5.53	5.54	-90.32	-0.34	-60.00	60.00	48.93	11.07	5.420	
1,650.00	1,650.00	1,649.20	1,649.20	5.71	5.71	-90.32	-0.34	-60.00	60.00	48.58	11.42	5.253	
1,700.00	1,700.00	1,700.80	1,699.20	5.89	5.89	-90.32	-0.34	-60.00	60.00	48.22	11.79	5.091	
1,750.00	1,750.00	1,749.20	1,749.20	6.07	6.07	-90.32	-0.34	-60.00	60.00	47.87	12.14	4.944	Alert
1,800.00	1,800.00	1,800.80	1,799.20	6.25	6.25	-90.32	-0.34	-60.00	60.00	47.50	12.50	4.800	Alert
1,850.00	1,850.00	1,849.20	1,849.20	6.43	6.42	-90.32	-0.34	-60.00	60.00	47.15	12.85	4.669	Alert
1,900.00	1,900.00	1,900.80	1,899.20	6.61	6.61	-90.32	-0.34	-60.00	60.00	46.79	13.21	4.541	Alert
1,950.00	1,950.00	1,949.20	1,949.20	6.78	6.78	-90.32	-0.34	-60.00	60.00	46.44	13.57	4.423	Alert
2,000.00	2,000.00	2,000.80	1,999.20	6.96	6.97	-90.32	-0.34	-60.00	60.00	46.07	13.93	4.308	Alert
2,050.00	2,050.00	2,049.20	2,049.20	7.14	7.14	-90.32	-0.34	-60.00	60.00	45.72	14.28	4.202	Alert
2,100.00	2,100.00	2,100.80	2,099.20	7.32	7.32	-90.32	-0.34	-60.00	60.00	45.36	14.64	4.097	Alert
2,150.00	2,150.00	2,149.20	2,149.20	7.50	7.50	-90.32	-0.34	-60.00	60.00	45.01	15.00	4.001	Alert
2,200.00	2,200.00	2,200.80	2,199.20	7.68	7.68	-90.32	-0.34	-60.00	60.00	44.64	15.36	3.907	Alert
2,250.00	2,250.00	2,249.20	2,249.20	7.86	7.85	-90.32	-0.34	-60.00	60.00	44.29	15.71	3.819	Alert
2,300.00	2,300.00	2,300.80	2,299.20	8.04	8.04	-90.32	-0.34	-60.00	60.00	43.93	16.08	3.733	Alert
2,350.00	2,350.00	2,349.20	2,349.20	8.22	8.21	-90.32	-0.34	-60.00	60.00	43.58	16.43	3.653	Alert
2,400.00	2,400.00	2,400.80	2,399.20	8.39	8.40	-90.32	-0.34	-60.00	60.00	43.21	16.79	3.574	Alert
2,450.00	2,450.00	2,449.20	2,449.20	8.57	8.57	-90.32	-0.34	-60.00	60.00	42.86	17.14	3.500	Alert
2,500.00	2,500.00	2,499.20	2,499.20	8.75	8.75	-90.32	-0.34	-60.00	60.00	42.50	17.50	3.429	Alert, CC, ES
2,550.00	2,550.00	2,548.76	2,548.76	8.93	8.92	166.43	-0.45	-60.18	60.40	42.55	17.84	3.385	Alert, SF
2,600.00	2,599.99	2,598.29	2,598.29	9.10	9.09	166.27	-0.77	-60.73	61.58	43.40	18.19	3.366	Alert
2,650.00	2,649.98	2,647.78	2,647.77	9.27	9.26	166.00	-1.32	-61.64	63.57	45.05	18.52	3.433	Alert
2,700.00	2,699.96	2,697.22	2,697.18	9.44	9.42	165.66	-2.09	-62.91	66.35	47.50	18.85	3.520	Alert
2,750.00	2,749.92	2,746.58	2,746.50	9.61	9.58	165.26	-3.08	-64.55	69.93	50.75	19.18	3.646	Alert
2,800.00	2,799.86	2,795.85	2,795.71	9.78	9.75	164.83	-4.28	-66.54	74.30	54.80	19.50	3.809	Alert
2,850.00	2,849.78	2,845.00	2,844.79	9.95	9.92	164.37	-5.70	-68.89	79.48	59.64	19.83	4.007	Alert
2,900.00	2,899.68	2,894.01	2,893.70	10.12	10.08	163.91	-7.34	-71.60	85.44	65.29	20.16	4.239	Alert
2,950.00	2,949.54	2,942.88	2,942.44	10.29	10.25	163.46	-9.18	-74.65	92.21	71.72	20.48	4.501	Alert
3,000.00	2,999.37	2,992.08	2,991.48	10.46	10.41	163.05	-11.20	-78.00	99.66	78.66	20.82	4.789	Alert
3,050.00	3,049.16	3,041.44	3,040.69	10.64	10.58	162.76	-13.24	-81.39	107.59	86.44	21.15	5.086	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36_25 State Fed Com 233H - Wellbore #1 - Permit Plan 1													0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:
													0.50 ft
Reference	Offset	Semi Major Axis		Distance		Minimum		Separation		Warning			
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
3,100.00	3,098.90	3,109.25	3,089.83	10.81	10.81	162.56	-15.28	-84.77	115.91	94.36	21.55	5.378	
3,150.00	3,148.61	3,139.98	3,138.90	10.99	10.92	162.45	-17.32	-88.15	124.64	102.82	21.83	5.711	
3,200.00	3,198.26	3,189.13	3,187.90	11.16	11.09	162.40	-19.36	-91.52	133.79	111.62	22.16	6.036	
3,250.00	3,247.86	3,238.21	3,236.82	11.34	11.26	162.41	-21.39	-94.89	143.34	120.84	22.50	6.370	
3,300.00	3,297.40	3,287.21	3,285.66	11.52	11.43	162.47	-23.42	-98.25	153.30	130.46	22.84	6.712	
3,350.00	3,346.89	3,336.12	3,334.42	11.70	11.60	162.55	-25.44	-101.60	163.67	140.49	23.18	7.061	
3,400.00	3,396.30	3,384.95	3,383.09	11.88	11.77	162.67	-27.46	-104.95	174.44	150.92	23.52	7.418	
3,450.00	3,445.65	3,433.68	3,431.66	12.06	11.94	162.81	-29.48	-108.29	185.62	161.77	23.86	7.781	
3,500.00	3,494.97	3,482.36	3,480.18	12.24	12.11	162.98	-31.49	-111.63	197.02	172.83	24.20	8.143	
3,550.00	3,544.28	3,531.04	3,528.71	12.43	12.28	163.14	-33.51	-114.97	208.42	183.89	24.53	8.495	
3,600.00	3,593.59	3,579.72	3,577.23	12.61	12.45	163.28	-35.52	-118.31	219.83	194.95	24.87	8.837	
3,650.00	3,642.90	3,628.40	3,625.75	12.80	12.62	163.40	-37.54	-121.64	231.23	206.01	25.22	9.170	
3,700.00	3,692.21	3,677.08	3,674.28	12.98	12.79	163.52	-39.55	-124.98	242.63	217.08	25.56	9.494	
3,750.00	3,741.53	3,725.75	3,722.80	13.17	12.97	163.62	-41.56	-128.32	254.04	228.14	25.90	9.809	
3,800.00	3,790.84	3,774.43	3,771.32	13.36	13.14	163.71	-43.58	-131.66	265.45	239.21	26.24	10.116	
3,850.00	3,840.15	3,823.11	3,819.85	13.55	13.31	163.80	-45.59	-135.00	276.85	250.27	26.58	10.414	
3,900.00	3,889.46	3,871.79	3,868.37	13.74	13.48	163.88	-47.61	-138.34	288.26	261.33	26.93	10.705	
3,950.00	3,938.77	3,920.47	3,916.89	13.93	13.66	163.95	-49.62	-141.68	299.67	272.40	27.27	10.988	
4,000.00	3,988.09	3,969.15	3,965.42	14.12	13.83	164.02	-51.64	-145.01	311.08	283.46	27.62	11.264	
4,050.00	4,037.40	4,017.83	4,013.94	14.32	14.00	164.08	-53.65	-148.35	322.49	294.52	27.96	11.532	
4,100.00	4,086.71	4,066.51	4,062.46	14.51	14.18	164.14	-55.67	-151.69	333.89	305.58	28.31	11.795	
4,150.00	4,136.02	4,115.19	4,110.99	14.70	14.35	164.20	-57.68	-155.03	345.30	316.65	28.66	12.050	
4,200.00	4,185.33	4,163.87	4,159.51	14.90	14.53	164.25	-59.70	-158.37	356.71	327.71	29.00	12.299	
4,250.00	4,234.65	4,212.55	4,208.03	15.09	14.70	164.30	-61.71	-161.71	368.12	338.77	29.35	12.542	
4,300.00	4,283.96	4,261.23	4,256.56	15.29	14.88	164.34	-63.73	-165.05	379.53	349.83	29.70	12.780	
4,350.00	4,333.27	4,309.91	4,305.08	15.48	15.05	164.39	-65.74	-168.38	390.94	360.90	30.05	13.011	
4,400.00	4,382.58	4,358.59	4,353.60	15.68	15.23	164.43	-67.75	-171.72	402.35	371.96	30.40	13.237	
4,450.00	4,431.90	4,407.27	4,402.13	15.87	15.40	164.47	-69.77	-175.06	413.76	383.02	30.74	13.458	
4,500.00	4,481.21	4,455.95	4,450.65	16.07	15.58	164.50	-71.78	-178.40	425.18	394.08	31.09	13.674	
4,550.00	4,530.52	4,504.63	4,499.18	16.27	15.75	164.54	-73.80	-181.74	436.59	405.14	31.44	13.885	
4,600.00	4,579.83	4,553.31	4,547.70	16.47	15.93	164.57	-75.81	-185.08	448.00	416.20	31.79	14.091	
4,650.00	4,629.14	4,601.99	4,596.22	16.67	16.10	164.60	-77.83	-188.42	459.41	427.26	32.14	14.292	
4,700.00	4,678.46	4,650.67	4,644.75	16.86	16.28	164.63	-79.84	-191.75	470.82	438.32	32.50	14.489	
4,750.00	4,727.77	4,700.65	4,693.27	17.06	16.46	164.66	-81.86	-195.09	482.23	449.38	32.85	14.679	
4,800.00	4,777.08	4,748.03	4,741.79	17.26	16.63	164.68	-83.87	-198.43	493.64	460.44	33.20	14.869	
4,850.00	4,826.39	4,803.29	4,790.32	17.46	16.83	164.71	-85.89	-201.77	505.05	471.48	33.57	15.043	
4,900.00	4,875.70	4,845.39	4,838.84	17.66	16.99	164.73	-87.90	-205.11	516.47	482.56	33.90	15.234	
4,950.00	4,925.02	4,905.93	4,897.36	17.86	17.21	164.76	-89.92	-208.45	527.88	493.58	34.30	15.391	
5,000.00	4,974.33	4,942.75	4,935.89	18.06	17.34	164.78	-91.93	-211.78	539.29	504.68	34.61	15.583	
5,050.00	5,023.64	4,991.43	4,984.41	18.27	17.52	164.80	-93.95	-215.12	550.70	515.74	34.96	15.752	
5,100.00	5,072.95	5,040.11	5,032.93	18.47	17.70	164.82	-95.96	-218.46	562.11	526.80	35.31	15.917	
5,150.00	5,122.26	5,088.79	5,081.46	18.67	17.87	164.84	-97.97	-221.80	573.53	537.86	35.67	16.080	
5,200.00	5,171.58	5,137.47	5,129.98	18.87	18.05	164.86	-99.99	-225.14	584.94	548.92	36.02	16.239	
5,250.00	5,220.89	5,186.15	5,178.50	19.07	18.23	164.88	-102.00	-228.48	596.35	559.97	36.38	16.394	
5,300.00	5,270.20	5,234.83	5,227.03	19.28	18.41	164.90	-104.02	-231.82	607.76	571.03	36.73	16.547	
5,350.00	5,319.51	5,283.51	5,275.55	19.48	18.58	164.91	-106.03	-235.15	619.18	582.09	37.08	16.696	
5,400.00	5,368.83	5,332.19	5,324.07	19.68	18.76	164.93	-108.05	-238.49	630.59	593.15	37.44	16.843	
5,450.00	5,418.14	5,380.87	5,372.60	19.89	18.94	164.95	-110.06	-241.83	642.00	604.21	37.79	16.987	
5,500.00	5,467.45	5,429.55	5,421.12	20.09	19.12	164.96	-112.08	-245.17	653.41	615.26	38.15	17.128	
5,550.00	5,516.76	5,478.23	5,469.64	20.29	19.30	164.97	-114.09	-248.51	664.83	626.32	38.51	17.266	
5,600.00	5,566.07	5,526.91	5,518.17	20.50	19.48	164.99	-116.11	-251.85	676.24	637.38	38.86	17.402	
5,650.00	5,615.39	5,575.59	5,566.69	20.70	19.65	165.00	-118.12	-255.19	687.65	648.43	39.22	17.535	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

Company:	WCDSO Permian NM	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Project:	Eddy County (NAD 83 NM Eastern)	TVD Reference:	RKB @ 3533.80ft
Reference Site:	Sec. 36-T23S-R31E	MD Reference:	RKB @ 3533.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

Offset Design												Sec. 36-T23S-R31E - Todd 36_25 State Fed Com 233H - Wellbore #1 - Permit Plan 1		Offset Site Error: 0.00 ft	
Survey Program: 0-MWD+HDGM												Offset Well Error: 0.50 ft			
Reference		Offset		Semi Major Axis		Distance									
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning		
5,700.00	5,664.70	5,624.27	5,615.21	20.91	19.83	165.02	-120.14	-258.52	699.06	659.49	39.57	17.665			
5,750.00	5,714.01	5,672.95	5,663.74	21.11	20.01	165.03	-122.15	-261.86	710.48	670.55	39.93	17.793			
5,800.00	5,763.32	5,721.63	5,712.26	21.32	20.19	165.04	-124.16	-265.20	721.89	681.60	40.29	17.919			
5,850.00	5,812.63	5,770.31	5,760.78	21.52	20.37	165.05	-126.18	-268.54	733.30	692.66	40.64	18.043			
5,900.00	5,861.95	5,818.99	5,809.31	21.73	20.55	165.06	-128.19	-271.88	744.71	703.72	41.00	18.164			
5,950.00	5,911.26	5,867.67	5,857.83	21.93	20.73	165.08	-130.21	-275.22	756.13	714.77	41.36	18.283			
6,000.00	5,960.57	5,916.35	5,906.35	22.14	20.91	165.09	-132.22	-278.56	767.54	725.83	41.71	18.401			
6,050.00	6,009.88	5,965.03	5,954.88	22.34	21.08	165.10	-134.24	-281.89	778.95	736.88	42.07	18.516			
6,100.00	6,059.19	6,013.71	6,003.40	22.55	21.26	165.11	-136.25	-285.23	790.37	747.94	42.43	18.629			
6,150.00	6,108.51	6,062.39	6,051.92	22.76	21.44	165.12	-138.27	-288.57	801.78	758.99	42.79	18.740			
6,200.00	6,157.82	6,111.07	6,100.45	22.96	21.62	165.13	-140.28	-291.91	813.19	770.05	43.14	18.849			
6,250.00	6,207.13	6,159.75	6,148.97	23.17	21.80	165.14	-142.30	-295.25	824.60	781.10	43.50	18.956			
6,300.00	6,256.44	6,208.43	6,197.49	23.38	21.98	165.15	-144.31	-298.59	836.02	792.16	43.86	19.061			
6,350.00	6,305.76	6,257.11	6,246.02	23.58	22.16	165.16	-146.33	-301.93	847.43	803.21	44.22	19.165			
6,400.00	6,355.07	6,305.79	6,294.54	23.79	22.34	165.16	-148.34	-305.26	858.84	814.27	44.58	19.267			
6,450.00	6,404.38	6,354.47	6,343.06	24.00	22.52	165.17	-150.35	-308.60	870.26	825.32	44.93	19.367			
6,500.00	6,453.69	6,403.15	6,391.59	24.20	22.70	165.18	-152.37	-311.94	881.67	836.38	45.29	19.466			
6,550.00	6,503.00	6,451.83	6,440.11	24.41	22.88	165.19	-154.38	-315.28	893.08	847.43	45.65	19.563			
6,600.00	6,552.32	6,500.51	6,488.64	24.62	23.06	165.20	-156.40	-318.62	904.50	858.49	46.01	19.658			
6,650.00	6,601.63	6,549.19	6,537.16	24.83	23.24	165.20	-158.41	-321.96	915.91	869.54	46.37	19.752			
6,700.00	6,650.94	6,602.13	6,585.68	25.03	23.43	165.21	-160.43	-325.30	927.32	880.58	46.74	19.838			
6,750.00	6,700.25	6,646.55	6,634.21	25.24	23.60	165.22	-162.44	-328.63	938.74	891.65	47.09	19.936			
6,800.00	6,749.56	6,704.78	6,682.73	25.45	23.81	165.23	-164.46	-331.97	950.15	902.67	47.48	20.011			
6,850.00	6,798.88	6,743.90	6,731.25	25.66	23.96	165.23	-166.47	-335.31	961.56	913.75	47.81	20.113			
6,900.00	6,848.19	6,807.42	6,779.78	25.87	24.19	165.24	-168.49	-338.65	972.97	924.75	48.22	20.178			
6,950.00	6,897.50	6,841.26	6,828.30	26.08	24.32	165.25	-170.50	-341.99	984.39	935.86	48.53	20.286			
7,000.00	6,946.81	6,889.94	6,876.82	26.28	24.50	165.25	-172.52	-345.33	995.80	946.92	48.89	20.370			
7,050.00	6,996.12	6,938.62	6,925.35	26.49	24.68	165.26	-174.53	-348.67	1,007.21	957.97	49.25	20.453			
7,100.00	7,045.44	6,987.30	6,973.87	26.70	24.86	165.27	-176.55	-352.00	1,018.63	969.02	49.61	20.534			
7,150.00	7,094.75	7,035.98	7,022.39	26.91	25.04	165.27	-178.56	-355.34	1,030.04	980.07	49.97	20.615			
7,200.00	7,144.06	7,084.66	7,070.92	27.12	25.22	165.28	-180.57	-358.68	1,041.45	991.13	50.33	20.694			
7,250.00	7,193.37	7,133.34	7,119.44	27.33	25.40	165.28	-182.59	-362.02	1,052.87	1,002.18	50.69	20.772			
7,300.00	7,242.69	7,182.02	7,167.96	27.54	25.58	165.29	-184.60	-365.36	1,064.28	1,013.23	51.05	20.849			
7,350.00	7,292.00	7,230.70	7,216.49	27.75	25.76	165.30	-186.62	-368.70	1,075.69	1,024.29	51.41	20.925			
7,400.00	7,341.31	7,279.38	7,265.01	27.95	25.94	165.30	-188.63	-372.03	1,087.11	1,035.34	51.77	20.999			
7,450.00	7,390.62	7,328.06	7,313.53	28.16	26.12	165.31	-190.65	-375.37	1,098.52	1,046.39	52.13	21.073			
7,500.00	7,439.93	7,376.74	7,362.06	28.37	26.30	165.31	-192.66	-378.71	1,109.93	1,057.44	52.49	21.145			
7,550.00	7,489.25	7,425.42	7,410.58	28.58	26.48	165.32	-194.68	-382.05	1,121.35	1,068.50	52.85	21.217			
7,600.00	7,538.56	7,474.10	7,459.10	28.79	26.67	165.32	-196.69	-385.39	1,132.76	1,079.55	53.21	21.287			
7,650.00	7,587.87	7,522.78	7,507.63	29.00	26.85	165.33	-198.71	-388.73	1,144.17	1,090.60	53.57	21.357			
7,700.00	7,637.18	7,571.46	7,556.15	29.21	27.03	165.33	-200.72	-392.07	1,155.59	1,101.65	53.94	21.426			
7,750.00	7,686.49	7,620.14	7,604.67	29.42	27.21	165.34	-202.74	-395.40	1,167.00	1,112.70	54.30	21.493			
7,800.00	7,735.81	7,668.82	7,653.20	29.63	27.39	165.34	-204.75	-398.74	1,178.41	1,123.76	54.66	21.560			
7,850.00	7,785.12	7,717.50	7,701.72	29.84	27.57	165.34	-206.76	-402.08	1,189.83	1,134.81	55.02	21.626			
7,900.00	7,834.43	7,766.18	7,750.24	30.05	27.75	165.35	-208.78	-405.42	1,201.24	1,145.86	55.38	21.690			
7,950.00	7,883.74	7,814.86	7,798.77	30.26	27.93	165.35	-210.79	-408.76	1,212.65	1,156.91	55.74	21.754			
8,000.00	7,933.05	7,863.54	7,847.29	30.47	28.11	165.36	-212.81	-412.10	1,224.07	1,167.96	56.10	21.818			
8,050.00	7,982.37	7,912.22	7,895.81	30.68	28.29	165.36	-214.82	-415.44	1,235.48	1,179.01	56.47	21.880			
8,100.00	8,031.68	7,960.90	7,944.34	30.89	28.47	165.37	-216.84	-418.77	1,246.89	1,190.07	56.83	21.941			
8,150.00	8,080.99	8,009.58	7,992.86	31.10	28.65	165.37	-218.85	-422.11	1,258.31	1,201.12	57.19	22.002			
8,200.00	8,130.30	8,058.26	8,041.38	31.31	28.84	165.37	-220.87	-425.45	1,269.72	1,212.17	57.55	22.062			
8,250.00	8,179.62	8,106.94	8,089.91	31.52	29.02	165.38	-222.88	-428.79	1,281.13	1,223.22	57.91	22.121			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36_25 State Fed Com 233H - Wellbore #1 - Permit Plan 1													0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error: 0.50 ft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
8,300.00	8,228.93	8,155.62	8,138.43	31.73	29.20	165.38	-224.90	-432.13	1,292.55	1,234.27	58.28	22.179	
8,350.00	8,278.24	8,204.30	8,186.95	31.94	29.38	165.39	-226.91	-435.47	1,303.96	1,245.32	58.64	22.237	
8,400.00	8,327.55	8,252.98	8,235.48	32.15	29.56	165.39	-228.93	-438.81	1,315.37	1,256.37	59.00	22.294	
8,450.00	8,376.86	8,301.66	8,284.00	32.36	29.74	165.39	-230.94	-442.14	1,326.79	1,267.42	59.36	22.350	
8,500.00	8,426.18	8,350.34	8,332.53	32.57	29.92	165.40	-232.95	-445.48	1,338.20	1,278.48	59.73	22.405	
8,550.00	8,475.49	8,400.98	8,381.05	32.78	30.11	165.40	-234.97	-448.82	1,349.62	1,289.52	60.10	22.458	
8,600.00	8,524.80	8,447.70	8,429.57	33.00	30.29	165.40	-236.98	-452.16	1,361.03	1,300.58	60.45	22.514	
8,650.00	8,574.11	8,503.62	8,478.10	33.21	30.49	165.41	-239.00	-455.50	1,372.44	1,311.60	60.84	22.558	
8,700.00	8,623.42	8,545.06	8,526.62	33.42	30.65	165.41	-241.01	-458.84	1,383.86	1,322.68	61.18	22.620	
8,750.00	8,672.74	8,606.26	8,575.14	33.63	30.88	165.41	-243.03	-462.18	1,395.27	1,333.68	61.59	22.656	
8,800.00	8,722.05	8,642.42	8,623.67	33.84	31.01	165.42	-245.04	-465.51	1,406.68	1,344.78	61.90	22.724	
8,850.00	8,771.36	8,691.10	8,672.19	34.05	31.19	165.42	-247.06	-468.85	1,418.10	1,355.83	62.27	22.775	
8,900.00	8,820.67	8,739.78	8,720.71	34.26	31.37	165.42	-249.07	-472.19	1,429.51	1,366.88	62.63	22.825	
8,950.00	8,869.98	8,788.46	8,769.24	34.47	31.55	165.43	-251.09	-475.53	1,440.92	1,377.93	62.99	22.874	
9,000.00	8,919.30	8,837.14	8,817.76	34.68	31.74	165.43	-253.10	-478.87	1,452.34	1,388.98	63.36	22.923	
9,050.00	8,968.61	8,885.82	8,866.28	34.89	31.92	165.43	-255.12	-482.21	1,463.75	1,400.03	63.72	22.972	
9,100.00	9,017.92	8,934.50	8,914.81	35.11	32.10	165.44	-257.13	-485.55	1,475.16	1,411.08	64.08	23.020	
9,150.00	9,067.23	8,983.18	8,963.33	35.32	32.28	165.44	-259.15	-488.88	1,486.58	1,422.13	64.45	23.067	
9,200.00	9,116.55	9,031.86	9,011.85	35.53	32.46	165.44	-261.16	-492.22	1,497.99	1,433.18	64.81	23.114	



# Anticollision Report

Company:	WCDSC Permian NM	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Project:	Eddy County (NAD 83 NM Eastern)	TVD Reference:	RKB @ 3533.80ft
Reference Site:	Sec. 36-T23S-R31E	MD Reference:	RKB @ 3533.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore:	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	0.00 ft
Sec. 36-T23S-R31E - Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit Plan 1												Offset Well Error:	0.50 ft
Survey Program: 0-MWD+HDGM													
Reference	Offset	Semi Major Axis		Distance		Minimum		Separation		Warning			
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
0.00	0.00	0.30	-0.30	0.50	0.50	-90.32	-0.17	-30.02	30.02				
50.00	50.00	49.70	49.70	0.50	0.50	-90.32	-0.17	-30.02	30.02	29.01	1.01	29.825	
100.00	100.00	100.30	99.70	0.52	0.52	-90.32	-0.17	-30.02	30.02	28.98	1.04	28.980	
150.00	150.00	149.70	149.70	0.59	0.59	-90.32	-0.17	-30.02	30.02	28.84	1.18	25.441	
200.00	200.00	200.30	199.70	0.70	0.70	-90.32	-0.17	-30.02	30.02	28.61	1.40	21.365	
250.00	250.00	249.70	249.70	0.84	0.84	-90.32	-0.17	-30.02	30.02	28.34	1.67	17.926	
300.00	300.00	300.30	299.70	0.99	0.99	-90.32	-0.17	-30.02	30.02	28.04	1.98	15.194	
350.00	350.00	349.70	349.70	1.15	1.14	-90.32	-0.17	-30.02	30.02	27.73	2.29	13.108	
400.00	400.00	400.30	399.70	1.31	1.31	-90.32	-0.17	-30.02	30.02	27.40	2.62	11.461	
450.00	450.00	449.70	449.70	1.48	1.48	-90.32	-0.17	-30.02	30.02	27.07	2.95	10.170	
500.00	500.00	500.30	499.70	1.65	1.65	-90.32	-0.17	-30.02	30.02	26.72	3.29	9.115	
550.00	550.00	549.70	549.70	1.82	1.82	-90.32	-0.17	-30.02	30.02	26.38	3.63	8.260	
600.00	600.00	600.30	599.70	1.99	1.99	-90.32	-0.17	-30.02	30.02	26.04	3.98	7.538	
650.00	650.00	649.70	649.70	2.16	2.16	-90.32	-0.17	-30.02	30.02	25.69	4.33	6.936	
700.00	700.00	700.30	699.70	2.34	2.34	-90.32	-0.17	-30.02	30.02	25.34	4.68	6.414	
750.00	750.00	749.70	749.70	2.51	2.51	-90.32	-0.17	-30.02	30.02	24.99	5.03	5.970	
800.00	800.00	800.30	799.70	2.69	2.69	-90.32	-0.17	-30.02	30.02	24.64	5.38	5.577	
850.00	850.00	849.70	849.70	2.87	2.87	-90.32	-0.17	-30.02	30.02	24.28	5.73	5.236	
900.00	900.00	900.30	899.70	3.04	3.04	-90.32	-0.17	-30.02	30.02	23.93	6.09	4.930 Alert	
950.00	950.00	949.70	949.70	3.22	3.22	-90.32	-0.17	-30.02	30.02	23.58	6.44	4.661 Alert	
1,000.00	1,000.00	1,000.30	999.70	3.40	3.40	-90.32	-0.17	-30.02	30.02	23.22	6.80	4.417 Alert	
1,050.00	1,050.00	1,049.70	1,049.70	3.58	3.57	-90.32	-0.17	-30.02	30.02	22.87	7.15	4.199 Alert	
1,100.00	1,100.00	1,100.30	1,099.70	3.75	3.75	-90.32	-0.17	-30.02	30.02	22.51	7.51	3.999 Alert	
1,150.00	1,150.00	1,149.70	1,149.70	3.93	3.93	-90.32	-0.17	-30.02	30.02	22.16	7.86	3.819 Alert	
1,200.00	1,200.00	1,200.30	1,199.70	4.11	4.11	-90.32	-0.17	-30.02	30.02	21.80	8.22	3.653 Alert	
1,250.00	1,250.00	1,249.70	1,249.70	4.29	4.29	-90.32	-0.17	-30.02	30.02	21.45	8.57	3.502 Alert	
1,300.00	1,300.00	1,300.30	1,299.70	4.46	4.47	-90.32	-0.17	-30.02	30.02	21.09	8.93	3.362 Alert	
1,350.00	1,350.00	1,349.70	1,349.70	4.64	4.64	-90.32	-0.17	-30.02	30.02	20.73	9.28	3.233 Alert	
1,400.00	1,400.00	1,400.30	1,399.70	4.82	4.82	-90.32	-0.17	-30.02	30.02	20.38	9.64	3.113 Alert	
1,450.00	1,450.00	1,449.70	1,449.70	5.00	5.00	-90.32	-0.17	-30.02	30.02	20.02	10.00	3.003 Alert	
1,500.00	1,500.00	1,500.30	1,499.70	5.18	5.18	-90.32	-0.17	-30.02	30.02	19.66	10.36	2.899 Alert	
1,550.00	1,550.00	1,549.70	1,549.70	5.36	5.35	-90.32	-0.17	-30.02	30.02	19.31	10.71	2.803 Alert	
1,600.00	1,600.00	1,600.30	1,599.70	5.53	5.54	-90.32	-0.17	-30.02	30.02	18.95	11.07	2.712 Alert	
1,650.00	1,650.00	1,649.70	1,649.70	5.71	5.71	-90.32	-0.17	-30.02	30.02	18.59	11.42	2.628 Alert	
1,700.00	1,700.00	1,700.30	1,699.70	5.89	5.89	-90.32	-0.17	-30.02	30.02	18.23	11.78	2.547 Alert	
1,750.00	1,750.00	1,749.70	1,749.70	6.07	6.07	-90.32	-0.17	-30.02	30.02	17.88	12.14	2.473 Minor Risk	
1,800.00	1,800.00	1,800.30	1,799.70	6.25	6.25	-90.32	-0.17	-30.02	30.02	17.52	12.50	2.402 Minor Risk	
1,850.00	1,850.00	1,849.70	1,849.70	6.43	6.43	-90.32	-0.17	-30.02	30.02	17.16	12.85	2.335 Minor Risk	
1,900.00	1,900.00	1,900.30	1,899.70	6.61	6.61	-90.32	-0.17	-30.02	30.02	16.80	13.21	2.272 Minor Risk	
1,950.00	1,950.00	1,949.70	1,949.70	6.78	6.78	-90.32	-0.17	-30.02	30.02	16.45	13.57	2.212 Minor Risk	
2,000.00	2,000.00	2,000.30	1,999.70	6.96	6.96	-90.32	-0.17	-30.02	30.02	16.09	13.93	2.155 Minor Risk	
2,050.00	2,050.00	2,049.70	2,049.70	7.14	7.14	-90.32	-0.17	-30.02	30.02	15.73	14.28	2.102 Minor Risk	
2,100.00	2,100.00	2,100.30	2,099.70	7.32	7.32	-90.32	-0.17	-30.02	30.02	15.37	14.64	2.050 Minor Risk	
2,150.00	2,150.00	2,149.70	2,149.70	7.50	7.50	-90.32	-0.17	-30.02	30.02	15.02	15.00	2.001 Minor Risk	
2,200.00	2,200.00	2,200.30	2,199.70	7.68	7.68	-90.32	-0.17	-30.02	30.02	14.66	15.36	1.954 Minor Risk	
2,250.00	2,250.00	2,249.70	2,249.70	7.86	7.86	-90.32	-0.17	-30.02	30.02	14.30	15.71	1.910 Minor Risk	
2,300.00	2,300.00	2,300.30	2,299.70	8.04	8.04	-90.32	-0.17	-30.02	30.02	13.94	16.07	1.867 Minor Risk	
2,350.00	2,350.00	2,349.70	2,349.70	8.22	8.21	-90.32	-0.17	-30.02	30.02	13.59	16.43	1.827 Minor Risk	
2,400.00	2,400.00	2,400.30	2,399.70	8.39	8.40	-90.32	-0.17	-30.02	30.02	13.23	16.79	1.788 Minor Risk	
2,450.00	2,450.00	2,449.70	2,449.70	8.57	8.57	-90.32	-0.17	-30.02	30.02	12.87	17.15	1.751 Minor Risk	
2,500.00	2,500.00	2,500.30	2,499.70	8.75	8.75	-90.32	-0.17	-30.02	30.02	12.51	17.51	1.715 Minor Risk, CC	
2,550.00	2,550.00	2,549.70	2,549.70	8.93	8.93	166.58	-0.17	-30.02	30.23	12.37	17.86	1.693 Minor Risk, ES, SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.50 ft
Reference	Offset	Semi Major Axis		Distance		Minimum		Separation		Warning				
Measured	Vertical	Measured	Vertical	Reference	Offset	Highside	Offset Wellbore Centre	Between	Between	Minimum	Separation	Factor		
Depth	Depth	Depth	Depth	(ft)	(ft)	Tooface	+N/-S	Centres	Ellipses	Separation	Factor			
(ft)	(ft)	(ft)	(ft)	(ft)	(ft)	(°)	(ft)	(ft)	(ft)	(ft)				
2,600.00	2,599.99	2,600.31	2,599.69	9.10	9.11	166.86	-0.17	-30.02	30.87	12.66	18.21	1.695 Minor Risk		
2,650.00	2,649.98	2,649.68	2,649.68	9.27	9.29	167.30	-0.17	-30.02	31.93	13.37	18.55	1.721 Minor Risk		
2,700.00	2,699.96	2,700.34	2,699.66	9.44	9.47	167.87	-0.17	-30.02	33.42	14.52	18.90	1.788 Minor Risk		
2,750.00	2,749.92	2,749.62	2,749.62	9.61	9.65	168.54	-0.17	-30.02	35.34	16.09	19.25	1.836 Minor Risk		
2,800.00	2,799.86	2,800.44	2,799.56	9.78	9.83	169.26	-0.17	-30.02	37.70	18.10	19.60	1.923 Minor Risk		
2,850.00	2,849.78	2,849.48	2,849.48	9.95	10.00	170.00	-0.17	-30.02	40.49	20.54	19.95	2.030 Minor Risk		
2,900.00	2,899.68	2,900.62	2,899.38	10.12	10.19	170.74	-0.17	-30.02	43.71	23.41	20.30	2.153 Minor Risk		
2,950.00	2,949.54	2,949.24	2,949.24	10.29	10.36	171.46	-0.17	-30.02	47.37	26.73	20.64	2.295 Minor Risk		
3,000.00	2,999.37	3,000.93	2,999.07	10.46	10.55	172.14	-0.17	-30.02	51.47	30.47	21.00	2.451 Minor Risk		
3,050.00	3,049.16	3,048.86	3,048.86	10.64	10.72	172.77	-0.17	-30.02	56.01	34.66	21.34	2.624 Alert		
3,100.00	3,098.90	3,101.40	3,098.60	10.81	10.91	173.36	-0.17	-30.02	60.98	39.28	21.70	2.810 Alert		
3,150.00	3,148.61	3,148.31	3,148.31	10.99	11.07	173.89	-0.17	-30.02	66.39	44.35	22.04	3.012 Alert		
3,200.00	3,198.26	3,202.04	3,197.96	11.16	11.27	174.38	-0.17	-30.02	72.24	49.83	22.40	3.224 Alert		
3,250.00	3,247.86	3,247.56	3,247.56	11.34	11.43	174.83	-0.17	-30.02	78.52	55.78	22.74	3.453 Alert		
3,300.00	3,297.40	3,302.90	3,297.10	11.52	11.63	175.23	-0.17	-30.02	85.24	62.13	23.11	3.689 Alert		
3,350.00	3,346.89	3,346.59	3,346.59	11.70	11.78	175.60	-0.17	-30.02	92.39	68.95	23.43	3.942 Alert		
3,400.00	3,396.30	3,404.00	3,396.00	11.88	11.99	175.93	-0.17	-30.02	99.97	76.16	23.81	4.198 Alert		
3,450.00	3,445.65	3,445.35	3,445.35	12.06	12.14	176.22	-0.17	-30.02	107.99	83.86	24.13	4.475 Alert		
3,500.00	3,494.97	3,505.33	3,494.67	12.24	12.35	176.49	-0.17	-30.02	116.24	91.72	24.52	4.741 Alert		
3,550.00	3,544.28	3,543.98	3,543.98	12.43	12.49	176.72	-0.17	-30.02	124.49	99.66	24.83	5.014		
3,600.00	3,593.59	3,606.71	3,593.29	12.61	12.71	176.93	-0.17	-30.02	132.75	107.52	25.23	5.262		
3,650.00	3,642.90	3,642.60	3,642.60	12.80	12.84	177.11	-0.17	-30.02	141.00	115.47	25.53	5.523		
3,700.00	3,692.21	3,708.09	3,691.91	12.98	13.08	177.27	-0.17	-30.02	149.26	123.32	25.94	5.755		
3,750.00	3,741.53	3,741.23	3,741.23	13.17	13.20	177.41	-0.17	-30.02	157.51	131.28	26.23	6.006		
3,800.00	3,790.84	3,809.46	3,790.54	13.36	13.44	177.54	-0.17	-30.02	165.77	139.12	26.65	6.221		
3,850.00	3,840.15	3,839.85	3,839.85	13.55	13.55	177.66	-0.17	-30.02	174.03	147.10	26.93	6.462		
3,900.00	3,889.46	3,889.16	3,889.16	13.74	13.73	177.76	-0.17	-30.02	182.29	155.01	27.28	6.682		
3,950.00	3,938.77	3,938.47	3,938.47	13.93	13.90	177.86	-0.17	-30.02	190.55	162.91	27.63	6.896		
4,000.00	3,988.09	3,987.79	3,987.79	14.12	14.08	177.95	-0.17	-30.02	198.81	170.82	27.98	7.104		
4,050.00	4,037.40	4,038.69	4,038.68	14.32	14.26	178.01	-0.27	-29.89	206.92	178.59	28.34	7.302		
4,100.00	4,086.71	4,090.25	4,090.25	14.51	14.43	178.01	-0.69	-29.30	214.55	185.86	28.69	7.477		
4,150.00	4,136.02	4,141.98	4,141.96	14.70	14.61	177.95	-1.46	-28.24	221.68	192.64	29.04	7.633		
4,200.00	4,185.33	4,193.85	4,193.79	14.90	14.78	177.82	-2.58	-26.70	228.30	198.91	29.39	7.769		
4,250.00	4,234.65	4,245.85	4,245.73	15.09	14.95	177.64	-4.04	-24.68	234.40	204.67	29.73	7.884		
4,300.00	4,283.96	4,297.97	4,297.76	15.29	15.12	177.42	-5.85	-22.18	240.00	209.93	30.07	7.980		
4,350.00	4,333.27	4,350.19	4,349.85	15.48	15.30	177.14	-8.02	-19.19	245.10	214.68	30.42	8.058		
4,400.00	4,382.58	4,402.50	4,401.99	15.68	15.47	176.81	-10.54	-15.72	249.68	218.93	30.76	8.118		
4,450.00	4,431.90	4,452.90	4,452.18	15.87	15.64	176.46	-13.20	-12.05	253.92	222.82	31.10	8.164		
4,500.00	4,481.21	4,502.70	4,501.77	16.07	15.81	176.13	-15.85	-8.41	258.15	226.70	31.45	8.209		
4,550.00	4,530.52	4,552.50	4,551.37	16.27	15.98	175.81	-18.49	-4.77	262.39	230.59	31.79	8.253		
4,600.00	4,579.83	4,602.30	4,600.96	16.47	16.15	175.50	-21.13	-1.12	266.63	234.49	32.14	8.296		
4,650.00	4,629.14	4,652.10	4,650.56	16.67	16.32	175.20	-23.77	2.52	270.89	238.40	32.49	8.338		
4,700.00	4,678.46	4,701.89	4,700.15	16.86	16.49	174.91	-26.41	6.16	275.15	242.31	32.84	8.379		
4,750.00	4,727.77	4,751.69	4,749.75	17.06	16.66	174.63	-29.05	9.80	279.41	246.23	33.19	8.419		
4,800.00	4,777.08	4,801.49	4,799.35	17.26	16.83	174.36	-31.70	13.44	283.69	250.15	33.54	8.459		
4,850.00	4,826.39	4,851.29	4,848.94	17.46	17.00	174.09	-34.34	17.09	287.97	254.08	33.89	8.498		
4,900.00	4,875.70	4,901.09	4,898.54	17.66	17.17	173.83	-36.98	20.73	292.25	258.01	34.24	8.536		
4,950.00	4,925.02	4,950.89	4,948.13	17.86	17.34	173.58	-39.62	24.37	296.54	261.95	34.59	8.573		
5,000.00	4,974.33	5,000.69	4,997.73	18.06	17.51	173.34	-42.26	28.01	300.84	265.90	34.94	8.610		
5,050.00	5,023.64	5,050.49	5,047.32	18.27	17.68	173.11	-44.90	31.65	305.14	269.85	35.29	8.646		
5,100.00	5,072.95	5,100.29	5,096.92	18.47	17.86	172.88	-47.55	35.30	309.45	273.80	35.65	8.681		
5,150.00	5,122.26	5,150.09	5,146.51	18.67	18.03	172.65	-50.19	38.94	313.76	277.76	36.00	8.716		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSO Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit Plan 1													0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:
													0.50 ft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
5,200.00	5,171.58	5,200.12	5,196.11	18.87	18.20	172.44	-52.83	42.58	318.08	281.72	36.35	8.749	
5,250.00	5,220.89	5,249.68	5,245.70	19.07	18.38	172.22	-55.47	46.22	322.40	285.69	36.71	8.783	
5,300.00	5,270.20	5,300.52	5,295.30	19.28	18.55	172.02	-58.11	49.86	326.73	289.66	37.07	8.815	
5,350.00	5,319.51	5,349.28	5,344.89	19.48	18.73	171.82	-60.75	53.50	331.05	293.64	37.42	8.847	
5,400.00	5,368.83	5,399.08	5,394.49	19.68	18.90	171.62	-63.40	57.15	335.39	297.61	37.77	8.879	
5,450.00	5,418.14	5,448.88	5,444.09	19.89	19.07	171.43	-66.04	60.79	339.72	301.60	38.13	8.910	
5,500.00	5,467.45	5,501.32	5,493.68	20.09	19.26	171.25	-68.68	64.43	344.07	305.57	38.50	8.938	
5,550.00	5,516.76	5,548.48	5,543.28	20.29	19.43	171.07	-71.32	68.07	348.41	309.57	38.84	8.970	
5,600.00	5,566.07	5,601.72	5,592.87	20.50	19.61	170.89	-73.96	71.71	352.76	313.55	39.21	8.996	
5,650.00	5,615.39	5,648.08	5,642.47	20.70	19.78	170.72	-76.61	75.36	357.11	317.55	39.56	9.027	
5,700.00	5,664.70	5,702.13	5,692.06	20.91	19.97	170.55	-79.25	79.00	361.46	321.53	39.93	9.052	
5,750.00	5,714.01	5,747.87	5,741.66	21.11	20.13	170.39	-81.89	82.64	365.82	325.54	40.27	9.083	
5,800.00	5,763.32	5,802.53	5,791.25	21.32	20.32	170.23	-84.53	86.28	370.18	329.53	40.65	9.106	
5,850.00	5,812.63	5,847.27	5,840.85	21.52	20.48	170.07	-87.17	89.92	374.54	333.55	40.99	9.137	
5,900.00	5,861.95	5,897.07	5,890.44	21.73	20.66	169.92	-89.81	93.56	378.91	337.56	41.35	9.163	
5,950.00	5,911.26	5,946.87	5,940.04	21.93	20.84	169.77	-92.46	97.21	383.27	341.56	41.71	9.189	
6,000.00	5,960.57	6,003.33	5,989.63	22.14	21.04	169.62	-95.10	100.85	387.64	345.55	42.09	9.209	
6,050.00	6,009.88	6,046.47	6,039.23	22.34	21.19	169.48	-97.74	104.49	392.02	349.59	42.43	9.239	
6,100.00	6,059.19	6,103.73	6,088.83	22.55	21.40	169.34	-100.38	108.13	396.39	353.57	42.82	9.258	
6,150.00	6,108.51	6,146.07	6,138.42	22.76	21.55	169.20	-103.02	111.77	400.77	357.62	43.15	9.287	
6,200.00	6,157.82	6,204.13	6,188.02	22.96	21.76	169.07	-105.66	115.42	405.15	361.61	43.54	9.305	
6,250.00	6,207.13	6,245.68	6,237.61	23.17	21.91	168.94	-108.31	119.06	409.53	365.66	43.88	9.334	
6,300.00	6,256.44	6,304.54	6,287.21	23.38	22.12	168.81	-110.95	122.70	413.92	369.65	44.27	9.350	
6,350.00	6,305.76	6,345.26	6,336.80	23.58	22.26	168.69	-113.59	126.34	418.30	373.70	44.60	9.379	
6,400.00	6,355.07	6,404.94	6,386.40	23.79	22.48	168.56	-116.23	129.98	422.69	377.69	45.00	9.394	
6,450.00	6,404.38	6,444.86	6,435.99	24.00	22.62	168.44	-118.87	133.63	427.08	381.76	45.32	9.423	
6,500.00	6,453.69	6,494.68	6,485.59	24.20	22.80	168.32	-121.52	137.27	431.47	385.78	45.69	9.444	
6,550.00	6,503.00	6,544.46	6,535.18	24.41	22.98	168.21	-124.16	140.91	435.86	389.81	46.05	9.465	
6,600.00	6,552.32	6,605.74	6,584.78	24.62	23.20	168.10	-126.80	144.55	440.26	393.81	46.45	9.477	
6,650.00	6,601.63	6,644.06	6,634.37	24.83	23.34	167.99	-129.44	148.19	444.66	397.88	46.78	9.506	
6,700.00	6,650.94	6,693.86	6,683.97	25.03	23.52	167.88	-132.08	151.83	449.06	401.91	47.14	9.526	
6,750.00	6,700.25	6,743.65	6,733.56	25.24	23.70	167.77	-134.72	155.48	453.45	405.95	47.51	9.545	
6,800.00	6,749.56	6,806.55	6,783.16	25.45	23.93	167.67	-137.37	159.12	457.86	409.94	47.92	9.555	
6,850.00	6,798.88	6,843.25	6,832.76	25.66	24.06	167.56	-140.01	162.76	462.26	414.02	48.23	9.584	
6,900.00	6,848.19	6,906.95	6,892.35	25.87	24.29	167.46	-142.65	166.40	466.66	418.02	48.65	9.593	
6,950.00	6,897.50	6,942.85	6,931.95	26.08	24.42	167.36	-145.29	170.04	471.07	422.11	48.96	9.621	
7,000.00	6,946.81	7,007.35	6,981.54	26.28	24.66	167.27	-147.93	173.69	475.48	426.10	49.38	9.629	
7,050.00	6,996.12	7,042.45	7,031.14	26.49	24.78	167.17	-150.57	177.33	479.89	430.19	49.89	9.657	
7,100.00	7,045.44	7,092.25	7,080.73	26.70	24.97	167.08	-153.22	180.97	484.29	434.23	50.06	9.674	
7,150.00	7,094.75	7,142.05	7,130.33	26.91	25.15	166.99	-155.86	184.61	488.71	438.28	50.43	9.692	
7,200.00	7,144.06	7,208.15	7,179.92	27.12	25.39	166.90	-158.50	188.25	493.12	442.27	50.85	9.697	
7,250.00	7,193.37	7,241.64	7,229.52	27.33	25.51	166.81	-161.14	191.89	497.53	446.37	51.16	9.725	
7,300.00	7,242.69	7,291.44	7,279.11	27.54	25.69	166.72	-163.78	195.54	501.95	450.42	51.52	9.742	
7,350.00	7,292.00	7,341.24	7,328.71	27.75	25.87	166.64	-166.43	199.18	506.36	454.47	51.89	9.758	
7,400.00	7,341.31	7,408.96	7,378.30	27.95	26.12	166.55	-169.07	202.82	510.78	458.46	52.32	9.762	
7,450.00	7,390.62	7,440.84	7,427.90	28.16	26.24	166.47	-171.71	206.46	515.20	462.57	52.62	9.790	
7,500.00	7,439.93	7,509.38	7,477.50	28.37	26.49	166.39	-174.35	210.10	519.62	466.56	53.06	9.793	
7,550.00	7,489.25	7,540.44	7,527.09	28.58	26.60	166.31	-176.99	213.75	524.04	470.68	53.36	9.821	
7,600.00	7,538.56	7,609.76	7,576.69	28.79	26.85	166.23	-179.63	217.39	528.46	474.66	53.80	9.823	
7,650.00	7,587.87	7,640.04	7,626.28	29.00	26.97	166.16	-182.28	221.03	532.88	478.78	54.09	9.851	
7,700.00	7,637.18	7,689.84	7,675.88	29.21	27.15	166.08	-184.92	224.67	537.30	482.84	54.46	9.866	
7,750.00	7,686.49	7,739.64	7,725.47	29.42	27.33	166.00	-187.56	228.31	541.72	486.90	54.83	9.880	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore:</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit Plan 1													0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:
													0.50 ft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
7,800.00	7,735.81	7,789.43	7,775.07	29.63	27.51	165.93	-190.20	231.96	546.15	490.95	55.20	9.894	
7,850.00	7,785.12	7,839.23	7,824.66	29.84	27.70	165.86	-192.84	235.60	550.57	495.01	55.57	9.909	
7,900.00	7,834.43	7,889.03	7,874.26	30.05	27.88	165.79	-195.48	239.24	555.00	499.07	55.93	9.922	
7,950.00	7,883.74	7,938.83	7,923.85	30.26	28.06	165.72	-198.13	242.88	559.43	503.13	56.30	9.936	
8,000.00	7,933.05	7,988.63	7,973.45	30.47	28.25	165.65	-200.77	246.52	563.86	507.19	56.67	9.950	
8,050.00	7,982.37	8,038.43	8,023.04	30.68	28.43	165.58	-203.41	250.16	568.28	511.25	57.04	9.963	
8,100.00	8,031.68	8,088.23	8,072.64	30.89	28.61	165.52	-206.05	253.81	572.71	515.31	57.41	9.976	
8,150.00	8,080.99	8,138.03	8,122.24	31.10	28.79	165.45	-208.69	257.45	577.14	519.37	57.78	9.989	
8,200.00	8,130.30	8,187.83	8,171.83	31.31	28.98	165.39	-211.33	261.09	581.58	523.43	58.15	10.002	
8,250.00	8,179.62	8,237.63	8,221.43	31.52	29.16	165.32	-213.98	264.73	586.01	527.49	58.52	10.014	
8,300.00	8,228.93	8,287.42	8,271.02	31.73	29.35	165.26	-216.62	268.37	590.44	531.55	58.89	10.027	
8,350.00	8,278.24	8,337.22	8,320.62	31.94	29.53	165.20	-219.26	272.02	594.87	535.62	59.25	10.039	
8,400.00	8,327.55	8,387.02	8,370.21	32.15	29.71	165.14	-221.90	275.66	599.31	539.68	59.62	10.051	
8,450.00	8,376.86	8,436.82	8,419.81	32.36	29.90	165.08	-224.54	279.30	603.74	543.75	59.99	10.063	
8,500.00	8,426.18	8,486.62	8,469.40	32.57	30.08	165.02	-227.19	282.94	608.18	547.81	60.36	10.075	
8,550.00	8,475.49	8,536.42	8,519.00	32.78	30.26	164.96	-229.83	286.58	612.61	551.88	60.73	10.087	
8,600.00	8,524.80	8,586.22	8,568.59	33.00	30.45	164.90	-232.47	290.22	617.05	555.94	61.10	10.098	
8,650.00	8,574.11	8,636.02	8,618.19	33.21	30.63	164.85	-235.11	293.87	621.49	560.01	61.47	10.110	
8,700.00	8,623.42	8,685.82	8,667.78	33.42	30.82	164.79	-237.75	297.51	625.92	564.08	61.84	10.121	
8,750.00	8,672.74	8,735.62	8,717.38	33.63	31.00	164.73	-240.39	301.15	630.36	568.15	62.22	10.132	
8,800.00	8,722.05	8,785.41	8,766.98	33.84	31.18	164.68	-243.04	304.79	634.80	572.21	62.59	10.143	
8,850.00	8,771.36	8,835.21	8,816.57	34.05	31.37	164.63	-245.68	308.43	639.24	576.28	62.96	10.154	
8,900.00	8,820.67	8,885.01	8,866.17	34.26	31.55	164.57	-248.32	312.08	643.68	580.35	63.33	10.164	
8,950.00	8,869.98	8,934.81	8,915.76	34.47	31.74	164.52	-250.96	315.72	648.12	584.42	63.70	10.175	
9,000.00	8,919.30	8,984.61	8,965.36	34.68	31.92	164.47	-253.60	319.36	652.56	588.49	64.07	10.185	
9,050.00	8,968.61	9,034.41	9,014.95	34.89	32.11	164.42	-256.24	323.00	657.00	592.56	64.44	10.196	
9,100.00	9,017.92	9,084.21	9,064.55	35.11	32.29	164.37	-258.89	326.64	661.44	596.63	64.81	10.206	
9,150.00	9,067.23	9,134.01	9,114.14	35.32	32.48	164.32	-261.53	330.29	665.89	600.70	65.18	10.216	
9,200.00	9,116.55	9,183.81	9,163.74	35.53	32.66	164.27	-264.17	333.93	670.33	604.78	65.55	10.226	
9,250.00	9,165.86	9,233.61	9,213.33	35.74	32.85	164.22	-266.81	337.57	674.77	608.85	65.93	10.235	
9,300.00	9,215.17	9,283.40	9,262.93	35.95	33.03	164.18	-269.45	341.21	679.22	612.92	66.30	10.245	
9,350.00	9,264.48	9,330.66	9,309.99	36.16	33.21	164.14	-271.94	344.83	683.70	617.04	66.66	10.257	
9,400.00	9,313.79	9,374.29	9,353.48	36.37	33.37	164.12	-273.98	347.45	688.55	621.55	67.00	10.277	
9,450.00	9,363.11	9,417.84	9,396.93	36.59	33.53	164.13	-275.74	349.87	693.85	626.51	67.34	10.304	
9,500.00	9,412.42	9,461.30	9,440.32	36.80	33.68	164.16	-277.19	351.88	699.59	631.92	67.67	10.339	
9,550.00	9,461.73	9,504.66	9,483.64	37.01	33.84	164.22	-278.36	353.49	705.77	637.78	67.99	10.380	
9,600.00	9,511.04	9,547.91	9,526.86	37.22	33.99	164.30	-279.24	354.70	712.39	644.08	68.31	10.429	
9,650.00	9,560.35	9,591.04	9,569.98	37.43	34.14	164.41	-279.82	355.51	719.46	650.84	68.62	10.485	
9,700.00	9,609.67	9,634.03	9,612.97	37.64	34.29	164.54	-280.12	355.92	726.97	658.04	68.93	10.547	
9,750.00	9,658.98	9,679.74	9,658.68	37.86	34.45	164.69	-280.17	355.98	734.88	665.63	69.25	10.612	
9,800.00	9,708.29	9,729.08	9,707.99	38.07	34.62	164.86	-280.17	355.98	742.86	673.26	69.60	10.674	
9,850.00	9,757.60	9,778.37	9,757.30	38.28	34.79	165.03	-280.17	355.98	750.85	680.90	69.95	10.734	
9,900.00	9,806.91	9,827.68	9,806.61	38.49	34.96	165.19	-280.17	355.98	758.84	688.54	70.30	10.794	
9,950.00	9,856.23	9,876.99	9,855.93	38.70	35.13	165.34	-280.17	355.98	766.84	696.19	70.65	10.854	
10,000.00	9,905.54	9,926.31	9,905.24	38.91	35.29	165.50	-280.17	355.98	774.85	703.85	71.00	10.913	
10,050.00	9,954.85	9,975.62	9,954.55	39.13	35.46	165.65	-280.17	355.98	782.86	711.51	71.36	10.971	
10,100.00	10,004.17	10,025.16	10,004.09	39.34	35.63	179.25	-279.92	355.98	790.88	719.17	71.71	11.029	
10,150.00	10,053.46	10,075.07	10,053.85	39.54	35.80	-151.64	-276.26	355.96	798.90	726.85	72.05	11.088	
10,200.00	10,102.38	10,124.86	10,102.99	39.73	35.96	-131.99	-268.31	355.92	806.86	734.48	72.38	11.147	
10,250.00	10,150.55	10,174.56	10,151.16	39.91	36.11	-120.07	-256.16	355.86	814.71	742.01	72.69	11.207	
10,300.00	10,197.60	10,224.18	10,198.03	40.08	36.25	-112.46	-239.91	355.77	822.37	749.38	72.99	11.267	
10,350.00	10,243.19	10,273.73	10,243.25	40.23	36.39	-107.23	-219.70	355.67	829.80	756.53	73.27	11.325	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

Company:	WCDSC Permian NM	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Project:	Eddy County (NAD 83 NM Eastern)	TVD Reference:	RKB @ 3533.80ft
Reference Site:	Sec. 36-T23S-R31E	MD Reference:	RKB @ 3533.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit Plan 1													0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:
													0.50 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Semi Major Axis Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
10,400.00	10,286.97	10,323.22	10,286.51	40.37	36.51	-103.39	-195.68	355.55	836.93	763.40	73.54	11.381	
10,450.00	10,328.59	10,372.68	10,327.51	40.49	36.62	-100.45	-168.04	355.40	843.72	769.93	73.79	11.435	
10,500.00	10,367.74	10,422.11	10,365.94	40.60	36.72	-98.10	-137.00	355.24	850.10	776.07	74.03	11.484	
10,550.00	10,404.14	10,471.51	10,401.55	40.69	36.80	-96.20	-102.77	355.06	856.03	781.78	74.25	11.529	
10,600.00	10,437.49	10,520.90	10,434.06	40.76	36.88	-94.63	-65.61	354.87	861.47	787.00	74.47	11.568	
10,650.00	10,467.54	10,570.27	10,463.25	40.83	36.94	-93.34	-25.81	354.67	866.37	791.69	74.68	11.601	
10,700.00	10,494.07	10,619.63	10,488.90	40.88	37.01	-92.26	16.34	354.45	870.70	795.81	74.89	11.627	
10,750.00	10,516.88	10,668.98	10,510.82	40.92	37.06	-91.38	60.54	354.22	874.41	799.33	75.09	11.645	
10,800.00	10,535.78	10,718.30	10,528.85	40.95	37.13	-90.68	106.43	353.98	877.50	802.22	75.28	11.656	
10,850.00	10,550.65	10,767.61	10,542.86	40.97	37.21	-90.13	153.69	353.74	879.92	804.45	75.48	11.658	
10,900.00	10,561.35	10,816.88	10,552.75	40.99	37.29	-89.73	201.94	353.49	881.67	806.00	75.67	11.651	
10,950.00	10,567.82	10,866.11	10,558.46	41.01	37.39	-89.48	250.82	353.23	882.73	806.87	75.87	11.636	
11,000.00	10,570.00	10,915.42	10,560.00	41.03	37.49	-89.37	300.09	352.98	883.09	807.03	76.06	11.611	
11,050.00	10,570.00	10,965.42	10,560.00	41.06	37.61	-89.37	350.09	352.72	883.09	806.80	76.28	11.576	
11,100.00	10,570.00	11,015.42	10,560.00	41.11	37.73	-89.37	400.09	352.46	883.08	806.57	76.51	11.541	
11,150.00	10,570.00	11,065.42	10,560.00	41.16	37.88	-89.37	450.09	352.20	883.08	806.29	76.79	11.500	
11,200.00	10,570.00	11,115.42	10,560.00	41.23	38.04	-89.37	500.09	351.94	883.08	806.00	77.08	11.457	
11,250.00	10,570.00	11,165.42	10,560.00	41.31	38.21	-89.37	550.09	351.68	883.08	805.67	77.40	11.409	
11,300.00	10,570.00	11,215.42	10,560.00	41.41	38.39	-89.37	600.09	351.42	883.07	805.33	77.74	11.359	
11,350.00	10,570.00	11,265.42	10,560.00	41.52	38.59	-89.37	650.09	351.16	883.07	804.95	78.12	11.304	
11,400.00	10,570.00	11,315.42	10,560.00	41.66	38.80	-89.37	700.09	350.91	883.07	804.56	78.51	11.248	
11,450.00	10,570.00	11,365.42	10,560.00	41.80	39.02	-89.37	750.08	350.65	883.06	804.13	78.94	11.187	
11,500.00	10,570.00	11,415.42	10,560.00	41.97	39.25	-89.37	800.08	350.39	883.06	803.68	79.38	11.125	
11,550.00	10,570.00	11,465.42	10,560.00	42.15	39.50	-89.37	850.08	350.13	883.06	803.20	79.86	11.058	
11,600.00	10,570.00	11,515.42	10,560.00	42.35	39.76	-89.37	900.08	349.87	883.06	802.71	80.34	10.991	
11,650.00	10,570.00	11,565.42	10,560.00	42.56	40.03	-89.37	950.08	349.61	883.05	802.19	80.87	10.920	
11,700.00	10,570.00	11,615.42	10,560.00	42.79	40.30	-89.37	1,000.08	349.35	883.05	801.65	81.40	10.849	
11,750.00	10,570.00	11,665.42	10,560.00	43.04	40.60	-89.37	1,050.08	349.09	883.05	801.08	81.97	10.773	
11,800.00	10,570.00	11,715.42	10,560.00	43.29	40.90	-89.37	1,100.08	348.83	883.04	800.50	82.54	10.698	
11,850.00	10,570.00	11,765.42	10,560.00	43.56	41.21	-89.37	1,150.08	348.57	883.04	799.88	83.16	10.619	
11,900.00	10,570.00	11,815.42	10,560.00	43.85	41.53	-89.37	1,200.08	348.32	883.04	799.26	83.78	10.540	
11,950.00	10,570.00	11,865.42	10,560.00	44.14	41.87	-89.37	1,250.08	348.06	883.04	798.61	84.43	10.459	
12,000.00	10,570.00	11,915.42	10,560.00	44.45	42.21	-89.37	1,300.08	347.80	883.03	797.94	85.09	10.378	
12,050.00	10,570.00	11,965.42	10,560.00	44.77	42.56	-89.37	1,350.08	347.54	883.03	797.25	85.78	10.294	
12,100.00	10,570.00	12,015.42	10,560.00	45.10	42.92	-89.37	1,400.08	347.28	883.03	796.55	86.48	10.210	
12,150.00	10,570.00	12,065.42	10,560.00	45.44	43.29	-89.37	1,450.08	347.02	883.03	795.81	87.21	10.125	
12,200.00	10,570.00	12,115.42	10,560.00	45.78	43.67	-89.37	1,500.07	346.76	883.02	795.07	87.95	10.040	
12,250.00	10,570.00	12,165.42	10,560.00	46.15	44.06	-89.37	1,550.07	346.50	883.02	794.30	88.72	9.953	
12,300.00	10,570.00	12,215.42	10,560.00	46.51	44.45	-89.37	1,600.07	346.24	883.02	793.53	89.49	9.868	
12,350.00	10,570.00	12,265.42	10,560.00	46.89	44.86	-89.37	1,650.07	345.98	883.01	792.73	90.29	9.780	
12,400.00	10,570.00	12,315.42	10,560.00	47.27	45.27	-89.37	1,700.07	345.73	883.01	791.92	91.09	9.694	
12,450.00	10,570.00	12,365.42	10,560.00	47.67	45.69	-89.37	1,750.07	345.47	883.01	791.09	91.92	9.606	
12,500.00	10,570.00	12,415.42	10,560.00	48.07	46.12	-89.37	1,800.07	345.21	883.01	790.25	92.76	9.519	
12,550.00	10,570.00	12,465.42	10,560.00	48.48	46.56	-89.37	1,850.07	344.95	883.00	789.38	93.62	9.432	
12,600.00	10,570.00	12,515.42	10,560.00	48.90	47.00	-89.37	1,900.07	344.69	883.00	788.51	94.49	9.345	
12,650.00	10,570.00	12,565.42	10,560.00	49.33	47.45	-89.37	1,950.07	344.43	883.00	787.62	95.38	9.258	
12,700.00	10,570.00	12,615.42	10,560.00	49.76	47.91	-89.37	2,000.07	344.17	882.99	786.72	96.27	9.172	
12,750.00	10,570.00	12,665.42	10,560.00	50.20	48.37	-89.37	2,050.07	343.91	882.99	785.80	97.19	9.085	
12,800.00	10,570.00	12,715.42	10,560.00	50.64	48.84	-89.37	2,100.07	343.65	882.99	784.88	98.11	9.000	
12,850.00	10,570.00	12,765.42	10,560.00	51.10	49.32	-89.37	2,150.07	343.39	882.99	783.93	99.06	8.914	
12,900.00	10,570.00	12,815.42	10,560.00	51.55	49.80	-89.37	2,200.07	343.14	882.98	782.98	100.00	8.829	
12,950.00	10,570.00	12,865.42	10,560.00	52.02	50.29	-89.37	2,250.06	342.88	882.98	782.01	100.97	8.745	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore:</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit Plan 1													0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error: 0.50 ft
Reference	Offset	Semi Major Axis		Distance		Minimum		Separation		Warning			
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
13,000.00	10,570.00	12,915.42	10,560.00	52.49	50.78	-89.37	2,300.06	342.62	882.98	781.03	101.94	8.661	
13,050.00	10,570.00	12,965.42	10,560.00	52.97	51.28	-89.37	2,350.06	342.36	882.97	780.04	102.93	8.578	
13,100.00	10,570.00	13,015.42	10,560.00	53.45	51.78	-89.37	2,400.06	342.10	882.97	779.04	103.93	8.496	
13,150.00	10,570.00	13,065.42	10,560.00	53.94	52.29	-89.37	2,450.06	341.84	882.97	778.03	104.94	8.414	
13,200.00	10,570.00	13,115.42	10,560.00	54.44	52.81	-89.37	2,500.06	341.58	882.97	777.01	105.96	8.333	
13,250.00	10,570.00	13,165.42	10,560.00	54.94	53.33	-89.37	2,550.06	341.32	882.96	775.98	106.99	8.253	
13,300.00	10,570.00	13,215.42	10,560.00	55.44	53.85	-89.37	2,600.06	341.06	882.96	774.94	108.02	8.174	
13,350.00	10,570.00	13,265.42	10,560.00	55.95	54.38	-89.37	2,650.06	340.80	882.96	773.88	109.07	8.095	
13,400.00	10,570.00	13,315.42	10,560.00	56.46	54.92	-89.37	2,700.06	340.55	882.96	772.83	110.13	8.017	
13,450.00	10,570.00	13,365.42	10,560.00	56.98	55.46	-89.37	2,750.06	340.29	882.95	771.75	111.20	7.940	
13,500.00	10,570.00	13,415.42	10,560.00	57.51	56.00	-89.37	2,800.06	340.03	882.95	770.68	112.27	7.864	
13,550.00	10,570.00	13,465.42	10,560.00	58.04	56.54	-89.37	2,850.06	339.77	882.95	769.59	113.36	7.789	
13,600.00	10,570.00	13,515.42	10,560.00	58.57	57.10	-89.37	2,900.06	339.51	882.94	768.50	114.45	7.715	
13,650.00	10,570.00	13,565.42	10,560.00	59.10	57.65	-89.37	2,950.05	339.25	882.94	767.39	115.55	7.641	
13,700.00	10,570.00	13,615.42	10,560.00	59.64	58.21	-89.37	3,000.05	338.99	882.94	766.28	116.66	7.569	
13,750.00	10,570.00	13,665.42	10,560.00	60.19	58.77	-89.37	3,050.05	338.73	882.94	765.16	117.77	7.497	
13,800.00	10,570.00	13,715.42	10,560.00	60.74	59.34	-89.37	3,100.05	338.47	882.93	764.04	118.89	7.426	
13,850.00	10,570.00	13,765.42	10,560.00	61.29	59.91	-89.37	3,150.05	338.21	882.93	762.90	120.03	7.356	
13,900.00	10,570.00	13,815.42	10,560.00	61.84	60.48	-89.37	3,200.05	337.96	882.93	761.76	121.16	7.287	
13,950.00	10,570.00	13,865.42	10,560.00	62.40	61.06	-89.37	3,250.05	337.70	882.92	760.62	122.31	7.219	
14,000.00	10,570.00	13,915.42	10,560.00	62.97	61.64	-89.37	3,300.05	337.44	882.92	759.46	123.46	7.152	
14,050.00	10,570.00	13,965.42	10,560.00	63.53	62.22	-89.37	3,350.05	337.18	882.92	758.30	124.62	7.085	
14,100.00	10,570.00	14,015.42	10,560.00	64.10	62.80	-89.37	3,400.05	336.92	882.92	757.14	125.78	7.020	
14,150.00	10,570.00	14,065.42	10,560.00	64.68	63.39	-89.37	3,450.05	336.66	882.91	755.96	126.95	6.955	
14,200.00	10,570.00	14,115.42	10,560.00	65.25	63.98	-89.37	3,500.05	336.40	882.91	754.79	128.12	6.891	
14,250.00	10,570.00	14,165.42	10,560.00	65.83	64.58	-89.37	3,550.05	336.14	882.91	753.60	129.30	6.828	
14,300.00	10,570.00	14,215.42	10,560.00	66.41	65.17	-89.37	3,600.05	335.88	882.90	752.42	130.49	6.766	
14,350.00	10,570.00	14,265.42	10,560.00	67.00	65.77	-89.37	3,650.05	335.62	882.90	751.22	131.68	6.705	
14,400.00	10,570.00	14,315.42	10,560.00	67.58	66.38	-89.37	3,700.04	335.37	882.90	750.02	132.88	6.644	
14,450.00	10,570.00	14,365.42	10,560.00	68.17	66.98	-89.37	3,750.04	335.11	882.90	748.81	134.08	6.585	
14,500.00	10,570.00	14,415.42	10,560.00	68.76	67.59	-89.37	3,800.04	334.85	882.89	747.61	135.29	6.526	
14,550.00	10,570.00	14,465.42	10,560.00	69.36	68.20	-89.37	3,850.04	334.59	882.89	746.39	136.50	6.468	
14,600.00	10,570.00	14,515.42	10,560.00	69.96	68.81	-89.37	3,900.04	334.33	882.89	745.17	137.72	6.411	
14,650.00	10,570.00	14,565.42	10,560.00	70.56	69.42	-89.37	3,950.04	334.07	882.89	743.95	138.94	6.354	
14,700.00	10,570.00	14,615.42	10,560.00	71.16	70.04	-89.37	4,000.04	333.81	882.88	742.72	140.16	6.299	
14,750.00	10,570.00	14,665.42	10,560.00	71.77	70.66	-89.37	4,050.04	333.55	882.88	741.48	141.40	6.244	
14,800.00	10,570.00	14,715.42	10,560.00	72.37	71.28	-89.37	4,100.04	333.29	882.88	740.25	142.63	6.190	
14,850.00	10,570.00	14,765.42	10,560.00	72.98	71.90	-89.37	4,150.04	333.03	882.87	739.01	143.87	6.137	
14,900.00	10,570.00	14,815.42	10,560.00	73.59	72.52	-89.37	4,200.04	332.78	882.87	737.76	145.11	6.084	
14,950.00	10,570.00	14,865.42	10,560.00	74.21	73.15	-89.37	4,250.04	332.52	882.87	736.51	146.36	6.032	
15,000.00	10,570.00	14,915.42	10,560.00	74.82	73.78	-89.37	4,300.04	332.26	882.87	735.26	147.61	5.981	
15,050.00	10,570.00	14,965.42	10,560.00	75.44	74.41	-89.37	4,350.04	332.00	882.86	734.00	148.86	5.931	
15,100.00	10,570.00	15,015.42	10,560.00	76.06	75.04	-89.37	4,400.04	331.74	882.86	732.74	150.12	5.881	
15,150.00	10,570.00	15,065.42	10,560.00	76.68	75.67	-89.37	4,450.03	331.48	882.86	731.48	151.38	5.832	
15,200.00	10,570.00	15,115.42	10,560.00	77.30	76.31	-89.37	4,500.03	331.22	882.85	730.21	152.65	5.784	
15,250.00	10,570.00	15,165.42	10,560.00	77.93	76.95	-89.37	4,550.03	330.96	882.85	728.94	153.92	5.736	
15,300.00	10,570.00	15,215.42	10,560.00	78.56	77.58	-89.37	4,600.03	330.70	882.85	727.66	155.19	5.689	
15,350.00	10,570.00	15,265.42	10,560.00	79.18	78.22	-89.37	4,650.03	330.44	882.85	726.38	156.46	5.643	
15,400.00	10,570.00	15,315.42	10,560.00	79.81	78.87	-89.37	4,700.03	330.19	882.84	725.10	157.74	5.597	
15,450.00	10,570.00	15,365.42	10,560.00	80.45	79.51	-89.37	4,750.03	329.93	882.84	723.82	159.02	5.552	
15,500.00	10,570.00	15,415.42	10,560.00	81.08	80.15	-89.37	4,800.03	329.67	882.84	722.53	160.30	5.507	
15,550.00	10,570.00	15,465.42	10,560.00	81.72	80.80	-89.37	4,850.03	329.41	882.83	721.24	161.59	5.463	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDCS Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.50 ft
Reference	Offset	Semi Major Axis		Distance		Minimum		Separation		Warning				
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
15,600.00	10,570.00	15,515.42	10,560.00	82.35	81.45	-89.37	4,900.03	329.15	882.83	719.95	162.88	5.420		
15,650.00	10,570.00	15,565.42	10,560.00	82.99	82.10	-89.37	4,950.03	328.89	882.83	718.65	164.17	5.377		
15,700.00	10,570.00	15,615.42	10,560.00	83.63	82.74	-89.37	5,000.03	328.63	882.83	717.36	165.47	5.335		
15,750.00	10,570.00	15,665.42	10,560.00	84.27	83.40	-89.37	5,050.03	328.37	882.82	716.06	166.77	5.294		
15,800.00	10,570.00	15,715.42	10,560.00	84.91	84.05	-89.37	5,100.03	328.11	882.82	714.75	168.07	5.253		
15,850.00	10,570.00	15,765.42	10,560.00	85.56	84.70	-89.37	5,150.03	327.85	882.82	713.45	169.37	5.212		
15,900.00	10,570.00	15,815.42	10,560.00	86.20	85.36	-89.37	5,200.02	327.60	882.81	712.14	170.68	5.172		
15,950.00	10,570.00	15,865.42	10,560.00	86.85	86.01	-89.37	5,250.02	327.34	882.81	710.83	171.99	5.133		
16,000.00	10,570.00	15,915.42	10,560.00	87.50	86.67	-89.37	5,300.02	327.08	882.81	709.51	173.29	5.094		
16,050.00	10,570.00	15,965.42	10,560.00	88.15	87.33	-89.37	5,350.02	326.82	882.81	708.20	174.61	5.056		
16,100.00	10,570.00	16,015.42	10,560.00	88.80	87.99	-89.37	5,400.02	326.56	882.80	706.88	175.92	5.018		
16,150.00	10,570.00	16,065.42	10,560.00	89.45	88.65	-89.37	5,450.02	326.30	882.80	705.56	177.24	4.981 Alert		
16,200.00	10,570.00	16,115.42	10,560.00	90.10	89.31	-89.37	5,500.02	326.04	882.80	704.24	178.56	4.944 Alert		
16,250.00	10,570.00	16,165.42	10,560.00	90.75	89.97	-89.37	5,550.02	325.78	882.80	702.91	179.88	4.908 Alert		
16,300.00	10,570.00	16,215.42	10,560.00	91.41	90.64	-89.37	5,600.02	325.52	882.79	701.59	181.20	4.872 Alert		
16,350.00	10,570.00	16,265.42	10,560.00	92.07	91.30	-89.37	5,650.02	325.26	882.79	700.26	182.53	4.836 Alert		
16,400.00	10,570.00	16,315.42	10,560.00	92.72	91.97	-89.37	5,700.02	325.01	882.79	698.93	183.86	4.801 Alert		
16,450.00	10,570.00	16,365.42	10,560.00	93.38	92.63	-89.37	5,750.02	324.75	882.78	697.60	185.19	4.767 Alert		
16,500.00	10,570.00	16,415.42	10,560.00	94.04	93.30	-89.37	5,800.02	324.49	882.78	696.26	186.52	4.733 Alert		
16,550.00	10,570.00	16,465.42	10,560.00	94.70	93.97	-89.37	5,850.02	324.23	882.78	694.93	187.85	4.699 Alert		
16,600.00	10,570.00	16,515.42	10,560.00	95.36	94.64	-89.37	5,900.02	323.97	882.78	693.59	189.19	4.666 Alert		
16,650.00	10,570.00	16,565.42	10,560.00	96.02	95.31	-89.37	5,950.01	323.71	882.77	692.25	190.52	4.633 Alert		
16,700.00	10,570.00	16,615.42	10,560.00	96.69	95.98	-89.37	6,000.01	323.45	882.77	690.91	191.86	4.601 Alert		
16,750.00	10,570.00	16,665.42	10,560.00	97.35	96.65	-89.37	6,050.01	323.19	882.77	689.56	193.20	4.569 Alert		
16,800.00	10,570.00	16,715.42	10,560.00	98.01	97.32	-89.37	6,100.01	322.93	882.76	688.22	194.55	4.538 Alert		
16,850.00	10,570.00	16,765.42	10,560.00	98.68	98.00	-89.37	6,150.01	322.67	882.76	686.87	195.89	4.506 Alert		
16,900.00	10,570.00	16,815.42	10,560.00	99.35	98.67	-89.37	6,200.01	322.42	882.76	685.52	197.23	4.476 Alert		
16,950.00	10,570.00	16,865.42	10,560.00	100.02	99.35	-89.37	6,250.01	322.16	882.76	684.17	198.58	4.445 Alert		
17,000.00	10,570.00	16,915.42	10,560.00	100.68	100.02	-89.37	6,300.01	321.90	882.75	682.82	199.93	4.415 Alert		
17,050.00	10,570.00	16,965.42	10,560.00	101.35	100.70	-89.37	6,350.01	321.64	882.75	681.47	201.28	4.386 Alert		
17,100.00	10,570.00	17,015.42	10,560.00	102.02	101.38	-89.37	6,400.01	321.38	882.75	680.12	202.63	4.356 Alert		
17,150.00	10,570.00	17,065.42	10,560.00	102.69	102.05	-89.37	6,450.01	321.12	882.74	678.76	203.98	4.328 Alert		
17,200.00	10,570.00	17,115.42	10,560.00	103.37	102.73	-89.37	6,500.01	320.86	882.74	677.40	205.34	4.299 Alert		
17,250.00	10,570.00	17,165.42	10,560.00	104.04	103.41	-89.37	6,550.01	320.60	882.74	676.05	206.69	4.271 Alert		
17,300.00	10,570.00	17,215.42	10,560.00	104.71	104.09	-89.37	6,600.01	320.34	882.74	674.69	208.05	4.243 Alert		
17,350.00	10,570.00	17,265.42	10,560.00	105.38	104.77	-89.37	6,650.01	320.09	882.73	673.32	209.41	4.215 Alert		
17,400.00	10,570.00	17,315.42	10,560.00	106.06	105.45	-89.37	6,700.00	319.83	882.73	671.96	210.77	4.188 Alert		
17,450.00	10,570.00	17,365.42	10,560.00	106.73	106.14	-89.37	6,750.00	319.57	882.73	670.60	212.13	4.161 Alert		
17,500.00	10,570.00	17,415.42	10,560.00	107.41	106.82	-89.37	6,800.00	319.31	882.73	669.23	213.49	4.135 Alert		
17,550.00	10,570.00	17,465.42	10,560.00	108.09	107.50	-89.37	6,850.00	319.05	882.72	667.87	214.85	4.108 Alert		
17,600.00	10,570.00	17,515.42	10,560.00	108.76	108.18	-89.37	6,900.00	318.79	882.72	666.50	216.22	4.083 Alert		
17,650.00	10,570.00	17,565.42	10,560.00	109.44	108.87	-89.37	6,950.00	318.53	882.72	665.13	217.59	4.057 Alert		
17,700.00	10,570.00	17,615.42	10,560.00	110.12	109.55	-89.37	7,000.00	318.27	882.71	663.76	218.95	4.032 Alert		
17,750.00	10,570.00	17,665.42	10,560.00	110.80	110.24	-89.37	7,050.00	318.01	882.71	662.39	220.32	4.006 Alert		
17,800.00	10,570.00	17,715.42	10,560.00	111.48	110.92	-89.37	7,100.00	317.75	882.71	661.02	221.69	3.982 Alert		
17,850.00	10,570.00	17,765.42	10,560.00	112.16	111.61	-89.37	7,150.00	317.50	882.71	659.65	223.06	3.957 Alert		
17,900.00	10,570.00	17,815.42	10,560.00	112.84	112.30	-89.37	7,200.00	317.24	882.70	658.27	224.43	3.933 Alert		
17,950.00	10,570.00	17,865.42	10,560.00	113.52	112.99	-89.37	7,250.00	316.98	882.70	656.90	225.80	3.909 Alert		
18,000.00	10,570.00	17,915.42	10,560.00	114.20	113.67	-89.37	7,300.00	316.72	882.70	655.52	227.18	3.886 Alert		
18,050.00	10,570.00	17,965.42	10,560.00	114.89	114.36	-89.37	7,350.00	316.46	882.69	654.14	228.55	3.862 Alert		
18,100.00	10,570.00	18,015.42	10,560.00	115.57	115.05	-89.37	7,400.00	316.20	882.69	652.76	229.93	3.839 Alert		
18,150.00	10,570.00	18,065.42	10,560.00	116.25	115.74	-89.37	7,449.99	315.94	882.69	651.38	231.30	3.816 Alert		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit Plan 1													0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error: 0.50 ft
Reference	Offset	Semi Major Axis		Distance		Minimum		Separation		Warning			
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N-S (ft)	+E-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
18,200.00	10,570.00	18,115.42	10,560.00	116.94	116.43	-89.37	7,499.99	315.68	882.69	650.00	232.68	3.794	Alert
18,250.00	10,570.00	18,165.42	10,560.00	117.62	117.12	-89.37	7,549.99	315.42	882.68	648.62	234.06	3.771	Alert
18,300.00	10,570.00	18,215.42	10,560.00	118.31	117.81	-89.37	7,599.99	315.16	882.68	647.24	235.44	3.749	Alert
18,350.00	10,570.00	18,265.42	10,560.00	119.00	118.50	-89.37	7,649.99	314.91	882.68	645.86	236.82	3.727	Alert
18,400.00	10,570.00	18,315.42	10,560.00	119.68	119.19	-89.37	7,699.99	314.65	882.67	644.47	238.20	3.706	Alert
18,450.00	10,570.00	18,365.42	10,560.00	120.37	119.89	-89.37	7,749.99	314.39	882.67	643.09	239.58	3.684	Alert
18,500.00	10,570.00	18,415.42	10,560.00	121.06	120.58	-89.37	7,799.99	314.13	882.67	641.70	240.97	3.663	Alert
18,550.00	10,570.00	18,465.42	10,560.00	121.74	121.27	-89.37	7,849.99	313.87	882.67	640.32	242.35	3.642	Alert
18,600.00	10,570.00	18,515.42	10,560.00	122.43	121.97	-89.37	7,899.99	313.61	882.66	638.93	243.73	3.621	Alert
18,650.00	10,570.00	18,565.42	10,560.00	123.12	122.66	-89.37	7,949.99	313.35	882.66	637.54	245.12	3.601	Alert
18,700.00	10,570.00	18,615.42	10,560.00	123.81	123.35	-89.37	7,999.99	313.09	882.66	636.15	246.51	3.581	Alert
18,750.00	10,570.00	18,665.42	10,560.00	124.50	124.05	-89.37	8,049.99	312.83	882.65	634.76	247.89	3.561	Alert
18,800.00	10,570.00	18,715.42	10,560.00	125.19	124.74	-89.37	8,099.99	312.57	882.65	633.37	249.28	3.541	Alert
18,850.00	10,570.00	18,765.42	10,560.00	125.88	125.44	-89.37	8,149.99	312.32	882.65	631.98	250.67	3.521	Alert
18,900.00	10,570.00	18,815.42	10,560.00	126.57	126.13	-89.37	8,199.98	312.06	882.65	630.59	252.06	3.502	Alert
18,950.00	10,570.00	18,865.42	10,560.00	127.26	126.83	-89.37	8,249.98	311.80	882.64	629.19	253.45	3.483	Alert
19,000.00	10,570.00	18,915.42	10,560.00	127.95	127.53	-89.37	8,299.98	311.54	882.64	627.80	254.84	3.463	Alert
19,050.00	10,570.00	18,965.42	10,560.00	128.65	128.22	-89.37	8,349.98	311.28	882.64	626.40	256.23	3.445	Alert
19,100.00	10,570.00	19,015.42	10,560.00	129.34	128.92	-89.37	8,399.98	311.02	882.64	625.01	257.63	3.426	Alert
19,150.00	10,570.00	19,065.42	10,560.00	130.03	129.62	-89.37	8,449.98	310.76	882.63	623.61	259.02	3.408	Alert
19,200.00	10,570.00	19,115.42	10,560.00	130.73	130.32	-89.37	8,499.98	310.50	882.63	622.22	260.41	3.389	Alert
19,250.00	10,570.00	19,165.42	10,560.00	131.42	131.01	-89.37	8,549.98	310.24	882.63	620.82	261.81	3.371	Alert
19,300.00	10,570.00	19,215.42	10,560.00	132.11	131.71	-89.37	8,599.98	309.98	882.62	619.42	263.20	3.353	Alert
19,350.00	10,570.00	19,265.42	10,560.00	132.81	132.41	-89.37	8,649.98	309.73	882.62	618.02	264.60	3.336	Alert
19,400.00	10,570.00	19,315.42	10,560.00	133.50	133.11	-89.37	8,699.98	309.47	882.62	616.62	266.00	3.318	Alert
19,450.00	10,570.00	19,365.42	10,560.00	134.20	133.81	-89.37	8,749.98	309.21	882.62	615.22	267.39	3.301	Alert
19,500.00	10,570.00	19,415.42	10,560.00	134.89	134.51	-89.37	8,799.98	308.95	882.61	613.82	268.79	3.284	Alert
19,550.00	10,570.00	19,465.42	10,560.00	135.59	135.21	-89.37	8,849.98	308.69	882.61	612.42	270.19	3.267	Alert
19,600.00	10,570.00	19,515.42	10,560.00	136.29	135.91	-89.37	8,899.98	308.43	882.61	611.02	271.59	3.250	Alert
19,650.00	10,570.00	19,565.42	10,560.00	136.98	136.61	-89.37	8,949.97	308.17	882.60	609.62	272.99	3.233	Alert
19,700.00	10,570.00	19,615.42	10,560.00	137.68	137.31	-89.37	8,999.97	307.91	882.60	608.21	274.39	3.217	Alert
19,750.00	10,570.00	19,665.42	10,560.00	138.38	138.01	-89.37	9,049.97	307.65	882.60	606.81	275.79	3.200	Alert
19,800.00	10,570.00	19,715.42	10,560.00	139.07	138.71	-89.37	9,099.97	307.39	882.60	605.41	277.19	3.184	Alert
19,850.00	10,570.00	19,765.42	10,560.00	139.77	139.42	-89.37	9,149.97	307.14	882.59	604.00	278.59	3.168	Alert
19,900.00	10,570.00	19,815.42	10,560.00	140.47	140.12	-89.37	9,199.97	306.88	882.59	602.60	279.99	3.152	Alert
19,950.00	10,570.00	19,865.42	10,560.00	141.17	140.82	-89.37	9,249.97	306.62	882.59	601.19	281.40	3.136	Alert
20,000.00	10,570.00	19,915.42	10,560.00	141.87	141.52	-89.37	9,299.97	306.36	882.58	599.78	282.80	3.121	Alert
20,050.00	10,570.00	19,965.42	10,560.00	142.57	142.23	-89.37	9,349.97	306.10	882.58	598.38	284.21	3.105	Alert
20,100.00	10,570.00	20,015.42	10,560.00	143.27	142.93	-89.37	9,399.97	305.84	882.58	596.97	285.61	3.090	Alert
20,150.00	10,570.00	20,065.42	10,560.00	143.97	143.63	-89.37	9,449.97	305.58	882.58	595.56	287.01	3.075	Alert
20,200.00	10,570.00	20,115.42	10,560.00	144.67	144.34	-89.37	9,499.97	305.32	882.57	594.15	288.42	3.060	Alert
20,250.00	10,570.00	20,165.42	10,560.00	145.37	145.04	-89.37	9,549.97	305.06	882.57	592.74	289.83	3.045	Alert
20,300.00	10,570.00	20,215.42	10,560.00	146.07	145.74	-89.37	9,599.97	304.80	882.57	591.33	291.23	3.030	Alert
20,350.00	10,570.00	20,265.42	10,560.00	146.77	146.45	-89.37	9,649.97	304.55	882.57	589.92	292.64	3.016	Alert
20,400.00	10,570.00	20,315.42	10,560.00	147.47	147.15	-89.37	9,699.96	304.29	882.56	588.51	294.05	3.001	Alert
20,450.00	10,570.00	20,365.42	10,560.00	148.17	147.86	-89.37	9,749.96	304.03	882.56	587.10	295.46	2.987	Alert
20,500.00	10,570.00	20,415.42	10,560.00	148.87	148.56	-89.37	9,799.96	303.77	882.56	585.69	296.86	2.973	Alert
20,550.00	10,570.00	20,465.42	10,560.00	149.57	149.27	-89.37	9,849.96	303.51	882.55	584.28	298.27	2.959	Alert
20,600.00	10,570.00	20,515.42	10,560.00	150.27	149.97	-89.37	9,899.96	303.25	882.55	582.87	299.68	2.945	Alert
20,650.00	10,570.00	20,565.42	10,560.00	150.98	150.68	-89.37	9,949.96	302.99	882.55	581.45	301.09	2.931	Alert
20,700.00	10,570.00	20,615.42	10,560.00	151.68	151.38	-89.37	9,999.96	302.73	882.55	580.04	302.50	2.917	Alert
20,750.00	10,570.00	20,665.42	10,560.00	152.38	152.09	-89.37	10,049.96	302.47	882.54	578.63	303.91	2.904	Alert

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

Company:	WCDSC Permian NM	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Project:	Eddy County (NAD 83 NM Eastern)	TVD Reference:	RKB @ 3533.80ft
Reference Site:	Sec. 36-T23S-R31E	MD Reference:	RKB @ 3533.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.50 ft
Sec. 36-T23S-R31E - Todd 36-25 State Fed Com 234H - Wellbore #1 - Permit Plan 1														
Reference		Offset		Semi Major Axis			Distance							
Measured Depth	Vertical Depth	Measured Depth	Vertical Depth	Reference	Offset	Highside Toolface	Offset Wellbore Centre		Between Centres	Between Ellipses	Minimum Separation	Separation Factor	Warning	
(ft)	(ft)	(ft)	(ft)	(ft)	(ft)	(°)	+N/-S (ft)	+E/-W (ft)	(ft)	(ft)	(ft)			
20,800.00	10,570.00	20,715.42	10,560.00	153.08	152.80	-89.37	10,099.96	302.21	882.54	577.21	305.33	2.890	Alert	
20,850.00	10,570.00	20,765.42	10,560.00	153.79	153.50	-89.37	10,149.96	301.96	882.54	575.80	306.74	2.877	Alert	
20,900.00	10,570.00	20,815.42	10,560.00	154.49	154.21	-89.37	10,199.96	301.70	882.53	574.38	308.15	2.864	Alert	
20,908.38	10,570.00	20,823.79	10,560.00	154.61	154.33	-89.37	10,208.33	301.65	882.53	574.15	308.39	2.862	Alert	



# Anticollision Report

<b>Company:</b>	WCDCS Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Offset Design													Offset Site Error:
Sec. 36-T23S-R31E - Todd 36B State 20H (Offset) - Wellbore #1 - Wellbore #1													0.00 ft
Survey Program: 100-GYRO-NS-CT, 8402-MWD+IGRF													Offset Well Error: 0.50 ft
Reference	Offset	Semi Major Axis		Distance		Minimum		Separation		Warning			
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
7,750.00	7,686.49	13,949.41	9,025.95	29.42	120.16	-55.86	53.61	1,299.09	1,453.49	1,376.39	77.09	18.854	
7,800.00	7,735.81	13,954.88	9,026.03	29.63	120.28	-55.17	48.53	1,301.12	1,405.70	1,327.58	78.12	17.995	
7,850.00	7,785.12	13,960.34	9,026.11	29.84	120.40	-54.47	43.46	1,303.16	1,358.05	1,278.84	79.21	17.145	
7,900.00	7,834.43	13,965.81	9,026.19	30.05	120.52	-53.76	38.38	1,305.19	1,310.55	1,230.17	80.38	16.305	
7,950.00	7,883.74	13,971.28	9,026.27	30.26	120.64	-53.05	33.31	1,307.23	1,263.21	1,181.58	81.63	15.475	
8,000.00	7,933.05	13,976.75	9,026.35	30.47	120.76	-52.34	28.23	1,309.26	1,216.07	1,133.10	82.98	14.656	
8,050.00	7,982.37	13,975.00	9,026.33	30.68	120.72	-52.57	29.86	1,308.61	1,169.17	1,084.80	84.37	13.858	
8,100.00	8,031.68	13,975.00	9,026.33	30.89	120.72	-52.57	29.86	1,308.61	1,122.52	1,036.64	85.89	13.070	
8,150.00	8,080.99	13,975.00	9,026.33	31.10	120.72	-52.57	29.86	1,308.61	1,076.18	988.64	87.54	12.294	
8,200.00	8,130.30	13,975.00	9,026.33	31.31	120.72	-52.57	29.86	1,308.61	1,030.19	940.85	89.33	11.532	
8,250.00	8,179.62	13,975.00	9,026.33	31.52	120.72	-52.57	29.86	1,308.61	984.58	893.29	91.29	10.785	
8,300.00	8,228.93	13,975.00	9,026.33	31.73	120.72	-52.57	29.86	1,308.61	939.42	845.99	93.42	10.055	
8,350.00	8,278.24	13,975.00	9,026.33	31.94	120.72	-52.57	29.86	1,308.61	894.77	799.01	95.76	9.344	
8,400.00	8,327.55	13,975.00	9,026.33	32.15	120.72	-52.57	29.86	1,308.61	850.72	752.40	98.32	8.653	
8,450.00	8,376.86	13,975.00	9,026.33	32.36	120.72	-52.57	29.86	1,308.61	807.37	706.24	101.13	7.984	
8,500.00	8,426.18	13,975.00	9,026.33	32.57	120.72	-52.57	29.86	1,308.61	764.82	660.62	104.20	7.340	
8,550.00	8,475.49	13,975.00	9,026.33	32.78	120.72	-52.57	29.86	1,308.61	723.23	615.65	107.58	6.723	
8,600.00	8,524.80	13,975.00	9,026.33	33.00	120.72	-52.57	29.86	1,308.61	682.77	571.50	111.27	6.136	
8,650.00	8,574.11	13,975.00	9,026.33	33.21	120.72	-52.57	29.86	1,308.61	643.65	528.37	115.28	5.583	
8,700.00	8,623.42	13,975.00	9,026.33	33.42	120.72	-52.57	29.86	1,308.61	606.13	486.52	119.62	5.067	
8,750.00	8,672.74	13,975.00	9,026.33	33.63	120.72	-52.57	29.86	1,308.61	570.54	446.29	124.24	4.592	Alert
8,800.00	8,722.05	13,975.00	9,026.33	33.84	120.72	-52.57	29.86	1,308.61	537.24	408.14	129.09	4.162	Alert
8,850.00	8,771.36	13,975.00	9,026.33	34.05	120.72	-52.57	29.86	1,308.61	506.69	372.66	134.03	3.780	Alert
8,900.00	8,820.67	13,975.00	9,026.33	34.26	120.72	-52.57	29.86	1,308.61	479.42	340.56	138.87	3.452	Alert
8,950.00	8,869.98	13,975.00	9,026.33	34.47	120.72	-52.57	29.86	1,308.61	456.02	312.72	143.30	3.182	Alert
9,000.00	8,919.30	13,975.00	9,026.33	34.68	120.72	-52.57	29.86	1,308.61	437.11	290.16	146.96	2.974	Alert
9,050.00	8,968.61	13,975.00	9,026.33	34.89	120.72	-52.57	29.86	1,308.61	423.30	273.87	149.43	2.833	Alert
9,100.00	9,017.92	13,975.00	9,026.33	35.11	120.72	-52.57	29.86	1,308.61	415.08	264.75	150.33	2.761	Alert
9,143.88	9,061.20	13,975.00	9,026.33	35.29	120.72	-52.57	29.86	1,308.61	412.76	263.11	149.64	2.758	Alert, CC, ES, SF
9,150.00	9,067.23	13,975.00	9,026.33	35.32	120.72	-52.57	29.86	1,308.61	412.80	263.37	149.43	2.762	Alert
9,200.00	9,116.55	13,975.00	9,026.33	35.53	120.72	-52.57	29.86	1,308.61	416.55	269.82	146.73	2.839	Alert
9,250.00	9,165.86	13,975.00	9,026.33	35.74	120.72	-52.57	29.86	1,308.61	426.18	283.73	142.45	2.992	Alert
9,300.00	9,215.17	13,975.00	9,026.33	35.95	120.72	-52.57	29.86	1,308.61	441.29	304.30	136.99	3.221	Alert
9,350.00	9,264.48	13,975.00	9,026.33	36.16	120.72	-52.57	29.86	1,308.61	461.36	330.53	130.83	3.526	Alert
9,400.00	9,313.79	13,975.00	9,026.33	36.37	120.72	-52.57	29.86	1,308.61	485.76	361.36	124.40	3.905	Alert
9,450.00	9,363.11	13,975.00	9,026.33	36.59	120.72	-52.57	29.86	1,308.61	513.88	395.83	118.05	4.353	Alert
9,500.00	9,412.42	13,975.00	9,026.33	36.80	120.72	-52.57	29.86	1,308.61	545.15	433.13	112.02	4.867	Alert
9,550.00	9,461.73	13,975.00	9,026.33	37.01	120.72	-52.57	29.86	1,308.61	579.05	472.62	106.43	5.441	
9,600.00	9,511.04	13,975.00	9,026.33	37.22	120.72	-52.57	29.86	1,308.61	615.15	513.78	101.37	6.089	
9,650.00	9,560.35	13,975.00	9,026.33	37.43	120.72	-52.57	29.86	1,308.61	653.09	556.25	96.83	6.745	
9,700.00	9,609.67	13,975.00	9,026.33	37.64	120.72	-52.57	29.86	1,308.61	692.56	599.74	92.81	7.462	
9,750.00	9,658.98	13,975.00	9,026.33	37.86	120.72	-52.57	29.86	1,308.61	733.31	644.04	89.27	8.214	
9,800.00	9,708.29	13,975.00	9,026.33	38.07	120.72	-52.57	29.86	1,308.61	775.15	688.98	86.17	8.995	
9,850.00	9,757.60	13,975.00	9,026.33	38.28	120.72	-52.57	29.86	1,308.61	817.90	734.44	83.46	9.800	
9,900.00	9,806.91	13,975.00	9,026.33	38.49	120.72	-52.57	29.86	1,308.61	861.44	780.34	81.10	10.622	
9,950.00	9,856.23	13,975.00	9,026.33	38.70	120.72	-52.57	29.86	1,308.61	905.64	826.60	79.05	11.457	
10,000.00	9,905.54	13,975.00	9,026.33	38.91	120.72	-52.57	29.86	1,308.61	950.42	873.16	77.26	12.301	
10,050.00	9,954.85	13,975.00	9,026.33	39.13	120.72	-52.57	29.86	1,308.61	995.70	919.98	75.71	13.151	
10,100.00	10,004.17	13,975.00	9,026.33	39.34	120.72	-43.09	29.86	1,308.61	1,041.30	966.94	74.36	14.004	
10,150.00	10,053.46	13,975.00	9,026.33	39.54	120.72	-21.98	29.86	1,308.61	1,086.25	1,013.16	73.09	14.863	
10,200.00	10,102.38	13,975.00	9,026.33	39.73	120.72	-8.79	29.86	1,308.61	1,130.16	1,058.27	71.89	15.721	
10,250.00	10,150.55	13,975.00	9,026.33	39.91	120.72	-2.14	29.86	1,308.61	1,172.82	1,102.05	70.77	16.573	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



# Anticollision Report

Company:	WCDSC Permian NM	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Project:	Eddy County (NAD 83 NM Eastern)	TVD Reference:	RKB @ 3533.80ft
Reference Site:	Sec. 36-T23S-R31E	MD Reference:	RKB @ 3533.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

<b>Offset Design</b> Sec. 36-T23S-R31E - Todd 36B State 20H (Offset) - Wellbore #1 - Wellbore #1												Offset Site Error:	0.00 ft
Survey Program: 100-GYRO-NS-CT, 8402-MWD+IGRF												Offset Well Error:	0.50 ft
Reference	Offset	Semi Major Axis		Distance		Warning							
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
10,300.00	10,197.60	13,975.00	9,026.33	40.08	120.72	1.13	29.86	1,308.61	1,214.06	1,144.33	69.73	17.410	
10,350.00	10,243.19	13,975.00	9,026.33	40.23	120.72	2.75	29.86	1,308.61	1,253.73	1,184.94	68.79	18.226	
10,400.00	10,286.97	13,975.00	9,026.33	40.37	120.72	3.54	29.86	1,308.61	1,291.67	1,223.74	67.94	19.012	
10,450.00	10,328.59	13,975.00	9,026.33	40.49	120.72	3.90	29.86	1,308.61	1,327.77	1,260.58	67.19	19.763	
10,500.00	10,367.74	13,975.00	9,026.33	40.60	120.72	4.01	29.86	1,308.61	1,361.90	1,295.37	66.53	20.470	
10,550.00	10,404.14	13,975.00	9,026.33	40.69	120.72	4.00	29.86	1,308.61	1,393.95	1,327.97	65.98	21.128	
10,600.00	10,437.49	13,975.00	9,026.33	40.76	120.72	3.91	29.86	1,308.61	1,423.83	1,358.31	65.52	21.730	
10,650.00	10,467.54	13,975.00	9,026.33	40.83	120.72	3.79	29.86	1,308.61	1,451.46	1,386.29	65.17	22.271	
10,700.00	10,494.07	13,976.39	9,026.35	40.88	120.75	3.67	28.56	1,309.13	1,476.75	1,411.81	64.94	22.741	
10,750.00	10,516.88	13,936.87	9,025.77	40.92	119.89	2.75	65.24	1,294.42	1,499.16	1,434.72	64.44	23.265	




# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Reference Depths are relative to RKB @ 3533.80ft  
Offset Depths are relative to Offset Datum  
Central Meridian is -104.333334

Coordinates are relative to: Todd 36\_25 State Fed Com 235H  
Coordinate System is US State Plane 1983, New Mexico Eastern Zone  
Grid Convergence at Surface is: 0.32°

## Ladder Plot

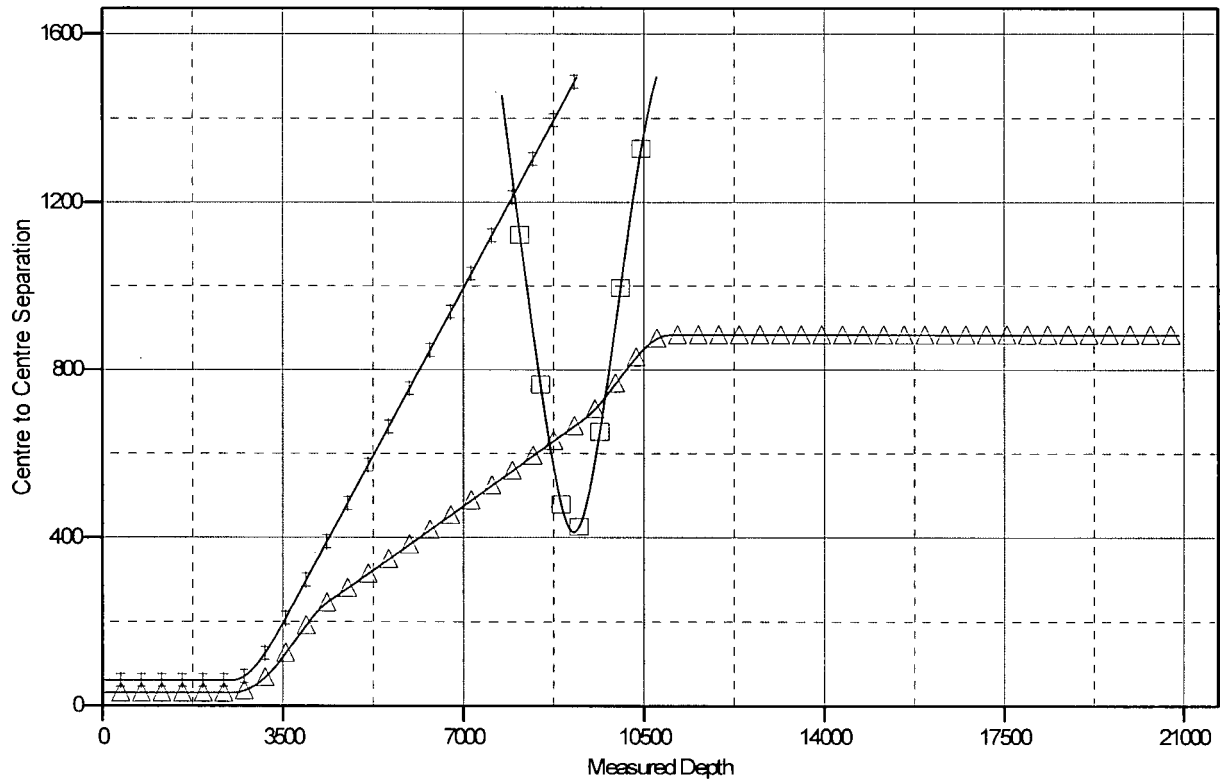

## LEGEND

Todd 36\_25 State Fed Com 235H, Wellbore #1, Permit Plan 1 VO
 Todd 36\_25 State Fed Com 235H, Wellbore #1, Permit Plan 1 VO
 Todd 36B State 20H (Offset), Wellbore #1, Wellbore #1 VO

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation




# Anticollision Report

<b>Company:</b>	WCDSC Permian NM	<b>Local Co-ordinate Reference:</b>	Well Todd 36_25 State Fed Com 235H
<b>Project:</b>	Eddy County (NAD 83 NM Eastern)	<b>TVD Reference:</b>	RKB @ 3533.80ft
<b>Reference Site:</b>	Sec. 36-T23S-R31E	<b>MD Reference:</b>	RKB @ 3533.80ft
<b>Site Error:</b>	0.00 ft	<b>North Reference:</b>	Grid
<b>Reference Well:</b>	Todd 36_25 State Fed Com 235H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Well Error:</b>	0.50 ft	<b>Output errors are at</b>	2.00 sigma
<b>Reference Wellbore</b>	Wellbore #1	<b>Database:</b>	EDM r5000.141_Prod US
<b>Reference Design:</b>	Permit Plan 1	<b>Offset TVD Reference:</b>	Offset Datum

Reference Depths are relative to RKB @ 3533.80ft  
Offset Depths are relative to Offset Datum  
Central Meridian is -104.333334

Coordinates are relative to: Todd 36\_25 State Fed Com 235H  
Coordinate System is US State Plane 1983, New Mexico Eastern Zone  
Grid Convergence at Surface is: 0.32°

## Separation Factor Plot

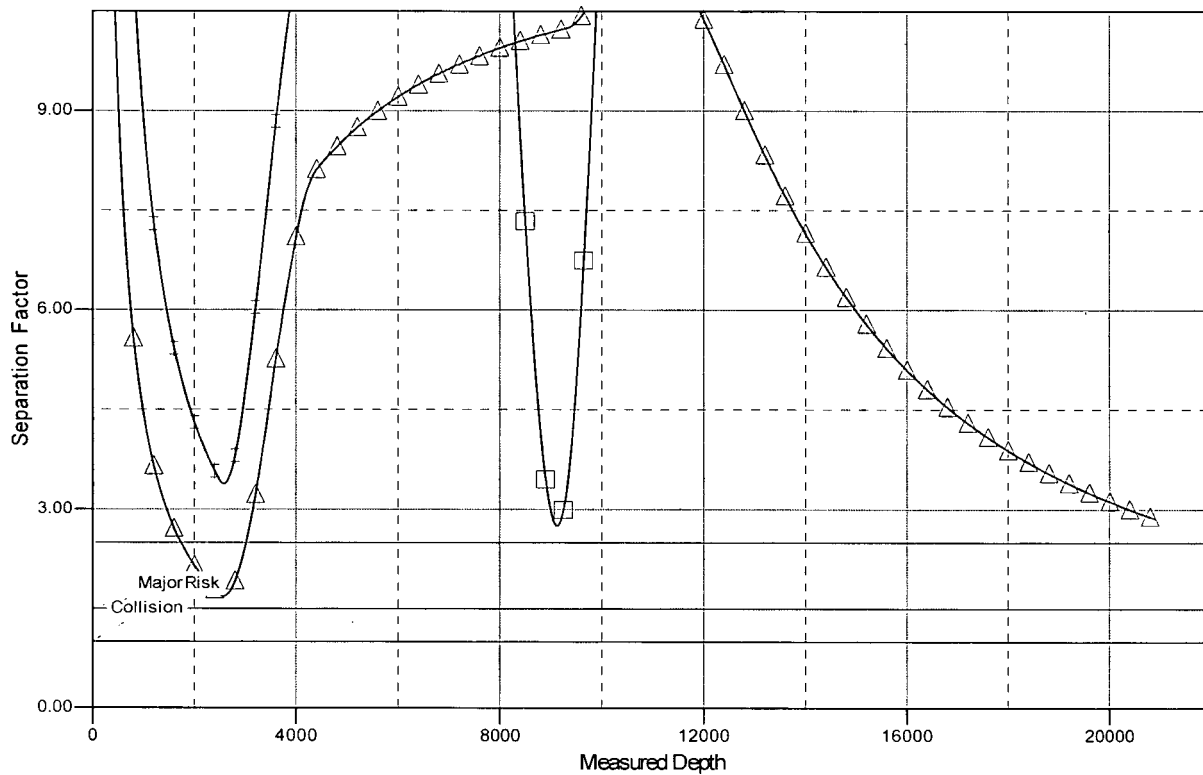

### LEGEND

Todd 36\_25 State Fed Com 234H, Wellbore #1, Permit Plan 1 V0
 Todd 36\_25 State Fed Com 233H, Wellbore #1, Permit Plan 1 V0
 Todd 36B State 20H (Offset) Wellbore #1, Wellbore #1 V0



# **WCDSC Permian NM**

**Eddy County (NAD 83 NM Eastern)**

**Sec. 36-T23S-R31E**

**Todd 36\_25 State Fed Com 235H**

**Wellbore #1**

**Plan: Permit Plan 1**

## **Standard Planning Report - Geographic**

**04 October, 2018**



06



# Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Company:	WCDSC Permian NM	TVD Reference:	RKB @ 3533.80ft
Project:	Eddy County (NAD 83 NM Eastern)	MD Reference:	RKB @ 3533.80ft
Site:	Sec. 36-T23S-R31E	North Reference:	Grid
Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Project	Eddy County (NAD 83 NM Eastern)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Sec. 36-T23S-R31E		
Site Position:	From: Map	Northing:	461,801.03 usft
		Easting:	724,712.45 usft
Position Uncertainty:	0.00 ft	Slot Radius:	13-3/16 "
		Latitude:	32.268172
		Longitude:	-103.740050
		Grid Convergence:	0.32 °

Well	Todd 36_25 State Fed Com 235H		
Well Position	+N/-S	0.00 ft	Northing:
	+E/-W	0.00 ft	Easting:
Position Uncertainty	0.50 ft	Wellhead Elevation:	Ground Level:
			3,508.80 ft

Wellbore	Wellbore #1		
Magnetics	Model Name	Sample Date	Declination
			(°)
	IGRF2015	10/1/2018	6.89
			Dip Angle
			(°)
			60.05
			Field Strength
			(nT)
			47,806.46341240

Design	Permit Plan 1		
Audit Notes:			
Version:	Phase:	PROTOTYPE	Tie On Depth:
			0.00
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W
	(ft)	(ft)	(ft)
	0.00	0.00	0.00
			Direction
			(°)
			6.61

Plan Survey Tool Program	Date	10/4/2018		
Depth From	Depth To	Survey (Wellbore)	Tool Name	Remarks
(ft)	(ft)			
1	0.00	20,908.38 Permit Plan 1 (Wellbore #1)	MWD+HDGM	
			OWSG MWD + HDGM	

Plan Sections										
Measured	Inclination	Azimuth	Vertical	+N/-S	+E/-W	Dogleg	Build	Turn	TFO	Target
Depth	(°)	(°)	Depth	(ft)	(ft)	Rate	Rate	Rate	(°)	
(ft)			(ft)			(°/100usft)	(°/100usft)	(°/100usft)		
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,451.51	9.52	103.19	3,447.14	-17.99	76.75	1.00	1.00	0.00	103.19	
10,078.23	9.52	103.19	9,982.69	-268.03	1,143.28	0.00	0.00	0.00	0.00	
11,000.34	90.00	359.70	10,570.00	305.00	1,236.00	10.00	8.73	-11.22	-103.31	
20,908.38	90.00	359.70	10,570.00	10,212.90	1,184.12	0.00	0.00	0.00	0.00	PBHL - Todd 36_25 S



# Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Company:	WCDSC Permian NM	TVD Reference:	RKB @ 3533.80ft
Project:	Eddy County (NAD 83 NM Eastern)	MD Reference:	RKB @ 3533.80ft
Site:	Sec. 36-T23S-R31E	North Reference:	Grid
Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
0.00	0.00	0.00	0.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
100.00	0.00	0.00	100.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
200.00	0.00	0.00	200.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
300.00	0.00	0.00	300.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
400.00	0.00	0.00	400.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
500.00	0.00	0.00	500.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
600.00	0.00	0.00	600.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
700.00	0.00	0.00	700.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
800.00	0.00	0.00	800.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
900.00	0.00	0.00	900.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,000.00	0.00	0.00	1,000.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,100.00	0.00	0.00	1,100.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,200.00	0.00	0.00	1,200.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,300.00	0.00	0.00	1,300.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,400.00	0.00	0.00	1,400.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,500.00	0.00	0.00	1,500.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,600.00	0.00	0.00	1,600.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,700.00	0.00	0.00	1,700.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,800.00	0.00	0.00	1,800.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
1,900.00	0.00	0.00	1,900.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
2,000.00	0.00	0.00	2,000.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
2,100.00	0.00	0.00	2,100.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
2,200.00	0.00	0.00	2,200.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
2,300.00	0.00	0.00	2,300.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
2,400.00	0.00	0.00	2,400.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
2,500.00	0.00	0.00	2,500.00	0.00	0.00	456,874.74	728,380.83	32.254575	-103.728272
2,600.00	1.00	103.19	2,599.99	-0.20	0.85	456,874.54	728,381.68	32.254575	-103.728269
2,700.00	2.00	103.19	2,699.96	-0.80	3.40	456,873.94	728,384.23	32.254573	-103.728261
2,800.00	3.00	103.19	2,799.86	-1.79	7.64	456,872.94	728,388.48	32.254570	-103.728247
2,900.00	4.00	103.19	2,899.68	-3.19	13.59	456,871.55	728,394.42	32.254566	-103.728228
3,000.00	5.00	103.19	2,999.37	-4.98	21.23	456,869.76	728,402.06	32.254561	-103.728203
3,100.00	6.00	103.19	3,098.90	-7.16	30.56	456,867.57	728,411.39	32.254555	-103.728173
3,200.00	7.00	103.19	3,198.26	-9.75	41.58	456,864.99	728,422.41	32.254548	-103.728138
3,300.00	8.00	103.19	3,297.40	-12.73	54.29	456,862.01	728,435.12	32.254539	-103.728096
3,400.00	9.00	103.19	3,396.30	-16.10	68.68	456,858.64	728,449.51	32.254530	-103.728050
3,451.51	9.52	103.19	3,447.14	-17.99	76.75	456,856.74	728,457.58	32.254524	-103.728024
3,500.00	9.52	103.19	3,494.97	-19.82	84.55	456,854.92	728,465.38	32.254519	-103.727999
3,600.00	9.52	103.19	3,593.59	-23.59	100.64	456,851.14	728,481.48	32.254509	-103.727947
3,700.00	9.52	103.19	3,692.21	-27.37	116.74	456,847.37	728,497.57	32.254498	-103.727895
3,800.00	9.52	103.19	3,790.84	-31.14	132.83	456,843.60	728,513.67	32.254487	-103.727843
3,900.00	9.52	103.19	3,889.46	-34.91	148.93	456,839.82	728,529.76	32.254477	-103.727791
4,000.00	9.52	103.19	3,988.09	-38.69	165.02	456,836.05	728,545.86	32.254466	-103.727739
4,100.00	9.52	103.19	4,086.71	-42.46	181.12	456,832.28	728,561.95	32.254456	-103.727687
4,200.00	9.52	103.19	4,185.33	-46.23	197.21	456,828.50	728,578.05	32.254445	-103.727635
4,300.00	9.52	103.19	4,283.96	-50.01	213.31	456,824.73	728,594.14	32.254434	-103.727583
4,400.00	9.52	103.19	4,382.58	-53.78	229.40	456,820.96	728,610.23	32.254424	-103.727531
4,500.00	9.52	103.19	4,481.21	-57.55	245.49	456,817.18	728,626.33	32.254413	-103.727479
4,600.00	9.52	103.19	4,579.83	-61.33	261.59	456,813.41	728,642.42	32.254402	-103.727427
4,700.00	9.52	103.19	4,678.46	-65.10	277.68	456,809.64	728,658.52	32.254392	-103.727375
4,800.00	9.52	103.19	4,777.08	-68.87	293.78	456,805.86	728,674.61	32.254381	-103.727323
4,900.00	9.52	103.19	4,875.70	-72.65	309.87	456,802.09	728,690.71	32.254371	-103.727271
5,000.00	9.52	103.19	4,974.33	-76.42	325.97	456,798.32	728,706.80	32.254360	-103.727219
5,100.00	9.52	103.19	5,072.95	-80.19	342.06	456,794.55	728,722.89	32.254349	-103.727167
5,200.00	9.52	103.19	5,171.58	-83.96	358.15	456,790.77	728,738.99	32.254339	-103.727115
5,300.00	9.52	103.19	5,270.20	-87.74	374.25	456,787.00	728,755.08	32.254328	-103.727063



# Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Company:	WCDSC Permian NM	TVD Reference:	RKB @ 3533.80ft
Project:	Eddy County (NAD 83 NM Eastern)	MD Reference:	RKB @ 3533.80ft
Site:	Sec. 36-T23S-R31E	North Reference:	Grid
Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
5,400.00	9.52	103.19	5,368.83	-91.51	390.34	456,783.23	728,771.18	32.254317	-103.727011
5,500.00	9.52	103.19	5,467.45	-95.28	406.44	456,779.45	728,787.27	32.254307	-103.726959
5,600.00	9.52	103.19	5,566.07	-99.06	422.53	456,775.68	728,803.37	32.254296	-103.726907
5,700.00	9.52	103.19	5,664.70	-102.83	438.63	456,771.91	728,819.46	32.254286	-103.726855
5,800.00	9.52	103.19	5,763.32	-106.60	454.72	456,768.13	728,835.55	32.254275	-103.726803
5,900.00	9.52	103.19	5,861.95	-110.38	470.82	456,764.36	728,851.65	32.254264	-103.726751
6,000.00	9.52	103.19	5,960.57	-114.15	486.91	456,760.59	728,867.74	32.254254	-103.726699
6,100.00	9.52	103.19	6,059.19	-117.92	503.00	456,756.81	728,883.84	32.254243	-103.726647
6,200.00	9.52	103.19	6,157.82	-121.70	519.10	456,753.04	728,899.93	32.254233	-103.726595
6,300.00	9.52	103.19	6,256.44	-125.47	535.19	456,749.27	728,916.03	32.254222	-103.726543
6,400.00	9.52	103.19	6,355.07	-129.24	551.29	456,745.50	728,932.12	32.254211	-103.726491
6,500.00	9.52	103.19	6,453.69	-133.02	567.38	456,741.72	728,948.22	32.254201	-103.726439
6,600.00	9.52	103.19	6,552.32	-136.79	583.48	456,737.95	728,964.31	32.254190	-103.726387
6,700.00	9.52	103.19	6,650.94	-140.56	599.57	456,734.18	728,980.40	32.254179	-103.726335
6,800.00	9.52	103.19	6,749.56	-144.33	615.67	456,730.40	728,996.50	32.254169	-103.726283
6,900.00	9.52	103.19	6,848.19	-148.11	631.76	456,726.63	729,012.59	32.254158	-103.726231
7,000.00	9.52	103.19	6,946.81	-151.88	647.85	456,722.86	729,028.69	32.254148	-103.726179
7,100.00	9.52	103.19	7,045.44	-155.65	663.95	456,719.08	729,044.78	32.254137	-103.726127
7,200.00	9.52	103.19	7,144.06	-159.43	680.04	456,715.31	729,060.88	32.254126	-103.726075
7,300.00	9.52	103.19	7,242.69	-163.20	696.14	456,711.54	729,076.97	32.254116	-103.726023
7,400.00	9.52	103.19	7,341.31	-166.97	712.23	456,707.76	729,093.06	32.254105	-103.725971
7,500.00	9.52	103.19	7,439.93	-170.75	728.33	456,703.99	729,109.16	32.254094	-103.725919
7,600.00	9.52	103.19	7,538.56	-174.52	744.42	456,700.22	729,125.25	32.254084	-103.725867
7,700.00	9.52	103.19	7,637.18	-178.29	760.51	456,696.44	729,141.35	32.254073	-103.725815
7,800.00	9.52	103.19	7,735.81	-182.07	776.61	456,692.67	729,157.44	32.254063	-103.725763
7,900.00	9.52	103.19	7,834.43	-185.84	792.70	456,688.90	729,173.54	32.254052	-103.725711
8,000.00	9.52	103.19	7,933.05	-189.61	808.80	456,685.13	729,189.63	32.254041	-103.725659
8,100.00	9.52	103.19	8,031.68	-193.39	824.89	456,681.35	729,205.72	32.254031	-103.725607
8,200.00	9.52	103.19	8,130.30	-197.16	840.99	456,677.58	729,221.82	32.254020	-103.725555
8,300.00	9.52	103.19	8,228.93	-200.93	857.08	456,673.81	729,237.91	32.254009	-103.725503
8,400.00	9.52	103.19	8,327.55	-204.70	873.18	456,670.03	729,254.01	32.253999	-103.725451
8,500.00	9.52	103.19	8,426.18	-208.48	889.27	456,666.26	729,270.10	32.253988	-103.725399
8,600.00	9.52	103.19	8,524.80	-212.25	905.36	456,662.49	729,286.20	32.253978	-103.725347
8,700.00	9.52	103.19	8,623.42	-216.02	921.46	456,658.71	729,302.29	32.253967	-103.725295
8,800.00	9.52	103.19	8,722.05	-219.80	937.55	456,654.94	729,318.39	32.253956	-103.725243
8,900.00	9.52	103.19	8,820.67	-223.57	953.65	456,651.17	729,334.48	32.253946	-103.725191
9,000.00	9.52	103.19	8,919.30	-227.34	969.74	456,647.39	729,350.57	32.253935	-103.725139
9,100.00	9.52	103.19	9,017.92	-231.12	985.84	456,643.62	729,366.67	32.253924	-103.725087
9,200.00	9.52	103.19	9,116.55	-234.89	1,001.93	456,639.85	729,382.76	32.253914	-103.725035
9,300.00	9.52	103.19	9,215.17	-238.66	1,018.02	456,636.07	729,398.86	32.253903	-103.724983
9,400.00	9.52	103.19	9,313.79	-242.44	1,034.12	456,632.30	729,414.95	32.253893	-103.724931
9,500.00	9.52	103.19	9,412.42	-246.21	1,050.21	456,628.53	729,431.05	32.253882	-103.724879
9,600.00	9.52	103.19	9,511.04	-249.98	1,066.31	456,624.76	729,447.14	32.253871	-103.724827
9,700.00	9.52	103.19	9,609.67	-253.75	1,082.40	456,620.98	729,463.23	32.253861	-103.724775
9,800.00	9.52	103.19	9,708.29	-257.53	1,098.50	456,617.21	729,479.33	32.253850	-103.724723
9,900.00	9.52	103.19	9,806.91	-261.30	1,114.59	456,613.44	729,495.42	32.253840	-103.724671
10,000.00	9.52	103.19	9,905.54	-265.07	1,130.69	456,609.66	729,511.52	32.253829	-103.724619
10,078.23	9.52	103.19	9,982.69	-268.03	1,143.28	456,606.71	729,524.11	32.253821	-103.724579
KOP @ 10078' MD, 50' FSL, 498' FEL									
10,100.00	9.26	89.91	10,004.17	-268.43	1,146.78	456,606.30	729,527.61	32.253819	-103.724567
10,200.00	13.57	42.17	10,102.38	-259.70	1,162.74	456,615.03	729,543.57	32.253843	-103.724515
10,300.00	21.93	23.58	10,197.60	-233.83	1,178.13	456,640.91	729,558.96	32.253914	-103.724465
10,306.32	22.50	22.87	10,203.46	-231.63	1,179.07	456,643.10	729,559.90	32.253920	-103.724462
FTP @ 10306' MD, 100' FSL, 460' FEL									



# Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Company:	WCDCS Permian NM	TVD Reference:	RKB @ 3533.80ft
Project:	Eddy County (NAD 83 NM Eastern)	MD Reference:	RKB @ 3533.80ft
Site:	Sec. 36-T23S-R31E	North Reference:	Grid
Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
10,400.00	31.24	15.29	10,286.97	-191.60	1,192.47	456,683.14	729,573.30	32.254030	-103.724418
10,500.00	40.85	10.57	10,367.74	-134.29	1,205.33	456,740.44	729,586.17	32.254187	-103.724375
10,600.00	50.59	7.40	10,437.49	-63.66	1,216.33	456,811.08	729,597.16	32.254381	-103.724339
10,700.00	60.40	5.01	10,494.07	18.17	1,225.13	456,892.91	729,605.96	32.254606	-103.724309
10,800.00	70.24	3.06	10,535.78	108.70	1,231.45	456,983.43	729,612.28	32.254855	-103.724286
10,900.00	80.10	1.33	10,561.35	205.17	1,235.11	457,079.91	729,615.95	32.255120	-103.724273
11,000.00	89.97	359.71	10,570.00	304.66	1,236.00	457,179.40	729,616.83	32.255393	-103.724268
11,000.34	90.00	359.70	10,570.00	305.00	1,236.00	457,179.74	729,616.83	32.255394	-103.724268
11,100.00	90.00	359.70	10,570.00	404.66	1,235.48	457,279.40	729,616.31	32.255668	-103.724268
11,200.00	90.00	359.70	10,570.00	504.66	1,234.95	457,379.40	729,615.79	32.255943	-103.724268
11,300.00	90.00	359.70	10,570.00	604.66	1,234.43	457,479.40	729,615.26	32.256218	-103.724268
11,400.00	90.00	359.70	10,570.00	704.66	1,233.91	457,579.39	729,614.74	32.256493	-103.724268
11,500.00	90.00	359.70	10,570.00	804.66	1,233.38	457,679.39	729,614.22	32.256768	-103.724267
11,600.00	90.00	359.70	10,570.00	904.66	1,232.86	457,779.39	729,613.69	32.257043	-103.724267
11,700.00	90.00	359.70	10,570.00	1,004.65	1,232.34	457,879.39	729,613.17	32.257317	-103.724267
11,800.00	90.00	359.70	10,570.00	1,104.65	1,231.81	457,979.39	729,612.64	32.257592	-103.724267
11,900.00	90.00	359.70	10,570.00	1,204.65	1,231.29	458,079.39	729,612.12	32.257867	-103.724267
12,000.00	90.00	359.70	10,570.00	1,304.65	1,230.77	458,179.39	729,611.60	32.258142	-103.724267
12,100.00	90.00	359.70	10,570.00	1,404.65	1,230.24	458,279.38	729,611.07	32.258417	-103.724267
12,200.00	90.00	359.70	10,570.00	1,504.65	1,229.72	458,379.38	729,610.55	32.258692	-103.724266
12,300.00	90.00	359.70	10,570.00	1,604.65	1,229.20	458,479.38	729,610.03	32.258967	-103.724266
12,400.00	90.00	359.70	10,570.00	1,704.65	1,228.67	458,579.38	729,609.50	32.259242	-103.724266
12,500.00	90.00	359.70	10,570.00	1,804.64	1,228.15	458,679.38	729,608.98	32.259516	-103.724266
12,600.00	90.00	359.70	10,570.00	1,904.64	1,227.62	458,779.38	729,608.46	32.259791	-103.724266
12,700.00	90.00	359.70	10,570.00	2,004.64	1,227.10	458,879.37	729,607.93	32.260066	-103.724266
12,800.00	90.00	359.70	10,570.00	2,104.64	1,226.58	458,979.37	729,607.41	32.260341	-103.724266
12,900.00	90.00	359.70	10,570.00	2,204.64	1,226.05	459,079.37	729,606.89	32.260616	-103.724265
13,000.00	90.00	359.70	10,570.00	2,304.64	1,225.53	459,179.37	729,606.36	32.260891	-103.724265
13,100.00	90.00	359.70	10,570.00	2,404.64	1,225.01	459,279.37	729,605.84	32.261166	-103.724265
13,200.00	90.00	359.70	10,570.00	2,504.63	1,224.48	459,379.37	729,605.31	32.261441	-103.724265
13,300.00	90.00	359.70	10,570.00	2,604.63	1,223.96	459,479.36	729,604.79	32.261715	-103.724265
13,400.00	90.00	359.70	10,570.00	2,704.63	1,223.44	459,579.36	729,604.27	32.261990	-103.724265
13,500.00	90.00	359.70	10,570.00	2,804.63	1,222.91	459,679.36	729,603.74	32.262265	-103.724265
13,600.00	90.00	359.70	10,570.00	2,904.63	1,222.39	459,779.36	729,603.22	32.262540	-103.724264
13,700.00	90.00	359.70	10,570.00	3,004.63	1,221.86	459,879.36	729,602.70	32.262815	-103.724264
13,800.00	90.00	359.70	10,570.00	3,104.63	1,221.34	459,979.36	729,602.17	32.263090	-103.724264
13,900.00	90.00	359.70	10,570.00	3,204.62	1,220.82	460,079.36	729,601.65	32.263365	-103.724264
14,000.00	90.00	359.70	10,570.00	3,304.62	1,220.29	460,179.35	729,601.13	32.263640	-103.724264
14,100.00	90.00	359.70	10,570.00	3,404.62	1,219.77	460,279.35	729,600.60	32.263915	-103.724264
14,200.00	90.00	359.70	10,570.00	3,504.62	1,219.25	460,379.35	729,600.08	32.264189	-103.724264
14,300.00	90.00	359.70	10,570.00	3,604.62	1,218.72	460,479.35	729,599.56	32.264464	-103.724263
14,400.00	90.00	359.70	10,570.00	3,704.62	1,218.20	460,579.35	729,599.03	32.264739	-103.724263
14,500.00	90.00	359.70	10,570.00	3,804.62	1,217.68	460,679.35	729,598.51	32.265014	-103.724263
14,600.00	90.00	359.70	10,570.00	3,904.62	1,217.15	460,779.34	729,597.98	32.265289	-103.724263
14,700.00	90.00	359.70	10,570.00	4,004.61	1,216.63	460,879.34	729,597.46	32.265564	-103.724263
14,800.00	90.00	359.70	10,570.00	4,104.61	1,216.11	460,979.34	729,596.94	32.265839	-103.724263
14,900.00	90.00	359.70	10,570.00	4,204.61	1,215.58	461,079.34	729,596.41	32.266114	-103.724263
15,000.00	90.00	359.70	10,570.00	4,304.61	1,215.06	461,179.34	729,595.89	32.266388	-103.724262
15,100.00	90.00	359.70	10,570.00	4,404.61	1,214.53	461,279.34	729,595.37	32.266663	-103.724262
15,200.00	90.00	359.70	10,570.00	4,504.61	1,214.01	461,379.33	729,594.84	32.266938	-103.724262
15,300.00	90.00	359.70	10,570.00	4,604.61	1,213.49	461,479.33	729,594.32	32.267213	-103.724262
15,400.00	90.00	359.70	10,570.00	4,704.60	1,212.96	461,579.33	729,593.80	32.267488	-103.724262
15,500.00	90.00	359.70	10,570.00	4,804.60	1,212.44	461,679.33	729,593.27	32.267763	-103.724262
15,600.00	90.00	359.70	10,570.00	4,904.60	1,211.92	461,779.33	729,592.75	32.268038	-103.724262



# Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Company:	WCDSC Permian NM	TVD Reference:	RKB @ 3533.80ft
Project:	Eddy County (NAD 83 NM Eastern)	MD Reference:	RKB @ 3533.80ft
Site:	Sec. 36-T23S-R31E	North Reference:	Grid
Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
15,620.00	90.00	359.70	10,570.00	4,924.60	1,211.81	461,799.33	729,592.64	32.268093	-103.724262
Cross Section @ 15620' MD, 0' FSL, 400' FEL									
15,700.00	90.00	359.70	10,570.00	5,004.60	1,211.39	461,879.33	729,592.22	32.268313	-103.724261
15,800.00	90.00	359.70	10,570.00	5,104.60	1,210.87	461,979.33	729,591.70	32.268587	-103.724261
15,900.00	90.00	359.70	10,570.00	5,204.60	1,210.35	462,079.32	729,591.18	32.268862	-103.724261
16,000.00	90.00	359.70	10,570.00	5,304.60	1,209.82	462,179.32	729,590.65	32.269137	-103.724261
16,100.00	90.00	359.70	10,570.00	5,404.59	1,209.30	462,279.32	729,590.13	32.269412	-103.724261
16,200.00	90.00	359.70	10,570.00	5,504.59	1,208.77	462,379.32	729,589.61	32.269687	-103.724261
16,300.00	90.00	359.70	10,570.00	5,604.59	1,208.25	462,479.32	729,589.08	32.269962	-103.724261
16,400.00	90.00	359.70	10,570.00	5,704.59	1,207.73	462,579.32	729,588.56	32.270237	-103.724260
16,500.00	90.00	359.70	10,570.00	5,804.59	1,207.20	462,679.31	729,588.04	32.270512	-103.724260
16,600.00	90.00	359.70	10,570.00	5,904.59	1,206.68	462,779.31	729,587.51	32.270786	-103.724260
16,700.00	90.00	359.70	10,570.00	6,004.59	1,206.16	462,879.31	729,586.99	32.271061	-103.724260
16,800.00	90.00	359.70	10,570.00	6,104.59	1,205.63	462,979.31	729,586.47	32.271336	-103.724260
16,900.00	90.00	359.70	10,570.00	6,204.58	1,205.11	463,079.31	729,585.94	32.271611	-103.724260
17,000.00	90.00	359.70	10,570.00	6,304.58	1,204.59	463,179.31	729,585.42	32.271886	-103.724260
17,100.00	90.00	359.70	10,570.00	6,404.58	1,204.06	463,279.31	729,584.89	32.272161	-103.724260
17,200.00	90.00	359.70	10,570.00	6,504.58	1,203.54	463,379.30	729,584.37	32.272436	-103.724259
17,300.00	90.00	359.70	10,570.00	6,604.58	1,203.02	463,479.30	729,583.85	32.272711	-103.724259
17,400.00	90.00	359.70	10,570.00	6,704.58	1,202.49	463,579.30	729,583.32	32.272985	-103.724259
17,500.00	90.00	359.70	10,570.00	6,804.58	1,201.97	463,679.30	729,582.80	32.273260	-103.724259
17,600.00	90.00	359.70	10,570.00	6,904.57	1,201.44	463,779.30	729,582.28	32.273535	-103.724259
17,700.00	90.00	359.70	10,570.00	7,004.57	1,200.92	463,879.30	729,581.75	32.273810	-103.724259
17,800.00	90.00	359.70	10,570.00	7,104.57	1,200.40	463,979.29	729,581.23	32.274085	-103.724259
17,900.00	90.00	359.70	10,570.00	7,204.57	1,199.87	464,079.29	729,580.71	32.274360	-103.724258
18,000.00	90.00	359.70	10,570.00	7,304.57	1,199.35	464,179.29	729,580.18	32.274635	-103.724258
18,100.00	90.00	359.70	10,570.00	7,404.57	1,198.83	464,279.29	729,579.66	32.274910	-103.724258
18,200.00	90.00	359.70	10,570.00	7,504.57	1,198.30	464,379.29	729,579.13	32.275184	-103.724258
18,300.00	90.00	359.70	10,570.00	7,604.56	1,197.78	464,479.29	729,578.61	32.275459	-103.724258
18,400.00	90.00	359.70	10,570.00	7,704.56	1,197.26	464,579.28	729,578.09	32.275734	-103.724258
18,500.00	90.00	359.70	10,570.00	7,804.56	1,196.73	464,679.28	729,577.56	32.276009	-103.724258
18,600.00	90.00	359.70	10,570.00	7,904.56	1,196.21	464,779.28	729,577.04	32.276284	-103.724257
18,700.00	90.00	359.70	10,570.00	8,004.56	1,195.68	464,879.28	729,576.52	32.276559	-103.724257
18,800.00	90.00	359.70	10,570.00	8,104.56	1,195.16	464,979.28	729,575.99	32.276834	-103.724257
18,900.00	90.00	359.70	10,570.00	8,204.56	1,194.64	465,079.28	729,575.47	32.277109	-103.724257
19,000.00	90.00	359.70	10,570.00	8,304.56	1,194.11	465,179.28	729,574.95	32.277383	-103.724257
19,100.00	90.00	359.70	10,570.00	8,404.55	1,193.59	465,279.27	729,574.42	32.277658	-103.724257
19,200.00	90.00	359.70	10,570.00	8,504.55	1,193.07	465,379.27	729,573.90	32.277933	-103.724257
19,300.00	90.00	359.70	10,570.00	8,604.55	1,192.54	465,479.27	729,573.38	32.278208	-103.724256
19,400.00	90.00	359.70	10,570.00	8,704.55	1,192.02	465,579.27	729,572.85	32.278483	-103.724256
19,500.00	90.00	359.70	10,570.00	8,804.55	1,191.50	465,679.27	729,572.33	32.278758	-103.724256
19,600.00	90.00	359.70	10,570.00	8,904.55	1,190.97	465,779.27	729,571.80	32.279033	-103.724256
19,700.00	90.00	359.70	10,570.00	9,004.55	1,190.45	465,879.26	729,571.28	32.279308	-103.724256
19,800.00	90.00	359.70	10,570.00	9,104.54	1,189.93	465,979.26	729,570.76	32.279582	-103.724256
19,900.00	90.00	359.70	10,570.00	9,204.54	1,189.40	466,079.26	729,570.23	32.279857	-103.724256
20,000.00	90.00	359.70	10,570.00	9,304.54	1,188.88	466,179.26	729,569.71	32.280132	-103.724255
20,100.00	90.00	359.70	10,570.00	9,404.54	1,188.35	466,279.26	729,569.19	32.280407	-103.724255
20,200.00	90.00	359.70	10,570.00	9,504.54	1,187.83	466,379.26	729,568.66	32.280682	-103.724255
20,300.00	90.00	359.70	10,570.00	9,604.54	1,187.31	466,479.25	729,568.14	32.280957	-103.724255
20,400.00	90.00	359.70	10,570.00	9,704.54	1,186.78	466,579.25	729,567.62	32.281232	-103.724255
20,500.00	90.00	359.70	10,570.00	9,804.53	1,186.26	466,679.25	729,567.09	32.281507	-103.724255
20,600.00	90.00	359.70	10,570.00	9,904.53	1,185.74	466,779.25	729,566.57	32.281782	-103.724255
20,700.00	90.00	359.70	10,570.00	10,004.53	1,185.21	466,879.25	729,566.04	32.282056	-103.724254
20,800.00	90.00	359.70	10,570.00	10,104.53	1,184.69	466,979.25	729,565.52	32.282331	-103.724254



# Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference:	Well Todd 36_25 State Fed Com 235H
Company:	WCDSC Permian NM	TVD Reference:	RKB @ 3533.80ft
Project:	Eddy County (NAD 83 NM Eastern)	MD Reference:	RKB @ 3533.80ft
Site:	Sec. 36-T23S-R31E	North Reference:	Grid
Well:	Todd 36_25 State Fed Com 235H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
20,828.37	90.00	359.70	10,570.00	10,132.90	1,184.54	467,007.62	729,565.37	32.282409	-103.724254
LTP @ 20828' MD, 100' FNL, 400' FEL									
20,900.00	90.00	359.70	10,570.00	10,204.53	1,184.17	467,079.25	729,565.00	32.282606	-103.724254
20,908.37	90.00	359.70	10,570.00	10,212.90	1,184.12	467,087.62	729,564.95	32.282629	-103.724254
PBHL; 20' FNL, 400' FEL									

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- hit/miss target									
- Shape									
PBHL - Todd 36_25 Stat	0.00	0.00	0.00	10,213.19	1,181.65	467,087.91	729,562.48	32.282630	-103.724262
- plan misses target center by 10281.32ft at 0.00ft MD (0.00 TVD, 0.00 N, 0.00 E)									
- Point									

Plan Annotations					
Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates			
		+N/-S (ft)	+E/-W (ft)	Comment	
10,078.23	9,982.69	-268.03	1,143.28	KOP @ 10078' MD, 50' FSL, 498' FEL	
10,306.32	10,203.46	-231.63	1,179.07	FTP @ 10306' MD, 100' FSL, 460' FEL	
15,620.00	10,570.00	4,924.60	1,211.81	Cross Section @ 15620' MD, 0' FSL, 400' FEL	
20,828.37	10,570.00	10,132.90	1,184.54	LTP @ 20828' MD, 100' FNL, 400' FEL	
20,908.37	10,570.00	10,212.90	1,184.12	PBHL; 20' FNL, 400' FEL	



# Devon Energy



WELL DETAILS: Todd 36\_25 State Fed Com 235H

RKB @ 3533.80ft  
3508.80


Northing 456874.74 Easting 728380.84 Latitude 32.254575 Longitude -103.728272

## SECTION DETAILS Permit Plan 1

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	VSect	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2500.00	0.00	0.00	2500.00	0.00	0.00	0.00	0.00	
3451.51	9.52	103.19	3447.14	-17.99	76.75	1.00	-9.03	
10078.23	9.52	103.19	9982.89	-268.03	1143.28	0.00	-134.57	KOP @ 10078' MD, 50' FSL, 498' FEL
11000.34	90.00	359.70	10570.00	305.00	1236.00	10.00	445.32	
20908.37	90.00	359.70	10570.00	10212.90	1184.12	0.00	10281.32	PBHL: 20' FNL, 400' FEL




# devon

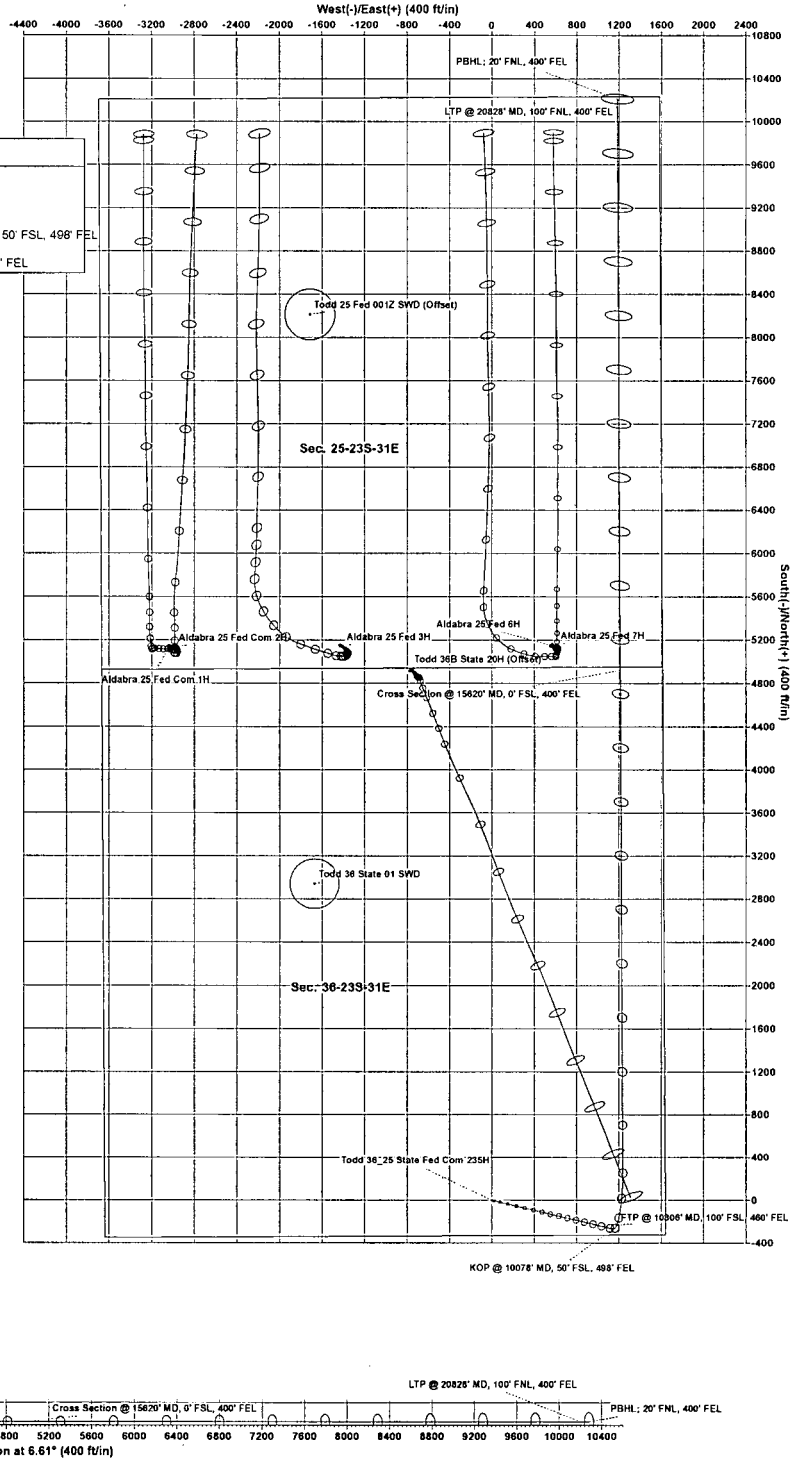





Commitment Runs Deep

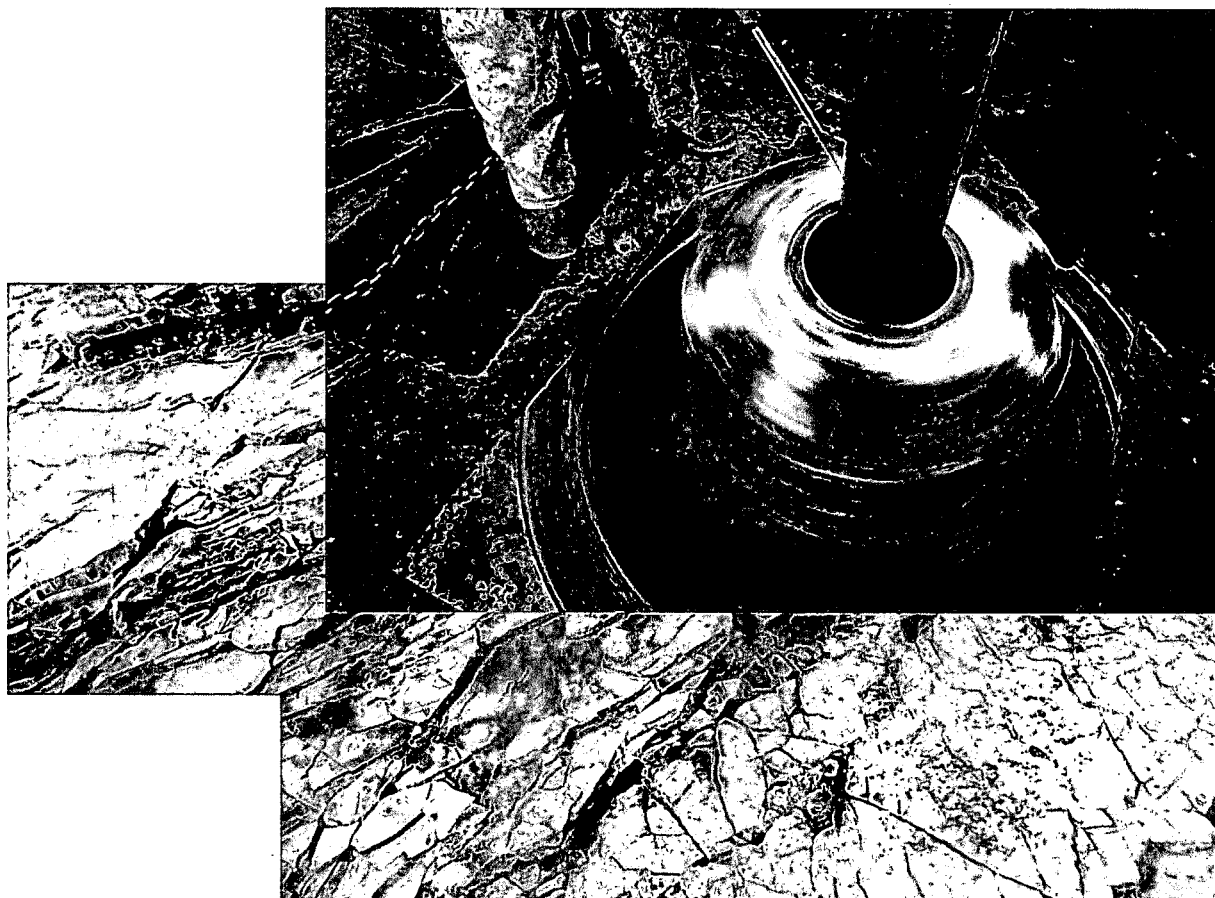

Design Plan  
Operation and Maintenance Plan  
Closure Plan

SENM - Closed Loop Systems  
June 2010



## **I. Design Plan**

Devon uses MI SWACO closed loop system (CLS). The MI SWACO CLS is designed to maintain drill solids at or below 5%. The equipment is arranged to progressively remove solids from the largest to the smallest size. Drilling fluids can thus be reused and savings is realized on mud and disposal costs. Dewatering may be required with the centrifuges to insure removal of ultra fine solids.

The drilling location is constructed to allow storm water to flow to a central sump normally the cellar. This insures no contamination leaves the drilling pad in the event of a spill. Storm water is reused in the mud system or stored in a reserve fluid tank farm until it can be reused. All lubricants, oils, or chemicals are removed immediately from the ground to prevent the contamination of storm water. An oil trap is normally installed on the sump if an oil spill occurs during a storm.

A tank farm is utilized to store drilling fluids including fresh water and brine fluids. The tank farm is constructed on a 20 ml plastic lined, bermed pad to prevent the contamination of the drilling site during a spill. Fluids from other sites may be stored in these tanks for processing by the solids control equipment and reused in the mud system. At the end of the well the fluids are transported from the tank farm to an adjoining well or to the next well for the rig.

Prior to installing a closed-loop system on site, the topsoil, if present, will be stripped and stockpiled for use as the final cover or fill at the time of closure.

Signs will be posted on the fence surrounding the closed-loop system unless the closed-loop system is located on a site where there is an existing well, that is operated by Devon.

## **II. Operations and Maintenance Plan**


*Primary Shakers:* The primary shakers make the first removal of drill solids from the drilling mud as it leaves the well bore. The shakers are sized to handle maximum drilling rate at optimal screen size. The shakers normally remove solids down to 74 microns.



**Mud Cleaner:** The Mud Cleaner cleans the fluid after it leaves the shakers. A set of hydrocyclones are sized to handle 1.25 to 1.5 times the maximum circulating rate. This ensures all the fluid is being processed to an average cut point of 25 microns. The wet discharged is dewatered on a shaker equipped with ultra fine mesh screens and generally cut at 40 microns.

**devon**

## Closed Loop Schematic

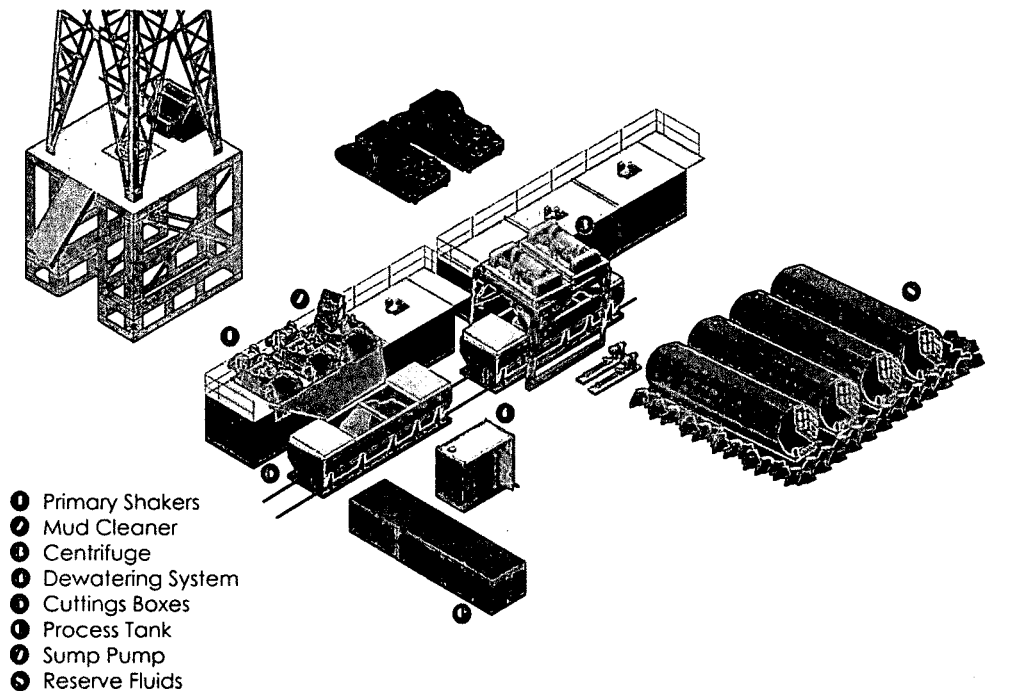

**Mi SWACO**

**Centrifuges:** The centrifuges can be one or two in number depending on the well geometry or depth of well. The centrifuges are sized to maintain low gravity solids at 5% or below. They may or may not need a dewatering system to enhance the removal rates. The centrifuges can make a cut point of 8-10 microns depending on bowl speed, feed rate, solids loading and other factors.

The centrifuge system is designed to work on the active system and be flexible to process incoming fluids from other locations. This set-up is also dependant on well factors.

**Dewatering System:** The dewatering system is a chemical mixing and dosing system designed to enhance the solids removal of the centrifuge. Not commonly used in shallow wells. It may contain pH adjustment, coagulant mixing and dosing, and polymer mixing and dosing. Chemical flocculation binds ultra fine solids into a mass that is within the centrifuge operating design. The



dewatering system improves the centrifuge cut point to infinity or allows for the return of clear water or brine fluid. This ability allows for the ultimate control of low gravity solids.

*Cuttings Boxes:* Cuttings boxes are utilized to capture drill solids that are discarded from the solids control equipment. These boxes are set upon a rail system that allows for the removal and replacement of a full box of cuttings with an empty one. They are equipped with a cover that insures no product is spilled into the environment during the transportation phase.

*Process Tank:* (Optional) The process tank allows for the holding and process of fluids that are being transferred into the mud system. Additionally, during times of lost circulation the process tank may hold active fluids that are removed for additional treatment. It can further be used as a mixing tank during well control conditions.

*Sump and Sump Pump:* The sump is used to collect storm water and the pump is used to transfer this fluid to the active system or to the tank for to hold in reserve. It can also be used to collect fluids that may escape during spills. The location contains drainage ditches that allow the location fluids to drain to the sump.

*Reserve Fluids (Tank Farm):* A series of frac tanks are used to replace the reserve pit. These are steel tanks that are equipped with a manifold system and a transfer pump. These tanks can contain any number of fluids used during the drilling process. These can include fresh water, cut brine, and saturated salt fluid. The fluid can be from the active well or reclaimed fluid from other locations. A 20 ml liner and berm system is employed to ensure the fluids do not migrate to the environment during a spill.

If a leak develops, the appropriate division district office will be notified within 48 hours of the discovery and the leak will be addressed. Spill prevention is accomplished by maintaining pump packing, hoses, and pipe fittings to insure no leaks are occurring. During an upset condition the source of the spill is isolated and repaired as soon as it is discovered. Free liquid is removed by a diaphragm pump and returned to the mud system. Loose topsoil may be used to stabilize the spill and the contaminated soil is excavated and placed in the cuttings boxes. After the well is finished and the rig has moved, the entire location is scrapped and testing will be performed to determine if a release has occurred.

All trash is kept in a wire mesh enclosure and removed to an approved landfill when full. All spent motor oils are kept in separate containers and they are removed and sent to an approved recycling center. Any spilled lubricants, pipe



dope, or regulated chemicals are removed from soil and sent to landfills approved for these products.

These operations are monitored by Mi Swaco service technicians. Daily logs are maintained to ensure optimal equipment operation and maintenance. Screen and chemical use is logged to maintain inventory control. Fluid properties are monitored and recorded and drilling mud volumes are accounted for in the mud storage farm. This data is kept for end of well review to insure performance goals are met. Lessons learned are logged and used to help with continuous improvement.

A MI SWACO field supervisor manages from 3-5 wells. They are responsible for training personnel, supervising installations, and inspecting sites for compliance of MI SWACO safety and operational policy.

### **III. Closure Plan**

A maximum 340' X 340' caliche pad is built per well. All of the trucks and steel tanks fit on this pad. All fluid cuttings go to the steel tanks to be hauled by various trucking companies to an agency approved disposal.



## Devon Energy, Todd 36-25 State Fed Com 235H

### 1. Geologic Formations

TVD of target	10570	Pilot hole depth	N/A
MD at TD:	20908	Deepest expected fresh water:	

#### Basin

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Rustler	811		
Salado	1146		
Base of Salt	4445		
Delaware	4506		
L Brushy Canyon	8056		
Bone Spring	8386		
Leonard 'A'	8486		
Leonard 'B'	8971		
Leonard 'C'	9136		
2nd BSPG Lime	9871		
2nd BSPG Sand	10036		
L 2nd BSPG Sand	10536		
Landing Point	10550		

\*H2S, water flows, loss of circulation, abnormal pressures, etc.



## Devon Energy, Todd 36-25 State Fed Com 235H

### 2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (PPF)	Grade	Conn.
	From	To				
17.5"	0	836	13.375"	48	H-40	STC
12.25"	0	6000	9.625"	40	J-55	BTC
8.75"	0	TD	5.5"	17	P-110	BTC
BLM Minimum Safety Factor				Collapse: 1.125	Burst: 1.00	Tension: 1.6 Dry 1.8 Wet

- All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h Must have table for contingency casing
- Rustler top will be validated via drilling parameters (i.e. reduction in ROP) and surface casing setting depth revised accordingly if needed.
- Variance is requested for collapse rating on intermediate casing. Operator will keep pipe full while running casing. No losses are expected in subsequent hole section.
- Int casing shoe will be selected based on drilling data, gamma, and flows experienced while drilling. Setting depth will be revised accordingly if needed.
- A variance is requested to wave the centralizer requirement for the intermediate and production casing strings if drilling conditions dictate



**Devon Energy, Todd 36-25 State Fed Com 235H**

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 <sup>rd</sup> string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 <sup>nd</sup> string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	



## Devon Energy, Todd 36-25 State Fed Com 235H

### 3. Cementing Program (3-String Primary Design)

Casing	# Sk	TOC	Wt. (lb/gal)	Yld (ft3/sack)	Slurry Description
Surface	873	Surf	13.2	1.33	Lead: Class C Cement + additives
Int	1095	Surf	9	1.94	Lead: Class C Cement + additives
	196	500' above shoe	13.2	1.33	Tail: Class H / C + additives
Int 1 Two Stage (optional) w/ DV @ ~4500	560	Surf	9	1.94	Stage 1 Lead: Class C Cement + additives
	196	500' above shoe	13.2	1.33	Stage 1 Tail: Class H / C + additives
	570	Surf	9	1.94	Stage 2 Lead: Class C Cement + additives
	196	500' above DV	13.2	1.33	Stage 2 Tail: Class H / C + additives
Int 1 Intermediate Squeeze	As Needed	Surf	13.2	1.33	Squeeze Lead: Class C Cement + additives
	1095	Surf	9	1.94	Lead: Class C Cement + additives
	196	500' above shoe	13.2	1.33	Tail: Class H / C + additives
Production	357	500' tieback	9	3.569	Lead: Class H / C + additives
	1885	KOP	13.2	1.46	Tail: Class H / C + additives

If a DV tool is ran the depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. Slurry weights will be adjusted based on estimated fracture gradient of the formation. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe. If cement is not returned to surface during the primary cement job on the surface casing string, a planned top job will be conducted immediately after completion of the primary job.

Casing String	% Excess
Surface	100%
Intermediate	50%
Production	10%



**Devon Energy, Todd 36-25 State Fed Com 235H**

**4. Pressure Control Equipment**

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
Int 1	13-5/8"	5M	Annular	X	50% of rated working pressure
			Blind Ram		5M
			Pipe Ram		
			Double Ram	X	
			Other*		
Production	13-5/8"	5M	Annular	X	50% of rated working pressure
			Blind Ram		5M
			Pipe Ram		
			Double Ram	X	
			Other*		
			Annular		
			Blind Ram		
			Pipe Ram		
			Double Ram		
			Other*		



## Devon Energy, Todd 36-25 State Fed Com 235H

### 5. Mud Program

Interval	Type	Weight (ppg)	Vis	Water Loss
Surface	FW	8.5 – 9.0	28-34	N/C
Intermediate	Brine	10 – 10.5	28-34	N/C
Production	WBM	8.5 – 9.0	28-34	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

### 6. Logging and Testing Procedures

Logging, Coring and Testing.	
X	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No Logs are planned based on well control or offset log information.
	Drill stem test? If yes, explain
	Coring? If yes, explain

Additional logs planned	Interval
Resistivity	
Density	
X CBL	Production casing
X Mud log	KOP to TD

### 7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	4947 psi
Abnormal Temperature	No

Mitigation measure for abnormal conditions. Describe. Lost circulation material/sweeps/mud scavengers.

Hydrogen Sulfide (H <sub>2</sub> S) monitors will be installed prior to drilling out the surface shoe. If H <sub>2</sub> S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.	
N	H <sub>2</sub> S is present
Y	H <sub>2</sub> S Plan attached



## Devon Energy, Todd 36-25 State Fed Com 235H

### 8. Other facets of operation

Is this a walking operation? Potentially

1. If operator elects, drilling rig will batch drill the surface holes and run/cement surface casing; walking the rig to next wells on the pad.
2. The drilling rig will then batch drill the intermediate sections and run/cement intermediate casing; the wellbore will be isolated with a blind flange and pressure gauge installed for monitoring the well before walking to the next well.
3. The drilling rig will then batch drill the production hole sections on the wells with OBM, run/cement production casing, and install TA caps or tubing heads for completions.

NOTE: During batch operations the drilling rig will be moved from well to well however, it will not be removed from the pad until all wells have production casing run/cemented.


Will be pre-setting casing? Potentially

1. Spudder rig will move in and drill surface hole.
  - a. Rig will utilize fresh water based mud to drill surface hole to TD. Solids control will be handled entirely on a closed loop basis.
2. After drilling the surface hole section, the spudder rig will run casing and cement following all of the applicable rules and regulations (OnShore Order 2, all COAs and NMOCD regulations).
3. The wellhead will be installed and tested once the surface casing is cut off and the WOC time has been reached.
4. A blind flange with the same pressure rating as the wellhead will be installed to seal the wellbore. Pressure will be monitored with a pressure gauge installed on the wellhead.
5. Spudder rig operations is expected to take 4-5 days per well on a multi well pad.
6. The NMOCD will be contacted and notified 24 hours prior to commencing spudder rig operations.
7. Drilling operations will be performed with the drilling rig. At that time an approved BOP stack will be nipped up and tested on the wellhead before drilling operations commences on each well.
  - a. The NMOCD will be contacted / notified 24 hours before the drilling rig moves back on to the pad with the pre-set surface casing.

Attachments

- ☒ Directional Plan  
☐ Other, describe



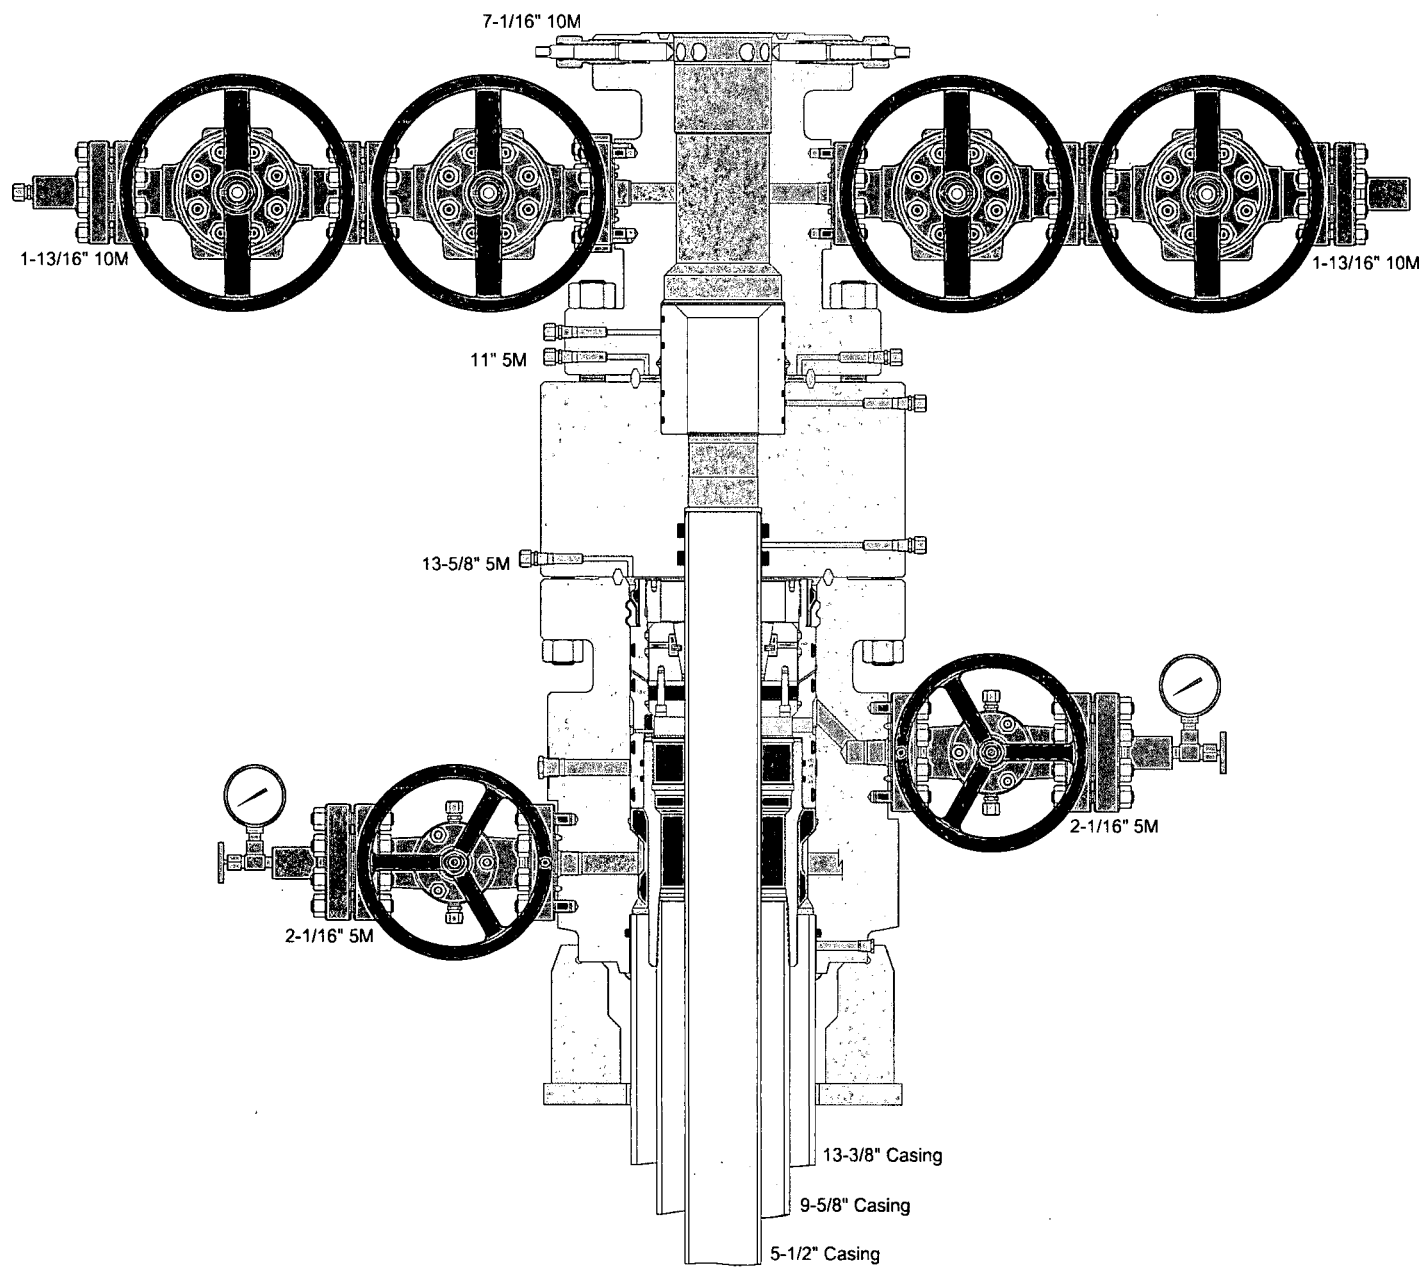



A multibowl wellhead may be used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

Devon proposes using a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 5000 (5M) psi.

- Wellhead will be installed by wellhead representatives.
- If the welding is performed by a third party, the wellhead representative will monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- Wellhead representative will install the test plug for the initial BOP test.
- Wellhead company will install a solid steel body pack-off to completely isolate the lower head after cementing intermediate casing. After installation of the pack-off, the pack-off and the lower flange will be tested to 5M, as shown on the attached schematic. Everything above the pack-off will not have been altered whatsoever from the initial nipple up. Therefore the BOP components will not be retested at that time.
- If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head will be cut and top out operations will be conducted.
- Devon will pressure test all seals above and below the mandrel (but still above the casing) to full working pressure rating.
- Devon will test the casing to 0.22 psi/ft or 1500 psi, whichever is greater, as per Onshore Order #2.

After running the 13-3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 5M will be installed on the wellhead system and will undergo a 250 psi low pressure test followed by a 5,000 psi high pressure test. The 5,000 psi high and 250 psi low test will cover testing requirements a maximum of 30 days, as per Onshore Order #2. If the well is not complete within 30 days of this BOP test, another full BOP test will be conducted, as per Onshore Order #2.

After running the 9-5/8" intermediate casing with a mandrel hanger, the 13-5/8" BOP/BOPE system with a minimum rating of 5M will already be installed on the wellhead.

The pipe rams will be operated and checked each 24 hour period and each time the drill pipe is out of the hole. These tests will be logged in the daily driller's log. A 2" kill line and 3" choke line will be incorporated into the drilling spool below the ram BOP. In addition to the rams and annular preventer, additional BOP accessories include a kelly cock, floor safety valve, choke lines, and choke manifold rated at 5,000 psi WP.

Devon's proposed wellhead manufactures will be FMC Technologies, Cactus Wellhead, or Cameron.



# **Devon Energy**

## **APD VARIANCE DATA**

**OPERATOR NAME:** Devon Energy

### **1. SUMMARY OF Variance:**

Devon Energy respectfully requests approval for the following additions to the drilling plan:

1. Potential utilization of a spudder rig to pre-set surface casing.

### **2. Description of Operations**

1. A spudder rig contractor may move in their rig to drill the surface hole section and pre-set surface casing on this well.
  - a. After drilling the surface hole section, the rig will run casing and cement following all of the applicable rules and regulations (OnShore Order 2, all COAs and NMOCD regulations).
  - b. Rig will utilize fresh water based mud to drill surface hole to TD.
2. The wellhead will be installed and tested once the surface casing is cut off and the WOC time has been reached.
3. A blind flange with the same pressure rating as the wellhead will be installed to seal the wellbore. Pressure will be monitored with needle valves installed on two wingvalves.
  - a. A means for intervention will be maintained while the drilling rig is not over the well.
4. The BLM will be contacted and notified 24 hours prior to commencing spudder rig operations.
5. Drilling operation will be performed with the big rig. At that time an approved BOP stack will be nipped up and tested on the wellhead before drilling operations commences on each well.
  - a. The BLM will be contacted / notified 24 hours before the big rig moves back on to the pad with the pre-set surface casing.
6. Devon Energy will have supervision on the rig to ensure compliance with all BLM and NMOCD regulations and to oversee operations.
7. Once the rig is removed, Devon Energy will secure the wellhead area by placing a guard rail around the cellar area.





**Fluid Technology**

ContiTech Beattie Corp.  
Website: [www.contitechbeattie.com](http://www.contitechbeattie.com)

Monday, June 14, 2010

RE: Drilling & Production Hoses  
Lifting & Safety Equipment

To Helmerich & Payne,

A Continental Contitech hose assembly can perform as intended and suitable for the application regardless of whether the hose is secured or unsecured in its configuration. As a manufacturer of High Pressure Hose Assemblies for use in Drilling & Production, we do offer the corresponding lifting and safety equipment, this has the added benefit of easing the lifting and handling of each hose assembly whilst affording hose longevity by ensuring correct handling methods and procedures as well as securing the hose in the unlikely event of a failure; but in no way does the lifting and safety equipment affect the performance of the hoses providing the hoses have been handled and installed correctly. It is good practice to use lifting & safety equipment but not mandatory.

Should you have any questions or require any additional information/clarifications then please do not hesitate to contact us.

ContiTech Beattie is part of the Continental AG Corporation and can offer the full support resources associated with a global organization.

Best regards,

Robin Hodgson  
Sales Manager  
ContiTech Beattie Corp

ContiTech Beattie Corp,  
11535 Brittmoore Park Drive,  
Houston, TX 77041  
Phone: +1 (832) 327-0141  
Fax: +1 (832) 327-0148  
[www.contitechbeattie.com](http://www.contitechbeattie.com)





RIG 212



## QUALITY DOCUMENT

**PHOENIX RUBBER  
INDUSTRIAL LTD.**

 6728 Szeged, Budapesti út 10. Hungary • H-6701 Szeged, P. O. Box 152  
 Phone: (3662) 566-737 • Fax: (3662) 566-738

 SALES & MARKETING: H-1092 Budapest, Ráday u. 42-44. Hungary • H-1440 Budapest, P. O. Box 26  
 Phone: (361) 456-4200 • Fax: (361) 217-2972, 456-4273 • www.taurusemerge.hu

QUALITY CONTROL INSPECTION AND TEST CERTIFICATE				CERT. N°: 552	
PURCHASER: Phoenix Beattie Co.			P.O. N°: 1519FA-871		
PHOENIX RUBBER order N°: 170466		HOSE TYPE: 3" ID Choke and Kill Hose			
HOSE SERIAL N°: 34128		NOMINAL / ACTUAL LENGTH: 11,43 m			
W.P. 68,96 MPa	10000	psi	T.P. 103,4 MPa	15000	psi
		Duration: 60		min.	
Pressure test with water at ambient temperature  <div style="text-align: center;">See attachment. (1 page)</div>					
↑ 10 mm = 10 Min. → 10 mm = 25 MPa					
COUPLINGS					
Type	Serial N°		Quality	Heat N°	
3" coupling with 4 1/16" Flange end	720	719	AISI 4130	C7626	
			AISI 4130	47357	
API Spec 16 C Temperature rate: "B"					
All metal parts are flawless					
WE CERTIFY THAT THE ABOVE HOSE HAS BEEN MANUFACTURED IN ACCORDANCE WITH THE TERMS OF THE ORDER AND PRESSURE TESTED AS ABOVE WITH SATISFACTORY RESULT.					
Date:	Inspector		Quality Control		
29. April. 2002.			PHOENIX RUBBER Industrial Ltd. Hose Inspection and VESSELS TRUE COPY PHOENIX RUBBER Q.C.		



40920-0-00015 N8006

8	GN4	+0.000	PC	14.00		
	RD4	+0.000	PC	14.00		
	DL	+0.000	PC	14.00		
7	GN4	+0.000	PC	13.40	40	60
	RD4	+0.000	PC	13.40		
	DL	+0.000	PC	13.40		
6	GN4	+0.000	PC	13.20		
	RD4	+0.000	PC	13.20		
	DL	+0.000	PC	13.20		
5	GN4	+0.000	PC	13.00		
	RD4	+0.000	PC	13.00		
	DL	+0.000	PC	13.00		
4						
3						
2						

**GENEX RUBBER**  
Industrial Ltd.  
Hose Inspection and  
Certification Dept.

VERIFIED TRUE CO.  
PHOENIX RUBBER CO.





U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## SUPO Data Report

04/18/2019

APD ID: 10400035068

Submission Date: 10/10/2018

Highlighted data  
reflects the most  
recent changes

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: TODD 36-25 STATE FED COM

Well Number: 235H

[Show Final Text](#)

Well Type: OIL WELL

Well Work Type: Drill

### Section 1 - Existing Roads

Will existing roads be used? YES

Existing Road Map:

TODD\_36\_25\_STATE\_FED\_COM\_235H\_EX\_ACCESS\_RD\_20181010091810.pdf

Existing Road Purpose: ACCESS, FLUID TRANSPORT

Row(s) Exist? NO

ROW ID(s)

ID:

Do the existing roads need to be improved? NO

Existing Road Improvement Description:

Existing Road Improvement Attachment:

### Section 2 - New or Reconstructed Access Roads

Will new roads be needed? YES

New Road Map:

TODD\_36\_25\_STATE\_FED\_COM\_235H\_ACCESS\_RD\_20181010091850.pdf

New road type: COLLECTOR, RESOURCE

Length: 46

Feet

Width (ft.): 30

Max slope (%): 6

Max grade (%): 4

Army Corp of Engineers (ACOE) permit required? NO

ACOE Permit Number(s):

New road travel width: 20

New road access erosion control: n/a

New road access plan or profile prepared? NO

New road access plan attachment:

Access road engineering design? NO

Access road engineering design attachment:



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

**Access surfacing type:** GRAVEL

**Access topsoil source:** BOTH

**Access surfacing type description:**

**Access onsite topsoil source depth:** 6

**Offsite topsoil source description:** n/a

**Onsite topsoil removal process:** See attached Interim reclamation diagram.

**Access other construction information:**

**Access miscellaneous information:**

**Number of access turnouts:**

**Access turnout map:**

### Drainage Control

**New road drainage crossing:** CULVERT

**Drainage Control comments:** n/a

**Road Drainage Control Structures (DCS) description:** n/a

**Road Drainage Control Structures (DCS) attachment:**

### Access Additional Attachments

**Additional Attachment(s):**

## Section 3 - Location of Existing Wells

**Existing Wells Map?** YES

**Attach Well map:**

Todd\_36\_25\_State\_Fed\_Com\_235H\_OneMileBuffer\_WA017432169\_20181010091908.pdf

**Existing Wells description:**

## Section 4 - Location of Existing and/or Proposed Production Facilities

**Submit or defer a Proposed Production Facilities plan?** DEFER

**Estimated Production Facilities description:** Wells will go to Todd 36 CTB 2 . Please refer to CTB plat.

## Section 5 - Location and Types of Water Supply

### Water Source Table



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

**Water source use type:** OTHER

**Water source type:** OTHER

**Describe type:** STIMULATION

**Source latitude:**

**Source longitude:**

**Source datum:**

**Water source permit type:** OTHER

**Source land ownership:** FEDERAL

**Water source transport method:** PIPELINE

**Source transportation land ownership:** STATE

**Water source volume (barrels):** 230000

**Source volume (acre-feet):** 29.645412

**Source volume (gal):** 9660000

**Water source and transportation map:**

TODD\_36\_25\_STATE\_FED\_COM\_233H\_234H\_235H\_water\_x\_map\_20181009092522.pdf

**Water source comments:** The attached Water Transfer Map is a proposal only and the final route and documentation will be provided by a Devon contractor prior to installation. When available Devon will always follow existing disturbance.

**New water well?** NO

### New Water Well Info

**Well latitude:**

**Well Longitude:**

**Well datum:**

**Well target aquifer:**

**Est. depth to top of aquifer(ft):**

**Est thickness of aquifer:**

**Aquifer comments:**

**Aquifer documentation:**

**Well depth (ft):**

**Well casing type:**

**Well casing outside diameter (in.):**

**Well casing inside diameter (in.):**

**New water well casing?**

**Used casing source:**

**Drilling method:**

**Drill material:**

**Grout material:**

**Grout depth:**

**Casing length (ft.):**

**Casing top depth (ft.):**

**Well Production type:**

**Completion Method:**

**Water well additional information:**

**State appropriation permit:**

**Additional information attachment:**



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

## Section 6 - Construction Materials

**Construction Materials description:** Dirt fill and caliche will be used to construct well pad. See attached map.

**Construction Materials source location attachment:**

Todd\_36\_Wellpad\_3\_Caliche\_Map\_20181010091951.pdf

## Section 7 - Methods for Handling Waste

**Waste type:** COMPLETIONS/STIMULATION

**Waste content description:** Flow back water during completion operations.

**Amount of waste:** 3000 barrels

**Waste disposal frequency :** One Time Only

**Safe containment description:** n/a

**Safe containmant attachment:**

**Waste disposal type:** HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

**Disposal type description:**

**Disposal location description:** Various disposal locations in Lea and Eddy counties.

**Waste type:** PRODUCED WATER

**Waste content description:** n/a

**Amount of waste:** 1000 barrels

**Waste disposal frequency :** Daily

**Safe containment description:** n/a

**Safe containmant attachment:**

**Waste disposal type:** ON-LEASE INJECTION **Disposal location ownership:** COMMERCIAL

**Disposal type description:**

**Disposal location description:** Multiple methods for handling waste will be utilized. Via trucking, Dvn owned disposal system and or third party pipeline take away.

**Waste type:** FLOWBACK

**Waste content description:** n/a

**Amount of waste:** 1500 barrels

**Waste disposal frequency :** Daily

**Safe containment description:** n/a

**Safe containmant attachment:**

**Waste disposal type:** ON-LEASE INJECTION **Disposal location ownership:** COMMERCIAL



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

**Disposal type description:**

**Disposal location description:** Various disposal locations in Lea and Eddy counties.

**Waste type:** DRILLING

**Waste content description:** Water Based Cuttings

**Amount of waste:** 2012 barrels

**Waste disposal frequency :** Daily

**Safe containment description:** n/a

**Safe containmant attachment:**

**Waste disposal type:** HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

**Disposal type description:**

**Disposal location description:** All cuttings will disposed of at R360, Sundance, or equivalent.

### Reserve Pit

**Reserve Pit being used?** NO

**Temporary disposal of produced water into reserve pit?**

**Reserve pit length (ft.)** **Reserve pit width (ft.)**

**Reserve pit depth (ft.)** **Reserve pit volume (cu. yd.)**

**Is at least 50% of the reserve pit in cut?**

**Reserve pit liner**

**Reserve pit liner specifications and installation description**

### Cuttings Area

**Cuttings Area being used?** NO

**Are you storing cuttings on location?** NO

**Description of cuttings location**

**Cuttings area length (ft.)** **Cuttings area width (ft.)**

**Cuttings area depth (ft.)** **Cuttings area volume (cu. yd.)**

**Is at least 50% of the cuttings area in cut?**

**WCuttings area liner**

**Cuttings area liner specifications and installation description**



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

## Section 8 - Ancillary Facilities

**Are you requesting any Ancillary Facilities?:** NO

**Ancillary Facilities attachment:**

**Comments:**

## Section 9 - Well Site Layout

**Well Site Layout Diagram:**

Todd\_36\_25\_State\_Fed\_Com\_235H\_RIGLAYOUT\_20181010092033.pdf

**Comments:**

## Section 10 - Plans for Surface Reclamation

**Type of disturbance:** New Surface Disturbance

**Multiple Well Pad Name:** TODD 36 WELLPAD

**Multiple Well Pad Number:** 3

**Recontouring attachment:**

**Drainage/Erosion control construction:** All areas disturbed shall be reclaimed as early and as nearly as practicable to their original condition or their final land use and shall be maintained to control dust and minimize erosion to the extent practicable.

**Drainage/Erosion control reclamation:** Topsoils and subsoils shall be replaced to their original relative positions and contoured so as to achieve erosion control, long-term stability and preservation of surface water flow patterns. The disturbed area then shall be reseeded in the first favorable growing season.

**Well pad proposed disturbance (acres):** 3.471

**Road proposed disturbance (acres):** 0.22

**Powerline proposed disturbance (acres):** 0.044

**Pipeline proposed disturbance (acres):** 0.637

**Other proposed disturbance (acres):** 5.165

**Total proposed disturbance:** 9.537

**Well pad interim reclamation (acres):** 2.018

**Road interim reclamation (acres):** 0

**Powerline interim reclamation (acres):** 0

**Pipeline interim reclamation (acres):** 0

**Other interim reclamation (acres):** 0

**Total interim reclamation:** 2.018

**Well pad long term disturbance (acres):** 1.641

**Road long term disturbance (acres):** 0.22

**Powerline long term disturbance (acres):** 0.044

**Pipeline long term disturbance (acres):** 0.637

**Other long term disturbance (acres):** 5.165

**Total long term disturbance:** 7.707

**Disturbance Comments:**

**Reconstruction method:** Operator will use Best Management Practices"BMP" to mechanically recontour to obtain the desired outcome.

**Topsoil redistribution:** Topsoils shall be replaced to their original relative positions and contoured so as to achieve erosion control, long-term stability and preservation of surface water flow patterns.

**Soil treatment:** Topsoils shall be replaced to their original relative positions and contoured so as to achieve erosion control, long-term stability and preservation of surface water flow patterns.

**Existing Vegetation at the well pad:**

**Existing Vegetation at the well pad attachment:**



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

**Existing Vegetation Community at the road:**

**Existing Vegetation Community at the road attachment:**

**Existing Vegetation Community at the pipeline:**

**Existing Vegetation Community at the pipeline attachment:**

**Existing Vegetation Community at other disturbances:**

**Existing Vegetation Community at other disturbances attachment:**

**Non native seed used?**

**Non native seed description:**

**Seedling transplant description:**

**Will seedlings be transplanted for this project?**

**Seedling transplant description attachment:**

**Will seed be harvested for use in site reclamation?**

**Seed harvest description:**

**Seed harvest description attachment:**

### Seed Management

#### Seed Table

**Seed type:**

**Seed source:**

**Seed name:**

**Source name:**

**Source address:**

**Source phone:**

**Seed cultivar:**

**Seed use location:**

**PLS pounds per acre:**

**Proposed seeding season:**

#### Seed Summary

**Total pounds/Acre:**

Seed Type	Pounds/Acre
-----------	-------------

**Seed reclamation attachment:**



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

### Operator Contact/Responsible Official Contact Info

**First Name:** JACOB

**Last Name:** OCHOA

**Phone:** (575)748-9934

**Email:** JACOB.OCHOA@DVN.COM

**Seedbed prep:**

**Seed BMP:**

**Seed method:**

**Existing invasive species?** NO

**Existing invasive species treatment description:**

**Existing invasive species treatment attachment:**

**Weed treatment plan description:** Maintain weeds on an as need basis.

**Weed treatment plan attachment:**

**Monitoring plan description:** Monitor as needed.

**Monitoring plan attachment:**

**Success standards:** n/a

**Pit closure description:** n/a

**Pit closure attachment:**

### Section 11 - Surface Ownership

**Disturbance type:** NEW ACCESS ROAD

**Describe:**

**Surface Owner:** BUREAU OF LAND MANAGEMENT

**Other surface owner description:**

**BIA Local Office:**

**BOR Local Office:**

**COE Local Office:**

**DOD Local Office:**

**NPS Local Office:**

**State Local Office:**

**Military Local Office:**

**USFWS Local Office:**

**Other Local Office:**

**USFS Region:**

**USFS Forest/Grassland:**

**USFS Ranger District:**



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

**Disturbance type:** EXISTING ACCESS ROAD

**Describe:**

**Surface Owner:** BUREAU OF LAND MANAGEMENT

**Other surface owner description:**

**BIA Local Office:**

**BOR Local Office:**

**COE Local Office:**

**DOD Local Office:**

**NPS Local Office:**

**State Local Office:**

**Military Local Office:**

**USFWS Local Office:**

**Other Local Office:**

**USFS Region:**

**USFS Forest/Grassland:**

**USFS Ranger District:**

**Disturbance type:** WELL PAD

**Describe:**

**Surface Owner:** BUREAU OF LAND MANAGEMENT

**Other surface owner description:**

**BIA Local Office:**

**BOR Local Office:**

**COE Local Office:**

**DOD Local Office:**

**NPS Local Office:**

**State Local Office:**

**Military Local Office:**

**USFWS Local Office:**

**Other Local Office:**

**USFS Region:**

**USFS Forest/Grassland:**

**USFS Ranger District:**



**Operator Name:** DEVON ENERGY PRODUCTION COMPANY LP

**Well Name:** TODD 36-25 STATE FED COM

**Well Number:** 235H

**Disturbance type:** PIPELINE

**Describe:**

**Surface Owner:** BUREAU OF LAND MANAGEMENT

**Other surface owner description:**

**BIA Local Office:**

**BOR Local Office:**

**COE Local Office:**

**DOD Local Office:**

**NPS Local Office:**

**State Local Office:**

**Military Local Office:**

**USFWS Local Office:**

**Other Local Office:**

**USFS Region:**

**USFS Forest/Grassland:**

**USFS Ranger District:**

## Section 12 - Other Information

**Right of Way needed?** NO

**Use APD as ROW?**

**ROW Type(s):**

### ROW Applications

**SUPO Additional Information:** flow lines are buried- added 2-25-2019 electric lines added 2-25-2019

**Use a previously conducted onsite?** NO

**Previous Onsite information:**

### Other SUPO Attachment


Pay.gov\_\_Receipt\_20181010094122.pdf

EL8249\_TODD\_36\_WP\_3\_EL\_P\_20190225084651.PDF


7660144F\_TODD\_36\_WP\_3\_TO\_CTB\_2\_FL\_P\_buried\_lines\_20190319130619.pdf



SECTION 36, TOWNSHIP 23 SOUTH, RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO  
AERIAL ACCESS ROUTE MAP

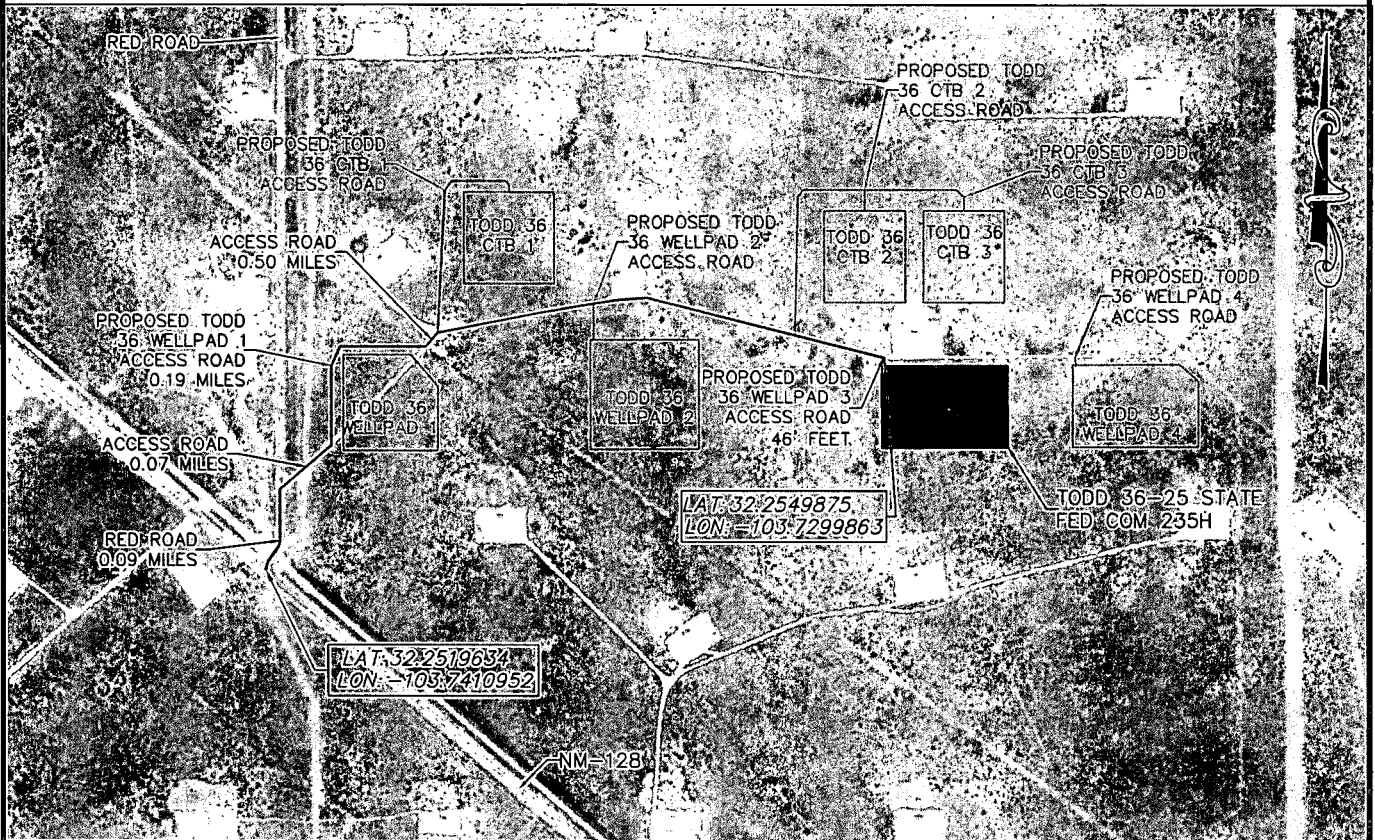

DEVON ENERGY PRODUCTION COMPANY, L.P.  
TODD 36-25 STATE FED COM 235H  
LOCATED 330 FT. FROM THE SOUTH LINE  
AND 1636 FT. FROM THE EAST LINE OF  
SECTION 36, TOWNSHIP 23 SOUTH,  
RANGE 31 EAST, N.M.P.M.  
EDDY COUNTY, STATE OF NEW MEXICO



HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

Drawn by:  
CHRIS MAAS


Date: 09/20/2018

Drawn for:

**devon**



EXHIBIT "A"  
ACCESS ROAD PLAT  
SECTION 36, T23S-R31E, N.M.P.M.  
EDDY COUNTY, NEW MEXICO

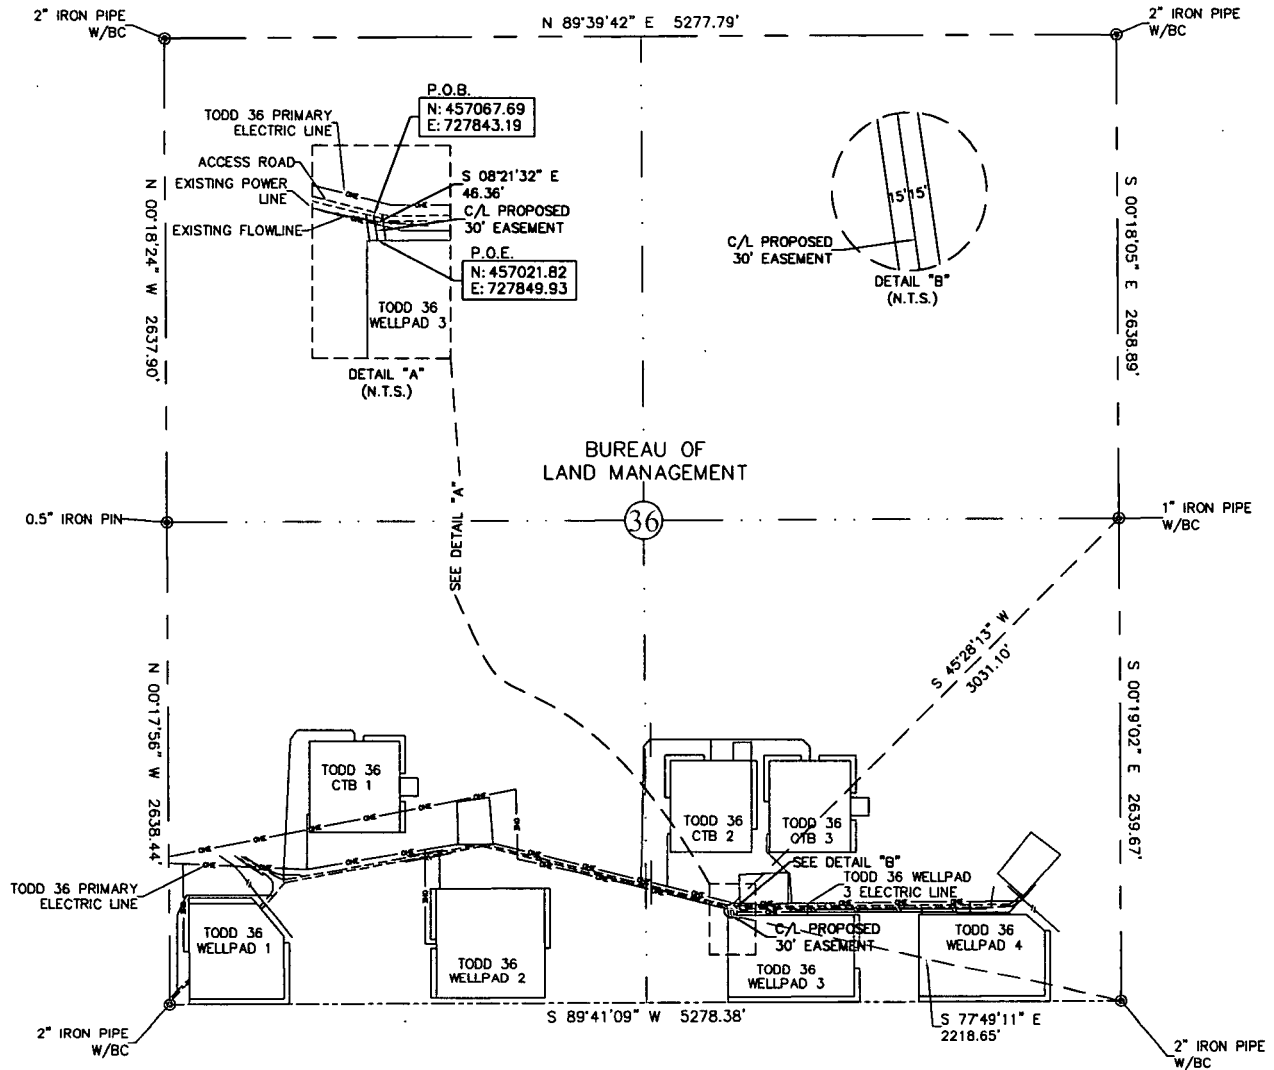

30' EASEMENT AREA = 0.032 ACRE(S)  
46.36 FEET OR 2.81 RODS


0+00.0 P.O.B./EXISTING ACCESS ROAD  
0+03.9 EDGE OF ROAD  
0+11.6 EXISTING FLOW LINE  
0+16.3 POWER LINE  
0+46.3 P.O.E./TODD 36 WELLPAD 3

SEE THE ATTACHED LEGAL DESCRIPTION

Note: All bearings recited herein are based on the New Mexico State Plane Coordinate System, NAD 83, New Mexico East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.

B.L. Laman  
Date Signed: 09-23-2018  
P.O. Box 548, Dry Creek, La.  
(903) 388-3045 70637  
Employee of Horizonrow, LLC



HORIZON ROW LLC

Drawn for:

devon

Drawn by:  
CHRIS MAAS

Date: 07/07/2018

DEVON ENERGY PRODUCTION COMPANY, L.P.

TODD 36  
WELLPAD 3 ACCESS ROAD

PROPOSED 30' EASEMENT  
ON THE PROPERTY OF  
BUREAU OF LAND MANAGEMENT  
SECTION 36, T23S-R31E, N.M.P.M.

LINE NUMBER:

WBS NUMBER:

SCALE:  
1" = 1000'

REVISIONS:

SURVEY DATE:  
6/30/18

0 1000 2000





**SECTION 36, T23S-R31E, N.M.P.M.,  
EDDY COUNTY, NEW MEXICO**

**ACCESS ROAD PLAT**

**LEGAL DESCRIPTION**

**FOR**

**DEVON ENERGY PRODUCTION COMPANY, L.P.**

**BUREAU OF LAND MANAGEMENT**

**30' EASEMENT DESCRIPTION:**

**BEING** an easement thirty (30) feet in width lying fifteen (15) feet on the right side and fifteen (15) feet on the left side of the survey centerline described below, being out of the southeast quarter (SE ¼) of Section 36, Township 23 South, Range 31 East, N.M.P.M., Eddy County, New Mexico, and being out of a parcel of land owned by the Bureau of Land Management. Said centerline of easement being more particularly described as follows:

Commencing from a 1" iron pipe w/BC for the east quarter corner of Section 36, T23S-R31E, N.M.P.M., Eddy County, New Mexico;


Thence S 45°28'13" W a distance of 3031.10' to the **Point of Beginning** of this easement having coordinates of Northing=457067.69, Easting=727843.19 feet and continuing the following course;

Thence S 08°21'32" E a distance of 46.36' to the **Point of Ending** having coordinates of Northing=457021.82, Easting=727849.93 feet from said point a 2" iron pipe w/BC for the southeast corner of Section 36, T23S-R31E bears S 77°49'11" E a distance of 2218.65', covering **46.36' or 2.81 rods** and having an area of **0.032 acres**.

**NOTES:**

Bearings, distances and coordinates shown herein are based on New Mexico State Plane Coordinate System, NAD 83, East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.



B.L. Laman PLS 22404

Date Signed: 09/23/2018

Horizon Row, LLC


P.O. Box 548, Dry Creek, La.

(903) 388-3045 70637

Employee of Horizon Row, LLC





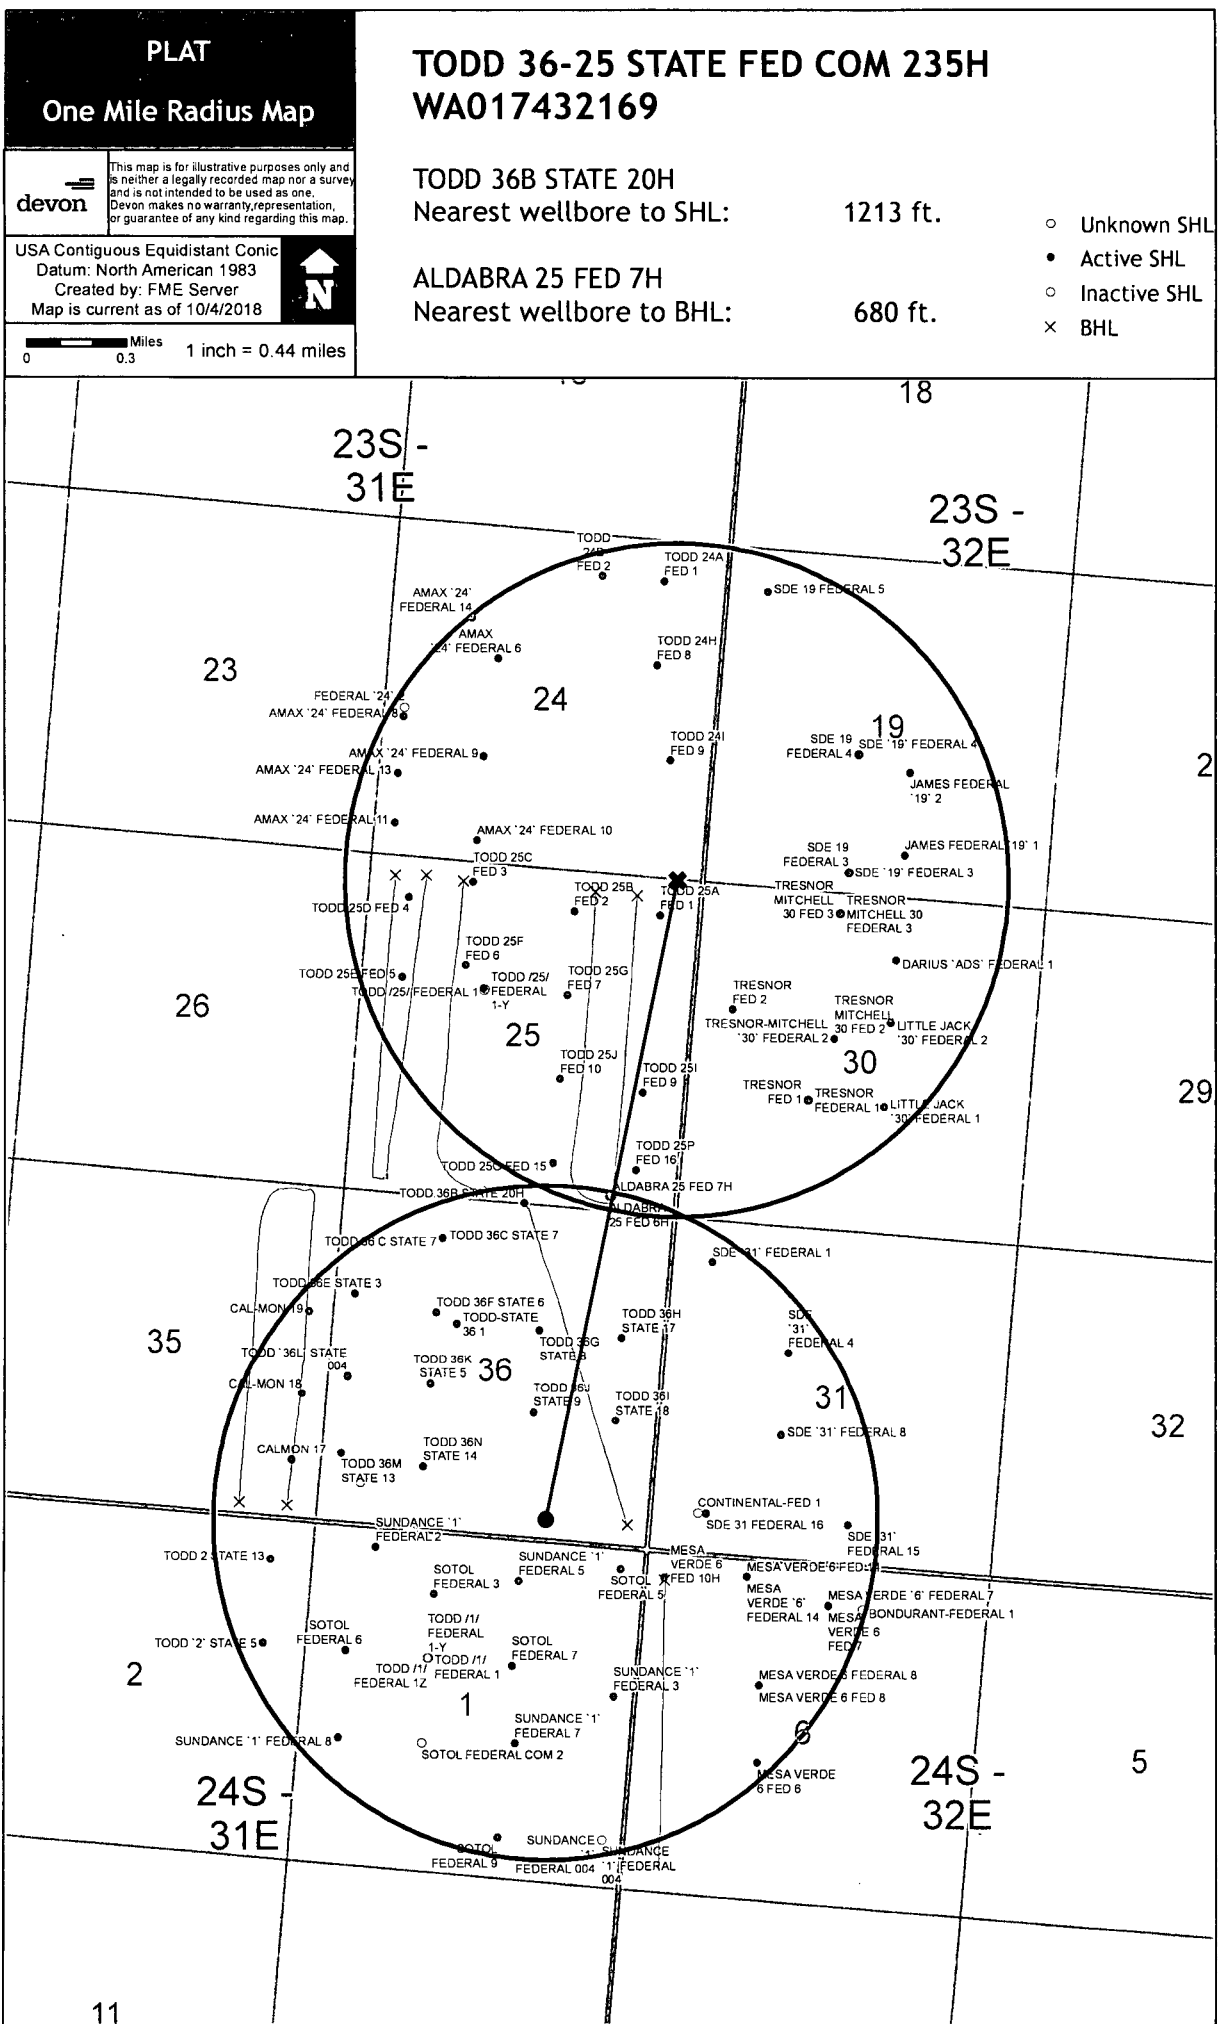



TODD 36-25 STATE FED COM

233H/234H/235H

devon

This map is for illustrative purposes only and is neither a legally recorded map nor survey and is not intended to be used as one. Devon makes no warranty, representation, or guarantee of any kind regarding this map.

WGS\_1984\_Web\_Mercator\_Auxiliary\_Sphere  
Prepared by: \_User  
Map is current as of: 08-Oct-2018



Miles  
0 0.25 0.50 1.12 1:56,913

TODD 2 TW POND

DEVON 30 DAY INSTALL DAYS PRIOR TO COMPLETION  
DEVON WILL CONTACT BLM IF ADDITIONAL TIME IS NEEDED  
DISTURBANCE: EXISTING  
CONTENTS: FRESH WATER  
TYPE OF PIPE: LAY FLAT  
SIZE OF PIPE: 12"  
LENGTH OF PIPE: 32,543' FOR TW WATER

TODD 36-25 STATE FED COM  
233H/234H/235H




TODD 36 WELLPAD 3  
CALICHE MAP

CALICHE PIT


TOTAL DISTANCE=2.55 MILES

TODD 36 WELLPAD 3

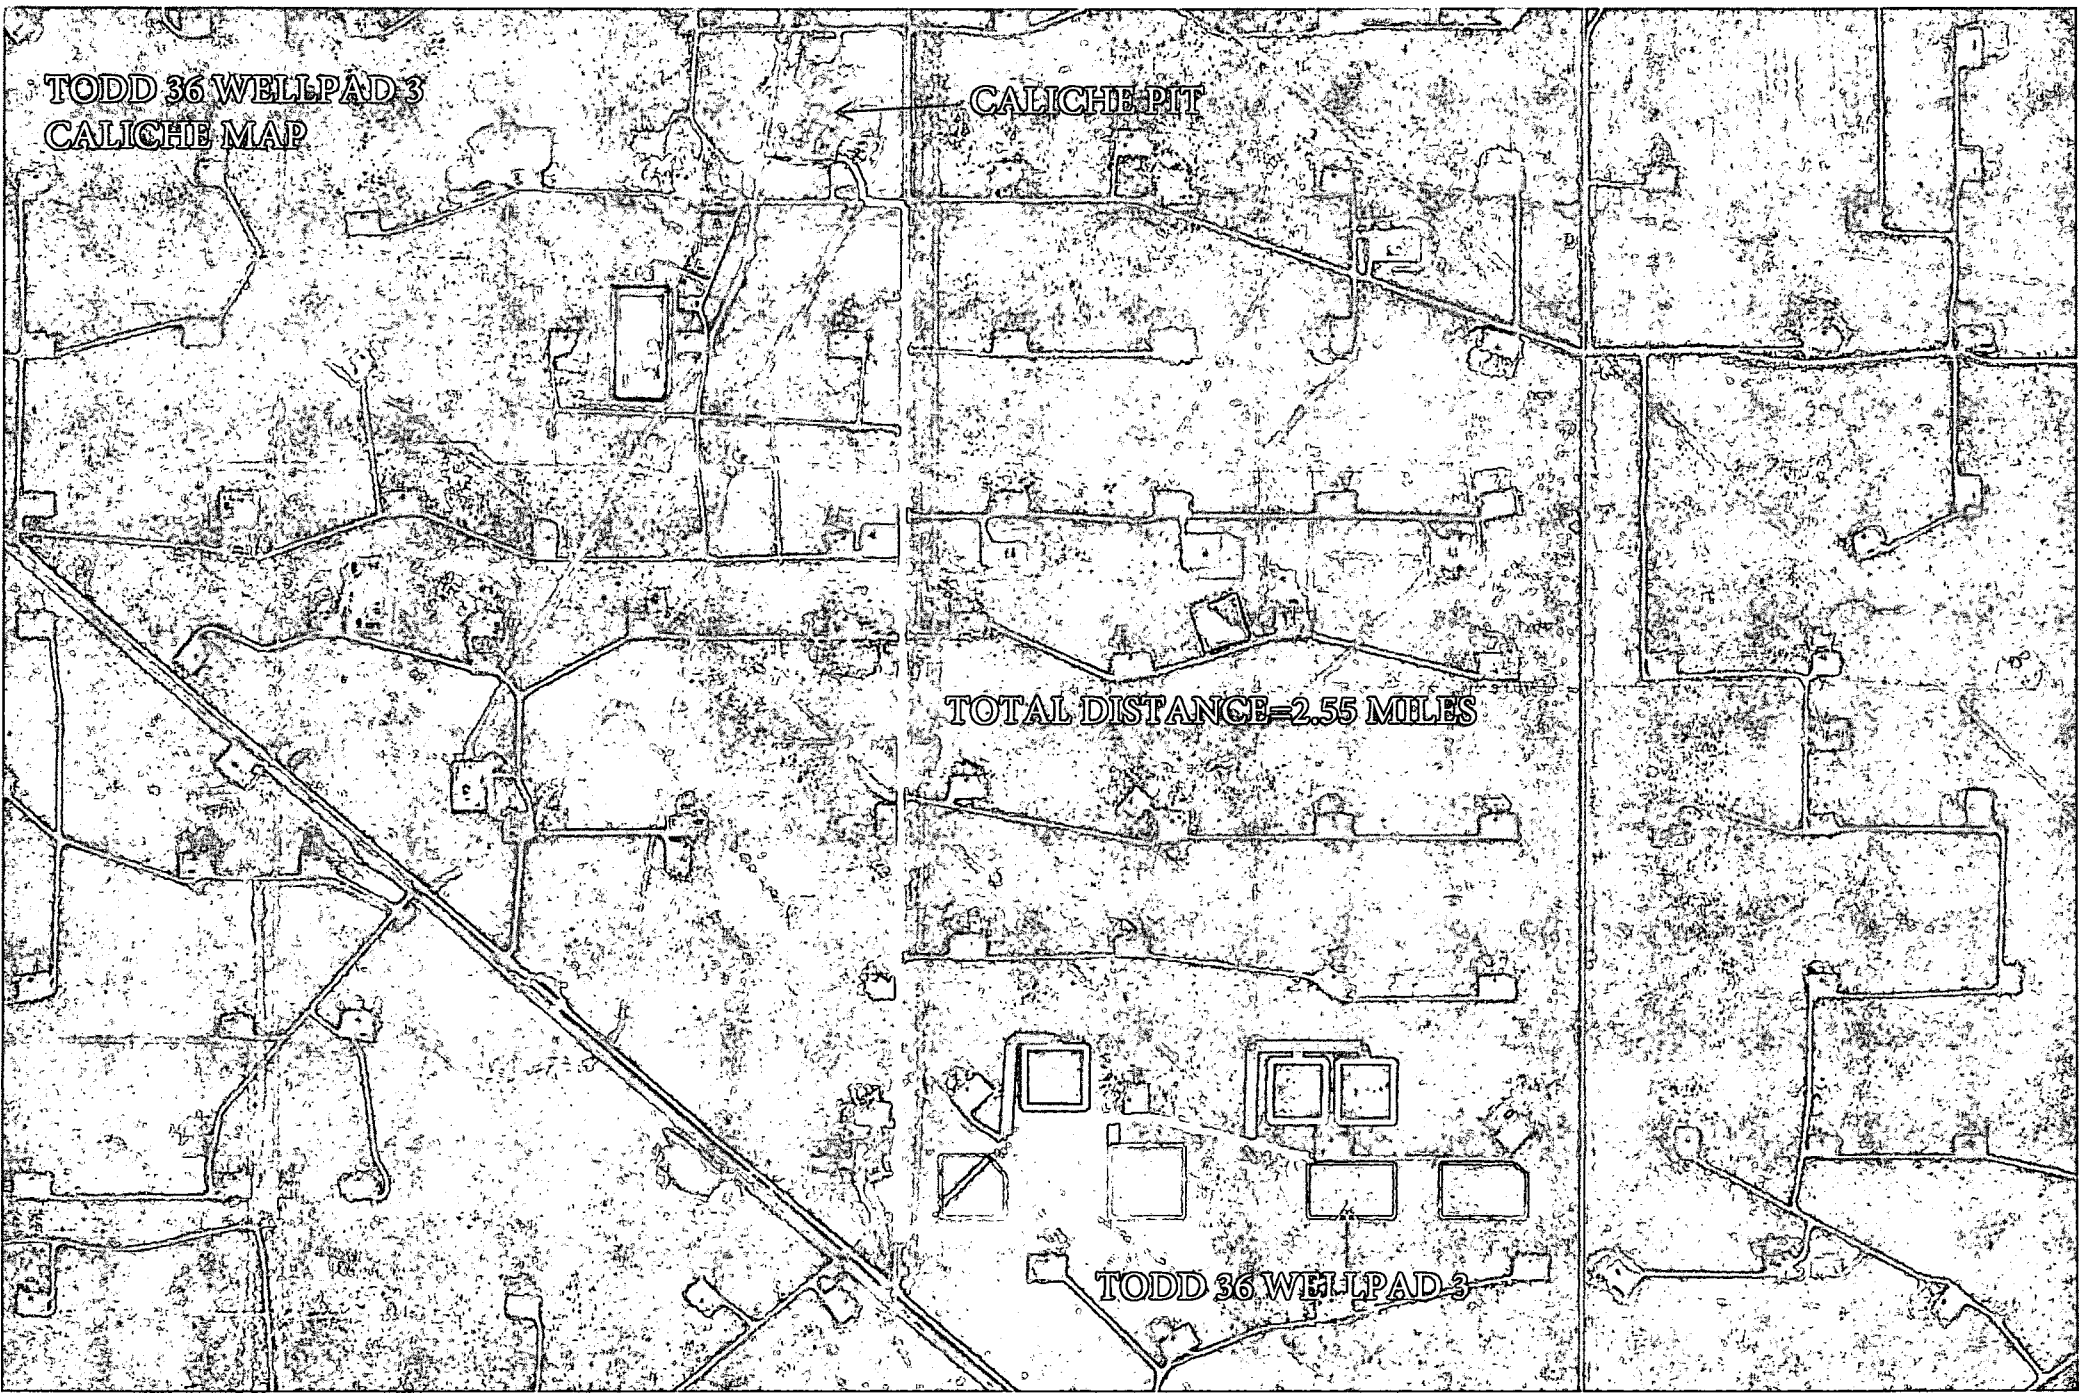



# Devon Energy - Well Pad Rig Location Layout Safety Equipment Location

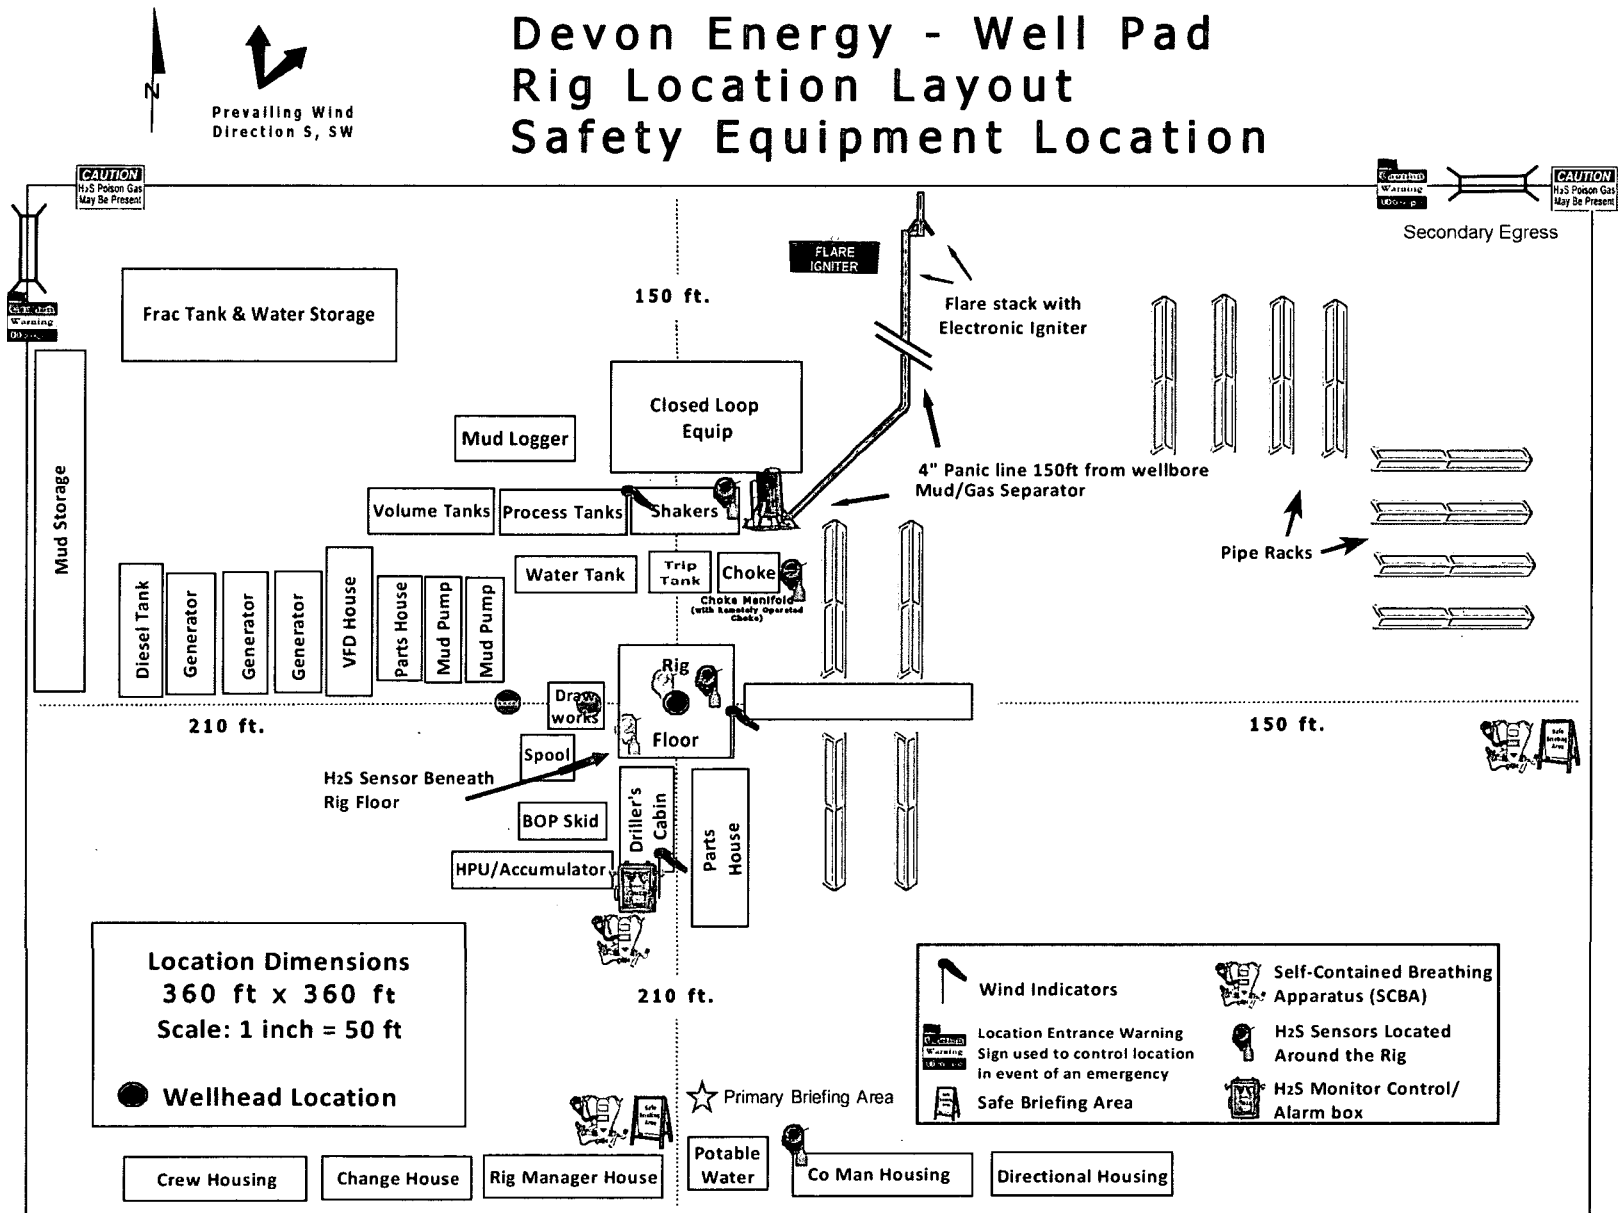





## Receipt

### Your payment is submitted

Pay.gov Tracking ID: 26CPORR8

Agency Tracking ID: 75591612551

Form Name: Bureau of Land Management (BLM) Application for Permit to Drill (APD) Fee

Application Name: BLM Oil and Gas Online Payment

### Payment Information

Payment Type: Bank account (ACH)

Payment Amount: \$30,150.00

Transaction Date: 10/10/2018 11:31:45 AM EDT

Payment Date: 10/11/2018

Company: DEVON ENERGY PRODUCTION CO., L.P.

APD IDs: 10400034900, 10400035010, 10400035068

Lease Numbers: NMNM0544986, NMNM0544986, NMNM0544986

Well Numbers: 233H, 234H, 235H

Note: You will need your Pay.gov Tracking ID to complete your APD transaction in AFMSS II. Please ensure you write this number down upon completion of payment.

### Account Information

Account Holder Name: Devon Energy Production Company, L.P.

Routing Number: 061000052

Account Number: \*\*\*\*\*9892

### Email Confirmation Receipt

Confirmation Receipts have been emailed to:


JENNY.HARMS@DVN.COM

jeff.walla@dvn.com

lisa.othon@dvn.com



EXHIBIT "A"  
PAGE 1 of 4  
ELECTRIC LINE PLAT  
SECTION 36, T23S-R31E, N.M.P.M.  
EDDY COUNTY, NEW MEXICO

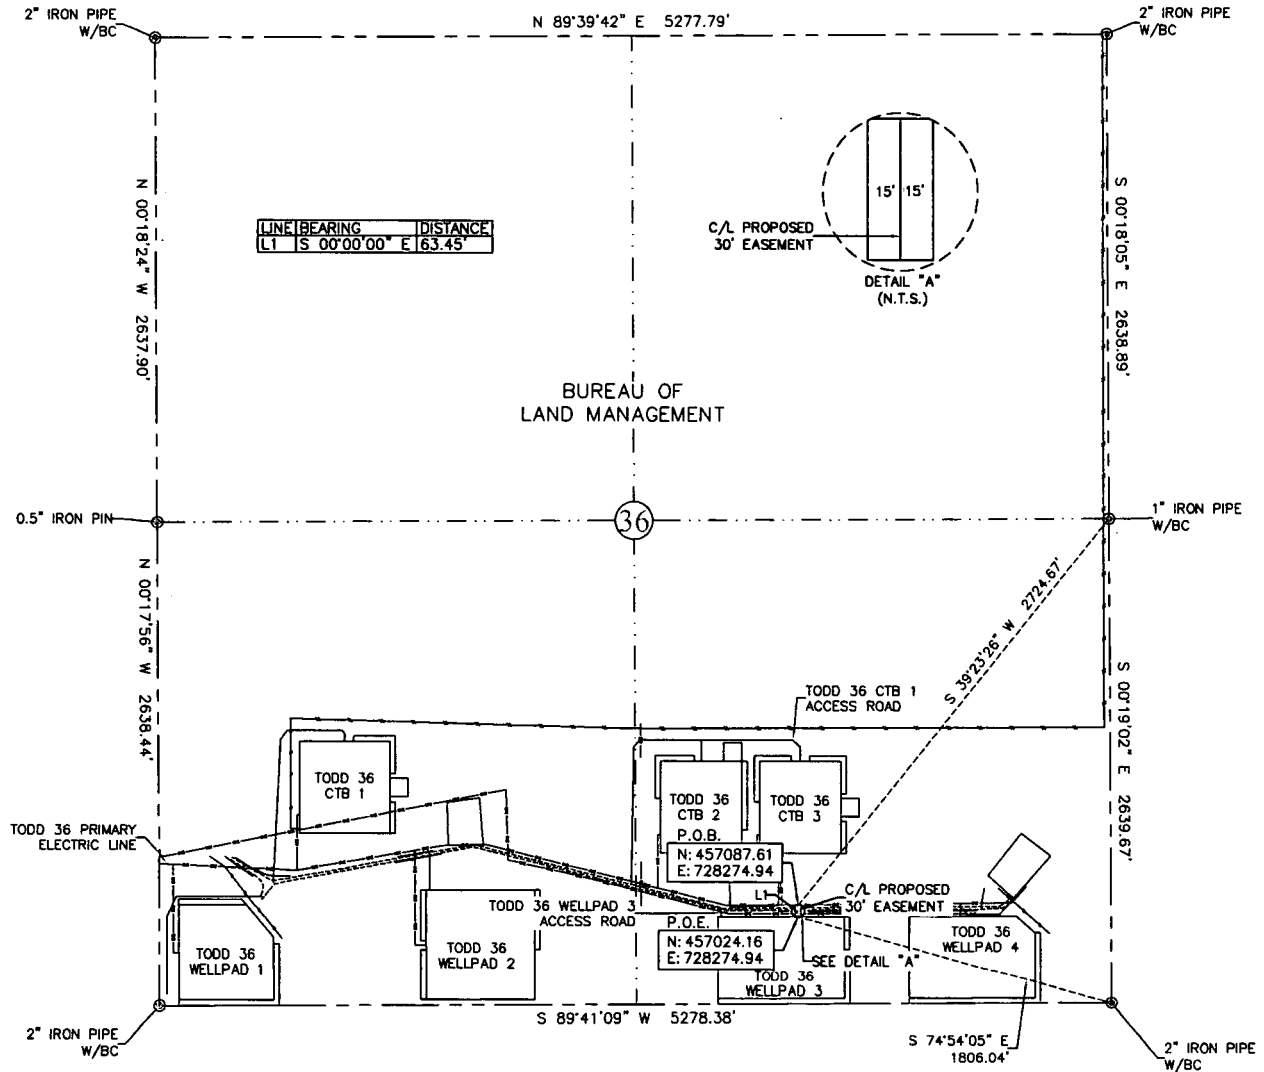

30' EASEMENT AREA = 0.044 ACRE(S)  
63.45 FEET OR 3.85 RODS

SEE THE ATTACHED LEGAL DESCRIPTION

Note: All bearings recited herein are based on the New Mexico State Plane Coordinate System, NAD 83, New Mexico East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect the actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.

**STATION TABLE**

0+00.0 P.O.B./TODD 36 PRIMARY ELECTRIC LINE  
0+14.2 EDGE OF LEASE ROAD  
0+21.1 CENTERLINE LEASE ROAD  
0+27.4 EDGE OF LEASE ROAD  
0+36.0 EXISTING FLOWLINE  
0+49.6 EXISTING POWER LINE  
0+63.5 P.O.E./TODD 36 WELLPAD 3

0 1000 2000



**HORIZON ROW LLC**

Drawn for:

**devon**

Drawn by:  
Jesus Rivera

Date: 07/03/2018

DEVON ENERGY PRODUCTION COMPANY, L.P.

TODD 36 WELLPAD 3  
ELECTRIC LINE

PROPOSED 30' EASEMENT  
ON THE PROPERTY OF  
BUREAU OF LAND MANAGEMENT  
SECTION 36, T23S-R31E, N.M.P.M.

LINE NUMBER:  
EL8249


WBS NUMBER:  
XX-129865.01.SLC

SCALE:  
1" = 1000'

REVISIONS:

SHEET:  
1 OF 4

B.L. Laman PLS #22404  
Date Signed: 09-07-2018  
P.O. Box 548, Dry Creek, La.  
(903) 388-3045 70637  
Employee of Horizonrow, LLC





**SECTION 36, T23S-R31E, N.M.P.M.,  
EDDY COUNTY, NEW MEXICO**

**ELECTRIC LINE PLAT**

**LEGAL DESCRIPTION**

**FOR**

**DEVON ENERGY PRODUCTION COMPANY, L.P.**

**BUREAU OF LAND MANAGEMENT**

**30' EASEMENT DESCRIPTION:**

**BEING** an easement thirty (30) feet in width lying fifteen (15) feet on the right side and fifteen (15) feet on the left side of the survey centerline described below, being out of the southeast quarter (SE ¼) of Section 36, Township 23 South, Range 31 East, N.M.P.M., Eddy County, New Mexico, and being out of a parcel of land owned by the Bureau of Land Management. Said centerline of easement being more particularly described as follows:

Commencing from a 1" iron pipe w/BC for the east quarter corner of Section 36, T23S-R31E, N.M.P.M., Eddy County, New Mexico;

Thence S 39°23'26" W a distance of 2724.67' to the **Point of Beginning** of this easement having coordinates of Northing=457087.61, Easting=728274.94 feet and continuing the following courses;

Thence S 00°00'00" E a distance of 63.45' to the **Point of Ending** having coordinates of Northing=457024.16, Easting=728274.94 feet from said point a 2" iron pipe w/BC for the southeast corner of Section 36, T23S-R31E bears S 74°54'05" E a distance of 1806.04', covering **63.45' or 3.85 rods** and having an area of **0.044 acres**.

**NOTES:**

Bearings, distances and coordinates shown herein are based on New Mexico State Plane Coordinate System, NAD 83, East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.


  
B.L. Laman      PLS 22404  
Date Signed: 09/07/2018  
Horizon Row, LLC  
P.O. Box 548, Dry Creek, La.  
(903) 388-3045 70637  
Employee of Horizon Row, LLC





EXHIBIT "A"  
PAGE 3 of 4

OXY USA INC.

BUREAU OF LAND MANAGEMENT

SECTION 35 T23S-R31E

RED ROAD

TODD 36 CTB 1

TODD 36 CTB 2

TODD 36 CTB 3

TODD 36 CTB 2 ACCESS ROAD

TODD 36 CTB 3 ACCESS ROAD

TODD 36 WELLPAD 1

TODD 36 WELLPAD 2

TODD 36 WELLPAD 3

TODD 36 WELLPAD 4

TODD 36 WELLPAD 1 ELECTRIC LINE

TODD 36 WELLPAD 2 ELECTRIC LINE

TODD 36 WELLPAD 3 ELECTRIC LINE

TODD 36 WELLPAD 4 ELECTRIC LINE

TODD 36 CTB 2 ACCESS ROAD

TODD 36 CTB 3 ACCESS ROAD

TODD 36 WELLPAD 4 ACCESS ROAD

TODD 36 WELLPAD 3 ACCESS ROAD

Gravel Pit

NM-128

SECTION 2 T24S-R31E

SECTION 1 T24S-R31E

BUREAU OF LAND MANAGEMENT

BUREAU OF LAND MANAGEMENT

Eddy Co

Lea Co

OXY CO

LEA CO

QUAD MAP


SECTION 36, T23S-R31E, N.M.P.M.;  
EDDY COUNTY, NEW MEXICO

SHEET:  
3 OF 4



# EXHIBIT "A"

## PAGE 4 of 4

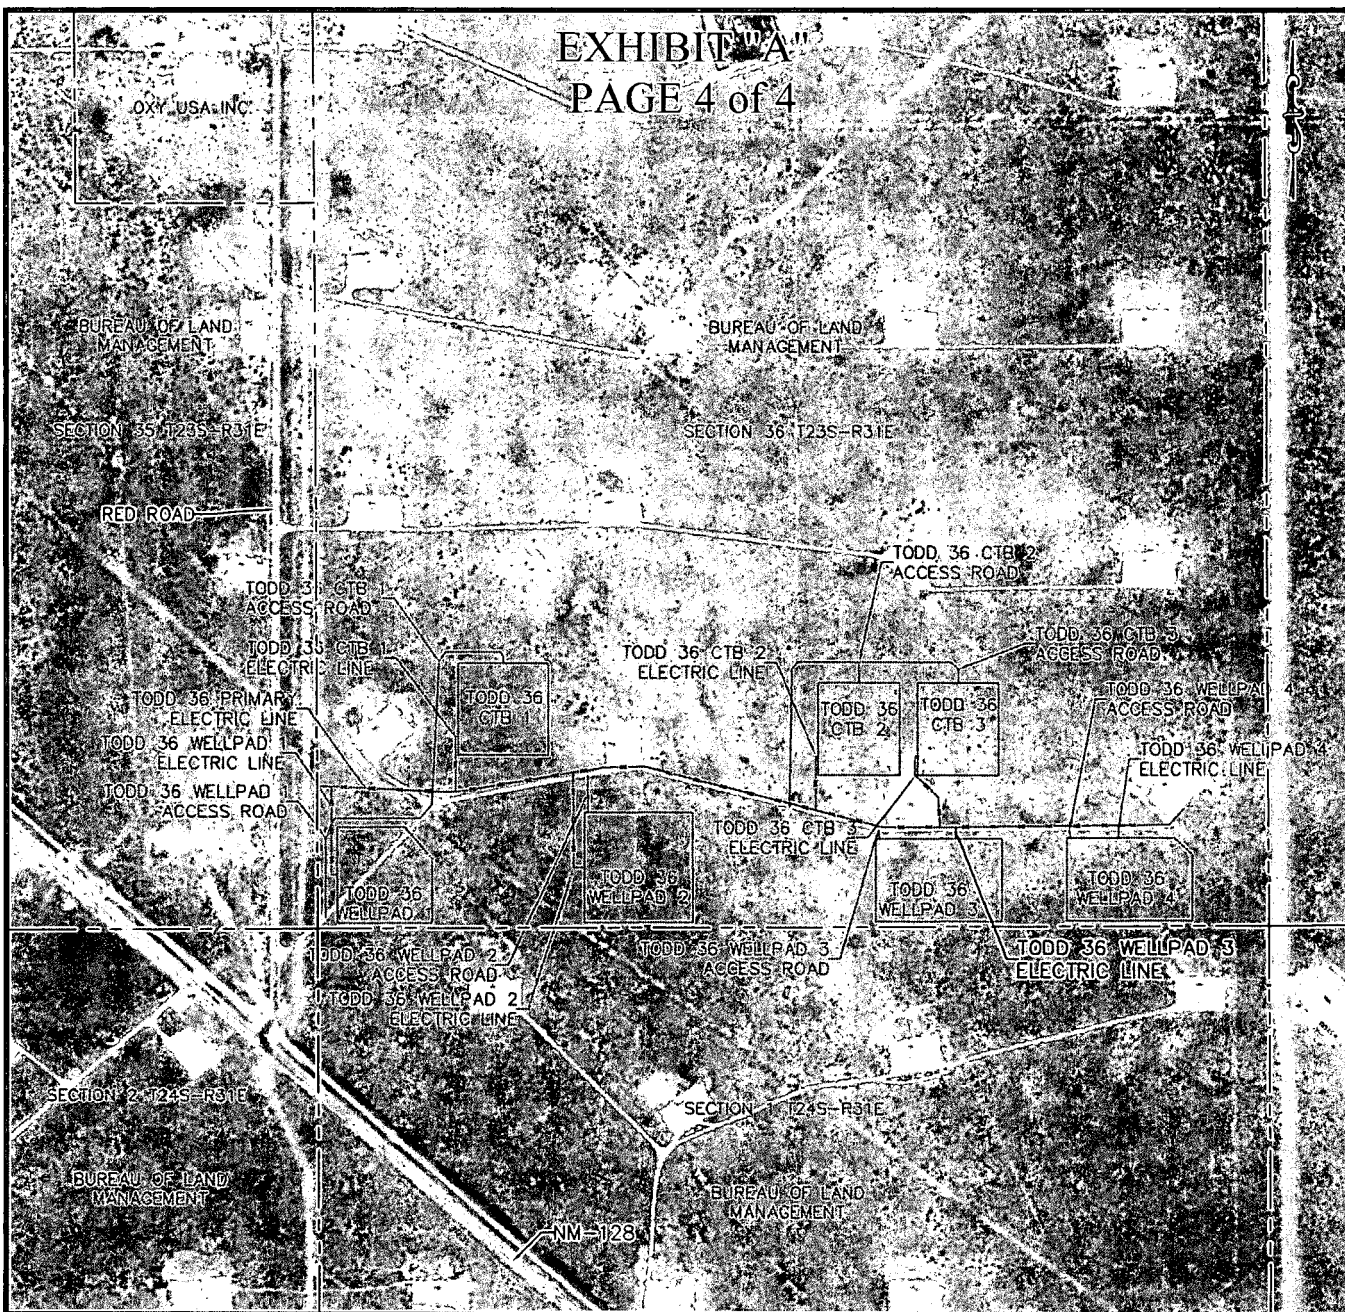

### AERIAL MAP

SECTION 36, T23S-R31E, N.M.P.M.;  
EDDY COUNTY, NEW MEXICO

**HORIZON ROW LLC**

DEVON ENERGY PRODUCTION CO., L.P.

PROPOSED 30' EASEMENT

Drawn by:  
Jesus Rivero

Date: 07/03/2018

Drawn for:



LINE NUMBER:  
EL8249

WBS NUMBER:  
XX-129865.01.SLC


SCALE:  
1" = 1000'

REVISIONS:

SHEET:  
4 OF 4



EXHIBIT "A"  
PAGE 1 of 4  
8" COMPOSITE PIPE  
SECTION 36, T23S-R31E, N.M.P.M.  
EDDY COUNTY, NEW MEXICO  
Flowlines are buried

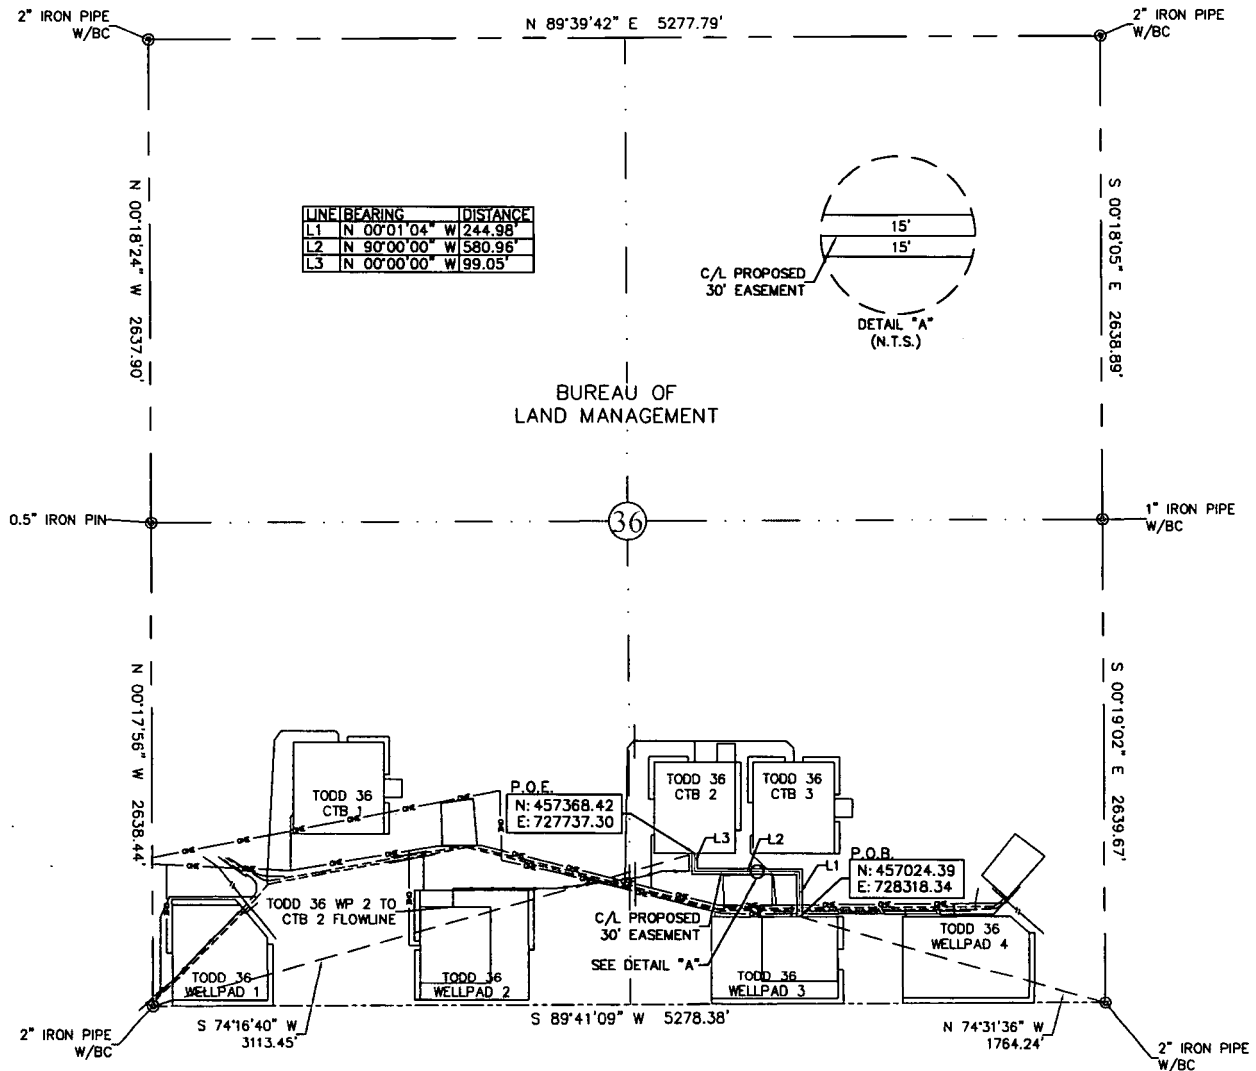

30' EASEMENT AREA = 0.637 ACRE(S)  
924.99 FEET OR 56.06 RODS

SEE THE ATTACHED LEGAL DESCRIPTION

Note: All bearings recited herein are based on the New Mexico State Plane Coordinate System, NAD 83, New Mexico East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.

0+00.0 P.O.B./TODD 36 WELLPAD 3  
0+14.5 POWER LINE  
0+30.4 FLOWLINE  
0+36.3 EDGE OF ROAD  
0+42.6 C/L ROAD  
0+49.5 EDGE OF ROAD  
4+09.4 TODD 36 CTB 3 ELECTRIC LINE  
9+25.0 P.O.E./TODD 36 CTB 2

0 1000 2000



HORIZON ROW LLC

Drawn for:

devon

Drawn by:  
CHRIS MAAS

Date: 09/27/2018

DEVON ENERGY PRODUCTION COMPANY, L.P.

TODD 36 WELLPAD 3 TO  
CTB 2 FLOWLINE

PROPOSED 30' EASEMENT  
ON THE PROPERTY OF  
BUREAU OF LAND MANAGEMENT  
SECTION 36, T23S-R31E, N.M.P.M.

LINE NUMBER:  
7660144F


WBS NUMBER:  
XX-129865.01.SLC

SCALE:  
1" = 1000'

REVISIONS:

DATE OF SURVEY:  
9/26/18

B.L. Laman PLS #22404  
Date Signed: 09-27-2018  
P.O. Box 548, Dry Creek, La.  
(903) 388-3045 70637  
Employee of Horizonrow, LLC





**SECTION 36, T23S-R31E, N.M.P.M.,  
EDDY COUNTY, NEW MEXICO**

**LEGAL DESCRIPTION**

**FOR**

**DEVON ENERGY PRODUCTION COMPANY, L.P.**

**BUREAU OF LAND MANAGEMENT**

**30' EASEMENT DESCRIPTION:**

**BEING** an easement thirty (30) feet in width lying fifteen (15) feet on the right side and fifteen (15) feet on the left side of the survey centerline described below, being out of the southeast quarter (SE ¼) of Section 36, Township 23 South, Range 31 East, N.M.P.M., Eddy County, New Mexico, and being out of a parcel of land owned by the Bureau of Land Management. Said centerline of easement being more particularly described as follows:

Commencing from a 2" iron pipe w/BC for the southeast corner of Section 36, T23S-R31E, N.M.P.M., Eddy County, New Mexico;

Thence N 74°31'36" W a distance of 1764.24' to the **Point of Beginning** of this easement having coordinates of Northing=457024.39, Easting=728318.34 feet and continuing the following courses;

Thence N 00°01'04" W a distance of 244.98' to an angle point;


Thence N 90°00'00" W a distance of 580.96' to an angle point;

Thence N 00°00'00" W a distance of 99.05' to the **Point of Ending** having coordinates of Northing=457368.42, Easting=727737.30 feet from said point a 2" iron pipe w/BC for the southwest corner of Section 36, T23S-R31E bears S 74°16'40" W a distance of 3113.45', covering **924.99' or 56.06 rods** and having an area of **0.637 acres**.

**NOTES:**

Bearings, distances and coordinates shown herein are based on New Mexico State Plane Coordinate System, NAD 83, East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.



B.L. Laman PLS 22404

Date Signed: 09/27/2018

Horizon Row, LLC


P.O. Box 548, Dry Creek, La.

(903) 388-3045 70637

Employee of Horizon Row, LLC





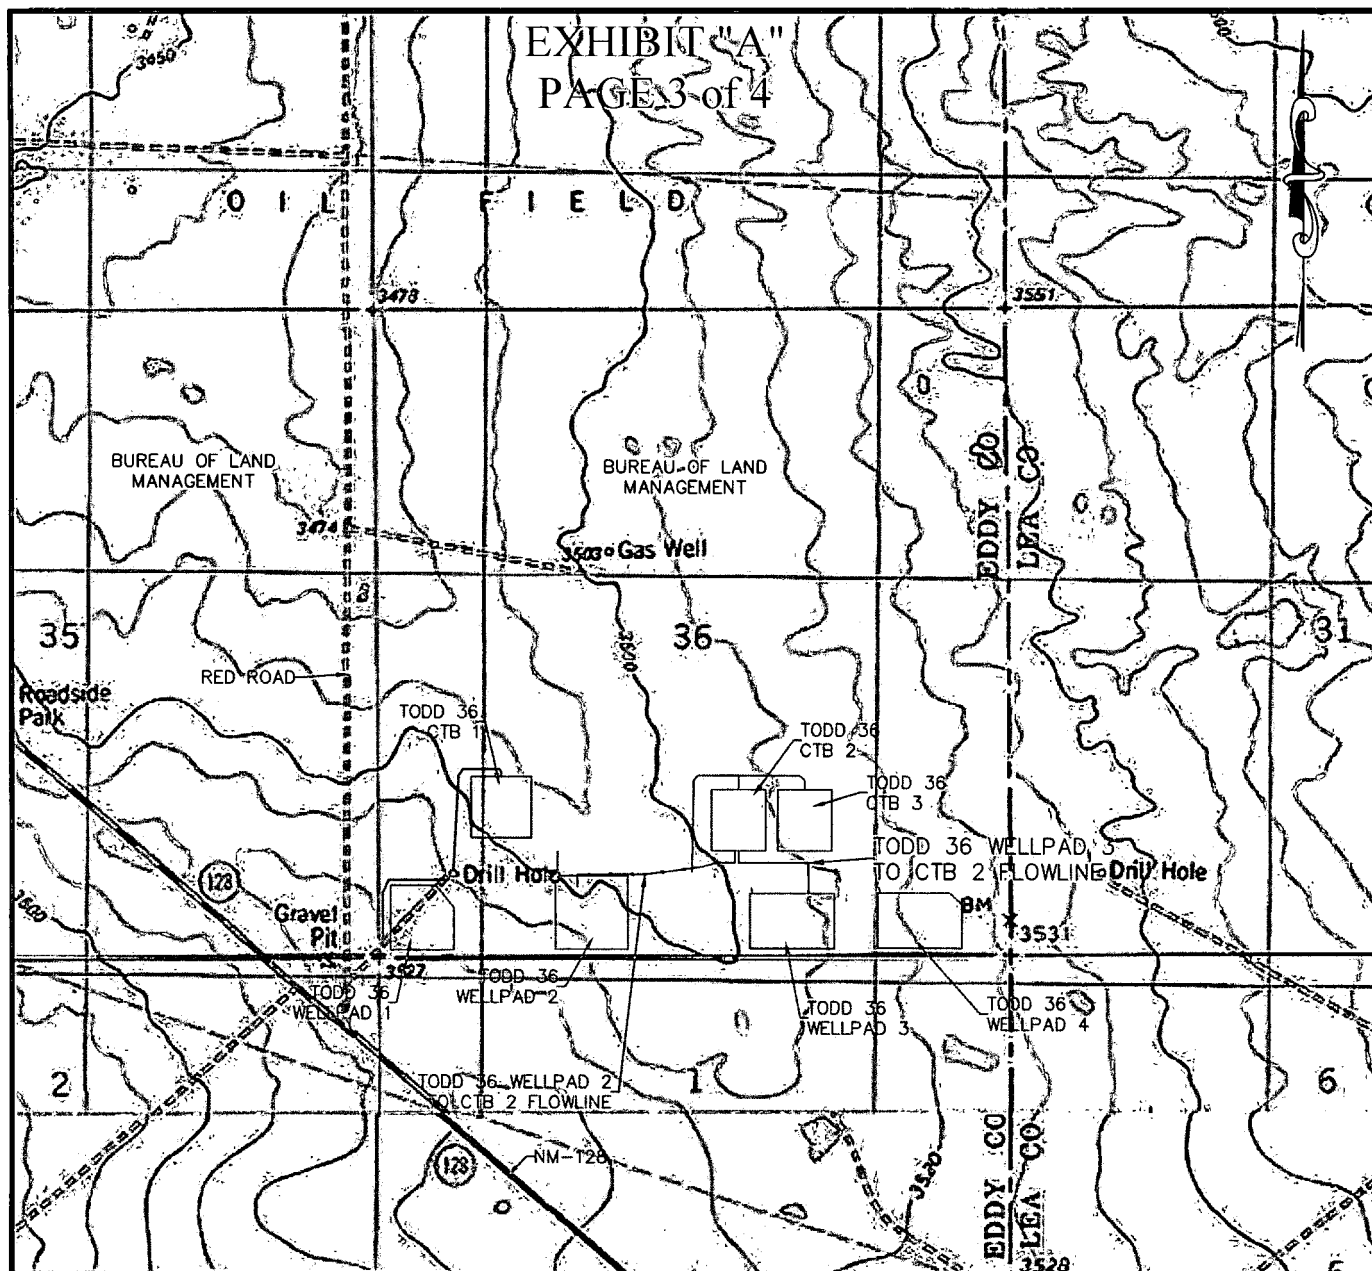

QUAD MAP

SECTION 36, T23S-R31E, N.M.P.M.;  
EDDY COUNTY, NEW MEXICO  
Flowlines are buried

**HORIZON ROW LLC**

DEVON ENERGY PRODUCTION CO., L.P.  
PROPOSED 30' EASEMENT

Drawn by:  
CHRIS MAAS

Date: 09/27/2018

Drawn for:



LINE NUMBER:  
7660144F

WBS NUMBER:  
XX-129865.01.SLC


SCALE:  
1" = 1500'

REVISIONS:

DATE OF SURVEY:  
9/27/18



EXHIBIT "A"  
PAGE 4 of 4

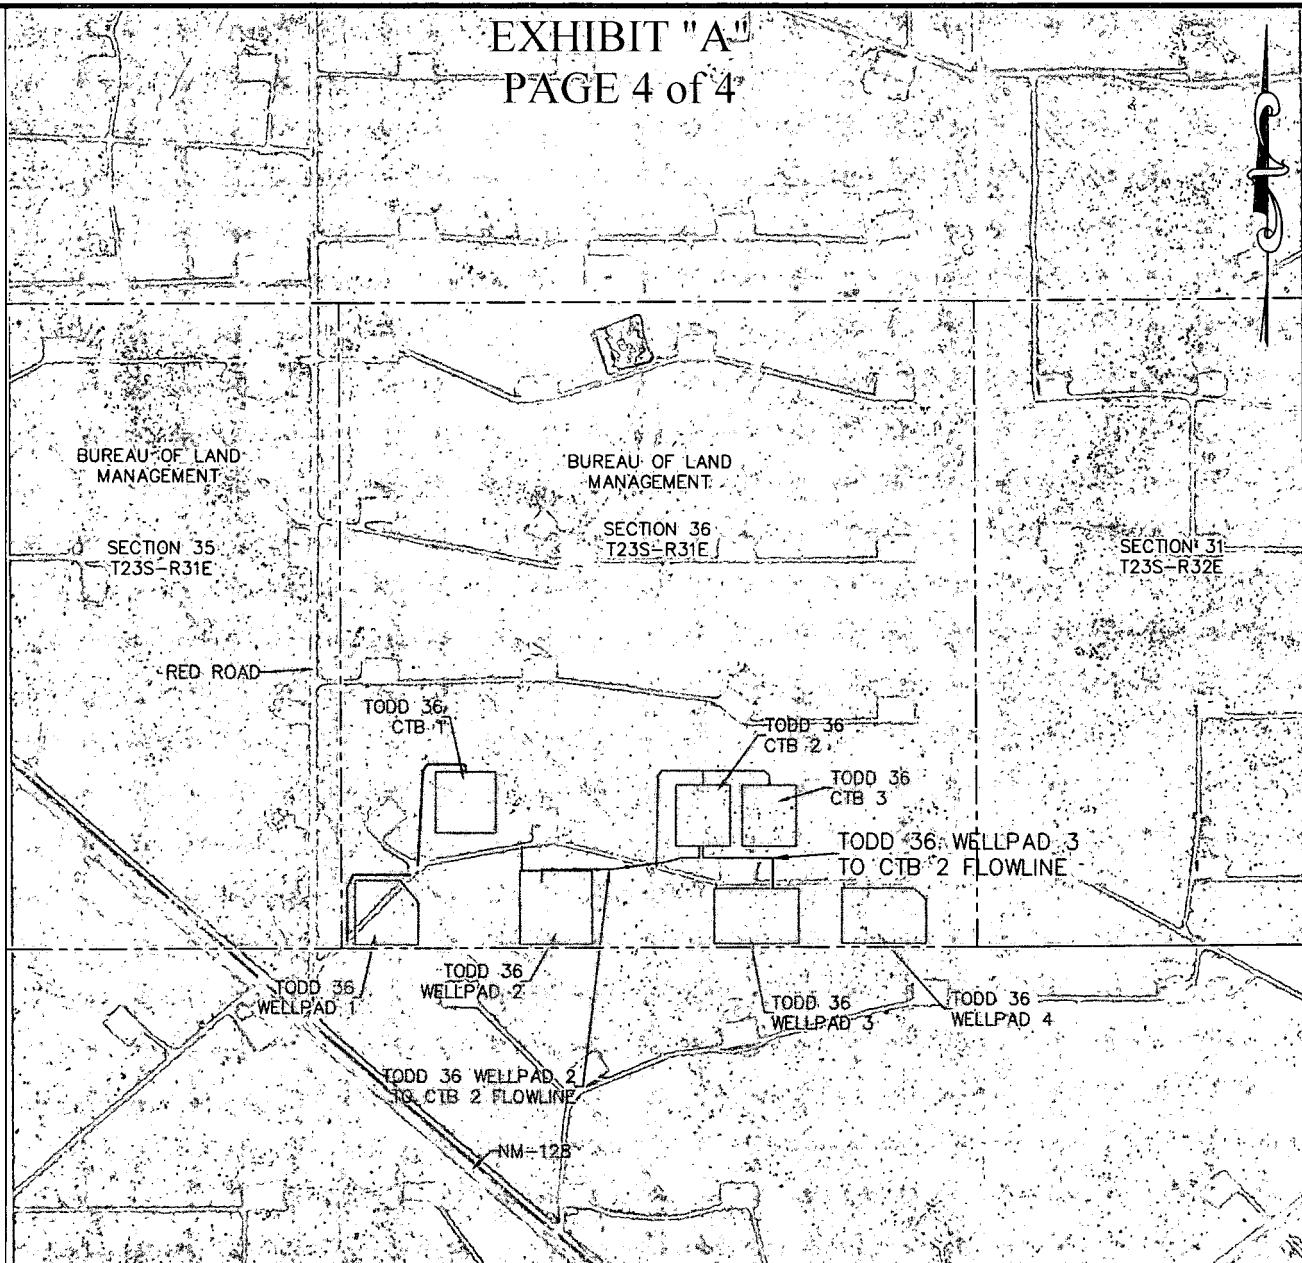

AERIAL MAP

SECTION 36, T23S-R31E, N.M.P.M.;  
EDDY COUNTY, NEW MEXICO  
Flowlines are buried

**HORIZON ROW LLC**

DEVON ENERGY PRODUCTION CO., L.P.  
PROPOSED 30' EASEMENT

Drawn by:  
CHRIS MAAS

Date: 09/27/2018

Drawn for:



**devon**

LINE NUMBER:  
7660144F

WBS NUMBER:  
XX-129865.01.SLC

SCALE:  
1" = 1500'

REVISIONS:

DATE OF SURVEY:  
9/27/18





U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## PWD Data Report

04/18/2019

### Section 1 - General

Would you like to address long-term produced water disposal? NO

### Section 2 - Lined Pits

Would you like to utilize Lined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Lined pit PWD on or off channel:

Lined pit PWD discharge volume (bbl/day):

Lined pit specifications:

Pit liner description:

Pit liner manufacturers information:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Lined pit precipitated solids disposal schedule:

Lined pit precipitated solids disposal schedule attachment:

Lined pit reclamation description:

Lined pit reclamation attachment:

Leak detection system description:

Leak detection system attachment:

Lined pit Monitor description:

Lined pit Monitor attachment:

Lined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Lined pit bond number:

Lined pit bond amount:

Additional bond information attachment:



### **Section 3 - Unlined Pits**

Would you like to utilize Unlined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Unlined pit PWD on or off channel:

Unlined pit PWD discharge volume (bbl/day):

Unlined pit specifications:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Unlined pit precipitated solids disposal schedule:

Unlined pit precipitated solids disposal schedule attachment:

Unlined pit reclamation description:

Unlined pit reclamation attachment:

Unlined pit Monitor description:

Unlined pit Monitor attachment:

Do you propose to put the produced water to beneficial use?

Beneficial use user confirmation:

Estimated depth of the shallowest aquifer (feet):

Does the produced water have an annual average Total Dissolved Solids (TDS) concentration equal to or less than that of the existing water to be protected?

TDS lab results:

Geologic and hydrologic evidence:

State authorization:

Unlined Produced Water Pit Estimated percolation:

Unlined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Unlined pit bond number:

Unlined pit bond amount:

Additional bond information attachment:

### **Section 4 - Injection**

Would you like to utilize Injection PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Injection PWD discharge volume (bbl/day):

Injection well mineral owner:



**Injection well type:**

**Injection well number:**

**Injection well name:**

**Assigned injection well API number?**

**Injection well API number:**

**Injection well new surface disturbance (acres):**

**Minerals protection information:**

**Mineral protection attachment:**

**Underground Injection Control (UIC) Permit?**

**UIC Permit attachment:**

### **Section 5 - Surface Discharge**

**Would you like to utilize Surface Discharge PWD options? NO**

**Produced Water Disposal (PWD) Location:**

**PWD surface owner:**

**PWD disturbance (acres):**

**Surface discharge PWD discharge volume (bbl/day):**

**Surface Discharge NPDES Permit?**

**Surface Discharge NPDES Permit attachment:**

**Surface Discharge site facilities information:**

**Surface discharge site facilities map:**

### **Section 6 - Other**

**Would you like to utilize Other PWD options? NO**

**Produced Water Disposal (PWD) Location:**

**PWD surface owner:**

**PWD disturbance (acres):**

**Other PWD discharge volume (bbl/day):**

**Other PWD type description:**

**Other PWD type attachment:**

**Have other regulatory requirements been met?**

**Other regulatory requirements attachment:**





U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## Bond Info Data Report

04/18/2019

### Bond Information

Federal/Indian APD: FED

BLM Bond number: CO1104

BIA Bond number:

Do you have a reclamation bond? NO

Is the reclamation bond a rider under the BLM bond?

Is the reclamation bond BLM or Forest Service?

BLM reclamation bond number:

Forest Service reclamation bond number:

Forest Service reclamation bond attachment:

Reclamation bond number:

Reclamation bond amount:

Reclamation bond rider amount:

Additional reclamation bond information attachment:
