


ENRON OIL & GAS
N. 3HUGART (BONE SPRINGS)
TD: 11,785' PSTD: 11,500'
GL: 9,642' KB: 8,656

7-2-80
CANADIAN KENWOOD No. 1
1980' FWL & 660' FSL
SECTION 17, T-18-S, R-31-E
EDDY COUNTY, NEW MEXICO
SPUD: 11-18-79
COMP: 1-3-80

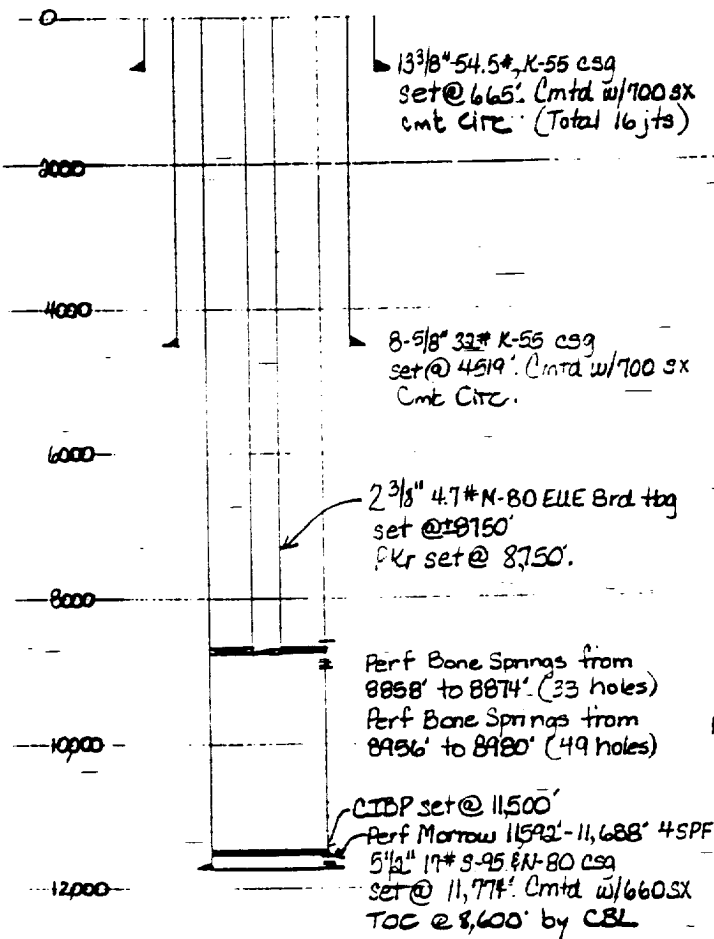

Completion History
Ran B-51a csg. DV tool @ 2310'.
Pmpd 700 SX Classic w/ 2% CaCl₂.
Opened DV tool circ w/ 200 bbls
fresh wtr. Circ DV tool, pmpd FW
to keep tool open. Cmtd thru DV
tool w/ 850 SX 65-34 Lite-Pox. 5#
salt, 5# Petrolite, 4% Bent, 2%
CaCl₂. TDC @ 11,000'.
Cmtd outside 0-78" csg from
990'-650' in 7 stages w/ 800 SX
Dowell RFC w/ 3% CaCl₂, followed
by 4 yds Redimix. Cmt to surface
Ram gun assy. & Lokset pkr on
23 1/8" 4.7# N-80 EUE Brd tbg.
Guns spaced to perf 11,592'-96',
11,624'-32', 11,652'-64' & 11,685'-88'
w/ 4 SPF.
SITP 3900', Flowed 8 hrs on -
32 1/64" chK @ 2100# - FARD
13 MMCFD, well cleaned up.
Ran AOF test, max rate 2922 mcf
2769' FTP on 1 1/4" chK. Morrow prodn
cum 520 MMCF & 8 MBO. ST in 1983,
pressure depleted - no longer capable of pr
1/90 ~~Recompletion to abandon Morrow~~
~~and perforate Bone Springs~~
TOH w/ tbg & packer.
RIH w/ CTDP & set it @ 11,500'.
Dump 35' of cement on top of CTDP.
Perf Bone Springs Carbonate
w/ 4" csg gun from 8992' to 8980'
w/ 2 SPF (Total 49 holes).
Acidize w/ 3000 gals of 15% HCl-FF
acid & 75 ball sealers. Swab &
flow test.
Perf w/ 4" csg gun from 8858' to
8874' w/ 2 SPF (33 holes).
TIH w/ RBP & retrievable packer. Set
RBP @ 8920' & pkr @ 8900'. Circ
2 SX on top of RBP. Set pkr
@ 8750' ±. Swab & flow test.
Acidize perfs 8858' to 8874' w/
2,000 gals 15% HCl-FF acid &
50 ball sealers. Swab & flow test

VM
1/92
