

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Road, Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy Minerals and Natural Resources
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

RECEIVED

JAN 16 2015

Submit Copy to appropriate District Office in accordance with 19.15.29 NMAC.

NMOCD

DISTRICT III

Form C-141
Revised August 8, 2011

Release Notification and Corrective Action

OPERATOR

☐ Initial Report ☒ Final Report

Name of Company: BP	Contact: Jeff Peace
Address: 200 Energy Court, Farmington, NM 87401	Telephone No.: 505-326-9479
Facility Name: Gallegos Canyon Unit 200E	Facility Type: Natural gas well

Surface Owner: Private	Mineral Owner: Private	API No. 3004524170
------------------------	------------------------	--------------------

LOCATION OF RELEASE

Unit Letter O	Section 29	Township 29N	Range 12W	Feet from the 815	North/South Line South	Feet from the 1,690	East/West Line East	County: San Juan
------------------	---------------	-----------------	--------------	----------------------	---------------------------	------------------------	------------------------	------------------

Latitude 36.69209 Longitude 108.11986

NATURE OF RELEASE

Type of Release: condensate/oil	Volume of Release: unknown	Volume Recovered: none
Source of Release: below grade tank	Date and Hour of Occurrence: unknown	Date and Hour of Discovery: October 4, 2013; 2:20 PM
Was Immediate Notice Given? ☐ Yes ☐ No ☒ Not Required	If YES, To Whom?	
By Whom?	Date and Hour:	
Was a Watercourse Reached? ☐ Yes ☒ No	If YES, Volume Impacting the Watercourse.	

If a Watercourse was Impacted, Describe Fully.*

Describe Cause of Problem and Remedial Action Taken.* During removal of the below grade tank (BGT) soil underneath the tank was sampled. Analysis results showed TPH values of 2,680 ppm by Method 418.1, indicating a release occurred at some time. Impacted soil was excavated and removed.

Describe Area Affected and Cleanup Action Taken.* Impacted soil under the BGT was excavated and removed until remaining soil samples resulted in TPH values of less than 100 ppm TPH, which is the cleanup standard for this site. Approximately 214 cubic yards of impacted soil were removed and transported to a landfarm for treatment. The excavated area was backfilled with clean soil and compacted. Attached are lab analyses, photos of the excavation, and a site map.

I hereby certify that the information given above is true and complete to the best of my knowledge and understand that pursuant to NMOCD rules and regulations all operators are required to report and/or file certain release notifications and perform corrective actions for releases which may endanger public health or the environment. The acceptance of a C-141 report by the NMOCD marked as "Final Report" does not relieve the operator of liability should their operations have failed to adequately investigate and remediate contamination that pose a threat to ground water, surface water, human health or the environment. In addition, NMOCD acceptance of a C-141 report does not relieve the operator of responsibility for compliance with any other federal, state, or local laws and/or regulations.

Signature: <i>Jeff Peace</i>	OIL CONSERVATION DIVISION	
Printed Name: Jeff Peace	Approved by Environmental Specialist: <i>[Signature]</i>	
Title: Field Environmental Coordinator	Approval Date: 3/23/15	Expiration Date:
E-mail Address: peace.jeffrey@bp.com	Conditions of Approval:	Attached ☐
Date: January 16, 2015	Phone: 505-326-9479	

* Attach Additional Sheets If Necessary

#NCS 1508241 540

26

BP America: GCU 200E
(O) Sec 29 – T29N – R12W
API: 30-045-24170
San Juan County, New Mexico

Summary Record of Impact Remediation

October 4, 2013 Soils impacted with hydrocarbons encountered during closure of 95 barrel BGT (Tank ID: A). Impacts limited to a small area on outside of northeast corner of the BGT and appeared to be from prior overflow events. An inflow hole cut near top of the BGT on the northeast side allowed run-out of fluids when high fluid levels were present in the BGT. A 5-point composite soil sample collected from immediately below the BGT that did not include the stained area was non-detect for TPH, BTEX and Chloride. A grab sample of the impacted soil stain at a depth of 3' below the BGT (8' below surface pad grade) yielded a TPH = 2,680 mg/Kg, total BTEX = 2.4 mg/Kg and was non-detect for Chloride. Additional investigation of the impact depth and areal extent could not be conducted due to the presence of 2 high pressure pipelines in the immediate area of the impact.

The site closure standard was determined at 100 ppm TPH based on:
Depth to Groundwater Estimated at < 50 feet based on known water depth at nearby GCU 188 (20 points)

February 6, 2014 Attempt to determine depth and areal extent of impacts using a contract environmental drill rig. Could not advance any borings deeper than 13' below grade due to large river cobbles and drilling was terminated.

September 19, 2014 Begin site remediation using trackhoe to remove soil impacts. Enterprise pipelines immediately north of the impact area made it necessary to conduct all excavations from the south side.

September 23, 2014 Excavation size is a triangular shape of approximately 35' x 25' x 18' deep. A dense sandstone encountered at the 18' depth. East, west and south sidewalls and the sandstone base visually appeared clean. The north sidewall from the ground surface to a depth of about 12' visually appeared clean, but gray staining was present from 12' to 16' along the middle of north sidewall. A grab sample of this stained area yielded a laboratory TPH of 5,670 mg/Kg by Method 8015B (DRO+GRO)

Conduct sidewall and base closure sampling of the east, west, south and base of the existing excavation:

Sample ID	Date/Time	Map ID	Field OVM	TPH 8015B	BTEX 8021	Chloride
SW Corner 3-pt 8' – 16'	9/23/2014 @ 11:24 am	1	28	11.3 mg/Kg	ND	ND
West Wall 3-pt 8' – 16'	9/23/2014 @ 11:28 am	2	ND	ND	ND	94 mg/Kg
East Wall 3-pt 8' – 16'	9/23/2014 @ 11:40 am	3	ND	ND	ND	ND
North Wall 3-pt 6' – 10'	9/23/2014 @ 11:56 am	4	ND	ND	ND	ND
Base 5-Point at -18'	9/23/2014 @ 12:02 pm	5	97	83.2 mg/Kg	0.25 mg/Kg	100 mg/Kg

September 25, 2014 Move excavation equipment off location. Conduct evaluation of residual impacts and consult with pipeline operator on procedure to remove impacts believed to exist below the transmission pipelines.


October 21, 2014 Continue site remediation by excavation of impacts using trackhoe. The existing excavation partially backfilled to allow the trackhoe to be sitting approximately 10' below surface grade while positioned on the south side of the pipelines. Excavate impacts from the north wall below the pipelines and remove all stained soils. Dense sandstone base at the 18' depth, dig approximately 6-inches vertically into this bedrock.

October 22, 2014 Sample north sidewall and sandstone base in the area below the transmission pipelines for closure:

Sample ID	Date/Time	Map ID	Field OVM	TPH 8015B	BTEX 8021	Chloride
North Base @ 18.5' - 3 pt Comp	10/22/2014 @ 12:39 pm	6	ND	ND	ND	ND
North Wall 3-pt 6' - 16.5'	10/22/2014 @ 12:42 pm	7	ND	ND	ND	ND

Final excavation in a triangular pattern, with surface dimensions at ground surface grade size approximately 50' x 28' x 18.5' deep. Impacted soil volume transported to landfarm = 214 cubic yards.

October 24, 2014 Excavation crew completes backfilling operation.

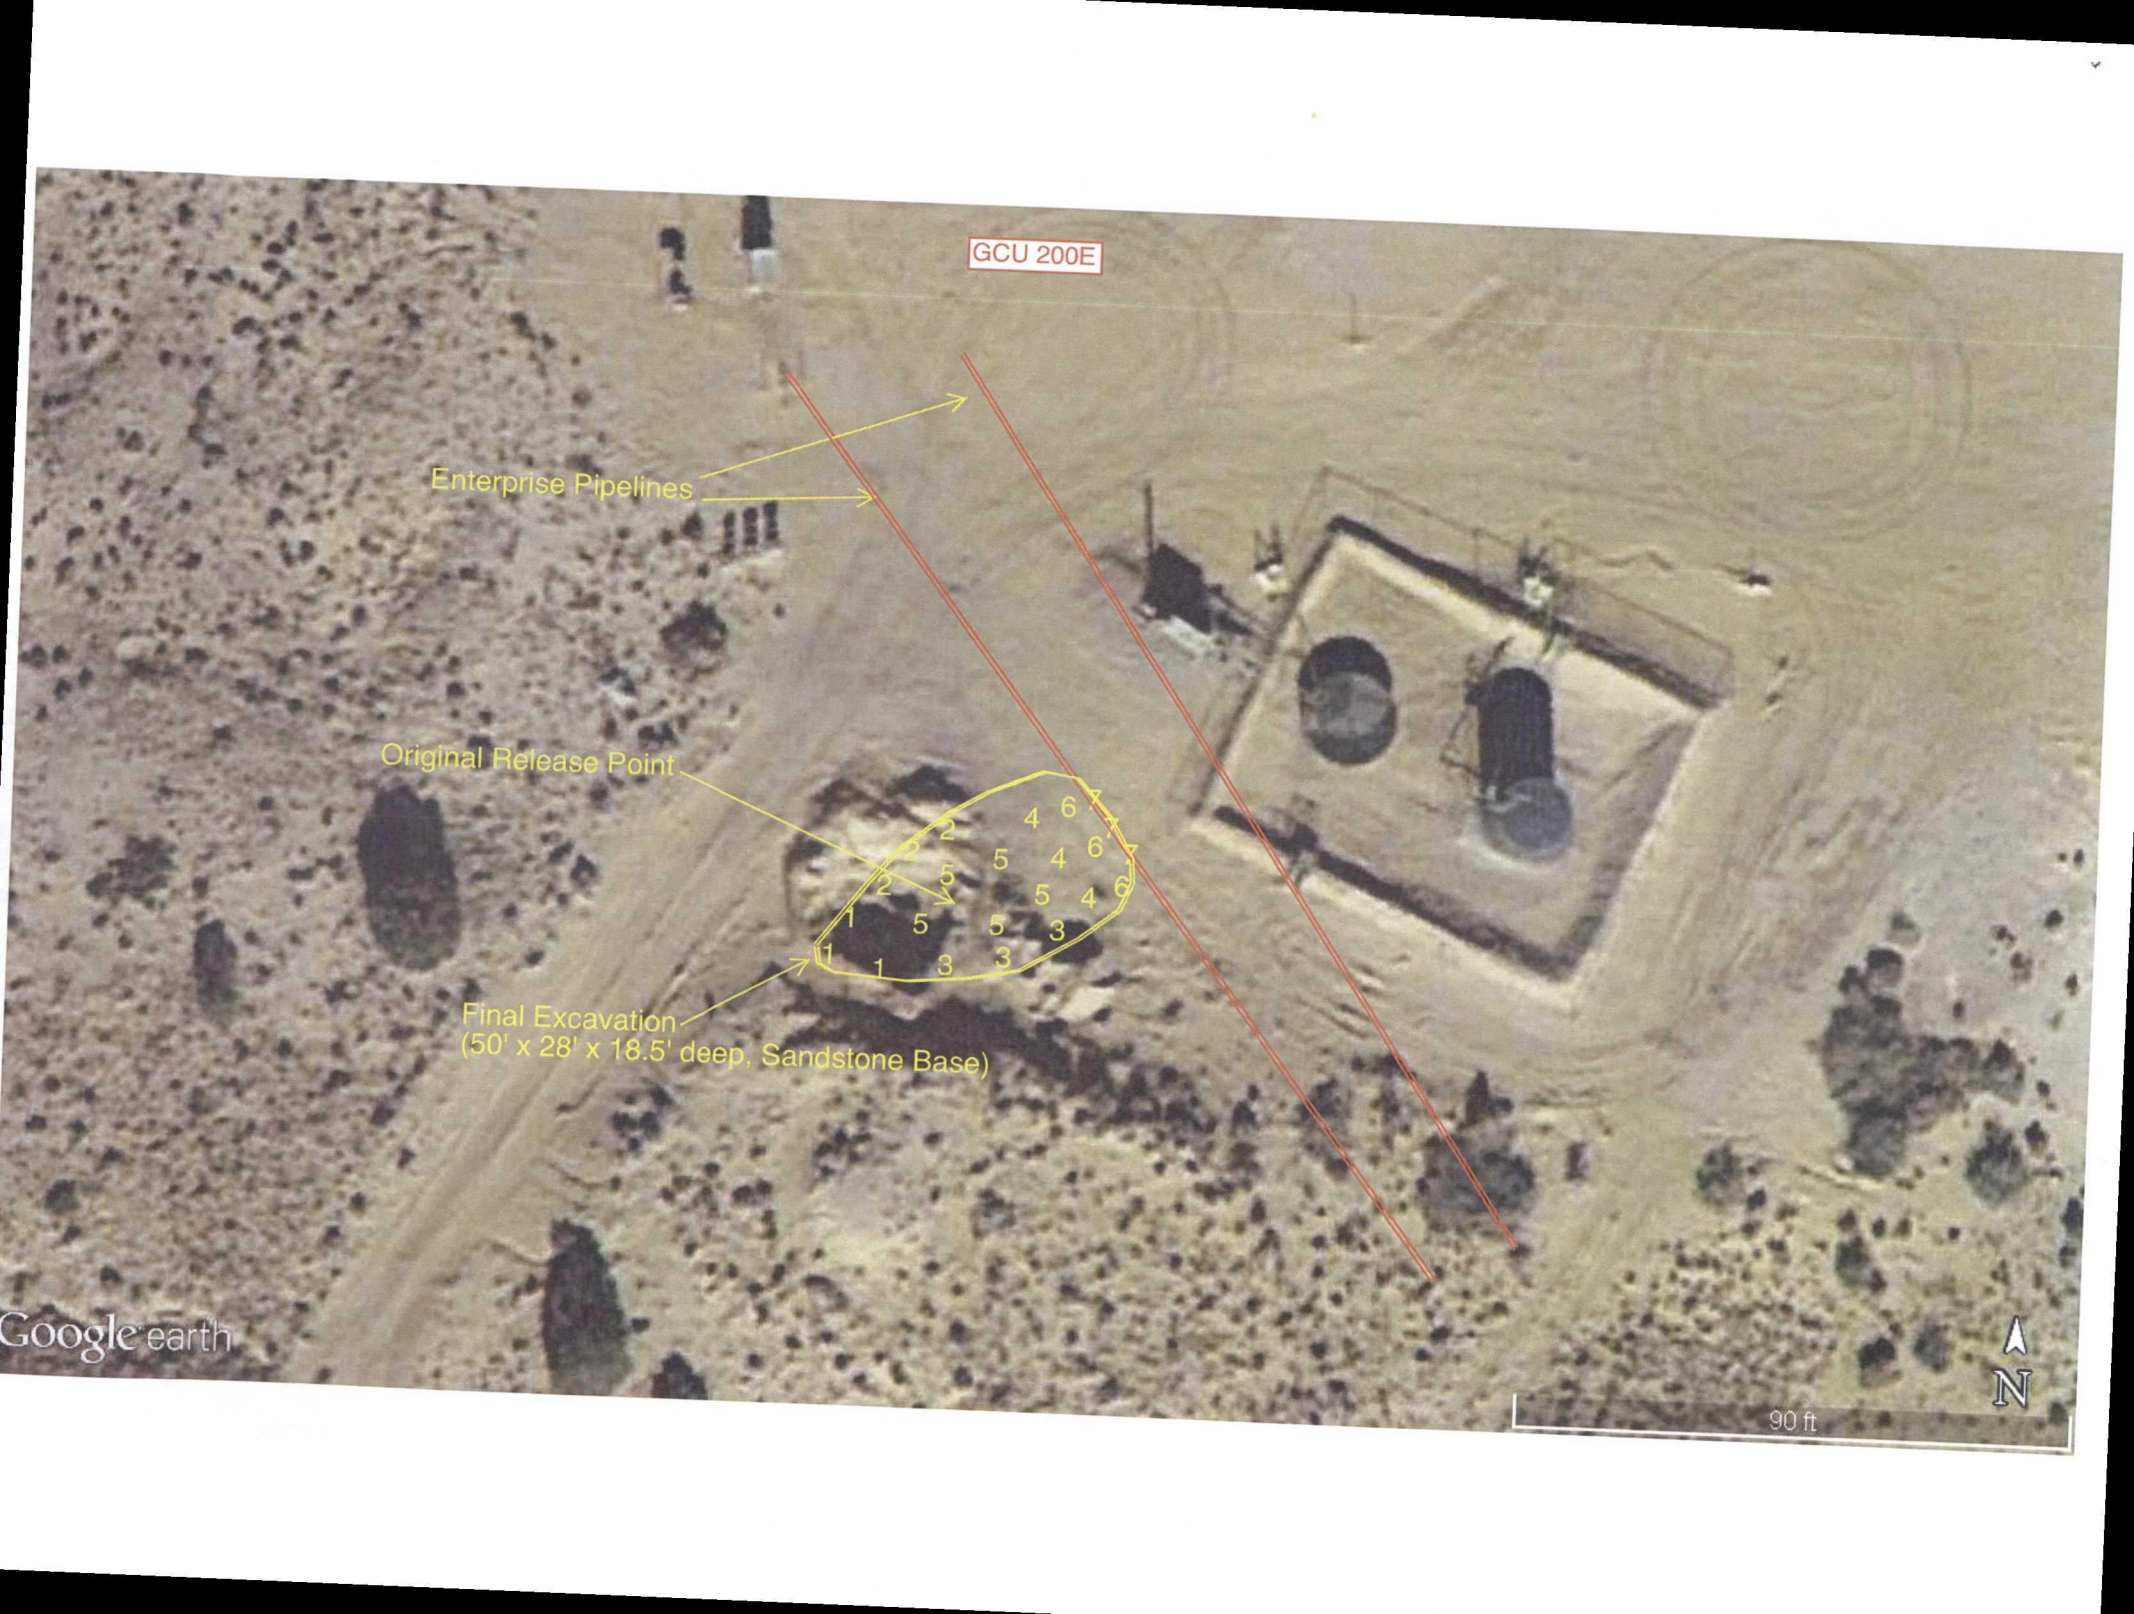

GCU 200E

Enterprise Pipelines

Original Release Point


Final Excavation
(50' x 28' x 18.5' deep, Sandstone Base)

Google earth


90 ft

N

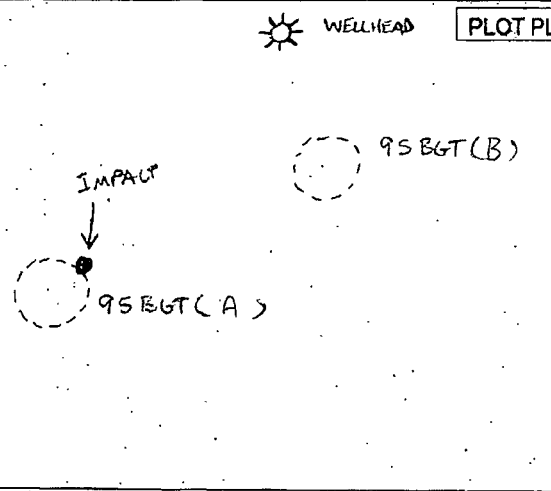

CLIENT: <u>BP</u>	BLAGG ENGINEERING, INC. P.O. BOX 87, BLOOMFIELD, NM 87413 (505) 632-1199	API #: <u>30-045-24170</u> TANK ID (if applicable): <u>A & B</u>								
FIELD REPORT: (circle one) <u>BGT CONFIRMATION</u> / RELEASE INVESTIGATION / OTHER:		PAGE #: <u>1</u> of <u>1</u>								
SITE INFORMATION: SITE NAME: <u>GCU 200E</u> QUAD/UNIT: <u>0 SEC: 29 TWP: 29N RNG: 12W PM: NM CNTY: SJ ST: NM</u> 1/4 - 1/4 FOOTAGE: LEASE TYPE: <u>FEDERAL / STATE / FEE / INDIAN</u> LEASE #: <u>NMNM 78391C</u> PROD. FORMATION: CONTRACTOR: <u>ELKHORN (P. ALLEN & ASSOC)</u>		DATE STARTED: <u>10-4-2013</u> DATE FINISHED: <u>10-4-2013</u> ENVIRONMENTAL SPECIALIST(S): <u>JCB</u>								
REFERENCE POINT: WELL HEAD (WH) GPS COORD.: GL ELEV.: <u>5414</u> 1) <u>95 BGT (B)</u> GPS COORD.: <u>36.69228 x 108.11927</u> DISTANCE/BEARING FROM WH.: <u>78' S 13° E</u> 2) <u>95 BGT (A)</u> GPS COORD.: <u>36.69209 x 108.11986</u> DISTANCE/BEARING FROM WH.: <u>195' S 45° W</u> 3) _____ GPS COORD.: _____ DISTANCE/BEARING FROM WH.: _____ 4) _____ GPS COORD.: _____ DISTANCE/BEARING FROM WH.: _____										
SAMPLING DATA: CHAIN OF CUSTODY RECORD(S) # OR LAB USED: <u>HALL</u>		OVM READING (ppm)								
1) SAMPLE ID: <u>95 BGT (B) @ 6'</u> SAMPLE DATE: <u>10-4-2013</u> SAMPLE TIME: <u>1355</u> LAB ANALYSIS: <u>TPH/BTEX/CL</u> 2) SAMPLE ID: <u>95 BGT (A) @ 5'</u> SAMPLE DATE: <u>"</u> SAMPLE TIME: <u>1415</u> LAB ANALYSIS: <u>" " "</u> 3) SAMPLE ID: <u>(A) IMPACT @ 6'</u> SAMPLE DATE: <u>"</u> SAMPLE TIME: <u>1420</u> LAB ANALYSIS: <u>"</u> 4) SAMPLE ID: <u>(A) IMPACT @ 8'</u> SAMPLE DATE: <u>"</u> SAMPLE TIME: <u>1425</u> LAB ANALYSIS: <u>"</u>		<u>0.0</u> <u>0.0</u> <u>237</u> <u>938</u>								
SOIL DESCRIPTION: SOIL TYPE: <u>SAND / SILTY SAND</u> / SILT / SILTY CLAY / CLAY / GRAVEL / OTHER _____ SOIL COLOR: <u>Yellow TAN</u> COHESION (ALL OTHERS): <u>NON COHESIVE</u> / SLIGHTLY COHESIVE / COHESIVE / HIGHLY COHESIVE CONSISTENCY (NON COHESIVE SOILS): <u>LOOSE</u> / FIRM / DENSE / VERY DENSE MOISTURE: DRY / <u>SLIGHTLY MOIST</u> / MOIST / WET / SATURATED / SUPER SATURATED SAMPLE TYPE: GRAB / <u>COMPOSITE</u> # OF PTS.: <u>5</u> DISCOLORATION/STAINING OBSERVED: <u>YES</u> / NO EXPLANATION: <u>TANK (A) IMPACT @ INLET - GRAY</u>		PLASTICITY (CLAYS): NON PLASTIC / SLIGHTLY PLASTIC / COHESIVE / MEDIUM PLASTIC / HIGHLY PLASTIC DENSITY (COHESIVE CLAYS & SILTS): SOFT / FIRM / STIFF / VERY STIFF / HARD HC ODOR DETECTED: <u>YES</u> / NO EXPLANATION: <u>TANK (A) @ IMPACT</u>								
ANY AREAS DISPLAYING WETNESS: YES / <u>NO</u> EXPLANATION: _____ APPARENT EVIDENCE OF A RELEASE OBSERVED AND/OR OCCURRED: <u>YES</u> / NO EXPLANATION: <u>TANK (A) @ IMPACT</u> ADDITIONAL COMMENTS: _____										
SOIL IMPACT DIMENSION ESTIMATION: _____ ft X _____ ft X _____ ft EXCAVATION ESTIMATION (Cubic Yards): _____ DEPTH TO GROUNDWATER: _____ NEAREST WATER SOURCE: _____ NEAREST SURFACE WATER: _____ NMOC TPH CLOSURE STD: _____ ppm										
SITE SKETCH:  PLOT PLAN circle: <u>attached</u>		OVM CALIB. READ. = <u>99.8</u> ppm RF = <u>0.52</u> OVM CALIB. GAS = <u>100.0</u> ppm TIME: <u>1310</u> am/pm DATE: <u>10-4-13</u>								
MISCELL. NOTES WO: <u>N15324801</u> PO #: _____ PK: <u>ZEVEH01BGT2</u> PJ #: <u>Z2-00600</u> Permit date(s): _____ OCD Appr. date(s): _____ <table border="1" style="width:100%; border-collapse: collapse;"> <tr> <td style="width:10%;">Tank ID</td> <td>OVM = Organic Vapor Meter ppm = parts per million</td> </tr> <tr> <td><u>A</u></td> <td>BGT Sidewalls Visible: <u>Y</u> / <u>N</u></td> </tr> <tr> <td><u>B</u></td> <td>BGT Sidewalls Visible: <u>Y</u> / <u>N</u></td> </tr> <tr> <td></td> <td>BGT Sidewalls Visible: <u>Y</u> / <u>N</u></td> </tr> </table> Magnetic declination: <u>10° E</u>		Tank ID	OVM = Organic Vapor Meter ppm = parts per million	<u>A</u>	BGT Sidewalls Visible: <u>Y</u> / <u>N</u>	<u>B</u>	BGT Sidewalls Visible: <u>Y</u> / <u>N</u>		BGT Sidewalls Visible: <u>Y</u> / <u>N</u>	
Tank ID	OVM = Organic Vapor Meter ppm = parts per million									
<u>A</u>	BGT Sidewalls Visible: <u>Y</u> / <u>N</u>									
<u>B</u>	BGT Sidewalls Visible: <u>Y</u> / <u>N</u>									
	BGT Sidewalls Visible: <u>Y</u> / <u>N</u>									
NOTES: BGT = BELOW-GRADE TANK; E.D. = EXCAVATION DEPRESSION; B.G. = BELOW GRADE; B = BELOW; T.H. = TEST HOLE; ~ = APPROX; WH = WELL HEAD; T.B. = TANK BOTTOM; PBGT = PREVIOUS BELOW-GRADE TANK LOCATION; SPD = SAMPLE POINT DESIGNATION; R.W. = RETAINING WALL; NA = NOT APPLICABLE OR NOT AVAILABLE; SW = SINGLE WALL; DW = DOUBLE WALL; SB = SINGLE BOTTOM; DB = DOUBLE BOTTOM.										
TRAVEL NOTES: CALLOUT: _____ ONSITE: <u>10/4/2013 @ 12:30 PM</u>										

GCU 200E
Hole Found Cut in NE Corner of 95 BGT
for Inflow Piping
Oct 4, 2013

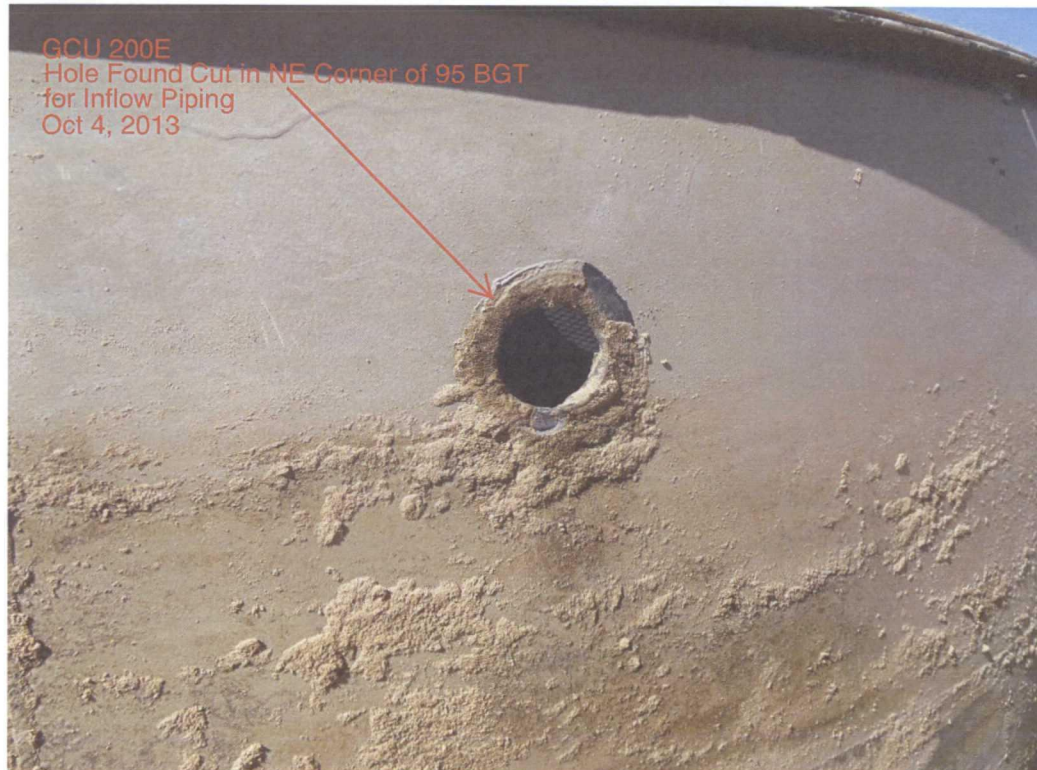



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 03143-0424
Project Manager: Jeff Blagg

Reported:
25-Sep-14 12:27

Analytical Report for Samples

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
North Wall Grab @-16'	P409092-01A	Soil	09/23/14	09/23/14	Glass Jar, 4 oz.
SW Corner 3-pt 8'-16'	P409092-02A	Soil	09/23/14	09/23/14	Glass Jar, 4 oz.
West Wall 3-pt 8'-16'	P409092-03A	Soil	09/23/14	09/23/14	Glass Jar, 4 oz.
East Wall 3-pt 8'-16'	P409092-04A	Soil	09/23/14	09/23/14	Glass Jar, 4 oz.
North Wall 3-pt 6'-10'	P409092-05A	Soil	09/23/14	09/23/14	Glass Jar, 4 oz.
Base 5-pt @ -18'	P409092-06A	Soil	09/23/14	09/23/14	Glass Jar, 4 oz.

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.

5796 US Highway 64, Farmington, NM 87401

Three Springs • 65 Mercado Street, Suite 115, Durango, CO 81301

Ph (505) 632-0615 Fx (505) 632-1865

Ph (970) 259-0615 Fr (800) 362-1879

envirotech-inc.com
laboratory@envirotech-inc.com



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 03143-0424
Project Manager: Jeff Blagg

Reported:
25-Sep-14 12:27

SW Corner 3-pt 8'-16'
P409092-02 (Solid)

Analyte	Result	Reporting		Dilution	Batch	Prepared	Analyzed	Method	Notes
		Limit	Units						
Volatile Organics by EPA 8021									
Benzene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Toluene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Ethylbenzene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
p,m-Xylene	ND	0.20	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
o-Xylene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Total Xylenes	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Total BTEX	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Surrogate: 4-Bromochlorobenzene-PID		97.0 %		50-150	1439011	09/24/14	09/24/14	EPA 8021B	
Nonhalogenated Organics by 8015									
Gasoline Range Organics (C6-C10)	11.3	9.99	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8015D	
Diesel Range Organics (C10-C28)	ND	25.0	mg/kg	1	1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: o-Terphenyl		96.1 %		50-200	1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: 4-Bromochlorobenzene-FID		88.5 %		50-150	1439011	09/24/14	09/24/14	EPA 8015D	
Cation/Anion Analysis									
Chloride	ND	9.98	mg/kg	1	1439012	09/24/14	09/24/14	EPA 300.0	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.	Project Name:	GCU 200E	Reported: 25-Sep-14 12:27
PO Box 22024	Project Number:	03143-0424	
Tulsa OK, 74121-2024	Project Manager:	Jeff Blagg	

West Wall 3-pt 8'-16'
P409092-03 (Solid)

Analyte	Result	Reporting		Units	Dilution	Batch	Prepared	Analyzed	Method	Notes
		Limit								
Volatile Organics by EPA 8021										
Benzene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Toluene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Ethylbenzene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
p,m-Xylene	ND	0.20	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
o-Xylene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Total Xylenes	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Total BTEX	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Surrogate: 4-Bromochlorobenzene-PID		103 %		50-150		1439011	09/24/14	09/24/14	EPA 8021B	
Nonhalogenated Organics by 8015										
Gasoline Range Organics (C6-C10)	ND	9.99	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8015D	
Diesel Range Organics (C10-C28)	ND	25.0	mg/kg	1		1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: o-Terphenyl		90.9 %		50-200		1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: 4-Bromochlorobenzene-FID		92.4 %		50-150		1439011	09/24/14	09/24/14	EPA 8015D	
Cation/Anion Analysis										
Chloride	94.0	9.85	mg/kg	1		1439012	09/24/14	09/24/14	EPA 300.0	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 03143-0424
Project Manager: Jeff Blagg

Reported:
25-Sep-14 12:27

East Wall 3-pt 8'-16'
P409092-04 (Solid)

Analyte	Result	Reporting		Units	Dilution	Batch	Prepared	Analyzed	Method	Notes
		Limit								
Volatile Organics by EPA 8021										
Benzene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Toluene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Ethylbenzene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
p,m-Xylene	ND	0.20	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
o-Xylene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Total Xylenes	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Total BTEX	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Surrogate: 4-Bromochlorobenzene-PID		104 %		50-150		1439011	09/24/14	09/24/14	EPA 8021B	
Nonhalogenated Organics by 8015										
Gasoline Range Organics (C6-C10)	ND	10.0	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8015D	
Diesel Range Organics (C10-C28)	ND	24.9	mg/kg	1		1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: o-Terphenyl		89.5 %		50-200		1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: 4-Bromochlorobenzene-FID		93.4 %		50-150		1439011	09/24/14	09/24/14	EPA 8015D	
Cation/Anion Analysis										
Chloride	ND	9.94	mg/kg	1		1439012	09/24/14	09/24/14	EPA 300.0	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co. PO Box 22024 Tulsa OK, 74121-2024	Project Name: GCU 200E Project Number: 03143-0424 Project Manager: Jeff Blagg	Reported: 25-Sep-14 12:27
---	---	------------------------------

North Wall 3-pt 6'-10'
P409092-05 (Solid)

Analyte	Result	Reporting		Dilution	Batch	Prepared	Analyzed	Method	Notes
		Limit	Units						
Volatile Organics by EPA 8021									
Benzene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Toluene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Ethylbenzene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
p,m-Xylene	ND	0.20	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
o-Xylene	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Total Xylenes	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Total BTEX	ND	0.10	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8021B	
Surrogate: 4-Bromochlorobenzene-PID		103 %		50-150	1439011	09/24/14	09/24/14	EPA 8021B	
Nonhalogenated Organics by 8015									
Gasoline Range Organics (C6-C10)	ND	10.0	mg/kg	1	1439011	09/24/14	09/24/14	EPA 8015D	
Diesel Range Organics (C10-C28)	ND	30.0	mg/kg	1	1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: o-Terphenyl		91.3 %		50-200	1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: 4-Bromochlorobenzene-FID		93.6 %		50-150	1439011	09/24/14	09/24/14	EPA 8015D	
Cation/Anion Analysis									
Chloride	ND	9.91	mg/kg	1	1439012	09/24/14	09/24/14	EPA 300.0	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 03143-0424
Project Manager: Jeff Blagg

Reported:
25-Sep-14 12:27

Base 5-pt @ -18'
P409092-06 (Solid)

Analyte	Result	Reporting		Units	Dilution	Batch	Prepared	Analyzed	Method	Notes
		Limit								
Volatile Organics by EPA 8021										
Benzene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Toluene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Ethylbenzene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
p,m-Xylene	0.25	0.20	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
o-Xylene	ND	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Total Xylenes	0.25	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Total BTEX	0.25	0.10	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8021B	
Surrogate: 4-Bromochlorobenzene-PID		104 %		50-150		1439011	09/24/14	09/24/14	EPA 8021B	
Nonhalogenated Organics by 8015										
Gasoline Range Organics (C6-C10)	17.6	9.98	mg/kg	1		1439011	09/24/14	09/24/14	EPA 8015D	
Diesel Range Organics (C10-C28)	65.6	25.0	mg/kg	1		1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: o-Terphenyl		101 %		50-200		1439009	09/24/14	09/24/14	EPA 8015D	
Surrogate: 4-Bromochlorobenzene-FID		93.8 %		50-150		1439011	09/24/14	09/24/14	EPA 8015D	
Cation/Anion Analysis										
Chloride	100	9.98	mg/kg	1		1439012	09/24/14	09/24/14	EPA 300.0	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.

5796 US Highway 64, Farmington, NM 87401

Three Springs • 65 Mercado Street, Suite 115, Durango, CO 81301

Ph (505) 632-0615 Fx (505) 632-1865

Ph (970) 259-0615 Fr (800) 362-1879

envirotech-inc.com

laboratory@envirotech-inc.com



BP America Production Co.	Project Name:	GCU 200E	Reported: 25-Sep-14 12:27
PO Box 22024	Project Number:	03143-0424	
Tulsa OK, 74121-2024	Project Manager:	Jeff Blagg	

Volatile Organics by EPA 8021 - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit	Notes
---------	--------	-----------------	-------	-------------	---------------	------	-------------	-----	-----------	-------

Batch 1439011 - Purge and Trap EPA 5030A

Blank (1439011-BLK1)

Prepared & Analyzed: 23-Sep-14

Benzene	ND	0.10	mg/kg							
Toluene	ND	0.10	"							
Ethylbenzene	ND	0.10	"							
p,m-Xylene	ND	0.20	"							
o-Xylene	ND	0.10	"							
Total Xylenes	ND	0.10	"							
Total BTEX	ND	0.10	"							
Surrogate: 4-Bromochlorobenzene-PID	0.393		"	0.400		98.3	50-150			

LCS (1439011-BS1)

Prepared & Analyzed: 23-Sep-14

Benzene	19.7	0.10	mg/kg	20.0		98.7	75-125			
Toluene	19.7	0.10	"	20.0		98.7	70-125			
Ethylbenzene	19.9	0.10	"	20.0		99.6	75-125			
p,m-Xylene	40.5	0.20	"	40.0		101	80-125			
o-Xylene	20.0	0.10	"	20.0		100	75-125			
Surrogate: 4-Bromochlorobenzene-PID	0.417		"	0.400		104	50-150			

Matrix Spike (1439011-MS1)

Source: P409094-01

Prepared & Analyzed: 23-Sep-14

Benzene	20.3	0.10	mg/kg	19.9	ND	102	75-125			
Toluene	20.3	0.10	"	19.9	ND	102	70-125			
Ethylbenzene	20.5	0.10	"	19.9	ND	103	75-125			
p,m-Xylene	41.6	0.20	"	39.9	ND	104	80-125			
o-Xylene	20.5	0.10	"	19.9	ND	103	75-125			
Surrogate: 4-Bromochlorobenzene-PID	0.412		"	0.399		103	50-150			

Matrix Spike Dup (1439011-MSD1)

Source: P409094-01

Prepared & Analyzed: 23-Sep-14

Benzene	20.2	0.10	mg/kg	20.0	ND	101	75-125	0.298	15	
Toluene	20.2	0.10	"	20.0	ND	101	70-125	0.282	15	
Ethylbenzene	20.4	0.10	"	20.0	ND	102	75-125	0.410	15	
p,m-Xylene	41.4	0.20	"	40.0	ND	104	80-125	0.537	15	
o-Xylene	20.4	0.10	"	20.0	ND	102	75-125	0.556	15	
Surrogate: 4-Bromochlorobenzene-PID	0.401		"	0.400		100	50-150			

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.

5796 US Highway 64, Farmington, NM 87401

Three Springs • 65 Mercado Street, Suite 115, Durango, CO 81301

Ph (505) 632-0615 Fx (505) 632-1865

Ph (970) 259-0615 Fr (800) 362-1879

envirotech-inc.com
laboratory@envirotech-inc.com



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 03143-0424
Project Manager: Jeff Blagg

Reported:
25-Sep-14 12:27

Nonhalogenated Organics by 8015 - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit	Notes
Batch 1439009 - DRO Extraction EPA 3550M										
Blank (1439009-BLK1)				Prepared & Analyzed: 23-Sep-14						
Diesel Range Organics (C10-C28)	ND	24.9	mg/kg							
Surrogate: o-Terphenyl	32.6		"	39.9		81.8	50-200			
LCS (1439009-BS1)				Prepared & Analyzed: 23-Sep-14						
Diesel Range Organics (C10-C28)	505	24.9	mg/kg	499		101	38-132			
Surrogate: o-Terphenyl	37.9		"	39.9		94.9	50-200			
Matrix Spike (1439009-MS1)				Source: P409090-01		Prepared & Analyzed: 23-Sep-14				
Diesel Range Organics (C10-C28)	521	25.0	mg/kg	499	ND	104	38-132			
Surrogate: o-Terphenyl	36.9		"	39.9		92.1	50-200			
Matrix Spike Dup (1439009-MSD1)				Source: P409090-01		Prepared & Analyzed: 23-Sep-14				
Diesel Range Organics (C10-C28)	512	24.9	mg/kg	498	ND	103	38-132	1.63	20	
Surrogate: o-Terphenyl	36.3		"	39.9		91.1	50-200			

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.	Project Name:	GCU 200E	Reported: 25-Sep-14 12:27
PO Box 22024	Project Number:	03143-0424	
Tulsa OK, 74121-2024	Project Manager:	Jeff Blagg	

Nonhalogenated Organics by 8015 - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit	Notes
Batch 1439011 - Purge and Trap EPA 5030A										
Blank (1439011-BLK1)				Prepared & Analyzed: 23-Sep-14						
Gasoline Range Organics (C6-C10)	ND	9.99	mg/kg							
Surrogate: 4-Bromochlorobenzene-FID	0.358		"	0.400		89.5	50-150			
LCS (1439011-BS1)				Prepared & Analyzed: 23-Sep-14						
Gasoline Range Organics (C6-C10)	275	10.0	mg/kg	292		94.2	80-120			
Surrogate: 4-Bromochlorobenzene-FID	0.379		"	0.400		94.8	50-150			
Matrix Spike (1439011-MS1)				Source: P409094-01		Prepared & Analyzed: 23-Sep-14				
Gasoline Range Organics (C6-C10)	282	9.97	mg/kg	291	ND	96.9	75-125			
Surrogate: 4-Bromochlorobenzene-FID	0.372		"	0.399		93.4	50-150			
Matrix Spike Dup (1439011-MSD1)				Source: P409094-01		Prepared & Analyzed: 23-Sep-14				
Gasoline Range Organics (C6-C10)	281	9.99	mg/kg	292	ND	96.3	75-125	0.403	15	
Surrogate: 4-Bromochlorobenzene-FID	0.364		"	0.400		91.2	50-150			

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.	Project Name:	GCU 200E	Reported: 25-Sep-14 12:27
PO Box 22024	Project Number:	03143-0424	
Tulsa OK, 74121-2024	Project Manager:	Jeff Blagg	

Cation/Anion Analysis - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC Limits	RPD	RPD Limit	Notes
Batch 1439012 - Anion Extraction EPA 300.0									
Blank (1439012-BLK1)					Prepared & Analyzed: 24-Sep-14				
Chloride	ND	9.88	mg/kg						
LCS (1439012-BS1)					Prepared & Analyzed: 24-Sep-14				
Chloride	484	9.84	mg/kg	492		98.4	90-110		
Matrix Spike (1439012-MS1)					Source: P409092-02 Prepared & Analyzed: 24-Sep-14				
Chloride	485	9.92	mg/kg	496	ND	97.8	80-120		
Matrix Spike Dup (1439012-MSD1)					Source: P409092-02 Prepared & Analyzed: 24-Sep-14				
Chloride	488	9.99	mg/kg	500	ND	97.7	80-120	0.531	20

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.

CHAIN OF CUSTODY RECORD

17810

Client: BP AMERICA			Project Name / Location: GCU 200E			ANALYSIS / PARAMETERS														
Email, results to: jeffcblagg@AOL.com peace.jeffrey@BP.com			Sampler Name: J. Blagg			TPH (Method 8015)	BTEX (Method 8021)	VOC (Method 8260)	RCRA 8 Metals	Cation / Anion	RCI	TCLP with H/P	CO Table 910-1	TPH (418.1)	CHLORIDE			Sample Cool	Sample Intact	
Client Phone No.: 505-320-1183			Client No.: 03143-0424																	
Sample No./ Identification	Sample Date	Sample Time	Lab No.	No./Volume of Containers	Preservative															
					HNO ₃	HCl														
NORTH wall Grab @ -16'	9/23/2014	1055	P409092-01	1 x 402				X	X							X			Y	Y
SW corner 3-pt @ -16'	"	1124	P409092-02	"				X	X							X				
West wall 3-pt @ -16'	"	1128	P409092-03	"				X	X							X				
EAST wall 3-pt @ -16'	"	1140	P409092-04	"				X	X							X				
NORTH wall 3-pt @ -16'	"	1156	P409092-05	"				X	X							X				
BASE 5-pt @ -18'	"	1202	P409092-06	"				X	X							X				
Relinquished by: (Signature) <i>[Signature]</i>					Date	Time	Received by: (Signature) <i>[Signature]</i>					Date	Time							
					9/23/14	1355						9/23/14	1355							
Relinquished by: (Signature)							Received by: (Signature)													
Sample Matrix																				
Soil ☒ Solid ☐ Sludge ☐ Aqueous ☐ Other ☐																				
☐ Sample(s) dropped off after hours to secure drop off area.																				
<i>Rush Bill BP</i>										16.5, 15.7 18.2 (16.8)										
5795 US Highway 64 • Farmington, NM 87401 • 505-632-0615 • Three Springs • 65 Mercado Street, Suite 115, Durango, CO 81301 • laboratory@envirotech-inc.com																				



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 94034-0011
Project Manager: Jeff Blagg

Reported:
24-Oct-14 10:23

Analytical Report for Samples

Client Sample ID	Lab Sample ID	Matrix	Sampled	Received	Container
North Base @ 18 1/2' 3-pt Comp	P410095-01A	Soil	10/22/14	10/22/14	Glass Jar, 4 oz.
North Wall 3-pt 6'-16 1/2'	P410095-02A	Soil	10/22/14	10/22/14	Glass Jar, 4 oz.

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 94034-0011
Project Manager: Jeff Blagg

Reported:
24-Oct-14 10:23

North Base @ 18 1/2' 3-pt Comp
P410095-01 (Solid)

Analyte	Result	Reporting		Units	Dilution	Batch	Prepared	Analyzed	Method	Notes
		Limit								
Volatile Organics by EPA 8021										
Benzene	ND	0.10	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8021B	
Toluene	ND	0.10	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8021B	
Ethylbenzene	ND	0.10	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8021B	
p,m-Xylene	ND	0.20	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8021B	
o-Xylene	ND	0.10	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8021B	
Total Xylenes	ND	0.10	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8021B	
Total BTEX	ND	0.10	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8021B	
Surrogate: 4-Bromochlorobenzene-PID		89.2 %		50-150		1443027	10/22/14	10/23/14	EPA 8021B	
Nonhalogenated Organics by 8015										
Gasoline Range Organics (C6-C10)	ND	9.99	mg/kg	1		1443027	10/22/14	10/23/14	EPA 8015D	
Diesel Range Organics (C10-C28)	ND	29.9	mg/kg	1		1443026	10/22/14	10/23/14	EPA 8015D	
Surrogate: o-Terphenyl		85.5 %		50-200		1443026	10/22/14	10/23/14	EPA 8015D	
Surrogate: 4-Bromochlorobenzene-FID		81.4 %		50-150		1443027	10/22/14	10/23/14	EPA 8015D	
Cation/Anion Analysis										
Chloride	ND	9.84	mg/kg	1		1443036	10/22/14	10/22/14	EPA 300.0	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 94034-0011
Project Manager: Jeff Blagg

Reported:
24-Oct-14 10:23

North Wall 3-pt 6'-16 1/2'
P410095-02 (Solid)

Analyte	Result	Reporting Limit	Units	Dilution	Batch	Prepared	Analyzed	Method	Notes
Volatile Organics by EPA 8021									
Benzene	ND	0.10	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8021B	
Toluene	ND	0.10	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8021B	
Ethylbenzene	ND	0.10	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8021B	
p,m-Xylene	ND	0.20	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8021B	
o-Xylene	ND	0.10	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8021B	
Total Xylenes	ND	0.10	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8021B	
Total BTEX	ND	0.10	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8021B	
<i>Surrogate: 4-Bromochlorobenzene-PID</i>		93.8 %		50-150	1443027	10/22/14	10/23/14	EPA 8021B	
Nonhalogenated Organics by 8015									
Gasoline Range Organics (C6-C10)	ND	9.98	mg/kg	1	1443027	10/22/14	10/23/14	EPA 8015D	
Diesel Range Organics (C10-C28)	ND	29.9	mg/kg	1	1443026	10/22/14	10/23/14	EPA 8015D	
<i>Surrogate: o-Terphenyl</i>		95.5 %		50-200	1443026	10/22/14	10/23/14	EPA 8015D	
<i>Surrogate: 4-Bromochlorobenzene-FID</i>		85.5 %		50-150	1443027	10/22/14	10/23/14	EPA 8015D	
Cation/Anion Analysis									
Chloride	ND	9.91	mg/kg	1	1443036	10/22/14	10/22/14	EPA 300.0	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.	Project Name:	GCU 200E	Reported: 24-Oct-14 10:23
PO Box 22024	Project Number:	94034-0011	
Tulsa OK, 74121-2024	Project Manager:	Jeff Blagg	

Volatile Organics by EPA 8021 - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit	Notes
---------	--------	-----------------	-------	-------------	---------------	------	-------------	-----	-----------	-------

Batch 1443027 - Purge and Trap EPA 5030A

Blank (1443027-BLK1)			Prepared: 21-Oct-14 Analyzed: 22-Oct-14							
Benzene	ND	0.10	mg/kg							
Toluene	ND	0.10	"							
Ethylbenzene	ND	0.10	"							
p,m-Xylene	ND	0.20	"							
o-Xylene	ND	0.10	"							
Total Xylenes	ND	0.10	"							
Total BTEX	ND	0.10	"							
Surrogate: 4-Bromochlorobenzene-PID	0.381		"	0.399		95.5	50-150			

LCS (1443027-BS1)			Prepared: 21-Oct-14 Analyzed: 22-Oct-14							
Benzene	19.1	0.10	mg/kg	20.0		95.6	75-125			
Toluene	19.4	0.10	"	20.0		96.8	70-125			
Ethylbenzene	19.4	0.10	"	20.0		97.3	75-125			
p,m-Xylene	39.3	0.20	"	40.0		98.3	80-125			
o-Xylene	19.3	0.10	"	20.0		96.7	75-125			
Surrogate: 4-Bromochlorobenzene-PID	0.379		"	0.400		94.8	50-150			

Matrix Spike (1443027-MS1)			Source: P410088-01	Prepared: 21-Oct-14 Analyzed: 22-Oct-14						
Benzene	20.8	0.10	mg/kg	19.9	0.51	102	75-125			
Toluene	21.9	0.10	"	19.9	2.04	99.9	70-125			
Ethylbenzene	24.4	0.10	"	19.9	3.70	104	75-125			
p,m-Xylene	62.0	0.20	"	39.9	21.9	101	80-125			
o-Xylene	22.7	0.10	"	19.9	2.41	102	75-125			
Surrogate: 4-Bromochlorobenzene-PID	0.393		"	0.399		98.7	50-150			

Matrix Spike Dup (1443027-MSD1)			Source: P410088-01	Prepared: 21-Oct-14 Analyzed: 22-Oct-14						
Benzene	20.6	0.10	mg/kg	19.9	0.51	101	75-125	0.995	15	
Toluene	21.8	0.10	"	19.9	2.04	99.2	70-125	0.618	15	
Ethylbenzene	23.1	0.10	"	19.9	3.70	97.2	75-125	5.38	15	
p,m-Xylene	60.1	0.20	"	39.9	21.9	95.9	80-125	3.14	15	
o-Xylene	22.8	0.10	"	19.9	2.41	102	75-125	0.239	15	
Surrogate: 4-Bromochlorobenzene-PID	0.396		"	0.399		99.4	50-150			

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.



BP America Production Co.	Project Name:	GCU 200E	Reported: 24-Oct-14 10:23
PO Box 22024	Project Number:	94034-0011	
Tulsa OK, 74121-2024	Project Manager:	Jeff Blagg	

Nonhalogenated Organics by 8015 - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit	Notes
Batch 1443026 - DRO Extraction EPA 3550M										
Blank (1443026-BLK1)				Prepared: 21-Oct-14 Analyzed: 22-Oct-14						
Diesel Range Organics (C10-C28)	ND	24.9	mg/kg							
Surrogate: o-Terphenyl	39.9		"	39.9		100	50-200			
LCS (1443026-BS1)				Prepared: 21-Oct-14 Analyzed: 22-Oct-14						
Diesel Range Organics (C10-C28)	471	24.9	mg/kg	498		94.5	38-132			
Surrogate: o-Terphenyl	40.8		"	39.9		102	50-200			
Matrix Spike (1443026-MS1)				Source: P410088-01		Prepared: 21-Oct-14 Analyzed: 22-Oct-14				
Diesel Range Organics (C10-C28)	510	29.9	mg/kg	499	43.1	93.7	38-132			
Surrogate: o-Terphenyl	39.5		"	39.9		99.0	50-200			
Matrix Spike Dup (1443026-MSD1)				Source: P410088-01		Prepared: 21-Oct-14 Analyzed: 22-Oct-14				
Diesel Range Organics (C10-C28)	493	29.9	mg/kg	499	43.1	90.2	38-132	3.46	20	
Surrogate: o-Terphenyl	40.8		"	39.9		102	50-200			

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.

5796 US Highway 64, Farmington, NM 87401

Three Springs • 65 Mercado Street, Suite 115, Durango, CO 81301

Ph (505) 632-0615 Fx (505) 632-1865

Ph (970) 259-0615 Fr (800) 362-1879

envirotech-inc.com

laboratory@envirotech-inc.com



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 94034-0011
Project Manager: Jeff Blagg

Reported:
24-Oct-14 10:23

Nonhalogenated Organics by 8015 - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit	Notes
Batch 1443027 - Purge and Trap EPA 5030A										
Blank (1443027-BLK1)				Prepared: 21-Oct-14 Analyzed: 22-Oct-14						
Gasoline Range Organics (C6-C10)	ND	9.97	mg/kg							
Surrogate: 4-Bromochlorobenzene-FID	0.345		"	0.399		86.4	50-150			
LCS (1443027-BS1)				Prepared: 21-Oct-14 Analyzed: 22-Oct-14						
Gasoline Range Organics (C6-C10)	272	9.99	mg/kg	292		93.2	80-120			
Surrogate: 4-Bromochlorobenzene-FID	0.344		"	0.400		86.0	50-150			
Matrix Spike (1443027-MS1)				Source: P410088-01		Prepared: 21-Oct-14 Analyzed: 22-Oct-14				
Gasoline Range Organics (C6-C10)	725	9.96	mg/kg	291	453	93.5	75-125			
Surrogate: 4-Bromochlorobenzene-FID	0.348		"	0.399		87.3	50-150			
Matrix Spike Dup (1443027-MSD1)				Source: P410088-01		Prepared: 21-Oct-14 Analyzed: 22-Oct-14				
Gasoline Range Organics (C6-C10)	708	9.97	mg/kg	291	453	87.7	75-125	2.35	15	
Surrogate: 4-Bromochlorobenzene-FID	0.349		"	0.399		87.6	50-150			

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.

5796 US Highway 64, Farmington, NM 87401

Three Springs • 65 Mercado Street, Suite 115, Durango, CO 81301

Ph (505) 632-0615 Fx (505) 632-1865

Ph (970) 259-0615 Fr (800) 362-1879

envirotech-inc.com

laboratory@envirotech-inc.com



BP America Production Co.
PO Box 22024
Tulsa OK, 74121-2024

Project Name: GCU 200E
Project Number: 94034-0011
Project Manager: Jeff Blagg

Reported:
24-Oct-14 10:23

Cation/Anion Analysis - Quality Control

Envirotech Analytical Laboratory

Analyte	Result	Reporting Limit	Units	Spike Level	Source Result	%REC	%REC Limits	RPD	RPD Limit	Notes
Batch 1443036 - Anion Extraction EPA 300.0										
Blank (1443036-BLK1)				Prepared & Analyzed: 22-Oct-14						
Chloride	ND	9.90	mg/kg							
LCS (1443036-BS1)				Prepared & Analyzed: 22-Oct-14						
Chloride	497	10.0	mg/kg	500		99.4	90-110			
Matrix Spike (1443036-MS1)				Source: P410095-01		Prepared & Analyzed: 22-Oct-14				
Chloride	486	9.81	mg/kg	490	ND	99.0	80-120			
Matrix Spike Dup (1443036-MSD1)				Source: P410095-01		Prepared & Analyzed: 22-Oct-14				
Chloride	488	9.83	mg/kg	491	ND	99.2	80-120	0.390	20	

Partial or incomplete reproduction of this report is prohibited, unless approved by Envirotech, Inc.

5796 US Highway 64, Farmington, NM 87401

Three Springs • 65 Mercado Street, Suite 115, Durango, CO 81301

Ph (505) 632-0615 Fx (505) 632-1865

Ph (970) 259-0615 Fr (800) 362-1879

envirotech-inc.com

laboratory@envirotech-inc.com

CHAIN OF CUSTODY RECORD

17910

Client: <u>BLAGG Engineering</u> <u>BP America</u>			Project Name / Location: <u>GCU 200E</u>			ANALYSIS / PARAMETERS														
Email results to: <u>Jeff Blagg & Jeff Peace</u>			Sampler Name: <u>J. Blagg</u>			TPH (Method 8015)	BTEX (Method 8021)	VOC (Method 8260)	RCRA 8 Metals	Cation / Anion	RCI	TCLP with H/P	CO Table 910-1	TPH (418.1)	CHLORIDE			Sample Cool	Sample Intact	
Client Phone No.: <u>505-320-1183</u>			Client No.: <u>08143-0424</u> 94034-0011																	
Sample No. / Identification	Sample Date	Sample Time	Lab No.	No./Volume of Containers	Preservative															
					HNO ₃	HCl														
NORTH BASE @ 18 1/2' 3-pt comp.	10/22/14	1239	P410095-01	1 x 402				X	X							X			Y	Y
NORTH wall 3-pt 6'-16 1/2'	11	1242	P410095-02	11				X	X							X			Y	Y
Relinquished by: (Signature) <u>Jeff Blagg</u>					Date	Time	Received by: (Signature) <u>[Signature]</u>										Date	Time		
Relinquished by: (Signature) <u>[Signature]</u>					10/22/14	1429	Received by: (Signature)										10/22/14	1429		
Sample Matrix: Soil ☒ Solid ☐ Sludge ☐ Aqueous ☐ Other ☐																				
☐ Sample(s) dropped off after hours to secure drop off area.					 11.6, 9.6, 10.6															
