

District I – (575) 393-6161
1625 N. French Dr., Hobbs, NM 88240
District II – (575) 748-1283
811 S. First St., Artesia, NM 88210
District III – (505) 334-6178
1000 Rio Brazos Rd., Aztec, NM 87410
District IV – (505) 476-3460
1220 S. St. Francis Dr., Santa Fe, NM 87505

OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

WELL API NO. 30-045-29158
5. Indicate Type of Lease STATE <input checked="" type="checkbox"/> FEE <input type="checkbox"/>
6. State Oil & Gas Lease No. VA-1121
7. Lease Name or Unit Agreement Name Marley
8. Well Number 1
9. OGRID Number 006515
10. Pool name or Wildcat Basin Fruitland Coal

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)

1. Type of Well: Oil Well ☐ Gas Well ☒ Other

2. Name of Operator
Dugan Production Corp.

3. Address of Operator
P O Box 420, Farmington, NM 87499-0420 505-325-1821

4. Well Location

Unit Letter N : 1190 feet from the South line and 1450 feet from the West line
Section 36 Township 23N Range 9W NMPM San Juan County

11. Elevation (Show whether DR, RKB, RT, GR, etc.)
6640' GL

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
DOWNHOLE COMMINGLE ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ P AND A ☐
CASING/CEMENT JOB ☐

OTHER: ☐

OTHER: TA ☒

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

BP set @ 750'. Dump sand on top of the bridge plug. Hole loaded. Check bradenhead. Check pressure – 0 psi. Pulled gauge. Left valve open 15 mins. Checked csg pressure – 0 psi. BH tested good. Hooked up truck. Pressure casing to 560 psi, tested casing for 30 mins. Ending pressure 550 psi. Test passed. Blew well down. Test witnessed by Paul Wiebe of NMOCD (signed chart).

OIL CONS. DIV DIST. 3

Spud Date:

Rig Release Date:


JUL 31 2015

Future Sundrys include dates work was completed
I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Aliph M. Reena TITLE Production Engineer DATE July 27, 2015

Type or print name Aliph Reena E-mail address: aliph.reena@duganproduction.com PHONE: 505-325-1821
For State Use Only

APPROVED BY: Bob Roll TITLE DEPUTY OIL & GAS INSPECTOR DATE 8-11-15
Conditions of Approval (if any): AV

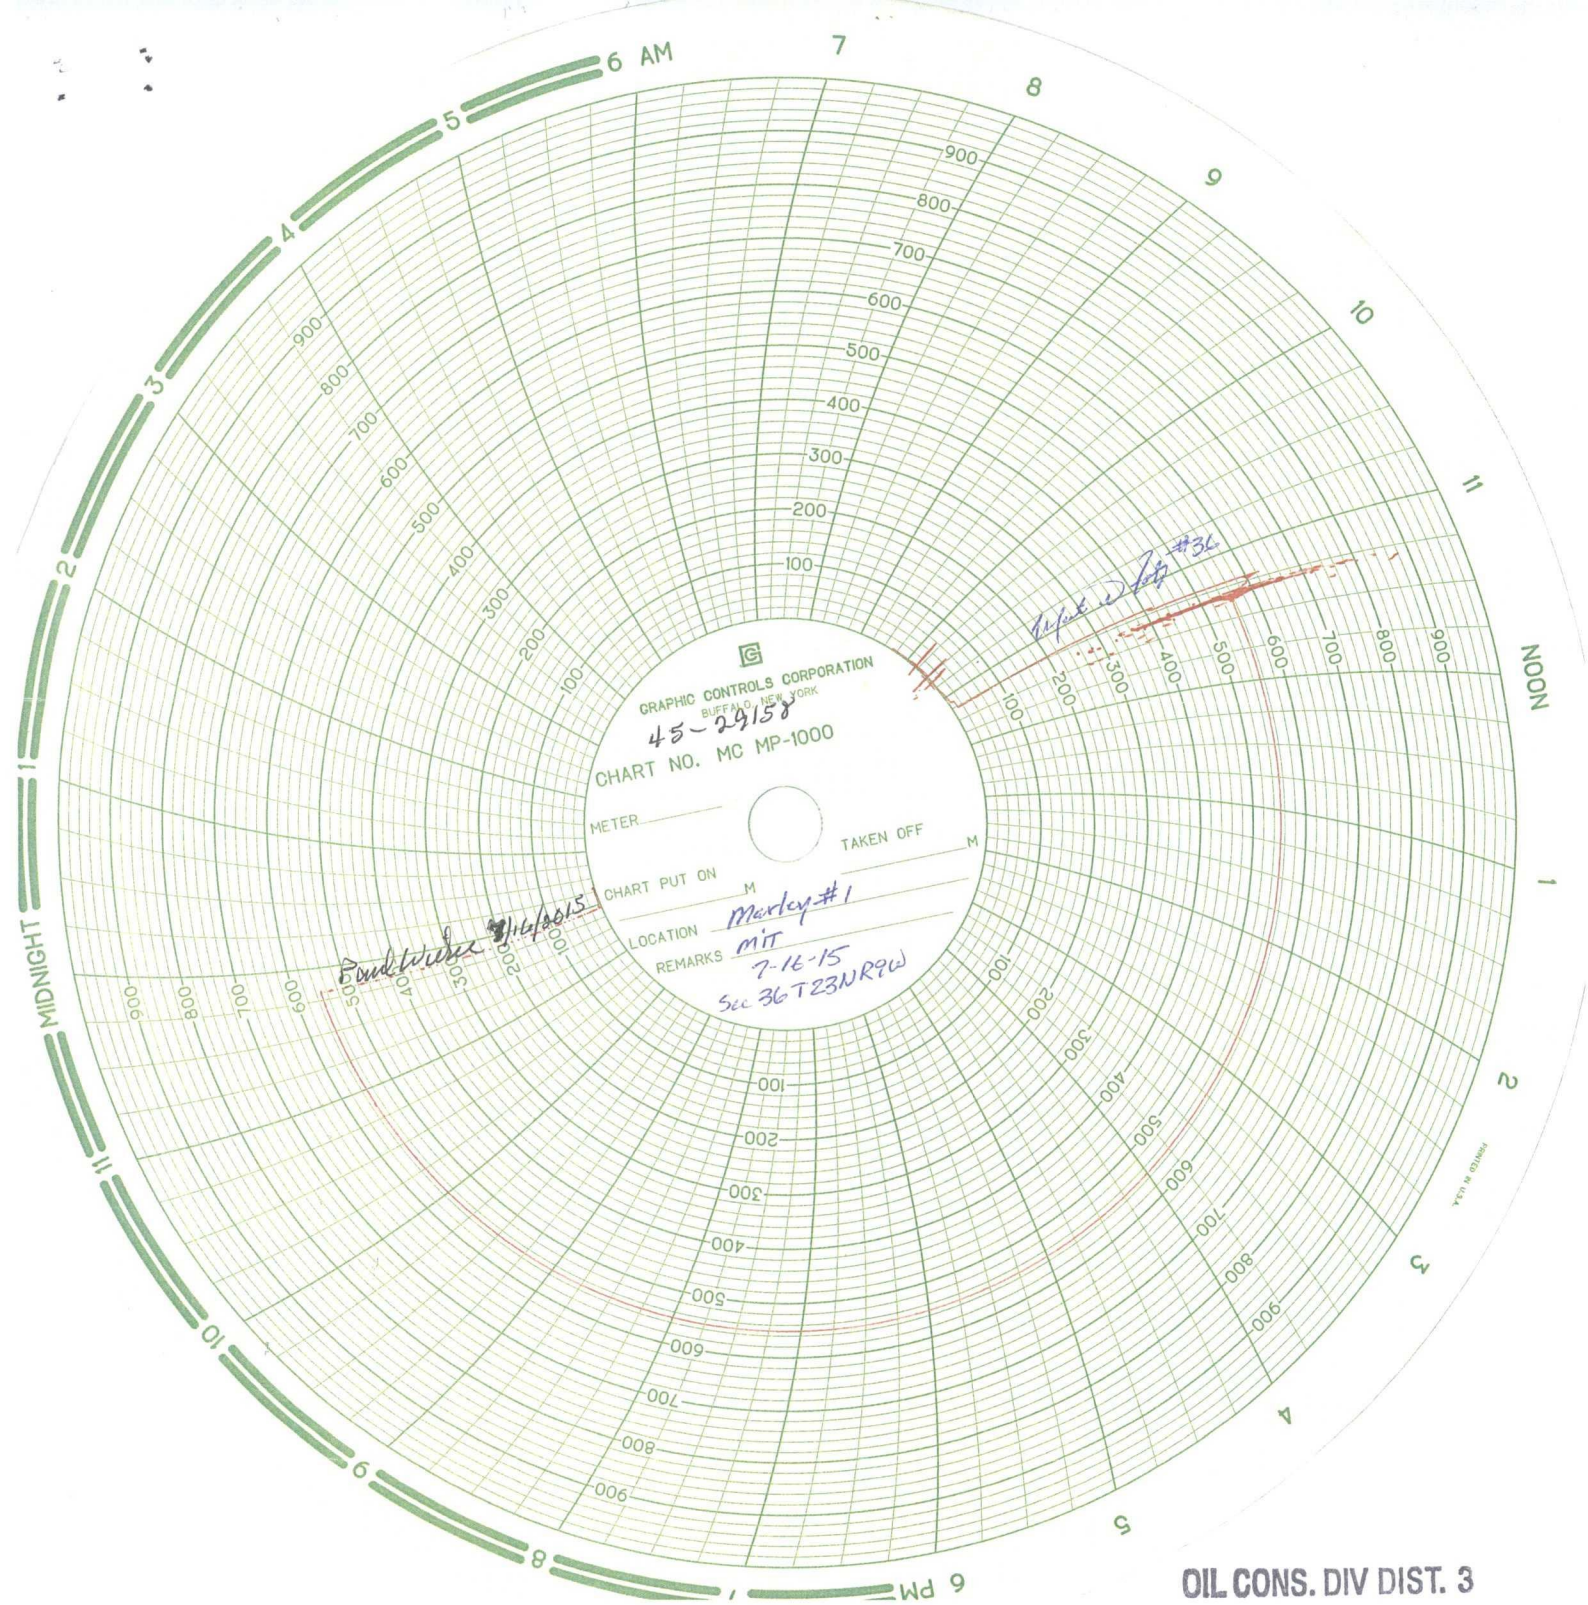

OIL CONS. DIV DIST. 3

JUL 31 2015
