

**NM 32-11 COM #1C
BLANCO MV/BASIN DK**

Spud Date 03-06-05
Completed 07-23-05
1st Delivered 08-05-05 MV
08-09-05 DK

Location: 1920' FSL & 805' FWL
NW/4 SW/4 Section 20(L), T32N, R11W
San Juan Co., NM


Elevation: 6639' GR
(API #: 30-045-32804)

<i>Tops</i>	<i>Depth</i>
Kirtland	1337'
Pictured Cliffs	3266'
Cliff House	5049'
Menefee	5212'
Point Lookout	5611'
Mancos	6149'
Dakota	7780'

Cliff House/Menefee 4821' - 5534' (83, 0.38" holes)
18,880# 14/30 LiteProp 125 & 4080# 20/40 brown sand
carried in slick water.

Point Lookout 5587' - 5902' (41, 0.38" holes) 9940# 14/30
LiteProp 125 & 4480# 20/40 brown sand carried in slick
water.

Dakota 7781' - 7998' (25, 0.32" holes) 60,160 bbls 20/40
Carbolite & 1326 bbls 60Q linked gel.

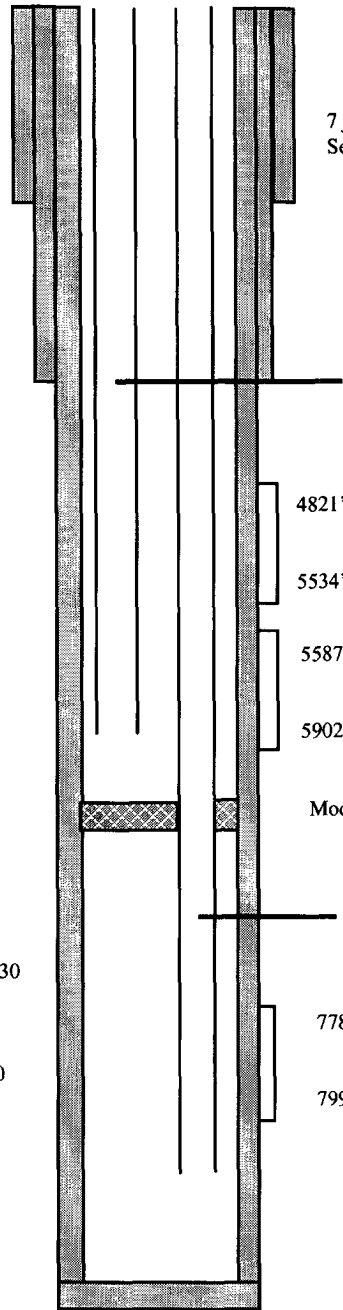

7 jts of 10 3/4", 45.5#, K-55, ST&C csg.
Set @ 320'.

61 jts of 7-5/8", 29.7#, P-110, LT&C csg. Set @
3848'.

Mesaverde Tubing: 1 jt tbg, SN @ 5883' & 185 jts tbg.
Landed @ 5889' (186 jts 2-1/16", 3.25#, J-55 tbg total)

4821'

5534'

5587'

5902'

Model "D" packer @ 6000'

Dakota Tubing: 1/2" mule shoe, 1.25" SN, 50
jts tbg, seal assembly, 190 jts tbg. Landed @
7549'. (240 jts 2-1/16", 3.25#, J-55 tbg total)

7781'

7998'

176 jts of 5-1/2", 17#, I-80 csg. Set @
7767', float collar @ 7747', marker jts @
7299' & 5061'.

TD @ 8069'
PBTd @ 8040'

<i>HOLE SIZE</i>	<i>CASING</i>	<i>CEMENT</i>	<i>CU. FT.</i>	<i>CMT TOP</i>
14 3/4"	10 3/4"	360 s xs	296 cu.ft.	surface
9 7/8"	7 5/8"	665 s xs	1332 cu.ft.	surface
6 3/4"	5 1/2"	285 s xs	635 cu.ft.	2360'
