



NEW MEXICO ENERGY, MINERALS and
NATURAL RESOURCES DEPARTMENT

MECHANICAL INTEGRITY TEST REPORT

(TA OR UIC)

Date of Test 11-7-07 Operator Burlington Res. API # 30-0 45-06180

Property Name Huerfano Unit Well # 82 Location: Unit D Sec 33 Twn 27 Rge 10

Land Type:

State _____
Federal ☒
Private _____
Indian _____

Well Type:

Water Injection _____
Salt Water Disposal _____
Gas Injection _____
Producing Oil/Gas ☒
Pressure observation _____

Temporarily Abandoned Well (YN): _____ TA Expires: 11-7-2012

DIST. 3

Casing Pres. 0
Bradenhead Pres. 0
Tubing Pres. 0
Int. Casing Pres. N/A

Tbg. SI Pres. _____
Tbg. Inj. Pres. _____

Max. Inj. Pres. _____
OIL CONS. DIV.

RCVD NOV 7 '07

Pressured annulus up to 620 psi. for 30 mins. Test passed failed

REMARKS: Rose to 622 then held.


Cast iron bridge plug set at 1748

By [Signature]
(Operator Representative)

Witness [Signature]
(NMOCD)

(Position)

Revised 02-11-02

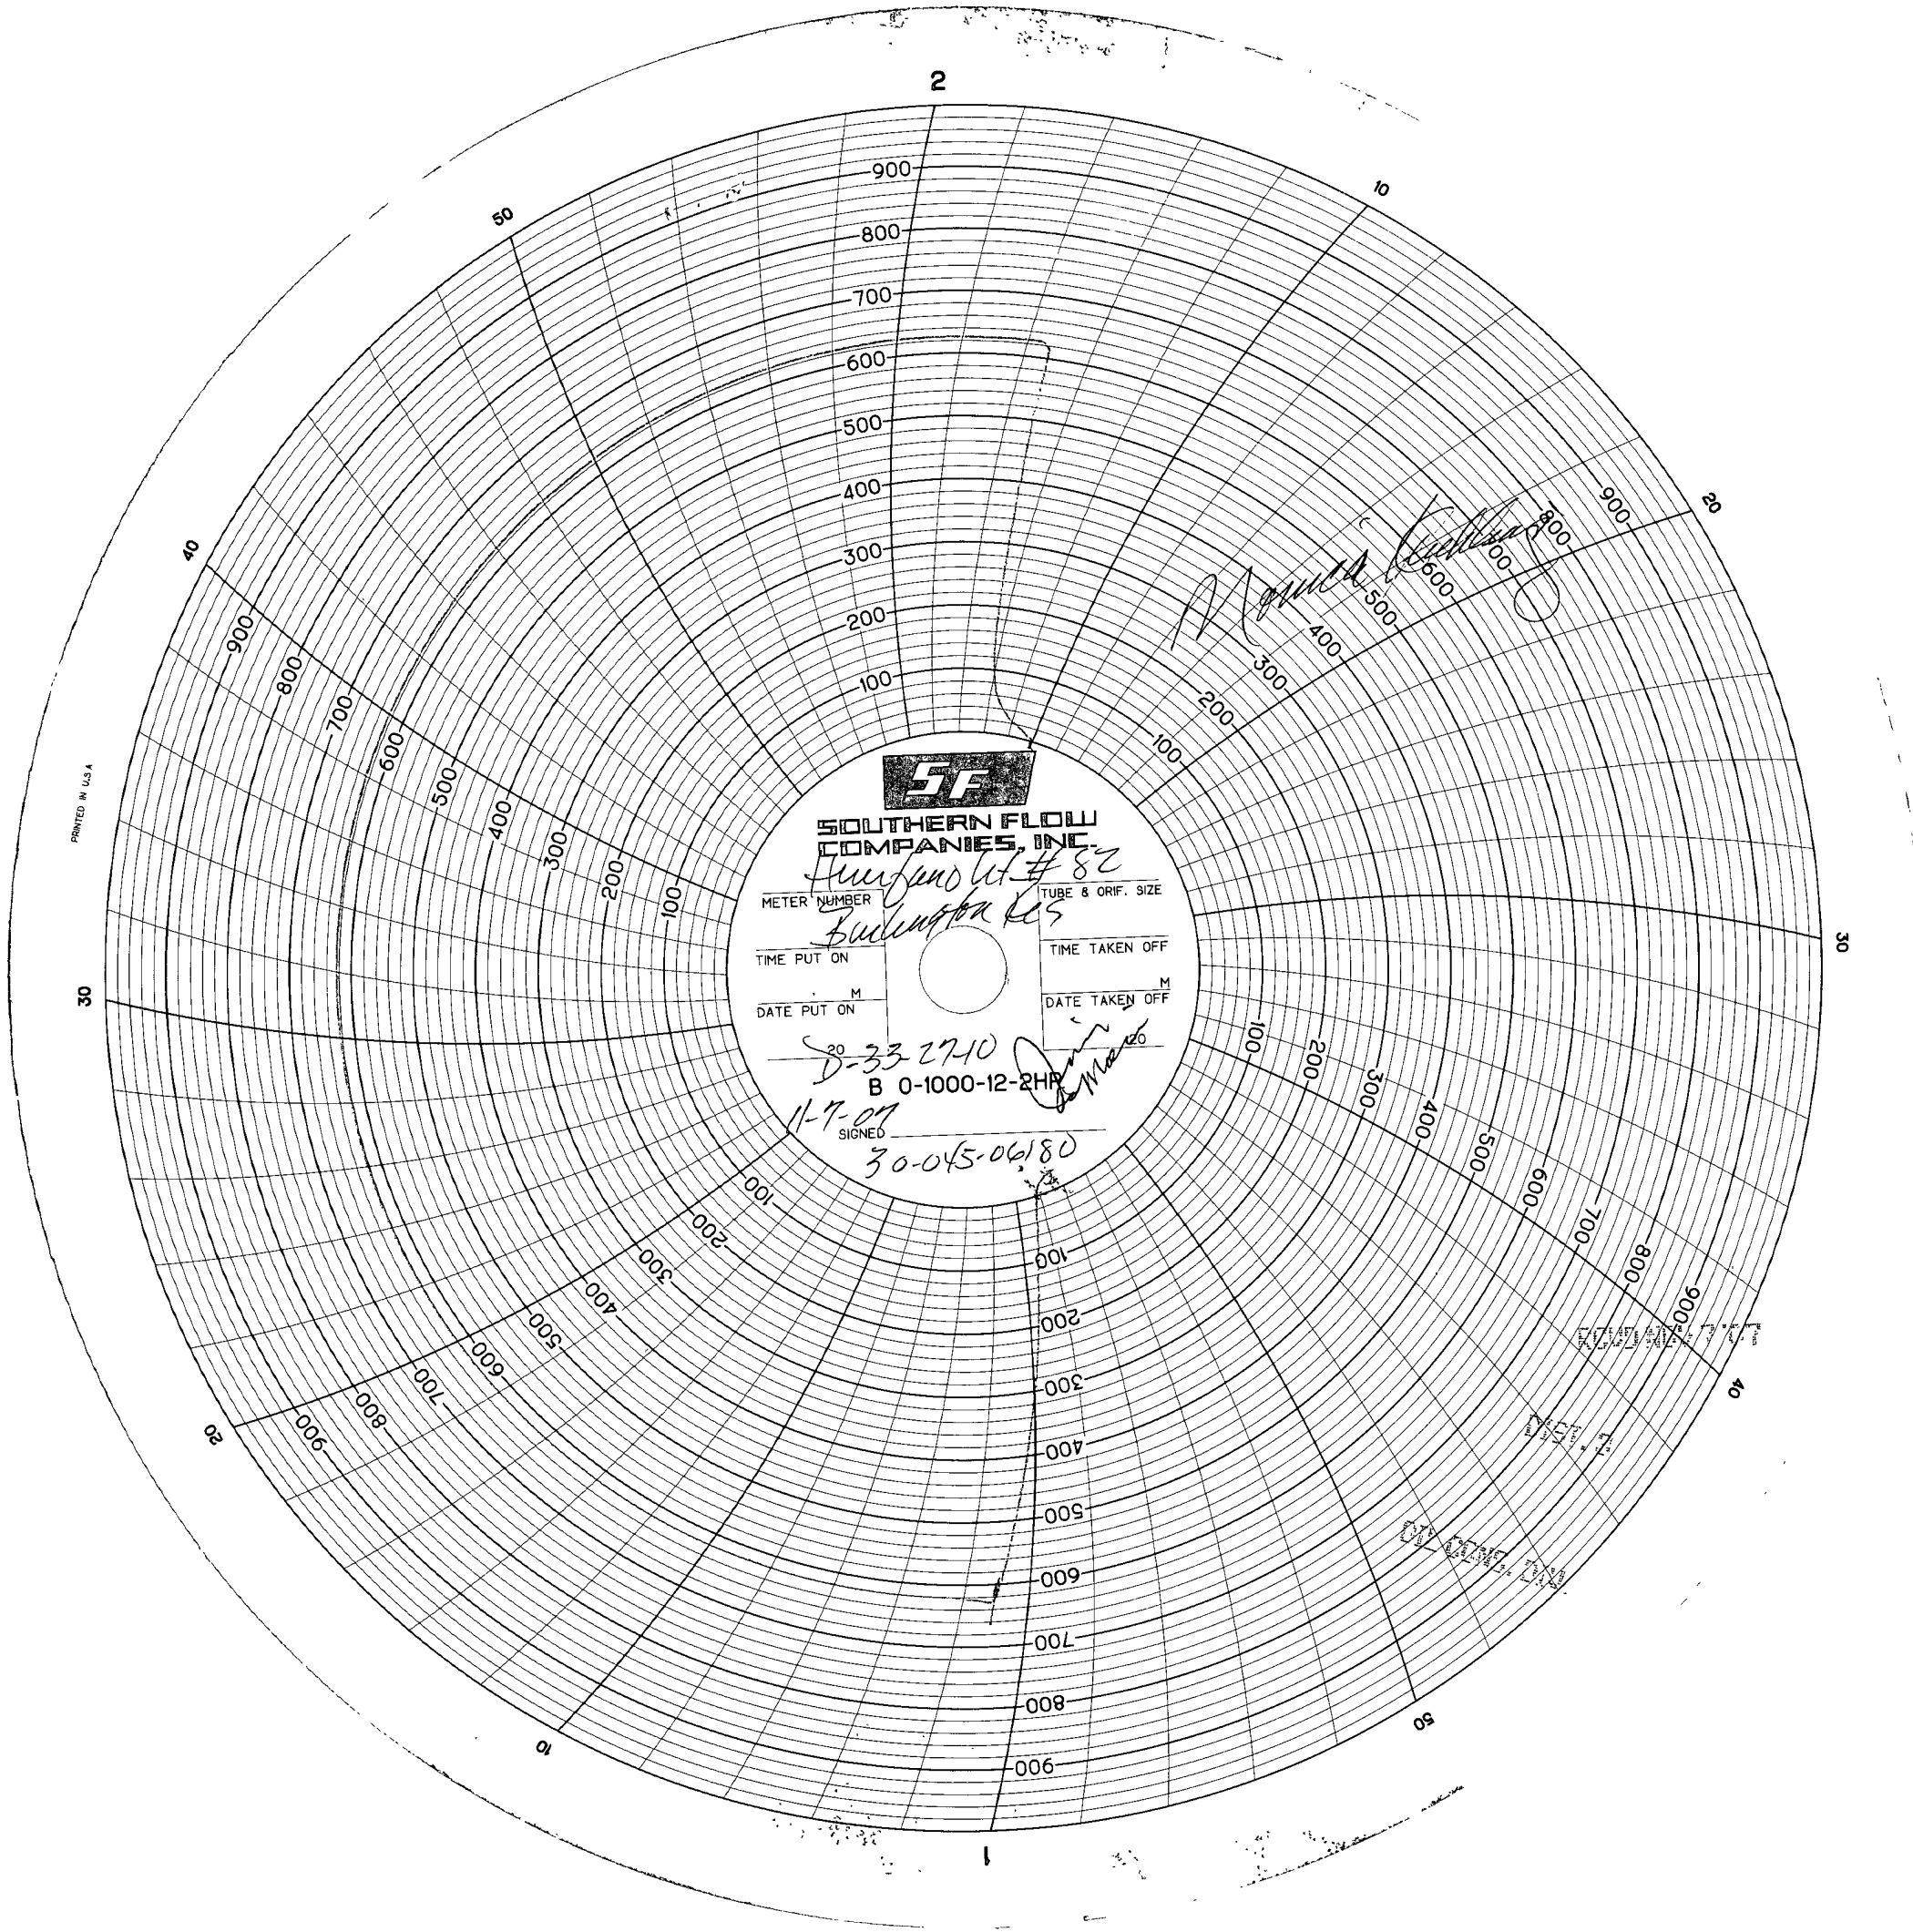

SF
SOUTHERN FLOW
COMPANIES, INC.
METER NUMBER *30-045-06180*
TUBE & ORIF. SIZE *B 0-1000-12-2HR*
TIME PUT ON *11-7-07* DATE PUT ON *11-7-07*
TIME TAKEN OFF DATE TAKEN OFF
SIGNED *[Signature]*

PRINTED IN U.S.A.
