

Aztec NM 87410

DEC 17 1998

Energy, Minerals and Natural Resources Department

2040 S. PACHECO

Santa Fe, New Mexico 87505

Submit 1 copy to

Appropriate District

and 1 copy to

Santa Fe Office

RECEIVED
MAR 6 1969

JUL 6 1998

PIT REMEDIATION AND CLOSURE REPORT

~~ONE MORE DAY.~~
PAGE 3

Operator: **Apache Corporation** Telephone: **505-325-0318**

Address: 2855 Southside River Road, Suite A, Farmington, NM 87401

Facility or Well Name: Apache # 103

Location:	Unit or Qtr/Qtr	Sec	E	Sec 3	T 24 N	R 4W	County	Rio Arriba
-----------	-----------------	-----	---	-------	--------	------	--------	------------

Pit Type:	Separator:	XX	Dehydrator	Other
-----------	------------	-----------	------------	-------

Land Type: Jicarilla Tribal

Beginning Pit Dimensions: Length **20'** Width **42'** Depth **5'**

Pit Location: _____ Ending Pit Dimensions: Length 23' Width 48' Depth 10'
(Attach diagram)

Reference: Wellhead **XXX** Other

Footage from reference: 110'

Direction from reference: 124 Degrees XX East North
of
West South XX


Depth To Groundwater:	Less than 50 feet	(20 points)	_____
(vertical distance from	50 feet to 99 feet	(10 points)	_____
contaminants to seasonal	Greater than 100 feet	(0 points)	<u>0</u>
high water elevation of			
groundwater)			

Wellhead Protection Area:	Yes	(20 points)	<u> </u>
(Less than 200 feet from a private domestic water source, or; less than 1000 feet from all other water sources)	No	(0 points)	<u> 0 </u>

Distance To Surface Water:	Less than 200 feet	(20 points)	<u> </u>
(Horizontal distance to perennial	200 feet to 1000 feet	(10 points)	<u> </u>
lakes, ponds, rivers, streams, creeks,	Greater than 1000 feet	(0 points)	<u> 0 </u>
irrigation canals and ditches)			

RANKING SCORE (TOTAL POINTS) 0

Date Remediation Started:		<u>12/3/95</u>		Date Completed:		<u>12/14/95</u>	
Remediation Method: (Check all appropriate sections)		Excavation <u>XXX</u>		Approx. cubic yards		<u>253</u>	
		Landfarmed <u>XX</u>		Insitu Bioremediation			
		Other _____					
Remediation Location: (i.e. landfarmed onsite, name and location of offsite facility)		Onsite <u>XX</u>		Offsite _____			
General Description of Remedial Action:		<u>Excavate pit to 10', took PID readings.</u>					
		<u>Spread soil on location for remediation. Took soil samples. Pit back filled w/ fill dirt</u>					

Groundwater Encountered:		No <u>XX</u>		Yes _____		Depth _____	
Final Pit:		Sample location		<u>5 point composite taken from pit sidewalls and pit bottom center</u>			
Closure Sampling: (in multiple samples, attach sample results and diagram of sample locations and depths)		Sample depth <u>10'</u>		<u>8 to 10" into pit sidewalls 10" into pit bottom</u>			
		Sample Date		<u>12/14/95</u>		Sample Time <u>3:20 P.M.</u>	
		Sample results					
		Benzene		(ppm)		<u>ND</u>	
		Total BTEX		(ppm)		<u>ND</u>	
		Field Headspace		(ppm)		<u>9.32</u>	
		TPH				<u>550</u>	
Groundwater Sample:		Yes _____		No <u>XX</u>		(If yes attach sample results)	
I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND BELIEF.							
DATE		<u>June 8, 1998</u>		PRINTED NAME		<u>Jeff Cross</u>	
SIGNATURE		<u></u>		AND TITLE		<u>Project Manager</u>	

JICARILLA APACHE TRIBE
ENVIRONMENTAL PROTECTION OFFICE
P. O. BOX 507
DULCE, NEW MEXICO 87528

Submit 1 copy to
Natural Resource Dept.
and Oil & Gas Administration

PIT REMEDIATION AND CLOSURE REPORT

Operator: <u>APACHE CORPORATION</u>		Telephone <u>505-325-0318</u>	
Address: <u>2855 SOUTHSIDE RIVER ROAD / SUITE A / FARMINGTON N.M. 87401-7947</u>			
Facility or Well Name: <u>APACHE # 103</u>			
Location:	Unit or Qtr/Qtr	Sec <u>E</u>	SEC 3 T 24N R 4W County <u>RIO ARRIBA</u>
Pit Type:	Separator: <u>XX</u>	Dehydrator	Other
Land Type:	<u>JIC. TRIBAL</u>		
Pit Location: (Attach diagram)	Pit Dimensions:	Length <u>23'</u>	Width <u>48'</u> Depth <u>10'</u>
	Reference:	Wellhead <u>XXX</u>	Other
	Footage from reference:	<u>110'</u>	
	Direction from reference:	<u>124</u> Degrees <u>XX</u> East	North
		West	South <u>X</u>
Depth To Groundwater: (vertical distance from contaminants to seasonal high water elevation of groundwater)	Less than 50 feet	(20 points)	
	50 feet to 99 feet	(10 points)	
	Greater than 100 feet	(0 points)	<u>0</u>
Distance to an Ephemeral Stream: (Downgradient dry wash greater than ten feet in width)	Less than 100 feet	(10 points)	
	Greater than 100 feet	(0 points)	<u>0</u>
Distance to Nearest Lake, Playa, or Watering Pond: (Downgradient lakes, playas and livestock or wildlife watering ponds)	Less than 100 feet	(10 points)	
	Greater than 100 feet	(0 points)	<u>0</u>
Wellhead Protection Area: (Less than 200 feet from a private domestic water source, or less than 1000 feet from all other water sources)	Yes	(20 points)	
	No	(0 points)	<u>0</u>
Distance To Surface Water: (Horizontal distance to perennial lakes, ponds, rivers, streams, creeks, irrigation canals and ditches)	Less than 100 feet	(20 points)	
	100 feet to 1000 feet	(10 points)	
	Greater than 1000 feet	(0 points)	<u>0</u>
	RANKING SCORE (TOTAL POINTS)		<u>0</u>

Date Remediation Started: 12/3/95 Date Completed: 12/14/95

Remediation Method: (Check all appropriate sections)
Excavation XXX Approx. cubic yards 253
Landfarmed XX Insitu Bioremediation _____
Other _____

Remediation Location: (i.e. landfarmed onsite, name and location of offsite facility)
Onsite XX Offsite _____

General Description of Remedial Action: Excavate pit to 10', took PID readings. spread soil on location for remediation. Took soil samples. Pit Back Filled w/ Fill Dirt

Groundwater Encountered: No XXX Yes _____ Depth _____

Final Pit: Sample location 5 point composite taken from pit sidewalls and pit bottom center.

Closure Sampling:

(in multiple samples, attach sample results and diagram of sample locations and depths)

Sample depth 10' 8" to 10" into pit side walls, 10" into pit bottom.

Sample Date 12/14/95 Sample Time 3:20PM
Sample results

Soil:	Benzene	(ppm)	<u>ND</u>	Water:	Benzene	(ppb)	<u>NA</u>
	Total BTEX	(ppm)	<u>ND</u>		Toluene	(ppb)	<u>NA</u>
	Field Headspace	(ppm)	<u>9.32</u>		Ethylbenzene	(ppb)	<u>NA</u>
	TPH	(ppm)	<u>550</u>		Total Xylenes	(ppb)	<u>NA</u>

Groundwater Sample: Yes _____ No XXX (If yes attach sample results)

I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND BELIEF.

DATE 5/26/98 PRINTED NAME JEFF CROSS
SIGNATURE Jeff Cross AND TITLE PROJECT MANAGER

AFTER REVIEW OF THE PIT CLOSURE INFORMATION, PIT CLOSURE IS APPROVED IN ACCORDANCE TO THE JICARILLA APACHE TRIBE PIT CLOSURE ORDINANCE.

APPROVED: YES X NO _____ (REASON) _____

SIGNED: Lee C Mammall DATE: 6-2-98



SAMPLE DATE 12/14/95

[illegible]

APACHE CORPORATION FARMINGTON DISTRICT
PIT EXCAVATION AND CLOSURE REPORT

LOCATION: APACHE 103

PIT COUNT: 1

JICARILLA APACHE TRIBAL EPO
REVIEW AND APPROVAL

EPO REPRESENTATIVE KCM

DATE OF REVIEW: 12-27-95

		EXCAVATION							
DIMENSIONS		START			FINISH				
	W	L	D		W	L	D	CU.YDS.	
PIT 1	42'	20'	5'	PIT 1	48'	23'	10'	253.0	
PIT 2				PIT 2					
PIT 3				PIT 3					
DATE: 12/03/95		PIT1@10'	PIT2@_'	PIT3@_'	DATE:	PIT1@_'	PIT2@_'	PIT3@_'	
P. I. D.	CENTER	46.9			P. I. D.	CENTER			
	NW CORNER	15.8				NW CORNER			
	NE CORNER	161.0				NE CORNER			
	SW CORNER	33.3				SW CORNER			
	SE CORNER	150.0				SE CORNER			

NOTES:

12/03/95 - Black to lt. gray staining to 9', cleared @ 10'

SOIL SAMPLING

DATE: 12/03/95		PIT1@10'	PIT2@	PIT3@	ANALYSIS RESULTS			PER LAB:	ASSAIGAI
	CENTER	46.9			PIT	TPH	BETEX	WITNESS	DATE
P.	NW CORNER	15.8			NO.				
I.	NE CORNER	161.0			1	ND	1.6	IF&S	12/03/95
D.	SW CORNER	33.3			2				
	SE CORNER	150.0			3				

RE-SAMPLE OR CELL(S) SAMPLE

DATE: 12/14/95		PIT1@10'	PIT2@	PIT3@	ANALYSIS RESULTS			PER LAB:	ASSAIGAI
	CENTER	1.9			PIT	TPH	BETEX	WITNESS	DATE
P.	NW CORNER	1.5			NO.				
I.	NE CORNER	6.2			1	550	ND	JDT	12/14/95
D.	SW CORNER	4.8			2				
	SE CORNER	32.2			3				

RE-SAMPLE OR CELL(S) SAMPLE

DATE:		PIT 1	PIT 2	PIT 3	ANALYSIS RESULTS			PER LAB:	
	CENTER				PIT	TPH	BETEX	WITNESS	DATE
P.	NW CORNER				NO.				
I.	NE CORNER				1				
D.	SW CORNER				2				
	SE CORNER				3				

Lab ID: 9512195-07A
Sample ID: AP #154

Collected: 12/14/95 15:05:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A						
Ethylbenzene	ND	mg/Kg	0.0010	100	12/27/95	SBTXME097
P-&m-Xylene	ND	mg/Kg	0.0010	100	12/27/95	SBTXME097
O-Xylene	ND	mg/Kg	0.0010	100	12/27/95	SBTXME097

Lab ID: 9512195-07B
Sample ID: AP #154

Collected: 12/14/95 15:05:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
HCs DIESEL/CAL DHS 8015M						
Diesel	840	mg/Kg	5.0	100	01/05/96	SLFTD57
HCs DSL XT/CAL DHS 8015M	12/21/95	N/A				

Lab ID: 9512195-08A
Sample ID: AP #103*

Collected: 12/14/95 15:20:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A						
Benzene	ND	mg/Kg	0.0010	50	12/27/95	SBTXME097
Toluene	ND	mg/Kg	0.0010	50	12/27/95	SBTXME097
Ethylbenzene	ND	mg/Kg	0.0010	50	12/27/95	SBTXME097
P-&m-Xylene	ND	mg/Kg	0.0010	50	12/27/95	SBTXME097
O-Xylene	ND	mg/Kg	0.0010	50	12/27/95	SBTXME097

Lab ID: 9512195-08B
Sample ID: AP #103*

Collected: 12/14/95 15:20:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
HCs DIESEL/CAL DHS 8015M						
Diesel	550	mg/Kg	5.0	100	01/05/96	SLFTD57
HCs DSL XT/CAL DHS 8015M	12/21/95	N/A				

Lab ID: 9512195-09A
Sample ID: AP #102-H

Collected: 12/14/95 15:30:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A						
Benzene	ND	mg/Kg	0.0010	50	12/27/95	SBTXME097
Toluene	ND	mg/Kg	0.0010	50	12/27/95	SBTXME097
Ethylbenzene	0.085	mg/Kg	0.0010	50	12/27/95	SBTXME097
P-&m-Xylene	0.23	mg/Kg	0.0010	50	12/27/95	SBTXME097

Lab ID: 9512030-09A
Sample ID: ~~9512030-09A~~


Collected: ~~12/03/95~~ 15:42:00
Matrix: SOIL


TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
HCs DIESEL/CAL DHS 8015M	ND	mg/Kg	5.0	500	12/08/95	SLFTD054
Diesel	12/06/95	N/A				
HCs DSL XT/CAL DHS 8015M						

Lab ID: 9512030-09B
Sample ID: AP #103

Collected: ~~12/03/95~~ 15:42:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A	ND	mg/Kg	0.0010	500	12/07/95	SBTXME094
Benzene	ND	mg/Kg	0.0010	500	12/07/95	SBTXME094
Toluene	ND	mg/Kg	0.0010	500	12/07/95	SBTXME094
Ethylbenzene	1.6	mg/Kg	0.0010	500	12/07/95	SBTXME094
P-&m-Xylene	ND	mg/Kg	0.0010	500	12/07/95	SBTXME094
O-Xylene						


James A. Seely
Operations Manager



ASSAIGAL
ANALYTICAL
LABORATORIES

Chain of Custody Record

7300 JEFFERSON, N.E.
ALBUQUERQUE, NEW MEXICO 87110
(505) 345-8964

3332 WEDGEWOOD
EL PASO, TEXAS 79925
(915) 593-6000

1910 N. BIG SPRING
MIDLAND, TEXAS 79705
(915) 570-1116

Client Apache Corporation

Address 204 N. Behrend

City/State/Zip FARMINGTON, NM 87401

Project Name / Number Oil Remediation - 45617

Contract / Purchase Order / Quote _____

Project Manager / Contact John Taylor

Telephone No. (505) 325-0318

Fax No. (505) 325-0325

Samplers: (Signature) _____

MELQUIADES ALANIS
6411 LOCAL UNO
CIUDAD JUAREZ, CHIHUAHUA MEXICO 32320

ALL FRACTION NUMBER	Field Sample Number / Location	Date	Time	Sample Type	Type / Size of Container	Temp.	Preservation Chemical
07A	AP # 154	12/14	3:05	Soil	4 oz. Glass		JCE
07B	AP # 154		3:05				
08A	AP # 103		3:20				
08B	AP # 103		3:20				
09A	AP # 102-H		3:30				
09B	AP # 102-H		3:30				
10A	AP # 102-C		3:40				
10B	AP # 102-C		3:40				
11A	AP # 123		3:55				
11B	AP # 123		3:55				
12A	AP # 155-H		4:10				
12B	AP # 155-H		4:10				

Relinquished by: Scott Duderstadt
Signature Scott Duderstadt
Printed Scott Duderstadt
Company Indian Fire & Safety
Reason Testing

Received by: John Taylor
Signature John Taylor
Printed John Taylor
Company APC
Reason Testing

Relinquished by: John Taylor
Signature John Taylor
Printed John Taylor
Company APC
Reason Testing

Received by: John Taylor
Signature John Taylor
Printed John Taylor
Company APC
Reason Testing

Relinquished by: John Taylor
Signature John Taylor
Printed John Taylor
Company APC
Reason Testing

Received by: John Taylor
Signature John Taylor
Printed John Taylor
Company APC
Reason Testing

Method of Shipment: _____

Shipment No. _____

Special Instructions: _____

Comments: _____

After analysis, samples are to be:

☐ Disposed of (additional fee)

☐ Stored (30 days max)

☐ Stored over 30 days (additional fee)

☐ Returned to customer

COURIER

GENERAL DRAINAGE

NORTH

APACHE

APACHE NUMBER 103 Lease # JAT 127

SW/4 NW/4 (E)

SECTION 3, TOWNSHIP 24N, RANGE 4W

RIO ARriba COUNTY, NM

Revised 6/1/97 mg

124° ESE

PIT 110' FWH

RECLAIMED


SEPARATOR



WELL HEAD



PUMP JACK

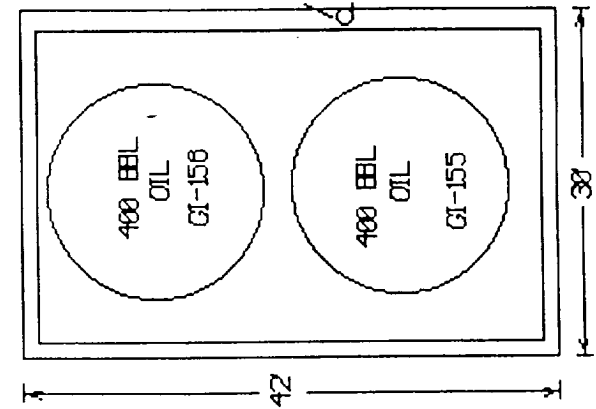

Cell
11' 21' 04' x 11'

4' X 40' ENG METER RUN



ENG LINE DRIP



JICARILLA APACHE TRIBE
ENVIRONMENTAL PROTECTION OFFICE
P. O. BOX 507
DULCE, NEW MEXICO 87528

Submit 1 copy to
Natural Resource Dept.
and Oil & Gas Administration

ON-SITE SOIL REMEDIATION REPORT

Operator: <u>APACHE CORPORATION</u> Telephone <u>505-325-0318</u>	
Address: <u>2855 SOUTHSIDE RIVER ROAD/SUITE A / FARMINGTON , N.M. 87401-7947</u>	
Facility or Well Name: <u>APACHE # 103</u>	
Location: Unit or Qtr/Qtr Sec <u>E</u> Sec <u>3</u> T <u>24N</u> R <u>4W</u> County <u>RIO ARRIBA</u>	
Land Type <u>JIC. TRIBAL</u>	
Date Remediation Started: <u>12/3/95</u> Date Completed: <u>5/12/98</u>	
Remediation Method: Landfarmed <u>XXX</u> Approx. cubic yards <u>253</u>	
Composted _____	
Other _____	
Depth to Groundwater: (pts) <u>0</u>	Final Closure Sampling Sampling Date: <u>5/12/98</u> Time: <u>12:45PM</u> Sample Results: Field Headspace (ppm) <u>0</u> TPH (ppm) <u>830</u> Method <u>M8015</u> Other <u>BTEX \ SW846 , 8020A (ND)</u>
Distance to an Ephemeral Stream: (pts) <u>0</u>	
Distance to Nearest Lake, Playa, or Watering Pond: (pts) <u>0</u>	
Wellhead Protection Area: (pts) <u>0</u>	
Distance To Surface Water: (pts) <u>0</u>	
RANKING SCORE (TOTAL POINTS) <u>0</u>	
I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND BELIEF	
DATE: <u>5/26/98</u> PRINTED NAME <u>JEFF CROSS</u>	
SIGNATURE <u>Jeff Cross</u> TITLE <u>PROJECT MANAGER</u>	
AFTER REVIEW OF THE SOIL REMEDIATION INFORMATION. ON-SITE REMEDIATION IS APPROVED IN ACCORDANCE TO THE JICARILLA APACHE TRIBE PIT CLOSURE ORDINANCE.	
APPROVED: YES <u>X</u> NO _____ (REASON) _____	
SIGNED: <u>[Signature]</u> DATE: <u>6-2-98</u>	

APACHE CORPORATION/FARMINGTON DISTRICT SOIL REMEDIATIONS STATUS REPORT

REMEDIATION SITE APACHE # 103

* AMOUNT OF SOIL UNDERGOING REMEDIATION 253 Yds.

CELL No. <u>1</u>	SampDATE 5/12/98	TPH 830	BTEX ND
DIMENSIONS(LxWxH) <u>110' X 40' X 12"</u>			
CELL LOCATION (dir. from well head) <u>NE</u>			
* DATE BEGAN: <u>12/3/95</u>			
DATE TERMINATED (TPH <5,000 ppm/BTEX< 50 ppm/Benzene < 10 ppm) <u>5/12/98</u>			
CELL No. <u>2</u>	SampDATE	TPH	BTEX
DIMENSIONS(LxWxH)			
CELL LOCATION (dir. from well head)			
* DATE BEGAN:			
DATE TERMINATED (TPH <5,000 ppm/BTEX< 50 ppm/Benzene < 10 ppm)			
CELL No. <u>3</u>	SampDATE	TPH	BTEX
DIMENSIONS(LxWxH)			
CELL LOCATION (dir. from well head)			
* DATE BEGAN:			
DATE TERMINATED (TPH <5,000 ppm/BTEX< 50 ppm/Benzene < 10 ppm)			
REMEDIATION RECORD: (Date, Treatment, Tilling)			
12/5/95 TREAT SOIL WITH 28-4-4 FERTILIZER, PLOW AND TILL SOIL.			
6/23/97 WATER , PLOW AND TILL SOIL.			
8/22/97 TREAT SOIL WITH 22 LBS. PHOSPHORUS, 55 LBS. 46-0-0 FERTILIZER, WATER ,PLOW AND TILL SOIL.			
8/25/97 TILL SOIL.			
5/3/98 PLOW SOIL.			
5/9/98 WATER AND TILL SOIL.			

From excavation reports.

WELL NAME:

Apache #103

SAMPLE DATE:


5-12-98

DIMENSIONS:

110' x 46' x 12"




= SAMPLE AREA

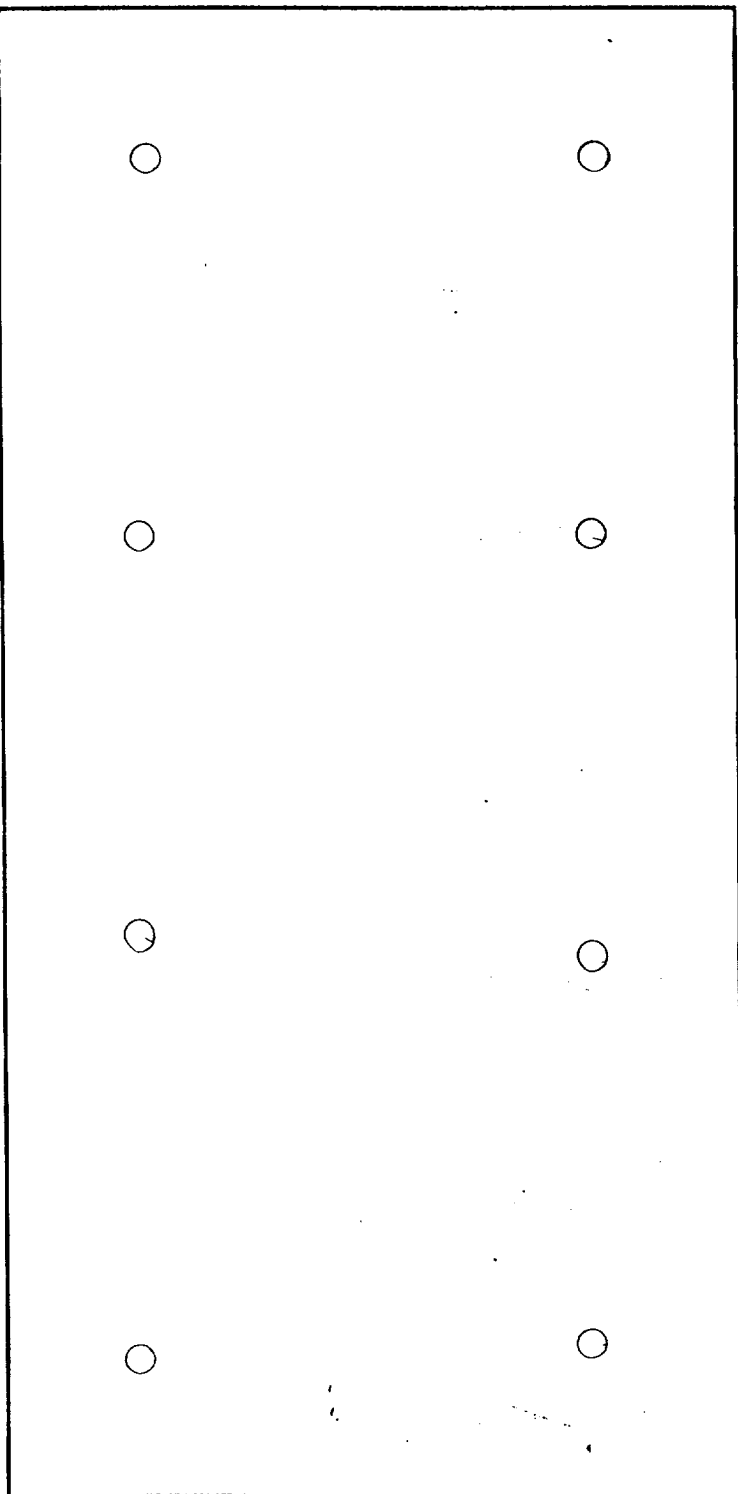

NOTES:

ALL SAMPLES TAKEN 10" TO 12" INTO CELL.

8 point composite sample




ASSAIGAI ANALYTICAL LABORATORIES, INC.

7300 Jefferson, N.E. • Albuquerque, New Mexico 87109 • (505) 345-8964 • FAX (505) 345-7259

3332 Wedgewood, E-5 • El Paso, Texas 79925 • (915) 593-6000 • FAX (915) 593-7820

APACHE CORPORATION
attn: JEFF CROSS
2855 SOUTHSIDE RIVER RD STE A
FARMINGTON, NM 87401-7947



* explanation of codes

B	analyte detected in Method Blank
E	result is estimated
H	analyzed out of hold time
N	tentatively identified compound
S	subcontracted
1-9	see footnote

Assaigai Analytical Laboratories, Inc.

Certificate of Analysis

Client: APACHE CORPORATION
Project: 9805127 JICARILLA PIT CLOSURE


William P. Biava
William P. Biava, President of Assaigai Analytical Laboratories, Inc.

Client Sample ID: APACHE #103 CELL Sample Matrix: SOIL Sample Collected: 05/12/98 12:45:00

Fraction	QC Group	CAS #	Result	Units	Dilution Factor	Detection Limit	* Sequence	Run Date
SW846-8020 Volatiles								
9805127-01A	X98267	71-43-2	Benzene	ND	mg / Kg	50	0.005	XG.1998.464-18 05/14/98
	X98267	100-41-4	Ethylbenzene	ND	mg / Kg	50	0.005	XG.1998.464-18
	X98267	95-47-6	o-Xylene	ND	mg / Kg	50	0.005	XG.1998.464-18
	X98267		p/m Xylenes	ND	mg / Kg	50	0.01	XG.1998.464-18
	X98267	108-88-3	Toluene	ND	mg / Kg	50	0.005	XG.1998.464-18
SW846-8015 Modified TPH								
9805127-01B	X98268		Diesel Range Organics	830	mg / Kg	25	25	XG.1998.465-17 05/15/98

*** Sample specific analytical Detection Limit is determined by multiplying the sample Dilution Factor by the listed method Detection Limit. ***





7300 JEFFERSON, N.E.
ALBUQUERQUE, NEW MEXICO 87109
(505) 345-8964

Lab job no.: 5127 Date 05/15/98

3332 WEDGEWOOD
EL PASO, TEXAS 79925
(915) 593-6000

Page _____ of _____

Client Apache Corporation Project Manager / Contact Jeff Cross

Address 2855 Southside River RD, Ste. A Telephone No. (505) 774-6643

City/State/Zip Parminster, NM 87401-7947 Fax No. (505) 774-6624

Project Name / Number _____

Samplers: (Signature) Jeff Wors

Contract / Purchase Order / Quote _____

[illegible]

Relinquished by: Signature <u>Jeff Uem</u> Printed <u>JEFF UEM</u> Company <u>Apache Corp</u>	Date <u>5-15-98</u> Time <u>9:30</u>	Received by: Signature <u>Scott Pratt</u> Printed <u>SCOTT PRATT</u> Company <u>AAL</u> Reason _____	Relinquished by: Signature <u>Scott Pratt</u> Printed <u>SCOTT PRATT</u> Company <u>AAL</u> Reason _____
--	--	--	--

Date	15 May 98
Time	11:30
Received by: <u>Bob Clark</u>	
Signature <u>Rich Clark</u>	
Printed <u>AAU</u>	
Company <u>Analysis</u>	
Reason <u>Analysis</u>	

After analysis, samples are to be:

☐ Disposed of (additional _____)

☐ Stored (30 days max)

☐ Stored over 30 days (address _____)

☐ Returned to customer

LABORATORY
