

Aztec, NM 87410

Brazos River Energy, Minerals & Chemicals
DEPUTY REGIONAL INSPECTOR

FILED 08/1999

Energy, Minerals and Natural Resources Department

Santa Fe, New Mexico 87505


Submit 1 copy to
~~Appropriate District~~
and 1 copy to
Santa Fe Office

PIT REMEDIATION AND CLOSURE REPORT

Approved

RECEIVED
PORT IN DEC - 8 1983
505-325-0318

Operator:		<u>Apache Corporation</u>		Telephone:		<u>505-325-0318</u>	
Address:		<u>2855 Southside River Road, Suite A, Farmington, NM 87401</u>					
Facility or Well Name:		<u>APACHE 122</u>					
Location:		Unit or Qtr/Qtr	<u>I</u>	Sec	<u>13</u>	T	<u>24 N</u>
		R	<u>4W</u>	County		<u>Rio Arriba</u>	
Pit Type:	Separator:	<u> </u>		Dehydrator	<u> </u>		Other
				<u>Tank Drain</u>		<u> </u>	
Land Type:		<u>Jicarilla Tribal</u>					
Beginning Pit Dimensions:		Length	<u>21'</u>	Width	<u>23'</u>	Depth	<u>6'</u>
Ending Pit Dimensions:		Length	<u>23'</u>	Width	<u>23'</u>	Depth	<u>10'</u>
(Attach diagram)							
Reference:		Wellhead	<u>XXX</u>	Other	<u> </u>		
Footage from reference:		<u>100'</u>					
Direction from reference:		<u>40</u>	Degrees	<u>X</u>	East	North	<u>XX</u>
					West	South	<u> </u>
Depth To Groundwater:		Less than 50 feet		(20 points)	<u> </u>		
(vertical distance from		50 feet to 99 feet		(10 points)	<u> </u>		
contaminants to seasonal		Greater than 100 feet		(0 points)	<u>0</u>		
high water elevation of groundwater)							
Wellhead Protection Area:		Yes		(20 points)	<u> </u>		
(Less than 200 feet from a private domestic water source, or; less than 1000 feet from all other water sources)		No		(0 points)	<u>0</u>		
Distance To Surface Water:		Less than 200 feet		(20 points)	<u> </u>		
(Horizontal distance to perennial lakes, ponds, rivers, streams, creeks, irrigation canals and ditches)		200 feet to 1000 feet		(10 points)	<u> </u>		
		Greater than 1000 feet		(0 points)	<u>0</u>		
RANKING SCORE (TOTAL POINTS)		<u>0</u>					

Date Remediation Started:		<u>10/6/95</u>	Date Completed:		<u>10/6/95</u>
Remediation Method: (Check all appropriate sections)		Excavation <u>XXX</u>	Approx. cubic yards		<u>78</u>
		Landfarmed <u>XX</u>	Insitu Bioremediation		
		Other _____			
Remediation Location: (i.e. landfarmed onsite, name and location of offsite facility)		Onsite <u>XX</u>	Offsite _____		
General Description of Remedial Action: <u>Excavate pit to 10', took PID readings. Backfill pit with</u>					
<u>clean soil. Remediated soil to be spread on location. Spread soil on location for remediation.</u>					
<u>Took soil samples</u>					
Groundwater Encountered: No <u>XX</u> Yes _____ Depth _____					
Final Pit:	Sample location		<u>5 point composite sample taken from pit sidewalls and pit</u>		
Closure Sampling: (in multiple samples, attach sample results and diagram of sample locations and depths)	Sample depth <u>10'</u>		<u>8 to 10" into pit sidewalls 10" into pit bottom</u>		
	Sample Date		Sample Time		<u>1:32 PM</u>
	Sample results				
	Benzene	(ppm)	<u>ND</u>		
	Total BTEX	(ppm)	<u>ND</u>		
	Field Headspace	(ppm)	<u>19.74</u>		
	TPH		<u>840</u>		
Groundwater Sample: Yes _____ No <u>XX</u> (If yes attach sample results)					
I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND BELIEF.					
DATE <u>December 1, 1998</u>		PRINTED NAME		<u>Jeff Cross</u>	
SIGNATURE <u></u>		AND TITLE		<u>Project Manager</u>	

JICARILLA APACHE TRIBE
ENVIRONMENTAL PROTECTION OFFICE
P. O. BOX 507
DULCE, NEW MEXICO 87528

Submit 1 copy to
Natural Resource Dept.
and Oil & Gas Administration

PIT REMEDIATION AND CLOSURE REPORT

Operator: <u>APACHE CORPORATION</u>		Telephone <u>505-325-0318</u>	
Address: <u>2855 Southside River Road, Suite A, Farmington, NM 87401</u>			
Facility or Well Name: <u>APACHE # 122</u>			
Location:	Unit or Qtr/Qtr	Sec	<u>I</u> SEC 13 T 24 N R 4W County <u>Rio Arriba</u>
Pit Type:	Separator: <u> </u>	Dehydrator <u> </u>	Other <u> </u> TANK DRAIN
Land Type: <u>Jicarilla Tribal</u>			

Pit Location: (Attach diagram)	Pit Dimensions:	Length <u>23'</u>	Width <u>23'</u>	Depth <u>10'</u>
	Reference:	Wellhead <u>XX</u>	Other <u> </u>	
	Footage from reference:	<u>100'</u>		
	Direction from reference:	<u>40</u> Degrees	<u>X</u> East	North <u>XX</u> of West South

Depth To Groundwater: (vertical distance from contaminants to seasonal high water elevation of groundwater)	Less than 50 feet	(20 points)	<u> </u>
	50 feet to 99 feet	(10 points)	<u> </u>
	Greater than 100 feet	(0 points)	<u>0</u>
Distance to an Ephemeral Stream: (Downgradient dry wash greater than ten feet in width)	Less than 100 feet	(10 points)	<u> </u>
	Greater than 100 feet	(0 points)	<u>0</u>
Distance to Nearest Lake, Playa, or Watering Pond: (Downgradient lakes, playas and livestock or wildlife watering ponds)	Less than 100 feet	(10 points)	<u> </u>
	Greater than 100 feet	(0 points)	<u>0</u>
Wellhead Protection Area: (Less than 200 feet from a private domestic water source, or less than 1000 feet from all other water sources)	Yes	(20 points)	<u> </u>
	No	(0 points)	<u>0</u>
Distance To Surface Water: (Horizontal distance to perennial lakes, ponds, rivers, streams, creeks, irrigation canals and ditches)	Less than 100 feet	(20 points)	<u> </u>
	100 feet to 1000 feet	(10 points)	<u> </u>
	Greater than 1000 feet	(0 points)	<u>0</u>
	RANKING SCORE (TOTAL POINTS)		<u>0</u>

Date Remediation Started: 10/6/95 **Date Completed:** 10-6-95

Remediation Method:
(Check all appropriate sections)

Excavation XXX Approx. cubic yards 78

Landfarmed XX Insitu Bioremediation _____

Other _____

Remediation Location:
(i.e. landfarmed onsite, name and location of offsite facility)

Onsite XX Offsite _____

General Description of Remedial Action: EXCAVATE PIT TO 10', TOOK PID READINGS. BACK FILL PIT WITH CLEAN SOIL. REMEDIATED SOIL TO BE SPREAD ON LOCATION. SPREAD SOIL ON LOCATION FOR REMEDIATION. TOOK SOIL SAMPLES.

Groundwater Encountered: No X Yes _____ Depth _____

Final Pit: Sample location 5 point composite taken from pit sidewalls , and pit bottom center.

Closure Sampling:
(in multiple samples, attach sample results and diagram of sample locations and depths)

Sample depth 10'

Sample Date 10-6-95 Sample Time 1:32 PM.

Sample results

Soil:	Benzene	(ppm)	<u>ND</u>	Water:	Benzene	(ppb)	<u>NA</u>
	Total BTEX	(ppm)	<u>ND</u>		Toluene	(ppb)	<u>NA</u>
	Field Headspace	(ppm)	<u>19.74</u>		Ethylbenzene	(ppb)	<u>NA</u>
	TPH	(ppm)	<u>840</u>		Total Xylenes	(ppb)	<u>NA</u>

Groundwater Sample: Yes _____ No X (If yes attach sample results)

I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND BELIEF.

DATE 9/30/98 PRINTED NAME JEFF CROSS

SIGNATURE Jeff Cross AND TITLE Project Manager

AFTER REVIEW OF THE PIT CLOSURE INFORMATION, PIT CLOSURE IS APPROVED IN ACCORDANCE TO THE JICARILLA APACHE TRIBE PIT CLOSURE ORDINANCE.

APPROVED: YES X NO _____ (REASON) _____

SIGNED: Kent M. M...ll DATE: 11-13-98

Lab ID: 9510085-07A
Sample ID: AP#121-SH

Collected: 10/05/95 10:40:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A						
Ethylbenzene	ND	mg/Kg	0.0010	5000	10/11/95	SBTXME082
P-&m-Xylene	56	mg/Kg	0.0010	5000	10/11/95	SBTXME082
O-Xylene	19	mg/Kg	0.0010	5000	10/11/95	SBTXME082

Lab ID: 9510085-07B
Sample ID: AP#121-SH

Collected: 10/05/95 10:40:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
HCs DIESEL/CAL DHS 8015M						
Diesel	7600	mg/Kg	5.0	500	10/16/95	SLFTD48
HCs DSL XT/CAL DHS 8015M	10/12/95	N/A				

Lab ID: 9510085-08A
Sample ID: AP#145-H

Collected: 10/05/95 16:40:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A						
Benzene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082
Toluene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082
Ethylbenzene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082
P-&m-Xylene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082
O-Xylene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082

Lab ID: 9510085-08B
Sample ID: AP#145-H

Collected: 10/05/95 16:40:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
HCs DIESEL/CAL DHS 8015M						
Diesel	ND	mg/Kg	5.0	10	10/16/95	SLFTD48
HCs DSL XT/CAL DHS 8015M	10/12/95	N/A				

Lab ID: 9510085-09A
Sample ID: AP#122-H

Collected: 10/06/95 13:32:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A						
Benzene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082
Toluene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082
Ethylbenzene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082
P-&m-Xylene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082

Lab ID: 9510085-09A
Sample ID: AP#122-H

Collected: 10/06/95 13:32:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A O-Xylene	ND	mg/Kg	0.0010	500	10/11/95	SBTXME082

Lab ID: 9510085-09B
Sample ID: AP#122-H

Collected: 10/06/95 13:32:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
HCS DIESEL/CAL DHS 8015M Diesel	840	mg/Kg	5.0	50	10/16/95	SLFTD48
HCS DSL NT/CAL DHS 8015M	10/12/95	N/A				

Lab ID: 9510085-10A
Sample ID: AP#120-H


Collected: 10/09/95 11:20:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
BTEX/SW846 8020A						
Benzene	ND	mg/Kg	0.0010	5000	10/11/95	SBTXME082
Toluene	14	mg/Kg	0.0010	5000	10/11/95	SBTXME082
Ethylbenzene	14	mg/Kg	0.0010	5000	10/11/95	SBTXME082
P-&m-Xylene	67	mg/Kg	0.0010	5000	10/11/95	SBTXME082
O-Xylene	17	mg/Kg	0.0010	5000	10/11/95	SBTXME082

Lab ID: 9510085-10B
Sample ID: AP#120-H

Collected: 10/09/95 11:20:00
Matrix: SOIL

TEST / METHOD	RESULT	UNITS	LIMIT	D_F	DATE ANAL	BATCH_ID
HCS DIESEL/CAL DHS 8015M Diesel	11000	mg/Kg	5.0	250	10/16/95	SLFTD48
HCS DSL NT/CAL DHS 8015M	10/12/95	N/A				


James A. Seely
Operations Manager

3332 WEDGEWOOD
EL PASO, TEXAS 79925
(915) 593-6000

CIUDAD JUÁREZ, CHIHUAHUA MEXICO 32320

Contract / Purchase Order / Quote

AAL FRACTION NUMBER	Field Sample Number/Location	Date	Time	Sample Type	Type / Size of Container	Preservation	
						Temp.	Chemical
1	AP# 121-SH	10/5	10:40	Soil	Glass 402		ICE
2	AP# 121-SH	10/5	10:40				
3	AP# 145-H	10/5	4:40				
4	AP# 145-H	10/5	4:40				
5	AP# 122-H	10/6	1:32				
6	AP# 122-H	11/6	1:32				
7	AP# 130-H	10/9	11:20				
8	AP# 130-H	10/9	11:20				

Signature _____
 Printed _____
 Company _____
 Reason _____

☐ Returned to customer

COURIER

APACHE CORPORATION FARMINGTON DISTRICT
PIT EXCAVATION AND CLOSURE REPORT

JICARILLA APACHE TRIBAL EPO
REVIEW AND APPROVAL

LOCATION: APACHE 122

PIT COUNT: 1

EPO REPRESENTATIVE _____

DATE OF REVIEW: _____

EXCAVATION								
DIMENSIONS			START			FINISH		
	W	L	D		W	L	D	CU.YDS.
PIT 1	21'	23'	6'	PIT 1	23'	23	10'	78
PIT 2				PIT 2				
PIT 3				PIT 3				
DATE:10/06/95			PIT1@07'	PIT2@	PIT3@	DATE:11/29/95		
P. I. D.	CENTER	43.2				P. I. D.	CENTER	6.9
	NW CORNER	36.0					NW CORNER	34.2
	NE CORNER	272.0					NE CORNER	25.3
	SW CORNER	320.0					SW CORNER	17.8
	SE CORNER	100.0					SE CORNER	14.5

NOTES:

10/06/95 - Black sand to 7', clearing to lt. gray @ 10'. Excavate side to remove staining.

SOIL SAMPLING									
DATE:10/06/95		PIT1@07'	PIT2@	PIT3@	ANALYSIS RESULTS			PER LAB:	ASSAIGAI
P. I. D.	CENTER	43.2			PIT	TPH	BETEX	WITNESS	DATE
	NW CORNER	36.0			NO.				
	NE CORNER	272.0			1	840	ND	IF&S	10/06/95
	SW CORNER	320.0			2				
	SE CORNER	100.0			3				

RE-SAMPLE OR CELL(S) SAMPLE

DATE:11/29/95		PIT1@10'	PIT2@	PIT3@	ANALYSIS RESULTS			PER LAB:	ASSAIGAI
P. I. D.	CENTER	6.9			PIT	TPH	BETEX	WITNESS	DATE
	NW CORNER	34.2			NO.				
	NE CORNER	25.3			1	840.0	ND	IF&S	10/06/95
	SW CORNER	17.8			2				
	SE CORNER	14.5			3				

RE-SAMPLE OR CELL(S) SAMPLE

DATE:		PIT 1	PIT 2	PIT 3	ANALYSIS RESULTS			PER LAB:	
P. I. D.	CENTER				PIT	TPH	BETEX	WITNESS	DATE
	NW CORNER				NO.				
	NE CORNER				1				
	SW CORNER				2				
	SE CORNER				3				



SAMPLE DATE 11/29/95


[illegible]

NORTH
↑
GENERAL DRAINAGE →

APACHE
APACHE NUMBER 122 Lease # JAT 129
NE/4 SE/4 (1)
SECTION 13, TOWNSHIP 24N, RANGE 4W
RIO ARriba COUNTY, NM

Revised 8/1/97 MG

TANK FIRE WALL IS 35' WIDE AT THE BASE, 1' WIDE AT THE TOP, AND 25' HIGH

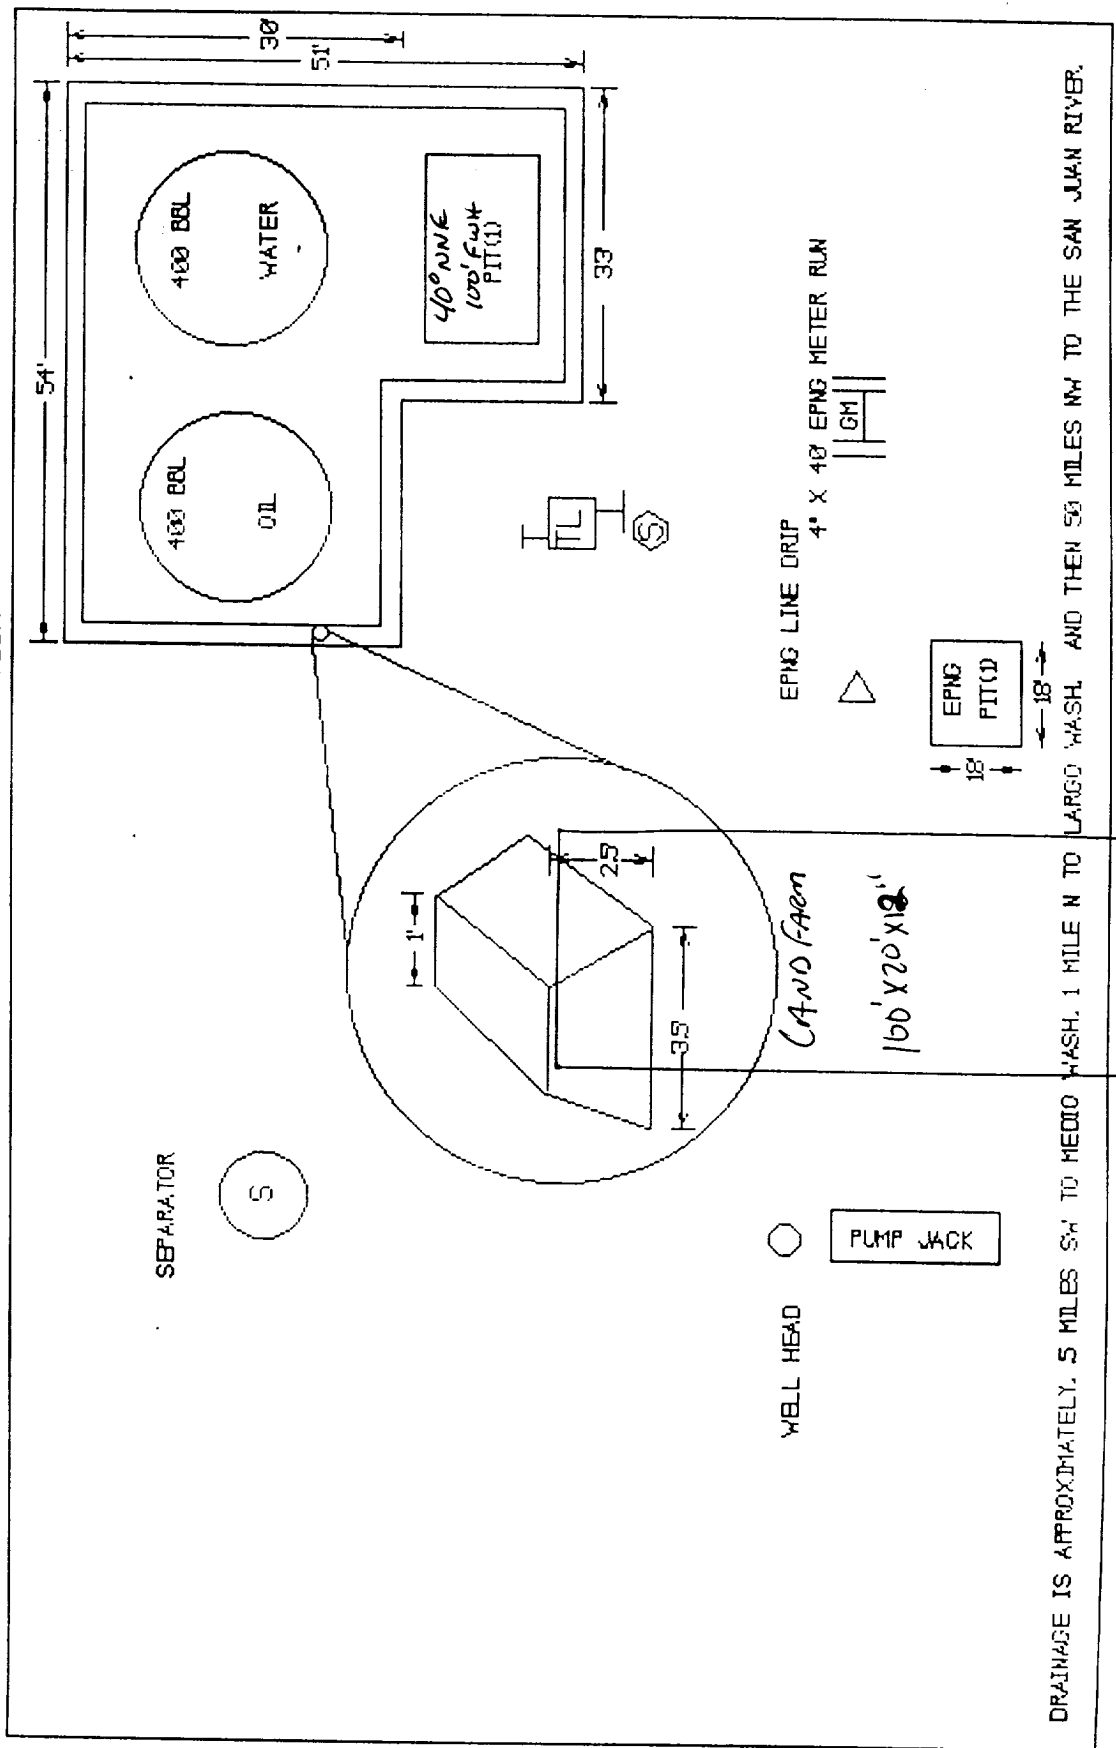

DRAINAGE IS APPROXIMATELY 5 MILES SW TO MEDIO WASH. 1 MILE N TO LARGO WASH. AND THEN 50 MILES NW TO THE SAN JUAN RIVER.

JICARILLA APACHE TRIBE
ENVIRONMENTAL PROTECTION OFFICE
P. O. BOX 507
DULCE, NEW MEXICO 87528

Submit 1 copy to
Natural Resource Dept.
and Oil & Gas Administration

ON-SITE SOIL REMEDIATION REPORT

Operator: <u>APACHE CORPORATION</u>		Telephone: <u>505-325-0318</u>	
Address: <u>2855 SOUTHSIDE RIVER ROAD/SUITE A/ FARMINGTON N.M. 87401-7947</u>			
Facility or Well Name: <u>APACHE # 122</u>			
Location: Unit or Qtr/Qtr Sec <u>I</u> SEC <u>13</u> T <u>24</u> N R <u>4</u> W County <u>RIO ARRIBA</u>			
Land Type <u>JIC. TRIBAL</u>			
Date Remediation Started: <u>10/6/95</u>		Date Completed: <u>8/17/98</u>	
Remediation Method: Landfarmed		<u>XXX</u> Approx. cubic yards <u>78</u>	
Composted		<u> </u>	
Other		<u>REMEDIATED SOIL TO BE SPREAD ON LOCATION.</u>	
Depth to Groundwater: (pts) <u>0</u>		Final Closure Sampling Sampling Date: <u>8/17/98</u> Time: <u>9:40AM</u> Sample Results: Field Headspace (ppm) <u>0</u> TPH (ppm) <u>1800</u> Method <u>M8015</u> Other <u>BTEX \ SW846 , 8020A (ND)</u>	
Distance to an Ephemeral Stream: (pts) <u>0</u>			
Distance to Nearest Lake, Playa, or Watering Pond: (pts) <u>0</u>			
Wellhead Protection Area: (pts) <u>0</u>			
Distance To Surface Water: (pts) <u>0</u>			
RANKING SCORE (TOTAL POINTS) <u>0</u>			
I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND BELIEF			
DATE: <u>9/30/98</u>		PRINTED NAME <u>JEFF CROSS</u>	
SIGNATURE <u>Jeff Cross</u>		TITLE <u>PROJECT MANAGER</u>	
AFTER REVIEW OF THE SOIL REMEDIATION INFORMATION. ON-SITE REMEDIATION IS APPROVED IN ACCORDANCE TO THE JICARILLA APACHE TRIBE PIT CLOSURE ORDINANCE.			
APPROVED: YES <u>X</u> NO <u> </u> (REASON) <u> </u>			
SIGNED: <u>Kurt C. M...ll</u>		DATE: <u>11-13-98</u>	

APACHE COPORATION/FARMINGTON DISTRICT SOIL REMEDIATIONS STATUS REPORT

REMEDIATION SITE APACHE # 122

* AMOUNT OF SOIL UNDERGOING REMEDIATION 78 Yds.

CELL No. <u>1</u>	SampDATE 8/17/98	TPH 1800	BTEX ND
DIMENSIONS(LxWxH) <u>100' X 20' X 12"</u>			
CELL LOCATION (dir. from well head) <u>EAST</u>			
* DATE BEGAN: <u>10/6/95</u>			
DATE TERMINATED (TPH <5,000 ppm/BTEX< 50 ppm/Benzene < 10 ppm) <u>8/17/98</u>			
CELL No. <u>2</u>	SampDATE	TPH	BTEX
DIMENSIONS(LxWxH)			
CELL LOCATION (dir. from well head)			
* DATE BEGAN:			
DATE TERMINATED (TPH <5,000 ppm/BTEX< 50 ppm/Benzene < 10 ppm)			
CELL No. <u>3</u>	SampDATE	TPH	BTEX
DIMENSIONS(LxWxH)			
CELL LOCATION (dir. from well head)			
* DATE BEGAN:			
DATE TERMINATED (TPH <5,000 ppm/BTEX< 50 ppm/Benzene < 10 ppm)			
REMEDATION RECORD: (Date, Treatment, Tilling)			
TREAT SOIL WITH 28-4-4 FERTILIZER		6/10/98 TREAT SOIL WITH 46-0-0 FERTILIZER.	
6/6/97 WATER,PLOW AND TILL SOIL.		6/10/98 WATER , PLOW AND TILL SOIL.	
6/13/97 PLOW AND TILL SOIL.		6/13/98 PLOW AND TILL SOIL.	
5/5/98 TILL SOIL.			
5/10/98 PLOW SOIL.			
5/30/98 PLOW SOIL.			
5/31/98 TILL SOIL.			

From excavation reports.

WELL NAME:

Apache #122

SAMPLE DATE:


8-17-98

DIMENSIONS:

100' x 20' x 18"




= SAMPLE AREA

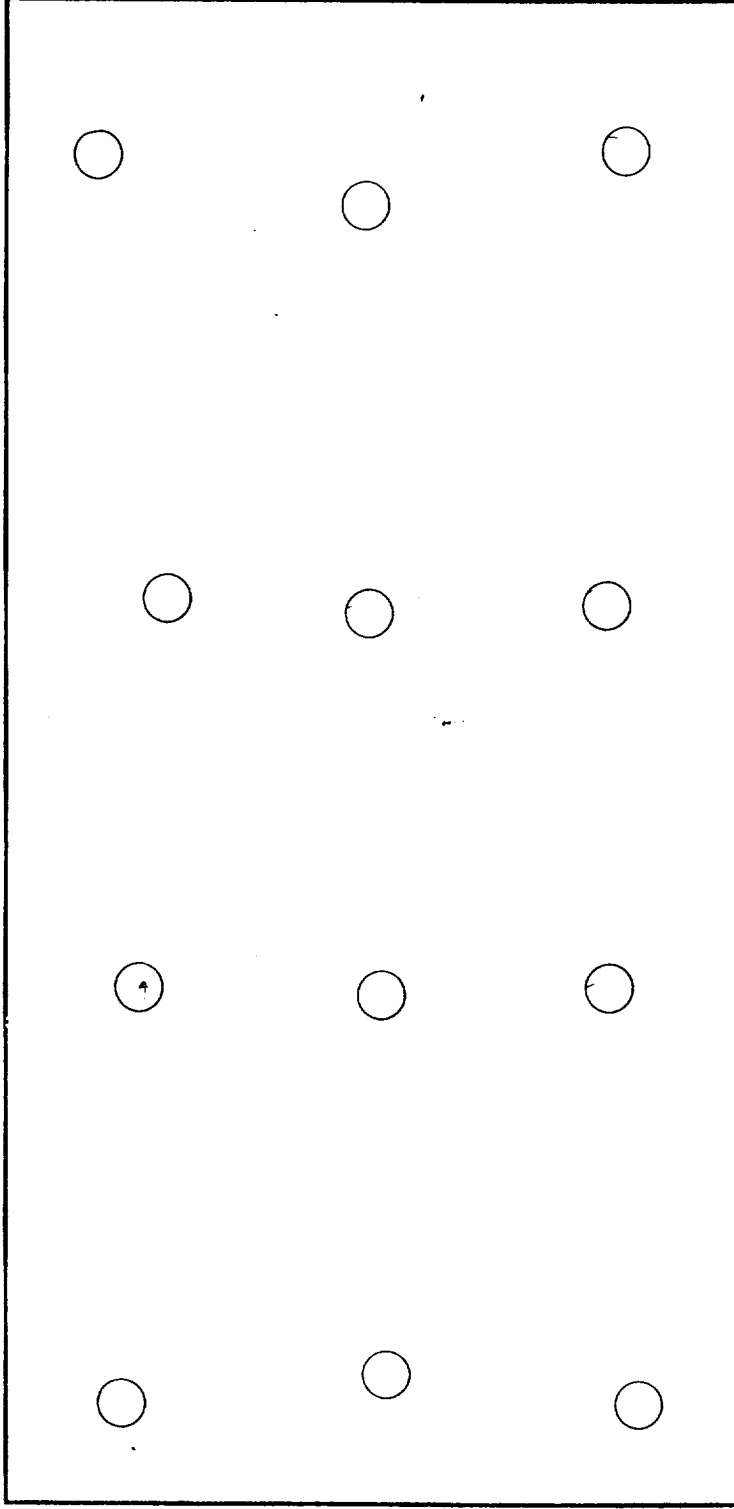

NOTES:

ALL SAMPLES TAKEN 10" TO 12" INTO CELL.


12 point composite sample



ASSAIGAI ANALYTICAL LABORATORIES, INC.

7300 Jefferson, NE • Albuquerque, New Mexico 87109 • (505) 345-8964 • FAX (505) 345-7259

3332 Wedgewood, E-5 • El Paso, Texas 79925 • (915) 593-6000 • FAX (915) 593-7820
127 Eastgate Drive, 212-C • Los Alamos, New Mexico 87544 • (505) 662-2558



APACHE CORPORATION
attn: **JEFF CROSS**
2855 SOUTHSIDE RIVER RD STE A
FARMINGTON, NM 87401-7947

* explanation of codes

B	analyte detected in Method Blank
E	result is estimated
H	analyzed out of hold time
N	tentatively identified compound
S	subcontracted
1-9	see footnote

Assaigai Analytical Laboratories, Inc.

Certificate of Analysis

Client: **APACHE CORPORATION**
Project: **9808183 JICARILLA PIT CLOSURES**

William P. Biava

William P. Biava: President of Assaigai Analytical Laboratories, Inc.

Client Sample ID: **APACHE #122 CELL** Sample Matrix: **SOIL** Sample Collected: **08/17/98 09:40:00**

<u>Fraction</u>	<u>QC Group</u>	<u>CAS #</u>	<u>Result</u>	<u>Units</u>	<u>Dilution Factor</u>	<u>Detection Limit</u>	*	<u>Sequence</u>	<u>Run Date</u>
Test: SW846 8010B/8020A Purgeable VOCs by GC/PID-ELCD									
9808183-01A	X98390	71-43-2	Benzene	ND	mg / Kg	50	0.005	XG.1998.702-4	08/20/98
	X98390	100-41-4	Ethylbenzene	ND	mg / Kg	50	0.005	XG.1998.702-4	
	X98390	95-47-6	o-Xylene	ND	mg / Kg	50	0.005	XG.1998.702-4	
	X98390		P/M-Xylenes	ND	mg / Kg	50	0.01	XG.1998.702-4	
	X98390	108-88-3	Toluene	ND	mg / Kg	50	0.005	XG.1998.702-4	
Test: SW846 8015A Diesel Range Organics by GC/FID									
9808183-01B	X98389		Diesel Range Organics	1800	mg / Kg	25	25	XG.1998.699-7	08/21/98

*** Sample specific analytical Detection Limit is determined by multiplying the sample Dilution Factor by the listed method Detection Limit. ***
*** Results relate only to the items tested. ***



Chain of Custody Record

Lab job no.: 8183 Date: _____

Page 1 of 1

ALBUQUERQUE, NEW MEXICO 87109
(505) 345-8964

3332 WEDGEWOOD
EL PASO, TEXAS 79925
(915) 593-6000

MELQUIADES ALANIS
6411 LOCAL UNO
CIUDAD JUAREZ, CHIHUAHUA MEXICO 32320

Project Manager / Contact ~~Jeff Cross~~

Telephone No. (505) 774-6643

Fax No. (505) 774-6624

Samplers: (Signature) Jeff Cox

Contract / Purchase Order / Quote

[illegible]

Analysis Required

Remarks

Issued by: <u>Jeff Green</u> Signature: <u>Jeff Green</u> Date: <u>8/19/98</u>	Received by: Signature: <u>Wm. P. Biava</u> Printed: <u>Wm. P. Biava</u> Company: <u>AAL</u> Reason: <u>Delivery</u>
Signature: <u>Wm. P. Biava</u> Printed: <u>Wm. P. Biava</u> Company: <u>AAL</u> Reason: <u>Analysis</u>	Refiniquished by: Signature: <u>Wm. P. Biava</u> Printed: <u>Wm. P. Biava</u> Company: <u>AAL</u> Reason: <u>Analysis</u>
Date: <u>8/28/98</u> Time: <u>1745</u>	Received by: Signature: <u>Rh. Ardun</u> Printed: <u>P. d. Ardun</u> Company: <u>AAL</u> Reason: <u>08/21/98 BAW</u>

After analysis, samples are to be:

☐ Disposed of (additional fee)

☐ Stored (30 days max)

☐ Stored over 30 days (additional fee)

☐ Returned to customer

LABORATORY
