

*Denny E. Faust*

DEPUTY OIL & GAS INSPECTOR

JICARILLA APACHE TRIBE

FEB 08 1999

ENVIRONMENTAL PROTECTION OFFICE

P.O. BOX 507  
DULCE, NEW MEXICO 87528

SUBMIT 1 COPY TO  
NATURAL  
RESOURCE DEPT  
AND OIL-GAS  
ADMINISTRATION

*Approved*

**PIT REMEDIATION AND CLOSURE REPORT**

Operator: PNM Gas Services (Williams) Telephone: 324-3764

Address: 603 W. Elm Street Farmington, NM 87401

Facility or Well Name: Jicarilla Contract 147-ZE Drp

Location: Unit: I Sec. 5 T. 25 N R. 5 W County Rio Arriba

Pit Type: Separator      Dehydrator      Other Manual drip blowdown

Land Type: Jicarilla Apache

Pit Location: Pit dimensions: length 20' width 20' depth 3'

(Attach diagram) Reference: wellhead      other Blowdown well

Footage from reference: 5'

Direction from reference: 27 Degrees X East of North X  
West South

**Depth to Ground Water:**

(Vertical distance from contaminants to seasonal high water elevation of ground water)

Less than 50 feet (20 points)  
50 feet to 99 feet (10 points)  
Greater than 100 feet (0 points)

0

**Wellhead Protection Area:**

(Less than 200 feet from a private domestic water source, or; less than 1,000 feet from all other water sources)

Yes (20 points)  
No (0 points)

0

**Distance to Surface Water:**

(Horizontal distance to perennial lakes, ponds, rivers, streams, creeks, irrigation canals and ditches)

Less than 200 feet (20 points)  
200 feet to 1,000 feet (10 points)  
Greater than 1,000 feet (0 points)

0

**Distance to Ephemeral Stream (dry wash):**

(Horizontal distance to all downgradient streams having a width of at least 10 feet)

Less than or equal to 100 feet (10 points)  
Greater than 100 feet (0 points)

0

**Distance to Nearest Lake, Playa, or Watering Pond:**

(Horizontal distance to all downgradient lakes, playas, and livestock or wildlife water ponds)

Less than or equal to 100 feet (10 points)  
Greater than 100 feet (0 points)

0

**RANKING SCORE (TOTAL POINTS):**

0

RECEIVED  
FEB - 1 1999

OIL CON. DIV  
DIST. 8

Date Remediation Started: 8-10-98 Date Completed: 11/2/98

Remediation Method: Excavation ☒ Approx. Cubic Yards 982

(Check all appropriate sections)

Landfarmed ☒ Amount Landfarmed (cubic yds): 982

Other \_\_\_\_\_

Remediation Location: Onsite 0 Offsite 982 yds farmed on Axi Apache JZIA  
(i.e., landfarmed onsite, name and location of offsite facility)

General Description of Remedial Action:

Removal of contaminated soil from all four sidewalls, as to get a below 100 ppm head space reading. Bottom is rock.  
Final excavation dimensions: 47'(N-S) X 47'(E-W) X 12' (D)

Ground Water Encountered: No ☒ Yes \_\_\_\_\_ Depth \_\_\_\_\_

Final Pit Closure Sampling: Sample Location North, East, South, and west Sidewalls, and a three point composite sample of bottom

(if multiple samples, attach sample result and diagram of sample locations and depths.)

Sample depth 12'

Sample date 8-12-98 Sample time 1255

Sample Results

Soil: Benzene (ppm) ND Water: Benzene (ppb) \_\_\_\_\_

Total BTEX (ppm) 5.54 Toluene (ppb) \_\_\_\_\_

Field headspace (ppm) 298 Ethylbenzene (ppb) \_\_\_\_\_

TPH 160 ppm Method PD15 Total Xylenes (ppb) \_\_\_\_\_

Ground Water Sample: Yes \_\_\_\_\_ No ☒ (If yes, attach sample results)

I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND MY BELIEF

DATE 8-31-98 PRINTED NAME Ray Haston

SIGNATURE Ray Haston AND TITLE Environmental Technician


AFTER REVIEW OF THE PIT CLOSURE INFORMATION, PIT CLOSURE IS APPROVED IN ACCORDANCE TO JICARILLA APACHE TRIBE PIT CLOSURE ORDINANCE.

APPROVED: YES ☒ NO \_\_\_\_\_ (REASON): \_\_\_\_\_

SIGNED: Kee C Mamm DATE: 9-3-98

View on  
 Axi Apache 147-2E Drip  
 (I) 5-25W-5W  
 Williams  
 8-10-98

N

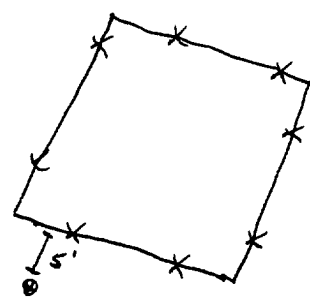


20' x 20' x 3'

O

Excavation Sampling

47'(N+S) x 47'(E+W) x 12'(D)

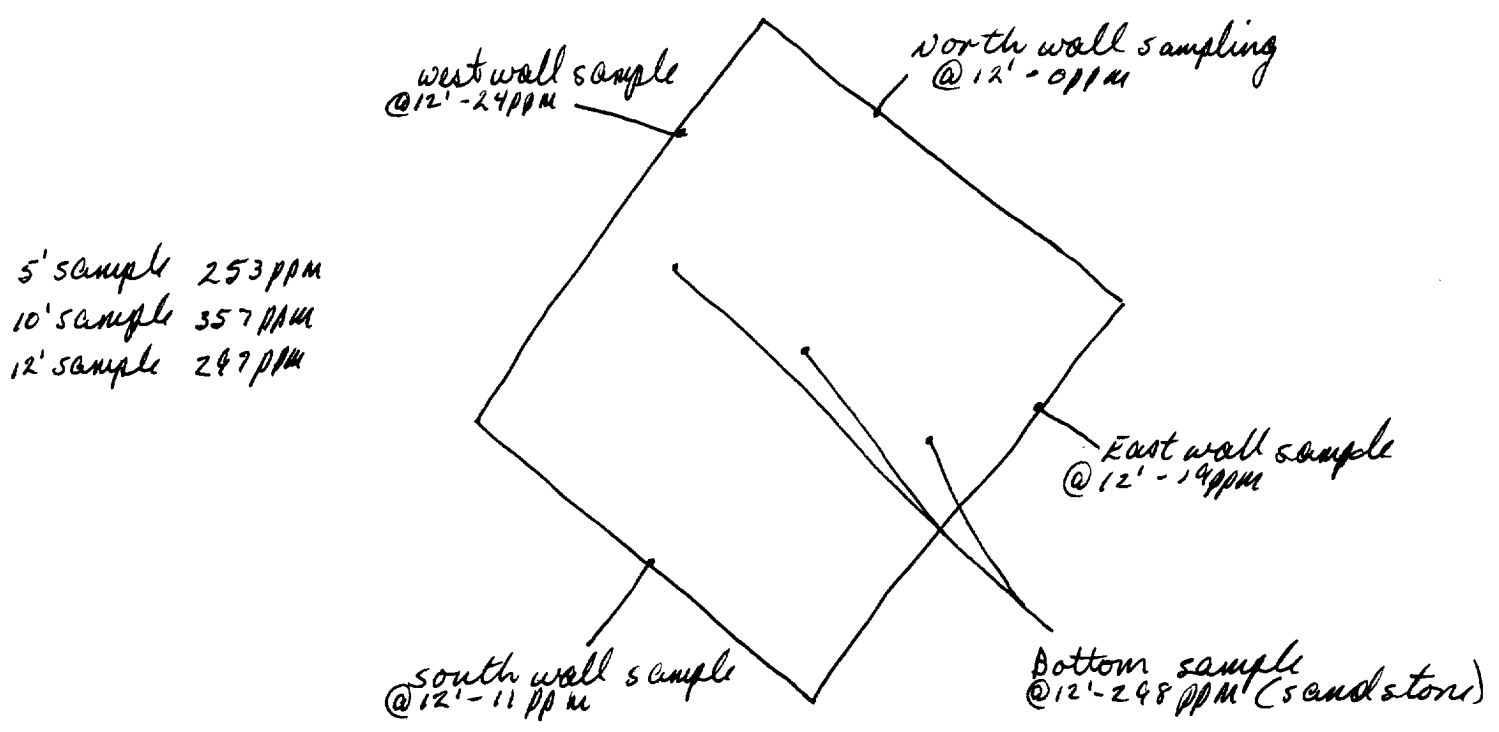

not to scale

OFF: (505) 325-5667



LAB: (505) 325-1556

**On Site Technologies, LTD.**

**Date:** 21-Aug-98

---

**CLIENT:** PNM - Public Service Company of NM

**Project:** PNM Pit Remediation

**Lab Order:** 9808028

## **CASE NARRATIVE**

---

Samples were analyzed using the methods outlined in the following references:

Test Methods for Evaluating Solid Waste, Physical/Chemical Methods, SW846, 3rd Edition

All method blanks, laboratory spikes, and/or matrix spikes met quality assurance objectives.

OFF: (505) 325-5667



LAB: (505) 325-1556

# ANALYTICAL REPORT

Date: 21-Aug-98

<b>Client:</b>	PNM - Public Service Company of NM	<b>Client Sample Info:</b>	Jic. Contract 147-2E Drip
<b>Work Order:</b>	9808028	<b>Client Sample ID:</b>	9808121255; 3pt. Comp. Bottom
<b>Lab ID:</b>	9808028-02A	<b>Matrix:</b>	SOIL
<b>Project:</b>	PNM Pit Remediation	<b>Collection Date:</b>	8/12/98 12:55:00 PM
		<b>COC Record:</b>	5751

Parameter	Result	PQL	Qual	Units	DF	Date Analyzed
<b>DIESEL RANGE ORGANICS</b>		<b>SW8015</b>				Analyst: HR
T/R Hydrocarbons: C10-C28	160	25		mg/Kg	1	8/19/98
<b>BTEX</b>		<b>SW8020A</b>				Analyst: DC
Benzene	ND	50		µg/Kg	50	8/18/98
Toluene	350	100		µg/Kg	50	8/18/98
Ethylbenzene	470	50		µg/Kg	50	8/18/98
m,p-Xylene	4600	100		µg/Kg	50	8/18/98
o-Xylene	120	50		µg/Kg	50	8/18/98

5,540  
5.54ppm

<b>Qualifiers:</b>	PQL - Practical Quantitation Limit	S - Spike Recovery outside accepted recovery limits
	ND - Not Detected at Practical Quantitation Limit	R - RPD outside accepted recovery limits
	J - Analyte detected below Practical Quantitation Limit	E - Value above quantitation range
	B - Analyte detected in the associated Method Blank	Surr: - Surrogate

1 of 1

P.O. BOX 2606 • FARMINGTON, NM 87499

- TECHNOLOGY BLENDING INDUSTRY WITH THE ENVIRONMENT -

OFF: (505) 325-5667



LAB: (505) 325-1556

## ANALYTICAL REPORT

Date: 21-Aug-98

<b>Client:</b>	PNM - Public Service Company of NM	<b>Client Sample Info:</b>	Jic. Contract 147-2E Drip
<b>Work Order:</b>	9808028	<b>Client Sample ID:</b>	9808121245; Wall Comp.
<b>Lab ID:</b>	9808028-01A	<b>Matrix:</b>	SOIL
<b>Project:</b>	PNM Pit Remediation	<b>Collection Date:</b>	8/12/98 12:45:00 PM
		<b>COC Record:</b>	5751

Parameter	Result	PQL	Qual	Units	DF	Date Analyzed
<b>DIESEL RANGE ORGANICS</b>		<b>SW8015</b>				Analyst: HR
T/R Hydrocarbons: C10-C28	ND	25		mg/Kg	1	8/18/98

**Qualifiers:**

- PQL - Practical Quantitation Limit
- ND - Not Detected at Practical Quantitation Limit
- J - Analyte detected below Practical Quantitation Limit
- B - Analyte detected in the associated Method Blank

- S - Spike Recovery outside accepted recovery limits
- R - RPD outside accepted recovery limits
- E - Value above quantitation range
- Surr: - Surrogate

1 of 1

P.O. BOX 2606 • FARMINGTON, NM 87499

- TECHNOLOGY BLENDING INDUSTRY WITH THE ENVIRONMENT -

JICARILLA APACHE TRIBE  
ENVIRONMENTAL  
PROTECTION OFFICE  
P.O. BOX 507  
DULCE, NEW MEXICO 87528

SUBMIT 1 COPY TO  
NATURAL  
RESOURCE DEPT  
AND OIL GAS  
ADMINISTRATION

ON-SITE SOIL REMEDIATION REPORT

Operator: PNM Gas Services ( WFS ) Telephone: 324-3764  
Address: 603 W. Elm Street Farmington, NM 87401  
Facility or Well Name: Jicarilla Contract 147-2E Drip  
Location: Unit: I Sec. 5 T. 25 N R. 5 W County Rio Arriba  
Land Type: Jicarilla Apache

Date Remediation Started: 8-10-98 Date Completed: 10-8-98  
Remediation Method: Landfarmed X Approx. cubic yards 982  
Composted —  
Other —

Depth to Ground Water: (pts.) 0  
Distance to an Ephemeral Stream: (pts.) 0  
Distance to Nearest Lake, Playa,  
or Watering Pond: (pts.) 0  
Wellhead Protection Area: (pts.) 0  
Distance to Surface Water: (pts.) 0  
Ranking Score (Total Points): 0

Final Closure Sampling:

Sampling Date: 4-30-98 Time 1318  
Sampling Results:  
Field Headspace (ppm) 5.7  
TPH (ppm) 46 Method 8015  
Other —

I HEREBY CERTIFY THAT THE INFORMATION ABOVE IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE AND BELIEF

DATE 10-24-98 PRINTED NAME ~~Roy Burnham~~ Ray Haston  
SIGNATURE Ray Haston AND TITLE Environmental Technician II

AFTER REVIEW OF THE SOIL REMEDIATION INFORMATION, ON-SITE REMEDIATION APPROVED IN ACCORDANCE TO THE  
JICARILLA APACHE TRIBE PIT CLOSURE ORDINANCE


APPROVED: YES X NO — (REASON) was no Backfill

SIGNED: Kenneth M. ... DATE: 11-2-98

7  
N

Jicavilla Contract 147-2E Drip  
WFS  
Sec. 5, 25N, 5W, I

Land Farm: Axi Apache J-21A  
Conoco  
Sec. 5, 25N, 5W, N

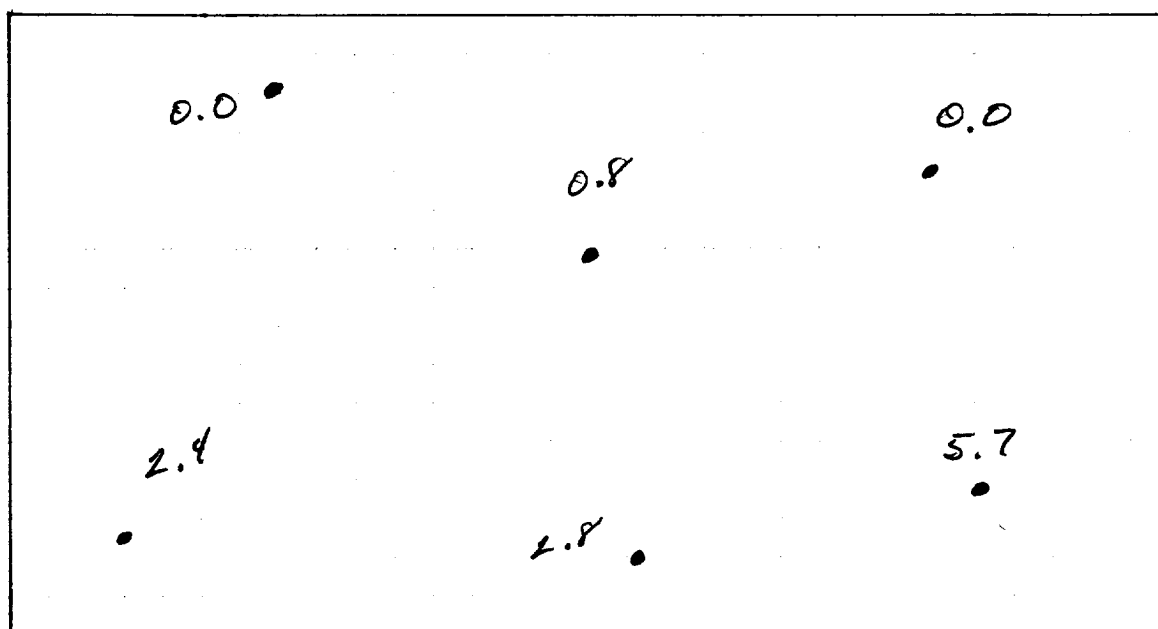

2"-12" depth  
soil vapor headspace reading = 5.7

not to scale



OFF: (505) 325-5667



LAB: (505) 325-1556

## ANALYTICAL REPORT

Date: 14-Oct-98

<b>Client:</b>	PNM - Public Service Company of NM	<b>Client Sample Info:</b>	Jicarilla Contract 147-2E Drip LF
<b>Work Order:</b>	9810006	<b>Client Sample ID:</b>	9809301318; 6pt. Composite
<b>Lab ID:</b>	9810006-01A	<b>Matrix:</b>	SOIL
<b>Project:</b>	Jicarilla Landfarms	<b>Collection Date:</b>	9/30/98 1:18:00 PM
		<b>COC Record:</b>	7510

Parameter	Result	PQL	Qual	Units	DF	Date Analyzed
<b>DIESEL RANGE ORGANICS</b>		<b>SW8015</b>				<b>Analyst: DC</b>
T/R Hydrocarbons: C10-C28	46	25		mg/Kg	1	10/8/98

**Qualifiers:**

PQL - Practical Quantitation Limit

ND - Not Detected at Practical Quantitation Limit

J - Analyte detected below Practical Quantitation Limit

B - Analyte detected in the associated Method Blank

S - Spike Recovery outside accepted recovery limits

R - RPD outside accepted recovery limits

E - Value above quantitation range

Surr: - Surrogate

1 of 1

P.O. BOX 2606 • FARMINGTON, NM 87499

- TECHNOLOGY BLENDING INDUSTRY WITH THE ENVIRONMENT -
