

# Lindrith B Unit #76

## Proposed P&A

Lindrith Gallup / Dakota West

NW, Section 1, T-24-N, R-3-W, Rio Arriba County, NM

Today's Date: 3/21/98

Spud: 3/8/90

Completed: 4/24/90

Elev: 7009' GL

Workover: Jan & April '91

Ojo Alamo @ 2730'

Kirtland / Fruitland @ 3090'

Pictured Cliffs @ 3294'


Mesaverde @ 5516'

Gallup @ 6648'

Dakota @ 7758'

17-1/2" Hole

7-7/8" Hole

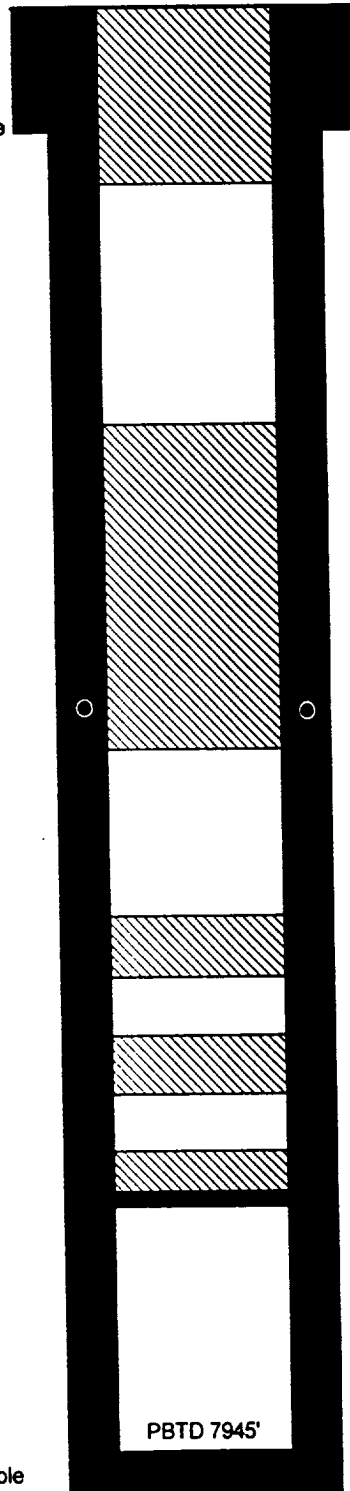

Cement Circulated to Surface

13-3/8" 48#, H-40 Csg set @ 420'  
475 sxs cement (Circulated to Surface)

Plug #5 470' - Surface  
Cmt with 53 sxs Class B

Plug #4 3344' - 2680'  
Cmt with 81 sxs Class B

Squeeze DV tool w/ 350 sxs (1991)

DV tool @ 3326'  
Cmt w/ 1200 sxs (1959 cf)  
Top of Cmt @ DV Tool (Calc, 75%)

Plug #3 5566' - 5466'  
Cmt with 17 sxs Class B

Plug #2 6698' - 6598'  
Cmt with 17 sxs Class B

Plug #1 7708' - 7608'  
Cmt with 17 sxs Class B

Set Cmt Retainer @ 7708'

Dakota Perforations:  
7758' - 7783'

5-1/2" 15.5#, K-55 Casing set @ 7950'  
Cemented with 1025 sxs (1590  
cf)

PBTD 7945'

TD 7950'
