

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN TRIPLICATE*
(Other instructions on re-
verse side)

Budget Bureau No. 1004-0135
Expires August 31, 1985

SUNDRY NOTICES AND REPORTS ON WELLS

(Do not use this form for proposals to drill or to deepen or plug back to a different reservoir.
Use "APPLICATION FOR PERMIT—" for such proposals.)

1. OIL WELL ☒ GAS WELL ☐ OTHER ☐

2. NAME OF OPERATOR

Amoco Production Co.

3. ADDRESS OF OPERATOR

2325 E. 30 St., Farmington, NM 87401

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.*
See also space 17 below.)
At surface

720' FSL X 570' FWL

BUREAU OF LAND MANAGEMENT
FARMINGTON RESOURCE AREA

14. PERMIT NO.

15. ELEVATIONS (Show whether DT, RT, OR, etc.)

5635' GL

5. LEASE DESIGNATION AND SERIAL NO.

N00-C-14-20-5523

6. IF INDIAN, ALLOTTEE OR TRIBE NAME

Navajo Tribe

7. UNIT AGREEMENT NAME

8. FARM OR LEASE NAME

Navajo Tribal Z

9. WELL NO.

1

10. FIELD AND POOL, OR WILDCAT

Tocito Dome Penn D

11. SEC., T., R., M., OR BLK. AND
SURVEY OR AREA

SW/SW Sec 14, T26N, R18W

12. COUNTY OR PARISH

San Juan

13. STATE

NM

16. Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:

TEST WATER SHUT-OFF

FRACTURE TREAT

SHOOT OR ACIDIZE

REPAIR WELL

(Other)

PULL OR ALTER CASING

MULTIPLE COMPLETE

ABANDON*

CHANGE PLANS

WATER SHUT-OFF

FRACTURE TREATMENT

SHOOTING OR ACIDIZING

(Other)

(Note: Report results of multiple completion on Well
Completion or Recompletion Report and Log form.)

REPAIRING WELL

ALTERING CASING

ABANDONMENT*

17. DESCRIBE PROPOSED OR COMPLETED OPERATIONS (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)

Amoco Production Company requests approval to plug and abandon the subject well according to the attached procedure.

NOTE: This procedure was discussed between Steve Mason and Ed Alizadeh of Amoco on 11-17-86. It is being submitted in response to File Letter 3162.3-4(016) dated 11-7-86.

18. I hereby certify that the foregoing is true and correct

SIGNED

TITLE Adm. Supervisor

DATE 11-19-86

(This space for Federal or State office use)

APPROVED BY

TITLE

DATE 11/19/86

CONDITIONS OF APPROVAL, IF ANY:

*See Instructions on Reverse Side

NMOCC

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

DEC 22 1986
John Skella
FARM AREA MANAGER

FARMINGTON DISTRICT
COMPLETION PROCEDURE
PxA

Date: 11/17/86

WELL NAME: Navajo Tribal 2#1

FIELD Tonto Dome

LOCATION: Sw/4 Sw/4 Sec. 14, 26N, 18W

FORMATION(S) Pennsylvanian "D"

San Juan County, New Mexico

ELEVATIONS: KB: 5649 TD: 6575

PBD: 6528

CASING: 13 3/8" @ 141'

9 5/8" @ 1534'

7" @ 6575'

LOGS: BHCS, Dual Production - SP

DV TOOL SET AT: 4303'

PURPOSE: Plug and Abandon the wellbore

~~DBE~~
~~SWH~~
GOM

TWE

GOM

MCH
RGH
BVD
GMK

BVE

~~RWO/AJM~~


2DF

EDA
ENGR

FILE

Procedure discussed w/ Steve Mason of the
BLM on 11/17/86.

WELLBORE SKETCH

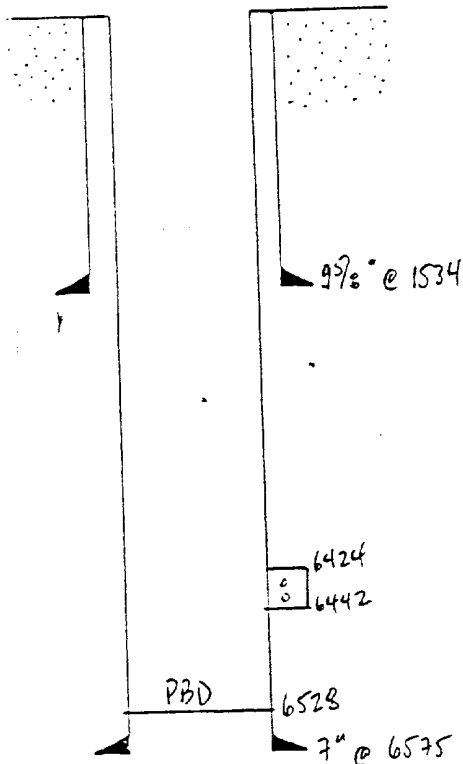

1) MIRUSU

2) Most recent records indicate the tbg was laid down in 1979. Thus, you may need a work string of tbg.

3) Set a casing BP @ 6400'

4) Spot 5 sacks of cement on the B.P.

5) Pull up and spot cement from 5014' - 4914'.

6) Pull up and spot cement from 3912' - 3812'.

7) Pull up and spot cement from 2950' - 2850'.

8) Pull up and spot cement from 2310' - 2210'.

DISTRICT MANAGER

R. J. Brown

11/17/86

DISTRICT ENGINEER

DISTRICT DRILLING SUPERVISOR

ENGINEER Ed Alizadeh x 229

326-2756

DATE

Navajo Tribal Z#1

- 9) Pull up and spot cement from 1584' - 1484'.
- 10) Pull up and spot cement from 50' to surface.
- 11) Erect a dry hole marker w/ a metal sheet displaying the section, township, and range on a concrete block at least 4' above ground level.
