

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN TRIPLICATE*
(Other instructions on re-
verse side)

Budget Bureau No. 1004-0145
Expires August 31, 1985

SUNDRY NOTICES AND REPORTS ON WELLS

(Do not use this form for proposals to drill or to deepen or plug a well. Use "APPLICATION FOR PERMIT" for such proposals.)

OCT 16 1985

OIL WELL ☐ GAS WELL ☒ OTHER

2. NAME OF OPERATOR

Amoco Production Co.

3. ADDRESS OF OPERATOR

501 Airport Drive, Farmington, N M 87401

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements. See also space 17 below.)
At surface

1800' FSL X 1590' FEL

6. PERMIT NO.

15. ELEVATIONS (Show whether of, RT, GR, etc.)

5925' GR

5. LEASE DESIGNATION AND SERIAL NO.

SF-078132

6. IF INDIAN, ALLOTTEE OR TRIBE NAME

7. UNIT AGREEMENT NAME

8. FARM OR LEASE NAME

Annie L. Elliott D

9. WELL NO.

9 E

10. FIELD AND POOL, OR WILDCAT

Basin Dakota

11. SEC., T., R., M., OR BLK. AND SURVEY OR AREA

NW/SE Sec 11, T29N, R9W

12. COUNTY OR PARISH

San Juan

13. STATE

New Mexico

Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:

TEST WATER SHUT-OFF

FRACTURE TREAT

SHOOT OR ACIDIZE

REPAIR WELL

(Other)

REPAIR OR ALTER CASING

MULTIPLE COMPLETE

ABANDON*

CHANGE PLANS

SUBSEQUENT REPORT OF:

WATER SHUT-OFF

FRACTURE TREATMENT

SHOOTING OR ACIDIZING

(Other) Spud & Set Casing

REPAIRING WELL

ALTERING CASING

ABANDONMENT*

(NOTE: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

17. DESCRIBE PROPOSED OR COMPLETED OPERATIONS (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Spud a 12 1/4" hole on 9-16-85 at 1930 hours. Drilled to 355' Set 9 5/8", 36#, J-55 casing at 353' and cemented with 325 c.f. class B Portland. Circulated cement to surface. Pressure tested casing to 1000 psi for 30 minutes. Drilled an 8 3/4" hole to 2959' on 9-19-85. Set 7", 20# J-55 intermediate casing at 2956'. Cemented with 425 c.f. class B Portland and tailed in with 118 c.f. class B Portland. Ran a temperature survey (attached) which indicated the top of the cement to be at 350'. Drilled a 6 1/4" hole to a TD of 7172' on 9-27-85. Set 4 1/2", 11.6#, K-55 production casing at 7169'. Stage 1: Cemented with 542 c.f. class B 65:35: poz and tailed in with 142 c.f. class B 50:50 poz. Stage 2: Cemented with 177 c.f. class B 65:35 poz. Ran a temperature survey (attached) which indicated the top of the cement to be at 2100'. The DV tool was set at 3615' and the rig was released on 9-28-85.

I hereby certify that the foregoing is true and correct

SIGNED BSShaw TITLE Adm. Supervisor

DATE 10-8-85 DIV. 3

(Use space for Federal or State office use)

PROVED BY _____
CONDITIONS OF APPROVAL, IF ANY:

TITLE _____

DATE 10-8-85

*See Instructions on Reverse Side

NMOCC

FARMINGTON RESOURCE AREA

WILSON

FORM 432-2

SERVICE COMPANY

TEMPERATURE SURVEY

COMPANY Amoco Production

WELL 9_E LEASE A.L. Elliott "D"

COUNTY San Juan STATE New Mexico

SEC. 11 TWP. 29N RGE. 9W

APPROX. TOP CEMENT 350'

Survey Begins at 100' Ft. Ends at 2895' Ft.

Approx. Fill-Up Max. Temp.

Log Measured From KB Run No. 1

Casing Size	Casing Depth	Diam of Hole	Depth
7" from <u> </u> to <u> </u>		from <u>8 3/4"</u> to <u> </u>	
from <u> </u> to <u> </u>		from <u> </u> to <u> </u>	

Date of Cementing 9/19/85 Time 11:20 pm

Date of Survey 9/20/85 Time 1:30 pm


Amount of Cement 390 sx 65/35 Poz + 100 sx cl B Neat


Recorded by Ebert Witnessed by


REMARKS OR OTHER DATA

OA 1554' FC 2914'

TEMPERATURE IN DEGREES FAHRENHEIT

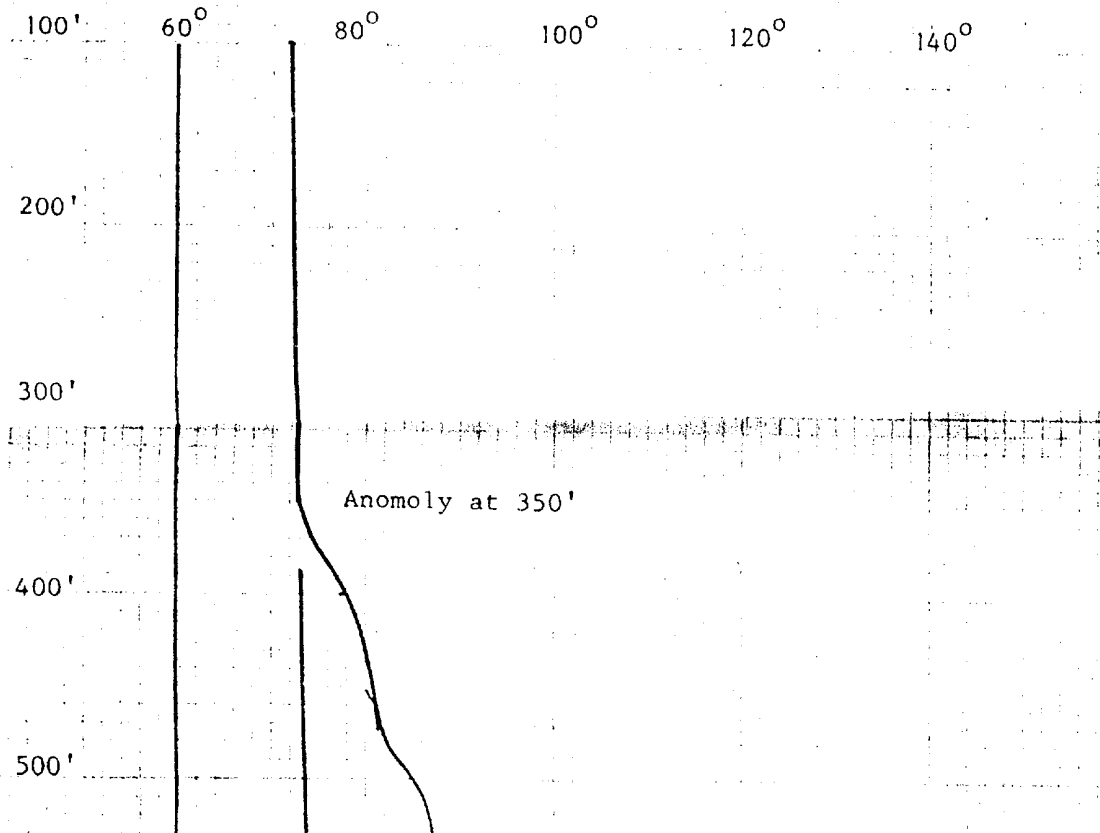

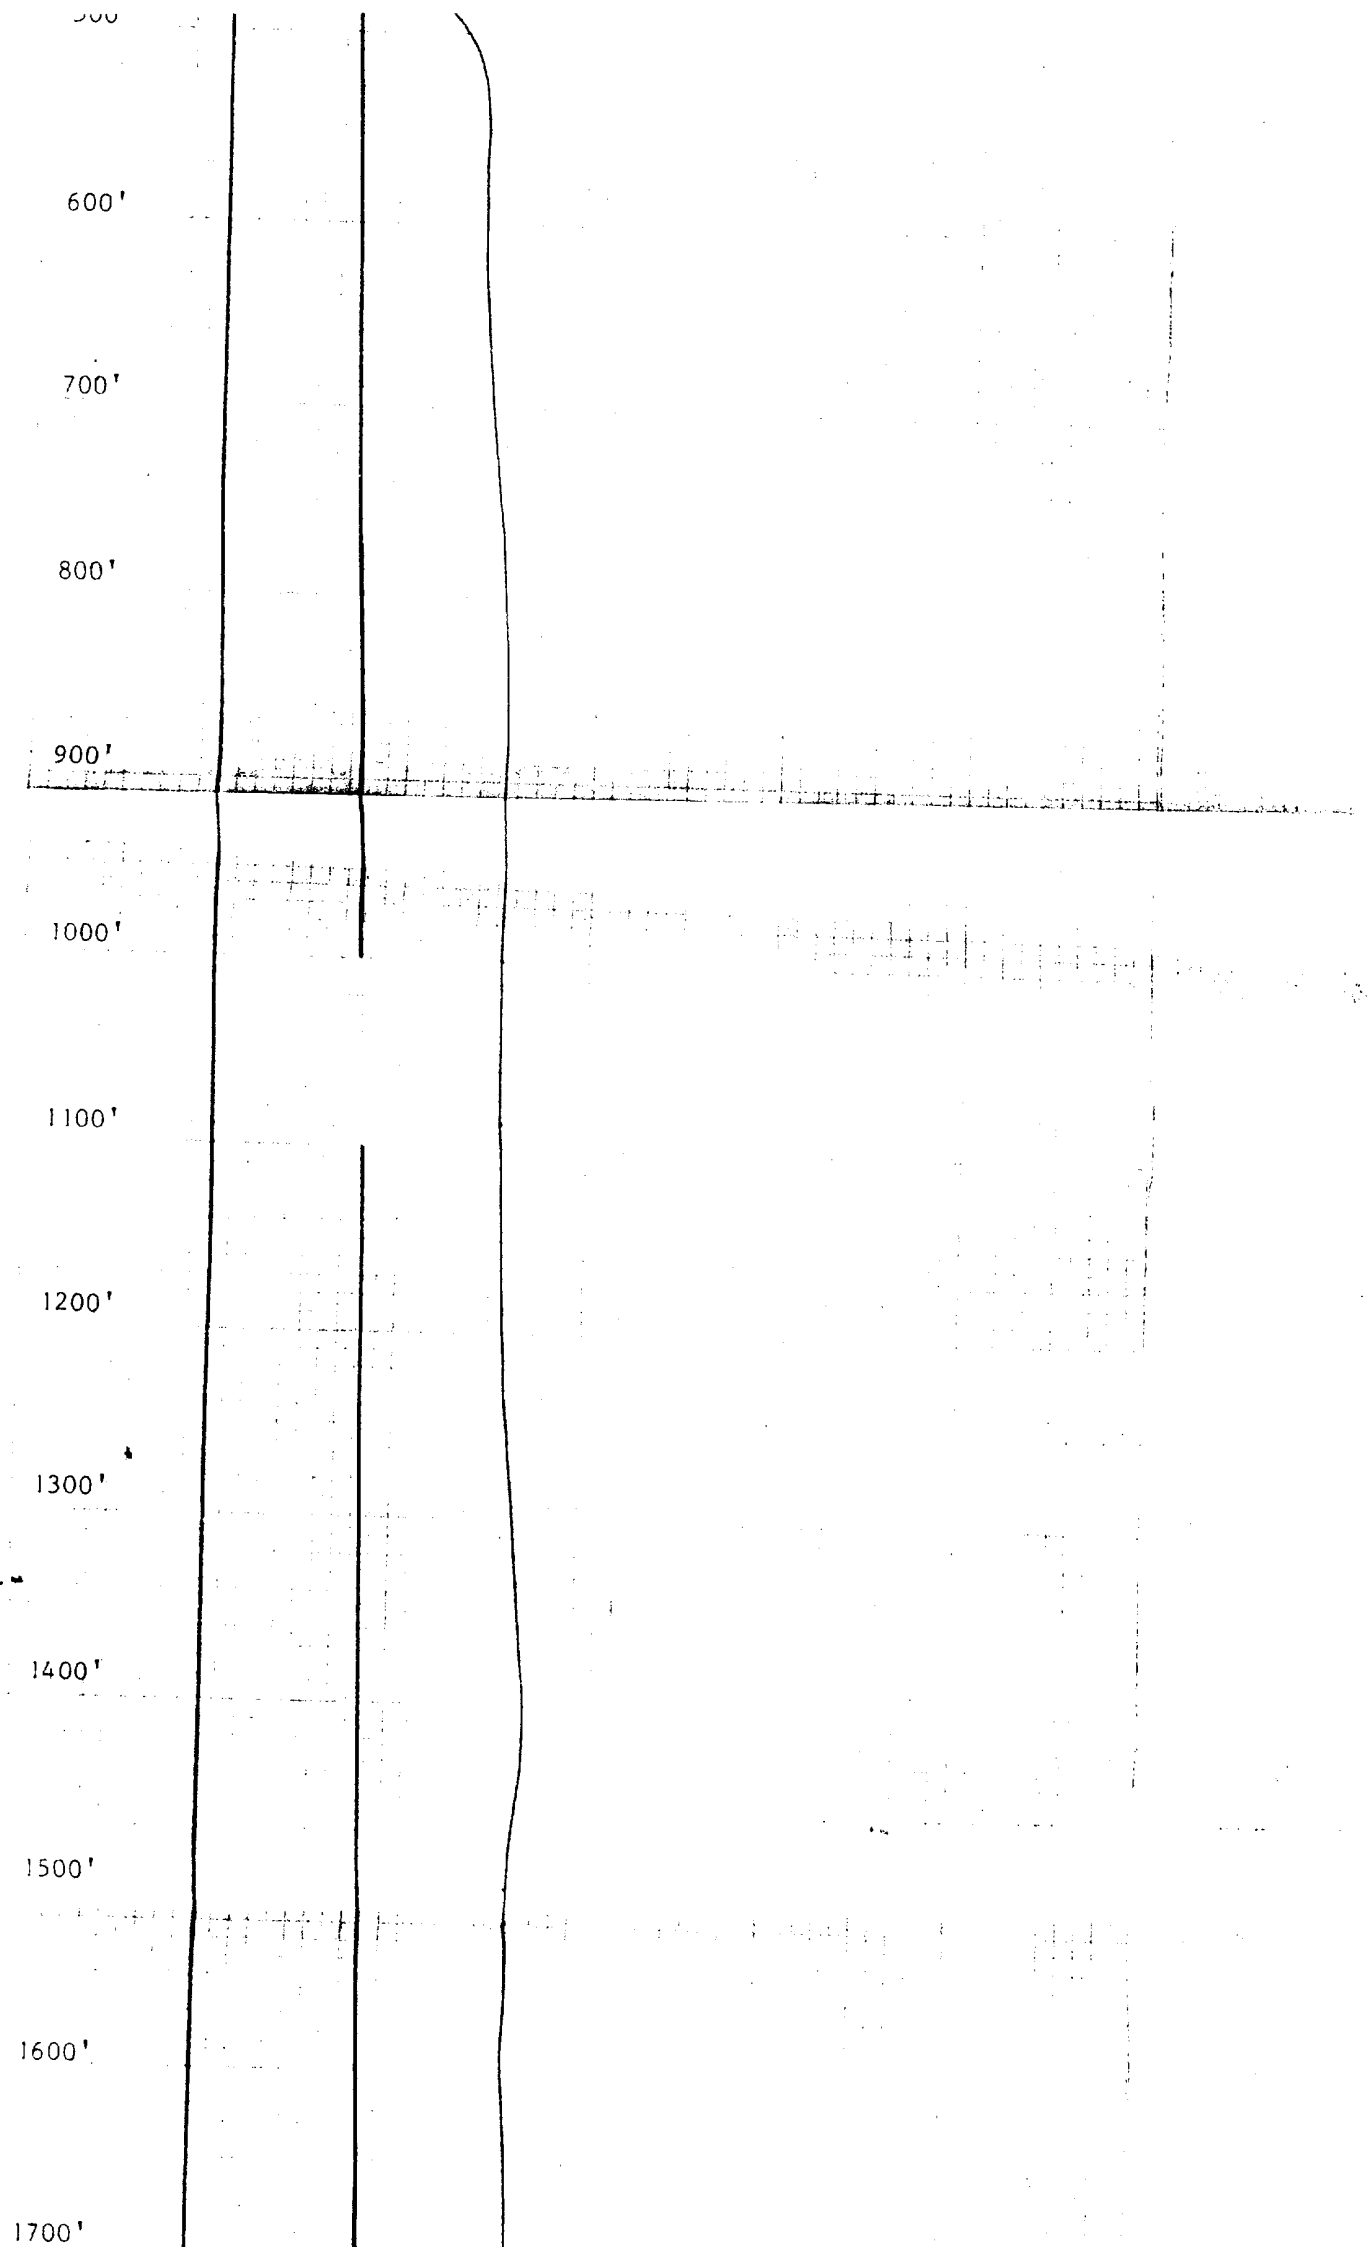

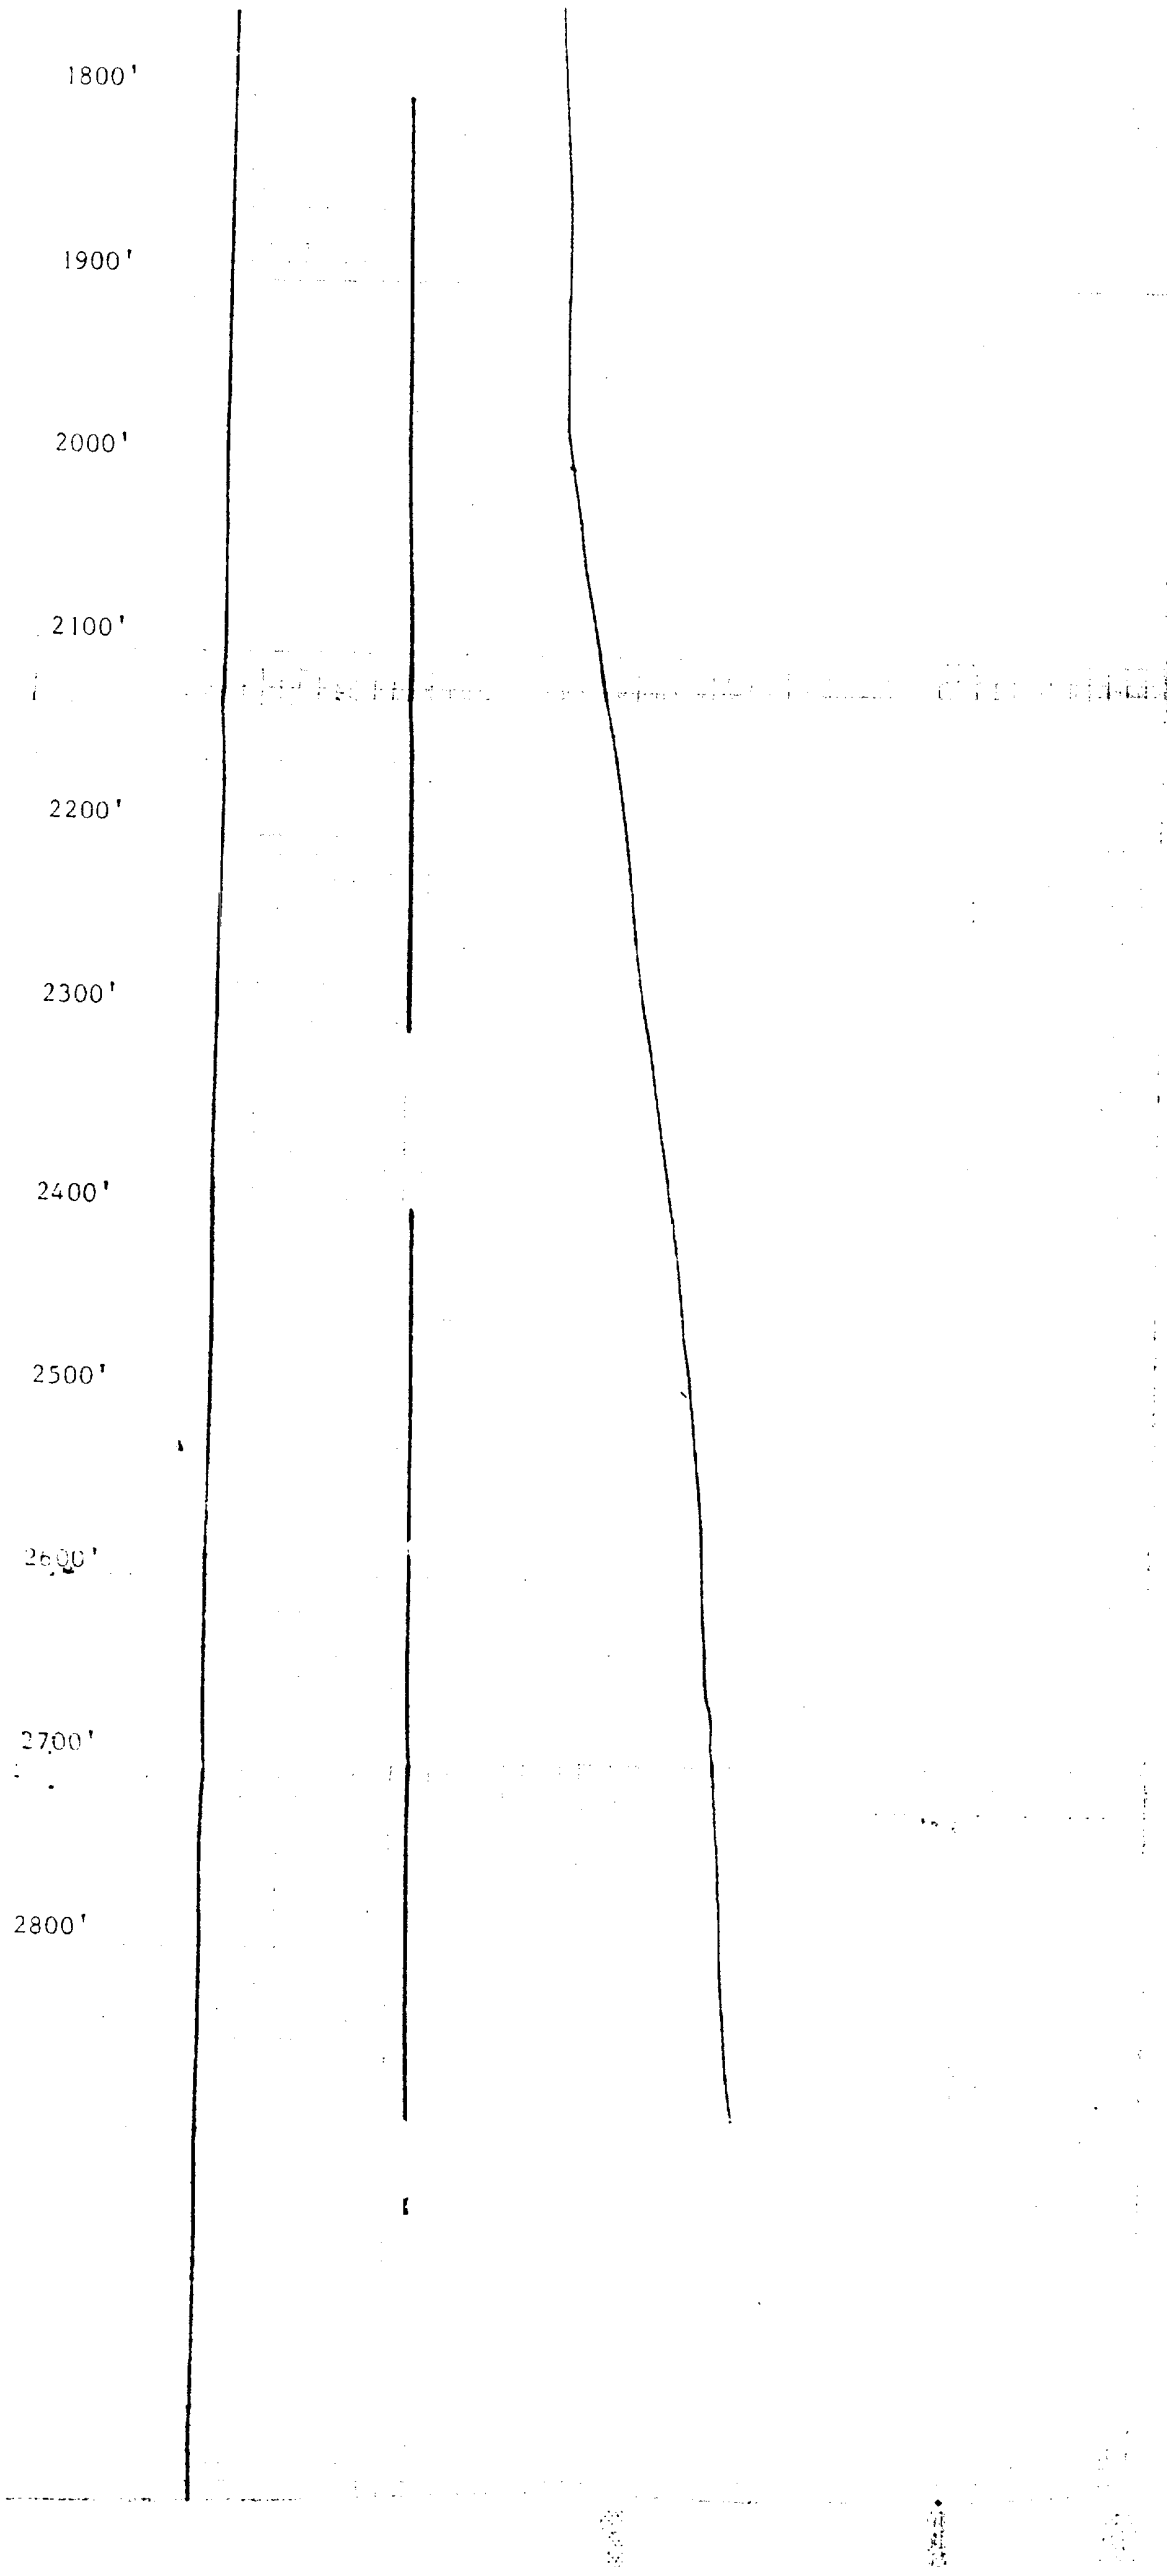

WILSON

FORM 432-2

SERVICE COMPANY

TEMPERATURE SURVEY

COMPANY.....Amoco Production

WELL.....9-E.....LEASE.....ALElliott D

COUNTY.....San Juan.....STATE.....New Mexico

SEC.....11.....TWP.....29N.....RGE.....9W

APPROX. TOP CEMENT.....2100'

Survey Begins at.....100'.....Ft. Ends at.....3570'.....Ft.

Approx. Fill-Up.....Max. Temp.

Log Measured From.....KB.....Run No.1

Casing Size	Casing Depth	Diam of Hole	Depth
4½" from	to	from 6½"	to
from	to	from	to

Date of Cementing.....9/28/85.....Time 3:20 AM

Date of Survey.....9/28/85.....Time 3:00 PM


Amount of Cement.....275 Cu Ft.

Recorded by.....Wilson.....Witnessed by.....

REMARKS OR OTHER DATA

Requested By Ed Merheny.....DV Tool 3615' / Ojo Alamo 1554'.

TEMPERATURE IN DEGREES FAHRENHEIT

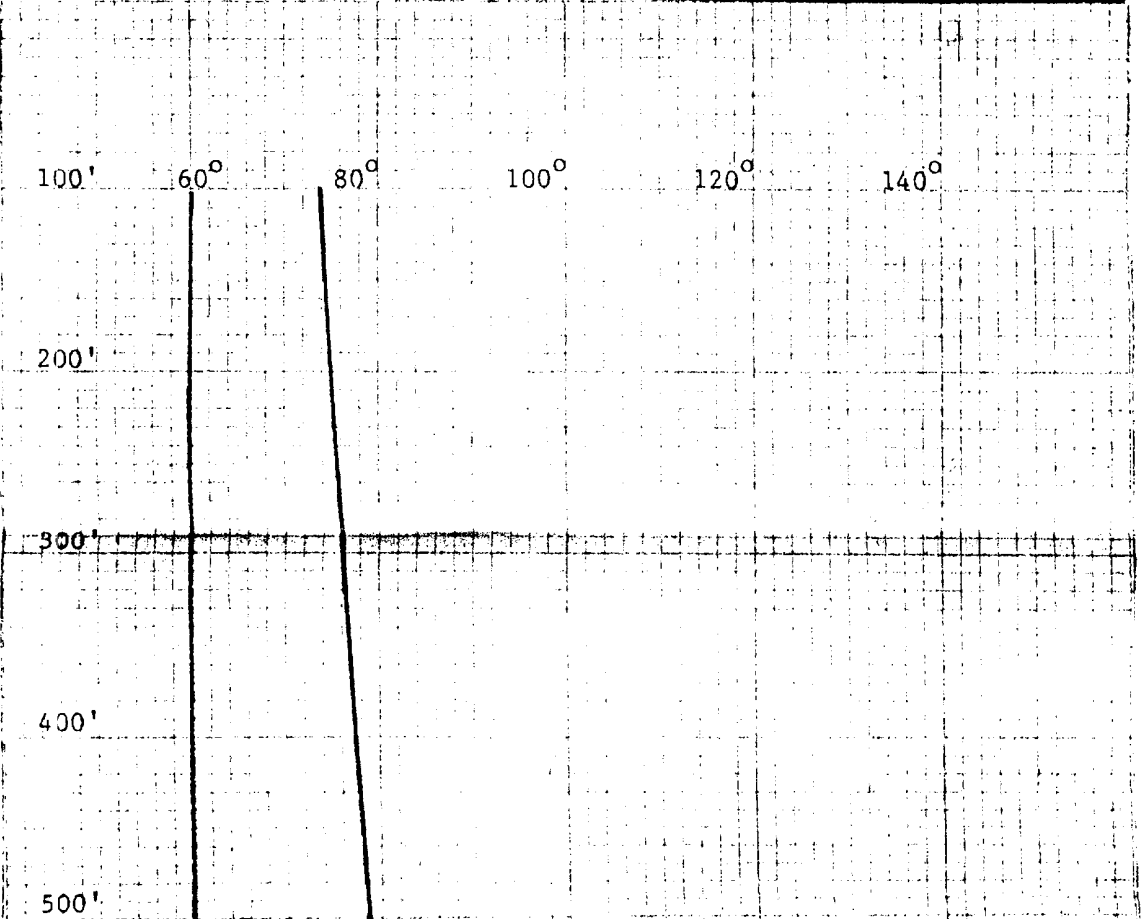

600'

700'

800'

900'

1000'

1100'

1200'

1300'

1400'

1500'

1600'

1700'

1800'

1900'

1900'

2000'

2100'

Anomaly 2100'

2200'

2300'

2400'

2500'

2600'

2700'

2800'

2900'

3000'

3100'

3200'

2700'

2800'

2900'

3000'

3100'

3200'

3300'

3400'

3500'

TD Surveyed 3570'
