




Midland Division
Exploration Production

Conoco Inc.
10 Desta Drive, Suite 100W
Midland, TX 79705-4500
(915) 686-5400

May 18, 1995

Mr. Johnny Robinson
Deputy O&G Inspector
Oil Conservation Division
Aztec District Office
1000 Rio Brazos Road
Aztec, New Mexico 87410



**Re: Federal #6, 30-045-08835, B-06-29N-11W
Failed Packer Leakage Test Response**

Dear Mr. Robinson:

As per the attached letter from your office on January 19, 1995 Conoco had proposed to repair the casing leak in this well which caused the failed packer leakage test and return it to dual completion. However, it was discovered in the process that additional problems with equipment and fill above the packer (shown by the attached diagram) make it uneconomical to completely repair the well for dual production.

Therefore, a new procedure will be prepared to plug back from the lower Dakota zone and repair the casing leak in order to return only the upper completion to production. This change in plans will require a new evaluation of the wellbore and the development of a new procedure.

Conoco requests that the initial remedial deadline of June 6, 1995 be extended to June 30 for submittal of a new procedure and to July 31 for initiation of activity. Thank you for your consideration of this change in plans for this well.

Very truly yours,

Jerry W. Hoover
Sr. Conservation Coordinator



STATE OF NEW MEXICO
ENERGY, MINERALS AND NATURAL RESOURCES DEPARTMENT
OIL CONSERVATION DIVISION
AZTEC DISTRICT OFFICE



GARY E. JOHNSON
GOVERNOR

JENNIFER A. SALISBURY
CABINET SECRETARY

1000 RIO BRAZOS ROAD
AZTEC, NEW MEXICO 87410
(505) 334-6178

January 19, 1995

Mr Dan Phillips
Conoco Inc
3315 Bloomfield Hwy
Farmington NM 87401

Post-It™ brand fax transmittal memo 7571		# of pages >
To <i>Scott Listiak</i>	From <i>Dan Phillips</i>	
Co.	Co.	
Dept.	Phone #	
Fax #	Fax #	

RE: Conoco Inc, Federal #6, 30-045-08835, B-06-29N-11W

Dear Dan:

The 1994 Packer Leakage Tests on the referenced well indicates communication between the producible zones. In order to comply with Rule #112A you are hereby directed to initiate remedial activity prior to June 6, 1994. 1995

Sincerely,

Johnny Robinson

Johnny Robinson
Deputy O&G Inspector

JR/sh

cc: well file

Please call prior to starting work

MOBILE # 320-0214

FEDERAL 6

6-T29N-R11W

EST RATE - 80-150
EST RES - .5-.8 BCF

HOMCO
53007 OR BACK OFF
TBS


1993

1.66 x 2 3/8" X-OVER SCREWED
ON DOWNHOLE.

FILL,
BRIDGE,
OR
CSG COLLAPSE

15M slate feel comfortable

5 1/2"
6881'

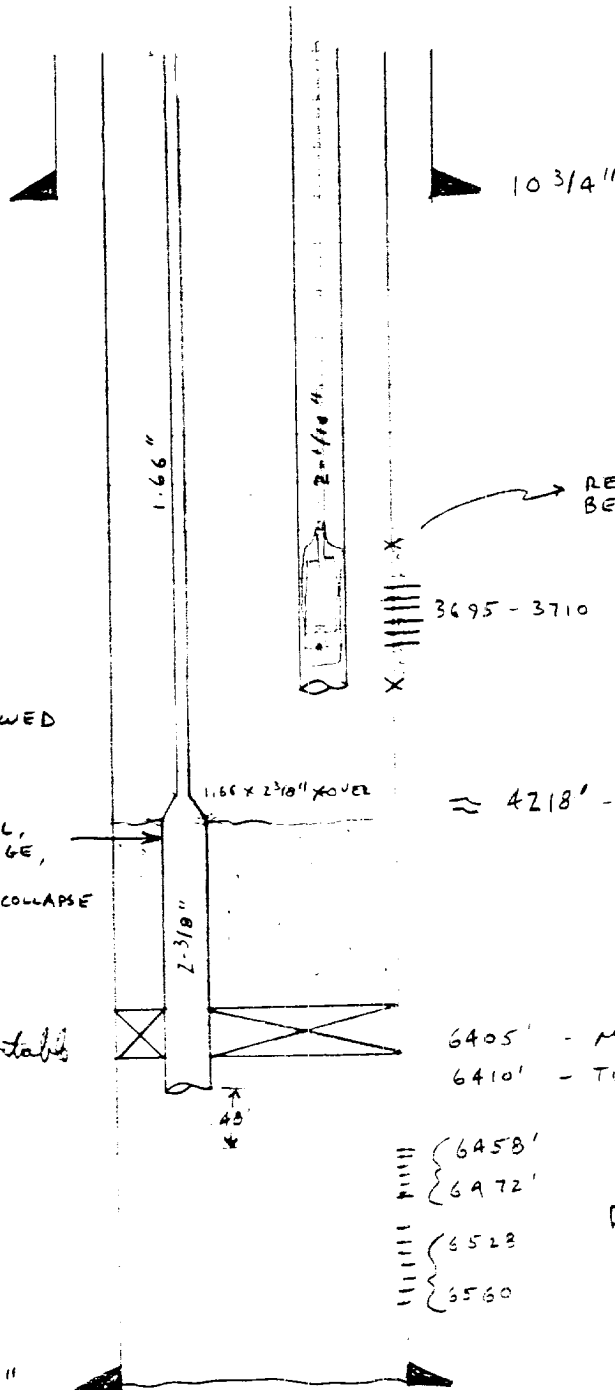

10 3/4"

REMEDIAL SQZ
BEFORE CH COMPLETION

3695-3710 (CLIFFHOUSE)

≈ 4218' - FREEPOINT RUN IN
2-3/8" - 1.66"

6405' - MODEL D '2.682' ? BORE)
6410' - TSG 2 3/8"

{ 6458'
6472'
6523
6560

DAKOTA

SCOTT LISTIAK
915 686-6139
