

CONFIDENTIAL

Form 3160-3
(March 2012)

HOBBS OCD

FORM APPROVED
OMB No. 1004-0137
Expires October 31, 2014UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APR 27 2016

APPLICATION FOR PERMIT TO DRILL OR REENTER

RECEIVED

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. NMNM121489
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator Devon Energy Production Company, L.P. (6137) ✓		7. If Unit or CA Agreement, Name and No.
3a. Address 333 West Sheridan Avenue Oklahoma City, OK 73102-5010		8. Lease Name and Well No. Coachwhip 26 Fed 4H (313483) ✓
3b. Phone No. (include area code) 405-552-6558		9. API Well No. 30-025-43189
4. Location of Well (Report location clearly and in accordance with any State requirements.) At surface Unit A, 330' FNL 300' FEL PP: 330' FNL, 400' FEL At proposed prod. zone Unit P, 330' FSL 350' FEL		10. Field and Pool, or Exploratory Triple X; Bone Spring (59900) ✓ K2
11. Sec., T. R. M. or Blk. and Survey or Area Sec, 26-T23S-R33E		12. County or Parish Lca
13. State NM		
14. Distance in miles and direction from nearest town or post office* Approximately 23 miles NW of Jal, NM.	15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) See attached map	16. No. of acres in lease 640 Acres
17. Spacing Unit dedicated to this well 160 Acres	18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. See attached map	19. Proposed Depth 15,201' MD / 10,557' TVD
20. BLM/BIA Bond No. on file CO-1104; NBM-000801	21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3661.6' GL	22. Approximate date work will start* 4/15/2016
23. Estimated duration 45 Days	24. Attachments	

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the BLM.

25. Signature <i>Linda Good</i>	Name (Printed/Typed) Linda Good	Date 6/11/2015
Title Regulatory Compliance Specialist		
Approved by (Signature) <i>/s/George MacDonald</i>	Name (Printed/Typed) George MacDonald	Date APR 22 2016
Title FIELD MANAGER		
Office CARLSBAD FIELD OFFICE		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 States any false, fictitious or fraudulent

(Continued on page 2)

The NMOCD Gas Capture Plan notice has been posted on the web site under Announcements/Notice to Operators. A copy of the GCP form is included with the notice and is also in the Forms section under Unnumbered forms. Please submit accordingly in a timely manner.

y department or agency of the United

*(Instructions on page 2)

Carlsbad Controlled Water Basin

K2
04/27/16Approval Subject to General Requirements
& Special Stipulations AttachedSEE ATTACHED FOR
CONDITIONS OF APPROVAL

APR 28 2016

Devon Energy, Coachwhip 26 Fed 4H

1. Geologic Formations

TVD of target	10,557'	Pilot hole depth	n/a
MD at TD:	15,201'	Deepest expected fresh water:	

Basin

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Rustler	1360	Barren	
Top of Salt	1630	Barren	
Base of Salt	5090	Barren	
Delaware	5285	Oil	
Cherry Canyon	6250	Oil	
Brushy Canyon	7590	Oil	
Bone Spring	9150	Oil	
1st BSPG Sand	10250	Oil	
2nd BSPG Lime	10697	Oil	

*H2S, water flows, loss of circulation, abnormal pressures, etc.

Devon Energy, Coachwhip 26 Fed 4H

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn	SF Collapse	SF Burst	SF Tension
	From	To							
17.5"	0	1,420'	13.375	48	H-40	STC	1.15	2.21	2.02
12.25"	0	4,300'	9.625	40	J-55	BTC	1.15	1.38	2.27
12.25"	4,300'	5,200'	9.625	40	HCK-55	BTC	1.41	2.77	4.82
8.75"	0	10,040'	7"	29	HCP-110	BTC	1.73	1.32	2.61
8.75"	10,040'	15,201'	5.5"	17	P-110	BTC	1.44	1.25	3.12
BLM Minimum Safety Factor							1.125	1.00	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Devon Energy, Coachwhip 26 Fed 4H

3. Cementing Program

Casing	# Sks	Wt. lb/ gal	H ₂ O gal/sk	Yld ft ³ / sack	500# Comp. Strength (hours)	Slurry Description
13-3/8" Surface	700	12.9	9.81	1.85	14	Lead: (65:35) Class C Cement: Poz (Fly Ash): 6% BWOC Bentonite + 5% BWOW Sodium Chloride + 0.125 lbs/sack Poly-E-Flake
	550	14.8	6.32	1.33	6	Tail: Class C Cement + 0.125 lbs/sack Poly-E-Flake
9-5/8" Inter.	1090	12.9	9.81	1.85	14	Lead: (65:35) Class C Cement: Poz (Fly Ash): 6% BWOC Bentonite + 5% BWOW Sodium Chloride + 0.125 lbs/sack Poly-E-Flake
	430	14.8	6.32	1.33	6	Tail: Class C Cement + 0.125 lbs/sack Poly-E-Flake
7 x 5- 1/2" Combo Prod.	310	10.4	16.9	3.17	16	Lead: Tuned Light [®] + 0.125 lb/sk Pol-E-Flake
	1360	14.5	5.31	1.2	25	Tail: (50:50) Class H Cement: Poz (Fly Ash) + 0.5% bwoc HALAD-344 + 0.4% bwoc CFR-3 + 0.2% BWOC HR-601 + 2% bwoc Bentonite

Actual cement volumes will be adjusted based on fluid caliper and caliper log data.

Casing String	TOC	% Excess
13-3/8" Surface	0'	100%
9-5/8" Intermediate	0'	75%
7 x 5-1/2" Production Casing	5000'	25%

4. Pressure Control Equipment

N	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
---	--

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
12-1/4"	13-5/8"	3M	Annular	x	50% of working pressure
			Blind Ram		3M
			Pipe Ram		
			Double Ram	x	
			Other*		
8-3/4"	13-5/8"	3M	Annular	x	50% testing pressure
			Blind Ram		3M
			Pipe Ram		
			Double Ram	x	
			Other*		

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

Y	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
---	---

Devon Energy, Coachwhip 26 Fed 4H

See
COA

See
COA

Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
Y	Are anchors required by manufacturer?
Y	<p>A <u>multibowl wellhead is being used</u>. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.</p> <p>Devon proposes using a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 3000 (3M) psi.</p> <ul style="list-style-type: none"> Wellhead will be installed by vendor's representatives. If the welding is performed by a third party, the vendor's representative will monitor the temperature to verify that it does not exceed the maximum temperature of the seal. Vendor representative will install the test plug for the initial BOP test. Vendor will install a solid steel body pack-off to completely isolate the lower head after cementing intermediate casing. After installation of the pack-off, the pack-off and the lower flange will be tested to 3M, as shown on the attached schematic. Everything above the pack-off will not have been altered whatsoever from the initial nipple up. Therefore the BOP components will not be retested at that time. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head will be cut and top out operations will be conducted. Devon will pressure test all seals above and below the mandrel (but still above the casing) to full working pressure rating. Devon will test the casing to 0.22 psi/ft or 1500 psi, whichever is greater, as per Onshore Order #2. <p>After running the 13-3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 3M will be installed on the wellhead system and will undergo a 250 psi low pressure test followed by a 3,000 psi high pressure test. The 3,000 psi high and 250 psi low test will cover testing requirements a maximum of 30 days, as per Onshore Order #2. If the well is not complete within 30 days of this BOP test, another full BOP test will be conducted, as per Onshore Order #2.</p> <p>After running the 9-5/8' intermediate casing with a mandrel hanger, the 13-5/8" BOP/BOPE system with a minimum rating of 3M will already be installed the wellhead.</p> <p>The pipe rams will be operated and checked each 24 hour period and each time the drill pipe is out of the hole. These tests will be logged in the daily driller's log. A 2" kill line and 3" choke line will be incorporated into the drilling spool below the ram BOP. In addition to the rams and annular preventer, additional BOP accessories include a kelly cock, floor safety valve, choke lines, and choke manifold rated at 3,000 psi WP.</p>

Devon Energy, Coachwhip 26 Fed 4H

	Devon requests a variance to use a flexible line with flanged ends between the BOP and the choke manifold (choke line). The line will be kept as straight as possible with minimal turns.
	See attached schematic.

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	1,420'	FW Gel	8.6-8.8	28-34	N/C
1,420'	5,300'	Saturated Brine	10.0-10.2	28-34	N/C
5,300'	15,201'	Cut Brine	8.5-9.3	28-34	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

*See
COA*

6. Logging and Testing Procedures

Logging, Coring and Testing	
x	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No Logs are planned based on well control or offset log information.
	Drill stem test? If yes, explain
	Coring? If yes, explain

Additional logs planned	Interval
Resistivity	Int. shoe to KOP
Density	Int. shoe to KOP
X CBL	Production casing
X Mud log	Intermediate shoe to TD
PEX	

Devon Energy, Coachwhip 26 Fed 4H

See
CORA

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	5105 psi
Abnormal Temperature	No

Mitigation measure for abnormal conditions: Lost circulation material/sweeps/mud scavengers.

Hydrogen Sulfide (H2S) monitors will be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

<input checked="" type="checkbox"/>	H2S is present
<input type="checkbox"/>	H2S Plan attached

8. Other facets of operation

Is this a walking operation? No.

Will be pre-setting casing? No.

Attachments

☒ Directional Plan

☐ Other, describe

devon

Coachwhip 26 Fed 4H
Lea Co, NM





Weatherford

Plan Data for Coachwhip 26 Fed 4H
Well: Coachwhip 26 Fed 4H
Type: Main Well
File Number:
Plan Folder: P1 Plan: P1-V1
Vertical Section: Position offset of origin from Slot centre:
+N/-S: 0.00USft Azimuth: 179.53°
+E/-W: 0.00USft
Magnetic Parameters:
Model: Field Strength: Declination: Dip: Date:
ICM: 4887(m) 7.2° 60.11° 2015-10-01



KB-3687
GL-3662

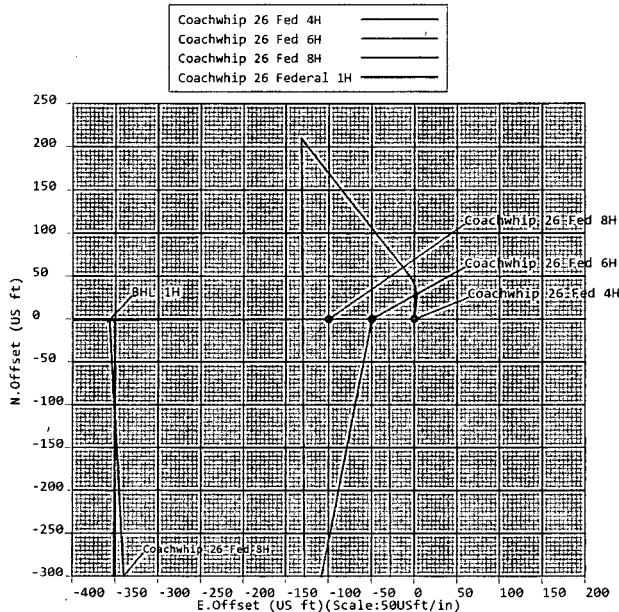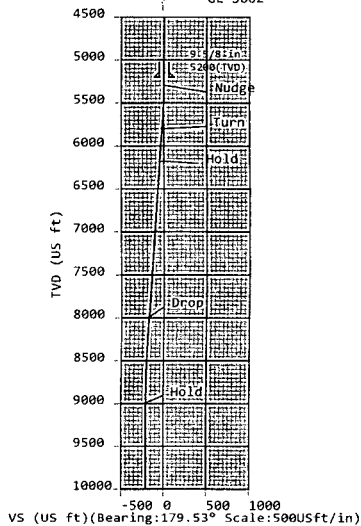

Plan Data for Coachwhip 26 Fed 4H

Plan Point Information:

MD	Inc	Az	TVD	+N/-S	+E/-W	Northing	Easting	VSec	DLS
(USft)	(°)	(°)	(USft)	(USft)	(USft)	(USft)	(USft)	(USft)	(DLSU)
0.00	0.00	0.00	0.00	0.00	0.00	467236.68	787875.60	0.00	0.00
5300.00	0.00	0.00	5300.00	0.00	0.00	467236.68	787875.60	0.00	0.00
5800.00	5.00	6.00	5799.37	21.68	2.28	467258.36	787877.88	-21.66	1.00
6178.24	5.00	321.50	6176.30	50.99	-6.26	467287.67	787869.34	-51.04	1.00
8000.00	5.00	321.50	7991.13	175.25	-105.10	467411.93	787770.50	-176.10	0.00
9000.00	0.00	0.00	8989.86	209.37	-132.25	467446.05	787743.35	-210.45	0.50
10090.00	0.00	0.00	10079.95	209.37	-132.25	467446.05	787743.35	-210.45	0.00
10841.23	90.14	179.53	10557.41	-269.22	-128.28	466967.46	787747.32	268.16	12.00
15201.09	90.14	179.53	10547.00	-4628.92	-92.18	462607.76	787783.42	4628.01	0.00



Plan Data for Coachwhip 26 Fed 4H

Slot: Coachwhip 26 Fed 4H
Position:
Offset is from Site centre
+N/-S: 0.00USft Northing: 467236.68USft Latitude: 32°16'55.2"
+E/-W: 0.00USft Easting: 787875.60USft Longitude: -103°32'8.1"
Elevation Above VRD: 3662.00USft

Plan Data for Coachwhip 26 Fed 4H

Target Set Information:

Name	TVD	+N/-S	+E/-W	Northing	Easting	Shape	Comment
(USft)	(USft)	(USft)	(USft)	(USft)	(USft)		
PBHL 4H	10547.00	-4628.92	-92.18	462607.76	787783.42	Cuboid	

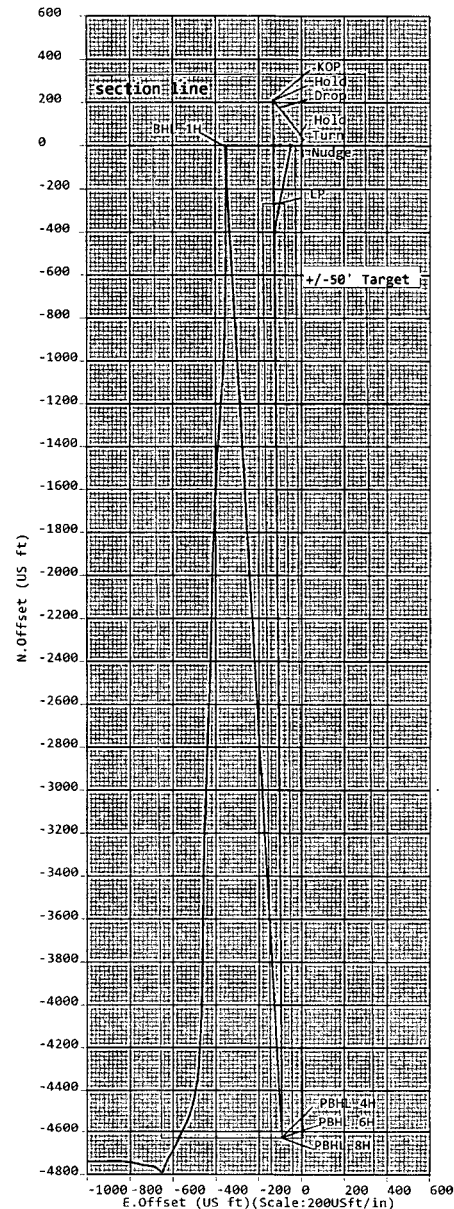

Sign Off: Russell Joyner
