

REENTRY &
COMPLETION
REPORT
W.D.W # 1

UIC-CL1-008

TELEPHONE
(505) 748-3311

EASYLINK
62905278



REFINING COMPANY

501 EAST MAIN STREET • P. O. BOX 159
ARTESIA, NEW MEXICO 88211-0159

FAX
(505) 746-6410 ACCTG
(505) 746-6155 EXEC
(505) 748-9077 ENGR
(505) 746-4438 P / L

October 7, 1998

Mr. Roger Anderson
Environmental Bureau
Oil Conservation Division
2040 S. Pacheco St.
Santa Fe, NM 87505-5472

Certified Receipt
Z 378 881 148

RE: Re-entry and Completion Report, Waste Disposal Well #1, Navajo Refining Co.

Dear Roger,

Enclosed, please find the final report on the above referenced well. This report is a complete account of all operations and testing done on the well. If there are any questions, please call me at 505-748-3311. Thank you for your attention to this matter.

Sincerely,
NAVAJO REFINING CO.

Darrell Moore
Environmental Mgr. for Water and Waste

Encl.



**REENTRY AND COMPLETION REPORT
WASTE DISPOSAL WELL NO. 1**

**NAVAJO REFINING COMPANY
ARTESIA, NEW MEXICO**

Envirocorp Project No. 70A4614

SEPTEMBER 1998

Prepared By:

**ENVIROCORP WELL SERVICES, INC.
Houston, Texas**

TABLE OF CONTENTS

| | |
|---|----|
| EXECUTIVE SUMMARY | vi |
| 1.0 INTRODUCTION | 1 |
| 2.0 SUMMARY OF DAILY OPERATIONS | 2 |
| 2.1 Preparation of the Drill Site | 2 |
| 2.2 Mobilization of the Drilling Equipment | 3 |
| 2.3 Reentry Operations | 3 |
| 2.4 Installation of the Protection Casing | 4 |
| 2.5 Perforating and Testing the Cisco Formation | 5 |
| 2.6 Installation of Injection Tubing | 7 |
| 2.7 Chronology of Daily Operations | 7 |
| 3.0 MECHANICAL INTEGRITY TESTING | 8 |
| 3.1 7 inch Protection Casing Inspection Log | 8 |
| 3.2 7 inch Protection Casing Pressure Test | 8 |
| 3.3 Cement Bond Logging | 8 |
| 3.3.1 9-5/8 inch Cement Bond Log | 8 |
| 3.3.2 7 inch Cement Bond Log | 9 |
| 3.4 Radioactive Tracer Survey | 9 |
| 3.5 Annular Pressure Test | 10 |
| 3.6 Differential Temperature Survey | 10 |
| 4.0 RESERVOIR EVALUATION | 12 |
| 4.1 Bottom-Hole Pressure Testing | 12 |
| 4.1.1 Static Gradient Survey and Bottom-Hole Pressure Analysis | 12 |
| 4.1.2 Analysis of the Falloff Test | 12 |
| 5.0 REGULATORY COMPLIANCE | 16 |
| 5.1 Siting | 16 |
| 5.2 Casing and Cementing | 16 |
| 5.3 Tubing and Packer | 17 |
| 5.4 Description of the Logging Program and Tests in the Intermediate and Long-String Sections of WDW-1 | 18 |
| 5.4.1 Directional Surveys | 18 |
| 5.4.2 Logging Program | 18 |
| 5.5 Mechanical Integrity Testing | 19 |

TABLE OF CONTENTS (Continued)

| | | |
|-----|---|----|
| 5.6 | Pressure Tests Conducted on WDW-1 | 19 |
| 5.7 | Physical and Chemical Characteristics of the Formation Fluids | 20 |
| 5.8 | Regulatory Witnessing | 20 |
| 6.0 | CERTIFICATION | 21 |

TABLES

| | |
|----------------|--|
| TABLE 2.0-I: | 13-3/8 inch Surface Casing Detail |
| TABLE 2.0-II: | 9-5/8 inch Intermediate Casing Detail |
| TABLE 2.0-III: | Detailed Tubular Program for WDW-1 |
| TABLE 2.4-I: | 7 inch Protection Casing Detail |
| TABLE 2.4-II: | Plugged-Back Record |
| TABLE 2.5-I: | Perforating Record |
| TABLE 2.6-I: | 4-1/2 inch Injection Tubing Detail |
| TABLE 4.1.1-I: | Bottom-Hole Pressure Survey, Static Gradient Measurement |
| TABLE 5.2-I: | Cementing Program for WDW-1 |
| TABLE 5.4.1-I: | Deviation Survey Record |

FIGURES

| | |
|-----------------|--|
| FIGURE 1.0-1: | Surveyor's Plat of Well Location, WDW-1 |
| FIGURE 2.0-1: | Plugged and Abandoned Wellbore Schematic, Mewbourne Oil Company Chalk Bluff "31" State, Well No. 1 |
| FIGURE 2.0-2: | Current Wellbore Schematic, WDW-1 |
| FIGURE 2.6-1: | Schematic of EVI Oil Tools (Arrow) Model X-1 Retrievable Packer |
| FIGURE 3.5-1: | Annular Pressure Test Chart, WDW-1 |
| FIGURE 4.1.1-1: | Bottom-Hole Static Gradient Survey, WDW-1 |

TABLE OF CONTENTS (Continued)

- FIGURE 4.1.2-1: Test Overview for WDW-1**
- FIGURE 4.1.2-2: Log-Log Plot with Derivative for WDW-1**
- FIGURE 4.1.2-3: Horner Plot of Falloff Data for WDW-1**
- FIGURE 4.1.2-4: Expanded Horner Plot of Falloff Data for WDW-1**
- FIGURE 4.1.2-5: Cartesian Plot with Simulated Results Overlaid**
- FIGURE 4.1.2-6: Horner Plot with Simulated Results Overlaid**
- FIGURE 4.1.2-7: Log-Log Plot with Simulated Results Overlaid**

APPENDICES

- APPENDIX 1.0-1: Approval Letters from the New Mexico Water Quality Control Commission, dated May 21, 1998 and July 2, 1998**
- APPENDIX 2.0-1: Original Well Installation Daily Reports, Mewbourne Oil Company, Chalk Bluff State "31", Well No. 1**
- APPENDIX 2.0-2: Well Completion or Recompletion Report and Log, Form C-105**
- APPENDIX 2.0-3: Sundry Notice for Plug and Abandonment, Form C-103**
- APPENDIX 2.5-1: Formation Fluid Analysis**
- APPENDIX 2.5-2: Packer Fluid Corrosion Inhibitor**
- APPENDIX 2.7-1: Chronology of Daily Activities**
- APPENDIX 4.1-1: Bottom-Hole Pressure Field Data Recorded During the Injectivity/Falloff Test for WDW-1**
- APPENDIX 4.1.2-1: PanSystem2, Well Test Analysis Report, WDW-1**

TABLE OF CONTENTS (Continued)

EXHIBITS

- EXHIBIT 2.0-1:** Long-String Hole, Dual Laterlog/Gamma Ray/Micro-Spherically Focused Electric Log
- EXHIBIT 2.0-2:** Long-String Hole, Spectral Density/Gamma Ray/Dual Spaced Neutron Log
- EXHIBIT 2.0-3:** Long-String Hole, Compensated Sonic Log
- EXHIBIT 2.3-1:** Long-String Hole, Formation Microscanner Imaging Results
- EXHIBIT 2.3-2:** Long-String Hole, Caliper/Gamma Ray Log
- EXHIBIT 3.1-1:** Protection Casing Inspection Log
- EXHIBIT 3.3.1-1:** Intermediate Casing Cement Bond/Variable Density Log
- EXHIBIT 3.3.1-2:** Letter of Interpretation of the Intermediate Casing Cement Bond/Variable Density Log
- EXHIBIT 3.3.2-1:** Protection Casing Cement Bond/Variable Density Log
- EXHIBIT 3.3.2-2:** Letter of Interpretation of the Protection Casing Cement Bond/Variable Density Log
- EXHIBIT 3.4-1:** Radioactive Tracer Log, Conducted on July 31, 1998
- EXHIBIT 3.4-2:** Injection Profile Analysis Log
- EXHIBIT 3.6-1:** First Differential Temperature Survey, Conducted on July 23, 1998
- EXHIBIT 3.6-2:** Second Differential Temperature Survey, Conducted on July 31, 1998

EXECUTIVE SUMMARY

Navajo Refining Company (Navajo) contracted Envirocorp Well Services, Inc. (Envirocorp) to prepare an application for permit to reenter a plugged and abandoned Class II well to conduct injection testing within the Wolfcamp, Cisco, and Canyon Formations. The permit application was submitted to the State of New Mexico Oil Conservation Commission (OCD) in February 1998.

The OCD granted approval for the reentry and testing on the wellbore by letter dated May 21, 1998. In June 1998, Navajo contracted Envirocorp to prepare a detailed engineering plan to reenter, test and complete the plugged and abandoned Mewbourne Oil Company Chalk Bluff State "31", Well No. 1.

Under contract with Navajo, Envirocorp commenced field operations on July 6, 1998. An area was cleared and a drill pad was constructed for the drilling rig. The abandoned wellbore was located and a riser was welded on for the installation of a blowout preventer assembly. A lined reserve pit was constructed for the containment of drill cuttings and fluids.

A rotary drilling rig was moved in and rigged up and the OCD was notified, and verbally approved the commencement of reentry operations on July 8, 1998. An 8-3/4 inch bit was lowered into the wellbore to drill out cement plugs within the 9-5/8 inch intermediate casing. The 9-5/8 inch intermediate casing was successfully pressure tested to 900 pounds per square inch (psi) prior to drilling out the cement plug across the shoe.

The 8-3/4 inch bit was lowered into the open-hole portion of the wellbore and drilled out cement plugs were drilled out to a total reentry depth of 9160 feet. A cement bond log was conducted within the 9-5/8 inch intermediate casing. A fracture identification log, 4-arm caliper, and gamma-ray log were conducted within the open-hole portion of the wellbore.

The seven inch protection casing was installed with cement circulated through the annular space from bottom to the surface using a two-stage pump and plug method on July 14, 1998. Good returns were observed at the surface while cementing. The rotary drilling equipment was released and moved off site.

A completion rig and blowout preventers were moved in and rigged up on July 20, 1998. A 6-1/8 inch bit was lowered into the wellbore to clean out and pressure test the seven inch protection casing. On July 20, 1998, the seven inch casing was successfully pressure tested

to 1559 pounds per square inch gauge (psig) above the differential valve tool at 5498 feet. On July 21, 1998, the seven inch casing was successfully pressure tested to 1573 psig from surface to the plugged-back total depth of 9004 feet.

The wellbore was displaced with a clean brine fluid and a baseline temperature and casing inspection survey were performed. A cement bond log was performed over the length of the seven inch protection casing. The injection interval (Cisco Formation) was perforated from 8220 feet to 8476 feet at two jet shots per foot. A sample of the formation fluid was obtained for analysis and the lower injection interval was stimulated using 5000 gallons of 15% HCl acid and rock salt as a diverter.

The injection interval (Cisco Formation) was perforated from 7924 feet to 8188 feet at two jet shots per foot. A retrievable bridge plug and packer were set to isolate the newly perforated interval. A sample of the formation fluid was obtained for analysis and the perforations were stimulated using 5000 gallons of 15% HCl acid and rock salt as a diverter. The packer and bridge plug were removed from the wellbore in preparation for the pressure buildup portion of the falloff test.

On July 30, 1998 and July 31, 1998, an injection pressure buildup and falloff test was conducted. Upon completion of the falloff test a differential temperature log was conducted from surface to a total depth of 8997 feet. A radioactive tracer log was conducted and the results obtained from the survey confirmed external mechanical integrity of the wellbore.

A 4-1/2 inch outside diameter (OD) injection tubing and packer were installed in the well to 7879 feet. An extended annular pressure test was performed to confirm stabilization within the well system. On August 4, 1998, an annular pressure test was performed in accordance with the requirements of the OCD. The OCD witnessed the annular pressure test which successfully confirmed internal mechanical integrity at a pressure of 704 psig.

Upon conclusion of the annular pressure test, the wellhead tree assembly was installed and all equipment was rigged down and moved out.

1.0 INTRODUCTION

Navajo reentered, tested and completed the plugged and abandoned Mewbourne Oil Company Chalk Bluff State "31", Well No. 1 wellbore for injection of plant waste effluent. The name of the new waste disposal well will be designated as Waste Disposal Well No. 1 (WDW-1). The wellbore is located in Section 31, T17S, R28E, Unit Letter O, approximately 11 miles east-southeast of Artesia, in Eddy County, New Mexico. A surveyor's plat of the well location is shown on Figure 1.0-1. The construction and testing of this well were performed in compliance with the provisions of the New Mexico Water Quality Control Commission Regulations (NMWQCCR), dated November 15, 1996, Subpart V, Section Nos. 5204 and 5205, and the United States Environmental Protection Agency Code of Federal Regulations, 40 CFR 146.12, Subpart B.

Envirocorp was contracted by Navajo to reenter and test WDW-1. The construction and testing of this Non-Commercial Class I Nonhazardous Waste Disposal Well were permitted by the New Mexico Energy, Minerals, and Natural Resources Department, OCD by letters dated May 21, 1998 and July 2, 1998 (Appendix 1.0-1). All work associated with WDW-1 was completed in accordance with the provisions specified in the permit approved by the OCD.

The work for WDW-1 was designated as Envirocorp's Project No. 70A4614. This report summarizes all work performed on WDW-1 and includes the filing of the necessary documents.

2.0 SUMMARY OF DAILY OPERATIONS

The original wellbore was designated as the Mewbourne Oil Company, Chalk Bluff "31" State, Well No. 1, installed July 1992 to September 1993. The Daily Reports are presented in Appendix 2.0-1. The wellbore was constructed with a 13-3/8 inch OD surface casing set at 390 feet and cemented to surface. Table 2.0-I presents the 13-3/8 inch surface casing detail.

A 12-1/4 inch hole was drilled to a depth of 2555 feet. Open-hole logs were conducted to include resistivity, spontaneous potential, porosity, and gamma ray as presented in Exhibits 2.0-1 through 2.0-3.

A 9-5/8 inch intermediate casing was installed across the salt sections to a depth of 2555 feet and cemented to surface. Table 2.0-II presents the 9-5/8 inch intermediate casing detail. An 8-3/4 inch hole was drilled to a depth of 10,200 feet to test potentially productive hydrocarbon zones. Subsequently, the wellbore was abandoned in September 1993, as presented on Figure 2.0-1.

A well completion report, OCD Form C-105, is presented as Appendix 2.0-2. The Sundry notice, OCD Form C-103, following plug and abandonment operations, is presented as Appendix 2.0-3.

The reentry, testing, and completion operations for WDW-1 are presented in this section. Details of certain operations are referenced in the text and included as figures, exhibits, tables, and appendices.

Figure 2.0-2 is the current wellbore schematic for WDW-1. Table 2.0-III contains the detailed tubular program for WDW-1.

2.1 Preparation of the Drill Site

From June 26, 1998 to June 29, 1998, the location was prepared for the selected rig. An 80-foot by 50-foot divided reserve pit, lined with six-mil plastic, was constructed for circulating while drilling the cement plugs. An extension to the 9-5/8 inch casing and rental wellhead was installed as a base for the blowout preventers. A rathole and mousehole were constructed as specified by the selected drilling contractor.

2.2 Mobilization of the Drilling Equipment

From July 6, 1998 to July 8, 1998, the drilling rig was moved in and rigged up. A double ram and annular blowout preventer were installed and tested for pressure control.

2.3 Reentry Operations

On July 8, 1998, drilling operations commenced at 4:00 PM. The top of the first cement plug was encountered at 374 feet and drilled out at 445 feet. The drillpipe was lowered into the hole to 1620 feet and a pressure test within the 9-5/8 inch surface casing was performed. The surface casing was successfully pressure tested to 900 psi for 30 minutes with a loss of only 35 psi (-3.89%). The drillpipe was lowered into the well to tag the top of the second cement plug at 2188 feet.

On July 9, 1998, the cement plug was drilled out at 2465 feet. The drillpipe was lowered into the well to tag the third cement plug at 3543 feet. The plug was drilled out at 4479 feet. The drillpipe was lowered into the well to tag the top of the fourth cement plug at 5092 feet. The cement plug was drilled out at 5220 feet. The wellbore was washed down to tag the top of the fifth cement plug at 5785 feet. The cement plug was drilled out at 5840 feet. The drillpipe was lowered into the hole to 6240 feet and became differentially stuck.

On July 10, 1998, 50 barrels of oil were spotted around the drill collars and the drill string worked free. The drillpipe was washed in hole to tag the top of the sixth cement plug at 6395 feet. The cement plug was drilled out at 6745 feet and the drillpipe was washed in hole to 6808 feet.

On July 11, 1998, the drillpipe was washed in hole to tag the top of the seventh cement plug at 7613 feet. The cement plug was drilled out at 7726 feet and the drillpipe was washed in the hole to tag the top of the eighth cement plug at 8293 feet. The cement plug was drilled out to 8385 feet and the drillpipe was washed in hole to 8635 feet.

On July 12, 1998, the drillpipe was washed in hole to the final reentry depth of 9160 feet. The drillpipe, collars, and bit were removed from the well in preparation for logging operations. Schlumberger performed a cement bond, gamma ray, casing collar locator survey within the 9-5/8 inch surface casing from 2548 feet to surface.

On July 13, 1998, Schlumberger performed a fracture identification survey from 9144 feet to 4000 feet (Exhibit 2.3-1). Schlumberger's interpretation describing the results obtained from the Formation Microscanner Imaging results is also presented in Exhibit 2.3-1. A 4-arm caliper survey was processed from 9143 feet to the base of the 9-5/8 inch surface casing. Cement volumes were determined based on the results from the caliper survey plus 20% excess as shown in Exhibit 2.3-2.

The drillpipe was lowered into the well to 9115 feet and the wellbore was circulated and cleaned prior to pulling out of the hole and laying down the drillpipe and collars.

2.4 Installation of the Protection Casing

On July 14, 1998, 259 joints of seven inch 26- and 29-pound-per-foot casing were installed to 9094 feet. Table 2.4-I presents the seven inch protection casing detail. The float collar was placed two joints above the pack-off float shoe at 9007 feet. A stage tool was emplaced at 5498 feet. Halliburton Energy Services pumped the first-stage cement consisting of 600 sacks of Modified Class H cement plus additives mixed at 13 pounds per gallon (ppg). The stage tool was opened and a total of 142 sacks of cement were observed circulating back to the surface. Good returns were observed during the first stage cement operations.

The well was circulated for eight hours and the second-stage cement was pumped consisting of 220 sacks of Interfill Class C plus additives mixed at 11.7 ppg; followed by 163 sacks of Modified Class H plus additives mixed at 13 ppg. The second stage was circulated to surface in excess of 75 sacks. A one inch tremie line was lowered into the well annulus to 20 feet. A total of 20 sacks of premium cement plus 3% calcium chloride cement were circulated to the surface.

On July 15, 1998, waited on the cement, cleaned the mud pits, cut the casing and removed the blowout preventers. The drilling rig was released at 15:00 hours. A seven inch Type "R" Larkin wellhead was installed and the drilling rig was rigged down.

On July 16, 1998, the drilling rig was stacked adjacent to the wellsite location. Anchors were installed and the seven inch casing was stabilized at the surface with six yards of ready mix cement.

On July 20, 1998, the completion rig, reverse unit, work string, and blowout preventers were moved in and rigged up. A 6-1/8 inch OD bit was picked up on six 4-1/8 inch

OD drill collars and lowered into the well on the work string to 5455 feet. The well system was pressurized to 1580 psig and monitored for test. A loss of six psi per 30 minutes was observed (-0.38%) during the pressure test. The differential valve tool was partially drilled out.

On July 21, 1998, the differential valve tool was drilled out and the bit was lowered into the well to drill and wash to a plugged-back total depth of 9004 feet. Table 2.4-II presents the plug-back record. The well system was pressurized to 1600 psi and monitored for test. A loss of eight psi per 30 minutes was observed (-0.51%) during the pressure test.

On July 22, 1998, a bit and casing scraper were lowered into the wellbore to 8823 feet. A total of 250 gallons of 15% HCl inhibited acid preceded displacement of 350 barrels of clean brine water. Fluid returns were circulated to the reserve pit.

On July 23, 1998, a differential temperature log was conducted within the seven inch protection casing from surface to 8997 feet. The well system was pressurized to 1000 psi and a cement bond log was conducted from 8997 feet to 135 feet. A casing inspection survey, consisting of an electromagnetic thickness tool and multi-finger casing caliper tool, was conducted from 8991 feet to surface.

2.5 Perforating and Testing the Cisco Formation

On July 24, 1998, the wellbore was perforated within the injection interval at two jet shots per foot using retrievable casing guns. The selected intervals were as follows: 8220-54 feet, 8260-70 feet, 8280-8302 feet, 8370-78 feet, 8360-66 feet, 8400-10 feet, 8419-23 feet, 8430-46 feet, 8460-64 feet, and 8470-76 feet (Table 2.5-I). The wellbore fluid level dropped during the perforating operations.

On July 25, 1998, a packer was set above the perforated interval with tailpipe to 8479 feet (bottom perforation at 8476 feet). A swab line was rigged up and a total of 139 barrels (2.39 tubing volumes) were recovered. Samples of the formation fluid were retained for analysis, which is presented as Appendix 2.5-1. The fluid level maintained approximately 1700 feet to 1800 feet during the swabbing operations.

On July 26, 1998, an initial step-rate test was performed down the 2-7/8 inch work string using an 8.7 ppg brine water. A maximum rate of 4.85 barrels per minute (bpm) was attained within the permitted injection pressure. The well was acidized in four stages using 5000 gallons of 15% HCl and 2400 pounds of gelled rock salt as

diverter. Injectivity significantly improved as the well accepted fluid on a vacuum at four bpm to 10 bpm. The pump-in pressure at 12 bpm was 73 psi after friction pressure was subtracted from the surface injection pressure.

On July 27, 1998, the wellbore was perforated within the injection interval at two jet shots per foot using retrievable casing guns. The selected intervals were as follows: 8170-88 feet, 8160-64 feet, 8118-27 feet, 8132-40 feet, 8066-80 feet, 8050-56 feet, 7974-8030 feet, and 7924-42 feet (Table 2.5-I). A total of sixteen 500-barrel storage tanks were moved in and manifolded together. An 8.7 ppg brine water was loaded into each tank.

On July 28, 1998, a retrievable bridge plug and packer were lowered into the wellbore. The packer assembly began hanging up at 4830 feet and was removed from the wellbore and replaced.

On July 29, 1998, the retrievable bridge plug was set at 8214 feet and pressure tested to 500 psi with the packer set at 8193 feet. The packer was pulled up hole and set at 7852 feet. A swab line was rigged up and a total of 112 barrels (2.33 tubing volumes) were recovered. Samples of the formation fluid were retained for analysis, which is presented as Appendix 2.5-1. The fluid level maintained approximately 1500 feet to 1600 feet during the swabbing operations.

An initial step-rate test was performed down the seven inch casing using an 8.7 ppg brine water. A maximum rate of 4.36 bpm was attained within the permitted injection pressure. The well was acidized in four stages using 5000 gallons of 15% HCl and 2300 pounds of gelled rock salt as a diverter. Injectivity significantly improved as the well accepted fluid on a vacuum at four bpm to four bpm.

On July 30, 1998, a digital quartz surface readout pressure gauge and memory backup were lowered into the wellbore to 7924 feet. The initial bottom-hole pressure was 2928.16 pounds per square inch absolute (psia) at 125.41°F. Injection of an 8.7 ppg brine water was initiated at 10 bpm on a vacuum and continued for 12.45 hours. The final injection pressure was 3071.85 psia at 90.80°F. Injection of brine was discontinued and the bottom-hole pressure falloff was monitored at the surface.

On July 31, 1998, the pressure falloff test was discontinued and the tools were removed from the wellbore while making static gradient stops at 6000 feet, 3000 feet, 1700 feet, and at the surface. A differential temperature survey was performed from

the surface to a wireline total depth of 8997 feet. A radioactive tracer survey was performed below 7800 feet. The results from the radioactive tracer survey confirmed external mechanical integrity of the seven inch casing and provided an injection profile across the perforated intervals.

On August 1, 1998, the 2-7/8 inch work string was laid down and the 4-1/2 inch, 11.60 lb/ft, N-80, LT&C injection tubing was delivered and tallied. The wellbore was displaced with an 8.7 ppg corrosion inhibited brine water as packer fluid. The corrosion inhibitor was a Unichem TECHNI-HIB 370, as presented in the product information and Material Safety Data Sheets presented in Appendix 2.5-2.

2.6 Installation of Injection Tubing

On August 2, 1998, a 7" x 3.5" EVI Oil Tools Model X-1 packer (Figure 2.6-1) was lowered into the wellbore on the 4-1/2 inch injection tubing (Table 2.6-I). The packer was set at 7879 feet with 15,000 pounds of compression and the annulus was pressurized to 700 psig. The annular pressure was monitored for stabilization through August 4, 1998.

On August 4, 1998, an annulus pressure test was performed. The OCD elected to witness the test. The annulus was pressurized to 704 psig and monitored for 30 minutes. The final test pressure was 705 psig for an increase of 1 psi (0.14%) per 30 minutes, which is within the 10% allowed by the regulations. The wellhead tree assembly was installed and all rig and ancillary equipment were rigged down and moved off site.

The installation of WDW-1 was completed on August 4, 1998. The wellhead was secured and the well remained shutin pending approval of the permit by the OCD.

2.7 Chronology of Daily Operations

Appendix 2.7-1 is a Chronology of Daily Activities from the Field Activity Reports.

3.0 MECHANICAL INTEGRITY TESTING

The demonstration of the mechanical integrity of WDW-1, required by NMWQCCR Subpart V, Section 5204(A) to (D) and Section 5205(A)(1)(a), included a casing inspection log of the seven inch protection casing, pressure testing of the seven inch protection casing, cement bond log of the 9-5/8 inch and seven inch casings, a radioactive tracer survey, a differential temperature survey, and an annular pressure test. Results of these tests demonstrated that the well had internal and external mechanical integrity.

3.1 7 Inch Protection Casing Inspection Log

On July 23, 1998, Wedge Dia-Log, Inc. conducted a casing inspection log from 8997 feet to the surface (Exhibit 3.1-1). A 60-arm multi-finger caliper tool and an electromagnetic thickness tool were used to conduct the casing inspection survey. The data obtained from the survey may be used as a baseline for future comparison.

3.2 7 Inch Protection Casing Pressure Test

The protection casing was successfully pressure tested to 704 psig on August 4, 1998 for 30 minutes. A pressure gain of 1 psi was observed, as indicated on the pressure test chart shown on Figure 3.5-1.

3.3 Cement Bond Logging

A cement bond log was conducted within the 9-5/8 inch intermediate casing during the reentry operations from 2548 feet to the surface. Upon installation of the seven inch protection casing, a cement bond log was conducted. There are a total of three strings of casing which were successfully installed and cemented across the base of the underground source of drinking water (USDW).

3.3.1 9-5/8 inch Cement Bond Log

On July 12, 1998, a cement bond with variable density log was performed within the 9-5/8 protection casing from 2548 feet to the surface (Exhibit 3.3.1-1). The data obtained from the cement bond log confirmed a continuous column of cement with good bonding characteristics behind the 9-5/8 protection casing from 2548 feet to 400 feet. The hydraulic coupling was lost above 400 feet and the tool would not respond. A letter of interpretation of the intermediate casing cement bond/variable density log is presented as Exhibit 3.3.1-2.

3.3.2 7 Inch Cement Bond Log

A cement bond with variable density log was conducted on the seven inch protection casing on July 23, 1998 (Exhibit 3.3.2-1). As indicated on the log, a continuous column of cement extends from the base of the protection casing at 8997 feet to the surface. Cement bonding was indicated to be sufficient for completion of the well. A letter of interpretation of the protection casing cement bond/variable density log is presented as Exhibit 3.3.2-2.

The adequacy of the cement above the top of the perforations was successfully confirmed in the subsequent radioactive tracer survey discussed in Section 3.4 and differential temperature survey discussed in section 3.6.

The results obtained from the cement bond and variable density logs conducted on the surface casing and the protection casing established that a continuous column of cement, with good compressive strength and cement bond, existed behind both casings. The installation of three casing strings across the base of the USDW, two of which demonstrate a continuous column of cement from surface to bottom, assures protection of the USDW.

3.4 Radioactive Tracer Survey

A radioactive tracer survey for WDW-1 was performed on July 31, 1998, following the reservoir evaluation testing operations and prior to the installation of the injection packer. The radioactive tracer survey consisted of running statistical checks, two baseline gamma ray surveys, and ejecting four slugs of radioactive material. Two (2) of the slug tests were stationary time-drive surveys and two were moving surveys. The radioactive tracer log, conducted July 31, 1998, is presented as Exhibit 3.4-1. An injection profile analysis log is presented as Exhibit 3.4-2. All tests were conducted while injecting a nonhazardous brine water into the well.

The radioactive tracer tool was lowered into the well to tag the total depth at 8997 feet. A pre-survey baseline gamma ray log was conducted from 7800 feet to 8997 feet. A pre-survey statistical check was performed at 7904 feet (20 feet above the top perforation) for five minutes.

The moving surveys were conducted with the radioactive tracer tool initially positioned at 7800 feet (above the intended packer setting depth). The injection of a nonhazardous brine was initiated at a rate of one bpm. A slug of radioactive

material was ejected and verified for intensity. The slug's downward movement was recorded by logging upward through the slug intermittently as it moved downward and dissipated into the perforated interval. This test was repeated at an injection rate of one bpm. The results obtained from the moving surveys determined that the ejected radioactive material was exiting into the permitted injection interval; therefore, mechanical integrity was confirmed between the intended packer setting depth and the top of the injection interval.

The injection of a nonhazardous brine was increased to 10 bpm. The radioactive tracer tool was positioned with the bottom detector at 7904 feet, which is 20 feet above the top of the top perforation, and a stationary time-drive survey was conducted. The tool remained stationary across the interval and the well was monitored for upward migration above 7904 feet for 15 minutes. This test was repeated and monitored for upward migration above 7904 feet for 15 minutes. No upward migration of radioactive material was observed during either survey.

A post-survey baseline gamma ray log was performed from 8997 feet to 7800 feet, with no residual radioactive material.

3.5 Annular Pressure Test

The official annular pressure test was conducted on August 4, 1998. The injection packer and tubing had been installed and the wellbore allowed to attain a thermal equilibrium. A Barton circular chart recorder (Serial Number MFG-1438), scaled from 0 psig to 1000 psig, was installed to monitor the annulus pressure. The OCD representative was present to witness the annulus pressure test. At 0900 hours, the initial annulus pressure was 704 psig. At 0930 hours, the final annulus pressure was 705 psig. This represents a pressure gain of 1.00 psi in 30 minutes, which is within the limit of 10% in 30 minutes allowed by the OCD. An annulus pressure test chart is presented as Figure 3.5-1.

3.6 Differential Temperature Survey

A baseline differential temperature survey was performed on July 23, 1998 (Exhibit 3.6-1) following the cleanout of the seven inch protection casing to 8997 feet. On July 31, 1998, a second differential temperature survey was performed following the reservoir evaluation testing, which included 12-hour injection of an 8.7 ppg brine water into the permitted injection interval (Exhibit 3.6-2).

As indicated on the July 23, 1998 baseline differential temperature log, the wellbore temperature increased steadily from 78.0 degrees at the surface to 137.9 degrees at 8993 feet. A temperature gradient of 0.01 degrees per foot was observed.

On July 31, 1998, a second differential temperature log was performed following the injection of brine water into the injection interval. A temperature gradient of .01 degrees per foot was observed from surface to the top perforation at 7924 feet. A significant cooling anomaly was observed within the perforated injection interval as temperatures cooled to 95.2 degrees. The data obtained from the differential temperature survey confirmed external mechanical integrity of the seven inch protection casing and may be used for comparison during future surveys.

4.0 RESERVOIR EVALUATION

4.1 Bottom-Hole Pressure Testing

The bottom-hole pressure testing which was conducted on WDW-1, following the completion of the well, was designed to obtain the best estimate of permeability and transmissibility in the reservoir. The pressure testing on WDW-1 consisted of a static gradient survey and an injectivity/falloff test. Appendix 4.1-1 lists the time and pressure data recorded during the static gradient survey, injection period, and falloff period.

4.1.1 Static Gradient Survey and Bottom-Hole Pressure Analysis

On July 31, 1998, static gradient measurements were performed after conducting the injection/falloff test on WDW-1. Pressure data from the gradient stops made at the surface, 1700 feet, 3000 feet, 6000 feet, and 7924 feet are shown on Table 4.1.1-I. The gradient data are presented graphically as Figure 4.1.1-1. The static fluid gradient at 7924 feet was determined to be 0.456 psi per foot. The fluid level was at approximately 1500 feet.

4.1.2 Analysis of the Falloff Test

On July 30, 1998, an Eccosetex surface readout digital quartz pressure transducer was positioned at 7924 feet in WDW-1 and allowed to stabilize for approximately 45 minutes. Injection into WDW-1 commenced at 0920 hours at an injection rate of 420 gallons per minute (gpm). WDW-1 was shut in at 2153 hours and the bottom-hole pressure and temperature were recorded for 9.2 hours.

The pressure data obtained during the falloff test were analyzed with the assistance of the commercially available pressure transient analysis software program "PanSystem2, Version 2.5". Appendix 4.1.2-1 contains the output from this software program. Figure 4.1.2-1 shows the pressure response recorded by the surface pressure tool from the time the tool was in place through the 9.2-hour shutin period. Figure 4.1.2-2 is a log-log diagnostic plot of the falloff data, showing change in pressure and pressure derivative versus equivalent shutin time. The radial flow period is denoted on Figure 4.1.2-2.

The reservoir permeability was determined from the radial flow region of the superposition Horner plot (Figure 4.1.2-3). The radial flow regime begins at a Horner time of 23.9 and continues to 12.0. Figure 4.1.2-4 shows an expanded view of the

superposition Horner plot. The slope of the radial flow period was determined to be 4.356711 psi per cycle.

An estimate of mobility-thickness, kh/μ , for the reservoir was determined from the following equation:

$$\frac{kh}{\mu} = 162.6 \frac{qB}{m}$$

where,

kh/μ = transmissibility, md-ft/cp

q = flow rate, barrels per day

μ = viscosity, centipoise

B = formation volume factor, reservoir vol/surface vol

m = slope of semi-log straight line, psi/cycle

Using an injection rate of 420 gpm (14,400 barrels per day) and the information previously mentioned results in a transmissivity of 537,433 md-ft/cp:

$$\begin{aligned} \frac{kh}{\mu} &= 162.6 \frac{(14,400)(1.0)}{4.356711} \\ &= 537,433 \text{ md-ft/cp} \end{aligned}$$

Multiplying this value by the viscosity, μ , results in transmissibility, kh :

$$\begin{aligned} kh &= \left(\frac{kh}{\mu} \right) \mu \\ &= (537,433)(0.53) \\ &= 284,839 \text{ md-ft} \end{aligned}$$

And finally, permeability is determined by dividing transmissibility by the formation thickness. The formation thickness is 253 feet, which results in a permeability of 1126 md.

$$\begin{aligned}
 k &= \frac{(k h)}{h} \\
 &= \frac{284,839}{253} \\
 &= 1126 \text{ md}
 \end{aligned}$$

The skin factor was determined from the following equation:

$$s = 1.151 \left[\frac{p_{wf} - p_{1 \text{ hr}}}{m_1} - \log \left(\frac{k_p}{\phi \mu c_i r_w^2} \right) + 3.23 \right]$$

where,

- s = formation skin damage at open perforations, dimensionless
- 1.151 = constant
- p_{wf} = flowing pressure immediately prior to shutin, psi
- $p_{1 \text{ hr}}$ = pressure determined by extrapolating the first radial flow semi-log line to a Δt of one hour, psi
- m_1 = slope of the first radial flow semi-log line, psi/cycle
- k_p = permeability of the formation opposite the open perforations, md
- ϕ = porosity of the injection interval, fraction
- μ = viscosity of the fluid the pressure transient is traveling through, centipoise
- c_i = total compressibility of the formation plus fluid, psi^{-1}
- r_w = radius of the wellbore, feet
- 3.23 = constant

The final flowing pressure, p_{wf} , was 3071.61 psia. The pressure determined by extrapolating the radial flow semi-log line to a Δt of one hour, $p_{1 \text{ hr}}$, was 2930.27 psi. The porosity of the injection interval, ϕ , is 0.10 and the total compressibility, c_i , is $8.4 \times 10^{-6} \text{ psi}^{-1}$. The wellbore radius, r_w , is 0.3646 feet. Using these values in addition to the previously determined parameters, m and k , results in a skin of 29.23:

$$s = 1.151 \left[\frac{3071.61 - 2930.27}{4.356711} - \log \left(\frac{1126}{(0.10)(0.53)(8.4 \times 10^{-6})(0.3646)^2} \right) + 3.23 \right]$$

$$= 29.23$$

The "Auto-Match" feature of PanSystem2 was used to improve upon the reservoir parameters. The final results of the auto-match are shown on Figures 4.1.2-5 through 4.1.2-7. These figures show the falloff data in cartesian, superposition Horner, and log-log formats with the simulated pressures overlaid.

5.0 REGULATORY COMPLIANCE

The construction of WDW-1 was performed in accordance to the regulatory considerations and standards specified in the approved permit application dated February 27, 1998; the NMWQCCR, dated November 15, 1998, Subpart V, Section Nos. 5204 and 5205; and the United States Environmental Protection Agency 40 CFR 146.12.

5.1 Siting

Navajo reentered, tested, and completed a plugged and abandoned wellbore located in Section 31, T17S, R28E, Unit Letter O, approximately 11 miles east-southeast of Artesia, in Eddy County, New Mexico. The disposal well permit, dated February 27, 1998, includes provisions for the location, depth of injection, and specific reentry and completion requirements. The Navajo WDW-1 will inject plant effluent into a formation which is beneath the lowermost formation containing, within one quarter of a mile of the wellbore, ground water having 10,000 mg/l total dissolved solids or less. A plat of the Navajo WDW-1 well location is shown on Figure 1.0-1.

5.2 Casing and Cementing

Installation and cementing of the casing were completed in accordance with NMWQCCR Subpart V, Section 5205(B)(2).

Table 2.0-III is the detailed tubular program for WDW-1. Table 5.2-I is the Cement Program for WDW-1.

A 17-1/2 inch surface hole was drilled to a depth of 390 feet RKB. A 13-3/8 inch OD, 48 lb/ft, J-55 grade surface casing was installed to a depth of 390 feet RKB and cemented in place using the pump and plug method. The surface casing was cemented with a lead slurry of 375 sacks of Class "C" Lite cement containing 3% calcium chloride and 1/2 pound per sack (lb/sx) Flocele. This was followed by a tail slurry of 150 sacks of Class C cement containing 3% calcium chloride. The cement was circulated to surface. A total of 525 sacks of cement was used and recorded on Form C-105 (Appendix 2.0-2).

A 12-1/4 inch intermediate hole was drilled to a depth of 2555 feet RKB. A 9-5/8 inch OD, 36 lb/ft, J-55 grade intermediate casing was installed to a depth of 2555 feet RKB and cemented in place using the pump and plug method. The intermediate

casing was cemented with a lead slurry of 800 sacks of Class "C" Lite cement containing 1/2 lb/sx Flocele, two lb/sx Gilsonite, and 12% salt. This was followed by a tail slurry of 200 sacks of Class C cement containing 2% calcium chloride. The cement was circulated to surface. A total of 1000 sacks of cement was used and recorded on Form C-105 (Appendix 2.0-2).

An 8-3/4 inch hole was drilled to a total depth of 10,200 feet and the wellbore was originally plugged and abandoned to surface. The abandoned 8-3/4 inch wellbore was reentered and cleaned out to 9160 feet RKB. A seven inch OD, 26 lb/ft and 29 lb/ft, N-80 and P-110 grade protection casing was installed to a depth of 9094 feet RKB. A differential valve tool was positioned at 5498 feet and the protection casing was cemented in two stages. The first stage, from 9094 feet to 5498 feet, consisted of 600 sacks of modified Class "H" cement containing 0.4% CFR-3, five lb/sx Gilsonite, 0.5% Halad-344, and one lb/sx salt mixed at 13 ppg. The differential valve tool was opened and cement returns were observed at the surface. The well was circulated for approximately eight hours prior to performing the second stage. The second stage, from 5498 feet to surface, consisted of two cement slurries. The lead slurry consisted of 220 sacks of Interfill C (35% Pozalin, 65% Class "C" cement, and 6% gel). The tail slurry consisted of 550 sacks of a modified Class "H" cement containing 0.4% CFR-3, five lb/sx Gilsonite, 0.5% Halad-344, and one lb/sx salt mixed at 13 ppg. The cement were circulated to the surface in excess of 75 sacks of cement returns. A total of 1370 sacks of cement were used to cement the protection casing in place. A CBL/VDL log was run on the protection casing and established a full column of annular cement from the bottom to the surface.

5.3 Tubing and Packer

Installation of the tubing and packer were conducted in accordance with NMWQCCR Subpart V, Section 5205(B)(3).

The WDW-1 injection tubing is a 4-1/2 inch OD, 11.60 lb/ft, N-80, LT&C connection, carbon steel pipe. The injection tubing was connected directly into an EVI Oil Tools Model X-1 injection packer set at 7879 feet. The tubing was designed to withstand possible future corrosion due to the injected fluids and the maximum burst and collapse pressures and tensile stresses, which may be experienced during the operational life of the well. Table 2.0-III is the detailed tabular program for WDW-1. Figure 2.6-1 is a schematic of the EVI Oil Tools Model X-1 injection packer installed in WDW-1.

5.4 Description of the Logging Program and Tests in the Intermediate and Long-String Sections of WDW-1

5.4.1 Directional Surveys

Deviation checks were obtained during the reentry of WDW-1, which were in accordance with NMWQCCR Subpart V, Section 5205(A)(4)(a).

The deviation checks were conducted within the 8-3/4 inch open-hole interval below the 9-5/8 inch surface casing. Deviation checks were obtained during the reentry of WDW-1 at frequent intervals to determine the location of the borehole and to assure that vertical avenues for fluid movement, in the form of diverging holes, were not created.

Table 5.4.1-I contains the deviation survey data obtained by a Totco survey tool from the surface to 9160 feet RKB.

5.4.2 Logging Program

The logging program for WDW-1 was completed in accordance with the regulations specified in NMWQCCR Subpart V, Section 5205(A)(4)(b).

| <u>TYPE OF LOG</u> | <u>TYPE OF HOLE LOGGED</u> | <u>INTERVAL (ft)</u> | <u>REFERENCE</u> |
|--|--------------------------------|--------------------------|------------------|
| <u>Intermediate Casing</u> | | | |
| Cement Bond Log Variable Density Log Gamma Ray | Cased Hole | 0 to 2548 | Exhibit 3.3.1-1 |
| <u>Long-String Casing</u> | | | |
| Dual Laterolog Gamma Ray Micro-Spherically Focused Electric Log | Open Hole | 2546 to 10,182 | Exhibit 2.0-1 |
| Spectral Density Dual Spaced Neutron Log Gamma Ray | Open Hole | 350 to 10,139 | Exhibit 2.0-2 |
| Compensated Sonic Log Gamma Ray | Open Hole | 350 to 10,181 | Exhibit 2.0-3 |
| Formation Microscanner Imaging Results | Open Hole | 4000 to 9143 | Exhibit 2.3-1 |

| <u>TYPE OF LOG</u> | <u>TYPE OF HOLE LOGGED</u> | <u>INTERVAL (ft)</u> | <u>REFERENCE</u> |
|--|--------------------------------|--------------------------|------------------|
| <u>Long-String Casing</u> | | | |
| Caliper Log Gamma Ray | Open Hole | 2553 to 9143 | Exhibit 2.3-2 |
| Cement Bond Log Variable Density Log Gamma Ray | Cased Hole | 0 to 8990 | Exhibit 3.3.2-1 |
| Casing Evaluation Log w/Multi-Finger Caliper Tool w/Electromagnetic Casing Caliper Thickness Tool | Cased Hole | 0 to 8997 | Exhibit 3.1-1 |
| Temperature Log | Cased Hole | 0 to 8997 | Exhibit 3.6-1 |
| Temperature Log | Cased Hole | 0 to 8997 | Exhibit 3.6-2 |

5.5 Mechanical Integrity Testing

The demonstration of the mechanical integrity of WDW-1, required by NMWQCCR Subpart V, Section 5204(A) to (D) and Section 5205(A)(1)(a), is discussed in detail in Section 3.0 of this report. The associated logs and interpretation of results obtained from the mechanical integrity tests are also included in Section 3.0 of this report.

5.6 Pressure Tests Conducted on WDW-1

The 9-5/8 inch and seven inch casing strings were tested for internal mechanical integrity using a liquid medium. These tests were conducted in accordance with NMWQCCR Subpart V, Section 5204(A) and (B)(1)(a).

On July 8, 1998, the 9-5/8 inch intermediate casing was successfully pressure tested to 900 psig for 30 minutes using an 8.3 ppg freshwater-based mud system. A pressure loss of 35 psi was observed during the test period, which is below the 10% tolerance allowed by the OCD.

The seven inch protection casing was successfully pressure tested to 704 psig on August 4, 1998 for 30 minutes using an 8.7 ppg brine water system. A pressure gain of one psi was observed, as indicated on the pressure test chart shown on Figure 3.5-1.

5.7 Physical and Chemical Characteristics of the Formation Fluids

In accordance with NMWQCCR Subpart V, Section 5205(A)(3)(h), an analysis describing the physical and chemical characteristics of the formation fluids, extracted from the Cisco Formation, is presented as Appendix 2.5-1.

The well materials used to construct WDW-1 were compatible with fluids with which the materials may be expected to come into contact. Well materials would be deemed to have compatibility as long as the materials used in the construction of the well meet or exceed standards developed for such materials by the American Petroleum Institute (API), The American Society for Testing Materials (ASTM), or comparable standards acceptable to the NMWQCC.

5.8 Regulatory Witnessing

In accordance with NMWQCCR Subpart V, Section 5205(A)(5), notification prior to commencement of the reentry, cementing and casing, well logging, and mechanical integrity tests was communicated with the OCD, Artesia, New Mexico office. The OCD had an opportunity to witness all installation, logging, and testing as required in NMWQCCR Section 5205(A)(5).

6.0 CERTIFICATION

I certify under penalty of law that I have personally examined and am familiar with the information submitted in this document and all attachments and that, based on my inquiry of those individuals immediately responsible for obtaining the information, I believe that the information is true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment.

NAME: Darrell Moore

TITLE: Env. Mgr. for Water and Waste

SIGNATURE: Darrell Moore

DATE: 10/7/98

TABLES

TABLE 2.0-I**13-3/8 INCH SURFACE CASING DETAIL**

| JOINTS | DESCRIPTION | LENGTH (feet) | DEPTH TO TOP (feet) |
|---------------|---|--------------------------|--------------------------------|
| | KB to Top of Casing | | -3.25 |
| 8 | 13-3/8 inch, 48 lb/ft, J-55, STC | 348.21 | + 3.25 (above KB) |
| 1 | 13-3/8 inch, 48 lb/ft, J-55, STC SJ w/If | 43.83 | 344.96 |
| 1 | 13-3/8 inch, Notched Texas Pattern Shoe | 1.21 | 388.79 |
| | Casing Bottom at 390 feet KB | | |

TABLE 2.0-II**9-5/8 INCH INTERMEDIATE CASING DETAIL**

| JOINTS | DESCRIPTION | LENGTH (feet) | DEPTH TO TOP (feet) |
|---------------|---|--------------------------|--------------------------------|
| | KB to Top of Casing | | -8.18 |
| 56 | 9-5/8 inch, 36 lb/ft, J-55, STC | 2518.23 | +8.18 |
| 1 | Davis-Lynch Float Collar | 1.40 | 2510.05 |
| 1 | 9-5/8 inch, 36 lb/ft, J-55, LTC | 42.55 | 2511.45 |
| 1 | Davis-Lynch Guide Shoe | 1.00 | 2554.00 |
| | 9-5/8 inch casing bottom at 2555 feet KB | | |

TABLE 2.0-III
DETAILED TUBULAR PROGRAM, WDW-1

| TYPE | DEPTH ¹ | DESCRIPTION |
|---------------------|------------------------|---|
| Surface Casing | 0 feet to 390 feet | 13-3/8 inch outside diameter, 0.330 inch wall, 48 lb/ft, J-55, STC |
| Intermediate Casing | 0 feet to 2555 feet | 9-5/8 inch outside diameter, 0.400 inch wall, 36 lb/ft, J-55, STC |
| Protection Casing | 0 feet to 5845 feet | 7 inch outside diameter, 0.362 inch wall, 26 lb/ft, P-110, LTC |
| | 5845 feet to 7031 feet | 7 inch outside diameter, 0.408 inch wall, 29 lb/ft, P-110, LTC |
| | 7031 feet to 9094 feet | 7 inch outside diameter, 0.408 inch wall, 29 lb/ft, N-80, LTC |
| Injection Tubing | 0 feet to 7879 feet | 4-1/2 inch outside diameter, 0.250 inch wall, 11.60 lb/ft, N-80, LT&C |
| Packer | Set at 7879 feet | EVI Oil Tools (Arrow) Model X-1 Retrievable Packer, 7 inch x 3.5 inch, minimum inside diameter = 3.0 inches, carbon steel |

¹ All depths are relative to the Kelly Bushing.

NAVAJO REFINING COMPANY, WDW-1

7" CASING TALLEY
PROTECTORS OFF - 7/12/98

TD=9160 FEET 7/12/98

| JT # | LENGTH | BOTTOM | TOP |
|------------|--------|----------|------|
| Fit Shoe | 2.60 | N-80 | 9094 |
| 1 | 42.00 | 29#N-80 | 9091 |
| 2 | 42.02 | 29#N-80 | 9049 |
| Fit Collar | 0.60 | N-80 | 9007 |
| 3 | 38.19 | 29#N-80 | 9007 |
| 4 | 39.13 | 29#N-80 | 8969 |
| 5 | 47.14 | 29#N-80 | 8929 |
| 6 | 41.84 | 29#N-80 | 8882 |
| 7 | 40.78 | 29#N-80 | 8840 |
| 8 | 42.11 | 29#N-80 | 8800 |
| 9 | 38.83 | 29#N-80 | 8758 |
| 10 | 40.84 | 29#N-80 | 8719 |
| 11 | 38.70 | 29#N-80 | 8678 |
| 12 | 41.50 | 29#N-80 | 8639 |
| 13 | 42.00 | 29#N-80 | 8598 |
| 14 | 41.93 | 29#N-80 | 8556 |
| 15 | 39.56 | 29#N-80 | 8514 |
| 16 | 39.15 | 29#N-80 | 8474 |
| 17 | 42.50 | 29#N-80 | 8435 |
| 18 | 43.99 | 29#N-80 | 8393 |
| 19 | 41.44 | 29#N-80 | 8349 |
| 20 | 40.20 | 29#N-80 | 8307 |
| 21 | 43.25 | 29#N-80 | 8267 |
| 22 | 42.15 | 29#N-80 | 8224 |
| 23 | 40.66 | 29#N-80 | 8182 |
| 24 | 40.48 | 29#N-80 | 8141 |
| 25 | 39.02 | 29#N-80 | 8101 |
| 26 | 42.19 | 29#N-80 | 8062 |
| 27 | 41.54 | 29#N-80 | 8019 |
| 28 | 43.03 | 29#N-80 | 7978 |
| 29 | 39.43 | 29#N-80 | 7935 |
| 30 | 40.84 | 29#N-80 | 7895 |
| 31 | 39.08 | 29#N-80 | 7855 |
| 32 | 46.03 | 29#N-80 | 7815 |
| 33 | 40.45 | 29#N-80 | 7769 |
| 34 | 38.84 | 29#N-80 | 7729 |
| 35 | 38.20 | 29#N-80 | 7692 |
| 36 | 37.60 | 29#N-80 | 7654 |
| 37 | 47.55 | 29#N-80 | 7617 |
| 38 | 43.78 | 29#N-80 | 7569 |
| 39 | 41.25 | 29#N-80 | 7525 |
| 40 | 47.07 | 29#N-80 | 7484 |
| 41 | 42.02 | 29#N-80 | 7437 |
| 42 | 41.40 | 29#N-80 | 7395 |
| 43 | 40.96 | 29#N-80 | 7354 |
| 44 | 39.20 | 29#N-80 | 7313 |
| 45 | 45.89 | 29#N-80 | 7273 |
| 46 | 39.31 | 29#N-80 | 7227 |
| 47 | 35.37 | 29#N-80 | 7188 |
| 48 | 40.95 | 29#N-80 | 7153 |
| 49 | 40.90 | 29#N-80 | 7112 |
| 50 | 40.00 | 29#N-80 | 7071 |
| 51 | 34.48 | 29#P-110 | 7031 |
| 52 | 34.51 | 29#P-110 | 6996 |
| 53 | 37.19 | 29#P-110 | 6962 |
| 54 | 33.14 | 29#P-110 | 6925 |
| 55 | 34.4 | 29#P-110 | 6892 |
| 56 | 34.51 | 29#P-110 | 6857 |
| 57 | 34.38 | 29#P-110 | 6823 |
| 58 | 34.51 | 29#P-110 | 6788 |

| JT # | LENGTH | BOTTOM | TOP |
|---------|--------|----------|------|
| 59 | 35.13 | 29#P-110 | 6754 |
| 60 | 34.37 | 29#P-110 | 6719 |
| 61 | 34.43 | 29#P-110 | 6684 |
| 62 | 34.34 | 29#P-110 | 6650 |
| 63 | 37.16 | 29#P-110 | 6616 |
| 64 | 34.42 | 29#P-110 | 6578 |
| 65 | 34.40 | 29#P-110 | 6544 |
| 66 | 36.65 | 29#P-110 | 6510 |
| 67 | 37.03 | 29#P-110 | 6473 |
| 68 | 34.50 | 29#P-110 | 6436 |
| 69 | 34.51 | 29#P-110 | 6401 |
| 70 | 32.63 | 29#P-110 | 6367 |
| 71 | 34.36 | 29#P-110 | 6334 |
| 72 | 34.40 | 29#P-110 | 6300 |
| 73 | 37.12 | 29#P-110 | 6265 |
| 74 | 36.82 | 29#P-110 | 6228 |
| 75 | 34.09 | 29#P-110 | 6192 |
| 76 | 34.40 | 29#P-110 | 6157 |
| 77 | 34.42 | 29#P-110 | 6123 |
| 78 | 34.50 | 29#P-110 | 6089 |
| 79 | 34.45 | 29#P-110 | 6054 |
| 80 | 34.50 | 29#P-110 | 6020 |
| 81 | 37.13 | 29#P-110 | 5985 |
| 82 | 34.49 | 29#P-110 | 5948 |
| 83 | 34.46 | 29#P-110 | 5914 |
| 84 | 34.48 | 29#P-110 | 5879 |
| 85 | 34.46 | 26#P-110 | 5845 |
| 86 | 34.50 | 26#P-110 | 5810 |
| 87 | 34.54 | 26#P-110 | 5776 |
| 88 | 34.42 | 26#P-110 | 5741 |
| 89 | 34.45 | 26#P-110 | 5707 |
| 90 | 34.57 | 26#P-110 | 5672 |
| 91 | 34.51 | 26#P-110 | 5638 |
| 92 | 34.48 | 26#P-110 | 5603 |
| 93 | 34.42 | 26#P-110 | 5569 |
| 94 | 34.52 | 26#P-110 | 5534 |
| DV Tool | 2.20 | 26# N-80 | 5500 |
| 95 | 34.51 | 26#P-110 | 5468 |
| 96 | 34.28 | 26#P-110 | 5434 |
| 97 | 34.57 | 26#P-110 | 5399 |
| 98 | 34.40 | 26#P-110 | 5364 |
| 99 | 34.48 | 26#P-110 | 5329 |
| 100 | 33.70 | 26#P-110 | 5292 |
| 101 | 34.45 | 26#P-110 | 5257 |
| 102 | 34.48 | 26#P-110 | 5223 |
| 103 | 34.35 | 26#P-110 | 5188 |
| 104 | 34.43 | 26#P-110 | 5154 |
| 105 | 34.50 | 26#P-110 | 5119 |
| 106 | 34.62 | 26#P-110 | 5085 |
| 107 | 34.39 | 26#P-110 | 5050 |
| 108 | 34.36 | 26#P-110 | 5016 |
| 109 | 34.42 | 26#P-110 | 4982 |
| 110 | 34.49 | 26#P-110 | 4947 |
| 111 | 34.30 | 26#P-110 | 4913 |
| 112 | 34.40 | 26#P-110 | 4878 |
| 113 | 34.36 | 26#P-110 | 4844 |
| 114 | 34.48 | 26#P-110 | 4810 |
| 115 | 34.55 | 26#P-110 | 4775 |
| 116 | 34.45 | 26#P-110 | 4741 |
| 117 | 34.52 | 26#P-110 | 4708 |

Shoe to 2340.19 FEET
58Joint # 59 2047.75 FEET
to 117

TOTAL PIPE FOOTAGE= 9266.63 FEET

NAVAJO REFINING COMPANY, WDW-1

| JT # | LENGTH | BOTTOM | TOP |
|------|--------|----------|------|
| 118 | 34.40 | 26#P-110 | 4706 |
| 119 | 34.51 | 26#P-110 | 4672 |
| 120 | 34.38 | 26#P-110 | 4637 |
| 121 | 34.43 | 26#P-110 | 4603 |
| 122 | 34.46 | 26#P-110 | 4568 |
| 123 | 34.47 | 26#P-110 | 4534 |
| 124 | 34.46 | 26#P-110 | 4499 |
| 125 | 36.50 | 26#P-110 | 4465 |
| 126 | 34.52 | 26#P-110 | 4428 |
| 127 | 34.42 | 26#P-110 | 4394 |
| 128 | 34.45 | 26#P-110 | 4360 |
| 129 | 34.50 | 26#P-110 | 4325 |
| 130 | 34.44 | 26#P-110 | 4291 |
| 131 | 34.42 | 26#P-110 | 4256 |
| 132 | 34.56 | 26#P-110 | 4222 |
| 133 | 34.40 | 26#P-110 | 4187 |
| 134 | 34.55 | 26#P-110 | 4153 |
| 135 | 34.45 | 26#P-110 | 4118 |
| 136 | 34.60 | 26#P-110 | 4084 |
| 137 | 34.44 | 26#P-110 | 4049 |
| 138 | 34.40 | 26#P-110 | 4015 |
| 139 | 34.54 | 26#P-110 | 3980 |
| 140 | 34.44 | 26#P-110 | 3946 |
| 141 | 34.41 | 26#P-110 | 3911 |
| 142 | 34.56 | 26#P-110 | 3877 |
| 143 | 33.78 | 26#P-110 | 3842 |
| 144 | 34.43 | 26#P-110 | 3809 |
| 145 | 34.44 | 26#P-110 | 3774 |
| 146 | 34.46 | 26#P-110 | 3740 |
| 147 | 34.48 | 26#P-110 | 3705 |
| 148 | 34.46 | 26#P-110 | 3671 |
| 149 | 34.54 | 26#P-110 | 3636 |
| 150 | 34.49 | 26#P-110 | 3602 |
| 151 | 34.46 | 26#P-110 | 3567 |
| 152 | 34.44 | 26#P-110 | 3533 |
| 153 | 34.40 | 26#P-110 | 3498 |
| 154 | 34.55 | 26#P-110 | 3464 |
| 155 | 34.48 | 26#P-110 | 3429 |
| 156 | 34.40 | 26#P-110 | 3395 |
| 157 | 34.48 | 26#P-110 | 3361 |
| 158 | 34.5 | 26#P-110 | 3326 |
| 159 | 34.44 | 26#P-110 | 3292 |
| 160 | 34.49 | 26#P-110 | 3257 |
| 161 | 34.48 | 26#P-110 | 3223 |
| 162 | 34.42 | 26#P-110 | 3188 |
| 163 | 34.38 | 26#P-110 | 3154 |
| 164 | 34.09 | 26#P-110 | 3119 |
| 165 | 34.45 | 26#P-110 | 3085 |
| 166 | 34.35 | 26#P-110 | 3051 |
| 167 | 34.48 | 26#P-110 | 3016 |
| 168 | 34.42 | 26#P-110 | 2982 |
| 169 | 34.18 | 26#P-110 | 2948 |
| 170 | 34.48 | 26#P-110 | 2913 |
| 171 | 34.46 | 26#P-110 | 2879 |
| 172 | 34.51 | 26#P-110 | 2844 |
| 173 | 34.40 | 26#P-110 | 2810 |
| 174 | 34.33 | 26#P-110 | 2776 |
| 175 | 34.38 | 26#P-110 | 2741 |
| 176 | 34.44 | 26#P-110 | 2707 |
| 177 | 34.44 | 26#P-110 | 2672 |

Joint # 118 2068.12 FEET
to 177

| JT # | LENGTH | BOTTOM | TOP |
|------|--------|----------|------|
| 178 | 34.40 | 26#P-110 | 2638 |
| 179 | 34.41 | 26#P-110 | 2604 |
| 180 | 34.53 | 26#P-110 | 2569 |
| 181 | 34.40 | 26#P-110 | 2535 |
| 182 | 34.48 | 26#P-110 | 2500 |
| 183 | 34.43 | 26#P-110 | 2466 |
| 184 | 34.45 | 26#P-110 | 2431 |
| 185 | 34.33 | 26#P-110 | 2397 |
| 186 | 34.45 | 26#P-110 | 2363 |
| 187 | 34.52 | 26#P-110 | 2328 |
| 188 | 34.02 | 26#P-110 | 2294 |
| 189 | 34.48 | 26#P-110 | 2260 |
| 190 | 33.97 | 26#P-110 | 2225 |
| 191 | 34.40 | 26#P-110 | 2191 |
| 192 | 34.27 | 26#P-110 | 2157 |
| 193 | 34.40 | 26#P-110 | 2122 |
| 194 | 34.44 | 26#P-110 | 2088 |
| 195 | 34.56 | 26#P-110 | 2054 |
| 196 | 34.53 | 26#P-110 | 2019 |
| 197 | 34.33 | 26#P-110 | 1984 |
| 198 | 34.48 | 26#P-110 | 1950 |
| 199 | 34.47 | 26#P-110 | 1916 |
| 200 | 34.47 | 26#P-110 | 1881 |
| 201 | 34.45 | 26#P-110 | 1847 |
| 202 | 34.44 | 26#P-110 | 1812 |
| 203 | 34.45 | 26#P-110 | 1778 |
| 204 | 34.50 | 26#P-110 | 1743 |
| 205 | 34.45 | 26#P-110 | 1709 |
| 206 | 34.53 | 26#P-110 | 1674 |
| 207 | 34.52 | 26#P-110 | 1640 |
| 208 | 34.44 | 26#P-110 | 1605 |
| 209 | 34.39 | 26#P-110 | 1571 |
| 210 | 34.41 | 26#P-110 | 1537 |
| 211 | 34.46 | 26#P-110 | 1502 |
| 212 | 34.53 | 26#P-110 | 1468 |
| 213 | 34.42 | 26#P-110 | 1433 |
| 214 | 34.33 | 26#P-110 | 1399 |
| 215 | 34.52 | 26#P-110 | 1364 |
| 216 | 34.36 | 26#P-110 | 1330 |
| 217 | 34.57 | 26#P-110 | 1296 |
| 218 | 34.45 | 26#P-110 | 1261 |
| 219 | 34.45 | 26#P-110 | 1227 |
| 220 | 34.25 | 26#P-110 | 1192 |
| 221 | 34.40 | 26#P-110 | 1158 |
| 222 | 34.36 | 26#P-110 | 1123 |
| 223 | 34.43 | 26#P-110 | 1089 |
| 224 | 33.75 | 26#P-110 | 1055 |
| 225 | 34.38 | 26#P-110 | 1021 |
| 226 | 34.43 | 26#P-110 | 986 |
| 227 | 34.40 | 26#P-110 | 952 |
| 228 | 34.55 | 26#P-110 | 918 |
| 229 | 34.40 | 26#P-110 | 883 |
| 230 | 34.50 | 26#P-110 | 849 |
| 231 | 34.45 | 26#P-110 | 814 |
| 232 | 34.48 | 26#P-110 | 780 |
| 233 | 34.40 | 26#P-110 | 745 |
| 234 | 34.47 | 26#P-110 | 711 |
| 235 | 31.48 | 26#P-110 | 676 |
| 236 | 32.67 | 26#P-110 | 645 |
| 237 | 34.44 | 26#P-110 | 612 |

Joint # 178 2060.13 FEET
to 237

NAVAJO REFINING COMPANY, WDW-1

| JT # | LENGTH | | BOTTOM | TOP |
|------|--------|----------|--------|-----|
| 238 | 34.5 | 26#P-110 | 578 | 543 |
| 239 | 34.4 | 26#P-110 | 543 | 509 |
| 240 | 34.39 | 26#P-110 | 509 | 475 |
| 241 | 34.49 | 26#P-110 | 475 | 440 |
| 242 | 34.48 | 26#P-110 | 440 | 406 |
| 243 | 34.41 | 26#P-110 | 406 | 371 |
| 244 | 34.44 | 26#P-110 | 371 | 337 |
| 245 | 34.5 | 26#P-110 | 337 | 302 |
| 246 | 34.5 | 26#P-110 | 302 | 268 |
| 247 | 34.45 | 26#P-110 | 268 | 233 |
| 248 | 34.55 | 26#P-110 | 233 | 199 |
| 249 | 34.5 | 26#P-110 | 199 | 164 |
| 250 | 34.48 | 26#P-110 | 164 | 130 |
| 251 | 34.47 | 26#P-110 | 130 | 95 |
| 252 | 34.40 | 26#P-110 | 95 | 61 |
| 253 | 31.59 | 26#P-110 | 61 | 29 |
| 254 | 34.43 | 26#P-110 | 29 | -5 |
| 255 | 32.07 | 26#P-110 | OUT | |
| 256 | 34.32 | 26#P-110 | OUT | |
| 257 | 33.41 | 26#P-110 | OUT | |
| 258 | 33.22 | 26#P-110 | OUT | |
| 259 | 34.44 | 26#P-110 | OUT | |
| 260 | | | | |
| 261 | | | | |
| 262 | | | | |
| 263 | | | | |
| 264 | | | | |
| 265 | | | | |
| 266 | | | | |
| 267 | | | | |
| 268 | | | | |
| 269 | | | | |
| 270 | | | | |
| 271 | | | | |
| 272 | | | | |
| 273 | | | | |
| 274 | | | | |
| 275 | | | | |
| 276 | | | | |
| 277 | | | | |
| 278 | | | | |
| 279 | | | | |
| 280 | | | | |
| 281 | | | | |
| 282 | | | | |
| 283 | | | | |
| 284 | | | | |
| 285 | | | | |
| 286 | | | | |
| 287 | | | | |
| 288 | | | | |
| 289 | | | | |
| 290 | | | | |
| 291 | | | | |
| 292 | | | | |
| 293 | | | | |
| 294 | | | | |
| 295 | | | | |
| 296 | | | | |
| 297 | | | | |

Joint # 238 750.44 FEET
to 297

15-Jul-98DATE

TABLE 2.4-II
PLUGGED-BACK RECORD

| DATE | PLUGGED-BACK DEPTH ¹ (feet) | DESCRIPTION OF WORK |
|---------|---|--|
| 7/21/98 | 9004 | Top of Cement. Did not drill out float collar. |

¹ All depths relative to the Kelly Bushing.

TABLE 2.5-I
PERFORATION RECORD

| DATE | ZONE | DEPTH INTERVALS ¹ (feet) | SHOT DENSITY (shots/foot) | NO. OF HOLES |
|---------|-------|--|------------------------------|--------------|
| 7/24/98 | Cisco | 8220 to 8254 | 2 | 70 |
| 7/24/98 | Cisco | 8260 to 8270 | 2 | 22 |
| 7/24/98 | Cisco | 8280 to 8302 | 2 | 46 |
| 7/24/98 | Cisco | 8370 to 8378 | 2 | 18 |
| 7/24/98 | Cisco | 8360 to 8366 | 2 | 14 |
| 7/24/98 | Cisco | 8400 to 8410 | 2 | 22 |
| 7/24/98 | Cisco | 8419 to 8423 | 2 | 10 |
| 7/24/98 | Cisco | 8430 to 8446 | 2 | 34 |
| 7/24/98 | Cisco | 8460 to 8464 | 2 | 10 |
| 7/24/98 | Cisco | 8470 to 8476 | 2 | 14 |
| 7/27/98 | Cisco | 7924 to 7942 | 2 | 38 |
| 7/27/98 | Cisco | 7974 to 8030 | 2 | 114 |
| 7/27/98 | Cisco | 8050 to 8056 | 2 | 14 |
| 7/27/98 | Cisco | 8066 to 8080 | 2 | 30 |
| 7/27/98 | Cisco | 8132 to 8140 | 2 | 18 |
| 7/27/98 | Cisco | 8118 to 8127 | 2 | 20 |
| 7/27/98 | Cisco | 8160 to 8164 | 2 | 10 |
| 7/27/98 | Cisco | 8170 to 8188 | 2 | 38 |

¹ All depths are relative to the Kelly Bushing.

TABLE 2.6-1

NAVAJO REFINING COMPANY, WDW-1

4-1/2", 11.00 lb/ft, N-80, SMLS, LT&C (NEW) TALLY
PROTECTORS OFF - 8/1/98 PACKER @ 7879'

| JT # | LENGTH | BOTTOM | TOP |
|--------|--------|--------|---------------|
| Packer | 9.01 | Packer | 7879 7870 |
| 1 | 40.13 | Tubing | 7870 7830 |
| 2 | 41.00 | Tubing | 7830 7789 |
| 3 | 41.00 | Tubing | 7789 7748 |
| 4 | 40.07 | Tubing | 7748 7708 |
| 5 | 40.13 | Tubing | 7708 7668 |
| 6 | 40.53 | Tubing | 7668 7627 |
| 7 | 41.00 | Tubing | 7627 7586 |
| 8 | 40.85 | Tubing | 7586 7545 |
| 9 | 41.00 | Tubing | 7545 7504 |
| 10 | 40.90 | Tubing | 7504 7463 |
| 11 | 40.72 | Tubing | 7463 7423 |
| 12 | 40.55 | Tubing | 7423 7382 |
| 13 | 41.07 | Tubing | 7382 7341 |
| 14 | 40.42 | Tubing | 7341 7301 |
| 15 | 40.54 | Tubing | 7301 7260 |
| 16 | 40.58 | Tubing | 7260 7220 |
| 17 | 40.50 | Tubing | 7220 7179 |
| 18 | 41.02 | Tubing | 7179 7138 |
| 19 | 40.55 | Tubing | 7138 7097 |
| 20 | 40.50 | Tubing | 7097 7057 |
| 21 | 40.27 | Tubing | 7057 7017 |
| 22 | 40.63 | Tubing | 7017 6976 |
| 23 | 40.91 | Tubing | 6976 6935 |
| 24 | 41.00 | Tubing | 6935 6894 |
| 25 | 41.02 | Tubing | 6894 6853 |
| 26 | 40.87 | Tubing | 6853 6812 |
| 27 | 41.02 | Tubing | 6812 6771 |
| 28 | 40.94 | Tubing | 6771 6730 |
| 29 | 40.58 | Tubing | 6730 6690 |
| 30 | 40.12 | Tubing | 6690 6650 |
| 31 | 40.52 | Tubing | 6650 6609 |
| 32 | 41.02 | Tubing | 6609 6568 |
| 33 | 40.63 | Tubing | 6568 6527 |
| 34 | 0.00 | Tubing | 6527 6527 out |
| 35 | 38.64 | Tubing | 6527 6488 |
| 36 | 40.50 | Tubing | 6488 6447 |
| 37 | 40.52 | Tubing | 6447 6407 |
| 38 | 40.90 | Tubing | 6407 6366 |
| 39 | 41.02 | Tubing | 6366 6325 |
| 40 | 41.00 | Tubing | 6325 6284 |
| 41 | 39.78 | Tubing | 6284 6244 |
| 42 | 41.02 | Tubing | 6244 6203 |
| 43 | 40.58 | Tubing | 6203 6162 |
| 44 | 40.95 | Tubing | 6162 6122 |
| 45 | 41.00 | Tubing | 6122 6081 |
| 46 | 40.91 | Tubing | 6081 6040 |
| 47 | 40.95 | Tubing | 6040 5999 |
| 48 | 41.00 | Tubing | 5999 5958 |
| 49 | 41.04 | Tubing | 5958 5917 |
| 50 | 41.02 | Tubing | 5917 5876 |
| 51 | 41.01 | Tubing | 5876 5835 |
| 52 | 40.55 | Tubing | 5835 5794 |
| 53 | 41.00 | Tubing | 5794 5753 |
| 54 | 41.00 | Tubing | 5753 5712 |
| 55 | 41.00 | Tubing | 5712 5671 |
| 56 | 40.97 | Tubing | 5671 5630 |
| 57 | 40.17 | Tubing | 5630 5590 |
| 58 | 41.01 | Tubing | 5590 5549 |
| 59 | 40.20 | Tubing | 5549 5508 |
| 60 | 41.00 | Tubing | 5508 5468 |

| JT # | LENGTH | BOTTOM | TOP |
|------|--------|--------|-----------|
| 81 | 40.30 | Tubing | 5468 5427 |
| 82 | 39.80 | Tubing | 5427 5388 |
| 83 | 40.54 | Tubing | 5388 5347 |
| 84 | 41.00 | Tubing | 5347 5306 |
| 85 | 40.95 | Tubing | 5306 5265 |
| 86 | 41.00 | Tubing | 5265 5224 |
| 87 | 40.50 | Tubing | 5224 5184 |
| 88 | 40.71 | Tubing | 5184 5143 |
| 89 | 40.55 | Tubing | 5143 5103 |
| 90 | 40.17 | Tubing | 5103 5062 |
| 91 | 40.87 | Tubing | 5062 5021 |
| 92 | 40.55 | Tubing | 5021 4981 |
| 93 | 41.02 | Tubing | 4981 4940 |
| 94 | 41.00 | Tubing | 4940 4899 |
| 95 | 41.00 | Tubing | 4899 4858 |
| 96 | 40.70 | Tubing | 4858 4817 |
| 97 | 41.00 | Tubing | 4817 4776 |
| 98 | 40.82 | Tubing | 4776 4735 |
| 99 | 40.98 | Tubing | 4735 4694 |
| 100 | 41.00 | Tubing | 4694 4653 |
| 101 | 41.00 | Tubing | 4653 4612 |
| 102 | 41.00 | Tubing | 4612 4571 |
| 103 | 41.00 | Tubing | 4571 4530 |
| 104 | 40.65 | Tubing | 4530 4490 |
| 105 | 41.00 | Tubing | 4490 4449 |
| 106 | 41.00 | Tubing | 4449 4408 |
| 107 | 41.02 | Tubing | 4408 4367 |
| 108 | 40.82 | Tubing | 4367 4326 |
| 109 | 41.00 | Tubing | 4326 4285 |
| 110 | 41.00 | Tubing | 4285 4244 |
| 111 | 39.70 | Tubing | 4244 4204 |
| 112 | 40.15 | Tubing | 4204 4164 |
| 113 | 41.00 | Tubing | 4164 4123 |
| 114 | 40.12 | Tubing | 4123 4083 |
| 115 | 41.00 | Tubing | 4083 4042 |
| 116 | 40.60 | Tubing | 4042 4001 |
| 117 | 41.05 | Tubing | 4001 3960 |
| 118 | 40.53 | Tubing | 3960 3920 |
| 119 | 40.82 | Tubing | 3920 3879 |
| 120 | 41.00 | Tubing | 3879 3838 |
| 121 | 40.80 | Tubing | 3838 3797 |
| 122 | 40.57 | Tubing | 3797 3757 |
| 123 | 40.87 | Tubing | 3757 3716 |
| 124 | 40.30 | Tubing | 3716 3675 |
| 125 | 40.55 | Tubing | 3675 3635 |
| 126 | 41.00 | Tubing | 3635 3594 |
| 127 | 40.55 | Tubing | 3594 3553 |
| 128 | 40.54 | Tubing | 3553 3513 |
| 129 | 40.97 | Tubing | 3513 3472 |
| 130 | 41.00 | Tubing | 3472 3431 |
| 131 | 40.70 | Tubing | 3431 3390 |
| 132 | 41.00 | Tubing | 3390 3349 |
| 133 | 41.00 | Tubing | 3349 3308 |
| 134 | 40.55 | Tubing | 3308 3268 |
| 135 | 41.00 | Tubing | 3268 3227 |
| 136 | 40.57 | Tubing | 3227 3186 |
| 137 | 40.54 | Tubing | 3186 3145 |
| 138 | 40.98 | Tubing | 3145 3104 |
| 139 | 40.50 | Tubing | 3104 3064 |
| 140 | 40.60 | Tubing | 3064 3023 |
| 141 | 41.00 | Tubing | 3023 2982 |

Pkr-#60 2411.32 FEET

 JT 61-121 = 2485.31 FEET
 TOTAL PIPE FOOTAGE = 4896.63 FEET
 IN HOLE

02-Aug-98 DATE

| JT # | LENGTH | BOTTOM | TOP |
|------|--------|--------|------|
| 122 | 40.55 | Tubing | 2982 |
| 123 | 40.45 | Tubing | 2942 |
| 124 | 41.00 | Tubing | 2901 |
| 125 | 40.60 | Tubing | 2860 |
| 126 | 41.00 | Tubing | 2820 |
| 127 | 40.17 | Tubing | 2779 |
| 128 | 41.00 | Tubing | 2739 |
| 129 | 41.00 | Tubing | 2698 |
| 130 | 40.05 | Tubing | 2657 |
| 131 | 41.00 | Tubing | 2617 |
| 132 | 40.40 | Tubing | 2576 |
| 133 | 40.85 | Tubing | 2535 |
| 134 | 40.55 | Tubing | 2494 |
| 135 | 41.00 | Tubing | 2454 |
| 136 | 40.10 | Tubing | 2413 |
| 137 | 40.55 | Tubing | 2373 |
| 138 | 41.00 | Tubing | 2332 |
| 139 | 41.00 | Tubing | 2291 |
| 140 | 40.60 | Tubing | 2250 |
| 141 | 40.12 | Tubing | 2209 |
| 142 | 40.97 | Tubing | 2169 |
| 143 | 40.12 | Tubing | 2128 |
| 144 | 40.85 | Tubing | 2088 |
| 145 | 41.00 | Tubing | 2047 |
| 146 | 40.97 | Tubing | 2006 |
| 147 | 40.10 | Tubing | 1965 |
| 148 | 40.97 | Tubing | 1925 |
| 149 | 40.56 | Tubing | 1884 |
| 150 | 40.56 | Tubing | 1844 |
| 151 | 40.55 | Tubing | 1803 |
| 152 | 41.00 | Tubing | 1763 |
| 153 | 41.00 | Tubing | 1722 |
| 154 | 39.90 | Tubing | 1681 |
| 155 | 41.00 | Tubing | 1641 |
| 156 | 39.57 | Tubing | 1600 |
| 157 | 41.00 | Tubing | 1560 |
| 158 | 40.55 | Tubing | 1519 |
| 159 | 40.55 | Tubing | 1479 |
| 160 | 40.60 | Tubing | 1438 |
| 161 | 40.55 | Tubing | 1398 |
| 162 | 41.00 | Tubing | 1357 |
| 163 | 40.85 | Tubing | 1316 |
| 164 | 41.00 | Tubing | 1275 |
| 165 | 40.18 | Tubing | 1234 |
| 166 | 41.00 | Tubing | 1194 |
| 167 | 40.90 | Tubing | 1153 |
| 168 | 40.94 | Tubing | 1112 |
| 169 | 40.90 | Tubing | 1071 |
| 170 | 40.80 | Tubing | 1030 |
| 171 | 40.92 | Tubing | 989 |
| 172 | 41.00 | Tubing | 949 |
| 173 | 41.00 | Tubing | 908 |
| 174 | 40.54 | Tubing | 867 |
| 175 | 40.85 | Tubing | 826 |
| 176 | 41.00 | Tubing | 785 |
| 177 | 41.00 | Tubing | 744 |
| 178 | 40.82 | Tubing | 703 |
| 179 | 41.00 | Tubing | 662 |
| 180 | 40.18 | Tubing | 621 |
| 181 | 41.00 | Tubing | 581 |
| 182 | 41.00 | Tubing | 540 |

[illegible]

02-Aug-98DATE

TABLE 4.1.1-I**Bottom-Hole Pressure Survey, Static Gradient Measurement**

| DEPTH (feet) | PRESSURE (psia) | PRESSURE GRADIENT (psi/ft) | TEMPERATURE (°F) | TEMPERATURE GRADIENT (°F/ft) |
|-------------------------|----------------------------|---|-----------------------------|---|
| 0 | 14.12 | -- | 82.82 | -- |
| 1700 | 85.30 | 0.042 | 83.40 | 0.0003 |
| 3000 | 679.62 | 0.457 | 87.81 | 0.0034 |
| 6000 | 2050.61 | 0.457 | 102.63 | 0.0049 |
| 7924 | 2928.40 | 0.456 | 104.06 | 0.0007 |

Note: Static gradient survey performed following the pressure buildup/falloff test.

TABLE 5.2-I
CEMENTING PROGRAM FOR WDW-1



| Type Casing | Casing Size (inches) | Hole Size (inches) | Depth (feet) | Cementing Detail |
|--------------|----------------------|--------------------|--------------|--|
| Surface | 13-3/8 | 17-1/2 | 390 | <p>Single stage, cemented to surface.</p> <p>Lead Slurry: 375 sacks Class 'C' Lite + 3% calcium chloride + 1/2 lb/sx Flocele</p> <p>Tail slurry: 150 sacks Class 'C' + 3% calcium chloride</p> <p>86 sacks cement returns to surface</p> |
| Intermediate | 9-5/8 | 12-1/4 | 2555 | <p>Single stage, cemented to surface</p> <p>Lead Slurry: 800 sacks Class 'C' lite + 1/2 lb/sx Flocele + 2 lb/sx Gilsonite + 12% salt</p> <p>Tail Slurry: 200 sacks Class 'C' + 2% calcium chloride</p> <p>133 sacks cement returns to surface</p> |
| Protection | 7 | 8-3/4 | 9094 | <p>Two stage, DV tool at 5498 feet</p> <p>Stage 1: 600 sacks modified Class 'H' + 0.4% CFR-3 + 5 lb/sx Gilsonite + 0.5% Halad-344 + 1 lb/sx salt mixed at 13.0 ppg</p> <p>Caliper volume plus 20% excess, circulated 142 sacks cement to surface.</p> <p>Stage 2 (lead): 220 sacks Interfill C (35:65:6) mixed at 11.7 ppg</p> <p>Stage 2 (tail): 550 sacks modified Class 'H' + 0.5% Halad - 344 + 0.1% HR-7 + 0.4% CFR-3 + 5 lb/sx Gilsonite + 1 lb/sx salt mixed at 13.0 ppg</p> <p>Caliper volume plus 20% excess, circulated 75 sacks cement to surface</p> |

TABLE 5.4.1-I
DEVIATION SURVEYS

| DEPTH (feet) | DEVIATION (degrees) |
|-----------------|------------------------|
| 2481 | 1 |
| 3441 | 1-1/4 |
| 4432 | 1-3/4 |
| 5277 | 4-1/4 |
| 6768 | 3-1/2 |
| 7571 | 1-3/4 |
| 8604 | 1-1/4 |
| 9160 | 1 |

FIGURES

SECTION 31, TOWNSHIP 17 SOUTH, RANGE 28 EAST, N.M.P.M.,
EDDY COUNTY NEW MEXICO

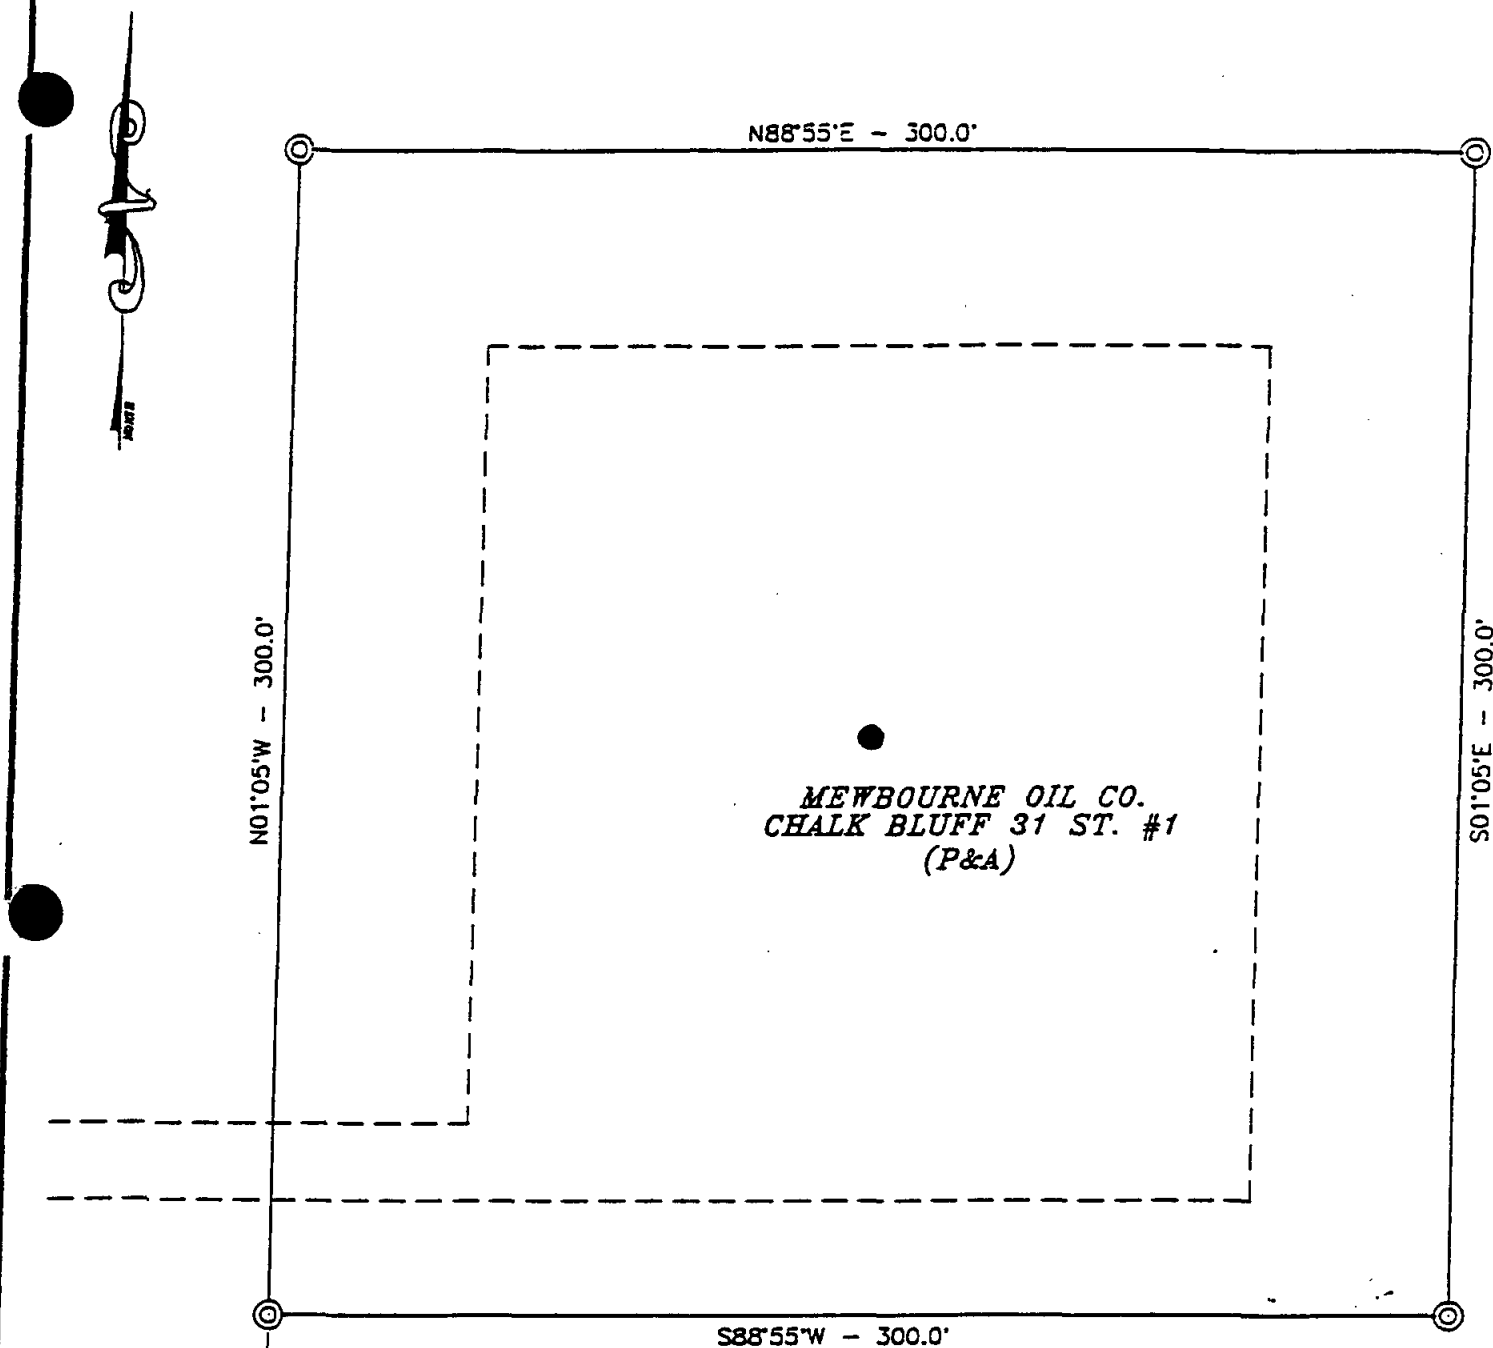

© DENOTES: SET 1/2" IRON ROD.
W/ PVC CAP MARKED
"PS 3239 PS 12641"

JOHN W. WEST ENGINEERING COMPANY
CONSULTING ENGINEERS & SURVEYORS - HOBBS, NEW MEXICO


NAVAJO REFINING COMPANY

CHALK BLUFF 31 STATE #1 LOCATED 660 FEET FROM
THE SOUTH LINE AND 2310 FEET FROM THE EAST LINE
SECTION 31, TOWNSHIP 17 SOUTH, RANGE 28 EAST,
N.M.P.M., EDDY COUNTY, NEW MEXICO.

FIGURE 1.0-1

| | |
|-------------------------|----------------------|
| Survey Date: 11/24/97 | Sheet 1 of 1 Sheets |
| W.O. Number: 97-11-1922 | Drawn By: CDG |
| Date: 12/1/97 | DISK: NAVAJO NAV1922 |

FIGURE 2.0-1

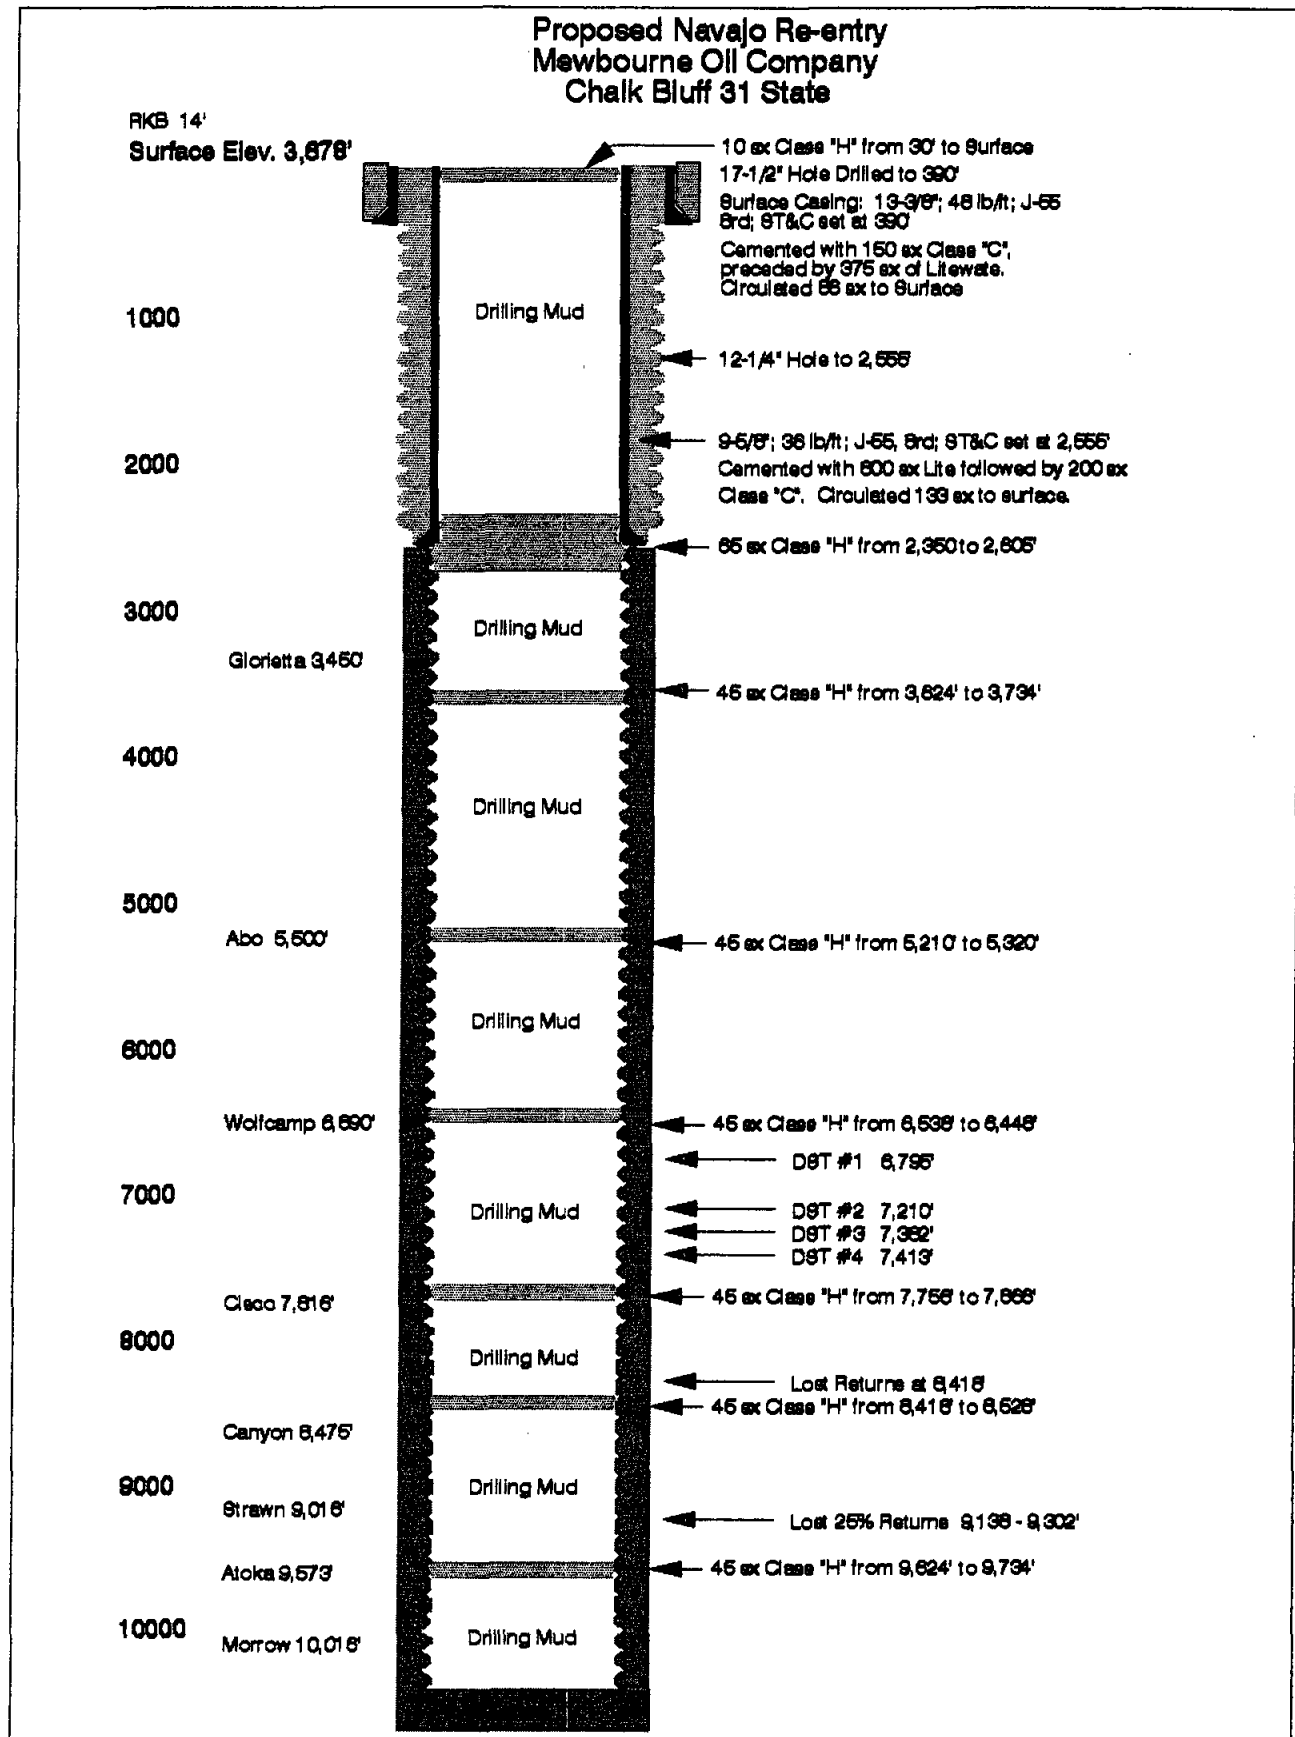

BELOW GROUND DETAIL

All depths are referenced to the kelly bushing elevation of 12.5 feet. Surface elevation is 3678 feet.

1. Surface Casing: 13-3/8", 48 lb/ft, J-55, ST&C set at 390' in a 17-1/2" hole. Cemented with 150 sx Class C with 3% calcium chloride, 375 sx Class C Litewater w/ 3% calcium chloride and 1/2 lb/sx flocele. Circulated 86 sx to surface.

2. Intermediate Casing: 9-5/8", 36 lb/ft, J-55, ST&C set at 2555' in a 12-1/4" hole. Cemented w/ 800 sx of Class C Lite w/ 1/2 lb/sx flocele and 2 lb/sx Gilsonite and 12% salt. Followed by 200 sx of Class C w/ 2% calcium chloride. Circulated 133 sx to surface.

3. Base of the USDW at 493'.

4. Injection Tubing: 4-1/2", 11.6 lb/ft, N-80, SMLS, R3, LT&C set at 7879'.

5. DV Tool: at 5498'.

6. Annulus Fluid: 8.7 lb/gal brine water mixed w/ UniChem Techni-Hib 370 corrosion inhibitor.

7. Protection Casing: 7", 29 lb/ft, N-80, LT&C: 9094' to 7031'. 7", 29 lb/ft, P-110, LT&C: 7031' to 5845'. 7", 26 lb/ft, P-110, LT&C: 5845' to surface. Set in 8-3/4" hole. Casing cemented in two stages as follows:

First Stage

600 sx modified Class H w/ 0.4% CFR-3, 5 lb/sx Gilsonite, 0.5% Halad-344, and 1 lb/sx salt mixed at 13.0 ppg. Opened DV tool at 5498' and circulated 142 sx to surface.

Second Stage

Lead Slurry: 220 sx Interfill 'C' (35:65:6) mixed at 11.7 ppg. Tail Slurry: 550 sx modified Class H w/ 0.4% CFR-3, 5 lb/sx, Gilsonite, 0.5% Halad-344, 0.1% HR-7, and 1 lb/sx salt mixed at 13.0 ppg. Circulated 75 sx to surface. Top out w/ 20 sx premium plus 3% calcium chloride.

8. Packer: 7" x 3.5" EVI Oil Tools (Arrow), Model X-1 retrievable packer set at 7879'. Minimum I.D. is 3.0". Wireline reentry guide on bottom. To release: turn 1/4 turn to the right and pick up.

9. Perforations (2 SPF):

Upper Zone:


7924-7942', 7974-8030', 8050-8056', 8066-8080', 8118-8127', 8132-8140', 8160-8164', 8170-8188'.

Lower Zone:

8220-8254', 8260-8270', 8280-8302', 8360-8366', 8370-8378', 8400-8410', 8419-8423', 8430-8446', 8460-8464', 8470-8476'.

10. PBTD: 9004'

11. Cement Plug: 45 sx Class H from 9624' to 9734'.

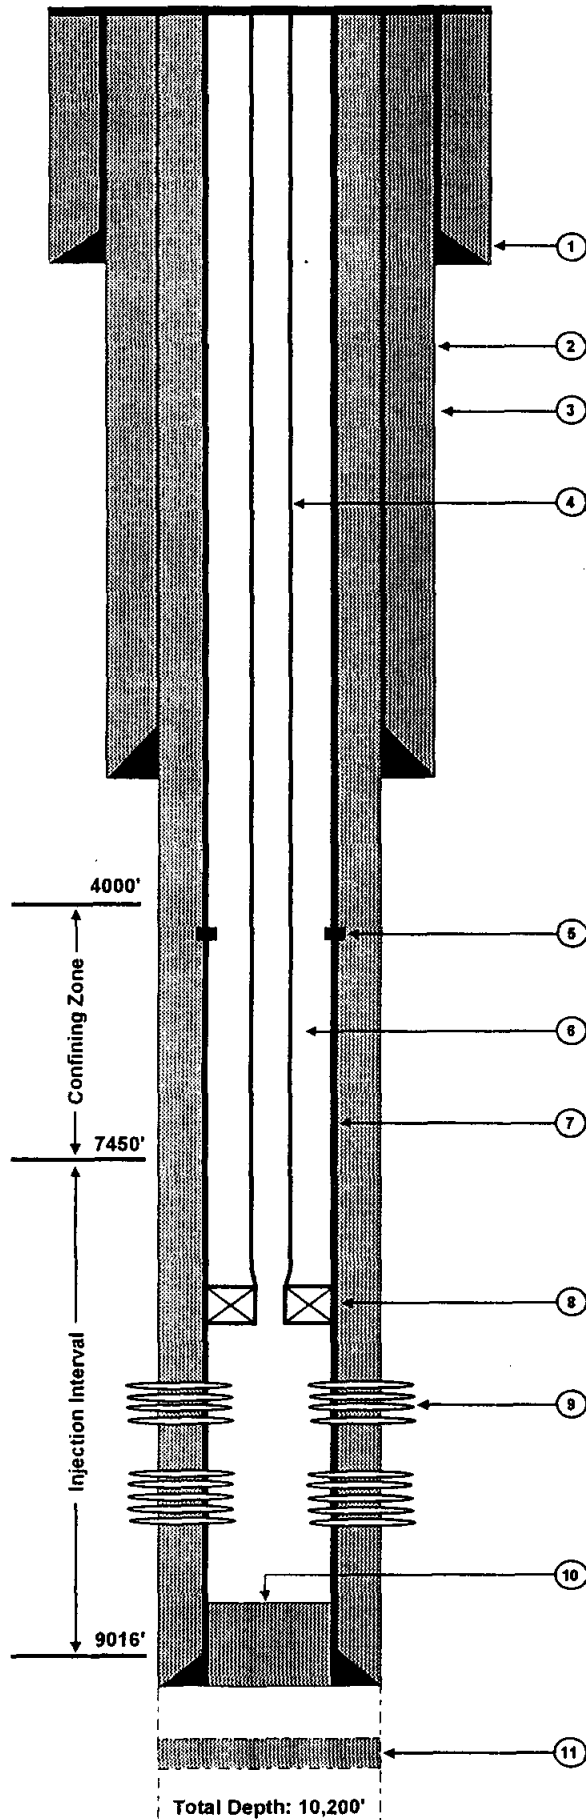

ENVIROCORP

HOUSTON, TX.
SOUTH BEND, IN.
BATON ROUGE, LA.

FIGURE 2.0-2
NAVAJO REFINING COMPANY
WDW-1
ARTESIA, NEW MEXICO

Date: 09/15/98 Checked By: B.R. Job No.: 70A4614
Drawn By: LKM Approved By: B.R. File: WDW1.DS4

FIGURE 2.6-1

| WELL PROFILE | | OPERATOR <u>ENVIROCORP</u> | | SIZE | WEIGHT | GRADE | THREAD | |
|-------------------------|-----------------|--|--------------------|---|---------------------------------|---------------|-----------------------------|----------------------------|
| | | COMPANY REP. <u>Brian Rogers</u> | | CASING | <u>7"</u> | <u>29.0#</u> | <u>N-80</u> <u>P-110</u> | |
| | | WELL # <u>Chalk Bluff 31 State</u> | | LINER | — | — | — | |
| | | FIELD | | TUBING | LONG STRING | <u>4 1/2"</u> | <u>11.6#</u> | <u>N-80</u> <u>LT+C</u> |
| | | COUNTY <u>Eddy</u> | | | SHORT STRING | — | — | — |
| STATE <u>NEW MEXICO</u> | | TYPE COMPLETION FLUID IN CASING | | | | | | |
| DATE <u>8-1-98</u> | | <input type="checkbox"/> New Completion <input checked="" type="checkbox"/> Workover | | TUBING WT. ON | LONG STRING <u>15,000#</u> ↓ | | SHORT STRING | |
| ITEM | LENGTH | FROM | TO | DESCRIPTION | | OD | ID | |
| | <u>10.50'</u> | <u>12.50'</u> | <u>2.0' A.G.L.</u> | <u>K.B. Correction</u> | | | | |
| | <u>7859.86'</u> | <u>10.50'</u> | <u>7870.36'</u> | <u>193 Hts. - 4 1/2" - 11.6# N-80</u> <u>LT+C CASING</u> | | <u>5.0"</u> | <u>4.0"</u> | |
| | <u>0.60'</u> | <u>7870.36'</u> | <u>7870.96'</u> | <u>4 1/2" LT+C Box X 3 1/2" EVBID Pin</u> | | <u>4.97"</u> | <u>3.068"</u> | |
| | <u>7.90'</u> | <u>7870.96'</u> | <u>7878.86'</u> | <u>7 X 3 1/2" Arrowset I-X Packer</u> | | <u>5.844"</u> | <u>3.068"</u> | |
| | <u>0.51'</u> | <u>7878.86'</u> | <u>7879.37'</u> | <u>Wireline Re-Entry Guide</u> | | <u>5.5"</u> | <u>3.5"</u> | |
| | <u>7879.37'</u> | | | <u>Total Depth of Tubing</u> | | | | |
| | | <u>7924'</u> | <u>8188'</u> | <u>Perforations</u> | | | | |
| | | <u>8220'</u> | <u>8476'</u> | <u>Perforations</u> | | | | |


WATSON PACKER

P.O. BOX 60690
MIDLAND, TX 79711
1-800-777-7957


PREPARED BY: Mitch Johnson OFFICE: Artesia PHONE: 748-1341

REMARKS:
- 7' for Wireline Correction

4 1/2" LTC CASING BOX X 3 1/2" EU BRD PIN X-OVER

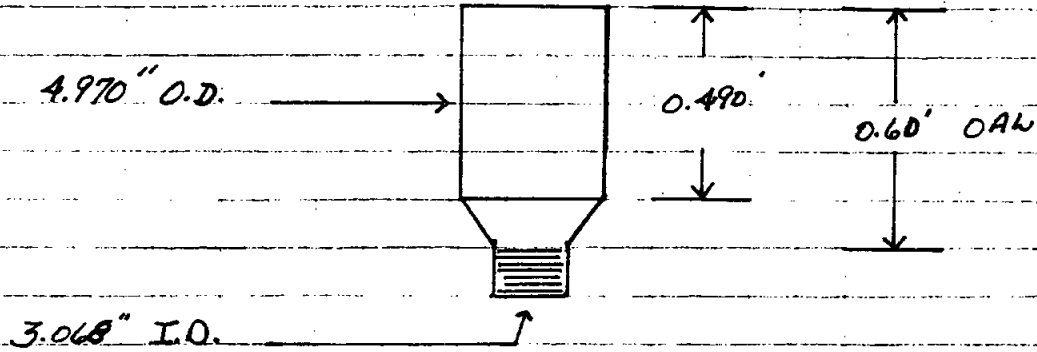

WIRELINE ENTRY GUIDE



7" X 3 1/2" Arrowset I-X Packer

4.344" O.O.

5.844" O.O.

5.344" O.O.

5.719" O.O.

5.719" O.O.

5.844" O.O.

5.844" O.O.

5.844" O.O.

5.719" O.O.

5.844" O.O.

5.490" O.O.

5.719" O.O.

3.068" I.O.

0.660'

0.210'

1.04'

0.28'

0.11'

0.790'

0.08'

0.05'

0.05'

0.08'

0.43'

0.11'

0.59'

0.07'

2.01'

0.75'

7.90' OAL

Lengths IN - Lin. ft.

NAVAJO REFINING COMPANY
WDW-1 STATIC GRADIENT SURVEY

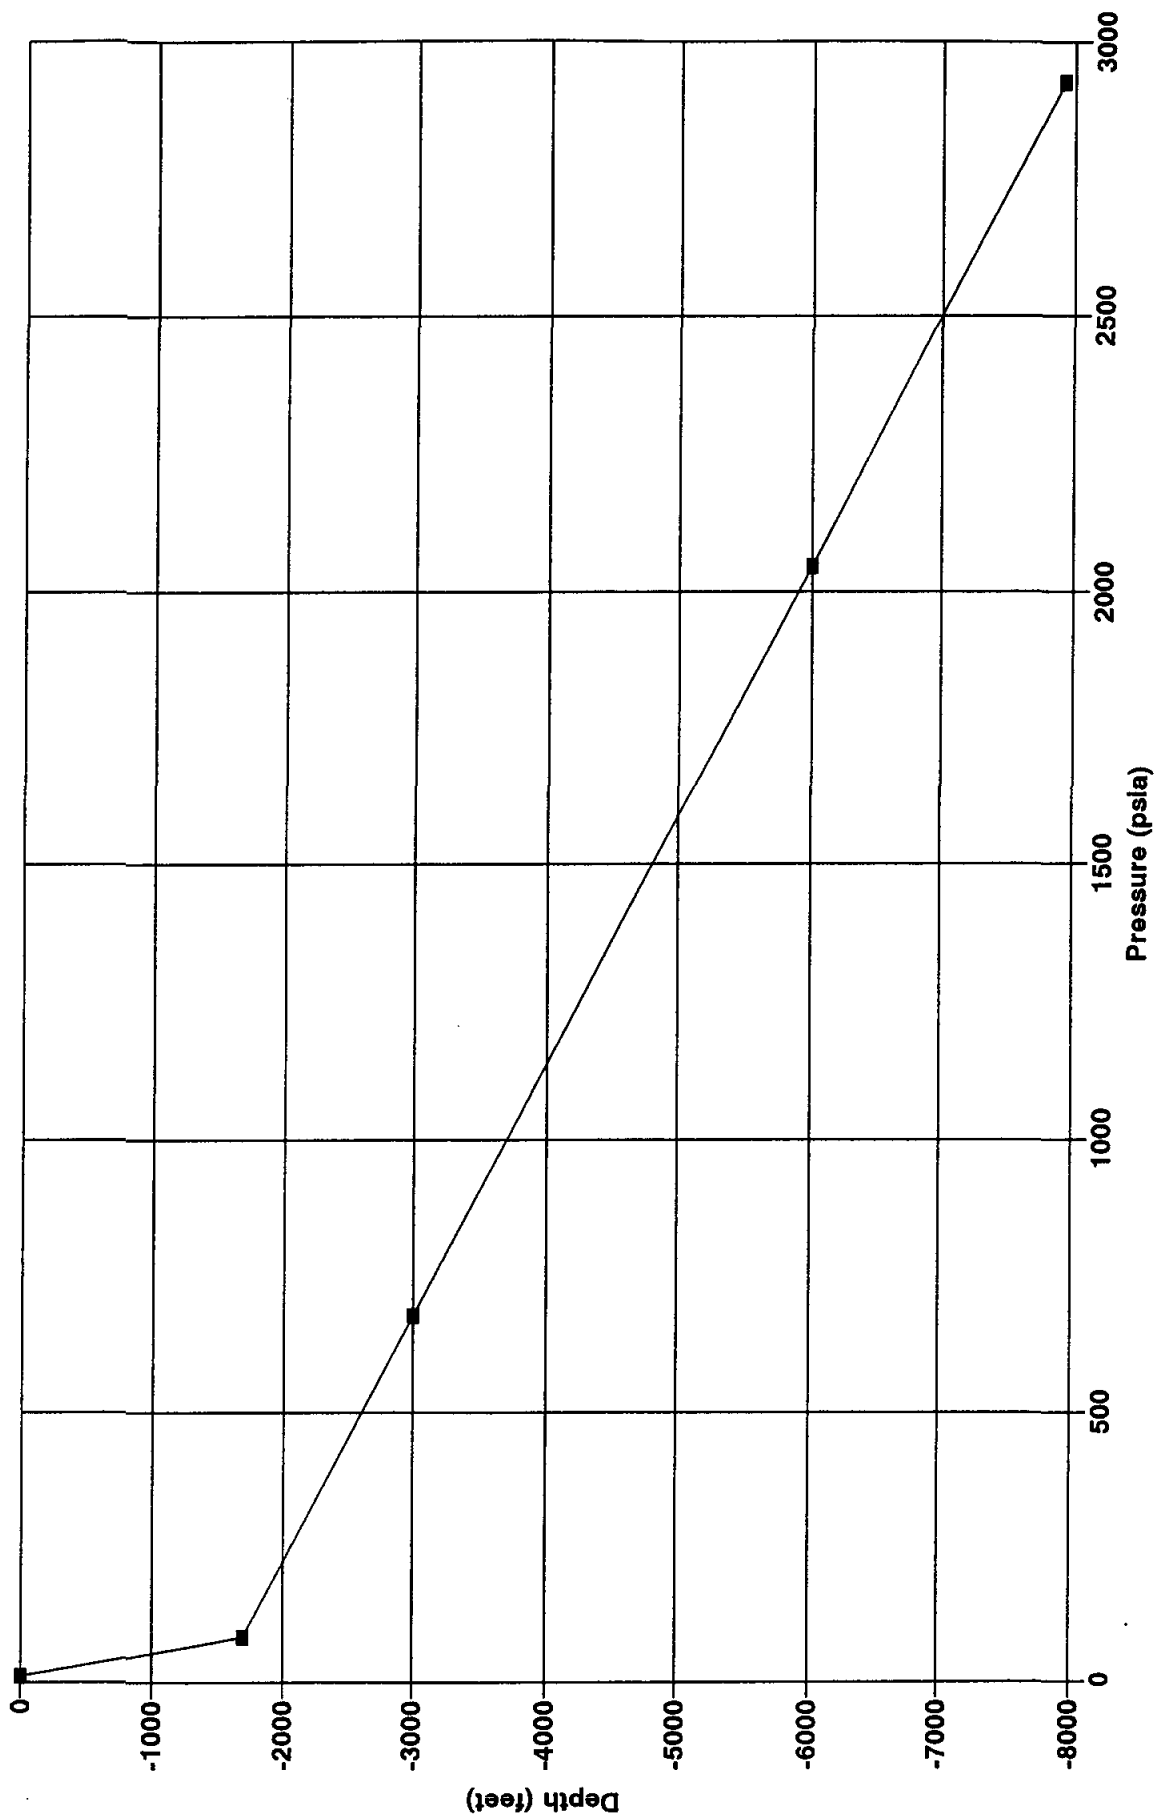


FIGURE 4.1.1-1

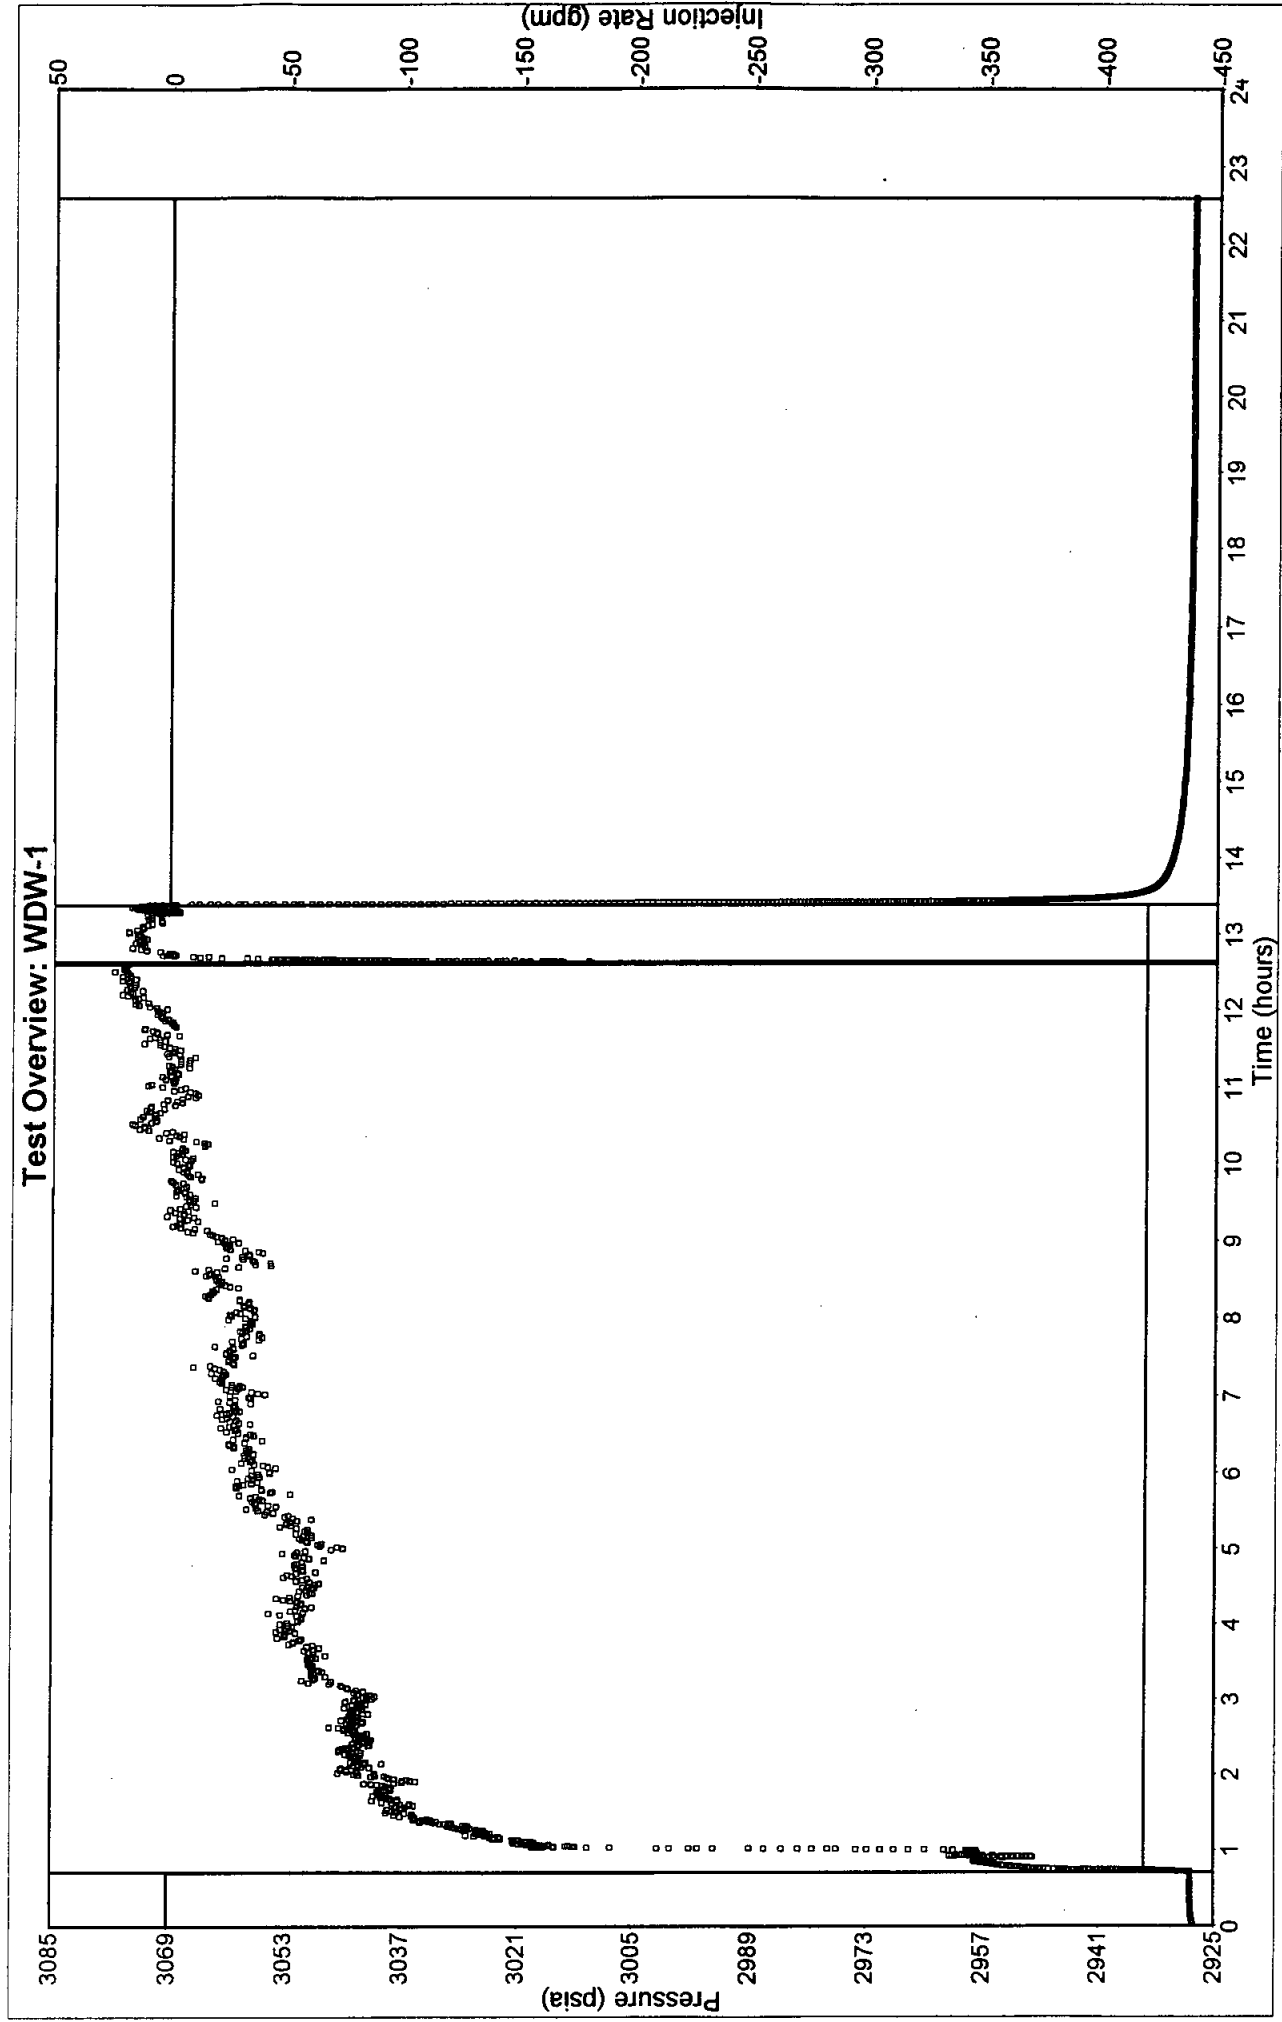


FIGURE 4.1.2-1

Log-Log Plot: WDW-1

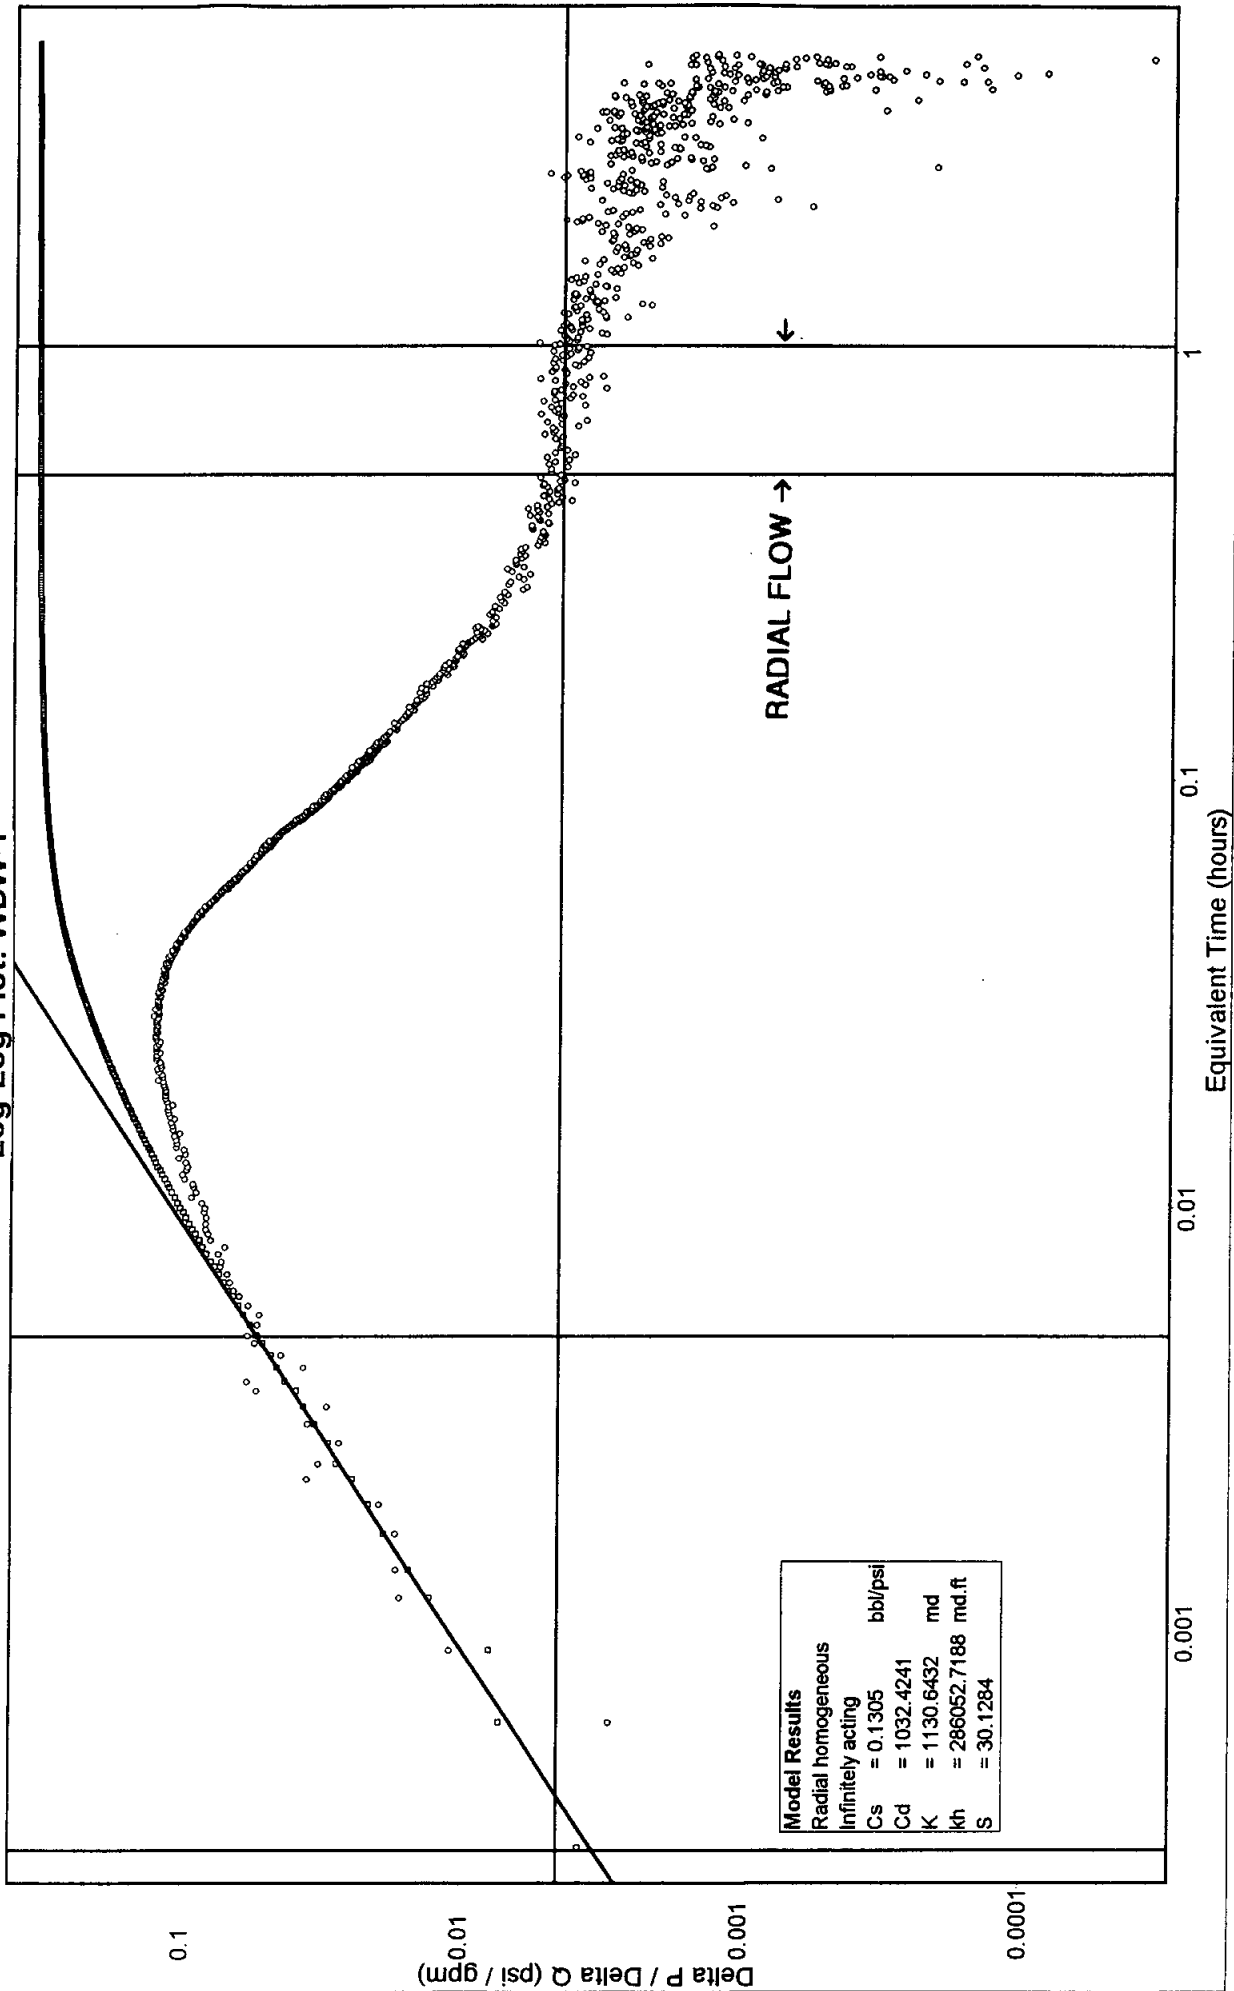


FIGURE 4.1.2-2

Radial Flow Plot

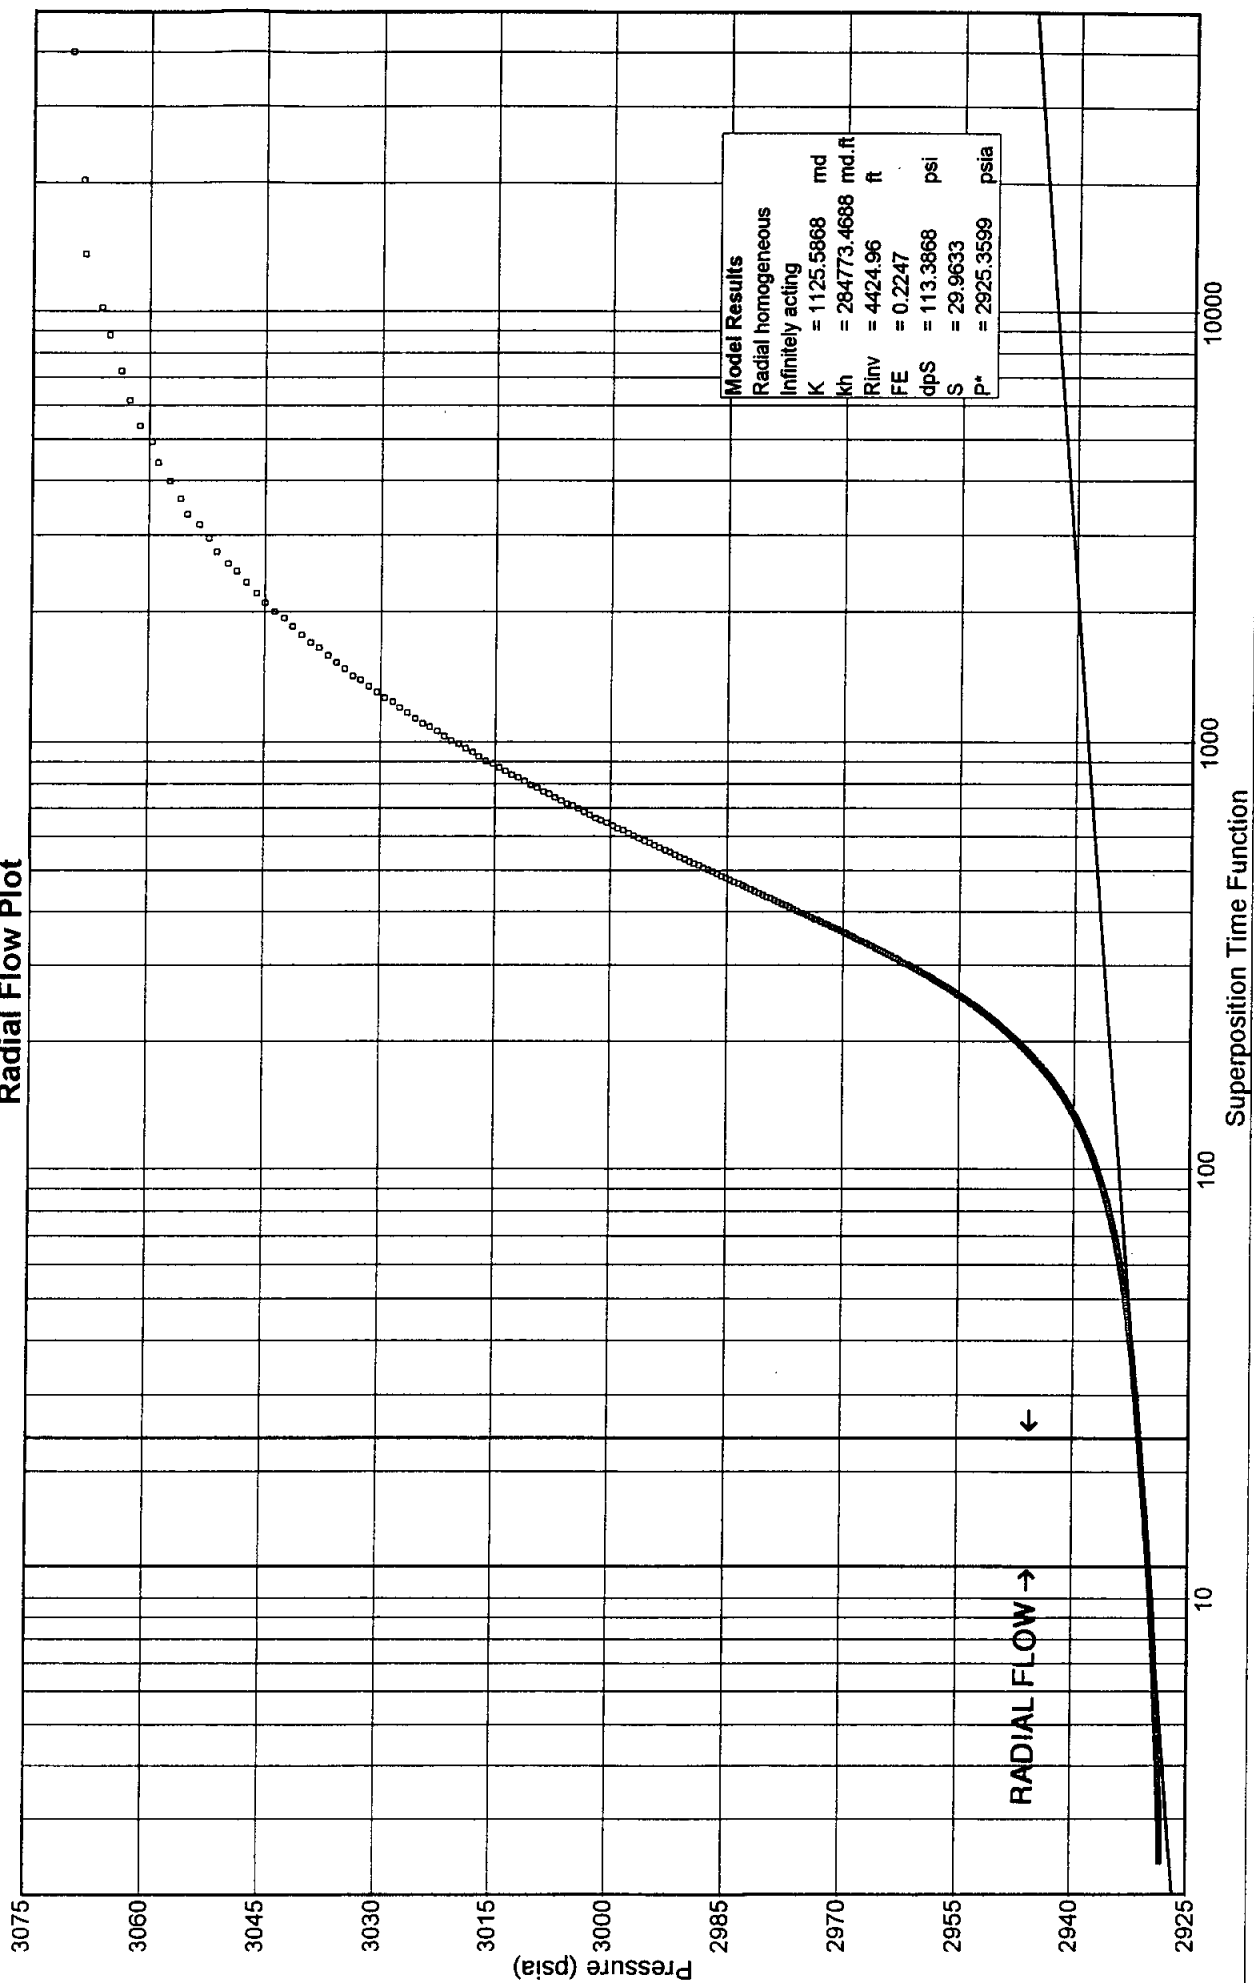


FIGURE 4.1.2-3

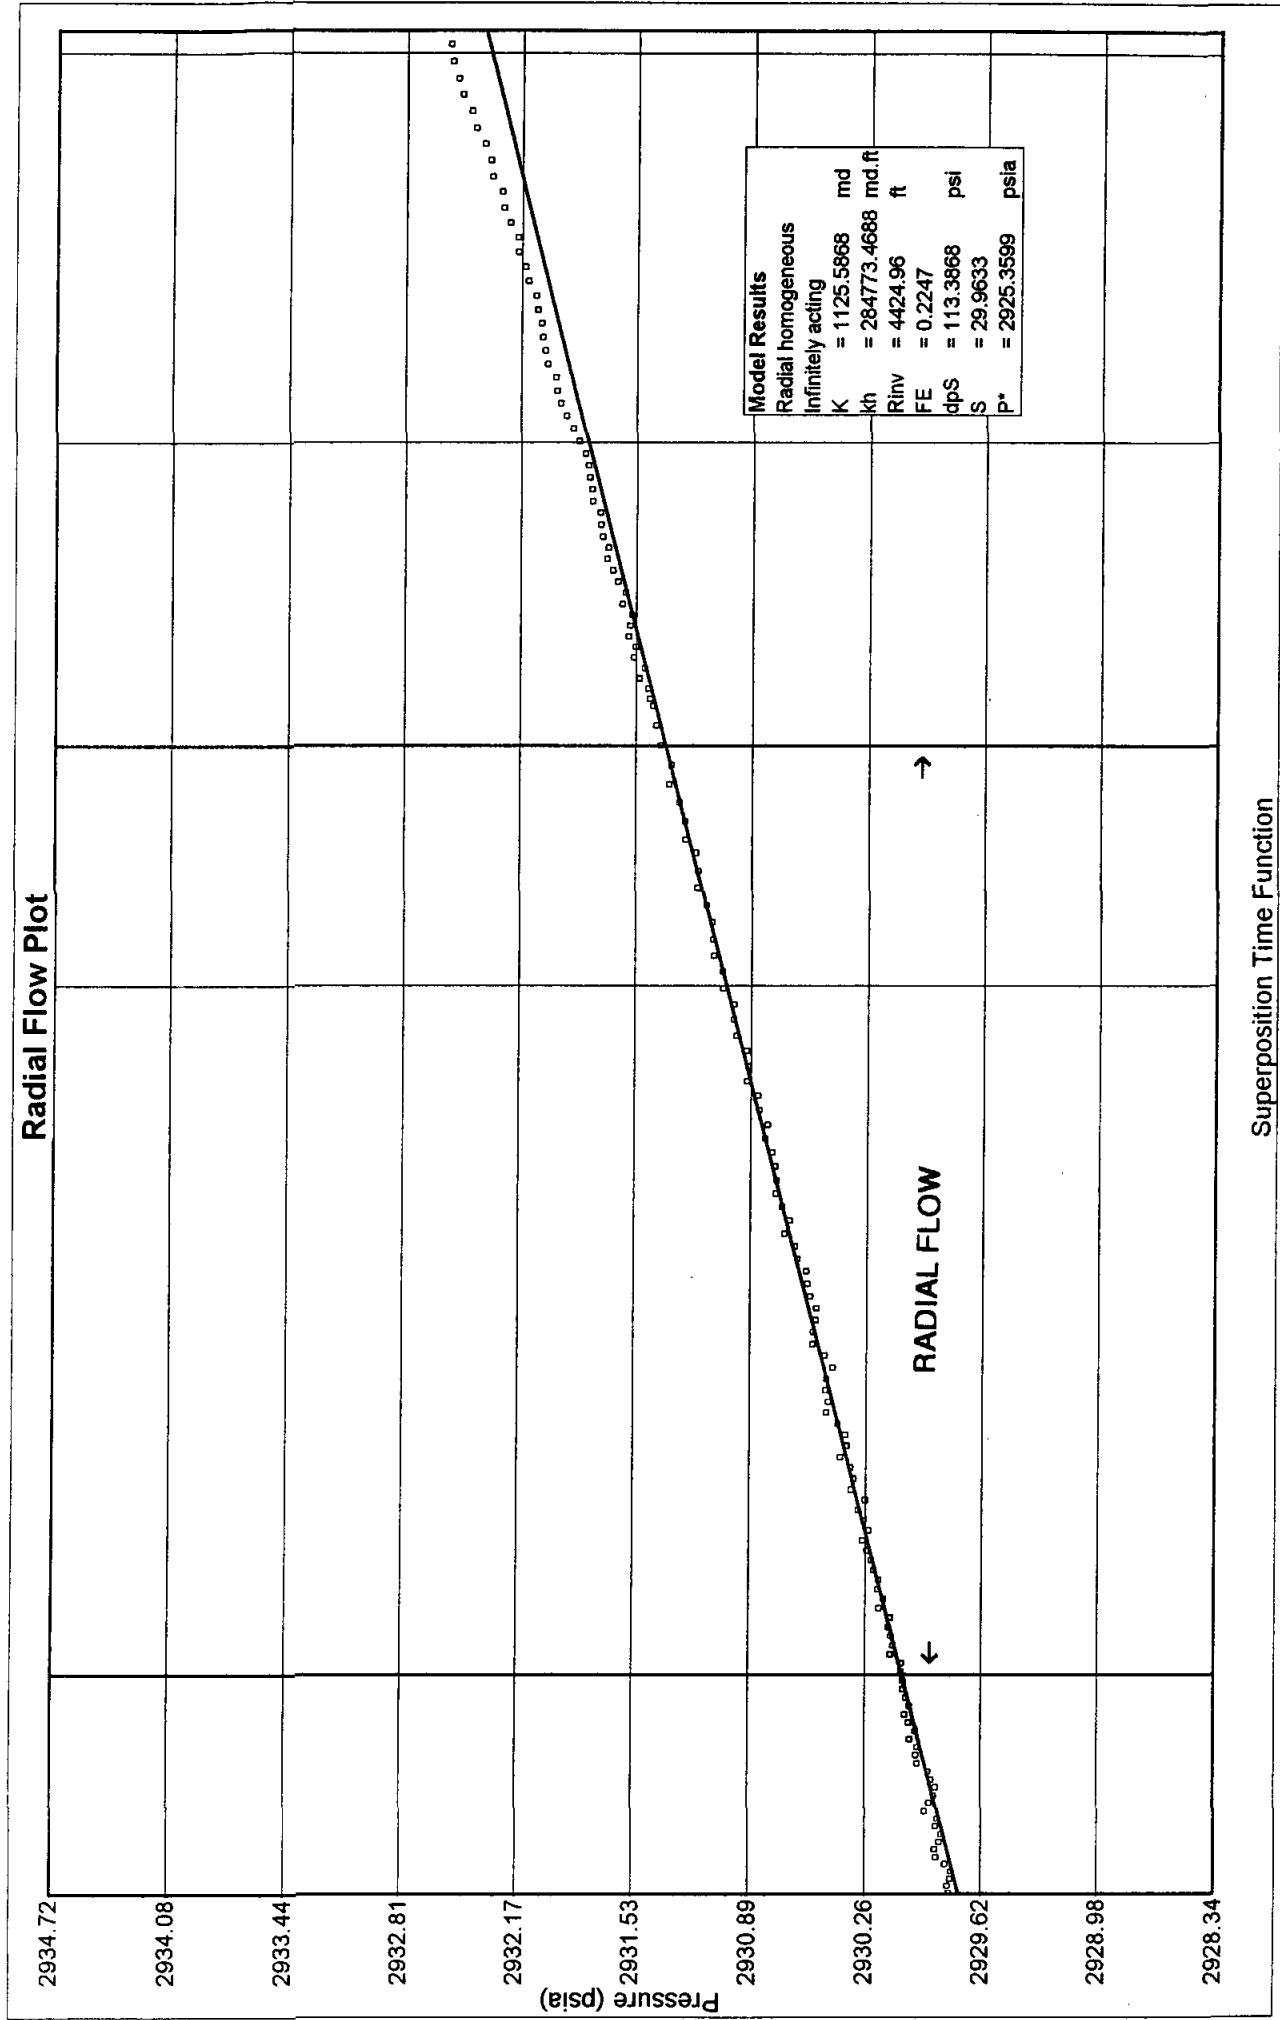


FIGURE 4.1.2-4

Cartesian Plot: WDW-1

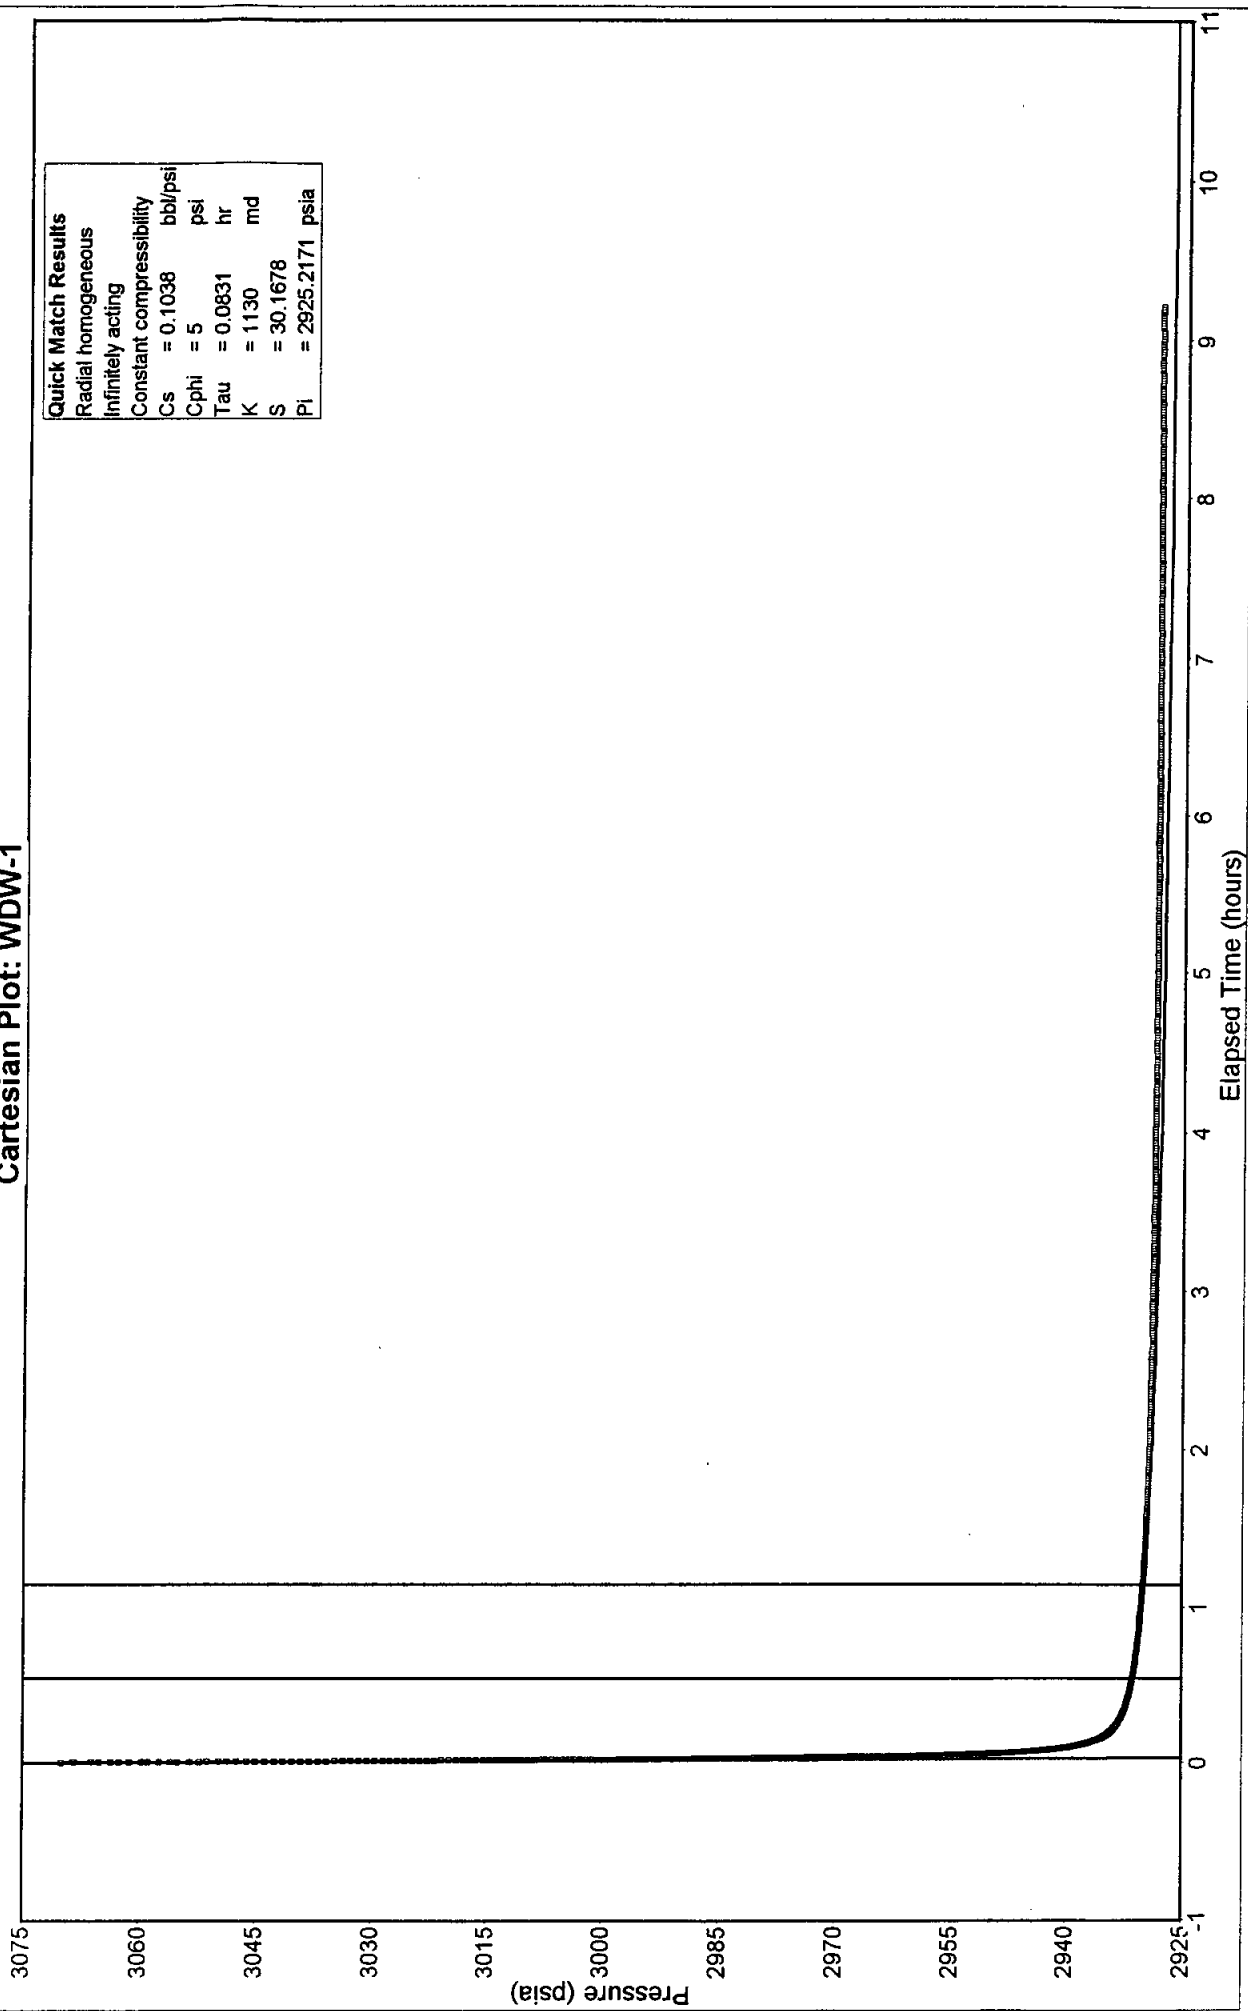


FIGURE 4.1.2-5

Radial Flow Plot

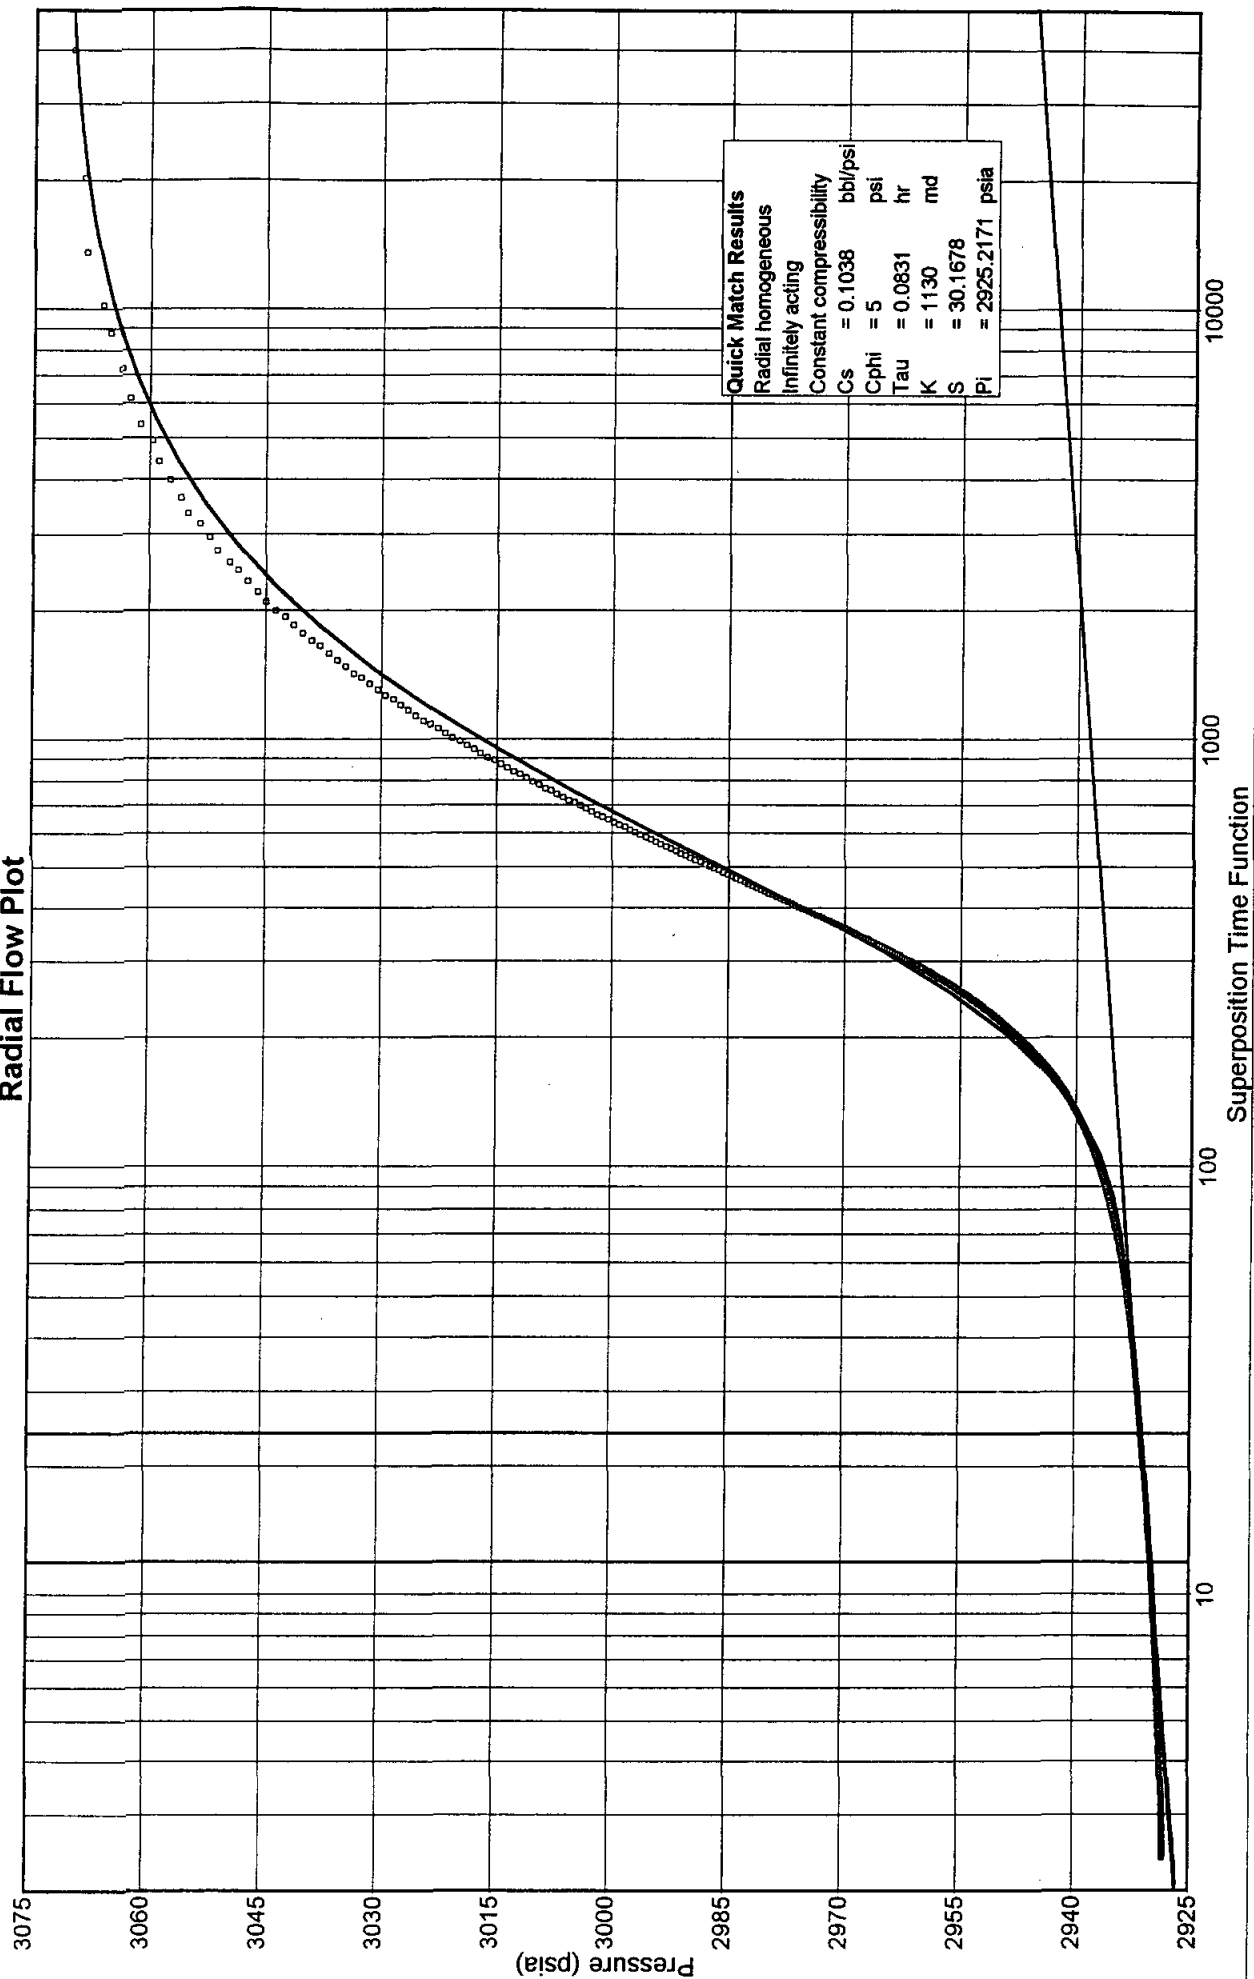


FIGURE 4.1.2-6

Log-Log Plot: WDW-1

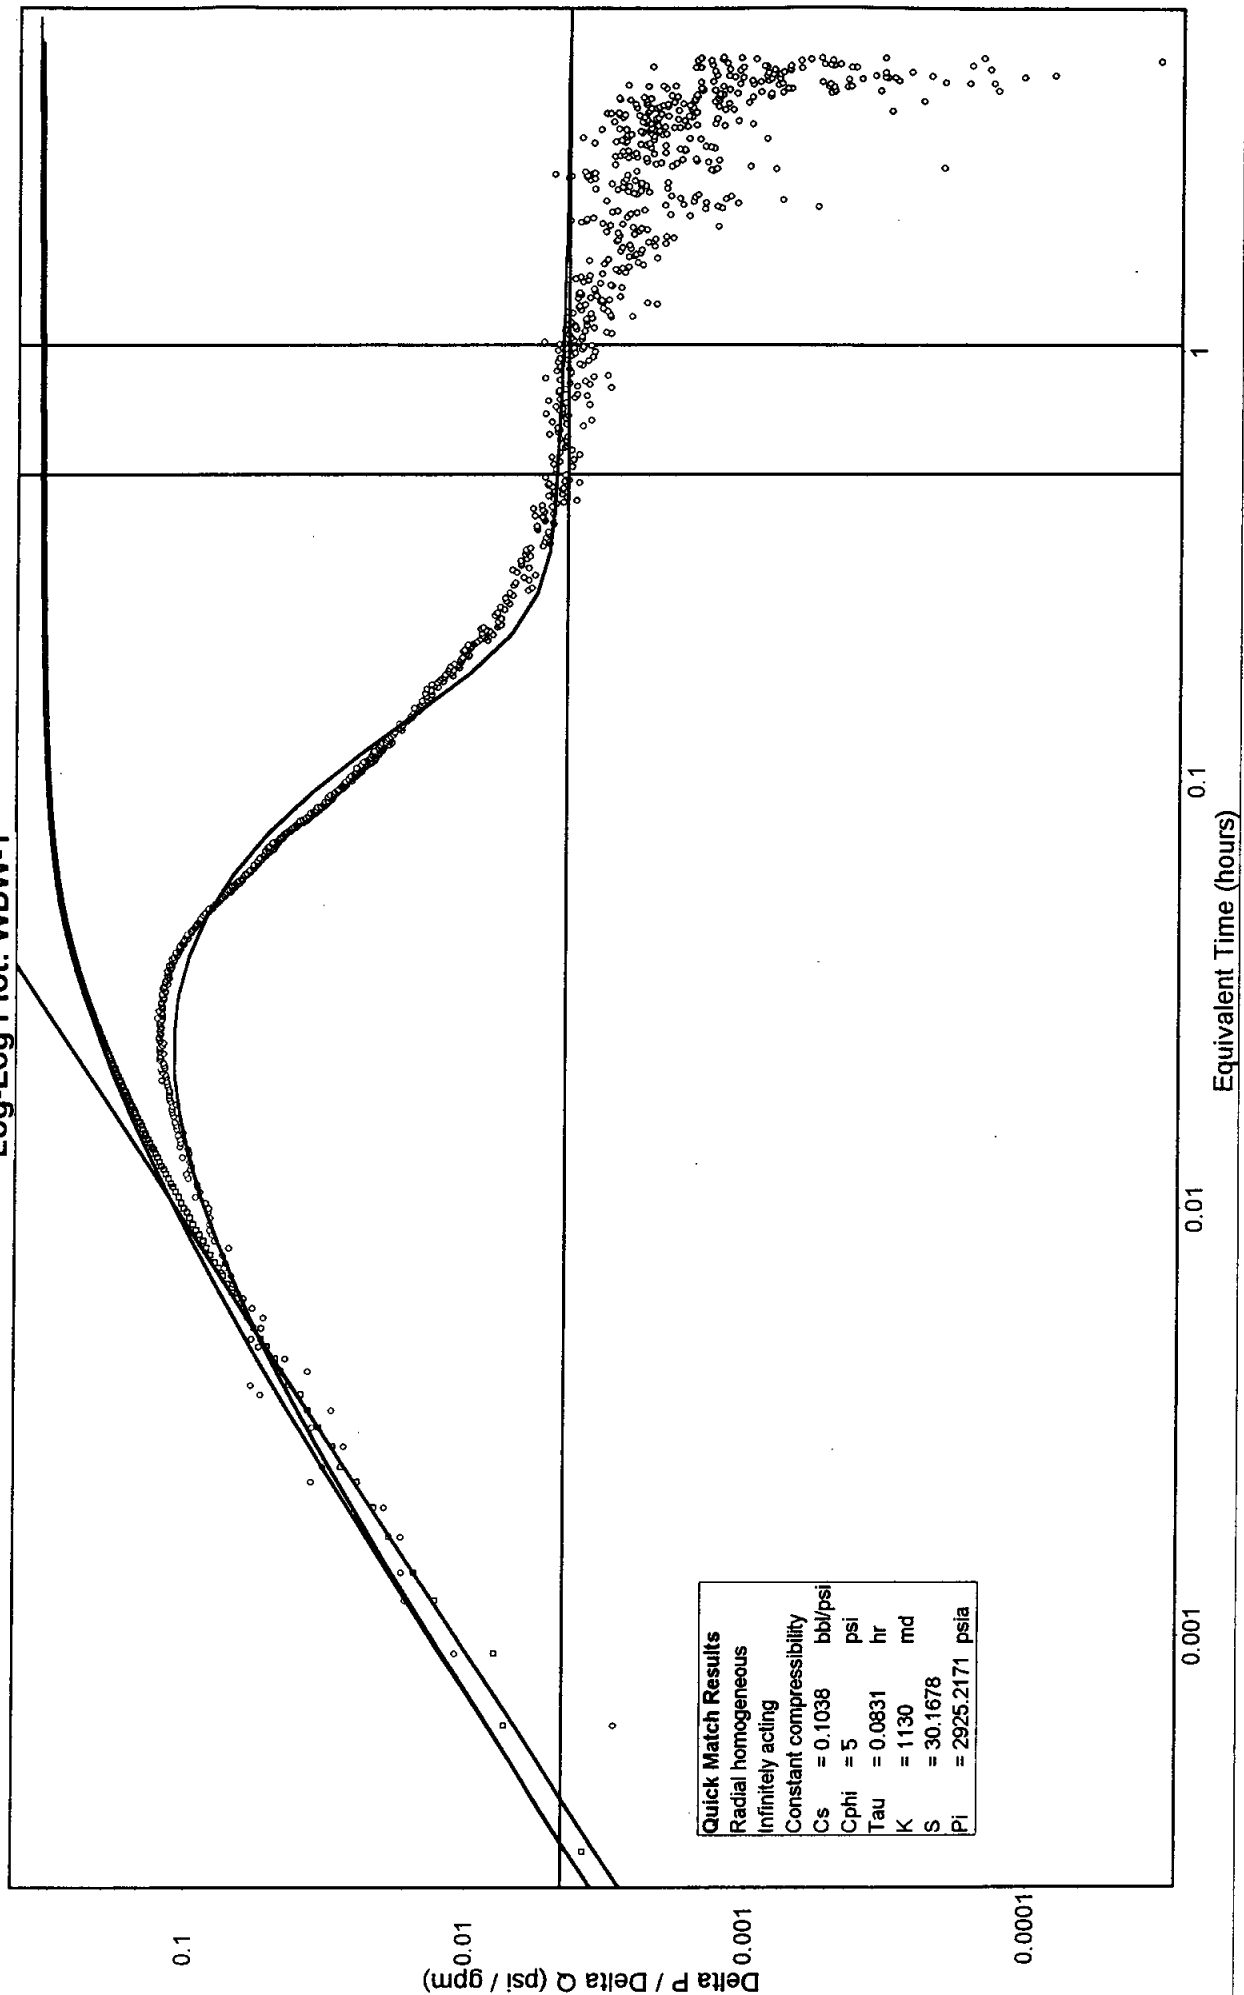


FIGURE 4.1.2-7

APPENDICES

APPENDIX 1.0-1

**APPROVAL LETTERS FROM THE
NEW MEXICO WATER QUALITY CONTROL COMMISSION,
DATED MAY 21, 1998 AND JULY 2, 1998**



NEW MEXICO ENERGY, MINERALS
& NATURAL RESOURCES DEPARTMENT

APPENDIX 1.0-1

OIL CONSERVATION DIVISION
2040 South Pacheco Street
Santa Fe, New Mexico 87505
(505) 827-7131

RECEIVED

JUN 01 1998

Envirocorp Services & Technology Inc.
Houston

May 21, 1998

60A4305

CERTIFIED MAIL

RETURN RECEIPT NO. P-288-259-070

Mr. Darrell Moore
Navajo Refining Company
P.O. Box 159
Artesia, New Mexico 88211


Re: Recent Request for Injectivity Tests

Dear Mr. Moore:

Reference is made to your recent request to conduct tests on the Mewbourne Oil Company, Chalk Bluff 31 No. 1 located in Section 31, T17S, R28E to determine approximately stable injection rates and pressures. My staff has reviewed your request and the same is hereby approved for a period of 90 days, concluding on August 20, 1998. Fluids for testing will be limited to fresh water. The wellhead pressure will not exceed 1,490 psi.

If my staff may be of further assistance, please do not hesitate to call Mr. Mark Ashley at (505) 827-7155.

Sincerely,


Lori Wrotenbery
Director

LW/mwa

xc: OCD Artesia Office



NEW MEXICO ENERGY, MINERALS
& NATURAL RESOURCES DEPARTMENT

OIL CONSERVATION DIVISION
2040 South Pacheco Street
Santa Fe, New Mexico 87505
(505) 827-7131

RECEIVED

JUL 06 1998

July 2, 1998

Envirocorp Services & Technology Inc.
Houston

CERTIFIED MAIL
RETURN RECEIPT NO. P-288-259-084

Mr. Darrell Moore
Navajo Refining Company
P.O. Box 159
Artesia, New Mexico 88211

Re: Modification of Recent Request for Injectivity Tests

Dear Mr. Moore:

Reference is made to your recent request to use light brine (approximately nine pounds per gallon) or fresh water for injectivity testing on the Mowbourne Oil Company, Chalk Bluff 31 No. 1 located in Section 31, T17S, R28E to determine approximately stable injection rates and pressures. Based on the information received, your request is hereby approved.

If you have any questions, please call me at (505) 827-7155.

Sincerely,

Mark Ashley
Geologist

xc: OCD Artesia Office
Ms. Nancy Niemann, Envirocorp, 7020 Portwest Dr., #100, Houston, Texas 77024

APPENDIX 2.0-1

**ORIGINAL WELL INSTALLATION DAILY REPORTS,
MEWBOURNE OIL COMPANY, CHALK BLUFF STATE "31",
WELL NO. 1**

HEWBOURNE OIL COMPANY
P. O. BOX 7698
TYLER, TEXAS 75711

Lease Chalk Bluff "31" State Well No. 1 Location 660' FBL & 2310' FBL
County Eddy State New Mexico Section 31
Block _____ Township 17S Range 28E Page 1

| DATE | DAILY REPORTS | | | | | | | | | | | | |
|-------------------------------------|--|------------------------------------|-------|-------------------------------------|--------|------------------------------------|---------|--------------|---------|--------------------|-------|---------------|---------|
| OCT 31 1992 | Staked well @ 660' FBL & 2310' FBL of Sec 31-17S-28E in Eddy County, New Mexico. Location drillable. | | | | | | | | | | | | |
| JUL 27 1993 | Move in construction equipment. Will start building location today. | | | | | | | | | | | | |
| JUL 28 1993 | Continue building location. | | | | | | | | | | | | |
| JUL 31 1993 | Continue building location. | | | | | | | | | | | | |
| AUG 01 1993 | Continue building location. | | | | | | | | | | | | |
| AUG 02 1993 | Continue building location. | | | | | | | | | | | | |
| AUG 03 1993 | Continue building location. | | | | | | | | | | | | |
| AUG 04 1993 | Continue building location. Should finish today. | | | | | | | | | | | | |
| AUG 05 1993 | 390' (350'). Circ in Red Beds & Anhydrite. MW 10.4, Vis 32. Bit #1, Size: 17 1/2", Type: R-1, SN: RT, Jets 3/12's, IN @ 40' OUT @ 390' (made 350' in 6 3/4 hrs). PP 1023#, RPM 59, WOB All, RPM 100, Collars 42,000#. (Drilling 6 3/4, Circ 1/4, Idle 6, RU 11). REMARKS: Spud 17 1/2" hole @ 11:00 PM, 8/04/93. DAY 1 | | | | | | | | | | | | |
| AUG 06 1993 | H15' (425'). Drilling in Red Beds & Anhydrite. Dev. @ 390' - 1/2 deg. MW 8.4, Vis 28, CL 4,000, pH 10. Bit #2, Size: 12 1/4", Type: F37, SN: RR, Jets 10/11/11, IN @ 390' (made 425' in 7 3/4 hrs). PP 1375#, RPM 60, WOB 65,000#, RPM 55, Collars 71,000#. (Drilling 7 3/4, Trip 3/4, Circ 1/4, RU Run Csg & Cmt 3 1/4, WOC & NU ROP 12). Ran 13 3/8" surface casing as follows: <table> <tr> <td>13 3/8" Notched Texas Pattern Shoe</td><td>1.21'</td></tr> <tr> <td>1-13 3/8" 48# J-55 8rd STAC SJ w/IR</td><td>43.83'</td></tr> <tr> <td>8-13 3/8" 48# J-55 8rd STAC Casing</td><td>348.21'</td></tr> <tr> <td>Total Casing</td><td>393.25'</td></tr> <tr> <td>Less KB Correction</td><td>3.25'</td></tr> <tr> <td>Casing Set At</td><td>390.00'</td></tr> </table> Halliburton cmtd w/375 sks Class "C" lite containing 1/2W/sk + 3% CaCl2 followed by 150 sks Class "C" containing 3% CaCl2. PD to 348' @ 10:13 AM 8/5/93. Circ 06 sks to pit. | 13 3/8" Notched Texas Pattern Shoe | 1.21' | 1-13 3/8" 48# J-55 8rd STAC SJ w/IR | 43.83' | 8-13 3/8" 48# J-55 8rd STAC Casing | 348.21' | Total Casing | 393.25' | Less KB Correction | 3.25' | Casing Set At | 390.00' |
| 13 3/8" Notched Texas Pattern Shoe | 1.21' | | | | | | | | | | | | |
| 1-13 3/8" 48# J-55 8rd STAC SJ w/IR | 43.83' | | | | | | | | | | | | |
| 8-13 3/8" 48# J-55 8rd STAC Casing | 348.21' | | | | | | | | | | | | |
| Total Casing | 393.25' | | | | | | | | | | | | |
| Less KB Correction | 3.25' | | | | | | | | | | | | |
| Casing Set At | 390.00' | | | | | | | | | | | | |
| AUG 07 1993 | 1735' (920'). Drilling in Anhydrite & Dolomite. Dev. @ 867' - 3/4 degs; @ 1338' - 3/4 degs. MW 8.5, Vis 28, CL 2000, pH 10. Bit #2 (made 1345' in 31 1/4 hrs). PP 1375#, RPM 59, WOB 65,000#, RPM 55, Collars 71,000#. (Drilling 23 1/4, Totco 1/2). DAY 3 | | | | | | | | | | | | |
| AUG 08 1993 | 2150' (415'). Drilling in Dolomite. Dev. @ 1839' - 1 1/4 degs; @ 1988' - 1 1/2 degs. MW 8.6, Vis 28, CL 6000, Bit #2, OUT @ 1988' (made 1598' in 42 1/2 hrs). Bit #3, Size: 12 1/4", Type: J44, SN: RR, Jets 3/11's. IN @ 1988' (made 162' in 8 hrs). PP 1300#, RPM 59, WOB 65,000#, Collars 71,000#. (Drilling 19 1/4, Trip 2 3/4 hrs, Totco 1/2, Wash 120' to Btm w/100' Fill 1 1/2). DAY 4 | | | | | | | | | | | | |
| AUG 09 1993 | 2555' (405'). Circulating in Dolomite. Dev. @ 2201' - 3/4 degs. MW 8.6, Vis 28, CL 16,000, pH 9. Bit #3, Size: 12 1/4", Type: J44, SN: RR, Jets 3/11's. IN @ 1988' OUT @ 2201' (made 213' in 10 1/2 hrs). Bit #4, Size: 12 1/4", Type: J55, SN: RR, Jets 3/12's. IN @ 2201' OUT @ 2555' (made 354' in 17 3/4 hrs). PP 1100#, RPM 59, WOB 65,000#, RPM 55, Collars 71,000#. (Drilling 20 1/4, Trip 2 3/4, Circ 3/4, Wash 60' to Btm w/45' of Fill 1/4). REMARKS: Preparing to TOOH & run 9 5/8" casing. DAY 5 | | | | | | | | | | | | |

NEWBOURNE OIL COMPANY
P. O. BOX 7698
TYLER, TEXAS 75711

Lease Chalk Bluff "31" State Well No. 1 Location 660' PSL & 2310' FEL
County Hddy State New Mexico Section 31
Block _____ Township 17S Range 20E Page 2

| DATE | DAILY REPORTS | | | | | | | | | | | | | | |
|---------------------------------------|---|------------------------|-------|---------------------------------------|--------|--------------------------|-------|---------------------------------------|----------|--------------|----------|--------------------|-------|---------------|----------|
| AUG 10 1993 | <p>1700' (145'). Drilling in Dolomite. Dev. @ 2555' - 0 deg. MW 8.6, Vis 28, CL 16,000, pH 11.5. Bit #4, Size: 8 3/4", Type: Varel B537C, SN: 15789, Jets 3/11's, IN @ 2555' (made 145' in 3 hrs). PP 1475#, SPH 58, WOB 60,000#, RPM 55, Collars 68,000#. (Drilling 3, Trip 2, Circ 1/2, Run Csg & Cmt 6 1/2, WOC & NU BOP 12). Ran 9 5/0" csg as follows:</p> <table> <tr> <td>Davis-Lynch Guide Shoe</td><td>1.00'</td></tr> <tr> <td>1-9 5/0", 36#, J-55, 8rd, LTC Shoe Jt</td><td>12.55'</td></tr> <tr> <td>Davis-Lynch Float Collar</td><td>1.40'</td></tr> <tr> <td>56-9 5/8", 36#, J-55, 8rd, BTC Casing</td><td>2518.23'</td></tr> <tr> <td>Total Casing</td><td>2563.18'</td></tr> <tr> <td>Less KB Correction</td><td>8.18'</td></tr> <tr> <td>Casing Net At</td><td>2555.00'</td></tr> </table> <p>Halliburton cmtd w/800 sks Howco Lite "C" containing 1/2#/sk floccia + 2#/sk Gilsonite + 12% NaCl followed by 200 sks Class "C" Neut containing 2% CaCl2. Plug down to 2518' @ 3:00 PM, 8/9/93. Circ 133 sks to pit.</p> | Davis-Lynch Guide Shoe | 1.00' | 1-9 5/0", 36#, J-55, 8rd, LTC Shoe Jt | 12.55' | Davis-Lynch Float Collar | 1.40' | 56-9 5/8", 36#, J-55, 8rd, BTC Casing | 2518.23' | Total Casing | 2563.18' | Less KB Correction | 8.18' | Casing Net At | 2555.00' |
| Davis-Lynch Guide Shoe | 1.00' | | | | | | | | | | | | | | |
| 1-9 5/0", 36#, J-55, 8rd, LTC Shoe Jt | 12.55' | | | | | | | | | | | | | | |
| Davis-Lynch Float Collar | 1.40' | | | | | | | | | | | | | | |
| 56-9 5/8", 36#, J-55, 8rd, BTC Casing | 2518.23' | | | | | | | | | | | | | | |
| Total Casing | 2563.18' | | | | | | | | | | | | | | |
| Less KB Correction | 8.18' | | | | | | | | | | | | | | |
| Casing Net At | 2555.00' | | | | | | | | | | | | | | |
| AUG 11 1993 | <p>3545' (845'). Drilling in Dolomite. Dev. @ 3051' - 1/2 degs; @ 3520' - 3/4 degs. MW 8.4, Vis 28, CL 16,000, pH 11.0. Bit #5, Size: 8 3/4" (made 990' in 26 1/2 hrs). PP 1475#, SPH 59, WOB 60,000#, RPM 55, Collars 68,000#. (Drilling 23 1/2, Totco 1/2). DAY 7</p> | | | | | | | | | | | | | | |
| AUG 12 1993 | <p>4120' (575'). Drilling in Dolomite. Dev. @ 3983' - 1 1/4 degs. MW 9.0, Vis 29, CL 35,000, pH 9.5. Bit #5, Size: 8 3/4" OUT @ 3900' (made 1433' in 41 hrs). Bit #6, Size: 8 3/4", Type: B547, SN: 19373, Jets 12/12/11. IN @ 3988' (made 132' in 5 3/4 hrs) PP 1425#, SPH 58, WOB 60,000#. RPM 55, Collars 68,000#. (Drilling 20 1/4, Trip 1/4, Totco 1/4, Wash to Btm w/no fill 1/4). DAY 8</p> | | | | | | | | | | | | | | |
| AUG 13 1993 | <p>4635' (515'). Drilling in Dolomite. Dev. @ 4635' - 1 3/4". MW 9.0, Vis 29, CL 63,000, pH 9.5. Bit #6, Size: 8 3/4", Type: B547, SN: 19373, Jets 12/12/11. IN @ 3988' (made 647' in 129 1/4 hrs) PP 1425#, SPH 58, WOB 60,000#. RPM 60, Collars 68,000#. (Drilling 23 1/2, Totco 1/2). DAY 9</p> | | | | | | | | | | | | | | |
| AUG 14 1993 | <p>5055' (430'). Drig in Dolomite. Dev. @ 4995' - 3 1/4". MW 9.1, Vis 29, CL 65,000. Bit #6 OUT @ 5005' (made 1017' in 47 hrs). Bit #7, Type: 8 3/4", Type: V547, SN: 19480, Jets 12/12/11. IN @ 5005' (made 50' in 2 hrs). PP 1475#, SPH 58, WOB 50,000#, RPM 60, Collars 68,000#. (Drig 19 3/4, Trip 3 3/4, Wash 40' to Btm w/No Fill 1/2). DAY 10</p> | | | | | | | | | | | | | | |
| AUG 15 1993 | <p>5315' (260'). Drilling in Dolomite. Dev. @ 5120' - 3 3/4"; @ 5215' - 4 1/4"; @ 5310' - 4 1/4". MW 9.1, Vis 29, CL 80,000. Bit #7, (made 310' in 24 1/2 hrs). PP 1475#, SPH 58, WOB 20,000#, Collars 68,000#. (Drilling 22 1/2, Totco 1 1/2). DAY 11</p> | | | | | | | | | | | | | | |
| AUG 16 1993 | <p>5503' (187'). Drilling in Dolomite. Dev. @ 5403' - 4"; @ 5497' - 4 1/2". MW 9.2, Vis 29, CL 81,000, pH 10. Bit #7, (made 497' in 47 1/2 hrs). PP 1475#, SPH 58, WOB 20,000#, RPM 60, Collars 68,000#. (Drilling 23, Totco 1). DAY 12</p> | | | | | | | | | | | | | | |
| AUG 17 1993 | <p>5595' (92'). Drilling in Dolomite. Dev. @ 5527' - 4 1/4". MW 9.1, Vis 29, CL 93,000, pH 10. Bit #7, OUT @ 5527' (made 525' in 53 3/4 hrs). Bit #8, Size 8 3/4", Type: J44C, SN: RR, Jets 11/12/12, IN @ 5527' (made 68' in 12 1/4 hrs) PP 1475#, SPH 58, WOB 20,000#, RPM 60, Collars 68,000#. (Drilling 18 3/4, Trip 4 1/2, Totco 1/4, Ream 75' to Btm 1/2). REMARKS: Picked up RT tool and installed on top of collars during bit trip.</p> | | | | | | | | | | | | | | |

HEWBOURNE OIL COMPANY
P. O. BOX 7698
TYLER, TEXAS 75711

Lease Chalk Bluff "31" STATE Well No. 1 Location 650' FSL & 2310' FEL
County Eddy State New Mexico Section 31
Block Township 17S Range 28E Page 3

| DATE | DAILY REPORTS |
|-------------|---|
| AUG 18 1993 | 5786' (191'). Drilling in Dolomite. Dev. @ 5529' - 4", @ 5712' - 3 1/4". MW 9.2. Vis 29. CL 89,000. PH 10. Bit #8, Size 8 3/4", Type: J44C, SN: RR, Jets 11/12/12, IN @ 5527' (made 259' in 35 1/4 hrs) PP 1475#, SPH 58, WOB 30,000#, RPM 60, Collars 68,000#. (Drilling 22 3/4, Totco 1 1/4). DAY 14 |
| AUG 19 1993 | 6225' (439'). Drig in Dolomite. Dev. @ 5786' - 3 1/2"; @ 5879' - 3"; @ 5974' - 3"; 6195' - 3 1/2". MW 9.2. Vis 29. CL 90,000. PH 9. Bit #8, Size 8 3/4", Type: J44C, SN: RR, Jets 11/12/12, IN @ 5527' (made 698' in 50 hrs) PP 1500#, SPH 58, WOB 65,000#, RPM 60, Collars 68,000#. (Drig 19 3/4. Trip hole in DP 2 1/4. Totco 2). REMARKS: @ 5849' hole in DP 30 stds dwn. No fill after trip. DAY 15 |
| AUG 20 1993 | 6790' (565'). Drilling in Dolomite. Dev. @ 6352' - 3 1/4". MW 9.2. Vis 29. CL 88,000. PH 10. Bit #8, (made 1263' in 78 1/2 hrs) PP 1500#, SPH 58, WOB 65,000#, RPM 65, Collars 68,000#. (Drilling 23 1/2, Survey 1/2). REMARKS: Circulated through steel pits for 30 minutes on evening lower, had full returns. DAY 16 |
| AUG 21 1993 | 6825' (85'). Drig in Dolomite. Dev. @ 6795' - 2 1/2". MW 9.1. Vis 29. CL 87,000. PH 9. Bit #8 OUT @ 6795' (made 1260' in 79 hrs). Bit #2, Type: @ 3/4", Type: ATJ44C, SN: D48WC, Jets 12/12/12. IN @ 6795' (made 30' in 1 hrs). PP 1500#, SPH 58, WOB 65,000#, RPM 60, Collars 68,000#. (Drig 1 1/2, Trip 10 1/2, Circ 2. PU DST Tools 2, DST #1 5 1/4, Reverse Out 3/4, LD DST Tools 2). REMARKS: Ran DST #1 in Wolfcamp fm from 6605' to 6795'. IHP 3088#, IFP 421-1149#, ISIP 1795#, FFP 1121-1795#, FSIP 1823#, FHP 3088#, Temp 94". Opened tool w/good blow off btm of bucket increasing to 6#. No shows to surface. FF had max of 2# in 30 mins, decreasing to 10 ounces at end of flow. No shows to surface. Rec 4002' of fm fluid. Sample chamber recovery: 2400 cc's of fm wtr. DAY 17 |
| AUG 22 1993 | 7210' (385'). TOH. DST #2. Dolomite & Lime. MW 9.1. Vis 29. CL 88,000. PH 9. Bit #9, (made 415' in 19 hrs). PP 1500#, SPH 58, WOB 65,000#, RPM 60, Collars 68,000#. (Drig 18, Trip 2 1/4, Circ 3 3/4). DAY 18 |
| AUG 23 1993 | 7350' (140'). Drilling in Lime & Dolomite. MW 9.1. Vis 29. CL 88,000. PH 9. Bit #9, (made 555' in 24 3/4 hrs). PP 1500#, SPH 58, WOB 65,000#, RPM 60, Collars 68,000#. (Drilling 5 3/4, Trip 8, Wash 86' to bottom w/no fill 1/2, Cut Drig Line 3/4, Run DST #2 2, PU Test Tools 3 1/2, Pull On Stuck Pipe 1, LD Test Tools 2 1/2). REMARKS: Checked for loss thru steel pits @ 7230'. Lost 4 bbls in 30 mins. Ran DST #2 in Wolfcamp fm from 7016'-7210'. IHP 3305#, IFP 44-67#, ISIP 986#. Attempted to open tool for final flow. Unable to open tool due to collars above tool being hydrostatically stuck. Worked pipe and were unable to work loose. Dropped bar and opened circ sub. Were able to work collars loose and TOOH w/tools. Opened tool w/weak blow increasing to 16 3/4 ounces at end of IF period. No show to surface. Rec 20 stds of drill string w/small show of gas. Sample Chamber Recovery: 70#, 1000 cc's of gas-cut drig mud. Temp 120". DAY 19 |
| AUG 24 1993 | 7382' (32'). TII w/bit. Dev. @ 7382' - 2 1/4". MW 9.1. Vis 28. CL 82,000. PH 8.5. Bit #9, (made 587' in 26 1/2 hrs) PP 1500#, SPH 58, WOB 65,000#, RPM 60, Collars 68,000#. (Drilling 1 3/4, Tripping 9 3/4, Circ 4 1/4, Run DST #3 4 1/2, PU Test Tools 1 1/2, Reverse Out 3/4, LD Test Tools 1 1/2). REMARKS: Ran DST #3 in Wolfcamp fm from 7230'-7382' (152'). IHP 3451#, IFP 2094-355#, ISIP 2418#, FFP 355#-924#, FSIP 2435#. Surface Action: Opened tool w/weak blow increasing to btm of bucket in 8 mins. Max surface press 14 1/2 ozs. FF: opened w/weak blow. Max surface press 12 ozs. No show to surface on either flow period. <u>Drill Pipe Recovery: 406'</u> of slightly gas-cut drig mud & 1533' of fm wtr w/strong sulfur smell. <u>Sample Chamber Recovery: 330#, 1.01 cuft of gas, 1600 cc's of wli.</u> |

HEMBOURNE OIL COMPANY
P. O. BOX 7698
TYLER, TEXAS 75711

Lease Chalk Bluff "31" State Well No. 1 Location 860' FSL & 2310' FSL.
County Eddy State New Mexico Section 31
Block Township 17S Range 28E Page 4

| DATE | DAILY REPORTS |
|-------------|---|
| AUG 25 1993 | <p>7441' (59'). Drig in Ln & Dolo. MW 9.1, Vis 29, CL 82,000, pH 10. Bit #9, (made 646' in 28 3/4 hrs) PP 1300#, SPM 58, WOB 65,000#, RPM 60, Collars 60,000#. (Drig 2 1/4, Trip 1 1/4, Wash 90' to Btm w/No Fill 3/4, Circ 2 1/2, Run DST #4 4 1/2, PU Test Tools 1, LD Test Tools 1 3/4). REMARKS: Ran DST #4 in Wolfcamp Fm from 7385'-7413' (28'). IHP 3485#, IFP 1918-156# in 30 mins, ISIP 991# in 60 mins, FPP 1274-174# in 60 mins, PSIP 488# in 120 mins. <u>SURFACE ACTION</u>: Initial opening w/weak blow increasing to btm of bucket in 2 mins. Built to 15# in 30 mins thru 1/8" bubble hose. Shut tool in. Gas to surface in 38 mins, volume TSTM. FF: opened w/weak blow turned thru 1/4" choke. 12# in 5 mins, decreasing to 4# in 30 mins. Remained 4# to end of final flow. Gas volume TSTM, 1 1/2' 2' lazy flame. <u>Drill Pipe Recovery</u>: Rec 300' of slightly gas-cut rat hole drig mud w/trace of sulfur water. <u>Sample Chamber Recovery</u>: 80#, .57 cuft of gas, 350 cc's of wtr. CL 63,000 ppm. DAY 21</p> |
| AUG 26 1993 | <p>7851' (410'). TO for DST #5 in Dolomite. MW 9.1, Vis 28, CL 80,000, pH 9. Bit #9, (made 1056' in 46 1/2 hrs) PP 1500#, SPM 58, RPM 60, Collars 60,000#. (Drilling 17 3/4, Tripping 2 1/4, Circ Samples 8 7840' 1, Circ for DST #5 3). DAY 22</p> |
| AUG 27 1993 | <p>8215' (364'). Drilling in Dolomite. Dev. @ 7851' - 1 1/4". MW 9.1, Vis 28, CL 80,000, pH 9.5. Bit #9, (made 1420' in 53 1/4 hrs) PP 1575#, SPM 58, WOB 65,000#, RPM 60, Collars 60,000#. (Drilling 6 3/4, Tripping 0 1/4, Wash 70' to btm w/no fill 1/4, RR 1/2, DST #5 4 1/2, PU test tools 1 1/4, Reverse out 3/4, LD test tools 1 3/4). REMARKS: At 7995', lost 25-30# returns. At 8028' circ thru steel pits & lost 34 bbls in 30 mins. At 8123' pumped 30 bbl. LCM sweep. At report time, drilling w/95# returns.</p> <p>Ran DST #5 in Cisco Fm from 7015'-7051' (34'). IHP 3032#, IFP 1613#-2913#, ISIP 2913#, FPP 2913#-2913#, PSIP 2913#, FHP 3804#. <u>SURFACE ACTION</u>: FF started w/good blow on 1/4" choke beginning w/5.5# increasing to 40# in 25 mins, decreasing to 30# in 30 mins. No gas to surface. FF started w/good blow on 1/4" choke beginning w/6 oz. in 5 mins, decreasing to 0 oz. in 20 mins. remained dead throughout rest of FF. <u>DRILL STRING RECOVERY</u>: Rec 6060' (78.7 bbls) FW. No show of oil. Mud pit sample: RW=.11 @ 60", CL 78,000. Sample Recovery: RW=.35 @ 60", CL 75,000. <u>SAMPLE CHAMBER RECOVERY</u>: 1100#, .08 cuft of gas, 2575 cc's from wtr.</p> |
| AUG 28 1993 | <p>8494' (279'). Working stuck drill string. Dolomite. Dev. @ 8342' - 1 1/2". MW 9.3, Vis 37, WL 20, CL 80,000, pH 9. Bit #9, (made 1699' in 59 hrs). PP 1500#, SPM 58, WOB 65,000#, RPM 60, Collars 60,000#. (Drilling 5 3/4, Trip 5 1/2, Totco 1/2, Mix LCM 7 1/4, Work Stuck String 3, Spot Oil & Work Stuck string 2). REMARKS: Hit 5' void while drig @ 8414', lost complete returns. Pumped LCM pill & regained 95# returns. Lost complete returns @ 8414'. Pumped LCM pill & regained partial returns. TOOH & removed jets from bit & built up 400 bbl LCM pill containing 70#/bbl LCM material. TTH & spotted pill @ 8434'. While spotting pill & rotating, drill string became stuck. Attempted to work string loose unsuccessfully. Spotted 70 bbls oil around collars & let soak. Periodically working string in an attempt to get loose. At report time all efforts have been unsuccessful. DAY 24</p> |
| AUG 29 1993 | <p>8494' (0'). Laying down fishing tools. Dolomite. MW 9.3, Vis 37, WL 20, CL 80,000, pH 9. (Tripping @, Working stuck drill string @ 1/4, Run Free Point & Make Back Off 1 1/4, PU & LD Fishing Tools 3, Jar on Fish 1/2). REMARKS: Continued working drill string unsuccessfully. RU Jerrel Services & ran free point. Found collars stuck @ 8300'. Backed off collars @ 8255'. TOOH w/collars & PU fishing tools. TTH. Engaged fish & jarred same loose. TOOH & started laying down fishing tools. DAY 25</p> |

NEWMOURNE OIL COMPANY
P. O. BOX 7698
TILER, TEXAS 75711

Lease Chalk Bluff "31" State Well No. 1 Location 660' FSL & 2318' FSL
County Eddy State New Mexico Section 31
Block Township 17S Range 28E Page 5

| DATE | DAILY REPORTS |
|-------------|--|
| AUG 30 1993 | 8650' (156'). Drilling in Lime. MW 9.2, Vis 38, WL 10, CL 80,000, PH 9, PV 6, YP 10, Gels 7/18, FC Film, Calcium 1560, Solids 2.2%, LCM 8#. Bit #9 (made 1855' in 73 1/2 hrs). PP 1625#, SPM 54, WOB 60,000#, RPM 60, Collars 83,000# (840'). (Drilling 14 1/2, Tripping 3 1/4, Wash 20 jts to Btm 4 1/4, Finish LD Fishing Tools 2). REMARKS: Rejected Bit #9. TIM & washed 20 jts to Btm. Had loss of 2 bbls on evening tour & 15 bbls on morning tour. DAY 26 |
| AUG 31 1993 | 8895' (245'). Drilling in Lime. Dev. @ 8876' - 1 1/4". MW 9.2, Vis 38, WL 12, CL 78,000, PH 9.5, PV 7, YP 9, Gels 6/14, FC 1/31, Calcium 1480, Solids 2.5%, LCM 7#. Bit #9, (made 2100' in 97 hrs) PP 1650#, SPM 54, WOC 60,000#, RPM 60, Collars 63,000#. (Drilling 23 1/2, Totco 1/2). REMARKS: Lost 3 bbls on daylight, 15 bbls on evening, 20 bbls on morning tour. DAY 27 |
| SEP 01 1993 | 9077' (182'). Circ & mixing LCM in Lime. MW 9.3, Vis 38, WL 12, CL 79,000, PH 9.5, PV 9, YP 8, Gels 7/17, FC 1/32. Bit #9, (made 2202' in 110 hrs) PP 1500#, SPM 54, WOC 60,000#, RPM 60, Collars 63,000#. (Drilling 21, Mix LCM Mud 1 1/2, RR 1 1/2). REMARKS: At 9080' lost 40 bbls mud. Pumped swept & regained full returns. Resumed drlg w/full returns but started losing returns. Pumped additional sweep. At report time have 85% returns. In last 4 hrs, lost 40 bbls mud. |
| SEP 02 1993 | 9138' (61'). Drilling in Lime. Dev. @ 9077' - 1/2". MW 9.2, Vis 39, WL 12, CL 75,000, PH 10, Bit #9 OUT @ 9077' (made 2282' in 118 hrs). Bit #10, Size: 8 3/4", Type: HP62, SN: TH6443, Jets 3/13's. IN @ 9077' (made 61' in 8 3/4 hrs). PP 1250#, SPM 59, WOC 60,000#, RPM 60, Collars 63,000#. (Drilling 8 3/4, Tripping 6, Totco 1/4, Circ 3 1/4, Cut Drlg Line 1, Test BOP Stack 4, Jet Pits 3/4). REMARKS: Have lost 86 bbls mud in 16 hrs. DAY 29 |
| SEP 03 1993 | 9302' (164'). Drilling in Lime. MW 9.4, Vis 41, WL 10, CL 70,000, PH 9.5, PV 12, YP 15, Gels 14/29, FC 1/32, Solids 3.3%, LCM 8#. Bit #10, Size: 8 3/4", Type: HP62, SN: TH6443, Jets 3/13's. IN @ 9077' (made 275' in 32 3/4 hrs). PV 1375#, SPM 58, WOC 60,000#, RPM 60, Collars 63,000#. (Drilling 24). REMARKS: Lost 170 bbls on daylight, 75 bbls on evening, 12 bbls on morning tour. Total loss for past 24 hrs is 257 bbls. At report time drilling w/95% returns. DAY 30 |
| SEP 04 1993 | 9474' (172'). Drilling in Lime. MW 9.4, Vis 45, WL 10, CL 65,000, PH 9.5, PV 14, YP 15, Gels 18/34, FC 1/32, Calcium 1000, Solids 3.8%, LCM 10#. Bit #10, Size: 8 3/4", Type: HP62, SN: TH6443, Jets 3/13's. IN @ 9077' (made 397' in 56 3/4 hrs). PP 1375#, SPM 58, WOC 60,000#, RPM 60, Collars 63,000#. (Drilling 24). REMARKS: Lost 40 bbls on daylight, 30 bbls on evening, 20 bbls on morning tour. Total loss for past 24 hrs is 90 bbls. At report time drilling w/95% returns. DAY 31 |
| SEP 05 1993 | 9568' (158'). Drilling in Lime & Shale. MW 9.4, Vis 48, WL 12, CL 68,000, PH 9.5, PV 14, YP 19, Gels 16/30, FC 1/32, Calcium 880, Solids 4.0%, LCM 9#. Bit #10, Size: 8 3/4", Type: HP62, SN: TH6443, Jets 3/13's. IN @ 9077' (made 555' in 80 1/4 hrs). PP 1375#, SPM 58, WOB 60,000#, RPM 60, Collars 63,000#. (Drilling 23 1/2, Totco 1/2). REMARKS: Lost 25 bbls on daylight, 50 bbls on evening, 8 bbls on morning tour. Total loss for past 24 hrs is 83 bbls. At report time drilling w/95% returns. Rigged up mud filter and put in service at 3:30 PM. DAY 32 |
| SEP 06 1993 | 9791' (159'). Drilling in Lime & Shale. MW 9.3, Vis 38, LS 12, CL 81,000, PH 9.5, PV 13, YP 21, Gels 15/28, FC 1/32, Calcium 1100, Solids 2.8%. Bit #10 (made 714' in 104 1/4 hrs). PP 1375#, SPM 58, WOB 60,000#, RPM 60, Collars 63,000#. (Drlg 24). REMARKS: No mud lost in last 24 hrs. DAY 33 |

NEWMOURNE OIL COMPANY

P. O. BOX 7698
TYLER, TEXAS 75711

Lease Chalk Bluff "31" State Well No. 1 Location 660' FSL & 2310' FEL
County Eddy State New Mexico Section 31
Block _____ To ship 178 Range 28E Page 6

| DATE | DAILY REPORTS |
|-------------|---|
| SEP 07 1993 | 9945' (154'). Drilling in Lime & Shale. MW 9.5, Vis 39, WL 7, CL 82,000, pH 9.5, PV 15, YP 19, Gels 16/31, FC 1/32, Solids 3.4%, LCM 7#. Bit #10 (made 868' in 128 1/4 hrs). PP 1325#, SPH 57, WOB 60,000#, RPM 60, Collars 63,000# (840'). (Drilling 24). REMARKS: No mud lost past 24 hrs. DAY 34 |
| SEP 08 1993 | 10,039' (94'). Drilling in Lime & Shale. MW 9.5, Vis 40, WL 97, CL 81,000, pH 9.5, PV 16, YP 18, Gels 17/34, FC 1/32, Solids 3.5%, LCM 6#. Dev. @ 9959' - 1 3/4". Bit #10, OUT @ 9959' (made 714' in 104 1/4 hrs). Bit #11, Size 8 3/4", Type: RR. IN @ 9959' (made 80' in 13 hrs) PP 1350#, SPH 57, WOB 60,000#, RPM 60, Collars 63,000# (840'). (Drilling 15 3/4, Trip 6 1/2, Totco 1 1/4, Wash 60' to Btn w/No Fill 1/2). REMARKS: Lost 25 bbls in last 13 hrs. DAY 35 |
| SEP 09 1993 | 10,177' (138'). Drilling in Lime & Shale. MW 9.5, Vis 40, WL 8, CL 80,000, pH 9.5, PV 16, YP 15, Gels 12/26, FC 1/32, Calcium 800, Solids 3.7%, LCM 6.5#. Bit #11, Size 8 3/4", Type: RR. IN @ 9959' (made 218' in 37 hrs) PP 1350#, SPH 57, WOB 60,000#, RPM 60, Collars 63,000#. (Drilling 24). REMARKS: Lost 29 bbls mud past 24 hrs. DAY 36 |
| SEP 10 1993 | 10,200' (23'). Drilling in Shale. MW 9.6, Vis 40, WL 8, CL 85,000, pH 8.5, PV 12, YP 14, Gels 11/25, FC 1/32, Solids 3.6%, LCM 5#. Bit #11, Size 8 3/4", Type: RR. IN @ 9959' (made 218' in 37 hrs) PP 1350#, SPH 57, WOB 60,000#, RPM 60, Collars 63,000#. (Drilling 1 1/2, Trip 5 1/2, Circ 2, Logging 13). REMARKS: TD @ 9:30 AM on 9/9/93. Steel line TD 10,197'. Logger's TD 10,184'. DAY 37 |
| SEP 11 1993 | 10,200' (0'). Plugging well. (Trip 3 1/4, Circ 2 1/2, Logging 1, WOC 9, LDDG's 1 3/4, Plugging Well 6 1/2). REMARKS: Set 45 sk "H" Neat @ 9734' & 8528'. Set 55 sk "H" Neat @ 7866'. Set 45 sk "H" Neat @ 6648', 5320' & 3734'. DAY 38 |
| SEP 12 1993 | 10,200' (0'). IDLE. (WOC 4, ND & Clean Fits 4, Plugging Well 5 Idle 11). REMARKS: Set 65 sk "H" + 2% CaCl2 @ 2605'. WOC 4 hrs Tagged cmt @ 2350'. Set 40 sk "H" Neat @ 440'. Set 10 sk "H" Neat at surface. P&A operations complete @ 3:00 PM 9/11/93. Released rig @ 7:00 PM 9/11/93. DAY 39 |

APPENDIX 2.0-2

**WELL COMPLETION OR RECOMPLETION REPORT
AND LOG, FORM C-105**

Submit to Appropriate
Office

State Lease - 6 copies

Fee Lease - 5 copies

DISTRICT I

P.O. Box 1980, Hobbs, NM 88240

DISTRICT II

P.O. Drawer DD, Artesia, NM 88210

DISTRICT III

1000 Rio Brazos Rd., Aztec, NM 87410

IN DIVISION State of New Mexico

Energy, Minerals and Natural Resources Department

APPENDIX 2.0-2

Form C-105

Revised 1-1-89

OIL & GAS CONSERVATION DIVISION

P.O. Box 2088

Santa Fe, New Mexico 87504-2088

WELL API NO.

30-015-27592

5. Indicate Type of Lease

STATE ☒

FEE ☐

6. State Oil & Gas Lease No.

B-2071-28

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. Type of Well:

OIL WELL ☐

GAS WELL ☐

DRY ☒

OTHER ☐

b. Type of Completion:

NEW WELL ☐

WORK OVER ☐

DEEPEN ☐

PLUG BACK ☐

DEEP RESVR ☐

OTHER ☐

2. Name of Operator

Newbourne Oil Company

3. Address of Operator

P.O. Box 5270 Hobbs, New Mexico 88241

4. Well Location

Unit Letter 0

2310

Feet From The East

Line and 660

Feet From The South

Line

Section 31

Township 17S

Range 28E

NMPM

Eddy

County

10. Date Spudded

08/04/93

11. Date T.D. Reached

09/09/93

12. Date Compl. (Ready to Prod.)

13. Elevations (DF& RKB, RT, GR, etc.)

3078' GR

14. Elev. Casinghead

15. Total Depth

10,200'

16. Plug Back T.D.

17. If Multiple Compl. How Many Zones?

18. Intervals Drilled By

Rotary Tools

Cable Tools

19. Producing Interval(s), of this completion - Top, Bottom, Name

20. Was Directional Survey Made

No

21. Type Electric and Other Logs Run

Dual Laterlog, Density Neutron, Sonic (Already Submitted)

22. Was Well Cored

No

CASING RECORD (Report all strings set in well)

| CASING SIZE | WEIGHT LB./FT. | DEPTH SET | HOLE SIZE | CEMENTING RECORD | AMOUNT PULLED |
|-------------|----------------|-----------|-----------|---------------------|---------------|
| 13-3/8" | 48# | 390' | 17-1/2" | 375 sks. "C" Lite + | None |
| | | | | 150 sks. "C" Neet | |
| 9-5/8" | 36# | 2555' | 12-1/4" | 800 sks. "C" Lite + | None |
| | | | | 200 sks. "C" Neet | |

24.

LINER RECORD

| SIZE | TOP | BOTTOM | SACKS CEMENT | SCREEN |
|------|-----|--------|--------------|--------|
| | | | | |
| | | | | |

25. TUBING RECORD

| SIZE | DEPTH SET | PACKER SET |
|------|-----------|------------|
| | | |
| | | |

26. Perforation record (interval, size, and number)

N/A

27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.

DEPTH INTERVAL AMOUNT AND KIND MATERIAL USED

| | |
|--|--|
| | |
| | |
| | |

28.

PRODUCTION

| | | | | | | | |
|-----------------------|---|-------------------------|------------------------|------------|--------------|--------------------------------|-----------------|
| Date First Production | Production Method (Flowing, gas lift, pumping - Size and type pump) | | | | | Well Status (Prod. or Shut-in) | |
| Date of Test | Hours Tested | Choke Size | Prod'n For Test Period | Oil - Bbl. | Gas - MCF | Water - Bbl. | Gas - Oil Ratio |
| Flow Tubing Press. | Casing Pressure | Calculated 24-Hour Rate | Oil - Bbl. | Gas - MCF | Water - Bbl. | Oil Gravity - API - (Corr.) | |

29. Disposition of Gas (Sold, used for fuel, vented, etc.)

Test Witnessed By

30. List Attachments

Deviation Report

31. I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief

Signature

Bill Pierce

Printed Name

Bill Pierce

Title Drlgr. Supt.

Date 09/23/93

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well. It shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, Items 25 through 29 shall be reported for each zone. The form is to be filed in quintuplicate except on state land, where six copies are required. See Rule 1105.

Southeastern New Mexico

| | | | |
|--------------------|-------|------------------|--------|
| T. Anhy | | T. Canyon | 8782' |
| T. Salt | | T. Strawn | 9016' |
| B. Salt | | T. Atoka | 9573' |
| T. Yates | 506' | T. Miss | |
| T. 7 Rivers | 596' | T. Devonian | |
| T. Queen | 1176' | T. Silurian | |
| T. Grayburg | 1462' | T. Montoya | |
| T. San Andres | 1500' | T. Simpson | |
| T. Glorieta | 3386' | T. McKee | |
| T. Paddock | | T. Ellenburger | |
| T. Blinebry | | T. Gr. Wash | |
| T. Tubb | | T. Delaware Sand | |
| T. Drinkard | | T. Bone Springs | |
| T. Abo | 5398' | T. Morrow | 10016' |
| T. Wolfcamp | 6593' | T. | |
| T. Perm | | T. | |
| T. Cisco (Bough C) | 7816' | T. | |

| | |
|-----------------------------|------------------------|
| T. Ojo Alamo _____ | T. Penn. "B" _____ |
| T. Kirtland-Fruitland _____ | T. Penn. "C" _____ |
| T. Pictured Cliffs _____ | T. Penn. "D" _____ |
| T. Cliff House _____ | T. Leadville _____ |
| T. Menefee _____ | T. Madison _____ |
| T. Point Lookout _____ | T. Elbert _____ |
| T. Mancos _____ | T. McCracken _____ |
| T. Gallup _____ | T. Ignacio Otzte _____ |
| Base Greenhorn _____ | T. Granite _____ |
| T. Dakota _____ | T. _____ |
| T. Morrison _____ | T. _____ |
| T. Todilto _____ | T. _____ |
| T. Entrada _____ | T. _____ |
| T. Wingate _____ | T. _____ |
| T. Chinle _____ | T. _____ |
| T. Permain _____ | T. _____ |
| T. Perm "A" _____ | T. _____ |

No. 1, from to
No. 2, from to
No. 3, from to
No. 4, from to

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from to feet

No. 2, from to feet

No. 3, from to feet

| From | To | Thickness in Feet | Lithology | From | To | Thickness in Feet | Lithology |
|-------|--------|----------------------|--------------------------------------|------|----|----------------------|-----------|
| 0' | 400' | 400' | Surface rock, Anhydrite | | | | |
| 400' | 6900' | 6500' | Dolomite, Chert, Sandstone, Shale | | | | |
| 6900' | 7800' | 900' | Limestone, Shale, Chert | | | | |
| 7800' | 8500' | 700' | Dolomite, Shale | | | | |
| 8500' | 9600' | 1100' | Limestone, Shale | | | | |
| 9600' | 10200' | 600' | Limestone, Sandstone, Chert, & Shale | | | | |

APPENDIX 2.0-3

**SUNDRY NOTICE FOR PLUG AND ABANDONMENT,
FORM C-103**

Submit 3 Copies
to Appropriate
District Office

State of New Mexico
Energy, Minerals and Natural Resources Department

APPENDIX 2.0-3

Form C-103
Revised 1-1-89

CONSERVATION DIVISION

REIL CONSERVATION DIVISION

DISTRICT I
P.O. Box 1980, Hobbs, NM 88240

DISTRICT II
P.O. Drawer DD, Artesia, NM 88210

DISTRICT III
1000 Rio Brazos Rd., Aztec, NM 87410

P.O. Box 2088
P.O. Box 2088
New Mexico 87504-2088

| |
|---|
| WELL API NO. 30-015-27592 |
| 5. Indicate Type of Lease STATE <input checked="" type="checkbox"/> FEE <input type="checkbox"/> |
| 6. State Oil & Gas Lease No. B-2071-28 |
| 7. Lease Name or Unit Agreement Name Chalk Bluff "31" State |
| 8. Well No. 1 |
| 9. Pool name or Wildcat Illinois Camp Morrow, North |
| 10. Elevation (Show whether DF, RKB, RT, GR, etc.) 3678' GR |

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A
DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT"
(FORM C-101) FOR SUCH PROPOSALS.)

| |
|---|
| 1. Type of Well: OIL WELL <input type="checkbox"/> GAS WELL <input checked="" type="checkbox"/> OTHER |
| 2. Name of Operator Mewbourne Oil Company |
| 3. Address of Operator P. O. Box 5270 ; Hobbs, New Mexico 88241 |
| 4. Well Location Unit Letter <u>0</u> : <u>2310</u> Feet From The <u>East</u> Line and <u>600'</u> Feet From The <u>South</u> Line Section <u>31</u> Township <u>17S</u> Range <u>28E</u> NMPM <u>Eddy</u> County |
| 10. Elevation (Show whether DF, RKB, RT, GR, etc.) 3678' GR |

| | |
|---|--|
| 11. Check Appropriate Box to Indicate Nature of Notice, Report, or Other Data | |
| NOTICE OF INTENTION TO: | SUBSEQUENT REPORT OF: |
| PERFORM REMEDIAL WORK <input type="checkbox"/> | REMEDIAL WORK <input type="checkbox"/> |
| TEMPORARILY ABANDON <input type="checkbox"/> | ALTERING CASING <input type="checkbox"/> |
| PULL OR ALTER CASING <input type="checkbox"/> | COMMENCE DRILLING OPNS. <input type="checkbox"/> |
| OTHER: <input type="checkbox"/> | PLUG AND ABANDONMENT <input checked="" type="checkbox"/> |
| | CASING TEST AND CEMENT JOB <input type="checkbox"/> |
| | OTHER: <input type="checkbox"/> |

12. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work) SEE RULE 1103.

9-9-93: Drilled 8 3/4" production hole to a T.D. of 10,200' K.B. Ran electric logs and evaluated well.

9-10-93: Decided to plug well. Received verbal permission from Mike Stubblefield w/NMOCD office in Artesia to plug well. Placed cement plugs at following depths:

| | |
|--|---------------------------------|
| 45 sacks of Class "H" Neet @ 9734' | 40 sacks of Class "H" Neet @ 44 |
| 45 sacks of Class "H" Neet @ 8523' | 10 sacks of Class "H" Neet From |
| 55 sacks of Class "H" Neet @ 7866' | 30' to surface. |
| 45 sacks of Class "H" Neet @ 6648' | Rig released @ 7:00 PM, 9-11-93 |
| 45 sacks of Class "H" Neet @ 5320' | Installed dry hole marker. |
| 45 sacks of Class "H" Neet @ 3734' | |
| 65 sacks of Class "H" Neet w/2% CaCl ₂ @ 2605'. WOC 4 hours. Tagged | |
| top of cement plug @ 2350'. | |

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Bill Price TITLE Drilling Superintendent DATE Sept. 13, 1993

TYPE OR PRINT NAME TELEPHONE NO.

(This space for State Use)

APPROVED BY Mike Stubblefield TITLE Field Rep. 1 DATE April 11-94

CONDITIONS OF APPROVAL, IF ANY:

APPENDIX 2.5-1
FORMATION FLUID ANALYSIS

TRACE ANALYSIS, INC.

6701 Aberdeen Avenue

Lubbock, Texas 79424

806-734-1296

FAX 806-734-1298

September 16, 1988

Receiving Date: 08/01/88

Sample Type: Water

Project No: NA

Project Location: Wastewater Wells - Artesia

ANALYTICAL RESULTS FOR

NAVAJO REFINING

Attention: Darrell Moore

501 E. Main

Artesia, NM 88210

Prep Date: 09/02/88

Analysis Date: 09/11/88

Sampling Date: 07/31/88

Sample Condition: Intact & Cool

Sample Received by: MS

Project Name: NA

After 16 hours @ 130 F

| TA# | Field Code | POTASSIUM (mg/L) | MAGNESIUM (mg/L) | CALCIUM (mg/L) | SODIUM (mg/L) |
|-----------------------|----------------|---------------------|---------------------|-------------------|------------------|
| T103911 | Upper Zone | 120 | 152 | 215 | 4,470 |
| T103912 | Lower Zone | 403 | 166 | 372 | 11,000 |
| T103993 | Upper Zone 2:1 | 92 | 111 | 175 | 2,960 |
| T103994 | Upper Zone 1:1 | 74 | 91 | 158 | 2,280 |
| T103995 | Upper Zone 1:2 | 55 | 70 | 170 | 1,630 |
| T103996 | Lower Zone 2:1 | 264 | 122 | 334 | 6,300 |
| T103997 | Lower Zone 1:1 | 203 | 98 | 272 | 6,230 |
| T103998 | Lower Zone 1:2 | 139 | 77 | 237 | 4,400 |
| ICV | | 24 | 25 | 28 | 25 |
| CCV | | 24 | 26 | 25 | 26 |
| Reporting Limit | | 0.50 | 0.50 | 0.50 | 0.50 |
| METHOD BLANK | | <0.50 | <0.50 | <0.50 | <0.50 |
| RPD | | 2 | 1 | 1 | 6 |
| % Extraction Accuracy | | 120 | 93 | 94 | 105 |
| % Instrument Accuracy | | 99 | 102 | 104 | 104 |

METHODS: EPA 200.7.

CHEMIST: RR

SPIKE: 1,000 mg/L POTASSIUM, MAGNESIUM, CALCIUM, SODIUM.

CV: 25 mg/L POTASSIUM, MAGNESIUM, CALCIUM, SODIUM.

Director, Dr. Blair Lefwich

Date

9-16-88

TRACE ANALYSIS, INC.

6701 Aberdeen Avenue

Lubbock, Texas 79424

806-794-1236

FAX 806-794-1236

September 16, 1988

Receiving Date: 08/01/88

Sample Type: Water

Project No: NA

Project Location: Wastewater Wells - Artesia

ANALYTICAL RESULTS FOR

NAVAJO REFINING

Attention: Darrell Moore

501 E. Main

Artesia, NM 88210

Prep Date: 08/11/88

Analysis Date: 08/18/88

Sampling Date: 07/31/88

Sample Condition: Intact & Cool

Sample Received by: MS

Project Name: NA

ROOM TEMPERATURE

| TA# | Field Code | POTASSIUM (mg/L) | MAGNESIUM (mg/L) | CALCIUM (mg/L) | SODIUM (mg/L) |
|-----|------------|------------------|------------------|----------------|---------------|
|-----|------------|------------------|------------------|----------------|---------------|

| | | | | | |
|---------|----------------|-----|-----|-----|--------|
| T103811 | Upper Zone | 61 | 128 | 276 | 4,785 |
| T103812 | Lower Zone | 213 | 143 | 390 | 12,770 |
| T103883 | Upper Zone 2:1 | 26 | 80 | 214 | 3,114 |
| T103884 | Upper Zone 1:1 | 18 | 65 | 282 | 2,481 |
| T103885 | Upper Zone 1:2 | 5.3 | 39 | 213 | 1,675 |
| T103886 | Lower Zone 2:1 | 138 | 99 | 384 | 8,920 |
| T103887 | Lower Zone 1:1 | 88 | 70 | 277 | 6,778 |
| T103888 | Lower Zone 1:2 | 54 | 43 | 201 | 4,547 |
| ICV | | 25 | 25 | 25 | 26 |
| CCV | | 25 | 25 | 25 | 26 |

Reporting Limit
METHOD BLANK

RPD
% Extraction Accuracy
% Instrument Accuracy

*NOTE: Used LCS for Extraction Accuracy and RPD due to high concentration in sample.

METHODS: EPA 200.7.

CHEMIST: RR

SPIKE: 100 mg/L POTASSIUM, MAGNESIUM, CALCIUM, SODIUM.

CV: 25 mg/L POTASSIUM, MAGNESIUM, CALCIUM, SODIUM.

9-16-88

Director, Dr. Blair Lefkovich

Date

TRACE ANALYSIS, INC.

8701 Aberdeen Avenue, Suite 9 Lubbock, Texas 79424 800-378-1298 H16-794-1298 FAX 808-794-1298
4725 Ripley Avenue, Suite A El Paso, Texas 79922 888-588-3443 915-585-3443 FAX 915-585-4944
E-Mail: lab@traceanalysis.com

ANALYTICAL RESULTS FOR NAVAJO REFINING

September 18, 1998
Receiving Date: 08/01/98
Sample Type: Water
Project No: NA
Project Location: Wastewater Wells - Artesia

Attention: Darrell Moore
501 E. Main
Artesia, NM 88210

Sampling Date: 07/31/98
Sample Condition: I & C
Sample Received by: MS
Project Name: NA

ROOM TEMPERATURE

| TA# | FIELD CODE | N03-N* (mg/L) | TSS (mg/L) | TDS (mg/L) | FLUORIDE (mg/L) | CHLORIDE (mg/L) | SULFATE (mg/L) |
|-----------------------|----------------|------------------|---------------|---------------|--------------------|--------------------|-------------------|
| T103911 | Upper Zone | <10 | 48 | 15,000 | 3.7 | 8,500 | 1,800 |
| T103912 | Lower Zone | <10 | 170 | 33,000 | 2.6 | 19,000 | 2,200 |
| T103994 | Upper Zone 1:1 | <10 | 230 | 9,000 | 16 | 3,900 | 1,200 |
| ICV | | 4.8 | --- | --- | 0.97 | 12 | 12 |
| CCV | | 4.8 | --- | --- | 0.94 | 12 | 12 |
| RPD | | 4 | 0 | 8 | 8 | 0 | 1 |
| % Extraction Accuracy | | 95 | --- | --- | 104 | 96 | 99 |
| % Instrument Accuracy | | 97 | --- | 98 | 97 | 98 | 98 |
| REPORTING LIMIT | | 10 | --- | --- | 0.1 | 0.5 | 0.6 |

PREP DATE 08/08/98 08/08/98 08/08/98 08/07/98 08/08/98 08/08/98
ANALYSIS DATE 08/08/98 08/08/98 08/08/98 08/07/98 08/08/98 08/08/98

| | | ALKALINITY (mg/L as CaCO3) | | SPECIFIC GRAVITY (g/mL) | SPECIFIC CONDUCTANCE (uMHOS/cm) | pH (s.u.) |
|-----------------------|----------------|-------------------------------|-------|-------------------------------|---------------------------------------|--------------|
| | | HC03 | CO3 | | | |
| T103911 | Upper Zone | 1,400 | <1.0 | 1.018 | 27,000 | 7.8 |
| T103912 | Lower Zone | 1,000 | <1.0 | 1.034 | 52,000 | 8.1 |
| T103994 | Upper Zone 1:1 | 410 | 8 | 1.005 | 13,000 | 8.5 |
| ICV | | 1,100 | 1,100 | --- | 1,386 | 7.0 |
| CCV | | 1,130 | 1,060 | --- | 1,387 | 7.0 |
| RPD | | 1 | 1 | 0 | 1 | 0 |
| % Extraction Accuracy | | --- | --- | --- | 98 | --- |
| % Instrument Accuracy | | 91 | 91 | --- | 99 | 100 |
| REPORTING LIMIT | | --- | --- | --- | --- | --- |

PREP DATE 08/11/98 08/08/98 08/07/98 08/08/98
ANALYSIS DATE 08/11/98 08/08/98 08/07/98 08/08/98

*NOTE: Out of holding time for N03-N.

METHODS: EPA 150.1, 300.0, 160.2, 160.1, 340.2, 120.1, 310.1; ASTM D854-92.

CHEMIST: pH/TSS: BP N03-N/FLUORIDE/CHLORIDE/SULFATE/SPECIFIC GRAVITY: JS

TDS/SPECIFIC CONDUCTANCE/ALKALINITY: RS

N03-N SPIKE: 125 mg/L N03-N.

FLUORIDE SPIKE: 10 mg/L FLUORIDE.

CHLORIDE SPIKE: 312.5 mg/L CHLORIDE.

SULFATE SPIKE: 312.5 mg/L SULFATE.

N03-N CV: 5.0 mg/L N03-N.

FLUORIDE CV: 1.0 mg/L FLUORIDE.

CHLORIDE CV: 12.5 mg/L CHLORIDE.

SULFATE CV: 12.5 mg/L SULFATE.

Director, Dr. Blair Leftwich

DATE

TRACE ANALYSIS, INC.

6701 Aberdeen Avenue, Suite 9 Lubbock, Texas 79424 800-378-1296 806-794-1796 FAX 806-794-1298
 4726 Ripley Avenue, Suite A El Paso, Texas 79922 889-588-3443 915-585-3443 FAX 915-585-4544
 E-Mail: lab@traceanalysis.com

ANALYTICAL RESULTS FOR NAVAJO REFINING

September 18, 1998
 Receiving Date: 08/01/98
 Sample Type: Water
 Project No: NA
 Project Location: Wastewater Wells - Artesia

Attention: Darrell Moore
 501 E. Main
 Artesia, NM 86210

Sampling Date: 07/31/98
 Sample Condition: I & C
 Sample Received by: MS
 Project Name: NA

ROOM TEMPERATURE

| TA# | FIELD CODE | N03-N* (mg/L) | | TSS (mg/L) | TDS (mg/L) | FLUORIDE (mg/L) | CHLORIDE (mg/L) | SULFATE (mg/L) |
|-----------------------|----------------|------------------|-------|---------------|---------------|--------------------|--------------------|-------------------|
| T103993 | Upper Zone 2:1 | <10 | | 560 | 11,000 | 14 | 6,000 | 1,400 |
| ICV | | 4.8 | | --- | --- | 0.97 | 11 | 12 |
| CCV | | 4.8 | | --- | --- | 0.94 | 11 | 12 |
| RPD | | 4 | | 0 | 8 | 8 | 5 | 1 |
| % Extraction Accuracy | | 95 | | --- | --- | 104 | 93 | 99 |
| % Instrument Accuracy | | 97 | | --- | 98 | 97 | 93 | 98 |
| REPORTING LIMIT | | 10 | | --- | --- | 0.1 | 0.5 | 0.5 |
| PREP DATE | | 08/06/98 | | 08/09/98 | 08/06/98 | 08/07/98 | 08/10/98 | 08/06/98 |
| ANALYSIS DATE | | 08/08/98 | | 08/09/98 | 08/06/98 | 08/07/98 | 08/10/98 | 08/06/98 |
| | | ALKALINITY | | SPECIFIC | SPECIFIC | | | |
| | | (mg/L as CaCO3) | | GRAVITY | CONDUCTANCE | pH | | |
| | | HC03 | C03 | (g/mL) | (uMHOS/cm) | (s.u.) | | |
| T103993 | Upper Zone 2:1 | 700 | <1.0 | 1.010 | 18,000 | 8.2 | | |
| ICV | | 1.100 | 1.100 | --- | 1,396 | 7.0 | | |
| CCV | | 1.130 | 1.080 | --- | 1,387 | 7.0 | | |
| RPD | | 1 | 1 | 0 | 1 | 0 | | |
| % Extraction Accuracy | | --- | --- | --- | 98 | --- | | |
| % Instrument Accuracy | | 91 | 91 | --- | 99 | 100 | | |
| REPORTING LIMIT | | --- | --- | --- | --- | --- | | |
| PREP DATE | | 08/11/98 | | 08/06/98 | 08/07/98 | 08/09/98 | | |
| ANALYSIS DATE | | 08/11/98 | | 08/06/98 | 08/07/98 | 08/09/98 | | |

*NOTE: Out of holding time for N03-N.

METHODS: EPA 150.1, 300.0, 160.2, 160.1, 340.2, 120.1, 310.1; ASTM D854-92.

CHEMIST: pH/TSS: BP N03-N/FLUORIDE/CHLORIDE/SULFATE/SPECIFIC GRAVITY: JS

TDS/SPECIFIC CONDUCTANCE/ALKALINITY: RS

N03-N SPIKE: 125 mg/L N03-N.

FLUORIDE SPIKE: 10 mg/L FLUORIDE.

CHLORIDE SPIKE: 1,250 mg/L CHLORIDE.

SULFATE SPIKE: 312.5 mg/L SULFATE.

N03-N CV: 5.0 mg/L N03-N.

FLUORIDE CV: 1.0 mg/L FLUORIDE.

CHLORIDE CV: 12.5 mg/L CHLORIDE.

SULFATE CV: 12.5 mg/L SULFATE.


 Director, Dr. Blair Leftwich

9-16-98
 DATE

TRACE ANALYSIS, INC.

8701 Aberdeen Avenue, Suite 9 Lubbock, Texas 79424 800-378-1298 808-794-1298 FAX 808-794-1298
 4725 Ripley Avenue, Suite A El Paso, Texas 79922 888-588-3443 915-585-3443 FAX 915-585-4944
 E-Mail: lab@traceanalysis.com

ANALYTICAL RESULTS FOR NAVAJO REFINING

September 16, 1998
 Receiving Date: 08/01/98
 Sample Type: Water
 Project No: NA
 Project Location: Wastewater Wells - Artesia

Attention: Darrell Moore
 501 E. Main
 Artesia, NM 88210

Sampling Date: 07/31/98
 Sample Condition: I & C
 Sample Received by: MS
 Project Name: NA

ROOM TEMPERATURE

| TA# | FIELD CODE | NO3-N* (mg/L) | TSS (mg/L) | TDS (mg/L) | FLUORIDE (mg/L) | CHLORIDE (mg/L) | SULFATE (mg/L) |
|-----------------------|----------------|------------------|---------------|---------------|--------------------|--------------------|-------------------|
| T103995 | Upper Zone 1:2 | <10 | 320 | 8,000 | 24 | 2,600 | 960 |
| T103996 | Lower Zone 2:1 | <10 | 530 | 23,000 | 13 | 14,000 | 1,700 |
| T103997 | Lower Zone 1:1 | <10 | 430 | 18,000 | 20 | 12,000 | 1,500 |
| T103998 | Lower Zone 1:2 | <10 | 230 | 13,000 | 23 | 13,000 | 1,100 |
| ICV | | 4.8 | — | — | 0.97 | 12 | 12 |
| CCV | | 4.8 | — | — | 0.94 | 12 | 12 |
| RPD | | 1 | 0 | 8 | 8 | 1 | 4 |
| % Extraction Accuracy | | 106 | — | — | 104 | 90 | 109 |
| % Instrument Accuracy | | 97 | — | 98 | 97 | 97 | 97 |
| REPORTING LIMIT | | 10 | — | — | 0.1 | 0.5 | 0.5 |

| | | | | | | |
|---------------|-----------------|----------|----------|-----------|-------------|----------|
| PREP DATE | 08/08/98 | 08/08/98 | 08/08/98 | 08/07/98 | 08/08/98 | 08/08/98 |
| ANALYSIS DATE | 08/08/98 | 08/09/98 | 08/08/98 | 08/07/98 | 08/08/98 | 08/06/98 |
| | ALKALINITY | | SPECIFIC | | SPECIFIC | |
| | (mg/L as CaCO3) | | GRAVITY | | CONDUCTANCE | |
| | HC03 | CO3 | (g/mL) | (uMHO/cm) | pH | |
| | | | | | (s.u.) | |

| | | | | | | |
|-----------------------|----------------|-------|-------|-------|--------|-----|
| T103995 | Upper Zone 1:2 | 340 | 4 | 1.010 | 9,300 | 8.5 |
| T103996 | Lower Zone 2:1 | 570 | <1.0 | 1.018 | 44,000 | 8.2 |
| T103997 | Lower Zone 1:1 | 540 | 2.0 | 1.023 | 34,000 | 8.4 |
| T103998 | Lower Zone 1:2 | 370 | 10 | 1.009 | 20,000 | 8.6 |
| ICV | | 1,100 | 1,100 | — | 1,396 | 7.0 |
| CCV | | 1,130 | 1,080 | — | 1,387 | 7.0 |
| RPD | | 1 | 1 | 0 | 1 | 0 |
| % Extraction Accuracy | | — | — | — | 98 | — |
| % Instrument Accuracy | | 91 | 91 | — | 99 | 100 |
| REPORTING LIMIT | | — | — | — | — | — |

| | | | | |
|---------------|----------|----------|----------|----------|
| PREP DATE | 08/11/98 | 08/08/98 | 08/07/98 | 08/09/98 |
| ANALYSIS DATE | 08/11/98 | 08/08/98 | 08/07/98 | 08/09/98 |

*NOTE: Out of holding time for NO3-N.

METHODS: EPA 150.1, 300.0, 160.2, 160.1, 340.2, 120.1, 310.1; ASTM D854-82.

CHEMIST: pH/TSS: BP NO3-N/FLUORIDE/CHLORIDE/SULFATE/SPECIFIC GRAVITY: JS

TDS/SPECIFIC CONDUCTANCE/ALKALINITY: RS

NO3-N SPIKE: 125 mg/L NO3-N.

FLUORIDE SPIKE: 10 mg/L FLUORIDE.

CHLORIDE SPIKE: 312.5 mg/L CHLORIDE.

SULFATE SPIKE: 312.5 mg/L SULFATE.

NO3-N CV: 5.0 mg/L NO3-N.

FLUORIDE CV: 1.0 mg/L FLUORIDE.

CHLORIDE CV: 12.5 mg/L CHLORIDE.

SULFATE CV: 12.5 mg/L SULFATE.

RS

Director, Dr. Blair Leftwich

9-16-98

DATE

TRACE ANALYSIS, INC.

6701 Aberdeen Avenue, Suite H Lubbock, Texas 79424 800-378-1298 808-794-1298 FAX 808-794-1298
 4725 Hixley Avenue, Suite A El Paso, Texas 79922 888-588-3443 915-585-3443 FAX 915-585-4944
 E-Mail: lab@traceanalysis.com

ANALYTICAL RESULTS FOR NAVAJO REFINING

September 16, 1998
 Receiving Date: 08/01/98
 Sample Type: Water
 Project No: NA

Attention: Darrell Moore
 501 E. Main
 Artesia, NM 88210

Sampling Date: 07/31/98
 Sample Condition: I & C
 Sample Received by: MS
 Project Name: NA

Project Location: Wastewater Wells - Artesia

After 16 hours @ 130 ° F

| TA# | FIELD CODE | NO ₃ -N* (mg/L) | TSS (mg/L) | TDS (mg/L) | FLUORIDE (mg/L) | CHLORIDE (mg/L) | SULFATE (mg/L) |
|-----------------------|----------------|-------------------------------|---------------|---------------|--------------------|--------------------|-------------------|
| T103911 | Upper Zone | <10 | 3,200 | 17,000 | 2.7 | 7,200 | 1,800 |
| T103912 | Lower Zone | <10 | 1,040 | 38,000 | 2.0 | 22,000 | 2,100 |
| T103993 | Upper Zone 2:1 | <10 | 1,900 | 11,000 | 12 | 49,000 | 1,300 |
| ICV | | 4.7 | --- | --- | 0.97 | 11 | 12 |
| CCV | | 4.7 | --- | --- | 0.98 | 11 | 11 |
| RPD | | 3 | 3 | 1 | 0 | 5 | 0 |
| % Extraction Accuracy | | 105 | --- | --- | 100 | 93 | 110 |
| % Instrument Accuracy | | 96 | --- | 101 | 97 | 93 | 97 |
| REPORTING LIMIT | | 10 | --- | --- | 0.1 | 0.5 | 0.5 |

| | | | | | | |
|---------------|------------------------------|-----------------|----------|------------|-------------|----------|
| PREP DATE | 08/28/98 | 08/12/98 | 08/10/98 | 08/12/98 | 08/10/98 | 08/10/98 |
| ANALYSIS DATE | 08/28/98 | 08/12/98 | 08/10/98 | 08/12/98 | 08/10/98 | 08/10/98 |
| | ALKALINITY | | SPECIFIC | | SPECIFIC | |
| | (mg/L as CaCO ₃) | | GRAVITY | | CONDUCTANCE | |
| | HCO ₃ | CO ₃ | (g/mL) | (uMHOS/cm) | pH | |
| | | | | | (s.u.) | |

| | | | | | | |
|-----------------------|----------------|-------|-------|-------|--------|-----|
| T103911 | Upper Zone | 720 | 36 | 1.016 | 27,000 | 8.6 |
| T103912 | Lower Zone | 570 | 8.0 | 1.036 | 68,000 | 8.4 |
| T103993 | Upper Zone 2:1 | 480 | 24 | 1.016 | 18,000 | 8.8 |
| ICV | | 1,080 | 1.100 | --- | 1,335 | 7.0 |
| CCV | | 1,040 | 1,120 | --- | 1,327 | 7.0 |
| RPD | | 1 | 1 | 0 | 2 | 0 |
| % Extraction Accuracy | | --- | --- | --- | 94 | --- |
| % Instrument Accuracy | | 90 | 80 | --- | 94 | 100 |
| REPORTING LIMIT | | --- | --- | --- | --- | --- |

| | | | | |
|---------------|----------|----------|----------|----------|
| PREP DATE | 08/14/98 | 08/11/98 | 08/10/98 | 08/12/98 |
| ANALYSIS DATE | 08/14/98 | 08/11/98 | 08/10/98 | 08/12/98 |

*NOTE: Out of holding time for NO₃-N.

METHODS: EPA 150.1, 300.0, 180.2, 180.1, 340.2, 120.1, 310.1; ASTM D854-92.

CHEMIST: pH/TSS: BP NO₃-N/FLUORIDE/CHLORIDE/SULFATE/SPECIFIC GRAVITY: JS

TDS/SPECIFIC CONDUCTANCE/ALKALINITY: RS

NO₃-N SPIKE: 125 mg/L NO₃-N.

FLUORIDE SPIKE: 10 mg/L FLUORIDE.

CHLORIDE SPIKE: 1,250 mg/L CHLORIDE.

SULFATE SPIKE: 1,250 mg/L SULFATE.

NO₃-N CV: 5.0 mg/L NO₃-N.

FLUORIDE CV: 1.0 mg/L FLUORIDE.

CHLORIDE CV: 12.5 mg/L CHLORIDE.

SULFATE CV: 12.5 mg/L SULFATE.


 Director, Dr. Blair Leftwich

9-16-98
 DATE

TRACE ANALYSIS, INC.

6701 Aberdeen Avenue, Suite 9
4725 Ripley Avenue, Suite A

Lubbock, Texas 79424 800-378-1296
El Paso, Texas 79922 989-688-3443
E-Mail: lab@traceanalysis.com

806-794-1296 FAX 806-794-1296
915-585-3443 FAX 915-585-4944

ANALYTICAL RESULTS FOR NAVAJO REFINING

September 16, 1998
Receiving Date: 08/01/98
Sample Type: Water
Project No: NA
Project Location: Wastewater Wells - Artesia

Attention: Darrell Moore
601 E. Main
Artesia, NM 88210

Sampling Date: 07/31/98
Sample Condition: I & C
Sample Received by: MS
Project Name: NA

After 16 hours @ 130 °F

| TA# | FIELD CODE | N03-N* (mg/L) | TSS (mg/L) | TDS (mg/L) | FLUORIDE (mg/L) | CHLORIDE (mg/L) | SULFATE (mg/L) |
|-----------------------|----------------|------------------|---------------|---------------|--------------------|--------------------|-------------------|
| T103994 | Upper Zone 1:1 | <10 | 370 | 8,700 | 17 | 3,500 | 1,100 |
| T103995 | Upper Zone 1:2 | <10 | 300 | 6,600 | 24 | 2,400 | 880 |
| T103996 | Lower Zone 2:1 | <10 | 300 | 27,000 | 12 | 14,000 | 1,600 |
| ICV | | 4.7 | — | — | 0.97 | 11 | 11 |
| CCV | | 4.7 | — | — | 0.98 | 11 | 11 |
| RPD | | 3 | 3 | 1 | 0 | 2 | 2 |
| % Extraction Accuracy | | 105 | — | — | 100 | 92** | 95** |
| % Instrument Accuracy | | 98 | — | 101 | 97 | 93 | 95 |

REPORTING LIMIT

10

—

—

0.1

0.5

0.5

PREP DATE

08/28/98

08/12/98

08/10/98

08/12/98

08/10/98

08/10/98

ANALYSIS DATE

08/28/98

08/12/98

08/10/98

08/12/98

08/10/98

08/10/98

ALKALINITY
(mg/L as CaCO₃)
HCO₃ CO₃

SPECIFIC
GRAVITY
(g/mL)

SPECIFIC
CONDUCTANCE
(uMHOS/cm)

pH
(s.u.)

| | | | | | | |
|---------|----------------|-------|-------|-------|--------|-----|
| T103994 | Upper Zone 1:1 | 520 | 58 | 1.012 | 14,000 | 8.7 |
| T103995 | Upper Zone 1:2 | 370 | 20 | 1.004 | 11,000 | 9.0 |
| T103996 | Lower Zone 2:1 | 430 | 8.0 | 1.021 | 48,000 | 8.5 |
| ICV | | 1,080 | 1,100 | — | 1,335 | 7.0 |
| CCV | | 1,040 | 1,120 | — | 1,327 | 7.0 |

RPD

1

1

0

2

0

% Extraction Accuracy

—

—

—

94

—

% Instrument Accuracy

90

90

—

94

100

REPORTING LIMIT

—

—

—

—

—

PREP DATE

08/14/98

08/11/98

08/10/98

08/12/98

ANALYSIS DATE

08/14/98

08/11/98

08/10/98

08/12/98

*NOTE: Out of holding time for N03-N.

**NOTE: Chloride and Sulfate spikes % Extraction Accuracy low. LRB spikes % Extraction Accuracy used due to matrix difficulties. LRB spikes in range.

METHODS: EPA 160.1, 300.0, 160.2, 160.1, 340.2, 120.1, 310.1; ASTM D854-92.

CHEMIST: pH/TSS: BP N03-N/FLUORIDE/CHLORIDE/SULFATE/SPECIFIC GRAVITY: JS

TDS/SPECIFIC CONDUCTANCE/ALKALINITY: RS

N03-N SPIKE: 125 mg/L N03-N.

FLUORIDE SPIKE: 10 mg/L FLUORIDE.

CHLORIDE SPIKE: 312.5 mg/L CHLORIDE.

SULFATE SPIKE: 312.5 mg/L SULFATE.

N03-N CV: 5.0 mg/L N03-N.

FLUORIDE CV: 1.0 mg/L FLUORIDE.

CHLORIDE CV: 12.5 mg/L CHLORIDE.

SULFATE CV: 12.5 mg/L SULFATE.

9-16-98

Director, Dr. Blair Leftwich

DATE

TRACE ANALYSIS, INC.

6701 Aberdeen Avenue, Suite 9 Lubbock, Texas 79424 800-378-1296 806-734-1796 FAX 806-794-1298
4725 Ripley Avenue, Suite A El Paso, Texas 79922 888-588-3443 915-585-3443 FAX 915-585-4944
E-Mail: lab@traceanalysis.com

ANALYTICAL RESULTS FOR NAVAJO REFINING

September 16, 1998
Receiving Date: 08/01/98
Sample Type: Water
Project No: NA
Project Location: Wastewater Wells - Artesia

Attention: Darrell Moore
501 E. Main
Artesia, NM 88210

Sampling Date: 07/31/98
Sample Condition: I & C
Sample Received by: MS
Project Name: NA

After 16 hours @ 130 °F

| TA# | FIELD CODE | N03-N* (mg/L) | TSS (mg/L) | TDS (mg/L) | FLUORIDE (mg/L) | CHLORIDE (mg/L) | SULFATE (mg/L) |
|-----------------------|----------------|------------------|---------------|---------------|--------------------|--------------------|-------------------|
| T103997 | Lower Zone 1:1 | <10 | 180 | 22,000 | 16 | 11,000 | 1,500 |
| T103998 | Lower Zone 1:2 | <10 | 340 | 15,000 | 22 | 7,100 | 1,000 |
| ICV | | 4.7 | --- | --- | 0.97 | 11 | 11 |
| CCV | | 4.7 | --- | --- | 0.98 | 11 | 12 |
| RPD | | 3 | 3 | 1 | 0 | 1 | 1 |
| % Extraction Accuracy | | 105 | --- | --- | 100 | 91 | 93 |
| % Instrument Accuracy | | 98 | --- | 101 | 97 | 94 | 97 |
| REPORTING LIMIT | | 10 | --- | --- | 0.1 | 0.5 | 0.5 |

| PREP DATE | 08/28/98 | 08/12/98 | 08/10/98 | 08/12/98 | 08/10/98 | 08/10/98 |
|-----------------------|------------------------------|-----------------|------------------|----------|----------------------|----------|
| ANALYSIS DATE | 08/28/98 | 08/12/98 | 08/10/98 | 08/12/98 | 08/10/98 | 08/10/98 |
| | ALKALINITY | | SPECIFIC GRAVITY | | SPECIFIC CONDUCTANCE | |
| | (mg/L as CaCO ₃) | | (g/mL) | | (uMHOS/cm) | |
| | HCO ₃ | CO ₃ | | | pH | (s.u.) |
| T103997 | Lower Zone 1:1 | 340 32 | 1.012 | 37,000 | 8.8 | |
| T103998 | Lower Zone 1:2 | 300 16 | 1.009 | 28,000 | 8.8 | |
| ICV | | 1,080 1,100 | --- | 1,335 | 7.0 | |
| CCV | | 1,040 1,120 | --- | 1,327 | 7.0 | |
| RPD | | 1 1 | 0 | 2 | 0 | |
| % Extraction Accuracy | | --- | --- | 94 | --- | |
| % Instrument Accuracy | | 90 90 | --- | 94 | 100 | |
| REPORTING LIMIT | | --- | --- | --- | --- | |

| | | | | |
|---------------|----------|----------|----------|----------|
| PREP DATE | 08/14/98 | 08/11/98 | 08/10/98 | 08/12/98 |
| ANALYSIS DATE | 08/14/98 | 08/11/98 | 08/10/98 | 08/12/98 |

*NOTE: Out of holding time for N03-N.

METHODS: EPA 150.1, 300.0, 180.2, 180.1, 340.2, 120.1, 310.1; ASTM D854-92.

CHEMIST: pH/TSS: BP N03-N/FLUORIDE/CHLORIDE/SULFATE/SPECIFIC GRAVITY: JS
TDS/SPECIFIC CONDUCTANCE/ALKALINITY: RS

N03-N SPIKE: 125 mg/L N03-N.

FLUORIDE SPIKE: 10 mg/L FLUORIDE.

CHLORIDE SPIKE: 62.5 mg/L CHLORIDE.

SULFATE SPIKE: 62.5 mg/L SULFATE.

N03-N CV: 5.0 mg/L N03-N.

FLUORIDE CV: 1.0 mg/L FLUORIDE.

CHLORIDE CV: 12.5 mg/L CHLORIDE.

SULFATE CV: 12.5 mg/L SULFATE.

Director, Dr. Blair Leftwich

5-16-98

DATE

Client: Trace Analysis, Inc.
 Attn: Neil Green
 Address: 6701 Aberdeen Ave, Ste. 9
 Lubbock, TX 79424
 Phone: (806) 794-1296 FAX: (806) 794-1298

Report #/Lab ID#: 92840 Report Date: 8/31/98
 Project ID:
 Sample Name: 103911
 Sample Matrix: water
 Date Received: 8/5/98 Time: 10:00:00
 Date Sampled: Not specific Time: 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQL ⁵ | Blank | Date | Method | Prec. ² | Recov. ³ | CCV ⁴ | I.C.S. ⁴ |
|-----------|--------|-------|------------------|-------|---------|------------|--------------------|---------------------|------------------|---------------------|
| Viscosity | 0.6 | cps | | | 8/26/98 | Brookfield | | | | |


QUALITY ASSURANCE DATA¹

Room Temperature - Upper Zone
Note: Could not run heated sample due to sulfide hazard.

This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and to the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program. © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,
Richard Laster
 Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measure ments.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analyte.
6. Method numbers typically denote USEPA procedures. Less than ("<") values reflect nonnatural quantitation limits, adjusted for any required dilution.



4221 Friedrich Lane, Suite 190, Austin, TX 78744
A. 9310 Up River Road, Corpus Christi, TX 78409
(512) 444-5896 • FAX (512) 447-6766

Client: Trace Analysis, Inc.
Attn: Neil Green
Address: 6701 Aberdeen Ave, Ste. 9
Lubbock, TX 79424

Phone: (806) 794-1296 FAX: (806) 794-1298

Report #/Lab ID#: 92841 Report Date: 8/31/98
Project ID:
Sample Name: 103912
Sample Matrix: water
Date Received: 8/5/98 Time: 10:00:00
Date Sampled: Not specific Time: 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQL ⁵ | Blank | Date | Method | Prec. ² Recov. ³ CCV ⁴ | LCS ⁴ |
|-----------|--------|-------|------------------|-------|---------|------------|---|------------------|
| Viscosity | 0.7 | cps | | | 8/26/98 | Brookfield | | |


QUALITY ASSURANCE DATA¹

Room Temperature - Lower zone
Note: Could not run heated sample due to spillage hazard

This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and to the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,
Richard Laster
Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measurements.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analyte.
6. Method numbers typically denote USEPA procedures. Less than (<) values reflect nominal quantitation limits, adjusted for any required dilution.



4221 Friedrich Lane, Suite 198, Austin, TX 78744
A 9320 Up River Road, Corpus Christi, TX 78409
(512) 644-5096 • FAX (512) 447-4766

Client: Trace Analysis, Inc.
Attn: Nell Green
Address: 6701 Aberdeen Ave, Ste. 9
Lubbock, TX 79424

Phone: (806) 794-1296 FAX: (806) 794-1298

Report #/Lab ID#: 92842 Report Date: 8/31/98
Project ID:
Sample Name: 103993
Sample Matrix: water
Date Received: 8/5/98 Time: 10:00:00
Date Sampled: Not specific Time: 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQL ¹ | Blank | Date | Method | Prec. ² | Recov. ³ | CCV ⁴ | LCS ⁴ |
|-----------|--------|-------|------------------|-------|---------|------------|--------------------|---------------------|------------------|------------------|
| Viscosity | 0.6 | cps | | | 8/26/98 | Brookfield | | | | |

QUALITY ASSURANCE DATA¹

Room Temp - approx 20:1
Note: Could not run heated sample due to Sulfide hazard

This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and to the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program. © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,

Richard Laster

Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measurements.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analyte.
6. Method numbers typically denote USEPA procedures. Less than (" $<$ ") values reflect minimal quantitation limits, adjusted for any required dilution.

Client: Trace Analysis, Inc.
 Attn: Neil Green
 Address: 6701 Aberdeen Ave, Ste. 9
 Lubbock, TX 79424
 Phone: (806) 794-1296 FAX: (806) 794-1298

Report #/Lab ID#: 92843 Report Date: 8/31/98
 Project ID:
 Sample Name: 103994
 Sample Matrix: water
 Date Received: 8/5/98 Time: 10:00:00
 Date Sampled: Not specific Time: 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQL ⁵ | Blank | Date | Method | Prec. ² | Recov. ³ | CCV ⁴ | LCS ⁶ |
|-----------|--------|-------|------------------|-------|---------|------------|--------------------|---------------------|------------------|------------------|
| Viscosity | 0.6 | cps | | | 8/26/98 | Brookfield | | | | |

QUALITY ASSURANCE DATA¹

Room Temperature - Upper Zone 1:1
Note: Could not run heated sample due to Sulfide hazard

This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and to the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program. © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,
Richard Laster
 Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measurements.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analysis.
6. Method numbers typically denote USEPA procedures. Less than ("<") values reflect nominal quantitation limits, adjusted for any required dilution.



4221 Freidrich Lane, Suite 190, Austin, TX 78744
A 5320 Up River Road, Corpus Christi, TX 78409
(512) 444-5894 - FAX (512) 447-4766

Client: Trace Analysis, Inc.
Attn: Neil Green
Address: 6701 Aberteen Ave, Ste. 9
Lubbock, TX 79424
Phone: (806) 794-1296 FAX: (806) 794-1298

Report #/Lab ID#: 92844 Report Date: 8/31/98
Project ID:
Sample Name: 103995
Sample Matrix: water
Date Received: 8/5/98 Time: 10:00:00
Date Sampled: Not specific Time: 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQI.1 | Blank | Date | Method | Prec.2 | Recov.3 | CCV.4 | LCS.4 |
|-----------|--------|-------|-------|-------|---------|------------|--------|---------|-------|-------|
| Viscosity | 0.6 | cps | | | 8/26/98 | Brookfield | | | | |

QUALITY ASSURANCE DATA¹

Room Temperature - Upper Zone 1:2

Note: Could not run heated sample due to sulfide hazard


This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and to the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program. © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,

Richard Laster

Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measurements.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analyte.
6. Method numbers typically denote USEPA procedures. Less than (<) values reflect nominal quantitation limits, adjusted for any required dilution.



4221 Friedrich Lane, Suite 190, Austin, TX 78746
& 9320 Up River Road, Corpus Christi, TX 78409
(312) 444-5894 • FAX (512) 447-4766

Client: Trace Analysis, Inc.

Attn: Neil Green

Address: 6701 Aberdeen Ave, Ste. 9

Lubbock, TX 79424

Phone: (806) 794-1296 FAX: (806) 794-1298

Report #/Lab ID#: 92845 Report Date: 8/31/98

Project ID:

Sample Name: 103996

Sample Matrix: water

Date Received: 8/5/98 Time: 10:00:00

Date Sampled: Not specific Time: 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQL ¹ | Blank | Date | Method | Prec. ² | Recov. ³ | CCV ⁴ | LCS ⁴ |
|-----------|--------|-------|------------------|-------|---------|------------|--------------------|---------------------|------------------|------------------|
| Viscosity | 0.1 | cps | | | 8/26/98 | Brookfield | | | | |

QUALITY ASSURANCE DATA¹

Room Temperature - Lower Zone 2:1
Note: Could not run heated sample due to sulphide hazard

This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and in the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program. © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,

Richard Laster

Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measurements.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analyte.
6. Method numbers typically denote USEPA procedures. Less than (" $<$ ") values reflect nominal quantitation limits, adjusted for any required dilution.

Client: Tacos Analysis, Inc.
 Attn: Neil Green
 Address: 6701 Aberdeen Ave, Ste. 9
 Labdock, TX 79424
 Phone: (806) 794-1296 FAX: (806) 794-1298

Report #/Lab ID#: 92846 Report Date: 8/31/98
 Project ID:
 Sample Name: 103997
 Sample Matrix: water
 Date Received: 8/5/98 Time: 10:00:00
 Date Sampled: Not specific Time: 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQL ⁵ | Blank | Date | Method | Prec. ² | Recov. ³ | CCV ⁴ | I.C.S. ⁴ |
|-----------|--------|-------|------------------|-------|---------|------------|--------------------|---------------------|------------------|---------------------|
| Viscosity | 0.6 | cps | | | 8/26/98 | Brookfield | | | | |

QUALITY ASSURANCE DATA¹

Room Temp - Lower Zone 1:1
 Note: Could not run heated sample due to sulfide hazard

This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and to the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,

Richard Laster

Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measurements.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analyte.
6. Method numbers typically denote USEPA procedures. Less than (<) values reflect nominal quantitation limits, adjusted for any required dilution.

Client: Trace Analysis, Inc.
Attn: Neil Green
Address: 6701 Aberdeen Ave, Ste. 9
 Lubbock, TX 79424
Phone: (806) 794-1296 **FAX:** (806) 794-1298

Report #/Lab ID#: 92847 **Report Date:** 8/31/98
Project ID:
Sample Name: 103998
Sample Matrix: water
Date Received: 8/5/98 **Time:** 10:00:00
Date Sampled: Not specific **Time:** 00:00:00

REPORT OF ANALYSIS

| Parameter | Result | Units | RQI. ⁵ | Blank | Date | Method | Prec. ² | Recov. ³ | CCV ⁴ | LCS ⁶ |
|-----------|--------|-------|-------------------|-------|---------|------------|--------------------|---------------------|------------------|------------------|
| Viscosity | 0.5 | cps | | | 8/26/98 | Brookfield | | | | |

QUALITY ASSURANCE DATA¹

Room Temp - Lower Zone 1:2

Note: Could not run heated sample due to sulfide hazard

This analytical report respectfully submitted by AnalySys, Inc. The enclosed results have been reviewed and to the best of my knowledge the analytical results are consistent with AnalySys, Inc.'s Quality Assurance/Quality Control Program © Copyright 1998 AnalySys, Inc., Austin, Texas. All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means without the express written permission of AnalySys, Inc.

Respectfully Submitted,

Richard Laster

Richard Laster

1. Quality assurance data reported is for the lot analyzed which included this sample.
2. Precision (Prec.) is the absolute value of the relative percent (%) difference between duplicate measurements.
3. Recovery (Recov.) is the percent (%) of analyte recovered from a spiked sample.
4. Calibration Verification (CCV) and Lab Control Sample (LCS) results expressed as the percent (%) recovery of analyte from a known standard.
5. Reporting Quantitation Limit. The Practical Quantitation Limit (PQL) or the Method Detection Limit (MDL) reported for the analyte.
6. Method numbers typically denote USEPA procedures. Less than (<) values reflect nominal quantitation limits, adjusted for any required dilution.

APPENDIX 2.5-2

PACKER FLUID CORROSION INHIBITOR

TECHNI-HIB™ 370

UNICHEM

A Division of BJ Services Company

**PRODUCT BULLETIN****DESCRIPTION:**

TECHNI-HIB 370 is a cationic blend of water soluble, film forming corrosion inhibitors, formulated for use in water, and water/oil systems.

USES:

TECHNI-HIB 370 is recommended for the inhibition of corrosion caused by carbon dioxide, hydrogen sulfide and bacterial deposits. TECHNI-HIB 370 has been developed for use in water floods, brine disposal operations, producing oil wells with a high water-to-oil ratio and gas transmission lines. TECHNI-HIB 370 also has excellent solubility and dispersibility for use under static conditions such as packer fluids.

APPLICATION:

1. TECHNI-HIB 370 should be fed continuously with a chemical injector for all surface applications.
2. For gas transmission lines, TECHNI-HIB 370 should be injected with a spray nozzle or atomizer. The use concentration is normally 10-60 ppm. Gas transmission lines will require ½ pint to 1 quart per 1 MM cubic feet of gas.
3. Optimum treatment is determined by monitoring with corrosion coupons, electronic instruments, or iron/ manganese counts.
4. For use as a packer fluid inhibitor, TECHNI-HIB 370 should be mixed with fresh water or brine at a rate of 1/4% to 1% of the fluid volume.

TYPICAL PROPERTIES:

| | |
|--------------------------|--------------------|
| Specific Gravity @ 60°F | 0.96 |
| Pounds Per Gallon @ 60°F | 7.97 |
| Pour Point | -5°F |
| Flash Point | 98°F |
| pH | 6-7 |
| SOLUBILITIES: | |
| Fresh Water | Soluble |
| 2% Brine | Soluble |
| 15% Brine | Dispersible |
| Crude Oil | Insoluble |
| Appearance | Clear Amber Liquid |

HANDLING:

WARNING! FLAMMABLE. Keep away from heat, sparks, and open flame. Keep container closed when not in use. Do not breathe vapors, use with adequate ventilation. Avoid contact with eyes, skin, and clothing. Refer to Material Safety Data Sheet for additional information and first aid.

PACKAGING:

TECHNI-HIB 370 is sold in 55-gallon drums and bulk.

3/92

Product Name: TECHNI-HIB 370

Section: 01 PRODUCT IDENTIFICATION

| | | |
|-------------------------------|-----------------------|--------------|
| UNICHEM | Emergency Telephone | 505-393-7751 |
| A DIVISION OF BJ SERVICES CO. | Previous Version Date | 9/21/93 |
| 707 N. LEECH | Date Prepared | 10/01/96 |
| HOBBS, NM 88241-1499 | Version: 0000005 | |

Product Name: TECHNI-HIB 370

Trade Name: Corrosion Inhibitor

Chemical Description:
Proprietary blend of cationic compounds-----
Section: 02 HAZARDOUS INGREDIENTS

| <u>Component Name</u> | <u>CAS#</u> | <u>% Range</u> |
|-----------------------|-------------|----------------|
| isopropyl alcohol | 00067-63-0 | < 25% |
| methanol | 00067-56-1 | < 5% |

Section: 03 PHYSICAL DATA

Freezing Point: 2 Deg.F.
Boiling Point, 760 mm Hg: appx 190 Deg.F
Specific Gravity(H2O=1) : 0.956 Solubility in water: Complete
Appearance and Odor: Clear amber liquid; pungent odor.

Section: 04 FIRE AND EXPLOSION HAZARD DATA
-----Flash Point (Test Method): 98 Deg.F TCCExtinguishing Media

CO2, dry chemical, water spray or fog, or foam. Use water to keep containers cool. Isolate "fuel" supply from fire. Contain fire fighting liquids for proper disposal.

Special Fire Fighting Procedures

Do not enter confined fire space without proper personal protective equipment including NIOSH approved self-contained breathing apparatus with full facepiece operated in the positive pressure demand mode. Do not inject a solid stream of water or foam into hot, burning pools; this may cause splattering and increase fire intensity. Evacuate personnel to a safe area. Keep unnecessary people away.

Unusual Fire and Explosion Hazards

This material is volatile and readily gives off vapors that may travel along the ground or be moved by ventilation and ignited by pilot lights, other flames, sparks, heaters, smoking, electrical motors, static discharge, or other

Product Name: TECHN-HIB 370

Section: 04 FIRE AND EXPLOSION HAZARD DATA CONTINUED

Ignition sources at locations distant from material handling point. Never use welding or cutting torch on or near drum (even empty) because product (even just residue) can ignite explosively. Containers may explode from internal pressure if confined to fire. Keep containers cool. Keep unnecessary people away.

Section: 05 HEALTH HAZARD DATA

Effects of Overexposure

Eye Contact: the liquid is irritating to the eyes and produces intense stinging and burning. If not promptly removed, may cause eye damage.

Skin Contact: repeated or prolonged contact with the skin may cause irritation and dermatitis.

Inhalation: vapors may cause irritation of the eyes, nose, and throat. Prolonged exposures may cause nausea, headache, dizziness, unconsciousness, cardiac depression, optic complications and death.

Ingestion: can cause burning of the gastrointestinal tract, nausea, vomiting, bleeding, CNS depression, hemolysis, blindness and pulmonary damage. Can be fatal.

Chronic Exposure: For methanol, chronic poisoning from repeated exposure has been manifested by conjunctivitis, headache, giddiness, sleeplessness, gastric disturbances and failure of vision.

Emergency and First Aid Procedures

SKIN

Wash with soap and water. Remove contaminated clothing and launder contaminated clothing before reuse. Get medical attention if redness or irritation develops.

EYES

Flush eyes immediately with large amounts of water for at least 15 minutes. Lift lower and upper lids occasionally. Get medical attention.

INHALATION

Remove victim to fresh air. Give artificial respiration if not breathing. If breathing is difficult, administer oxygen. Keep person warm, quiet and get medical attention.

INGESTION

Call a physician immediately. Give victim a glass of water. Do NOT induce vomiting unless instructed by a physician or poison control center. Never give anything by mouth to an unconscious person.

Section: 06 REACTIVITY DATA

Product Name: TECHN-HIB 370

Section: 06 REACTIVITY DATACONTINUED
-----Stability -- Conditions to Avoid

None known.

Incompatibility (Materials to Avoid)

Avoid contact with strong oxidizing agents, strong alkalies, and strong mineral acids.

Hazardous Decomposition Products

Thermal decomposition or combustion may produce smoke, carbon monoxide and carbon dioxide.

Hazardous Polymerization May Occur (Y=Yes/N=No): NHazardous Polymerization -- Conditions to AvoidNone

Section: 07 SPILL OR LEAK PROCEDURES

Steps to be Taken if Material is Released or Spilled

Eliminate sources of ignition. Persons not wearing suitable personal protective equipment should be excluded from area of spill until clean-up has been completed. Shut off source of spill if possible to do so without hazard. Prevent material from entering sewers or watercourses. Provide adequate ventilation. Contain spilled materials with sand or earth. Recover undamaged and minimally contaminated material for reuse or reclamation. Place all collected material and spill absorbents into DOT approved containers.

Advise authorities. If this product is an EPA hazardous substance (see Section 10), notify the U.S.EPA and/or the National Response Center. Additional notification pursuant to SARA Section 302/304 (40 CFR 355) may also be required.

Waste Disposal MethodTreatment, storage, transportation and disposal must be in accordance with EPA or State regulations under authority of the Resource Conservation and Recovery Act (40 CFR 260-271).

Section: 08 SPECIAL PROTECTIVE INFORMATION

Respiratory Protection

If workplace exposure limit(s) of product or any component is exceeded, an NIOSH/MSHA approved air supplied respirator is advised in absence of proper environmental control. OSHA regulations also permit other NIOSH/MSHA respirators (negative pressure organic vapor type) under specified conditions. Engineering or administrative controls should be implemented to reduce exposure.

Ventilation

Product Name: **TECHNI-HIB 370**

Section: 08 SPECIAL PROTECTIVE INFORMATION CONTINUED

The use of mechanical dilution ventilation is recommended whenever this product is used in confined spaces, is heated above ambient temperatures or is agitated. When applicable, sufficient local ventilation should be provided to maintain employee exposures below safe working limits (TWA's).

Protective Gloves

Neoprene, nitrile, polyvinyl alcohol (PVA), polyvinyl chloride (PVC)

Eye Protection

Chemical splash goggles or face shield in compliance with OSHA regulations is advised; however OSHA regulations also permits safety glasses under certain conditions. The use of contact lenses is not recommended.

Other Protective Equipment

Eye wash and safety shower

Section: 09 SPECIAL PRECAUTIONS

Precautions to be Taken in Handling and Storing

Avoid contact with eyes, skin or clothing. Avoid breathing vapors or mist. Keep away from heat, sparks, and open flames and never use a cutting torch on or near container (even empty) or explosion may result. Vapors may travel to areas away from the work site and ignite.

Other Precautions

Containers of this material may be hazardous when emptied. Since emptied containers retain product residues (vapor, liquid, and/or solid), all hazard precautions given in the data sheet must be observed. Do not transfer to improperly marked container. Do not use pressure to empty container. Do not cut, heat, weld, or expose containers to flame or other sources of ignition. Keep container closed. Use with adequate ventilation. Wash thoroughly after handling. Containers should be grounded and bonded to receiving container(s) when being emptied. Containers should not be washed out and used for other purposes.

FOR INDUSTRIAL USE ONLY

Section: 10 REGULATORY INFORMATION

Superfund Amendments and Reauthorization Act of 1986(SARA) Title III

Section 302/304-Extremely Hazardous Substances (40 CFR 355)

SARA requires emergency planning based on Threshold Planning Quantities (TPQs) and release reporting based on Reportable Quantities (RQs) in 40 CFR 355 (used for SARA 302, 304, 311

Product Name: TECHN1-HUB 370

Section: 10 REGULATORY INFORMATION

CONTINUED

and 312). These values are subject to change and the regulations should be consulted to verify current statutory requirements.

Components present in this product at a level which could require reporting under the statute are:

Component NameRQ TPQ % Range

NONE

Section 311/312 Chemical Inventory Reporting Requirements (40 CFR 370)

The Superfund Amendments and Reauthorization Act (SARA) may require submission of reports (chemical list, MSDS, Tier I & Tier II) to the State Emergency Response Commission, Local Emergency Response Committee and the local fire department. The SARA physical and health hazards related to this product are:

☒ Acute Health Hazard
☒ Chronic Health Hazard

☐ Sudden Release of Pressure
☐ Reactive

☒ Fire

Section 313-List of Toxic Chemicals (40 CFR 372)

This product contains the following toxic chemicals subject to the reporting requirements of Section 313 of the Emergency Planning and Community Right-to-Know Act of 1986 (40 CFR 372). This information should be included in all MSDSs that are copied and distributed for this material.

Component NameCAS #% Range

methanol

00067-56-1 < 5+

CERCLA, 40 CFR 261 AND 302

The Comprehensive Environmental Response, Compensation, and Liability Act of 1980 (CERCLA) requires notification of the National Response Center 1-800-424-8802 of any release of a Hazardous Substances equal to or greater than the reportable quantities (RQs) listed in 40CFR 302.4. Values are given in pounds for the component and not the mixture, if applicable. (These values are subject to change and the regulations should be consulted to verify current statutory levels.)

Component NameCAS #CERCLA RQ

methanol

00067-56-1 5000

OSHA Exposure LimitsComponent Name

isopropyl alcohol

TWA ppm: 400.0 TWA MG/M3: 980.0 STEL ppm: 500.0 STEL MG/M3: 1225.0

methanol

TWA ppm: 200.0 TWA MG/M3: 260.0 STEL ppm: 250.0 STEL MG/M3: 325.0 Skin: X

National Fire Protection Agency2 Health3 Fire0 Reactive Other

Product Name: TECHNIB 370

Section: 10 REGULATORY INFORMATION

CONTINUED

Department of Transportation Shipping Information

Proper Shipping Name: Flammable liquids, n.o.s.

Hazard Class: 3

Identification: UN1993

Packaging Group: PG III

Contains: methanol, isopropyl alcohol

Hazardous Substance RQ: 100000#

Emergency Response Guide Number: 128

Labels: Flammable liquid

Toxic Substances Control Act (TSCA), 40 CFR 261

This product, or components if product is a mixture, is/are listed on the Toxic Substance Control Act (TSCA) inventory.

- -

Section 10 information is to remain attached to the material safety data sheet for this product.

- -

While UNICHEM believes that the above data is correct, UNICHEM expressly disclaims liability for any loss or injury arising out of the use of this information or the use of any materials designated.

- -

END OF MSDS

APPENDIX 2.7-1
CHRONOLOGY OF FIELD ACTIVITIES

APPENDIX 2.7-1

CHRONOLOGY OF FIELD ACTIVITIES

Monday, July 6, 1998

Brian Rogers traveled to Artesia, New Mexico. Met with the drilling contractor during move-in and rig-up. L&M's Rig No. 1 was moved in and rigged up the steel mud pits, pumps, and substructure.

Tom Ball traveled to Artesia, New Mexico. Rigged up L&M's Rig No. 1.

Tuesday, July 7, 1998

Tom Ball arrived on site. Continued to rig up. Nipped up the blowout preventer and flow line. The location had been prepared for the selected rig. A divided reserve pit, lined with a 6-mil plastic and fenced, was complete. An extension was welded onto the 9-5/8 inch surface casing with a rental 9-5/8" sow x 11" 3000 flange to the blowout preventer. A cellar was completed with a rathole and mousehole.

Brian Rogers arrived on site. Continued nipping up the blowout preventer and flow line. Went in the hole with Kelly to 40 feet. Did not tag cement. Filled the hole with water. Picked up a Smith 8-3/4 inch FDSH+ (Journal Bearing bit with gauge protection) dressed with 13-13-13-blank (Serial No. LS0625). Went in the hole. Attempted to test the hydril. Test failed. Pulled out of the hole with the bit and drill collar. Closed blind rams and attempted to test. Test failed. Ordered out a replacement hydril. Nipped down the flow line and blowout preventers.

Wednesday, July 8, 1998

Tom Ball arrived on site. Replaced the ring gasket on the flange. Received the replacement Hydril. Nipped up same. Tested casing to 1000 psi for 30 minutes. Test okay. Started at 1600 hours. Picked up the bit and 13 drill collars. Tagged top plug at 374 feet. Washed the cement from 374 feet to 445 feet.

Brian Rogers arrived on site. Went in the hole with 13 drill collars. Worked through the cement plug at 445 feet. Tallied 4-1/2 inch drillpipe and went in the hole to 1620 feet. 0115 hours, closed the pipe rams and pressured up the well system to 750 psi at the standpipe. 0115 hours, Test No. 1 at 750 psi. 0145 hours, Test No. 1 ended at 690 psi. Pressure loss was -60 psi per 30 minutes. 0150 hours, Test No. 2 started at 900 psi. 0220 hours, Test No. 2 ended at 865 psi. Pressure loss was -35 psi per 30 minutes (-3.89%).

Continued in the hole with the 4-1/2 inch drillpipe. Tagged the top of plug at 2188 feet with 10 feet out on Joint No. 72 and no kelly. Picked up kelly and drilled cement plug to 2301 feet. 0700 hours, changed shifts.

Thursday, July 9, 1998

Tom Ball arrived on site. Drilled the cement to 2465 feet. Washed to 2521 feet. Ran mud sweep. Totco survey was 1° at 2481 feet. Washed to 3543 feet. Survey at 3441 feet was 1-1/4°. Drilled 3543 feet to 3573 feet. Went in the hole to 4200 feet. Washed down the bridges to 4440 feet.

Brian Rogers arrived on site. 1900 hours to 2200 hours, drilled to 4479 feet. Survey at 4432 feet was 1-3/4°. 2200 hours to 2400 hours, went in the hole. Tagged to the top of the cement at 5092 feet. Drilled cement from 5092 feet to 5220 feet (128 feet). Washed to 5296 feet. Swept the hole clean and surveyed at 5277 feet, 4-1/4°. 0130 hours to 0300 hours, washed in the hole 5317 feet to 5785 feet. Tagged. Circulated hole for one hour while moving the drill collar and drillpipe on the rack. 0400 hours to 0430 hours, drilled cement from 5785 feet to 5840 feet (55 feet). Felt spotty. 0430 hours to 0530 hours, went in the hole with the pipe to 6265 feet. Tagged hard. Picked up to circulate with the kelly. The pipe stuck at 6240 feet. Rigged up the kelly. Circulated with full returns. Worked the pipe. Mixed gelled pill for the sweep.

Friday, July 10, 1998

Tom Ball arrived on site. Pumped sweep while working the pipe 140,000 lbs down to 40,000 pounds (pipe weight 115,000 pounds). Circulated heavy concentration of drilling detergent around the drill collars. Did not free pipe. Pipe was stuck near the bit from stretch calculations. Spotted 50 barrels of oil with 30 barrels around the drill collars. Worked the pipe and moved 2 barrels oil each hour.

Brian Rogers arrived on site. 1900 hours, pumped two barrels (20 strokes) and worked pipe, 40,000 pounds to 190,000 pounds. 1930 hours, the pipe was free. Circulated and rotated the kelly down. Continued washing in the hole. 2015 hours, tagged hard cement at 6395 feet. Drilled cement with $\pm 15,000$ pounds WOB, 52 strokes per minute, 900 psi, 8.6 ppg, 45-second viscosity, 10.5 pH. Drilled to 6475 feet. Washed from 6475 feet to 6635 feet. Tagged hard cement at 6635 feet. Drilled to 6650 feet. Washed in the hole to 6745 feet. Spotted the gelled pill and swept the hole. Attempted to survey at 6705 feet. Failed twice. Mud was too thick and would not allow the tool to be lowered into the well before setting. Continued washing in the hole to 6808 feet. Mud was extremely thick. Jet mud to reserve

pit and added fresh water to dilute. Rotated and worked the pipe while conditioning the mud. Surveyed at 6768 feet, 3-1/2°.

Saturday, July 11, 1998

Tom Ball arrived on site. Continued to wash in the hole. Circulated and conditioned the mud as the pipe was worked downhole. Washed to 7274 feet and circulated to thin the mud. 1545 hours, tagged the cement at 7613 feet. 1545 hours to 1725 hours, short tripped 16 stands. No bridges or tight spots. 1725 hours to 1830 hours, surveyed at 7571 feet, 1-3/4°. 1830 hours to 1900 hours, drilled the cement at 7613 feet.

Brian Rogers arrived on site. 1900 hours, drilled the cement at 7613 feet. 2115 hours, broke out of the cement at 7726 feet (113 feet). Continued washing in the hole. Mud weight was 8.7 pounds per gallon (ppg), viscosity was 34 seconds, pH was 12, string weight was 130,000 pounds. 0200 hours, washed in the hole to tag cement at 8293 feet. 0200 hours to 0320 hours, drilled cement at 8293 feet to 8385 feet (92 feet). Conditioned mud with SAPP and Desco, as needed. Added premix at suction while drilling. Set marker in the pit. Did not observe loss of circulation or pit gain while washing to 8635 feet. Slowly regained full returns. Circulated the hole clean. Spotted a 25-barrel (42 viscosity) gelled pill for sweep. Mud weight was 8.9 ppg, 37 viscosity. Survey at 8604 feet was 1-1/4°.

Sunday, July 12, 1998

Tom Ball arrived on site. Installed an overflow for the reserve pit. Lined over flow with 6-mil plastic. Circulated the well clean. 1930 hours to 1330 hours, washed in the hole at 8635 feet to 9160 feet. 1330 hours, attained total depth of 9160.95 feet. 1330 hours to 1700 hours, circulated and swept the hole clean. 1700 hours to 1900 hours, short tripped 20 stands. No fill, bridges, or tight spots observed. 1900 hours, changed shift.

Brian Rogers arrived on site. 1900 hours to 2100 hours, circulated well and tallied seven inch casing. 2100 hours to 2115 hours, spotted a gelled pill. 2115 hours to 2130 hours, pumped gelled pill out of the drillpipe and into the bottom of the hole. 2200 hours, started pulling drillpipe out of the hole. Strapped the pipe as it was pulled from the well. Survey at 9160 feet was 1°. 2400 hours, moved in and rigged up Schlumberger. 0300 hours, pulled out of the hole. Went in the hole with 9-5/8 inch casing cement bond log, gamma ray, and casing collar locator logging tool to log 2548 feet to 400 feet. Correlated depths to the gamma ray curve/casing setting depth on the Halliburton spectral density, dual-spaced neutron log, dated September 8, 1993.

Monday, July 13, 1998

Tom Ball arrived on site. Performed a fracture identification survey with gamma ray from 9144 feet to 4000 feet. Integrated the four-arm caliper survey from 9144 feet to 2555 feet. Calculated the cement volume from the log and added 20% excess cement. Went in the hole with drillpipe and broke circulation at 5000 feet and 7000 feet. Continued in the hole. Good returns with no lost circulation.

Brian Rogers arrived on site. Set bit at 9115 feet and circulated the hole. Monitored returns. Swept the hole with 100 barrels, 40-second viscosity gelled pill. Monitored returns. Spotted a viscous gel pill at 9105 feet. Rigged up a lay-down machine. Pulled out of the hole. Laid down drillpipe and drill collars.

Tuesday, July 14, 1998

Tom Ball arrived on site. Rigged up Bull Rogers' casing crews. Picked up a seven inch packoff float shoe, Baker weld to the Bottom Joint No. 1. Ran two joints, float collar at 9007 feet and differential valve (DV) tool at 5498 feet. All equipment was Baker welded to the pipe. Ran Joint Nos. 1-50, 29 lb/ft N-80; Joint Nos. 51-84, 29 lb/ft, P-110; Joint Nos. 85-259, 26 lb/ft, P110. Torque turned and monitored each connection. 1550 hours, positioned float shoe at 9094 feet. Circulated well and reciprocated pipe for one seven inch casing volume. 1615 hours, dropped the ball and set a packoff float shoe at 9094 feet. Moved in and rigged up Halliburton. Cemented 7 inch casing with 20 barrels of fresh water, 12 barrels of mud flush, 20 barrels of fresh water, 12 barrels of Super Flush, 20 barrels of fresh water, and 600 sacks (171 barrels) modified Class H + 0.4% CFR-3 plus five pounds per sack (lb/sx) Gilsonite + 0.5% Halad-344, + one lb/sx of salt mixed at 13.0 ppg (yield at 1.66 ft³ per sack). Displaced with 150 barrels of fresh water and 194 barrels of mud. Did not bump plug. Floats were holding. Dropped dart and opened the DV tool at 824 psi. Circulated well with good returns throughout.

Brian Rogers arrived on site. Circulated through the DV tool for eight hours. Observed 42 barrels (142 sacks) of cement circulated to the surface. 0310 hours, pumped 20 barrels of fresh water, 12 barrels of super flush, 20 barrels of fresh water, Mixed (103 barrels) 220 sacks interfill C (lead slurry) at 11.7 ppg, followed by 163 barrels (550 sacks) Modified Class H + 0.5% Halad-344 + 0.1% HR7 + 0.4% CFR-3, + 5 lb/sx Gilsonite + one lb/sx salt at 13.0 ppg. Released the closing plug and displaced with 210 barrels of fresh water. Landed the plug and closed the DV tool with 3000 psi. Checked flowback. Okay. Tool closed. Circulated 35 barrels (75 sacks) to the surface. Picked up 1 inch tremie line and lowered to 20 feet (could not work past 7 inch collar) and cemented the 9-5/8" x 7" annulus

with 20 sacks of premium cement containing 3% calcium chloride. Waited on cement. Cleaned the mud pits.

Wednesday, July 15, 1998

Brian Rogers arrived on site. Waited on cement. Mud pits were clean. 1215 hours, slacked off on casing and cut to remove the blowout preventers. 1500 hours, released the drilling rig. Installed the seven inch Larkin Type R tubinghead. Returned the surplus mud inventory and inspected 13 drill collars. Rigged down the drilling rig.

Thursday, July 16, 1998

Brian Rogers arrived on site. Rigged down, moved out the drilling rig. Installed anchors and stabilized the seven inch casing with cement and filled in the rathole and mousehole. Delivered two 6-1/8 inch bits an coordinated completion operations.

Monday, July 20, 1998

Brian Rogers arrived on site. Moved in and rigged up Real Well Service's completion rig; Star Tool Company's pump, tank, pipe racks, catwalk, power swivel, and tools; and Knight Oil Tools' 2-7/8 inch, 6.50 lb/ft, N-80 work string. Purchased wellhead valves and fittings. Picked up the 6-1/8 inch bit, sub, six drill collars, and x-over (BHA at 183.80 feet) on the 2-7/8 inch work string. Went in the hole to tag soft bottom at 5455 feet. Picked up and pressure tested the well system above the DV tool at 5498 feet as shown below in Test Nos. 1 and 2:

Pressure Test No. 1 above DV tool at 5498 feet. Bottom of work string at 5450 feet:

| Time (hours) | Pressure (psig) | Δ P (psi) |
|-----------------|--------------------|------------------------|
| 1441 | 1580 | -- |
| 1446 | 1574 | -6 |
| 1451 | 1571 | -3 |
| 1456 | 1568 | -3 |
| 1501 | 1565 | -3 |
| 1506 | 1563 | -2 |
| 1511 | 1561 | -2 |
| TOTAL | | -19 psi/ 30 minutes |

Pressure Test No. 2 above DV tool at 5498 feet. Bottom of work string at 5450 feet:

| Time (hours) | Pressure (psig) | ΔP (psi) |
|-----------------|--------------------|-----------------------|
| 1516 | 1559 | -- |
| 1521 | 1558 | -1 |
| 1526 | 1556 | -2 |
| 1531 | 1555 | -1 |
| 1536 | 1555 | 0 |
| 1541 | 1554 | -1 |
| 1546 | 1553 | -1 |
| TOTAL | | -6 psi/ 30 minutes |

Washed in the hole to tag the top of the DV at 5498 feet. Drilled out the DV tool part way, circulated the tubing clean, and installed the TIW valve. 1900 hours, shut down for the night.

Note: Monitored the well system pressures using an Adalet digital pressure gauge (Catalog No. XIHFGCXZ-54967) with an Iniex Certificate Rating No. EX88B103703U. Pressure range was 0 to 2000 psig.

Tuesday, July 21, 1998

Brian Rogers arrived on site. 0700 hours, finished drilling out the DV tool. Went into the hole to tag soft bottom at 8896 feet. Drilled and washed in the hole to 9004 feet. Circulated the well clean. Picked up and pressure tested the well system above the top of the float collar, as shown below in Test Nos. 3 and 4.

Pressure Test No. 3 above the float collar at 9007 feet. Bottom of the work string at 8972 feet.

| Time (hours) | Pressure (psig) | ΔP (psi) |
|-----------------|--------------------|------------------------|
| 1405 | 1600 | -- |
| 1410 | 1592 | -8 |
| 1415 | 1588 | -4 |
| 1420 | 1584 | -4 |
| 1425 | 1580 | -4 |
| 1430 | 1577 | -3 |
| 1435 | 1575 | -2 |
| TOTAL | | -25 psi/ 30 minutes |

Pressure Test No. 4 above the float collar at 9007 feet. Bottom of the work string at 8972 feet:

| Time (hours) | Pressure (psig) | ΔP (psi) |
|-----------------|--------------------|-----------------------|
| 1440 | 1573 | -- |
| 1445 | 1571 | -2 |
| 1450 | 1569 | -2 |
| 1455 | 1568 | -1 |
| 1500 | 1567 | -1 |
| 1505 | 1566 | -1 |
| 1510 | 1565 | -1 |
| TOTAL | | -8 psi/ 30 minutes |

Monitored the well system pressures using an Adalet digital pressure gauge (Catalog No. XIHFGCXZ-54967) with an Inix Certificate Rating No. EX88B103703U. Pressure range was 0 to 2000 psig.

Pulled out of the hole. Laid down the drill collars. Cleaned out the rig tank and filled it with clean fresh water.

Wednesday, July 22, 1998

Brian Rogers arrived on site. 0700 hours, went in the hole with a bit and scraper to 8823 feet. Reverse circulated bottoms up. Pickled the wellbore with six barrels 15% HCl (inhibited) pumped down the tubing and up the casing. Displaced the well with an 8.7 ppg brine water. Laid down 11 joints and tripped out of the hole. Secured the well for the night. Loaded the storage tank with 500 barrels of 8.7 ppg brine.

Thursday, July 23, 1998

Brian Rogers arrived on site. 0600 hours, moved in and rigged up Wedge Wireline. Performed a differential temperature survey from the surface to total depth. Performed a cement bond log from 8997 feet to 135 feet. Cement bond log performed with 1000 psi applied to the well system. Conducted a casing inspection survey from 8997 feet to the surface.

Friday, July 24, 1998

Brian Rogers arrived on site. Moved in and rigged up Wedge Wireline with eight 4 inch retrievable cased-hole perforating guns. Perforated selected intervals at two jet shots per foot as follows:

| Run No. | Feet |
|---------|--------------|
| 1 | 8470 to 8476 |
| | 8460 to 8464 |
| 2 | 8430 to 8446 |
| 3 | 8419 to 8423 |
| | 8400 to 8410 |

| Run No. | Feet |
|---------|--------------|
| 4 | 8360 to 8366 |
| | 8370 to 8378 |
| 5 | 8280 to 8302 |
| 6 | 8260 to 8270 |
| 7 & 8 | 8220 to 8254 |

All shots were fired. Fluid level dropped from the surface to ± 1380 feet. Bottom-hole pressure at 8220 feet was measured at 3176 psia. A static gradient survey was performed as the tool was pulled out of the well. Static stays were conducted at 6000 feet, 3000 feet, 1500 feet, and at the surface. The well was secured for the night.

Saturday, July 25, 1998

Brian Rogers arrived on site. 0700 hours, strapped in the hole with nine joints 2-7/8" work string (287.56 feet), Arrow X-1 packer (6.25 feet), seating nipple (one foot), and 133 joints 2-7/8 inch work string (8178.32 feet) to set the end of the tubing below the bottom perforation (8476 feet) at 8479 feet. Packer element was at 8189 feet. Rigged up swab line and went into the hole to tag the fluid level at 1700 feet. Swab tested the perforated interval and recovered two tubing volumes of fluid. Strong hydrogen sulfide smell was observed while swabbing. Retained samples of the formation water for analysis. A total of 139 barrels of fluid was recovered. Secured the well for the night.

Sunday, July 26, 1998

Brian Rogers arrived on site. 0700 hours, set end of tubing at 8158 feet (top perforation was 8220 feet). Moved in and rigged up Dowell Schlumberger and performed step rate test using 8.7 ppg brine water. Results of Step Rate Test No. 1 (before acid) are as follows:

| Rate (bpm) | Volume Pumped (barrels) | Pressure (psig) | Friction Pressure (psig) | Pump-in Pressure (psig) |
|---------------|-------------------------------|--------------------|--------------------------------|-------------------------------|
| 2 | 50 | 560 | 285 | + 275 |
| 4 | 35 | 2020 | 734 | + 1286 |
| 4.85 | 35 | 2673 | 1020 | + 1653 |
| 5 | 3 | + 2850 | 1020 | + 1830 |

Maximum allowable pump-in = 8220 ft x 0.2 psi/ft = 1644 psig.

Acidized perforations 8220 feet to 8476 feet in four stages as follows:

Spotted acid (9.5 barrels) across perforations and pulled out of the hole to set end of the tubing at 8158 feet. Stage 1: 27 barrels of 15% HCl + 20 barrels of gelled salt for block at 800 pounds; Stage 2: 27 barrels of 15% HCl + 26 barrels of 8.7 brine pad + 21 barrels of gelled salt for block at 800 pounds; Stage 3: 27 barrels of 15% HCl + 26 barrels of 8.7 brine pad + 20 barrels of gelled salt for block at 800 pounds; Stage 4: 27 barrels of 15% HCl + 65 barrels of 8.7 brine for displacement at 10 bpm and 2450 psi. Allowed acid to soak for two hours and performed Step Rate Test No. 2. Results of Step Rate Test No. 2 are:

| Rate (bpm) | Volume Pumped (Barrels) | Pressure (psig) | Friction Pressure (psig) | Pump-in Pressure (psig) |
|---------------|-------------------------------|--------------------|--------------------------------|-------------------------------|
| 4 | 20 | 86 | 734 | -648 |
| 7 | 130 | 1085 | 1632 | -547 |
| 10 | 35 | 2674 | 2774 | -100 |
| 12 | 50 | 3948 | 3875 | + 73 |

Well went on a vacuum following both tests.

Laid down nine joints and pulled out of the hole with the tubing and the packer.

Monday, July 27, 1998

Brian Rogers arrived on site. Moved in and rigged up Wedge Wireline with eight 4 inch retrievable cased-hole perforating guns. Perforated selected intervals at two jet shots per foot as follows: 8170 feet to 8188 feet, 8160 feet to 8164 feet, 8118 feet to 8127 feet, 8132 feet to 8140 feet, 8066 feet to 8080 feet, 8050 feet to 8056 feet, 7974 feet to 8030 feet, and 7924 feet to 7942 feet. Started loading the tanks with an 8.7 ppg brine water. Secured the well and shut down for the night.

Tuesday, July 28, 1998

Brian Rogers arrived on site. Went into the hole with an Arrow retrievable bridge plug and packer on the work string. Tool hung up at 4830 feet. Pulled out of the hole. Lower slip cage on the plug was broken. Called for a replacement. Went into the hole with a 6-1/8 inch bit on the work string. Did not encounter any obstructions. Pulled out of the hole. Went into the hole with a replacement retrievable bridge plug and packer on 88 stands. Had mechanical failure on rig. Shut down. Secured the well for the night.

Wednesday, July 29, 1998

Brian Rogers arrived on site. Went into the hole with an Arrow retrievable bridge plug and packer. Set the retrievable bridge plug at 8214 feet. Set the packer at 8193 feet. Pressure tested between the packers at 500 psi. Tested okay. Pulled up the hole. Set the packer at 7852 feet. Swab tested the perforated interval and recovered 112 barrels (more than two tubing volumes). Moved in and rigged up Dowell Schlumberger to perform Step Rate Test No. 1 using an 8.7 ppg brine water. Acidized perforations 7924 feet to 8188 feet in four stages as follows: (1) 30 barrels 15% HCl + 10 barrels of gelled salt at 500 pounds; (2) 30

barrels 15% HCl + 20 barrels 8.7 brine pad + 16 barrels of gelled salt for block at 800 pounds; (3) 30 barrels 15% HCl + 20 barrels 8.7 brine pad + 21 barrels of gelled salt for block at 1000 pounds; and (4) 30 barrels 15% HCl + 60 barrels 8.7 brine for displacement at 6.5 bpm and 1050 psi.

Allowed acid to soak for one hour and performed Step Rate Test No. 2. Lowered the retrieving head onto the retrievable bridge plug. Unset the retrievable bridge plug and pulled out of the hole with the tools. Laid down the retrievable bridge plug and the packer. Secured the well for the night.

All storage tanks were loaded with an 8.7 ppg brine, totaling 7840 barrels.

Results of Step Rate Test No. 1 (before acid):

| Rate (bpm) | Volume Pumped (barrels) | Pressure (psig) | Friction Pressure (psig) | Pump-in Pressure (psig) |
|---------------|-------------------------------|--------------------|--------------------------------|-------------------------------|
| 2 | 47 | 400 | 275 | 125 |
| 4 | 15 | 1780 | 706 | 1074 |
| 4.36 | 2 | 2416 | 706 | 1710 |

Maximum allowable pump-in = $7924 \text{ ft} \times 0.2 \text{ psi/ft} = 1585 \text{ psig}$.

Step Rate Test No. 2 (after 5000 gallons 15% HCl acid):

| Rate (bpm) | Volume Pumped (Barrels) | Pressure (psig) | Friction Pressure (psig) | Pump-in Pressure (psig) |
|---------------|-------------------------------|--------------------|--------------------------------|-------------------------------|
| 4 | 25 | 7 | 706 | -700 |
| 7 | 25 | 1070 | 1570 | -500 |

Well went on a vacuum following both tests.

Thursday, July 30, 1998

Brian Rogers arrived on site. 0600 hours, moved in and rigged up Wedge Dia-Log with a digital quartz surface readout gauge, Eccosse Tex, Serial No. 009, 0 psia to 5000 psia and a Z.I. Probe memory recorder, Serial No. P59, 0 psia to 5000 psia with a casing collar

locator for depth control. 0700 hours, went into the hole and correlated logging depths to the July 23, 1998, cement bond log. Set the surface readout gauge at 7924 feet (top perforation). 0830 hours, bottom-hole pressure was 2928.16 psia at 125.41°F. Moved in and rigged up Halliburton's pump truck and booster pump. 0920 hours, started pumping 8.7 ppg brine at 10 bpm. Well on vacuum at surface. 2153 hours, final bottom-hole pressure injection pressure at 7924 feet was 3071.85 psia at 90.80°F. Shut down injection. Pumped a total of 7490 barrels of 8.7 ppg brine while monitoring the bottom-hole pressure. Monitored the pressure falloff.

Friday, July 31, 1998

Brian Rogers arrived on site. 0700 hours, discontinued the pressure falloff test. Pulled out of the hole making static gradient stops at 6000 feet, 3000 feet, 1700 feet and at the surface. Rigged up a differential temperature tool and casing collar locator and conducted a survey from the surface to wireline total depth at 8997 feet. Pulled out of the hole and laid down the temperature tool. Picked up a dual detector gamma ray tool configured with an upper detector, ejector, casing collar locator, and lower detector. Went into the hole. Performed a pre-survey baseline 7800 feet to wireline total depth at 8997 feet. Conducted a five-minute statistical survey at 7904 feet. Performed two injection profile surveys at 1 bpm. Conducted two stationary surveys at 7904 feet, pumping at 10 bpm. No upward migration was observed behind the casing. Performed a post-survey baseline. Rigged down and moved out wireline and pump equipment. Note: Released all 16 frac tanks at 0900 hours.

Saturday, August 1, 1998

Brian Rogers arrived on site. Laid down the 2-7/8 inch work string and returned to Knight Oil Tools. Delivered 197 joints, new 4-1/2 inch, 11.60 lb/ft, N-80, SMLS, R3, LT&C injection tubing.

Sunday, August 2, 1998

Brian Rogers arrived on site. Picked up an Arrow Model X-1 (7" x 3.5") retrievable packer (minimum ID = 3.0 inches) with a wireline reentry guide on bottom and a X/O 3.5 EUE 8rd pin x 4-1/2" LTC box on top. Total length was 9.01 feet. Made up and went in the hole with 193 joints, 4-1/2 inch, 11.60 lb/ft, N-80, SMLS, R3, LT&C injection tubing. Set the packer at 7879 feet and loaded the annulus with 8.7 ppg corrosion inhibited brine water. Slacked off 15,000-pound compression on the packer. Pressure tested the annulus at 600 psi. Lost 90 psi/30 minutes. Repressurized the annulus and lost 20 psi/30 minutes. Released the pump truck and left the annulus open during stabilization. Shut down for the night.

Monday, August 3, 1998

Brian Rogers arrived on site. Pressurized the annulus to 700 psi and monitored overnight. Notified the New Mexico Oil Conservation Division (OCD) of the test to begin at 0700 hours on Tuesday, August 4, 1998. Returned the rental tools and moved out the tanks.

Tuesday, August 4, 1998

Brian Rogers arrived on site. Continued monitoring the annulus pressure. 0700 hours, annulus pressure was 702 psig. 0900 hours, the OCD representatives witnessed the annulus pressure test. Mr. E. L. Gonzales and Gerry Williams represented the OCD. 0900 hours, started the annulus pressure test at 704 psig. 0930 hours, ended the annulus pressure test at 705 psig. Pressure change was +1 psi/30-minute period (0.14%), which is within the regulatory guidelines.

Rigged down and released the completion unit and all ancillary equipment.

APPENDIX 4.1-1

**BOTTOM-HOLE PRESSURE FIELD DATA RECORDED
DURING THE INJECTIVITY/FALLOFF TEST FOR WDW-1**

APPENDIX 4.1-1 **Navajo Refining Company** **Pressure Falloff Data**

Well Name : WDW-1
Started on : 07/30/1998
Ended on : 07/31/1998

| Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) |
|--------|-----------------|------------------|--------|-----------------|------------------|--------|-----------------|------------------|
| 0.0000 | 2927.912 | 123.434 | 0.6672 | 2928.221 | 125.592 | 0.6842 | 2928.235 | 125.607 |
| 0.0003 | 2927.912 | 123.439 | 0.6675 | 2928.214 | 125.587 | 0.6844 | 2928.196 | 125.584 |
| 0.0006 | 2927.904 | 123.444 | 0.6678 | 2928.214 | 125.587 | 0.6847 | 2928.211 | 125.589 |
| 0.0008 | 2927.904 | 123.444 | 0.6681 | 2928.211 | 125.584 | 0.6850 | 2928.207 | 125.592 |
| 0.0011 | 2927.903 | 123.459 | 0.6683 | 2928.211 | 125.589 | 0.6853 | 2928.231 | 125.604 |
| 0.0014 | 2927.899 | 123.457 | 0.6686 | 2928.214 | 125.587 | 0.6856 | 2928.207 | 125.592 |
| 0.0017 | 2927.899 | 123.467 | 0.6689 | 2928.238 | 125.604 | 0.6858 | 2928.218 | 125.594 |
| 0.0019 | 2927.877 | 123.462 | 0.6692 | 2928.183 | 125.569 | 0.6861 | 2928.203 | 125.589 |
| 0.0022 | 2927.894 | 123.474 | 0.6694 | 2928.231 | 125.599 | 0.6864 | 2928.218 | 125.594 |
| 0.0025 | 2927.886 | 123.485 | 0.6697 | 2928.208 | 125.582 | 0.6867 | 2928.210 | 125.594 |
| 0.0028 | 2927.889 | 123.487 | 0.6700 | 2928.221 | 125.597 | 0.6869 | 2928.231 | 125.604 |
| 0.0031 | 2927.892 | 123.500 | 0.6703 | 2928.208 | 125.582 | 0.6872 | 2928.200 | 125.587 |
| 0.0033 | 2927.881 | 123.497 | 0.6706 | 2928.225 | 125.594 | 0.6875 | 2928.214 | 125.592 |
| 0.0200 | 2927.845 | 123.822 | 0.6708 | 2928.214 | 125.592 | 0.6878 | 2928.224 | 125.599 |
| 0.0367 | 2927.879 | 124.129 | 0.6711 | 2928.214 | 125.587 | 0.6881 | 2928.210 | 125.594 |
| 0.0533 | 2927.914 | 124.377 | 0.6714 | 2928.214 | 125.587 | 0.6883 | 2928.207 | 125.592 |
| 0.0700 | 2927.958 | 124.595 | 0.6717 | 2928.207 | 125.587 | 0.6886 | 2928.211 | 125.589 |
| 0.0867 | 2928.012 | 124.782 | 0.6719 | 2928.225 | 125.594 | 0.6889 | 2928.224 | 125.604 |
| 0.1033 | 2928.041 | 124.924 | 0.6722 | 2928.207 | 125.587 | 0.6892 | 2928.214 | 125.592 |
| 0.1200 | 2928.073 | 125.036 | 0.6725 | 2928.236 | 125.597 | 0.6894 | 2928.218 | 125.594 |
| 0.1367 | 2928.096 | 125.124 | 0.6728 | 2928.194 | 125.577 | 0.6897 | 2928.199 | 125.592 |
| 0.1533 | 2928.120 | 125.208 | 0.6731 | 2928.235 | 125.602 | 0.6900 | 2928.214 | 125.592 |
| 0.1700 | 2928.117 | 125.256 | 0.6733 | 2928.211 | 125.584 | 0.6903 | 2928.220 | 125.602 |
| 0.1867 | 2928.131 | 125.299 | 0.6736 | 2928.221 | 125.592 | 0.6906 | 2928.218 | 125.594 |
| 0.2033 | 2928.158 | 125.352 | 0.6739 | 2928.204 | 125.584 | 0.6908 | 2928.207 | 125.592 |
| 0.2200 | 2928.158 | 125.379 | 0.6742 | 2928.232 | 125.594 | 0.6911 | 2928.210 | 125.594 |
| 0.2367 | 2928.162 | 125.410 | 0.6744 | 2928.214 | 125.592 | 0.6914 | 2928.224 | 125.599 |
| 0.2533 | 2928.178 | 125.438 | 0.6747 | 2928.221 | 125.592 | 0.6917 | 2928.213 | 125.597 |
| 0.2700 | 2928.169 | 125.448 | 0.6750 | 2928.218 | 125.589 | 0.6919 | 2928.203 | 125.589 |
| 0.2867 | 2928.184 | 125.470 | 0.6753 | 2928.214 | 125.587 | 0.6922 | 2928.218 | 125.594 |
| 0.3033 | 2928.195 | 125.483 | 0.6756 | 2928.221 | 125.592 | 0.6925 | 2928.213 | 125.597 |
| 0.3200 | 2928.211 | 125.501 | 0.6758 | 2928.207 | 125.587 | 0.6928 | 2928.220 | 125.602 |
| 0.3367 | 2928.202 | 125.506 | 0.6761 | 2928.228 | 125.597 | 0.6931 | 2928.221 | 125.597 |
| 0.3533 | 2928.191 | 125.508 | 0.6764 | 2928.214 | 125.592 | 0.6933 | 2928.203 | 125.589 |
| 0.3700 | 2928.208 | 125.521 | 0.6767 | 2928.207 | 125.587 | 0.6936 | 2928.213 | 125.597 |
| 0.3867 | 2928.207 | 125.526 | 0.6769 | 2928.228 | 125.597 | 0.6939 | 2928.224 | 125.599 |
| 0.4033 | 2928.193 | 125.521 | 0.6772 | 2928.204 | 125.584 | 0.6942 | 2928.217 | 125.599 |
| 0.4200 | 2928.203 | 125.534 | 0.6775 | 2928.221 | 125.597 | 0.6944 | 2928.207 | 125.592 |
| 0.4367 | 2928.205 | 125.541 | 0.6778 | 2928.207 | 125.587 | 0.6947 | 2928.218 | 125.594 |
| 0.4533 | 2928.190 | 125.546 | 0.6781 | 2928.228 | 125.597 | 0.6950 | 2928.217 | 125.599 |
| 0.4700 | 2928.199 | 125.559 | 0.6783 | 2928.214 | 125.592 | 0.6953 | 2928.210 | 125.594 |
| 0.4867 | 2928.220 | 125.574 | 0.6786 | 2928.211 | 125.589 | 0.6956 | 2928.227 | 125.607 |
| 0.5033 | 2928.196 | 125.556 | 0.6789 | 2928.214 | 125.592 | 0.6958 | 2928.218 | 125.594 |
| 0.5200 | 2928.189 | 125.556 | 0.6792 | 2928.218 | 125.594 | 0.6961 | 2928.203 | 125.589 |
| 0.5367 | 2928.209 | 125.572 | 0.6794 | 2928.214 | 125.592 | 0.6964 | 2928.224 | 125.604 |
| 0.5481 | 2928.219 | 125.584 | 0.6797 | 2928.218 | 125.589 | 0.6967 | 2928.213 | 125.597 |
| 0.5647 | 2928.232 | 125.594 | 0.6800 | 2928.210 | 125.594 | 0.6969 | 2928.224 | 125.599 |
| 0.5814 | 2928.215 | 125.582 | 0.6803 | 2928.214 | 125.587 | 0.6972 | 2928.200 | 125.587 |
| 0.5981 | 2928.202 | 125.572 | 0.6806 | 2928.224 | 125.599 | 0.6975 | 2928.220 | 125.602 |
| 0.6147 | 2928.205 | 125.574 | 0.6808 | 2928.214 | 125.592 | 0.6978 | 2928.217 | 125.599 |
| 0.6314 | 2928.212 | 125.579 | 0.6811 | 2928.214 | 125.592 | 0.6981 | 2928.210 | 125.594 |
| 0.6481 | 2928.219 | 125.584 | 0.6814 | 2928.214 | 125.592 | 0.6983 | 2928.220 | 125.602 |
| 0.6647 | 2928.218 | 125.594 | 0.6817 | 2928.221 | 125.597 | 0.6986 | 2928.207 | 125.592 |
| 0.6650 | 2928.214 | 125.587 | 0.6819 | 2928.203 | 125.589 | 0.6989 | 2928.224 | 125.604 |
| 0.6653 | 2928.214 | 125.587 | 0.6822 | 2928.218 | 125.594 | 0.6992 | 2928.210 | 125.594 |
| 0.6656 | 2928.208 | 125.577 | 0.6825 | 2928.221 | 125.597 | 0.6994 | 2928.224 | 125.599 |
| 0.6658 | 2928.218 | 125.594 | 0.6828 | 2928.200 | 125.587 | 0.6997 | 2928.196 | 125.589 |
| 0.6661 | 2928.221 | 125.592 | 0.6831 | 2928.228 | 125.602 | 0.7000 | 2928.234 | 125.612 |
| 0.6664 | 2928.218 | 125.589 | 0.6833 | 2928.204 | 125.584 | 0.7003 | 2928.213 | 125.597 |
| 0.6667 | 2928.201 | 125.577 | 0.6836 | 2928.217 | 125.599 | 0.7006 | 2928.213 | 125.597 |
| 0.6669 | 2928.218 | 125.594 | 0.6839 | 2928.211 | 125.589 | 0.7008 | 2928.210 | 125.594 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|-----------------|------------------|
| 0.7011 | 2928.217 | 125.599 |
| 0.7014 | 2928.220 | 125.602 |
| 0.7017 | 2928.220 | 125.602 |
| 0.7019 | 2928.210 | 125.594 |
| 0.7022 | 2928.207 | 125.592 |
| 0.7025 | 2928.230 | 125.610 |
| 0.7028 | 2928.209 | 125.599 |
| 0.7031 | 2928.220 | 125.602 |
| 0.7033 | 2928.210 | 125.594 |
| 0.7036 | 2928.217 | 125.599 |
| 0.7039 | 2928.213 | 125.602 |
| 0.7042 | 2928.217 | 125.599 |
| 0.7044 | 2928.217 | 125.599 |
| 0.7047 | 2928.213 | 125.597 |
| 0.7050 | 2928.220 | 125.602 |
| 0.7053 | 2928.224 | 125.604 |
| 0.7056 | 2928.217 | 125.599 |
| 0.7058 | 2928.202 | 125.594 |
| 0.7061 | 2928.224 | 125.604 |
| 0.7064 | 2928.220 | 125.602 |
| 0.7067 | 2928.220 | 125.602 |
| 0.7069 | 2928.202 | 125.594 |
| 0.7072 | 2928.213 | 125.597 |
| 0.7075 | 2928.224 | 125.604 |
| 0.7078 | 2928.217 | 125.599 |
| 0.7081 | 2928.209 | 125.599 |
| 0.7083 | 2928.217 | 125.599 |
| 0.7086 | 2928.209 | 125.599 |
| 0.7089 | 2928.228 | 125.602 |
| 0.7092 | 2928.213 | 125.602 |
| 0.7094 | 2928.209 | 125.599 |
| 0.7097 | 2928.224 | 125.604 |
| 0.7100 | 2928.217 | 125.599 |
| 0.7103 | 2928.217 | 125.599 |
| 0.7106 | 2928.209 | 125.599 |
| 0.7108 | 2928.220 | 125.602 |
| 0.7111 | 2928.213 | 125.597 |
| 0.7114 | 2928.227 | 125.607 |
| 0.7117 | 2928.210 | 125.594 |
| 0.7119 | 2928.235 | 125.607 |
| 0.7122 | 2928.218 | 125.594 |
| 0.7125 | 2928.238 | 125.610 |
| 0.7128 | 2928.228 | 125.597 |
| 0.7131 | 2928.235 | 125.602 |
| 0.7133 | 2928.231 | 125.599 |
| 0.7136 | 2928.260 | 125.610 |
| 0.7139 | 2928.236 | 125.597 |
| 0.7142 | 2928.250 | 125.597 |
| 0.7144 | 2928.261 | 125.604 |
| 0.7147 | 2928.262 | 125.599 |
| 0.7150 | 2928.279 | 125.607 |
| 0.7153 | 2928.280 | 125.602 |
| 0.7156 | 2928.298 | 125.604 |
| 0.7158 | 2928.292 | 125.594 |
| 0.7161 | 2928.313 | 125.610 |
| 0.7164 | 2928.332 | 125.607 |
| 0.7167 | 2928.275 | 125.554 |
| 0.7169 | 2928.406 | 125.640 |
| 0.7172 | 2928.380 | 125.610 |
| 0.7175 | 2928.381 | 125.599 |
| 0.7178 | 2928.410 | 125.604 |
| 0.7181 | 2928.412 | 125.594 |
| 0.7183 | 2928.469 | 125.615 |
| 0.7186 | 2928.464 | 125.594 |
| 0.7189 | 2928.514 | 125.615 |
| 0.7192 | 2928.527 | 125.597 |
| 0.7194 | 2928.560 | 125.604 |
| 0.7197 | 2928.594 | 125.602 |
| 0.7200 | 2928.634 | 125.610 |
| 0.7203 | 2928.657 | 125.599 |
| 0.7206 | 2928.716 | 125.610 |
| 0.7208 | 2928.736 | 125.597 |
| 0.7211 | 2928.783 | 125.610 |
| 0.7214 | 2928.822 | 125.599 |
| 0.7217 | 2928.884 | 125.607 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|-----------------|------------------|
| 0.7219 | 2928.915 | 125.602 |
| 0.7222 | 2928.981 | 125.607 |
| 0.7225 | 2929.026 | 125.607 |
| 0.7228 | 2929.083 | 125.599 |
| 0.7231 | 2929.138 | 125.607 |
| 0.7233 | 2929.192 | 125.597 |
| 0.7236 | 2929.276 | 125.615 |
| 0.7239 | 2929.315 | 125.599 |
| 0.7242 | 2929.375 | 125.599 |
| 0.7244 | 2929.449 | 125.599 |
| 0.7247 | 2929.526 | 125.612 |
| 0.7250 | 2929.580 | 125.602 |
| 0.7253 | 2929.672 | 125.615 |
| 0.7256 | 2929.719 | 125.594 |
| 0.7258 | 2929.803 | 125.607 |
| 0.7261 | 2929.867 | 125.604 |
| 0.7264 | 2929.938 | 125.602 |
| 0.7267 | 2930.021 | 125.597 |
| 0.7269 | 2930.105 | 125.610 |
| 0.7272 | 2930.187 | 125.610 |
| 0.7275 | 2930.252 | 125.602 |
| 0.7278 | 2930.335 | 125.597 |
| 0.7281 | 2930.427 | 125.604 |
| 0.7283 | 2930.517 | 125.604 |
| 0.7286 | 2930.602 | 125.612 |
| 0.7289 | 2930.693 | 125.597 |
| 0.7292 | 2930.771 | 125.599 |
| 0.7294 | 2930.876 | 125.599 |
| 0.7297 | 2930.986 | 125.615 |
| 0.7300 | 2931.084 | 125.604 |
| 0.7303 | 2931.164 | 125.592 |
| 0.7306 | 2931.282 | 125.602 |
| 0.7308 | 2931.387 | 125.602 |
| 0.7311 | 2931.502 | 125.610 |
| 0.7314 | 2931.596 | 125.607 |
| 0.7317 | 2931.684 | 125.589 |
| 0.7319 | 2931.802 | 125.599 |
| 0.7322 | 2931.902 | 125.602 |
| 0.7325 | 2931.999 | 125.607 |
| 0.7328 | 2932.064 | 125.589 |
| 0.7331 | 2932.160 | 125.604 |
| 0.7333 | 2932.232 | 125.597 |
| 0.7336 | 2932.313 | 125.607 |
| 0.7339 | 2932.345 | 125.587 |
| 0.7342 | 2932.398 | 125.582 |
| 0.7344 | 2932.513 | 125.617 |
| 0.7347 | 2932.568 | 125.602 |
| 0.7350 | 2932.628 | 125.592 |
| 0.7353 | 2932.710 | 125.597 |
| 0.7356 | 2932.789 | 125.594 |
| 0.7358 | 2932.859 | 125.597 |
| 0.7361 | 2932.930 | 125.594 |
| 0.7364 | 2933.021 | 125.594 |
| 0.7367 | 2933.082 | 125.584 |
| 0.7369 | 2933.191 | 125.599 |
| 0.7372 | 2933.271 | 125.592 |
| 0.7375 | 2933.372 | 125.594 |
| 0.7378 | 2933.469 | 125.584 |
| 0.7381 | 2933.596 | 125.589 |
| 0.7383 | 2933.711 | 125.592 |
| 0.7386 | 2933.853 | 125.592 |
| 0.7389 | 2933.992 | 125.584 |
| 0.7392 | 2934.154 | 125.582 |
| 0.7394 | 2934.347 | 125.587 |
| 0.7397 | 2934.537 | 125.589 |
| 0.7400 | 2934.721 | 125.582 |
| 0.7403 | 2934.927 | 125.579 |
| 0.7406 | 2935.135 | 125.584 |
| 0.7408 | 2935.341 | 125.582 |
| 0.7411 | 2935.516 | 125.584 |
| 0.7414 | 2935.723 | 125.572 |
| 0.7417 | 2935.905 | 125.579 |
| 0.7419 | 2936.066 | 125.577 |
| 0.7422 | 2936.261 | 125.577 |
| 0.7425 | 2936.384 | 125.574 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|-----------------|------------------|
| 0.7428 | 2936.534 | 125.574 |
| 0.7431 | 2936.687 | 125.572 |
| 0.7433 | 2936.808 | 125.584 |
| 0.7436 | 2936.935 | 125.562 |
| 0.7439 | 2937.105 | 125.572 |
| 0.7442 | 2937.249 | 125.562 |
| 0.7444 | 2937.452 | 125.574 |
| 0.7447 | 2937.648 | 125.564 |
| 0.7450 | 2937.816 | 125.562 |
| 0.7453 | 2938.067 | 125.559 |
| 0.7456 | 2938.285 | 125.572 |
| 0.7458 | 2938.499 | 125.564 |
| 0.7461 | 2938.740 | 125.549 |
| 0.7464 | 2938.964 | 125.554 |
| 0.7467 | 2939.239 | 125.559 |
| 0.7469 | 2939.503 | 125.567 |
| 0.7472 | 2939.693 | 125.541 |
| 0.7475 | 2940.009 | 125.554 |
| 0.7478 | 2940.275 | 125.546 |
| 0.7481 | 2940.555 | 125.554 |
| 0.7483 | 2940.929 | 125.549 |
| 0.7486 | 2941.198 | 125.539 |
| 0.7489 | 2941.552 | 125.546 |
| 0.7492 | 2941.918 | 125.546 |
| 0.7494 | 2942.199 | 125.539 |
| 0.7497 | 2942.610 | 125.539 |
| 0.7500 | 2942.928 | 125.536 |
| 0.7503 | 2943.233 | 125.541 |
| 0.7506 | 2943.578 | 125.531 |
| 0.7508 | 2943.777 | 125.529 |
| 0.7511 | 2944.113 | 125.529 |
| 0.7514 | 2944.344 | 125.534 |
| 0.7517 | 2944.557 | 125.526 |
| 0.7519 | 2944.823 | 125.519 |
| 0.7522 | 2944.906 | 125.513 |
| 0.7525 | 2945.171 | 125.544 |
| 0.7528 | 2945.240 | 125.501 |
| 0.7531 | 2945.321 | 125.506 |
| 0.7533 | 2945.559 | 125.521 |
| 0.7536 | 2945.596 | 125.526 |
| 0.7539 | 2945.647 | 125.498 |
| 0.7542 | 2945.746 | 125.516 |
| 0.7544 | 2945.845 | 125.496 |
| 0.7547 | 2945.852 | 125.506 |
| 0.7550 | 2945.953 | 125.503 |
| 0.7553 | 2945.980 | 125.496 |
| 0.7556 | 2945.995 | 125.496 |
| 0.7558 | 2946.076 | 125.501 |
| 0.7561 | 2946.059 | 125.488 |
| 0.7564 | 2946.064 | 125.481 |
| 0.7567 | 2946.118 | 125.498 |
| 0.7569 | 2946.123 | 125.486 |
| 0.7583 | 2946.342 | 125.470 |
| 0.7597 | 2946.994 | 125.450 |
| 0.7611 | 2947.771 | 125.445 |
| 0.7625 | 2948.461 | 125.420 |
| 0.7639 | 2948.858 | 125.415 |
| 0.7653 | 2948.980 | 125.385 |
| 0.7667 | 2949.150 | 125.372 |
| 0.7681 | 2949.417 | 125.321 |
| 0.7694 | 2949.969 | 125.326 |
| 0.7708 | 2950.390 | 125.296 |
| 0.7722 | 2950.584 | 125.268 |
| 0.7736 | 2950.593 | 125.258 |
| 0.7750 | 2950.695 | 125.213 |
| 0.7764 | 2950.717 | 125.190 |
| 0.7778 | 2951.029 | 125.167 |
| 0.7792 | 2951.606 | 125.142 |
| 0.7806 | 2952.135 | 125.124 |
| 0.7819 | 2952.151 | 125.081 |
| 0.7833 | 2952.090 | 125.053 |
| 0.7847 | 2952.004 | 125.023 |
| 0.7861 | 2952.313 | 124.987 |
| 0.7875 | 2952.483 | 124.937 |
| 0.7889 | 2952.800 | 124.912 |

| Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) |
|--------|--------------------|---------------------|--------|--------------------|---------------------|--------|--------------------|---------------------|
| 0.7903 | 2952.953 | 124.876 | 0.8944 | 2957.880 | 121.019 | 0.9986 | 2957.772 | 116.631 |
| 0.7917 | 2953.042 | 124.838 | 0.8958 | 2957.673 | 120.957 | 1.0000 | 2958.427 | 116.577 |
| 0.7931 | 2953.086 | 124.805 | 0.8972 | 2957.375 | 120.911 | 1.0014 | 2959.110 | 116.551 |
| 0.7944 | 2953.169 | 124.767 | 0.8986 | 2957.168 | 120.830 | 1.0028 | 2959.156 | 116.469 |
| 0.7958 | 2953.278 | 124.722 | 0.9000 | 2957.337 | 120.771 | 1.0042 | 2958.985 | 116.389 |
| 0.7972 | 2953.527 | 124.696 | 0.9014 | 2957.499 | 120.723 | 1.0056 | 2958.925 | 116.345 |
| 0.7986 | 2953.581 | 124.643 | 0.9028 | 2957.574 | 120.656 | 1.0069 | 2960.832 | 116.339 |
| 0.8000 | 2953.920 | 124.613 | 0.9042 | 2957.307 | 120.595 | 1.0083 | 2962.101 | 116.333 |
| 0.8014 | 2954.069 | 124.575 | 0.9056 | 2956.637 | 120.528 | 1.0097 | 2964.754 | 116.327 |
| 0.8028 | 2954.117 | 124.534 | 0.9069 | 2955.792 | 120.460 | 1.0111 | 2966.967 | 116.255 |
| 0.8042 | 2954.151 | 124.494 | 0.9083 | 2955.081 | 120.411 | 1.0125 | 2968.985 | 116.211 |
| 0.8056 | 2954.156 | 124.443 | 0.9097 | 2954.180 | 120.355 | 1.0139 | 2970.896 | 116.180 |
| 0.8069 | 2954.193 | 124.405 | 0.9111 | 2953.331 | 120.288 | 1.0153 | 2972.739 | 116.137 |
| 0.8083 | 2954.189 | 124.370 | 0.9125 | 2952.516 | 120.219 | 1.0167 | 2974.210 | 116.095 |
| 0.8097 | 2954.570 | 124.316 | 0.9139 | 2951.436 | 120.143 | 1.0181 | 2976.977 | 116.049 |
| 0.8111 | 2954.921 | 124.278 | 0.9153 | 2950.818 | 120.112 | 1.0194 | 2978.117 | 115.998 |
| 0.8125 | 2955.347 | 124.235 | 0.9167 | 2950.159 | 120.028 | 1.0208 | 2980.255 | 115.952 |
| 0.8139 | 2955.368 | 124.169 | 0.9181 | 2950.051 | 119.984 | 1.0222 | 2982.153 | 115.911 |
| 0.8153 | 2955.231 | 124.152 | 0.9194 | 2950.249 | 119.915 | 1.0236 | 2984.456 | 115.832 |
| 0.8167 | 2954.919 | 124.093 | 0.9208 | 2950.860 | 119.869 | 1.0250 | 2986.898 | 115.721 |
| 0.8181 | 2955.019 | 124.053 | 0.9222 | 2951.833 | 119.800 | 1.0264 | 2988.887 | 115.525 |
| 0.8194 | 2955.359 | 123.997 | 0.9236 | 2952.802 | 119.754 | 1.0278 | 2993.896 | 115.296 |
| 0.8208 | 2955.763 | 123.954 | 0.9250 | 2953.647 | 119.649 | 1.0292 | 2995.964 | 115.027 |
| 0.8222 | 2955.726 | 123.901 | 0.9264 | 2954.265 | 119.613 | 1.0306 | 2997.171 | 114.998 |
| 0.8236 | 2955.528 | 123.855 | 0.9278 | 2955.349 | 119.565 | 1.0319 | 2999.813 | 114.735 |
| 0.8250 | 2955.282 | 123.797 | 0.9292 | 2956.813 | 119.501 | 1.0333 | 3001.492 | 115.290 |
| 0.8264 | 2955.435 | 123.761 | 0.9306 | 2958.861 | 119.439 | 1.0347 | 3011.142 | 115.320 |
| 0.8278 | 2955.962 | 123.700 | 0.9319 | 2960.637 | 119.391 | 1.0361 | 3015.741 | 115.377 |
| 0.8292 | 2956.361 | 123.660 | 0.9333 | 2961.325 | 119.311 | 1.0375 | 3007.901 | 116.068 |
| 0.8306 | 2956.432 | 123.604 | 0.9347 | 2961.391 | 119.255 | 1.0389 | 3018.019 | 116.347 |
| 0.8319 | 2956.200 | 123.566 | 0.9361 | 2960.984 | 119.186 | 1.0403 | 3018.755 | 117.125 |
| 0.8333 | 2955.780 | 123.500 | 0.9375 | 2960.515 | 119.150 | 1.0417 | 3018.801 | 117.119 |
| 0.8347 | 2955.514 | 123.459 | 0.9389 | 2959.948 | 119.083 | 1.0431 | 3017.091 | 117.473 |
| 0.8361 | 2955.708 | 123.406 | 0.9403 | 2959.645 | 119.019 | 1.0444 | 3017.476 | 117.980 |
| 0.8375 | 2956.395 | 123.342 | 0.9417 | 2959.294 | 118.973 | 1.0458 | 3017.145 | 117.703 |
| 0.8389 | 2956.842 | 123.304 | 0.9431 | 2958.920 | 118.901 | 1.0472 | 3017.984 | 117.881 |
| 0.8403 | 2957.140 | 123.251 | 0.9444 | 2958.670 | 118.832 | 1.0486 | 3012.824 | 117.259 |
| 0.8417 | 2956.879 | 123.198 | 0.9458 | 2958.468 | 118.791 | 1.0500 | 3012.926 | 117.698 |
| 0.8431 | 2956.312 | 123.144 | 0.9472 | 2958.429 | 118.740 | 1.0514 | 3013.444 | 117.466 |
| 0.8444 | 2956.119 | 123.076 | 0.9486 | 2958.353 | 118.668 | 1.0528 | 3013.021 | 117.467 |
| 0.8458 | 2956.432 | 123.027 | 0.9500 | 2958.032 | 118.627 | 1.0542 | 3015.803 | 117.279 |
| 0.8472 | 2957.045 | 122.997 | 0.9514 | 2957.896 | 118.545 | 1.0556 | 3018.625 | 117.169 |
| 0.8486 | 2957.226 | 122.903 | 0.9528 | 2957.842 | 118.463 | 1.0569 | 3014.113 | 117.325 |
| 0.8500 | 2957.202 | 122.875 | 0.9542 | 2958.121 | 118.440 | 1.0583 | 3018.374 | 116.198 |
| 0.8514 | 2956.952 | 122.814 | 0.9556 | 2958.234 | 118.381 | 1.0597 | 3017.375 | 116.322 |
| 0.8528 | 2956.556 | 122.761 | 0.9569 | 2958.132 | 118.312 | 1.0611 | 3016.556 | 116.394 |
| 0.8542 | 2956.357 | 122.715 | 0.9583 | 2957.911 | 118.268 | 1.0625 | 3018.841 | 116.978 |
| 0.8556 | 2957.170 | 122.651 | 0.9597 | 2957.622 | 118.204 | 1.0639 | 3013.757 | 116.861 |
| 0.8569 | 2957.904 | 122.611 | 0.9611 | 2957.602 | 118.140 | 1.0653 | 3017.574 | 117.857 |
| 0.8583 | 2958.026 | 122.544 | 0.9625 | 2957.599 | 118.073 | 1.0667 | 3016.946 | 117.635 |
| 0.8597 | 2957.821 | 122.483 | 0.9639 | 2957.851 | 118.027 | 1.0681 | 3017.526 | 117.771 |
| 0.8611 | 2957.392 | 122.422 | 0.9653 | 2957.711 | 117.963 | 1.0694 | 3018.244 | 117.516 |
| 0.8625 | 2956.841 | 122.382 | 0.9667 | 2957.627 | 117.927 | 1.0708 | 3019.199 | 116.794 |
| 0.8639 | 2956.793 | 122.305 | 0.9681 | 2957.565 | 117.850 | 1.0722 | 3019.124 | 116.383 |
| 0.8653 | 2956.997 | 122.265 | 0.9694 | 2957.845 | 117.783 | 1.0736 | 3019.331 | 116.438 |
| 0.8667 | 2957.455 | 122.198 | 0.9708 | 2958.126 | 117.737 | 1.0742 | 3019.550 | 116.744 |
| 0.8681 | 2957.569 | 122.132 | 0.9722 | 2958.239 | 117.678 | 1.0783 | 3018.981 | 116.123 |
| 0.8694 | 2957.542 | 122.081 | 0.9736 | 2958.267 | 117.631 | 1.0825 | 3016.417 | 115.808 |
| 0.8708 | 2957.231 | 122.020 | 0.9750 | 2958.097 | 117.572 | 1.0867 | 3020.184 | 115.714 |
| 0.8722 | 2957.063 | 121.959 | 0.9764 | 2957.674 | 117.513 | 1.0908 | 3020.730 | 115.556 |
| 0.8736 | 2957.150 | 121.916 | 0.9778 | 2957.626 | 117.457 | 1.0950 | 3018.411 | 111.400 |
| 0.8750 | 2957.417 | 121.852 | 0.9792 | 2958.149 | 117.403 | 1.0992 | 3021.348 | 111.126 |
| 0.8764 | 2957.461 | 121.788 | 0.9806 | 2958.800 | 117.325 | 1.1033 | 3018.552 | 111.506 |
| 0.8778 | 2957.437 | 121.725 | 0.9819 | 2959.014 | 117.290 | 1.1075 | 3019.752 | 111.173 |
| 0.8792 | 2957.331 | 121.681 | 0.9833 | 2958.896 | 117.225 | 1.1117 | 3019.509 | 111.124 |
| 0.8806 | 2957.143 | 121.613 | 0.9847 | 2958.507 | 117.179 | 1.1158 | 3018.809 | 110.957 |
| 0.8819 | 2957.406 | 121.557 | 0.9861 | 2958.154 | 117.127 | 1.1200 | 3021.578 | 110.478 |
| 0.8833 | 2957.795 | 121.501 | 0.9875 | 2957.775 | 117.063 | 1.1242 | 3020.136 | 109.912 |
| 0.8847 | 2957.838 | 121.442 | 0.9889 | 2957.828 | 117.019 | 1.1283 | 3020.964 | 109.987 |
| 0.8861 | 2957.710 | 121.383 | 0.9903 | 2958.438 | 116.955 | 1.1325 | 3021.163 | 109.687 |
| 0.8875 | 2957.324 | 121.322 | 0.9917 | 2958.908 | 116.906 | 1.1367 | 3020.681 | 109.491 |
| 0.8889 | 2957.073 | 121.256 | 0.9931 | 2958.983 | 116.852 | 1.1408 | 3021.506 | 108.302 |
| 0.8903 | 2957.414 | 121.192 | 0.9944 | 2958.689 | 116.796 | 1.1450 | 3024.089 | 107.316 |
| 0.8917 | 2957.747 | 121.138 | 0.9958 | 2958.214 | 116.747 | 1.1492 | 3023.971 | 105.586 |
| 0.8931 | 2957.890 | 121.072 | 0.9972 | 2957.764 | 116.690 | 1.1533 | 3023.281 | 105.557 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|--------------------|---------------------|
| 1.1575 | 3023.140 | 106.178 |
| 1.1617 | 3023.929 | 107.811 |
| 1.1658 | 3024.548 | 107.693 |
| 1.1700 | 3023.795 | 107.720 |
| 1.1742 | 3023.765 | 107.105 |
| 1.1783 | 3023.355 | 106.822 |
| 1.1825 | 3024.549 | 106.277 |
| 1.1867 | 3025.226 | 105.650 |
| 1.1908 | 3026.732 | 105.276 |
| 1.1950 | 3024.874 | 105.712 |
| 1.1992 | 3027.866 | 105.525 |
| 1.2033 | 3025.389 | 105.162 |
| 1.2075 | 3025.660 | 104.956 |
| 1.2117 | 3025.544 | 104.650 |
| 1.2158 | 3025.892 | 104.426 |
| 1.2200 | 3026.531 | 104.151 |
| 1.2242 | 3024.534 | 103.890 |
| 1.2283 | 3025.066 | 103.615 |
| 1.2325 | 3025.537 | 103.493 |
| 1.2367 | 3025.488 | 103.102 |
| 1.2408 | 3026.308 | 102.850 |
| 1.2450 | 3025.981 | 102.585 |
| 1.2492 | 3025.807 | 102.578 |
| 1.2533 | 3026.400 | 102.114 |
| 1.2575 | 3026.094 | 101.867 |
| 1.2617 | 3025.542 | 101.700 |
| 1.2658 | 3028.294 | 101.440 |
| 1.2700 | 3026.430 | 101.187 |
| 1.2742 | 3028.150 | 100.922 |
| 1.2783 | 3028.556 | 100.696 |
| 1.2825 | 3028.904 | 100.483 |
| 1.2867 | 3027.725 | 100.185 |
| 1.2908 | 3027.367 | 99.996 |
| 1.2950 | 3027.972 | 99.941 |
| 1.2992 | 3029.438 | 99.524 |
| 1.3033 | 3029.510 | 99.570 |
| 1.3075 | 3029.722 | 99.386 |
| 1.3117 | 3030.407 | 98.881 |
| 1.3158 | 3027.983 | 98.609 |
| 1.3200 | 3027.677 | 98.406 |
| 1.3242 | 3028.238 | 98.230 |
| 1.3283 | 3028.190 | 98.080 |
| 1.3325 | 3029.915 | 97.797 |
| 1.3367 | 3030.180 | 97.633 |
| 1.3408 | 3030.952 | 97.616 |
| 1.3450 | 3031.439 | 97.160 |
| 1.3492 | 3029.839 | 96.921 |
| 1.3533 | 3029.834 | 96.720 |
| 1.3575 | 3032.410 | 96.490 |
| 1.3617 | 3030.239 | 96.299 |
| 1.3658 | 3032.472 | 96.084 |
| 1.3700 | 3034.314 | 95.870 |
| 1.3742 | 3032.960 | 95.671 |
| 1.3783 | 3031.984 | 95.469 |
| 1.3825 | 3033.338 | 95.335 |
| 1.3867 | 3034.104 | 94.999 |
| 1.3908 | 3032.794 | 94.889 |
| 1.3950 | 3033.671 | 94.765 |
| 1.3992 | 3033.674 | 94.320 |
| 1.4033 | 3033.823 | 94.326 |
| 1.4058 | 3035.134 | 94.186 |
| 1.4142 | 3033.250 | 93.776 |
| 1.4225 | 3035.015 | 93.296 |
| 1.4308 | 3034.955 | 93.005 |
| 1.4392 | 3035.091 | 92.594 |
| 1.4475 | 3037.052 | 92.270 |
| 1.4514 | 3035.447 | 92.118 |
| 1.4597 | 3037.855 | 91.782 |
| 1.4681 | 3035.232 | 91.517 |
| 1.4764 | 3035.322 | 91.674 |
| 1.4847 | 3036.387 | 90.845 |
| 1.4931 | 3038.930 | 90.623 |
| 1.5014 | 3037.500 | 90.405 |
| 1.5097 | 3037.682 | 90.215 |
| 1.5181 | 3038.093 | 89.995 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|--------------------|---------------------|
| 1.5264 | 3038.751 | 89.824 |
| 1.5347 | 3038.824 | 89.686 |
| 1.5431 | 3036.912 | 89.571 |
| 1.5514 | 3036.623 | 89.490 |
| 1.5597 | 3037.738 | 89.373 |
| 1.5681 | 3036.297 | 89.286 |
| 1.5764 | 3037.434 | 89.394 |
| 1.5847 | 3035.125 | 89.082 |
| 1.5931 | 3035.666 | 89.038 |
| 1.6014 | 3037.004 | 89.003 |
| 1.6097 | 3035.659 | 88.916 |
| 1.6181 | 3038.110 | 88.829 |
| 1.6264 | 3039.499 | 88.961 |
| 1.6347 | 3037.330 | 88.752 |
| 1.6431 | 3037.409 | 88.583 |
| 1.6514 | 3040.908 | 88.510 |
| 1.6597 | 3038.173 | 88.412 |
| 1.6681 | 3037.366 | 88.284 |
| 1.6764 | 3038.583 | 88.232 |
| 1.6847 | 3038.404 | 88.090 |
| 1.6931 | 3039.049 | 87.850 |
| 1.7014 | 3039.678 | 87.796 |
| 1.7097 | 3039.370 | 87.637 |
| 1.7181 | 3040.737 | 87.512 |
| 1.7264 | 3039.796 | 87.373 |
| 1.7347 | 3038.973 | 87.184 |
| 1.7431 | 3040.045 | 87.017 |
| 1.7514 | 3039.806 | 86.903 |
| 1.7597 | 3039.804 | 86.766 |
| 1.7681 | 3040.195 | 86.673 |
| 1.7764 | 3039.878 | 86.473 |
| 1.7847 | 3038.912 | 86.356 |
| 1.7931 | 3038.322 | 86.328 |
| 1.8014 | 3039.569 | 86.241 |
| 1.8097 | 3038.612 | 86.090 |
| 1.8181 | 3038.244 | 85.907 |
| 1.8264 | 3038.553 | 85.855 |
| 1.8347 | 3038.958 | 85.721 |
| 1.8431 | 3039.434 | 85.630 |
| 1.8514 | 3039.398 | 85.526 |
| 1.8597 | 3040.171 | 85.441 |
| 1.8681 | 3041.009 | 85.359 |
| 1.8764 | 3041.993 | 85.318 |
| 1.8847 | 3037.846 | 85.175 |
| 1.8931 | 3036.729 | 85.327 |
| 1.9014 | 3034.890 | 85.085 |
| 1.9097 | 3035.590 | 84.925 |
| 1.9181 | 3036.662 | 84.873 |
| 1.9264 | 3036.072 | 84.020 |
| 1.9347 | 3037.825 | 84.785 |
| 1.9431 | 3038.485 | 84.799 |
| 1.9514 | 3038.499 | 84.684 |
| 1.9597 | 3038.805 | 84.645 |
| 1.9681 | 3041.017 | 84.591 |
| 1.9764 | 3039.103 | 84.544 |
| 1.9847 | 3040.425 | 84.522 |
| 1.9931 | 3042.733 | 84.500 |
| 2.0014 | 3043.406 | 84.407 |
| 2.0097 | 3040.577 | 84.398 |
| 2.0181 | 3045.565 | 84.913 |
| 2.0264 | 3042.995 | 84.321 |
| 2.0347 | 3043.057 | 84.723 |
| 2.0431 | 3044.380 | 84.231 |
| 2.0514 | 3042.977 | 84.102 |
| 2.0597 | 3045.221 | 84.192 |
| 2.0681 | 3044.350 | 84.168 |
| 2.0764 | 3045.273 | 84.137 |
| 2.0847 | 3045.161 | 84.099 |
| 2.0931 | 3041.219 | 84.030 |
| 2.1014 | 3042.338 | 84.113 |
| 2.1097 | 3042.890 | 84.014 |
| 2.1181 | 3043.374 | 83.994 |
| 2.1264 | 3042.878 | 83.978 |
| 2.1347 | 3041.991 | 83.975 |
| 2.1431 | 3039.606 | 83.382 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|--------------------|---------------------|
| 2.1514 | 3041.945 | 83.582 |
| 2.1597 | 3043.861 | 83.937 |
| 2.1681 | 3041.760 | 83.981 |
| 2.1764 | 3043.330 | 83.917 |
| 2.1847 | 3042.952 | 83.956 |
| 2.1931 | 3043.226 | 83.538 |
| 2.2014 | 3042.726 | 83.909 |
| 2.2097 | 3043.066 | 83.917 |
| 2.2181 | 3043.071 | 83.162 |
| 2.2264 | 3043.461 | 83.417 |
| 2.2347 | 3043.209 | 83.699 |
| 2.2431 | 3043.886 | 83.931 |
| 2.2514 | 3042.495 | 83.926 |
| 2.2597 | 3044.604 | 83.989 |
| 2.2681 | 3044.086 | 83.950 |
| 2.2764 | 3043.688 | 83.753 |
| 2.2847 | 3042.371 | 83.989 |
| 2.2931 | 3043.476 | 83.994 |
| 2.3014 | 3045.483 | 83.948 |
| 2.3097 | 3045.507 | 84.000 |
| 2.3181 | 3044.056 | 84.005 |
| 2.3264 | 3045.295 | 84.137 |
| 2.3347 | 3044.419 | 84.033 |
| 2.3431 | 3045.022 | 84.000 |
| 2.3514 | 3044.383 | 84.258 |
| 2.3597 | 3043.324 | 84.077 |
| 2.3681 | 3042.898 | 84.077 |
| 2.3764 | 3041.400 | 84.195 |
| 2.3847 | 3041.271 | 84.397 |
| 2.3931 | 3042.685 | 84.484 |
| 2.4014 | 3043.691 | 84.191 |
| 2.4097 | 3043.496 | 84.297 |
| 2.4181 | 3042.208 | 84.228 |
| 2.4264 | 3041.602 | 84.297 |
| 2.4347 | 3041.343 | 84.310 |
| 2.4431 | 3041.845 | 84.360 |
| 2.4514 | 3042.751 | 84.228 |
| 2.4597 | 3041.123 | 84.277 |
| 2.4681 | 3043.033 | 84.255 |
| 2.4764 | 3042.552 | 84.165 |
| 2.4847 | 3041.961 | 84.449 |
| 2.4931 | 3043.229 | 84.121 |
| 2.5014 | 3042.517 | 84.066 |
| 2.5097 | 3042.448 | 84.091 |
| 2.5181 | 3041.935 | 83.992 |
| 2.5264 | 3042.856 | 83.945 |
| 2.5347 | 3043.422 | 83.901 |
| 2.5431 | 3041.623 | 83.857 |
| 2.5514 | 3044.156 | 83.761 |
| 2.5597 | 3044.138 | 83.711 |
| 2.5681 | 3043.213 | 83.667 |
| 2.5764 | 3043.504 | 83.585 |
| 2.5847 | 3044.707 | 83.576 |
| 2.5931 | 3044.258 | 83.447 |
| 2.6014 | 3043.549 | 83.464 |
| 2.6097 | 3044.815 | 83.414 |
| 2.6181 | 3045.537 | 83.312 |
| 2.6264 | 3046.855 | 83.296 |
| 2.6347 | 3043.623 | 83.221 |
| 2.6431 | 3043.977 | 83.656 |
| 2.6514 | 3043.534 | 83.133 |
| 2.6597 | 3042.998 | 83.100 |
| 2.6681 | 3044.393 | 83.056 |
| 2.6764 | 3043.873 | 83.252 |
| 2.6847 | 3042.308 | 83.252 |
| 2.6931 | 3043.370 | 83.131 |
| 2.7014 | 3042.106 | 83.147 |
| 2.7097 | 3042.819 | 82.861 |
| 2.7181 | 3045.122 | 82.852 |
| 2.7264 | 3043.116 | 82.167 |
| 2.7347 | 3044.347 | 82.862 |
| 2.7431 | 3044.093 | 82.811 |
| 2.7514 | 3043.776 | 82.657 |
| 2.7597 | 3043.144 | 82.615 |
| 2.7681 | 3042.837 | 82.778 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|--------------------|---------------------|
| 2.7764 | 3044.088 | 82.728 |
| 2.7847 | 3043.743 | 82.972 |
| 2.7931 | 3043.438 | 82.000 |
| 2.8014 | 3041.471 | 82.624 |
| 2.8097 | 3042.180 | 82.739 |
| 2.8181 | 3043.030 | 82.329 |
| 2.8264 | 3043.897 | 82.025 |
| 2.8347 | 3043.851 | 82.665 |
| 2.8431 | 3043.827 | 82.646 |
| 2.8514 | 3043.657 | 82.704 |
| 2.8597 | 3042.292 | 82.759 |
| 2.8681 | 3043.461 | 82.720 |
| 2.8764 | 3042.224 | 82.772 |
| 2.8847 | 3044.702 | 82.912 |
| 2.8931 | 3042.674 | 82.748 |
| 2.9014 | 3042.667 | 82.726 |
| 2.9097 | 3042.508 | 82.753 |
| 2.9181 | 3043.637 | 82.511 |
| 2.9264 | 3041.833 | 82.753 |
| 2.9347 | 3042.665 | 82.411 |
| 2.9431 | 3041.757 | 82.814 |
| 2.9514 | 3042.854 | 82.593 |
| 2.9597 | 3042.363 | 82.717 |
| 2.9681 | 3044.638 | 82.830 |
| 2.9764 | 3044.493 | 82.087 |
| 2.9847 | 3043.438 | 82.367 |
| 2.9931 | 3043.282 | 82.872 |
| 3.0014 | 3041.746 | 82.186 |
| 3.0097 | 3040.899 | 82.833 |
| 3.0181 | 3041.585 | 82.951 |
| 3.0264 | 3042.053 | 82.954 |
| 3.0347 | 3040.582 | 82.913 |
| 3.0431 | 3041.713 | 83.034 |
| 3.0514 | 3041.299 | 83.062 |
| 3.0597 | 3042.729 | 83.064 |
| 3.0644 | 3042.914 | 83.380 |
| 3.0811 | 3043.342 | 83.180 |
| 3.0978 | 3042.185 | 83.252 |
| 3.1144 | 3043.144 | 83.610 |
| 3.1311 | 3044.276 | 83.758 |
| 3.1478 | 3044.367 | 83.788 |
| 3.1644 | 3045.007 | 83.810 |
| 3.1811 | 3045.209 | 83.214 |
| 3.1978 | 3046.833 | 83.656 |
| 3.2144 | 3049.644 | 83.964 |
| 3.2311 | 3046.539 | 84.394 |
| 3.2478 | 3050.614 | 84.244 |
| 3.2644 | 3049.021 | 84.151 |
| 3.2811 | 3048.756 | 84.574 |
| 3.2978 | 3047.335 | 84.750 |
| 3.3133 | 3049.331 | 84.997 |
| 3.3300 | 3048.990 | 84.873 |
| 3.3467 | 3049.280 | 85.038 |
| 3.3633 | 3047.765 | 84.871 |
| 3.3800 | 3048.272 | 85.008 |
| 3.3967 | 3049.124 | 85.019 |
| 3.4133 | 3049.177 | 85.038 |
| 3.4300 | 3049.410 | 85.052 |
| 3.4467 | 3049.138 | 85.052 |
| 3.4633 | 3049.792 | 85.158 |
| 3.4800 | 3049.545 | 86.048 |
| 3.4967 | 3049.490 | 85.952 |
| 3.5133 | 3049.762 | 85.723 |
| 3.5300 | 3049.841 | 85.308 |
| 3.5467 | 3048.697 | 85.074 |
| 3.5633 | 3049.177 | 85.368 |
| 3.5800 | 3047.381 | 85.378 |
| 3.5967 | 3049.007 | 85.019 |
| 3.6133 | 3049.731 | 85.180 |
| 3.6300 | 3049.625 | 85.661 |
| 3.6467 | 3050.298 | 85.159 |
| 3.6633 | 3049.042 | 85.148 |
| 3.6800 | 3048.232 | 85.139 |
| 3.6967 | 3049.957 | 85.183 |
| 3.7133 | 3049.163 | 85.268 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|--------------------|---------------------|
| 3.7300 | 3052.430 | 85.282 |
| 3.7467 | 3051.838 | 85.257 |
| 3.7633 | 3051.778 | 85.216 |
| 3.7800 | 3050.998 | 85.282 |
| 3.7967 | 3050.755 | 85.608 |
| 3.8133 | 3054.032 | 85.397 |
| 3.8300 | 3053.021 | 85.414 |
| 3.8467 | 3052.927 | 85.739 |
| 3.8633 | 3053.045 | 85.504 |
| 3.8800 | 3051.540 | 85.564 |
| 3.8967 | 3054.196 | 85.685 |
| 3.9133 | 3052.310 | 85.723 |
| 3.9300 | 3053.646 | 85.479 |
| 3.9467 | 3052.703 | 86.174 |
| 3.9633 | 3051.997 | 86.008 |
| 3.9800 | 3052.528 | 86.454 |
| 3.9967 | 3053.634 | 86.317 |
| 4.0133 | 3052.678 | 86.224 |
| 4.0300 | 3051.165 | 86.153 |
| 4.0467 | 3051.147 | 87.085 |
| 4.0633 | 3050.755 | 87.012 |
| 4.0800 | 3050.658 | 87.173 |
| 4.0967 | 3051.353 | 87.378 |
| 4.1133 | 3053.614 | 87.392 |
| 4.1300 | 3055.224 | 87.463 |
| 4.1467 | 3050.471 | 87.386 |
| 4.1633 | 3052.273 | 87.446 |
| 4.1800 | 3051.510 | 87.304 |
| 4.1967 | 3050.180 | 87.405 |
| 4.2133 | 3049.304 | 87.045 |
| 4.2300 | 3051.355 | 86.864 |
| 4.2467 | 3050.774 | 86.673 |
| 4.2633 | 3050.729 | 86.534 |
| 4.2800 | 3051.275 | 86.348 |
| 4.2967 | 3052.208 | 86.194 |
| 4.3133 | 3053.225 | 86.049 |
| 4.3300 | 3054.157 | 85.896 |
| 4.3467 | 3052.284 | 85.729 |
| 4.3633 | 3051.154 | 85.767 |
| 4.3800 | 3049.935 | 85.611 |
| 4.3967 | 3049.195 | 85.493 |
| 4.4133 | 3049.593 | 85.430 |
| 4.4300 | 3051.028 | 85.375 |
| 4.4467 | 3049.987 | 85.403 |
| 4.4633 | 3049.325 | 85.246 |
| 4.4800 | 3048.921 | 85.183 |
| 4.4803 | 3050.515 | 85.268 |
| 4.4969 | 3049.733 | 85.252 |
| 4.5136 | 3048.830 | 85.145 |
| 4.5303 | 3048.368 | 85.175 |
| 4.5469 | 3049.562 | 85.244 |
| 4.5636 | 3051.426 | 85.194 |
| 4.5803 | 3050.590 | 85.213 |
| 4.5969 | 3049.895 | 85.271 |
| 4.6136 | 3053.192 | 85.255 |
| 4.6303 | 3052.078 | 85.312 |
| 4.6469 | 3052.681 | 85.353 |
| 4.6636 | 3051.436 | 85.463 |
| 4.6803 | 3048.765 | 85.562 |
| 4.6969 | 3050.467 | 85.564 |
| 4.7136 | 3050.647 | 85.737 |
| 4.7303 | 3051.339 | 85.838 |
| 4.7469 | 3051.653 | 86.057 |
| 4.7636 | 3050.594 | 86.181 |
| 4.7803 | 3051.686 | 86.298 |
| 4.7969 | 3051.355 | 86.440 |
| 4.8136 | 3050.615 | 86.539 |
| 4.8303 | 3047.648 | 86.605 |
| 4.8469 | 3047.671 | 86.695 |
| 4.8636 | 3049.646 | 86.709 |
| 4.8803 | 3050.338 | 86.758 |
| 4.8969 | 3051.481 | 86.752 |
| 4.9136 | 3051.716 | 86.763 |
| 4.9303 | 3053.402 | 86.791 |
| 4.9469 | 3051.347 | 86.725 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|--------------------|---------------------|
| 4.9636 | 3050.159 | 86.700 |
| 4.9803 | 3046.631 | 86.689 |
| 4.9969 | 3045.079 | 86.670 |
| 5.0136 | 3045.848 | 86.624 |
| 5.0303 | 3048.133 | 86.646 |
| 5.0469 | 3048.508 | 86.575 |
| 5.0636 | 3048.016 | 86.564 |
| 5.0803 | 3049.940 | 86.577 |
| 5.0969 | 3050.082 | 86.605 |
| 5.1136 | 3050.649 | 86.553 |
| 5.1303 | 3051.024 | 86.512 |
| 5.1469 | 3049.343 | 86.479 |
| 5.1636 | 3050.472 | 86.523 |
| 5.1803 | 3049.409 | 86.509 |
| 5.1969 | 3051.556 | 86.539 |
| 5.2136 | 3049.948 | 86.536 |
| 5.2303 | 3050.280 | 86.575 |
| 5.2469 | 3049.901 | 86.580 |
| 5.2636 | 3051.438 | 86.640 |
| 5.2803 | 3053.698 | 86.657 |
| 5.2969 | 3052.255 | 86.719 |
| 5.3136 | 3052.829 | 86.780 |
| 5.3303 | 3052.729 | 86.867 |
| 5.3469 | 3052.330 | 86.930 |
| 5.3636 | 3051.326 | 86.985 |
| 5.3803 | 3049.407 | 87.105 |
| 5.3969 | 3051.986 | 87.247 |
| 5.4136 | 3053.035 | 87.310 |
| 5.4303 | 3052.592 | 87.531 |
| 5.4469 | 3055.729 | 87.752 |
| 5.4636 | 3054.580 | 87.313 |
| 5.4803 | 3055.518 | 88.338 |
| 5.4969 | 3056.766 | 88.281 |
| 5.5136 | 3058.369 | 88.515 |
| 5.5303 | 3056.976 | 88.624 |
| 5.5469 | 3054.276 | 88.712 |
| 5.5636 | 3055.348 | 88.657 |
| 5.5803 | 3057.091 | 88.600 |
| 5.5969 | 3057.154 | 88.420 |
| 5.6136 | 3057.515 | 88.235 |
| 5.6303 | 3056.112 | 88.066 |
| 5.6469 | 3056.574 | 87.823 |
| 5.6636 | 3057.765 | 87.615 |
| 5.6803 | 3056.989 | 87.463 |
| 5.6969 | 3059.323 | 87.250 |
| 5.7136 | 3052.330 | 87.080 |
| 5.7303 | 3055.072 | 86.930 |
| 5.7469 | 3054.807 | 86.799 |
| 5.7636 | 3056.186 | 86.621 |
| 5.7803 | 3056.285 | 86.525 |
| 5.7969 | 3059.622 | 86.312 |
| 5.8136 | 3059.826 | 86.457 |
| 5.8303 | 3059.311 | 86.233 |
| 5.8389 | 3058.792 | 86.167 |
| 5.8556 | 3057.597 | 86.142 |
| 5.8722 | 3056.813 | 86.098 |
| 5.8889 | 3059.578 | 86.044 |
| 5.9056 | 3057.426 | 85.970 |
| 5.9222 | 3058.054 | 85.923 |
| 5.9389 | 3056.522 | 85.940 |
| 5.9556 | 3057.658 | 85.923 |
| 5.9722 | 3056.761 | 85.882 |
| 5.9889 | 3055.153 | 85.920 |
| 6.0056 | 3055.280 | 85.940 |
| 6.0222 | 3057.643 | 85.923 |
| 6.0389 | 3060.250 | 85.978 |
| 6.0556 | 3054.375 | 86.033 |
| 6.0722 | 3055.430 | 86.098 |
| 6.0889 | 3055.999 | 86.208 |
| 6.1056 | 3057.295 | 86.276 |
| 6.1222 | 3059.083 | 86.438 |
| 6.1389 | 3057.820 | 86.558 |
| 6.1556 | 3057.509 | 86.763 |
| 6.1722 | 3057.783 | 86.933 |
| 6.1889 | 3058.601 | 87.151 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|-----------------|------------------|
| 6.2056 | 3058.084 | 87.394 |
| 6.2222 | 3058.719 | 87.637 |
| 6.2389 | 3057.404 | 87.894 |
| 6.2556 | 3058.265 | 88.197 |
| 6.2722 | 3057.987 | 88.398 |
| 6.2889 | 3058.386 | 88.551 |
| 6.3056 | 3057.976 | 88.703 |
| 6.3222 | 3060.124 | 88.684 |
| 6.3389 | 3060.048 | 88.793 |
| 6.3556 | 3060.656 | 88.758 |
| 6.3722 | 3060.785 | 88.638 |
| 6.3889 | 3058.583 | 88.592 |
| 6.4056 | 3056.252 | 88.475 |
| 6.4222 | 3060.231 | 88.379 |
| 6.4389 | 3058.454 | 88.267 |
| 6.4556 | 3058.410 | 88.180 |
| 6.4722 | 3057.377 | 88.047 |
| 6.4889 | 3057.845 | 87.992 |
| 6.5056 | 3059.517 | 87.899 |
| 6.5222 | 3061.076 | 87.831 |
| 6.5389 | 3059.939 | 87.738 |
| 6.5556 | 3059.673 | 87.651 |
| 6.5722 | 3061.874 | 87.667 |
| 6.5889 | 3060.659 | 87.561 |
| 6.6056 | 3060.060 | 87.525 |
| 6.6222 | 3057.875 | 87.457 |
| 6.6389 | 3059.385 | 87.435 |
| 6.6556 | 3060.672 | 87.424 |
| 6.6722 | 3059.781 | 87.337 |
| 6.6889 | 3061.686 | 87.345 |
| 6.7056 | 3061.056 | 87.433 |
| 6.7222 | 3060.234 | 87.400 |
| 6.7389 | 3062.373 | 87.482 |
| 6.7556 | 3061.115 | 87.452 |
| 6.7722 | 3060.753 | 87.515 |
| 6.7889 | 3059.322 | 87.539 |
| 6.8056 | 3059.726 | 87.599 |
| 6.8222 | 3061.977 | 87.678 |
| 6.8389 | 3060.193 | 87.763 |
| 6.8556 | 3060.230 | 87.842 |
| 6.8722 | 3059.938 | 87.976 |
| 6.8889 | 3057.843 | 88.142 |
| 6.9056 | 3060.619 | 88.284 |
| 6.9222 | 3062.188 | 88.436 |
| 6.9389 | 3059.951 | 88.660 |
| 6.9556 | 3057.811 | 88.842 |
| 6.9722 | 3058.086 | 88.973 |
| 6.9889 | 3060.646 | 89.125 |
| 7.0056 | 3055.850 | 89.229 |
| 7.0222 | 3056.868 | 89.272 |
| 7.0389 | 3057.698 | 89.332 |
| 7.0556 | 3059.821 | 89.376 |
| 7.0722 | 3061.181 | 89.406 |
| 7.0889 | 3059.448 | 89.362 |
| 7.1056 | 3060.363 | 89.435 |
| 7.1222 | 3058.949 | 89.446 |
| 7.1389 | 3059.304 | 89.425 |
| 7.1556 | 3060.328 | 89.433 |
| 7.1722 | 3061.714 | 89.571 |
| 7.1889 | 3062.085 | 89.493 |
| 7.2056 | 3061.729 | 89.529 |
| 7.2222 | 3061.807 | 89.877 |
| 7.2389 | 3062.704 | 89.520 |
| 7.2556 | 3061.664 | 89.230 |
| 7.2722 | 3061.543 | 89.152 |
| 7.2889 | 3061.263 | 89.040 |
| 7.3056 | 3063.188 | 89.672 |
| 7.3222 | 3061.533 | 89.691 |
| 7.3389 | 3062.009 | 89.740 |
| 7.3556 | 3062.764 | 89.735 |
| 7.3722 | 3065.635 | 89.941 |
| 7.3889 | 3063.368 | 89.941 |
| 7.4056 | 3060.067 | 90.012 |
| 7.4222 | 3060.302 | 90.115 |
| 7.4389 | 3060.878 | 90.215 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|-----------------|------------------|
| 7.4408 | 3060.812 | 90.308 |
| 7.4575 | 3060.811 | 90.615 |
| 7.4742 | 3060.176 | 90.617 |
| 7.4908 | 3059.929 | 90.631 |
| 7.5075 | 3057.564 | 90.861 |
| 7.5242 | 3061.129 | 91.062 |
| 7.5408 | 3061.180 | 91.208 |
| 7.5575 | 3060.650 | 91.909 |
| 7.5742 | 3060.746 | 91.975 |
| 7.5908 | 3060.177 | 91.590 |
| 7.6075 | 3060.307 | 91.674 |
| 7.6242 | 3062.727 | 91.723 |
| 7.6408 | 3059.009 | 91.739 |
| 7.6575 | 3058.792 | 91.726 |
| 7.6742 | 3058.808 | 91.769 |
| 7.6908 | 3060.375 | 91.780 |
| 7.7075 | 3056.728 | 91.799 |
| 7.7242 | 3059.133 | 91.777 |
| 7.7408 | 3056.258 | 91.834 |
| 7.7575 | 3058.459 | 91.799 |
| 7.7742 | 3056.764 | 91.476 |
| 7.7908 | 3056.631 | 91.077 |
| 7.8075 | 3058.991 | 91.842 |
| 7.8242 | 3059.292 | 91.869 |
| 7.8408 | 3058.386 | 91.985 |
| 7.8575 | 3058.021 | 91.991 |
| 7.8742 | 3058.444 | 91.512 |
| 7.8908 | 3058.608 | 92.021 |
| 7.9075 | 3058.002 | 92.067 |
| 7.9242 | 3057.604 | 92.280 |
| 7.9408 | 3057.931 | 92.215 |
| 7.9575 | 3057.931 | 92.251 |
| 7.9742 | 3060.932 | 92.318 |
| 7.9908 | 3058.629 | 92.903 |
| 8.0075 | 3057.258 | 92.475 |
| 8.0242 | 3060.492 | 92.440 |
| 8.0408 | 3060.750 | 92.616 |
| 8.0575 | 3059.308 | 92.718 |
| 8.0742 | 3059.817 | 92.824 |
| 8.0908 | 3057.458 | 92.894 |
| 8.1075 | 3057.320 | 92.219 |
| 8.1242 | 3057.928 | 92.345 |
| 8.1408 | 3058.671 | 92.994 |
| 8.1575 | 3058.861 | 93.283 |
| 8.1742 | 3058.028 | 93.648 |
| 8.1908 | 3058.168 | 93.585 |
| 8.2075 | 3058.067 | 93.771 |
| 8.2242 | 3059.409 | 93.916 |
| 8.2408 | 3059.373 | 94.035 |
| 8.2575 | 3063.637 | 94.226 |
| 8.2742 | 3063.749 | 94.927 |
| 8.2908 | 3064.091 | 94.898 |
| 8.3075 | 3063.377 | 95.155 |
| 8.3242 | 3063.190 | 95.155 |
| 8.3408 | 3062.925 | 95.381 |
| 8.3575 | 3063.098 | 95.970 |
| 8.3742 | 3062.569 | 95.714 |
| 8.3908 | 3059.613 | 95.348 |
| 8.4075 | 3060.685 | 95.940 |
| 8.4242 | 3061.353 | 95.756 |
| 8.4408 | 3061.834 | 95.534 |
| 8.4575 | 3062.265 | 95.347 |
| 8.4742 | 3061.771 | 94.751 |
| 8.4908 | 3062.548 | 94.690 |
| 8.5075 | 3062.693 | 94.443 |
| 8.5242 | 3062.338 | 93.930 |
| 8.5408 | 3063.956 | 93.556 |
| 8.5575 | 3063.528 | 93.194 |
| 8.5742 | 3063.386 | 92.725 |
| 8.5908 | 3062.462 | 92.656 |
| 8.6075 | 3065.505 | 92.418 |
| 8.6242 | 3063.634 | 92.686 |
| 8.6408 | 3061.454 | 92.053 |
| 8.6575 | 3059.610 | 91.977 |
| 8.6742 | 3055.146 | 91.574 |

| Time | Pressure (Psia) | Temperature (°F) |
|--------|-----------------|------------------|
| 8.6908 | 3057.271 | 91.495 |
| 8.7075 | 3055.253 | 91.352 |
| 8.7242 | 3057.361 | 91.295 |
| 8.7408 | 3057.642 | 91.195 |
| 8.7575 | 3058.939 | 91.075 |
| 8.7742 | 3061.209 | 91.000 |
| 8.7908 | 3059.166 | 91.013 |
| 8.8075 | 3058.057 | 90.964 |
| 8.8242 | 3058.193 | 90.812 |
| 8.8408 | 3056.277 | 90.823 |
| 8.8575 | 3056.803 | 90.900 |
| 8.8742 | 3058.675 | 90.062 |
| 8.8908 | 3060.719 | 90.766 |
| 8.9075 | 3061.221 | 90.810 |
| 8.9242 | 3061.086 | 90.850 |
| 8.9408 | 3060.782 | 90.403 |
| 8.9575 | 3061.430 | 90.703 |
| 8.9742 | 3059.534 | 91.021 |
| 8.9908 | 3062.381 | 91.162 |
| 9.0075 | 3061.406 | 91.238 |
| 9.0242 | 3060.401 | 91.387 |
| 9.0408 | 3061.894 | 91.571 |
| 9.0575 | 3062.645 | 91.815 |
| 9.0742 | 3063.075 | 92.026 |
| 9.0908 | 3063.479 | 92.286 |
| 9.1075 | 3065.755 | 92.613 |
| 9.1242 | 3066.590 | 92.918 |
| 9.1408 | 3063.935 | 93.261 |
| 9.1575 | 3065.623 | 93.650 |
| 9.1742 | 3067.499 | 93.946 |
| 9.1908 | 3068.557 | 94.216 |
| 9.2075 | 3068.100 | 94.436 |
| 9.2242 | 3067.748 | 94.485 |
| 9.2408 | 3067.413 | 94.480 |
| 9.2575 | 3065.157 | 94.412 |
| 9.2742 | 3066.536 | 94.318 |
| 9.2908 | 3067.631 | 94.170 |
| 9.3075 | 3065.674 | 93.968 |
| 9.3242 | 3069.410 | 93.747 |
| 9.3408 | 3067.098 | 93.528 |
| 9.3575 | 3066.980 | 93.364 |
| 9.3742 | 3068.198 | 93.126 |
| 9.3908 | 3066.476 | 92.940 |
| 9.4075 | 3068.926 | 92.778 |
| 9.4242 | 3067.596 | 92.553 |
| 9.4408 | 3065.438 | 92.410 |
| 9.4575 | 3066.773 | 92.213 |
| 9.4742 | 3066.150 | 92.156 |
| 9.4908 | 3062.874 | 92.091 |
| 9.5075 | 3066.233 | 91.939 |
| 9.5242 | 3065.744 | 91.969 |
| 9.5408 | 3066.357 | 91.904 |
| 9.5575 | 3065.514 | 91.845 |
| 9.5742 | 3066.710 | 91.788 |
| 9.5908 | 3068.191 | 91.761 |
| 9.6075 | 3066.280 | 91.728 |
| 9.6242 | 3066.925 | 91.777 |
| 9.6408 | 3068.180 | 91.755 |
| 9.6575 | 3067.760 | 91.774 |
| 9.6742 | 3068.075 | 91.758 |
| 9.6908 | 3067.114 | 91.717 |
| 9.7075 | 3066.758 | 91.810 |
| 9.7242 | 3068.269 | 91.926 |
| 9.7408 | 3067.216 | 91.926 |
| 9.7575 | 3068.622 | 91.945 |
| 9.7742 | 3068.853 | 92.013 |
| 9.7908 | 3064.671 | 91.967 |
| 9.8075 | 3064.622 | 92.159 |
| 9.8242 | 3066.186 | 92.459 |
| 9.8408 | 3066.512 | 92.261 |
| 9.8575 | 3065.120 | 92.386 |
| 9.8742 | 3066.778 | 92.562 |
| 9.8908 | 3067.148 | 92.586 |
| 9.9075 | 3066.679 | 92.645 |
| 9.9242 | 3067.773 | 92.834 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 9.9408 | 3067.109 | 92.897 |
| 9.9575 | 3067.073 | 93.202 |
| 9.9742 | 3066.307 | 93.315 |
| 9.9908 | 3066.481 | 93.404 |
| 10.0075 | 3068.025 | 93.590 |
| 10.0242 | 3068.577 | 94.022 |
| 10.0408 | 3066.137 | 93.935 |
| 10.0575 | 3066.909 | 94.178 |
| 10.0742 | 3065.875 | 94.315 |
| 10.0908 | 3068.625 | 94.375 |
| 10.1075 | 3068.123 | 94.528 |
| 10.1242 | 3067.381 | 94.407 |
| 10.1408 | 3067.812 | 94.275 |
| 10.1575 | 3068.601 | 94.224 |
| 10.1742 | 3066.908 | 94.059 |
| 10.1908 | 3067.231 | 93.854 |
| 10.2075 | 3067.318 | 93.650 |
| 10.2242 | 3064.288 | 93.539 |
| 10.2408 | 3064.215 | 93.339 |
| 10.2575 | 3063.793 | 93.194 |
| 10.2742 | 3064.216 | 93.372 |
| 10.2908 | 3065.438 | 92.807 |
| 10.3075 | 3069.127 | 92.713 |
| 10.3242 | 3067.208 | 92.345 |
| 10.3408 | 3070.536 | 92.383 |
| 10.3575 | 3067.712 | 92.253 |
| 10.3742 | 3068.163 | 92.029 |
| 10.3908 | 3067.055 | 92.004 |
| 10.4075 | 3069.578 | 92.099 |
| 10.4242 | 3068.679 | 91.785 |
| 10.4408 | 3071.913 | 91.820 |
| 10.4575 | 3073.201 | 91.677 |
| 10.4742 | 3072.445 | 91.647 |
| 10.4908 | 3072.565 | 91.878 |
| 10.5075 | 3073.824 | 91.711 |
| 10.5242 | 3074.177 | 91.590 |
| 10.5408 | 3071.608 | 91.471 |
| 10.5575 | 3070.959 | 91.509 |
| 10.5742 | 3070.764 | 91.531 |
| 10.5908 | 3073.096 | 91.506 |
| 10.6075 | 3071.159 | 91.653 |
| 10.6242 | 3072.777 | 91.682 |
| 10.6408 | 3071.086 | 91.746 |
| 10.6575 | 3070.939 | 91.948 |
| 10.6742 | 3070.328 | 92.056 |
| 10.6908 | 3071.822 | 92.307 |
| 10.7075 | 3072.232 | 92.656 |
| 10.7242 | 3069.797 | 92.678 |
| 10.7408 | 3071.714 | 93.072 |
| 10.7575 | 3071.573 | 93.196 |
| 10.7742 | 3068.343 | 93.391 |
| 10.7908 | 3069.877 | 93.493 |
| 10.8075 | 3067.356 | 93.520 |
| 10.8242 | 3068.069 | 93.582 |
| 10.8408 | 3069.349 | 93.428 |
| 10.8575 | 3067.341 | 93.516 |
| 10.8742 | 3065.518 | 93.053 |
| 10.8908 | 3066.575 | 92.848 |
| 10.9075 | 3065.131 | 92.540 |
| 10.9242 | 3065.492 | 92.310 |
| 10.9408 | 3066.298 | 91.905 |
| 10.9575 | 3068.507 | 91.923 |
| 10.9742 | 3067.556 | 91.617 |
| 10.9908 | 3066.910 | 91.425 |
| 11.0075 | 3070.101 | 91.214 |
| 11.0242 | 3072.009 | 90.964 |
| 11.0408 | 3071.600 | 90.897 |
| 11.0575 | 3068.523 | 90.739 |
| 11.0742 | 3068.605 | 90.571 |
| 11.0908 | 3068.361 | 90.452 |
| 11.1075 | 3069.621 | 90.376 |
| 11.1242 | 3068.267 | 90.245 |
| 11.1408 | 3070.100 | 90.142 |
| 11.1575 | 3068.823 | 90.090 |
| 11.1742 | 3067.900 | 90.001 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 11.1908 | 3068.090 | 89.974 |
| 11.2075 | 3069.125 | 89.968 |
| 11.2242 | 3068.899 | 89.947 |
| 11.2408 | 3068.394 | 89.933 |
| 11.2575 | 3066.408 | 89.903 |
| 11.2742 | 3068.777 | 89.952 |
| 11.2908 | 3069.252 | 89.985 |
| 11.3075 | 3067.561 | 90.020 |
| 11.3242 | 3066.398 | 90.066 |
| 11.3408 | 3067.536 | 90.126 |
| 11.3575 | 3066.323 | 90.237 |
| 11.3742 | 3067.538 | 90.226 |
| 11.3908 | 3065.623 | 90.367 |
| 11.4075 | 3069.189 | 90.419 |
| 11.4242 | 3067.737 | 90.571 |
| 11.4408 | 3069.502 | 90.758 |
| 11.4575 | 3068.592 | 90.910 |
| 11.4742 | 3068.419 | 91.162 |
| 11.4908 | 3067.618 | 91.206 |
| 11.5075 | 3068.415 | 91.422 |
| 11.5242 | 3069.106 | 91.615 |
| 11.5408 | 3069.803 | 92.031 |
| 11.5575 | 3070.423 | 92.315 |
| 11.5742 | 3072.575 | 92.456 |
| 11.5908 | 3070.472 | 92.664 |
| 11.6075 | 3069.708 | 92.156 |
| 11.6242 | 3070.427 | 92.691 |
| 11.6408 | 3071.865 | 92.575 |
| 11.6575 | 3071.152 | 92.191 |
| 11.6742 | 3067.785 | 91.985 |
| 11.6908 | 3069.490 | 91.685 |
| 11.7075 | 3070.776 | 91.390 |
| 11.7242 | 3070.897 | 91.272 |
| 11.7408 | 3071.436 | 90.538 |
| 11.7575 | 3072.568 | 90.139 |
| 11.7742 | 3072.516 | 89.773 |
| 11.7908 | 3068.239 | 89.318 |
| 11.8075 | 3068.467 | 89.226 |
| 11.8242 | 3068.557 | 88.613 |
| 11.8408 | 3068.895 | 88.352 |
| 11.8575 | 3068.670 | 88.082 |
| 11.8742 | 3069.740 | 87.831 |
| 11.8908 | 3069.286 | 87.689 |
| 11.9075 | 3070.070 | 87.444 |
| 11.9242 | 3070.297 | 87.244 |
| 11.9408 | 3070.239 | 87.072 |
| 11.9575 | 3070.832 | 86.884 |
| 11.9742 | 3070.095 | 86.025 |
| 11.9908 | 3070.566 | 86.692 |
| 12.0075 | 3070.772 | 86.446 |
| 12.0242 | 3069.519 | 86.389 |
| 12.0408 | 3070.886 | 86.265 |
| 12.0575 | 3071.867 | 86.230 |
| 12.0742 | 3073.390 | 86.186 |
| 12.0908 | 3073.844 | 86.096 |
| 12.1075 | 3072.016 | 86.030 |
| 12.1242 | 3073.813 | 86.014 |
| 12.1408 | 3073.938 | 85.953 |
| 12.1575 | 3073.434 | 85.948 |
| 12.1742 | 3072.785 | 85.899 |
| 12.1908 | 3074.881 | 85.929 |
| 12.2075 | 3075.575 | 85.893 |
| 12.2242 | 3074.177 | 85.948 |
| 12.2408 | 3074.501 | 85.915 |
| 12.2575 | 3072.843 | 85.983 |
| 12.2742 | 3074.960 | 86.087 |
| 12.2908 | 3074.526 | 86.559 |
| 12.3075 | 3074.018 | 86.202 |
| 12.3242 | 3074.554 | 86.265 |
| 12.3408 | 3073.849 | 86.337 |
| 12.3575 | 3074.641 | 86.391 |
| 12.3742 | 3074.731 | 86.482 |
| 12.3908 | 3075.619 | 86.575 |
| 12.4075 | 3073.700 | 86.462 |
| 12.4242 | 3074.443 | 86.781 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 12.4408 | 3075.559 | 86.577 |
| 12.4575 | 3074.530 | 86.618 |
| 12.4742 | 3074.979 | 86.607 |
| 12.4908 | 3074.833 | 86.575 |
| 12.5075 | 3076.600 | 86.643 |
| 12.5242 | 3075.087 | 86.498 |
| 12.5408 | 3075.438 | 86.064 |
| 12.5575 | 3075.022 | 86.465 |
| 12.5742 | 3075.219 | 86.446 |
| 12.5908 | 3075.122 | 86.367 |
| 12.6075 | 3074.793 | 86.353 |
| 12.6242 | 3046.591 | 86.339 |
| 12.6408 | 3011.372 | 86.287 |
| 12.6433 | 3015.056 | 86.427 |
| 12.6436 | 3015.329 | 86.175 |
| 12.6439 | 3016.249 | 86.435 |
| 12.6442 | 3017.002 | 86.369 |
| 12.6444 | 3017.489 | 86.167 |
| 12.6447 | 3017.918 | 86.735 |
| 12.6450 | 3019.651 | 86.525 |
| 12.6453 | 3020.694 | 86.317 |
| 12.6456 | 3021.832 | 86.484 |
| 12.6458 | 3022.917 | 86.424 |
| 12.6461 | 3023.740 | 86.304 |
| 12.6464 | 3024.128 | 86.296 |
| 12.6467 | 3025.468 | 86.375 |
| 12.6469 | 3026.277 | 86.263 |
| 12.6472 | 3026.679 | 86.337 |
| 12.6475 | 3027.435 | 86.317 |
| 12.6478 | 3028.048 | 86.334 |
| 12.6481 | 3028.619 | 86.328 |
| 12.6483 | 3029.769 | 86.274 |
| 12.6486 | 3030.742 | 86.399 |
| 12.6489 | 3030.997 | 86.293 |
| 12.6492 | 3032.000 | 86.298 |
| 12.6494 | 3032.051 | 86.298 |
| 12.6497 | 3032.223 | 86.326 |
| 12.6500 | 3034.044 | 86.378 |
| 12.6503 | 3034.468 | 86.320 |
| 12.6506 | 3035.256 | 86.309 |
| 12.6508 | 3035.795 | 86.306 |
| 12.6511 | 3035.959 | 86.383 |
| 12.6514 | 3035.105 | 86.304 |
| 12.6517 | 3035.654 | 86.287 |
| 12.6519 | 3036.930 | 86.353 |
| 12.6522 | 3037.325 | 86.304 |
| 12.6525 | 3038.330 | 86.246 |
| 12.6528 | 3037.590 | 86.405 |
| 12.6531 | 3037.941 | 86.326 |
| 12.6533 | 3038.054 | 86.334 |
| 12.6536 | 3037.840 | 86.334 |
| 12.6539 | 3040.107 | 86.290 |
| 12.6542 | 3040.824 | 86.555 |
| 12.6544 | 3041.117 | 86.408 |
| 12.6547 | 3041.216 | 86.290 |
| 12.6550 | 3039.648 | 86.315 |
| 12.6553 | 3039.240 | 86.279 |
| 12.6556 | 3041.112 | 86.304 |
| 12.6558 | 3041.673 | 86.380 |
| 12.6561 | 3042.608 | 86.298 |
| 12.6564 | 3042.223 | 86.331 |
| 12.6567 | 3040.360 | 86.153 |
| 12.6569 | 3041.516 | 86.383 |
| 12.6572 | 3044.474 | 86.410 |
| 12.6575 | 3044.411 | 86.356 |
| 12.6578 | 3043.845 | 86.304 |
| 12.6581 | 3043.241 | 86.317 |
| 12.6583 | 3043.338 | 86.315 |
| 12.6586 | 3043.965 | 86.372 |
| 12.6589 | 3044.060 | 86.282 |
| 12.6592 | 3045.908 | 86.339 |
| 12.6594 | 3046.452 | 86.268 |
| 12.6597 | 3045.627 | 86.421 |
| 12.6600 | 3043.927 | 86.233 |
| 12.6603 | 3044.240 | 86.430 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 12.6606 | 3045.188 | 86.246 |
| 12.6608 | 3047.291 | 86.276 |
| 12.6611 | 3045.929 | 86.350 |
| 12.6614 | 3044.858 | 86.378 |
| 12.6617 | 3046.621 | 86.328 |
| 12.6619 | 3047.507 | 86.263 |
| 12.6622 | 3048.854 | 86.402 |
| 12.6625 | 3047.634 | 86.290 |
| 12.6628 | 3046.591 | 86.309 |
| 12.6631 | 3047.244 | 86.331 |
| 12.6633 | 3049.520 | 86.213 |
| 12.6636 | 3050.042 | 86.416 |
| 12.6639 | 3048.207 | 86.372 |
| 12.6642 | 3046.919 | 86.323 |
| 12.6644 | 3047.677 | 86.241 |
| 12.6647 | 3048.662 | 86.342 |
| 12.6650 | 3049.281 | 86.380 |
| 12.6653 | 3048.211 | 86.265 |
| 12.6656 | 3048.174 | 86.337 |
| 12.6658 | 3049.965 | 86.309 |
| 12.6661 | 3050.420 | 86.361 |
| 12.6664 | 3049.830 | 86.323 |
| 12.6667 | 3049.143 | 86.317 |
| 12.6669 | 3049.823 | 86.293 |
| 12.6672 | 3051.353 | 86.271 |
| 12.6675 | 3051.499 | 86.424 |
| 12.6678 | 3051.413 | 86.339 |
| 12.6681 | 3051.346 | 86.290 |
| 12.6683 | 3049.452 | 86.265 |
| 12.6686 | 3050.276 | 86.378 |
| 12.6689 | 3051.744 | 86.391 |
| 12.6692 | 3050.750 | 86.260 |
| 12.6694 | 3050.261 | 86.326 |
| 12.6697 | 3051.317 | 86.361 |
| 12.6700 | 3051.896 | 86.312 |
| 12.6703 | 3051.111 | 86.331 |
| 12.6706 | 3050.756 | 86.293 |
| 12.6708 | 3052.371 | 86.378 |
| 12.6711 | 3052.109 | 86.282 |
| 12.6714 | 3053.111 | 86.279 |
| 12.6717 | 3053.347 | 86.369 |
| 12.6719 | 3053.159 | 86.345 |
| 12.6722 | 3053.638 | 86.394 |
| 12.6725 | 3053.599 | 86.224 |
| 12.6728 | 3053.090 | 86.298 |
| 12.6731 | 3052.095 | 86.372 |
| 12.6733 | 3052.649 | 86.358 |
| 12.6736 | 3052.337 | 86.282 |
| 12.6739 | 3051.995 | 86.317 |
| 12.6742 | 3052.445 | 86.408 |
| 12.6744 | 3052.358 | 86.375 |
| 12.6747 | 3052.650 | 86.265 |
| 12.6750 | 3053.396 | 86.342 |
| 12.6753 | 3054.092 | 86.285 |
| 12.6756 | 3053.952 | 86.254 |
| 12.6758 | 3055.238 | 86.367 |
| 12.6761 | 3055.096 | 86.369 |
| 12.6764 | 3054.914 | 86.378 |
| 12.6819 | 3057.137 | 86.364 |
| 12.6875 | 3058.577 | 86.345 |
| 12.6931 | 3062.026 | 86.342 |
| 12.6986 | 3064.924 | 86.287 |
| 12.7042 | 3063.784 | 86.361 |
| 12.7097 | 3065.968 | 86.369 |
| 12.7153 | 3068.587 | 86.315 |
| 12.7208 | 3069.581 | 86.293 |
| 12.7264 | 3070.134 | 86.413 |
| 12.7319 | 3068.316 | 86.345 |
| 12.7375 | 3069.079 | 86.389 |
| 12.7431 | 3069.067 | 86.405 |
| 12.7486 | 3068.654 | 86.304 |
| 12.7539 | 3069.175 | 86.181 |
| 12.7706 | 3070.451 | 86.391 |
| 12.7872 | 3072.322 | 86.479 |
| 12.8039 | 3073.071 | 86.740 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 12.8206 | 3074.289 | 86.451 |
| 12.8372 | 3072.556 | 86.479 |
| 12.8539 | 3072.593 | 86.050 |
| 12.8706 | 3072.926 | 86.183 |
| 12.8872 | 3073.772 | 86.629 |
| 12.9039 | 3073.265 | 86.304 |
| 12.9206 | 3072.788 | 86.047 |
| 12.9372 | 3072.335 | 86.156 |
| 12.9539 | 3072.764 | 86.065 |
| 12.9706 | 3073.509 | 86.843 |
| 12.9872 | 3073.217 | 87.037 |
| 13.0039 | 3073.426 | 87.863 |
| 13.0206 | 3074.675 | 87.411 |
| 13.0372 | 3074.774 | 87.626 |
| 13.0539 | 3073.653 | 87.801 |
| 13.0706 | 3072.921 | 88.210 |
| 13.0872 | 3072.715 | 88.682 |
| 13.1039 | 3072.923 | 88.464 |
| 13.1206 | 3072.149 | 88.611 |
| 13.1372 | 3071.611 | 88.580 |
| 13.1539 | 3070.229 | 89.085 |
| 13.1706 | 3070.311 | 89.748 |
| 13.1872 | 3070.243 | 89.762 |
| 13.2039 | 3072.074 | 89.868 |
| 13.2206 | 3071.697 | 90.058 |
| 13.2372 | 3072.195 | 90.240 |
| 13.2539 | 3071.670 | 90.270 |
| 13.2706 | 3070.499 | 90.384 |
| 13.2808 | 3070.002 | 90.443 |
| 13.2811 | 3069.367 | 90.538 |
| 13.2814 | 3070.407 | 90.706 |
| 13.2817 | 3070.317 | 90.639 |
| 13.2819 | 3069.654 | 90.492 |
| 13.2822 | 3069.954 | 90.495 |
| 13.2825 | 3069.402 | 90.457 |
| 13.2828 | 3070.206 | 90.465 |
| 13.2831 | 3071.059 | 90.503 |
| 13.2833 | 3071.066 | 90.121 |
| 13.2836 | 3070.441 | 90.075 |
| 13.2839 | 3070.478 | 90.484 |
| 13.2842 | 3069.869 | 90.378 |
| 13.2844 | 3069.871 | 90.563 |
| 13.2847 | 3070.993 | 90.484 |
| 13.2850 | 3070.322 | 90.541 |
| 13.2853 | 3068.969 | 90.400 |
| 13.2856 | 3069.504 | 90.560 |
| 13.2858 | 3069.268 | 90.441 |
| 13.2861 | 3070.569 | 90.509 |
| 13.2864 | 3069.676 | 90.427 |
| 13.2867 | 3069.070 | 90.606 |
| 13.2869 | 3069.522 | 90.473 |
| 13.2872 | 3069.510 | 90.479 |
| 13.2875 | 3068.922 | 90.479 |
| 13.2878 | 3069.363 | 90.525 |
| 13.2881 | 3068.579 | 90.557 |
| 13.2883 | 3067.832 | 90.433 |
| 13.2886 | 3067.821 | 90.492 |
| 13.2889 | 3068.227 | 90.776 |
| 13.2892 | 3068.537 | 90.536 |
| 13.2894 | 3068.986 | 90.435 |
| 13.2897 | 3069.264 | 90.557 |
| 13.2900 | 3068.574 | 90.471 |
| 13.2903 | 3068.401 | 90.522 |
| 13.2906 | 3068.964 | 90.509 |
| 13.2908 | 3069.057 | 90.503 |
| 13.2911 | 3068.759 | 90.544 |
| 13.2914 | 3069.484 | 90.400 |
| 13.2917 | 3069.204 | 90.595 |
| 13.2919 | 3068.122 | 90.465 |
| 13.2922 | 3069.531 | 90.620 |
| 13.2925 | 3069.530 | 90.500 |
| 13.2928 | 3069.532 | 90.498 |
| 13.2931 | 3069.757 | 90.538 |
| 13.2933 | 3068.249 | 90.593 |
| 13.2936 | 3069.409 | 90.457 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 13.2939 | 3069.575 | 90.528 |
| 13.2942 | 3069.670 | 90.519 |
| 13.2944 | 3069.802 | 94.049 |
| 13.2947 | 3069.184 | 90.259 |
| 13.2950 | 3070.109 | 90.587 |
| 13.2953 | 3069.957 | 90.454 |
| 13.2956 | 3069.531 | 90.536 |
| 13.2958 | 3069.372 | 90.598 |
| 13.2961 | 3068.524 | 90.525 |
| 13.2964 | 3068.657 | 90.487 |
| 13.2967 | 3069.673 | 90.598 |
| 13.2969 | 3069.434 | 90.741 |
| 13.2972 | 3069.800 | 90.568 |
| 13.2975 | 3069.961 | 90.449 |
| 13.2978 | 3069.702 | 90.682 |
| 13.2981 | 3070.522 | 90.465 |
| 13.2983 | 3069.889 | 90.576 |
| 13.2986 | 3070.079 | 90.522 |
| 13.2989 | 3070.661 | 90.568 |
| 13.2992 | 3069.390 | 90.566 |
| 13.2994 | 3069.108 | 90.568 |
| 13.2997 | 3070.416 | 90.460 |
| 13.3000 | 3070.476 | 90.617 |
| 13.3003 | 3069.779 | 90.473 |
| 13.3011 | 3070.461 | 90.506 |
| 13.3014 | 3070.071 | 90.736 |
| 13.3017 | 3070.646 | 90.430 |
| 13.3019 | 3070.682 | 90.571 |
| 13.3022 | 3070.068 | 90.528 |
| 13.3025 | 3070.764 | 90.541 |
| 13.3028 | 3070.467 | 90.655 |
| 13.3031 | 3070.667 | 90.533 |
| 13.3033 | 3070.667 | 90.625 |
| 13.3036 | 3069.729 | 90.509 |
| 13.3039 | 3070.599 | 90.536 |
| 13.3042 | 3070.308 | 90.642 |
| 13.3044 | 3070.141 | 90.528 |
| 13.3047 | 3069.710 | 90.579 |
| 13.3050 | 3069.780 | 90.547 |
| 13.3053 | 3068.718 | 90.568 |
| 13.3056 | 3068.103 | 90.666 |
| 13.3058 | 3068.517 | 90.506 |
| 13.3061 | 3068.611 | 90.582 |
| 13.3064 | 3068.005 | 90.604 |
| 13.3067 | 3069.465 | 90.536 |
| 13.3069 | 3069.089 | 90.666 |
| 13.3072 | 3068.582 | 90.471 |
| 13.3075 | 3068.493 | 90.008 |
| 13.3078 | 3069.941 | 90.511 |
| 13.3081 | 3070.290 | 90.609 |
| 13.3083 | 3071.036 | 90.495 |
| 13.3086 | 3069.990 | 90.560 |
| 13.3089 | 3070.781 | 90.650 |
| 13.3092 | 3071.708 | 90.623 |
| 13.3094 | 3070.735 | 90.595 |
| 13.3097 | 3071.178 | 90.492 |
| 13.3100 | 3071.630 | 90.701 |
| 13.3103 | 3070.523 | 90.650 |
| 13.3106 | 3070.687 | 90.555 |
| 13.3108 | 3071.382 | 90.606 |
| 13.3111 | 3071.364 | 90.593 |
| 13.3114 | 3071.017 | 90.639 |
| 13.3117 | 3071.611 | 90.549 |
| 13.3119 | 3071.335 | 90.582 |
| 13.3122 | 3070.794 | 90.633 |
| 13.3125 | 3071.451 | 90.585 |
| 13.3128 | 3072.054 | 90.669 |
| 13.3131 | 3071.106 | 90.547 |
| 13.3133 | 3071.513 | 90.663 |
| 13.3136 | 3071.556 | 90.647 |
| 13.3139 | 3071.853 | 90.579 |
| 13.3142 | 3072.236 | 90.606 |
| 13.3144 | 3071.521 | 90.552 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|-----------------|------------------|
| 13.3147 | 3071.910 | 90.655 |
| 13.3150 | 3071.950 | 90.614 |
| 13.3153 | 3071.626 | 90.614 |
| 13.3156 | 3071.582 | 90.642 |
| 13.3158 | 3071.233 | 90.617 |
| 13.3161 | 3071.527 | 90.628 |
| 13.3164 | 3072.310 | 90.633 |
| 13.3167 | 3072.359 | 90.806 |
| 13.3169 | 3072.615 | 90.666 |
| 13.3172 | 3073.032 | 90.726 |
| 13.3175 | 3072.551 | 90.525 |
| 13.3178 | 3071.914 | 90.623 |
| 13.3181 | 3071.242 | 90.865 |
| 13.3183 | 3071.472 | 90.669 |
| 13.3186 | 3070.440 | 90.587 |
| 13.3189 | 3071.830 | 90.644 |
| 13.3192 | 3070.719 | 90.606 |
| 13.3194 | 3072.298 | 90.723 |
| 13.3197 | 3071.280 | 90.614 |
| 13.3200 | 3070.990 | 90.571 |
| 13.3203 | 3071.301 | 90.717 |
| 13.3206 | 3072.342 | 90.492 |
| 13.3208 | 3072.041 | 90.723 |
| 13.3211 | 3072.632 | 90.701 |
| 13.3214 | 3072.503 | 90.623 |
| 13.3217 | 3072.404 | 90.617 |
| 13.3219 | 3072.592 | 90.623 |
| 13.3222 | 3071.956 | 90.652 |
| 13.3225 | 3072.437 | 90.631 |
| 13.3228 | 3072.603 | 90.914 |
| 13.3231 | 3072.569 | 90.828 |
| 13.3233 | 3072.177 | 90.755 |
| 13.3236 | 3070.609 | 90.652 |
| 13.3239 | 3071.866 | 90.590 |
| 13.3242 | 3070.756 | 90.717 |
| 13.3244 | 3070.059 | 90.631 |
| 13.3247 | 3071.240 | 90.582 |
| 13.3250 | 3070.960 | 90.720 |
| 13.3253 | 3072.051 | 90.644 |
| 13.3256 | 3072.136 | 90.696 |
| 13.3258 | 3071.254 | 90.536 |
| 13.3261 | 3072.923 | 90.761 |
| 13.3264 | 3071.907 | 90.631 |
| 13.3267 | 3071.183 | 90.644 |
| 13.3269 | 3072.694 | 90.623 |
| 13.3272 | 3073.576 | 90.764 |
| 13.3275 | 3071.804 | 90.669 |
| 13.3278 | 3072.288 | 90.541 |
| 13.3281 | 3072.269 | 90.731 |
| 13.3283 | 3072.280 | 90.717 |
| 13.3286 | 3072.791 | 90.658 |
| 13.3289 | 3073.411 | 90.647 |
| 13.3292 | 3072.596 | 90.671 |
| 13.3294 | 3072.946 | 90.704 |
| 13.3297 | 3072.418 | 90.563 |
| 13.3300 | 3073.240 | 90.723 |
| 13.3303 | 3073.102 | 90.647 |
| 13.3306 | 3072.812 | 90.780 |
| 13.3308 | 3072.222 | 90.487 |
| 13.3311 | 3072.007 | 90.254 |
| 13.3314 | 3072.266 | 90.745 |
| 13.3317 | 3071.675 | 90.701 |
| 13.3319 | 3071.292 | 90.636 |
| 13.3322 | 3071.146 | 90.957 |
| 13.3325 | 3071.188 | 90.628 |
| 13.3328 | 3071.021 | 90.617 |
| 13.3331 | 3070.834 | 90.739 |
| 13.3333 | 3071.907 | 90.677 |
| 13.3336 | 3071.655 | 90.680 |
| 13.3339 | 3072.379 | 90.992 |
| 13.3342 | 3072.880 | 90.612 |
| 13.3344 | 3072.479 | 90.791 |
| 13.3347 | 3072.470 | 90.506 |
| 13.3350 | 3073.574 | 90.812 |
| 13.3353 | 3072.510 | 90.642 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|-----------------|------------------|
| 13.3356 | 3073.063 | 90.723 |
| 13.3358 | 3072.561 | 90.726 |
| 13.3361 | 3072.314 | 90.685 |
| 13.3364 | 3072.953 | 90.704 |
| 13.3367 | 3073.070 | 90.696 |
| 13.3369 | 3072.678 | 90.652 |
| 13.3372 | 3073.070 | 90.742 |
| 13.3375 | 3073.074 | 90.709 |
| 13.3378 | 3072.919 | 90.682 |
| 13.3381 | 3073.368 | 90.655 |
| 13.3383 | 3072.508 | 90.736 |
| 13.3386 | 3072.826 | 90.745 |
| 13.3389 | 3071.836 | 90.938 |
| 13.3392 | 3071.487 | 90.734 |
| 13.3394 | 3071.719 | 90.636 |
| 13.3397 | 3071.895 | 90.693 |
| 13.3400 | 3070.984 | 90.717 |
| 13.3403 | 3072.567 | 90.717 |
| 13.3406 | 3072.669 | 90.709 |
| 13.3408 | 3071.512 | 90.693 |
| 13.3411 | 3072.524 | 90.680 |
| 13.3414 | 3073.234 | 90.758 |
| 13.3417 | 3072.316 | 90.709 |
| 13.3419 | 3073.399 | 90.717 |
| 13.3422 | 3072.999 | 90.693 |
| 13.3425 | 3072.632 | 90.793 |
| 13.3428 | 3072.188 | 90.685 |
| 13.3431 | 3072.635 | 90.734 |
| 13.3433 | 3072.490 | 90.685 |
| 13.3436 | 3073.628 | 90.745 |
| 13.3439 | 3072.609 | 90.693 |
| 13.3442 | 3072.521 | 90.987 |
| 13.3444 | 3073.098 | 90.699 |
| 13.3447 | 3072.117 | 90.952 |
| 13.3450 | 3072.268 | 90.769 |
| 13.3453 | 3072.299 | 90.666 |
| 13.3456 | 3072.048 | 90.777 |
| 13.3458 | 3071.503 | 90.685 |
| 13.3461 | 3073.305 | 90.753 |
| 13.3464 | 3072.059 | 90.690 |
| 13.3467 | 3072.586 | 90.731 |
| 13.3469 | 3071.616 | 90.051 |
| 13.3472 | 3071.948 | 90.663 |
| 13.3475 | 3072.968 | 90.769 |
| 13.3478 | 3073.152 | 90.769 |
| 13.3481 | 3072.666 | 90.650 |
| 13.3483 | 3072.729 | 90.005 |
| 13.3486 | 3072.888 | 90.712 |
| 13.3489 | 3071.948 | 90.821 |
| 13.3492 | 3072.975 | 90.761 |
| 13.3494 | 3071.426 | 90.579 |
| 13.3497 | 3072.203 | 90.804 |
| 13.3500 | 3072.961 | 90.981 |
| 13.3503 | 3072.862 | 90.829 |
| 13.3506 | 3072.838 | 90.701 |
| 13.3508 | 3072.983 | 90.685 |
| 13.3511 | 3073.257 | 90.804 |
| 13.3514 | 3072.966 | 90.726 |
| 13.3517 | 3073.173 | 90.761 |
| 13.3519 | 3072.042 | 90.720 |
| 13.3522 | 3074.347 | 90.766 |
| 13.3525 | 3073.709 | 90.726 |
| 13.3528 | 3072.673 | 90.742 |
| 13.3531 | 3073.166 | 90.761 |
| 13.3533 | 3073.366 | 90.769 |
| 13.3536 | 3073.170 | 90.682 |
| 13.3539 | 3073.973 | 90.875 |
| 13.3542 | 3073.092 | 90.576 |
| 13.3544 | 3073.581 | 90.878 |
| 13.3547 | 3073.711 | 90.807 |
| 13.3550 | 3072.915 | 90.707 |
| 13.3553 | 3073.027 | 90.769 |
| 13.3556 | 3073.229 | 90.747 |
| 13.3558 | 3073.411 | 90.758 |
| 13.3561 | 3072.304 | 90.761 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|-----------------|------------------|
| 13.3564 | 3072.208 | 90.734 |
| 13.3567 | 3072.393 | 90.807 |
| 13.3569 | 3071.941 | 90.736 |
| 13.3572 | 3072.363 | 90.807 |
| 13.3575 | 3072.122 | 90.712 |
| 13.3578 | 3071.525 | 90.723 |
| 13.3581 | 3071.989 | 90.769 |
| 13.3583 | 3071.733 | 90.859 |
| 13.3586 | 3072.027 | 90.766 |
| 13.3589 | 3073.179 | 90.726 |
| 13.3592 | 3071.512 | 90.785 |
| 13.3594 | 3073.951 | 90.755 |
| 13.3597 | 3071.780 | 90.717 |
| 13.3600 | 3071.980 | 90.826 |
| 13.3603 | 3073.267 | 90.745 |
| 13.3606 | 3073.303 | 90.810 |
| 13.3608 | 3073.177 | 90.747 |
| 13.3611 | 3073.146 | 90.804 |
| 13.3614 | 3072.789 | 90.799 |
| 13.3617 | 3072.714 | 90.783 |
| 13.3619 | 3071.960 | 90.750 |
| 13.3622 | 3071.389 | 90.764 |
| 13.3625 | 3071.282 | 90.769 |
| 13.3628 | 3071.109 | 90.902 |
| 13.3631 | 3070.774 | 90.696 |
| 13.3633 | 3070.261 | 90.774 |
| 13.3636 | 3070.659 | 90.728 |
| 13.3639 | 3071.628 | 90.861 |
| 13.3642 | 3071.328 | 90.766 |
| 13.3644 | 3071.444 | 90.769 |
| 13.3647 | 3070.918 | 90.736 |
| 13.3650 | 3071.435 | 90.945 |
| 13.3653 | 3072.828 | 90.704 |
| 13.3656 | 3072.598 | 90.845 |
| 13.3658 | 3071.085 | 90.701 |
| 13.3661 | 3072.975 | 90.880 |
| 13.3664 | 3071.448 | 90.717 |
| 13.3667 | 3070.678 | 90.769 |
| 13.3669 | 3072.225 | 90.842 |
| 13.3672 | 3071.919 | 90.810 |
| 13.3675 | 3070.810 | 90.761 |
| 13.3678 | 3071.555 | 90.804 |
| 13.3681 | 3071.622 | 90.785 |
| 13.3683 | 3071.564 | 90.812 |
| 13.3686 | 3071.424 | 90.008 |
| 13.3689 | 3071.700 | 90.826 |
| 13.3692 | 3071.726 | 90.831 |
| 13.3694 | 3070.622 | 90.747 |
| 13.3697 | 3071.402 | 90.766 |
| 13.3700 | 3070.584 | 90.878 |
| 13.3703 | 3070.550 | 90.745 |
| 13.3706 | 3071.424 | 90.793 |
| 13.3708 | 3070.618 | 90.853 |
| 13.3711 | 3070.915 | 90.796 |
| 13.3714 | 3071.677 | 90.864 |
| 13.3717 | 3070.410 | 90.745 |
| 13.3719 | 3071.514 | 90.736 |
| 13.3722 | 3071.595 | 90.929 |
| 13.3725 | 3070.450 | 90.796 |
| 13.3728 | 3070.915 | 90.804 |
| 13.3731 | 3070.496 | 90.878 |
| 13.3733 | 3070.295 | 90.723 |
| 13.3736 | 3070.061 | 90.850 |
| 13.3739 | 3069.498 | 90.818 |
| 13.3742 | 3069.464 | 90.823 |
| 13.3744 | 3068.753 | 90.856 |
| 13.3747 | 3068.567 | 90.766 |
| 13.3750 | 3069.693 | 90.878 |
| 13.3753 | 3069.207 | 90.777 |
| 13.3756 | 3070.271 | 90.818 |
| 13.3758 | 3070.700 | 90.861 |
| 13.3761 | 3070.093 | 90.755 |
| 13.3764 | 3070.892 | 90.861 |
| 13.3767 | 3070.747 | 90.793 |
| 13.3769 | 3069.943 | 90.869 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 13.3772 | 3070.879 | 90.747 |
| 13.3775 | 3071.741 | 90.840 |
| 13.3778 | 3070.426 | 90.772 |
| 13.3781 | 3070.447 | 90.727 |
| 13.3783 | 3070.613 | 90.490 |
| 13.3786 | 3071.313 | 90.812 |
| 13.3789 | 3070.718 | 90.821 |
| 13.3792 | 3070.975 | 90.859 |
| 13.3794 | 3071.262 | 90.840 |
| 13.3797 | 3070.486 | 90.834 |
| 13.3800 | 3071.297 | 90.796 |
| 13.3803 | 3071.384 | 90.826 |
| 13.3806 | 3070.873 | 90.848 |
| 13.3808 | 3070.546 | 90.842 |
| 13.3811 | 3071.594 | 90.840 |
| 13.3814 | 3070.604 | 90.780 |
| 13.3817 | 3071.435 | 90.918 |
| 13.3819 | 3071.062 | 90.823 |
| 13.3822 | 3071.571 | 90.859 |
| 13.3825 | 3071.262 | 90.812 |
| 13.3828 | 3070.750 | 90.707 |
| 13.3831 | 3070.846 | 90.964 |
| 13.3833 | 3071.309 | 90.864 |
| 13.3836 | 3070.924 | 90.886 |
| 13.3839 | 3071.764 | 90.783 |
| 13.3842 | 3071.922 | 90.861 |
| 13.3844 | 3071.323 | 90.883 |
| 13.3847 | 3071.607 | 90.804 |
| 13.3850 | 3070.648 | 90.880 |
| 13.3853 | 3070.995 | 90.823 |
| 13.3856 | 3070.919 | 90.845 |
| 13.3858 | 3069.965 | 90.878 |
| 13.3861 | 3070.609 | 90.902 |
| 13.3864 | 3071.626 | 90.826 |
| 13.3867 | 3071.226 | 90.867 |
| 13.3869 | 3070.879 | 90.812 |
| 13.3872 | 3071.850 | 90.869 |
| 13.3875 | 3071.864 | 90.842 |
| 13.3878 | 3071.812 | 90.880 |
| 13.3881 | 3071.630 | 90.812 |
| 13.3883 | 3071.161 | 90.883 |
| 13.3886 | 3071.898 | 90.856 |
| 13.3889 | 3071.538 | 90.872 |
| 13.3892 | 3071.067 | 90.872 |
| 13.3894 | 3071.090 | 90.853 |
| 13.3897 | 3070.029 | 90.872 |
| 13.3900 | 3068.561 | 90.848 |
| 13.3903 | 3068.290 | 90.883 |
| 13.3906 | 3066.185 | 90.845 |
| 13.3908 | 3065.160 | 90.875 |
| 13.3911 | 3063.679 | 90.867 |
| 13.3914 | 3062.587 | 90.869 |
| 13.3917 | 3061.271 | 90.867 |
| 13.3919 | 3059.736 | 90.872 |
| 13.3922 | 3058.903 | 90.872 |
| 13.3925 | 3057.352 | 90.869 |
| 13.3928 | 3055.996 | 90.880 |
| 13.3931 | 3055.061 | 90.861 |
| 13.3933 | 3053.468 | 90.875 |
| 13.3936 | 3052.206 | 90.878 |
| 13.3939 | 3051.227 | 90.878 |
| 13.3942 | 3049.744 | 90.872 |
| 13.3944 | 3048.665 | 90.886 |
| 13.3947 | 3047.397 | 90.869 |
| 13.3950 | 3046.087 | 90.878 |
| 13.3953 | 3044.987 | 90.872 |
| 13.3956 | 3043.783 | 90.886 |
| 13.3958 | 3042.563 | 90.875 |
| 13.3961 | 3041.499 | 90.888 |
| 13.3964 | 3040.290 | 90.880 |
| 13.3967 | 3039.149 | 90.880 |
| 13.3969 | 3038.077 | 90.886 |
| 13.3972 | 3036.920 | 90.886 |
| 13.3975 | 3035.850 | 90.880 |
| 13.3978 | 3034.775 | 90.888 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 13.3981 | 3033.661 | 90.883 |
| 13.3983 | 3032.650 | 90.886 |
| 13.3986 | 3031.605 | 90.894 |
| 13.3989 | 3030.531 | 90.883 |
| 13.3992 | 3029.541 | 90.897 |
| 13.3994 | 3028.481 | 90.878 |
| 13.3997 | 3027.510 | 90.894 |
| 13.4000 | 3026.536 | 90.897 |
| 13.4003 | 3025.527 | 90.897 |
| 13.4006 | 3024.527 | 90.878 |
| 13.4008 | 3023.626 | 90.907 |
| 13.4011 | 3022.622 | 90.883 |
| 13.4014 | 3021.716 | 90.902 |
| 13.4017 | 3020.773 | 90.894 |
| 13.4019 | 3019.857 | 90.905 |
| 13.4022 | 3018.929 | 90.897 |
| 13.4025 | 3018.019 | 90.894 |
| 13.4028 | 3017.140 | 90.897 |
| 13.4031 | 3016.289 | 90.910 |
| 13.4033 | 3015.372 | 90.888 |
| 13.4036 | 3014.528 | 90.902 |
| 13.4039 | 3013.694 | 90.905 |
| 13.4042 | 3012.827 | 90.902 |
| 13.4044 | 3012.013 | 90.907 |
| 13.4047 | 3011.157 | 90.891 |
| 13.4050 | 3010.393 | 90.915 |
| 13.4053 | 3009.568 | 90.907 |
| 13.4056 | 3008.742 | 90.899 |
| 13.4058 | 3007.959 | 90.902 |
| 13.4061 | 3007.222 | 90.921 |
| 13.4064 | 3006.424 | 90.915 |
| 13.4067 | 3005.640 | 90.902 |
| 13.4069 | 3004.879 | 90.905 |
| 13.4072 | 3004.163 | 90.915 |
| 13.4075 | 3003.410 | 90.918 |
| 13.4078 | 3002.660 | 90.907 |
| 13.4081 | 3001.946 | 90.915 |
| 13.4083 | 3001.205 | 90.913 |
| 13.4086 | 3000.505 | 90.921 |
| 13.4089 | 2999.763 | 90.902 |
| 13.4092 | 2999.085 | 90.921 |
| 13.4094 | 2998.377 | 90.921 |
| 13.4097 | 2997.673 | 90.918 |
| 13.4100 | 2996.990 | 90.915 |
| 13.4103 | 2996.326 | 90.926 |
| 13.4106 | 2995.643 | 90.924 |
| 13.4108 | 2994.960 | 90.913 |
| 13.4111 | 2994.327 | 90.929 |
| 13.4114 | 2993.680 | 90.929 |
| 13.4117 | 2992.993 | 90.913 |
| 13.4119 | 2992.371 | 90.926 |
| 13.4122 | 2991.738 | 90.926 |
| 13.4125 | 2991.114 | 90.932 |
| 13.4128 | 2990.475 | 90.921 |
| 13.4131 | 2989.851 | 90.918 |
| 13.4133 | 2989.271 | 90.934 |
| 13.4136 | 2988.654 | 90.924 |
| 13.4139 | 2988.091 | 90.945 |
| 13.4142 | 2987.448 | 90.913 |
| 13.4144 | 2986.904 | 90.937 |
| 13.4147 | 2986.342 | 90.940 |
| 13.4150 | 2985.760 | 90.940 |
| 13.4153 | 2985.143 | 90.913 |
| 13.4156 | 2984.662 | 90.951 |
| 13.4158 | 2984.069 | 90.937 |
| 13.4161 | 2983.524 | 90.937 |
| 13.4164 | 2982.951 | 90.918 |
| 13.4167 | 2982.467 | 90.951 |
| 13.4169 | 2981.926 | 90.945 |
| 13.4172 | 2981.393 | 90.940 |
| 13.4175 | 2980.867 | 90.934 |
| 13.4178 | 2980.367 | 90.943 |
| 13.4181 | 2979.861 | 90.948 |
| 13.4183 | 2979.341 | 90.937 |
| 13.4186 | 2978.853 | 90.948 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 13.4189 | 2978.349 | 90.943 |
| 13.4192 | 2977.880 | 90.948 |
| 13.4194 | 2977.377 | 90.943 |
| 13.4197 | 2976.900 | 90.940 |
| 13.4200 | 2976.460 | 90.964 |
| 13.4203 | 2975.983 | 90.953 |
| 13.4206 | 2975.476 | 90.934 |
| 13.4208 | 2975.065 | 90.959 |
| 13.4211 | 2974.611 | 90.956 |
| 13.4214 | 2974.144 | 90.951 |
| 13.4217 | 2973.687 | 90.943 |
| 13.4219 | 2973.285 | 90.956 |
| 13.4222 | 2972.864 | 90.967 |
| 13.4225 | 2972.401 | 90.948 |
| 13.4228 | 2972.004 | 90.964 |
| 13.4231 | 2971.576 | 90.956 |
| 13.4233 | 2971.155 | 90.959 |
| 13.4236 | 2970.767 | 90.964 |
| 13.4239 | 2970.341 | 90.953 |
| 13.4242 | 2969.931 | 90.951 |
| 13.4244 | 2969.589 | 90.981 |
| 13.4247 | 2969.171 | 90.962 |
| 13.4250 | 2968.763 | 90.956 |
| 13.4253 | 2968.385 | 90.959 |
| 13.4256 | 2968.047 | 90.975 |
| 13.4258 | 2967.659 | 90.972 |
| 13.4261 | 2967.243 | 90.951 |
| 13.4264 | 2966.917 | 90.970 |
| 13.4267 | 2966.577 | 90.981 |
| 13.4269 | 2966.213 | 90.975 |
| 13.4272 | 2965.832 | 90.964 |
| 13.4275 | 2965.496 | 90.970 |
| 13.4278 | 2965.155 | 90.972 |
| 13.4281 | 2964.834 | 90.986 |
| 13.4283 | 2964.470 | 90.964 |
| 13.4286 | 2964.146 | 90.972 |
| 13.4289 | 2963.825 | 90.978 |
| 13.4292 | 2963.521 | 90.989 |
| 13.4294 | 2963.160 | 90.962 |
| 13.4297 | 2962.855 | 90.975 |
| 13.4300 | 2962.583 | 90.991 |
| 13.4303 | 2962.263 | 90.986 |
| 13.4306 | 2961.953 | 90.978 |
| 13.4308 | 2961.632 | 90.975 |
| 13.4311 | 2961.380 | 90.994 |
| 13.4314 | 2961.083 | 90.989 |
| 13.4317 | 2960.775 | 90.978 |
| 13.4319 | 2960.496 | 90.986 |
| 13.4322 | 2960.221 | 90.989 |
| 13.4325 | 2959.956 | 90.997 |
| 13.4328 | 2959.653 | 90.981 |
| 13.4331 | 2959.386 | 90.983 |
| 13.4333 | 2959.151 | 91.000 |
| 13.4336 | 2958.871 | 90.991 |
| 13.4339 | 2958.621 | 91.000 |
| 13.4342 | 2958.334 | 90.981 |
| 13.4344 | 2958.097 | 90.991 |
| 13.4347 | 2957.872 | 91.005 |
| 13.4350 | 2957.629 | 91.005 |
| 13.4353 | 2957.345 | 90.983 |
| 13.4356 | 2957.145 | 91.002 |
| 13.4358 | 2956.913 | 91.008 |
| 13.4361 | 2956.667 | 91.002 |
| 13.4364 | 2956.420 | 90.989 |
| 13.4367 | 2956.215 | 91.005 |
| 13.4369 | 2955.984 | 91.000 |
| 13.4372 | 2955.781 | 91.013 |
| 13.4375 | 2955.557 | 91.008 |
| 13.4378 | 2955.316 | 90.997 |
| 13.4381 | 2955.128 | 91.010 |
| 13.4383 | 2954.931 | 91.016 |
| 13.4386 | 2954.705 | 91.005 |
| 13.4389 | 2954.509 | 91.010 |
| 13.4392 | 2954.301 | 91.013 |
| 13.4394 | 2954.116 | 91.013 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 13.4397 | 2953.925 | 91.021 |
| 13.4400 | 2953.693 | 91.000 |
| 13.4403 | 2953.527 | 91.013 |
| 13.4406 | 2953.336 | 91.013 |
| 13.4408 | 2953.205 | 91.046 |
| 13.4411 | 2952.921 | 90.989 |
| 13.4414 | 2952.818 | 91.032 |
| 13.4417 | 2952.609 | 91.019 |
| 13.4419 | 2952.427 | 91.016 |
| 13.4422 | 2952.268 | 91.021 |
| 13.4425 | 2952.075 | 91.013 |
| 13.4428 | 2951.954 | 91.035 |
| 13.4431 | 2951.755 | 91.027 |
| 13.4433 | 2951.618 | 91.032 |
| 13.4436 | 2951.400 | 91.010 |
| 13.4439 | 2951.276 | 91.027 |
| 13.4442 | 2951.147 | 91.040 |
| 13.4444 | 2950.964 | 91.029 |
| 13.4447 | 2950.807 | 91.024 |
| 13.4450 | 2950.645 | 91.024 |
| 13.4453 | 2950.543 | 91.048 |
| 13.4456 | 2950.361 | 91.029 |
| 13.4458 | 2950.216 | 91.035 |
| 13.4461 | 2950.098 | 91.043 |
| 13.4464 | 2949.914 | 91.027 |
| 13.4467 | 2949.801 | 91.037 |
| 13.4469 | 2949.664 | 91.043 |
| 13.4472 | 2949.511 | 91.032 |
| 13.4475 | 2949.404 | 91.054 |
| 13.4478 | 2949.246 | 91.032 |
| 13.4481 | 2949.139 | 91.054 |
| 13.4483 | 2948.978 | 91.035 |
| 13.4486 | 2948.861 | 91.043 |
| 13.4489 | 2948.734 | 91.046 |
| 13.4492 | 2948.630 | 91.054 |
| 13.4494 | 2948.483 | 91.046 |
| 13.4497 | 2948.360 | 91.043 |
| 13.4500 | 2948.238 | 91.048 |
| 13.4503 | 2948.142 | 91.056 |
| 13.4506 | 2948.017 | 91.056 |
| 13.4508 | 2947.879 | 91.046 |
| 13.4511 | 2947.771 | 91.051 |
| 13.4514 | 2947.666 | 91.054 |
| 13.4517 | 2947.568 | 91.065 |
| 13.4519 | 2947.450 | 91.065 |
| 13.4522 | 2947.312 | 91.046 |
| 13.4525 | 2947.231 | 91.062 |
| 13.4528 | 2947.119 | 91.065 |
| 13.4531 | 2946.995 | 91.054 |
| 13.4533 | 2946.895 | 91.059 |
| 13.4536 | 2946.797 | 91.062 |
| 13.4539 | 2946.709 | 91.070 |
| 13.4542 | 2946.599 | 91.070 |
| 13.4544 | 2946.498 | 91.067 |
| 13.4547 | 2946.365 | 91.051 |
| 13.4550 | 2946.307 | 91.075 |
| 13.4553 | 2946.183 | 91.065 |
| 13.4556 | 2946.128 | 91.086 |
| 13.4558 | 2945.977 | 91.056 |
| 13.4561 | 2945.931 | 91.084 |
| 13.4564 | 2945.783 | 91.059 |
| 13.4567 | 2945.750 | 91.089 |
| 13.4569 | 2945.601 | 91.065 |
| 13.4572 | 2945.546 | 91.078 |
| 13.4575 | 2945.438 | 91.075 |
| 13.4578 | 2945.349 | 91.075 |
| 13.4581 | 2945.286 | 91.089 |
| 13.4583 | 2945.160 | 91.073 |
| 13.4586 | 2945.099 | 91.084 |
| 13.4589 | 2945.003 | 91.084 |
| 13.4592 | 2944.918 | 91.089 |
| 13.4594 | 2944.856 | 91.092 |
| 13.4597 | 2944.723 | 91.075 |
| 13.4600 | 2944.662 | 91.086 |
| 13.4603 | 2944.579 | 91.089 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 13.4606 | 2944.488 | 91.084 |
| 13.4608 | 2944.435 | 91.103 |
| 13.4611 | 2944.295 | 91.067 |
| 13.4614 | 2944.273 | 91.103 |
| 13.4617 | 2944.176 | 91.094 |
| 13.4619 | 2944.123 | 91.105 |
| 13.4622 | 2944.010 | 91.092 |
| 13.4625 | 2943.936 | 91.092 |
| 13.4628 | 2943.870 | 91.100 |
| 13.4631 | 2943.814 | 91.113 |
| 13.4633 | 2943.720 | 91.103 |
| 13.4636 | 2943.598 | 91.073 |
| 13.4639 | 2943.579 | 91.113 |
| 13.4642 | 2943.479 | 91.092 |
| 13.4644 | 2943.481 | 91.132 |
| 13.4647 | 2943.292 | 91.078 |
| 13.4650 | 2943.298 | 91.113 |
| 13.4653 | 2943.220 | 91.111 |
| 13.4656 | 2943.098 | 91.089 |
| 13.4658 | 2943.110 | 91.127 |
| 13.4661 | 2942.991 | 91.103 |
| 13.4664 | 2942.912 | 91.100 |
| 13.4667 | 2942.904 | 91.127 |
| 13.4669 | 2942.785 | 91.103 |
| 13.4672 | 2942.749 | 91.119 |
| 13.4675 | 2942.677 | 91.116 |
| 13.4678 | 2942.604 | 91.108 |
| 13.4681 | 2942.572 | 91.127 |
| 13.4683 | 2942.478 | 91.116 |
| 13.4686 | 2942.462 | 91.135 |
| 13.4689 | 2942.361 | 91.116 |
| 13.4692 | 2942.279 | 91.108 |
| 13.4694 | 2942.233 | 91.119 |
| 13.4697 | 2942.227 | 91.143 |
| 13.4700 | 2942.133 | 91.124 |
| 13.4703 | 2942.066 | 91.124 |
| 13.4706 | 2941.977 | 91.108 |
| 13.4708 | 2941.956 | 91.124 |
| 13.4711 | 2941.922 | 91.138 |
| 13.4714 | 2941.868 | 91.141 |
| 13.4717 | 2941.776 | 91.119 |
| 13.4719 | 2941.753 | 91.138 |
| 13.4722 | 2941.696 | 91.135 |
| 13.4725 | 2941.632 | 91.132 |
| 13.4728 | 2941.588 | 91.132 |
| 13.4731 | 2941.549 | 91.143 |
| 13.4733 | 2941.472 | 91.130 |
| 13.4736 | 2941.413 | 91.130 |
| 13.4739 | 2941.415 | 91.154 |
| 13.4742 | 2941.330 | 91.141 |
| 13.4744 | 2941.301 | 91.149 |
| 13.4747 | 2941.219 | 91.132 |
| 13.4750 | 2941.178 | 91.138 |
| 13.4753 | 2941.149 | 91.146 |
| 13.4756 | 2941.100 | 91.151 |
| 13.4758 | 2941.079 | 91.159 |
| 13.4761 | 2940.981 | 91.135 |
| 13.4764 | 2940.920 | 91.130 |
| 13.4767 | 2940.949 | 91.165 |
| 13.4769 | 2940.870 | 91.154 |
| 13.4772 | 2940.853 | 91.165 |
| 13.4775 | 2940.761 | 91.143 |
| 13.4778 | 2940.706 | 91.138 |
| 13.4781 | 2940.700 | 91.162 |
| 13.4783 | 2940.664 | 91.162 |
| 13.4786 | 2940.620 | 91.162 |
| 13.4789 | 2940.558 | 91.157 |
| 13.4792 | 2940.485 | 91.138 |
| 13.4794 | 2940.502 | 91.170 |
| 13.4797 | 2940.453 | 91.168 |
| 13.4800 | 2940.396 | 91.165 |
| 13.4803 | 2940.374 | 91.173 |
| 13.4806 | 2940.285 | 91.149 |
| 13.4808 | 2940.263 | 91.157 |
| 13.4811 | 2940.259 | 91.178 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 13.4814 | 2940.177 | 91.162 |
| 13.4817 | 2940.168 | 91.173 |
| 13.4819 | 2940.129 | 91.176 |
| 13.4822 | 2940.060 | 91.162 |
| 13.4825 | 2940.053 | 91.178 |
| 13.4828 | 2939.999 | 91.173 |
| 13.4831 | 2939.982 | 91.184 |
| 13.4833 | 2939.945 | 91.184 |
| 13.4836 | 2939.835 | 91.149 |
| 13.4839 | 2939.847 | 91.178 |
| 13.4842 | 2939.823 | 91.181 |
| 13.4844 | 2939.788 | 91.187 |
| 13.4847 | 2939.744 | 91.187 |
| 13.4850 | 2939.695 | 91.176 |
| 13.4853 | 2939.652 | 91.173 |
| 13.4856 | 2939.628 | 91.184 |
| 13.4858 | 2939.609 | 91.189 |
| 13.4861 | 2939.575 | 91.195 |
| 13.4864 | 2939.496 | 91.176 |
| 13.4867 | 2939.479 | 91.178 |
| 13.4869 | 2939.465 | 91.195 |
| 13.4872 | 2939.425 | 91.189 |
| 13.4875 | 2939.411 | 91.206 |
| 13.4878 | 2939.366 | 91.197 |
| 13.4881 | 2939.299 | 91.181 |
| 13.4883 | 2939.250 | 91.178 |
| 13.4886 | 2939.293 | 91.214 |
| 13.4889 | 2939.189 | 91.181 |
| 13.4892 | 2939.225 | 91.216 |
| 13.4894 | 2939.153 | 91.197 |
| 13.4897 | 2939.104 | 91.187 |
| 13.4900 | 2939.086 | 91.197 |
| 13.4903 | 2939.055 | 91.200 |
| 13.4906 | 2939.058 | 91.214 |
| 13.4908 | 2938.988 | 91.200 |
| 13.4911 | 2938.976 | 91.206 |
| 13.4914 | 2938.935 | 91.203 |
| 13.4917 | 2938.893 | 91.200 |
| 13.4919 | 2938.898 | 91.219 |
| 13.4922 | 2938.836 | 91.206 |
| 13.4925 | 2938.842 | 91.216 |
| 13.4928 | 2938.772 | 91.203 |
| 13.4931 | 2938.753 | 91.208 |
| 13.4933 | 2938.734 | 91.214 |
| 13.4936 | 2938.692 | 91.211 |
| 13.4939 | 2938.713 | 91.230 |
| 13.4942 | 2938.638 | 91.214 |
| 13.4944 | 2938.605 | 91.208 |
| 13.4947 | 2938.554 | 91.200 |
| 13.4950 | 2938.587 | 91.230 |
| 13.4953 | 2938.550 | 91.230 |
| 13.4956 | 2938.518 | 91.225 |
| 13.4958 | 2938.473 | 91.216 |
| 13.4961 | 2938.449 | 91.219 |
| 13.4964 | 2938.410 | 91.214 |
| 13.4967 | 2938.406 | 91.227 |
| 13.4969 | 2938.409 | 91.241 |
| 13.4972 | 2938.346 | 91.227 |
| 13.4975 | 2938.329 | 91.230 |
| 13.4978 | 2938.280 | 91.219 |
| 13.4981 | 2938.261 | 91.225 |
| 13.4983 | 2938.258 | 91.235 |
| 13.4986 | 2938.240 | 91.241 |
| 13.4989 | 2938.192 | 91.235 |
| 13.4992 | 2938.175 | 91.238 |
| 13.4994 | 2938.113 | 91.216 |
| 13.4997 | 2938.113 | 91.233 |
| 13.5000 | 2938.116 | 91.246 |
| 13.5003 | 2938.117 | 91.262 |
| 13.5006 | 2938.037 | 91.235 |
| 13.5008 | 2938.008 | 91.235 |
| 13.5011 | 2937.980 | 91.233 |
| 13.5014 | 2937.958 | 91.233 |
| 13.5017 | 2937.954 | 91.246 |
| 13.5019 | 2937.930 | 91.249 |

| Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|---------|--------------------|---------------------|---------|--------------------|---------------------|
| 13.5022 | 2937.928 | 91.260 | 13.5519 | 2935.153 | 91.420 | 13.7111 | 2932.555 | 91.994 |
| 13.5025 | 2937.879 | 91.249 | 13.5533 | 2935.137 | 91.447 | 13.7153 | 2932.523 | 92.004 |
| 13.5028 | 2937.852 | 91.246 | 13.5547 | 2935.086 | 91.447 | 13.7194 | 2932.497 | 92.010 |
| 13.5031 | 2937.797 | 91.233 | 13.5561 | 2935.052 | 91.460 | 13.7236 | 2932.450 | 92.013 |
| 13.5033 | 2937.812 | 91.249 | 13.5575 | 2934.968 | 91.447 | 13.7278 | 2932.426 | 92.031 |
| 13.5036 | 2937.801 | 91.262 | 13.5589 | 2934.949 | 91.460 | 13.7319 | 2932.377 | 92.029 |
| 13.5039 | 2937.763 | 91.254 | 13.5603 | 2934.890 | 91.460 | 13.7361 | 2932.343 | 92.034 |
| 13.5042 | 2937.767 | 91.268 | 13.5617 | 2934.883 | 91.485 | 13.7403 | 2932.334 | 92.053 |
| 13.5044 | 2937.664 | 91.225 | 13.5631 | 2934.802 | 91.468 | 13.7444 | 2932.282 | 92.053 |
| 13.5047 | 2937.695 | 91.257 | 13.5644 | 2934.785 | 91.487 | 13.7486 | 2932.270 | 92.067 |
| 13.5050 | 2937.673 | 91.257 | 13.5658 | 2934.691 | 91.468 | 13.7528 | 2932.236 | 92.072 |
| 13.5053 | 2937.656 | 91.260 | 13.5672 | 2934.677 | 91.485 | 13.7569 | 2932.192 | 92.072 |
| 13.5056 | 2937.646 | 91.271 | 13.5686 | 2934.636 | 91.490 | 13.7611 | 2932.190 | 92.091 |
| 13.5058 | 2937.619 | 91.268 | 13.5700 | 2934.581 | 91.485 | 13.7653 | 2932.151 | 92.094 |
| 13.5061 | 2937.547 | 91.241 | 13.5714 | 2934.565 | 91.504 | 13.7694 | 2932.131 | 92.099 |
| 13.5064 | 2937.549 | 91.254 | 13.5728 | 2934.541 | 91.514 | 13.7736 | 2932.090 | 92.096 |
| 13.5067 | 2937.538 | 91.260 | 13.5742 | 2934.479 | 91.509 | 13.7778 | 2932.080 | 92.115 |
| 13.5069 | 2937.515 | 91.260 | 13.5756 | 2934.448 | 91.520 | 13.7819 | 2932.058 | 92.123 |
| 13.5072 | 2937.516 | 91.276 | 13.5769 | 2934.416 | 91.523 | 13.7861 | 2932.051 | 92.140 |
| 13.5075 | 2937.489 | 91.273 | 13.5783 | 2934.375 | 91.528 | 13.7903 | 2932.037 | 92.148 |
| 13.5078 | 2937.469 | 91.271 | 13.5797 | 2934.346 | 91.536 | 13.7944 | 2932.023 | 92.156 |
| 13.5081 | 2937.410 | 91.254 | 13.5811 | 2934.329 | 91.547 | 13.7986 | 2931.978 | 92.156 |
| 13.5083 | 2937.405 | 91.260 | 13.5825 | 2934.302 | 91.552 | 13.8028 | 2931.969 | 92.167 |
| 13.5086 | 2937.406 | 91.276 | 13.5839 | 2934.273 | 91.560 | 13.8069 | 2931.949 | 92.172 |
| 13.5089 | 2937.376 | 91.268 | 13.5853 | 2934.216 | 91.558 | 13.8111 | 2931.917 | 92.175 |
| 13.5092 | 2937.392 | 91.292 | 13.5867 | 2934.194 | 91.566 | 13.8153 | 2931.878 | 92.178 |
| 13.5094 | 2937.316 | 91.260 | 13.5881 | 2934.180 | 91.574 | 13.8194 | 2931.851 | 92.175 |
| 13.5097 | 2937.317 | 91.276 | 13.5894 | 2934.133 | 91.577 | 13.8236 | 2931.817 | 92.180 |
| 13.5100 | 2937.280 | 91.268 | 13.5908 | 2934.094 | 91.579 | 13.8278 | 2931.797 | 92.186 |
| 13.5103 | 2937.275 | 91.273 | 13.5922 | 2934.060 | 91.585 | 13.8319 | 2931.790 | 92.202 |
| 13.5106 | 2937.264 | 91.279 | 13.5936 | 2934.003 | 91.574 | 13.8361 | 2931.778 | 92.207 |
| 13.5108 | 2937.257 | 91.287 | 13.5950 | 2934.012 | 91.598 | 13.8403 | 2931.772 | 92.224 |
| 13.5111 | 2937.235 | 91.287 | 13.5964 | 2933.959 | 91.590 | 13.8444 | 2931.732 | 92.218 |
| 13.5114 | 2937.187 | 91.273 | 13.5978 | 2933.943 | 91.601 | 13.8486 | 2931.727 | 92.232 |
| 13.5117 | 2937.180 | 91.281 | 13.5992 | 2933.931 | 91.615 | 13.8528 | 2931.716 | 92.245 |
| 13.5119 | 2937.150 | 91.273 | 13.6006 | 2933.867 | 91.596 | 13.8569 | 2931.684 | 92.240 |
| 13.5122 | 2937.143 | 91.281 | 13.6019 | 2933.883 | 91.628 | 13.8611 | 2931.692 | 92.264 |
| 13.5125 | 2937.137 | 91.290 | 13.6033 | 2933.836 | 91.623 | 13.8653 | 2931.662 | 92.264 |
| 13.5128 | 2937.122 | 91.298 | 13.6047 | 2933.809 | 91.628 | 13.8694 | 2931.632 | 92.264 |
| 13.5131 | 2937.089 | 91.284 | 13.6061 | 2933.809 | 91.644 | 13.8736 | 2931.591 | 92.261 |
| 13.5133 | 2937.062 | 91.281 | 13.6075 | 2933.775 | 91.650 | 13.8778 | 2931.609 | 92.283 |
| 13.5136 | 2937.016 | 91.276 | 13.6089 | 2933.740 | 91.647 | 13.8819 | 2931.554 | 92.270 |
| 13.5139 | 2937.026 | 91.281 | 13.6103 | 2933.714 | 91.653 | 13.8861 | 2931.565 | 92.291 |
| 13.5142 | 2937.031 | 91.300 | 13.6117 | 2933.687 | 91.658 | 13.8903 | 2931.573 | 92.307 |
| 13.5144 | 2936.979 | 91.284 | 13.6131 | 2933.668 | 91.663 | 13.8944 | 2931.533 | 92.302 |
| 13.5147 | 2937.009 | 91.309 | 13.6144 | 2933.641 | 91.669 | 13.8986 | 2931.544 | 92.324 |
| 13.5150 | 2936.962 | 91.295 | 13.6158 | 2933.632 | 91.680 | 13.9028 | 2931.486 | 92.305 |
| 13.5153 | 2936.920 | 91.284 | 13.6172 | 2933.605 | 91.685 | 13.9069 | 2931.512 | 92.334 |
| 13.5156 | 2936.926 | 91.295 | 13.6186 | 2933.575 | 91.685 | 13.9111 | 2931.463 | 92.324 |
| 13.5158 | 2936.881 | 91.287 | 13.6200 | 2933.556 | 91.690 | 13.9153 | 2931.456 | 92.332 |
| 13.5172 | 2936.817 | 91.300 | 13.6214 | 2933.540 | 91.701 | 13.9181 | 2931.440 | 92.332 |
| 13.5186 | 2936.735 | 91.311 | 13.6228 | 2933.510 | 91.701 | 13.9264 | 2931.421 | 92.345 |
| 13.5200 | 2936.641 | 91.309 | 13.6242 | 2933.490 | 91.707 | 13.9347 | 2931.395 | 92.359 |
| 13.5214 | 2936.558 | 91.311 | 13.6256 | 2933.483 | 91.715 | 13.9431 | 2931.338 | 92.356 |
| 13.5228 | 2936.462 | 91.311 | 13.6269 | 2933.466 | 91.726 | 13.9514 | 2931.346 | 92.388 |
| 13.5242 | 2936.409 | 91.330 | 13.6278 | 2933.442 | 91.720 | 13.9597 | 2931.290 | 92.378 |
| 13.5256 | 2936.333 | 91.333 | 13.6319 | 2933.394 | 91.742 | 13.9681 | 2931.258 | 92.388 |
| 13.5269 | 2936.247 | 91.330 | 13.6361 | 2933.330 | 91.755 | 13.9764 | 2931.256 | 92.416 |
| 13.5283 | 2936.176 | 91.336 | 13.6403 | 2933.254 | 91.758 | 13.9825 | 2931.199 | 92.397 |
| 13.5297 | 2936.128 | 91.349 | 13.6444 | 2933.246 | 91.801 | 13.9908 | 2931.185 | 92.413 |
| 13.5311 | 2936.051 | 91.352 | 13.6486 | 2933.187 | 91.810 | 13.9992 | 2931.188 | 92.434 |
| 13.5325 | 2935.985 | 91.360 | 13.6528 | 2933.129 | 91.818 | 14.0075 | 2931.141 | 92.437 |
| 13.5339 | 2935.927 | 91.368 | 13.6569 | 2933.048 | 91.818 | 14.0158 | 2931.110 | 92.440 |
| 13.5353 | 2935.838 | 91.360 | 13.6611 | 2932.994 | 91.828 | 14.0242 | 2931.103 | 92.464 |
| 13.5367 | 2935.785 | 91.371 | 13.6653 | 2932.968 | 91.850 | 14.0325 | 2931.100 | 92.483 |
| 13.5381 | 2935.689 | 91.363 | 13.6694 | 2932.946 | 91.875 | 14.0408 | 2931.051 | 92.472 |
| 13.5394 | 2935.672 | 91.390 | 13.6736 | 2932.871 | 91.877 | 14.0492 | 2931.049 | 92.491 |
| 13.5408 | 2935.604 | 91.393 | 13.6778 | 2932.844 | 91.891 | 14.0575 | 2930.987 | 92.478 |
| 13.5422 | 2935.553 | 91.401 | 13.6819 | 2932.782 | 91.893 | 14.0658 | 2930.986 | 92.497 |
| 13.5436 | 2935.489 | 91.398 | 13.6861 | 2932.774 | 91.921 | 14.0742 | 2930.973 | 92.510 |
| 13.5450 | 2935.443 | 91.409 | 13.6903 | 2932.753 | 91.945 | 14.0825 | 2930.919 | 92.505 |
| 13.5464 | 2935.407 | 91.425 | 13.6944 | 2932.689 | 91.962 | 14.0908 | 2930.909 | 92.516 |
| 13.5478 | 2935.315 | 91.411 | 13.6986 | 2932.677 | 91.964 | 14.0992 | 2930.913 | 92.537 |
| 13.5492 | 2935.302 | 91.436 | 13.7028 | 2932.638 | 91.975 | 14.1075 | 2930.854 | 92.529 |
| 13.5506 | 2935.232 | 91.430 | 13.7069 | 2932.566 | 91.964 | 14.1158 | 2930.846 | 92.545 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 14.1242 | 2930.802 | 92.537 |
| 14.1325 | 2930.815 | 92.564 |
| 14.1408 | 2930.778 | 92.564 |
| 14.1492 | 2930.758 | 92.570 |
| 14.1575 | 2930.752 | 92.586 |
| 14.1658 | 2930.754 | 92.599 |
| 14.1742 | 2930.720 | 92.597 |
| 14.1825 | 2930.678 | 92.594 |
| 14.1908 | 2930.706 | 92.621 |
| 14.1992 | 2930.649 | 92.610 |
| 14.2075 | 2930.634 | 92.618 |
| 14.2158 | 2930.588 | 92.613 |
| 14.2242 | 2930.580 | 92.621 |
| 14.2325 | 2930.566 | 92.629 |
| 14.2408 | 2930.531 | 92.626 |
| 14.2492 | 2930.534 | 92.648 |
| 14.2575 | 2930.549 | 92.672 |
| 14.2658 | 2930.552 | 92.686 |
| 14.2742 | 2930.483 | 92.672 |
| 14.2825 | 2930.439 | 92.664 |
| 14.2908 | 2930.474 | 92.699 |
| 14.2992 | 2930.477 | 92.721 |
| 14.3075 | 2930.462 | 92.729 |
| 14.3158 | 2930.475 | 92.764 |
| 14.3242 | 2930.411 | 92.745 |
| 14.3325 | 2930.367 | 92.745 |
| 14.3408 | 2930.360 | 92.761 |
| 14.3492 | 2930.395 | 92.797 |
| 14.3575 | 2930.341 | 92.783 |
| 14.3658 | 2930.323 | 92.786 |
| 14.3742 | 2930.336 | 92.805 |
| 14.3825 | 2930.259 | 92.783 |
| 14.3908 | 2930.297 | 92.824 |
| 14.3992 | 2930.265 | 92.818 |
| 14.4075 | 2930.236 | 92.818 |
| 14.4158 | 2930.273 | 92.851 |
| 14.4242 | 2930.249 | 92.853 |
| 14.4325 | 2930.224 | 92.856 |
| 14.4408 | 2930.209 | 92.864 |
| 14.4492 | 2930.185 | 92.875 |
| 14.4575 | 2930.190 | 92.894 |
| 14.4658 | 2930.158 | 92.888 |
| 14.4742 | 2930.181 | 92.913 |
| 14.4825 | 2930.119 | 92.899 |
| 14.4908 | 2930.127 | 92.915 |
| 14.4992 | 2930.114 | 92.921 |
| 14.5075 | 2930.105 | 92.932 |
| 14.5158 | 2930.118 | 92.951 |
| 14.5242 | 2930.059 | 92.934 |
| 14.5325 | 2930.058 | 92.942 |
| 14.5408 | 2930.047 | 92.956 |
| 14.5492 | 2930.049 | 92.969 |
| 14.5575 | 2930.030 | 92.975 |
| 14.5658 | 2930.012 | 92.978 |
| 14.5742 | 2930.037 | 93.007 |
| 14.5825 | 2930.015 | 93.007 |
| 14.5908 | 2929.976 | 93.002 |
| 14.5992 | 2930.008 | 93.032 |
| 14.6075 | 2929.967 | 93.021 |
| 14.6158 | 2929.974 | 93.045 |
| 14.6242 | 2929.967 | 93.053 |
| 14.6325 | 2929.907 | 93.037 |
| 14.6408 | 2929.888 | 93.034 |
| 14.6492 | 2929.865 | 93.042 |
| 14.6575 | 2929.874 | 93.067 |
| 14.6658 | 2929.898 | 93.096 |
| 14.6742 | 2929.926 | 93.131 |
| 14.6825 | 2929.857 | 93.110 |
| 14.6908 | 2929.869 | 93.137 |
| 14.6992 | 2929.835 | 93.134 |
| 14.7075 | 2929.848 | 93.161 |
| 14.7158 | 2929.870 | 93.185 |
| 14.7242 | 2929.863 | 93.202 |
| 14.7325 | 2929.816 | 93.196 |
| 14.7408 | 2929.780 | 93.188 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 14.7492 | 2929.787 | 93.212 |
| 14.7575 | 2929.802 | 93.237 |
| 14.7658 | 2929.794 | 93.245 |
| 14.7742 | 2929.795 | 93.261 |
| 14.7825 | 2929.776 | 93.266 |
| 14.7908 | 2929.739 | 93.258 |
| 14.7992 | 2929.711 | 93.264 |
| 14.8075 | 2929.741 | 93.288 |
| 14.8158 | 2929.734 | 93.296 |
| 14.8242 | 2929.744 | 93.318 |
| 14.8325 | 2929.737 | 93.326 |
| 14.8408 | 2929.690 | 93.320 |
| 14.8492 | 2929.702 | 93.339 |
| 14.8575 | 2929.710 | 93.355 |
| 14.8658 | 2929.690 | 93.361 |
| 14.8742 | 2929.683 | 93.369 |
| 14.8825 | 2929.671 | 93.374 |
| 14.8908 | 2929.671 | 93.391 |
| 14.8992 | 2929.651 | 93.396 |
| 14.9075 | 2929.659 | 93.412 |
| 14.9158 | 2929.624 | 93.409 |
| 14.9242 | 2929.632 | 93.426 |
| 14.9325 | 2929.646 | 93.450 |
| 14.9408 | 2929.625 | 93.450 |
| 14.9492 | 2929.622 | 93.461 |
| 14.9533 | 2929.590 | 93.447 |
| 14.9700 | 2929.652 | 93.517 |
| 14.9867 | 2929.605 | 93.520 |
| 15.0033 | 2929.588 | 93.539 |
| 15.0200 | 2929.598 | 93.569 |
| 15.0264 | 2929.524 | 93.544 |
| 15.0431 | 2929.535 | 93.582 |
| 15.0597 | 2929.495 | 93.593 |
| 15.0764 | 2929.495 | 93.633 |
| 15.0931 | 2929.500 | 93.668 |
| 15.1097 | 2929.498 | 93.703 |
| 15.1264 | 2929.466 | 93.714 |
| 15.1431 | 2929.496 | 93.771 |
| 15.1597 | 2929.459 | 93.795 |
| 15.1764 | 2929.422 | 93.811 |
| 15.1931 | 2929.412 | 93.838 |
| 15.2097 | 2929.402 | 93.873 |
| 15.2264 | 2929.400 | 93.908 |
| 15.2431 | 2929.410 | 93.954 |
| 15.2597 | 2929.397 | 94.000 |
| 15.2764 | 2929.371 | 94.022 |
| 15.2931 | 2929.380 | 94.076 |
| 15.3097 | 2929.357 | 94.108 |
| 15.3264 | 2929.362 | 94.159 |
| 15.3431 | 2929.318 | 94.183 |
| 15.3597 | 2929.330 | 94.243 |
| 15.3764 | 2929.346 | 94.305 |
| 15.3931 | 2929.352 | 94.356 |
| 15.4097 | 2929.300 | 94.380 |
| 15.4264 | 2929.284 | 94.428 |
| 15.4431 | 2929.310 | 94.488 |
| 15.4597 | 2929.266 | 94.504 |
| 15.4764 | 2929.263 | 94.539 |
| 15.4931 | 2929.292 | 94.587 |
| 15.5097 | 2929.250 | 94.617 |
| 15.5264 | 2929.249 | 94.649 |
| 15.5431 | 2929.249 | 94.681 |
| 15.5597 | 2929.266 | 94.743 |
| 15.5764 | 2929.230 | 94.781 |
| 15.5931 | 2929.244 | 94.846 |
| 15.6097 | 2929.214 | 94.886 |
| 15.6264 | 2929.204 | 94.921 |
| 15.6431 | 2929.203 | 94.945 |
| 15.6597 | 2929.222 | 94.964 |
| 15.6764 | 2929.198 | 94.967 |
| 15.6931 | 2929.197 | 94.991 |
| 15.7097 | 2929.192 | 95.012 |
| 15.7264 | 2929.169 | 95.029 |
| 15.7431 | 2929.178 | 95.058 |
| 15.7597 | 2929.173 | 95.080 |

| Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|
| 15.7764 | 2929.175 | 95.101 |
| 15.7931 | 2929.149 | 95.160 |
| 15.8097 | 2929.159 | 95.252 |
| 15.8264 | 2929.128 | 95.332 |
| 15.8431 | 2929.106 | 95.402 |
| 15.8597 | 2929.083 | 95.459 |
| 15.8764 | 2929.095 | 95.531 |
| 15.8931 | 2929.101 | 95.580 |
| 15.9097 | 2929.110 | 95.625 |
| 15.9264 | 2929.104 | 95.663 |
| 15.9431 | 2929.112 | 95.709 |
| 15.9597 | 2929.154 | 95.773 |
| 15.9764 | 2929.106 | 95.808 |
| 15.9931 | 2929.051 | 95.851 |
| 16.0097 | 2929.066 | 95.913 |
| 16.0264 | 2929.008 | 95.942 |
| 16.0431 | 2928.961 | 96.015 |
| 16.0597 | 2928.970 | 96.168 |
| 16.0764 | 2928.959 | 96.302 |
| 16.0931 | 2928.970 | 96.398 |
| 16.1097 | 2928.983 | 96.468 |
| 16.1264 | 2929.030 | 96.535 |
| 16.1431 | 2929.050 | 96.575 |
| 16.1597 | 2929.071 | 96.600 |
| 16.1764 | 2929.063 | 96.600 |
| 16.1931 | 2929.006 | 96.567 |
| 16.2097 | 2929.017 | 96.648 |
| 16.2264 | 2928.983 | 96.720 |
| 16.2431 | 2928.968 | 96.790 |
| 16.2597 | 2929.011 | 96.851 |
| 16.2764 | 2929.035 | 96.881 |
| 16.2931 | 2929.026 | 96.905 |
| 16.3097 | 2929.044 | 96.932 |
| 16.3264 | 2929.015 | 96.916 |
| 16.3431 | 2929.023 | 96.916 |
| 16.3597 | 2928.985 | 96.894 |
| 16.3764 | 2929.009 | 96.908 |
| 16.3931 | 2929.040 | 96.913 |
| 16.4097 | 2929.016 | 96.892 |
| 16.4264 | 2929.015 | 96.841 |
| 16.4431 | 2928.954 | 96.774 |
| 16.4597 | 2929.056 | 96.843 |
| 16.4764 | 2928.976 | 96.827 |
| 16.4931 | 2928.930 | 96.843 |
| 16.5097 | 2928.960 | 96.897 |
| 16.5264 | 2928.909 | 96.926 |
| 16.5431 | 2928.883 | 97.036 |
| 16.5597 | 2928.848 | 97.170 |
| 16.5764 | 2928.859 | 97.310 |
| 16.5931 | 2928.814 | 97.409 |
| 16.6097 | 2928.822 | 97.529 |
| 16.6264 | 2928.850 | 97.612 |
| 16.6431 | 2928.871 | 97.636 |
| 16.6597 | 2928.902 | 97.657 |
| 16.6764 | 2928.897 | 97.647 |
| 16.6931 | 2928.889 | 97.625 |
| 16.7097 | 2928.845 | 97.639 |
| 16.7264 | 2928.887 | 97.724 |
| 16.7431 | 2928.841 | 97.786 |
| 16.7597 | 2928.819 | 97.853 |
| 16.7764 | 2928.828 | 97.895 |
| 16.7931 | 2928.825 | 97.936 |
| 16.8097 | 2928.823 | 97.930 |
| 16.8264 | 2928.859 | 97.909 |
| 16.8431 | 2928.886 | 97.845 |
| 16.8597 | 2928.908 | 97.778 |
| 16.8764 | 2928.874 | 97.692 |
| 16.8931 | 2928.862 | 97.660 |
| 16.9097 | 2928.803 | 97.660 |
| 16.9264 | 2928.821 | 97.708 |
| 16.9431 | 2928.798 | 97.732 |
| 16.9597 | 2928.779 | 97.751 |
| 16.9764 | 2928.808 | 97.797 |
| 16.9931 | 2928.766 | 97.831 |
| 17.0097 | 2928.750 | 97.914 |

| Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|---------|--------------------|---------------------|---------|--------------------|---------------------|
| 17.0264 | 2928.783 | 97.970 | 18.2658 | 2928.583 | 98.825 | 19.5147 | 2928.435 | 99.932 |
| 17.0431 | 2928.787 | 98.010 | 18.2825 | 2928.605 | 98.855 | 19.5314 | 2928.454 | 99.934 |
| 17.0597 | 2928.756 | 98.064 | 18.2992 | 2928.583 | 98.884 | 19.5481 | 2928.407 | 99.916 |
| 17.0764 | 2928.758 | 98.166 | 18.3158 | 2928.583 | 98.913 | 19.5647 | 2928.425 | 99.927 |
| 17.0931 | 2928.716 | 98.267 | 18.3325 | 2928.571 | 98.940 | 19.5814 | 2928.479 | 99.910 |
| 17.1097 | 2928.730 | 98.371 | 18.3492 | 2928.536 | 98.967 | 19.5981 | 2928.476 | 99.892 |
| 17.1264 | 2928.758 | 98.425 | 18.3658 | 2928.542 | 98.991 | 19.6147 | 2928.462 | 99.913 |
| 17.1431 | 2928.803 | 98.446 | 18.3825 | 2928.542 | 98.991 | 19.6314 | 2928.445 | 99.929 |
| 17.1597 | 2928.802 | 98.417 | 18.3992 | 2928.576 | 99.007 | 19.6481 | 2928.432 | 99.934 |
| 17.1764 | 2928.798 | 98.414 | 18.4158 | 2928.563 | 98.999 | 19.6647 | 2928.484 | 99.956 |
| 17.1931 | 2928.799 | 98.406 | 18.4325 | 2928.530 | 98.980 | 19.6814 | 2928.513 | 99.977 |
| 17.2097 | 2928.779 | 98.411 | 18.4492 | 2928.552 | 99.039 | 19.6981 | 2928.432 | 99.956 |
| 17.2264 | 2928.802 | 98.417 | 18.4658 | 2928.537 | 99.089 | 19.7147 | 2928.460 | 99.993 |
| 17.2431 | 2928.824 | 98.395 | 18.4814 | 2928.558 | 99.097 | 19.7314 | 2928.490 | 99.993 |
| 17.2597 | 2928.790 | 98.393 | 18.4981 | 2928.573 | 99.097 | 19.7481 | 2928.478 | 100.004 |
| 17.2764 | 2928.757 | 98.433 | 18.5147 | 2928.564 | 99.084 | 19.7647 | 2928.386 | 100.036 |
| 17.2931 | 2928.722 | 98.497 | 18.5314 | 2928.527 | 99.063 | 19.7814 | 2928.400 | 100.129 |
| 17.3097 | 2928.739 | 98.540 | 18.5481 | 2928.540 | 99.087 | 19.7981 | 2928.448 | 100.246 |
| 17.3264 | 2928.768 | 98.540 | 18.5647 | 2928.574 | 99.119 | 19.8147 | 2928.387 | 100.283 |
| 17.3431 | 2928.785 | 98.516 | 18.5814 | 2928.529 | 99.119 | 19.8314 | 2928.404 | 100.331 |
| 17.3597 | 2928.759 | 98.438 | 18.5981 | 2928.562 | 99.167 | 19.8481 | 2928.464 | 100.374 |
| 17.3764 | 2928.758 | 98.358 | 18.6147 | 2928.544 | 99.177 | 19.8647 | 2928.409 | 100.411 |
| 17.3931 | 2928.744 | 98.313 | 18.6314 | 2928.563 | 99.188 | 19.8814 | 2928.403 | 100.509 |
| 17.4097 | 2928.746 | 98.296 | 18.6481 | 2928.540 | 99.167 | 19.8981 | 2928.447 | 100.595 |
| 17.4264 | 2928.741 | 98.264 | 18.6647 | 2928.582 | 99.170 | 19.9147 | 2928.392 | 100.605 |
| 17.4431 | 2928.722 | 98.232 | 18.6814 | 2928.507 | 99.177 | 19.9314 | 2928.428 | 100.712 |
| 17.4597 | 2928.731 | 98.200 | 18.6981 | 2928.538 | 99.255 | 19.9481 | 2928.442 | 100.754 |
| 17.4764 | 2928.700 | 98.166 | 18.7147 | 2928.538 | 99.263 | 19.9647 | 2928.437 | 100.738 |
| 17.4931 | 2928.681 | 98.184 | 18.7314 | 2928.493 | 99.271 | 19.9814 | 2928.480 | 100.746 |
| 17.5097 | 2928.693 | 98.187 | 18.7481 | 2928.530 | 99.300 | 19.9981 | 2928.508 | 100.741 |
| 17.5264 | 2928.704 | 98.168 | 18.7647 | 2928.557 | 99.316 | 20.0147 | 2928.440 | 100.693 |
| 17.5431 | 2928.701 | 98.171 | 18.7814 | 2928.522 | 99.322 | 20.0314 | 2928.427 | 100.733 |
| 17.5597 | 2928.731 | 98.141 | 18.7981 | 2928.509 | 99.407 | 20.0481 | 2928.433 | 100.770 |
| 17.5764 | 2928.716 | 98.149 | 18.8147 | 2928.497 | 99.497 | 20.0647 | 2928.419 | 100.783 |
| 17.5931 | 2928.694 | 98.208 | 18.8314 | 2928.498 | 99.540 | 20.0814 | 2928.447 | 100.813 |
| 17.6097 | 2928.674 | 98.243 | 18.8481 | 2928.498 | 99.612 | 20.0981 | 2928.467 | 100.794 |
| 17.6264 | 2928.642 | 98.305 | 18.8647 | 2928.536 | 99.676 | 20.1147 | 2928.446 | 100.743 |
| 17.6431 | 2928.663 | 98.379 | 18.8814 | 2928.524 | 99.695 | 20.1314 | 2928.470 | 100.693 |
| 17.6597 | 2928.676 | 98.403 | 18.8981 | 2928.521 | 99.676 | 20.1481 | 2928.481 | 100.661 |
| 17.6764 | 2928.659 | 98.398 | 18.9147 | 2928.508 | 99.681 | 20.1647 | 2928.492 | 100.629 |
| 17.6931 | 2928.637 | 98.435 | 18.9314 | 2928.452 | 99.721 | 20.1814 | 2928.464 | 100.571 |
| 17.7097 | 2928.644 | 98.494 | 18.9481 | 2928.487 | 99.852 | 20.1981 | 2928.486 | 100.557 |
| 17.7158 | 2928.624 | 98.521 | 18.9647 | 2928.488 | 99.937 | 20.2147 | 2928.460 | 100.525 |
| 17.7325 | 2928.663 | 98.585 | 18.9814 | 2928.476 | 99.985 | 20.2314 | 2928.478 | 100.536 |
| 17.7492 | 2928.646 | 98.588 | 18.9981 | 2928.509 | 99.996 | 20.2481 | 2928.480 | 100.563 |
| 17.7658 | 2928.680 | 98.561 | 19.0147 | 2928.472 | 99.932 | 20.2647 | 2928.459 | 100.597 |
| 17.7825 | 2928.680 | 98.532 | 19.0314 | 2928.487 | 99.966 | 20.2814 | 2928.385 | 100.597 |
| 17.7992 | 2928.676 | 98.529 | 19.0481 | 2928.492 | 99.948 | 20.2981 | 2928.428 | 100.648 |
| 17.8158 | 2928.624 | 98.588 | 19.0647 | 2928.508 | 99.961 | 20.3147 | 2928.419 | 100.664 |
| 17.8325 | 2928.615 | 98.692 | 19.0814 | 2928.517 | 100.009 | 20.3314 | 2928.400 | 100.696 |
| 17.8492 | 2928.629 | 98.759 | 19.0981 | 2928.456 | 100.004 | 20.3481 | 2928.443 | 100.767 |
| 17.8658 | 2928.640 | 98.799 | 19.1147 | 2928.473 | 100.030 | 20.3647 | 2928.448 | 100.762 |
| 17.8825 | 2928.608 | 98.801 | 19.1314 | 2928.490 | 100.006 | 20.3814 | 2928.372 | 100.786 |
| 17.8992 | 2928.614 | 98.788 | 19.1481 | 2928.499 | 99.977 | 20.3981 | 2928.386 | 100.884 |
| 17.9158 | 2928.652 | 98.772 | 19.1647 | 2928.518 | 99.937 | 20.4147 | 2928.427 | 100.951 |
| 17.9325 | 2928.652 | 98.743 | 19.1814 | 2928.510 | 99.852 | 20.4314 | 2928.425 | 100.932 |
| 17.9492 | 2928.660 | 98.764 | 19.1981 | 2928.522 | 99.804 | 20.4481 | 2928.445 | 100.906 |
| 17.9658 | 2928.586 | 98.823 | 19.2147 | 2928.575 | 99.796 | 20.4647 | 2928.447 | 100.890 |
| 17.9825 | 2928.595 | 98.916 | 19.2314 | 2928.477 | 99.719 | 20.4814 | 2928.455 | 100.868 |
| 17.9992 | 2928.609 | 98.953 | 19.2481 | 2928.515 | 99.711 | 20.4981 | 2928.458 | 100.866 |
| 18.0158 | 2928.621 | 98.927 | 19.2647 | 2928.521 | 99.727 | 20.5147 | 2928.423 | 100.948 |
| 18.0325 | 2928.662 | 98.908 | 19.2814 | 2928.517 | 99.716 | 20.5314 | 2928.378 | 101.047 |
| 18.0492 | 2928.644 | 98.889 | 19.2981 | 2928.479 | 99.724 | 20.5481 | 2928.387 | 101.150 |
| 18.0658 | 2928.653 | 98.903 | 19.3147 | 2928.487 | 99.716 | 20.5647 | 2928.411 | 101.190 |
| 18.0825 | 2928.664 | 98.884 | 19.3314 | 2928.454 | 99.684 | 20.5814 | 2928.412 | 101.225 |
| 18.0992 | 2928.668 | 98.873 | 19.3481 | 2928.501 | 99.703 | 20.5981 | 2928.430 | 101.227 |
| 18.1158 | 2928.638 | 98.852 | 19.3647 | 2928.452 | 99.679 | 20.6147 | 2928.453 | 101.227 |
| 18.1325 | 2928.611 | 98.871 | 19.3814 | 2928.506 | 99.727 | 20.6314 | 2928.445 | 101.193 |
| 18.1492 | 2928.529 | 98.879 | 19.3981 | 2928.454 | 99.684 | 20.6481 | 2928.455 | 101.155 |
| 18.1658 | 2928.617 | 98.916 | 19.4147 | 2928.463 | 99.711 | 20.6647 | 2928.474 | 101.145 |
| 18.1825 | 2928.625 | 98.879 | 19.4314 | 2928.492 | 99.761 | 20.6814 | 2928.451 | 101.089 |
| 18.1992 | 2928.596 | 98.849 | 19.4481 | 2928.458 | 99.801 | 20.6981 | 2928.469 | 101.031 |
| 18.2158 | 2928.587 | 98.865 | 19.4647 | 2928.420 | 99.817 | 20.7147 | 2928.479 | 101.028 |
| 18.2325 | 2928.577 | 98.868 | 19.4814 | 2928.429 | 99.823 | 20.7314 | 2928.442 | 101.070 |
| 18.2492 | 2928.622 | 98.868 | 19.4981 | 2928.441 | 99.897 | 20.7481 | 2928.409 | 101.094 |

| Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) | Time | Pressure (Psia) | Temperature (°F) |
|---------|--------------------|---------------------|---------|--------------------|---------------------|---------|--------------------|---------------------|
| 20.7647 | 2928.421 | 101.166 | 22.0147 | 2928.415 | 103.541 | 23.4411 | 85.526 | 85.027 |
| 20.7814 | 2928.409 | 101.206 | 22.0314 | 2928.435 | 103.536 | 23.4494 | 85.494 | 84.783 |
| 20.7981 | 2928.396 | 101.211 | 22.0481 | 2928.441 | 103.530 | 23.4578 | 85.449 | 84.560 |
| 20.8147 | 2928.423 | 101.248 | 22.0647 | 2928.461 | 103.485 | 23.4661 | 85.433 | 84.382 |
| 20.8314 | 2928.436 | 101.264 | 22.0814 | 2928.449 | 103.443 | 23.4744 | 85.419 | 84.217 |
| 20.8481 | 2928.411 | 101.267 | 22.0981 | 2928.446 | 103.419 | 23.4828 | 85.384 | 84.052 |
| 20.8647 | 2928.445 | 101.339 | 22.1147 | 2928.447 | 103.525 | 23.4911 | 85.372 | 83.906 |
| 20.8814 | 2928.432 | 101.365 | 22.1314 | 2928.375 | 103.610 | 23.4994 | 85.356 | 83.774 |
| 20.8981 | 2928.431 | 101.331 | 22.1481 | 2928.393 | 103.673 | 23.5078 | 85.333 | 83.651 |
| 20.9147 | 2928.475 | 101.317 | 22.1647 | 2928.393 | 103.734 | 23.5161 | 85.325 | 83.554 |
| 20.9314 | 2928.462 | 101.344 | 22.1814 | 2928.421 | 103.795 | 23.5244 | 85.316 | 83.458 |
| 20.9481 | 2928.406 | 101.410 | 22.1981 | 2928.425 | 103.758 | 23.5269 | 85.313 | 83.428 |
| 20.9647 | 2928.394 | 101.541 | 22.2147 | 2928.440 | 103.744 | 23.5283 | 85.301 | 83.398 |
| 20.9814 | 2928.377 | 101.618 | 22.2314 | 2928.438 | 103.713 | 23.5339 | 83.839 | 86.632 |
| 20.9981 | 2928.382 | 101.620 | 22.2481 | 2928.442 | 103.702 | 23.5353 | 82.457 | 86.807 |
| 21.0147 | 2928.434 | 101.607 | 22.2647 | 2928.470 | 103.697 | 23.5367 | 80.235 | 85.931 |
| 21.0314 | 2928.464 | 101.599 | 22.2814 | 2928.416 | 103.660 | 23.5381 | 79.278 | 86.640 |
| 21.0481 | 2928.405 | 101.633 | 22.2981 | 2928.415 | 103.747 | 23.5394 | 75.037 | 83.340 |
| 21.0647 | 2928.406 | 101.716 | 22.3147 | 2928.374 | 103.784 | 23.5408 | 73.573 | 83.398 |
| 21.0814 | 2928.413 | 101.750 | 22.3314 | 2928.364 | 103.840 | 23.5422 | 72.016 | 83.337 |
| 21.0981 | 2928.408 | 101.769 | 22.3481 | 2928.420 | 103.921 | 23.5436 | 70.467 | 83.296 |
| 21.1147 | 2928.407 | 101.846 | 22.3647 | 2928.430 | 103.932 | 23.5450 | 68.907 | 83.232 |
| 21.1314 | 2928.456 | 101.883 | 22.3814 | 2928.391 | 103.948 | 23.5464 | 67.458 | 83.307 |
| 21.1481 | 2928.432 | 101.947 | 22.3981 | 2928.397 | 104.035 | 23.5478 | 65.966 | 83.331 |
| 21.1647 | 2928.410 | 101.994 | 22.4147 | 2928.374 | 104.122 | 23.5492 | 64.377 | 83.243 |
| 21.1814 | 2928.412 | 102.047 | 22.4314 | 2928.354 | 104.212 | 23.5533 | 59.712 | 83.070 |
| 21.1981 | 2928.428 | 102.066 | 22.4481 | 2928.354 | 104.304 | 23.5561 | 56.716 | 83.097 |
| 21.2147 | 2928.430 | 102.045 | 22.4647 | 2928.411 | 104.326 | 23.5589 | 53.779 | 83.142 |
| 21.2314 | 2928.479 | 102.013 | 22.4814 | 2928.453 | 104.289 | 23.5603 | 52.276 | 83.144 |
| 21.2481 | 2928.459 | 101.976 | 22.4981 | 2928.419 | 104.194 | 23.5617 | 50.721 | 83.086 |
| 21.2647 | 2928.455 | 101.952 | 22.5147 | 2928.449 | 104.141 | 23.5644 | 47.538 | 82.902 |
| 21.2814 | 2928.440 | 101.939 | 22.5314 | 2928.446 | 104.091 | 23.5658 | 46.125 | 83.020 |
| 21.2981 | 2928.431 | 101.933 | 22.5481 | 2928.409 | 104.104 | 23.5672 | 44.639 | 83.053 |
| 21.3147 | 2928.433 | 101.952 | 22.5647 | 2928.360 | 104.101 | 23.5686 | 43.036 | 82.938 |
| 21.3314 | 2928.447 | 101.973 | 22.5814 | 2928.426 | 104.101 | 23.5756 | 35.452 | 82.935 |
| 21.3481 | 2928.403 | 101.973 | 22.5981 | 2928.395 | 104.056 | 23.5769 | 33.793 | 82.761 |
| 21.3647 | 2928.380 | 102.016 | 22.6147 | 2909.964 | 104.386 | 23.5797 | 30.942 | 82.979 |
| 21.3814 | 2928.395 | 102.098 | 22.6208 | 2889.494 | 104.885 | 23.5811 | 29.313 | 82.841 |
| 21.3981 | 2928.385 | 102.148 | 22.7767 | 2051.202 | 105.796 | 23.5825 | 27.830 | 82.885 |
| 21.4147 | 2928.388 | 102.172 | 22.7850 | 2051.117 | 105.415 | 23.5839 | 26.189 | 82.734 |
| 21.4314 | 2928.418 | 102.220 | 22.7933 | 2051.041 | 105.040 | 23.5853 | 24.766 | 82.841 |
| 21.4481 | 2928.425 | 102.241 | 22.8017 | 2050.997 | 104.721 | 23.5867 | 23.335 | 82.949 |
| 21.4647 | 2928.452 | 102.222 | 22.8100 | 2050.933 | 104.415 | 23.5881 | 21.688 | 82.789 |
| 21.4814 | 2928.446 | 102.201 | 22.8183 | 2050.896 | 104.159 | 23.5894 | 20.172 | 82.794 |
| 21.4981 | 2928.476 | 102.193 | 22.8267 | 2050.861 | 103.927 | 23.5908 | 18.675 | 82.814 |
| 21.5147 | 2928.366 | 102.233 | 22.8350 | 2050.813 | 103.697 | 23.5922 | 17.123 | 82.767 |
| 21.5314 | 2928.406 | 102.381 | 22.8433 | 2050.780 | 103.506 | 23.5936 | 15.603 | 82.759 |
| 21.5481 | 2928.385 | 102.456 | 22.8517 | 2050.720 | 103.313 | 23.5950 | 14.123 | 82.800 |
| 21.5647 | 2928.377 | 102.538 | 22.8600 | 2050.720 | 103.171 | 23.5964 | 14.123 | 82.808 |
| 21.5814 | 2928.384 | 102.585 | 22.8683 | 2050.680 | 103.020 | 23.5978 | 14.123 | 82.731 |
| 21.5981 | 2928.454 | 102.596 | 22.8767 | 2050.665 | 102.893 | 23.5992 | 14.123 | 82.819 |
| 21.6147 | 2928.431 | 102.570 | 22.8850 | 2050.661 | 102.792 | 23.5997 | 14.123 | 82.818 |
| 21.6314 | 2928.407 | 102.577 | 22.8933 | 2050.630 | 102.670 | | | |
| 21.6481 | 2928.463 | 102.628 | 22.8964 | 2050.609 | 102.628 | | | |
| 21.6647 | 2928.431 | 102.609 | 23.1733 | 680.106 | 91.531 | | | |
| 21.6814 | 2928.415 | 102.577 | 23.1817 | 680.042 | 91.124 | | | |
| 21.6981 | 2928.430 | 102.617 | 23.1900 | 679.972 | 90.728 | | | |
| 21.7147 | 2928.393 | 102.652 | 23.1983 | 679.937 | 90.408 | | | |
| 21.7314 | 2928.393 | 102.699 | 23.2067 | 679.880 | 90.082 | | | |
| 21.7481 | 2928.421 | 102.816 | 23.2150 | 679.814 | 89.786 | | | |
| 21.7647 | 2928.403 | 102.927 | 23.2233 | 679.770 | 89.528 | | | |
| 21.7814 | 2928.376 | 103.033 | 23.2317 | 679.731 | 89.291 | | | |
| 21.7981 | 2928.347 | 103.186 | 23.2400 | 679.708 | 89.093 | | | |
| 21.8147 | 2928.350 | 103.345 | 23.2483 | 679.678 | 88.902 | | | |
| 21.8314 | 2928.334 | 103.432 | 23.2567 | 679.647 | 88.725 | | | |
| 21.8481 | 2928.428 | 103.501 | 23.2650 | 679.740 | 88.570 | | | |
| 21.8647 | 2928.449 | 103.496 | 23.2733 | 679.716 | 88.445 | | | |
| 21.8814 | 2928.434 | 103.469 | 23.2817 | 679.704 | 88.316 | | | |
| 21.8981 | 2928.433 | 103.451 | 23.2900 | 679.684 | 88.197 | | | |
| 21.9147 | 2928.445 | 103.406 | 23.2983 | 679.667 | 88.093 | | | |
| 21.9314 | 2928.454 | 103.358 | 23.3067 | 679.658 | 87.997 | | | |
| 21.9481 | 2928.450 | 103.361 | 23.3150 | 679.623 | 87.886 | | | |
| 21.9647 | 2928.449 | 103.395 | 23.3233 | 679.621 | 87.812 | | | |
| 21.9814 | 2928.397 | 103.430 | 23.4244 | 85.500 | 85.570 | | | |
| 21.9981 | 2928.426 | 103.504 | 23.4328 | 85.556 | 85.296 | | | |

APPENDIX 4.1.2-1

**PANSYSTEM2 VERSION 2.5, WELL TEST ANALYSIS REPORT,
WDW-1**

ENVIROCORPENVIROCORP SERVICES
AND TECHNOLOGY, INC.HOUSTON, TX - SOUTH BEND, IN
BATON ROUGE, LA

Envirocorp Services & Technology, Inc.

PanSystem Version 2.5

Well Test Analysis Report

Report File:

WDW1.PAN

Analysis Date:

9/15/1998

| | |
|------------------------|------------------------------------|
| Company | Navajo Refining Company |
| Location | Artesia, New Mexico |
| Well | WDW-1 |
| Test Type | Injection/Falloff |
| Test Date | July 30 - 31, 1998 |
| Gauge Type/Serial # | Eccossetex/009 |
| Gauge Depth | 7924 Feet |
| Injection Interval | 7924 - 8115 Feet; 8220 - 8476 Feet |
| Completion Type | Perforated |
| Top of Fill | 8997 Feet |
| Last Stabilization | New Completion |
| Analyst | LKM |
| Envirocorp Project No. | 70A4614 |

Reservoir Description

Fluid type : Water

Well orientation : Vertical

Number of wells : 1

Number of layers : 1

Layer Parameters Data

| | Layer 1 |
|------------------------------|-----------------|
| Formation thickness | 253.00 ft |
| Average formation porosity | 0.10 |
| Water saturation | 0.00 |
| Gas saturation | 0.00 |
| Formation compressibility | 0.0000 psi-1 |
| Total system compressibility | 8.4000e-6 psi-1 |
| Layer pressure | 2925.3599 psia |
| Temperature | 0.0000 deg F |

Well Parameters Data

| | WDW-1 |
|--|----------------|
| Well radius | 0.3696 ft |
| Distance from observation to active well | 0.0000 ft |
| Wellbore storage coefficient | 0.1038 bbl/psi |
| Well offset - x direction | 0.00 ft |
| Well offset - y direction | 0.00 ft |

Fluid Parameters Data

| | Layer 1 |
|-----------------------------|----------------|
| Oil gravity | 0.0000 API |
| Gas gravity | 0.0000 sp grav |
| Gas-oil ratio (produced) | 0.0000 scf/STB |
| Water cut | 0.0000 |
| Water salinity | 0.0000 ppm |
| Check Pressure | 0.0000 psia |
| Check Temperature | 0.0000 deg F |
| Gas-oil ratio (solution) | 0.0000 scf/STB |
| Bubble-point pressure | 0.0000 psia |
| Oil density | 0.000 lb/ft3 |
| Oil viscosity | 0.000 cp |
| Oil formation volume factor | 0.000 RB/STB |



ENVIROCORP SERVICES
AND TECHNOLOGY, INC.
HOUSTON, TX - SOUTH BEND, IN
BATON ROUGE, LA

Envirocorp Services & Technology, Inc.

PanSystem Version 2.5

Well Test Analysis Report

Report File:

WDW1.PAN

Analysis Date:

9/15/1998

Fluid Parameters Data (cont)

| | Layer 1 |
|-------------------------------|---------------|
| Gas density | 0.000 lb/ft3 |
| Gas viscosity | 0.0 cp |
| Gas formation volume factor | 0.000 ft3/scf |
| Water density | 0.000 lb/ft3 |
| Water viscosity | 0.530 cp |
| Water formation volume factor | 1.000 RB/STB |
| Oil compressibility | 0.0000 psi-1 |
| Initial Gas compressibility | 0.0000 psi-1 |
| Water compressibility | 0.0000 psi-1 |

Layer 1 Correlations

Not Used


Layer 1 Model Data


Layer 1 Model Type : Radial homogeneous

| | Layer 1 |
|----------------------|------------|
| Permeability | 1130.00 md |
| Skin factor (Well 1) | 30.1678 |

Rate Change Data

| Time | Pressure | Rate |
|----------|-----------|-----------|
| Hours | psia | gpm |
| 0.71330 | 2928.2310 | 0.0000 |
| 12.60750 | 3074.7930 | -420.0000 |
| 12.64080 | 3011.3721 | -200.0000 |
| 13.38939 | 3071.6079 | -420.0000 |
| 22.59810 | 2928.3950 | 0.0000 |

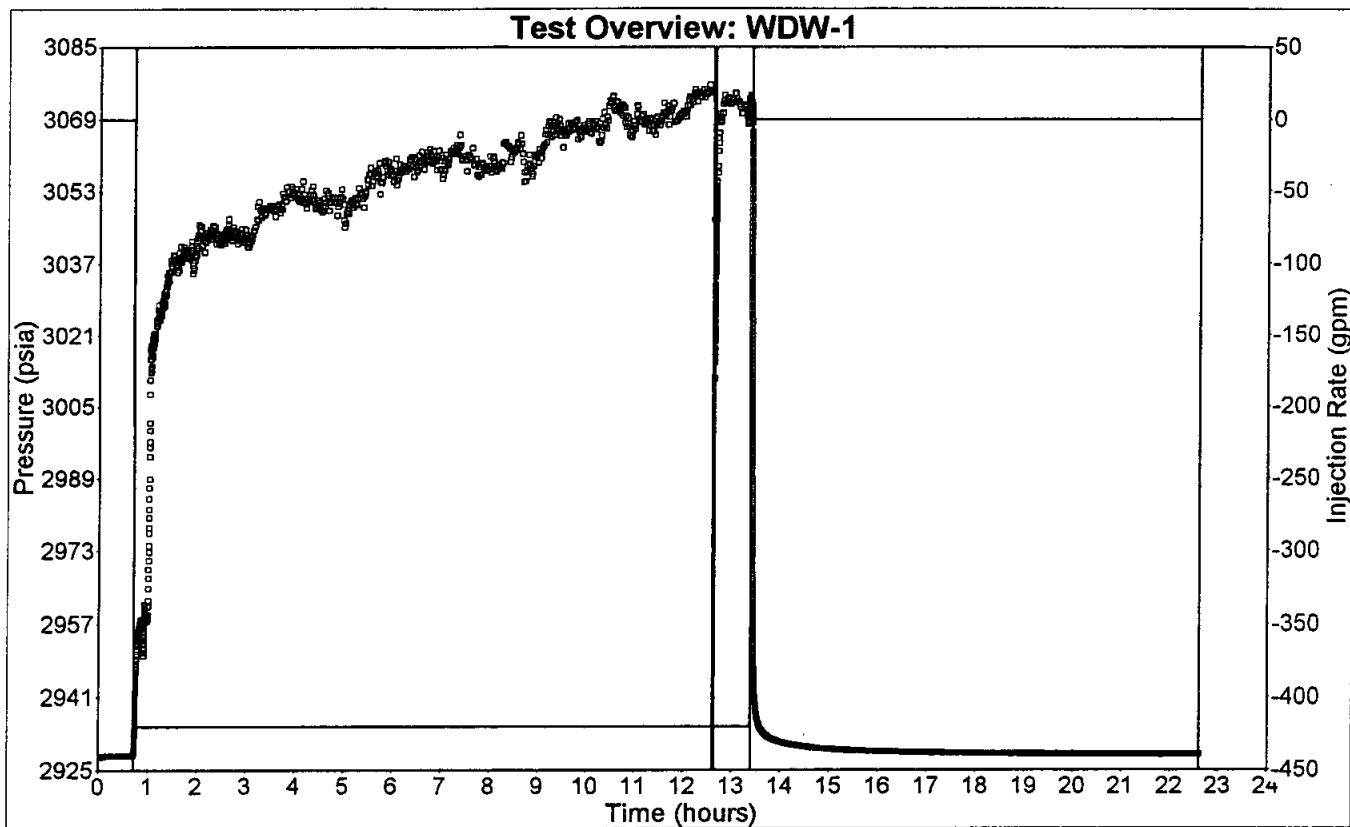

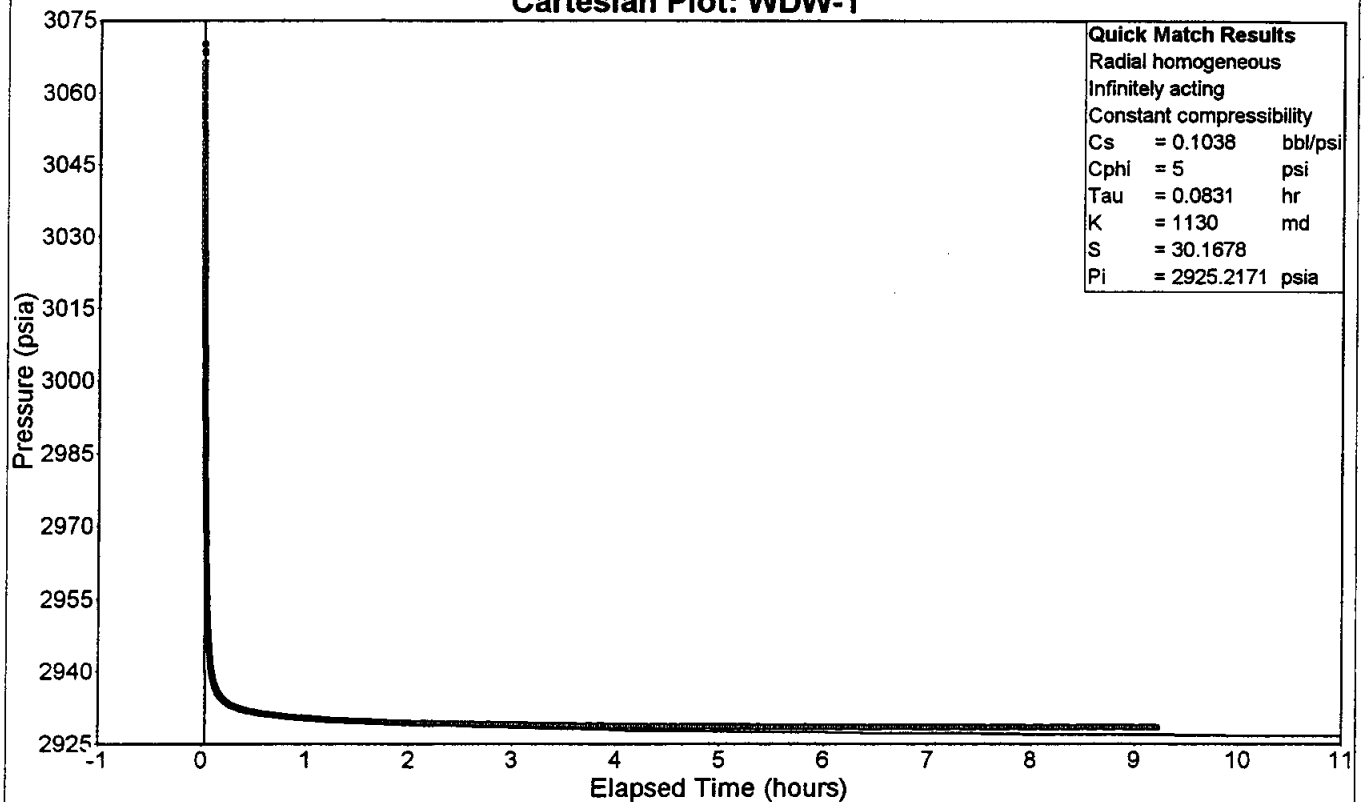Cartesian Plot: WDW-1

Cartesian Plot: WDW-1 Model Results

Radial homogeneous

Infinitely acting

| | Value |
|--------------------------------|----------------|
| Wellbore storage coefficient | 0.1309 bbl/psi |
| Dimensionless wellbore storage | 1035.9075 |

Cartesian Plot: WDW-1 Line Details


Line type : Wellbore storage

Slope : -4582.2

Intercept : 3071.68

Coefficient of Determination : 0.997527

Number of Intersections = 0

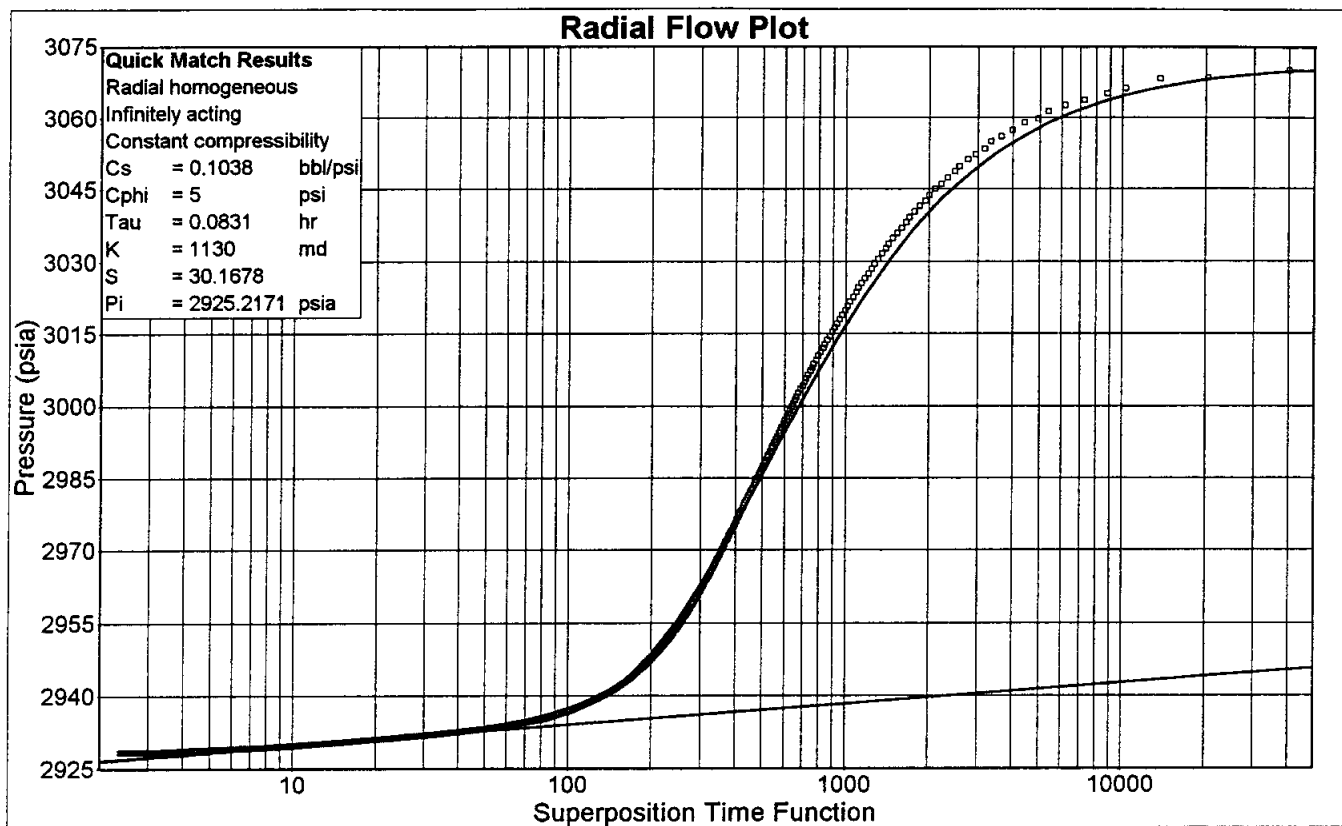

Radial Flow Plot Model Results

Radial homogeneous

Infinitely acting

| | Value |
|-------------------------|----------------|
| Permeability | 1125.5867 md |
| Permeability-thickness | 2.8477e5 md.ft |
| Radius of investigation | 4424.9595 ft |
| Flow efficiency | 0.2247 |
| dP skin (constant rate) | 113.3868 psi |
| Skin factor | 29.9633 |
| Extrapolated pressure | 2925.3599 psia |

Radial Flow Plot Line Details

Line type : Radial flow

Slope : 4.35671

Intercept : 2925.36

Coefficient of Determination : 0.996956



Envirocorp Services
and Technology, Inc.

Houston, TX - South Bend, IN
Baton Rouge, LA

Envirocorp Services & Technology, Inc.

PanSystem Version 2.5

Well Test Analysis Report

Report File:


WDW1.PAN

Analysis Date:

9/15/1998

| | Radial flow |
|-------------------------|----------------|
| Extrapolated pressure | 2925.3599 psia |
| Pressure at dt = 1 hour | 2930.2690 psia |

Number of Intersections = 0

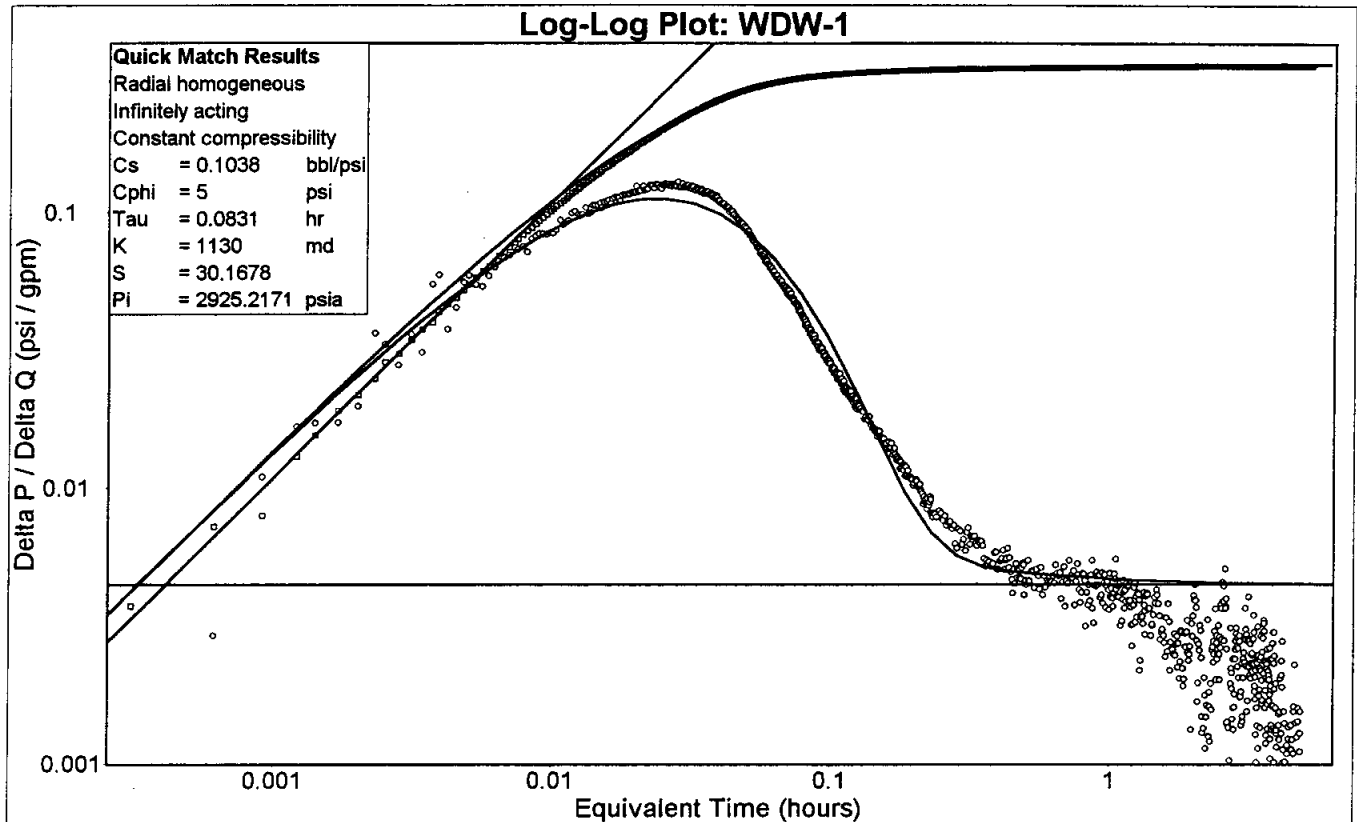
Log-Log Plot: WDW-1 Model Results

Radial homogeneous

Infinitely acting

| | Value |
|--------------------------------|----------------|
| Wellbore storage coefficient | 0.1305 bbl/psi |
| Dimensionless wellbore storage | 1032.4241 |
| Permeability | 1130.6444 md |
| Permeability-thickness | 2.8605e5 md.ft |
| Skin factor | 30.1285 |

Log-Log Plot: WDW-1 Line Details

Line type : Radial flow

Slope : 0

Intercept : 0.00448484

Coefficient of Determination : Not Used

Line type : Wellbore storage

Slope : 1

Intercept : 10.9468

Coefficient of Determination : Not Used



ENVIROCORP SERVICES
AND TECHNOLOGY, INC.
HOUSTON, TX - SOUTH BEND, IN
BATON ROUGE, LA

Envirocorp Services & Technology, Inc.

PanSystem Version 2.5

Well Test Analysis Report


Report File:

WDW1.PAN

Analysis Date:

9/15/1998

Number of Intersections = 0

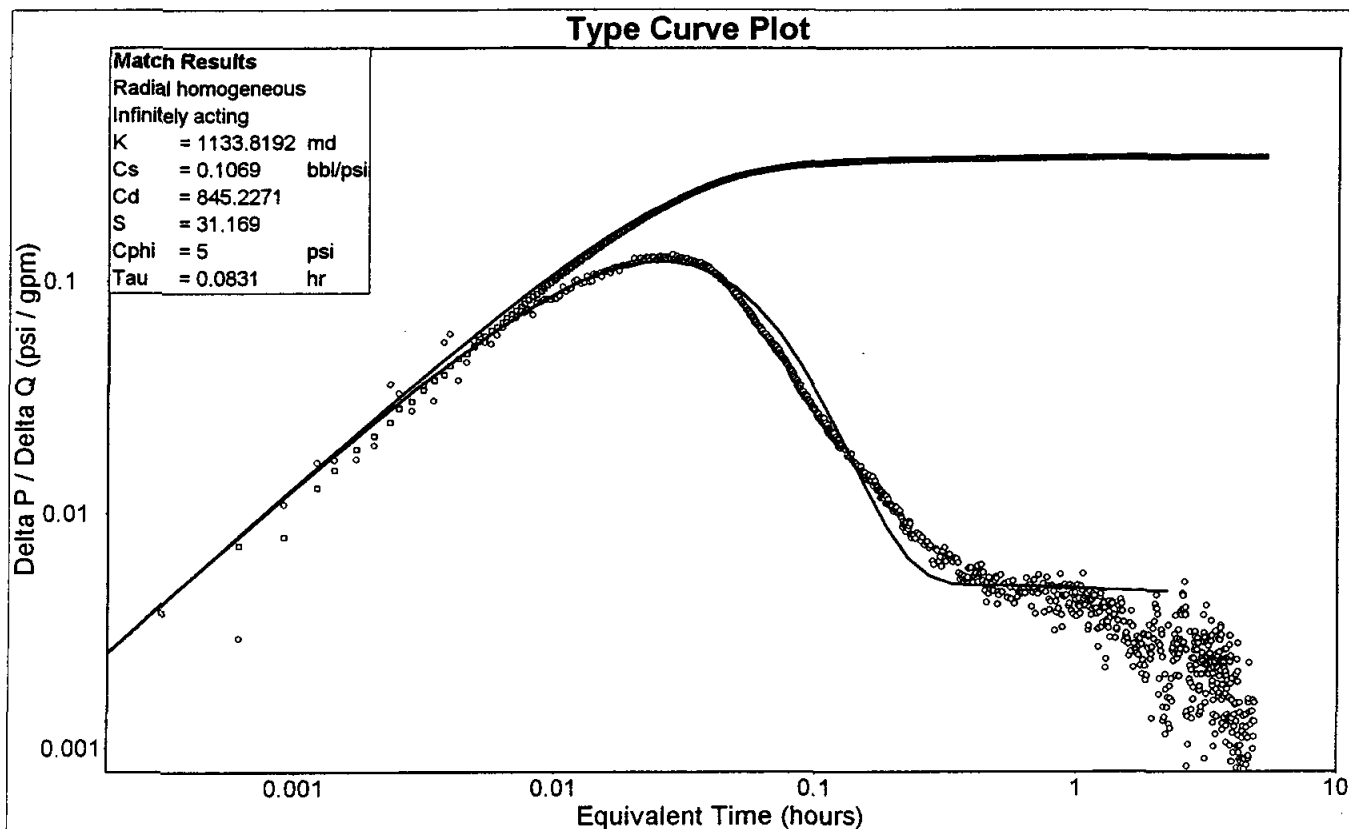
Type Curve Plot Model Results

Radial homogeneous

Infinitely acting

| | Value |
|--------------------------------|----------------|
| Permeability | 1133.8192 md |
| Wellbore storage coefficient | 0.1069 bbl/psi |
| Dimensionless wellbore storage | 845.2271 |
| Skin factor | 31.169 |

Type Curve Details

Stage 1 File Name : C:\pan25\typecurv\radhomog.tch

Axis Type : Td/Cd

| | Stage 1 |
|-----------------|-----------|
| Match point - X | -3.1743 |
| Match point - Y | 3.5836 |
| Curve Number | 13.0000 |
| Curve Value | 1.0000e30 |
