

District I
1625 N. French Dr., Hobbs, NM 88240

District II
811 S. First St., Artesia, NM 88210

District III
1000 Rio Brazos Rd., Aztec, NM 87410

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals & Natural Resources

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-104
Revised August 1, 2011

Submit one copy to appropriate District Office

☐ AMENDED REPORT

I. REQUEST FOR ALLOWABLE AND AUTHORIZATION TO TRANSPORT

¹ Operator name and Address COG Operating LLC 2208 W. Main Street Artesia, NM 88210		² OGRID Number 229137	
		³ Reason for Filing Code/ Effective Date RT	
API Number 30-015-46786	⁵ Pool Name Willow Lake Bone Spring ; Southeast		⁶ Pool Code 96217
⁷ Property Code 313927	⁸ Property Name Admiral Federal Com		⁹ Well Number 503H

II. ¹⁰ Surface Location

Ul or lot no. N	Section 28	Township 25S	Range 29E	Lot Idn	Feet from the 220	North/South Line South	Feet from the 2630	East/West line West	County Eddy
--------------------	---------------	-----------------	--------------	---------	----------------------	---------------------------	-----------------------	------------------------	----------------

¹¹ Bottom Hole Location

Ul or lot no. C	Section 21	Township 25S	Range 29E	Lot Idn	Feet from the 51	North/South Line North	Feet from the 2614	East/West line West	County Eddy
¹² Lse Code F	¹³ Producing Method Code		¹⁴ Gas Connection Date		¹⁵ C-129 Permit Number	¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date	

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
	ACC	O
298751	ETC	G
278421	Holly Refining and Marketing PO Box 159 Artesia, NM 88210	O

IV. Well Completion Data

²¹ Spud Date 3/2/20	²² Ready Date 3/15/21	²³ TD 18,945’	²⁴ PBTD 18,800’	²⁵ Perforations 8,800-18,830’	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size		²⁹ Depth Set	³⁰ Sacks Cement
17 1/2”		13 3/8”		677’	525
12 1/4”		9 5/8”		3,030’	960
8 1/2”		5 1/2”		18,935’	3250
		2 7/8”		8,052’	

V. Well Test Data

³¹ Date New Oil	³² Gas Delivery Date	³³ Test Date	³⁴ Test Length	³⁵ Tbg. Pressure	³⁶ Csg. Pressure
³⁷ Choke Size	³⁸ Oil	³⁹ Water	⁴⁰ Gas		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: <i>Amanda Avery</i>			OIL CONSERVATION DIVISION Approved by: KURT SIMMONS		
Printed name: Amanda Avery			Title: NMOCD, SANTA FE		
Title: Regulatory Analyst			Approval Date: 04/15/2021		
E-mail Address:			RT C-104 EXPIRES 07/14/2021 (90 DAYS)		
Date: 3 /15/21	Phone: 575-748-6962				

DISTRICT I
1625 N. FRENCH DR., HOBBS, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

DISTRICT II
511 S. FIRST ST., ARTESIA, NM 88210
Phone: (575) 746-1283 Fax: (575) 746-9720

DISTRICT III
1000 RIO BRAZOS RD., AZTEC, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

DISTRICT IV
1220 S. ST. FRANCIS DR., SANTA FE, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 SOUTH ST. FRANCIS DR.
Santa Fe, New Mexico 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☒ AMENDED REPORT
As Drilled

WELL LOCATION AND ACREAGE DEDICATION PLAT

API Number 30-015-46786	Pool Code 96217	Pool Name Willow Lake; Bone Spring; Southeast
Property Code 313927	Property Name ADMIRAL FEDERAL COM	Well Number 503H
OGRID No. 229137	Operator Name COG OPERATING, LLC	Elevation 2986.2'

Surface Location

UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
N	28	25-S	29-E		220	SOUTH	2630	WEST	EDDY

Bottom Hole Location If Different From Surface

UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
C	21	25-S	29-E		51	NORTH	2614	WEST	EDDY
Dedicated Acres 1280	Joint or Infill	Consolidation Code	Order No.						

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION


SEE PAGE 2

PAGE 1 OF 2


W.O. #21-89

DRAWN BY: WN

Property Code 313927	Property Name ADMIRAL FEDERAL COM	Well Number 503H
OGRID No. 229137	Operator Name COG OPERATING, LLC	Elevation 2986.2'

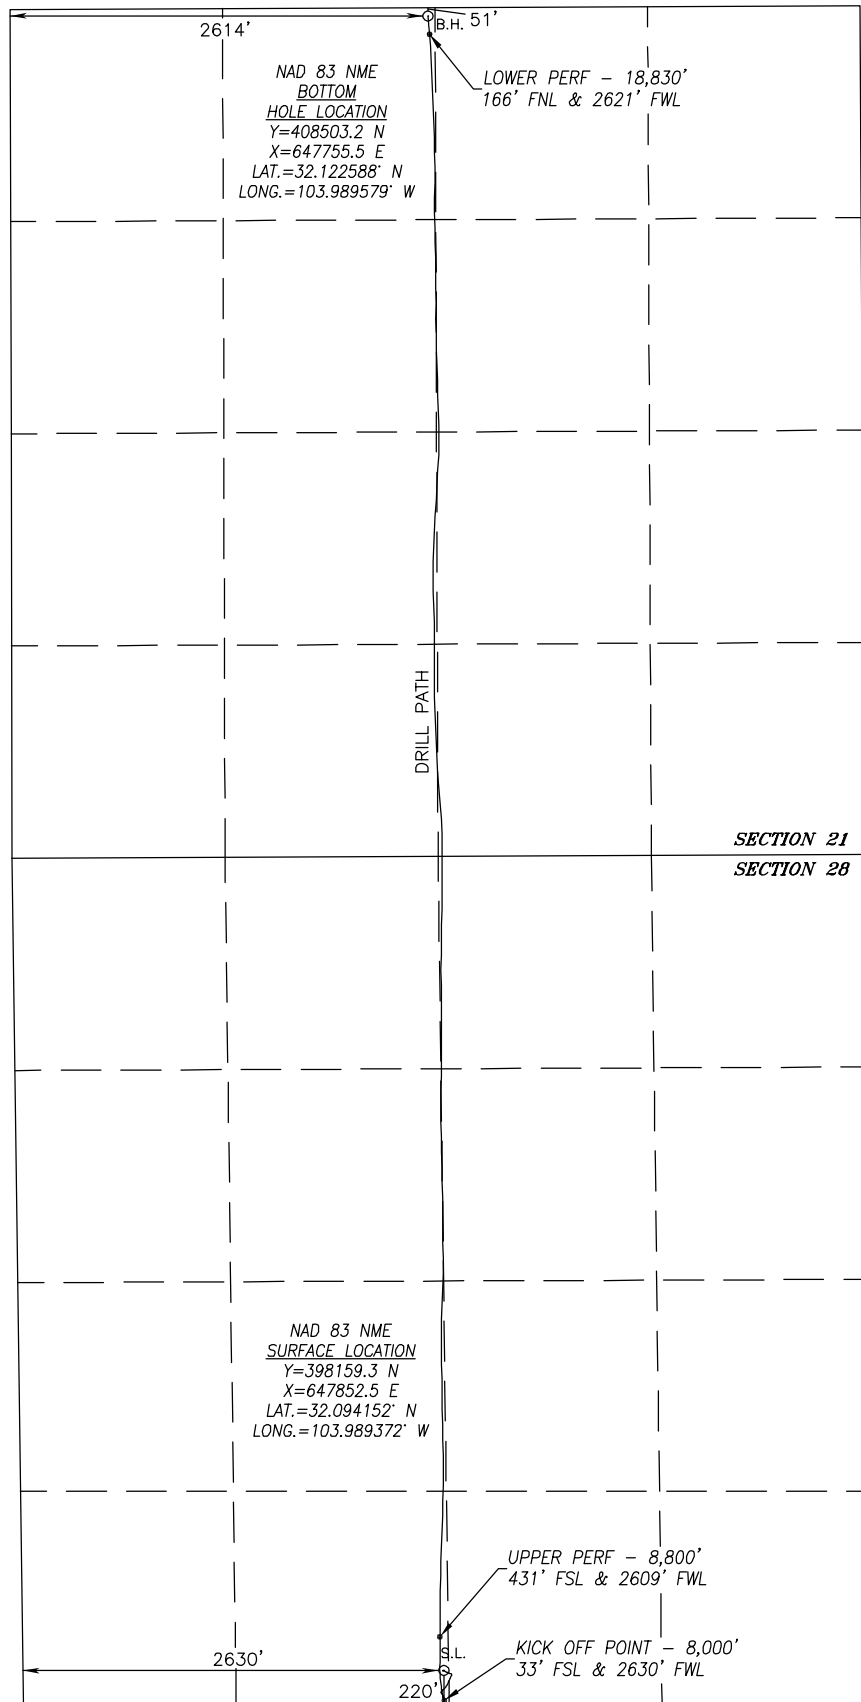

SURFACE INFO AND BOREPATH SHOWN HEREON IS BASED ON DIRECTIONAL SURVEY REPORT PROVIDED BY COG OPERATING, LLC FOR THE ADMIRAL FEDERAL COM 503H SUPPLIED TO HARCROW SURVEYING, LLC ON JANUARY 27, 2021



OPERATOR CERTIFICATION

I hereby certify that the information herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

3/15/21

Signature

Date

Amanda Avery

Printed Name

amanda.lavery@conocophillips.com

E-mail Address

SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

AUG. 23, 2019/MAR. 26, 2020

Date of Survey/Date of Geographic Survey

Signature & Seal of Professional Surveyor



Chad Harcrow 2/1/21

Certificate No. CHAD HARCROW 17777

PAGE 2 OF 2

W.O. #21-89

DRAWN BY: WN

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018



COG Operating LLC

Eddy County, NM (NAD27 NME)

Admiral Fed Com

503H

OH / 66375

Design: Surveys (Pioneer 84)

Standard Survey Report

26 March, 2020





Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well 503H
Project:	Eddy County, NM (NAD27 NME)	TVD Reference:	RKB @ 3011.20usft (Pioneer 84)
Site:	Admiral Fed Com	MD Reference:	RKB @ 3011.20usft (Pioneer 84)
Well:	503H	North Reference:	Grid
Wellbore:	OH / 66375	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Pioneer 84)	Database:	USA Compass

Project	Eddy County, NM (NAD27 NME)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	Admiral Fed Com		
Site Position:		Northing:	398,093.60 usft
From:	Map	Easting:	604,917.40 usft
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 5' 38.479918 N
		Longitude:	103° 59' 40.340397 W
		Grid Convergence:	0.18 °

Well	503H		
Well Position	+N/-S	0.00 usft	Northing: 398,101.30 usft
	+E/-W	0.00 usft	Easting: 606,667.40 usft
Position Uncertainty	1.00 usft	Wellhead Elevation:	usft
		Latitude:	32° 5' 38.501256 N
		Longitude:	103° 59' 19.996798 W
		Ground Level:	2,986.20 usft

Wellbore	OH / 66375		
Magnetics	Model Name	Sample Date	Declination (°)
	User Defined	3/13/2020	6.74
			Dip Angle (°) 59.72
			Field Strength (nT) 47,771.20000000

Design	Surveys (Pioneer 84)		
Audit Notes:			
Version:	1.0	Phase:	ACTUAL
		Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)
	0.00	0.00	0.00
			Direction (°) 359.55

Survey Program	Date	3/26/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
20.00	597.00	Surface MWD Surveys (OH / 66375)	MWD+HRGM	OWSG MWD + HRGM
597.00	18,945.00	Phoenix MWD Surveys (OH / 66375)	MWD+IFR1+FDIR	OWSG MWD + IFR1 + FDIR Correction

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
20.00	0.09	48.41	20.00	0.01	0.01	0.01	0.45	0.45	0.00
97.00	0.37	208.28	97.00	-0.17	-0.06	-0.17	0.59	0.36	207.62
184.00	0.69	258.73	184.00	-0.52	-0.71	-0.51	0.62	0.37	57.99
282.00	1.26	262.83	281.98	-0.77	-2.36	-0.75	0.59	0.58	4.18
373.00	1.37	252.21	372.96	-1.23	-4.38	-1.19	0.29	0.12	-11.67
457.00	0.43	213.69	456.95	-1.79	-5.51	-1.75	1.27	-1.12	-45.86
548.00	0.26	216.94	547.95	-2.24	-5.83	-2.20	0.19	-0.19	3.57
597.00	0.56	262.80	596.94	-2.36	-6.13	-2.31	0.86	0.61	93.59
Tie In									



Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well 503H
Project:	Eddy County, NM (NAD27 NME)	TVD Reference:	RKB @ 3011.20usft (Pioneer 84)
Site:	Admiral Fed Com	MD Reference:	RKB @ 3011.20usft (Pioneer 84)
Well:	503H	North Reference:	Grid
Wellbore:	OH / 66375	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Pioneer 84)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
697.00	0.36	354.47	696.94	-2.11	-6.65	-2.06	0.67	-0.20	91.67
First Phoenix MWD Survey									
774.00	0.41	9.99	773.94	-1.60	-6.62	-1.55	0.15	0.06	20.16
869.00	0.36	46.64	868.94	-1.06	-6.35	-1.01	0.26	-0.05	38.58
963.00	0.51	70.68	962.94	-0.72	-5.74	-0.67	0.25	0.16	25.57
1,058.00	0.75	82.68	1,057.93	-0.50	-4.72	-0.46	0.29	0.25	12.63
1,153.00	1.12	90.94	1,152.92	-0.43	-3.18	-0.41	0.41	0.39	8.69
1,248.00	1.53	113.01	1,247.89	-0.95	-1.08	-0.94	0.68	0.43	23.23
1,342.00	1.50	115.50	1,341.86	-1.97	1.18	-1.98	0.08	-0.03	2.65
1,437.00	1.62	113.45	1,436.82	-3.04	3.54	-3.06	0.14	0.13	-2.16
1,532.00	1.72	115.52	1,531.78	-4.18	6.06	-4.23	0.12	0.11	2.18
1,627.00	1.91	118.66	1,626.74	-5.56	8.73	-5.63	0.23	0.20	3.31
1,722.00	1.80	116.45	1,721.69	-6.98	11.46	-7.07	0.14	-0.12	-2.33
1,817.00	1.59	118.62	1,816.64	-8.28	13.95	-8.39	0.23	-0.22	2.28
1,912.00	1.51	114.64	1,911.61	-9.43	16.25	-9.56	0.14	-0.08	-4.19
2,006.00	1.12	116.54	2,005.58	-10.36	18.19	-10.50	0.42	-0.41	2.02
2,101.00	1.09	106.67	2,100.57	-11.03	19.89	-11.19	0.20	-0.03	-10.39
2,196.00	1.28	116.27	2,195.55	-11.76	21.71	-11.93	0.29	0.20	10.11
2,291.00	2.13	113.96	2,290.50	-12.95	24.27	-13.14	0.90	0.89	-2.43
2,386.00	3.63	114.71	2,385.38	-14.92	28.62	-15.15	1.58	1.58	0.79
2,480.00	3.27	108.09	2,479.21	-17.00	33.87	-17.26	0.57	-0.38	-7.04
2,575.00	2.63	99.30	2,574.09	-18.19	38.59	-18.49	0.82	-0.67	-9.25
2,670.00	4.49	113.42	2,668.90	-20.02	44.16	-20.37	2.15	1.96	14.86
2,765.00	3.64	150.09	2,763.68	-24.11	49.08	-24.50	2.82	-0.89	38.60
2,860.00	4.03	204.50	2,858.49	-29.77	49.19	-30.15	3.71	0.41	57.27
2,955.00	3.91	207.48	2,953.26	-35.68	46.32	-36.04	0.25	-0.13	3.14
2,961.00	3.89	208.01	2,959.25	-36.04	46.13	-36.40	0.69	-0.33	8.83
3,052.00	3.70	207.53	3,050.05	-41.37	43.32	-41.71	0.21	-0.21	-0.53
3,147.00	3.65	204.95	3,144.86	-46.83	40.63	-47.15	0.18	-0.05	-2.72
3,242.00	3.52	205.59	3,239.67	-52.20	38.09	-52.50	0.14	-0.14	0.67
3,336.00	3.34	204.36	3,333.50	-57.30	35.72	-57.58	0.21	-0.19	-1.31
3,432.00	3.17	207.51	3,429.35	-62.20	33.34	-62.46	0.26	-0.18	3.28
3,526.00	2.84	203.64	3,523.22	-66.64	31.20	-66.88	0.41	-0.35	-4.12
3,621.00	2.64	204.07	3,618.11	-70.79	29.37	-71.02	0.21	-0.21	0.45
3,716.00	2.59	201.53	3,713.01	-74.79	27.69	-75.00	0.13	-0.05	-2.67
3,811.00	2.51	205.78	3,807.92	-78.66	25.99	-78.86	0.22	-0.08	4.47
3,906.00	2.21	201.97	3,902.83	-82.23	24.40	-82.42	0.36	-0.32	-4.01
4,001.00	2.00	203.34	3,997.77	-85.45	23.06	-85.63	0.23	-0.22	1.44
4,096.00	2.13	208.61	4,092.71	-88.52	21.56	-88.69	0.24	0.14	5.55
4,190.00	1.91	206.99	4,186.65	-91.45	20.01	-91.60	0.24	-0.23	-1.72
4,285.00	1.96	203.99	4,281.60	-94.35	18.63	-94.49	0.12	0.05	-3.16
4,380.00	1.99	216.82	4,376.54	-97.15	16.98	-97.28	0.47	0.03	13.51
4,475.00	1.79	212.58	4,471.49	-99.72	15.20	-99.84	0.26	-0.21	-4.46



Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well 503H
Project:	Eddy County, NM (NAD27 NME)	TVD Reference:	RKB @ 3011.20usft (Pioneer 84)
Site:	Admiral Fed Com	MD Reference:	RKB @ 3011.20usft (Pioneer 84)
Well:	503H	North Reference:	Grid
Wellbore:	OH / 66375	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Pioneer 84)	Database:	USA Compass

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,570.00	1.59	214.14	4,566.45	-102.06	13.66	-102.17	0.22	-0.21	1.64
4,665.00	1.64	214.38	4,661.41	-104.27	12.15	-104.37	0.05	0.05	0.25
4,759.00	1.67	223.73	4,755.37	-106.37	10.44	-106.45	0.29	0.03	9.95
4,854.00	1.65	228.76	4,850.33	-108.28	8.46	-108.34	0.15	-0.02	5.29
4,949.00	1.64	227.75	4,945.29	-110.09	6.42	-110.14	0.03	-0.01	-1.06
5,044.00	1.49	235.55	5,040.26	-111.70	4.40	-111.74	0.27	-0.16	8.21
5,139.00	1.86	227.59	5,135.22	-113.44	2.24	-113.46	0.46	0.39	-8.38
5,234.00	2.29	225.21	5,230.15	-115.82	-0.24	-115.81	0.46	0.45	-2.51
5,328.00	2.42	223.18	5,324.07	-118.59	-2.93	-118.56	0.16	0.14	-2.16
5,423.00	2.26	226.41	5,418.99	-121.34	-5.66	-121.30	0.22	-0.17	3.40
5,518.00	2.02	222.47	5,513.93	-123.87	-8.15	-123.80	0.30	-0.25	-4.15
5,613.00	1.94	212.67	5,608.87	-126.46	-10.15	-126.38	0.37	-0.08	-10.32
5,707.00	1.87	212.75	5,702.82	-129.09	-11.84	-128.99	0.07	-0.07	0.09
5,802.00	1.81	214.48	5,797.77	-131.63	-13.53	-131.52	0.09	-0.06	1.82
5,897.00	1.92	210.61	5,892.72	-134.24	-15.19	-134.11	0.18	0.12	-4.07
5,992.00	1.62	204.60	5,987.68	-136.83	-16.55	-136.69	0.37	-0.32	-6.33
6,086.00	3.29	143.47	6,081.60	-140.20	-15.50	-140.08	3.06	1.78	-65.03
6,181.00	2.74	145.75	6,176.47	-144.27	-12.60	-144.17	0.59	-0.58	2.40
6,276.00	2.54	148.26	6,271.37	-147.94	-10.22	-147.85	0.24	-0.21	2.64
6,371.00	2.50	143.82	6,366.27	-151.40	-7.89	-151.33	0.21	-0.04	-4.67
6,466.00	2.63	147.57	6,461.18	-154.91	-5.49	-154.86	0.22	0.14	3.95
6,560.00	2.58	152.01	6,555.08	-158.60	-3.34	-158.57	0.22	-0.05	4.72
6,655.00	2.23	154.70	6,650.00	-162.16	-1.55	-162.14	0.39	-0.37	2.83
6,750.00	2.62	149.45	6,744.91	-165.70	0.34	-165.70	0.47	0.41	-5.53
6,845.00	2.22	157.49	6,839.83	-169.27	2.15	-169.28	0.55	-0.42	8.46
6,940.00	1.32	247.95	6,934.80	-171.38	1.84	-171.39	2.73	-0.95	95.22
7,034.00	0.92	216.60	7,028.78	-172.39	0.39	-172.39	0.76	-0.43	-33.35
7,129.00	0.53	200.34	7,123.77	-173.42	-0.22	-173.41	0.46	-0.41	-17.12
7,224.00	0.47	200.13	7,218.77	-174.20	-0.51	-174.19	0.06	-0.06	-0.22
7,319.00	0.54	162.71	7,313.76	-174.99	-0.51	-174.98	0.35	0.07	-39.39
7,413.00	0.76	217.08	7,407.76	-175.91	-0.75	-175.90	0.67	0.23	57.84
7,508.00	1.63	141.77	7,502.74	-177.47	-0.30	-177.47	1.70	0.92	-79.27
7,603.00	1.51	127.62	7,597.71	-179.30	1.53	-179.31	0.43	-0.13	-14.89
7,698.00	0.99	149.53	7,692.68	-180.77	2.94	-180.79	0.73	-0.55	23.06
7,793.00	1.36	176.71	7,787.66	-182.60	3.42	-182.62	0.69	0.39	28.61
7,887.00	1.49	188.60	7,881.64	-184.92	3.30	-184.95	0.34	0.14	12.65
7,937.00	0.88	189.64	7,931.62	-185.95	3.14	-185.97	1.22	-1.22	2.08
7,996.00	0.63	196.92	7,990.62	-186.70	2.97	-186.72	0.45	-0.42	12.34
8,044.00	2.00	311.25	8,038.61	-186.40	2.26	-186.42	4.86	2.85	238.19
8,091.00	5.60	334.30	8,085.50	-183.80	0.65	-183.79	8.17	7.66	49.04
8,138.00	11.13	337.83	8,131.98	-177.52	-2.06	-177.50	11.81	11.77	7.51
8,185.00	14.28	345.40	8,177.83	-167.71	-5.23	-167.66	7.57	6.70	16.11
8,233.00	18.08	348.97	8,223.92	-154.67	-8.15	-154.60	8.18	7.92	7.44
8,280.00	21.16	351.81	8,268.19	-139.11	-10.75	-139.02	6.86	6.55	6.04



Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well 503H
Project:	Eddy County, NM (NAD27 NME)	TVD Reference:	RKB @ 3011.20usft (Pioneer 84)
Site:	Admiral Fed Com	MD Reference:	RKB @ 3011.20usft (Pioneer 84)
Well:	503H	North Reference:	Grid
Wellbore:	OH / 66375	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Pioneer 84)	Database:	USA Compass

Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,328.00	24.12	352.88	8,312.49	-120.80	-13.20	-120.69	6.23	6.17	2.23
8,328.63	24.18	352.89	8,313.06	-120.54	-13.24	-120.43	9.62	9.62	1.00
FTP @ 8328.6' MD									
8,375.00	28.64	353.28	8,354.58	-100.07	-15.71	-99.94	9.62	9.62	0.85
8,423.00	33.63	353.10	8,395.65	-75.43	-18.66	-75.28	10.40	10.40	-0.38
8,470.00	37.61	353.87	8,433.85	-48.24	-21.75	-48.07	8.52	8.47	1.64
8,518.00	39.81	357.50	8,471.31	-18.32	-23.99	-18.13	6.58	4.58	7.56
8,565.00	44.24	0.30	8,506.22	13.12	-24.56	13.32	10.23	9.43	5.96
8,613.00	48.98	1.36	8,539.18	47.99	-24.04	48.18	10.00	9.88	2.21
8,660.00	55.80	1.28	8,567.85	85.19	-23.19	85.37	14.51	14.51	-0.17
8,707.00	61.76	0.17	8,592.20	125.36	-22.69	125.54	12.84	12.68	-2.36
8,754.00	67.96	359.03	8,612.16	167.89	-23.00	168.06	13.37	13.19	-2.43
8,803.00	73.64	359.01	8,628.27	214.14	-23.79	214.32	11.59	11.59	-0.04
8,850.00	80.19	359.39	8,638.90	259.89	-24.43	260.07	13.96	13.94	0.81
8,897.00	83.87	0.72	8,645.42	306.42	-24.38	306.61	8.32	7.83	2.83
8,992.00	85.08	1.21	8,654.56	400.97	-22.79	401.13	1.37	1.27	0.52
9,087.00	84.87	0.57	8,662.88	495.59	-21.32	495.74	0.71	-0.22	-0.67
9,182.00	85.65	0.51	8,670.73	590.26	-20.42	590.40	0.82	0.82	-0.06
9,276.00	90.68	1.55	8,673.74	684.17	-18.73	684.29	5.46	5.35	1.11
9,371.00	92.87	3.25	8,670.80	779.03	-14.76	779.12	2.92	2.31	1.79
9,466.00	93.85	3.08	8,665.23	873.72	-9.52	873.77	1.05	1.03	-0.18
9,561.00	91.33	0.98	8,660.94	968.55	-6.16	968.57	3.45	-2.65	-2.21
9,655.00	91.43	0.93	8,658.68	1,062.51	-4.60	1,062.51	0.12	0.11	-0.05
9,750.00	89.84	0.05	8,657.62	1,157.50	-3.79	1,157.49	1.91	-1.67	-0.93
9,845.00	91.02	0.44	8,656.91	1,252.49	-3.38	1,252.48	1.31	1.24	0.41
9,939.00	89.36	359.22	8,656.60	1,346.48	-3.66	1,346.47	2.19	-1.77	-1.30
10,034.00	89.45	358.73	8,657.59	1,441.46	-5.36	1,441.46	0.52	0.09	-0.52
10,129.00	89.44	358.76	8,658.51	1,536.44	-7.44	1,536.45	0.03	-0.01	0.03
10,224.00	87.78	359.13	8,660.81	1,631.39	-9.19	1,631.41	1.79	-1.75	0.39
10,318.00	86.88	359.41	8,665.19	1,725.28	-10.38	1,725.31	1.00	-0.96	0.30
10,413.00	87.45	359.01	8,669.89	1,820.15	-11.69	1,820.19	0.73	0.60	-0.42
10,508.00	87.97	358.70	8,673.68	1,915.06	-13.59	1,915.10	0.64	0.55	-0.33
10,603.00	88.95	358.67	8,676.24	2,010.00	-15.77	2,010.06	1.03	1.03	-0.03
10,697.00	92.09	1.21	8,675.38	2,103.97	-15.87	2,104.03	4.30	3.34	2.70
10,792.00	92.36	2.55	8,671.70	2,198.85	-12.75	2,198.88	1.44	0.28	1.41
10,887.00	90.54	1.62	8,669.29	2,293.75	-9.30	2,293.75	2.15	-1.92	-0.98
10,982.00	89.78	2.40	8,669.03	2,388.69	-5.97	2,388.66	1.15	-0.80	0.82
11,077.00	87.39	0.26	8,671.37	2,483.62	-3.76	2,483.58	3.38	-2.52	-2.25
11,171.00	86.56	359.22	8,676.33	2,577.49	-4.19	2,577.44	1.41	-0.88	-1.11
11,266.00	87.69	359.09	8,681.10	2,672.36	-5.59	2,672.32	1.20	1.19	-0.14
11,361.00	89.28	359.49	8,683.61	2,767.31	-6.76	2,767.28	1.73	1.67	0.42
11,456.00	90.36	359.95	8,683.91	2,862.31	-7.23	2,862.28	1.24	1.14	0.48
11,551.00	90.97	359.14	8,682.80	2,957.30	-7.98	2,957.27	1.07	0.64	-0.85



Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well 503H
Project:	Eddy County, NM (NAD27 NME)	TVD Reference:	RKB @ 3011.20usft (Pioneer 84)
Site:	Admiral Fed Com	MD Reference:	RKB @ 3011.20usft (Pioneer 84)
Well:	503H	North Reference:	Grid
Wellbore:	OH / 66375	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Pioneer 84)	Database:	USA Compass

Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
11,645.00	92.56	359.04	8,679.91	3,051.24	-9.47	3,051.22	1.69	1.69	-0.11	
11,740.00	91.03	358.76	8,676.93	3,146.17	-11.30	3,146.16	1.64	-1.61	-0.29	
11,835.00	90.85	359.16	8,675.38	3,241.14	-13.02	3,241.15	0.46	-0.19	0.42	
11,930.00	91.67	358.41	8,673.29	3,336.10	-15.03	3,336.11	1.17	0.86	-0.79	
12,024.00	90.39	359.79	8,671.60	3,430.07	-16.51	3,430.09	2.00	-1.36	1.47	
12,120.00	90.05	0.28	8,671.23	3,526.07	-16.45	3,526.09	0.62	-0.35	0.51	
12,214.00	92.19	359.78	8,669.39	3,620.04	-16.40	3,620.06	2.34	2.28	-0.53	
12,309.00	89.32	0.95	8,668.14	3,715.02	-15.80	3,715.03	3.26	-3.02	1.23	
12,404.00	87.97	0.37	8,670.39	3,809.98	-14.70	3,809.98	1.55	-1.42	-0.61	
12,499.00	88.37	359.93	8,673.42	3,904.94	-14.45	3,904.93	0.63	0.42	-0.46	
12,594.00	89.79	0.53	8,674.94	3,999.92	-14.07	3,999.91	1.62	1.49	0.63	
12,688.00	89.88	359.05	8,675.22	4,093.92	-14.42	4,093.90	1.58	0.10	-1.57	
12,783.00	92.07	0.23	8,673.60	4,188.89	-15.01	4,188.88	2.62	2.31	1.24	
12,878.00	89.81	358.84	8,672.04	4,283.87	-15.79	4,283.86	2.79	-2.38	-1.46	
12,973.00	90.09	359.93	8,672.12	4,378.86	-16.80	4,378.86	1.18	0.29	1.15	
13,068.00	92.39	0.77	8,670.07	4,473.83	-16.22	4,473.82	2.58	2.42	0.88	
13,162.00	88.46	1.36	8,669.37	4,567.79	-14.48	4,567.77	4.23	-4.18	0.63	
13,257.00	87.06	0.83	8,673.08	4,662.70	-12.66	4,662.66	1.58	-1.47	-0.56	
13,352.00	87.85	0.66	8,677.30	4,757.60	-11.43	4,757.54	0.85	0.83	-0.18	
13,447.00	88.92	0.47	8,679.98	4,852.55	-10.49	4,852.49	1.14	1.13	-0.20	
13,541.00	90.34	0.19	8,680.59	4,946.55	-9.95	4,946.47	1.54	1.51	-0.30	
13,636.00	92.22	0.31	8,678.46	5,041.52	-9.54	5,041.44	1.98	1.98	0.13	
13,731.00	89.72	359.81	8,676.86	5,136.50	-9.44	5,136.41	2.68	-2.63	-0.53	
13,826.00	89.25	358.09	8,677.71	5,231.47	-11.18	5,231.40	1.88	-0.49	-1.81	
13,919.00	90.34	357.70	8,678.04	5,324.41	-14.60	5,324.36	1.24	1.17	-0.42	
14,014.00	88.52	353.68	8,678.99	5,419.11	-21.73	5,419.12	4.64	-1.92	-4.23	
14,109.00	89.86	354.34	8,680.33	5,513.58	-31.64	5,513.66	1.57	1.41	0.69	
14,204.00	91.42	356.11	8,679.27	5,608.24	-39.55	5,608.38	2.48	1.64	1.86	
14,298.00	90.35	358.35	8,677.82	5,702.11	-44.09	5,702.28	2.64	-1.14	2.38	
14,393.00	91.30	357.61	8,676.45	5,797.04	-47.44	5,797.23	1.27	1.00	-0.78	
14,488.00	91.28	357.75	8,674.31	5,891.94	-51.29	5,892.16	0.15	-0.02	0.15	
14,583.00	90.73	359.10	8,672.65	5,986.89	-53.90	5,987.12	1.53	-0.58	1.42	
14,678.00	90.53	357.49	8,671.60	6,081.83	-56.72	6,082.09	1.71	-0.21	-1.69	
14,773.00	89.71	359.96	8,671.40	6,176.80	-58.84	6,177.07	2.74	-0.86	2.60	
14,868.00	90.96	1.65	8,670.85	6,271.79	-57.50	6,272.04	2.21	1.32	1.78	
14,963.00	89.74	359.75	8,670.27	6,366.77	-56.34	6,367.02	2.38	-1.28	-2.00	
15,058.00	89.98	358.55	8,670.50	6,461.76	-57.75	6,462.01	1.29	0.25	-1.26	
15,152.00	90.72	358.40	8,669.92	6,555.72	-60.25	6,555.99	0.80	0.79	-0.16	
15,247.00	91.32	358.41	8,668.23	6,650.67	-62.90	6,650.96	0.63	0.63	0.01	
15,342.00	92.84	358.42	8,664.78	6,745.57	-65.52	6,745.88	1.60	1.60	0.01	
15,437.00	91.42	359.47	8,661.25	6,840.48	-67.27	6,840.80	1.86	-1.49	1.11	
15,532.00	90.10	1.31	8,659.99	6,935.47	-66.62	6,935.78	2.38	-1.39	1.94	
15,627.00	89.43	2.45	8,660.38	7,030.41	-63.51	7,030.69	1.39	-0.71	1.20	



Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well 503H
Project:	Eddy County, NM (NAD27 NME)	TVD Reference:	RKB @ 3011.20usft (Pioneer 84)
Site:	Admiral Fed Com	MD Reference:	RKB @ 3011.20usft (Pioneer 84)
Well:	503H	North Reference:	Grid
Wellbore:	OH / 66375	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Pioneer 84)	Database:	USA Compass

Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
15,722.00	90.59	2.54	8,660.37	7,125.32	-59.37	7,125.57	1.22	1.22	0.09
15,816.00	88.59	3.42	8,661.04	7,219.19	-54.48	7,219.39	2.32	-2.13	0.94
15,911.00	88.49	4.10	8,663.46	7,313.95	-48.26	7,314.10	0.72	-0.11	0.72
16,006.00	86.37	3.49	8,667.72	7,408.64	-41.98	7,408.74	2.32	-2.23	-0.64
16,101.00	86.27	2.77	8,673.82	7,503.30	-36.80	7,503.36	0.76	-0.11	-0.76
16,195.00	85.96	2.84	8,680.19	7,596.97	-32.21	7,596.99	0.34	-0.33	0.07
16,290.00	85.81	359.42	8,687.00	7,691.70	-30.34	7,691.70	3.59	-0.16	-3.60
16,385.00	86.68	358.66	8,693.23	7,786.48	-31.93	7,786.49	1.21	0.92	-0.80
16,480.00	87.82	358.35	8,697.78	7,881.33	-34.40	7,881.36	1.24	1.20	-0.33
16,575.00	90.20	358.99	8,699.43	7,976.29	-36.61	7,976.33	2.59	2.51	0.67
16,670.00	91.47	358.32	8,698.04	8,071.25	-38.84	8,071.30	1.51	1.34	-0.71
16,764.00	92.85	358.01	8,694.50	8,165.13	-41.85	8,165.21	1.50	1.47	-0.33
16,859.00	91.77	358.46	8,690.67	8,260.01	-44.77	8,260.10	1.23	-1.14	0.47
16,954.00	91.56	358.61	8,687.91	8,354.94	-47.20	8,355.05	0.27	-0.22	0.16
17,049.00	90.66	359.95	8,686.07	8,449.91	-48.39	8,450.03	1.70	-0.95	1.41
17,144.00	90.27	0.45	8,685.30	8,544.90	-48.06	8,545.02	0.67	-0.41	0.53
17,239.00	89.02	359.03	8,685.89	8,639.90	-48.49	8,640.01	1.99	-1.32	-1.49
17,334.00	90.34	358.94	8,686.42	8,734.88	-50.17	8,735.00	1.39	1.39	-0.09
17,429.00	91.40	358.67	8,684.97	8,829.84	-52.15	8,829.98	1.15	1.12	-0.28
17,524.00	92.50	358.41	8,681.74	8,924.76	-54.57	8,924.91	1.19	1.16	-0.27
17,618.00	91.76	359.68	8,678.25	9,018.68	-56.14	9,018.84	1.56	-0.79	1.35
17,713.00	89.71	0.10	8,677.03	9,113.66	-56.32	9,113.82	2.20	-2.16	0.44
17,808.00	89.63	359.96	8,677.58	9,208.66	-56.27	9,208.82	0.17	-0.08	-0.15
17,902.00	86.33	0.09	8,680.89	9,302.59	-56.23	9,302.74	3.51	-3.51	0.14
17,997.00	87.21	0.03	8,686.24	9,397.44	-56.13	9,397.59	0.93	0.93	-0.06
18,092.00	88.84	359.62	8,689.52	9,492.38	-56.42	9,492.53	1.77	1.72	-0.43
18,187.00	89.34	358.48	8,691.02	9,587.35	-58.00	9,587.51	1.31	0.53	-1.20
18,282.00	90.55	357.84	8,691.12	9,682.30	-61.05	9,682.48	1.44	1.27	-0.67
18,377.00	87.93	356.92	8,692.38	9,777.18	-65.39	9,777.39	2.92	-2.76	-0.97
18,472.00	88.53	357.79	8,695.31	9,872.03	-69.77	9,872.28	1.11	0.63	0.92
18,567.00	89.97	357.59	8,696.55	9,966.95	-73.60	9,967.22	1.53	1.52	-0.21
18,661.00	90.93	356.68	8,695.82	10,060.82	-78.30	10,061.13	1.41	1.02	-0.97
18,756.00	92.70	356.33	8,692.81	10,155.60	-84.08	10,155.94	1.90	1.86	-0.37
18,851.00	94.12	356.18	8,687.16	10,250.22	-90.28	10,250.62	1.50	1.49	-0.16
18,888.00	94.63	356.02	8,684.33	10,287.03	-92.79	10,287.44	1.44	1.38	-0.43
Final Phoenix MWD Survey									
18,895.92	94.63	356.02	8,683.69	10,294.91	-93.34	10,295.32	0.00	0.00	0.00
LTP @ 18896' MD									
18,945.00	94.63	356.02	8,679.73	10,343.71	-96.73	10,344.15	0.00	0.00	0.00
Projection @ TD									



Survey Report



Company:	COG Operating LLC	Local Co-ordinate Reference:	Well 503H
Project:	Eddy County, NM (NAD27 NME)	TVD Reference:	RKB @ 3011.20usft (Pioneer 84)
Site:	Admiral Fed Com	MD Reference:	RKB @ 3011.20usft (Pioneer 84)
Well:	503H	North Reference:	Grid
Wellbore:	OH / 66375	Survey Calculation Method:	Minimum Curvature
Design:	Surveys (Pioneer 84)	Database:	USA Compass

Design Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
597.00	596.94	-2.36	-6.13	Tie In
697.00	696.94	-2.11	-6.65	First Phoenix MWD Survey
8,328.63	8,313.06	-120.54	-13.24	FTP @ 8328.6' MD
18,888.00	8,684.33	10,287.03	-92.79	Final Phoenix MWD Survey
18,895.92	8,683.69	10,294.91	-93.34	LTP @ 18896' MD
18,945.00	8,679.73	10,343.71	-96.73	Projection @ TD

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 20826

CONDITIONS OF APPROVAL

Operator:	COG OPERATING LLC	600 W Illinois Ave	Midland, TX79701	OGRID:	229137	Action Number:	20826	Action Type:	C-104C
OCD Reviewer									Condition
ksimmons									None
