

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No. <div style="text-align: center; font-weight: bold; font-size: 1.2em;">[331333]</div>
2. Name of Operator <div style="text-align: center; font-weight: bold; font-size: 1.2em;">[217955]</div>		9. API Well No. <div style="text-align: center; font-weight: bold; font-size: 1.2em;">30-025-49288</div>
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory <div style="text-align: center; font-weight: bold; font-size: 1.2em;">[97964]</div>
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish 13. State
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

NGMP Rec 08/05/2021

SL

(Continued on page 2)



Approval Date: 04/22/2021

KZ
08/06/2021

*(Instructions on page 2)

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM I: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

0. SHL: SESW / 230 FSL / 1440 FWL / TWSP: 24S / RANGE: 32E / SECTION: 35 / LAT: 32.167451 / LONG: -103.649333 (TVD: 0 feet, MD: 0 feet)

PPP: SESW / 100 FSL / 1650 FWL / TWSP: 24S / RANGE: 32E / SECTION: 35 / LAT: 32.167096 / LONG: -103.648654 (TVD: 10495 feet, MD: 10566 feet)

BHL: NENW / 50 FNL / 1650 FWL / TWSP: 24S / RANGE: 32E / SECTION: 23 / LAT: 32.210222 / LONG: -103.648631 (TVD: 10649 feet, MD: 26122 feet)

BLM Point of Contact

Name: Deborah Ham

Title: Legal Landlaw Examiner

Phone: (575) 234-5965

Email: dham@blm.gov

CONFIDENTIAL

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL

**PECOS DISTRICT
SURFACE USE
CONDITIONS OF APPROVAL**

OPERATOR'S NAME:	COG Operating LLC
LEASE NO.:	NMNM120907
COUNTY:	Lea

Wells:

Well Pad 1

Eider 35 Federal Com 501H

Surface Hole Location: 200' FSL & 1440' FWL, Section 35, T24S, R32E

Bottom Hole Location: 50' FNL & 330' FWL, Section 26, T24S, R32E

Eider 35 Federal Com 502H

Surface Hole Location: 230' FSL & 1440' FWL, Section 35, T24S, R32E

Bottom Hole Location: 50' FNL & 1650' FWL, Section 23, T24S, R32E

Well Pad 2

Eider 35 Federal Com 701H

Surface Hole Location: 290' FSL & 755' FWL, Section 35, T24S, R32E

Bottom Hole Location: 2590' FSL & 330' FWL, Section 26, T24S, R32E

Eider 35 Federal Com 702H

Surface Hole Location: 290' FSL & 785' FWL, Section 35, T24S, R32E

Bottom Hole Location: 2590' FSL & 1310' FWL, Section 26, T24S, R32E

TABLE OF CONTENTS

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
 - Watershed
 - Range
 - Lesser Prairie Chicken
 - VRM IV
- ☐ **Construction**
 - Notification
 - Topsoil
 - Closed Loop System
 - Federal Mineral Material Pits
 - Well Pads
 - Roads
- ☐ **Road Section Diagram**
- ☒ **Production (Post Drilling)**
 - Well Structures & Facilities
 - Pipelines
 - Electric Lines
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**

I. GENERAL PROVISIONS

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

II. PERMIT EXPIRATION

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See information below discussing NAGPRA.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

IV. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

SPECIAL REQUIREMENT(S)

Watershed:

The entire well pad(s) will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. The compacted berm shall be constructed at a minimum of 12 inches with impermeable mineral material (e.g. caliche). Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The integrity of the berm shall be maintained around the surfaced pad throughout the life of the well and around the downsized pad after interim reclamation has been completed. Any water erosion that may occur due to the construction of the well pad during the life of the well will be quickly corrected and proper measures will be taken to prevent future erosion. Stockpiling of topsoil is required. The topsoil shall be stockpiled in an appropriate location to prevent loss of soil due to water or wind erosion and not used for berming or erosion control. If fluid collects within the bermed area, the fluid must be vacuumed into a safe container and disposed of properly at a state approved facility.

TANK BATTERY:

Tank battery locations will be lined and bermed. A 20 mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Tank battery berms must be large enough to contain 1 ½ times the content of the largest tank or 24 hour production, whichever is greater. Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

BURIED/SURFACE LINE(S):

When crossing ephemeral drainages the pipeline(s) will be buried to a minimum depth of 48 inches from the top of pipe to ground level. Erosion control methods such as gabions and/or rock aprons should be placed on both up and downstream sides of the pipeline crossing. In addition, curled (weed free) wood/straw fiber wattles/logs and/or silt fences should be placed on the downstream side for sediment control during construction and maintained until soils and vegetation have stabilized. Water bars should be placed within the ROW to divert and dissipate surface runoff. A pipeline access road is not permitted to cross these ephemeral drainages. Traffic should be diverted to a preexisting route. Additional seeding may be required in floodplains and drainages to restore energy dissipating vegetation.

Prior to pipeline installation/construction a leak detection plan will be developed. The method(s) could incorporate gauges to detect pressure drops, situating valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present.

The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.

ELECTRIC LINE(S):

Any water erosion that may occur due to the construction of overhead electric line and during the life of the power line will be quickly corrected and proper measures will be taken to prevent future erosion. A power pole should not be placed in drainages, playas, wetlands, riparian areas, or floodplains and must span across the features at a distance away that would not promote further erosion.

Range:**Cattleguards**

Where a permanent cattlegaurd is approved, an appropriately sized cattleguard(s) sufficient to carry out the project shall be installed and maintained at fence crossing(s). Any existing cattleguard(s) on the access road shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattleguard(s) that are in place and are utilized during lease operations. A gate shall be constructed on one side of the cattleguard and fastened securely to H-braces.

Fence Requirement

Where entry granted across a fence line, the fence must be braced and tied off on both sides of the passageway prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fence(s).

Livestock Watering Requirement

Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

VRM IV:

Above-ground structures including meter housing that are not subject to safety requirements are painted a flat non-reflective paint color, Shale Green from the BLM Standard Environmental Color Chart (CC-001: June 2008).

Short-term mitigation measures include painting all above-ground structures that are not subject to safety requirements (including meter housing) Shale Green, which is a flat non-reflective paint color listed in the BLM Standard Environmental Color Chart (CC-001: June 2013). Long-term mitigation measures include the removal of wells and associated infrastructure following abandonment (end of cost-effective production). Previously impacted areas will be reclaimed by removing structures and caliche pads, returning disturbed areas to natural grade, and revegetating with an approved BLM seed mixture; thereby eliminating visual impacts.

Lesser Prairie Chicken:**Timing Limitation Stipulation/Condition of Approval for Lesser Prairie-Chicken:**

Oil and gas activities including 3-D geophysical exploration, and drilling will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Additionally, no new drilling will be allowed within up to 200 meters of leks known at the time of permitting.

Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

Timing Limitation Exceptions:

The Carlsbad Field Office will publish an annual map of where the LPC timing and noise stipulations and conditions of approval (Limitations) will apply for the identified year (between March 1 and June 15) based on the latest survey information. The LPC Timing Area map will identify areas which are Habitat Areas (HA), Isolated Population Area (IPA), and Primary Population Area (PPA). The LPC Timing Area map will also have an area in red crosshatch. The red crosshatch area is the only area where an operator is required to submit a request for exception to the LPC Limitations. If an operator is operating outside the red crosshatch area, the LPC Limitations do not apply for that year and an exception to LPC Limitations is not required.

Ground-level Abandoned Well Marker to avoid raptor perching:

Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well. For more installation details, contact the Carlsbad Field Office at 575-234-5972.

V. CONSTRUCTION

A. NOTIFICATION

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

B. TOPSOIL

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

C. CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

D. FEDERAL MINERAL MATERIALS PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

E. WELL PAD SURFACING

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

F. EXCLOSURE FENCING (CELLARS & PITS)**Exclosure Fencing**

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

G. ON LEASE ACCESS ROADS**Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

Surfacing

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

Crowning

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

Ditching

Ditching shall be required on both sides of the road.


Turnouts

Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

Drainage

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outsloping and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

Cross Section of a Typical Lead-off Ditch

All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

Formula for Spacing Interval of Lead-off Ditches

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

Cattle guards

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

Fence Requirement

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

Public Access

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes

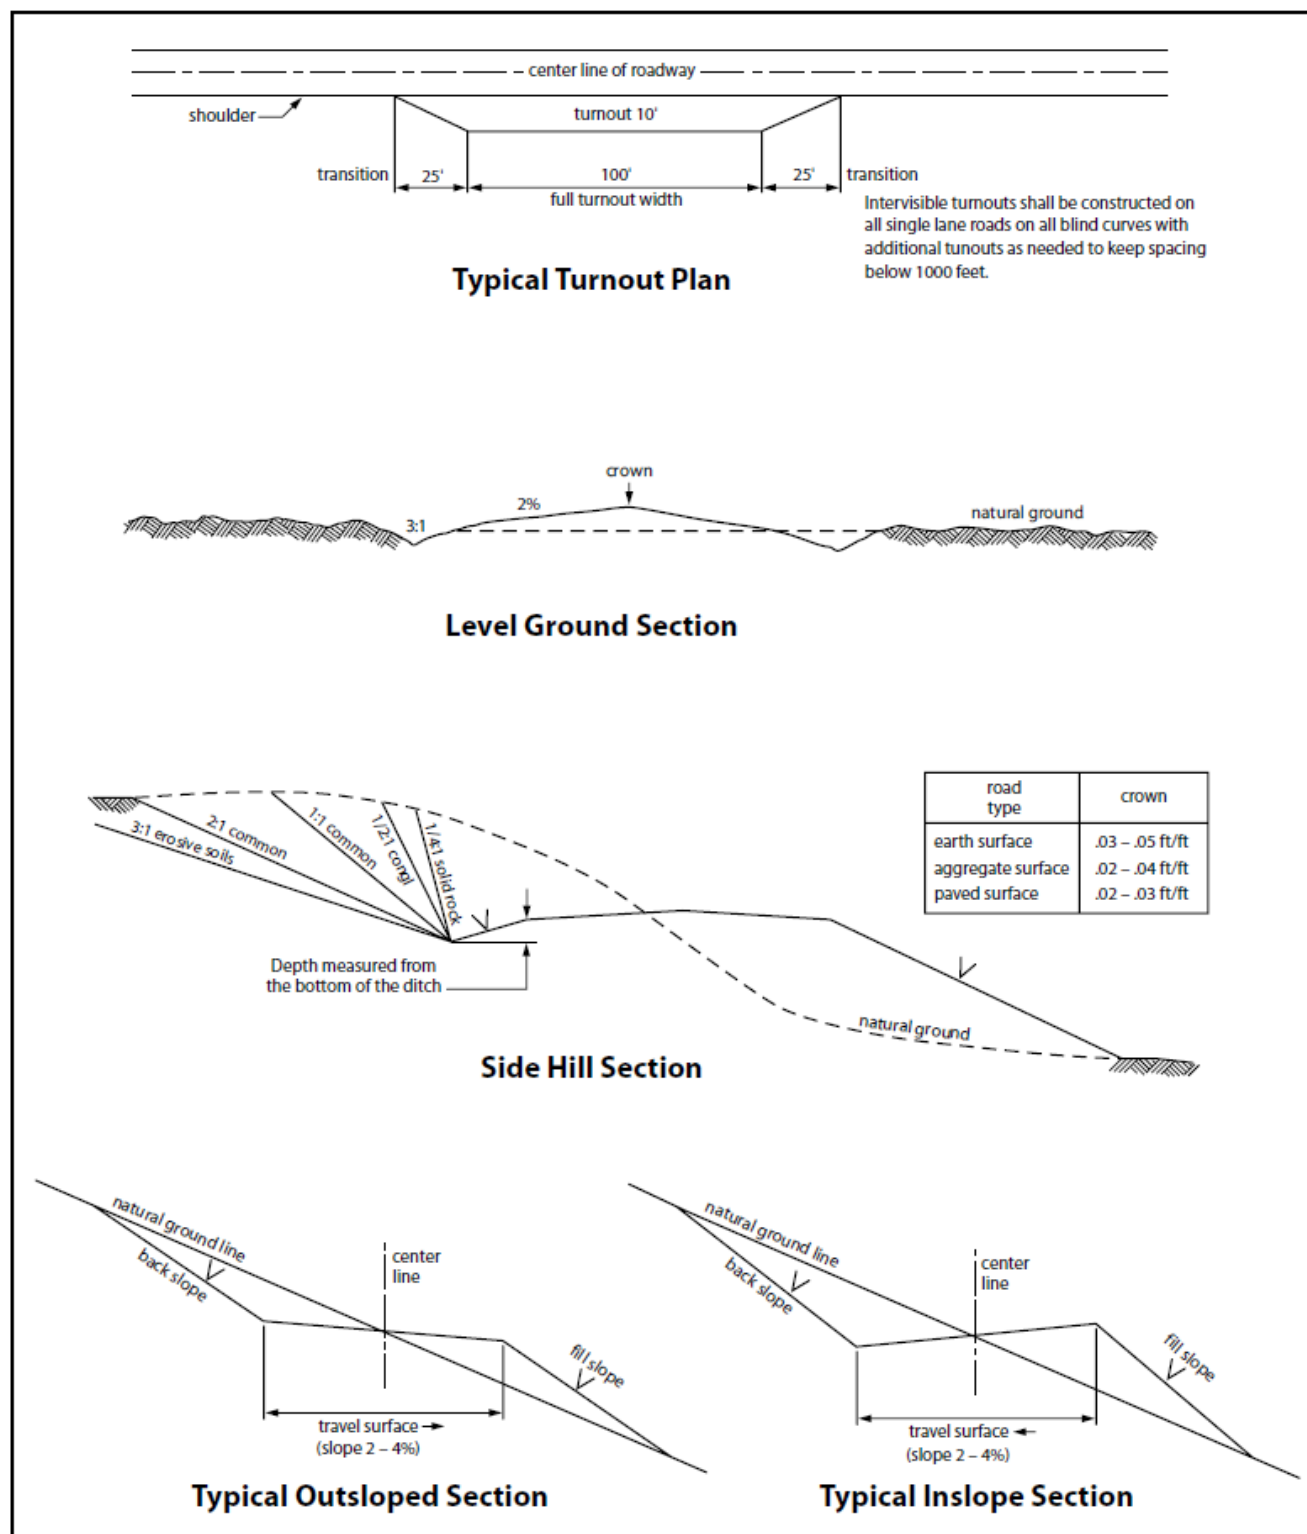


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

VI. PRODUCTION (POST DRILLING)

A. WELL STRUCTURES & FACILITIES

Placement of Production Facilities

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

Exclosure Netting (Open-top Tanks)

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

Chemical and Fuel Secondary Containment and Exclosure Screening

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

Open-Vent Exhaust Stack Exclosures

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

Containment Structures

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

Painting Requirement

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

B. PIPELINES

- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, passages, or voids are intersected by trenching, and no pipe will be laid in the trench at that point until clearance has been issued by the Authorized Officer.
- If a void is encountered alignments may be rerouted to avoid the karst feature and lessen; the potential of subsidence or collapse of karst features, buildup of toxic or combustible gas, or other possible impacts to cave and karst resources from the buried pipeline.
- Special restoration stipulations or realignment may be required at such intersections, if any.
- A leak detection plan **will be submitted to the BLM Carlsbad Field Office for approval** prior to pipeline installation. The method could incorporate gauges to detect pressure drops, siting valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.
- Regular monitoring is required to quickly identify leaks for their immediate and proper treatment.
- All spills or leaks will be reported to the BLM immediately for their immediate and proper treatment.

BURIED PIPELINE STIPULATIONS

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C.6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.

5. All construction and maintenance activity will be confined to the authorized right-of-way.

6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.

7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:

- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 20 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
- Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
- The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)

8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.

9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times.

The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.

11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.

12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- | | |
|--|--|
| <input type="checkbox"/> seed mixture 1 | <input type="checkbox"/> seed mixture 3 |
| <input checked="" type="checkbox"/> seed mixture 2 | <input type="checkbox"/> seed mixture 4 |
| <input type="checkbox"/> seed mixture 2/LPC | <input type="checkbox"/> Aplomado Falcon Mixture |

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 17 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

17. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

18. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

19. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

20. Escape Ramps - The operator will construct and maintain pipeline/utility trenches [that are not otherwise fenced, screened, or netted] to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.
- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

C. ELECTRIC LINES

- Smaller powerlines will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize changes to runoff or possible leaks and spills from entering karst systems. Larger powerlines will adjust their pole spacing to avoid cave and karst features.
- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, cave passages, or voids are penetrated during construction.
- No further construction will be done until clearance has been issued by the Authorized Officer.
- Special restoration stipulations or realignment may be required.

STANDARD STIPULATIONS FOR OVERHEAD ELECTRIC DISTRIBUTION LINES

A copy of the grant and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.)

Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. There will be no clearing or blading of the right-of-way unless otherwise agreed to in writing by the Authorized Officer.

5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the holder without liability or expense to the United States.

Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.

6. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

7. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.

8. Upon cancellation, relinquishment, or expiration of this grant, the holder shall comply with those abandonment procedures as prescribed by the Authorized Officer.

9. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this grant, whichever comes first. This will not apply where the power line extends service to an active, adjoining facility or facilities.

10. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 11 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

11. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

12. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

13. Special Stipulations:

For reclamation remove poles, lines, transformer, etc. and dispose of properly.
Fill in any holes from the poles removed.

VII. INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

VIII. FINAL ABANDONMENT & RECLAMATION

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Ground-level Abandoned Well Marker to avoid raptor perching: Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well.

Seed Mixture 2, for Sandy Sites

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law (s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed* per acre:

Species

	<u>lb/acre</u>
Sand dropseed (<i>Sporobolus cryptandrus</i>)	1.0
Sand love grass (<i>Eragrostis trichodes</i>)	1.0
Plains bristlegrass (<i>Setaria macrostachya</i>)	2.0

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed.

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	COG Production, LLC
LEASE NO.:	NMNM-029694
WELL NAME & NO.:	Eider 35 Federal Com 502H
SURFACE HOLE FOOTAGE:	0230' FSL & 1440' FWL
BOTTOM HOLE FOOTAGE:	0050' FNL & 1650' FWL Sec. 23, T.24 S., R.32 E.
LOCATION:	Section 35, T.24 S., R.32 E., NMPM
COUNTY:	Lea County, New Mexico

COA

H2S	<input checked="" type="radio"/> Yes	<input type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input checked="" type="radio"/> Conventional	<input type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input type="checkbox"/> Fluid Filled	<input type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit

Possible water flows in the Salado and Castile

Possible lost circulation in the Rustler, Red Beds, and Delaware

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H2S) Drilling Plan shall be activated 500 feet prior to drilling into the **Delaware** formation. As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **1010** feet (a minimum of 25 feet (Lea County) into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.
3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **2000 (2M)** psi.
2. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **3000 (3M)** psi.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
4. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
5. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
6. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- c. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- d. The results of the test shall be reported to the appropriate BLM office.
- e. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JAM 01082021

DISTRICT I

1025 N. FRENCH DR., MOORE, NM 88240
Phone: (505) 308-0101 Fax: (505) 308-0700

DISTRICT II

511 E. VIKING ST., ARTESIA, NM 88210
Phone: (505) 748-1253 Fax: (505) 748-0720

DISTRICT III

1000 ETO BRAZOS RD., AZTEC, NM 87410
Phone: (505) 334-0178 Fax: (505) 334-0170

DISTRICT IV

1220 S. ST. FRANCIS DR., SANTA FE, NM 87505
Phone: (505) 476-3485 Fax: (505) 476-3482

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 SOUTH ST. FRANCIS DR.
Santa Fe, New Mexico 87505

Form C-102

Revised August 1, 2011

Submit one copy to appropriate
District Office☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

API Number 30-025-49288	Pool Code 97964	Pool Name WC-025 G-08 S263225A; Lower Bone Spring
Property Code 331333	Property Name EIDER 35 FEDERAL COM	Well Number 502H
OGRIID No. 217955	Operator Name COG PRODUCTION, LLC	Elevation 3522.0'

Surface Location


UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
N	35	24-S	32-E		230	SOUTH	1440	WEST	LEA

Bottom Hole Location If Different From Surface

UL or lot No.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
C	23	24-S	32-E		50	NORTH	1650	WEST	LEA

Dedicated Acres	Joint or Infill	Consolidation Code	Order No.
960			

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED
OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

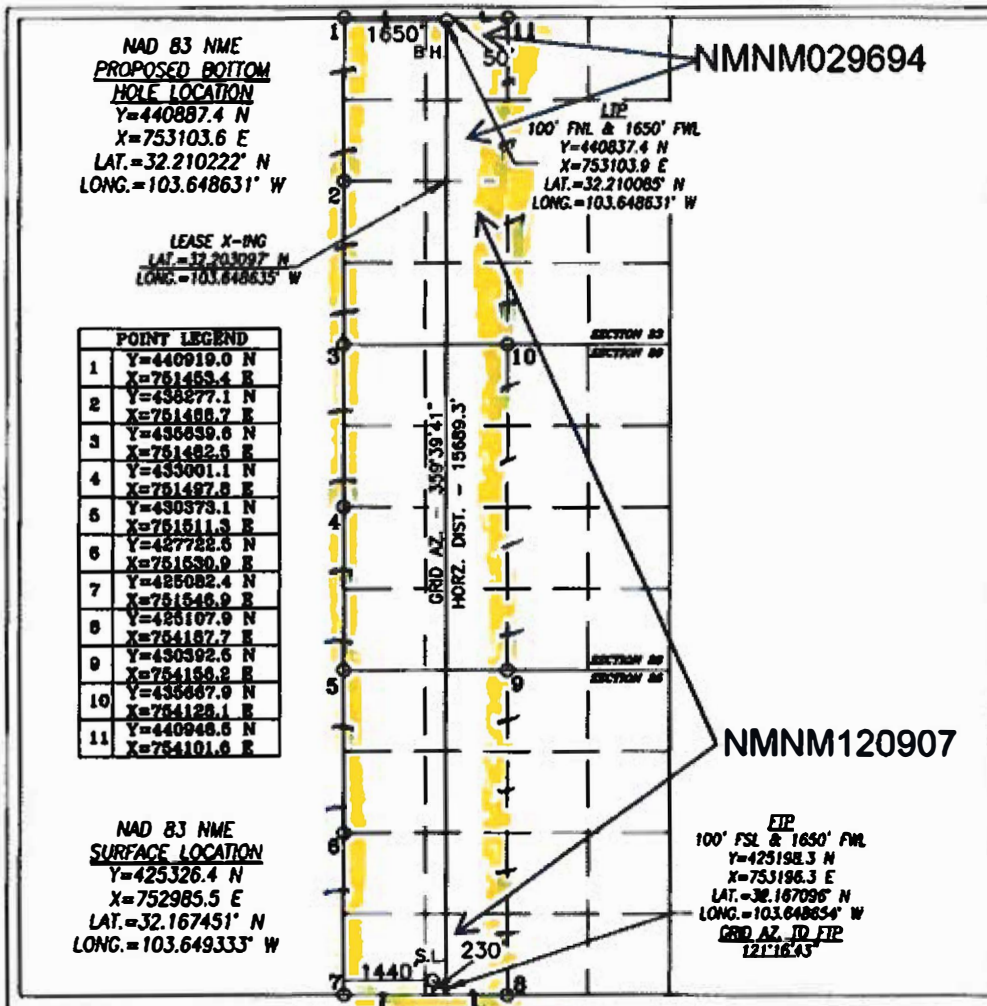

OPERATOR CERTIFICATION

I hereby certify that the information herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unless mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Signature: *Mayte Reyes* Date: *11-9-2020*

Printed Name
Mayte Reyes

E-mail Address
mreyes1@concho.com

E-mail Address

SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

OCTOBER 12, 2020

Date of Survey

Signature & Seal of Professional Surveyor



Signature: *Chad L. Harcrow* Date: *10/21/20*
Certificate No. CHAD HARCROW 17777
W.O. # 20-1359 DRAWN BY: AH

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: COG Production LLC **OGRID:** 217955 **Date:** 07 / 08 / 21

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Eider 35 Federal 502H		N-35-24S-32E	230 FSL & 1440 FWL	± 2378	± 3128	± 1751
30-025-49288						

IV. Central Delivery Point Name: _____ [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Eider 35 Federal 502H	Pending	4/16/22	± 25 days from spud	8/20/22	8/30/22	9/4/22
30-025-49288						

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☐ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

VI. Separation Equipment

How Operator will size separation equipment to optimize gas capture:

All ConocoPhillips production facility equipment will be sized per industry standards (API 12J) with adequate retention time to effectively separate all phases of production. Each project will take into consideration the number of wells and type curves for each formation pool to ensure adequate facility capacity. Design considerations will also include review of all piping, tanks, VRU's and associated equipment to ensure optimized gas capture minimized risk of release.

VII. Operational Practices

Actions Operator will take to comply with the requirements below:

B. Drilling Operations

- During drilling, flare stacks will be located a minimum of 100 feet from the nearest surface hole location. All gas is captured or combusted. If an emergency or malfunction occurs, gas will be flared or vented for public health, safety, and the environment and be properly reported to the NMOCD pursuant to 19.15.27.8.G.
- Measure or estimate the volume of natural gas that is vented, flared or beneficially used during drilling, completion and production operations, regardless of the reason or authorization for such venting or flaring.

C. Completion Operations

- During completion operations, operator does not produce oil or gas but maintains adequate well control through completion operations.
- Individual well test separators will be set to properly separate gas and liquids. A temporary test separator will be utilized initially to process volumes. In addition, separators will be tied into flowback tanks which will be tied into the gas processing equipment for sales down a pipeline.

D. Venting and flaring during production operations

- During each phase of well life (drilling, completion and production) of a ConocoPhillips well, COP personnel will follow all necessary procedures to ensure both the operation and the equipment are within the NMAC 19.15.27.8 Subsection D guidelines.
- During well operations that require unloading of the well to atmospheric pressure, all reasonable actions will be taken to minimize vented gas
- Through the life of the well all flaring shall be measured, and venting events quantified using the data available and industry best practice.

E. Performance standards for separation, storage tank and flare equipment

- All storage tanks and separation equipment are designed minimize risk of liquid or vapor release and optimize gas capture. This includes automation for automatic gauging and pressure monitoring.

- All flare stacks are equipped with auto ignition devices and/or continuous pilots and are designed to operate at maximum combustion efficiency pursuant NMAC 19.15.27.8 Subsection E. Flares will follow COP spacing guidelines to ensure they are a safe distance from combustibles and operations equipment.
- COP personnel will conduct routine AVO inspections on a regular basis per NMAC 19.15.27.8 Subsection E guidelines.

F. Measurement of vented and flared natural gas.

- Measurement equipment will be installed to quantify gas flared during drilling, completion and production of the well.
- All measurement devices installed will meet accuracy ratings per AGA and API standards.
- Measurement devices will be installed without manifolds that allow diversion of gas around the metering element, except for the sole purpose of inspection of servicing the measurement device.

VIII. Best Management Practices

- Operator will curtail or shut in production, within reasonable limits, during upset conditions to minimize venting and flaring.
- When feasible, Operator will use equipment to capture gas that would otherwise be vented or flared.
- During completions and production operations Operator will minimize blowdowns to atmosphere
- When feasible, Operator will use electric or air actuated equipment to reduce bleed emissions

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: <i>Mayte Reyes</i>
Printed Name: Mayte Reyes
Title: Sr. Regulatory Coordinator
E-mail Address: mayte.x.reyes@conocophillips.com
Date: 7/08/2021
Phone: 575-748-6945
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

APD Print Report

05/18/2021

APD ID: 10400065052

Submission Date: 11/10/2020

Highlighted data
reflects the most
recent changes

Operator Name: COG PRODUCTION LLC

Federal/Indian APD: FED

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

[Show Final Text](#)

Well Type: OIL WELL

Well Work Type: Drill

Application

Section 1 - General

APD ID: 10400065052

Tie to previous NOS? N

Submission Date: 11/10/2020

BLM Office: CARLSBAD

User: MAYTE REYES

Title: Regulatory Analyst

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMNM120907

Lease Acres:

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? NO

Federal or Indian agreement:

Agreement number:

Agreement name:

Keep application confidential? Y

Permitting Agent? NO

APD Operator: COG PRODUCTION LLC

Operator letter of designation:

Operator Info

Operator Organization Name: COG PRODUCTION LLC

Operator Address: 2208 West Main Street

Zip: 88210

Operator PO Box:

Operator City: Artesia

State: NM

Operator Phone: (575)748-6940

Operator Internet Address: mreyes1@concho.com

Section 2 - Well Information

Well in Master Development Plan? NO

Master Development Plan name:

Well in Master SUPO? NO

Master SUPO name:

Approval Date: 04/22/2021

Page 1 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Well in Master Drilling Plan?** NO**Master Drilling Plan name:****Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Well API Number:****Field/Pool or Exploratory?** Field and Pool**Field Name:** WC-025 G-08
S263225A**Pool Name:** LOWER BONE
SPRING**Is the proposed well in an area containing other mineral resources?** NATURAL GAS,OIL**Is the proposed well in a Helium production area?** N**Use Existing Well Pad?** N**New surface disturbance?****Type of Well Pad:** MULTIPLE WELL**Multiple Well Pad Name:** EIDER**Number:** 501H and 502H
35 FEDERAL COM**Well Class:** HORIZONTAL**Number of Legs:** 1**Well Work Type:** Drill**Well Type:** OIL WELL**Describe Well Type:****Well sub-Type:** EXPLORATORY (WILDCAT)**Describe sub-type:****Distance to town:** 24 Miles**Distance to nearest well:** 30 FT**Distance to lease line:** 50 FT**Reservoir well spacing assigned acres Measurement:** 480 Acres**Well plat:** COG_Eider_35_502H_C102_20201110090803.pdf**Well work start Date:** 02/01/2021**Duration:** 30 DAYS**Section 3 - Well Location Table****Survey Type:** RECTANGULAR**Describe Survey Type:****Datum:** NAD83**Vertical Datum:** NAVD88**Survey number:****Reference Datum:** GROUND LEVEL

Wellbore	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD	Will this well produce from this lease?
SHL Leg #1	230	FSL	1440	FWL	24S	32E	35	Aliquot SESW 1	32.167451	-103.649333	LEA	NEW MEXICO	NEW MEXICO	F	NMNM 120907	3522	0	0	Y
KOP Leg #1	230	FSL	1440	FWL	24S	32E	35	Aliquot SESW 1	32.167451	-103.649333	LEA	NEW MEXICO	NEW MEXICO	F	NMNM 120907	3522	0	0	Y

Approval Date: 04/22/2021

Page 2 of 23

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Wellbore	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD	Will this well produce from this lease?
PPP Leg #1-1	100	FSL	1650	FWL	24S	32E	35	Aliquot SESW	32.167096	-103.648654	LEA	NEW MEXICO	NEW MEXICO	F	NMNM 120907	-6973	10566	10495	Y
EXIT Leg #1	100	FNL	1650	FWL	24S	32E	23	Aliquot NENW	32.210085	-103.648631	LEA	NEW MEXICO	NEW MEXICO	F	NMNM 29694	-7127	26072	10649	Y
BHL Leg #1	50	FNL	1650	FWL	24S	32E	23	Aliquot NENW	32.210222	-103.648631	LEA	NEW MEXICO	NEW MEXICO	F	NMNM 29694	-7127	26122	10649	Y

Drilling Plan

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
1139498	---	3522	0	0	ALLUVIUM	NONE	N
1139502	RUSTLER	2578	944	944	ALLUVIUM	NONE	N
1139503	TOP SALT	2257	1265	1265	SALT	NONE	N
1139504	BASE OF SALT	-1075	4597	4597	ANHYDRITE	NONE	N
1139509	LAMAR	-1292	4814	4814	LIMESTONE	NONE	N
1139510	BELL CANYON	-1361	4883	4883	LIMESTONE	NONE	N
1139505	CHERRY CANYON	-2246	5768	5768	SANDSTONE	NATURAL GAS, OIL	N
1139511	BRUSHY CANYON	-3661	7183	7183	SANDSTONE	NATURAL GAS, OIL	N
1139506	BONE SPRING LIME	-5253	8775	8775	SHALE	NATURAL GAS, OIL	N
1139501	UPPER AVALON SHALE	-5626	9148	9148	SHALE, SILTSTONE	NATURAL GAS, OIL	N
1139512	---	-6000	9522	9522	SHALE, SILTSTONE	NATURAL GAS, OIL	N

Approval Date: 04/22/2021

Page 3 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
1139507	BONE SPRING 1ST	-6373	9895	9895	SANDSTONE	NATURAL GAS, OIL	N
1139508	BONE SPRING 2ND	-7026	10548	10548	SANDSTONE	NATURAL GAS, OIL	Y

Section 2 - Blowout Prevention

Pressure Rating (PSI): 2M**Rating Depth:** 4800

Equipment: Annular. The BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold.

Requesting Variance? NO

Variance request: A variance is requested for the use of a flexible choke line from the BOP to choke manifold. See attached for specs and hydrostatic test chart.

Testing Procedure: BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all of the components installed will be functional and tested.

Choke Diagram Attachment:

COG_Eider_2M_Choke_20201110084015.pdf

BOP Diagram Attachment:

COG_Eider_Flex_Hose_Variance_20201107144844.pdf

COG_Eider_2M_BOP_20201110084028.pdf

Pressure Rating (PSI): 3M**Rating Depth:** 10649

Equipment: Annular. Blind Ram. Pipe Ram. The BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold.

Requesting Variance? YES

Variance request: A variance is requested for the use of a flexible choke line from the BOP to choke manifold. See attached for specs and hydrostatic test chart.

Testing Procedure: BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all of the components installed will be functional and tested.

Choke Diagram Attachment:

COG_Eider_3M_Choke_20201110084444.pdf

BOP Diagram Attachment:

COG_Eider_Flex_Hose_Variance_20201107144917.pdf

COG_Eider_3M_BOP_20201110084456.pdf

Approval Date: 04/22/2021

Page 4 of 23

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	970	0	970	3522	2552	970	J-55	54.5	ST&C	2.55	1.26	DRY	9.72	DRY	9.72
2	INTERMEDIATE	12.25	9.625	NEW	API	Y	0	4800	0	3500	-6907	22	4800	L-80	40	LT&C	1.23	1.41	DRY	6.54	DRY	6.54
3	PRODUCTION	8.75	5.5	NEW	API	N	0	26122	0	10649	-6907	-7127	26122	P-110	17	LT&C	1.45	2.6	DRY	2.46	DRY	2.46

Casing Attachments

Casing ID: 1 String Type: SURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

COG_Eider_35_502H_Casing_Prog_20201110102641.pdf

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Casing Attachments

Casing ID: 2 String Type: INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

COG_Eider_35_502H_Casing_Prog_20201110102705.pdf

Casing Design Assumptions and Worksheet(s):

COG_Eider_35_502H_Casing_Prog_20201110102723.pdf

Casing ID: 3 String Type: PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

COG_Eider_35_502H_Casing_Prog_20201110102807.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead	1	0	970	390	1.75	13.5	682	50	Class C	4% Gel + 1% CaCl ₂
SURFACE	Tail		0	970	250	1.34	14.8	335	50	C	2% CaCl ₂
INTERMEDIATE	Lead	1	0	4800	910	2	12.7	1820	50	35:65:6 C Blend	No additives
INTERMEDIATE	Tail		0	4800	250	1.34	14.8	335	50	Class C	2% CaCl

Approval Date: 04/22/2021

Page 6 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
PRODUCTION	Lead	1	3000	2612 2	820	2.5	11.9	2050	25	Lead: 50:50:10 H Blend	No additives
PRODUCTION	Tail		3000	2612 2	4070	1.24	14.4	5046	25	Tail: 50:50:2 Class H Blend	No additives

Section 5 - Circulating Medium

Mud System Type: Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:****Describe what will be on location to control well or mitigate other conditions:** Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times**Describe the mud monitoring system utilized:** PVT/Pason/Visual Monitoring

Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
970	4800	OTHER : Saturated Brine	10	10.1							Saturated Brine
4800	2612 2	OTHER : Cut Brine	8.6	9.3							Cut Brine
0	970	OTHER : Fresh water gel	8.6	8.8							Fresh water gel

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

None planned

List of open and cased hole logs run in the well:

COMPENSATED NEUTRON LOG, GAMMA RAY LOG,

Coring operation description for the well:

None planned

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 5150**Anticipated Surface Pressure:** 2807**Anticipated Bottom Hole Temperature(F):** 165**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO**Describe:****Contingency Plans geohazards description:****Contingency Plans geohazards attachment:****Hydrogen Sulfide drilling operations plan required?** YES**Hydrogen sulfide drilling operations plan:**

COG_Eider_35_501H_502H_H2S_Schematic_20201110090156.pdf

COG_Eider_H2S_Plan_20201107144816.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

COG_Eider_35_502H_AC_RPT_20201110103156.pdf

COG_Eider_35_502H_Directional_Plan_20201110103202.pdf

Other proposed operations facets description:

Drilling Program.

Cement Program.

GCP.

Other proposed operations facets attachment:

COG_Eider_35_502H_Drilling_Prog_20201110103216.pdf

COG_Eider_35_502H_Cement_Prog_20201110103224.pdf

COG_Eider_35_502H_GCP_20201110103231.pdf

Other Variance attachment:

SUPO

Approval Date: 04/22/2021

Page 8 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Section 1 - Existing Roads****Will existing roads be used?** YES**Existing Road Map:**

COG_Eider_35_Existing_Road_20201109161810.pdf

Existing Road Purpose: ACCESS**Row(s) Exist?** YES**ROW ID(s)****ID:****Do the existing roads need to be improved?** NO**Existing Road Improvement Description:****Existing Road Improvement Attachment:****Section 2 - New or Reconstructed Access Roads****Will new roads be needed?** YES**New Road Map:**

COG_Eider_35_Road_Plat_20201109161904.pdf

New road type: RESOURCE**Length:** 162.4 Feet**Width (ft.):** 30**Max slope (%):** 33**Max grade (%):** 1**Army Corp of Engineers (ACOE) permit required?** N**ACOE Permit Number(s):****New road travel width:** 14**New road access erosion control:** Water will be diverted where necessary to avoid ponding, prevent erosion, maintain good drainage and to be consistent with local drainage patterns.**New road access plan or profile prepared?** N**New road access plan attachment:****Access road engineering design?** N**Access road engineering design attachment:****Turnout?** N**Access surfacing type:** OTHER

Approval Date: 04/22/2021

Page 9 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Access topsoil source:** OFFSITE**Access surfacing type description:** Caliche**Access onsite topsoil source depth:****Offsite topsoil source description:** Caliche**Onsite topsoil removal process:****Access other construction information:****Access miscellaneous information:****Number of access turnouts:****Access turnout map:****Drainage Control****New road drainage crossing:** OTHER**Drainage Control comments:** None needed.**Road Drainage Control Structures (DCS) description:** None needed.**Road Drainage Control Structures (DCS) attachment:****Access Additional Attachments****Section 3 - Location of Existing Wells****Existing Wells Map?** YES**Attach Well map:**

COG_Eider_35_502H_1_Mile_Data_20201110092620.pdf

Section 4 - Location of Existing and/or Proposed Production Facilities**Submit or defer a Proposed Production Facilities plan?** SUBMIT

Production Facilities description: The existing Eider Fed 35 N CTB. This CTB will be modified to accommodate the Eider Fed Com #701H, #702, #501, #502. We plan to install (1) buried 4 FP 601HT production flowline from each wellhead to the inlet manifold of the proposed CTB (4 lines total); the route for these flowlines will follow the flowlines route as shown in the diagram below. We will install (1) buried 4 gas lines for gas lift supply from the CTB to each well pad (2 lines total); the route for the gas lift lines will follow the gas lift route as shown in the attached layout.

Production Facilities map:

COG_Eider_35_N_CTB_20201109161958.pdf

Section 5 - Location and Types of Water Supply**Water Source Table**

Approval Date: 04/22/2021

Page 10 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Water source type:** OTHER**Describe type:** Fresh Water. See Below.

Water source use type: ICE PAD CONSTRUCTION &
MAINTENANCE
SURFACE CASING
STIMULATION

Source latitude:**Source longitude:****Source datum:****Water source permit type:** PRIVATE CONTRACT**Water source transport method:** PIPELINE**Source land ownership:** PRIVATE**Source transportation land ownership:** PRIVATE**Water source volume (barrels):** 450000**Source volume (acre-feet):** 58.001892**Source volume (gal):** 18900000**Water source type:** OTHER**Describe type:** Brine Water. See Below.

Water source use type: INTERMEDIATE/PRODUCTION
CASING

Source latitude:**Source longitude:****Source datum:****Water source permit type:** PRIVATE CONTRACT**Water source transport method:** TRUCKING**Source land ownership:** COMMERCIAL**Source transportation land ownership:** COMMERCIAL**Water source volume (barrels):** 30000**Source volume (acre-feet):** 3.866793**Source volume (gal):** 1260000

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Water source and transportation map:

COG_Eider_35_500s_700s_Brine_H2O_20201109162045.pdf

COG_Eider_35_500s_700s_Fresh_H2O_20201109162051.pdf

Water source comments: Fresh water will be obtained from the Gadwall Frac Pond located in Section 26. T24S. R32E. Brine water will be obtained from the Malaga II Brine station in Section 12. T23S. R28E.

New water well? N**New Water Well Info****Well latitude:****Well Longitude:****Well datum:****Well target aquifer:****Est. depth to top of aquifer(ft):****Est thickness of aquifer:****Aquifer comments:****Aquifer documentation:****Well depth (ft):****Well casing type:****Well casing outside diameter (in.):****Well casing inside diameter (in.):****New water well casing?****Used casing source:****Drilling method:****Drill material:****Grout material:****Grout depth:****Casing length (ft.):****Casing top depth (ft.):****Well Production type:****Completion Method:****Water well additional information:****State appropriation permit:****Additional information attachment:****Section 6 - Construction Materials****Using any construction materials:** YES

Construction Materials description: Caliche will be obtained from the actual well site if available. If not available onsite, caliche will be hauled from Mack Chase caliche pit located in Section 20, T24S, R33E. Phone # (575) 748-1288.

Construction Materials source location attachment:**Section 7 - Methods for Handling Waste****Waste type:** SEWAGE**Waste content description:** Human waste and gray water**Amount of waste:** 1000 gallons**Waste disposal frequency :** One Time Only**Safe containment description:** Waste will be properly contained and disposed of properly at a state approved disposal

Approval Date: 04/22/2021

Page 12 of 23

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

facility.

Safe containmant attachment:**Waste disposal type:** HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** PRIVATE**Disposal type description:****Disposal location description:** Trucked to an approved disposal facility**Waste type:** GARBAGE**Waste content description:** Garbage and trash produced during drilling and completion operations.**Amount of waste:** 500 pounds**Waste disposal frequency :** One Time Only**Safe containment description:** Garbage and trash produced during drilling and completion operations will be collected in a trash container and disposed of properly at a state approved disposal facility**Safe containmant attachment:****Waste disposal type:** HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL**Disposal type description:****Disposal location description:** Trucked to an approved disposal facility.**Waste type:** DRILLING**Waste content description:** Drilling fluids and produced oil land water while drilling and completion operations**Amount of waste:** 6000 barrels**Waste disposal frequency :** One Time Only**Safe containment description:** All drilling waste will be stored safely and disposed of properly**Safe containmant attachment:****Waste disposal type:** HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL**Disposal type description:****Disposal location description:** Trucked to an approved disposal facility**Reserve Pit****Reserve Pit being used?** NO**Temporary disposal of produced water into reserve pit?** NO**Reserve pit length (ft.)** **Reserve pit width (ft.)****Reserve pit depth (ft.)** **Reserve pit volume (cu. yd.)****Is at least 50% of the reserve pit in cut?**

Approval Date: 04/22/2021

Page 13 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Reserve pit liner****Reserve pit liner specifications and installation description**

Cuttings Area

Cuttings Area being used? NO**Are you storing cuttings on location?** Y**Description of cuttings location** Roll off cutting containers on tracks**Cuttings area length (ft.)****Cuttings area width (ft.)****Cuttings area depth (ft.)****Cuttings area volume (cu. yd.)****Is at least 50% of the cuttings area in cut?****WCuttings area liner****Cuttings area liner specifications and installation description**

Section 8 - Ancillary Facilities

Are you requesting any Ancillary Facilities?: N**Ancillary Facilities attachment:****Comments:**

Section 9 - Well Site Layout

Well Site Layout Diagram:

COG_Eider_35_501H_502H_Layout_20201109171058.pdf

Comments:

Section 10 - Plans for Surface Reclamation

Type of disturbance: New Surface Disturbance**Multiple Well Pad Name:** EIDER 35 FEDERAL COM**Multiple Well Pad Number:** 501H and 502H**Recontouring attachment:**

COG_Eider_35_501H_502H_Reclamation_20201109171114.pdf

Drainage/Erosion control construction: Immediately following construction, straw waddles will be placed as necessary at the well site to reduce sediment impacts to fragile/sensitive soils.**Drainage/Erosion control reclamation:** North 50'.

Approval Date: 04/22/2021

Page 14 of 23

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Well pad proposed disturbance (acres): 3.67	Well pad interim reclamation (acres): 0.06	Well pad long term disturbance (acres): 2.81
Road proposed disturbance (acres): 0.06	Road interim reclamation (acres): 0.06	Road long term disturbance (acres): 0.06
Powerline proposed disturbance (acres): 0	Powerline interim reclamation (acres): 0	Powerline long term disturbance (acres): 0
Pipeline proposed disturbance (acres): 0.11	Pipeline interim reclamation (acres): 0.11	Pipeline long term disturbance (acres): 0.11
Other proposed disturbance (acres): 3.67	Other interim reclamation (acres): 3.67	Other long term disturbance (acres): 3.67
Total proposed disturbance: 7.51	Total interim reclamation: 3.9	Total long term disturbance: 6.65

Disturbance Comments:

Reconstruction method: Portions of the pad not needed for production operations will be re-contoured to its original state as much as possible. The caliche that is removed will be reused. The stockpiled topsoil will be spread out over reclaimed area and reseeded with BLM approved seed mixture.

Topsoil redistribution: North 50'.

Soil treatment: None

Existing Vegetation at the well pad: Shinnery Oak/Mesquite grassland

Existing Vegetation at the well pad attachment:

Existing Vegetation Community at the road: Shinnery Oak/Mesquite grassland

Existing Vegetation Community at the road attachment:

Existing Vegetation Community at the pipeline: Shinnery Oak/Mesquite grassland

Existing Vegetation Community at the pipeline attachment:

Existing Vegetation Community at other disturbances: N/A

Existing Vegetation Community at other disturbances attachment:

Non native seed used? N

Non native seed description:

Seedling transplant description:

Will seedlings be transplanted for this project? N

Seedling transplant description attachment:

Will seed be harvested for use in site reclamation? N

Seed harvest description:

Seed harvest description attachment:

Approval Date: 04/22/2021

Page 15 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Seed Management****Seed Table****Seed Summary****Total pounds/Acre:****Seed Type****Pounds/Acre****Seed reclamation attachment:****Operator Contact/Responsible Official Contact Info****First Name:****Last Name:****Phone:****Email:****Seedbed prep:****Seed BMP:****Seed method:****Existing invasive species?** N**Existing invasive species treatment description:****Existing invasive species treatment attachment:****Weed treatment plan description:** N/A**Weed treatment plan attachment:****Monitoring plan description:** N/A**Monitoring plan attachment:****Success standards:** N/A**Pit closure description:** N/A**Pit closure attachment:**

COG_Eider_Closed_Loop_20201107161726.pdf

Section 11 - Surface Ownership

Approval Date: 04/22/2021

Page 16 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Disturbance type:** WELL PAD**Describe:****Surface Owner:** BUREAU OF LAND MANAGEMENT**Other surface owner description:****BIA Local Office:****BOR Local Office:****COE Local Office:****DOD Local Office:****NPS Local Office:****State Local Office:****Military Local Office:****USFWS Local Office:****Other Local Office:****USFS Region:****USFS Forest/Grassland:****USFS Ranger District:**

Section 12 - Other Information

Right of Way needed? N**Use APD as ROW?****ROW Type(s):**

ROW Applications

SUPO Additional Information: SUP Attached**Use a previously conducted onsite?** Y**Previous Onsite information:** Onsite completed on October 6th, 2020 by Gerald Herrera (COG) and Zane Kirsch (BLM).

Other SUPO Attachment

Approval Date: 04/22/2021

Page 17 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H

COG_Eider_35_501H_502H_Layout_20201109171237.pdf

COG_Eider_35_501H_502H_Reclamation_20201109171242.pdf

COG_Eider_35_Existing_Road_20201109162401.pdf

COG_Eider_35_Flow_Gas_Line_20201109162446.pdf

COG_Eider_35_N_CTB_20201109162332.pdf

COG_Eider_35_Road_Plat_20201109162354.pdf

COG_Eider_35_502H_C102_20201110092708.pdf

COG_Eider_35_502H_SUP_20201110092724.pdf

PWD

Section 1 - General**Would you like to address long-term produced water disposal?** NO**Section 2 - Lined Pits****Would you like to utilize Lined Pit PWD options?** N**Produced Water Disposal (PWD) Location:****PWD surface owner:****PWD disturbance (acres):****Lined pit PWD on or off channel:****Lined pit PWD discharge volume (bbl/day):****Lined pit specifications:****Pit liner description:****Pit liner manufacturers information:****Precipitated solids disposal:****Describe precipitated solids disposal:****Precipitated solids disposal permit:****Lined pit precipitated solids disposal schedule:****Lined pit precipitated solids disposal schedule attachment:**

Approval Date: 04/22/2021

Page 18 of 23

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Lined pit reclamation description:

Lined pit reclamation attachment:

Leak detection system description:

Leak detection system attachment:

Lined pit Monitor description:

Lined pit Monitor attachment:

Lined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Lined pit bond number:

Lined pit bond amount:

Additional bond information attachment:

Section 3 - Unlined Pits

Would you like to utilize Unlined Pit PWD options? N

Produced Water Disposal (PWD) Location:

PWD disturbance (acres):

PWD surface owner:

Unlined pit PWD on or off channel:

Unlined pit PWD discharge volume (bbl/day):

Unlined pit specifications:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Unlined pit precipitated solids disposal schedule:

Unlined pit precipitated solids disposal schedule attachment:

Unlined pit reclamation description:

Unlined pit reclamation attachment:

Unlined pit Monitor description:

Unlined pit Monitor attachment:

Do you propose to put the produced water to beneficial use?

Beneficial use user confirmation:

Estimated depth of the shallowest aquifer (feet):

Does the produced water have an annual average Total Dissolved Solids (TDS) concentration equal to or less than that of the existing water to be protected?

Approval Date: 04/22/2021

Page 19 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**TDS lab results:****Geologic and hydrologic evidence:****State authorization:****Unlined Produced Water Pit Estimated percolation:****Unlined pit: do you have a reclamation bond for the pit?****Is the reclamation bond a rider under the BLM bond?****Unlined pit bond number:****Unlined pit bond amount:****Additional bond information attachment:**

Section 4 - Injection

Would you like to utilize Injection PWD options? N**Produced Water Disposal (PWD) Location:****PWD surface owner:****PWD disturbance (acres):****Injection PWD discharge volume (bbl/day):****Injection well mineral owner:****Injection well type:****Injection well number:****Injection well name:****Assigned injection well API number?****Injection well API number:****Injection well new surface disturbance (acres):****Minerals protection information:****Mineral protection attachment:****Underground Injection Control (UIC) Permit?****UIC Permit attachment:**

Section 5 - Surface Discharge

Would you like to utilize Surface Discharge PWD options? N**Produced Water Disposal (PWD) Location:****PWD surface owner:****PWD disturbance (acres):****Surface discharge PWD discharge volume (bbl/day):****Surface Discharge NPDES Permit?****Surface Discharge NPDES Permit attachment:**

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Surface Discharge site facilities information:****Surface discharge site facilities map:****Section 6 - Other****Would you like to utilize Other PWD options?** N**Produced Water Disposal (PWD) Location:****PWD surface owner:****PWD disturbance (acres):****Other PWD discharge volume (bbl/day):****Other PWD type description:****Other PWD type attachment:****Have other regulatory requirements been met?****Other regulatory requirements attachment:****Bond Info****Bond Information****Federal/Indian APD:** FED**BLM Bond number:****BIA Bond number:****Do you have a reclamation bond?** NO**Is the reclamation bond a rider under the BLM bond?****Is the reclamation bond BLM or Forest Service?****BLM reclamation bond number:****Forest Service reclamation bond number:****Forest Service reclamation bond attachment:****Reclamation bond number:****Reclamation bond amount:****Reclamation bond rider amount:****Additional reclamation bond information attachment:****Operator Certification**

Approval Date: 04/22/2021

Page 21 of 23

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Operator Certification**

I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.

NAME: MAYTE REYES**Signed on:** 11/10/2020**Title:** Regulatory Analyst**Street Address:** 925 N ELDRIDGE PARKWAY**City:** HOUSTON**State:** TX**Zip:** 77252**Phone:** (281)293-1000**Email address:** MAYTE.X.REYES@CONOCOPHILLIPS.COM**Field Representative****Representative Name:** Gerald Herrera**Street Address:** 2208 West Main Street**City:** Artesia**State:** NM**Zip:** 88210**Phone:** (575)748-6940**Email address:** gherrera@concho.com**Payment Info****Payment****APD Fee Payment Method:** PAY.GOV**pay.gov Tracking ID:** 26QE4FVU

Approval Date: 04/22/2021

Page 22 of 23

CONFIDENTIAL



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

05/18/2021

APD ID: 10400065052

Submission Date: 11/10/2020

Highlighted data
reflects the most
recent changes

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

[Show Final Text](#)

Well Type: OIL WELL

Well Work Type: Drill

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
1139498	---	3522	0	0	ALLUVIUM	NONE	N
1139502	RUSTLER	2578	944	944	ALLUVIUM	NONE	N
1139503	TOP SALT	2257	1265	1265	SALT	NONE	N
1139504	BASE OF SALT	-1075	4597	4597	ANHYDRITE	NONE	N
1139509	LAMAR	-1292	4814	4814	LIMESTONE	NONE	N
1139510	BELL CANYON	-1361	4883	4883	LIMESTONE	NONE	N
1139505	CHERRY CANYON	-2246	5768	5768	SANDSTONE	NATURAL GAS, OIL	N
1139511	BRUSHY CANYON	-3661	7183	7183	SANDSTONE	NATURAL GAS, OIL	N
1139506	BONE SPRING LIME	-5253	8775	8775	SHALE	NATURAL GAS, OIL	N
1139501	UPPER AVALON SHALE	-5626	9148	9148	SHALE, SILTSTONE	NATURAL GAS, OIL	N
1139512	---	-6000	9522	9522	SHALE, SILTSTONE	NATURAL GAS, OIL	N
1139507	BONE SPRING 1ST	-6373	9895	9895	SANDSTONE	NATURAL GAS, OIL	N
1139508	BONE SPRING 2ND	-7026	10548	10548	SANDSTONE	NATURAL GAS, OIL	Y

Section 2 - Blowout Prevention

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H**Pressure Rating (PSI):** 2M**Rating Depth:** 4800**Equipment:** Annular. The BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold.**Requesting Variance?** NO**Variance request:** A variance is requested for the use of a flexible choke line from the BOP to choke manifold. See attached for specs and hydrostatic test chart.**Testing Procedure:** BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all of the components installed will be functional and tested.**Choke Diagram Attachment:**

COG_Eider_2M_Choke_20201110084015.pdf

BOP Diagram Attachment:

COG_Eider_Flex_Hose_Variance_20201107144844.pdf

COG_Eider_2M_BOP_20201110084028.pdf

Pressure Rating (PSI): 3M**Rating Depth:** 10649**Equipment:** Annular. Blind Ram. Pipe Ram. The BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold.**Requesting Variance?** YES**Variance request:** A variance is requested for the use of a flexible choke line from the BOP to choke manifold. See attached for specs and hydrostatic test chart.**Testing Procedure:** BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all of the components installed will be functional and tested.**Choke Diagram Attachment:**

COG_Eider_3M_Choke_20201110084444.pdf

BOP Diagram Attachment:

COG_Eider_Flex_Hose_Variance_20201107144917.pdf

COG_Eider_3M_BOP_20201110084456.pdf

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	970	0	970	3522	2552	970	J-55	54.5	ST&C	2.55	1.26	DRY	9.72	DRY	9.72
2	INTERMEDIATE	12.25	9.625	NEW	API	Y	0	4800	0	3500	-6907	22	4800	L-80	40	LT&C	1.23	1.41	DRY	6.54	DRY	6.54
3	PRODUCTION	8.75	5.5	NEW	API	N	0	26122	0	10649	-6907	-7127	26122	P-110	17	LT&C	1.45	2.6	DRY	2.46	DRY	2.46

Casing Attachments

Casing ID: 1 String Type: SURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

COG_Eider_35_502H_Casing_Prog_20201110102641.pdf

Operator Name: COG PRODUCTION LLC

Well Name: EIDER 35 FEDERAL COM

Well Number: 502H

Casing Attachments

Casing ID: 2 String Type: INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

COG_Eider_35_502H_Casing_Prog_20201110102705.pdf

Casing Design Assumptions and Worksheet(s):

COG_Eider_35_502H_Casing_Prog_20201110102723.pdf

Casing ID: 3 String Type: PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

COG_Eider_35_502H_Casing_Prog_20201110102807.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead	1	0	970	390	1.75	13.5	682	50	Class C	4% Gel + 1% CaCl2
SURFACE	Tail		0	970	250	1.34	14.8	335	50	C	2% CaCl2
INTERMEDIATE	Lead	1	0	4800	910	2	12.7	1820	50	35:65:6 C Blend	No additives
INTERMEDIATE	Tail		0	4800	250	1.34	14.8	335	50	Class C	2% CaCl
PRODUCTION	Lead	1	3000	2612 2	820	2.5	11.9	2050	25	Lead: 50:50:10 H Blend	No additives

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
PRODUCTION	Tail		3000	2612 2	4070	1.24	14.4	5046	25	Tail: 50:50:2 Class H Blend	No additives

Section 5 - Circulating Medium

Mud System Type: Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:****Describe what will be on location to control well or mitigate other conditions:** Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times**Describe the mud monitoring system utilized:** PVT/Pason/Visual Monitoring

Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
970	4800	OTHER : Saturated Brine	10	10.1							Saturated Brine
4800	2612 2	OTHER : Cut Brine	8.6	9.3							Cut Brine
0	970	OTHER : Fresh water gel	8.6	8.8							Fresh water gel

Operator Name: COG PRODUCTION LLC**Well Name:** EIDER 35 FEDERAL COM**Well Number:** 502H

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

None planned

List of open and cased hole logs run in the well:

COMPENSATED NEUTRON LOG,GAMMA RAY LOG,

Coring operation description for the well:

None planned

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 5150**Anticipated Surface Pressure:** 2807**Anticipated Bottom Hole Temperature(F):** 165**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO**Describe:****Contingency Plans geohazards description:****Contingency Plans geohazards attachment:****Hydrogen Sulfide drilling operations plan required?** YES**Hydrogen sulfide drilling operations plan:**

COG_Eider_35_501H_502H_H2S_Schematic_20201110090156.pdf

COG_Eider_H2S_Plan_20201107144816.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

COG_Eider_35_502H_AC_RPT_20201110103156.pdf

COG_Eider_35_502H_Directional_Plan_20201110103202.pdf

Other proposed operations facets description:

Drilling Program.

Cement Program.

GCP.

Other proposed operations facets attachment:

COG_Eider_35_502H_Drilling_Prog_20201110103216.pdf

COG_Eider_35_502H_Cement_Prog_20201110103224.pdf

COG_Eider_35_502H_GCP_20201110103231.pdf

Other Variance attachment:

CONFIDENTIAL

DELAWARE BASIN EAST

BULLDOG PROSPECT (NM-E)

EIDER 35 FED PROJECT

EIDER 35 FED #502H

OWB

Plan: PWP1

Standard Survey Report

28 October, 2020

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Project	BULLDOG PROSPECT (NM-E)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	EIDER 35 FED PROJECT		
Site Position:		Northing:	425,024.10 usft
From:	Map	Easting:	710,361.82 usft
Position Uncertainty:	3.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 10' 0.054 N
		Longitude:	103° 39' 12.634 W
		Grid Convergence:	0.36 °

Well	EIDER 35 FED #502H		
Well Position	+N/-S	0.0 usft	Northing:
	+E/-W	0.0 usft	Easting:
Position Uncertainty	3.0 usft		Wellhead Elevation:
			Latitude:
			Longitude:
			Ground Level:

Wellbore	OWB		
Magnetics	Model Name	Sample Date	Declination (°)
	IGRF2020	10/27/2020	6.65
			Dip Angle (°)
			59.86
			Field Strength (nT)
			47,519.70658515

Design	PWP1		
Audit Notes:			
Version:	Phase:	PLAN	Tie On Depth:
			0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)
	0.0	0.0	0.0
			Direction (°)
			0.44

Survey Tool Program	Date	10/28/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
0.0	10,060.0	PWP1 (OWB)	Standard Keeper 104	Standard Wireline Keeper ver 1.0.4
10,060.0	26,122.2	PWP1 (OWB)	MWD+IFR1+FDIR	OWSG MWD + IFR1 + FDIR Correction

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
2,600.0	0.00	0.00	2,600.0	0.0	0.0	0.0	0.00	0.00	0.00
2,700.0	0.00	0.00	2,700.0	0.0	0.0	0.0	0.00	0.00	0.00
2,800.0	0.00	0.00	2,800.0	0.0	0.0	0.0	0.00	0.00	0.00
2,900.0	0.00	0.00	2,900.0	0.0	0.0	0.0	0.00	0.00	0.00
3,000.0	0.00	0.00	3,000.0	0.0	0.0	0.0	0.00	0.00	0.00
3,100.0	0.00	0.00	3,100.0	0.0	0.0	0.0	0.00	0.00	0.00
3,200.0	0.00	0.00	3,200.0	0.0	0.0	0.0	0.00	0.00	0.00
3,300.0	0.00	0.00	3,300.0	0.0	0.0	0.0	0.00	0.00	0.00
3,400.0	0.00	0.00	3,400.0	0.0	0.0	0.0	0.00	0.00	0.00
3,500.0	0.00	0.00	3,500.0	0.0	0.0	0.0	0.00	0.00	0.00
3,600.0	0.00	0.00	3,600.0	0.0	0.0	0.0	0.00	0.00	0.00
3,700.0	0.00	0.00	3,700.0	0.0	0.0	0.0	0.00	0.00	0.00
3,800.0	0.00	0.00	3,800.0	0.0	0.0	0.0	0.00	0.00	0.00
3,900.0	0.00	0.00	3,900.0	0.0	0.0	0.0	0.00	0.00	0.00
4,000.0	0.00	0.00	4,000.0	0.0	0.0	0.0	0.00	0.00	0.00
4,100.0	0.00	0.00	4,100.0	0.0	0.0	0.0	0.00	0.00	0.00
4,200.0	0.00	0.00	4,200.0	0.0	0.0	0.0	0.00	0.00	0.00
4,300.0	0.00	0.00	4,300.0	0.0	0.0	0.0	0.00	0.00	0.00
4,400.0	0.00	0.00	4,400.0	0.0	0.0	0.0	0.00	0.00	0.00
4,500.0	0.00	0.00	4,500.0	0.0	0.0	0.0	0.00	0.00	0.00
4,600.0	0.00	0.00	4,600.0	0.0	0.0	0.0	0.00	0.00	0.00
4,700.0	0.00	0.00	4,700.0	0.0	0.0	0.0	0.00	0.00	0.00
4,800.0	0.00	0.00	4,800.0	0.0	0.0	0.0	0.00	0.00	0.00
4,900.0	0.00	0.00	4,900.0	0.0	0.0	0.0	0.00	0.00	0.00
5,000.0	0.00	0.00	5,000.0	0.0	0.0	0.0	0.00	0.00	0.00
5,100.0	0.00	0.00	5,100.0	0.0	0.0	0.0	0.00	0.00	0.00
5,200.0	0.00	0.00	5,200.0	0.0	0.0	0.0	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,300.0	0.00	0.00	5,300.0	0.0	0.0	0.0	0.00	0.00	0.00
5,400.0	0.00	0.00	5,400.0	0.0	0.0	0.0	0.00	0.00	0.00
5,500.0	0.00	0.00	5,500.0	0.0	0.0	0.0	0.00	0.00	0.00
Start Build 2.00									
5,600.0	2.00	133.25	5,600.0	-1.2	1.3	-1.2	2.00	2.00	0.00
5,664.4	3.29	133.25	5,664.3	-3.2	3.4	-3.2	2.00	2.00	0.00
Start 4371.8 hold at 5664.4 MD									
5,700.0	3.29	133.25	5,699.9	-4.6	4.9	-4.6	0.00	0.00	0.00
5,800.0	3.29	133.25	5,799.7	-8.6	9.1	-8.5	0.00	0.00	0.00
5,900.0	3.29	133.25	5,899.5	-12.5	13.3	-12.4	0.00	0.00	0.00
6,000.0	3.29	133.25	5,999.4	-16.4	17.4	-16.3	0.00	0.00	0.00
6,100.0	3.29	133.25	6,099.2	-20.3	21.6	-20.2	0.00	0.00	0.00
6,200.0	3.29	133.25	6,199.0	-24.3	25.8	-24.1	0.00	0.00	0.00
6,300.0	3.29	133.25	6,298.9	-28.2	30.0	-28.0	0.00	0.00	0.00
6,400.0	3.29	133.25	6,398.7	-32.1	34.2	-31.9	0.00	0.00	0.00
6,500.0	3.29	133.25	6,498.5	-36.1	38.3	-35.8	0.00	0.00	0.00
6,600.0	3.29	133.25	6,598.4	-40.0	42.5	-39.7	0.00	0.00	0.00
6,700.0	3.29	133.25	6,698.2	-43.9	46.7	-43.6	0.00	0.00	0.00
6,800.0	3.29	133.25	6,798.0	-47.8	50.9	-47.5	0.00	0.00	0.00
6,900.0	3.29	133.25	6,897.9	-51.8	55.0	-51.4	0.00	0.00	0.00
7,000.0	3.29	133.25	6,997.7	-55.7	59.2	-55.3	0.00	0.00	0.00
7,100.0	3.29	133.25	7,097.5	-59.6	63.4	-59.2	0.00	0.00	0.00
7,200.0	3.29	133.25	7,197.4	-63.6	67.6	-63.0	0.00	0.00	0.00
7,300.0	3.29	133.25	7,297.2	-67.5	71.7	-66.9	0.00	0.00	0.00
7,400.0	3.29	133.25	7,397.1	-71.4	75.9	-70.8	0.00	0.00	0.00
7,500.0	3.29	133.25	7,496.9	-75.4	80.1	-74.7	0.00	0.00	0.00
7,600.0	3.29	133.25	7,596.7	-79.3	84.3	-78.6	0.00	0.00	0.00
7,700.0	3.29	133.25	7,696.6	-83.2	88.4	-82.5	0.00	0.00	0.00
7,800.0	3.29	133.25	7,796.4	-87.1	92.6	-86.4	0.00	0.00	0.00
7,900.0	3.29	133.25	7,896.2	-91.1	96.8	-90.3	0.00	0.00	0.00
8,000.0	3.29	133.25	7,996.1	-95.0	101.0	-94.2	0.00	0.00	0.00
8,100.0	3.29	133.25	8,095.9	-98.9	105.1	-98.1	0.00	0.00	0.00
8,200.0	3.29	133.25	8,195.7	-102.9	109.3	-102.0	0.00	0.00	0.00
8,300.0	3.29	133.25	8,295.6	-106.8	113.5	-105.9	0.00	0.00	0.00
8,400.0	3.29	133.25	8,395.4	-110.7	117.7	-109.8	0.00	0.00	0.00
8,500.0	3.29	133.25	8,495.2	-114.6	121.8	-113.7	0.00	0.00	0.00
8,600.0	3.29	133.25	8,595.1	-118.6	126.0	-117.6	0.00	0.00	0.00
8,700.0	3.29	133.25	8,694.9	-122.5	130.2	-121.5	0.00	0.00	0.00
8,800.0	3.29	133.25	8,794.8	-126.4	134.4	-125.4	0.00	0.00	0.00
8,900.0	3.29	133.25	8,894.6	-130.4	138.6	-129.3	0.00	0.00	0.00
9,000.0	3.29	133.25	8,994.4	-134.3	142.7	-133.2	0.00	0.00	0.00
9,100.0	3.29	133.25	9,094.3	-138.2	146.9	-137.1	0.00	0.00	0.00
9,200.0	3.29	133.25	9,194.1	-142.1	151.1	-141.0	0.00	0.00	0.00
9,300.0	3.29	133.25	9,293.9	-146.1	155.3	-144.9	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
9,400.0	3.29	133.25	9,393.8	-150.0	159.4	-148.8	0.00	0.00	0.00
9,500.0	3.29	133.25	9,493.6	-153.9	163.6	-152.7	0.00	0.00	0.00
9,600.0	3.29	133.25	9,593.4	-157.9	167.8	-156.6	0.00	0.00	0.00
9,700.0	3.29	133.25	9,693.3	-161.8	172.0	-160.5	0.00	0.00	0.00
9,800.0	3.29	133.25	9,793.1	-165.7	176.1	-164.4	0.00	0.00	0.00
9,900.0	3.29	133.25	9,892.9	-169.6	180.3	-168.3	0.00	0.00	0.00
10,000.0	3.29	133.25	9,992.8	-173.6	184.5	-172.2	0.00	0.00	0.00
10,036.2	3.29	133.25	10,028.9	-175.0	186.0	-173.6	0.00	0.00	0.00
Start DLS 10.00 TFO -133.59									
10,100.0	4.75	29.62	10,092.6	-174.0	188.6	-172.5	10.00	2.30	-162.40
10,200.0	14.31	8.99	10,191.1	-158.1	192.6	-156.6	10.00	9.56	-20.62
10,300.0	24.22	4.92	10,285.4	-125.4	196.3	-123.9	10.00	9.91	-4.08
10,400.0	34.19	3.12	10,372.6	-76.8	199.6	-75.2	10.00	9.96	-1.79
10,500.0	44.16	2.07	10,450.0	-13.7	202.4	-12.2	10.00	9.98	-1.06
10,600.0	54.15	1.34	10,515.4	61.8	204.6	63.3	10.00	9.98	-0.73
10,700.0	64.14	0.77	10,566.6	147.5	206.2	149.1	10.00	9.99	-0.57
10,800.0	74.13	0.29	10,602.2	240.8	207.0	242.4	10.00	9.99	-0.48
10,900.0	84.12	359.86	10,621.0	338.9	207.2	340.5	10.00	9.99	-0.43
10,957.9	89.91	359.62	10,624.0	396.7	206.9	398.3	10.00	9.99	-0.42
Start 4662.1 hold at 10957.9 MD									
11,000.0	89.91	359.62	10,624.1	438.8	206.6	440.4	0.00	0.00	0.00
11,100.0	89.91	359.62	10,624.2	538.8	206.0	540.4	0.00	0.00	0.00
11,200.0	89.91	359.62	10,624.4	638.8	205.3	640.3	0.00	0.00	0.00
11,300.0	89.91	359.62	10,624.6	738.8	204.6	740.3	0.00	0.00	0.00
11,400.0	89.91	359.62	10,624.7	838.8	204.0	840.3	0.00	0.00	0.00
11,500.0	89.91	359.62	10,624.9	938.8	203.3	940.3	0.00	0.00	0.00
11,600.0	89.91	359.62	10,625.1	1,038.8	202.7	1,040.3	0.00	0.00	0.00
11,700.0	89.91	359.62	10,625.2	1,138.8	202.0	1,140.3	0.00	0.00	0.00
11,800.0	89.91	359.62	10,625.4	1,238.8	201.3	1,240.3	0.00	0.00	0.00
11,900.0	89.91	359.62	10,625.5	1,338.8	200.7	1,340.3	0.00	0.00	0.00
12,000.0	89.91	359.62	10,625.7	1,438.8	200.0	1,440.3	0.00	0.00	0.00
12,100.0	89.91	359.62	10,625.9	1,538.8	199.3	1,540.3	0.00	0.00	0.00
12,200.0	89.91	359.62	10,626.0	1,638.8	198.7	1,640.2	0.00	0.00	0.00
12,300.0	89.91	359.62	10,626.2	1,738.8	198.0	1,740.2	0.00	0.00	0.00
12,400.0	89.91	359.62	10,626.4	1,838.8	197.4	1,840.2	0.00	0.00	0.00
12,500.0	89.91	359.62	10,626.5	1,938.8	196.7	1,940.2	0.00	0.00	0.00
12,600.0	89.91	359.62	10,626.7	2,038.8	196.0	2,040.2	0.00	0.00	0.00
12,700.0	89.91	359.62	10,626.8	2,138.8	195.4	2,140.2	0.00	0.00	0.00
12,800.0	89.91	359.62	10,627.0	2,238.8	194.7	2,240.2	0.00	0.00	0.00
12,900.0	89.91	359.62	10,627.2	2,338.8	194.0	2,340.2	0.00	0.00	0.00
13,000.0	89.91	359.62	10,627.3	2,438.8	193.4	2,440.2	0.00	0.00	0.00
13,100.0	89.91	359.62	10,627.5	2,538.8	192.7	2,540.1	0.00	0.00	0.00
13,200.0	89.91	359.62	10,627.7	2,638.7	192.0	2,640.1	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
13,300.0	89.91	359.62	10,627.8	2,738.7	191.4	2,740.1	0.00	0.00	0.00
13,400.0	89.91	359.62	10,628.0	2,838.7	190.7	2,840.1	0.00	0.00	0.00
13,500.0	89.91	359.62	10,628.2	2,938.7	190.1	2,940.1	0.00	0.00	0.00
13,600.0	89.91	359.62	10,628.3	3,038.7	189.4	3,040.1	0.00	0.00	0.00
13,700.0	89.91	359.62	10,628.5	3,138.7	188.7	3,140.1	0.00	0.00	0.00
13,800.0	89.91	359.62	10,628.6	3,238.7	188.1	3,240.1	0.00	0.00	0.00
13,900.0	89.91	359.62	10,628.8	3,338.7	187.4	3,340.1	0.00	0.00	0.00
14,000.0	89.91	359.62	10,629.0	3,438.7	186.7	3,440.1	0.00	0.00	0.00
14,100.0	89.91	359.62	10,629.1	3,538.7	186.1	3,540.0	0.00	0.00	0.00
14,200.0	89.91	359.62	10,629.3	3,638.7	185.4	3,640.0	0.00	0.00	0.00
14,300.0	89.91	359.62	10,629.5	3,738.7	184.8	3,740.0	0.00	0.00	0.00
14,400.0	89.91	359.62	10,629.6	3,838.7	184.1	3,840.0	0.00	0.00	0.00
14,500.0	89.91	359.62	10,629.8	3,938.7	183.4	3,940.0	0.00	0.00	0.00
14,600.0	89.91	359.62	10,629.9	4,038.7	182.8	4,040.0	0.00	0.00	0.00
14,700.0	89.91	359.62	10,630.1	4,138.7	182.1	4,140.0	0.00	0.00	0.00
14,800.0	89.91	359.62	10,630.3	4,238.7	181.4	4,240.0	0.00	0.00	0.00
14,900.0	89.91	359.62	10,630.4	4,338.7	180.8	4,340.0	0.00	0.00	0.00
15,000.0	89.91	359.62	10,630.6	4,438.7	180.1	4,440.0	0.00	0.00	0.00
15,100.0	89.91	359.62	10,630.8	4,538.7	179.5	4,539.9	0.00	0.00	0.00
15,200.0	89.91	359.62	10,630.9	4,638.7	178.8	4,639.9	0.00	0.00	0.00
15,300.0	89.91	359.62	10,631.1	4,738.7	178.1	4,739.9	0.00	0.00	0.00
15,400.0	89.91	359.62	10,631.2	4,838.7	177.5	4,839.9	0.00	0.00	0.00
15,500.0	89.91	359.62	10,631.4	4,938.7	176.8	4,939.9	0.00	0.00	0.00
15,600.0	89.91	359.62	10,631.6	5,038.7	176.1	5,039.9	0.00	0.00	0.00
15,620.0	89.91	359.62	10,631.6	5,058.7	176.0	5,059.9	0.00	0.00	0.00
Start DLS 2.00 TFO 91.46									
15,623.4	89.91	359.69	10,631.6	5,062.1	176.0	5,063.3	2.00	-0.05	2.00
Start 10498.8 hold at 15623.4 MD									
15,700.0	89.91	359.69	10,631.7	5,138.7	175.6	5,139.9	0.00	0.00	0.00
15,800.0	89.91	359.69	10,631.9	5,238.7	175.0	5,239.9	0.00	0.00	0.00
15,900.0	89.91	359.69	10,632.1	5,338.7	174.5	5,339.9	0.00	0.00	0.00
16,000.0	89.91	359.69	10,632.2	5,438.7	173.9	5,439.9	0.00	0.00	0.00
16,100.0	89.91	359.69	10,632.4	5,538.7	173.4	5,539.8	0.00	0.00	0.00
16,200.0	89.91	359.69	10,632.6	5,638.7	172.8	5,639.8	0.00	0.00	0.00
16,300.0	89.91	359.69	10,632.7	5,738.7	172.3	5,739.8	0.00	0.00	0.00
16,400.0	89.91	359.69	10,632.9	5,838.7	171.8	5,839.8	0.00	0.00	0.00
16,500.0	89.91	359.69	10,633.1	5,938.7	171.2	5,939.8	0.00	0.00	0.00
16,600.0	89.91	359.69	10,633.2	6,038.7	170.7	6,039.8	0.00	0.00	0.00
16,700.0	89.91	359.69	10,633.4	6,138.7	170.1	6,139.8	0.00	0.00	0.00
16,800.0	89.91	359.69	10,633.6	6,238.7	169.6	6,239.8	0.00	0.00	0.00
16,900.0	89.91	359.69	10,633.7	6,338.7	169.0	6,339.8	0.00	0.00	0.00
17,000.0	89.91	359.69	10,633.9	6,438.7	168.5	6,439.8	0.00	0.00	0.00
17,100.0	89.91	359.69	10,634.1	6,538.7	167.9	6,539.8	0.00	0.00	0.00
17,200.0	89.91	359.69	10,634.2	6,638.7	167.4	6,639.8	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
17,300.0	89.91	359.69	10,634.4	6,738.7	166.8	6,739.7	0.00	0.00	0.00
17,400.0	89.91	359.69	10,634.5	6,838.7	166.3	6,839.7	0.00	0.00	0.00
17,500.0	89.91	359.69	10,634.7	6,938.7	165.8	6,939.7	0.00	0.00	0.00
17,600.0	89.91	359.69	10,634.9	7,038.7	165.2	7,039.7	0.00	0.00	0.00
17,700.0	89.91	359.69	10,635.0	7,138.7	164.7	7,139.7	0.00	0.00	0.00
17,800.0	89.91	359.69	10,635.2	7,238.7	164.1	7,239.7	0.00	0.00	0.00
17,900.0	89.91	359.69	10,635.4	7,338.7	163.6	7,339.7	0.00	0.00	0.00
18,000.0	89.91	359.69	10,635.5	7,438.7	163.0	7,439.7	0.00	0.00	0.00
18,100.0	89.91	359.69	10,635.7	7,538.7	162.5	7,539.7	0.00	0.00	0.00
18,200.0	89.91	359.69	10,635.9	7,638.7	161.9	7,639.7	0.00	0.00	0.00
18,300.0	89.91	359.69	10,636.0	7,738.6	161.4	7,739.7	0.00	0.00	0.00
18,400.0	89.91	359.69	10,636.2	7,838.6	160.8	7,839.6	0.00	0.00	0.00
18,500.0	89.91	359.69	10,636.4	7,938.6	160.3	7,939.6	0.00	0.00	0.00
18,600.0	89.91	359.69	10,636.5	8,038.6	159.7	8,039.6	0.00	0.00	0.00
18,700.0	89.91	359.69	10,636.7	8,138.6	159.2	8,139.6	0.00	0.00	0.00
18,800.0	89.91	359.69	10,636.9	8,238.6	158.7	8,239.6	0.00	0.00	0.00
18,900.0	89.91	359.69	10,637.0	8,338.6	158.1	8,339.6	0.00	0.00	0.00
19,000.0	89.91	359.69	10,637.2	8,438.6	157.6	8,439.6	0.00	0.00	0.00
19,100.0	89.91	359.69	10,637.4	8,538.6	157.0	8,539.6	0.00	0.00	0.00
19,200.0	89.91	359.69	10,637.5	8,638.6	156.5	8,639.6	0.00	0.00	0.00
19,300.0	89.91	359.69	10,637.7	8,738.6	155.9	8,739.6	0.00	0.00	0.00
19,400.0	89.91	359.69	10,637.9	8,838.6	155.4	8,839.6	0.00	0.00	0.00
19,500.0	89.91	359.69	10,638.0	8,938.6	154.8	8,939.6	0.00	0.00	0.00
19,600.0	89.91	359.69	10,638.2	9,038.6	154.3	9,039.5	0.00	0.00	0.00
19,700.0	89.91	359.69	10,638.4	9,138.6	153.7	9,139.5	0.00	0.00	0.00
19,800.0	89.91	359.69	10,638.5	9,238.6	153.2	9,239.5	0.00	0.00	0.00
19,900.0	89.91	359.69	10,638.7	9,338.6	152.7	9,339.5	0.00	0.00	0.00
20,000.0	89.91	359.69	10,638.9	9,438.6	152.1	9,439.5	0.00	0.00	0.00
20,100.0	89.91	359.69	10,639.0	9,538.6	151.6	9,539.5	0.00	0.00	0.00
20,200.0	89.91	359.69	10,639.2	9,638.6	151.0	9,639.5	0.00	0.00	0.00
20,300.0	89.91	359.69	10,639.4	9,738.6	150.5	9,739.5	0.00	0.00	0.00
20,400.0	89.91	359.69	10,639.5	9,838.6	149.9	9,839.5	0.00	0.00	0.00
20,500.0	89.91	359.69	10,639.7	9,938.6	149.4	9,939.5	0.00	0.00	0.00
20,600.0	89.91	359.69	10,639.9	10,038.6	148.8	10,039.5	0.00	0.00	0.00
20,700.0	89.91	359.69	10,640.0	10,138.6	148.3	10,139.4	0.00	0.00	0.00
20,800.0	89.91	359.69	10,640.2	10,238.6	147.7	10,239.4	0.00	0.00	0.00
20,900.0	89.91	359.69	10,640.3	10,338.6	147.2	10,339.4	0.00	0.00	0.00
21,000.0	89.91	359.69	10,640.5	10,438.6	146.7	10,439.4	0.00	0.00	0.00
21,100.0	89.91	359.69	10,640.7	10,538.6	146.1	10,539.4	0.00	0.00	0.00
21,200.0	89.91	359.69	10,640.8	10,638.6	145.6	10,639.4	0.00	0.00	0.00
21,300.0	89.91	359.69	10,641.0	10,738.6	145.0	10,739.4	0.00	0.00	0.00
21,400.0	89.91	359.69	10,641.2	10,838.6	144.5	10,839.4	0.00	0.00	0.00
21,500.0	89.91	359.69	10,641.3	10,938.6	143.9	10,939.4	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
21,600.0	89.91	359.69	10,641.5	11,038.6	143.4	11,039.4	0.00	0.00	0.00
21,700.0	89.91	359.69	10,641.7	11,138.6	142.8	11,139.4	0.00	0.00	0.00
21,800.0	89.91	359.69	10,641.8	11,238.6	142.3	11,239.4	0.00	0.00	0.00
21,900.0	89.91	359.69	10,642.0	11,338.6	141.7	11,339.3	0.00	0.00	0.00
22,000.0	89.91	359.69	10,642.2	11,438.6	141.2	11,439.3	0.00	0.00	0.00
22,100.0	89.91	359.69	10,642.3	11,538.6	140.6	11,539.3	0.00	0.00	0.00
22,200.0	89.91	359.69	10,642.5	11,638.6	140.1	11,639.3	0.00	0.00	0.00
22,300.0	89.91	359.69	10,642.7	11,738.6	139.6	11,739.3	0.00	0.00	0.00
22,400.0	89.91	359.69	10,642.8	11,838.6	139.0	11,839.3	0.00	0.00	0.00
22,500.0	89.91	359.69	10,643.0	11,938.6	138.5	11,939.3	0.00	0.00	0.00
22,600.0	89.91	359.69	10,643.2	12,038.6	137.9	12,039.3	0.00	0.00	0.00
22,700.0	89.91	359.69	10,643.3	12,138.6	137.4	12,139.3	0.00	0.00	0.00
22,800.0	89.91	359.69	10,643.5	12,238.6	136.8	12,239.3	0.00	0.00	0.00
22,900.0	89.91	359.69	10,643.7	12,338.6	136.3	12,339.3	0.00	0.00	0.00
23,000.0	89.91	359.69	10,643.8	12,438.6	135.7	12,439.2	0.00	0.00	0.00
23,100.0	89.91	359.69	10,644.0	12,538.6	135.2	12,539.2	0.00	0.00	0.00
23,200.0	89.91	359.69	10,644.2	12,638.6	134.6	12,639.2	0.00	0.00	0.00
23,300.0	89.91	359.69	10,644.3	12,738.6	134.1	12,739.2	0.00	0.00	0.00
23,400.0	89.91	359.69	10,644.5	12,838.6	133.6	12,839.2	0.00	0.00	0.00
23,500.0	89.91	359.69	10,644.7	12,938.6	133.0	12,939.2	0.00	0.00	0.00
23,600.0	89.91	359.69	10,644.8	13,038.6	132.5	13,039.2	0.00	0.00	0.00
23,700.0	89.91	359.69	10,645.0	13,138.6	131.9	13,139.2	0.00	0.00	0.00
23,800.0	89.91	359.69	10,645.2	13,238.6	131.4	13,239.2	0.00	0.00	0.00
23,900.0	89.91	359.69	10,645.3	13,338.6	130.8	13,339.2	0.00	0.00	0.00
24,000.0	89.91	359.69	10,645.5	13,438.6	130.3	13,439.2	0.00	0.00	0.00
24,100.0	89.91	359.69	10,645.6	13,538.6	129.7	13,539.2	0.00	0.00	0.00
24,200.0	89.91	359.69	10,645.8	13,638.6	129.2	13,639.1	0.00	0.00	0.00
24,300.0	89.91	359.69	10,646.0	13,738.6	128.6	13,739.1	0.00	0.00	0.00
24,400.0	89.91	359.69	10,646.1	13,838.6	128.1	13,839.1	0.00	0.00	0.00
24,500.0	89.91	359.69	10,646.3	13,938.5	127.6	13,939.1	0.00	0.00	0.00
24,600.0	89.91	359.69	10,646.5	14,038.5	127.0	14,039.1	0.00	0.00	0.00
24,700.0	89.91	359.69	10,646.6	14,138.5	126.5	14,139.1	0.00	0.00	0.00
24,800.0	89.91	359.69	10,646.8	14,238.5	125.9	14,239.1	0.00	0.00	0.00
24,900.0	89.91	359.69	10,647.0	14,338.5	125.4	14,339.1	0.00	0.00	0.00
25,000.0	89.91	359.69	10,647.1	14,438.5	124.8	14,439.1	0.00	0.00	0.00
25,100.0	89.91	359.69	10,647.3	14,538.5	124.3	14,539.1	0.00	0.00	0.00
25,200.0	89.91	359.69	10,647.5	14,638.5	123.7	14,639.1	0.00	0.00	0.00
25,300.0	89.91	359.69	10,647.6	14,738.5	123.2	14,739.0	0.00	0.00	0.00
25,400.0	89.91	359.69	10,647.8	14,838.5	122.6	14,839.0	0.00	0.00	0.00
25,500.0	89.91	359.69	10,648.0	14,938.5	122.1	14,939.0	0.00	0.00	0.00
25,600.0	89.91	359.69	10,648.1	15,038.5	121.5	15,039.0	0.00	0.00	0.00
25,700.0	89.91	359.69	10,648.3	15,138.5	121.0	15,139.0	0.00	0.00	0.00
25,800.0	89.91	359.69	10,648.5	15,238.5	120.5	15,239.0	0.00	0.00	0.00
25,900.0	89.91	359.69	10,648.6	15,338.5	119.9	15,339.0	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Well:	EIDER 35 FED #502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
26,000.0	89.91	359.69	10,648.8	15,438.5	119.4	15,439.0	0.00	0.00	0.00
26,100.0	89.91	359.69	10,649.0	15,538.5	118.8	15,539.0	0.00	0.00	0.00
26,122.2	89.91	359.69	10,649.0	15,560.7	118.7	15,561.2	0.00	0.00	0.00
TD at 26122.2									

Design Targets

Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
POI 1 (EIDER 35 FED - hit/miss target - Shape - Rectangle (sides W100.0 H5,236.0 D20.0)	-0.09	179.62	10,631.6	5,058.7	176.0	430,326.74	711,976.41	32° 10' 52.426 N	103° 38' 53.458 W
LTP (EIDER 35 FED # - plan misses target center by 0.1usft at 26072.2usft MD (10648.9 TVD, 15510.7 N, 119.0 E) - Point	0.00	0.00	10,649.0	15,510.7	119.0	440,778.70	711,919.40	32° 12' 35.860 N	103° 38' 53.347 W
PBHL (EIDER 35 FED - plan hits target center - Rectangle (sides W100.0 H10,504.0 D20.0)	-0.09	179.69	10,649.0	15,560.7	118.7	440,828.70	711,919.10	32° 12' 36.354 N	103° 38' 53.346 W
FTP (EIDER 35 FED # - plan misses target center by 249.1usft at 10566.2usft MD (10494.8 TVD, 35.0 N, 204.0 E) - Circle (radius 50.0)	0.00	0.01	10,683.0	-128.0	210.8	425,140.00	712,011.20	32° 10' 1.097 N	103° 38' 53.438 W


Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Comment
5500	5500	0	0	Start Build 2.00
5664	5664	-3	3	Start 4371.8 hold at 5664.4 MD
10,036	10,029	-175	186	Start DLS 10.00 TFO -133.59
10,958	10,624	397	207	Start 4662.1 hold at 10957.9 MD
15,620	10,632	5059	176	Start DLS 2.00 TFO 91.46
15,623	10,632	5062	176	Start 10498.8 hold at 15623.4 MD
26,122	10,649	15,561	119	TD at 26122.2

Checked By: _____ Approved By: _____ Date: _____




Project: BULLDOG PROSPECT (NM-E)
Site: EIDER 35 FED PROJECT
Well: EIDER 35 FED #502H
Wellbore: OWB
Design: PWP1
GL: 3222.0
KB=26' @ 3248.0usft (MCVAY 8)







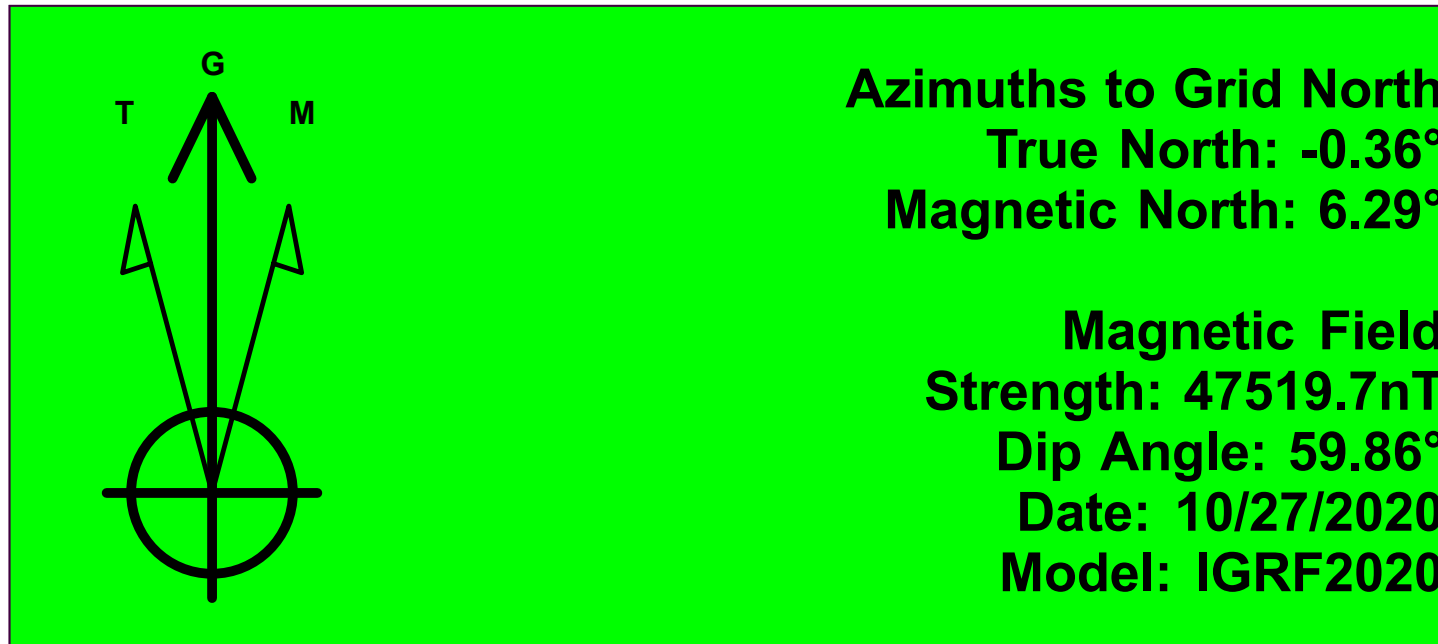


WELL DETAILS: EIDER 35 FED #502H					
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.0	0.0	425268.00	711800.40	32° 10' 2.377 N	103° 38' 55.880 W

DESIGN TARGET DETAILS					
Name	TVD	+N/-S	+E/-W	Northing	Easting
POI 1 (EIDER 35 FED #502H)	10631.6	5058.7	176.0	430326.74	711976.41
LTP (EIDER 35 FED #502H)	10649.0	15510.7	119.0	440778.70	711919.40
PBHL (EIDER 35 FED #502H)	10649.0	15560.7	118.7	440828.70	711919.10
FTP (EIDER 35 FED #502H)	10683.0	-128.0	210.8	425140.00	712011.20

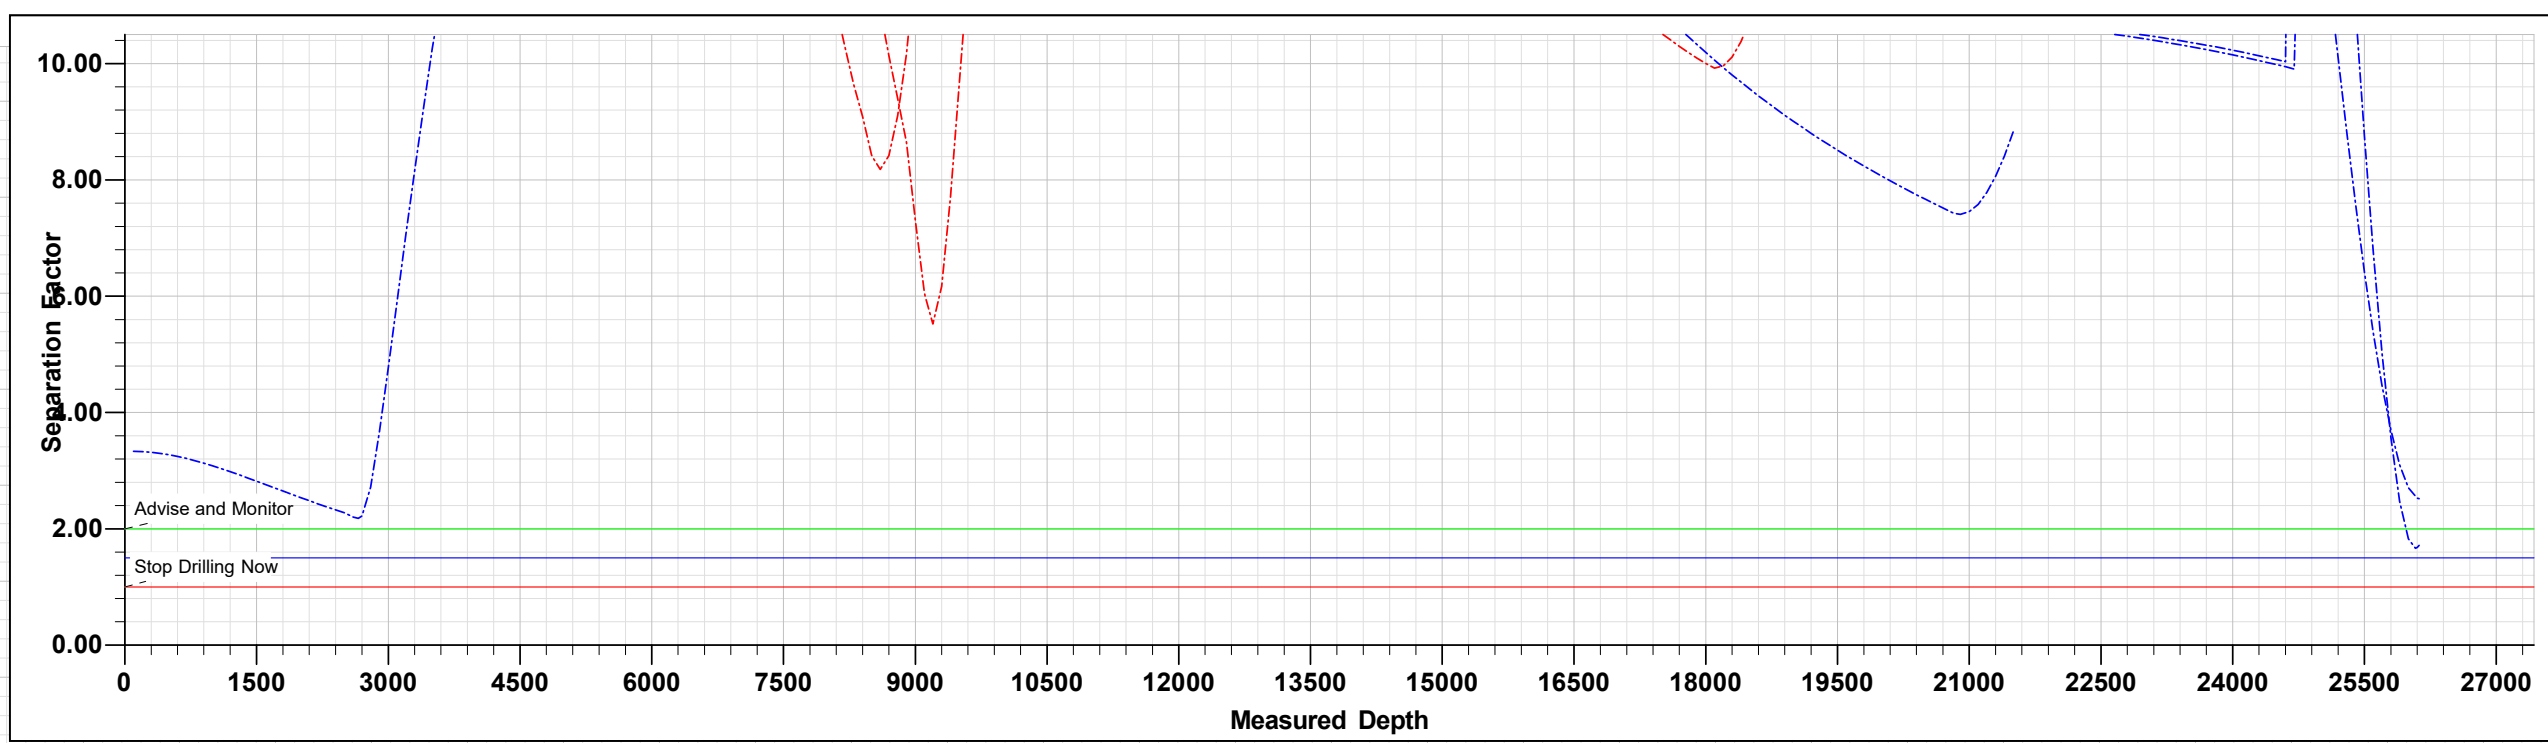

EIDER 35 FED #502H									
MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Annotation
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
5500.0	0.00	0.00	5500.0	0.0	0.0	0.00	0.00	0.0	Start Build 2.00
5664.4	3.29	133.25	5664.3	-3.2	3.4	2.00	133.25	-3.2	Start 4371.8 hold at 5664.4 MD
10036.2	3.29	133.25	10028.9	-175.0	186.0	0.00	0.00	-173.6	Start DLS 10.00 TFO -133.59
10957.9	89.91	359.62	10624.0	396.7	206.9	10.00	-133.59	398.3	Start 4662.1 hold at 10957.9 MD
15620.0	89.91	359.62	10631.6	5058.7	176.0	0.00	0.00	5059.9	Start DLS 2.00 TFO 91.46
15623.4	89.91	359.69	10631.6	5062.1	176.0	2.00	91.46	5063.3	Start 10498.8 hold at 15623.4 MD
26122.2	89.91	359.69	10649.0	15560.7	118.7	0.00	0.00	15561.2	TD at 26122.2

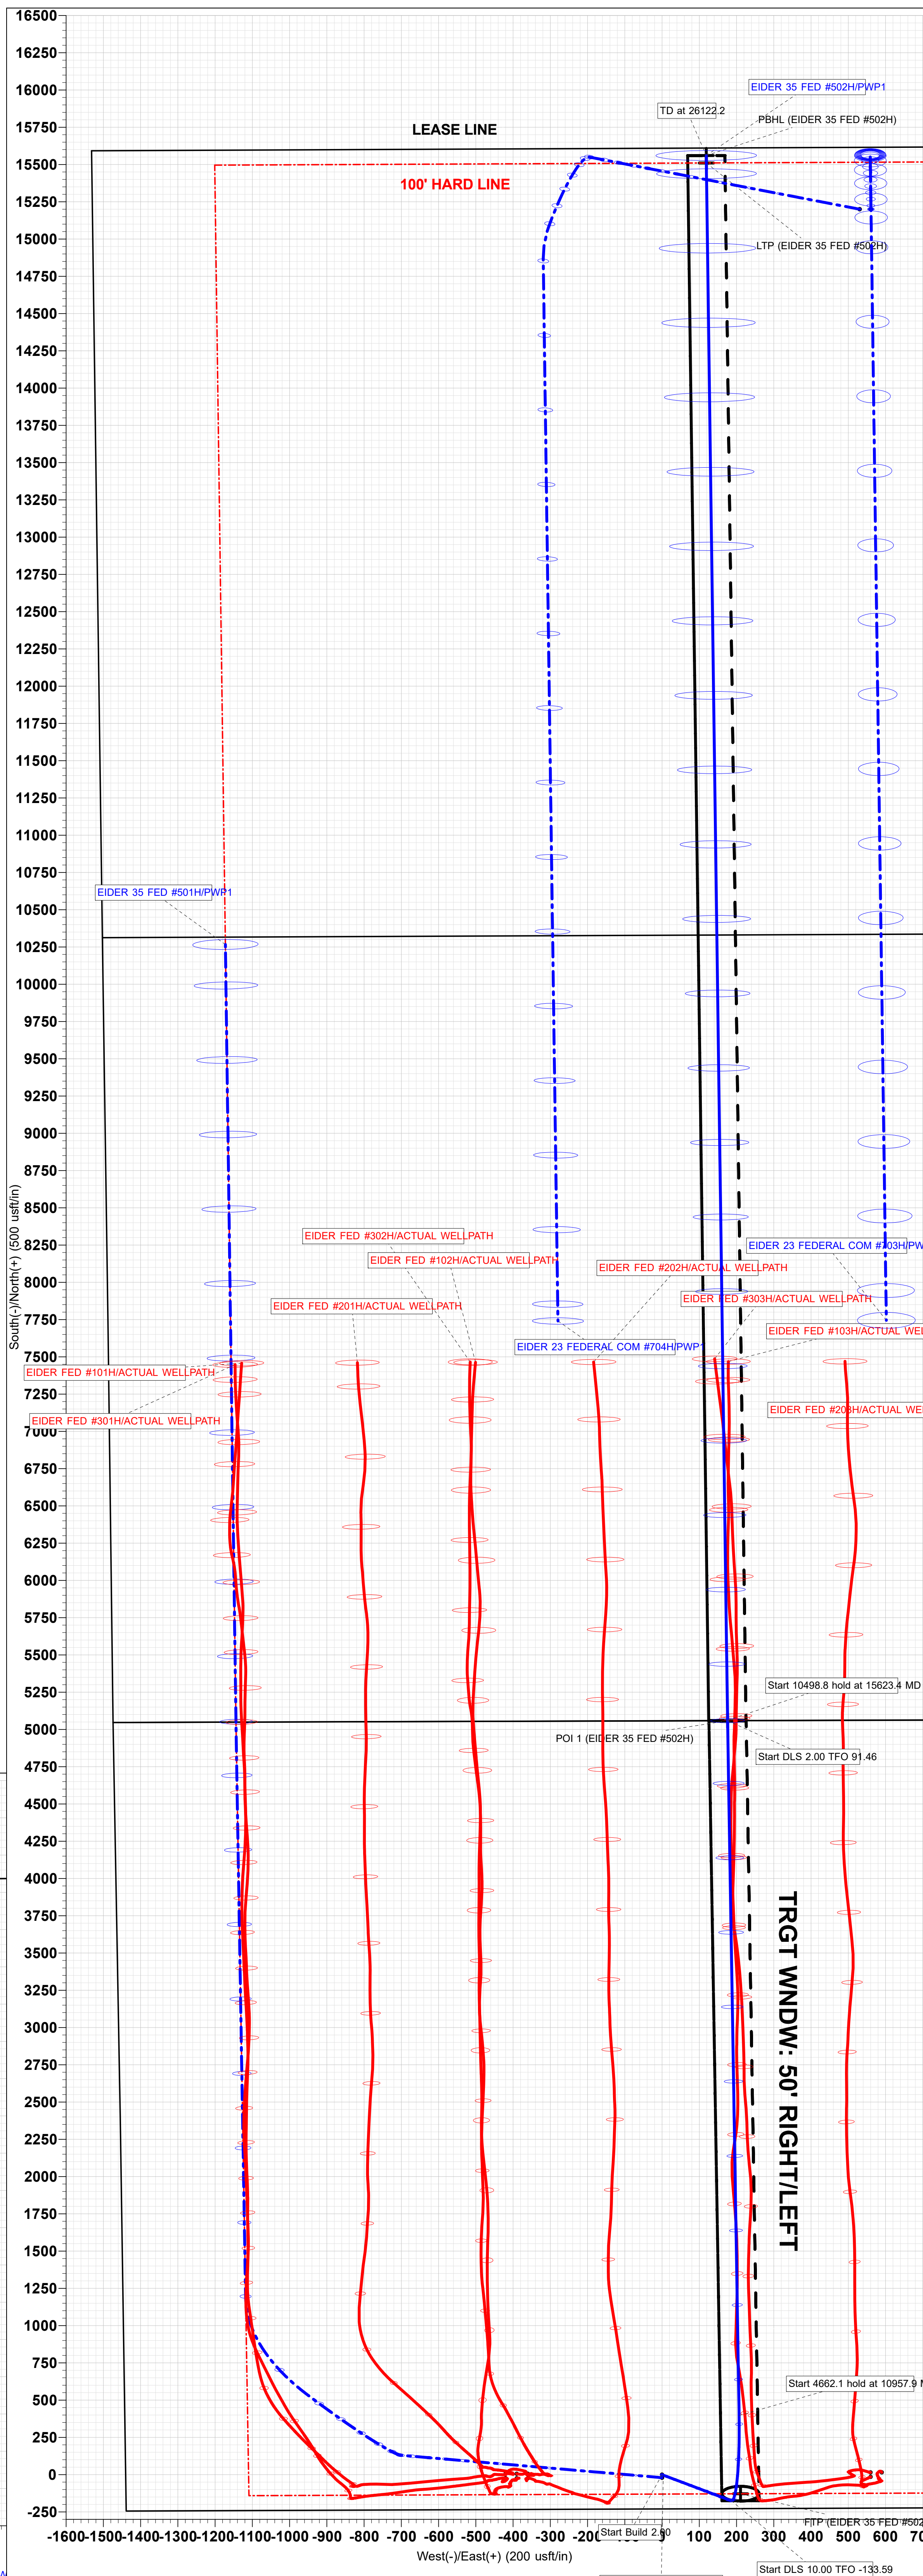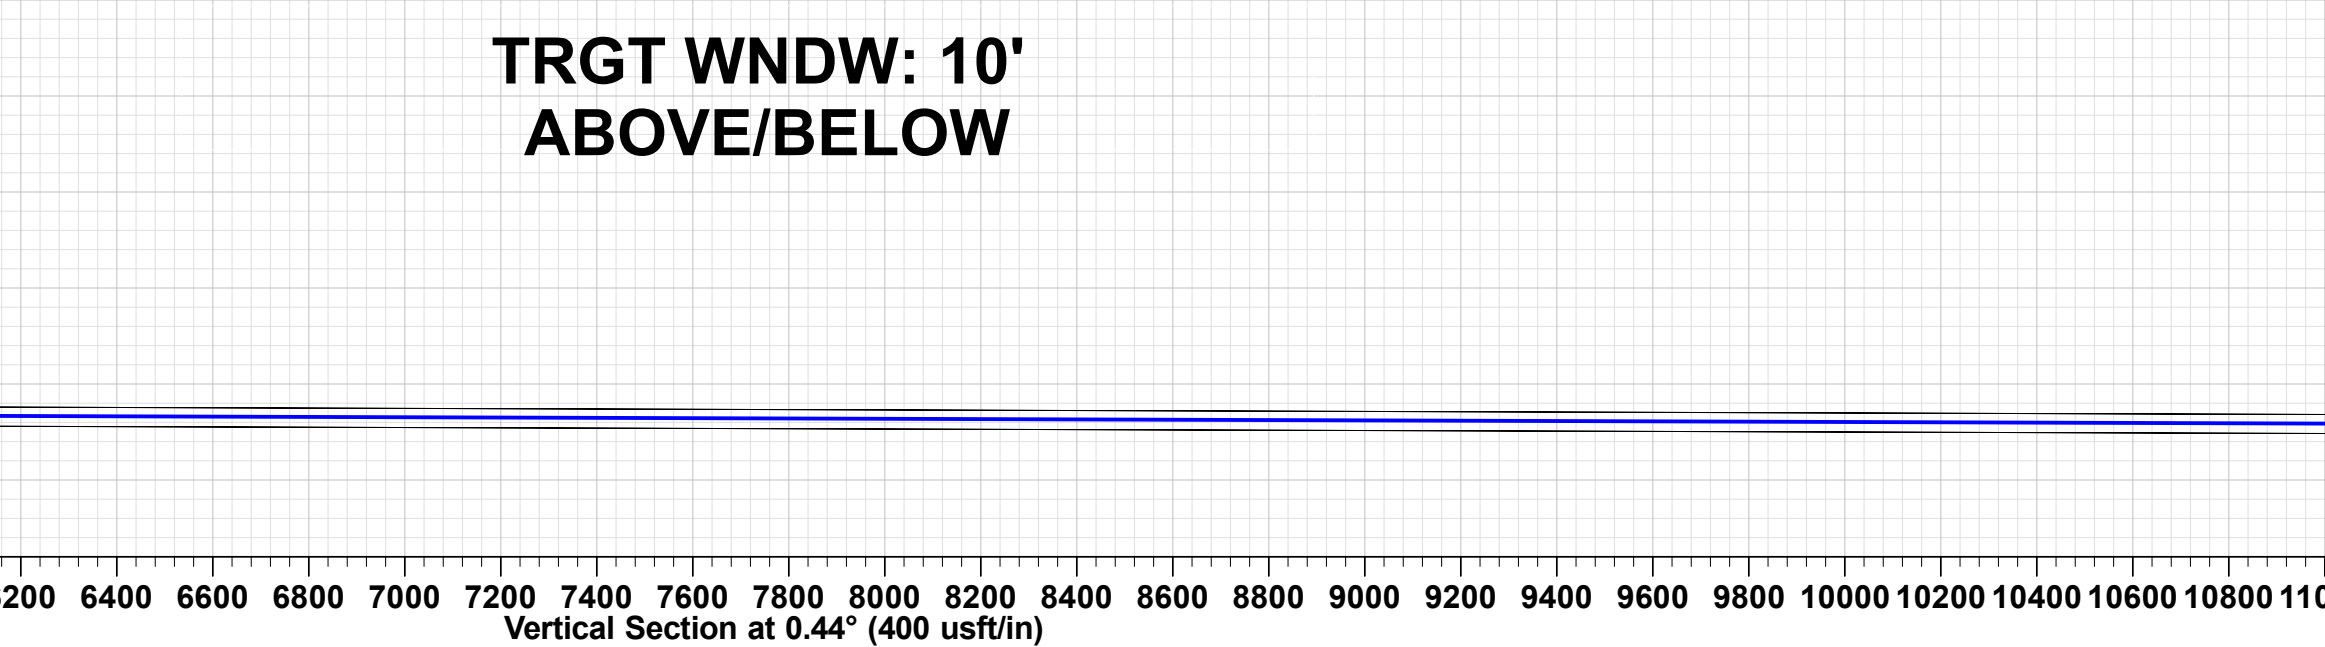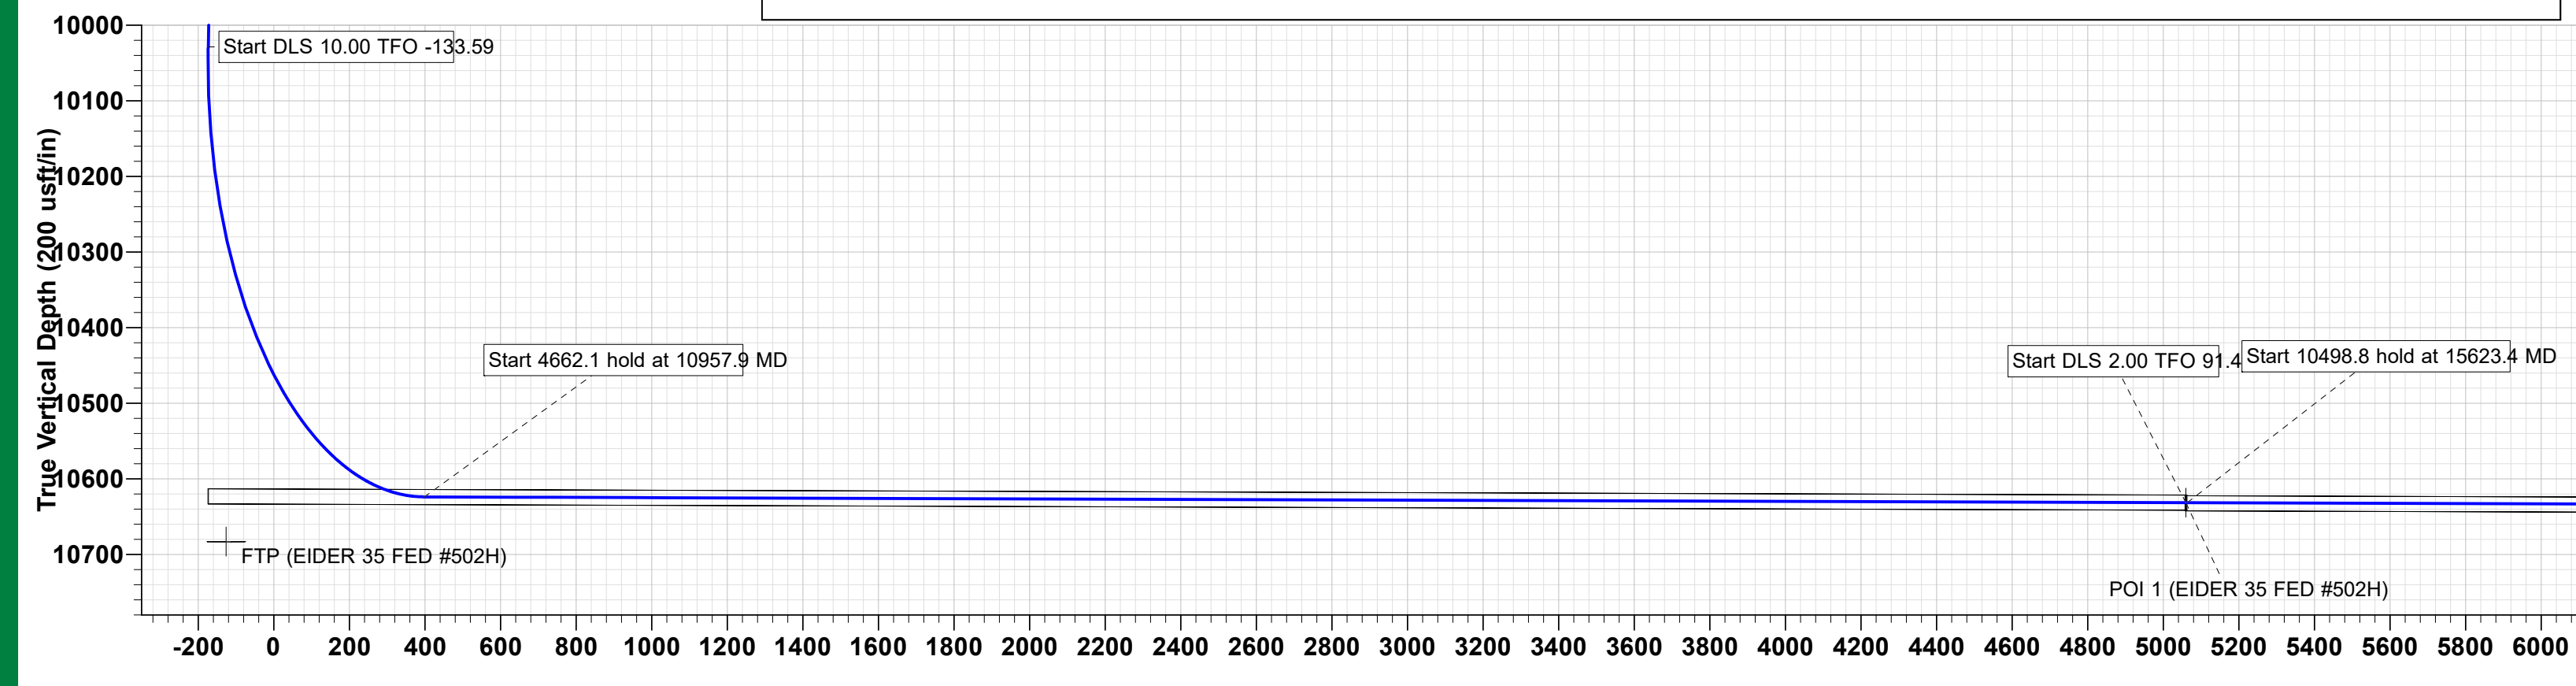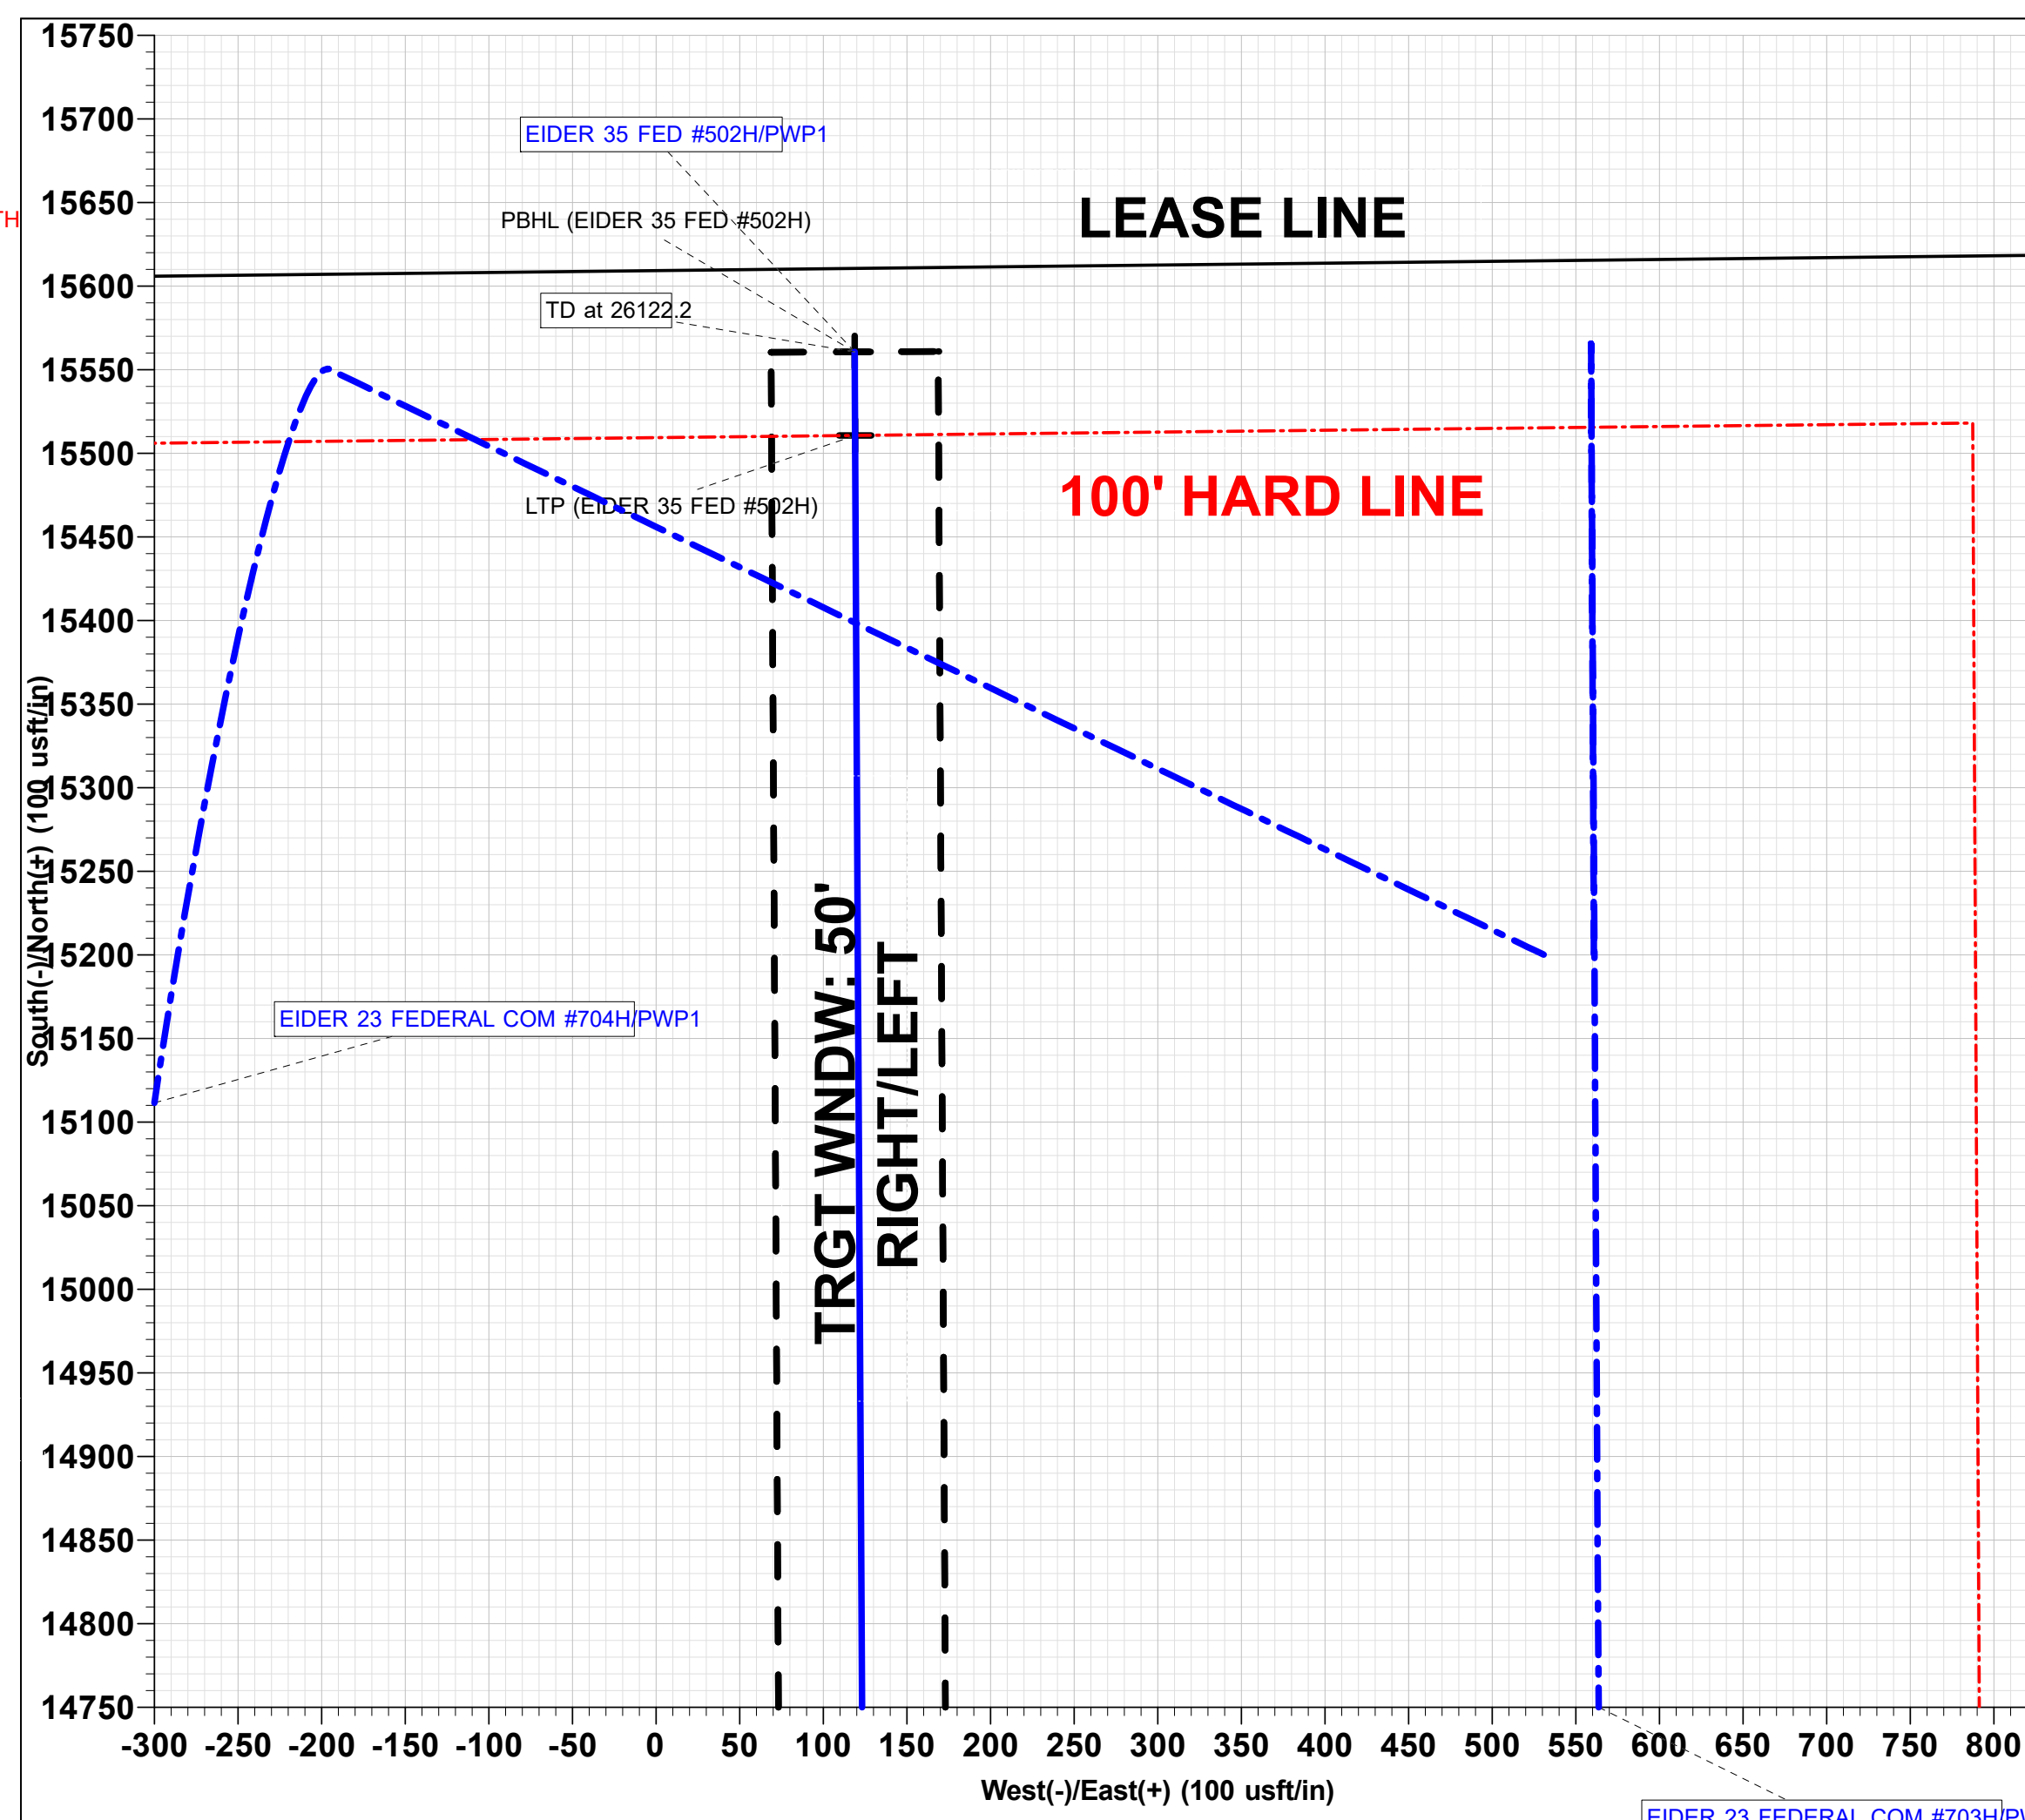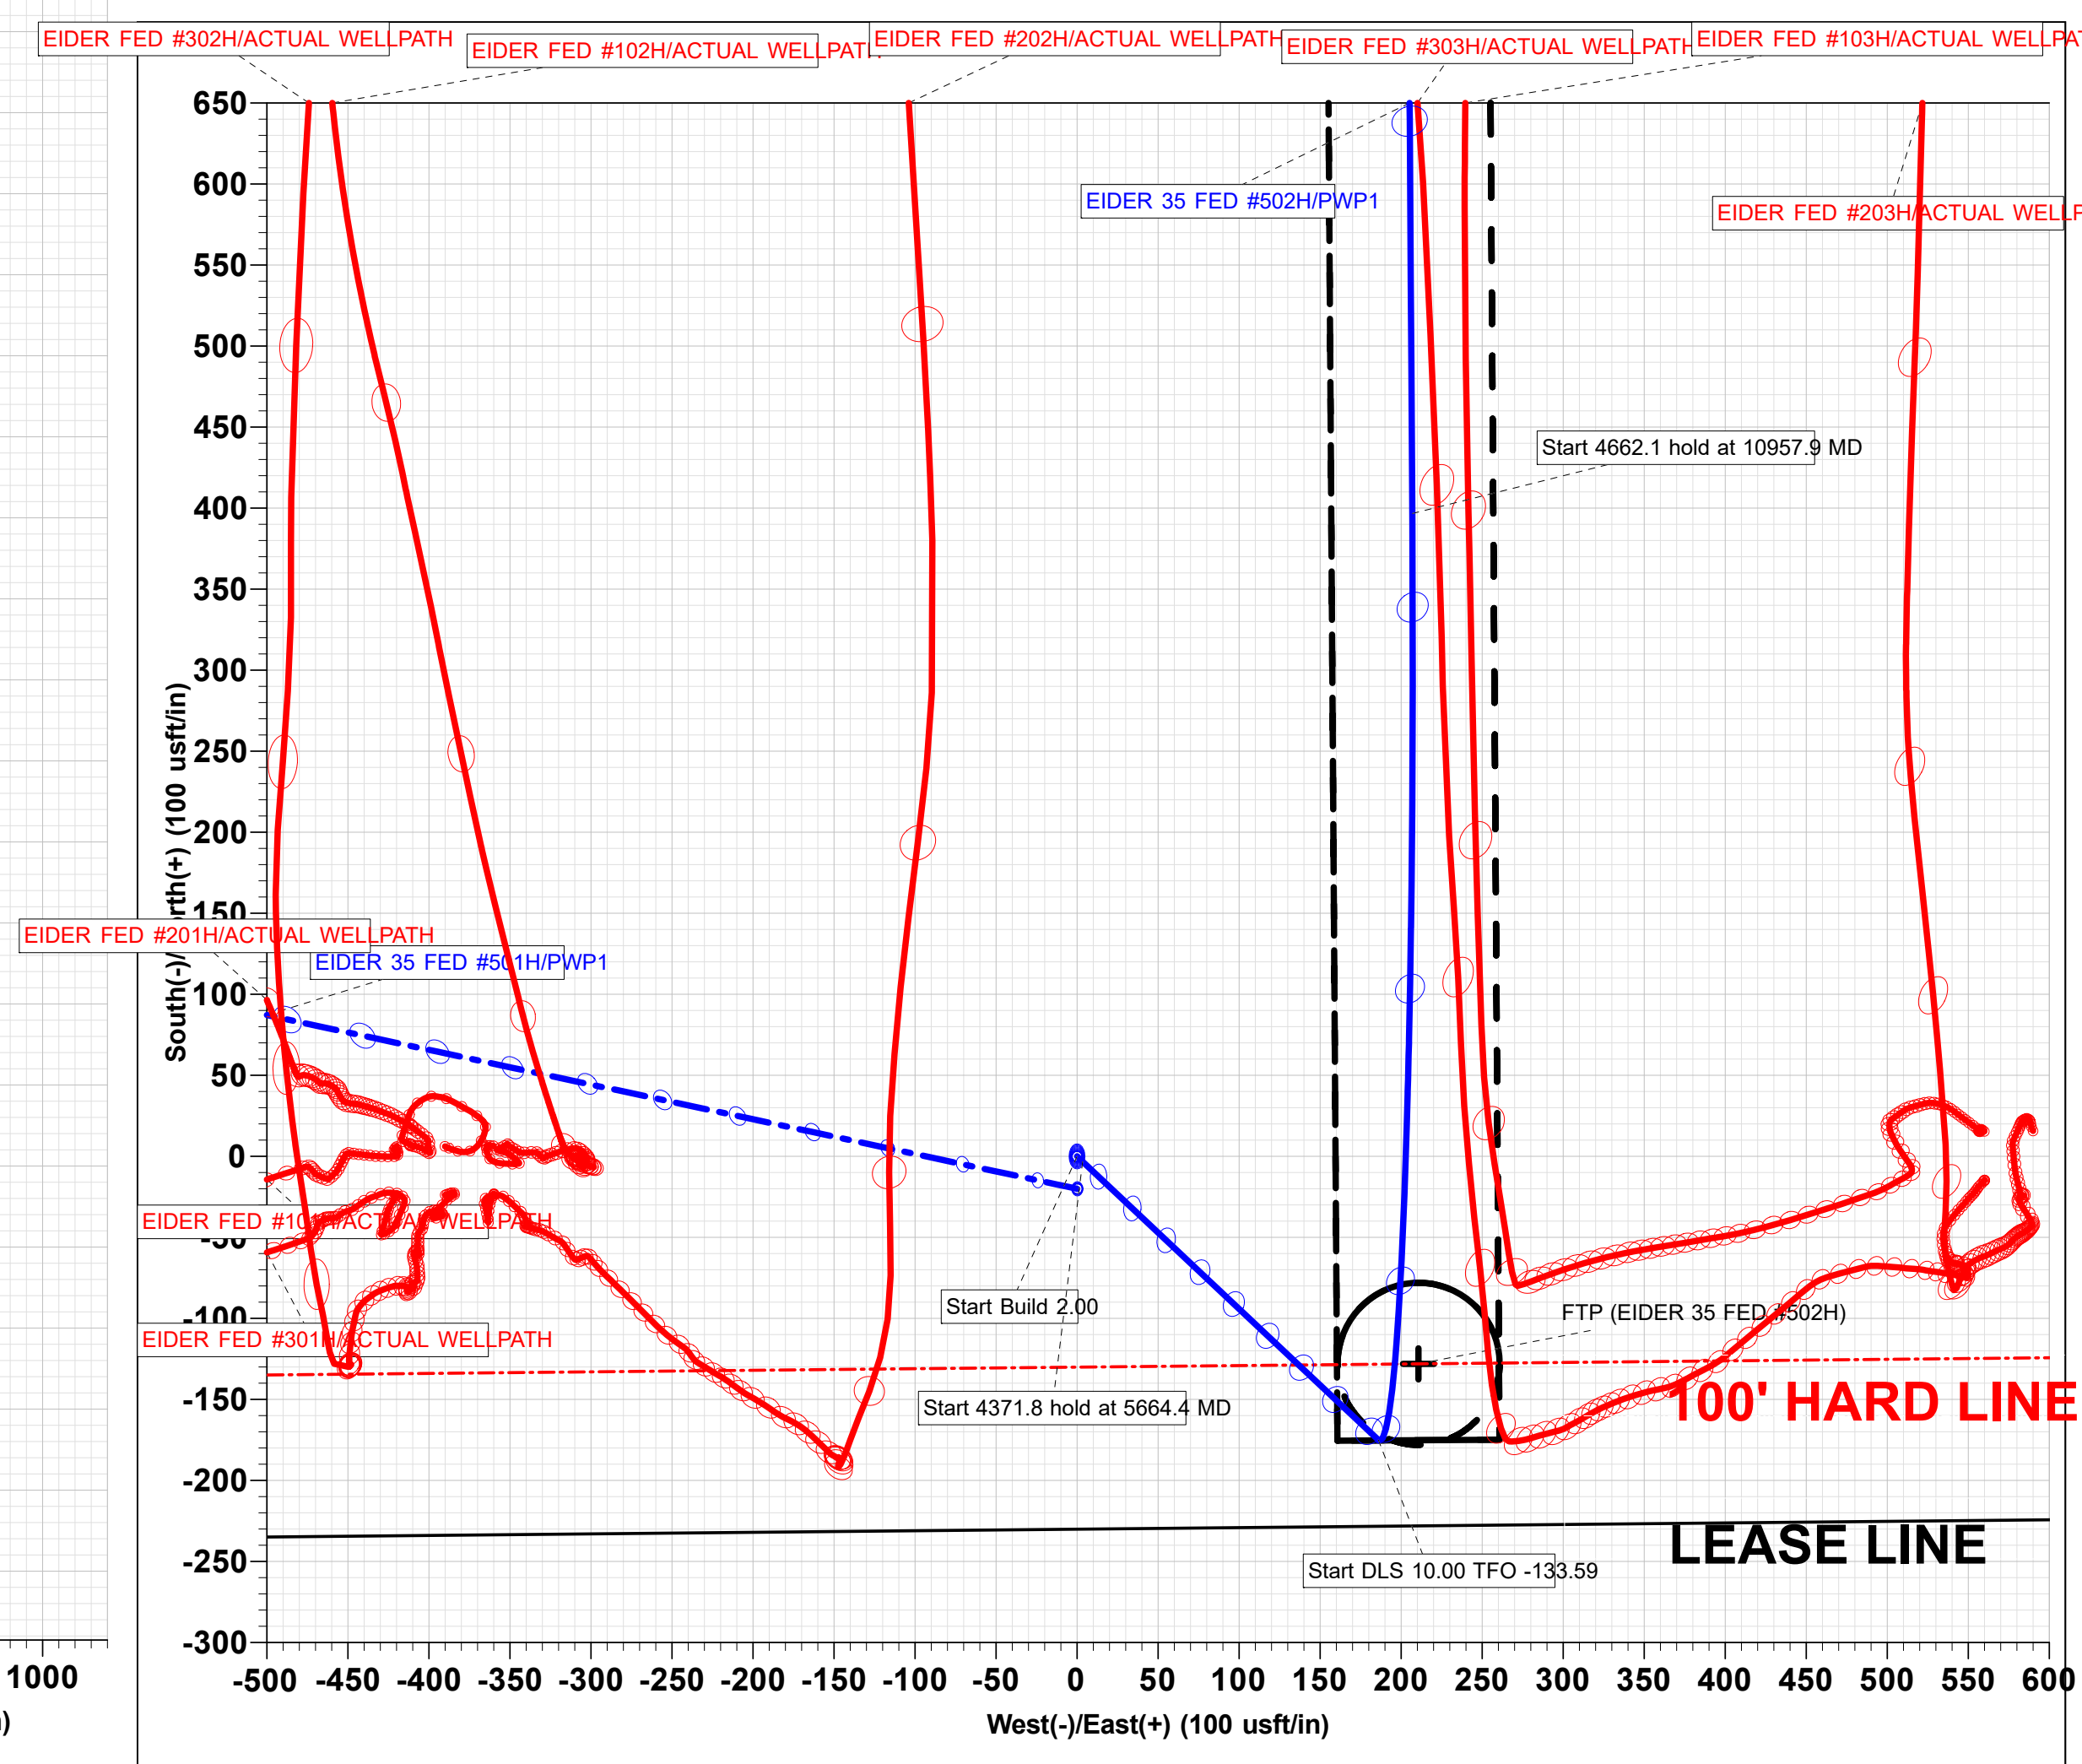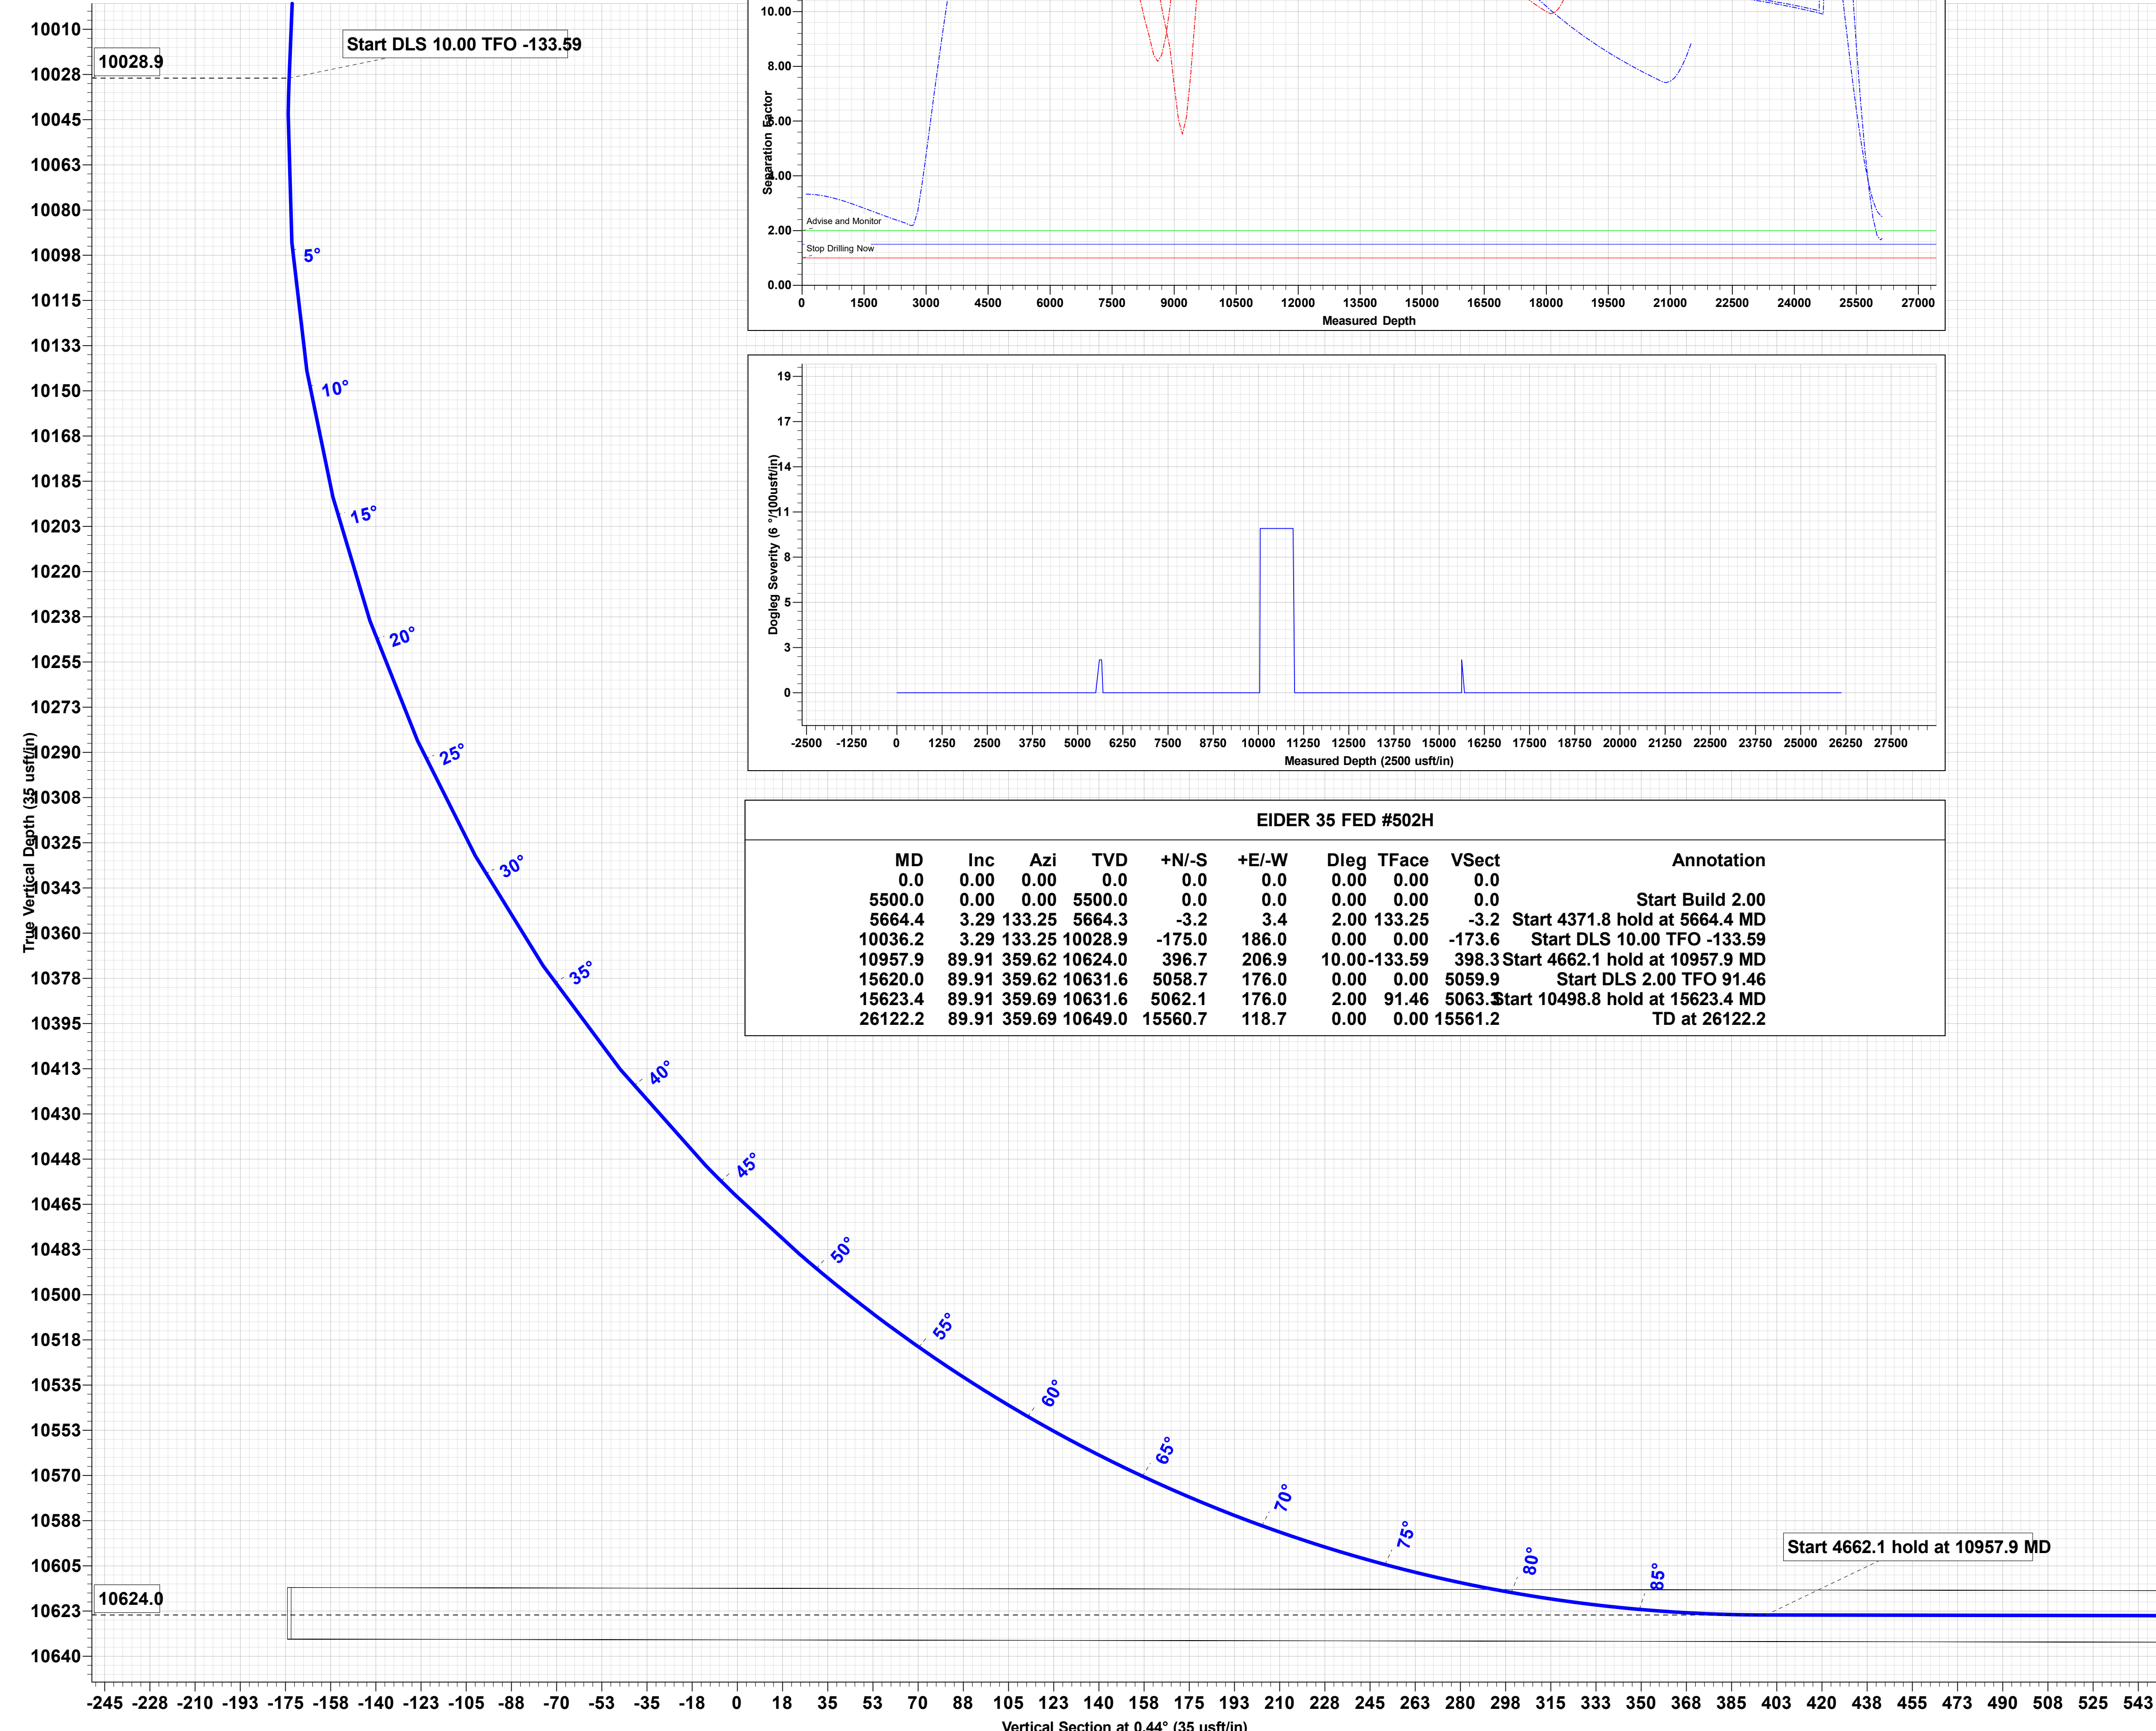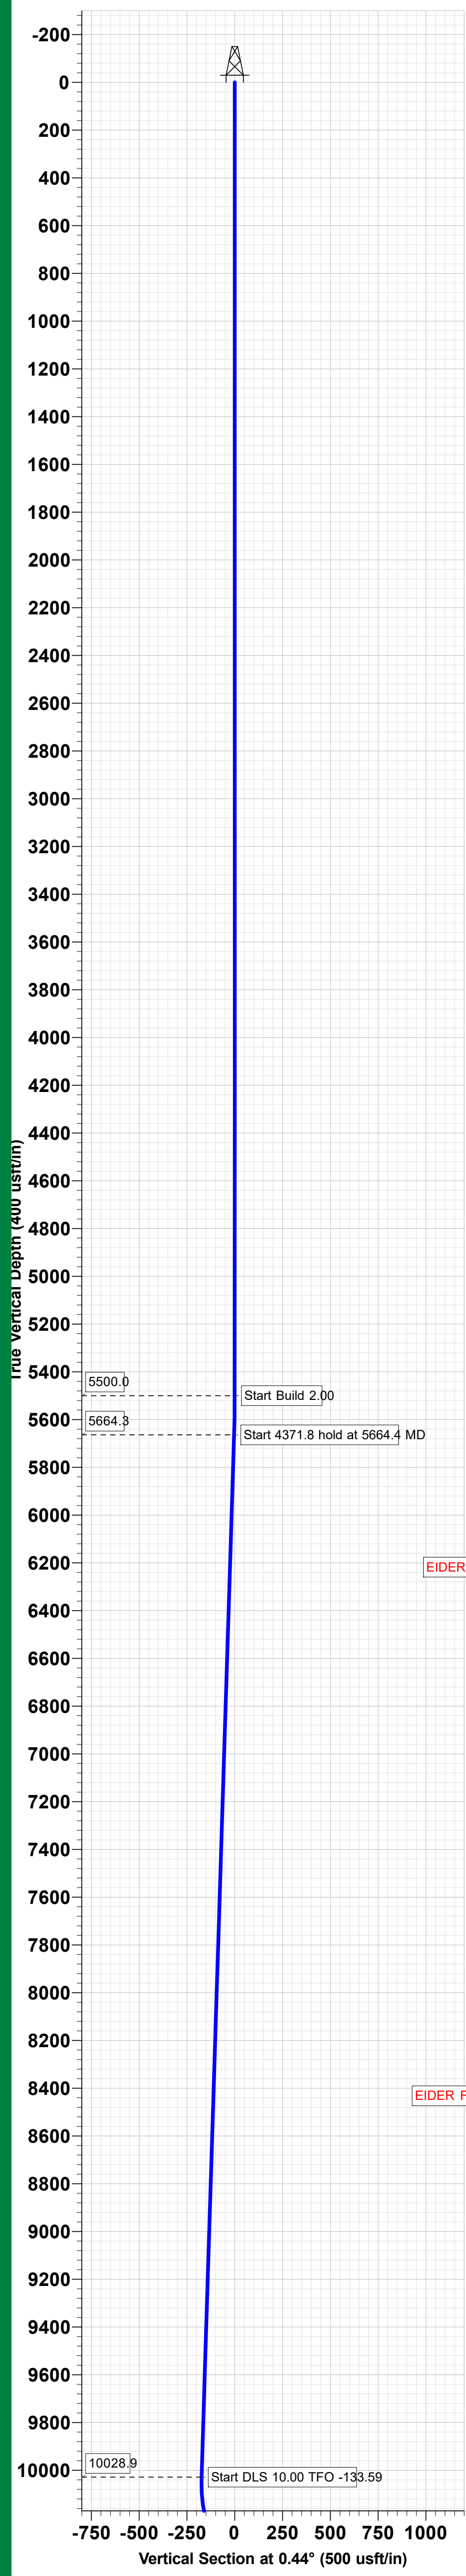

TRGT WNDW: 10' ABOVE/BELOW

TRGT WNDW: 50' RIGHT/LEFT

DELAWARE BASIN EAST

BULLDOG PROSPECT (NM-E)

EIDER 35 FED PROJECT

EIDER 35 FED #502H

OWB

PWP1

Anticollision Report

28 October, 2020

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Reference	PWP1		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	Stations	Error Model:	ISCWSA
Depth Range:	Unlimited	Scan Method:	Closest Approach 3D
Results Limited by:	Maximum ellipse separation of 1,000.0 usft	Error Surface:	Pedal Curve
Warning Levels Evaluated at:	2.00 Sigma	Casing Method:	Not applied

Survey Tool Program		Date	10/28/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.0	10,060.0	PWP1 (OWB)	Standard Keeper 104	Standard Wireline Keeper ver 1.0.4	
10,060.0	26,122.2	PWP1 (OWB)	MWD+IFR1+FDIR	OWSG MWD + IFR1 + FDIR Correction	

Summary						
Site Name	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
EIDER 23 FED COM PROJECT						
EIDER 23 FEDERAL COM #703H - OWB - PWP1	26,122.2	11,021.7	440.4	265.6	2.519	CC, ES, SF
EIDER 23 FEDERAL COM #704H - OWB - PWP1	26,079.5	11,018.7	245.4	98.2	1.667	Advise and Monitor, CC, I
EIDER 35 FED PROJECT						
EIDER 35 FED #501H - OWB - PWP1	2,658.7	2,658.6	19.5	10.6	2.181	CC, ES, SF
EIDER FEDERAL PROJECT (BULLDOG 2434)						
EIDER FED #101H - OWB - ACTUAL WELLPATH	357.4	655.2	418.6	411.4	57.535	CC, ES
EIDER FED #101H - OWB - ACTUAL WELLPATH	3,900.0	4,178.5	477.6	467.6	47.782	SF
EIDER FED #102H - OWB - ACTUAL WELLPATH	5,408.3	5,708.3	298.2	286.7	26.005	CC, ES
EIDER FED #102H - OWB - ACTUAL WELLPATH	5,500.0	5,796.4	299.1	287.6	25.979	SF
EIDER FED #103H - OWB - ACTUAL WELLPATH	8,508.8	8,815.6	152.9	134.7	8.401	CC, ES
EIDER FED #103H - OWB - ACTUAL WELLPATH	8,600.0	8,894.8	157.5	138.3	8.179	SF
EIDER FED #201H - OWB - ACTUAL WELLPATH	391.0	689.8	365.5	358.2	49.883	CC, ES
EIDER FED #201H - OWB - ACTUAL WELLPATH	9,100.0	9,092.0	785.0	764.7	38.588	SF
EIDER FED #202H - OWB - ACTUAL WELLPATH	8,790.1	9,121.7	252.6	235.0	14.340	CC, ES
EIDER FED #202H - OWB - ACTUAL WELLPATH	8,800.0	9,131.0	252.7	235.1	14.339	SF
EIDER FED #203H - OWB - ACTUAL WELLPATH	8,778.4	9,068.7	408.2	390.9	23.585	CC, ES
EIDER FED #203H - OWB - ACTUAL WELLPATH	9,200.0	9,341.0	481.2	458.0	20.721	SF
EIDER FED #301H - OWB - ACTUAL WELLPATH	1,910.5	2,208.6	415.8	408.0	53.378	CC, ES
EIDER FED #301H - OWB - ACTUAL WELLPATH	4,900.0	5,166.8	488.4	477.5	44.850	SF
EIDER FED #302H - OWB - ACTUAL WELLPATH	346.9	644.4	384.6	377.3	52.465	CC, ES
EIDER FED #302H - OWB - ACTUAL WELLPATH	9,400.0	9,447.5	755.6	734.2	35.301	SF
EIDER FED #303H - OWB - ACTUAL WELLPATH	9,109.9	9,426.8	107.9	90.0	6.007	CC, ES
EIDER FED #303H - OWB - ACTUAL WELLPATH	9,200.0	9,495.2	120.7	98.8	5.521	SF

Offset Design	EIDER 23 FED COM PROJECT - EIDER 23 FEDERAL COM #703H - OWB - PWP1										Offset Site Error:	3.0 usft
Survey Program:	0-MWD+IFR1+FDIR										Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Minimum Separation		Warning				
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Separation (usft)	Factor
25,500.0	10,648.0	11,020.6	11,005.2	130.0	39.5	89.87	15,565.6	559.1	764.3	645.3	119.06	6.420
25,600.0	10,648.1	11,020.8	11,005.3	130.9	39.5	89.89	15,565.6	559.1	685.0	557.7	127.37	5.378
25,700.0	10,648.3	11,021.0	11,005.5	131.8	39.5	89.91	15,565.6	559.1	611.8	474.7	137.12	4.462

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER 23 FED COM PROJECT - EIDER 23 FEDERAL COM #703H - OWB - PWP1													Offset Site Error:	3.0 usft
Survey Program: 0-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured	Vertical	Measured	Vertical	Reference	Offset	Highside	Offset Wellbore Centre		Between	Between	Minimum	Separation		
Depth	Depth	Depth	Depth			Toolface	+N/-S	+E/-W	Centres	Ellipses	Separation	Factor		
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)			
25,800.0	10,648.5	11,021.1	11,005.7	132.6	39.5	89.93	15,565.6	559.1	547.2	399.1	148.09	3.695		
25,900.0	10,648.6	11,021.3	11,005.8	133.5	39.5	89.95	15,565.6	559.1	494.4	335.0	159.38	3.102		
26,000.0	10,648.8	11,021.5	11,006.0	134.3	39.5	89.97	15,565.6	559.1	457.7	288.7	169.07	2.707		
26,100.0	10,649.0	11,021.6	11,006.2	135.2	39.5	89.99	15,565.6	559.1	441.1	266.7	174.44	2.529		
26,122.2	10,649.0	11,021.7	11,006.2	135.4	39.5	90.00	15,565.6	559.1	440.4	265.6	174.82	2.519	CC, ES, SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER 23 FED COM PROJECT - EIDER 23 FEDERAL COM #704H - OWB - PWP1												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 11907-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
25,400.0	10,647.8	10,991.7	10,960.2	129.2	13.9	-79.24	15,515.7	-123.6	722.0	655.8	66.14	10.915	
25,500.0	10,648.0	10,995.7	10,964.2	130.0	13.9	-80.16	15,515.8	-123.9	628.9	557.1	71.78	8.761	
25,600.0	10,648.1	10,999.6	10,968.2	130.9	13.9	-81.08	15,516.0	-124.3	538.3	458.9	79.42	6.779	
25,700.0	10,648.3	11,003.6	10,972.1	131.8	13.9	-82.01	15,516.1	-124.6	451.7	361.8	89.92	5.023	
25,800.0	10,648.5	11,007.6	10,976.1	132.6	13.9	-82.93	15,516.3	-124.9	371.8	267.4	104.35	3.563	
25,900.0	10,648.6	11,011.6	10,980.1	133.5	13.9	-83.86	15,516.4	-125.2	304.0	181.1	122.91	2.473	
26,000.0	10,648.8	11,015.6	10,984.0	134.3	13.9	-84.78	15,516.6	-125.5	258.0	116.8	141.19	1.827	Advise and Monitor
26,079.5	10,648.9	11,018.7	10,987.2	135.0	13.9	-85.52	15,516.7	-125.7	245.4	98.2	147.24	1.667	Advise and Monitor, CC, ES, SF
26,100.0	10,649.0	11,019.5	10,988.0	135.2	13.9	-85.71	15,516.7	-125.8	246.3	99.5	146.76	1.678	Advise and Monitor
26,122.2	10,649.0	11,020.4	10,988.9	135.4	13.9	-85.92	15,516.8	-125.9	249.1	103.8	145.28	1.715	Advise and Monitor

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 4

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
EIDER 35 FED PROJECT - EIDER 35 FED #501H - OWB - PWP1												Offset Well Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10208-MWD+IFR1+FDIR													
Reference		Offset		Semi Major Axis		Distance							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	0.0	0.0	3.0	3.0	179.43	-20.0	0.2	20.0				
100.0	100.0	99.8	99.8	3.0	3.0	179.43	-20.0	0.2	20.0	14.0	6.00	3.333	
200.0	200.0	199.8	199.8	3.0	3.0	179.43	-20.0	0.2	20.0	14.0	6.01	3.327	
300.0	300.0	299.8	299.8	3.0	3.0	179.43	-20.0	0.2	20.0	14.0	6.03	3.316	
400.0	400.0	399.8	399.8	3.0	3.0	179.43	-20.0	0.2	20.0	13.9	6.07	3.298	
500.0	500.0	499.8	499.8	3.1	3.1	179.43	-20.0	0.2	20.0	13.9	6.11	3.274	
600.0	600.0	599.8	599.8	3.1	3.1	179.43	-20.0	0.2	20.0	13.8	6.16	3.244	
700.0	700.0	699.8	699.8	3.1	3.1	179.43	-20.0	0.2	20.0	13.8	6.23	3.210	
800.0	800.0	799.8	799.8	3.2	3.2	179.43	-20.0	0.2	20.0	13.7	6.31	3.171	
900.0	900.0	899.8	899.8	3.2	3.2	179.43	-20.0	0.2	20.0	13.6	6.39	3.129	
1,000.0	1,000.0	999.8	999.8	3.2	3.2	179.43	-20.0	0.2	20.0	13.5	6.49	3.082	
1,100.0	1,100.0	1,099.8	1,099.8	3.3	3.3	179.43	-20.0	0.2	20.0	13.4	6.59	3.033	
1,200.0	1,200.0	1,199.8	1,199.8	3.4	3.4	179.43	-20.0	0.2	20.0	13.3	6.71	2.982	
1,300.0	1,300.0	1,299.8	1,299.8	3.4	3.4	179.43	-20.0	0.2	20.0	13.2	6.83	2.929	
1,400.0	1,400.0	1,399.8	1,399.8	3.5	3.5	179.43	-20.0	0.2	20.0	13.0	6.96	2.874	
1,500.0	1,500.0	1,499.8	1,499.8	3.5	3.5	179.43	-20.0	0.2	20.0	12.9	7.10	2.819	
1,600.0	1,600.0	1,599.8	1,599.8	3.6	3.6	179.43	-20.0	0.2	20.0	12.8	7.24	2.762	
1,700.0	1,700.0	1,699.8	1,699.8	3.7	3.7	179.43	-20.0	0.2	20.0	12.6	7.39	2.706	
1,800.0	1,800.0	1,799.8	1,799.8	3.8	3.8	179.43	-20.0	0.2	20.0	12.5	7.55	2.650	
1,900.0	1,900.0	1,899.8	1,899.8	3.9	3.9	179.43	-20.0	0.2	20.0	12.3	7.71	2.594	
2,000.0	2,000.0	1,999.8	1,999.8	3.9	3.9	179.43	-20.0	0.2	20.0	12.1	7.88	2.538	
2,100.0	2,100.0	2,099.8	2,099.8	4.0	4.0	179.43	-20.0	0.2	20.0	11.9	8.05	2.484	
2,200.0	2,200.0	2,199.8	2,199.8	4.1	4.1	179.43	-20.0	0.2	20.0	11.8	8.23	2.430	
2,300.0	2,300.0	2,299.8	2,299.8	4.2	4.2	179.43	-20.0	0.2	20.0	11.6	8.41	2.377	
2,400.0	2,400.0	2,399.8	2,399.8	4.3	4.3	179.43	-20.0	0.2	20.0	11.4	8.60	2.326	
2,500.0	2,500.0	2,499.8	2,499.8	4.4	4.4	179.43	-20.0	0.2	20.0	11.2	8.79	2.275	
2,600.0	2,600.0	2,599.9	2,599.9	4.5	4.5	-175.62	-19.6	-1.5	19.7	10.7	8.95	2.201	
2,658.7	2,658.7	2,658.6	2,658.5	4.6	4.5	-167.90	-19.1	-4.1	19.5	10.6	8.95	2.181	CC, ES, SF
2,700.0	2,700.0	2,699.8	2,699.6	4.6	4.5	-160.38	-18.5	-6.6	19.7	10.8	8.86	2.222	
2,800.0	2,800.0	2,799.3	2,798.7	4.7	4.6	-138.27	-16.8	-14.9	22.5	14.2	8.28	2.715	
2,900.0	2,900.0	2,898.8	2,897.8	4.8	4.6	-121.46	-14.8	-24.2	28.4	20.7	7.74	3.669	
3,000.0	3,000.0	2,998.4	2,997.0	4.9	4.7	-110.99	-12.8	-33.4	35.9	28.4	7.50	4.783	
3,100.0	3,100.0	3,097.9	3,096.1	5.0	4.7	-104.26	-10.8	-42.6	44.1	36.7	7.44	5.927	
3,200.0	3,200.0	3,197.5	3,195.2	5.1	4.8	-99.70	-8.9	-51.8	52.8	45.3	7.48	7.056	
3,300.0	3,300.0	3,297.0	3,294.3	5.2	4.8	-96.43	-6.9	-61.0	61.7	54.1	7.56	8.157	
3,400.0	3,400.0	3,396.6	3,393.4	5.3	4.9	-93.99	-4.9	-70.2	70.7	63.0	7.67	9.224	
3,500.0	3,500.0	3,496.1	3,492.5	5.4	5.0	-92.11	-2.9	-79.5	79.9	72.1	7.79	10.256	
3,600.0	3,600.0	3,595.7	3,591.6	5.5	5.0	-90.62	-1.0	-88.7	89.1	81.2	7.92	11.252	
3,700.0	3,700.0	3,695.2	3,690.7	5.7	5.1	-89.40	1.0	-97.9	98.3	90.3	8.05	12.212	
3,800.0	3,800.0	3,794.8	3,789.8	5.8	5.2	-88.40	3.0	-107.1	107.6	99.4	8.19	13.137	
3,900.0	3,900.0	3,894.3	3,888.9	5.9	5.3	-87.55	5.0	-116.3	117.0	108.6	8.34	14.028	
4,000.0	4,000.0	3,993.9	3,988.0	6.0	5.4	-86.83	6.9	-125.6	126.3	117.8	8.48	14.886	
4,100.0	4,100.0	4,093.4	4,087.1	6.1	5.4	-86.21	8.9	-134.8	135.7	127.0	8.63	15.712	
4,200.0	4,200.0	4,193.0	4,186.2	6.2	5.5	-85.67	10.9	-144.0	145.0	136.3	8.79	16.507	
4,300.0	4,300.0	4,292.5	4,285.3	6.3	5.6	-85.20	12.9	-153.2	154.4	145.5	8.94	17.272	
4,400.0	4,400.0	4,392.1	4,384.4	6.5	5.7	-84.78	14.8	-162.4	163.8	154.7	9.10	18.008	
4,500.0	4,500.0	4,491.6	4,483.5	6.6	5.8	-84.40	16.8	-171.6	173.2	164.0	9.26	18.716	
4,600.0	4,600.0	4,491.2	4,482.6	6.7	5.9	-84.07	18.8	-180.9	182.6	173.2	9.42	19.397	
4,700.0	4,700.0	4,490.7	4,481.7	6.8	6.0	-83.76	20.8	-190.1	192.1	182.5	9.58	20.053	
4,800.0	4,800.0	4,490.3	4,480.8	6.9	6.1	-83.49	22.7	-199.3	201.5	191.7	9.74	20.685	
4,900.0	4,900.0	4,489.8	4,479.9	7.0	6.2	-83.24	24.7	-208.5	210.9	201.0	9.91	21.293	
5,000.0	5,000.0	4,989.4	4,979.0	7.2	6.2	-83.01	26.7	-217.7	220.3	210.3	10.07	21.878	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER 35 FED PROJECT - EIDER 35 FED #501H - OWB - PWP1												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10208-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Warning							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
5,100.0	5,100.0	5,088.9	5,078.1	7.3	6.3	-82.80	28.7	-227.0	229.8	219.5	10.24	22.442	
5,200.0	5,200.0	5,188.5	5,177.2	7.4	6.4	-82.61	30.7	-236.2	239.2	228.8	10.41	22.985	
5,300.0	5,300.0	5,288.0	5,276.3	7.5	6.5	-82.43	32.6	-245.4	248.7	238.1	10.58	23.509	
5,400.0	5,400.0	5,387.6	5,375.4	7.6	6.6	-82.26	34.6	-254.6	258.1	247.4	10.75	24.013	
5,500.0	5,500.0	5,487.1	5,474.5	7.8	6.7	-82.11	36.6	-263.8	267.5	256.6	10.92	24.500	
5,600.0	5,600.0	5,586.5	5,573.5	7.8	6.9	144.86	38.5	-273.0	278.4	267.3	11.09	25.094	
5,664.4	5,664.3	5,650.3	5,636.9	7.8	6.9	145.19	39.8	-278.9	286.9	275.7	11.21	25.591	
5,700.0	5,699.9	5,685.5	5,672.0	7.8	7.0	145.46	40.5	-282.2	292.0	280.7	11.28	25.887	
5,800.0	5,799.7	5,784.5	5,770.5	7.8	7.1	146.17	42.5	-291.4	306.1	294.7	11.46	26.704	
5,900.0	5,899.5	5,883.4	5,869.0	7.8	7.2	146.81	44.4	-300.5	320.3	308.7	11.65	27.502	
6,000.0	5,999.4	5,982.3	5,967.5	7.7	7.3	147.40	46.4	-309.7	334.6	322.8	11.83	28.281	
6,100.0	6,099.2	6,081.2	6,066.0	7.7	7.4	147.95	48.4	-318.8	348.9	336.9	12.01	29.041	
6,200.0	6,199.0	6,180.2	6,164.4	7.7	7.5	148.45	50.3	-328.0	363.2	351.0	12.20	29.781	
6,300.0	6,298.9	6,279.1	6,262.9	7.7	7.6	148.91	52.3	-337.2	377.5	365.2	12.38	30.502	
6,400.0	6,398.7	6,378.0	6,361.4	7.7	7.7	149.34	54.3	-346.3	391.9	379.4	12.56	31.203	
6,500.0	6,498.5	6,476.9	6,459.9	7.7	7.8	149.73	56.2	-355.5	406.3	393.6	12.74	31.885	
6,600.0	6,598.4	6,575.8	6,558.3	7.7	7.9	150.11	58.2	-364.6	420.7	407.8	12.93	32.548	
6,700.0	6,698.2	6,674.8	6,656.8	7.7	8.0	150.45	60.1	-373.8	435.1	422.0	13.11	33.192	
6,800.0	6,798.0	6,773.7	6,755.3	7.7	8.1	150.78	62.1	-383.0	449.5	436.3	13.29	33.817	
6,900.0	6,897.9	6,872.6	6,853.8	7.7	8.3	151.08	64.1	-392.1	464.0	450.5	13.48	34.424	
7,000.0	6,997.7	6,971.5	6,952.3	7.7	8.4	151.36	66.0	-401.3	478.4	464.8	13.67	35.012	
7,100.0	7,097.5	7,070.5	7,050.7	7.7	8.5	151.63	68.0	-410.4	492.9	479.1	13.85	35.583	
7,200.0	7,197.4	7,169.4	7,149.2	7.7	8.6	151.89	70.0	-419.6	507.4	493.4	14.04	36.136	
7,300.0	7,297.2	7,268.3	7,247.7	7.8	8.7	152.13	71.9	-428.8	521.9	507.6	14.23	36.672	
7,400.0	7,397.1	7,367.2	7,346.2	7.8	8.8	152.35	73.9	-437.9	536.4	522.0	14.42	37.191	
7,500.0	7,496.9	7,466.1	7,444.6	7.8	8.9	152.57	75.8	-447.1	550.9	536.3	14.61	37.694	
7,600.0	7,596.7	7,565.1	7,543.1	7.8	9.1	152.77	77.8	-456.2	565.4	550.6	14.81	38.181	
7,700.0	7,696.6	7,664.0	7,641.6	7.8	9.2	152.96	79.8	-465.4	579.9	564.9	15.00	38.653	
7,800.0	7,796.4	7,762.9	7,740.1	7.9	9.3	153.15	81.7	-474.5	594.4	579.2	15.20	39.109	
7,900.0	7,896.2	7,861.8	7,838.6	7.9	9.4	153.32	83.7	-483.7	609.0	593.6	15.40	39.551	
8,000.0	7,996.1	7,960.8	7,937.0	7.9	9.5	153.49	85.7	-492.9	623.5	607.9	15.60	39.978	
8,100.0	8,095.9	8,059.7	8,035.5	7.9	9.6	153.65	87.6	-502.0	638.0	622.2	15.80	40.391	
8,200.0	8,195.7	8,158.6	8,134.0	8.0	9.8	153.80	89.6	-511.2	652.6	636.6	16.00	40.791	
8,300.0	8,295.6	8,257.5	8,232.5	8.0	9.9	153.95	91.5	-520.3	667.1	650.9	16.20	41.178	
8,400.0	8,395.4	8,356.4	8,330.9	8.1	10.0	154.09	93.5	-529.5	681.7	665.3	16.41	41.552	
8,500.0	8,495.2	8,455.4	8,429.4	8.1	10.1	154.22	95.5	-538.7	696.2	679.6	16.61	41.914	
8,600.0	8,595.1	8,554.3	8,527.9	8.1	10.2	154.35	97.4	-547.8	710.8	694.0	16.82	42.264	
8,700.0	8,694.9	8,653.2	8,626.4	8.2	10.3	154.47	99.4	-557.0	725.4	708.3	17.03	42.602	
8,800.0	8,794.8	8,752.1	8,724.9	8.2	10.5	154.59	101.4	-566.1	739.9	722.7	17.24	42.929	
8,900.0	8,894.6	8,851.1	8,823.3	8.3	10.6	154.70	103.3	-575.3	754.5	737.0	17.45	43.246	
9,000.0	8,994.4	8,950.0	8,921.8	8.3	10.7	154.81	105.3	-584.5	769.1	751.4	17.66	43.552	
9,100.0	9,094.3	9,048.9	9,020.3	8.4	10.8	154.92	107.2	-593.6	783.6	765.8	17.87	43.848	
9,200.0	9,194.1	9,147.8	9,118.8	8.5	10.9	155.02	109.2	-602.8	798.2	780.1	18.09	44.134	

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #101H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8589-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	296.5	296.4	4.2	3.0	-89.52	3.5	-420.5	420.5				
100.0	100.0	396.9	396.9	4.2	3.0	-89.38	4.5	-420.7	420.7	413.5	7.25	58.010	
200.0	200.0	501.9	501.9	4.2	3.0	-89.25	5.5	-420.5	420.6	413.3	7.26	57.932	
300.0	300.0	603.6	603.5	4.3	3.0	-89.54	3.4	-419.0	419.1	411.8	7.27	57.655	
357.4	357.4	655.2	655.1	4.3	3.0	-89.65	2.5	-418.6	418.6	411.4	7.28	57.535 CC, ES	
400.0	400.0	691.0	690.9	4.3	3.0	-89.66	2.5	-418.9	419.0	411.7	7.28	57.549	
500.0	500.0	790.0	789.9	4.3	3.0	-89.47	3.9	-420.9	421.0	413.7	7.30	57.707	
600.0	600.0	903.4	903.3	4.3	3.1	-89.50	3.7	-421.3	421.3	414.0	7.32	57.576	
700.0	700.0	1,002.6	1,002.5	4.3	3.1	-89.71	2.1	-420.0	420.1	412.7	7.34	57.253	
800.0	800.0	1,100.0	1,099.8	4.4	3.1	-89.94	0.4	-419.1	419.1	411.8	7.36	56.946	
808.8	808.8	1,106.6	1,106.5	4.4	3.1	-89.95	0.3	-419.1	419.1	411.7	7.36	56.928	
900.0	900.0	1,184.8	1,184.6	4.4	3.1	-90.01	0.0	-420.8	421.0	413.6	7.38	57.038	
1,000.0	1,000.0	1,284.3	1,284.1	4.4	3.2	-90.01	0.0	-424.0	424.2	416.8	7.41	57.221	
1,100.0	1,100.0	1,384.8	1,384.5	4.5	3.2	-90.02	-0.1	-427.2	427.4	420.0	7.45	57.352	
1,200.0	1,200.0	1,485.1	1,484.8	4.5	3.2	-90.00	0.0	-430.3	430.5	423.0	7.50	57.414	
1,300.0	1,300.0	1,585.6	1,585.2	4.5	3.3	-89.98	0.2	-433.2	433.4	425.8	7.55	57.403	
1,400.0	1,400.0	1,686.6	1,686.2	4.6	3.3	-89.93	0.6	-436.0	436.2	428.6	7.61	57.336	
1,500.0	1,500.0	1,785.7	1,785.2	4.6	3.3	-89.89	0.8	-438.8	439.0	431.3	7.67	57.242	
1,600.0	1,600.0	1,886.6	1,886.1	4.7	3.4	-89.85	1.1	-441.5	441.7	433.9	7.74	57.078	
1,700.0	1,700.0	1,987.5	1,987.0	4.8	3.4	-89.81	1.5	-444.2	444.3	436.5	7.81	56.879	
1,800.0	1,800.0	2,086.8	2,086.2	4.8	3.5	-89.78	1.7	-446.7	446.8	438.9	7.89	56.636	
1,900.0	1,900.0	2,187.8	2,187.2	4.9	3.6	-89.73	2.1	-449.2	449.3	441.3	7.97	56.356	
2,000.0	2,000.0	2,294.1	2,293.5	5.0	3.6	-89.80	1.6	-450.9	450.9	442.9	8.06	55.933	
2,100.0	2,100.0	2,394.2	2,393.5	5.0	3.7	-89.99	0.1	-451.9	451.9	443.8	8.14	55.538	
2,200.0	2,200.0	2,494.4	2,493.8	5.1	3.8	-90.20	-1.6	-452.8	452.8	444.6	8.21	55.144	
2,300.0	2,300.0	2,593.7	2,593.0	5.2	3.8	-90.43	-3.4	-453.8	453.8	445.5	8.29	54.755	
2,400.0	2,400.0	2,693.8	2,693.1	5.2	3.9	-90.68	-5.4	-454.8	454.8	446.5	8.37	54.360	
2,500.0	2,500.0	2,793.5	2,792.8	5.3	4.0	-90.93	-7.4	-455.8	455.9	447.4	8.45	53.963	
2,600.0	2,600.0	2,891.9	2,891.1	5.4	4.0	-91.17	-9.3	-456.9	457.0	448.5	8.53	53.565	
2,700.0	2,700.0	2,990.1	2,989.3	5.5	4.1	-91.36	-10.9	-458.6	458.8	450.1	8.63	53.167	
2,800.0	2,800.0	3,089.9	3,089.1	5.6	4.2	-91.57	-12.6	-460.3	460.6	451.9	8.73	52.762	
2,900.0	2,900.0	3,189.9	3,189.1	5.7	4.3	-91.73	-14.0	-462.1	462.4	453.6	8.84	52.335	
3,000.0	3,000.0	3,289.3	3,288.5	5.7	4.4	-91.67	-13.5	-464.1	464.4	455.5	8.95	51.890	
3,100.0	3,100.0	3,390.3	3,389.5	5.8	4.4	-91.56	-12.7	-466.1	466.3	457.3	9.07	51.440	
3,200.0	3,200.0	3,489.9	3,489.0	5.9	4.5	-91.47	-12.0	-468.0	468.2	459.0	9.18	50.984	
3,300.0	3,300.0	3,591.7	3,590.8	6.0	4.6	-91.35	-11.1	-469.7	469.9	460.6	9.30	50.510	
3,400.0	3,400.0	3,694.5	3,693.5	6.1	4.7	-91.22	-10.0	-470.7	470.8	461.4	9.41	50.022	
3,500.0	3,500.0	3,794.4	3,793.5	6.2	4.7	-91.09	-9.0	-471.6	471.7	462.2	9.52	49.546	
3,600.0	3,600.0	3,894.2	3,893.3	6.3	4.8	-90.96	-7.9	-472.5	472.6	463.0	9.63	49.072	
3,700.0	3,700.0	3,993.8	3,992.8	6.4	4.8	-90.86	-7.1	-473.5	473.6	463.9	9.75	48.579	
3,800.0	3,800.0	4,091.0	4,090.1	6.5	4.9	-90.77	-6.4	-474.6	474.7	464.8	9.87	48.091	
3,900.0	3,900.0	4,178.5	4,177.5	6.6	5.0	-90.82	-6.8	-477.1	477.6	467.6	10.00	47.782 SF	
4,000.0	4,000.0	4,260.2	4,259.0	6.7	5.1	-91.01	-8.5	-482.0	483.6	473.5	10.12	47.807	
4,100.0	4,100.0	4,347.2	4,345.7	6.8	5.2	-91.29	-11.1	-490.1	493.0	482.7	10.24	48.121	
4,200.0	4,200.0	4,450.2	4,448.0	6.9	5.3	-91.67	-14.6	-500.7	503.4	493.0	10.39	48.458	
4,300.0	4,300.0	4,557.9	4,555.2	7.0	5.4	-92.13	-18.9	-510.0	512.2	501.6	10.54	48.609	
4,400.0	4,400.0	4,650.0	4,646.9	7.1	5.5	-92.51	-22.7	-518.0	521.0	510.3	10.68	48.807	
4,500.0	4,500.0	4,735.2	4,731.5	7.2	5.6	-92.75	-25.3	-527.4	532.2	521.3	10.81	49.208	
4,600.0	4,600.0	4,836.0	4,831.5	7.3	5.7	-92.93	-27.7	-540.0	544.8	533.8	10.96	49.689	
4,700.0	4,700.0	4,937.6	4,932.4	7.4	5.8	-93.08	-29.7	-551.8	556.5	545.3	11.12	50.061	
4,800.0	4,800.0	5,039.4	5,033.5	7.6	5.9	-93.22	-31.7	-563.4	567.9	556.7	11.27	50.400	
4,900.0	4,900.0	5,140.0	5,133.5	7.7	6.0	-93.38	-33.9	-574.5	579.1	567.6	11.42	50.693	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #101H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8589-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,000.0	5,000.0	5,239.5	5,232.3	7.8	6.1	-93.52	-36.0	-585.3	590.1	578.5	11.58	50.967	
5,100.0	5,100.0	5,337.4	5,329.6	7.9	6.2	-93.67	-38.2	-596.2	601.3	589.6	11.73	51.244	
5,200.0	5,200.0	5,438.5	5,430.1	8.0	6.3	-93.82	-40.6	-607.4	612.5	600.6	11.89	51.506	
5,300.0	5,300.0	5,539.4	5,530.3	8.1	6.5	-93.98	-43.0	-618.4	623.5	611.5	12.05	51.734	
5,400.0	5,400.0	5,641.3	5,631.7	8.2	6.6	-94.14	-45.5	-629.1	634.2	622.0	12.21	51.924	
5,500.0	5,500.0	5,747.7	5,737.5	8.3	6.7	-94.32	-48.3	-639.4	644.1	631.7	12.38	52.038	
5,600.0	5,600.0	5,848.8	5,838.1	8.4	6.8	132.22	-50.9	-648.4	654.3	641.8	12.54	52.172	
5,664.4	5,664.3	5,909.4	5,898.5	8.4	6.9	132.19	-52.4	-654.0	662.3	649.6	12.65	52.367	
5,700.0	5,699.9	5,941.7	5,930.7	8.4	6.9	132.26	-53.1	-657.1	667.2	654.5	12.71	52.511	
5,800.0	5,799.7	6,038.8	6,027.2	8.3	7.0	132.51	-55.1	-666.9	681.2	668.3	12.87	52.927	
5,900.0	5,899.5	6,137.6	6,125.5	8.3	7.1	132.75	-57.1	-676.8	695.3	682.2	13.04	53.331	
6,000.0	5,999.4	6,236.2	6,223.6	8.3	7.2	132.97	-59.2	-686.9	709.5	696.3	13.20	53.730	
6,100.0	6,099.2	6,329.7	6,316.5	8.3	7.4	133.17	-61.2	-696.9	724.1	710.7	13.38	54.138	
6,200.0	6,199.0	6,427.6	6,413.8	8.3	7.5	133.39	-63.3	-707.7	739.2	725.7	13.55	54.569	
6,300.0	6,298.9	6,528.9	6,514.5	8.3	7.6	133.60	-65.3	-718.7	754.0	740.3	13.72	54.962	
6,400.0	6,398.7	6,613.8	6,598.8	8.3	7.7	133.85	-66.1	-728.6	769.7	755.8	13.90	55.381	
6,500.0	6,498.5	6,713.9	6,698.1	8.3	7.8	134.27	-65.1	-741.4	786.4	772.4	14.07	55.905	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 8

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #102H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8177-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toelface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
0.0	0.0	293.1	293.1	4.2	3.0	-88.92	6.8	-363.8	363.9				
100.0	100.0	397.8	397.7	4.2	3.0	-89.00	6.4	-364.6	364.6	357.3	7.27	50.148	
200.0	200.0	498.6	498.6	4.2	3.0	-89.13	5.5	-364.5	364.6	357.3	7.28	50.095	
300.0	300.0	599.4	599.3	4.3	3.1	-89.31	4.4	-364.4	364.4	357.1	7.29	50.014	
400.0	400.0	700.5	700.4	4.3	3.1	-89.62	2.4	-364.1	364.1	356.8	7.30	49.895	
500.0	500.0	806.3	806.1	4.3	3.1	-90.15	-0.9	-362.8	362.9	355.5	7.31	49.649	
600.0	600.0	918.9	918.7	4.3	3.1	-90.61	-3.8	-358.2	358.8	351.5	7.31	49.066	
700.0	700.0	1,020.7	1,020.2	4.3	3.1	-90.74	-4.5	-351.8	352.5	345.2	7.33	48.114	
800.0	800.0	1,113.7	1,113.1	4.4	3.1	-90.78	-4.7	-346.4	346.7	339.4	7.36	47.131	
900.0	900.0	1,200.0	1,199.3	4.4	3.2	-90.70	-4.2	-344.2	344.3	336.9	7.39	46.594	
906.8	906.8	1,205.7	1,205.1	4.4	3.2	-90.69	-4.1	-344.2	344.3	336.9	7.39	46.581	
1,000.0	1,000.0	1,285.2	1,284.5	4.4	3.2	-90.31	-1.9	-346.5	346.8	339.4	7.41	46.810	
1,100.0	1,100.0	1,385.5	1,384.6	4.5	3.2	-89.77	1.4	-350.6	350.9	343.5	7.44	47.175	
1,200.0	1,200.0	1,489.7	1,488.7	4.5	3.2	-89.54	2.8	-353.8	353.9	346.4	7.48	47.330	
1,300.0	1,300.0	1,590.0	1,589.0	4.5	3.2	-89.43	3.5	-356.3	356.5	348.9	7.52	47.408	
1,400.0	1,400.0	1,704.0	1,703.0	4.6	3.2	-89.31	4.3	-357.8	357.9	350.3	7.57	47.288	
1,500.0	1,500.0	1,805.9	1,804.9	4.6	3.3	-89.18	5.1	-356.2	356.3	348.7	7.60	46.871	
1,600.0	1,600.0	1,906.1	1,905.1	4.7	3.3	-89.02	6.0	-354.3	354.4	346.8	7.64	46.386	
1,700.0	1,700.0	2,006.0	2,004.9	4.8	3.3	-88.86	7.0	-352.3	352.5	344.8	7.69	45.860	
1,800.0	1,800.0	2,100.5	2,099.5	4.8	3.3	-88.79	7.4	-351.2	351.3	343.6	7.73	45.422	
1,900.0	1,900.0	2,203.8	2,202.7	4.9	3.4	-88.93	6.5	-350.5	350.6	342.8	7.79	45.012	
2,000.0	2,000.0	2,305.3	2,304.2	5.0	3.4	-89.12	5.4	-348.9	348.9	341.1	7.85	44.471	
2,100.0	2,100.0	2,405.0	2,403.9	5.0	3.4	-89.27	4.4	-347.2	347.3	339.4	7.91	43.908	
2,200.0	2,200.0	2,505.1	2,503.9	5.1	3.5	-89.43	3.4	-345.5	345.6	337.6	7.98	43.322	
2,300.0	2,300.0	2,606.5	2,605.3	5.2	3.6	-89.60	2.4	-343.8	343.8	335.8	8.05	42.716	
2,400.0	2,400.0	2,711.0	2,709.8	5.2	3.6	-89.63	2.2	-340.7	340.9	332.8	8.13	41.940	
2,500.0	2,500.0	2,811.3	2,810.0	5.3	3.7	-89.59	2.4	-337.2	337.4	329.2	8.21	41.081	
2,600.0	2,600.0	2,907.8	2,906.5	5.4	3.7	-89.58	2.5	-334.0	334.1	325.8	8.30	40.253	
2,700.0	2,700.0	3,003.1	3,001.7	5.5	3.8	-89.68	1.8	-332.7	332.7	324.3	8.39	39.667	
2,800.0	2,800.0	3,103.6	3,102.3	5.6	3.9	-89.91	0.5	-331.6	331.6	323.1	8.47	39.140	
2,900.0	2,900.0	3,203.4	3,202.1	5.7	3.9	-90.09	-0.5	-330.3	330.3	321.7	8.56	38.565	
3,000.0	3,000.0	3,303.2	3,301.8	5.7	4.0	-90.19	-1.1	-329.1	329.1	320.4	8.66	37.995	
3,100.0	3,100.0	3,402.3	3,400.9	5.8	4.1	-90.06	-0.4	-328.2	328.2	319.4	8.76	37.462	
3,200.0	3,200.0	3,503.1	3,501.7	5.9	4.1	-89.98	0.1	-327.2	327.2	318.4	8.87	36.910	
3,300.0	3,300.0	3,605.1	3,603.7	6.0	4.2	-89.90	0.6	-325.9	325.9	317.0	8.98	36.301	
3,400.0	3,400.0	3,706.6	3,705.2	6.1	4.3	-89.78	1.3	-323.9	324.0	314.9	9.09	35.628	
3,500.0	3,500.0	3,807.0	3,805.6	6.2	4.4	-89.63	2.1	-321.8	321.9	312.7	9.21	34.947	
3,600.0	3,600.0	3,907.9	3,906.4	6.3	4.4	-89.48	2.9	-319.2	319.3	310.0	9.33	34.222	
3,700.0	3,700.0	4,008.3	4,006.8	6.4	4.5	-89.31	3.8	-316.6	316.8	307.3	9.45	33.506	
3,800.0	3,800.0	4,110.6	4,109.1	6.5	4.6	-89.17	4.5	-313.6	313.8	304.2	9.58	32.748	
3,900.0	3,900.0	4,209.8	4,208.2	6.6	4.7	-89.08	5.0	-310.0	310.2	300.5	9.71	31.944	
4,000.0	4,000.0	4,303.2	4,301.6	6.7	4.8	-89.13	4.7	-308.4	308.4	298.6	9.83	31.362	
4,100.0	4,100.0	4,404.6	4,402.9	6.8	4.9	-89.26	3.9	-307.1	307.2	297.2	9.96	30.835	
4,200.0	4,200.0	4,504.5	4,502.8	6.9	5.0	-89.51	2.6	-305.5	305.6	295.5	10.09	30.298	
4,300.0	4,300.0	4,603.5	4,601.8	7.0	5.1	-89.74	1.4	-304.4	304.4	294.2	10.20	29.830	
4,400.0	4,400.0	4,702.3	4,700.6	7.1	5.2	-89.95	0.3	-303.4	303.4	293.1	10.32	29.392	
4,500.0	4,500.0	4,801.4	4,799.7	7.2	5.2	-90.11	-0.6	-302.9	302.9	292.5	10.43	29.032	
4,600.0	4,600.0	4,900.0	4,898.3	7.3	5.3	-90.24	-1.3	-302.8	302.8	292.3	10.53	28.759	
4,700.0	4,700.0	5,000.3	4,998.6	7.4	5.4	-90.37	-1.9	-302.7	302.7	292.1	10.62	28.501	
4,800.0	4,800.0	5,100.1	5,098.4	7.6	5.4	-90.52	-2.8	-302.6	302.7	291.9	10.71	28.250	
4,900.0	4,900.0	5,200.8	5,199.1	7.7	5.5	-90.75	-3.9	-302.5	302.6	291.8	10.81	28.000	
5,000.0	5,000.0	5,300.8	5,299.1	7.8	5.6	-90.93	-4.9	-302.3	302.4	291.5	10.90	27.732	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 9

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #102H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8177-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,100.0	5,100.0	5,403.5	5,401.8	7.9	5.7	-91.06	-5.6	-301.7	301.8	290.7	11.03	27.364	
5,200.0	5,200.0	5,504.1	5,502.4	8.0	5.8	-91.14	-6.0	-300.4	300.5	289.3	11.17	26.897	
5,300.0	5,300.0	5,603.9	5,602.1	8.1	5.9	-91.21	-6.3	-299.2	299.2	287.9	11.32	26.439	
5,400.0	5,400.0	5,700.0	5,698.3	8.2	6.0	-91.28	-6.7	-298.2	298.2	286.8	11.46	26.023	
5,408.3	5,408.3	5,708.3	5,706.6	8.2	6.0	-91.28	-6.7	-298.1	298.2	286.7	11.47	26.005	CC, ES
5,500.0	5,500.0	5,796.4	5,794.7	8.3	6.0	-91.23	-6.4	-299.0	299.1	287.6	11.51	25.979	SF
5,600.0	5,600.0	5,895.8	5,894.1	8.4	6.0	135.80	-6.0	-300.3	301.7	290.1	11.56	26.093	
5,664.4	5,664.3	5,959.4	5,957.6	8.4	6.0	136.19	-5.7	-301.3	304.8	293.2	11.60	26.288	
5,700.0	5,699.9	5,994.8	5,993.1	8.4	6.0	136.48	-5.6	-301.9	306.9	295.3	11.62	26.421	
5,800.0	5,799.7	6,094.1	6,092.3	8.3	6.0	137.31	-5.0	-303.6	312.8	301.1	11.67	26.793	
5,900.0	5,899.5	6,193.5	6,191.7	8.3	6.0	138.10	-4.5	-305.4	318.9	307.1	11.73	27.177	
6,000.0	5,999.4	6,295.4	6,293.6	8.3	6.0	138.91	-3.7	-307.2	325.0	313.2	11.79	27.551	
6,100.0	6,099.2	6,394.8	6,392.9	8.3	6.0	139.78	-2.4	-308.5	330.6	318.7	11.87	27.853	
6,200.0	6,199.0	6,495.9	6,494.1	8.3	6.0	140.60	-1.3	-309.6	336.2	324.3	11.94	28.151	
6,300.0	6,298.9	6,600.5	6,598.6	8.3	6.0	141.41	-0.3	-309.8	340.9	328.9	12.05	28.302	
6,400.0	6,398.7	6,701.6	6,699.8	8.3	6.1	142.09	0.2	-309.1	344.7	332.5	12.19	28.279	
6,500.0	6,498.5	6,801.8	6,799.9	8.3	6.2	142.69	0.2	-308.2	348.5	336.1	12.34	28.231	
6,600.0	6,598.4	6,901.9	6,900.0	8.3	6.3	143.15	-0.6	-307.4	352.1	339.6	12.49	28.195	
6,700.0	6,698.2	7,002.3	7,000.4	8.3	6.4	143.53	-1.7	-306.5	355.7	343.1	12.63	28.160	
6,800.0	6,798.0	7,103.2	7,101.3	8.3	6.5	143.82	-3.5	-305.5	359.2	346.4	12.77	28.119	
6,900.0	6,897.9	7,202.8	7,200.8	8.3	6.6	144.01	-5.9	-304.4	362.4	349.4	12.91	28.067	
7,000.0	6,997.7	7,293.6	7,291.7	8.3	6.6	144.36	-6.6	-304.7	367.2	354.2	13.01	28.227	
7,100.0	7,097.5	7,388.8	7,386.8	8.3	6.6	144.93	-5.8	-306.8	374.1	361.1	13.09	28.591	
7,200.0	7,197.4	7,494.0	7,492.0	8.3	6.6	145.76	-3.6	-307.8	380.1	367.0	13.17	28.869	
7,300.0	7,297.2	7,595.8	7,593.8	8.3	6.7	146.54	-1.5	-308.1	385.6	372.3	13.27	29.062	
7,400.0	7,397.1	7,695.3	7,693.3	8.3	6.7	147.18	-0.3	-308.4	390.8	377.5	13.37	29.242	
7,500.0	7,496.9	7,795.3	7,793.3	8.3	6.7	147.70	0.3	-308.9	396.2	382.8	13.45	29.462	
7,600.0	7,596.7	7,896.0	7,893.9	8.4	6.7	148.13	0.3	-309.3	401.5	388.0	13.53	29.687	
7,700.0	7,696.6	7,996.1	7,994.0	8.4	6.8	148.52	0.1	-309.6	406.7	393.1	13.62	29.862	
7,800.0	7,796.4	8,095.9	8,093.8	8.4	6.8	148.85	-0.5	-309.9	411.7	398.0	13.73	29.995	
7,900.0	7,896.2	8,196.0	8,194.0	8.4	6.9	149.15	-1.3	-310.1	416.7	402.8	13.83	30.123	
8,000.0	7,996.1	8,293.5	8,291.4	8.5	6.9	149.42	-2.0	-310.7	422.1	408.1	13.94	30.268	
8,100.0	8,095.9	8,392.4	8,390.4	8.5	7.0	149.94	-0.9	-311.2	427.8	413.7	14.10	30.339	
8,200.0	8,195.7	8,491.1	8,489.0	8.5	7.1	150.45	0.4	-312.0	433.8	419.5	14.28	30.382	
8,300.0	8,295.6	8,591.4	8,589.3	8.6	7.2	150.88	1.0	-313.0	440.0	425.5	14.42	30.515	
8,400.0	8,395.4	8,683.0	8,680.9	8.6	7.3	151.29	2.0	-314.2	446.5	431.9	14.62	30.545	
8,500.0	8,495.2	8,756.0	8,753.6	8.6	7.5	152.03	6.7	-317.0	457.0	442.1	14.99	30.486	
8,600.0	8,595.1	8,817.2	8,813.4	8.7	8.4	153.57	19.2	-321.5	475.0	459.3	15.77	30.124	
8,700.0	8,694.9	8,880.4	8,872.8	8.7	9.1	155.83	39.4	-328.1	500.7	483.9	16.83	29.756	
8,800.0	8,794.8	8,944.0	8,930.6	8.8	9.4	158.45	64.7	-335.9	533.0	515.0	17.95	29.698	
8,900.0	8,894.6	9,004.7	8,983.6	8.8	9.7	161.19	93.3	-343.6	571.2	552.1	19.15	29.829	
9,000.0	8,994.4	9,038.0	9,011.2	8.9	9.9	162.81	111.4	-348.1	616.9	596.0	20.92	29.489	
9,100.0	9,094.3	9,085.0	9,047.5	8.9	10.3	165.23	140.3	-355.4	670.0	647.5	22.54	29.731	
9,200.0	9,194.1	9,110.7	9,065.9	9.0	10.5	166.59	157.7	-359.8	729.9	705.6	24.28	30.065	
9,300.0	9,293.9	9,132.0	9,080.3	9.0	10.7	167.73	172.9	-363.4	795.5	769.6	25.88	30.736	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 10

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #103H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8586-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Warning							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toelface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
0.0	0.0	306.9	306.9	4.2	3.0	88.29	16.7	558.1	558.3				
100.0	100.0	406.0	406.0	4.2	3.0	88.30	16.6	557.7	558.0	550.7	7.27	76.765	
200.0	200.0	505.3	505.3	4.2	3.0	88.31	16.4	557.5	557.7	550.4	7.29	76.537	
300.0	300.0	606.0	606.0	4.3	3.1	88.32	16.3	557.2	557.5	550.1	7.31	76.246	
400.0	400.0	706.4	706.4	4.3	3.1	88.34	16.1	556.9	557.1	549.8	7.34	75.890	
500.0	500.0	805.9	805.9	4.3	3.1	88.36	15.9	556.6	556.8	549.5	7.38	75.501	
599.2	599.2	903.6	903.6	4.3	3.1	88.39	15.6	556.5	556.7	549.3	7.40	75.222	
600.0	600.0	904.4	904.4	4.3	3.1	88.39	15.6	556.5	556.7	549.3	7.40	75.221	
700.0	700.0	1,002.7	1,002.7	4.3	3.1	88.41	15.4	556.8	557.0	549.6	7.40	75.225	
800.0	800.0	1,103.0	1,103.0	4.4	3.1	88.42	15.4	557.0	557.2	549.8	7.41	75.233	
900.0	900.0	1,202.0	1,202.0	4.4	3.1	88.43	15.3	557.3	557.5	550.1	7.42	75.176	
1,000.0	1,000.0	1,310.3	1,310.3	4.4	3.2	88.40	15.5	557.2	557.5	550.0	7.44	74.904	
1,100.0	1,100.0	1,413.1	1,413.0	4.5	3.2	88.27	16.8	555.7	556.1	548.6	7.49	74.282	
1,200.0	1,200.0	1,514.3	1,514.2	4.5	3.2	88.11	18.3	554.0	554.4	546.8	7.53	73.588	
1,300.0	1,300.0	1,614.4	1,614.3	4.5	3.3	87.96	19.7	552.1	552.6	545.0	7.59	72.839	
1,400.0	1,400.0	1,714.6	1,714.5	4.6	3.3	87.81	21.0	550.2	550.7	543.1	7.64	72.057	
1,500.0	1,500.0	1,814.6	1,814.4	4.6	3.3	87.66	22.4	548.4	548.9	541.2	7.70	71.251	
1,600.0	1,600.0	1,913.7	1,913.5	4.7	3.4	87.51	23.7	546.6	547.2	539.4	7.77	70.434	
1,700.0	1,700.0	2,013.9	2,013.7	4.8	3.5	87.37	25.0	544.9	545.6	537.7	7.84	69.606	
1,800.0	1,800.0	2,113.9	2,113.7	4.8	3.5	87.22	26.3	543.1	543.8	535.9	7.91	68.750	
1,900.0	1,900.0	2,214.5	2,214.2	4.9	3.6	87.07	27.7	541.3	542.1	534.1	7.99	67.881	
2,000.0	2,000.0	2,314.9	2,314.7	5.0	3.6	86.92	29.0	539.4	540.3	532.2	8.07	66.976	
2,100.0	2,100.0	2,415.3	2,415.0	5.0	3.7	86.78	30.2	537.4	538.4	530.2	8.15	66.040	
2,200.0	2,200.0	2,515.3	2,514.9	5.1	3.8	86.67	31.1	535.4	536.4	528.2	8.24	65.075	
2,300.0	2,300.0	2,615.0	2,614.7	5.2	3.9	86.58	31.9	533.4	534.5	526.1	8.34	64.094	
2,400.0	2,400.0	2,715.9	2,715.5	5.2	3.9	86.51	32.4	531.4	532.5	524.1	8.44	63.091	
2,500.0	2,500.0	2,816.3	2,815.9	5.3	4.0	86.45	32.8	529.2	530.4	521.8	8.55	62.063	
2,600.0	2,600.0	2,916.6	2,916.2	5.4	4.1	86.41	33.0	527.0	528.2	519.5	8.66	61.019	
2,700.0	2,700.0	3,017.1	3,016.7	5.5	4.2	86.41	32.9	524.7	525.9	517.1	8.77	59.963	
2,800.0	2,800.0	3,117.1	3,116.6	5.6	4.3	86.45	32.4	522.4	523.6	514.7	8.89	58.917	
2,900.0	2,900.0	3,216.8	3,216.3	5.7	4.4	86.51	31.8	520.1	521.2	512.2	9.01	57.878	
3,000.0	3,000.0	3,317.2	3,316.7	5.7	4.5	86.56	31.1	517.8	518.9	509.8	9.13	56.853	
3,100.0	3,100.0	3,417.1	3,416.5	5.8	4.5	86.61	30.6	515.5	516.6	507.3	9.25	55.836	
3,200.0	3,200.0	3,517.6	3,517.0	5.9	4.6	86.69	29.7	513.1	514.1	504.8	9.38	54.822	
3,300.0	3,300.0	3,616.8	3,616.2	6.0	4.7	86.80	28.6	510.7	511.6	502.1	9.50	53.834	
3,400.0	3,400.0	3,714.4	3,713.8	6.1	4.8	86.95	27.1	508.8	509.7	500.0	9.62	52.957	
3,500.0	3,500.0	3,814.9	3,814.2	6.2	4.9	87.07	26.0	507.0	507.8	498.0	9.75	52.078	
3,600.0	3,600.0	3,915.0	3,914.3	6.3	5.0	87.21	24.6	505.2	505.9	496.0	9.88	51.217	
3,700.0	3,700.0	4,014.4	4,013.6	6.4	5.1	87.36	23.2	503.4	504.0	494.0	10.00	50.380	
3,800.0	3,800.0	4,110.8	4,110.0	6.5	5.1	87.52	21.7	501.9	502.4	492.3	10.12	49.635	
3,900.0	3,900.0	4,206.5	4,205.7	6.6	5.2	87.74	19.8	501.3	501.7	491.5	10.22	49.105	
3,939.4	3,939.4	4,244.6	4,243.8	6.6	5.2	87.84	18.9	501.3	501.7	491.4	10.25	48.953	
4,000.0	4,000.0	4,303.9	4,303.1	6.7	5.2	87.99	17.6	501.4	501.8	491.5	10.29	48.751	
4,100.0	4,100.0	4,400.8	4,400.0	6.8	5.3	88.27	15.1	502.0	502.2	491.9	10.36	48.489	
4,200.0	4,200.0	4,496.9	4,496.0	6.9	5.3	88.63	12.0	503.3	503.5	493.1	10.41	48.361	
4,300.0	4,300.0	4,593.6	4,592.6	7.0	5.3	89.09	8.0	505.4	505.6	495.2	10.46	48.325	
4,400.0	4,400.0	4,690.4	4,689.3	7.1	5.3	89.58	3.7	508.0	508.3	497.8	10.51	48.352	
4,500.0	4,500.0	4,790.9	4,789.6	7.2	5.3	90.08	-0.7	511.0	511.2	500.7	10.56	48.416	
4,600.0	4,600.0	4,893.0	4,891.6	7.3	5.4	90.52	-4.7	513.9	514.0	503.4	10.61	48.457	
4,700.0	4,700.0	5,004.3	5,002.9	7.4	5.4	90.92	-8.3	515.2	515.3	504.6	10.67	48.271	
4,800.0	4,800.0	5,123.8	5,122.3	7.6	5.5	91.28	-11.5	513.2	513.7	502.9	10.80	47.556	
4,900.0	4,900.0	5,235.0	5,233.2	7.7	5.6	91.68	-14.8	507.4	508.4	497.5	10.95	46.420	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #103H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8586-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,000.0	5,000.0	5,335.0	5,333.0	7.8	5.7	92.07	-18.1	501.5	502.7	491.6	11.09	45.330	
5,100.0	5,100.0	5,443.4	5,441.2	7.9	5.8	92.50	-21.6	494.6	496.5	485.2	11.24	44.155	
5,200.0	5,200.0	5,548.0	5,545.3	8.0	6.0	92.89	-24.6	486.1	488.4	477.0	11.40	42.854	
5,300.0	5,300.0	5,648.4	5,645.3	8.1	6.1	93.30	-27.6	477.4	480.0	468.4	11.54	41.583	
5,400.0	5,400.0	5,747.5	5,744.1	8.2	6.2	93.71	-30.4	468.8	471.4	459.7	11.69	40.338	
5,500.0	5,500.0	5,848.0	5,844.1	8.3	6.3	94.13	-33.2	460.0	462.9	451.1	11.84	39.111	
5,600.0	5,600.0	5,948.1	5,943.8	8.4	6.4	-38.97	-35.9	451.3	453.0	441.0	11.98	37.807	
5,664.4	5,664.3	6,010.9	6,006.4	8.4	6.5	-39.03	-37.6	445.8	445.3	433.2	12.07	36.879	
5,700.0	5,699.9	6,046.3	6,041.6	8.4	6.5	-39.05	-38.5	442.7	440.6	428.5	12.13	36.337	
5,800.0	5,799.7	6,145.4	6,140.3	8.3	6.6	-39.11	-41.0	434.0	427.7	415.4	12.28	34.840	
5,900.0	5,899.5	6,244.7	6,239.2	8.3	6.7	-39.18	-43.4	425.4	414.8	402.4	12.43	33.371	
6,000.0	5,999.4	6,343.0	6,337.1	8.3	6.8	-39.28	-45.7	416.8	401.8	389.3	12.58	31.934	
6,100.0	6,099.2	6,437.6	6,431.3	8.3	6.9	-39.47	-47.3	409.5	389.8	377.1	12.73	30.625	
6,200.0	6,199.0	6,535.4	6,528.9	8.3	7.0	-39.75	-48.6	402.7	378.5	365.6	12.89	29.362	
6,300.0	6,298.9	6,633.5	6,626.8	8.3	7.1	-40.07	-49.7	396.1	367.5	354.4	13.06	28.142	
6,400.0	6,398.7	6,732.5	6,725.5	8.3	7.3	-40.43	-50.8	389.7	356.7	343.5	13.23	26.959	
6,500.0	6,498.5	6,831.7	6,824.6	8.3	7.4	-40.80	-51.9	383.4	346.1	332.7	13.41	25.807	
6,600.0	6,598.4	6,930.9	6,923.5	8.3	7.5	-41.21	-53.0	377.2	335.6	322.0	13.59	24.686	
6,700.0	6,698.2	7,030.0	7,022.5	8.3	7.6	-41.66	-54.0	371.2	325.2	311.5	13.78	23.604	
6,800.0	6,798.0	7,128.1	7,120.4	8.3	7.7	-42.14	-54.9	365.4	315.1	301.1	13.97	22.562	
6,900.0	6,897.9	7,226.6	7,218.8	8.3	7.8	-42.67	-55.8	359.9	305.3	291.1	14.16	21.564	
7,000.0	6,997.7	7,326.4	7,318.4	8.3	8.0	-43.22	-56.7	354.4	295.6	281.3	14.36	20.589	
7,100.0	7,097.5	7,426.0	7,417.8	8.3	8.1	-43.83	-57.7	348.9	286.0	271.4	14.56	19.636	
7,200.0	7,197.4	7,525.4	7,517.1	8.3	8.2	-44.45	-58.7	343.4	276.3	261.5	14.77	18.707	
7,300.0	7,297.2	7,627.8	7,619.3	8.3	8.3	-45.09	-59.9	337.2	266.1	251.1	15.00	17.747	
7,400.0	7,397.1	7,727.6	7,718.9	8.3	8.4	-45.69	-61.5	330.5	255.4	240.2	15.21	16.791	
7,500.0	7,496.9	7,826.1	7,817.1	8.3	8.5	-46.34	-63.0	323.9	244.6	229.2	15.42	15.868	
7,600.0	7,596.7	7,924.9	7,915.8	8.4	8.7	-47.06	-64.6	317.7	234.4	218.7	15.63	14.993	
7,700.0	7,696.6	8,025.2	8,015.8	8.4	8.8	-47.78	-66.4	311.3	224.0	208.2	15.86	14.127	
7,800.0	7,796.4	8,124.2	8,114.6	8.4	8.9	-48.52	-68.3	305.0	213.6	197.6	16.08	13.288	
7,900.0	7,796.2	8,223.1	8,213.2	8.4	9.0	-49.30	-70.4	298.8	203.5	187.2	16.30	12.486	
8,000.0	7,996.1	8,322.2	8,312.2	8.5	9.1	-50.14	-72.5	292.9	193.6	177.1	16.52	11.720	
8,100.0	8,095.9	8,421.6	8,411.3	8.5	9.3	-51.06	-74.6	287.1	183.9	167.2	16.75	10.980	
8,200.0	8,195.7	8,520.3	8,509.9	8.5	9.4	-52.08	-76.7	281.6	174.5	157.6	16.98	10.281	
8,300.0	8,295.6	8,619.5	8,609.0	8.6	9.5	-53.25	-78.7	276.3	165.5	148.3	17.16	9.642	
8,400.0	8,395.4	8,716.9	8,706.2	8.6	9.5	-54.73	-79.9	271.7	157.2	139.9	17.30	9.084	
8,500.0	8,495.2	8,807.8	8,796.4	8.6	10.2	-59.98	-70.6	268.3	152.9	134.8	18.12	8.439	
8,508.8	8,504.0	8,815.6	8,804.1	8.6	10.2	-60.74	-69.0	268.0	152.9	134.7	18.20	8.401 CC, ES	
8,600.0	8,595.1	8,894.8	8,879.6	8.7	10.7	-70.65	-45.8	264.3	157.5	138.3	19.26	8.179 SF	
8,700.0	8,694.9	8,974.5	8,951.8	8.7	10.9	-82.81	-12.6	259.0	175.9	155.0	20.89	8.419	
8,800.0	8,794.8	9,039.0	9,006.9	8.8	11.1	-92.50	20.6	254.1	210.8	187.7	23.16	9.104	
8,900.0	8,894.6	9,085.0	9,043.0	8.8	11.4	-98.67	48.8	251.3	262.9	237.1	25.86	10.169	
9,000.0	8,894.4	9,132.0	9,076.6	8.9	11.7	-103.96	81.6	249.6	327.7	299.9	27.78	11.796	
9,100.0	9,094.3	9,179.0	9,107.5	8.9	11.9	-108.23	117.1	248.4	400.3	371.3	29.00	13.805	
9,200.0	9,194.1	9,201.0	9,120.8	9.0	11.9	-109.96	134.5	247.8	478.0	447.6	30.39	15.732	
9,300.0	9,293.9	9,226.0	9,134.9	9.0	12.0	-111.75	155.2	247.2	560.4	529.0	31.40	17.847	
9,400.0	9,393.8	9,246.0	9,145.2	9.1	12.1	-113.05	172.3	246.7	645.9	613.6	32.29	20.003	
9,500.0	9,493.6	9,272.0	9,157.6	9.1	12.1	-114.60	195.1	245.9	734.0	700.9	33.02	22.227	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 12

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #201H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8667-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Warning							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
0.0	0.0	319.0	318.9	4.2	3.0	-89.50	3.3	-382.5	383.1				
100.0	100.0	421.1	420.8	4.2	3.0	-89.57	2.8	-376.3	377.1	369.8	7.26	51.918	
200.0	200.0	518.8	518.2	4.2	3.1	-89.07	6.0	-370.5	371.1	363.8	7.29	50.939	
300.0	300.0	609.0	608.1	4.3	3.1	-88.11	12.1	-366.5	366.9	359.5	7.31	50.179	
391.0	391.0	689.8	688.7	4.3	3.1	-87.25	17.5	-365.1	365.5	358.2	7.33	49.883 CC, ES	
400.0	400.0	697.5	696.4	4.3	3.1	-87.18	18.0	-365.1	365.5	358.2	7.33	49.877	
500.0	500.0	777.3	776.0	4.3	3.1	-86.49	22.5	-367.3	368.6	361.3	7.32	50.332	
600.0	600.0	870.5	868.9	4.3	3.1	-85.81	27.4	-373.7	375.8	368.5	7.32	51.343	
700.0	700.0	969.1	967.1	4.3	3.1	-85.27	31.6	-381.1	383.7	376.3	7.33	52.356	
800.0	800.0	1,069.3	1,066.9	4.4	3.1	-84.79	35.5	-388.8	391.6	384.2	7.34	53.315	
900.0	900.0	1,170.8	1,168.2	4.4	3.1	-84.65	37.1	-396.4	399.2	391.8	7.37	54.176	
1,000.0	1,000.0	1,274.0	1,271.0	4.4	3.1	-85.03	35.1	-403.7	406.1	398.7	7.40	54.882	
1,100.0	1,100.0	1,384.0	1,380.8	4.5	3.2	-85.89	29.5	-410.2	411.6	404.2	7.44	55.325	
1,200.0	1,200.0	1,495.5	1,492.0	4.5	3.2	-86.76	23.4	-412.9	413.6	406.1	7.48	55.286	
1,300.0	1,300.0	1,594.6	1,591.0	4.5	3.2	-87.48	18.2	-414.6	415.0	407.5	7.52	55.211	
1,400.0	1,400.0	1,696.5	1,692.7	4.6	3.2	-88.19	13.1	-416.3	416.6	409.0	7.56	55.117	
1,500.0	1,500.0	1,810.1	1,806.2	4.6	3.3	-88.68	9.6	-416.4	416.6	409.0	7.60	54.804	
1,600.0	1,600.0	1,914.2	1,910.3	4.7	3.3	-88.85	8.3	-413.3	413.6	406.0	7.64	54.130	
1,700.0	1,700.0	2,003.4	1,999.4	4.8	3.3	-88.96	7.5	-411.4	411.5	403.8	7.69	53.546	
1,800.0	1,800.0	2,101.6	2,097.7	4.8	3.3	-88.96	7.5	-411.4	411.4	403.7	7.73	53.204	
1,807.1	1,807.1	2,108.9	2,105.0	4.8	3.3	-88.96	7.5	-411.3	411.4	403.7	7.74	53.179	
1,900.0	1,900.0	2,201.9	2,198.0	4.9	3.4	-88.96	7.4	-411.3	411.4	403.6	7.78	52.856	
2,000.0	2,000.0	2,302.0	2,298.1	5.0	3.4	-88.98	7.3	-411.3	411.4	403.5	7.84	52.499	
2,012.7	2,012.7	2,314.3	2,310.4	5.0	3.4	-88.98	7.3	-411.3	411.4	403.5	7.84	52.454	
2,100.0	2,100.0	2,401.3	2,397.4	5.0	3.4	-88.99	7.2	-411.4	411.5	403.6	7.89	52.157	
2,200.0	2,200.0	2,500.5	2,496.6	5.1	3.5	-89.03	7.0	-411.6	411.7	403.7	7.95	51.811	
2,300.0	2,300.0	2,606.8	2,602.9	5.2	3.5	-89.06	6.8	-410.8	410.9	402.9	8.01	51.322	
2,400.0	2,400.0	2,707.6	2,703.6	5.2	3.6	-89.10	6.4	-409.5	409.6	401.5	8.07	50.748	
2,500.0	2,500.0	2,807.2	2,803.2	5.3	3.6	-89.13	6.2	-408.1	408.1	400.0	8.14	50.146	
2,600.0	2,600.0	2,908.6	2,904.7	5.4	3.7	-89.18	5.8	-406.6	406.7	398.5	8.21	49.519	
2,700.0	2,700.0	3,008.7	3,004.7	5.5	3.7	-89.25	5.3	-405.0	405.1	396.8	8.29	48.855	
2,800.0	2,800.0	3,108.0	3,104.0	5.6	3.8	-89.37	4.4	-403.5	403.5	395.2	8.37	48.196	
2,900.0	2,900.0	3,208.4	3,204.4	5.7	3.9	-89.49	3.6	-401.9	402.0	393.5	8.46	47.525	
3,000.0	3,000.0	3,307.8	3,303.8	5.7	3.9	-89.62	2.7	-400.3	400.4	391.8	8.55	46.847	
3,100.0	3,100.0	3,402.0	3,398.0	5.8	4.0	-89.67	2.3	-399.2	399.2	390.5	8.63	46.240	
3,102.9	3,102.9	3,404.6	3,400.6	5.8	4.0	-89.66	2.4	-399.2	399.2	390.5	8.63	46.229	
3,200.0	3,200.0	3,497.9	3,493.8	5.9	4.0	-89.36	4.5	-399.8	399.9	391.2	8.70	45.969	
3,300.0	3,300.0	3,601.7	3,597.6	6.0	4.0	-89.03	6.8	-400.5	400.5	391.7	8.77	45.663	
3,400.0	3,400.0	3,701.7	3,697.6	6.1	4.0	-88.74	8.8	-400.4	400.5	391.7	8.85	45.266	
3,500.0	3,500.0	3,795.1	3,791.0	6.2	4.1	-88.48	10.6	-400.9	401.1	392.2	8.92	44.972	
3,600.0	3,600.0	3,893.1	3,888.9	6.3	4.1	-88.23	12.5	-402.9	403.2	394.2	8.98	44.874	
3,700.0	3,700.0	3,992.5	3,988.3	6.4	4.1	-88.02	14.0	-405.1	405.4	396.4	9.05	44.785	
3,800.0	3,800.0	4,094.6	4,090.4	6.5	4.1	-87.81	15.6	-407.2	407.5	398.4	9.13	44.661	
3,900.0	3,900.0	4,196.1	4,191.8	6.6	4.2	-87.65	16.8	-408.8	409.2	400.0	9.20	44.474	
4,000.0	4,000.0	4,296.0	4,291.7	6.7	4.2	-87.53	17.7	-410.2	410.7	401.4	9.28	44.253	
4,100.0	4,100.0	4,400.7	4,396.4	6.8	4.3	-87.41	18.6	-411.2	411.6	402.2	9.36	43.951	
4,200.0	4,200.0	4,501.4	4,497.1	6.9	4.3	-87.39	18.8	-411.4	411.8	402.4	9.45	43.583	
4,300.0	4,300.0	4,597.9	4,593.6	7.0	4.4	-87.35	19.1	-411.8	412.3	402.8	9.54	43.233	
4,400.0	4,400.0	4,693.6	4,689.3	7.1	4.4	-87.24	19.9	-413.5	414.1	404.4	9.63	43.013	
4,500.0	4,500.0	4,794.7	4,790.4	7.2	4.5	-87.09	21.1	-415.4	416.0	406.3	9.72	42.790	
4,600.0	4,600.0	4,893.2	4,888.8	7.3	4.5	-86.95	22.2	-417.3	418.0	408.2	9.82	42.568	
4,700.0	4,700.0	4,994.2	4,989.8	7.4	4.6	-86.82	23.3	-419.2	419.9	410.0	9.92	42.328	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #201H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8667-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
4,800.0	4,800.0	5,093.2	5,088.8	7.6	4.7	-86.70	24.3	-421.1	421.9	411.9	10.03	42.084	
4,900.0	4,900.0	5,194.2	5,189.8	7.7	4.7	-86.58	25.3	-423.2	424.0	413.9	10.13	41.841	
5,000.0	5,000.0	5,292.7	5,288.2	7.8	4.8	-86.48	26.2	-425.2	426.1	415.9	10.24	41.596	
5,100.0	5,100.0	5,393.8	5,389.3	7.9	4.9	-86.40	26.9	-427.4	428.3	418.0	10.36	41.349	
5,200.0	5,200.0	5,492.9	5,488.4	8.0	4.9	-86.30	27.7	-429.4	430.4	419.9	10.48	41.088	
5,300.0	5,300.0	5,592.9	5,588.4	8.1	5.0	-86.22	28.5	-431.6	432.6	422.0	10.60	40.833	
5,400.0	5,400.0	5,695.1	5,690.5	8.2	5.1	-86.14	29.3	-433.6	434.6	423.9	10.72	40.550	
5,500.0	5,500.0	5,794.4	5,789.8	8.3	5.2	-86.10	29.7	-435.3	436.4	425.5	10.84	40.241	
5,600.0	5,600.0	5,895.6	5,891.0	8.4	5.3	140.81	30.2	-436.8	439.3	428.3	10.97	40.045	
5,664.4	5,664.3	5,959.0	5,954.5	8.4	5.3	141.04	30.5	-437.8	442.6	431.5	11.05	40.048	
5,700.0	5,699.9	5,994.9	5,990.3	8.4	5.3	141.21	30.6	-438.4	444.8	433.7	11.10	40.078	
5,800.0	5,799.7	6,095.7	6,091.1	8.3	5.4	141.71	31.0	-439.9	450.7	439.5	11.23	40.140	
5,900.0	5,899.5	6,194.2	6,189.6	8.3	5.5	142.19	31.5	-441.4	456.8	445.5	11.36	40.205	
6,000.0	5,999.4	6,293.6	6,289.0	8.3	5.6	142.66	32.0	-443.0	463.0	451.5	11.50	40.270	
6,100.0	6,099.2	6,393.4	6,388.7	8.3	5.7	143.10	32.3	-444.8	469.4	457.8	11.64	40.337	
6,200.0	6,199.0	6,492.4	6,487.7	8.3	5.8	143.50	32.4	-446.6	475.9	464.1	11.78	40.401	
6,300.0	6,298.9	6,590.4	6,585.7	8.3	5.9	143.92	32.8	-448.5	482.5	470.6	11.92	40.472	
6,400.0	6,398.7	6,690.3	6,685.5	8.3	6.0	144.33	33.2	-450.8	489.4	477.3	12.07	40.555	
6,500.0	6,498.5	6,793.7	6,789.0	8.3	6.1	144.80	34.1	-452.6	496.0	483.8	12.21	40.608	
6,600.0	6,598.4	6,893.9	6,889.1	8.3	6.2	145.33	35.5	-453.8	502.1	489.7	12.35	40.640	
6,700.0	6,698.2	6,996.0	6,991.3	8.3	6.2	145.86	37.1	-454.7	507.9	495.4	12.49	40.664	
6,800.0	6,798.0	7,095.3	7,090.5	8.3	6.3	146.35	38.5	-455.6	513.8	501.2	12.63	40.679	
6,900.0	6,897.9	7,195.5	7,190.7	8.3	6.4	146.85	39.9	-456.3	519.5	506.7	12.77	40.689	
7,000.0	6,997.7	7,295.4	7,290.6	8.3	6.5	147.32	41.2	-456.9	525.2	512.3	12.91	40.691	
7,100.0	7,097.5	7,390.1	7,385.3	8.3	6.6	147.73	42.3	-458.0	531.3	518.3	13.06	40.696	
7,200.0	7,197.4	7,489.0	7,484.2	8.3	6.7	148.14	43.4	-459.8	538.2	525.0	13.21	40.727	
7,300.0	7,297.2	7,590.9	7,586.0	8.3	6.8	148.53	44.4	-461.5	545.0	531.6	13.38	40.744	
7,400.0	7,397.1	7,690.5	7,685.7	8.3	6.9	148.86	44.9	-463.2	551.6	538.0	13.54	40.739	
7,500.0	7,496.9	7,791.5	7,786.6	8.3	7.0	149.13	45.0	-464.8	558.1	544.4	13.71	40.719	
7,600.0	7,596.7	7,889.9	7,885.0	8.4	7.1	149.39	44.9	-466.4	564.6	550.7	13.87	40.697	
7,700.0	7,696.6	7,989.8	7,984.8	8.4	7.2	149.73	45.8	-467.8	571.1	557.1	14.04	40.684	
7,800.0	7,796.4	8,089.1	8,084.1	8.4	7.3	150.11	47.0	-469.3	577.8	563.6	14.20	40.678	
7,900.0	7,896.2	8,188.7	8,183.7	8.4	7.4	150.45	48.0	-470.8	584.4	570.1	14.37	40.657	
8,000.0	7,996.1	8,287.2	8,282.3	8.5	7.6	150.76	48.9	-472.4	591.3	576.7	14.55	40.640	
8,100.0	8,095.9	8,387.3	8,382.3	8.5	7.7	151.05	49.5	-474.2	598.2	583.5	14.73	40.621	
8,200.0	8,195.7	8,487.9	8,482.9	8.5	7.8	151.31	50.0	-476.0	605.1	590.2	14.91	40.594	
8,300.0	8,295.6	8,589.2	8,584.1	8.6	7.9	151.55	50.2	-477.6	611.6	596.6	15.08	40.547	
8,400.0	8,395.4	8,690.6	8,685.6	8.6	7.9	151.73	49.7	-479.1	618.0	602.8	15.21	40.638	
8,500.0	8,495.2	8,783.4	8,778.4	8.6	8.0	151.89	49.2	-480.6	624.5	609.2	15.31	40.780	
8,600.0	8,595.1	8,843.9	8,838.7	8.7	8.0	152.29	52.6	-482.6	634.5	618.9	15.58	40.718	
8,700.0	8,694.9	8,904.0	8,897.6	8.7	8.6	153.28	63.7	-486.8	651.5	635.3	16.15	40.343	
8,800.0	8,794.8	8,951.0	8,942.7	8.8	8.9	154.31	76.0	-491.4	674.5	657.6	16.99	39.710	
8,900.0	8,894.6	9,003.8	8,992.1	8.8	9.2	155.63	93.1	-498.5	704.2	686.3	17.92	39.295	
9,000.0	8,994.4	9,044.0	9,028.2	8.9	9.3	156.81	109.3	-505.7	741.2	722.1	19.10	38.810	
9,100.0	9,094.3	9,092.0	9,069.2	8.9	9.6	158.35	132.0	-515.8	785.0	764.7	20.34	38.588 SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 14

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #202H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8648-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	298.5	298.5	4.2	3.0	-93.67	-23.1	-359.9	360.6				
100.0	100.0	397.4	397.4	4.2	3.0	-93.67	-23.1	-359.8	360.5	353.3	7.25	49.705	
200.0	200.0	496.1	496.1	4.2	3.0	-93.77	-23.7	-360.2	360.9	353.7	7.26	49.722	
300.0	300.0	595.2	595.2	4.3	3.0	-93.96	-25.0	-360.7	361.6	354.4	7.27	49.751	
400.0	400.0	694.9	694.9	4.3	3.0	-94.24	-26.8	-361.5	362.5	355.2	7.28	49.783	
500.0	500.0	795.7	795.6	4.3	3.1	-94.59	-29.1	-362.2	363.3	356.0	7.30	49.778	
600.0	600.0	895.6	895.5	4.3	3.1	-95.01	-31.8	-362.6	364.0	356.7	7.32	49.743	
700.0	700.0	996.2	996.0	4.3	3.1	-95.57	-35.4	-363.1	364.8	357.5	7.34	49.699	
800.0	800.0	1,096.0	1,095.8	4.4	3.1	-96.13	-39.1	-363.5	365.6	358.3	7.37	49.635	
900.0	900.0	1,199.5	1,199.2	4.4	3.2	-96.41	-40.8	-363.4	365.6	358.3	7.39	49.458	
929.6	929.6	1,228.2	1,227.9	4.4	3.2	-96.36	-40.5	-363.4	365.6	358.2	7.40	49.404	
1,000.0	1,000.0	1,298.1	1,297.8	4.4	3.2	-96.11	-38.9	-363.6	365.7	358.3	7.42	49.278	
1,100.0	1,100.0	1,397.8	1,397.5	4.5	3.2	-95.74	-36.6	-364.0	365.9	358.4	7.45	49.092	
1,200.0	1,200.0	1,497.8	1,497.4	4.5	3.2	-95.35	-34.2	-364.5	366.1	358.6	7.49	48.901	
1,300.0	1,300.0	1,597.5	1,597.1	4.5	3.2	-94.96	-31.7	-365.0	366.4	358.9	7.52	48.703	
1,400.0	1,400.0	1,697.3	1,696.9	4.6	3.2	-94.58	-29.3	-365.6	366.8	359.2	7.56	48.500	
1,500.0	1,500.0	1,804.5	1,804.0	4.6	3.2	-94.16	-26.6	-365.4	366.4	358.8	7.60	48.182	
1,600.0	1,600.0	1,916.8	1,916.3	4.7	3.3	-93.84	-24.3	-361.7	363.0	355.3	7.64	47.508	
1,700.0	1,700.0	2,016.6	2,016.0	4.8	3.3	-93.86	-24.1	-356.6	357.8	350.1	7.69	46.558	
1,800.0	1,800.0	2,108.6	2,107.9	4.8	3.3	-94.13	-25.5	-353.2	354.3	346.6	7.74	45.790	
1,900.0	1,900.0	2,208.3	2,207.5	4.9	3.4	-94.52	-27.7	-350.4	351.6	343.8	7.79	45.128	
2,000.0	2,000.0	2,308.3	2,307.4	5.0	3.4	-94.99	-30.3	-347.6	349.1	341.2	7.85	44.464	
2,100.0	2,100.0	2,408.8	2,407.9	5.0	3.4	-95.48	-33.1	-344.6	346.3	338.4	7.91	43.772	
2,200.0	2,200.0	2,506.6	2,505.6	5.1	3.5	-96.00	-35.9	-341.8	343.8	335.8	7.98	43.099	
2,300.0	2,300.0	2,602.2	2,601.1	5.2	3.5	-96.50	-38.8	-340.3	342.5	334.5	8.04	42.601	
2,400.0	2,400.0	2,700.0	2,698.9	5.2	3.6	-96.99	-41.6	-339.5	342.0	333.9	8.10	42.196	
2,414.6	2,414.6	2,714.0	2,712.9	5.3	3.6	-97.05	-42.0	-339.4	342.0	333.9	8.11	42.146	
2,500.0	2,500.0	2,796.8	2,795.7	5.3	3.6	-97.29	-43.5	-339.6	342.4	334.2	8.16	41.934	
2,600.0	2,600.0	2,899.2	2,898.0	5.4	3.7	-97.23	-43.2	-340.4	343.1	334.9	8.22	41.728	
2,700.0	2,700.0	3,001.4	3,000.3	5.5	3.7	-97.23	-43.1	-340.0	342.7	334.4	8.30	41.287	
2,800.0	2,800.0	3,100.4	3,099.3	5.6	3.8	-97.26	-43.3	-339.4	342.2	333.8	8.38	40.824	
2,900.0	2,900.0	3,201.2	3,200.0	5.7	3.8	-97.31	-43.5	-338.9	341.7	333.2	8.46	40.364	
3,000.0	3,000.0	3,303.0	3,301.8	5.7	3.9	-97.37	-43.8	-338.2	341.1	332.5	8.55	39.870	
3,100.0	3,100.0	3,402.3	3,401.1	5.8	4.0	-97.42	-44.0	-337.6	340.5	331.8	8.65	39.379	
3,200.0	3,200.0	3,502.1	3,500.9	5.9	4.0	-97.48	-44.2	-336.8	339.7	331.0	8.74	38.857	
3,300.0	3,300.0	3,603.8	3,602.6	6.0	4.1	-97.57	-44.6	-335.7	338.7	329.8	8.84	38.293	
3,400.0	3,400.0	3,705.6	3,704.4	6.1	4.2	-97.67	-45.0	-334.0	337.1	328.2	8.95	37.663	
3,500.0	3,500.0	3,805.8	3,804.6	6.2	4.3	-97.81	-45.5	-331.8	335.0	325.9	9.06	36.979	
3,600.0	3,600.0	3,905.5	3,904.3	6.3	4.3	-97.96	-46.2	-330.0	333.3	324.1	9.17	36.347	
3,700.0	3,700.0	4,005.9	4,004.7	6.4	4.4	-98.16	-47.1	-328.1	331.5	322.2	9.28	35.724	
3,800.0	3,800.0	4,108.9	4,107.6	6.5	4.5	-98.47	-48.5	-325.5	329.3	319.9	9.39	35.046	
3,900.0	3,900.0	4,211.9	4,210.5	6.6	4.6	-98.95	-50.7	-321.7	325.9	316.4	9.51	34.258	
4,000.0	4,000.0	4,308.7	4,307.2	6.7	4.7	-99.46	-53.0	-317.8	322.3	312.7	9.63	33.489	
4,100.0	4,100.0	4,405.0	4,403.5	6.8	4.8	-100.04	-55.9	-315.6	320.5	310.8	9.73	32.945	
4,200.0	4,200.0	4,506.6	4,504.9	6.9	4.9	-100.80	-59.7	-313.0	318.7	308.8	9.84	32.393	
4,300.0	4,300.0	4,606.5	4,604.7	7.0	5.0	-101.56	-63.5	-310.1	316.6	306.7	9.95	31.825	
4,400.0	4,400.0	4,707.0	4,705.2	7.1	5.1	-101.64	-63.5	-308.0	314.6	304.5	10.08	31.215	
4,500.0	4,500.0	4,805.6	4,803.7	7.2	5.1	-101.58	-62.7	-306.1	312.5	302.3	10.21	30.612	
4,600.0	4,600.0	4,906.0	4,904.1	7.3	5.2	-101.52	-62.0	-304.4	310.7	300.4	10.35	30.033	
4,700.0	4,700.0	5,005.6	5,003.7	7.4	5.3	-101.45	-61.3	-302.7	308.9	298.4	10.48	29.467	
4,800.0	4,800.0	5,105.6	5,103.7	7.6	5.4	-101.77	-62.7	-300.7	307.2	296.6	10.61	28.948	
4,900.0	4,900.0	5,205.6	5,203.6	7.7	5.5	-102.39	-65.5	-298.3	305.5	294.8	10.73	28.463	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #202H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8648-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
5,000.0	5,000.0	5,307.0	5,305.0	7.8	5.6	-103.06	-68.6	-295.7	303.6	292.7	10.86	27.960	
5,100.0	5,100.0	5,412.3	5,410.0	7.9	5.7	-104.11	-73.2	-291.1	300.4	289.4	11.00	27.318	
5,200.0	5,200.0	5,512.7	5,510.1	8.0	5.8	-105.39	-78.6	-285.5	296.4	285.3	11.13	26.627	
5,300.0	5,300.0	5,613.0	5,610.1	8.1	5.9	-106.76	-84.2	-279.7	292.4	281.1	11.27	25.942	
5,400.0	5,400.0	5,712.1	5,708.9	8.2	6.0	-108.20	-90.0	-273.9	288.5	277.1	11.41	25.280	
5,500.0	5,500.0	5,811.6	5,808.1	8.3	6.1	-109.61	-95.6	-268.4	285.1	273.5	11.56	24.664	
5,600.0	5,600.0	5,911.8	5,908.0	8.4	6.2	116.04	-101.2	-262.7	282.5	270.7	11.71	24.127	
5,664.4	5,664.3	5,976.1	5,972.0	8.4	6.3	115.63	-104.9	-258.9	281.5	269.7	11.80	23.861	
5,700.0	5,699.9	6,011.9	6,007.7	8.4	6.3	115.47	-106.9	-256.8	281.2	269.3	11.85	23.731	
5,800.0	5,799.7	6,113.6	6,109.0	8.3	6.4	115.10	-112.1	-250.7	279.9	267.9	11.99	23.334	
5,900.0	5,899.5	6,214.0	6,209.2	8.3	6.6	114.84	-116.6	-244.5	278.3	266.1	12.14	22.924	
5,970.9	5,970.3	6,280.2	6,275.2	8.3	6.6	114.72	-119.5	-240.9	277.5	265.3	12.23	22.694	
6,000.0	5,999.4	6,306.5	6,301.5	8.3	6.7	114.72	-120.5	-239.9	277.7	265.4	12.26	22.643	
6,100.0	6,099.2	6,405.3	6,400.2	8.3	6.8	114.92	-124.1	-237.4	279.0	266.6	12.39	22.529	
6,200.0	6,199.0	6,511.9	6,506.6	8.3	6.9	115.07	-127.7	-233.5	279.3	266.7	12.53	22.287	
6,300.0	6,298.9	6,612.5	6,607.0	8.3	7.0	115.17	-130.8	-228.4	278.2	265.5	12.68	21.945	
6,400.0	6,398.7	6,712.0	6,706.4	8.3	7.1	115.29	-133.7	-223.6	277.2	264.3	12.82	21.616	
6,500.0	6,498.5	6,811.5	6,805.7	8.3	7.2	115.50	-136.4	-219.0	276.3	263.3	12.97	21.305	
6,600.0	6,598.4	6,910.3	6,904.5	8.3	7.3	115.68	-139.3	-214.7	275.8	262.7	13.11	21.035	
6,700.0	6,698.2	7,010.7	7,004.7	8.3	7.4	115.82	-142.5	-210.3	275.4	262.1	13.26	20.767	
6,800.0	6,798.0	7,112.3	7,106.1	8.3	7.6	115.91	-145.8	-205.7	274.8	261.4	13.41	20.486	
6,900.0	6,897.9	7,217.3	7,210.9	8.3	7.7	115.77	-149.7	-198.9	272.5	259.0	13.59	20.062	
7,000.0	6,997.7	7,317.5	7,310.6	8.3	7.8	115.31	-154.6	-191.1	269.5	255.8	13.74	19.617	
7,100.0	7,097.5	7,416.2	7,408.9	8.3	7.9	114.79	-159.7	-183.5	266.7	252.8	13.89	19.204	
7,200.0	7,197.4	7,515.8	7,508.3	8.3	8.0	114.72	-163.0	-177.0	264.3	250.2	14.04	18.822	
7,300.0	7,297.2	7,613.6	7,605.8	8.3	8.2	114.65	-166.4	-171.1	262.4	248.2	14.19	18.492	
7,400.0	7,397.1	7,711.9	7,703.8	8.3	8.3	114.45	-170.8	-165.6	261.2	246.9	14.33	18.225	
7,500.0	7,496.9	7,810.9	7,802.6	8.3	8.4	114.16	-175.6	-160.3	260.6	246.1	14.48	18.000	
7,600.0	7,596.7	7,911.0	7,902.4	8.4	8.5	113.83	-180.7	-155.1	260.0	245.4	14.62	17.783	
7,700.0	7,696.6	8,011.2	8,002.4	8.4	8.6	113.73	-184.8	-150.1	259.4	244.7	14.77	17.561	
7,740.3	7,736.8	8,050.0	8,041.2	8.4	8.7	113.86	-185.7	-148.7	259.3	244.5	14.83	17.481	
7,800.0	7,796.4	8,104.9	8,096.1	8.4	8.7	114.34	-186.1	-147.8	260.0	245.0	14.93	17.410	
7,900.0	7,896.2	8,204.5	8,195.6	8.4	8.8	115.52	-185.8	-147.6	262.1	247.0	15.12	17.337	
8,000.0	7,996.1	8,304.0	8,295.2	8.5	8.9	116.65	-185.6	-147.1	264.1	248.8	15.31	17.253	
8,100.0	8,095.9	8,402.8	8,394.0	8.5	9.0	117.59	-186.3	-146.8	266.6	251.2	15.46	17.244	
8,200.0	8,195.7	8,502.5	8,493.6	8.5	9.1	118.44	-187.3	-146.8	269.7	254.1	15.59	17.298	
8,300.0	8,295.6	8,600.0	8,591.1	8.6	9.1	119.16	-189.0	-146.9	273.1	257.4	15.72	17.375	
8,400.0	8,395.4	8,700.6	8,691.7	8.6	9.2	119.91	-190.6	-147.4	276.8	261.0	15.82	17.497	
8,500.0	8,495.2	8,807.6	8,798.7	8.6	9.2	120.75	-191.8	-147.2	279.9	264.0	15.97	17.533	
8,600.0	8,595.1	8,914.6	8,903.2	8.7	9.4	124.97	-175.6	-140.1	274.8	257.5	17.26	15.921	
8,700.0	8,694.9	9,060.1	9,041.3	8.7	9.4	134.23	-135.5	-124.9	259.9	241.8	18.05	14.398	
8,790.1	8,784.9	9,121.7	9,094.5	8.8	9.8	141.48	-105.4	-117.5	252.6	235.0	17.61	14.340 CC, ES	
8,800.0	8,794.8	9,131.0	9,102.3	8.8	9.9	142.70	-100.3	-116.8	252.7	235.1	17.62	14.339 SF	
8,900.0	8,894.6	9,185.0	9,146.3	8.8	10.3	149.99	-69.1	-115.0	265.0	246.8	18.25	14.521	
9,000.0	8,994.4	9,242.2	9,189.6	8.9	10.6	157.90	-31.8	-115.5	296.4	276.4	19.96	14.848	
9,100.0	9,094.3	9,297.9	9,227.8	8.9	10.8	165.49	8.7	-115.8	343.2	321.0	22.18	15.473	
9,200.0	9,194.1	9,342.2	9,255.2	9.0	11.0	171.36	43.5	-114.2	401.3	376.8	24.55	16.350	
9,300.0	9,293.9	9,366.0	9,268.4	9.0	11.1	174.43	63.3	-112.7	469.6	442.7	26.92	17.442	
9,400.0	9,393.8	9,396.6	9,283.5	9.1	11.3	178.26	89.7	-110.3	545.1	516.4	28.73	18.971	
9,500.0	9,493.6	9,413.0	9,290.8	9.1	11.3	-179.77	104.4	-108.9	626.2	595.8	30.31	20.657	
9,600.0	9,593.4	9,431.3	9,298.2	9.2	11.4	-177.63	121.0	-107.1	711.1	679.5	31.57	22.526	
9,700.0	9,693.3	9,444.2	9,303.0	9.3	11.4	-176.17	132.9	-105.7	798.8	766.2	32.62	24.486	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #203H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8881-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	306.1	306.0	4.2	3.0	88.06	19.9	588.7	589.0				
100.0	100.0	405.7	405.7	4.2	3.0	87.92	21.4	588.4	588.8	581.5	7.25	81.167	
200.0	200.0	506.9	506.8	4.2	3.1	87.83	22.3	588.1	588.5	581.2	7.26	81.034	
300.0	300.0	608.2	608.2	4.3	3.1	87.78	22.7	587.6	588.0	580.7	7.28	80.810	
400.0	400.0	709.1	709.0	4.3	3.1	87.75	23.1	586.9	587.3	580.0	7.30	80.488	
500.0	500.0	807.8	807.7	4.3	3.1	87.72	23.3	586.3	586.8	579.4	7.32	80.113	
600.0	600.0	907.0	907.0	4.3	3.2	87.72	23.3	585.9	586.3	579.0	7.36	79.692	
700.0	700.0	1,006.8	1,006.7	4.3	3.2	87.75	23.1	585.5	586.0	578.6	7.40	79.240	
800.0	800.0	1,107.2	1,107.1	4.4	3.2	87.76	22.9	585.1	585.6	578.2	7.44	78.714	
900.0	900.0	1,206.8	1,206.7	4.4	3.2	87.77	22.8	584.8	585.2	577.7	7.49	78.126	
1,000.0	1,000.0	1,307.1	1,307.0	4.4	3.3	87.79	22.6	584.5	584.9	577.4	7.54	77.527	
1,100.0	1,100.0	1,407.8	1,407.7	4.5	3.3	87.82	22.2	584.0	584.5	576.9	7.60	76.901	
1,200.0	1,200.0	1,507.7	1,507.6	4.5	3.4	87.85	21.9	583.5	583.9	576.3	7.66	76.194	
1,300.0	1,300.0	1,607.1	1,607.0	4.5	3.4	87.88	21.6	583.2	583.6	575.8	7.73	75.526	
1,400.0	1,400.0	1,706.9	1,706.8	4.6	3.4	87.95	20.9	582.8	583.2	575.4	7.78	74.916	
1,500.0	1,500.0	1,807.4	1,807.4	4.6	3.5	88.02	20.2	582.4	582.7	574.9	7.84	74.285	
1,600.0	1,600.0	1,907.9	1,907.8	4.7	3.5	88.11	19.2	582.0	582.3	574.4	7.90	73.676	
1,700.0	1,700.0	2,008.7	2,008.6	4.8	3.6	88.23	18.0	581.5	581.8	573.8	7.96	73.057	
1,800.0	1,800.0	2,109.4	2,109.3	4.8	3.6	88.36	16.6	580.9	581.2	573.1	8.03	72.386	
1,900.0	1,900.0	2,210.2	2,210.1	4.9	3.7	88.54	14.8	580.1	580.3	572.3	8.09	71.695	
2,000.0	2,000.0	2,310.9	2,310.8	5.0	3.7	88.72	12.9	579.2	579.3	571.2	8.17	70.950	
2,100.0	2,100.0	2,410.5	2,410.3	5.0	3.8	88.92	10.9	578.3	578.4	570.2	8.24	70.235	
2,200.0	2,200.0	2,507.7	2,507.5	5.1	3.9	89.14	8.6	577.5	577.5	569.2	8.30	69.558	
2,240.9	2,240.9	2,545.9	2,545.7	5.1	3.9	89.23	7.7	577.4	577.4	569.1	8.33	69.357	
2,300.0	2,300.0	2,604.2	2,604.0	5.2	3.9	89.38	6.2	577.5	577.5	569.1	8.36	69.104	
2,400.0	2,400.0	2,703.4	2,703.1	5.2	4.0	89.66	3.4	577.7	577.7	569.3	8.41	68.697	
2,500.0	2,500.0	2,803.3	2,803.0	5.3	4.0	89.98	0.2	577.9	577.9	569.5	8.46	68.289	
2,600.0	2,600.0	2,903.0	2,902.6	5.4	4.1	90.32	-3.2	578.3	578.3	569.8	8.52	67.899	
2,700.0	2,700.0	3,001.9	3,001.4	5.5	4.1	90.70	-7.1	578.7	578.8	570.2	8.57	67.522	
2,800.0	2,800.0	3,102.2	3,101.7	5.6	4.2	91.07	-10.8	579.3	579.4	570.8	8.63	67.164	
2,900.0	2,900.0	3,200.9	3,200.4	5.7	4.3	91.33	-13.4	579.9	580.1	571.4	8.68	66.816	
3,000.0	3,000.0	3,300.1	3,299.5	5.7	4.3	91.59	-16.1	580.6	580.8	572.1	8.74	66.474	
3,100.0	3,100.0	3,401.1	3,400.5	5.8	4.4	91.87	-19.0	581.3	581.6	572.8	8.80	66.122	
3,200.0	3,200.0	3,501.5	3,500.8	5.9	4.5	92.15	-21.9	581.9	582.3	573.4	8.86	65.750	
3,300.0	3,300.0	3,602.4	3,601.7	6.0	4.5	92.32	-23.6	582.4	582.9	574.0	8.92	65.384	
3,400.0	3,400.0	3,700.3	3,699.6	6.1	4.6	92.36	-24.0	583.1	583.6	574.7	8.96	65.133	
3,500.0	3,500.0	3,801.4	3,800.7	6.2	4.6	92.38	-24.2	584.0	584.5	575.5	9.01	64.895	
3,600.0	3,600.0	3,912.1	3,911.3	6.3	4.7	92.42	-24.7	583.6	584.1	575.0	9.10	64.163	
3,700.0	3,700.0	4,011.5	4,010.8	6.4	4.8	92.46	-25.1	582.5	583.1	573.9	9.21	63.290	
3,800.0	3,800.0	4,109.1	4,108.4	6.5	4.8	92.52	-25.6	581.6	582.2	572.9	9.32	62.467	
3,870.4	3,870.4	4,175.9	4,175.2	6.6	4.9	92.59	-26.3	581.4	582.0	572.6	9.38	62.029	
3,900.0	3,900.0	4,204.1	4,203.4	6.6	4.9	92.62	-26.6	581.4	582.0	572.6	9.41	61.883	
4,000.0	4,000.0	4,301.3	4,300.5	6.7	5.0	92.78	-28.2	581.8	582.5	573.0	9.48	61.459	
4,100.0	4,100.0	4,396.4	4,395.6	6.8	5.1	92.96	-30.2	582.8	583.7	574.1	9.54	61.151	
4,200.0	4,200.0	4,490.1	4,489.2	6.9	5.1	93.24	-33.1	584.6	585.8	576.2	9.61	60.948	
4,300.0	4,300.0	4,593.7	4,592.8	7.0	5.2	93.61	-37.1	587.2	588.5	578.8	9.68	60.780	
4,400.0	4,400.0	4,695.6	4,694.6	7.1	5.3	93.89	-40.0	588.7	590.2	580.4	9.76	60.487	
4,500.0	4,500.0	4,807.8	4,806.7	7.2	5.4	94.09	-42.2	589.5	591.0	581.2	9.85	60.025	
4,600.0	4,600.0	4,908.3	4,907.3	7.3	5.5	94.16	-42.8	589.1	590.6	580.7	9.95	59.352	
4,700.0	4,700.0	5,008.5	5,007.5	7.4	5.6	94.21	-43.3	588.6	590.2	580.1	10.06	58.658	
4,800.0	4,800.0	5,108.1	5,107.1	7.6	5.7	94.26	-43.8	588.1	589.8	579.6	10.17	57.977	
4,900.0	4,900.0	5,208.2	5,207.2	7.7	5.8	94.32	-44.4	587.7	589.4	579.1	10.28	57.315	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 18

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #203H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8881-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,000.0	5,000.0	5,309.0	5,308.0	7.8	5.9	94.38	-44.9	587.1	588.9	578.5	10.40	56.635	
5,100.0	5,100.0	5,409.1	5,408.0	7.9	6.0	94.42	-45.4	586.6	588.4	577.9	10.52	55.951	
5,200.0	5,200.0	5,509.4	5,508.3	8.0	6.1	94.47	-45.8	586.0	587.8	577.2	10.64	55.252	
5,300.0	5,300.0	5,608.7	5,607.7	8.1	6.2	94.51	-46.1	585.4	587.3	576.5	10.76	54.565	
5,400.0	5,400.0	5,708.8	5,707.8	8.2	6.3	94.55	-46.5	584.9	586.8	575.9	10.89	53.895	
5,500.0	5,500.0	5,808.6	5,807.6	8.3	6.5	94.59	-46.9	584.4	586.3	575.3	11.01	53.243	
5,600.0	5,600.0	5,909.2	5,908.1	8.4	6.6	-38.75	-47.3	583.8	584.4	573.2	11.14	52.463	
5,664.4	5,664.3	5,973.4	5,972.3	8.4	6.6	-38.94	-47.6	583.4	581.7	570.5	11.22	51.834	
5,700.0	5,699.9	6,009.1	6,008.0	8.4	6.7	-39.06	-47.7	583.2	579.9	568.6	11.27	51.453	
5,800.0	5,799.7	6,108.5	6,107.5	8.3	6.8	-39.39	-47.9	582.6	574.8	563.4	11.41	50.386	
5,900.0	5,899.5	6,208.2	6,207.2	8.3	6.9	-39.72	-48.1	582.0	569.9	558.3	11.55	49.336	
6,000.0	5,999.4	6,307.9	6,306.8	8.3	7.0	-40.06	-48.5	581.5	565.0	553.3	11.70	48.307	
6,100.0	6,099.2	6,407.9	6,406.8	8.3	7.1	-40.41	-48.7	581.0	560.1	548.3	11.85	47.274	
6,200.0	6,199.0	6,509.2	6,508.1	8.3	7.2	-40.74	-49.3	580.3	555.1	543.1	12.00	46.257	
6,300.0	6,298.9	6,609.5	6,608.4	8.3	7.3	-41.04	-50.0	579.4	549.9	537.8	12.15	45.247	
6,400.0	6,398.7	6,710.7	6,709.6	8.3	7.4	-41.34	-51.0	578.4	544.6	532.3	12.31	44.235	
6,500.0	6,498.5	6,810.2	6,809.1	8.3	7.5	-41.64	-51.9	577.3	539.2	526.7	12.47	43.245	
6,600.0	6,598.4	6,910.1	6,909.0	8.3	7.7	-41.92	-53.1	576.1	533.8	521.2	12.63	42.277	
6,700.0	6,698.2	7,010.5	7,009.3	8.3	7.8	-42.20	-54.3	575.0	528.5	515.7	12.79	41.318	
6,800.0	6,798.0	7,111.6	7,110.4	8.3	7.9	-42.51	-55.4	573.6	522.8	509.8	12.96	40.333	
6,900.0	6,897.9	7,212.8	7,211.6	8.3	8.0	-42.84	-56.3	571.8	516.9	503.8	13.14	39.324	
7,000.0	6,997.7	7,312.7	7,311.5	8.3	8.1	-43.19	-57.1	570.0	510.9	497.6	13.33	38.322	
7,100.0	7,097.5	7,412.3	7,411.1	8.3	8.2	-43.54	-57.8	568.4	505.1	491.5	13.52	37.355	
7,200.0	7,197.4	7,512.3	7,511.1	8.3	8.3	-43.92	-58.6	566.6	499.2	485.4	13.72	36.394	
7,300.0	7,297.2	7,612.3	7,611.0	8.3	8.5	-44.28	-59.5	564.9	493.3	479.4	13.91	35.462	
7,400.0	7,397.1	7,714.1	7,712.8	8.3	8.6	-44.63	-60.5	562.8	487.1	473.0	14.11	34.519	
7,500.0	7,496.9	7,815.3	7,814.0	8.3	8.7	-45.02	-61.5	560.3	480.6	466.3	14.32	33.562	
7,600.0	7,596.7	7,914.8	7,913.5	8.4	8.8	-45.40	-62.4	557.7	473.9	459.3	14.52	32.624	
7,700.0	7,696.6	8,014.0	8,012.6	8.4	8.9	-45.76	-63.6	555.3	467.4	452.6	14.73	31.732	
7,800.0	7,796.4	8,112.1	8,110.7	8.4	9.0	-46.12	-64.9	553.1	461.2	446.2	14.93	30.891	
7,900.0	7,896.2	8,211.8	8,210.4	8.4	9.1	-46.48	-66.2	551.1	455.1	440.0	15.13	30.070	
8,000.0	7,996.1	8,310.9	8,309.5	8.5	9.3	-46.80	-67.9	549.2	449.1	433.8	15.33	29.295	
8,100.0	8,095.9	8,410.1	8,408.6	8.5	9.4	-47.00	-70.6	547.6	443.4	427.9	15.51	28.589	
8,200.0	8,195.7	8,509.0	8,507.4	8.5	9.5	-47.18	-73.5	546.1	437.8	422.1	15.68	27.916	
8,300.0	8,295.6	8,608.7	8,607.0	8.6	9.6	-47.35	-76.6	544.7	432.3	416.5	15.86	27.267	
8,400.0	8,395.4	8,708.4	8,706.7	8.6	9.7	-47.51	-79.7	543.4	426.9	410.9	16.03	26.637	
8,500.0	8,495.2	8,808.0	8,806.3	8.6	9.9	-47.69	-82.6	542.1	421.6	405.3	16.26	25.923	
8,600.0	8,595.1	8,906.0	8,904.2	8.7	10.2	-48.28	-82.6	541.1	416.6	400.0	16.63	25.057	
8,700.0	8,694.9	9,010.9	9,008.0	8.7	10.6	-50.85	-68.9	537.3	410.7	393.7	16.96	24.210	
8,778.4	8,773.1	9,068.7	9,063.9	8.8	10.8	-53.21	-54.7	535.3	408.2	390.9	17.31	23.585 CC, ES	
8,800.0	8,794.8	9,083.1	9,077.8	8.8	10.8	-53.83	-50.9	535.2	408.4	391.0	17.45	23.413	
8,900.0	8,894.6	9,158.1	9,148.8	8.8	11.1	-57.57	-26.6	536.4	414.3	396.0	18.27	22.678	
9,000.0	8,994.4	9,240.3	9,221.3	8.9	11.7	-63.13	11.8	535.7	426.5	407.0	19.50	21.871	
9,100.0	9,094.3	9,298.8	9,268.3	8.9	12.1	-67.92	46.5	533.1	447.6	426.4	21.19	21.118	
9,200.0	9,194.1	9,341.0	9,298.7	9.0	12.2	-71.69	75.5	530.7	481.2	458.0	23.22	20.721 SF	
9,300.0	9,293.9	9,372.0	9,318.3	9.0	12.3	-74.63	99.4	528.3	527.3	501.9	25.41	20.754	
9,400.0	9,393.8	9,392.6	9,329.8	9.1	12.3	-76.63	116.4	526.6	584.6	557.2	27.47	21.284	
9,500.0	9,493.6	9,404.0	9,335.6	9.1	12.4	-77.75	126.2	525.7	650.9	621.7	29.25	22.250	
9,600.0	9,593.4	9,435.0	9,349.8	9.2	12.4	-80.76	153.6	522.8	723.8	693.2	30.59	23.658	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #301H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 9129-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	295.9	295.9	4.2	3.0	-93.33	-24.5	-420.2	420.9				
100.0	100.0	393.7	393.7	4.2	3.0	-93.42	-25.2	-420.7	421.4	414.2	7.26	58.072	
200.0	200.0	490.2	490.2	4.2	3.0	-93.65	-26.9	-421.7	422.7	415.4	7.27	58.156	
300.0	300.0	590.1	590.0	4.3	3.1	-94.00	-29.6	-423.3	424.4	417.1	7.28	58.274	
400.0	400.0	691.5	691.4	4.3	3.1	-94.35	-32.3	-424.7	426.0	418.7	7.30	58.329	
500.0	500.0	795.4	795.2	4.3	3.1	-94.59	-34.2	-425.4	426.8	419.5	7.33	58.259	
600.0	600.0	894.1	894.0	4.3	3.2	-94.80	-35.8	-425.8	427.4	420.0	7.35	58.149	
700.0	700.0	991.9	991.7	4.3	3.2	-95.16	-38.5	-426.6	428.4	421.0	7.38	58.081	
800.0	800.0	1,091.2	1,090.9	4.4	3.3	-95.63	-42.1	-427.7	429.8	422.4	7.41	58.022	
900.0	900.0	1,192.0	1,191.6	4.4	3.3	-96.10	-45.8	-428.8	431.3	423.8	7.44	57.945	
1,000.0	1,000.0	1,298.0	1,297.6	4.4	3.4	-96.38	-48.0	-429.3	432.0	424.5	7.48	57.743	
1,100.0	1,100.0	1,406.3	1,406.0	4.5	3.4	-96.41	-48.1	-428.3	431.0	423.5	7.50	57.503	
1,200.0	1,200.0	1,508.3	1,507.9	4.5	3.4	-96.30	-47.0	-426.0	428.7	421.2	7.51	57.060	
1,300.0	1,300.0	1,608.2	1,607.7	4.5	3.4	-96.16	-45.7	-423.7	426.3	418.8	7.54	56.566	
1,400.0	1,400.0	1,706.0	1,705.5	4.6	3.4	-95.93	-43.8	-421.8	424.1	416.6	7.57	56.043	
1,500.0	1,500.0	1,806.2	1,805.6	4.6	3.4	-95.54	-40.8	-420.2	422.3	414.7	7.60	55.529	
1,600.0	1,600.0	1,906.1	1,905.5	4.7	3.4	-95.12	-37.5	-418.7	420.4	412.8	7.64	54.995	
1,700.0	1,700.0	2,006.3	2,005.6	4.8	3.4	-94.66	-34.0	-417.1	418.6	410.9	7.69	54.442	
1,800.0	1,800.0	2,105.4	2,104.7	4.8	3.4	-94.19	-30.4	-415.6	416.7	409.0	7.74	53.869	
1,900.0	1,900.0	2,199.2	2,198.4	4.9	3.4	-93.76	-27.3	-415.0	415.8	408.1	7.79	53.414	
1,910.5	1,910.5	2,208.6	2,207.8	4.9	3.4	-93.73	-27.0	-415.0	415.8	408.0	7.79	53.378 CC, ES	
2,000.0	2,000.0	2,291.9	2,291.0	5.0	3.4	-93.48	-25.3	-415.9	416.7	408.9	7.83	53.189	
2,100.0	2,100.0	2,388.8	2,387.9	5.0	3.4	-93.27	-23.8	-417.8	418.6	410.7	7.89	53.067	
2,200.0	2,200.0	2,481.9	2,480.9	5.1	3.5	-93.11	-22.9	-420.9	421.8	413.9	7.94	53.099	
2,300.0	2,300.0	2,581.2	2,580.2	5.2	3.5	-93.01	-22.4	-425.0	425.9	417.9	8.01	53.170	
2,400.0	2,400.0	2,680.0	2,678.9	5.2	3.5	-93.07	-23.0	-429.1	430.1	422.0	8.08	53.226	
2,500.0	2,500.0	2,779.2	2,778.0	5.3	3.6	-93.26	-24.7	-433.4	434.6	426.4	8.16	53.285	
2,600.0	2,600.0	2,881.5	2,880.2	5.4	3.7	-93.45	-26.4	-437.7	438.8	430.6	8.24	53.272	
2,700.0	2,700.0	2,984.4	2,983.0	5.5	3.7	-93.69	-28.4	-441.0	442.2	433.8	8.32	53.120	
2,800.0	2,800.0	3,084.9	3,083.4	5.6	3.8	-93.94	-30.5	-443.9	445.2	436.8	8.41	52.924	
2,900.0	2,900.0	3,183.2	3,181.7	5.7	3.9	-94.16	-32.5	-446.8	448.3	439.8	8.50	52.729	
3,000.0	3,000.0	3,283.1	3,281.5	5.7	3.9	-94.28	-33.7	-450.2	451.8	443.2	8.60	52.537	
3,100.0	3,100.0	3,386.7	3,385.0	5.8	4.0	-94.43	-35.1	-453.6	455.1	446.4	8.70	52.292	
3,200.0	3,200.0	3,489.5	3,487.9	5.9	4.1	-94.62	-36.8	-455.7	457.3	448.5	8.81	51.930	
3,300.0	3,300.0	3,593.1	3,591.4	6.0	4.2	-94.73	-37.8	-457.5	459.1	450.2	8.92	51.496	
3,400.0	3,400.0	3,693.0	3,691.3	6.1	4.2	-94.73	-38.0	-458.7	460.3	451.3	9.03	50.989	
3,500.0	3,500.0	3,791.8	3,790.1	6.2	4.3	-94.74	-38.1	-460.0	461.6	452.5	9.14	50.489	
3,600.0	3,600.0	3,892.5	3,890.7	6.3	4.4	-94.73	-38.2	-461.4	463.0	453.8	9.26	49.989	
3,700.0	3,700.0	3,993.3	3,991.6	6.4	4.5	-94.73	-38.3	-462.8	464.4	455.0	9.39	49.483	
3,800.0	3,800.0	4,095.3	4,093.5	6.5	4.6	-94.76	-38.6	-463.9	465.6	456.0	9.51	48.947	
3,900.0	3,900.0	4,194.6	4,192.9	6.6	4.7	-94.82	-39.2	-464.6	466.2	456.6	9.63	48.421	
4,000.0	4,000.0	4,290.5	4,288.7	6.7	4.8	-94.88	-39.8	-465.9	467.7	458.0	9.75	47.956	
4,100.0	4,100.0	4,392.1	4,390.3	6.8	4.9	-94.96	-40.6	-467.7	469.5	459.6	9.88	47.500	
4,200.0	4,200.0	4,494.9	4,493.1	6.9	4.9	-95.15	-42.2	-468.7	470.6	460.6	10.00	47.050	
4,300.0	4,300.0	4,594.8	4,593.0	7.0	5.0	-95.39	-44.3	-469.3	471.4	461.3	10.11	46.626	
4,400.0	4,400.0	4,693.8	4,692.0	7.1	5.1	-95.59	-46.1	-470.2	472.4	462.2	10.23	46.202	
4,500.0	4,500.0	4,793.8	4,791.9	7.2	5.2	-95.78	-47.7	-471.2	473.6	463.3	10.35	45.770	
4,600.0	4,600.0	4,891.9	4,890.1	7.3	5.3	-95.95	-49.2	-472.3	475.0	464.5	10.47	45.347	
4,700.0	4,700.0	4,983.9	4,982.0	7.4	5.4	-96.09	-50.6	-474.2	477.1	466.5	10.61	44.989	
4,800.0	4,800.0	5,070.2	5,068.2	7.6	5.5	-96.21	-52.0	-478.2	481.9	471.2	10.74	44.857	
4,900.0	4,900.0	5,166.8	5,164.6	7.7	5.6	-96.37	-54.1	-484.3	488.4	477.5	10.89	44.850 SF	
5,000.0	5,000.0	5,257.1	5,254.6	7.8	5.7	-96.54	-56.3	-490.9	495.9	484.9	11.04	44.923	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #301H - OWB - ACTUAL WELLPATH													Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 9129-MWD+IFR1+MS													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Warning								
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,100.0	5,100.0	5,356.7	5,353.8	7.9	5.8	-96.73	-58.9	-499.2	504.6	493.4	11.19	45.086		
5,200.0	5,200.0	5,456.2	5,453.0	8.0	5.9	-96.92	-61.6	-507.5	513.2	501.8	11.34	45.234		
5,300.0	5,300.0	5,555.6	5,552.0	8.1	6.0	-97.10	-64.3	-515.9	521.9	510.4	11.50	45.380		
5,400.0	5,400.0	5,656.1	5,652.1	8.2	6.1	-97.27	-66.9	-524.4	530.6	518.9	11.66	45.517		
5,500.0	5,500.0	5,759.0	5,754.6	8.3	6.2	-97.43	-69.5	-532.5	538.7	526.9	11.81	45.601		
5,600.0	5,600.0	5,857.0	5,852.3	8.4	6.3	129.15	-72.0	-540.1	547.8	535.9	11.97	45.753		
5,664.4	5,664.3	5,916.9	5,911.9	8.4	6.4	129.17	-73.5	-545.1	555.2	543.1	12.08	45.974		
5,700.0	5,699.9	5,950.6	5,945.5	8.4	6.4	129.27	-74.5	-548.1	559.8	547.6	12.13	46.134		
5,800.0	5,799.7	6,048.8	6,043.2	8.3	6.5	129.54	-77.3	-556.9	572.6	560.4	12.29	46.589		
5,900.0	5,899.5	6,146.8	6,140.8	8.3	6.6	129.80	-80.1	-565.8	585.7	573.2	12.45	47.039		
6,000.0	5,999.4	6,244.7	6,238.3	8.3	6.7	130.06	-82.8	-575.0	599.0	586.4	12.61	47.491		
6,100.0	6,099.2	6,345.0	6,338.0	8.3	6.8	130.33	-85.5	-584.5	612.4	599.6	12.77	47.940		
6,200.0	6,199.0	6,442.5	6,435.1	8.3	7.0	130.56	-88.2	-593.5	625.6	612.7	12.94	48.346		
6,300.0	6,298.9	6,541.3	6,533.4	8.3	7.1	130.81	-90.7	-603.0	639.2	626.1	13.11	48.770		
6,400.0	6,398.7	6,639.1	6,630.7	8.3	7.2	131.07	-93.0	-612.5	652.8	639.5	13.27	49.178		
6,500.0	6,498.5	6,737.3	6,728.4	8.3	7.3	131.34	-95.1	-622.3	666.6	653.2	13.44	49.590		
6,600.0	6,598.4	6,837.7	6,828.3	8.3	7.4	131.62	-97.1	-632.1	680.4	666.8	13.61	49.990		
6,700.0	6,698.2	6,935.0	6,925.1	8.3	7.5	131.89	-98.8	-641.7	694.2	680.4	13.78	50.366		
6,800.0	6,798.0	7,036.0	7,025.6	8.3	7.6	132.17	-100.6	-651.7	707.9	694.0	13.95	50.739		
6,900.0	6,897.9	7,128.9	7,118.1	8.3	7.7	132.38	-102.6	-660.9	721.8	707.7	14.13	51.069		
7,000.0	6,997.7	7,227.0	7,215.5	8.3	7.8	132.49	-106.1	-671.3	736.6	722.3	14.31	51.456		
7,100.0	7,097.5	7,325.1	7,313.0	8.3	8.0	132.57	-109.9	-681.6	751.2	736.7	14.50	51.815		
7,200.0	7,197.4	7,432.6	7,419.9	8.3	8.1	132.68	-113.9	-692.5	765.4	750.8	14.67	52.184		
7,300.0	7,297.2	7,537.8	7,524.6	8.3	8.2	132.78	-117.6	-702.3	778.8	764.0	14.84	52.468		
7,400.0	7,397.1	7,642.0	7,628.3	8.3	8.3	132.91	-120.7	-711.0	791.2	776.2	15.02	52.668		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 21

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #302H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8941-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	302.4	302.4	4.2	3.0	-93.40	-23.0	-387.8	388.5				
100.0	100.0	401.7	401.7	4.2	3.0	-93.34	-22.6	-386.6	387.2	380.0	7.27	53.245	
200.0	200.0	502.6	502.5	4.2	3.1	-93.33	-22.4	-385.3	385.9	378.7	7.30	52.905	
300.0	300.0	600.0	600.0	4.3	3.1	-93.39	-22.8	-384.1	384.8	377.5	7.32	52.552	
346.9	346.9	644.4	644.3	4.3	3.1	-93.44	-23.1	-383.9	384.6	377.3	7.33	52.465	CC, ES
400.0	400.0	692.9	692.8	4.3	3.1	-93.50	-23.5	-384.1	384.9	377.5	7.33	52.486	
500.0	500.0	790.6	790.5	4.3	3.1	-93.65	-24.6	-385.6	386.5	379.2	7.33	52.715	
600.0	600.0	890.0	889.9	4.3	3.1	-93.82	-25.9	-387.5	388.4	381.1	7.34	52.943	
700.0	700.0	987.8	987.7	4.3	3.1	-94.07	-27.7	-389.5	390.6	383.3	7.35	53.172	
800.0	800.0	1,086.9	1,086.7	4.4	3.1	-94.40	-30.2	-392.0	393.3	385.9	7.36	53.416	
900.0	900.0	1,185.2	1,184.9	4.4	3.1	-94.79	-33.1	-394.6	396.2	388.8	7.38	53.661	
1,000.0	1,000.0	1,288.4	1,288.1	4.4	3.1	-95.21	-36.2	-397.4	399.1	391.7	7.41	53.849	
1,100.0	1,100.0	1,408.2	1,407.8	4.5	3.2	-95.49	-38.2	-397.0	398.9	391.5	7.45	53.560	
1,200.0	1,200.0	1,512.1	1,511.6	4.5	3.2	-95.41	-37.3	-393.4	395.4	387.9	7.49	52.820	
1,300.0	1,300.0	1,600.0	1,599.5	4.5	3.2	-95.30	-36.3	-391.2	392.9	385.3	7.53	52.178	
1,323.3	1,323.3	1,621.2	1,620.7	4.6	3.2	-95.28	-36.1	-391.1	392.8	385.2	7.54	52.107	
1,400.0	1,400.0	1,694.9	1,694.4	4.6	3.2	-95.19	-35.5	-391.6	393.2	385.6	7.56	51.984	
1,500.0	1,500.0	1,795.5	1,795.1	4.6	3.3	-95.08	-34.8	-392.3	393.8	386.2	7.60	51.816	
1,600.0	1,600.0	1,894.7	1,894.2	4.7	3.3	-94.95	-34.0	-393.1	394.6	386.9	7.64	51.634	
1,700.0	1,700.0	1,996.4	1,995.9	4.8	3.3	-94.83	-33.2	-393.6	395.0	387.4	7.69	51.394	
1,800.0	1,800.0	2,091.1	2,090.5	4.8	3.3	-94.77	-32.9	-394.7	396.2	388.4	7.73	51.234	
1,900.0	1,900.0	2,190.0	2,189.4	4.9	3.4	-94.81	-33.4	-396.6	398.1	390.3	7.79	51.133	
2,000.0	2,000.0	2,289.1	2,288.5	5.0	3.4	-94.88	-34.0	-398.7	400.2	392.4	7.84	51.016	
2,100.0	2,100.0	2,388.8	2,388.3	5.0	3.4	-95.02	-35.2	-400.9	402.6	394.6	7.91	50.899	
2,200.0	2,200.0	2,493.1	2,492.5	5.1	3.5	-95.33	-37.5	-402.6	404.4	396.4	7.98	50.693	
2,300.0	2,300.0	2,595.4	2,594.8	5.2	3.5	-95.65	-39.9	-403.3	405.3	397.2	8.04	50.385	
2,400.0	2,400.0	2,695.6	2,694.9	5.2	3.6	-95.94	-42.0	-403.7	405.9	397.8	8.11	50.052	
2,500.0	2,500.0	2,794.2	2,793.5	5.3	3.6	-96.24	-44.2	-404.2	406.6	398.4	8.18	49.715	
2,600.0	2,600.0	2,892.4	2,891.7	5.4	3.7	-96.45	-45.8	-405.3	407.9	399.7	8.25	49.416	
2,700.0	2,700.0	2,994.6	2,993.8	5.5	3.8	-96.64	-47.3	-406.5	409.3	401.0	8.34	49.089	
2,800.0	2,800.0	3,097.2	3,096.5	5.6	3.8	-96.85	-48.9	-406.9	409.8	401.4	8.42	48.693	
2,900.0	2,900.0	3,196.7	3,196.0	5.7	3.9	-97.09	-50.6	-406.9	410.0	401.5	8.49	48.293	
3,000.0	3,000.0	3,298.0	3,297.2	5.7	4.0	-97.35	-52.5	-406.8	410.2	401.7	8.57	47.883	
3,100.0	3,100.0	3,396.8	3,396.0	5.8	4.0	-97.62	-54.4	-406.9	410.6	401.9	8.65	47.483	
3,200.0	3,200.0	3,496.5	3,495.6	5.9	4.1	-97.93	-56.7	-406.9	410.9	402.1	8.73	47.075	
3,300.0	3,300.0	3,596.7	3,595.9	6.0	4.2	-98.28	-59.2	-407.1	411.3	402.5	8.81	46.673	
3,400.0	3,400.0	3,699.2	3,698.3	6.1	4.2	-98.41	-60.2	-406.9	411.4	402.5	8.89	46.258	
3,500.0	3,500.0	3,800.0	3,799.1	6.2	4.2	-98.17	-58.4	-406.9	411.1	402.1	8.97	45.848	
3,524.2	3,524.2	3,822.4	3,821.6	6.2	4.2	-98.12	-58.1	-406.9	411.1	402.1	8.98	45.752	
3,600.0	3,600.0	3,895.6	3,894.7	6.3	4.3	-98.11	-58.1	-407.3	411.4	402.3	9.06	45.425	
3,700.0	3,700.0	3,994.8	3,993.9	6.4	4.4	-98.20	-58.8	-407.9	412.1	403.0	9.16	44.998	
3,800.0	3,800.0	4,095.6	4,094.7	6.5	4.5	-98.29	-59.6	-408.7	413.1	403.8	9.27	44.578	
3,900.0	3,900.0	4,197.1	4,196.2	6.6	4.5	-98.42	-60.5	-408.9	413.4	404.0	9.36	44.149	
4,000.0	4,000.0	4,297.3	4,296.4	6.7	4.6	-98.60	-61.8	-408.9	413.6	404.1	9.46	43.733	
4,100.0	4,100.0	4,400.1	4,399.1	6.8	4.7	-98.84	-63.5	-408.6	413.5	403.9	9.55	43.300	
4,200.0	4,200.0	4,499.4	4,498.5	6.9	4.8	-99.17	-65.9	-407.8	413.1	403.5	9.64	42.855	
4,275.3	4,275.3	4,573.7	4,572.7	7.0	4.9	-99.43	-67.7	-407.4	413.0	403.3	9.71	42.527	
4,300.0	4,300.0	4,597.5	4,596.5	7.0	4.9	-99.50	-68.2	-407.4	413.0	403.3	9.74	42.425	
4,400.0	4,400.0	4,697.3	4,696.3	7.1	5.0	-99.77	-70.1	-407.3	413.3	403.4	9.84	42.014	
4,500.0	4,500.0	4,797.9	4,796.9	7.2	5.1	-100.04	-72.1	-407.2	413.5	403.6	9.94	41.604	
4,600.0	4,600.0	4,897.2	4,896.2	7.3	5.2	-100.32	-74.1	-407.1	413.8	403.8	10.04	41.198	
4,700.0	4,700.0	4,997.0	4,995.9	7.4	5.2	-100.57	-76.0	-407.1	414.1	404.0	10.15	40.797	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #302H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 8941-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
4,800.0	4,800.0	5,090.2	5,089.1	7.6	5.3	-100.74	-77.3	-407.9	415.2	405.0	10.27	40.445	
4,900.0	4,900.0	5,189.5	5,188.4	7.7	5.4	-100.79	-78.1	-409.9	417.4	407.0	10.40	40.148	
5,000.0	5,000.0	5,303.1	5,301.9	7.8	5.5	-100.89	-78.9	-410.4	417.9	407.4	10.51	39.770	
5,100.0	5,100.0	5,401.9	5,400.7	7.9	5.6	-101.03	-79.7	-409.1	416.8	406.2	10.59	39.361	
5,123.0	5,123.0	5,421.5	5,420.4	7.9	5.6	-101.05	-79.9	-409.0	416.7	406.1	10.61	39.278	
5,200.0	5,200.0	5,487.9	5,486.7	8.0	5.6	-101.18	-80.9	-409.7	417.7	407.0	10.70	39.042	
5,300.0	5,300.0	5,585.2	5,584.0	8.1	5.7	-101.40	-83.1	-412.3	420.8	409.9	10.83	38.836	
5,400.0	5,400.0	5,698.5	5,697.3	8.2	5.8	-101.40	-83.4	-413.4	421.7	410.8	10.95	38.502	
5,494.8	5,494.8	5,793.4	5,792.2	8.3	5.8	-101.31	-82.7	-413.5	421.6	410.6	11.04	38.181	
5,500.0	5,500.0	5,798.3	5,797.1	8.3	5.8	-101.30	-82.6	-413.5	421.6	410.6	11.05	38.164	
5,600.0	5,600.0	5,899.6	5,898.4	8.4	5.8	125.72	-81.9	-413.4	422.5	411.4	11.14	37.927	
5,664.4	5,664.3	5,963.5	5,962.3	8.4	5.8	126.09	-81.4	-413.5	424.1	413.0	11.20	37.884	
5,700.0	5,699.9	5,998.5	5,997.2	8.4	5.8	126.34	-81.1	-413.5	425.3	414.1	11.23	37.885	
5,800.0	5,799.7	6,093.9	6,092.6	8.3	5.8	127.04	-80.4	-413.9	429.1	417.7	11.32	37.891	
5,900.0	5,899.5	6,187.3	6,186.1	8.3	5.9	127.70	-80.0	-415.8	434.4	423.0	11.44	37.964	
6,000.0	5,999.4	6,285.2	6,283.8	8.3	5.9	128.34	-79.9	-418.4	440.7	429.1	11.57	38.087	
6,100.0	6,099.2	6,378.1	6,376.8	8.3	6.0	128.91	-80.1	-421.8	447.8	436.1	11.70	38.265	
6,200.0	6,199.0	6,476.0	6,474.5	8.3	6.1	129.36	-81.5	-426.5	456.5	444.6	11.84	38.547	
6,300.0	6,298.9	6,580.8	6,579.2	8.3	6.2	129.80	-83.1	-430.6	464.1	452.2	11.98	38.754	
6,400.0	6,398.7	6,675.9	6,674.2	8.3	6.3	130.13	-85.1	-434.2	471.8	459.7	12.12	38.925	
6,500.0	6,498.5	6,779.8	6,778.0	8.3	6.4	130.37	-88.1	-438.3	479.8	467.5	12.26	39.126	
6,600.0	6,598.4	6,876.4	6,874.5	8.3	6.5	130.53	-91.4	-441.7	487.4	474.9	12.41	39.270	
6,700.0	6,698.2	6,988.2	6,986.1	8.3	6.6	130.50	-96.9	-445.0	494.6	482.1	12.55	39.407	
6,800.0	6,798.0	7,089.8	7,087.6	8.3	6.7	130.42	-102.2	-446.1	500.0	487.3	12.69	39.400	
6,900.0	6,897.9	7,189.7	7,187.3	8.3	6.8	130.32	-107.5	-447.2	505.4	492.6	12.83	39.391	
7,000.0	6,997.7	7,291.1	7,288.5	8.3	6.9	130.21	-113.1	-448.0	510.5	497.6	12.97	39.357	
7,100.0	7,097.5	7,391.0	7,388.2	8.3	7.0	130.08	-118.7	-448.7	515.5	502.4	13.11	39.312	
7,200.0	7,197.4	7,492.5	7,489.6	8.3	7.1	129.91	-124.8	-449.2	520.4	507.1	13.26	39.254	
7,300.0	7,297.2	7,597.6	7,594.7	8.3	7.2	130.02	-128.5	-449.0	524.3	510.9	13.39	39.169	
7,400.0	7,397.1	7,697.0	7,694.1	8.3	7.3	130.37	-129.6	-449.0	528.1	514.6	13.50	39.108	
7,500.0	7,496.9	7,798.0	7,795.0	8.3	7.3	130.86	-129.5	-448.9	531.7	518.1	13.60	39.103	
7,600.0	7,596.7	7,899.0	7,896.0	8.4	7.3	131.36	-129.1	-448.7	535.2	521.6	13.69	39.107	
7,700.0	7,696.6	7,999.5	7,996.5	8.4	7.3	131.87	-128.6	-448.2	538.6	524.8	13.78	39.098	
7,800.0	7,796.4	8,096.5	8,093.5	8.4	7.3	132.34	-128.3	-447.9	542.1	528.3	13.87	39.087	
7,900.0	7,896.2	8,195.2	8,192.2	8.4	7.4	132.76	-128.5	-448.1	546.2	532.2	14.01	38.985	
8,000.0	7,996.1	8,293.8	8,290.8	8.5	7.6	133.16	-128.9	-448.6	550.6	536.4	14.16	38.890	
8,100.0	8,095.9	8,391.6	8,388.6	8.5	7.7	133.53	-129.5	-449.3	555.3	541.0	14.31	38.811	
8,200.0	8,195.7	8,489.5	8,486.5	8.5	8.0	133.86	-130.3	-450.2	560.2	545.7	14.45	38.780	
8,300.0	8,295.6	8,587.7	8,584.7	8.6	9.0	134.24	-130.7	-451.4	565.5	550.9	14.59	38.755	
8,400.0	8,395.4	8,685.9	8,682.9	8.6	10.1	134.66	-130.6	-453.0	571.1	556.4	14.76	38.699	
8,500.0	8,495.2	8,784.1	8,781.0	8.6	11.1	135.12	-130.0	-454.9	577.0	562.1	14.92	38.672	
8,600.0	8,595.1	8,882.1	8,879.0	8.7	12.3	135.63	-128.9	-457.0	583.3	568.2	15.08	38.672	
8,700.0	8,694.9	8,979.5	8,976.3	8.7	13.4	136.25	-126.5	-459.4	589.9	574.5	15.33	38.480	
8,800.0	8,794.8	9,070.6	9,066.6	8.8	14.5	137.66	-115.4	-462.3	597.3	581.7	15.64	38.198	
8,900.0	8,894.6	9,131.0	9,124.3	8.8	15.2	139.53	-97.9	-465.3	608.5	592.5	16.02	37.987	
9,000.0	8,994.4	9,224.1	9,207.7	8.9	15.7	143.56	-57.3	-472.9	626.1	609.7	16.42	38.130	
9,100.0	9,094.3	9,280.5	9,255.8	8.9	15.8	146.31	-28.2	-477.0	647.9	630.6	17.34	37.364	
9,200.0	9,194.1	9,338.2	9,302.2	9.0	16.0	149.36	5.7	-482.1	677.2	658.7	18.51	36.581	
9,300.0	9,293.9	9,395.4	9,345.2	9.0	16.1	152.55	42.9	-486.8	713.1	693.2	19.89	35.856	
9,400.0	9,393.8	9,447.5	9,381.8	9.1	16.2	155.58	79.9	-490.5	755.6	734.2	21.41	35.301 SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 23

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #303H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 9155-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Warning							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Tooface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
0.0	0.0	304.2	304.2	4.2	3.0	91.52	-14.9	560.1	560.3				
100.0	100.0	404.3	404.3	4.2	3.0	91.51	-14.8	560.1	560.3	553.0	7.25	77.256	
200.0	200.0	505.1	505.1	4.2	3.0	91.52	-14.9	560.0	560.2	552.9	7.26	77.143	
300.0	300.0	606.3	606.3	4.3	3.0	91.55	-15.1	559.7	559.9	552.6	7.28	76.950	
400.0	400.0	708.1	708.1	4.3	3.1	91.61	-15.7	559.2	559.4	552.1	7.29	76.687	
500.0	500.0	810.8	810.7	4.3	3.1	91.73	-16.9	558.1	558.4	551.1	7.32	76.315	
600.0	600.0	910.8	910.8	4.3	3.1	91.87	-18.1	556.9	557.2	549.9	7.34	75.871	
700.0	700.0	1,007.1	1,007.0	4.3	3.1	91.97	-19.2	556.1	556.4	549.0	7.37	75.446	
800.0	800.0	1,108.7	1,108.6	4.4	3.2	92.09	-20.3	555.3	555.7	548.3	7.41	75.013	
900.0	900.0	1,208.3	1,208.2	4.4	3.2	92.19	-21.3	554.6	555.0	547.5	7.45	74.544	
1,000.0	1,000.0	1,308.2	1,308.1	4.4	3.3	92.30	-22.3	553.8	554.3	546.8	7.49	74.053	
1,100.0	1,100.0	1,408.2	1,408.1	4.5	3.3	92.40	-23.2	553.1	553.6	546.0	7.53	73.509	
1,200.0	1,200.0	1,510.3	1,510.3	4.5	3.4	92.51	-24.2	552.1	552.7	545.1	7.58	72.900	
1,300.0	1,300.0	1,609.7	1,609.6	4.5	3.5	92.60	-25.1	551.2	551.8	544.1	7.64	72.254	
1,400.0	1,400.0	1,710.1	1,710.0	4.6	3.5	92.73	-26.2	550.1	550.7	543.0	7.69	71.580	
1,500.0	1,500.0	1,811.3	1,811.2	4.6	3.6	92.90	-27.8	548.8	549.5	541.7	7.75	70.879	
1,600.0	1,600.0	1,914.2	1,914.1	4.7	3.7	93.12	-29.8	547.1	548.0	540.2	7.81	70.124	
1,700.0	1,700.0	2,013.8	2,013.6	4.8	3.8	93.34	-31.8	545.2	546.2	538.3	7.88	69.307	
1,800.0	1,800.0	2,114.3	2,114.1	4.8	3.8	93.58	-34.0	543.1	544.3	536.3	7.95	68.478	
1,900.0	1,900.0	2,215.3	2,215.0	4.9	3.9	93.86	-36.5	541.1	542.4	534.4	8.02	67.658	
2,000.0	2,000.0	2,315.5	2,315.2	5.0	4.0	94.18	-39.4	538.9	540.4	532.4	8.09	66.828	
2,100.0	2,100.0	2,414.9	2,414.4	5.0	4.1	94.52	-42.4	536.6	538.4	530.2	8.16	66.000	
2,200.0	2,200.0	2,508.1	2,507.6	5.1	4.2	94.84	-45.3	535.0	536.9	528.7	8.22	65.293	
2,248.6	2,248.6	2,553.3	2,552.8	5.1	4.2	94.97	-46.5	534.8	536.8	528.5	8.25	65.062	
2,300.0	2,300.0	2,604.9	2,604.3	5.2	4.2	95.11	-47.8	534.7	536.8	528.6	8.28	64.854	
2,354.7	2,354.7	2,659.5	2,658.9	5.2	4.3	95.24	-49.0	534.6	536.8	528.5	8.31	64.607	
2,400.0	2,400.0	2,702.5	2,701.9	5.2	4.3	95.36	-50.2	534.6	536.9	528.6	8.33	64.441	
2,500.0	2,500.0	2,801.5	2,800.9	5.3	4.4	95.66	-53.0	534.8	537.4	529.1	8.38	64.118	
2,600.0	2,600.0	2,900.0	2,899.4	5.4	4.5	95.98	-56.1	535.2	538.2	529.7	8.43	63.826	
2,700.0	2,700.0	3,000.9	3,000.3	5.5	4.6	96.27	-58.8	535.8	539.0	530.5	8.48	63.543	
2,800.0	2,800.0	3,102.2	3,101.5	5.6	4.6	96.41	-60.2	536.2	539.6	531.1	8.53	63.233	
2,900.0	2,900.0	3,201.0	3,200.2	5.7	4.7	96.56	-61.7	536.7	540.2	531.6	8.59	62.908	
3,000.0	3,000.0	3,300.6	3,299.8	5.7	4.8	96.69	-63.0	537.2	540.9	532.3	8.64	62.596	
3,100.0	3,100.0	3,400.0	3,399.3	5.8	4.8	96.77	-63.9	537.9	541.7	533.1	8.69	62.330	
3,200.0	3,200.0	3,500.0	3,499.2	5.9	4.9	96.84	-64.6	538.9	542.8	534.0	8.74	62.080	
3,300.0	3,300.0	3,595.2	3,594.5	6.0	4.9	96.92	-65.5	540.1	544.1	535.4	8.80	61.858	
3,400.0	3,400.0	3,695.9	3,695.1	6.1	5.0	96.96	-66.2	542.2	546.3	537.4	8.85	61.697	
3,500.0	3,500.0	3,807.4	3,806.7	6.2	5.0	96.95	-66.2	542.8	546.9	537.9	8.93	61.256	
3,600.0	3,600.0	3,906.9	3,906.1	6.3	5.0	96.95	-66.1	542.5	546.5	537.5	9.03	60.541	
3,700.0	3,700.0	4,007.2	4,006.4	6.4	5.1	96.94	-66.0	542.1	546.1	536.9	9.13	59.816	
3,758.4	3,758.4	4,063.4	4,062.6	6.5	5.1	96.92	-65.8	541.9	545.9	536.7	9.18	59.440	
3,800.0	3,800.0	4,102.4	4,101.6	6.5	5.1	96.93	-65.9	542.0	546.0	536.8	9.21	59.272	
3,900.0	3,900.0	4,191.9	4,191.1	6.6	5.1	96.95	-66.2	543.1	547.3	538.0	9.27	59.012	
4,000.0	4,000.0	4,287.0	4,286.1	6.7	5.2	96.99	-67.0	545.9	550.3	540.9	9.34	58.897	
4,100.0	4,100.0	4,393.1	4,392.2	6.8	5.2	97.02	-67.7	549.2	553.4	544.0	9.42	58.767	
4,200.0	4,200.0	4,504.8	4,503.9	6.9	5.3	97.18	-69.3	550.0	554.4	544.9	9.51	58.322	
4,300.0	4,300.0	4,605.7	4,604.7	7.0	5.4	97.52	-72.6	549.5	554.3	544.7	9.60	57.744	
4,308.0	4,308.0	4,613.1	4,612.2	7.0	5.4	97.55	-72.8	549.5	554.3	544.7	9.61	57.700	
4,400.0	4,400.0	4,704.3	4,703.4	7.1	5.5	97.75	-74.7	549.5	554.6	544.9	9.69	57.234	
4,500.0	4,500.0	4,828.2	4,827.2	7.2	5.5	97.70	-74.0	547.1	552.5	542.7	9.81	56.327	
4,600.0	4,600.0	4,930.1	4,929.0	7.3	5.6	97.69	-73.3	542.6	548.1	538.2	9.92	55.253	
4,700.0	4,700.0	5,030.3	5,029.1	7.4	5.6	97.69	-72.6	538.1	543.6	533.5	10.03	54.185	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #303H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 9155-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
4,800.0	4,800.0	5,129.7	5,128.4	7.6	5.7	97.66	-71.8	533.7	539.0	528.9	10.15	53.131	
4,900.0	4,900.0	5,233.4	5,231.9	7.7	5.8	97.64	-71.0	528.8	534.2	524.0	10.27	52.026	
5,000.0	5,000.0	5,338.0	5,336.4	7.8	5.8	97.64	-70.2	523.2	528.9	518.5	10.40	50.864	
5,100.0	5,100.0	5,451.3	5,449.4	7.9	5.9	97.67	-69.3	514.4	521.0	510.5	10.55	49.392	
5,200.0	5,200.0	5,551.1	5,548.8	8.0	6.0	97.71	-68.5	505.8	512.4	501.7	10.68	47.998	
5,300.0	5,300.0	5,652.0	5,649.2	8.1	6.0	97.76	-67.7	497.0	503.6	492.8	10.81	46.604	
5,400.0	5,400.0	5,750.0	5,746.9	8.2	6.1	97.90	-67.8	488.4	494.9	483.9	10.93	45.261	
5,500.0	5,500.0	5,849.6	5,846.1	8.3	6.2	98.32	-70.1	479.4	486.3	475.3	11.06	43.954	
5,600.0	5,600.0	5,948.6	5,944.6	8.4	6.3	-34.73	-72.4	470.5	476.3	465.1	11.19	42.575	
5,664.4	5,664.3	6,012.5	6,008.2	8.4	6.4	-34.73	-74.1	464.7	468.3	457.1	11.26	41.578	
5,700.0	5,699.9	6,047.8	6,043.4	8.4	6.4	-34.70	-75.0	461.5	463.6	452.3	11.31	41.006	
5,800.0	5,799.7	6,138.2	6,133.4	8.3	6.5	-34.47	-78.6	454.2	451.6	440.2	11.40	39.614	
5,900.0	5,899.5	6,236.3	6,231.1	8.3	6.6	-34.01	-84.3	447.1	440.6	429.1	11.51	38.278	
6,000.0	5,999.4	6,335.7	6,330.0	8.3	6.7	-33.48	-90.4	439.8	429.6	417.9	11.62	36.958	
6,100.0	6,099.2	6,434.5	6,428.4	8.3	6.8	-32.94	-96.3	432.6	418.7	407.0	11.74	35.678	
6,200.0	6,199.0	6,534.1	6,527.6	8.3	6.9	-32.37	-102.2	425.5	408.0	396.2	11.85	34.430	
6,300.0	6,298.9	6,632.8	6,625.8	8.3	7.0	-31.78	-108.1	418.5	397.2	385.3	11.96	33.208	
6,400.0	6,398.7	6,732.8	6,725.4	8.3	7.2	-31.16	-114.0	411.4	386.6	374.6	12.08	32.008	
6,500.0	6,498.5	6,831.9	6,824.1	8.3	7.3	-30.51	-119.8	404.3	376.0	363.8	12.19	30.837	
6,600.0	6,598.4	6,932.6	6,924.4	8.3	7.4	-29.79	-125.7	397.0	365.3	353.0	12.31	29.670	
6,700.0	6,698.2	7,033.9	7,025.3	8.3	7.5	-29.22	-130.4	389.2	354.0	341.6	12.44	28.449	
6,800.0	6,798.0	7,132.0	7,123.0	8.3	7.6	-28.76	-134.2	381.8	342.7	330.1	12.56	27.274	
6,900.0	6,897.9	7,231.9	7,222.6	8.3	7.7	-28.26	-138.1	374.5	331.5	318.8	12.69	26.121	
7,000.0	6,997.7	7,331.3	7,321.6	8.3	7.8	-27.79	-141.7	367.2	320.3	307.5	12.82	24.987	
7,100.0	7,097.5	7,431.0	7,421.1	8.3	7.9	-27.63	-143.4	360.1	308.9	296.0	12.96	23.835	
7,200.0	7,197.4	7,530.8	7,520.6	8.3	8.0	-27.47	-145.0	353.0	297.5	284.4	13.11	22.696	
7,300.0	7,297.2	7,629.2	7,618.7	8.3	8.1	-27.25	-146.9	346.2	286.2	273.0	13.24	21.612	
7,400.0	7,397.1	7,727.9	7,717.2	8.3	8.2	-26.98	-149.0	339.4	275.1	261.7	13.38	20.561	
7,500.0	7,496.9	7,823.0	7,812.1	8.3	8.3	-26.74	-151.0	333.8	265.0	251.5	13.50	19.634	
7,600.0	7,596.7	7,920.5	7,909.5	8.4	8.5	-26.61	-152.9	329.3	256.0	242.4	13.63	18.783	
7,700.0	7,696.6	8,019.6	8,008.4	8.4	8.6	-26.57	-154.6	325.3	247.5	233.8	13.78	17.971	
7,800.0	7,796.4	8,118.6	8,107.4	8.4	8.7	-26.57	-156.2	321.9	239.5	225.6	13.92	17.204	
7,900.0	7,896.2	8,217.9	8,206.6	8.4	8.8	-26.56	-157.9	318.5	231.6	217.6	14.07	16.460	
8,000.0	7,996.1	8,317.5	8,306.1	8.5	8.9	-26.47	-159.9	315.1	223.9	209.7	14.22	15.744	
8,100.0	8,095.9	8,420.0	8,408.5	8.5	9.0	-26.21	-162.4	310.9	215.5	201.1	14.38	14.986	
8,200.0	8,195.7	8,520.2	8,508.5	8.5	9.2	-25.77	-165.1	305.8	206.3	191.8	14.52	14.210	
8,300.0	8,295.6	8,620.2	8,608.3	8.6	9.3	-25.23	-168.0	300.6	197.0	182.4	14.66	13.441	
8,400.0	8,395.4	8,722.5	8,710.5	8.6	9.4	-24.78	-170.1	294.1	186.5	171.7	14.84	12.571	
8,500.0	8,495.2	8,821.3	8,809.1	8.6	9.5	-24.36	-171.7	287.6	175.6	160.6	14.97	11.724	
8,600.0	8,595.1	8,920.3	8,907.8	8.7	9.6	-23.88	-173.5	281.4	165.1	150.0	15.11	10.923	
8,700.0	8,694.9	9,019.7	9,007.0	8.7	9.7	-23.46	-175.1	275.5	154.7	139.4	15.26	10.137	
8,800.0	8,794.8	9,118.4	9,105.5	8.8	9.8	-23.32	-175.9	270.2	144.7	129.3	15.39	9.398	
8,900.0	8,894.6	9,220.3	9,207.3	8.8	9.9	-23.88	-175.2	265.2	134.6	119.0	15.57	8.646	
9,000.0	8,994.4	9,328.1	9,313.2	8.9	10.8	-32.11	-157.8	259.1	119.6	103.2	16.41	7.288	
9,100.0	9,094.3	9,418.6	9,397.3	8.9	11.4	-50.38	-124.9	254.1	108.0	90.3	17.70	6.103	
9,109.9	9,104.2	9,426.8	9,404.6	8.9	11.5	-52.57	-121.1	253.7	107.9	90.0	17.96	6.007 CC, ES	
9,200.0	9,194.1	9,495.2	9,461.9	9.0	11.9	-72.64	-84.0	250.3	120.7	98.8	21.85	5.521 SF	
9,300.0	9,293.9	9,559.1	9,510.6	9.0	12.2	-89.86	-42.9	245.8	162.8	136.4	26.39	6.170	
9,400.0	9,393.8	9,613.0	9,547.8	9.1	12.4	-100.84	-4.3	241.9	224.9	195.7	29.19	7.703	
9,500.0	9,493.6	9,659.0	9,577.1	9.1	12.5	-107.61	31.1	238.9	297.6	266.7	30.93	9.624	
9,600.0	9,593.4	9,689.9	9,595.5	9.2	12.6	-111.06	55.9	237.4	376.6	344.2	32.43	11.611	
9,700.0	9,693.3	9,706.0	9,604.5	9.3	12.6	-112.53	69.2	236.9	460.4	426.7	33.75	13.644	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design EIDER FEDERAL PROJECT (BULLDOG 2434) - EIDER FED #303H - OWB - ACTUAL WELLPATH												Offset Site Error:	0.0 usft
Survey Program: 100-Standard Keeper 104, 9155-MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
9,800.0	9,793.1	9,739.9	9,622.0	9.3	12.8	-115.24	98.3	235.9	547.0	512.5	34.54	15.838	
9,900.0	9,892.9	9,754.0	9,628.5	9.4	12.8	-116.25	110.7	235.2	636.3	600.9	35.39	17.979	
10,000.0	9,992.8	9,770.4	9,635.6	9.5	12.9	-117.37	125.5	234.3	727.6	691.4	36.14	20.130	
10,036.2	10,028.9	9,774.5	9,637.3	9.5	12.9	-117.63	129.3	234.1	761.0	724.6	36.39	20.909	
10,050.0	10,042.7	9,776.1	9,637.9	9.5	12.9	-95.42	130.7	234.0	773.7	737.2	36.49	21.204	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to KB=26' @ 3248.0usft (MCVAY 8)


Offset Depths are relative to Offset Datum

Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: EIDER 35 FED #502H

Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30

Grid Convergence at Surface is: 0.36°

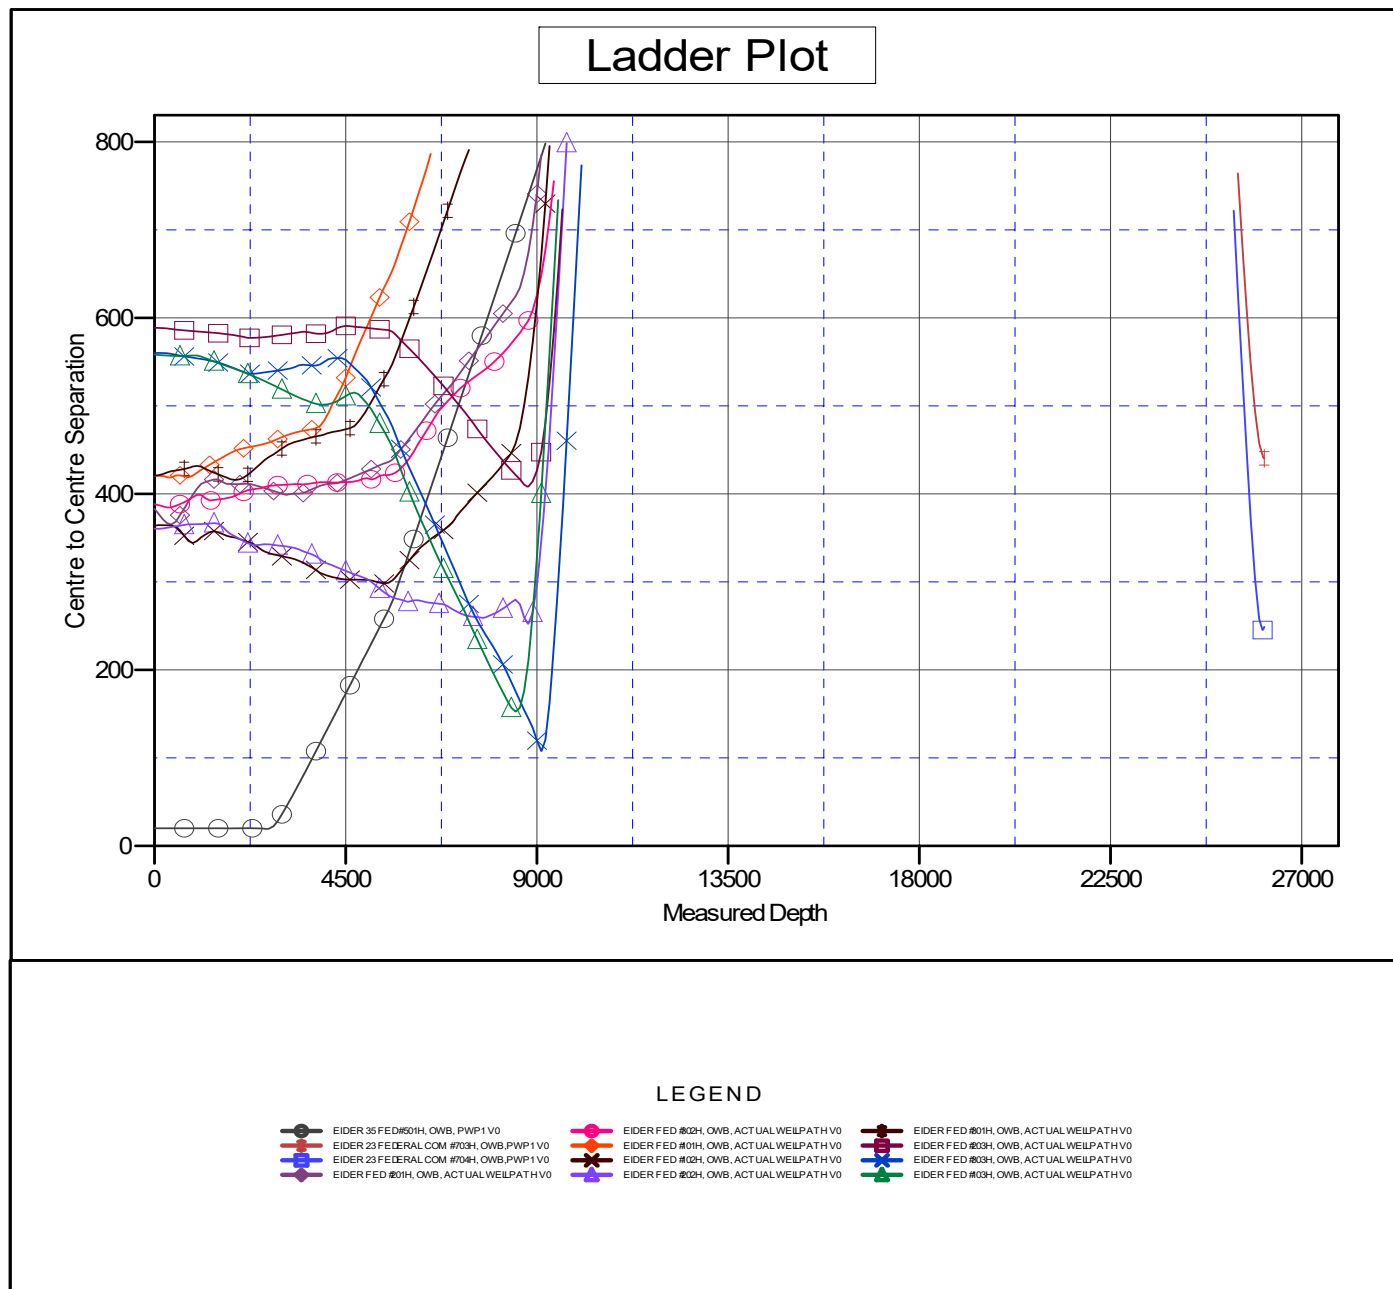

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 27

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well EIDER 35 FED #502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Reference Site:	EIDER 35 FED PROJECT	MD Reference:	KB=26' @ 3248.0usft (MCVAY 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	EIDER 35 FED #502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to KB=26' @ 3248.0usft (MCVAY 8)

Coordinates are relative to: EIDER 35 FED #502H


Offset Depths are relative to Offset Datum

Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30

Central Meridian is 104° 20' 0.000 W

Grid Convergence at Surface is: 0.36°

Separation Factor Plot

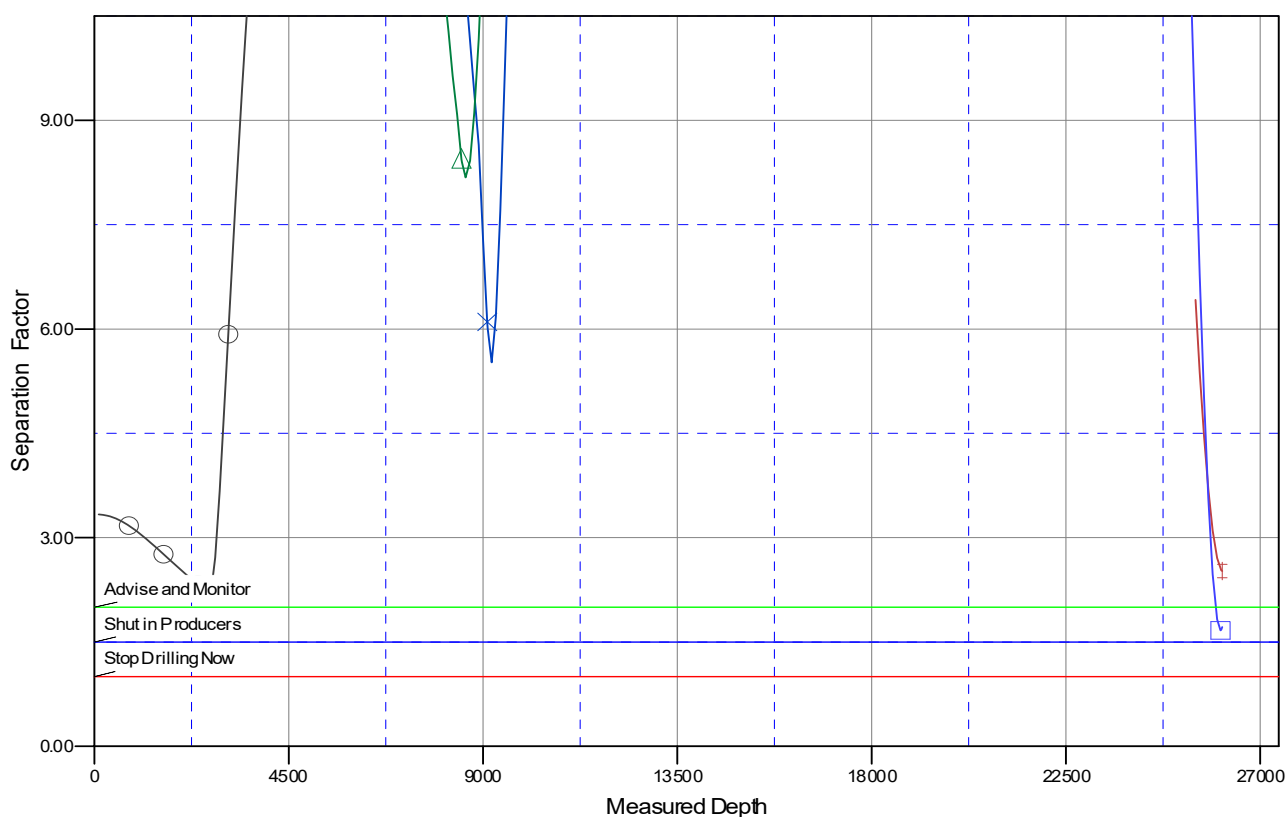

LEGEND

EIDER 35 FED#501H, OWB, PWP1 V0	EIDER FED #03H, OWB, ACTUAL WELPATH V0	EIDER FED #01H, OWB, ACTUAL WELPATH V0
EIDER 23 FEDERAL.COM #703H, OWB, PWP1 V0	EIDER FED #01H, OWB, ACTUAL WELPATH V0	EIDER FED #03H, OWB, ACTUAL WELPATH V0
EIDER 23 FEDERAL.COM #704H, OWB, PWP1 V0	EIDER FED #02H, OWB, ACTUAL WELPATH V0	EIDER FED #03H, OWB, ACTUAL WELPATH V0
EIDER FED #01H, OWB, ACTUAL WELPATH V0	EIDER FED #02H, OWB, ACTUAL WELPATH V0	EIDER FED #03H, OWB, ACTUAL WELPATH V0

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

10/28/2020 3:14:17PM

Page 28

COMPASS 5000.15 Build 91E

**PECOS DISTRICT
SURFACE USE
CONDITIONS OF APPROVAL**

OPERATOR'S NAME:	COG Operating LLC
LEASE NO.:	NMNM120907
COUNTY:	Lea

Wells:

Well Pad 1

Eider 35 Federal Com 501H

Surface Hole Location: 200' FSL & 1440' FWL, Section 35, T24S, R32E

Bottom Hole Location: 50' FNL & 330' FWL, Section 26, T24S, R32E

Eider 35 Federal Com 502H

Surface Hole Location: 230' FSL & 1440' FWL, Section 35, T24S, R32E

Bottom Hole Location: 50' FNL & 1650' FWL, Section 23, T24S, R32E

Well Pad 2

Eider 35 Federal Com 701H

Surface Hole Location: 290' FSL & 755' FWL, Section 35, T24S, R32E

Bottom Hole Location: 2590' FSL & 330' FWL, Section 26, T24S, R32E

Eider 35 Federal Com 702H

Surface Hole Location: 290' FSL & 785' FWL, Section 35, T24S, R32E

Bottom Hole Location: 2590' FSL & 1310' FWL, Section 26, T24S, R32E

TABLE OF CONTENTS

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
 - Watershed
 - Range
 - Lesser Prairie Chicken
 - VRM IV
- ☐ **Construction**
 - Notification
 - Topsoil
 - Closed Loop System
 - Federal Mineral Material Pits
 - Well Pads
 - Roads
- ☐ **Road Section Diagram**
- ☒ **Production (Post Drilling)**
 - Well Structures & Facilities
 - Pipelines
 - Electric Lines
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**

I. GENERAL PROVISIONS

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

II. PERMIT EXPIRATION

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See information below discussing NAGPRA.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

IV. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

SPECIAL REQUIREMENT(S)

Watershed:

The entire well pad(s) will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. The compacted berm shall be constructed at a minimum of 12 inches with impermeable mineral material (e.g. caliche). Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The integrity of the berm shall be maintained around the surfaced pad throughout the life of the well and around the downsized pad after interim reclamation has been completed. Any water erosion that may occur due to the construction of the well pad during the life of the well will be quickly corrected and proper measures will be taken to prevent future erosion. Stockpiling of topsoil is required. The topsoil shall be stockpiled in an appropriate location to prevent loss of soil due to water or wind erosion and not used for berming or erosion control. If fluid collects within the bermed area, the fluid must be vacuumed into a safe container and disposed of properly at a state approved facility.

TANK BATTERY:

Tank battery locations will be lined and bermed. A 20 mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Tank battery berms must be large enough to contain 1 ½ times the content of the largest tank or 24 hour production, whichever is greater. Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

BURIED/SURFACE LINE(S):

When crossing ephemeral drainages the pipeline(s) will be buried to a minimum depth of 48 inches from the top of pipe to ground level. Erosion control methods such as gabions and/or rock aprons should be placed on both up and downstream sides of the pipeline crossing. In addition, curled (weed free) wood/straw fiber wattles/logs and/or silt fences should be placed on the downstream side for sediment control during construction and maintained until soils and vegetation have stabilized. Water bars should be placed within the ROW to divert and dissipate surface runoff. A pipeline access road is not permitted to cross these ephemeral drainages. Traffic should be diverted to a preexisting route. Additional seeding may be required in floodplains and drainages to restore energy dissipating vegetation.

Prior to pipeline installation/construction a leak detection plan will be developed. The method(s) could incorporate gauges to detect pressure drops, situating valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present.

The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.

ELECTRIC LINE(S):

Any water erosion that may occur due to the construction of overhead electric line and during the life of the power line will be quickly corrected and proper measures will be taken to prevent future erosion. A power pole should not be placed in drainages, playas, wetlands, riparian areas, or floodplains and must span across the features at a distance away that would not promote further erosion.

Range:**Cattleguards**

Where a permanent cattlegaurd is approved, an appropriately sized cattleguard(s) sufficient to carry out the project shall be installed and maintained at fence crossing(s). Any existing cattleguard(s) on the access road shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattleguard(s) that are in place and are utilized during lease operations. A gate shall be constructed on one side of the cattleguard and fastened securely to H-braces.

Fence Requirement

Where entry granted across a fence line, the fence must be braced and tied off on both sides of the passageway prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fence(s).

Livestock Watering Requirement

Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

VRM IV:

Above-ground structures including meter housing that are not subject to safety requirements are painted a flat non-reflective paint color, Shale Green from the BLM Standard Environmental Color Chart (CC-001: June 2008).

Short-term mitigation measures include painting all above-ground structures that are not subject to safety requirements (including meter housing) Shale Green, which is a flat non-reflective paint color listed in the BLM Standard Environmental Color Chart (CC-001: June 2013). Long-term mitigation measures include the removal of wells and associated infrastructure following abandonment (end of cost-effective production). Previously impacted areas will be reclaimed by removing structures and caliche pads, returning disturbed areas to natural grade, and revegetating with an approved BLM seed mixture; thereby eliminating visual impacts.

Lesser Prairie Chicken:**Timing Limitation Stipulation/Condition of Approval for Lesser Prairie-Chicken:**

Oil and gas activities including 3-D geophysical exploration, and drilling will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Additionally, no new drilling will be allowed within up to 200 meters of leks known at the time of permitting.

Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

Timing Limitation Exceptions:

The Carlsbad Field Office will publish an annual map of where the LPC timing and noise stipulations and conditions of approval (Limitations) will apply for the identified year (between March 1 and June 15) based on the latest survey information. The LPC Timing Area map will identify areas which are Habitat Areas (HA), Isolated Population Area (IPA), and Primary Population Area (PPA). The LPC Timing Area map will also have an area in red crosshatch. The red crosshatch area is the only area where an operator is required to submit a request for exception to the LPC Limitations. If an operator is operating outside the red crosshatch area, the LPC Limitations do not apply for that year and an exception to LPC Limitations is not required.

Ground-level Abandoned Well Marker to avoid raptor perching:

Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well. For more installation details, contact the Carlsbad Field Office at 575-234-5972.

V. CONSTRUCTION

A. NOTIFICATION

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

B. TOPSOIL

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

C. CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

D. FEDERAL MINERAL MATERIALS PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

E. WELL PAD SURFACING

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

F. EXCLOSURE FENCING (CELLARS & PITS)**Exclosure Fencing**

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

G. ON LEASE ACCESS ROADS**Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

Surfacing

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

Crowning

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

Ditching

Ditching shall be required on both sides of the road.


Turnouts

Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

Drainage

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outsloping and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

Cross Section of a Typical Lead-off Ditch

All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

Formula for Spacing Interval of Lead-off Ditches

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

Cattle guards

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

Fence Requirement

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

Public Access

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes

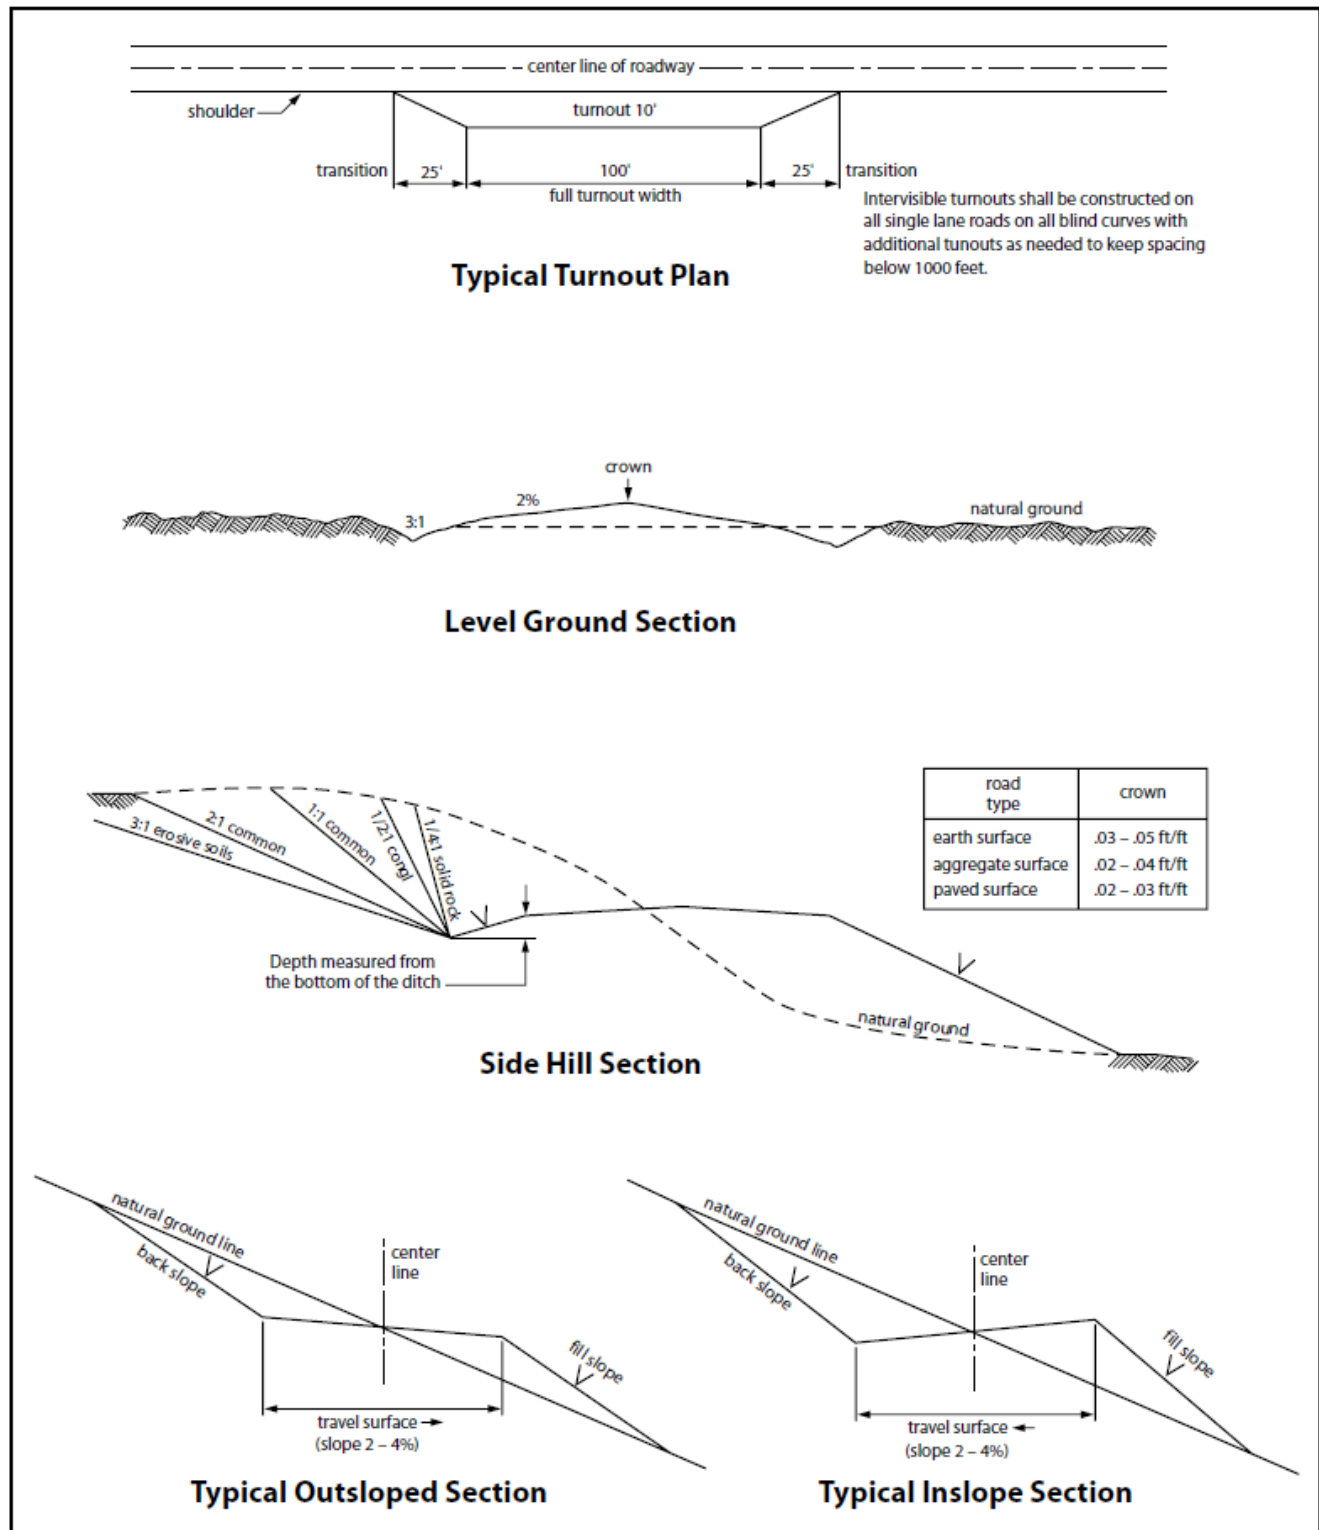


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

VI. PRODUCTION (POST DRILLING)

A. WELL STRUCTURES & FACILITIES

Placement of Production Facilities

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

Exclosure Netting (Open-top Tanks)

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

Chemical and Fuel Secondary Containment and Exclosure Screening

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

Open-Vent Exhaust Stack Exclosures

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

Containment Structures

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

Painting Requirement

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

B. PIPELINES

- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, passages, or voids are intersected by trenching, and no pipe will be laid in the trench at that point until clearance has been issued by the Authorized Officer.
- If a void is encountered alignments may be rerouted to avoid the karst feature and lessen; the potential of subsidence or collapse of karst features, buildup of toxic or combustible gas, or other possible impacts to cave and karst resources from the buried pipeline.
- Special restoration stipulations or realignment may be required at such intersections, if any.
- A leak detection plan will be submitted to the BLM Carlsbad Field Office for approval prior to pipeline installation. The method could incorporate gauges to detect pressure drops, siting valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.
- Regular monitoring is required to quickly identify leaks for their immediate and proper treatment.
- All spills or leaks will be reported to the BLM immediately for their immediate and proper treatment.

BURIED PIPELINE STIPULATIONS

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C.6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.

5. All construction and maintenance activity will be confined to the authorized right-of-way.

6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.

7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:

- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 20 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
- Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
- The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)

8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.

9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times.

The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.

11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.

12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- | | |
|--|--|
| <input type="checkbox"/> seed mixture 1 | <input type="checkbox"/> seed mixture 3 |
| <input checked="" type="checkbox"/> seed mixture 2 | <input type="checkbox"/> seed mixture 4 |
| <input type="checkbox"/> seed mixture 2/LPC | <input type="checkbox"/> Aplomado Falcon Mixture |

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 17 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

17. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

18. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

19. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

20. Escape Ramps - The operator will construct and maintain pipeline/utility trenches [that are not otherwise fenced, screened, or netted] to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.
- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

C. ELECTRIC LINES

- Smaller powerlines will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize changes to runoff or possible leaks and spills from entering karst systems. Larger powerlines will adjust their pole spacing to avoid cave and karst features.
- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, cave passages, or voids are penetrated during construction.
- No further construction will be done until clearance has been issued by the Authorized Officer.
- Special restoration stipulations or realignment may be required.

STANDARD STIPULATIONS FOR OVERHEAD ELECTRIC DISTRIBUTION LINES

A copy of the grant and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.)

Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.
 4. There will be no clearing or blading of the right-of-way unless otherwise agreed to in writing by the Authorized Officer.
 5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the holder without liability or expense to the United States.
- Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.
6. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.
 7. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.
 8. Upon cancellation, relinquishment, or expiration of this grant, the holder shall comply with those abandonment procedures as prescribed by the Authorized Officer.
 9. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this grant, whichever comes first. This will not apply where the power line extends service to an active, adjoining facility or facilities.

10. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 11 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

11. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

12. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

13. Special Stipulations:

For reclamation remove poles, lines, transformer, etc. and dispose of properly.
Fill in any holes from the poles removed.

VII. INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

VIII. FINAL ABANDONMENT & RECLAMATION

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Ground-level Abandoned Well Marker to avoid raptor perching: Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well.

Seed Mixture 2, for Sandy Sites

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law (s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed* per acre:

Species

	<u>lb/acre</u>
Sand dropseed (<i>Sporobolus cryptandrus</i>)	1.0
Sand love grass (<i>Eragrostis trichodes</i>)	1.0
Plains bristlegrass (<i>Setaria macrostachya</i>)	2.0

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed.

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	COG Production, LLC
LEASE NO.:	NMNM-029694
WELL NAME & NO.:	Eider 35 Federal Com 502H
SURFACE HOLE FOOTAGE:	0230' FSL & 1440' FWL
BOTTOM HOLE FOOTAGE:	0050' FNL & 1650' FWL Sec. 23, T.24 S., R.32 E.
LOCATION:	Section 35, T.24 S., R.32 E., NMPM
COUNTY:	Lea County, New Mexico

COA

H2S	<input checked="" type="radio"/> Yes	<input type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input checked="" type="radio"/> Conventional	<input type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input type="checkbox"/> Fluid Filled	<input type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit

Possible water flows in the Salado and Castile

Possible lost circulation in the Rustler, Red Beds, and Delaware

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H2S) Drilling Plan shall be activated 500 feet prior to drilling into the **Delaware** formation. As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **1010** feet (a minimum of 25 feet (Lea County) into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.
3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **2000 (2M)** psi.
2. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **3000 (3M)** psi.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
4. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
5. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
6. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- c. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- d. The results of the test shall be reported to the appropriate BLM office.
- e. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JAM 01082021

COG PRODUCTION LLC
HYDROGEN SULFIDE DRILLING OPERATIONS PLAN

1. HYDROGEN SULFIDE TRAINING

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

- a. The hazards and characteristics of hydrogen sulfide (H₂S).
- b. The proper use and maintenance of personal protective equipment and life support systems.
- c. The proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
- d. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

- a. The effects of H₂S on metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
- b. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
- c. The contents and requirements of the H₂S Drilling Operations Plan and the Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H₂S zone (within 3 days or 500 feet) and weekly H₂S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H₂S Drilling Operations Plan and the Public Protection Plan. This plan shall be available at the well site. All personnel will be required to carry documentation that they have received the proper training.

2. H₂S SAFETY EQUIPMENT AND SYSTEMS

Note: All H₂S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H₂S. If H₂S greater than 100 ppm is encountered in the gas stream we will shut in and install H₂S equipment.

- a. Well Control Equipment:
 - Flare line.
 - Choke manifold with remotely operated choke.
 - Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit.
 - Auxiliary equipment to include: annular preventer, mud-gas separator, rotating head.

- b. Protective equipment for essential personnel:
Mark II Surviveair 30-minute units located in the dog house and at briefing areas.
- c. H2S detection and monitoring equipment:
2 - portable H2S monitor positioned on location for best coverage and response. These units have warning lights and audible sirens when H2S levels of 20 ppm are reached.
- d. Visual warning systems:
Caution/Danger signs shall be posted on roads providing direct access to location. Signs will be painted a high visibility yellow with black lettering of sufficient size to be readable at a reasonable distance from the immediate location. Bilingual signs will be used, when appropriate. See example attached.
- e. Mud Program:
The mud program has been designed to minimize the volume of H2S circulated to the surface.
- f. Metallurgy:
All drill strings, casings, tubing, wellhead, blowout preventers, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service.
- g. Communication:
Company vehicles equipped with cellular telephone.

COG PRODUCTION LLC has conducted a review to determine if an H2S contingency plan is required for the above referenced well. We were able to conclude that any potential hazardous volume would be minimal. H2S concentrations of wells in this area from surface to TD are low enough; therefore, we do not believe that an H2S contingency plan is necessary.

W A R N I N G

**YOU ARE ENTERING AN H₂S AREA
AUTHORIZED PERSONNEL ONLY**

- 1. BEARDS OR CONTACT LENSES NOT ALLOWED***
- 2. HARD HATS REQUIRED***
- 3. SMOKING IN DESIGNATED AREAS ONLY***
- 4. BE WIND CONSCIOUS AT ALL TIMES***
- 5. CK WITH COG OPERATING LLC FOREMAN AT MAIN OFFICE***

COG PRODUCTION LLC


1-575-748-6940

EMERGENCY CALL LIST

	<u>OFFICE</u>	<u>MOBILE</u>
COG PRODUCTION LLC OFFICE	575-748-6940	
SETH WILD	432-683-7443	432-528-3633
WALTER ROYE	575-748-6940	432-934-1886

EMERGENCY RESPONSE NUMBERS

	<u>OFFICE</u>
STATE POLICE	575-748-9718
EDDY COUNTY SHERIFF	575-746-2701
EMERGENCY MEDICAL SERVICES (AMBULANCE)	911 or 575-746-2701
EDDY COUNTY EMERGENCY MANAGEMENT (HARRY BURGESS)	575-887-9511
STATE EMERGENCY RESPONSE CENTER (SERC)	575-476-9620
CARLSBAD POLICE DEPARTMENT	575-885-2111
CARLSBAD FIRE DEPARTMENT	575-885-3125
NEW MEXICO OIL CONSERVATION DIVISION	575-748-1283
INDIAN FIRE & SAFETY	800-530-8693
HALLIBURTON SERVICES	800-844-8451

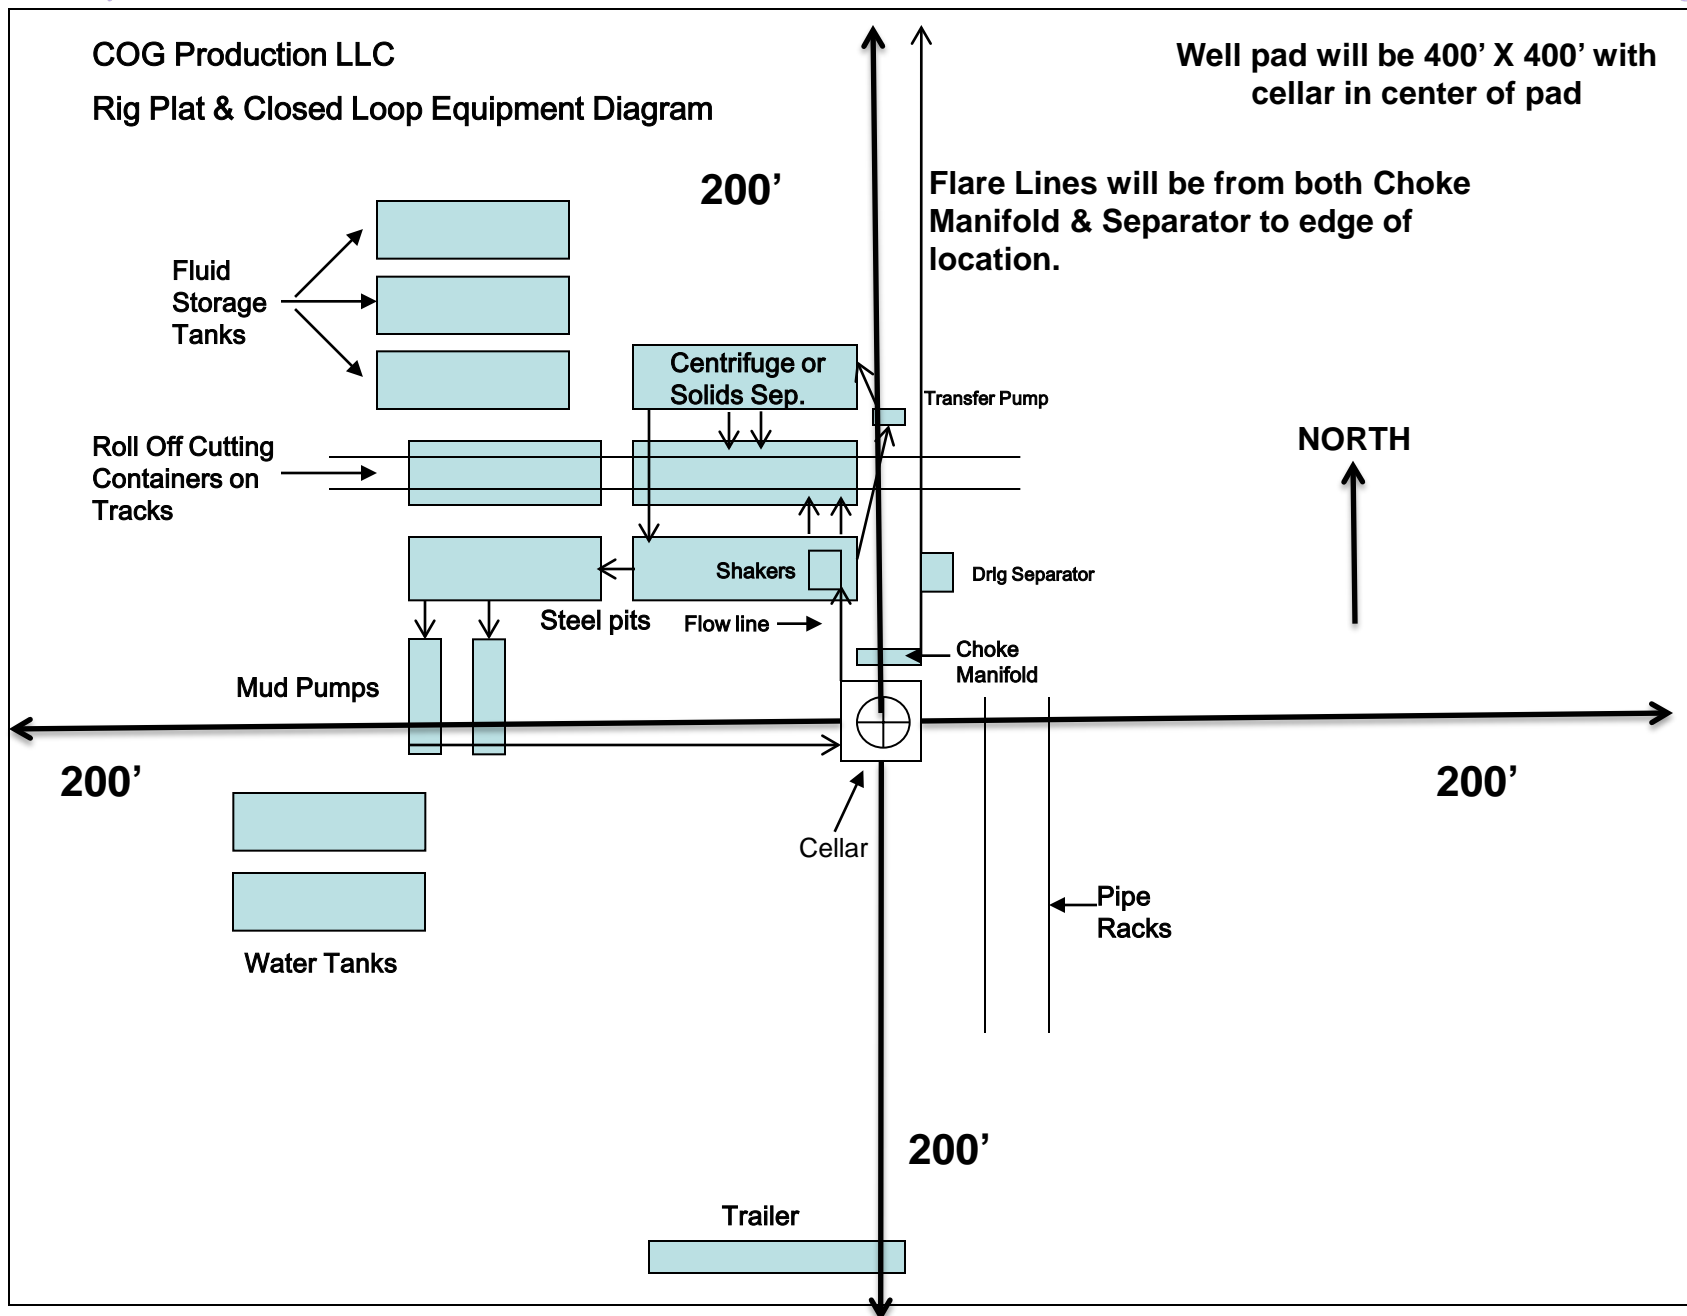

COG Operating, LLC - Eider 35 Federal Com #502H

1. Geologic Formations

TVD of target	10,649' EOL	Pilot hole depth	NA
MD at TD:	26,122'	Deepest expected fresh water:	380'

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Quaternary Fill	Surface	Water	
Rustler	944	Water	
Top of Salt	1265	Salt	
Base of Salt	4597	Salt	
Lamar	4814	Salt Water	
Bell Canyon	4883	Salt Water	
Cherry Canyon	5768	Oil/Gas	
Brushy Canyon	7183	Oil/Gas	
Bone Spring Lime	8775	Oil/Gas	
M. Avalon Shale	9148	Oil/Gas	
L. Avalon Shale	9522	Oil/Gas	
1st Bone Spring Sand	9895	Oil/Gas	
2nd Bone Spring Sand	10548	Target	
3rd Bone Spring Sand	X	Not Penetrated	
Wolfcamp	X	Not Penetrated	

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Tension
	From	To							
17.5"	0	970	13.375"	54.5	J55	STC	2.55	1.26	9.72
12.25"	0	3500	9.625"	40	J55	LTC	1.40	0.97	3.71
12.25"	3500	4800	9.625"	40	L80	LTC	1.23	1.41	6.54
8.75"	0	26,122	5.5"	17	P110	LTC	1.45	2.60	2.46
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet

Intermediate casing will be kept at least 1/3 full while running casing to mitigate collapse. Intermediate burst based on 0.7 frac gradient at the shoe with Gas Gradient 0.1 psi/ft to surface.

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

COG Operating, LLC - Eider 35 Federal Com #502H

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary?	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

COG Operating, LLC - Eider 35 Federal Com #502H

3. Cementing Program

Casing	# Sk	Wt. lb/ gal	Yld ft ³ / sack	H ₂ O gal/sk	500# Comp. Strength (hours)	Slurry Description
Surf.	390	13.5	1.75	9	12	Lead: Class C + 4% Gel + 1% CaCl ₂
	250	14.8	1.34	6.34	8	Tail: Class C + 2% CaCl ₂
Inter.	910	12.7	2.0	9.6	16	Lead: 35:65:6 C Blend
	250	14.8	1.34	6.34	8	Tail: Class C + 2% CaCl
5.5 Prod	820	11.9	2.5	19	72	Lead: 50:50:10 H Blend
	4070	14.4	1.24	5.7	19	Tail: 50:50:2 Class H Blend

Volumes Subject to Observed Hole Conditions and/or Fluid Caliper Results

Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

Casing String	TOC	% Excess
Surface	0'	50%
1 st Intermediate	0'	50%
Production	3,000'	25% OH in Lateral (KOP to EOL) – 40% OH in Vertical

COG Operating, LLC - Eider 35 Federal Com #502H

4. Pressure Control Equipment

N	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
---	---

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	x	Tested to:
12-1/4"	13-5/8"	2M	Annular	x	2000 psi
			Blind Ram		2M
			Pipe Ram		
			Double Ram		
			Other*		
8-3/4"	13-5/8"	3M	Annular	x	50% testing pressure
			Blind Ram	x	3M
			Pipe Ram	x	
			Double Ram		
			Other*		

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

X	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
N	Are anchors required by manufacturer?
N	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

COG Operating, LLC - Eider 35 Federal Com #502H

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	Surf. Shoe	FW Gel	8.6 - 8.8	28-34	N/C
Surf csg	9-5/8" Int shoe	Saturated Brine	10 - 10.1	28-34	N/C
9-5/8" Int shoe	Lateral TD	Cut Brine	8.6 - 9.3	28-34	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
Y	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
Y	No Logs are planned based on well control or offset log information.
N	Drill stem test? If yes, explain.
N	Coring? If yes, explain.

Additional logs planned		Interval
N	Resistivity	Pilot Hole TD to ICP
N	Density	Pilot Hole TD to ICP
Y	CBL	Production casing (If cement not circulated to surface)
Y	Mud log	Intermediate shoe to TD
N	PEX	

COG Operating, LLC - Eider 35 Federal Com #502H

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	5150 psi at 10649' TVD
Abnormal Temperature	NO 165 Deg. F.

No abnormal pressure or temperature conditions are anticipated. Sufficient mud materials to maintain mud properties and weight increase requirements will be kept on location at all times.

Sufficient supplies of Paper/LCM for periodic sweeps to control seepage and losses will be maintained on location.

Hydrogen Sulfide (H₂S) monitors will be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

N H₂S is present


Y H₂S Plan attached

8. Other Facets of Operation


Y	Is it a walking operation?
Y	Is casing pre-set?

x	H ₂ S Plan.
x	BOP & Choke Schematics.
x	Directional Plan


2,000 psi BOP Schematic

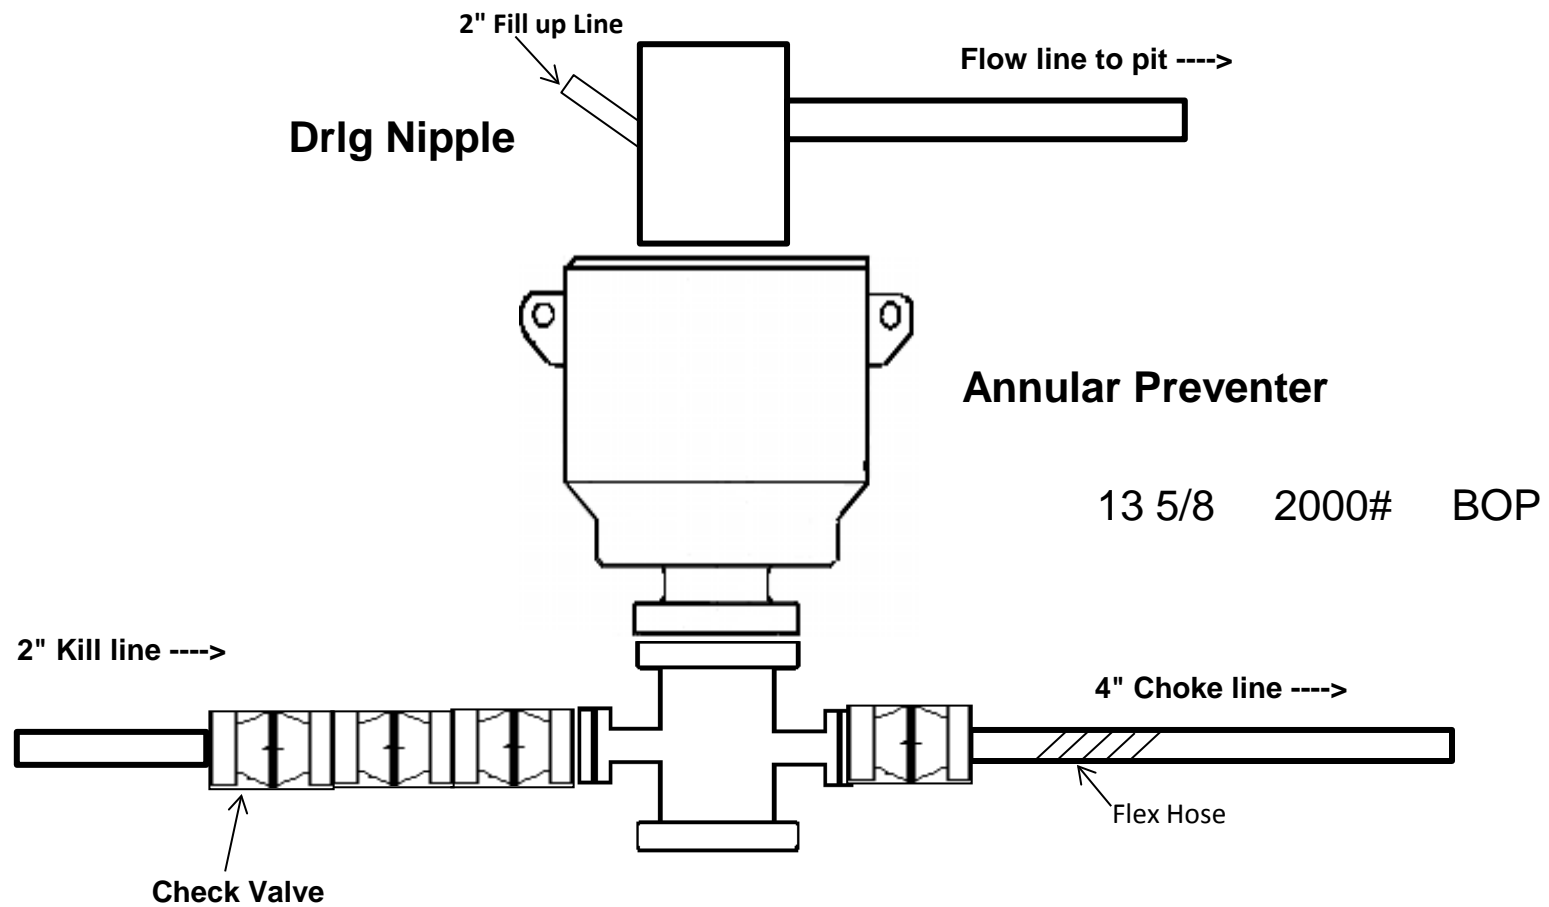


2M Choke Manifold Equipment (WITH MGS + CLOSED LOOP)

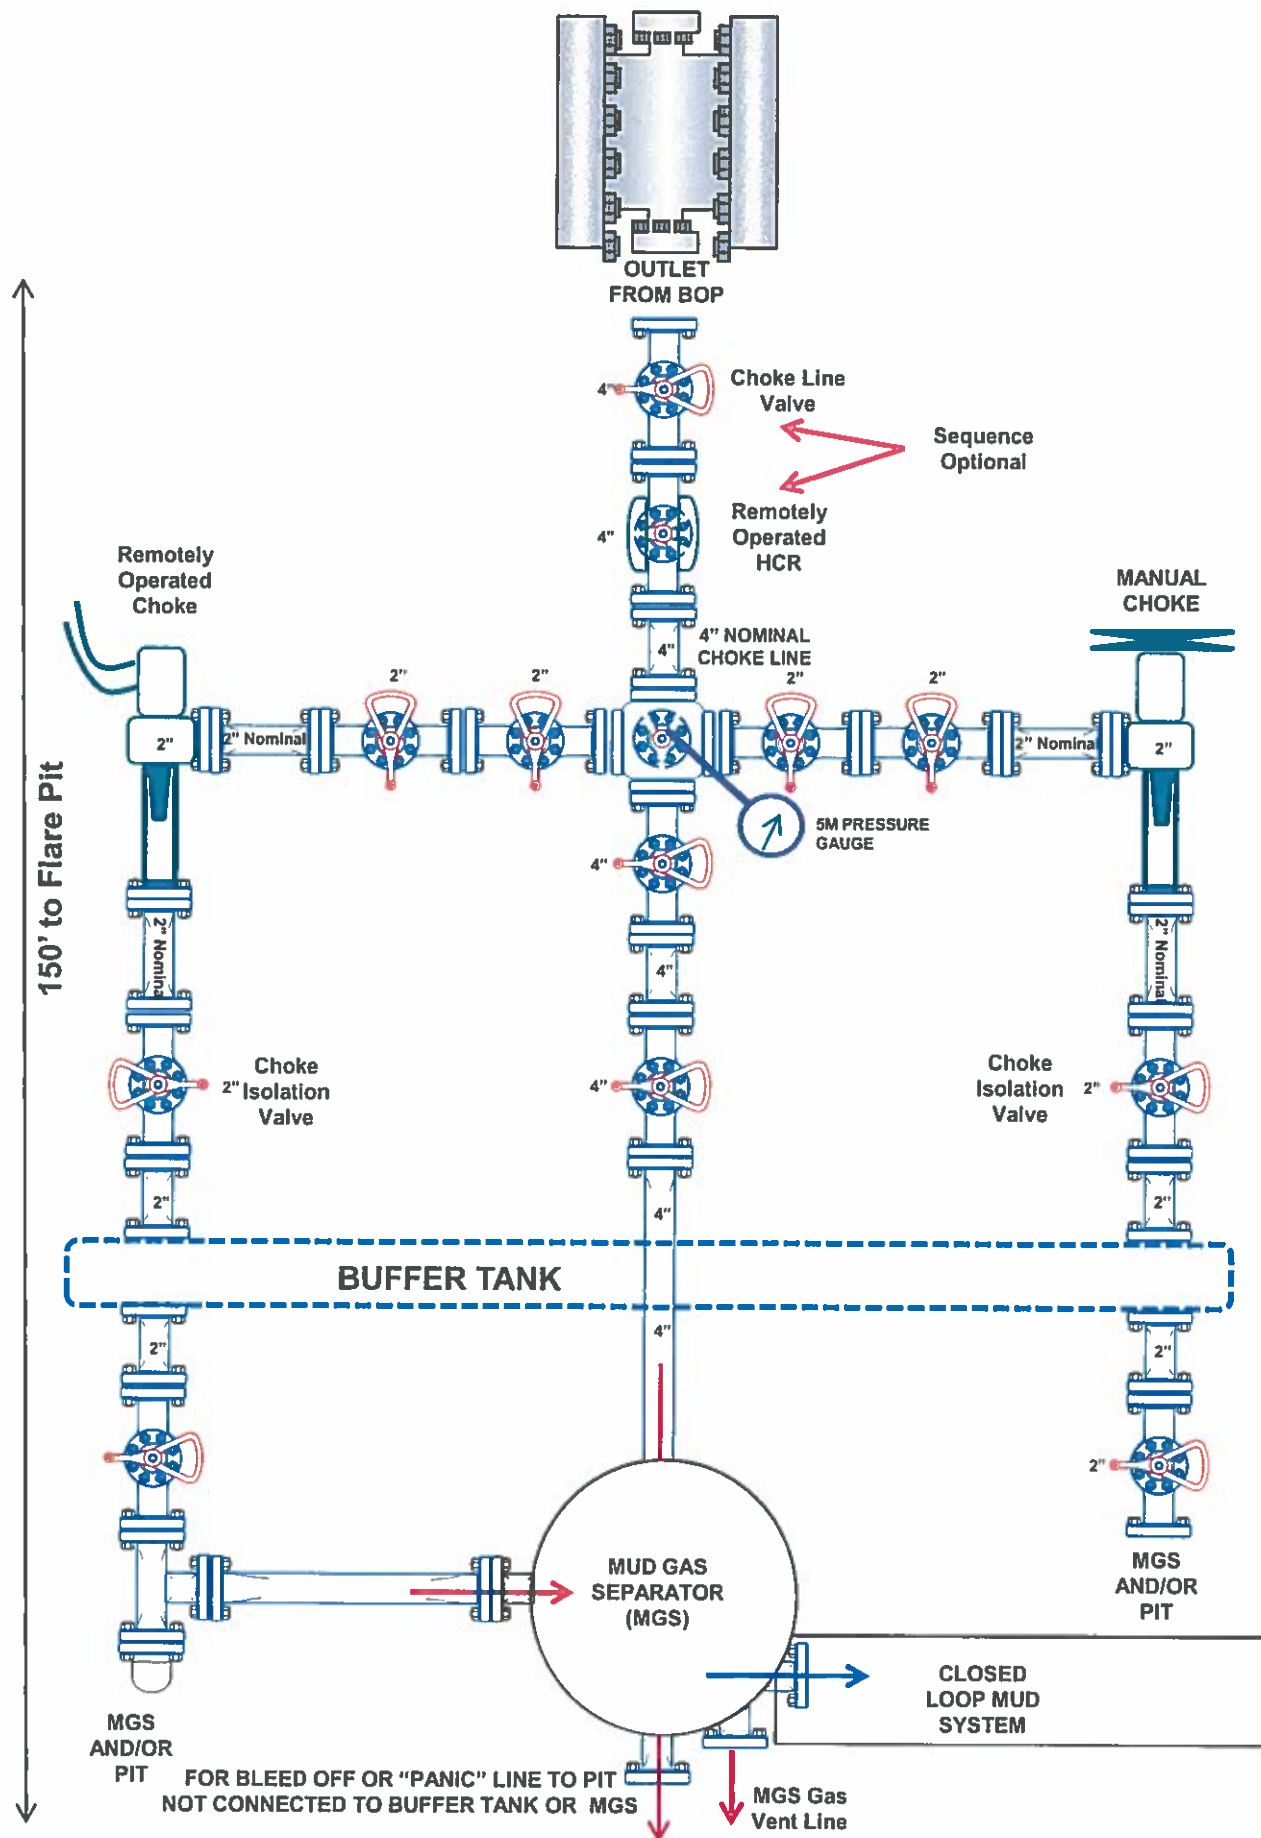

3,000 psi BOP Schematic

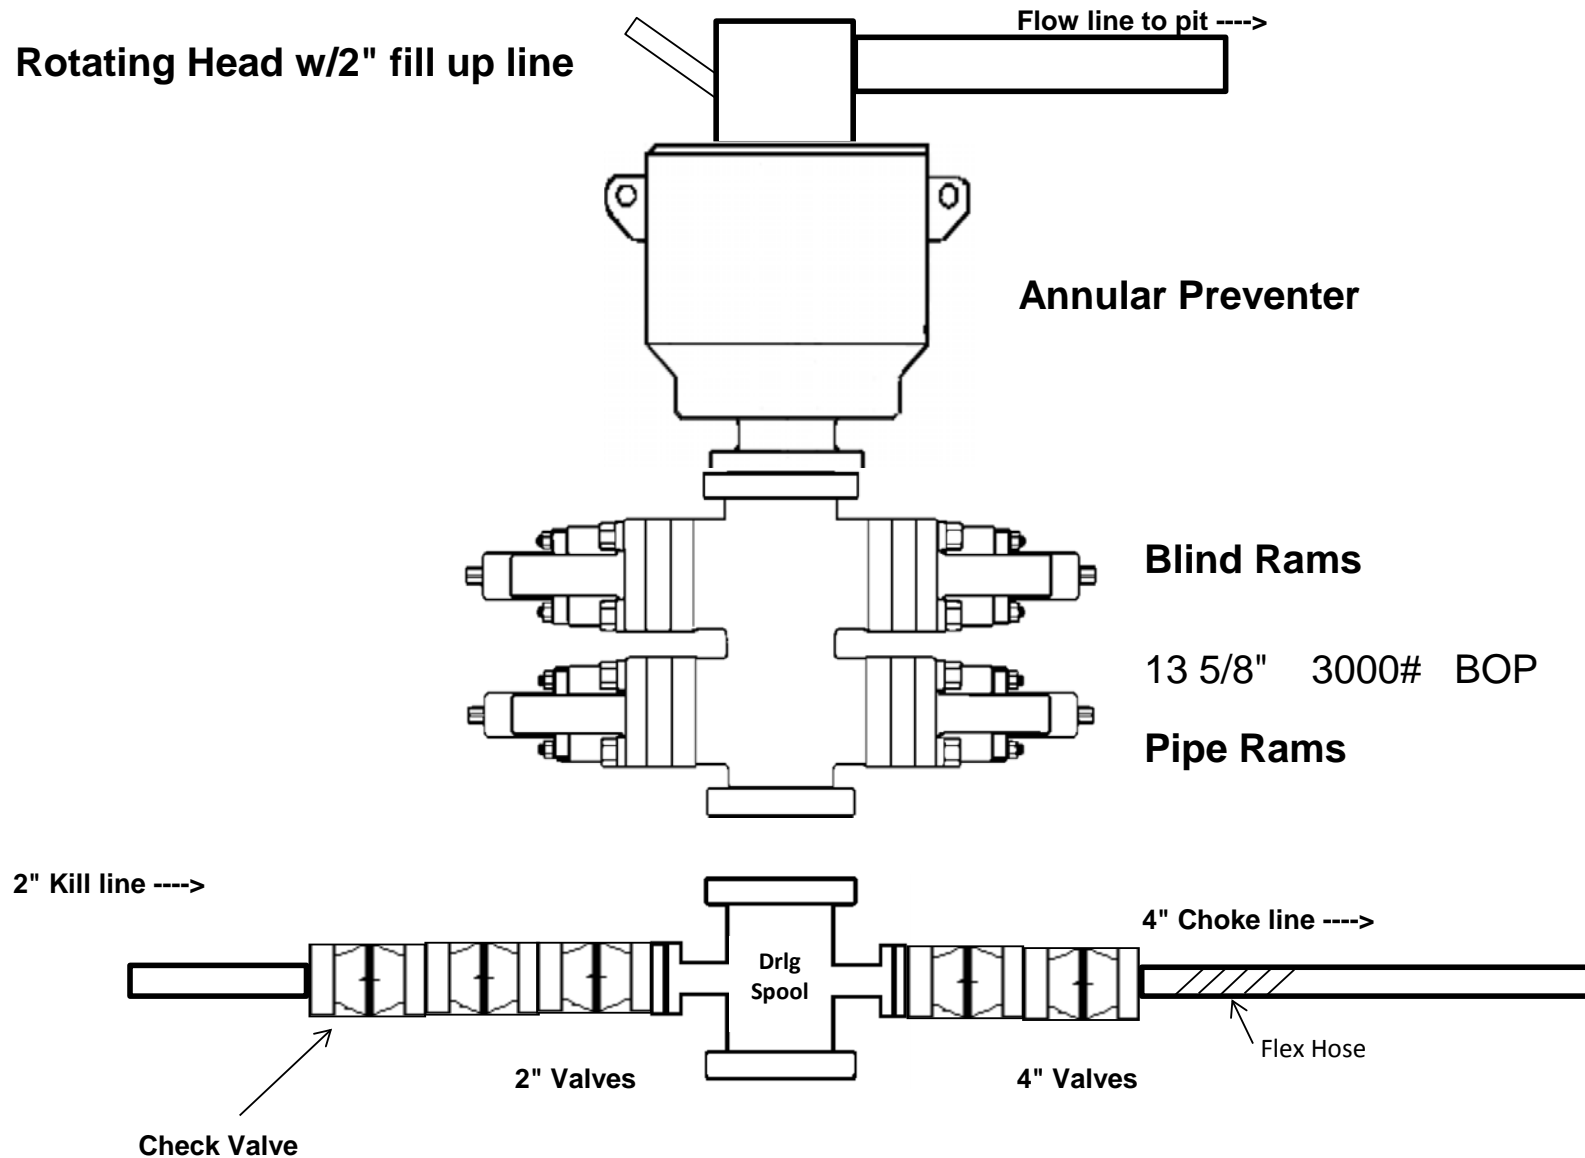

3M Choke Manifold Equipment (WITH MGS + CLOSED LOOP)

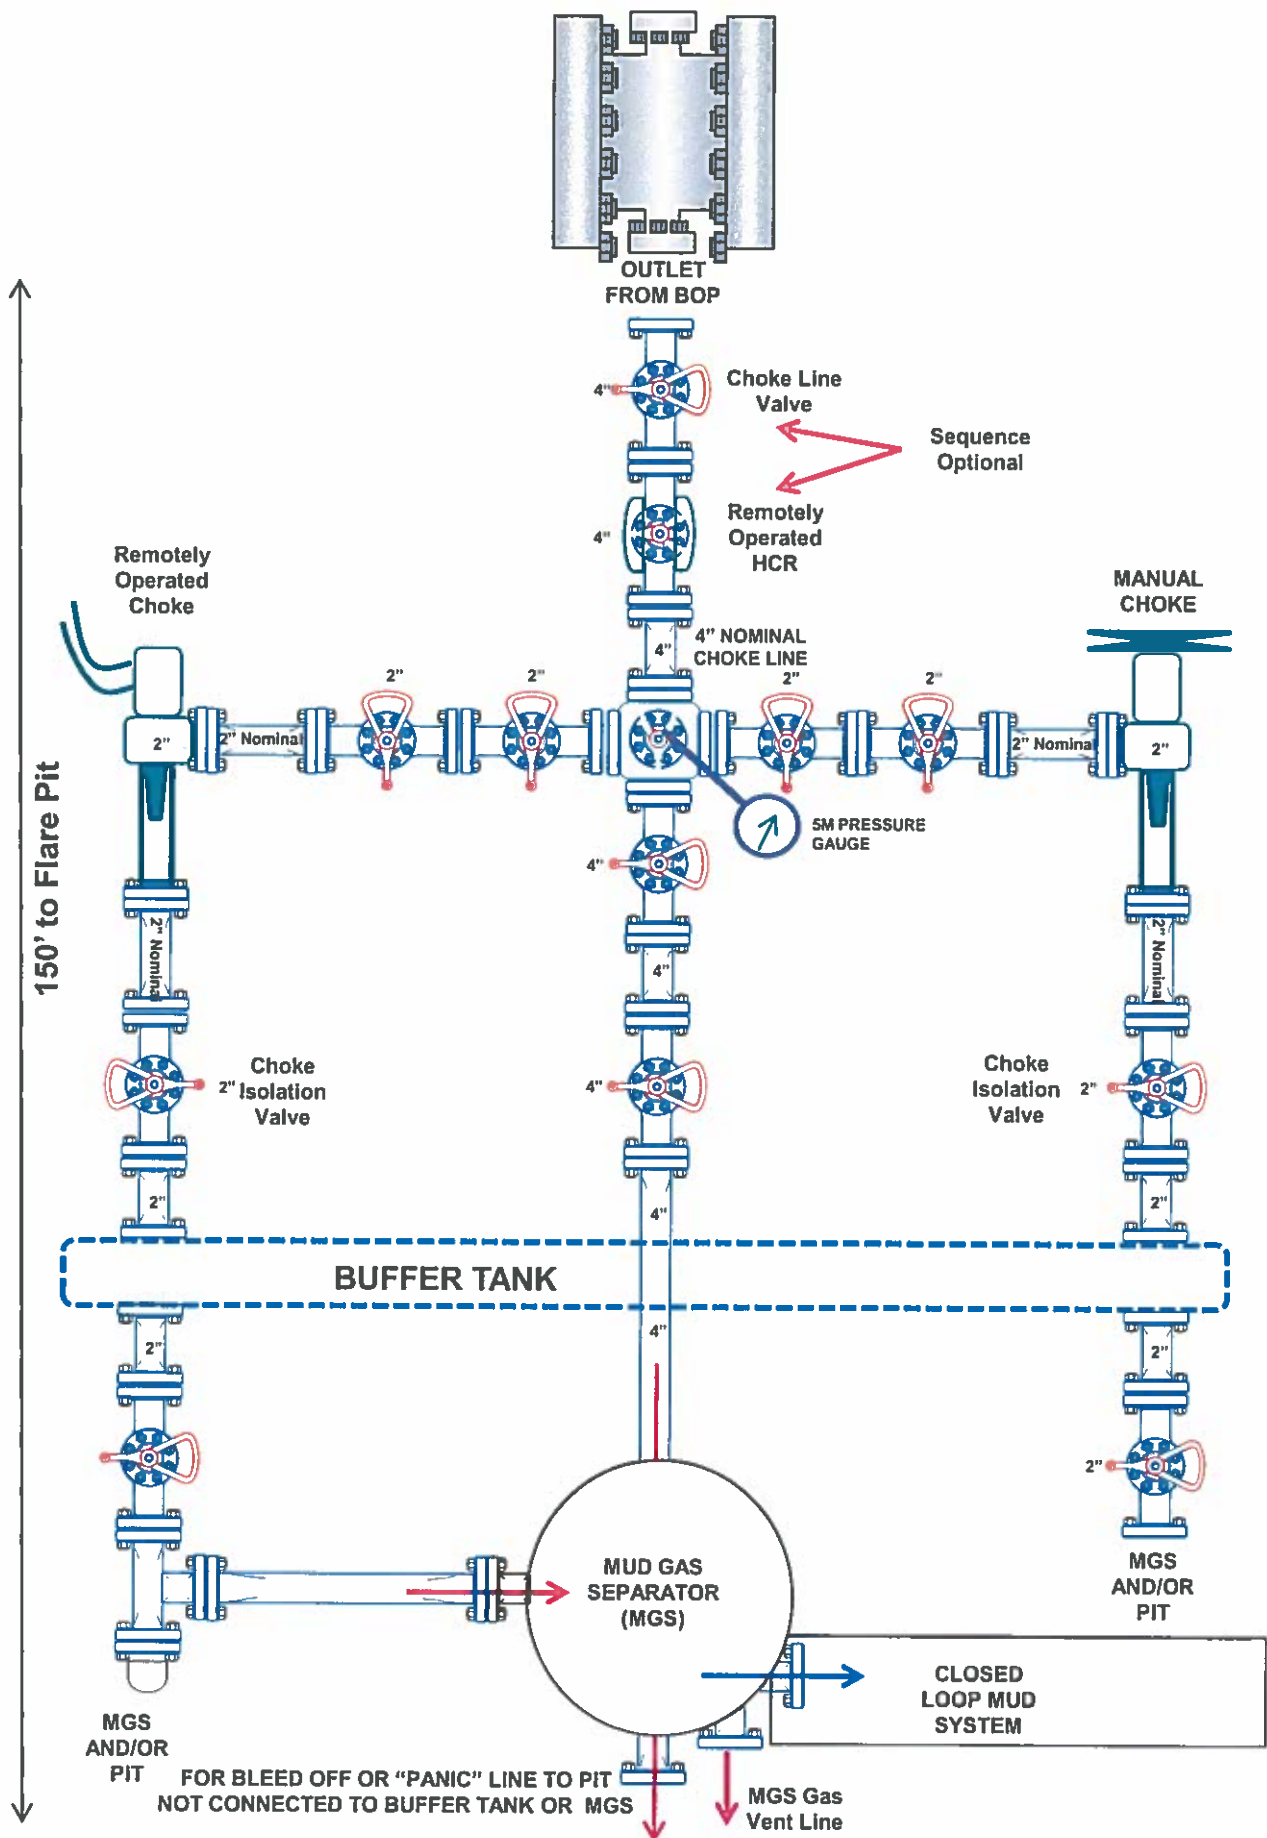

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 40242

CONDITIONS

Operator: COG PRODUCTION, LLC 600 W. Illinois Ave Midland, TX 79701	OGRID: 217955
	Action Number: 40242
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
pkautz	Will require a File As Drilled C-102 and a Directional Survey with the C-104	8/6/2021
pkautz	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	8/6/2021
