

Form 3160-3
(June 2015)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 20185. Lease Serial No.
NMNM048344

6. If Indian, Allottee or Tribe Name

7. If Unit or CA Agreement, Name and No.

8. Lease Name and Well No.

WELCH B 28 FEDERAL

50H

9. API Well No.

30-015-49235

10. Field and Pool, or Exploratory
ARTESIA/GLORIETA YESO11. Sec., T. R. M. or Blk. and Survey or Area
SEC 27/T17S/R28E/NMP1a. Type of work: ☒ DRILL ☐ REENTER
1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other
1c. Type of Completion: ☐ Hydraulic Fracturing ☒ Single Zone ☐ Multiple Zone2. Name of Operator
SPUR ENERGY PARTNERS LLC3a. Address
9655 KATY FREEWAY, SUITE 500, Houston, TX 770243b. Phone No. (include area code)
(832) 930-8548

4. Location of Well (Report location clearly and in accordance with any State requirements. *)

At surface SWNW / 1756 FNL / 775 FWL / LAT 32.8079545 / LONG -104.1698939

At proposed prod. zone SWNW / 2305 FNL / 50 FWL / LAT 32.8060262 / LONG -104.1891854

14. Distance in miles and direction from nearest town or post office*

12. County or Parish
EDDY13. State
NM15. Distance from proposed*
location to nearest
property or lease line, ft.
(Also to nearest drig. unit line, if any) 1 feet

16. No of acres in lease

17. Spacing Unit dedicated to this well

160.0

18. Distance from proposed location*
to nearest well, drilling, completed,
applied for, on this lease, ft. 20 feet

19. Proposed Depth

4040 feet / 9684 feet

20. BLM/BIA Bond No. in file

FED: NMB001783

21. Elevations (Show whether DF, KDB, RT, GL, etc.)
3660 feet22. Approximate date work will start*
02/21/202223. Estimated duration
10 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

1. Well plat certified by a registered surveyor.

2. A Drilling Plan.

3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).

4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).

5. Operator certification.

6. Such other site specific information and/or plans as may be requested by the BLM.

25. Signature
(Electronic Submission)

Name (Printed/Typed)

SARAH CHAPMAN / Ph: (832) 930-8548

Date

12/07/2020

Title

Regulatory Directory

Approved by (Signature)

(Electronic Submission)

Name (Printed/Typed)

Cody Layton / Ph: (575) 234-5959

Date

11/12/2021

Title

Assistant Field Manager Lands & Minerals

Office

Carlsbad Field Office

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



Approval Date: 11/12/2021

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

| | | | |
|--|--|--|---|
| ¹ API Number 30-015-49235 | | ² Pool Code 96830 | ³ Pool Name Artesia; Glorieta-Yeso (O) |
| ⁴ Property Code 332213 | ⁵ Property Name WELCH B 28 FED | | ⁶ Well Number 50H |
| ⁷ OGRID NO. 328947 | ⁸ Operator Name SPUR ENERGY PARTNERS LLC. | | ⁹ Elevation 3660' |

¹⁰ Surface Location

| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet From the | East/West line | County |
|---------------|-----------|------------|------------|---------|---------------|------------------|---------------|----------------|-------------|
| E | 27 | 17S | 28E | | 1756 | NORTH | 775 | WEST | EDDY |

¹¹ Bottom Hole Location If Different From Surface

| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|-----------|------------|------------|---------|---------------|------------------|---------------|----------------|-------------|
| E | 28 | 17S | 28E | | 2305 | NORTH | 50 | WEST | EDDY |

| ¹² Dedicated Acres | ¹³ Joint or Infill | ¹⁴ Consolidation Code | ¹⁵ Order No. |
|-------------------------------|-------------------------------|----------------------------------|-------------------------|
| 160 | | | |

No allowable will be assigned to this completion until all interest have been consolidated or a non-standard unit has been approved by the division.

| | |
|--|--|
| <p>¹⁶ GEODETIC DATA NAD 83 GRID - NM EAST</p> <p>SURFACE LOCATION (SL) N: 657705.2 - E: 591552.5 LAT: 32.8079545° N LONG: 104.1698939° W</p> <p>FIRST TAKE POINT (FTP) 2305' FNL & 100' FEL - SEC 28 N: 657150.3 - E: 590672.2 LAT: 32.8064331° N LONG: 104.1727620° W</p> <p>LAST TAKE POINT (LTP) 2305' FNL & 100' FWL - SEC 28 N: 656996.6 - E: 585676.3 LAT: 32.8060302° N LONG: 104.1890228° W</p> <p>BOTTOM HOLE (BH) N: 656995.0 - E: 585626.3 LAT: 32.8060262° N LONG: 104.1891854° W</p> <p>CORNER DATA NAD 83 GRID - NM EAST</p> <p>A: FOUND BRASS CAP "1941" N: 654104.0 - E: 585547.5</p> <p>B: FOUND BRASS CAP "1941" N: 656702.1 - E: 585573.1</p> <p>C: FOUND BRASS CAP "1941" N: 659297.8 - E: 585602.6</p> <p>D: FOUND BRASS CAP "1941" N: 659377.1 - E: 588198.9</p> <p>E: FOUND BRASS CAP "1941" N: 659457.7 - E: 590794.9</p> <p>F: FOUND BRASS CAP "1941" N: 659466.8 - E: 593406.4</p> <p>G: FOUND BRASS CAP "1941" N: 659475.1 - E: 596017.9</p> <p>H: FOUND BRASS CAP "1941" N: 656886.5 - E: 595997.7</p> <p>I: FOUND BRASS CAP "1941" N: 654298.0 - E: 595977.3</p> <p>J: FOUND BRASS CAP "1941" N: 654266.7 - E: 593360.1</p> <p>K: FOUND BRASS CAP "1941" N: 654235.0 - E: 590741.9</p> <p>L: FOUND BRASS CAP "1941" N: 654169.8 - E: 588139.7</p> <p>M: FOUND BRASS CAP "1941" N: 656846.0 - E: 590769.0</p> | <p>¹⁷ OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</p> <p><i>Sarah Chapman</i> 12/3/2020 Signature Date</p> <p>Sarah Chapman Printed Name</p> <p>schapman@spurepllc.com E-mail Address</p> <p>¹⁸ SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</p> <p>10-28-2020 Date of Survey</p> <p>Signature and Seal of Professional Surveyor</p> <p>19680 Certificate Number</p> <p>PROF. ROBERT M. HOWETT NEW MEXICO 19680 PROFESSIONAL SURVEYOR</p> <p>LS20100592</p> |
|--|--|

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: SPUR ENERGY PARTNERS LLC **OGRID:** 328947 **Date:** 01 / 27 / 2022

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

| Well Name | API | ULSTR | Footages | Anticipated Oil BBL/D | Anticipated Gas MCF/D | Anticipated Produced Water BBL/D |
|------------------------|----------------|--------------|--------------------|-----------------------|-----------------------|----------------------------------|
| WELCH B 28 FEDERAL 1H | 30-015-PENDING | E-27-17S-28E | 1745' FNL 792' FWL | 264 BBL/D | 299 MCF/D | 1318 BBL/D |
| WELCH B 28 FEDERAL 10H | 30-015-PENDING | E-27-17S-28E | 1735' FNL 809' FWL | 339 BBL/D | 384 MCF/D | 1693 BBL/D |
| WELCH B 28 FEDERAL 50H | 30-015-PENDING | E-27-17S-28E | 1756' FNL 775' FWL | 283 BBL/D | 468 MCF/D | 1695 BBL/D |
| WELCH B 28 FEDERAL 70H | 30-015-PENDING | E-27-17S-28E | 1725' FNL 826' FWL | 283 BBL/D | 468 MCF/D | 1695 BBL/D |
| WELCH B 28 FEDERAL 90H | 30-015-PENDING | E-27-17S-28E | 1766' FNL 758' FWL | 283 BBL/D | 468 MCF/D | 1695 BBL/D |

IV. Central Delivery Point Name: _____ [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

| Well Name | API | Spud Date | TD Reached Date | Completion Commencement Date | Initial Flow Back Date | First Production Date |
|------------------------|----------------|------------|-----------------|------------------------------|------------------------|-----------------------|
| WELCH B 28 FEDERAL 1H | 30-015-PENDING | 08/29/2023 | 09/05/2023 | 10/11/2023 | 10/29/2023 | 10/29/2023 |
| WELCH B 28 FEDERAL 10H | 30-015-PENDING | 09/24/2023 | 10/01/2023 | 10/11/2023 | 10/29/2023 | 10/29/2023 |
| WELCH B 28 FEDERAL 50H | 30-015-PENDING | 09/15/2023 | 09/23/2023 | 10/11/2023 | 10/29/2023 | 10/29/2023 |
| WELCH B 28 FEDERAL 70H | 30-015-PENDING | 08/20/2023 | 08/28/2023 | 10/11/2023 | 10/29/2023 | 10/29/2023 |
| WELCH B 28 FEDERAL 90H | 30-015-PENDING | 09/06/2023 | 09/14/2023 | 10/11/2023 | 10/29/2023 | 10/29/2023 |

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan
EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

| Well | API | Anticipated Average Natural Gas Rate MCF/D | Anticipated Volume of Natural Gas for the First Year MCF |
|------|-----|--|--|
| | | | |
| | | | |

X. Natural Gas Gathering System (NGGS):

| Operator | System | ULSTR of Tie-in | Anticipated Gathering Start Date | Available Maximum Daily Capacity of System Segment Tie-in |
|----------|--------|-----------------|----------------------------------|---|
| | | | | |
| | | | | |

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

| | |
|--|-------------------------|
| Signature: | <i>Sarah Chapman</i> |
| Printed Name: | SARAH CHAPMAN |
| Title: | REGULATORY DIRECTOR |
| E-mail Address: | SCHAPMAN@SPURENERGY.COM |
| Date: | 01/27/2022 |
| Phone: | 832-930-8613 |
| OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form) | |
| Approved By: | |
| Title: | |
| Approval Date: | |
| Conditions of Approval: | |



Natural Gas Management Plan – Attachment

VI. Separation equipment will be sized by construction engineering staff based on anticipated daily production to ensure adequate capacity.

VII. Spur Energy Partners LLC (“Spur”) will take the following actions to comply with the regulations listed in 19.15.27.8:

- A. Spur will maximize the recovery of natural gas by minimizing waste, as defined by 19.15.2 NMAC, of natural gas through venting and flaring. Spur will ensure that our wells will be connected to a natural gas gathering system with sufficient capacity to transport natural gas.
- B. All drilling operations will be equipped with a rig flare at least 100 feet from the nearest surface hole location. Rig flare will be utilized to combust any natural gas that is brought to surface during normal operations. In the case of emergency, flaring volumes will be reported appropriately.
- C. During completion operations any natural gas brought to surface will be flared. Immediately following completion operations, wells will flow to permanent separation equipment. Produced natural gas from separation equipment will be sent to sales. If natural gas does not meet gathering pipeline specifications, Spur will flare for 60 days or until natural gas meets the pipeline specifications. Spur will ensure flare is properly sized and is equipped with an automatic igniter or continuous pilot. Gas samples will be taken twice per week and natural gas will be routed into a gathering system as soon as the pipeline specifications are met.
- D. Natural gas will not be flared with the exception of 19.15.27.8(D)(1-4). If there is no adequate takeaway for the separator gas, wells will be shut-in until that natural gas gathering system is available with exception of emergency or malfunction situations. Volumes will be reported appropriately.
- E. Spur will comply with performance standards pursuant to 19.15.27.8(E)(1-8). All equipment will be designed and sized to handle maximum pressures to minimize waste. Storage tanks constructed after May 25, 2021 will be equipped with an automatic gauging system that reduces venting of natural gas. Flare stacks installed or replaced after May 25, 2021 will be equipped with an automatic igniter or continuous pilot. Spur will conduct AVO inspections as described in 19.15.27.8(E)(5)(a) with frequencies specified in 19.15.27.8(E)(5)(b) and (c). All emergencies or malfunctions will be resolved as quickly and safely as possible to minimize waste.
- F. The volume of natural gas that is vented or flared as the result of an emergency or malfunction during drilling and/or completion operations will be estimated and reported accordingly. The volume of natural gas that is vented, flared or beneficially used during production operations, will be measured and reported accordingly. Spur will install equipment to measure the volume of natural gas flared from existing piping or a flowline piped from equipment such as high-pressure separators, heater treaters, or VRUs associated with a well or facility associated with a well authorized by an APD after May 25, 2021 that has an average daily production of less than 60,000 cubic feet of natural gas. If metering is not practicable due to circumstances such as low flow rate or low pressure venting or flaring, Spur will estimate the volume of flared or vented natural gas. Measuring equipment will conform to industry standards and will not be equipped with a manifold



that allows the diversion of natural gas around the metering element except for the sole purpose of inspecting and servicing equipment.

VIII. For maintenance activities involving production equipment and compression, venting be limited to the depressurization of the subject equipment to ensure safe working conditions. For maintenance of production equipment, the associated producing wells will be shut-in to eliminate venting. For maintenance of VRUs, all natural gas normally routed to the VRU will be routed to flare.

Spur Energy Partners LLC – Welch B 28 Federal 50H

1. Geologic Formations

| Formation | Depth | Lithology | Expected Fluids |
|------------------|-------|--------------------------|------------------|
| Quaternary | 0' | Dolomite, other: Caliche | Useable Water |
| Tansill | 395' | Limestone, Dolomite | None |
| Yates | 475' | Sandstone | Natural Gas, Oil |
| Seven Rivers | 735' | Sandstone, Dolomite | Natural Gas, Oil |
| Queen | 1300' | Sandstone, Dolomite | Natural Gas, Oil |
| Grayburg | 1715' | Limestone, Dolomite | Natural Gas, Oil |
| San Andres | 1995' | Limestone, Dolomite | Natural Gas, Oil |
| Lower San Andres | 2955' | Limestone, Dolomite | Natural Gas, Oil |
| Glorieta | 3425' | Siltstone, Dolomite | Natural Gas, Oil |
| Top Yeso | 3545' | Dolomite | Natural Gas, Oil |
| Base Yeso | 5525' | Dolomite | Natural Gas, Oil |

*H₂S, water flows, loss of circulation, abnormal pressures, etc.

2. Casing Program

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

Primary Plan:

| Hole Size (in) | Casing Interval | | Csg. Size (in) | Weight (lbs) | Grade | Conn. | SF | SF Burst | Body SF | Joint SF |
|-------------------------------|-----------------|---------|-------------------|-----------------|-------|-------|----------|----------|---------|----------|
| | From (ft) | To (ft) | | | | | Collapse | | Tension | Tension |
| 12.25 | 0 | 1200 | 9.625 | 36 | J-55 | BTC | 1.125 | 1.2 | 1.4 | 1.4 |
| 8.75 | 0 | 4400 | 7 | 32 | L-80 | BK-HT | 1.125 | 1.2 | 1.4 | 1.4 |
| 8.75 | 4400 | 9684 | 5.5 | 20 | L-80 | BK-HT | 1.125 | 1.2 | 1.4 | 1.4 |
| SF Values will meet or Exceed | | | | | | | | | | |

Spur Energy Partners LLC – Welch B 28 Federal 50H

| | Y or N |
|--|--------|
| Is casing new? If used, attach certification as required in Onshore Order #1 | Y |
| Does casing meet API specifications? If no, attach casing specification sheet. | Y |
| Is premium or uncommon casing planned? If yes attach casing specification sheet. | N |
| Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria). | Y |
| Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing? | Y |
| Is well located within Capitan Reef? | N |
| If yes, does production casing cement tie back a minimum of 50' above the Reef? | |
| Is well within the designated 4 string boundary. | |
| Is well located in SOPA but not in R-111-P? | N |
| If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing? | |
| Is well located in R-111-P and SOPA? | N |
| If yes, are the first three strings cemented to surface? | |
| Is 2 nd string set 100' to 600' below the base of salt? | |
| Is well located in high Cave/Karst? | N |
| If yes, are there two strings cemented to surface? | |
| (For 2 string wells) If yes, is there a contingency casing if lost circulation occurs? | |
| Is well located in critical Cave/Karst? | N |
| If yes, are there three strings cemented to surface? | |

3. Cementing Program**Primary Plan:**

| Casing String | Top (ft) | Bottom (ft) | % Excess |
|-------------------|----------|-------------|----------|
| Surface (Lead) | 0 | 950 | 100% |
| Surface (Tail) | 950 | 1200 | 165% |
| Production (Lead) | 0 | 3400 | 0% |
| Production (Tail) | 3400 | 9684 | 50% |

| Casing String | # Sks | Wt. (lb/gal) | Yld (ft ³ /sack) | H ₂ O (gal/sk) | 500# Comp. Strength (hours) | Slurry Description |
|-------------------|-------|-----------------|--------------------------------|------------------------------|--------------------------------------|----------------------------|
| Surface (Lead) | 270 | 12.2 | 2.31 | 13.48 | 8:12 | Clas C Premium Plus Cement |
| Surface (Tail) | 123 | 13.2 | 1.84 | 9.92 | 6:59 | Clas C Premium Plus Cement |
| Production (Lead) | 210 | 11.8 | 2.54 | 15.29 | N/A | Clas C Premium Plus Cement |
| Production (Tail) | 1234 | 13.2 | 1.81 | 9.81 | N/A | Clas C Premium Plus Cement |

Spur Energy Partners LLC – Welch B 28 Federal 50H

4. Pressure Control Equipment

| BOP installed and tested before drilling which hole? | Size? | Min. Required WP | Type | ✓ | Tested to: |
|--|-------|------------------|------------|---|-------------------------|
| 12.25" Hole | 11" | 5M | Annular | ✓ | 70% of working pressure |
| | | 5M | Blind Ram | ✓ | 250 psi / 5000 psi |
| | | | Pipe Ram | ✓ | |
| | | | Double Ram | | |
| | | | Other* | | |
| 8.75" Hole | 11" | 5M | Annular | ✓ | 70% of working pressure |
| | | 5M | Blind Ram | ✓ | 250 psi / 5000 psi |
| | | | Pipe Ram | ✓ | |
| | | | Double Ram | | |
| | | | Other* | | |

Spur Energy Partners LLC will be utilizing a 5M BOP

| Condition | Specify what type and where? |
|-------------------------------|------------------------------|
| BH Pressure at deepest TVD | 1893 psi |
| Abnormal Temperature | No |
| BH Temperature at deepest TVD | 113°F |

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

| | |
|---|---|
| | Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i. |
| Y | Are anchors required by manufacturer? |
| | A conventional wellhead system will be employed. The wellhead and connection to the BOPE will meet all API 6A requirements. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. See attached schematics. |

Spur Energy Partners LLC – Welch B 28 Federal 50H**5. BOP Break Testing Request**

Spur Energy Partners LLC requests permission to adjust the BOP break testing requirements as per the verbal agreement reached over the phone between SPUR/BLM on September 7, 2020. A separate sundry will be sent prior to spud that reflects the pad-based break testing plan.

BOP break test under the following conditions:

- After a full BOP test is conducted
- When skidding to drill the production section, where the surface casing point is shallower than the 3 Bone Spring or 10,000 TVD.
- When skidding to drill a production section that does not penetrate the 3rd Bone Spring or deeper.

If the kill line is broken prior to skid, four tests will be performed.

- 1) The void between the wellhead and the spool (this consists of two tests)
- 2) The spool between the kill lines and the choke manifold (this consists of two tests)

If the kill line is not broken prior to skid, two tests will be performed.

- 1) The void between the wellhead and the pipe rams

6. Mud Program

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times. The following is a general list of products: Barite, Bentonite, Gypsum, Lime, Soda Ash, Caustic Soda, Nut Plug, Cedar Fiber, Cotton Seed Hulls, Drilling Paper, Salt Water Clay, CACL2. Spur will use a closed mud system.

| Depth | | Type | Weight (ppg) | Viscosity | Water Loss |
|-----------|---------|-----------------|--------------|-----------|------------|
| From (ft) | To (ft) | | | | |
| 0 | 1200 | Water-Based Mud | 8.6-8.9 | 32-36 | N/C |
| 1200 | 9684 | Water-Based Mud | 8.6-8.9 | 32-36 | N/C |

| | |
|---|-----------------------------|
| What will be used to monitor the loss or gain of fluid? | PVT/PASON/Visual Monitoring |
|---|-----------------------------|

Spur Energy Partners LLC – Welch B 28 Federal 50H**7. Logging and Testing Procedures**

| Logging, Coring and Testing. | | |
|-------------------------------------|---|-----------------|
| Yes | Will run GR from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM. | |
| No | Logs are planned based on well control or offset log information. | |
| No | Drill stem test? If yes, explain | |
| No | Coring? If yes, explain | |
| Additional logs planned | | Interval |
| No | Resistivity | |
| No | Density | |
| No | CBL | |
| Yes | Mud log | ICP - TD |
| No | PEX | |

8. Drilling Conditions

Pump high viscosity sweeps as needed for hole cleaning. The mud system will be monitored visually/manually as well as with an electronic PVT. The necessary mud products for additional weight and fluid loss control will be on location at all times. Appropriately weighted mud will be used to isolate potential gas, oil, and water zones until such time as casing can be cemented into place for zonal isolation.

| | |
|--|--------------------------------|
| Hydrogen Sulfide (H ₂ S) monitors will be installed prior to drilling out the surface shoe. If H ₂ S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM. | |
| N | H ₂ S is present |
| Y | H ₂ S Plan attached |

Total estimated cuttings volume: 895 bbls.

Spur Energy Partners LLC – Welch B 28 Federal 50H**9. Other facets of operation**

| | Yes/No |
|--|---------------|
| Will more than one drilling rig be used for drilling operations? If yes, describe. Spur Energy Partners LLC. requests the option to contract a Surface Rig to drill, set surface casing, and cement for this well. If the timing between rigs is such that Spur Energy Partners LLC. would not be able to preset surface, the Primary Rig will MIRU and drill the well in its entirety per the APD. Please see the attached document for information on the spudder rig. | Yes |

Attachments

- ☒ Directional Plan
☒ H2S Contingency Plan
☒ Akita 57 Attachments
☒ BOP Schematics
☒ Spudder Rig Attachments

10. Company Personnel

| Name | Title | Office Phone | Mobile Phone |
|--------------------|----------------------------------|---------------------|---------------------|
| Christopher Hollis | Drilling Manager | 832-930-8629 | 713-380-7754 |
| Johnny Nabors | Senior Vice President Operations | 832-930-8502 | 281-904-8811 |



Spur Energy Partners, LLC

Eddy County, NM (NAD 83 - NME)

Welch B 28 Fed

#50H

Wellbore #1

Plan: PERMIT

Standard Planning Report

20 November, 2020





Planning Report



| | | | |
|------------------|--------------------------------|-------------------------------------|-------------------------|
| Database: | WBDS_SQL_2 | Local Co-ordinate Reference: | Well #50H |
| Company: | Spur Energy Partners, LLC | TVD Reference: | RKB = 20' @ 3680.00usft |
| Project: | Eddy County, NM (NAD 83 - NME) | MD Reference: | RKB = 20' @ 3680.00usft |
| Site: | Welch B 28 Fed | North Reference: | Grid |
| Well: | #50H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | PERMIT | | |

| | | | |
|--------------------|--------------------------------|----------------------|----------------|
| Project | Eddy County, NM (NAD 83 - NME) | | |
| Map System: | US State Plane 1983 | System Datum: | Mean Sea Level |
| Geo Datum: | North American Datum 1983 | | |
| Map Zone: | New Mexico Eastern Zone | | |

| | | | | | |
|-----------------------|-----------|----------------|-----------------|-------------------|--------------|
| Site | | Welch B 28 Fed | | | |
| Site Position: | | Northing: | 657,715.70 usft | Latitude: | 32.8079833 |
| From: | Map | Easting: | 591,569.60 usft | Longitude: | -104.1698382 |
| Position Uncertainty: | 0.00 usft | Slot Radius: | 13.200 in | Grid Convergence: | 0.089 |

| | | | | | | |
|----------------------|-------|-------------|---------------------|-----------------|---------------|---------------|
| Well | #50H | | | | | |
| Well Position | +N/-S | -10.50 usft | Northing: | 657,705.20 usft | Latitude: | 32.8079545 |
| | +E/-W | -17.10 usft | Easting: | 591,552.50 usft | Longitude: | -104.1698939 |
| Position Uncertainty | | 0.00 usft | Wellhead Elevation: | | Ground Level: | 3,660.00 usft |

| | | | | | |
|------------------|-------------------|--------------------|------------------------|----------------------|----------------------------|
| Wellbore | Wellbore #1 | | | | |
| Magnetics | Model Name | Sample Date | Declination (°) | Dip Angle (°) | Field Strength (nT) |
| | IGRF2020 | 11/19/20 | 6.935 | 60.360 | 47,834.03335486 |

| | | | | | |
|--------------------------|--------------------------------|---------------------|---------------------|----------------------|------|
| Design | PERMIT | | | | |
| Audit Notes: | | | | | |
| Version: | | Phase: | PLAN | Tie On Depth: | 0.00 |
| Vertical Section: | Depth From (TVD) (usft) | +N/-S (usft) | +E/-W (usft) | Direction (°) | |
| | 0.00 | 0.00 | 0.00 | 268.24 | |

| | | | | | |
|---------------------------------|------------------------|--------------------------|----------------------|-----------------------|--|
| Plan Survey Tool Program | Date | 11/19/20 | | | |
| Depth From (usft) | Depth To (usft) | Survey (Wellbore) | Tool Name | Remarks | |
| 1 | 0.00 | 9,684.48 | PERMIT (Wellbore #1) | MWD+IGRF | |
| | | | | OWSG MWD + IGRF or WM | |

| | | | | | | | | | | |
|------------------------------|------------------------|--------------------|------------------------------|---------------------|---------------------|------------------------------|-----------------------------|----------------------------|----------------|------------------|
| Plan Sections | | | | | | | | | | |
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) | TFO (°) | Target |
| 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.000 | |
| 300.00 | 0.00 | 0.00 | 300.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.000 | |
| 788.59 | 9.77 | 171.61 | 786.23 | -41.12 | 6.06 | 2.00 | 2.00 | 0.00 | 171.611 | |
| 3,103.78 | 9.77 | 171.61 | 3,067.82 | -429.86 | 63.40 | 0.00 | 0.00 | 0.00 | 0.000 | |
| 4,130.27 | 60.00 | 268.24 | 3,913.27 | -540.58 | -415.16 | 6.00 | 4.89 | 9.41 | 102.032 | |
| 4,330.27 | 60.00 | 268.24 | 4,013.27 | -545.91 | -588.29 | 0.00 | 0.00 | 0.00 | 0.000 | |
| 4,635.94 | 90.57 | 268.24 | 4,090.00 | -554.90 | -880.30 | 10.00 | 10.00 | 0.00 | 0.000 | WELCH B 28 FED ; |
| 9,634.45 | 90.57 | 268.24 | 4,040.50 | -708.66 | -5,876.20 | 0.00 | 0.00 | 0.00 | 0.000 | WELCH B 28 FED ; |
| 9,684.48 | 90.57 | 268.24 | 4,040.00 | -710.20 | -5,926.20 | 0.00 | 0.00 | 0.00 | 0.000 | WELCH B 28 FED ; |



Planning Report



| | | | |
|------------------|--------------------------------|-------------------------------------|-------------------------|
| Database: | WBDS_SQL_2 | Local Co-ordinate Reference: | Well #50H |
| Company: | Spur Energy Partners, LLC | TVD Reference: | RKB = 20' @ 3680.00usft |
| Project: | Eddy County, NM (NAD 83 - NME) | MD Reference: | RKB = 20' @ 3680.00usft |
| Site: | Welch B 28 Fed | North Reference: | Grid |
| Well: | #50H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | PERMIT | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-----------------------|----------------------|---------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
| 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| 100.00 | 0.00 | 0.00 | 100.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| 200.00 | 0.00 | 0.00 | 200.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| 300.00 | 0.00 | 0.00 | 300.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| 400.00 | 2.00 | 171.61 | 399.98 | -1.73 | 0.25 | -0.20 | 2.00 | 2.00 | 0.00 |
| 500.00 | 4.00 | 171.61 | 499.84 | -6.90 | 1.02 | -0.81 | 2.00 | 2.00 | 0.00 |
| 600.00 | 6.00 | 171.61 | 599.45 | -15.53 | 2.29 | -1.81 | 2.00 | 2.00 | 0.00 |
| 700.00 | 8.00 | 171.61 | 698.70 | -27.58 | 4.07 | -3.22 | 2.00 | 2.00 | 0.00 |
| 788.59 | 9.77 | 171.61 | 786.23 | -41.12 | 6.06 | -4.80 | 2.00 | 2.00 | 0.00 |
| 800.00 | 9.77 | 171.61 | 797.47 | -43.03 | 6.35 | -5.02 | 0.00 | 0.00 | 0.00 |
| 900.00 | 9.77 | 171.61 | 896.02 | -59.83 | 8.82 | -6.98 | 0.00 | 0.00 | 0.00 |
| 1,000.00 | 9.77 | 171.61 | 994.57 | -76.62 | 11.30 | -8.94 | 0.00 | 0.00 | 0.00 |
| 1,100.00 | 9.77 | 171.61 | 1,093.12 | -93.41 | 13.78 | -10.90 | 0.00 | 0.00 | 0.00 |
| 1,200.00 | 9.77 | 171.61 | 1,191.67 | -110.20 | 16.25 | -12.86 | 0.00 | 0.00 | 0.00 |
| 1,300.00 | 9.77 | 171.61 | 1,290.22 | -126.99 | 18.73 | -14.82 | 0.00 | 0.00 | 0.00 |
| 1,400.00 | 9.77 | 171.61 | 1,388.76 | -143.78 | 21.20 | -16.78 | 0.00 | 0.00 | 0.00 |
| 1,500.00 | 9.77 | 171.61 | 1,487.31 | -160.57 | 23.68 | -18.74 | 0.00 | 0.00 | 0.00 |
| 1,600.00 | 9.77 | 171.61 | 1,585.86 | -177.36 | 26.16 | -20.70 | 0.00 | 0.00 | 0.00 |
| 1,700.00 | 9.77 | 171.61 | 1,684.41 | -194.15 | 28.63 | -22.66 | 0.00 | 0.00 | 0.00 |
| 1,800.00 | 9.77 | 171.61 | 1,782.96 | -210.94 | 31.11 | -24.62 | 0.00 | 0.00 | 0.00 |
| 1,900.00 | 9.77 | 171.61 | 1,881.51 | -227.73 | 33.59 | -26.58 | 0.00 | 0.00 | 0.00 |
| 2,000.00 | 9.77 | 171.61 | 1,980.06 | -244.53 | 36.06 | -28.54 | 0.00 | 0.00 | 0.00 |
| 2,100.00 | 9.77 | 171.61 | 2,078.61 | -261.32 | 38.54 | -30.49 | 0.00 | 0.00 | 0.00 |
| 2,200.00 | 9.77 | 171.61 | 2,177.16 | -278.11 | 41.01 | -32.45 | 0.00 | 0.00 | 0.00 |
| 2,300.00 | 9.77 | 171.61 | 2,275.71 | -294.90 | 43.49 | -34.41 | 0.00 | 0.00 | 0.00 |
| 2,400.00 | 9.77 | 171.61 | 2,374.26 | -311.69 | 45.97 | -36.37 | 0.00 | 0.00 | 0.00 |
| 2,500.00 | 9.77 | 171.61 | 2,472.80 | -328.48 | 48.44 | -38.33 | 0.00 | 0.00 | 0.00 |
| 2,600.00 | 9.77 | 171.61 | 2,571.35 | -345.27 | 50.92 | -40.29 | 0.00 | 0.00 | 0.00 |
| 2,700.00 | 9.77 | 171.61 | 2,669.90 | -362.06 | 53.40 | -42.25 | 0.00 | 0.00 | 0.00 |
| 2,800.00 | 9.77 | 171.61 | 2,768.45 | -378.85 | 55.87 | -44.21 | 0.00 | 0.00 | 0.00 |
| 2,900.00 | 9.77 | 171.61 | 2,867.00 | -395.64 | 58.35 | -46.17 | 0.00 | 0.00 | 0.00 |
| 3,000.00 | 9.77 | 171.61 | 2,965.55 | -412.43 | 60.83 | -48.13 | 0.00 | 0.00 | 0.00 |
| 3,103.78 | 9.77 | 171.61 | 3,067.82 | -429.86 | 63.40 | -50.16 | 0.00 | 0.00 | 0.00 |
| 3,150.00 | 9.58 | 188.13 | 3,113.40 | -437.55 | 63.42 | -49.96 | 6.00 | -0.41 | 35.73 |
| 3,200.00 | 10.25 | 205.19 | 3,162.66 | -445.70 | 60.94 | -47.22 | 6.00 | 1.33 | 34.12 |
| 3,250.00 | 11.66 | 219.17 | 3,211.76 | -453.64 | 55.86 | -41.90 | 6.00 | 2.83 | 27.96 |
| 3,300.00 | 13.60 | 229.71 | 3,260.55 | -461.36 | 48.18 | -33.99 | 6.00 | 3.87 | 21.07 |
| 3,350.00 | 15.86 | 237.48 | 3,308.91 | -468.83 | 37.93 | -23.52 | 6.00 | 4.53 | 15.54 |
| 3,400.00 | 18.33 | 243.28 | 3,356.70 | -476.04 | 25.15 | -10.52 | 6.00 | 4.94 | 11.60 |
| 3,450.00 | 20.94 | 247.71 | 3,403.79 | -482.97 | 9.86 | 4.98 | 6.00 | 5.21 | 8.87 |
| 3,500.00 | 23.63 | 251.19 | 3,450.06 | -489.59 | -7.90 | 22.93 | 6.00 | 5.39 | 6.95 |
| 3,550.00 | 26.39 | 253.98 | 3,495.36 | -495.89 | -28.07 | 43.29 | 6.00 | 5.52 | 5.59 |
| 3,600.00 | 29.19 | 256.28 | 3,539.59 | -501.85 | -50.61 | 66.00 | 6.00 | 5.61 | 4.59 |
| 3,650.00 | 32.03 | 258.21 | 3,582.62 | -507.45 | -75.44 | 90.99 | 6.00 | 5.67 | 3.85 |
| 3,700.00 | 34.89 | 259.85 | 3,624.33 | -512.68 | -102.50 | 118.20 | 6.00 | 5.72 | 3.28 |
| 3,750.00 | 37.77 | 261.27 | 3,664.61 | -517.53 | -131.72 | 147.55 | 6.00 | 5.76 | 2.84 |
| 3,800.00 | 40.66 | 262.51 | 3,703.34 | -521.98 | -163.01 | 178.97 | 6.00 | 5.79 | 2.49 |
| 3,850.00 | 43.57 | 263.62 | 3,740.43 | -526.02 | -196.29 | 212.36 | 6.00 | 5.81 | 2.22 |
| 3,900.00 | 46.49 | 264.62 | 3,775.76 | -529.63 | -231.48 | 247.64 | 6.00 | 5.83 | 1.99 |
| 3,950.00 | 49.41 | 265.52 | 3,809.25 | -532.82 | -268.46 | 284.70 | 6.00 | 5.85 | 1.81 |
| 4,000.00 | 52.34 | 266.35 | 3,840.79 | -535.56 | -307.15 | 323.46 | 6.00 | 5.86 | 1.66 |
| 4,050.00 | 55.28 | 267.12 | 3,870.31 | -537.85 | -347.44 | 363.79 | 6.00 | 5.87 | 1.53 |
| 4,100.00 | 58.22 | 267.83 | 3,897.73 | -539.69 | -389.20 | 405.60 | 6.00 | 5.88 | 1.42 |
| 4,130.27 | 60.00 | 268.24 | 3,913.27 | -540.58 | -415.16 | 431.57 | 6.00 | 5.89 | 1.35 |



Planning Report



| | | | |
|------------------|--------------------------------|-------------------------------------|-------------------------|
| Database: | WBDS_SQL_2 | Local Co-ordinate Reference: | Well #50H |
| Company: | Spur Energy Partners, LLC | TVD Reference: | RKB = 20' @ 3680.00usft |
| Project: | Eddy County, NM (NAD 83 - NME) | MD Reference: | RKB = 20' @ 3680.00usft |
| Site: | Welch B 28 Fed | North Reference: | Grid |
| Well: | #50H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | PERMIT | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-----------------------|----------------------|---------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
| 4,200.00 | 60.00 | 268.24 | 3,948.13 | -542.44 | -475.52 | 491.96 | 0.00 | 0.00 | 0.00 |
| 4,300.00 | 60.00 | 268.24 | 3,998.13 | -545.11 | -562.08 | 578.56 | 0.00 | 0.00 | 0.00 |
| 4,330.27 | 60.00 | 268.24 | 4,013.27 | -545.91 | -588.29 | 604.77 | 0.00 | 0.00 | 0.00 |
| 4,350.00 | 61.97 | 268.24 | 4,022.84 | -546.44 | -605.53 | 622.03 | 10.00 | 10.00 | 0.00 |
| 4,400.00 | 66.97 | 268.24 | 4,044.38 | -547.83 | -650.61 | 667.13 | 10.00 | 10.00 | 0.00 |
| 4,450.00 | 71.97 | 268.24 | 4,061.90 | -549.27 | -697.40 | 713.94 | 10.00 | 10.00 | 0.00 |
| 4,500.00 | 76.97 | 268.24 | 4,075.28 | -550.75 | -745.54 | 762.10 | 10.00 | 10.00 | 0.00 |
| 4,550.00 | 81.97 | 268.24 | 4,084.41 | -552.26 | -794.66 | 811.25 | 10.00 | 10.00 | 0.00 |
| 4,600.00 | 86.97 | 268.24 | 4,089.23 | -553.79 | -844.39 | 861.00 | 10.00 | 10.00 | 0.00 |
| 4,635.94 | 90.57 | 268.24 | 4,090.00 | -554.90 | -880.30 | 896.93 | 10.00 | 10.00 | 0.00 |
| 4,700.00 | 90.57 | 268.24 | 4,089.37 | -556.87 | -944.32 | 960.98 | 0.00 | 0.00 | 0.00 |
| 4,800.00 | 90.57 | 268.24 | 4,088.38 | -559.95 | -1,044.27 | 1,060.98 | 0.00 | 0.00 | 0.00 |
| 4,900.00 | 90.57 | 268.24 | 4,087.38 | -563.02 | -1,144.22 | 1,160.97 | 0.00 | 0.00 | 0.00 |
| 5,000.00 | 90.57 | 268.24 | 4,086.39 | -566.10 | -1,244.17 | 1,260.97 | 0.00 | 0.00 | 0.00 |
| 5,100.00 | 90.57 | 268.24 | 4,085.40 | -569.18 | -1,344.11 | 1,360.96 | 0.00 | 0.00 | 0.00 |
| 5,200.00 | 90.57 | 268.24 | 4,084.41 | -572.25 | -1,444.06 | 1,460.96 | 0.00 | 0.00 | 0.00 |
| 5,300.00 | 90.57 | 268.24 | 4,083.42 | -575.33 | -1,544.01 | 1,560.95 | 0.00 | 0.00 | 0.00 |
| 5,400.00 | 90.57 | 268.24 | 4,082.43 | -578.40 | -1,643.96 | 1,660.95 | 0.00 | 0.00 | 0.00 |
| 5,500.00 | 90.57 | 268.24 | 4,081.44 | -581.48 | -1,743.91 | 1,760.94 | 0.00 | 0.00 | 0.00 |
| 5,600.00 | 90.57 | 268.24 | 4,080.45 | -584.56 | -1,843.85 | 1,860.94 | 0.00 | 0.00 | 0.00 |
| 5,700.00 | 90.57 | 268.24 | 4,079.46 | -587.63 | -1,943.80 | 1,960.93 | 0.00 | 0.00 | 0.00 |
| 5,800.00 | 90.57 | 268.24 | 4,078.47 | -590.71 | -2,043.75 | 2,060.93 | 0.00 | 0.00 | 0.00 |
| 5,900.00 | 90.57 | 268.24 | 4,077.48 | -593.78 | -2,143.70 | 2,160.92 | 0.00 | 0.00 | 0.00 |
| 6,000.00 | 90.57 | 268.24 | 4,076.49 | -596.86 | -2,243.64 | 2,260.92 | 0.00 | 0.00 | 0.00 |
| 6,100.00 | 90.57 | 268.24 | 4,075.50 | -599.94 | -2,343.59 | 2,360.91 | 0.00 | 0.00 | 0.00 |
| 6,200.00 | 90.57 | 268.24 | 4,074.51 | -603.01 | -2,443.54 | 2,460.91 | 0.00 | 0.00 | 0.00 |
| 6,300.00 | 90.57 | 268.24 | 4,073.52 | -606.09 | -2,543.49 | 2,560.90 | 0.00 | 0.00 | 0.00 |
| 6,400.00 | 90.57 | 268.24 | 4,072.53 | -609.16 | -2,643.44 | 2,660.90 | 0.00 | 0.00 | 0.00 |
| 6,500.00 | 90.57 | 268.24 | 4,071.54 | -612.24 | -2,743.38 | 2,760.89 | 0.00 | 0.00 | 0.00 |
| 6,600.00 | 90.57 | 268.24 | 4,070.55 | -615.32 | -2,843.33 | 2,860.89 | 0.00 | 0.00 | 0.00 |
| 6,700.00 | 90.57 | 268.24 | 4,069.56 | -618.39 | -2,943.28 | 2,960.88 | 0.00 | 0.00 | 0.00 |
| 6,800.00 | 90.57 | 268.24 | 4,068.57 | -621.47 | -3,043.23 | 3,060.88 | 0.00 | 0.00 | 0.00 |
| 6,900.00 | 90.57 | 268.24 | 4,067.58 | -624.55 | -3,143.17 | 3,160.87 | 0.00 | 0.00 | 0.00 |
| 7,000.00 | 90.57 | 268.24 | 4,066.59 | -627.62 | -3,243.12 | 3,260.87 | 0.00 | 0.00 | 0.00 |
| 7,100.00 | 90.57 | 268.24 | 4,065.60 | -630.70 | -3,343.07 | 3,360.86 | 0.00 | 0.00 | 0.00 |
| 7,200.00 | 90.57 | 268.24 | 4,064.61 | -633.77 | -3,443.02 | 3,460.86 | 0.00 | 0.00 | 0.00 |
| 7,300.00 | 90.57 | 268.24 | 4,063.62 | -636.85 | -3,542.97 | 3,560.85 | 0.00 | 0.00 | 0.00 |
| 7,400.00 | 90.57 | 268.24 | 4,062.63 | -639.93 | -3,642.91 | 3,660.85 | 0.00 | 0.00 | 0.00 |
| 7,500.00 | 90.57 | 268.24 | 4,061.63 | -643.00 | -3,742.86 | 3,760.84 | 0.00 | 0.00 | 0.00 |
| 7,600.00 | 90.57 | 268.24 | 4,060.64 | -646.08 | -3,842.81 | 3,860.84 | 0.00 | 0.00 | 0.00 |
| 7,700.00 | 90.57 | 268.24 | 4,059.65 | -649.15 | -3,942.76 | 3,960.83 | 0.00 | 0.00 | 0.00 |
| 7,800.00 | 90.57 | 268.24 | 4,058.66 | -652.23 | -4,042.70 | 4,060.83 | 0.00 | 0.00 | 0.00 |
| 7,900.00 | 90.57 | 268.24 | 4,057.67 | -655.31 | -4,142.65 | 4,160.82 | 0.00 | 0.00 | 0.00 |
| 8,000.00 | 90.57 | 268.24 | 4,056.68 | -658.38 | -4,242.60 | 4,260.82 | 0.00 | 0.00 | 0.00 |
| 8,100.00 | 90.57 | 268.24 | 4,055.69 | -661.46 | -4,342.55 | 4,360.81 | 0.00 | 0.00 | 0.00 |
| 8,200.00 | 90.57 | 268.24 | 4,054.70 | -664.54 | -4,442.49 | 4,460.81 | 0.00 | 0.00 | 0.00 |
| 8,300.00 | 90.57 | 268.24 | 4,053.71 | -667.61 | -4,542.44 | 4,560.80 | 0.00 | 0.00 | 0.00 |
| 8,400.00 | 90.57 | 268.24 | 4,052.72 | -670.69 | -4,642.39 | 4,660.80 | 0.00 | 0.00 | 0.00 |
| 8,500.00 | 90.57 | 268.24 | 4,051.73 | -673.76 | -4,742.34 | 4,760.79 | 0.00 | 0.00 | 0.00 |
| 8,600.00 | 90.57 | 268.24 | 4,050.74 | -676.84 | -4,842.29 | 4,860.79 | 0.00 | 0.00 | 0.00 |
| 8,700.00 | 90.57 | 268.24 | 4,049.75 | -679.92 | -4,942.23 | 4,960.78 | 0.00 | 0.00 | 0.00 |
| 8,800.00 | 90.57 | 268.24 | 4,048.76 | -682.99 | -5,042.18 | 5,060.78 | 0.00 | 0.00 | 0.00 |
| 8,900.00 | 90.57 | 268.24 | 4,047.77 | -686.07 | -5,142.13 | 5,160.77 | 0.00 | 0.00 | 0.00 |
| 9,000.00 | 90.57 | 268.24 | 4,046.78 | -689.14 | -5,242.08 | 5,260.77 | 0.00 | 0.00 | 0.00 |



Planning Report



| | | | |
|------------------|--------------------------------|-------------------------------------|-------------------------|
| Database: | WBDS_SQL_2 | Local Co-ordinate Reference: | Well #50H |
| Company: | Spur Energy Partners, LLC | TVD Reference: | RKB = 20' @ 3680.00usft |
| Project: | Eddy County, NM (NAD 83 - NME) | MD Reference: | RKB = 20' @ 3680.00usft |
| Site: | Welch B 28 Fed | North Reference: | Grid |
| Well: | #50H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | PERMIT | | |

| Planned Survey | | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-----------------------|----------------------|---------------------|--|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) | |
| 9,100.00 | 90.57 | 268.24 | 4,045.79 | -692.22 | -5,342.02 | 5,360.76 | 0.00 | 0.00 | 0.00 | |
| 9,200.00 | 90.57 | 268.24 | 4,044.80 | -695.30 | -5,441.97 | 5,460.76 | 0.00 | 0.00 | 0.00 | |
| 9,300.00 | 90.57 | 268.24 | 4,043.81 | -698.37 | -5,541.92 | 5,560.76 | 0.00 | 0.00 | 0.00 | |
| 9,400.00 | 90.57 | 268.24 | 4,042.82 | -701.45 | -5,641.87 | 5,660.75 | 0.00 | 0.00 | 0.00 | |
| 9,500.00 | 90.57 | 268.24 | 4,041.83 | -704.53 | -5,741.82 | 5,760.75 | 0.00 | 0.00 | 0.00 | |
| 9,600.00 | 90.57 | 268.24 | 4,040.84 | -707.60 | -5,841.76 | 5,860.74 | 0.00 | 0.00 | 0.00 | |
| 9,634.45 | 90.57 | 268.24 | 4,040.50 | -708.66 | -5,876.20 | 5,895.19 | 0.00 | 0.00 | 0.00 | |
| 9,684.48 | 90.57 | 268.24 | 4,040.00 | -710.20 | -5,926.20 | 5,945.22 | 0.00 | 0.00 | 0.00 | |

| Design Targets | | | | | | | | | | |
|--|---------------|--------------|------------|--------------|--------------|-----------------|----------------|------------|--------------|--|
| Target Name - hit/miss target - Shape | Dip Angle (°) | Dip Dir. (°) | TVD (usft) | +N/-S (usft) | +E/-W (usft) | Northing (usft) | Easting (usft) | Latitude | Longitude | |
| WELCH B 28 FED #5 - plan hits target center - Point | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 657,705.20 | 591,552.50 | 32.8079545 | -104.1698939 | |
| WELCH B 28 FED #5 - plan hits target center - Point | 0.00 | 0.00 | 3,067.82 | -429.86 | 63.40 | 657,275.35 | 591,615.90 | 32.8067727 | -104.1696897 | |
| WELCH B 28 FED #5 - plan hits target center - Point | 0.00 | 0.00 | 4,040.00 | -710.20 | -5,926.20 | 656,995.00 | 585,626.30 | 32.8060261 | -104.1891855 | |
| WELCH B 28 FED #5 - plan misses target center by 0.06usft at 9634.45usft MD (4040.50 TVD, -708.66 N, -5876.20 E) - Point | 0.00 | 0.00 | 4,040.50 | -708.60 | -5,876.20 | 656,996.60 | 585,676.30 | 32.8060303 | -104.1890228 | |
| WELCH B 28 FED #5 - plan hits target center - Point | 0.00 | 0.00 | 4,090.00 | -554.90 | -880.30 | 657,150.30 | 590,672.20 | 32.8064330 | -104.1727618 | |




Company: Spur Energy Partners, LLC
Project: Eddy County, NM (NAD 83 - NME)
Site: Welch B 28 Fed
Well: #50H
Wellbore: Wellbore #1
Rig:
Design: PERMIT / 12:00, November 20 2020

| WELL DETAILS: #50H | | | | | | | | |
|-------------------------|---------|-----------|-----------|------------|--------------|----------|-------|---------|
| RKB = 20' @ 3680.00usft | | | | | | | | |
| 3660.00 | | | | | | | | |
| +N/-S | +E/-W | Northing | Easting | Latitude | Longitude | | | |
| 0.00 | 0.00 | 657705.20 | 591552.50 | 32.8079545 | -104.1698939 | | | |
| SECTION DETAILS | | | | | | | | |
| Sec | MD | Inc | Azi | TVD | +N/-S | +E/-W | Dleg | VSect |
| 1 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| 2 | 300.00 | 0.00 | 0.00 | 300.00 | 0.00 | 0.00 | 0.00 | 0.00 |
| 3 | 788.59 | 9.77 | 171.61 | 786.22 | -41.12 | 6.06 | 2.00 | -4.80 |
| 4 | 3103.78 | 9.77 | 171.61 | 3067.82 | -429.86 | 63.40 | 0.00 | -50.16 |
| 5 | 4130.27 | 60.00 | 268.24 | 3913.27 | -540.58 | -415.16 | 6.00 | 431.57 |
| 6 | 4330.27 | 60.00 | 268.24 | 4013.27 | -545.91 | -588.29 | 0.00 | 604.77 |
| 7 | 4635.94 | 90.57 | 268.24 | 4090.00 | -554.90 | -880.30 | 10.00 | 896.93 |
| 8 | 9634.45 | 90.57 | 268.24 | 4040.50 | -708.66 | -5876.20 | 0.00 | 5895.19 |
| 9 | 9684.48 | 90.57 | 268.24 | 4040.00 | -710.20 | -5926.20 | 0.00 | 5945.22 |

PROJECT DETAILS: Eddy County, NM (NAD 83 - NME)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level

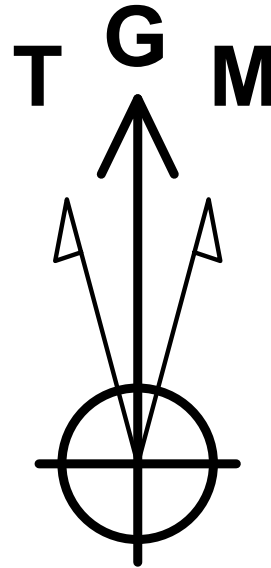


Azimuths to Grid North
True North: -0.09°
Magnetic North: 6.85°




Magnetic Field
Strength: 47834.03nT
Dip Angle: 60.36°
Date: 11/19/2020
Model: IGRF2020

CORRECTION REFERENCE DATA:

To convert a Magnetic Direction to a Grid Direction, Add 6.847°
To convert a True Direction to a Grid Direction, Subtract 0.089°
To convert a Magnetic Direction to a True Direction, Add 6.935° East
Magnetic Declination: 6.935°
Grid Convergence: 0.089° West
Magnetic Dip Angle: 60.360°
Magnetic Field Strength: 47834.03335486nT

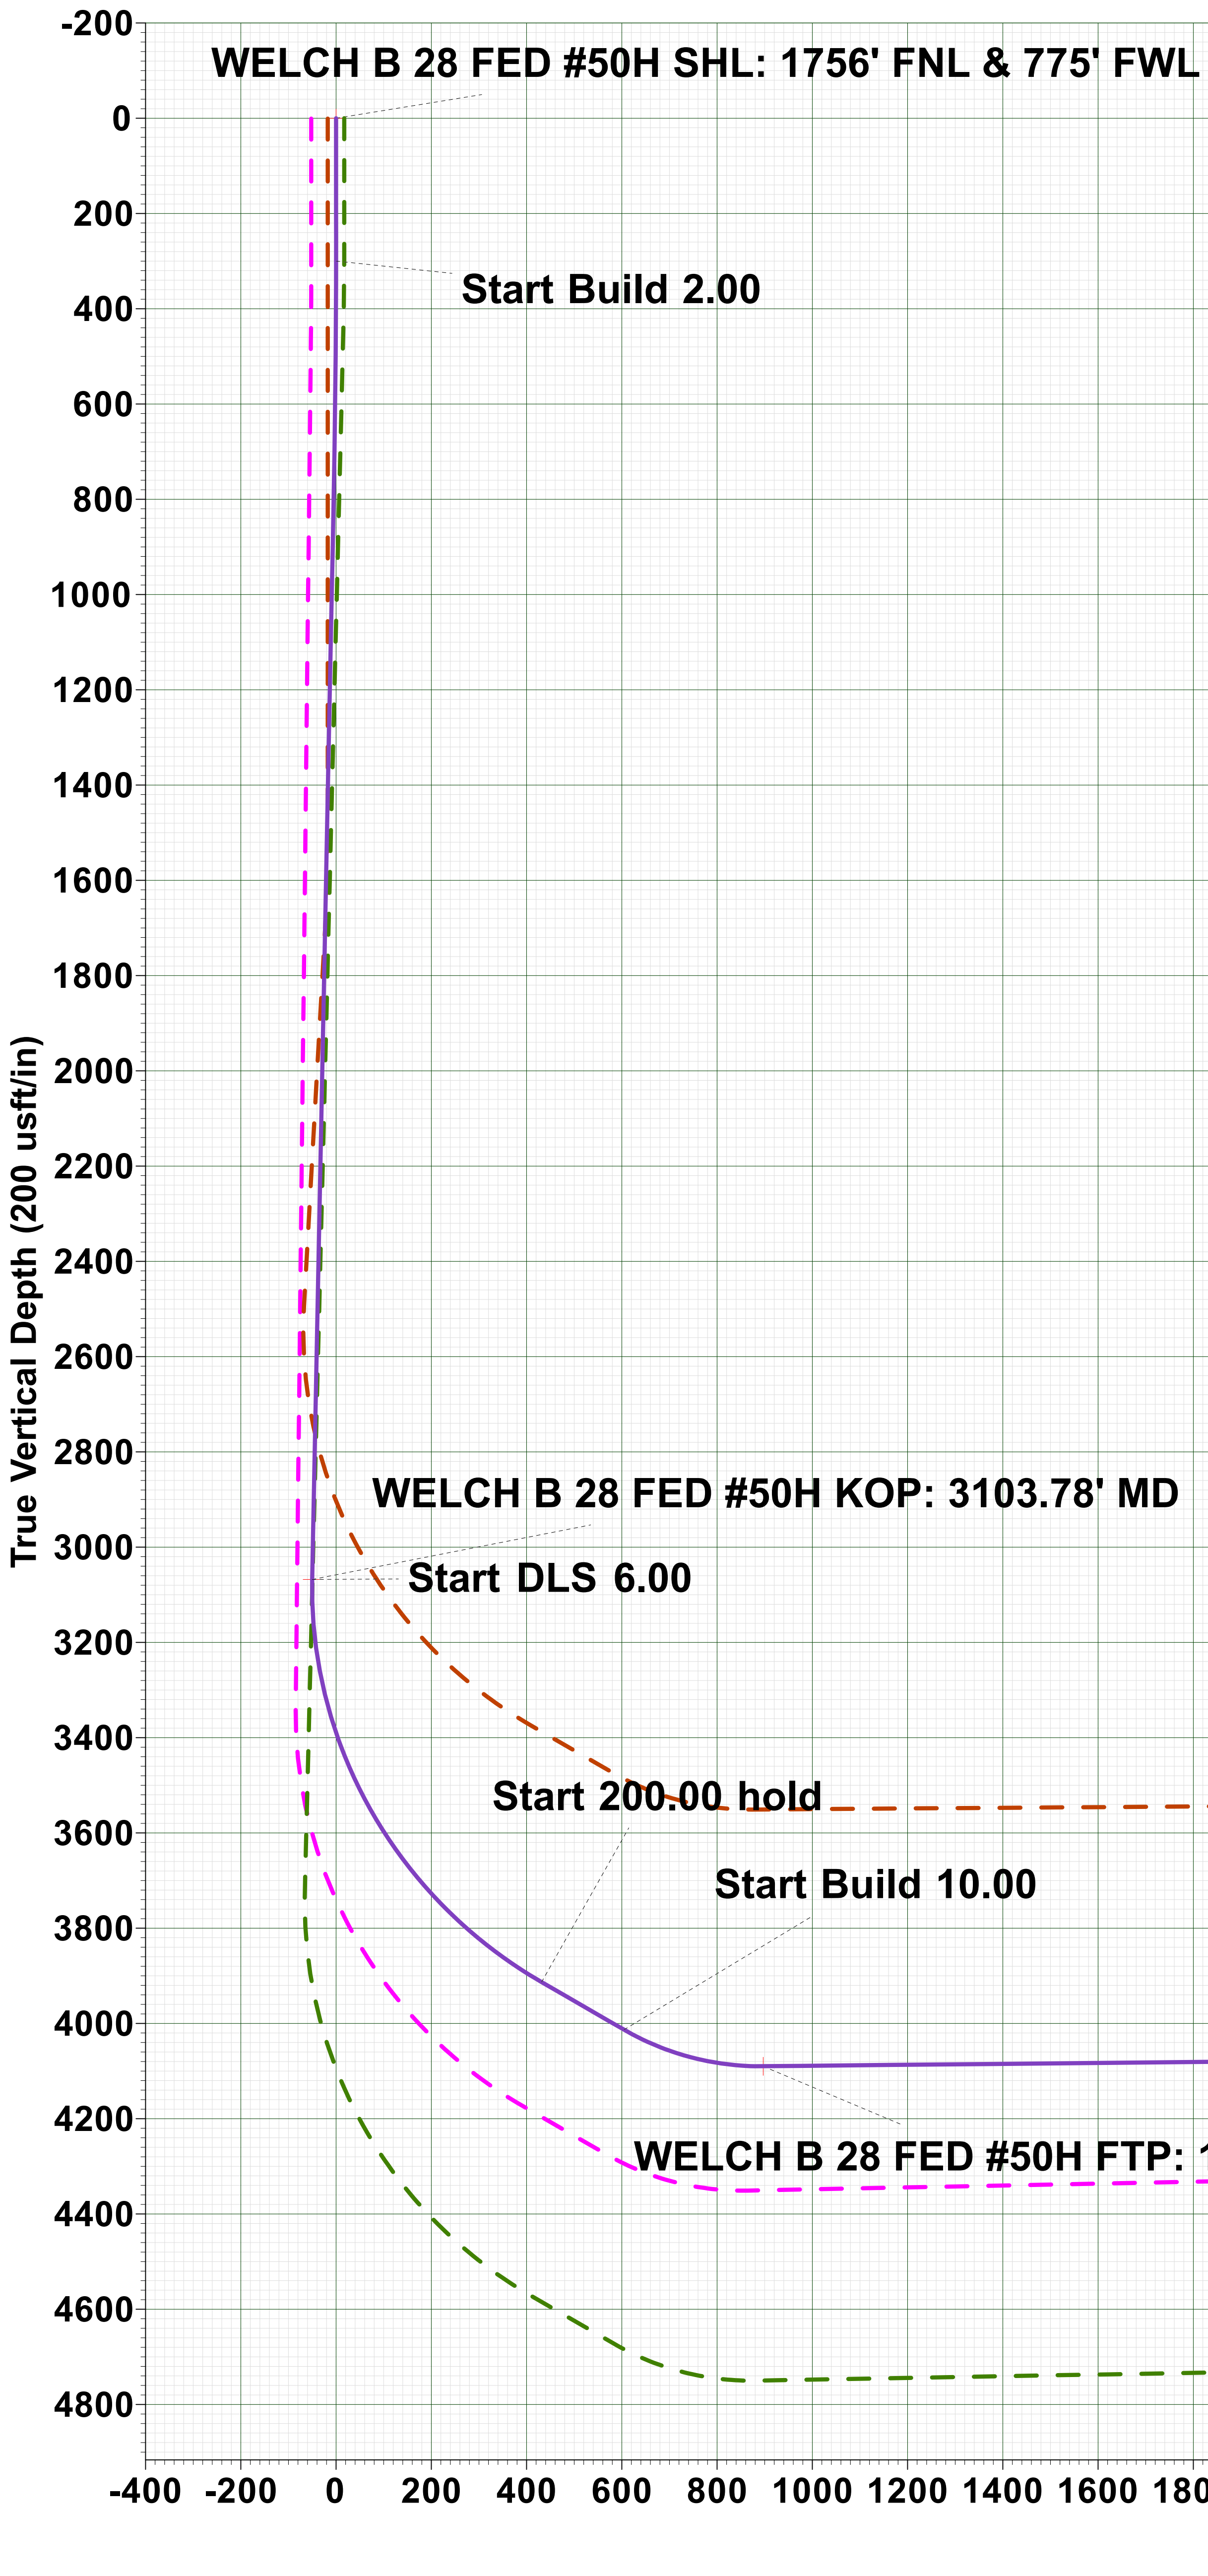

Vertical Section at 268.24° (200 usft/in)

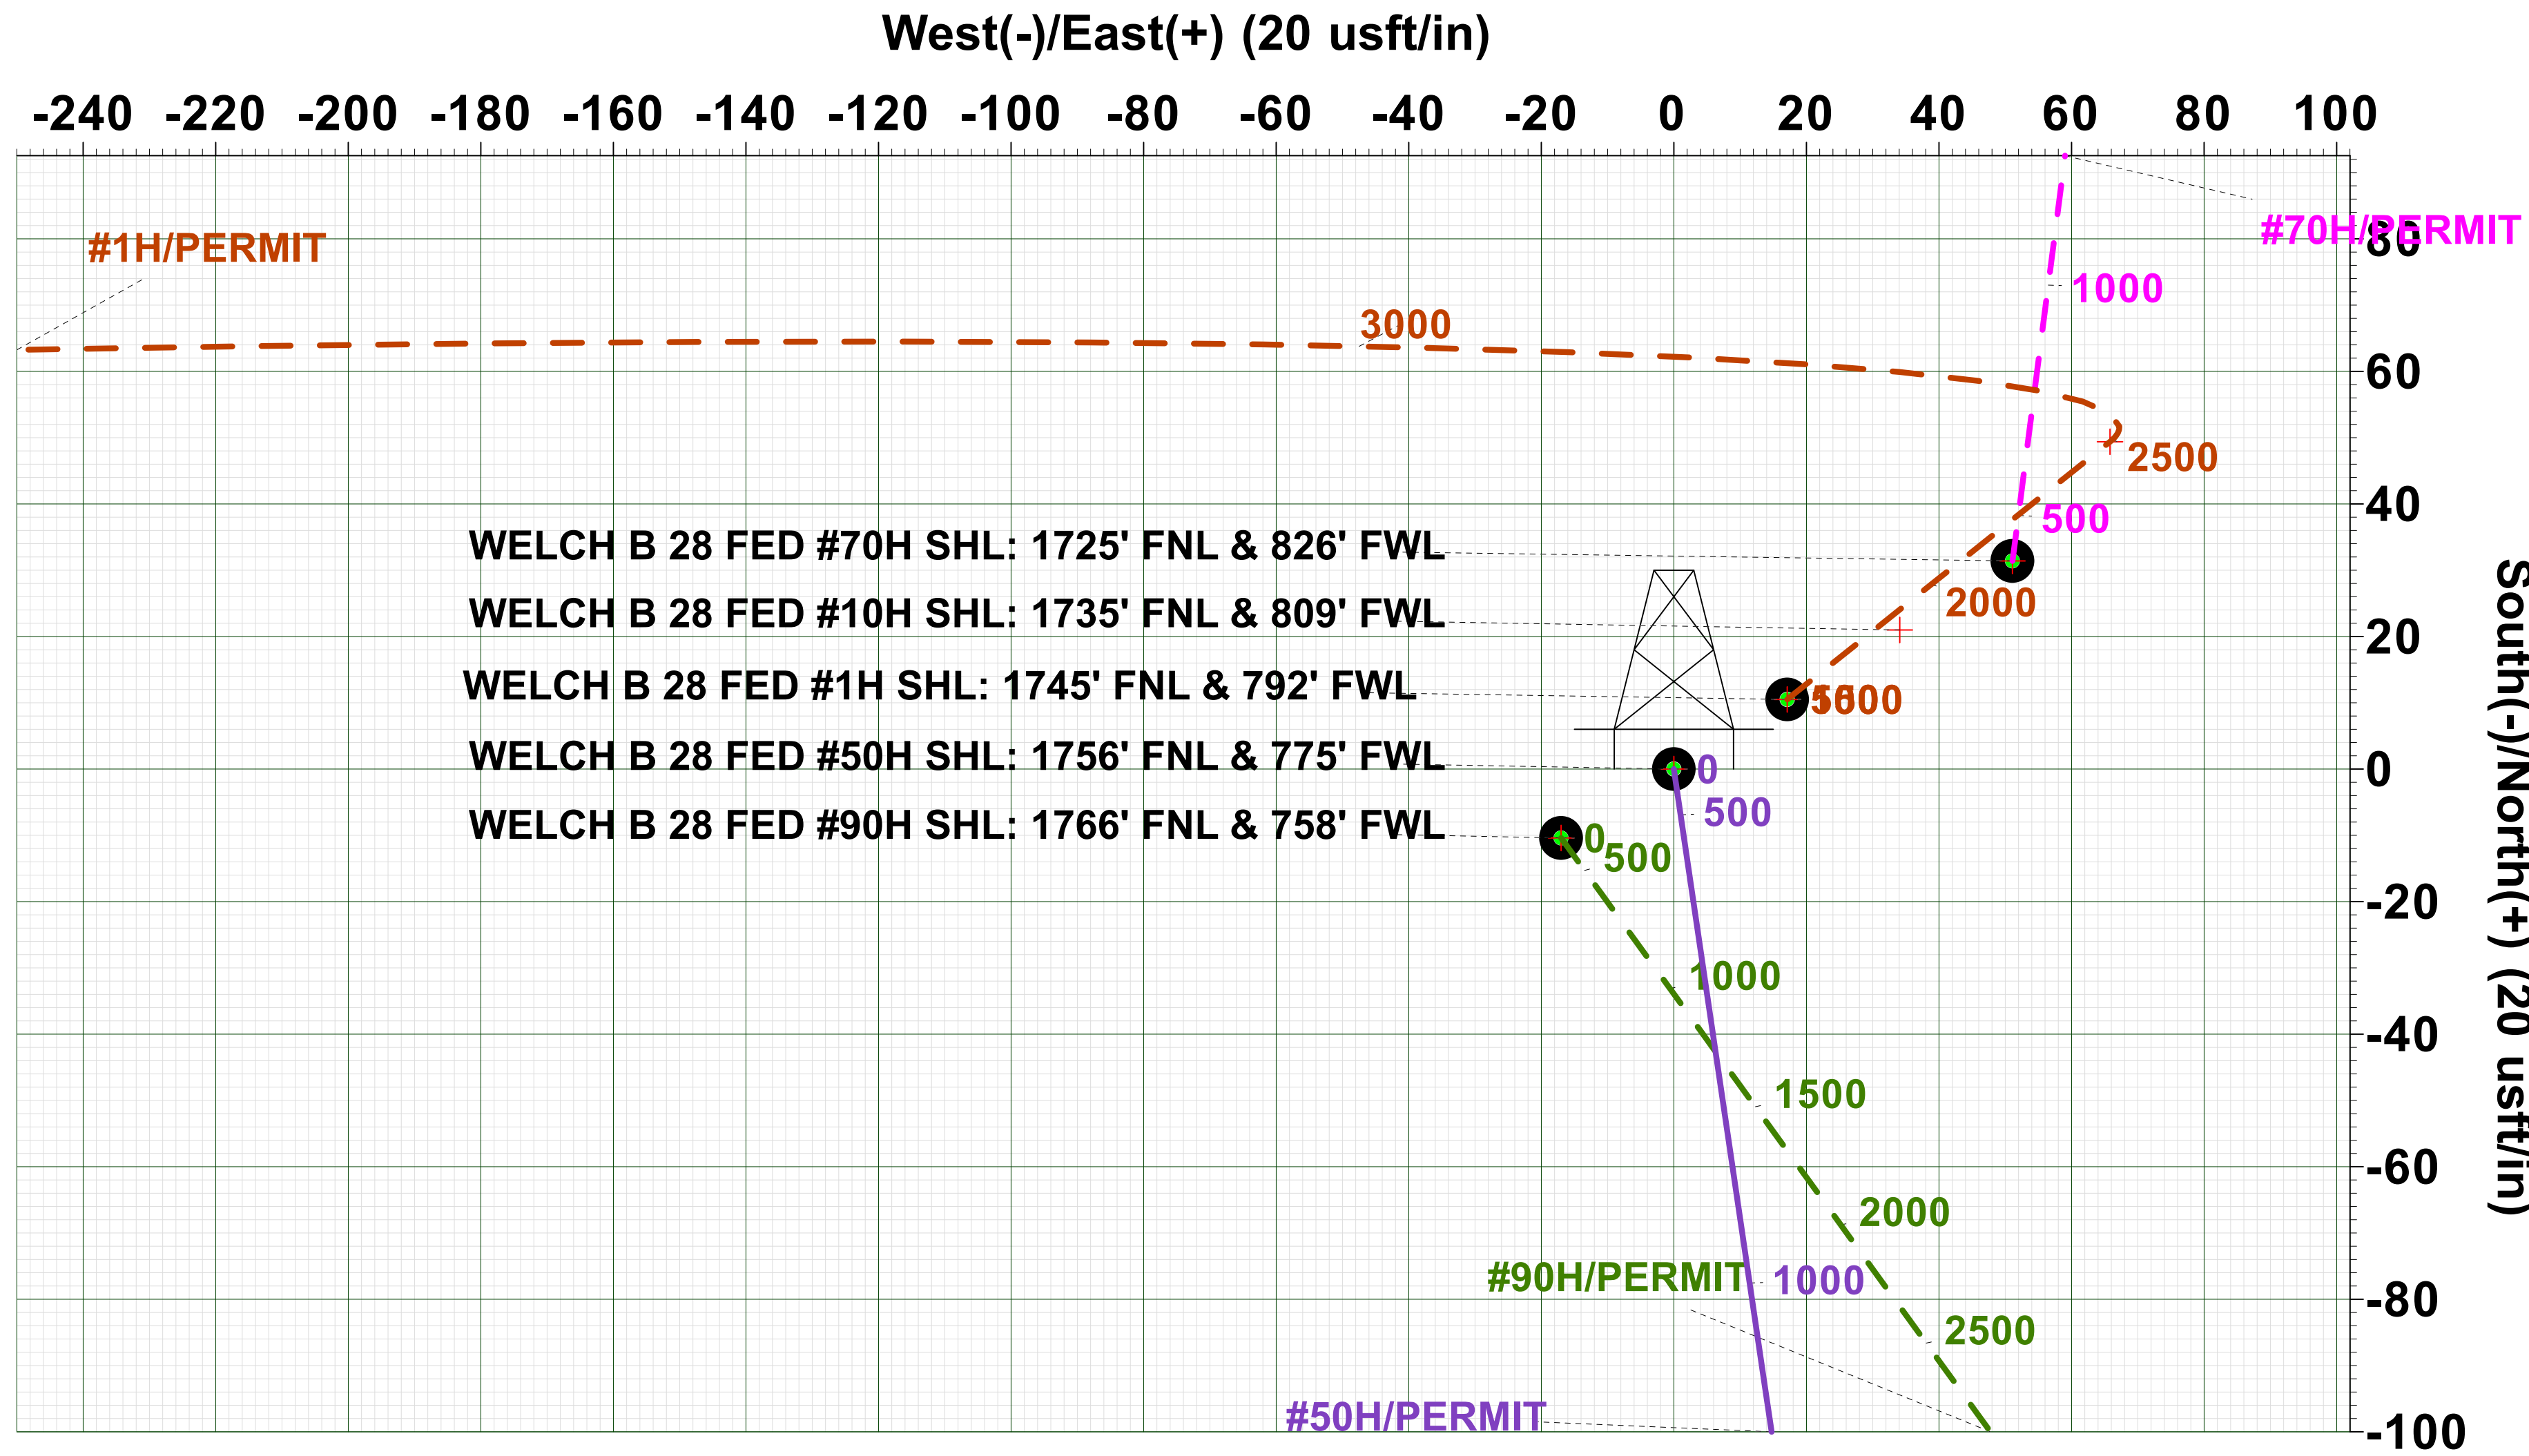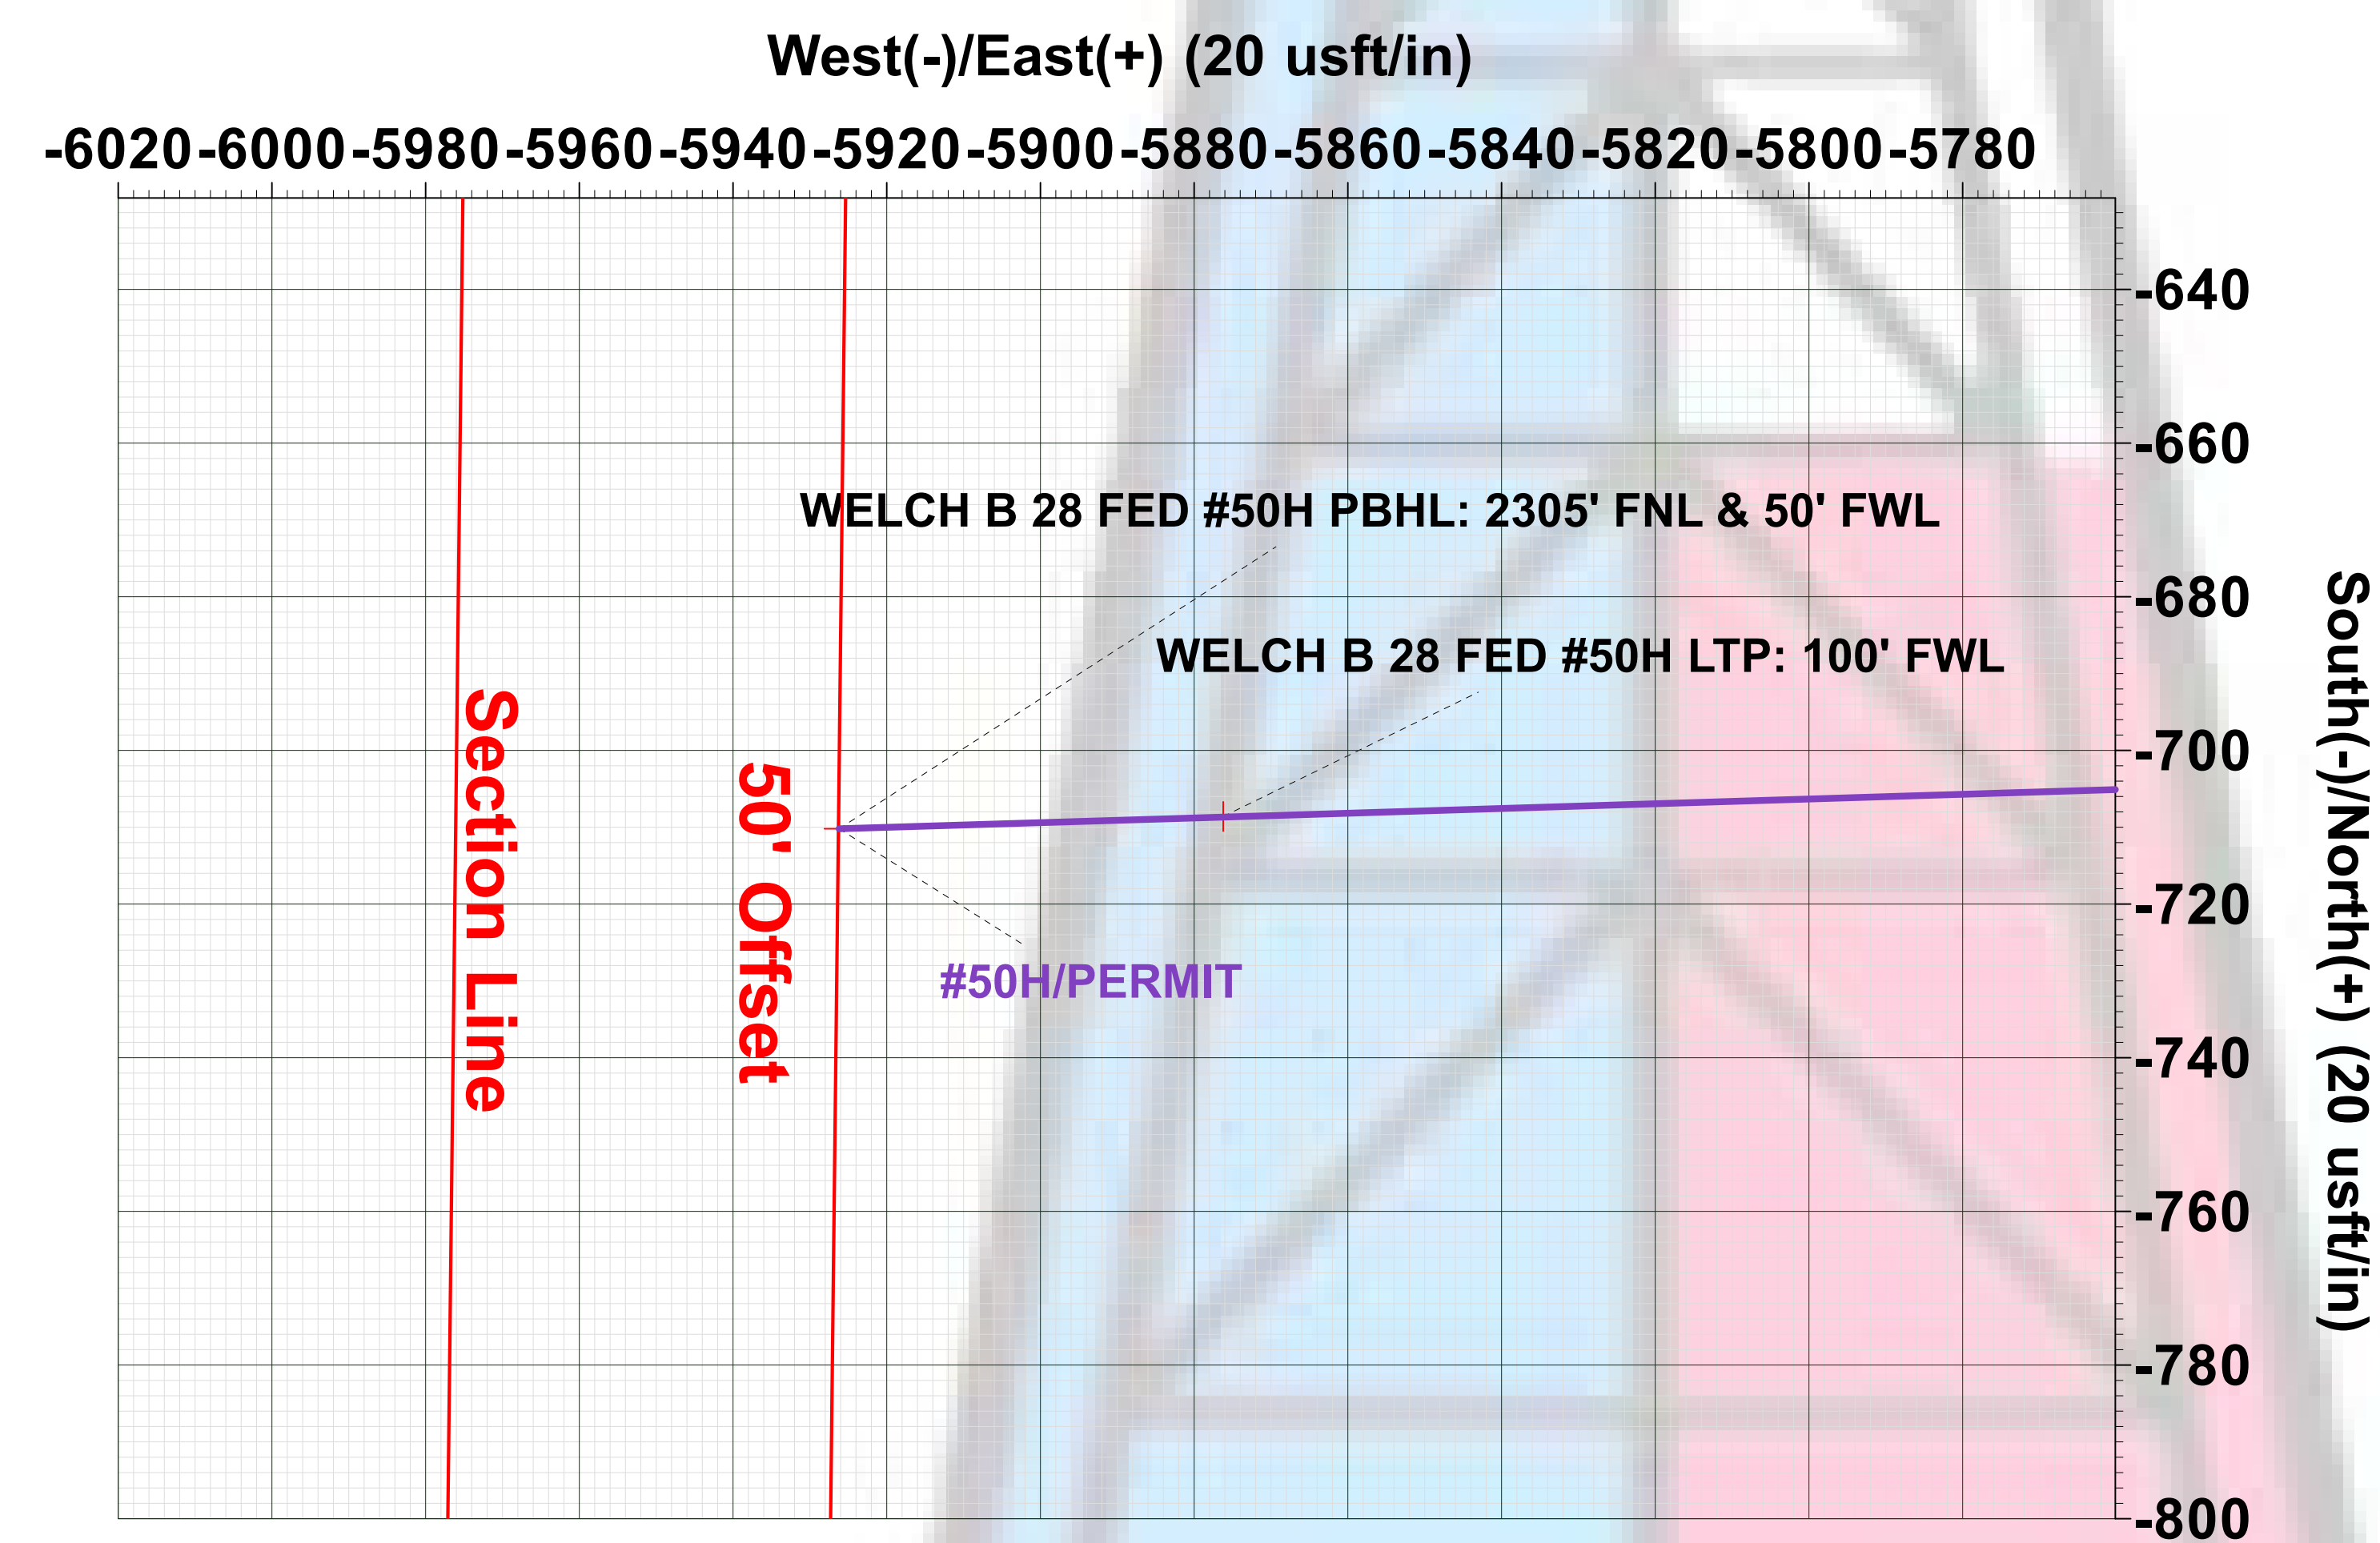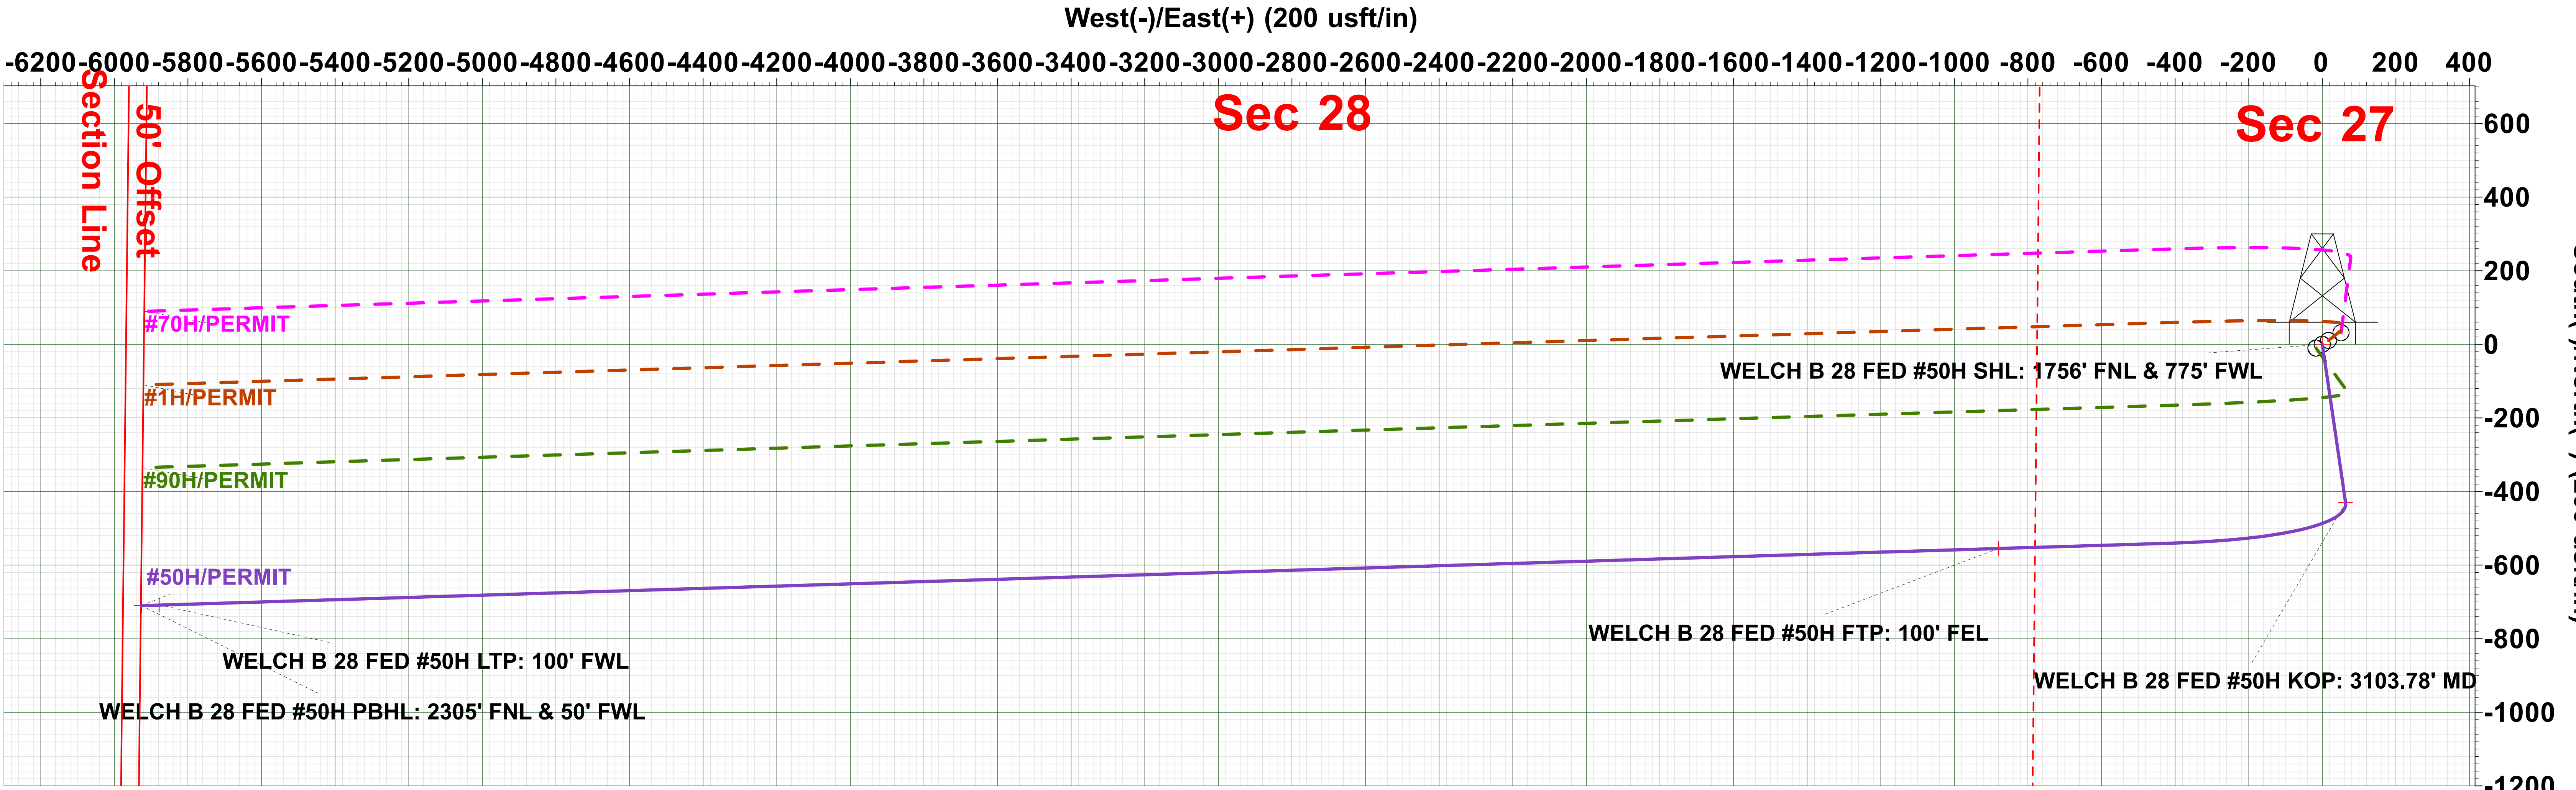

| DESIGN TARGET DETAILS | | | | | | | |
|---|---------|---------|----------|-----------|-----------|------------|--------------|
| Name | TVD | +N/-S | +E/-W | Northing | Easting | Latitude | Longitude |
| WELCH B 28 FED #50H SHL: 1756' FNL & 775' FWL | 0.00 | 0.00 | 0.00 | 657705.20 | 591552.50 | 32.8079545 | -104.1698939 |
| WELCH B 28 FED #50H KOP: 3103.78' MD | 3067.82 | -429.86 | 63.40 | 657275.34 | 591615.90 | 32.8067727 | -104.1696897 |
| WELCH B 28 FED #50H PBHL: 2305' FNL & 50' FWL | 4040.00 | -710.20 | -5926.20 | 656995.00 | 585626.30 | 32.8060261 | -104.1891855 |
| WELCH B 28 FED #50H LTP: 100' FWL | 4040.50 | -708.60 | -5876.20 | 656996.60 | 585676.30 | 32.8060303 | -104.1890228 |
| WELCH B 28 FED #50H FTP: 100' FEL | 4090.00 | -554.90 | -880.30 | 657150.30 | 590672.20 | 32.8064330 | -104.1727618 |

Disclaimer:

All Plan Details, boundary lines and offset well location/ survey data is provided by customer and subject to customer approval.



Plan: PERMIT (#50H/Wellbore #1)

Created By: Matthew May Date: 12:00, November 20 2020

Pecos District

Application for Permit to Drill

Conditions of Approval

Geology Concerns

| | | | |
|------------|--|--|--|
| Potash | <input checked="" type="checkbox"/> None | <input type="checkbox"/> Secretary | <input type="checkbox"/> R-111-P |
| Cave/Karst | <input type="checkbox"/> Medium | <input type="checkbox"/> High | <input type="checkbox"/> Critical |
| H2S | <input checked="" type="checkbox"/> None | <input type="checkbox"/> Below 100 PPM | <input type="checkbox"/> Above 100 PPM |
| Other | <input type="checkbox"/> 4 String Area | <input type="checkbox"/> Capitan Reef | <input type="checkbox"/> SWD Well |

Note: The geology of the area where the well is being drilled determines the COAs that apply, not the above table.

Additional Engineering Requirements

Surface casing must be set at: 400 feet

General Requirements

1. Changes to the approved APD casing program need prior approval.
2. The Bureau of Land Management (BLM) will be notified in advance to witness:
 - a. Well spudding (minimum 24 hours notice)
 - b. Setting and cementing of all casing strings (minimum 4 hours notice)
 - c. BOPE tests (minimum 4 hours notice)

Eddy County

620 East Greene Street, Carlsbad, NM 88220
(575) 361-2822

Lea County

414 West Taylor, Hobbs, NM 88240
(575) 393-3612

3. The initial wellhead installed on the well will remain on the well with spools used as needed.
4. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig:

- i. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with a Spudder Rig:
 - i. Notify the BLM when moving in and removing the Spudder Rig.
 - ii. Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - iii. BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
5. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller, and will always be operational during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the doghouse or stairway area.
6. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

Pressure Control

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. 5M or higher system requires an HCR valve, remote kill line, and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
3. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE, and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - b. The results of the test shall be reported to the appropriate BLM office.
 - c. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.

- d. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
 - e. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.
 - f. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - g. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, no tests shall commence until the cement has had a minimum of 24 hours setup time.
 - h. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
4. If the operator has proposed using a 5,000 (5M) Annular on a 10M BOP:
- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 10,000 (10M) psi.
5. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
- a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.

- c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
6. If a variance is approved for break testing the BOPE, the following requirements apply:
- a. BOPE break testing is only approved for a BOP rated at 5M or less.
 - b. A full BOP test shall be performed every 21 days (at a minimum).
 - c. A full BOP test is required prior to drilling the first intermediate hole section (if applicable). If any subsequent intermediate hole interval is deeper than the first, a full BOP test shall be required.
 - d. A full BOP test is required prior to drilling the first production hole section. If any subsequent production hole interval is deeper than the first, a full BOP test shall be required.
 - e. While in transfer, the BOP shall be secured by the hydraulic carrier or cradle.
 - f. Pressure tests shall be performed on any BOPE components that have been disconnected. A low pressure (250-300 psi) and a high pressure (BOP max pressure rating) test are required.
 - g. If a testing plug is used, pressure shall be maintained for at least 10 minutes. If there is any bleed off in pressure, the test shall be considered to have failed.
 - h. If no testing plug is used, pressure shall be maintained for at least 30 minutes. If there is a decline in pressure of more than 10 percent, the test shall be considered to have failed.
 - i. The appropriate Bureau of Land Management (BLM) office shall be notified a minimum of 4 hours before testing occurs.
7. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply:
- a. The flex line must meet the requirements of API 16C.
 - b. Check condition of flexible line from BOP to choke manifold (replace if exterior is damaged or if line fails test).
 - c. Line is to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements.
 - d. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating.
 - e. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

Casing and Cement

1. Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.).
2. On any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. The formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
3. Provide compressive strengths (including hours to reach required 500 pounds compressive strength) prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
4. The surface casing shall be set at a minimum of 25 feet into the Rustler Anhydrite and 80 feet above the salt and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of 8 hours (or 24 hours in the Potash Area) or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
5. Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.
6. Intermediate casing must be cemented to surface. For medium/high cave/karst, potash, and Capitan Reef, wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
7. The production cement should tie-back at least 200 feet (500 feet in Secretary Potash, surface in R-111-P potash) into previous casing string. Operator shall provide method of verification.

8. Production liner cement should tie-back at least 100 feet into previous casing string. Operator shall provide verification of cement top.
9. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
10. No pea gravel permitted for remedial cement or fall back remedial cement without prior authorization from a BLM petroleum engineer.
11. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
12. DV tools:
 - a. First stage to DV tool (The DV tool may be cancelled if cement circulates to surface on the first stage):
 - i. Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
 - b. Second stage above DV tool:
 - i. For intermediate casing, cement to surface.
 - ii. For production casing, cement should tie-back at least 200 feet (500 feet in Secretary Potash, surface in R-111-P potash) into previous casing string. Operator shall provide method of verification.
 - iii. If cement does not circulate, contact the appropriate BLM office.
13. Wait on cement (WOC) for Potash Areas:
 - a. Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
 - b. After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met:
 - i. Cement reaches a minimum compressive strength of 500 psi for all cement blends
 - ii. Until cement has been in place at least 24 hours.
 - c. WOC time will be recorded in the driller's log.
 - d. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.
14. Wait on cement (WOC) for Water Basin:
 - a. After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met:

- i. Cement reaches a minimum compressive strength of 500 psi at the shoe
 - ii. Until cement has been in place at least 8 hours.
 - b. WOC time will be recorded in the driller's log.
15. Wait on cement (WOC) for Medium and High Cave/Karst Areas:
 - a. Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
16. If cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

Drilling Mud

1. Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

Waste Material and Fluids

1. All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.
2. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Special Requirements

1. Communitization Agreement
 - a. The operator will submit a Communitization Agreement to the Carlsbad Field Office (620 E Greene St. Carlsbad, New Mexico 88220), at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division.
 - b. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
 - i. If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
 - c. In addition, the well sign shall include the surface and bottom hole lease numbers.
 - i. When the Communitization Agreement number is known, it shall also be on the sign.

2. Unit Wells

- a. The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers.
 - i. If a participating area has not been established, the operator can use the general unit designation, but will replace the unit number with the participating area number when the sign is replaced.
- b. Commercial Well Determination
 - i. A commercial well determination shall be submitted after production has been established for at least six months (this is not necessary for secondary recovery unit wells).

3. Hydrogen Sulfide (H₂S)

- a. If H₂S is encountered, provide measured values and formations to the BLM.
- b. An H₂S area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items.
- c. An H₂S Drilling Plan shall be activated 500 feet prior to drilling into the any formation designated as having H₂S.
- d. Hydrogen Sulfide monitors shall be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items.

4. Capitan Reef

- a. If lost circulation (50% or greater) occurs below the Base of the Salt, the operator shall do the following (Use this for 3 string wells in the Capitan Reef, if 4 string well ensure fresh water based mud used across the Capitan interval):
 - i. Switch to fresh water mud to protect the Capitan Reef and use fresh water mud until setting the intermediate casing. The appropriate BLM office is to be notified for a PET to witness the switch to fresh water.
 - ii. Daily drilling reports from the Base of the Salt to the setting of the intermediate casing are to be submitted to the BLM CFO engineering staff via e-mail by 0800 hours each morning. Any lost circulation encountered is to be recorded on these drilling reports.
 - iii. The daily drilling report should show mud volume per shift/tour.
 - iv. Failure to submit these reports will result in an Incidence of Non-Compliance being issued for failure to comply with the Conditions of Approval.
 - v. If not already planned, the operator shall run a caliper survey for the intermediate well bore and submit to the appropriate BLM office.

5. Salt Water Disposal Wells

- a. The operator shall supply the BLM with a copy of a mudlog over the permitted disposal interval and estimated in situ water salinity based on open-hole logs.
- b. If hydrocarbons are encountered while drilling, the operator shall notify the BLM.
- c. The operator shall provide to the BLM a summary of formation depth picks based on mudlog and geophysical logs along with a copy of the mudlog and open-hole logs from total depth to top of Devonian.
- d. An NOI sundry with the completion procedure for this well shall be submitted and approved prior to commencing completion work. The procedure will be reviewed to verify that the completion proposal will allow the operator to:
 - i. Properly evaluate the injection zone utilizing open-hole logs, swab testing and/or any other method to confirm that hydrocarbons cannot be produced in paying quantities. This evaluation shall be reviewed by the BLM prior to injection commencing.
 - ii. Restrict the injection fluid to the approved formation.
 - iii. If a step rate test will be run, an NOI sundry shall be submitted to the BLM for approval.
- e. If off-lease water will be disposed in this well, the operator shall provide proof of right-of-way approval.




Permian Drilling Hydrogen Sulfide Drilling Operations Plan Welch B 28 Fed 50H

Open drill site. No homes or buildings are near the proposed location.

1. Escape

Personnel shall escape upwind of wellbore in the event of an emergency gas release. Escape can take place through the lease road on the Southeast side of the location. Personnel need to move to a safe distance and block the entrance to location. If the primary route is not an option due to the wind direction, then a secondary egress route should be taken.


Secondary Briefing Area

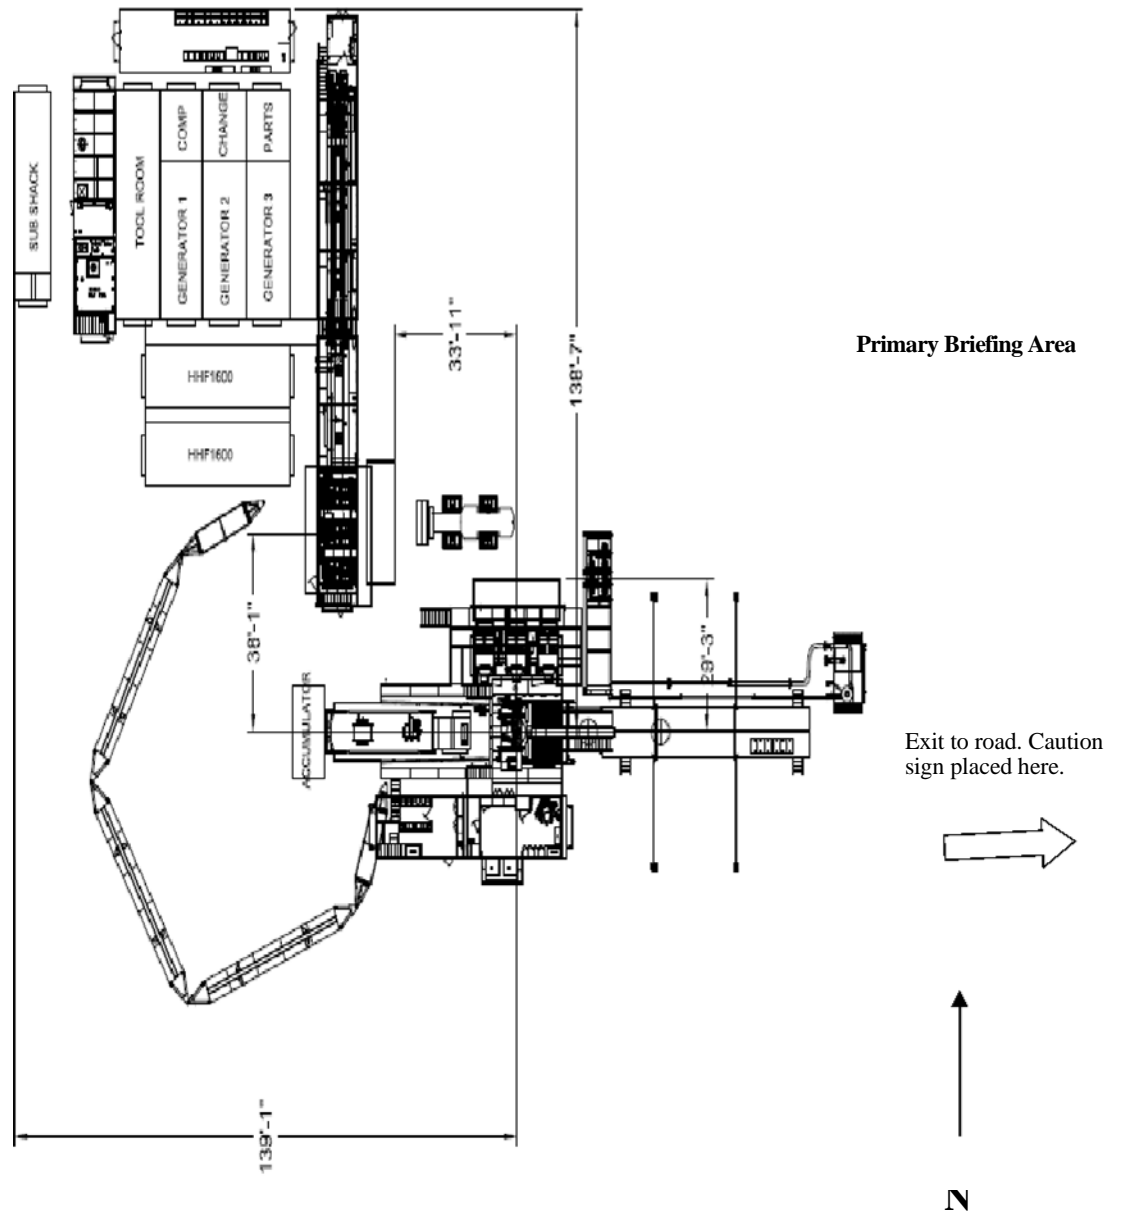

WIND: Prevailing winds are from the Southwest

Secondary Egress

SPUR ENERGY PARTNERS LLC.
WELCH B 28 FED #50H
(1756' FNL & 775' FWL)
SECTION 27, T17S, R28E
N. M. P. M., EDDY COUNTY, NEW MEXICO

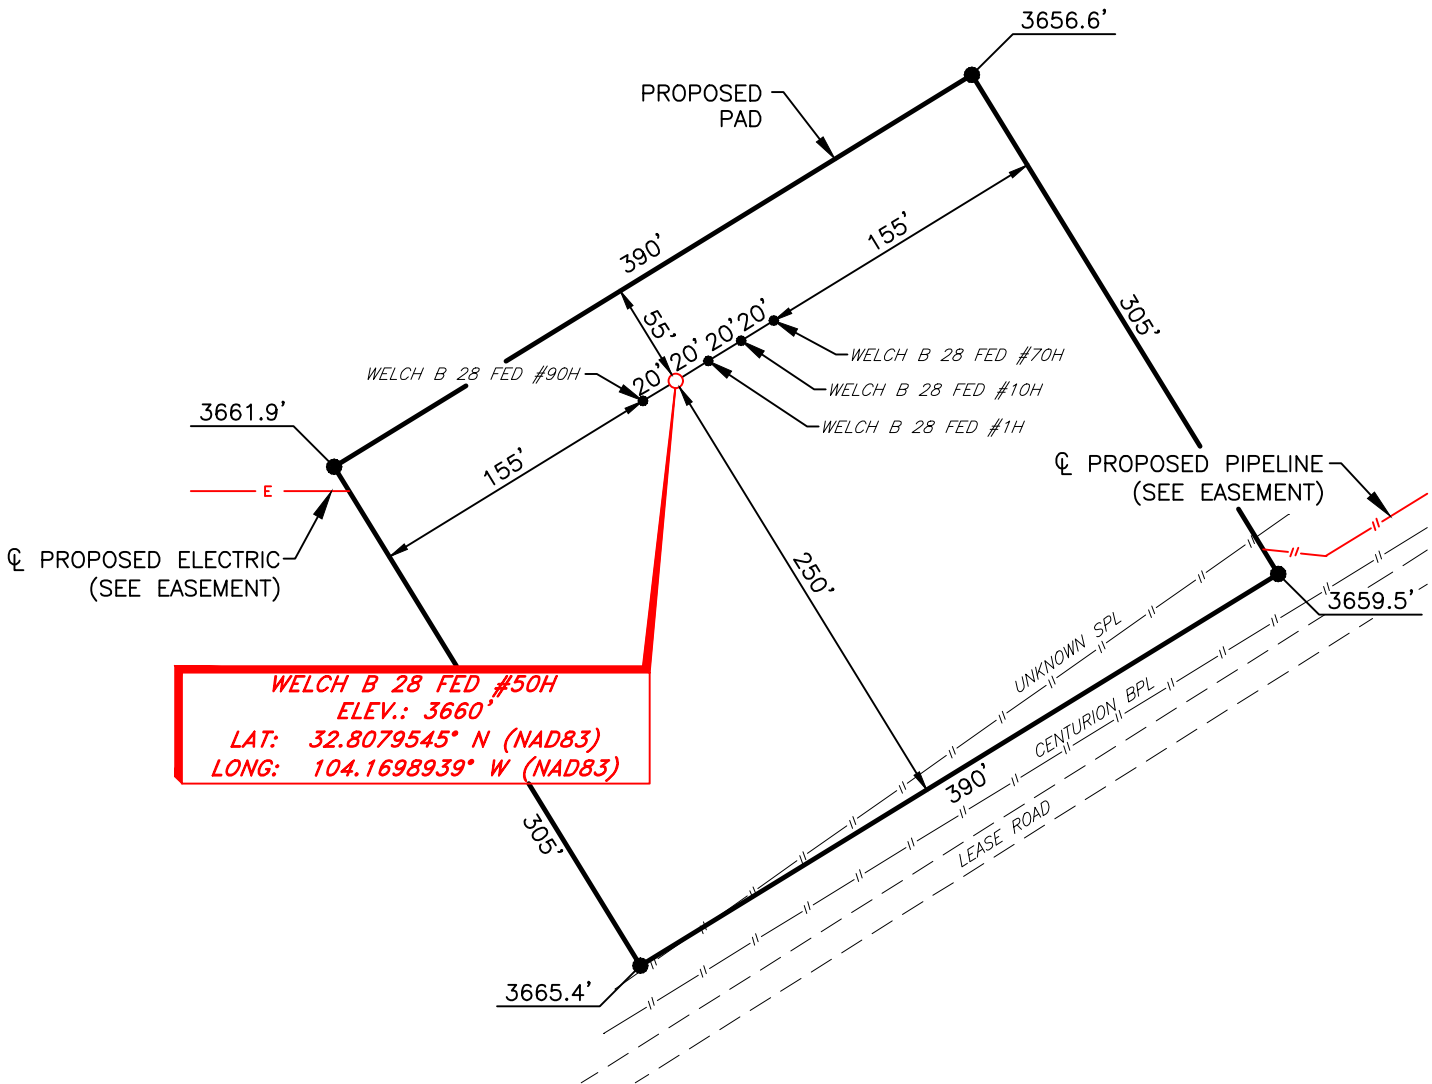

DIRECTIONS TO LOCATION

From the intersection of CR #208 (Red Lake Rd.) and U.S. Hwy 82 (Lovington Hwy);
Go North on CR #208 approx. 0.5 miles to a lease road on the right;
Turn right and go Northwest approx. 0.4 miles to location on the left;



SCALE: 1" = 100'
0 50 100
BEARINGS ARE
NAD 83 GRID - NM EAST
DISTANCES ARE GROUND

I, R. M. Howett, a N. M. Professional Surveyor, hereby certify that I prepared this unclassified survey of a well location from an actual survey made on the ground under my direct supervision, said survey and plat meet the Min. Stds. for Land Surveying in the State of N. M. and are true and correct to the best of my knowledge and belief.

Robert M. Howett
Robert M. Howett NM PS 19680




Copyright 2016 - All Rights Reserved

| | | |
|-----------|------------|------|
| NO. | REVISION | DATE |
| JOB NO.: | LS20100592 | |
| DWG. NO.: | 20100592-4 | |



701 S. CECIL ST., HOBBS, NM 88240 (575) 964-8200

| |
|--------------------|
| SCALE: 1" = 100' |
| DATE: 10-28-2020 |
| SURVEYED BY: TM/RU |
| DRAWN BY: GA |
| APPROVED BY: RMH |
| SHEET: 1 OF 1 |

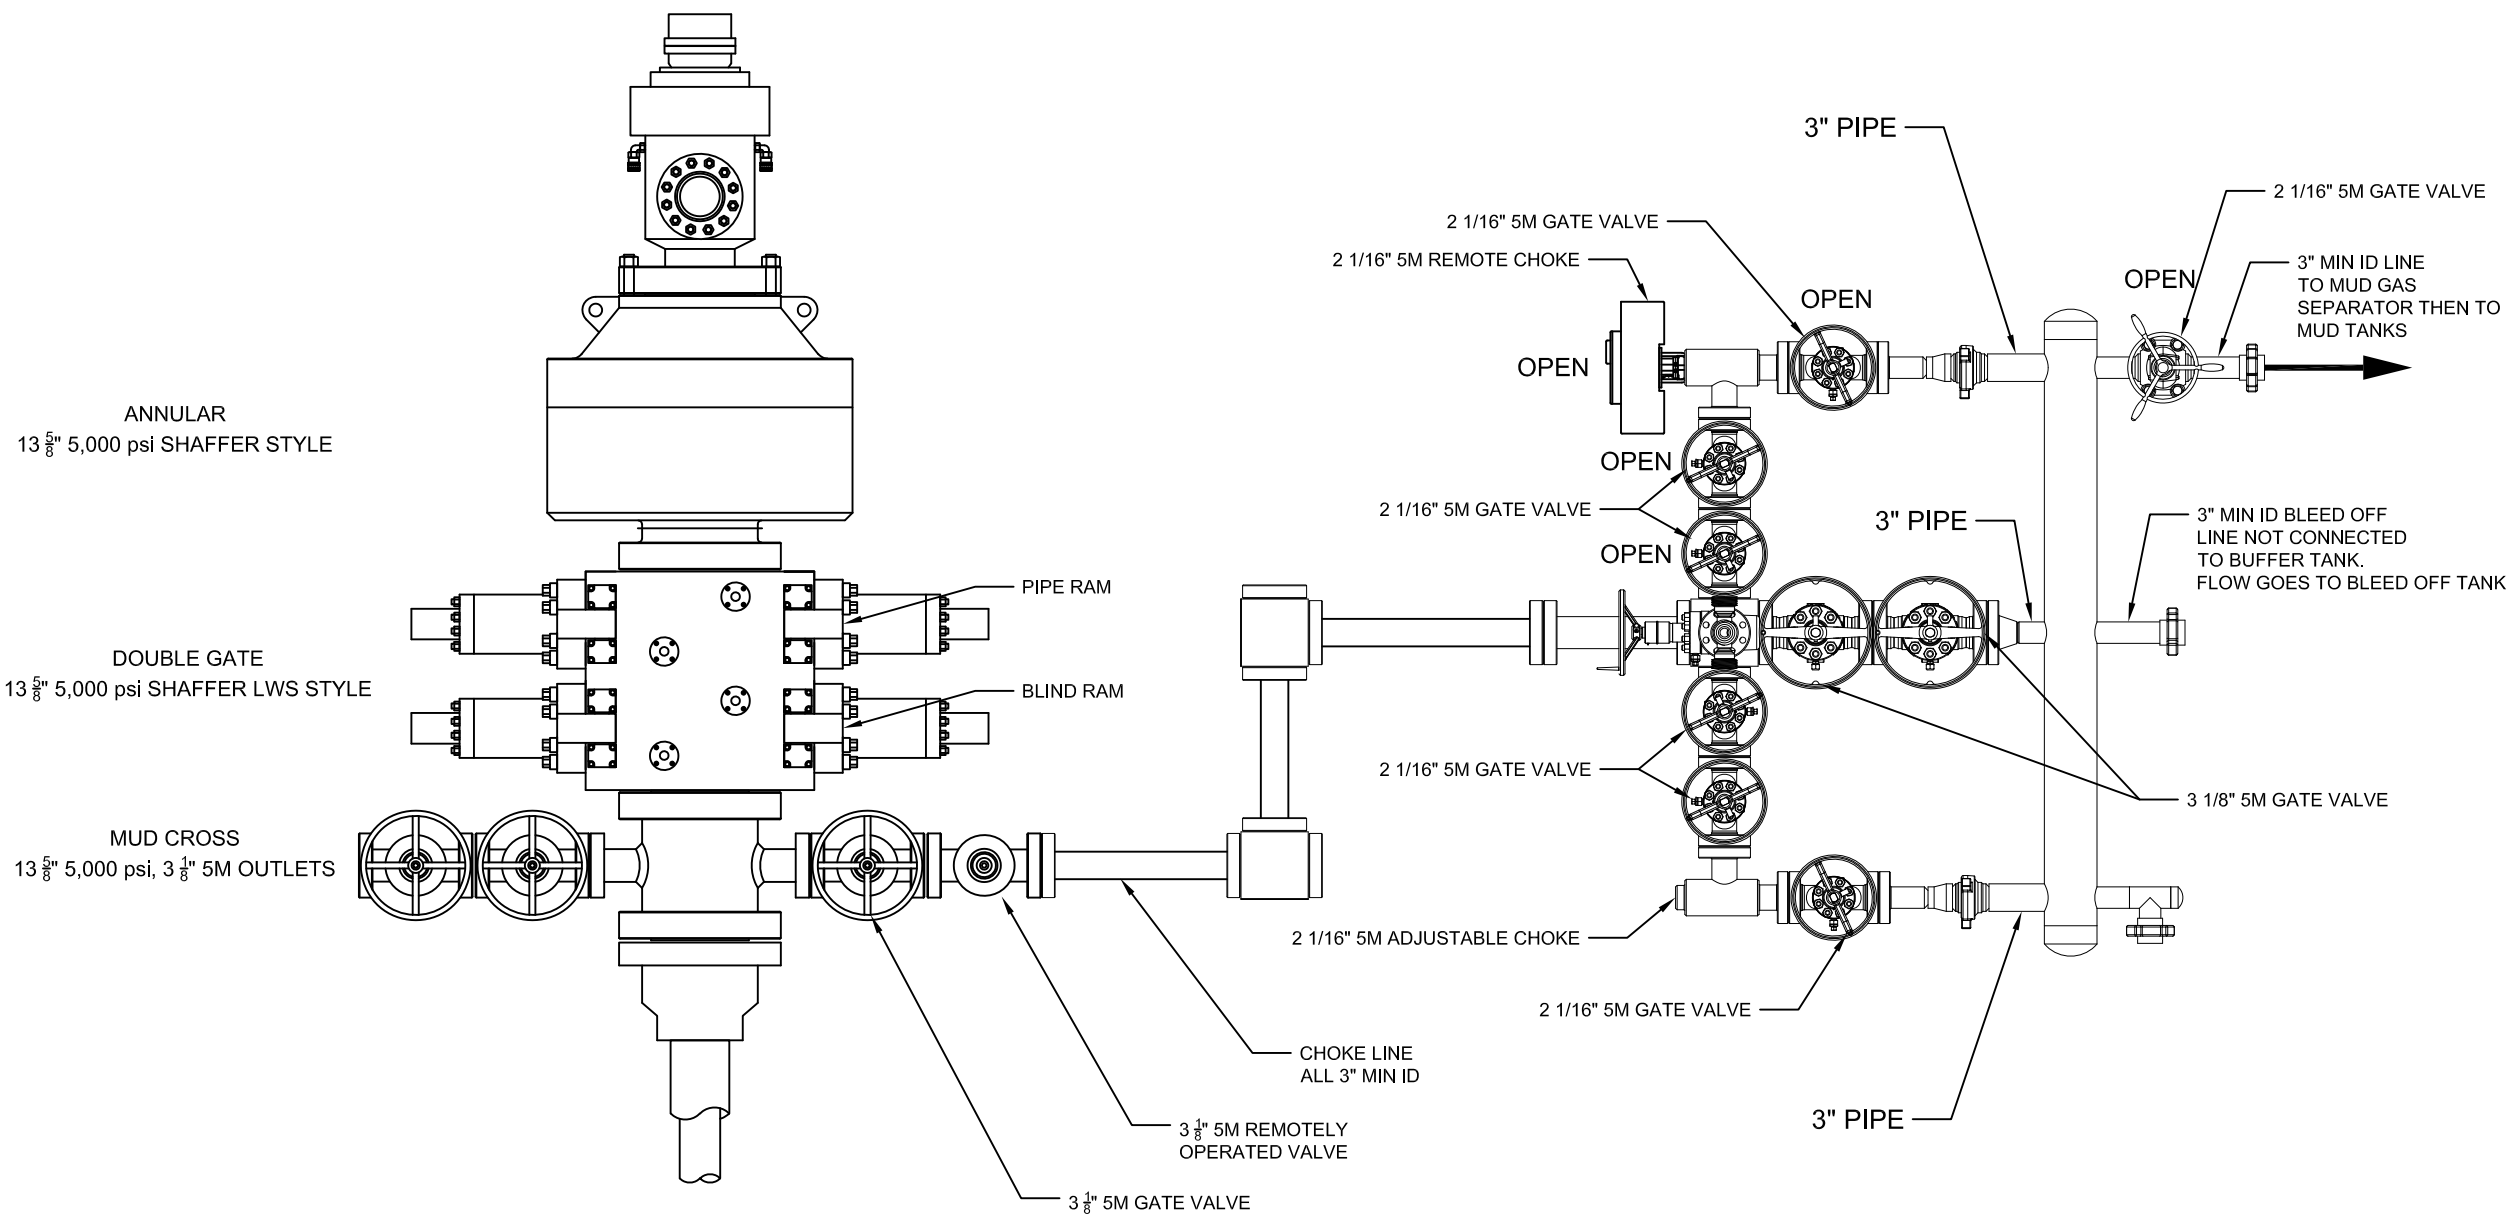

Notes
-
-
-

| No. | Revision | Date |
|-----|----------|------|
|-----|----------|------|



AKITA
DRILLING LTD.
2302 8th Street, Nisku Alberta
T9E 7Z2 Tel: (780) 955-6700

The information contained in this drawing is the sole property of AKITA Drilling Ltd. Any reproduction in whole or part without the express written consent of AKITA Drilling Ltd. is prohibited.

| | | | |
|----------------|----------|-----------|-----------------|
| Date | 5-6-2021 | Scale | NTS |
| Des / Chk'd By | BG | File Name | R57 13 5M dou.. |
| Project | R57 | | |

RIG 57 BOP SCHEMATIC

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 75947

CONDITIONS

| | |
|---|---|
| Operator: Spur Energy Partners LLC 9655 Katy Freeway Houston, TX 77024 | OGRID: 328947 |
| | Action Number: 75947 |
| | Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3) |

CONDITIONS

| Created By | Condition | Condition Date |
|------------|--|----------------|
| kpickford | Notify OCD 24 hours prior to casing & cement | 2/1/2022 |
| kpickford | Will require a File As Drilled C-102 and a Directional Survey with the C-104 | 2/1/2022 |
| kpickford | Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string | 2/1/2022 |
| kpickford | Cement is required to circulate on both surface and intermediate1 strings of casing | 2/1/2022 |
| kpickford | Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system | 2/1/2022 |
