

Form 3160-5
(June 2019)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB No. 1004-0137
Expires: October 31, 2021**SUNDRY NOTICES AND REPORTS ON WELLS**
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.5. Lease Serial No. **NMNM0039880**

6. If Indian, Allottee or Tribe Name

SUBMIT IN TRIPLICATE - Other instructions on page 2

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other2. Name of Operator **APACHE CORPORATION**3a. Address **303 VETERANS AIRPARK LANE SUITE 3000, N** 3b. Phone No. (include area code)
(432) 818-10004. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SEC 15/T24S/R32E/NMP

7. If Unit of CA/Agreement, Name and/or No.

8. Well Name and No. **GHOST RIDER 22 15 FEDERAL CC**9. API Well No. **30-025-50231** **#401H**10. Field and Pool or Exploratory Area
Upper Bone Spring/TRISTE DRAW BONE SPRING11. Country or Parish, State
LEA/NM**12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION				
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off	
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Hydraulic Fracturing	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity	
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other	
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon		
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal		

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Apache Corp requests APD change in well number, csg/cmt, mud, BOPE due to change in lateral target and well spacing. Apache also request a variance, per mtg on 4/7/22, listed in #4 and #5 of drlg program attached. OLD WELL NAME AND NUMBER: Ghost Rider 22 15 Federal Com 31H; **NEW WELL NAME AND NUMBER: Ghost Rider 22 15 Federal Com 401H.** Please see attached drilling program. Revised plat and directional survey attached.

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed)
SORINA FLORES / Ph: (432) 818-1167

Title **Supv of Drilling Services**

Signature

Date

05/25/2022**THE SPACE FOR FEDERAL OR STATE OFFICE USE**

Approved by

AJIBOLA OLABODE / Ph: (575) 234-2231 / Approved

Title **Engineer**

Date **06/27/2022**

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office **CARLSBAD**

Title 18 U.S.C Section 1001 and Title 43 U.S.C Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

GENERAL INSTRUCTIONS

This form is designed for submitting proposals to perform certain well operations and reports of such operations when completed as indicated on Federal and Indian lands pursuant to applicable Federal law and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local area or regional procedures and practices, are either shown below, will be issued by or may be obtained from the local Federal office.

SPECIFIC INSTRUCTIONS

Item 4 - Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult the local Federal office for specific instructions.

Item 13: Proposals to abandon a well and subsequent reports of abandonment should include such special information as is required by the local Federal office. In addition, such proposals and reports should include reasons for the abandonment; data on any former or present productive zones or other zones with present significant fluid contents not sealed off by cement or otherwise; depths (top and bottom) and method of placement of cement plugs; mud or other material placed below, between and above plugs; amount, size, method of parting of any casing, liner or tubing pulled and the depth to the top of any tubing left in the hole; method of closing top of well and date well site conditioned for final inspection looking for approval of the abandonment. If the proposal will involve **hydraulic fracturing operations**, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The privacy Act of 1974 and the regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 351 et seq., 25 U.S.C. 396; 43 CFR 3160.

PRINCIPAL PURPOSE: The information is used to: (1) Evaluate, when appropriate, approve applications, and report completion of subsequent well operations, on a Federal or Indian lease; and (2) document for administrative use, information for the management, disposal and use of National Resource lands and resources, such as: (a) evaluating the equipment and procedures to be used during a proposed subsequent well operation and reviewing the completed well operations for compliance with the approved plan; (b) requesting and granting approval to perform those actions covered by 43 CFR 3162.3-2, 3162.3-3, and 3162.3-4; (c) reporting the beginning or resumption of production, as required by 43 CFR 3162.4-1(c) and (d) analyzing future applications to drill or modify operations in light of data obtained and methods used.

ROUTINE USES: Information from the record and/or the record will be transferred to appropriate Federal, State, local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecutions in connection with congressional inquiries or to consumer reporting agencies to facilitate collection of debts owed the Government.

EFFECT OF NOT PROVIDING THE INFORMATION: Filing of this notice and report and disclosure of the information is mandatory for those subsequent well operations specified in 43 CFR 3162.3-2, 3162.3-3, 3162.3-4.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM collects this information to evaluate proposed and/or completed subsequent well operations on Federal or Indian oil and gas leases.

Response to this request is mandatory.

The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Collection Clearance Officer (WO-630), 1849 C St., N.W., Mail Stop 401 LS, Washington, D.C. 20240

Additional Information

Location of Well

0. SHL: NESE / 2272 FSL / 540 FEL / TWSP: 24S / RANGE: 32E / SECTION: 15 / LAT: 32.2165799 / LONG: -103.6557108 (TVD: 0 feet, MD: 0 feet)

PPP: SESE / 0 FSL / 744 FEL / TWSP: 24S / RANGE: 32E / SECTION: 15 / LAT: 32.2103336 / LONG: -103.6563709 (TVD: 9490 feet, MD: 11966 feet)

PPP: NESE / 2539 FSL / 1028 FEL / TWSP: 24S / RANGE: 32E / SECTION: 15 / LAT: 32.2173082 / LONG: -103.6572888 (TVD: 9232 feet, MD: 9284 feet)

BHL: SESE / 50 FSL / 743 FEL / TWSP: 24S / RANGE: 32E / SECTION: 22 / LAT: 32.195956 / LONG: -103.6563808 (TVD: 9490 feet, MD: 17196 feet)

CONFIDENTIAL

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

~~XX~~ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-50231	² Pool Code 96603	³ Pool Name TRISTE DRAW; BONE SPRING
⁴ Property Code 320516	⁵ Property Name GHOST RIDER 22 15 FEDERAL COM	
⁷ OGRID NO. 873	⁸ Operator Name APACHE CORPORATION	⁹ Elevation 3580'

¹⁰ Surface Location


UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet From the	East/West line	County
I	15	24S	32E		2272	SOUTH	540	EAST	LEA

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
P	22	24S	32E		50	SOUTH	380	EAST	LEA

¹² Dedicated Acres 240	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
---------------------------------------------	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interest have been consolidated or a non-standard unit has been approved by the division.

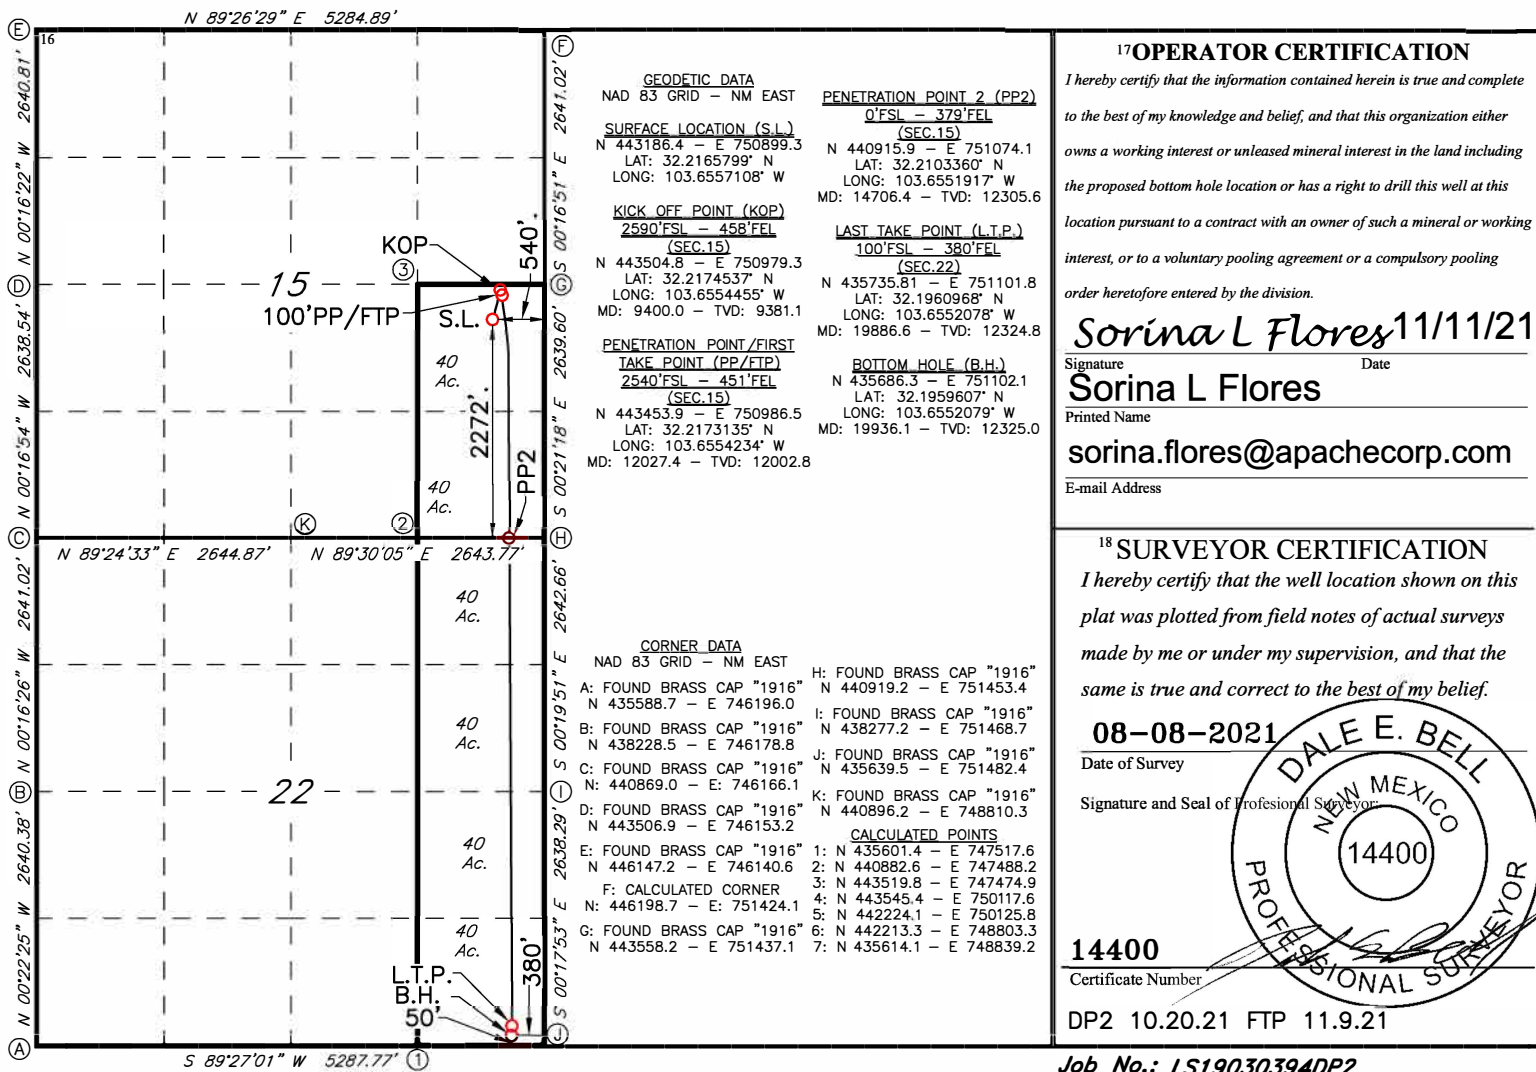

DRILLING PLAN: BLM COMPLIANCE

30-025-50231

Ghost Rider 22-15 Federal Com # 401H
 Projected TD: 19936' MD / 12325' TVD
 SHL: 2272' FSL & 540' FEL , Section 15, T24S, R32E
 BHL: 50' FSL & 380' FEL , Section 22, T24S, R32E
 Lea County, NM

1. Geologic Name of Surface Formation

A. Permian

2. Estimated Tops of Geological Markers & Depths of Anticipated Fresh Water, Oil or Gas

Formation	Well Depth (TVD)	Water/Oil/Gas
Rustler	1089'	Water
Salado	1418'	Water
Castile	3330'	Water
Delaware	4814'	Water/Oil/Gas
Cherry Canyon	5606'	Water/Oil/Gas
Brushy Canyon	7482'	Water/Oil/Gas
Bone Spring	8721'	Water/Oil/Gas
Avalon	8892'	Water/Oil/Gas
1st Bone Spring Sand	9883'	Water/Oil/Gas
2nd Bone Spring Carb	10093'	Water/Oil/Gas
2nd Bone Spring Sand	10437'	Water/Oil/Gas
3rd Bone Spring Carb	11047'	Water/Oil/Gas
3rd Bone Spring Sand	11841'	Water/Oil/Gas
Wolfcamp	12071'	Water/Oil/Gas
Wolfcamp A	12291'	Water/Oil/Gas
Target/Land Curve	12325'	Water/Oil/Gas

*** Hydrocarbons @ Brushy Canyon

*** Groundwater depth 40' (per NM State Engineers Office).

No other formations are expected to yield oil, gas or fresh water in measurable volumes. The surface fresh water sands will be protected by setting 13-3/8" casing @ 1114' (304' above the salt) and circulating cement back to surface. The 7-5/8" intermediate casing will be set at 11639' and bring TOC back to surface. A 6-3/4 inch curve and lateral hole will be drilled to MD/TD and 5-1/2" x 5-1/2" semi-flush casing will be set at TD and cemented back a minimum of 200' into the 7-5/8" casing shoe.

3. Casing Design

Hole Size	Depth	OD Csg	Weight	Collar	Grade	New/Used	SF Burst	SF Collapse	SF Tension
17-1/2"	0' – 1114'	13-3/8"	54.5	BTC	J-55	New	1.01	1.95	14.05
9-7/8"	0' – 11639'	7-5/8"	29.7	BTC	HCL-80	New	1.21	2.60	1.98
6-3/4"	0' – 11439'	5-1/2"	20	Semi-premium	CYP-110	New	1.05	1.32	2.11
6-3/4"	11439' - 19936'	5-1/2"	20	Semi-flush	CYP-110	New	1.05	1.32	1.82

- Apache Corporation requests to not utilize centralizers in the curve and lateral
- 7-5/8" Collapse analyzed using 50% evacuation based on regional experience.
- 5-1/2" Tension calculated using vertical hanging weight plus the lateral weight multiplied by a friction factor of 0.35
- Test on Casing will be limited to 70% burst of the casing or 1500 psi, whichever is less
- 5-1/2" 20 ppf casing will be run from surface to 11439 and crossed over to 5-1/2" 20 ppf semi-flush casing from 11439 to TD.
- Request to use 5" BTC Float equipment for the the production casing

Wellhead:

Permanent Wellhead – Multibowl System

A. Starting Head: 13-5/8" 10M top flange x 13-3/8" 10M SOW/BTC bottom

B. Tubing Head: 13-5/8" 10M bottom flange x 7-1/16" 10M top flange

- Wellhead will be installed by manufacturer's representatives.
- Manufacturer will monitor welding process to ensure appropriate temperature of seal.
- Operator will test the 7-5/8" casing per BLM Onshore Order 2
- Wellhead Manufacturer representative will not be present for BOP test plug installation

4. Cement Program

Surface Casing: 13-3/8", 54.5 New J-55, BTC casing to be set at +/- 1114'

Lead: 600 sxs Class - C + 1% CaCl (mixed at 12.8 ppg, 1.87 ft³/sx, 10.13 gal/sx water)

TOC: Surface

Tail: 300 sxs Class-C + 1% CaCl (mixed at 14.8 ppg, 1.35 ft³/sx, 6.39 gal/sx water)

Compressives: 12-hr = 900 psi 24 hr = 1500 psi

Intermediate Casing: 7-5/8", 29.7 New HCL-80, BTC casing to be set at +/- 11639'

1st Stage

Optional Lead: 650 sxs Class - C (mixed at 10.5 ppg, 2.77 ft³/sx, 15.59 gal/sx water)

TOC: Surface

Tail: 90 sxs Class - C (mixed at 14.8 ppg, 1.39 ft³/sx, 6.39 gal/sx water)

Compressives: 12-hr = 900 psi 24 hr = 1150psi

TOC: Brushy Canyon 7482'

2nd Stage

Tail: 320 sxs Class - C (mixed at 14.8 ppg, 1.33 ft³/sx, 5.29 gal/sx water)

Compressives: 12-hr = 900 psi 24 hr = 1150 psi

TOC: Surface

Per meeting on 4/7/2022, Apache requests to pump a two-stage cement job on the intermediate casing string with the first stage being pumped conventionally with the calculated top of cement at the Brushy Canyon and the second stage performed as a bradenhead squeeze with planned cement from the Brushy Canyon to surface. The final cement top after the second stage job will be verified by an Echometer. If necessary, a top out Job will be executed as a contingency to meet regulatory requirements. If cement is still not meeting the objective, then another Echometer will be performed for the cement top verification.

Apache will include the Echometer verified fluid top and the volume of displacement fluid above the cement slurry in the annulus in all post-drill sundries on wells utilizing this cement program.

Apache will report to the BLM the volume of fluid (limited to 5 bbl.) used to flush intermediate casing valves following the backside cementing procedures.

Apache requests to pump an Optional Lead if well conditions dictate to bring cement to surface on the first stage. If cement is brought to surface, the BLM will be notified and the second stage bradenhead squeeze and subsequent TOC verification will be negated.

In the event cement is not circulate to surface on the first stage, whether intentionally or unintentionally, Apache requests the option to conduct the bradenhead squeeze and TOC verification offline as per standard approval from BLM when unplanned remediate is needed and batch drilling is approved. In the event the bradenhead is conducted, we will ensure first stage cement job is cemented properly and the well is static with floats holding and no pressure on the casing annulus as with all other casing strings where batch drilling operations occur before moving off the rig. The TA cap will also be installed per wellhead manufacture procedure and pressure inside the casing will be monitored via the valve on the TA cap as per standard batch drilling operations.

Production Casing: 5-1/2", 20 New CYP-110, casing to be set at +/- 19936'

Due to possible lost circulation during the production cement jobs, Apache proposes a contingency bradenhead squeeze 4 hours after bumping the plug on the primary stage. A CBL will be ran after 7-10 days and will be submitted to the BLM.

Lead: 16 sxs Class - TXI (mixed at 11.5 ppg, 2.69 ft³/sx, 15.0 gal/sx water)

TOC inside the previous shoe by: 200'

Tail: 580 sxs Class - TXI (mixed at 13.2 ppg, 1.51 ft³/sx, 7.20 gal/sx water)

Compressives 12-hr = 800 psi 24 hr = 1500 psi

5. Pressure Control Equipment

Once the permanent WH is installed on the 13-3/8" casing, the blow out preventer equipment (BOP) will consist of a 13-5/8" minimum 3M Hydril and a 13-5/8" minimum 10M 3-Ram BOP. MASP should not exceed 2705 psi. In any instance where 10M BOP is required by BLM, Apache requests a variance to utilize 5M annular with 10M ram preventers (a common BOP configuration, which allows use of 10M rams in unlikely event that pressures exceed 5M). Also a variance is requested to test the 5M annular to 70% of working pressure at 3500 psi.

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
9-7/8"	13-5/8"	5M	Annular	x	70% of working pressure
			Blind Ram	x	5M
			Pipe Ram	x	
			Double Ram	x	
6-3/4"	13-5/8"	10M	Annular	x	70% of working pressure
			Blind Ram	x	10M
			Pipe Ram	x	
			Double Ram	x	

All BOP testing will be done by an independent service company. Annular pressure tests will be limited to 70% of the working pressure. When nipping up on the 13-3/8", 10M bradenhead and flange, the BOP test will be limited to 10000 psi. All BOP tests will include a low pressure test as per BLM regulations. The 10M BOP diagrams are attached. Blind rams will be functioned tested each trip, pipe rams will be functioned tested at a minimum every 7 days.

Equipment will consist of rotating head, mud gas separator, blowdown pit (panic line) and flare line just to name a few.

A variance is requested to allow use of a flex hose as the choke line from the BOP to the Choke Manifold. If this hose is used, a copy of the manufacturer's certification and pressure test chart will be kept on the rig. The manufacture does not require anchors.

Per meeting on 4/7/2022, Apache requests a variance to be able to batch drill this well if necessary. In doing so, Apache will set each casing string and ensure that the well is cemented properly and the well is static. With floats holding, no pressure on the csg annulus, and the installation of a TA cap as per wellhead recommendations, Apache will contact the BLM on each rig skid on the pad. Once surface and intermediate strings are all completed, **Apache will start preparing for the next production hole on each of the wells but will avoid drilling new formation while performing offline cementing simultaneously. Complete offline cementing on one well before embarking on drilling new formation on the next well on the same pad.**

Per meeting on 4/7/2022, A variance is requested to **ONLY** test broken pressure seals on the BOP equipment when moving from wellhead to wellhead which is in compliance with API Standard 53. API standard 53 states, that for pad drilling operation, moving from one wellhead to another within 21 days, pressure testing is required for pressure-containing and pressure-controlling connections when the integrity of a pressure seal is broken. We will also function test BOP equipment after each nipple up. A full BOP test will be required prior to drilling the 1st production hole and every 21 day after.

6. Proposed Mud Circulation System

INTERVAL	Hole Size	Mud Type	MW (ppg)	Viscosity (sec/qt)	Fluid Loss (cc)
0' - 1114'	17-1/2"	FW / Native (Spud mud)	9.3 - 10.5	35-40	NC
1114' - 11639'	9-7/8"	Brine / Cut Brine / Direct Emulsion	8 - 9.2	30-32	NC
11639' to 19936'	6-3/4"	Cut Brine / WBM / OBM	12.4 - 13.6	32-36	NC

The necessary mud products for weight addition and fluid loss control will be on location at all times.

The mud system type will be; **Closed**

Will an air gas system be used; **No**

Spud with fresh water/native mud and set 13-3/8" surface casing, isolating the fresh water aquifer. Drill out from under 13-3/8" surface casing with a brine/oil direct emulsion mud system. Use fibrous materials as needed to control seepage and lost circulation. Pump viscous sweeps as needed for hole cleaning. Pump speed will be recorded on a daily drilling report after mudding up. A Pason or Totco will be used to detect changes in loss or gain of mud volume. A mud test will be performed every 24 hours to determine: density, viscosity, strength, filtration and pH as necessary. Use available solids controls equipment to help keep mud weight down after mud up. Rig up solids control equipment to operate as a closed loop system.

7. Auxiliary Well Control and Monitoring Equipment

- An upper kelly valve will be used for the drill string at all times.
- A full opening drill pipe stabbing valve having appropriate connections will be on the rig floor at all times.
- H2S monitors will be on location when drilling below the 13-3/8" casing.

8. Logging, Coring and Testing Program

Mud Logger: Mud Logging Unit (2 man) below intermediate casing.

Will run GR/CNL from TD to surf (horizontal well - vertical portion of hole). Stated logs run will be in the completion report & submitted to BLM.

Open & cased hole logs run in well:

<input type="checkbox"/> CALIPER	<input type="checkbox"/> CEMENT BOND LOG	<input type="checkbox"/> CNL (Neutron log) /FDC (Formation Density log)
<input type="checkbox"/> COMPENSATED DENSILOG	<input type="checkbox"/> COMPENSATED NEUTRON LOG	<input type="checkbox"/> COMPUTER GENERATED LOG
<input type="checkbox"/> DIP METER LOG	<input type="checkbox"/> DIRECTIONAL SURVEY	<input type="checkbox"/> DUAL INDUCTION/MICRO-RESISTIVITY
<input type="checkbox"/> DUAL LATERAL LOG/MICRO-SPHERICALLY FOCUSED	<input type="checkbox"/> ELECTRIC LOG	<input type="checkbox"/> FORMATION DENSITY COMPENSATED LOG
<input checked="" type="checkbox"/> GAMMA RAY LOG	<input checked="" type="checkbox"/> MEASUREMENT WHILE DRILLING POROSITY-RESISTIVITY LOG	<input checked="" type="checkbox"/> MUD LOG/GEOLOGIC LITHOLOGY LOG
<input type="checkbox"/> OTHER	<input type="checkbox"/> SPONTANEOUS POTENTIAL LOG	<input type="checkbox"/> SIDEWALL NEUTRON LOG
<input type="checkbox"/> SONIC LOG		<input type="checkbox"/> TEMPERATURE LOG

9. Abnormal Pressures and Temperatures / Potential Hazards

BHT of 135 to 155 F is anticipated. No H₂S is expected but monitors will be in place to detect any H₂S occurrences. Should these circumstances be encountered the operator and drilling contractor are prepared to take all necessary steps to ensure safety of all personnel and environment. Lost circulation could occur but is not expected to be a serious problem in this area and hole seepage will be compensated for by additions of small amounts of LCM in the drilling fluid. Lost circulation during production cement job can occur in which the primary production cement job will be pumped as planned. If lift pressures do not indicate tieback, then a contingency bradenhead squeeze will be pumped 4 hours after primary job to achieve cement tieback into intermediate casing. A CBL will be ran afterwards and submitted to the BLM. The maximum anticipated bottom hole pressure for this well during the production section is 8396 psi.

10. Anticipated Starting Date and Duration of Operations

Road and location construction will begin after BLM have approved the APD. Anticipated spud date will be as soon after BLM approval and as soon as a rig will be available. Move in operations and drilling is expected to take 45 days. If production casing is run, an additional 30 days will be needed to complete well and construct surface facilities and/or lay flow lines in order to place well on production.

PERMIAN

NW DISTRICT - NM EZ NAD 83

GHOST RIDER 22-15 FED COM PAD (N East) NEW

Ghost Rider 22-15 Fed Com 401H

Ghost Rider 22-15 Fed Com 401H

30-025-50231

Plan: w/ lateral targets

Standard Planning Report

08 August, 2021

Planning Report

Database:	PEDM	Local Co-ordinate Reference:	Well Ghost Rider 22-15 Fed Com 401H
Company:	PERMIAN	TVD Reference:	WELL @ 3606.0ft (Original Well Elev)
Project:	NW DISTRICT - NM EZ NAD 83	MD Reference:	WELL @ 3606.0ft (Original Well Elev)
Site:	GHOST RIDER 22-15 FED COM PAD (N East) NEW	North Reference:	Grid
Well:	Ghost Rider 22-15 Fed Com 401H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Ghost Rider 22-15 Fed Com 401H		
Design:	w/ lateral targets		

Project	NW DISTRICT - NM EZ NAD 83		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	GHOST RIDER 22-15 FED COM PAD (N East) NEW		
Site Position:		Northing:	443,186.10 ft
From:	Map	Easting:	750,869.30 ft
Position Uncertainty:	0.0 ft	Slot Radius:	13.200 in
		Latitude:	32° 12' 59.678 N
		Longitude:	103° 39' 20.925 W
		Grid Convergence:	0.36 °

Well	Ghost Rider 22-15 Fed Com 401H		
Well Position	+N/-S	0.3 ft	Northing:
	+E/-W	30.0 ft	Easting:
Position Uncertainty		0.0 ft	Wellhead Elevation:
			Latitude:
			Longitude:
			Ground Level:

Wellbore	Ghost Rider 22-15 Fed Com 401H				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM_FILE	8/12/2019	6.67	59.87	47,876.80000000

Design	w/ lateral targets			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)
	0.0	0.0	0.0	178.45

Plan Survey Tool Program	Date	8/8/2021		
Depth From (ft)	Depth To (ft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	9,020.0 w/ lateral targets (Ghost Rider 22	MWD+HDGM (MWD)	
			OWSG MWD + HDGM	
2	9,020.0	19,936.1 w/ lateral targets (Ghost Rider 22	20180329 MWD+IFR1+SAG+I	
			OWSG MWD + IFR1 + Sag + I	

Planning Report

Database:	PEDM	Local Co-ordinate Reference:	Well Ghost Rider 22-15 Fed Com 401H
Company:	PERMIAN	TVD Reference:	WELL @ 3606.0ft (Original Well Elev)
Project:	NW DISTRICT - NM EZ NAD 83	MD Reference:	WELL @ 3606.0ft (Original Well Elev)
Site:	GHOST RIDER 22-15 FED COM PAD (N East) NEW	North Reference:	Grid
Well:	Ghost Rider 22-15 Fed Com 401H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Ghost Rider 22-15 Fed Com 401H		
Design:	w/ lateral targets		

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,466.7	7.00	14.10	2,465.5	27.6	6.9	1.50	1.50	0.00	14.10	
4,693.3	7.00	14.10	4,675.5	290.8	73.1	0.00	0.00	0.00	0.00	
5,159.9	0.00	0.00	5,141.0	318.4	80.0	1.50	-1.50	0.00	180.00	
11,839.4	0.00	0.00	11,820.5	318.4	80.0	0.00	0.00	0.00	0.00	
12,587.7	89.79	172.00	12,298.0	-152.7	146.2	12.00	12.00	0.00	172.00	
12,844.1	89.79	179.69	12,298.9	-408.2	164.8	3.00	0.00	3.00	89.99	
17,304.6	89.79	179.69	12,315.0	-4,868.7	188.8	0.00	0.00	0.00	0.00	t2 Ghost Rider 22-15
17,481.9	89.78	179.69	12,315.7	-5,045.9	189.7	0.01	-0.01	0.00	164.51	
19,936.1	89.78	179.69	12,325.0	-7,500.1	202.8	0.00	0.00	0.00	0.00	BHL Ghost Rider 22-1

Planning Report

Database:	PEDM	Local Co-ordinate Reference:	Well Ghost Rider 22-15 Fed Com 401H
Company:	PERMIAN	TVD Reference:	WELL @ 3606.0ft (Original Well Elev)
Project:	NW DISTRICT - NM EZ NAD 83	MD Reference:	WELL @ 3606.0ft (Original Well Elev)
Site:	GHOST RIDER 22-15 FED COM PAD (N East) NEW	North Reference:	Grid
Well:	Ghost Rider 22-15 Fed Com 401H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Ghost Rider 22-15 Fed Com 401H		
Design:	w/ lateral targets		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00	
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00	
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00	
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00	
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00	
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00	
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00	
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00	
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00	
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
2,100.0	1.50	14.10	2,100.0	1.3	0.3	-1.3	1.50	1.50	0.00	
2,200.0	3.00	14.10	2,199.9	5.1	1.3	-5.0	1.50	1.50	0.00	
2,300.0	4.50	14.10	2,299.7	11.4	2.9	-11.3	1.50	1.50	0.00	
2,400.0	6.00	14.10	2,399.3	20.3	5.1	-20.1	1.50	1.50	0.00	
2,466.7	7.00	14.10	2,465.5	27.6	6.9	-27.4	1.50	1.50	0.00	
2,500.0	7.00	14.10	2,498.6	31.6	7.9	-31.3	0.00	0.00	0.00	
2,600.0	7.00	14.10	2,597.8	43.4	10.9	-43.1	0.00	0.00	0.00	
2,700.0	7.00	14.10	2,697.1	55.2	13.9	-54.8	0.00	0.00	0.00	
2,800.0	7.00	14.10	2,796.4	67.0	16.8	-66.5	0.00	0.00	0.00	
2,900.0	7.00	14.10	2,895.6	78.8	19.8	-78.3	0.00	0.00	0.00	
3,000.0	7.00	14.10	2,994.9	90.7	22.8	-90.0	0.00	0.00	0.00	
3,100.0	7.00	14.10	3,094.1	102.5	25.7	-101.7	0.00	0.00	0.00	
3,200.0	7.00	14.10	3,193.4	114.3	28.7	-113.5	0.00	0.00	0.00	
3,300.0	7.00	14.10	3,292.6	126.1	31.7	-125.2	0.00	0.00	0.00	
3,400.0	7.00	14.10	3,391.9	137.9	34.7	-136.9	0.00	0.00	0.00	
3,500.0	7.00	14.10	3,491.1	149.7	37.6	-148.7	0.00	0.00	0.00	
3,600.0	7.00	14.10	3,590.4	161.6	40.6	-160.4	0.00	0.00	0.00	
3,700.0	7.00	14.10	3,689.6	173.4	43.6	-172.1	0.00	0.00	0.00	
3,800.0	7.00	14.10	3,788.9	185.2	46.5	-183.9	0.00	0.00	0.00	
3,900.0	7.00	14.10	3,888.2	197.0	49.5	-195.6	0.00	0.00	0.00	
4,000.0	7.00	14.10	3,987.4	208.8	52.5	-207.4	0.00	0.00	0.00	
4,100.0	7.00	14.10	4,086.7	220.7	55.4	-219.1	0.00	0.00	0.00	
4,200.0	7.00	14.10	4,185.9	232.5	58.4	-230.8	0.00	0.00	0.00	
4,300.0	7.00	14.10	4,285.2	244.3	61.4	-242.6	0.00	0.00	0.00	
4,400.0	7.00	14.10	4,384.4	256.1	64.4	-254.3	0.00	0.00	0.00	
4,500.0	7.00	14.10	4,483.7	267.9	67.3	-266.0	0.00	0.00	0.00	
4,600.0	7.00	14.10	4,582.9	279.8	70.3	-277.8	0.00	0.00	0.00	
4,693.3	7.00	14.10	4,675.5	290.8	73.1	-288.7	0.00	0.00	0.00	
4,700.0	6.90	14.10	4,682.2	291.6	73.3	-289.5	1.50	-1.50	0.00	
4,800.0	5.40	14.10	4,781.6	302.0	75.9	-299.8	1.50	-1.50	0.00	
4,900.0	3.90	14.10	4,881.3	309.8	77.8	-307.6	1.50	-1.50	0.00	
5,000.0	2.40	14.10	4,981.1	315.2	79.2	-312.9	1.50	-1.50	0.00	

Planning Report

Database:	PEDM	Local Co-ordinate Reference:	Well Ghost Rider 22-15 Fed Com 401H
Company:	PERMIAN	TVD Reference:	WELL @ 3606.0ft (Original Well Elev)
Project:	NW DISTRICT - NM EZ NAD 83	MD Reference:	WELL @ 3606.0ft (Original Well Elev)
Site:	GHOST RIDER 22-15 FED COM PAD (N East) NEW	North Reference:	Grid
Well:	Ghost Rider 22-15 Fed Com 401H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Ghost Rider 22-15 Fed Com 401H		
Design:	w/ lateral targets		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
5,100.0	0.90	14.10	5,081.1	317.9	79.9	-315.7	1.50	-1.50	0.00	
5,159.9	0.00	0.00	5,141.0	318.4	80.0	-316.1	1.50	-1.50	0.00	
5,200.0	0.00	0.00	5,181.1	318.4	80.0	-316.1	0.00	0.00	0.00	
5,300.0	0.00	0.00	5,281.1	318.4	80.0	-316.1	0.00	0.00	0.00	
5,400.0	0.00	0.00	5,381.1	318.4	80.0	-316.1	0.00	0.00	0.00	
5,500.0	0.00	0.00	5,481.1	318.4	80.0	-316.1	0.00	0.00	0.00	
5,600.0	0.00	0.00	5,581.1	318.4	80.0	-316.1	0.00	0.00	0.00	
5,700.0	0.00	0.00	5,681.1	318.4	80.0	-316.1	0.00	0.00	0.00	
5,800.0	0.00	0.00	5,781.1	318.4	80.0	-316.1	0.00	0.00	0.00	
5,900.0	0.00	0.00	5,881.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,000.0	0.00	0.00	5,981.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,100.0	0.00	0.00	6,081.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,200.0	0.00	0.00	6,181.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,300.0	0.00	0.00	6,281.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,400.0	0.00	0.00	6,381.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,500.0	0.00	0.00	6,481.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,600.0	0.00	0.00	6,581.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,700.0	0.00	0.00	6,681.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,800.0	0.00	0.00	6,781.1	318.4	80.0	-316.1	0.00	0.00	0.00	
6,900.0	0.00	0.00	6,881.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,000.0	0.00	0.00	6,981.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,100.0	0.00	0.00	7,081.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,200.0	0.00	0.00	7,181.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,300.0	0.00	0.00	7,281.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,400.0	0.00	0.00	7,381.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,500.0	0.00	0.00	7,481.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,600.0	0.00	0.00	7,581.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,700.0	0.00	0.00	7,681.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,800.0	0.00	0.00	7,781.1	318.4	80.0	-316.1	0.00	0.00	0.00	
7,900.0	0.00	0.00	7,881.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,000.0	0.00	0.00	7,981.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,100.0	0.00	0.00	8,081.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,200.0	0.00	0.00	8,181.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,300.0	0.00	0.00	8,281.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,400.0	0.00	0.00	8,381.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,500.0	0.00	0.00	8,481.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,600.0	0.00	0.00	8,581.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,700.0	0.00	0.00	8,681.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,800.0	0.00	0.00	8,781.1	318.4	80.0	-316.1	0.00	0.00	0.00	
8,900.0	0.00	0.00	8,881.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,000.0	0.00	0.00	8,981.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,100.0	0.00	0.00	9,081.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,200.0	0.00	0.00	9,181.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,300.0	0.00	0.00	9,281.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,400.0	0.00	0.00	9,381.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,500.0	0.00	0.00	9,481.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,600.0	0.00	0.00	9,581.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,700.0	0.00	0.00	9,681.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,800.0	0.00	0.00	9,781.1	318.4	80.0	-316.1	0.00	0.00	0.00	
9,900.0	0.00	0.00	9,881.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,000.0	0.00	0.00	9,981.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,100.0	0.00	0.00	10,081.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,200.0	0.00	0.00	10,181.1	318.4	80.0	-316.1	0.00	0.00	0.00	

Planning Report

Database:	PEDM	Local Co-ordinate Reference:	Well Ghost Rider 22-15 Fed Com 401H
Company:	PERMIAN	TVD Reference:	WELL @ 3606.0ft (Original Well Elev)
Project:	NW DISTRICT - NM EZ NAD 83	MD Reference:	WELL @ 3606.0ft (Original Well Elev)
Site:	GHOST RIDER 22-15 FED COM PAD (N East) NEW	North Reference:	Grid
Well:	Ghost Rider 22-15 Fed Com 401H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Ghost Rider 22-15 Fed Com 401H		
Design:	w/ lateral targets		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
10,300.0	0.00	0.00	10,281.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,400.0	0.00	0.00	10,381.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,500.0	0.00	0.00	10,481.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,600.0	0.00	0.00	10,581.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,700.0	0.00	0.00	10,681.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,800.0	0.00	0.00	10,781.1	318.4	80.0	-316.1	0.00	0.00	0.00	
10,900.0	0.00	0.00	10,881.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,000.0	0.00	0.00	10,981.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,100.0	0.00	0.00	11,081.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,200.0	0.00	0.00	11,181.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,300.0	0.00	0.00	11,281.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,400.0	0.00	0.00	11,381.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,500.0	0.00	0.00	11,481.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,600.0	0.00	0.00	11,581.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,700.0	0.00	0.00	11,681.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,800.0	0.00	0.00	11,781.1	318.4	80.0	-316.1	0.00	0.00	0.00	
11,839.4	0.00	0.00	11,820.5	318.4	80.0	-316.1	0.00	0.00	0.00	
11,900.0	7.27	172.00	11,880.9	314.6	80.5	-312.3	12.00	12.00	0.00	
12,000.0	19.27	172.00	11,978.1	291.9	83.7	-289.5	12.00	12.00	0.00	
12,100.0	31.27	172.00	12,068.3	249.7	89.7	-247.2	12.00	12.00	0.00	
12,200.0	43.27	172.00	12,147.8	189.9	98.1	-187.1	12.00	12.00	0.00	
12,300.0	55.27	172.00	12,212.9	115.0	108.6	-112.0	12.00	12.00	0.00	
12,400.0	67.27	172.00	12,260.9	28.3	120.8	-25.0	12.00	12.00	0.00	
12,500.0	79.27	172.00	12,289.6	-66.4	134.1	70.0	12.00	12.00	0.00	
12,587.7	89.79	172.00	12,298.0	-152.7	146.2	156.6	12.00	12.00	0.00	
12,600.0	89.79	172.37	12,298.0	-164.9	147.9	168.8	3.00	0.00	3.00	
12,700.0	89.79	175.37	12,298.4	-264.3	158.6	268.5	3.00	0.00	3.00	
12,800.0	89.79	178.37	12,298.7	-364.2	164.0	368.5	3.00	0.00	3.00	
12,844.1	89.79	179.69	12,298.9	-408.2	164.8	412.5	3.00	0.00	3.00	
12,900.0	89.79	179.69	12,299.1	-464.1	165.1	468.4	0.00	0.00	0.00	
13,000.0	89.79	179.69	12,299.5	-564.1	165.6	568.4	0.00	0.00	0.00	
13,100.0	89.79	179.69	12,299.8	-664.1	166.1	668.4	0.00	0.00	0.00	
13,200.0	89.79	179.69	12,300.2	-764.1	166.7	768.4	0.00	0.00	0.00	
13,300.0	89.79	179.69	12,300.5	-864.1	167.2	868.3	0.00	0.00	0.00	
13,400.0	89.79	179.69	12,300.9	-964.1	167.8	968.3	0.00	0.00	0.00	
13,500.0	89.79	179.69	12,301.3	-1,064.1	168.3	1,068.3	0.00	0.00	0.00	
13,600.0	89.79	179.69	12,301.6	-1,164.1	168.8	1,168.3	0.00	0.00	0.00	
13,700.0	89.79	179.69	12,302.0	-1,264.1	169.4	1,268.2	0.00	0.00	0.00	
13,800.0	89.79	179.69	12,302.3	-1,364.1	169.9	1,368.2	0.00	0.00	0.00	
13,900.0	89.79	179.69	12,302.7	-1,464.1	170.4	1,468.2	0.00	0.00	0.00	
14,000.0	89.79	179.69	12,303.1	-1,564.1	171.0	1,568.2	0.00	0.00	0.00	
14,100.0	89.79	179.69	12,303.4	-1,664.1	171.5	1,668.2	0.00	0.00	0.00	
14,200.0	89.79	179.69	12,303.8	-1,764.1	172.1	1,768.1	0.00	0.00	0.00	
14,300.0	89.79	179.69	12,304.2	-1,864.1	172.6	1,868.1	0.00	0.00	0.00	
14,400.0	89.79	179.69	12,304.5	-1,964.1	173.1	1,968.1	0.00	0.00	0.00	
14,500.0	89.79	179.69	12,304.9	-2,064.1	173.7	2,068.1	0.00	0.00	0.00	
14,600.0	89.79	179.69	12,305.2	-2,164.1	174.2	2,168.0	0.00	0.00	0.00	
14,700.0	89.79	179.69	12,305.6	-2,264.1	174.8	2,268.0	0.00	0.00	0.00	
14,800.0	89.79	179.69	12,306.0	-2,364.1	175.3	2,368.0	0.00	0.00	0.00	
14,900.0	89.79	179.69	12,306.3	-2,464.1	175.8	2,468.0	0.00	0.00	0.00	
15,000.0	89.79	179.69	12,306.7	-2,564.1	176.4	2,567.9	0.00	0.00	0.00	
15,100.0	89.79	179.69	12,307.0	-2,664.1	176.9	2,667.9	0.00	0.00	0.00	
15,200.0	89.79	179.69	12,307.4	-2,764.1	177.4	2,767.9	0.00	0.00	0.00	

Planning Report

Database:	PEDM	Local Co-ordinate Reference:	Well Ghost Rider 22-15 Fed Com 401H
Company:	PERMIAN	TVD Reference:	WELL @ 3606.0ft (Original Well Elev)
Project:	NW DISTRICT - NM EZ NAD 83	MD Reference:	WELL @ 3606.0ft (Original Well Elev)
Site:	GHOST RIDER 22-15 FED COM PAD (N East) NEW	North Reference:	Grid
Well:	Ghost Rider 22-15 Fed Com 401H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Ghost Rider 22-15 Fed Com 401H		
Design:	w/ lateral targets		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
15,300.0	89.79	179.69	12,307.8	-2,864.1	178.0	2,867.9	0.00	0.00	0.00
15,400.0	89.79	179.69	12,308.1	-2,964.1	178.5	2,967.8	0.00	0.00	0.00
15,500.0	89.79	179.69	12,308.5	-3,064.1	179.1	3,067.8	0.00	0.00	0.00
15,600.0	89.79	179.69	12,308.8	-3,164.1	179.6	3,167.8	0.00	0.00	0.00
15,700.0	89.79	179.69	12,309.2	-3,264.1	180.1	3,267.8	0.00	0.00	0.00
15,800.0	89.79	179.69	12,309.6	-3,364.1	180.7	3,367.7	0.00	0.00	0.00
15,900.0	89.79	179.69	12,309.9	-3,464.1	181.2	3,467.7	0.00	0.00	0.00
16,000.0	89.79	179.69	12,310.3	-3,564.1	181.8	3,567.7	0.00	0.00	0.00
16,100.0	89.79	179.69	12,310.7	-3,664.1	182.3	3,667.7	0.00	0.00	0.00
16,200.0	89.79	179.69	12,311.0	-3,764.1	182.8	3,767.6	0.00	0.00	0.00
16,300.0	89.79	179.69	12,311.4	-3,864.1	183.4	3,867.6	0.00	0.00	0.00
16,400.0	89.79	179.69	12,311.7	-3,964.1	183.9	3,967.6	0.00	0.00	0.00
16,500.0	89.79	179.69	12,312.1	-4,064.1	184.4	4,067.6	0.00	0.00	0.00
16,600.0	89.79	179.69	12,312.5	-4,164.1	185.0	4,167.6	0.00	0.00	0.00
16,700.0	89.79	179.69	12,312.8	-4,264.1	185.5	4,267.5	0.00	0.00	0.00
16,800.0	89.79	179.69	12,313.2	-4,364.1	186.1	4,367.5	0.00	0.00	0.00
16,900.0	89.79	179.69	12,313.5	-4,464.1	186.6	4,467.5	0.00	0.00	0.00
17,000.0	89.79	179.69	12,313.9	-4,564.1	187.1	4,567.5	0.00	0.00	0.00
17,100.0	89.79	179.69	12,314.3	-4,664.1	187.7	4,667.4	0.00	0.00	0.00
17,200.0	89.79	179.69	12,314.6	-4,764.1	188.2	4,767.4	0.00	0.00	0.00
17,300.0	89.79	179.69	12,315.0	-4,864.1	188.7	4,867.4	0.00	0.00	0.00
17,304.6	89.79	179.69	12,315.0	-4,868.7	188.8	4,872.0	0.00	0.00	0.00
17,400.0	89.79	179.69	12,315.3	-4,964.1	189.3	4,967.4	0.01	-0.01	0.00
17,481.9	89.78	179.69	12,315.7	-5,045.9	189.7	5,049.2	0.01	-0.01	0.00
17,500.0	89.78	179.69	12,315.7	-5,064.1	189.8	5,067.3	0.00	0.00	0.00
17,600.0	89.78	179.69	12,316.1	-5,164.1	190.4	5,167.3	0.00	0.00	0.00
17,700.0	89.78	179.69	12,316.5	-5,264.0	190.9	5,267.3	0.00	0.00	0.00
17,800.0	89.78	179.69	12,316.9	-5,364.0	191.4	5,367.3	0.00	0.00	0.00
17,900.0	89.78	179.69	12,317.2	-5,464.0	192.0	5,467.2	0.00	0.00	0.00
18,000.0	89.78	179.69	12,317.6	-5,564.0	192.5	5,567.2	0.00	0.00	0.00
18,100.0	89.78	179.69	12,318.0	-5,664.0	193.0	5,667.2	0.00	0.00	0.00
18,200.0	89.78	179.69	12,318.4	-5,764.0	193.5	5,767.2	0.00	0.00	0.00
18,300.0	89.78	179.69	12,318.8	-5,864.0	194.1	5,867.1	0.00	0.00	0.00
18,400.0	89.78	179.69	12,319.2	-5,964.0	194.6	5,967.1	0.00	0.00	0.00
18,500.0	89.78	179.69	12,319.5	-6,064.0	195.1	6,067.1	0.00	0.00	0.00
18,600.0	89.78	179.69	12,319.9	-6,164.0	195.7	6,167.1	0.00	0.00	0.00
18,700.0	89.78	179.69	12,320.3	-6,264.0	196.2	6,267.0	0.00	0.00	0.00
18,800.0	89.78	179.69	12,320.7	-6,364.0	196.7	6,367.0	0.00	0.00	0.00
18,900.0	89.78	179.69	12,321.1	-6,464.0	197.3	6,467.0	0.00	0.00	0.00
19,000.0	89.78	179.69	12,321.4	-6,564.0	197.8	6,567.0	0.00	0.00	0.00
19,100.0	89.78	179.69	12,321.8	-6,664.0	198.3	6,666.9	0.00	0.00	0.00
19,200.0	89.78	179.69	12,322.2	-6,764.0	198.9	6,766.9	0.00	0.00	0.00
19,300.0	89.78	179.69	12,322.6	-6,864.0	199.4	6,866.9	0.00	0.00	0.00
19,400.0	89.78	179.69	12,323.0	-6,964.0	199.9	6,966.9	0.00	0.00	0.00
19,500.0	89.78	179.69	12,323.3	-7,064.0	200.5	7,066.8	0.00	0.00	0.00
19,600.0	89.78	179.69	12,323.7	-7,164.0	201.0	7,166.8	0.00	0.00	0.00
19,700.0	89.78	179.69	12,324.1	-7,264.0	201.5	7,266.8	0.00	0.00	0.00
19,800.0	89.78	179.69	12,324.5	-7,364.0	202.1	7,366.8	0.00	0.00	0.00
19,900.0	89.78	179.69	12,324.9	-7,464.0	202.6	7,466.8	0.00	0.00	0.00
19,936.1	89.78	179.69	12,325.0	-7,500.1	202.8	7,502.8	0.00	0.00	0.00

Planning Report

Database:	PEDM	Local Co-ordinate Reference:	Well Ghost Rider 22-15 Fed Com 401H
Company:	PERMIAN	TVD Reference:	WELL @ 3606.0ft (Original Well Elev)
Project:	NW DISTRICT - NM EZ NAD 83	MD Reference:	WELL @ 3606.0ft (Original Well Elev)
Site:	GHOST RIDER 22-15 FED COM PAD (N East) NEW	North Reference:	Grid
Well:	Ghost Rider 22-15 Fed Com 401H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Ghost Rider 22-15 Fed Com 401H		
Design:	w/ lateral targets		

Design Targets									
Target Name									
- hit/miss target	Dip Angle	Dip Dir.	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
- Shape	(°)	(°)	(ft)	(ft)	(ft)	(ft)	(ft)		
BHL Ghost Rider 22-15 I	0.00	0.00	9,490.4	-7,504.1	-160.0	435,682.30	750,739.30	32° 11' 45.433 N	103° 39' 22.988 W
- plan misses target center by 2857.7ft at 19927.4ft MD (12325.0 TVD, -7491.4 N, 202.8 E)									
- Point									
t2 Ghost Rider 22-15 Fe	0.00	0.00	12,315.0	-4,868.7	188.8	438,317.72	751,088.07	32° 12' 11.490 N	103° 39' 18.736 W
- plan hits target center									
- Point									
BHL Ghost Rider 22-15 I	0.00	0.00	12,325.0	-7,500.1	202.8	435,686.30	751,102.10	32° 11' 45.450 N	103° 39' 18.766 W
- plan hits target center									
- Point									

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	APACHE CORPORATION
LEASE NO.:	NMNM039880
WELL NAME & NO.:	GHOST RIDER 22 15 FEDERAL COM 401H
SURFACE HOLE FOOTAGE:	2272'S & 540'E
BOTTOM HOLE FOOTAGE:	50'S & 380'E
LOCATION:	Section 15, T.24 S., R.32 E., NMP
COUNTY:	Lea County, New Mexico

COA

H2S	<input checked="" type="radio"/> Yes	<input type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input type="radio"/> Multibowl	<input checked="" type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input type="checkbox"/> Fluid Filled	<input checked="" type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit

All Previous COAs Still Apply.

NOTE: Approved for 10M BOP / BOPE and testing accordance to OO#2 requirements.

Flex hose variance is approved.

Break Testing is approved (**Note: For 5M BOPE or less**).

Batch drilling is approved.

A. CASING

Casing Design:

1. The **13-3/8** inch surface casing shall be set at approximately **1,114** feet (a minimum of **25 feet (Lea County)** into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.

- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The 7-5/8 inch intermediate casing shall be set at approximately **11,639** feet. The minimum required fill of cement behind the 7-5/8 inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.
Excess cement calculates to -33%, additional cement might be required

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
- b. Second stage above DV tool:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office.
Excess cement calculates to -79%, additional cement might be required

Operator has proposed to pump down 7-5/8" X 13-3/8" annulus. Operator must run a CBL / Echo-Meter from TD of the 7-5/8" casing to surface. Submit results to BLM.

3. The minimum required fill of cement behind the 5-1/2 inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

Operator has proposed to pump down 5-1/2" X 7-5/8" annulus. Operator must run a CBL / Echo-Meter from TD of the 5-1/2" casing to surface. Submit results to BLM.

B. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
- 2.

Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi**.
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **10,000 (10M) psi**. **Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi**.

Option 2:

1. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi**. **Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi**.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

C. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Carlsbad Field Office, 620 E Greene St. Carlsbad, New Mexico 88220, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

BOPE Break Testing Variance (Note: For 5M BOPE or less)

- BOPE Break Testing is ONLY permitted for 5M BOPE or less.
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required.
- The BLM is to be contacted **(575-393-3612 Lea County)** 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per Onshore Oil and Gas Order No. 2.

OTA06272022

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 120902

CONDITIONS

Operator: APACHE CORPORATION 303 Veterans Airpark Ln Midland, TX 79705	OGRID: 873
	Action Number: 120902
	Action Type: [C-103] NOI Change of Plans (C-103A)

CONDITIONS

Created By	Condition	Condition Date
pkautz	PREVIOUS COA'S APPLY	6/28/2022
