

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-015-54017
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720
District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-015-54017	² Pool Code 98220	³ Pool Name PURPLE SAGE; WOLFCAMP (GAS)
⁴ Property Code 334561	⁵ Property Name MAZER NORTH 17 WA FED COM	
⁷ OGRID No. 372098	⁸ Operator Name MARATHON OIL PERMIAN LLC	
		⁶ Well Number 1H
		⁹ Elevation 2872'

¹⁰ Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	20	26S	29E		965	NORTH	660	EAST	EDDY

¹¹ Bottom Hole Location If Different From Surface

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
A	17	26S	29E		100	NORTH	330	EAST	EDDY

¹² Dedicated Acres 320.0	¹³ Joint or Infill	¹⁴ Consolidation Code	¹⁵ Order No.
---	-------------------------------	----------------------------------	-------------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

	<p>CORNER COORDINATES NAD 83, SPCS NM EAST A - X: 645352.76' / Y: 381957.62' B - X: 645343.17' / Y: 379289.78' C - X: 645175.01' / Y: 376837.52' D - X: 642535.61' / Y: 376817.53' E - X: 642607.65' / Y: 379342.99' F - X: 642682.11' / Y: 381953.00'</p>	<p>17 OPERATOR CERTIFICATION I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</p> <p>06/04/2021</p> <p>Signature _____ Date</p> <p>Melissa Szudera</p> <p>Printed Name</p> <p>mszudera@marathonoil.com</p> <p>E-mail Address</p>
	<p>CORNER COORDINATES NAD 27, SPCS NM EAST A - X: 604167.34' / Y: 381899.95' B - X: 604157.68' / Y: 379232.16' C - X: 603989.47' / Y: 376779.95' D - X: 601350.13' / Y: 376759.99' E - X: 601422.24' / Y: 379285.39' F - X: 601496.75' / Y: 381895.34'</p>	
	<p>LAST TAKE POINT/BOTTOM HOLE LOCATION 100' FNL 330' FEL, SECTION 17 NAD 83, SPCS NM EAST X: 645022.39' / Y: 381857.05' LAT: 32.04936322N / LON: 103.99867448W NAD 27, SPCS NM EAST X: 603836.98' / Y: 381799.38' LAT: 32.04923842N / LON: 103.99819121W</p>	
	<p>KICK OFF POINT/FIRST TAKE POINT 100' FSL 330' FEL, SECTION 17 NAD 83, SPCS NM EAST X: 644850.93' / Y: 376935.07' LAT: 32.03583446N / LON: 103.99927705W NAD 27, SPCS NM EAST X: 603665.39' / Y: 376877.50' LAT: 32.03570950N / LON: 103.99879422W</p>	
<p>SURFACE HOLE LOCATION 965' FNL 660' FEL, SECTION 20 NAD 83, SPCS NM EAST X: 644521.27' / Y: 375867.75' LAT: 32.03290325N / LON: 104.00035151W NAD 27, SPCS NM EAST X: 603335.72' / Y: 375810.19' LAT: 32.03277824N / LON: 103.99986874W</p>		<p>18 SURVEYOR CERTIFICATION I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</p> <p>JUNE 3, 2021</p> <p>Date of Survey</p> <p>Signature and Seal of Professional Surveyor</p> <p>DAVID W. MYERS NEW MEXICO PROFESSIONAL SURVEYOR 11403</p>
<p>SHEET 1 OF 4 JOB No. R3893_031 REV 0 DEF 5/25/2021</p>		<p>Certificate Number DAVID W. MYERS 11403</p>

Distances/areas relative to NAD 83 Combined Scale Factor: 0.99978647 Convergence Angle: 00°10'35.39608"

☐ Horizontal Spacing Unit

State of New Mexico
Energy, Minerals and Natural Resources Department

Submit Electronically
Via E-permitting

Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: MARATHON OIL PERMIAN, LLC. **OGRID:** 372098 **Date:** 07 / 25 / 2023

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Mazer North 17 WA FED COM 1H		H-20-26S-29E	960 FNL 660 FNL	2700	5200	4900
Mazer North 17 WA FED COM 2H		H-20-26S-29E	960FNL 660 FNL	2700	5200	4900

IV. Central Delivery Point Name: Blue Steel WD Fee CTB [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Mazer North 17 WA FED COM 1H		02/20/2025	03/20/2025	09/20/2025	10/25/2025	10/25/2025
Mazer North 17 WA FED COM 2H		03/20/2025	04/20/2025	10/20/2025	11/25/2025	11/25/2025

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: *Thomas Moore*

Printed Name: Thomas Moore

Title: Regulatory and Land Technician

E-mail Address: tmoore@marathonoil.com

Date: 7/25/2023

Phone:

OIL CONSERVATION DIVISION
(Only applicable when submitted as a standalone form)

Approved By:

Title:

Approval Date:

Conditions of Approval:

APPENDIX

Section 1 - Parts VI, VII, and VIII

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

- Separation equipment is sized to allow for retention time and velocity to adequately separate oil, gas, and water at anticipated peak rates.
- All central tank battery equipment is designed to efficiently capture the remaining gas from the liquid phase.
- Valves and meters are designed to service without flow interruption or venting of gas.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

◆ **19.15.27.8 (A) – Venting and Flaring Of Natural Gas**

- Marathon Oil Permian's field operations are designed with the goal of minimizing flaring and preventing venting of natural gas. If capturing the gas is not possible then the gas is combusted/flared using properly sized flares or combustors in accordance with state air permit rules.

◆ **19.15.27.8 (B) – Venting and Flaring During Drilling Operations**

- A properly-sized flare stack will be located at a minimum 100' from the nearest surface hole location on the pad.
- All natural gas produced during drilling operations will be flared. Venting will only occur if there is an equipment malfunction and/or to avoid risk of an immediate and substantial adverse impact on safety, public health, or the environment.

◆ **19.15.27.8 (C) – Venting and Flaring During Completion or Recompletion Operations**

- During all phases of flowback, wells will flow through a sand separator, or other appropriate flowback separation equipment, and the well stream will be directed to a central tank battery (CTB) through properly sized flowlines.
- The CTB will have properly sized separation equipment for maximum anticipated flow rates.
- Multiple stages of separation will be used to separate gas from liquids. All gas will be routed to a sales outlet. Fluids will be routed to tanks equipped with a closed loop system that will recover any residual gas from the tanks and route such gas to a sales outlet.

◆ **19.15.27.8 (D) – Venting and Flaring During Production Operations**

- During production, the well stream will be routed to the CTB where multiple stages of separation will separate gas from liquids. All gas will be routed to a sales outlet. Fluids will be routed to tanks equipped with a closed loop system that will recover any residual gas from the tanks and route such gas to a sales outlet, minimizing tank emissions.
- Flares are equipped with auto-ignition systems and continuous pilot operations.
- Automatic gauging equipment is installed on all tanks.

◆ **19.15.27.8 (E) – Performance Standards**

- Production equipment will be designed to handle maximum anticipated rates and pressure.
- Automatic gauging equipment is installed on all tanks to minimize venting.
- All flared gas will be combusted in a flare stack that is properly sized and designed to ensure proper combustion.
- Flares are equipped with continuous pilots and auto-ignitors along with remote monitoring of the pilot status.
- Weekly AVOs and monthly LDAR inspections will be performed on all wells and facilities that produce more than 60 MCFD.
- Gas/H₂S detectors will be installed throughout the facilities and wellheads to detect leaks and enable timely repairs.

◆ 19.15.27.8 (F) – Measurement or Estimation of Vented and Flared Natural Gas

- All high pressure flared gas is measured by equipment conforming to API 14.10.
- No meter bypasses are installed.
- When metering is not practical due to low pressure/low rate, the vented or flared volume will be estimated through flare flow curves with the assistance of air emissions consultants, as necessary.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

- Marathon Oil Permian will use best management practices to vent as minimally as possible during well intervention operations and downhole well maintenance.
- All natural gas is routed into the gas gathering system and directed to one of Marathon Oil Permian's multiple gas sales outlets.
- All venting events will be recorded and all start-up, shutdown, maintenance logs will be kept for control equipment.
- All control equipment will be maintained to provide highest run-time possible.
- All procedures are drafted to keep venting and flaring to the absolute minimum.



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

07/21/2023

APD ID: 10400076437

Submission Date: 06/24/2021

Highlighted data
reflects the most
recent changes

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: MAZER NORTH 17 WA FED COM

Well Number: 1H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
6091392	PERMIAN	2872	0	0	ANHYDRITE	NONE	N
6194686	RUSTLER	2452	420	420	ANHYDRITE	OTHER : Brine	N
8369973	SALADO	2086	786	786	ANHYDRITE, SALT	OTHER : BRINE	N
6091394	CASTILE	1840	1032	1032	ANHYDRITE, SALT	OTHER : BRINE	N
6091397	BASE OF SALT	90	2782	2782	ANHYDRITE, SALT	OTHER : Brine	N
6091398	LAMAR	90	2782	2782	SANDSTONE, SHALE	NONE	N
6091402	BELL CANYON	49	2823	2823	SANDSTONE	OIL	N
6091405	CHERRY CANYON	-1026	3898	3898	SANDSTONE	OIL	N
6091406	BRUSHY CANYON	-2066	4938	4938	SANDSTONE	OIL	N
6091407	BONE SPRINGS	-3684	6556	6556	LIMESTONE	NONE	N
8369974	UPPER AVALON SHALE	-3708	6580	6580	SHALE	OIL	N
6091408	BONE SPRING 1ST	-4585	7457	7457	SANDSTONE	OIL	N
8369975	BONE SPRING 2ND	-4866	7738	7738	LIMESTONE, SHALE	NONE	N
6091409	BONE SPRING 2ND	-5359	8231	8231	SANDSTONE	OIL	N
8369976	BONE SPRING 3RD	-5757	8629	8629	LIMESTONE	OIL	N
6091410	BONE SPRING 3RD	-6437	9309	9309	SANDSTONE	OIL	N
6091411	WOLFCAMP	-6809	9681	9681	OTHER, SANDSTONE, SHALE : Carbonate	NATURAL GAS, OIL	Y

Operator Name: MARATHON OIL PERMIAN LLC**Well Name:** MAZER NORTH 17 WA FED COM**Well Number:** 1H**Section 2 - Blowout Prevention****Pressure Rating (PSI):** 10M**Rating Depth:** 10000**Equipment:** 13 5/8 BOP Annular (5,000 psi WP) and BOP Stack (10,000 psi WP) will be installed and tested before drilling all holes.**Requesting Variance?** YES**Variance request:** A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.**Testing Procedure:** BOP/BOPE will be tested to 250 psi low and 50% WP for Annular and 10,000 psi for BOP Stack. Testing will be conducted by an independent service company per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the Equipment Description above. If the system is upgraded all the components installed will be functional and tested. Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock, full opening safety valve / inside BOP and choke lines and choke manifold. See attached schematics. Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i. A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. See attached schematic.**Choke Diagram Attachment:**

2_5M_10M.TWO_CHOKE_MANIFOLD.BLM.r1_20210623093839.pdf

2_Choke_Line_Flex_III_Rig_20210623093839.pdf

2_Contitech_Hose_SN_663393_20210623093839.pdf

2_Choke_Line_Test_Chart_SN_63393_20210623093839.pdf

BOP Diagram Attachment:

2_10.75_x_7.625_x_5.5_WH_Design_20210623093853.pdf

2_10M_Flex.BOPE_x_5M_ANNULAR.BLM_20210623093853.pdf

Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	490	0	490	2872	2382	490	J-55	54.5	BUTT	5.22	1.81	BUOY	4.52	BUOY	4.52
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	9500	0	9405	2901	-6533	9500	P-110	40	BUTT	1.2	1.42	BUOY	2.44	BUOY	2.44

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: MAZER NORTH 17 WA FED COM

Well Number: 1H

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
3	PRODUCTI ON	8.75	5.5	NEW	API	N	0	14852	0	10078	2915	-7206	14852	P- 110	23	OTHER - TLW	2.53	1.26	BUOY	2.22	BUOY	2.22

Casing Attachments

Casing ID: 1StringSURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

3_Casing_Surface_13.375_DL_20220322083103.pdf

Casing ID: 2StringINTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

3_Casing_Intermediate_9.625_DL_20220322083200.pdf

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: MAZER NORTH 17 WA FED COM

Well Number: 1H

Casing Attachments

Casing ID: 3 String PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

3_Casing_Production_5.5_DL_TLW_SC_20220322083301.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
PRODUCTION	Lead		0	0	0	0	0	0	0	None, Tail Only.	None, Tail Only.
PRODUCTION	Tail		9200	1485 2	1103	1.68	13	1853	25	Class H	Retarder, Extender, Fluid Loss, Suspension Agent.
SURFACE	Lead		0	190	101	2.12	12.5	214	25	Class C	Extender, Accelerator, LCM
SURFACE	Tail		190	490	197	1.32	14.8	260	25	CLASS C	Accelerator
INTERMEDIATE	Lead		0	9000	1630	2.18	12.4	3554	25	CLASS C	Extender, Accelerator, LCM
INTERMEDIATE	Tail		9000	9500	147	1.33	14.8	196	25	CLASS C	Retarder

Operator Name: MARATHON OIL PERMIAN LLC**Well Name:** MAZER NORTH 17 WA FED COM**Well Number:** 1H**Section 5 - Circulating Medium****Mud System Type:** Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:****Describe what will be on location to control well or mitigate other conditions:** The necessary mud products for additional weight and fluid loss control will be on location at all times.**Describe the mud monitoring system utilized:** Losses or gains in the mud system will be monitored visually/manually as well as with an electronic PVT.**Circulating Medium Table**

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	490	WATER-BASED MUD	8.4	8.8							
490	9500	OTHER : Brine or OBM	9.2	10.2							
9500	14852	OIL-BASED MUD	10.5	12.5							

Section 6 - Test, Logging, Coring**List of production tests including testing procedures, equipment and safety measures:**

GR from TD to Surface (horizontal well - vertical portion of well)

List of open and cased hole logs run in the well:

GAMMA RAY LOG,

Coring operation description for the well:

Run gamma-ray (GR), corrected neutron log (CNL) or analogous to surface for future development of the area, one per shared well pad not to exceed 200 radial distance.

Operator Name: MARATHON OIL PERMIAN LLC**Well Name:** MAZER NORTH 17 WA FED COM**Well Number:** 1H

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 6551**Anticipated Surface Pressure:** 4333**Anticipated Bottom Hole Temperature(F):** 195**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO**Describe:****Contingency Plans geohazards description:****Contingency Plans geohazards****Hydrogen Sulfide drilling operations plan required?** YES**Hydrogen sulfide drilling operations**

7_GCP_MAZER_NORTH_17_FED_COM_WA1H2H_06.16_20210623105706.pdf

7_MAZER_NORTH_1H2H_H2S_Layout_20210623105706.pdf

7_MAZER_NORTH_1H2H_Rig_Layout_20210623105706.pdf

7_MAZER_NORTH_17_FED_COM_1H2H_H2S_Contingency_Plan_060721_20210623105707.pdf

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

8_Marathon_MazerN17_1H_PrelimA_WPReport_20210623114541.pdf

8_Marathon_MazerN17_1H_PrelimA_36x48WM_20210623114541.PDF

8_MAZER_NORTH_1H2H_Fed_Lse_Int_Doc_20210623114610.pdf

Drill_Ops_Plan_Mazer_North_17_WA_Fed_Com_1H_rev_03.14.22_20220322083727.pdf

Other proposed operations facets description:

- Kelly cock will be in the drill string at all times.
- A full opening drill pipe stabbing valve having the appropriate connections will be on the rig floor unobstructed and readily accessible at all times.
- Hydrogen Sulfide detection equipment will be in operation after drilling out the surface casing shoe until the production casing is cemented. Breathing equipment will be on location upon drilling the surface casing shoe until total depth is reached. If Hydrogen Sulfide is encountered, measured amounts and formations will be reported to the BLM.

Potential Hazards:

- H2S detection equipment will be in operation after drilling out the surface casing shoe until the production casing has been cemented. Breathing equipment will be on location from drilling out the surface shoe until production casing is cemented. If H2S is encountered the operator will comply with Onshore Order #6.
- No abnormal temperatures or pressures are anticipated. All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well. Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely.
- No losses are anticipated at this time.
- All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well.
- Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely.

Other proposed operations facets attachment:

Operator Name: MARATHON OIL PERMIAN LLC

Well Name: MAZER NORTH 17 WA FED COM

Well Number: 1H

8_Batch_Drilling_Plan_and_Surface_Rig_Request_20210623114620.pdf

Other Variance attachment:

CONFIDENTIAL

LEGEND

PROPOSED WELL PAD —————

STAKED PIPELINE -|-|-|-|

EXISTING LEASE ROAD - - - - -

RIG LAYOUT

MAZER NORTH 17 FED COM
SEC. 20 TWP. 26-S RGE. 29-E
SURVEY: N.M.P.M.

COUNTY: EDDY


COUNTY: EDDY

OPERATOR: MARATHON OIL PERMIAN LLC
U.S.G.S. TOPOGRAPHIC MAP: RED BLUFF, N.M.



MAZER NORTH 17 WA FED COM 2H
MARATHON OIL PERMIAN LLC
965' FNL 690' FEL, SECTION 20
NAD 83, SPCS NM EAST
X: 644491.27' / Y: 375867.75'
LAT: 32.03290350N / LON: 104.00044832W
NAD 27, SPCS NM EAST
X: 603305.72' / Y: 375810.19'
LAT: 32.03277850N / LON: 103.99996555W
ELEVATION = 2.872'

MAZER NORTH 17 WA FED COM 1H
MARATHON OIL PERMIAN LLC
965' FNL 660' FEL, SECTION 20
NAD 83, SPCS NM EAST
X: 644521.27' / Y: 375867.75'
LAT: 32.03290325N / LON: 104.00035151W
NAD 27, SPCS NM EAST
X: 603335.72' / Y: 375810.19'
LAT: 32.03277824N / LON: 103.99986874W
ELEVATION = 2.872'

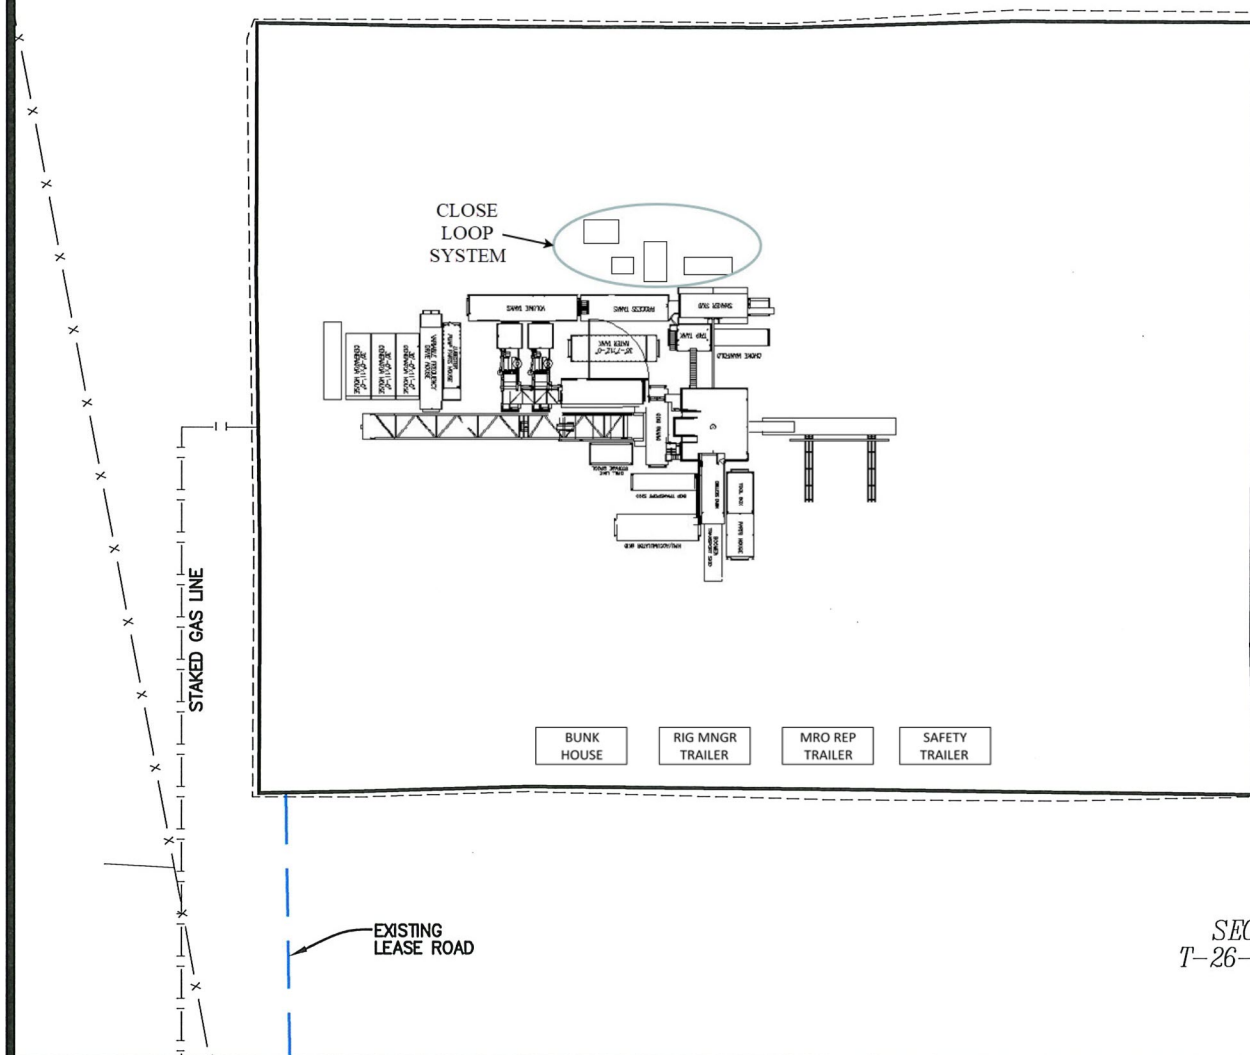

SECTION 20,
T-26-S, R-29-E

1	06/03/2021	DEF
REV.	DATE	BY

NOTE:
THIS IS NOT A BOUNDARY SURVEY,
APPARENT PROPERTY CORNERS AND
PROPERTY LINES ARE SHOWN FOR
INFORMATION ONLY. BOUNDARY DATA SHOWN
IS FROM STATE OF NEW MEXICO OIL
CONSERVATION DIVISION FORM C-102
INCLUDED IN THIS SUBMITTAL.

50' 0' 50' 100'

SCALE: 1" = 100'

SHEET 5 OF 6

**PREPARED BY:
R-SQUARED GLOBAL, LLC
510 TRENTON ST., UNIT B
WEST MONROE, LA 71291
318-323-6900 OFFICE
JOB No. R3893_031**



Pro Directional Survey Report

Marathon Oil

Company:	Marathon Oil	Local Co-ordinate Reference:	Well No. 2H
Project:	Eddy County, NM	TVD Reference:	well @ 2899.00usft
Site:	Mazer North 17	MD Reference:	well @ 2899.00usft
Well:	No. 2H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	Prelim Plan A	Database:	WellPlanner1

Project	Eddy County, NM		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site		Mazer North 17			
Site Position:		Northing:	375,810.19 usft	Latitude:	32.032778
From:	Map	Easting:	603,335.72 usft	Longitude:	-103.999869
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "	Grid Convergence:	0.18 °

Well		No. 2H				
Well Position	+N/-S	0.00 usft	Northing:	375,810.19 usft	Latitude:	32.032779
	+E/-W	0.00 usft	Easting:	603,305.72 usft	Longitude:	-103.999966
Position Uncertainty		0.00 usft	Wellhead Elevation:	usft	Ground Level:	2,872.00 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM	6/3/2021	6.62	59.58	47,567.90

Design	Prelim Plan A				
Audit Notes:					
Version:	Phase:	PLAN	Tie On Depth:	0.00	
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	2.02	

Survey Tool Program	Date	6/4/2021			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.00	14,679.92	Prelim Plan A (OH)	MWD+HDGM	OWSG MWD + HRGM	

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00	
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00	
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00	
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00	
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00	
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00	
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00	



Pro Directional Survey Report

MarathonOil

Company:	Marathon Oil	Local Co-ordinate Reference:	Well No. 2H
Project:	Eddy County, NM	TVD Reference:	well @ 2899.00usft
Site:	Mazer North 17	MD Reference:	well @ 2899.00usft
Well:	No. 2H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	Prelim Plan A	Database:	WellPlanner1

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00
Start Build 2.00									
1,600.00	2.00	344.12	1,599.98	1.68	-0.48	1.66	2.00	2.00	0.00
1,700.00	4.00	344.12	1,699.84	6.71	-1.91	6.64	2.00	2.00	0.00
1,800.00	6.00	344.12	1,799.45	15.09	-4.29	14.93	2.00	2.00	0.00
1,900.00	8.00	344.12	1,898.70	26.82	-7.63	26.53	2.00	2.00	0.00
2,000.00	10.00	344.12	1,997.47	41.86	-11.91	41.42	2.00	2.00	0.00
Start 5859.01 hold at 2000.00 MD									
2,100.00	10.00	344.12	2,095.95	58.56	-16.66	57.94	0.00	0.00	0.00
2,200.00	10.00	344.12	2,194.43	75.27	-21.41	74.46	0.00	0.00	0.00
2,300.00	10.00	344.12	2,292.91	91.97	-26.16	90.99	0.00	0.00	0.00
2,400.00	10.00	344.12	2,391.39	108.67	-30.92	107.51	0.00	0.00	0.00
2,500.00	10.00	344.12	2,489.87	125.37	-35.67	124.04	0.00	0.00	0.00
2,600.00	10.00	344.12	2,588.35	142.07	-40.42	140.56	0.00	0.00	0.00
2,700.00	10.00	344.12	2,686.83	158.78	-45.17	157.09	0.00	0.00	0.00
2,800.00	10.00	344.12	2,785.31	175.48	-49.92	173.61	0.00	0.00	0.00
2,900.00	10.00	344.12	2,883.79	192.18	-54.67	190.13	0.00	0.00	0.00
3,000.00	10.00	344.12	2,982.27	208.88	-59.42	206.66	0.00	0.00	0.00
3,100.00	10.00	344.12	3,080.75	225.58	-64.18	223.18	0.00	0.00	0.00
3,200.00	10.00	344.12	3,179.23	242.29	-68.93	239.71	0.00	0.00	0.00
3,300.00	10.00	344.12	3,277.72	258.99	-73.68	256.23	0.00	0.00	0.00
3,400.00	10.00	344.12	3,376.20	275.69	-78.43	272.76	0.00	0.00	0.00
3,500.00	10.00	344.12	3,474.68	292.39	-83.18	289.28	0.00	0.00	0.00
3,600.00	10.00	344.12	3,573.16	309.10	-87.93	305.80	0.00	0.00	0.00
3,700.00	10.00	344.12	3,671.64	325.80	-92.68	322.33	0.00	0.00	0.00
3,800.00	10.00	344.12	3,770.12	342.50	-97.44	338.85	0.00	0.00	0.00
3,900.00	10.00	344.12	3,868.60	359.20	-102.19	355.38	0.00	0.00	0.00
4,000.00	10.00	344.12	3,967.08	375.90	-106.94	371.90	0.00	0.00	0.00
4,100.00	10.00	344.12	4,065.56	392.61	-111.69	388.42	0.00	0.00	0.00
4,200.00	10.00	344.12	4,164.04	409.31	-116.44	404.95	0.00	0.00	0.00
4,300.00	10.00	344.12	4,262.52	426.01	-121.19	421.47	0.00	0.00	0.00
4,400.00	10.00	344.12	4,361.00	442.71	-125.95	438.00	0.00	0.00	0.00
4,500.00	10.00	344.12	4,459.48	459.41	-130.70	454.52	0.00	0.00	0.00
4,600.00	10.00	344.12	4,557.97	476.12	-135.45	471.05	0.00	0.00	0.00
4,700.00	10.00	344.12	4,656.45	492.82	-140.20	487.57	0.00	0.00	0.00
4,800.00	10.00	344.12	4,754.93	509.52	-144.95	504.09	0.00	0.00	0.00
4,900.00	10.00	344.12	4,853.41	526.22	-149.70	520.62	0.00	0.00	0.00
5,000.00	10.00	344.12	4,951.89	542.92	-154.45	537.14	0.00	0.00	0.00
5,100.00	10.00	344.12	5,050.37	559.63	-159.21	553.67	0.00	0.00	0.00



Pro Directional Survey Report

MarathonOil

Company:	Marathon Oil	Local Co-ordinate Reference:	Well No. 2H
Project:	Eddy County, NM	TVD Reference:	well @ 2899.00usft
Site:	Mazer North 17	MD Reference:	well @ 2899.00usft
Well:	No. 2H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	Prelim Plan A	Database:	WellPlanner1

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,200.00	10.00	344.12	5,148.85	576.33	-163.96	570.19	0.00	0.00	0.00	
5,300.00	10.00	344.12	5,247.33	593.03	-168.71	586.72	0.00	0.00	0.00	
5,400.00	10.00	344.12	5,345.81	609.73	-173.46	603.24	0.00	0.00	0.00	
5,500.00	10.00	344.12	5,444.29	626.43	-178.21	619.76	0.00	0.00	0.00	
5,600.00	10.00	344.12	5,542.77	643.14	-182.96	636.29	0.00	0.00	0.00	
5,700.00	10.00	344.12	5,641.25	659.84	-187.72	652.81	0.00	0.00	0.00	
5,800.00	10.00	344.12	5,739.73	676.54	-192.47	669.34	0.00	0.00	0.00	
5,900.00	10.00	344.12	5,838.22	693.24	-197.22	685.86	0.00	0.00	0.00	
6,000.00	10.00	344.12	5,936.70	709.95	-201.97	702.39	0.00	0.00	0.00	
6,100.00	10.00	344.12	6,035.18	726.65	-206.72	718.91	0.00	0.00	0.00	
6,200.00	10.00	344.12	6,133.66	743.35	-211.47	735.43	0.00	0.00	0.00	
6,300.00	10.00	344.12	6,232.14	760.05	-216.22	751.96	0.00	0.00	0.00	
6,400.00	10.00	344.12	6,330.62	776.75	-220.98	768.48	0.00	0.00	0.00	
6,500.00	10.00	344.12	6,429.10	793.46	-225.73	785.01	0.00	0.00	0.00	
6,600.00	10.00	344.12	6,527.58	810.16	-230.48	801.53	0.00	0.00	0.00	
6,700.00	10.00	344.12	6,626.06	826.86	-235.23	818.05	0.00	0.00	0.00	
6,800.00	10.00	344.12	6,724.54	843.56	-239.98	834.58	0.00	0.00	0.00	
6,900.00	10.00	344.12	6,823.02	860.26	-244.73	851.10	0.00	0.00	0.00	
7,000.00	10.00	344.12	6,921.50	876.97	-249.49	867.63	0.00	0.00	0.00	
7,100.00	10.00	344.12	7,019.99	893.67	-254.24	884.15	0.00	0.00	0.00	
7,200.00	10.00	344.12	7,118.47	910.37	-258.99	900.68	0.00	0.00	0.00	
7,300.00	10.00	344.12	7,216.95	927.07	-263.74	917.20	0.00	0.00	0.00	
7,400.00	10.00	344.12	7,315.43	943.77	-268.49	933.72	0.00	0.00	0.00	
7,500.00	10.00	344.12	7,413.91	960.48	-273.24	950.25	0.00	0.00	0.00	
Enter: 7500' MD										
7,500.46	10.00	344.12	7,414.36	960.55	-273.26	950.32	0.00	0.00	0.00	
[MazerN17#2H]Enter										
7,600.00	10.00	344.12	7,512.39	977.18	-277.99	966.77	0.00	0.00	0.00	
7,700.00	10.00	344.12	7,610.87	993.88	-282.75	983.30	0.00	0.00	0.00	
7,800.00	10.00	344.12	7,709.35	1,010.58	-287.50	999.82	0.00	0.00	0.00	
7,859.01	10.00	344.12	7,767.46	1,020.44	-290.30	1,009.57	0.00	0.00	0.00	
Start Drop -2.00										
7,900.00	9.18	344.12	7,807.88	1,027.01	-292.17	1,016.07	2.00	-2.00	0.00	
8,000.00	7.18	344.12	7,906.86	1,040.69	-296.06	1,029.61	2.00	-2.00	0.00	
8,100.00	5.18	344.12	8,006.27	1,051.05	-299.01	1,039.85	2.00	-2.00	0.00	
8,200.00	3.18	344.12	8,106.00	1,058.06	-301.00	1,046.79	2.00	-2.00	0.00	
8,300.00	1.18	344.12	8,205.92	1,061.72	-302.04	1,050.41	2.00	-2.00	0.00	
8,359.01	0.00	0.00	8,264.93	1,062.30	-302.21	1,050.99	2.00	-2.00	26.91	
Start 1065.07 hold at 8359.01 MD										
8,400.00	0.00	0.00	8,305.92	1,062.30	-302.21	1,050.99	0.00	0.00	0.00	
8,500.00	0.00	0.00	8,405.92	1,062.30	-302.21	1,050.99	0.00	0.00	0.00	
8,600.00	0.00	0.00	8,505.92	1,062.30	-302.21	1,050.99	0.00	0.00	0.00	
8,700.00	0.00	0.00	8,605.92	1,062.30	-302.21	1,050.99	0.00	0.00	0.00	
8,800.00	0.00	0.00	8,705.92	1,062.30	-302.21	1,050.99	0.00	0.00	0.00	



Pro Directional Survey Report

Marathon Oil

Company:	Marathon Oil	Local Co-ordinate Reference:	Well No. 1H
Project:	Eddy County, NM	TVD Reference:	well @ 2899.00usft
Site:	Mazer North 17	MD Reference:	well @ 2899.00usft
Well:	No. 1H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	Prelim Plan A	Database:	WellPlanner1

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,800.00	0.00	0.00	8,704.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
8,900.00	0.00	0.00	8,804.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
9,000.00	0.00	0.00	8,904.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
9,100.00	0.00	0.00	9,004.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
9,200.00	0.00	0.00	9,104.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
9,300.00	0.00	0.00	9,204.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
9,400.00	0.00	0.00	9,304.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
9,500.00	0.00	0.00	9,404.82	1,067.31	329.67	1,078.17	0.00	0.00	0.00
9,600.18	0.00	0.00	9,505.00	1,067.31	329.67	1,078.17	0.00	0.00	0.00
Start DLS 10.00 TFO 2.00 - [MazerN17#1H]FTP									
9,650.00	4.98	2.00	9,554.75	1,069.47	329.75	1,080.33	10.00	10.00	0.00
9,700.00	9.98	2.00	9,604.31	1,075.98	329.97	1,086.84	10.00	10.00	0.00
9,750.00	14.98	2.00	9,653.11	1,086.77	330.35	1,097.64	10.00	10.00	0.00
9,800.00	19.98	2.00	9,700.79	1,101.78	330.87	1,112.66	10.00	10.00	0.00
9,850.00	24.98	2.00	9,746.98	1,120.88	331.54	1,131.77	10.00	10.00	0.00
9,900.00	29.98	2.00	9,791.32	1,143.93	332.34	1,154.83	10.00	10.00	0.00
9,950.00	34.98	2.00	9,833.48	1,170.76	333.28	1,181.68	10.00	10.00	0.00
10,000.00	39.98	2.00	9,873.15	1,201.16	334.34	1,212.09	10.00	10.00	0.00
10,050.00	44.98	2.00	9,910.01	1,234.89	335.51	1,245.85	10.00	10.00	0.00
10,100.00	49.98	2.00	9,943.79	1,271.71	336.80	1,282.69	10.00	10.00	0.00
10,150.00	54.98	2.00	9,974.23	1,311.33	338.18	1,322.34	10.00	10.00	0.00
10,200.00	59.98	2.00	10,001.10	1,353.46	339.65	1,364.48	10.00	10.00	0.00
10,250.00	64.98	2.00	10,024.20	1,397.76	341.19	1,408.81	10.00	10.00	0.00
10,300.00	69.98	2.00	10,043.34	1,443.90	342.80	1,454.99	10.00	10.00	0.00
10,350.00	74.98	2.00	10,058.39	1,491.54	344.46	1,502.65	10.00	10.00	0.00
10,400.00	79.98	2.00	10,069.22	1,540.31	346.16	1,551.45	10.00	10.00	0.00
10,450.00	84.98	2.00	10,075.76	1,589.83	347.89	1,601.00	10.00	10.00	0.00
10,500.18	90.00	2.00	10,077.96	1,639.91	349.63	1,651.12	10.00	10.00	0.00
Start 4351.92 hold at 10500.18 MD									
10,600.00	90.00	2.00	10,077.96	1,739.68	353.11	1,750.94	0.00	0.00	0.00
10,700.00	90.00	2.00	10,077.96	1,839.61	356.59	1,850.94	0.00	0.00	0.00
10,800.00	90.00	2.00	10,077.96	1,939.55	360.08	1,950.94	0.00	0.00	0.00
10,900.00	90.00	2.00	10,077.96	2,039.49	363.56	2,050.94	0.00	0.00	0.00
11,000.00	90.00	2.00	10,077.96	2,139.43	367.05	2,150.94	0.00	0.00	0.00
11,058.75	90.00	2.00	10,077.96	2,198.15	369.09	2,209.69	0.00	0.00	0.00
[MazerN17#1H]PPP-2									
11,100.00	90.00	2.00	10,077.96	2,239.37	370.53	2,250.94	0.00	0.00	0.00
11,200.00	90.00	2.00	10,077.96	2,339.31	374.02	2,350.94	0.00	0.00	0.00
11,300.00	90.00	2.00	10,077.97	2,439.25	377.50	2,450.94	0.00	0.00	0.00
11,400.00	90.00	2.00	10,077.97	2,539.19	380.98	2,550.94	0.00	0.00	0.00
11,500.00	90.00	2.00	10,077.97	2,639.13	384.47	2,650.94	0.00	0.00	0.00
11,600.00	90.00	2.00	10,077.97	2,739.07	387.95	2,750.94	0.00	0.00	0.00
11,700.00	90.00	2.00	10,077.97	2,839.01	391.44	2,850.94	0.00	0.00	0.00
11,800.00	90.00	2.00	10,077.97	2,938.95	394.92	2,950.94	0.00	0.00	0.00



Marathon Oil

Pro Directional Survey Report

Company:	Marathon Oil	Local Co-ordinate Reference:	Well No. 1H
Project:	Eddy County, NM	TVD Reference:	well @ 2899.00usft
Site:	Mazer North 17	MD Reference:	well @ 2899.00usft
Well:	No. 1H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	Prelim Plan A	Database:	WellPlanner1

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
11,900.00	90.00	2.00	10,077.97	3,038.89	398.40	3,050.94	0.00	0.00	0.00	
12,000.00	90.00	2.00	10,077.97	3,138.83	401.89	3,150.94	0.00	0.00	0.00	
12,100.00	90.00	2.00	10,077.97	3,238.76	405.37	3,250.94	0.00	0.00	0.00	
12,200.00	90.00	2.00	10,077.97	3,338.70	408.86	3,350.94	0.00	0.00	0.00	
12,300.00	90.00	2.00	10,077.98	3,438.64	412.34	3,450.94	0.00	0.00	0.00	
12,400.00	90.00	2.00	10,077.98	3,538.58	415.83	3,550.94	0.00	0.00	0.00	
12,500.00	90.00	2.00	10,077.98	3,638.52	419.31	3,650.94	0.00	0.00	0.00	
12,600.00	90.00	2.00	10,077.98	3,738.46	422.79	3,750.94	0.00	0.00	0.00	
12,700.00	90.00	2.00	10,077.98	3,838.40	426.28	3,850.94	0.00	0.00	0.00	
12,800.00	90.00	2.00	10,077.98	3,938.34	429.76	3,950.94	0.00	0.00	0.00	
12,900.00	90.00	2.00	10,077.98	4,038.28	433.25	4,050.94	0.00	0.00	0.00	
13,000.00	90.00	2.00	10,077.98	4,138.22	436.73	4,150.94	0.00	0.00	0.00	
13,100.00	90.00	2.00	10,077.98	4,238.16	440.21	4,250.94	0.00	0.00	0.00	
13,200.00	90.00	2.00	10,077.98	4,338.10	443.70	4,350.94	0.00	0.00	0.00	
13,300.00	90.00	2.00	10,077.99	4,438.04	447.18	4,450.94	0.00	0.00	0.00	
13,400.00	90.00	2.00	10,077.99	4,537.98	450.67	4,550.94	0.00	0.00	0.00	
13,500.00	90.00	2.00	10,077.99	4,637.91	454.15	4,650.94	0.00	0.00	0.00	
13,600.00	90.00	2.00	10,077.99	4,737.85	457.64	4,750.94	0.00	0.00	0.00	
13,700.00	90.00	2.00	10,077.99	4,837.79	461.12	4,850.94	0.00	0.00	0.00	
13,800.00	90.00	2.00	10,077.99	4,937.73	464.60	4,950.94	0.00	0.00	0.00	
13,900.00	90.00	2.00	10,077.99	5,037.67	468.09	5,050.94	0.00	0.00	0.00	
14,000.00	90.00	2.00	10,077.99	5,137.61	471.57	5,150.94	0.00	0.00	0.00	
14,100.00	90.00	2.00	10,077.99	5,237.55	475.06	5,250.94	0.00	0.00	0.00	
14,200.00	90.00	2.00	10,077.99	5,337.49	478.54	5,350.94	0.00	0.00	0.00	
14,300.00	90.00	2.00	10,077.99	5,437.43	482.02	5,450.94	0.00	0.00	0.00	
14,400.00	90.00	2.00	10,078.00	5,537.37	485.51	5,550.94	0.00	0.00	0.00	
14,500.00	90.00	2.00	10,078.00	5,637.31	488.99	5,650.94	0.00	0.00	0.00	
14,600.00	90.00	2.00	10,078.00	5,737.25	492.48	5,750.94	0.00	0.00	0.00	
14,700.00	90.00	2.00	10,078.00	5,837.19	495.96	5,850.94	0.00	0.00	0.00	
14,800.00	90.00	2.00	10,078.00	5,937.13	499.44	5,950.94	0.00	0.00	0.00	
14,851.10	90.00	2.00	10,078.00	5,988.19	501.23	6,002.04	0.00	0.00	0.00	
TD at 14852.10										
14,852.10	90.00	2.00	10,078.00	5,989.19	501.26	6,003.04	0.00	0.00	0.00	
[MazerN17#1H]LTP/BHL										



Pro Directional Survey Report

Marathon Oil

Company:	Marathon Oil	Local Co-ordinate Reference:	Well No. 1H
Project:	Eddy County, NM	TVD Reference:	well @ 2899.00usft
Site:	Mazer North 17	MD Reference:	well @ 2899.00usft
Well:	No. 1H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	Prelim Plan A	Database:	WellPlanner1

Design Targets									
Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
[MazerN17#1H]Enter - plan misses target center by 1.59usft at 7587.14usft MD (7499.72 TVD, 968.57 N, 299.17 E) - Point	0.00	0.00	7,500.00	967.07	298.71	376,777.26	603,634.44	32.035434	-103.998895
[MazerN17#1H]FTP - plan hits target center - Point	0.00	0.00	9,505.00	1,067.31	329.67	376,877.50	603,665.39	32.035710	-103.998794
[MazerN17#1H]LTP/BHL - plan hits target center - Point	0.00	0.00	10,078.0 0	5,989.19	501.26	381,799.38	603,836.98	32.049239	-103.998191
[MazerN17#1H]PPP-2 - plan misses target center by 0.04usft at 11058.75usft MD (10077.96 TVD, 2198.15 N, 369.09 E) - Point	0.00	0.00	10,078.0 0	2,198.15	369.10	378,008.34	603,704.82	32.038818	-103.998656

Plan Annotations				
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
1500	1500	0	0	Start Build 2.00
2000	1997	42	13	Start 5931.64 hold at 2000.00 MD
7587	7500	969	299	Enter: 7587' MD
7932	7839	1026	317	Start Drop -2.00
8432	8336	1067	330	Start 1168.54 hold at 8431.64 MD
9600	9505	1067	330	Start DLS 10.00 TFO 2.00
10,500	10,078	1640	350	Start 4351.92 hold at 10500.18 MD
14,851	10,078	5988	501	TD at 14852.10

Checked By: _____	Approved By: _____	Date: _____
-------------------	--------------------	-------------



Marathon Oil
Eddy County, NM
Mazer North 17
No. 1H
Prelim Plan A

US State Plane 1927 (Exact solution)
NAD 1927 (NADCON CONUS)
Clarke 1866
New Mexico East 3001
Mean Sea Level

RKB Elevation: well @ 2899.00usft



+N/-S	+E/-W	Northing	Easting	Latitude	Longitude	Slot
0.00	0.00	375810.19	603335.72	32.032778	-103.999869	

SECTION DETAILS



Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	VSect
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2	1500.00	0.00	0.00	1500.00	0.00	0.00	0.00	0.00
3	2000.00	10.00	17.16	1997.47	41.58	12.84	2.00	42.01
4	7931.64	10.00	17.16	7838.99	1025.73	316.83	0.00	1036.16
5	8431.64	0.00	0.00	8336.46	1067.31	329.67	2.00	1078.17
6	9600.18	0.00	0.00	9505.00	1067.31	329.67	0.00	1078.17
7	10500.18	90.00	2.00	10077.96	1639.91	349.63	10.00	1651.12
8	14852.10	90.00	2.00	10078.00	5989.19	501.26	0.00	6003.04

WELLBORE TARGET DETAILS (MAP CO-ORDINATES)

Name	TVD	+N/-S	+E/-W	Northing	Easting
[MazerN17#1H]Enter	7500.00	967.07	298.71	376777.26	603634.43
[MazerN17#1H]FTP	9505.00	1067.31	329.67	376877.50	603665.39
[MazerN17#1H]LTP/BHL	10078.00	5989.19	501.26	381799.38	603836.98
[MazerN17#1H]PPP-2	10078.00	2198.15	369.10	378008.34	603704.82

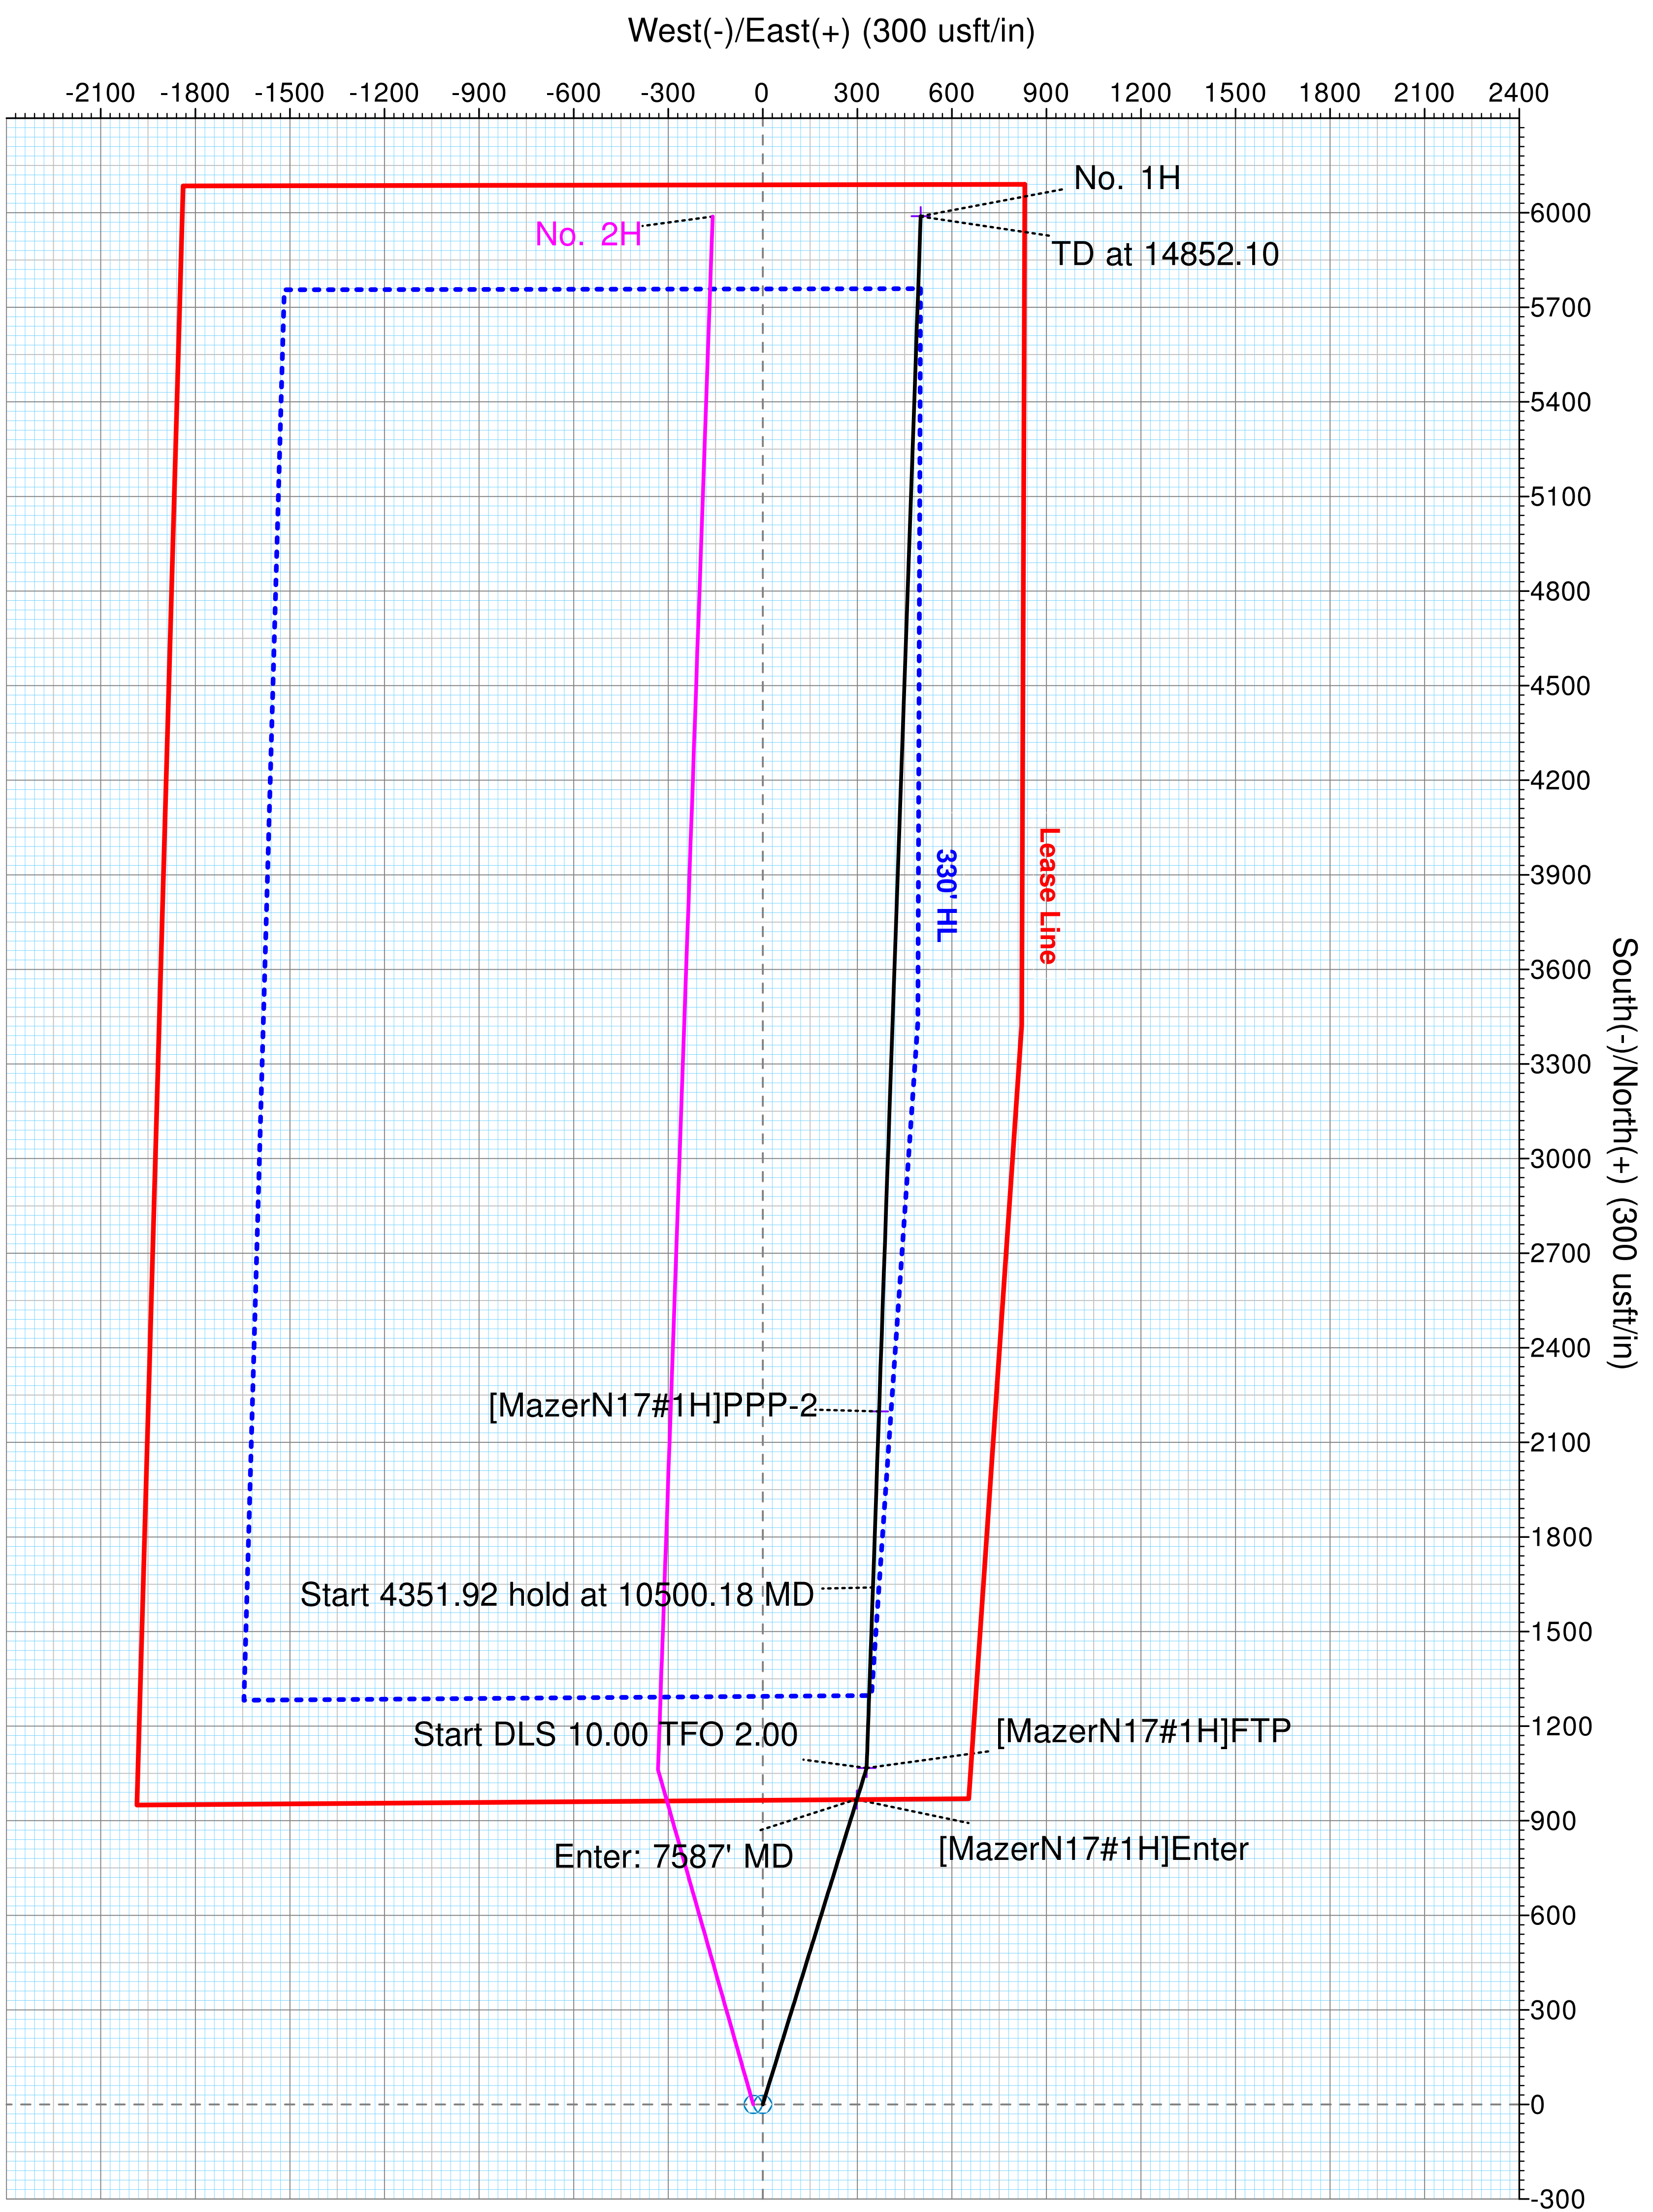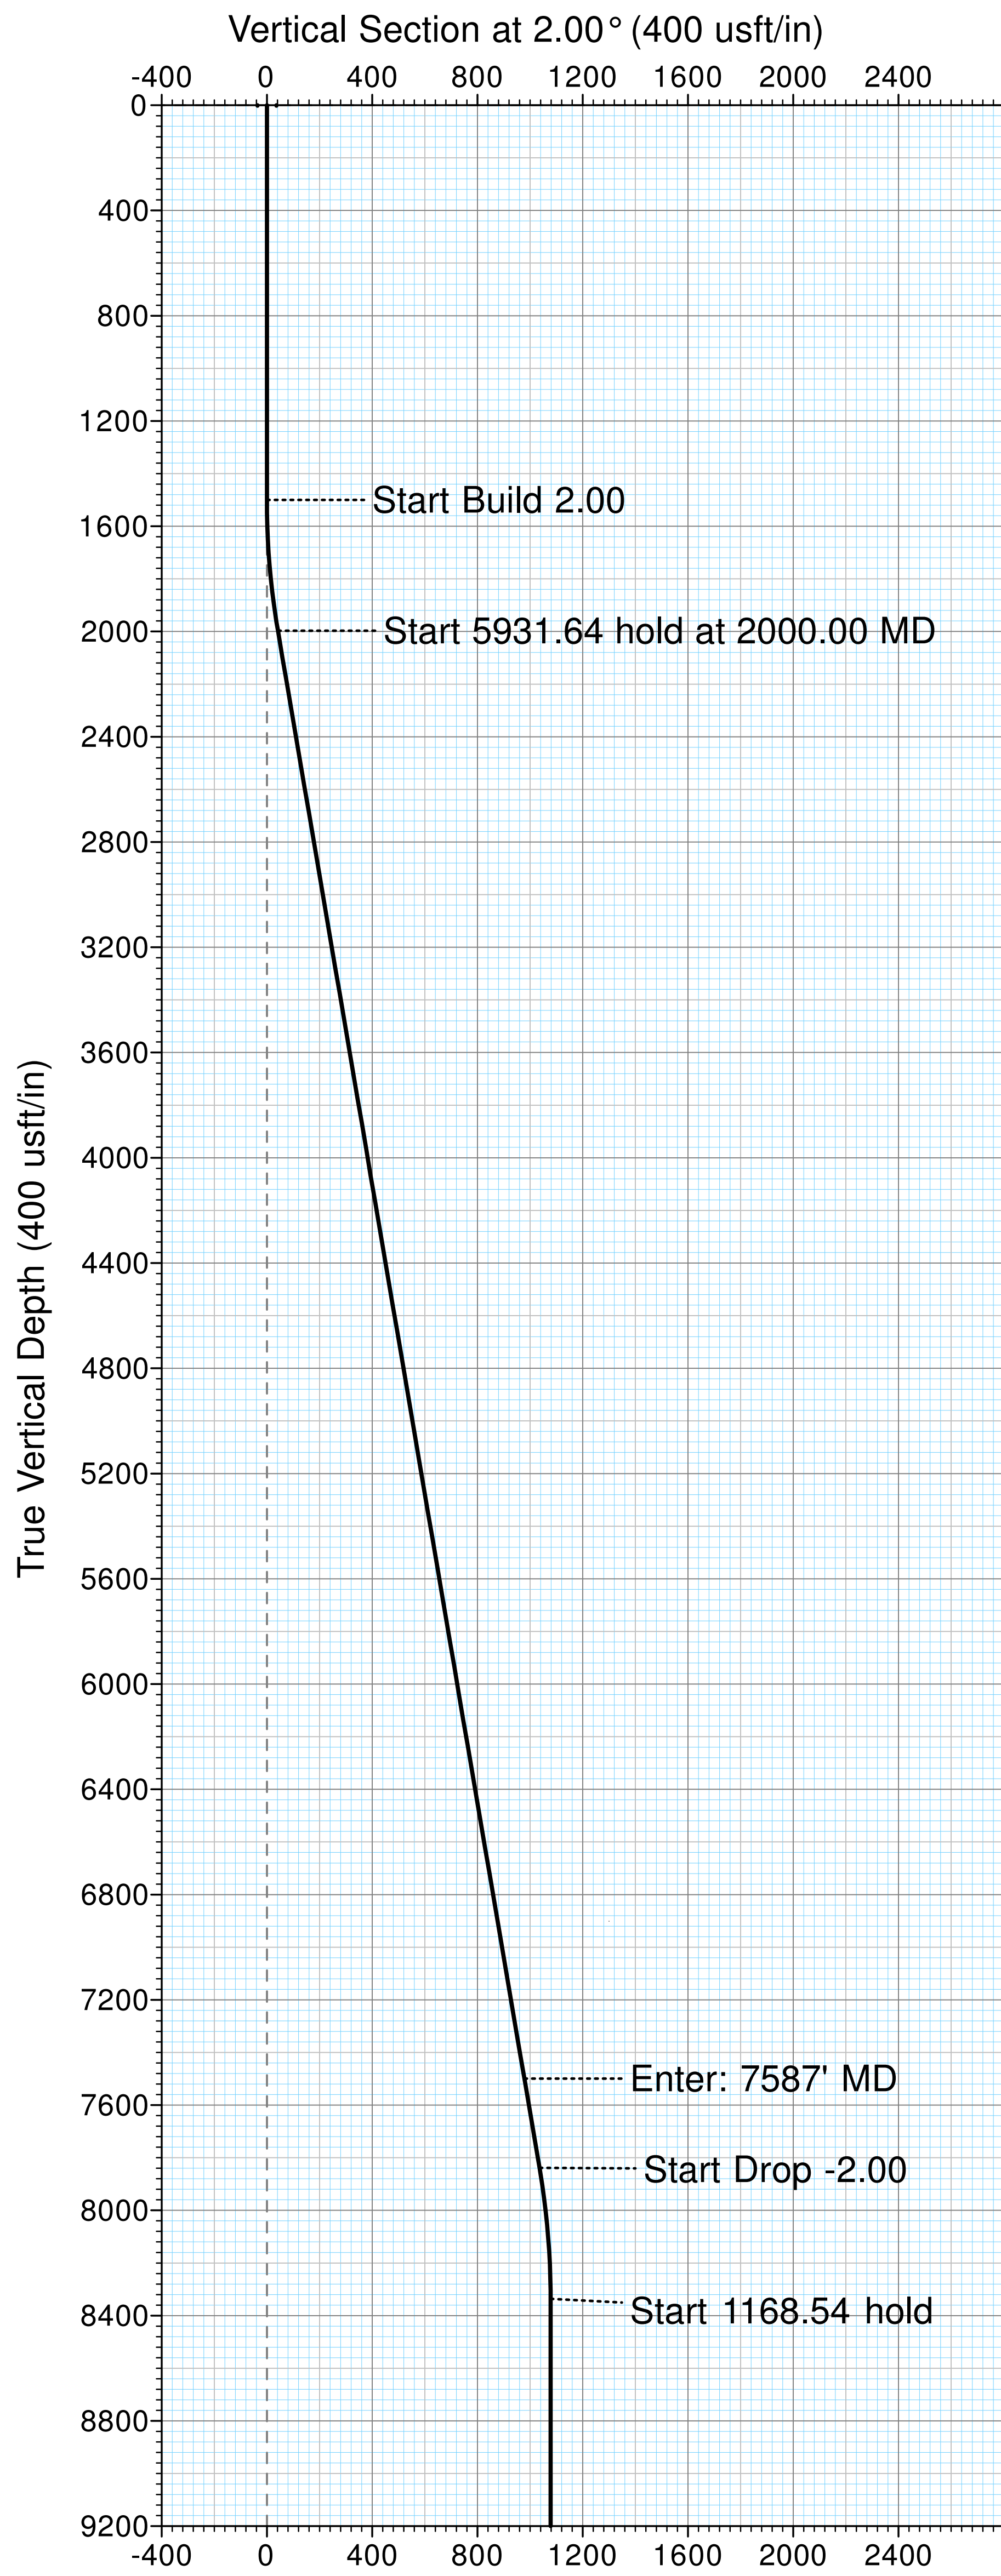

Target Line: 10078' TVD @ 0' VS: 90° INC

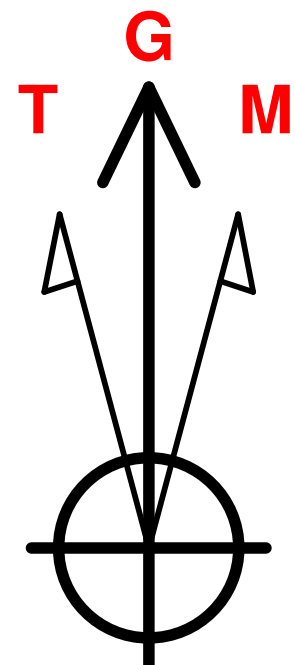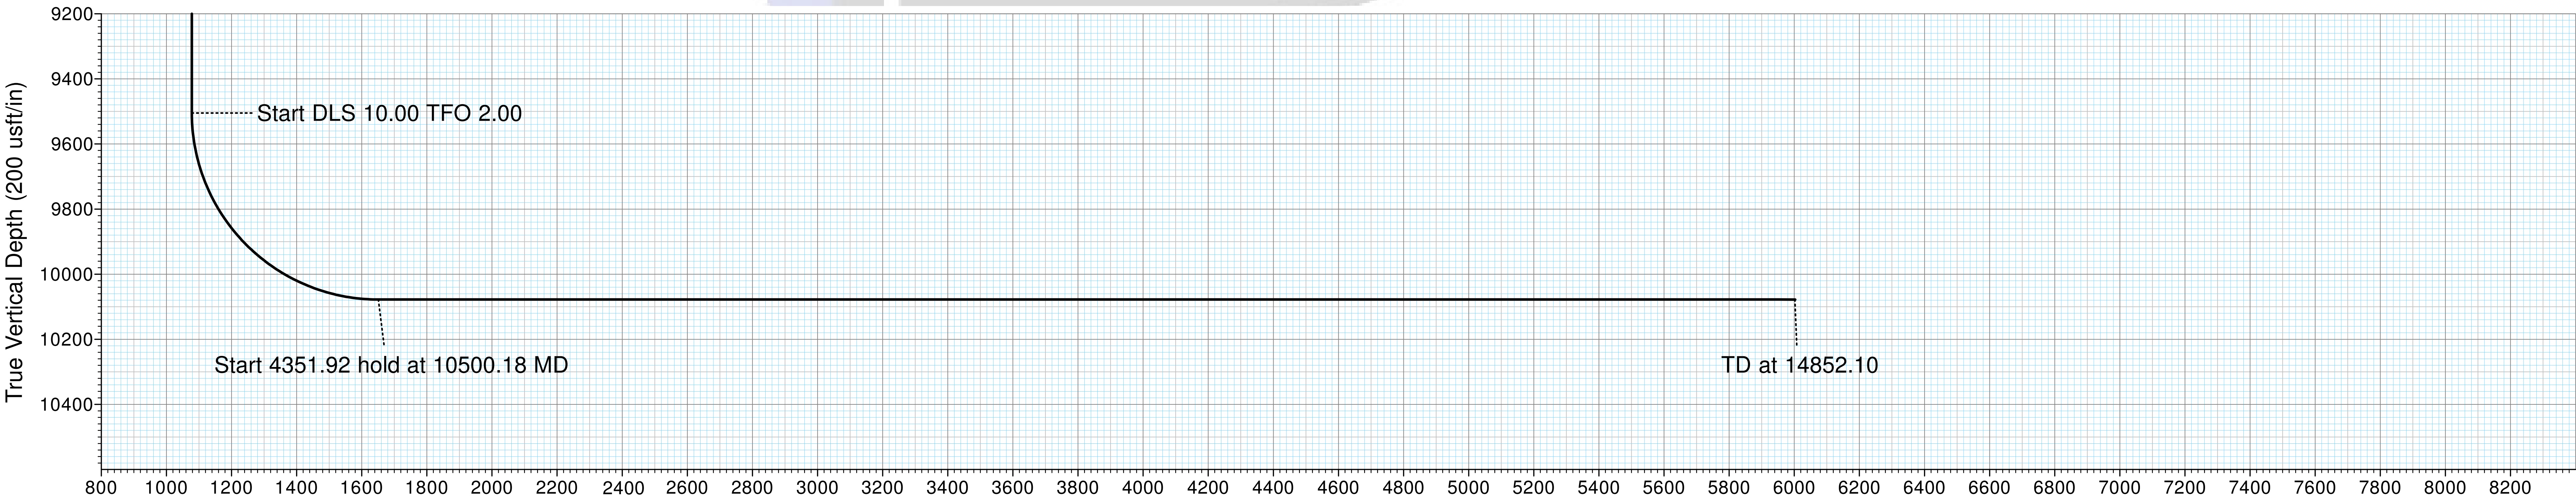

Azimuths to Grid North
True North: -0.18°
Magnetic North: 6.44°

Magnetic Field
Strength: 47567.9snT
Dip Angle: 59.58°
Date: 6/3/2021
Model: HDGM

Azimuth Corrections
Total Magnetic Corr. (M to G): 6.44°
Declination (M to T): 6.62° East

36" x 48"

MARATHON OIL PERMIAN, LLC.
DRILLING AND OPERATIONS PLAN



WELL NAME & NUMBER:

MAZER NORTH 17 WA FED COM 1H

LOCATION:

SECTION

20

TOWNSHIP

26S

RANGE

29E**EDDY**

COUNTY,

NEW MEXICO**Section 1:****GEOLOGICAL FORMATIONS**

Name of Surface Formation:

Permian

Elevation:

2872 feet

Estimated Tops of Important Geological Markers:

Formation	TVD (ft)	MD (ft)	Elevation (ft SS)	Lithologies	Mineral Resources	Producing Formation?
Rustler	420	420	2452	Anhydrite	Brine	No
Salado	786	786	2086	Salt/Anhydrite	Brine	No
Castile	1032	1032	1840	Salt/Anhydrite	Brine	No
Base of Salt (BX)	2782	2782	90	Salt/Anhydrite	Brine	No
Lamar	2782	2782	90	Sandstone/Shale	None	No
Bell Canyon	2823	2823	49	Sandstone	Oil	No
Cherry Canyon	3898	3898	-1026	Sandstone	Oil	No
Brushy Canyon	4938	4938	-2066	Sandstone	Oil	No
Bone Spring Lime	6556	6556	-3684	Limestone	None	No
Upper Avalon Shale	6580	6580	-3708	Shale	Oil	Yes
1st Bone Spring Sand	7457	7457	-4585	Sandstone	Oil	Yes
2nd Bone Spring Carbonate	7738	7738	-4866	Limestone/Shale	None	No
2nd Bone Spring Sand	8231	8231	-5359	Sandstone	Oil	Yes
3rd Bone Spring Carbonate	8629	8629	-5757	Limestone	Oil	No
3rd Bone Spring Sand	9309	9309	-6437	Sandstone	Oil	Yes
Wolfcamp	9681	9681	-6809	Sandstone/Shale/Carbonates	Natural Gas / Oil	Yes
Wolfcamp A	9817	9817	-6945	Sandstone/Shale/Carbonates	Natural Gas / Oil	Yes
Wolfcamp B	10155	10155	-7283	Sandstone/Shale/Carbonates	Natural Gas / Oil	No
Wolfcamp C	10467	10467	-7595	Sandstone/Shale/Carbonates	Natural Gas / Oil	No
Wolfcamp D	10991	10991	-8119	Sandstone/Shale/Carbonates	Natural Gas / Oil	No

Section 2:**BLOWOUT PREVENTER TESTING PROCEDURE**

Pressure Rating (PSI):

10M

Rating Depth:

10000

Equipment:

13 5/8 BOP Annular (5,000 psi WP) and BOP Stack (10,000 psi WP) will be installed and tested before drilling all holes.

Requesting Variance?

Yes

Variance Request:

A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.

Testing Procedure:

BOP/BOPE will be tested to 250 psi low and a high of 50% WP for the Annular and 10,000 psi for the BOP Stacking. Testing will be conducted by an independent service company per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the Equipment Description above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock, full opening safety valve / inside BOP and choke lines and choke manifold. See attached schematics.

Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i. A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested. See attached schematic.

Marathon Oil Permian LLC.

Drilling & Operations Plan - Page 2 of 4

Section 3:**CASING PROGRAM**

String Type	Hole Size	Casing Size	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Weight (lbs/ft)	Grade	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
Surface	17.5	13.375	0	490	0	490	2872	2382	54.5	J55	BTC	5.22	1.81	BUOY	4.52	BUOY	4.52
Intermediate	12.25	9.625	0	9500	0	9405	2872	-6533	40	P110HC	BTC	1.20	1.42	BUOY	2.44	BUOY	2.44
Production	8.75	5.5	0	14852	0	10078	2872	-7206	23	P110HC	TLW	2.53	1.26	BUOY	2.22	BUOY	2.22
All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h												Safety Factors will Meet or Exceed					

Casing Condition: New
Casing Standard: API
Tapered String? No

Yes or No

Is casing new? If used, attach certification as required in Onshore Order #1.	Yes
Does casing meet API specifications? If no, attach casing specification sheet.	Yes
Is premium or uncommon casing planned? If yes attach casing specification sheet.	No
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Yes
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Yes
Is well located within Capitan Reef?	No
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is proposed well within the designated four string boundary?	
Is well located in R-111-P and SOPA?	No
If yes, are the first three strings cemented to surface?	
Is the second string set 100' to 600' below the base of salt?	
Is well located in SOPA but not in R-111-P?	No
If yes, are the first 2 strings cemented to surface and third string cement tied back 500' into previous casing?	
Is well located in high Cave/Karst?	No
If yes, are there two strings cemented to surface?	
If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	No
If yes, are there three strings cemented to surface?	

Section 4:**CEMENT PROGRAM**

String Type	Lead/Tail	Top MD	Bottom MD	Quantity (sks)	Yield (ft ³ /sks)	Density (ppg)	Slurry Volume (ft ³)	Excess (%)	Cement Type	Additives
Surface	Lead	0	190	101	2.12	12.5	214	25	Class C	Extender, Accelerator, LCM
Surface	Tail	190	490	197	1.32	14.8	260	25	Class C	Accelerator
Intermediate	Lead	0	9000	1630	2.18	12.4	3554	25	Class C	Extender, Accelerator, LCM
Intermediate	Tail	9000	9500	147	1.33	14.8	196	25	Class C	Retarder
Production	Tail	9200	14852	1103	1.68	13	1853	25	Class H	Retarder, Extender, Fluid Loss, Suspension Agent

Stage tool depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. Stage tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe. Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

Pilot Hole? No **Plugging Procedure for Pilot Hole:** N/A
Pilot Hole Depth: N/A
KOP Depth: N/A

Plug Top	Plug Bottom	Excess (%)	Quantity (sx)	Density (ppg)	Yield (ft ³ /sks)	Water gal/sk	Slurry Description and Cement Type

Marathon Oil Permian LLC.

Drilling & Operations Plan - Page 3 of 4

Section 5:**CIRCULATING MEDIUM**

Mud System Type: Closed
Will an air or gas system be used? No

Describe what will be on location to control well or mitigate other conditions:

The necessary mud products for additional weight and fluid loss control will be on location at all times.

Describe the mud monitoring system utilized:

Losses or gains in the mud system will be monitored visually/manually as well as with an electronic PVT.

Circulating Medium Table:

Top Depth	Bottom Depth	Mud Type	Min. Weight (ppg)	Max Weight (ppg)
0	490	Water Based Mud	8.4	8.8
490	9500	Brine or Oil Based Mud	9.2	10.2
9500	14852	Oil Based Mud	10.5	12.5

Section 6:**TESTING, LOGGING, CORING****List of production tests including testing procedures, equipment and safety measures:**

GR from TD to surface (horizontal well - vertical portion of hole)

List of open and cased hole logs run in the well:

GR while drilling from Intermediate casing shoe to TD.

Coring operation description for the well:

Run gamma-ray (GR) and corrected neutron log (CNL) or analogous to surface for future development of the area, one per shared well pad not to exceed 200' radial distance.

Section 7:**ANTICIPATED PRESSURE**

Anticipated Bottom Hole Pressure: 6551 PSI
Anticipated Bottom Hole Temperature: 195 °F
Anticipated Abnormal Pressure? No
Anticipated Abnormal Temperature? No

Potential Hazards:

H2S detection equipment will be in operation after drilling out the surface casing shoe until the production casing has been cemented. Breathing equipment will be on location from drilling out the surface shoe until production casing is cemented. If H2S is encountered the operator will comply with Onshore Order #6. Adequate flare lines will be installed off the mud/gas separator where gas may be flared safely. All personnel will be familiar with all aspects of safe operation of equipment being used to drill this well. See attached H2S Contingency Plan.

Section 8:**OTHER INFORMATION****Auxiliary Well Control and Monitoring Equipment:**

A Kelly cock will be in the drill string at all times. A full opening drill pipe stabbing valve having the appropriate connections will be on the rig floor unobstructed and readily accessible at all times.

Hydrogen Sulfide detection equipment will be in operation after drilling out the surface casing shoe until the production casing is cemented. Breathing equipment will be on location upon drilling the surface casing shoe until total depth is reached. If Hydrogen Sulfide is encountered, measured amounts and formations will be reported to the BLM.

Anticipated Starting Date and Duration of Operations:

Road and location construction will begin after the BLM has approved the APD. Anticipated spud date will be as soon as possible after BLM approval and as soon as a rig will be available. Move in operations and drilling is expected to take 30 days.

Marathon Oil Permian LLC.

Drilling & Operations Plan - Page 4 of 4

DRILL PLAN CHANGE REGISTER

MAZER NORTH 17 WA FED COM 1H
SECTION 20, TOWNSHIP 26S, RANGE 29E
EDDY COUNTY, NEW MEXICO

Original Document Date:

Monday, June 7, 2021

Prepared By:

Kyler Rose

Submitted By:

Melissa Szudera

Revised Date: Monday, March 14, 2022
Revised By: Court Nelson (Drilling Engineer)
Matt Baker (Geologist)

Submittal Date: Tuesday, March 22, 2022
Submittal Type: Updated Submitted APD Deficiencies
Submitted By: Melissa Szudera

Summary of Revisions:

Section	Description
1 - Geology	Updated/Added missing formation tops
3 - Casing	SURFACE: Change Hole/Casing size, bottom set depth, weight, joint type, & SFs. INTERMEDIATE: Change Hole/Casing size, bottom set depth, weight, grade, joint type, & SFs. PRODUCTION: Change Hole/Casing size, weight, grade, joint type, & SFs.
4 - Cement	Updated Lead & Tail Depths, Sacks, Yield, Density, Volume and excess for all strings. Updated Cement Type for Intermediate tail & lead. Removed Production Lead, additives updated for Surface Lead, Intermediate Lead, and Production Tail.
5 - Mud	SURFACE: changed bottom depth & mud type INTERMEDIATE: changed top & bottom depth, added mud type Brine or OBM PRODUCTION: changed top depth.

Revised Date:
Revised By:

Submittal Date:
Submittal Type:
Submitted By:

Summary of Revisions:

Section	Description

Revised Date:
Revised By:

Submittal Date:
Submittal Type:
Submitted By:

Summary of Revisions:

Section	Description

Revised Date:
Revised By:

Submittal Date:
Submittal Type:
Submitted By:

Summary of Revisions:

Section	Description

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Marathon Oil
LEASE NO.:	NMNM114972
LOCATION:	Section 20, T.26 S., R.29 E., NMPM
COUNTY:	Eddy County, New Mexico

WELL NAME & NO.:	Mazer North 17 WA Fed Com 1H
SURFACE HOLE FOOTAGE:	965' /N & 660' /E
BOTTOM HOLE FOOTAGE:	100' /N & 330' /E

COA

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Cave/Karst Potential	<input type="radio"/> Critical		
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP
Other	<input checked="" type="checkbox"/> Fluid Filled	<input type="checkbox"/> Cement Squeeze	<input type="checkbox"/> Pilot Hole
Special Requirements	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **475** feet (a minimum of **70 feet (Eddy County)** into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8**

hours or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)

- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

Intermediate casing must be kept 1/3rd fluid filled to meet BLM minimum collapse requirement.

2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.

Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst or potash.

3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. **Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).**
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)**Communitization Agreement**

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.

- Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
 3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.

5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.

- c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
 - c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
 - d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - e. The results of the test shall be reported to the appropriate BLM office.

- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD


Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

ZS 051622

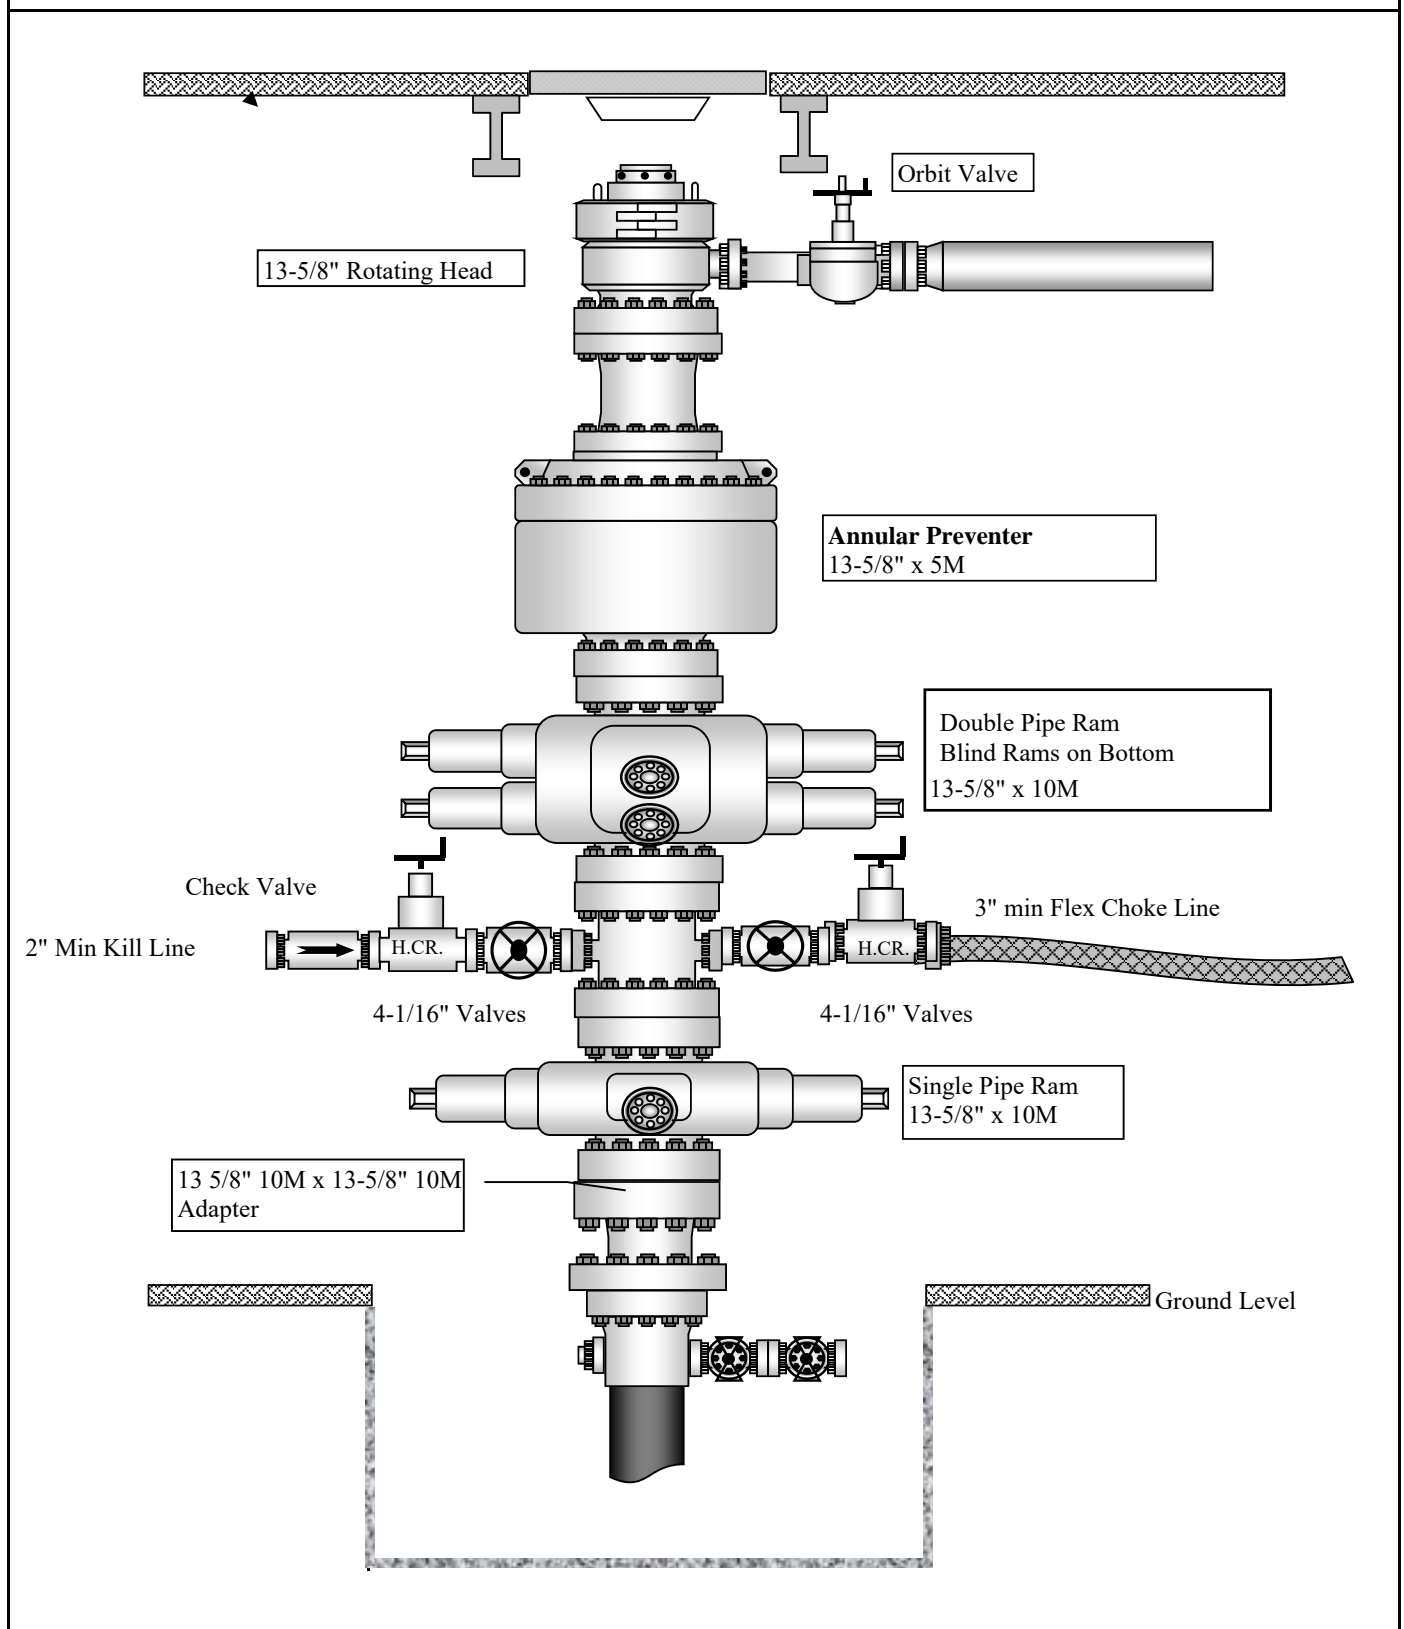Operator : Marathon Oil

District I

1625 N. French Dr., Hobbs, NM 88240
 Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
 Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
 Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
 Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 244363

CONDITIONS

Operator: MARATHON OIL PERMIAN LLC 990 Town & Country Blvd. Houston, TX 77024	OGRID: 372098
	Action Number: 244363
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
ward.rikala	Notify OCD 24 hours prior to casing & cement	7/31/2023
ward.rikala	Will require a File As Drilled C-102 and a Directional Survey with the C-104	7/31/2023
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	7/31/2023
ward.rikala	Cement is required to circulate on both surface and intermediate1 strings of casing	7/31/2023
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	7/31/2023
ward.rikala	Marathon can not produce this well until there is a name change to conform with NMOCD naming convention.	7/31/2023
