

Form 3160-5
(June 2019)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB No. 1004-0137
Expires: October 31, 2021**SUNDRY NOTICES AND REPORTS ON WELLS**
**Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.**

5. Lease Serial No. NMNM118731

6. If Indian, Allottee or Tribe Name
WESTERN NAVAJO**SUBMIT IN TRIPLICATE - Other instructions on page 2**

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other2. Name of Operator
ENDURING RESOURCES LLC3a. Address 200 ENERGY COURT, FARMINGTON, NM 87401
3b. Phone No. (include area code)
(505) 497-85744. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SEC 27/T23N/R9W/NMP7. If Unit of CA/Agreement, Name and/or No.
Greater Lybrook/NMNM144419X

8. Well Name and No. GREATER LYBROOK UNIT/830H

9. API Well No. 3004535814

10. Field and Pool or Exploratory Area
LYBROOK MANCOS W/LYBROOK MANCOS W11. Country or Parish, State
SAN JUAN/NM

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION				
☐ Notice of Intent	☐ Acidize	☐ Deepen	☐ Production (Start/Resume)	☐ Water Shut-Off	
☒ Subsequent Report	☐ Alter Casing	☐ Hydraulic Fracturing	☐ Reclamation	☐ Well Integrity	
☐ Final Abandonment Notice	☐ Casing Repair	☐ New Construction	☐ Recomplete	☒ Other	
	☐ Change Plans	☐ Plug and Abandon	☐ Temporarily Abandon		
	☐ Convert to Injection	☐ Plug Back	☐ Water Disposal		

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has detennined that the site is ready for final inspection.)

Enduring Resources performed a workover for tubing reconfiguration. Production tubing string was re-configured. An updated well schematic is attached.

EOT: 4,698 MD

Packer: None

GLVs: None

Orifice Valve: none - EOT

Job Start: 6/16/2023

Job End: 6/20/2023

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed)
HEATHER HUNTINGTON / Ph: (505) 636-9751

Title Permitting Technician

Signature

Date 07/20/2023

THE SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

MATTHEW H KADE / Ph: (505) 564-7736 / Accepted

Title Petroleum Engineer

Date 07/21/2023

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office FARMINGTON

Title 18 U.S.C Section 1001 and Title 43 U.S.C Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)




Wellbore Schematic - Components and Cement

Well Name: GREATER LYBROOK UNIT 830H (fka W LYBROOK)

API/UWI 30-045-35814		County SAN JUAN		State/Province NEW MEXICO		Surface Legal Location (UNIT C), NE/4, NW/4, SECTION 27, T23N, R09W							
Spud Date 2/7/2022		On Production Date		Abandon Date		Ground Elevation (ft) 6,641.00		Original KB Elevation (ft) 6,669.00		Total Depth (All) (ftKB) Original Hole - 12,753.0		PBTD (All) (ftKB)	

Horizontal, Original Hole, 7/5/2023 2:04:22 PM

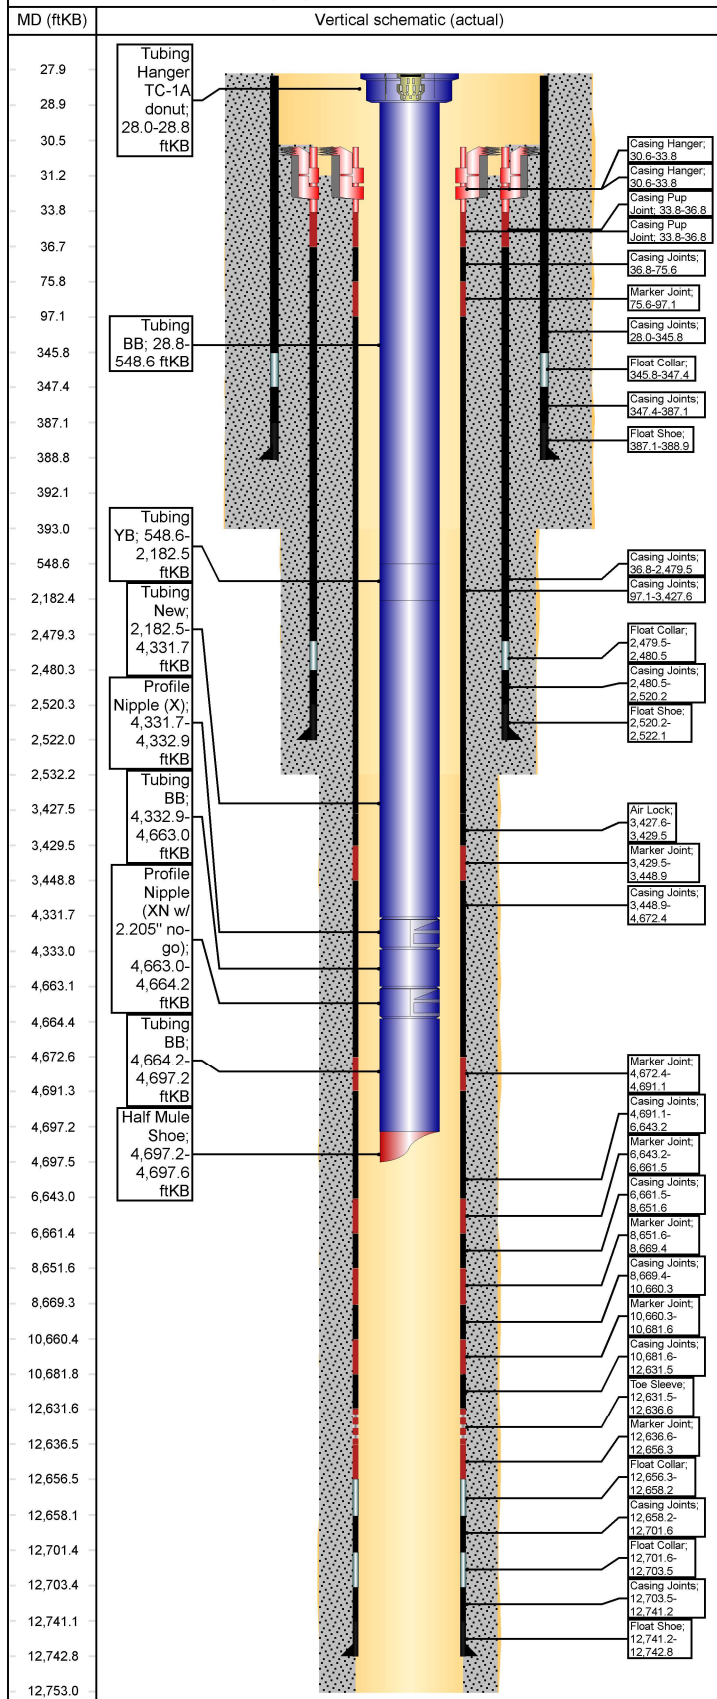

Other Strings

String Description	String Length (ft)	Set Depth (ftKB)	Run Date
--------------------	--------------------	------------------	----------

Other In Hole

Des	String	Top (ftKB)	Btm (ftKB)	Run Date
-----	--------	------------	------------	----------

Rod Strings

<des> on <dtmrun>

Rod Description	String Length (ft)	Set Depth (ftKB)	Run Date
-----------------	--------------------	------------------	----------

Jts	Item Des	OD (in)	Len (ft)	Top (ftKB)	Btm (ftKB)
-----	----------	---------	----------	------------	------------

Tubing Strings

Tubing - Production set at 4,697.6ftKB on 6/19/2023 17:30

Tubing Description	Len (ft)	Set Depth (f...	Run Date	Cut/Pull Date	Depth C...
--------------------	----------	-----------------	----------	---------------	------------

Jts	Item Des	OD (in)	Len (ft)	Top (ftKB)	Btm (ftKB)	Grade	Wt (lb/ft)
1	Tubing Hanger TC-1A donut	4 3/4	0.80	28.0	28.8		
16	Tubing BB	2 7/8	519.77	28.8	548.6	L-80	6.50
50	Tubing YB	2 7/8	1,633.96	548.6	2,182.5	L-80	6.50
66	Tubing New	2 7/8	2,149.17	2,182.5	4,331.7	J-55	6.50
1	Profile Nipple (X)	2 7/8	1.20	4,331.7	4,332.9		
10	Tubing BB	2 7/8	330.12	4,332.9	4,663.0	L-80	6.50
1	Profile Nipple (XN w/ 2.205\" no-go)	2 7/8	1.20	4,663.0	4,664.2		
1	Tubing BB	2 7/8	33.00	4,664.2	4,697.2	L-80	6.50
1	Half Mule Shoe	2 7/8	0.40	4,697.2	4,697.6		

Casing Strings

Surface, 388.9ftKB

Casing Description	OD (in)	Wt/Len (lb/ft)	String Grade	Top (ftKB)	Set Depth...	Depth C...	ID (in)
--------------------	---------	----------------	--------------	------------	--------------	------------	---------

Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)
Casing Joints	8	13 3/8	12.62	54.50	J-55	317.76
Float Collar	1	13 3/8	12.62	54.50	J-55	1.62
Casing Joints	1	13 3/8	12.62	54.50	J-55	39.65
Float Shoe	1	13 3/8	12.62	54.50	J-55	1.84

Intermediate, 2,522.1ftKB

Casing Description	OD (in)	Wt/Len (lb/ft)	String Grade	Top (ftKB)	Set Depth...	Depth C...	ID (in)
--------------------	---------	----------------	--------------	------------	--------------	------------	---------

Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)
Casing Joints	0	9 5/8	8.92	36.00	J-55	0.00
Landing Joint	0	9 5/8	8.92	36.00	J-55	0.00
Casing Hanger	1	9 5/8	8.92	36.00	J-55	3.20
Casing Pup Joint	1	9 5/8	8.92	36.00	J-55	3.00
Casing Joints	61	9 5/8	8.92	36.00	J-55	2,442.65
Float Collar	1	9 5/8	8.92	36.00	J-55	1.00
Casing Joints	1	9 5/8	8.92	36.00	J-55	39.73
Float Shoe	1	9 5/8	8.92	36.00	J-55	1.90


Production, 12,742.8ftKB

Casing Description	OD (in)	Wt/Len (lb/ft)	String Grade	Top (ftKB)	Set Depth...	Depth C...	ID (in)
--------------------	---------	----------------	--------------	------------	--------------	------------	---------

Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)
Casing Joints	0	5 1/2	4.89	17.00	P-110	0.00
Landing Joint	0	5 1/2	4.89	17.00	P-110	0.00
Casing Hanger	1	5 1/2	4.89	17.00	P-110	3.20
Casing Pup Joint	1	5 1/2	4.89	17.00	P-110	3.00
Casing Joints	1	5 1/2	4.89	17.00	P-110	38.81

WellView®**Wellbore Schematic - Components and Cement****Well Name: GREATER LYBROOK UNIT 830H (fka W LYBROOK)**

Horizontal, Original Hole, 7/5/2023 2:04:24 PM

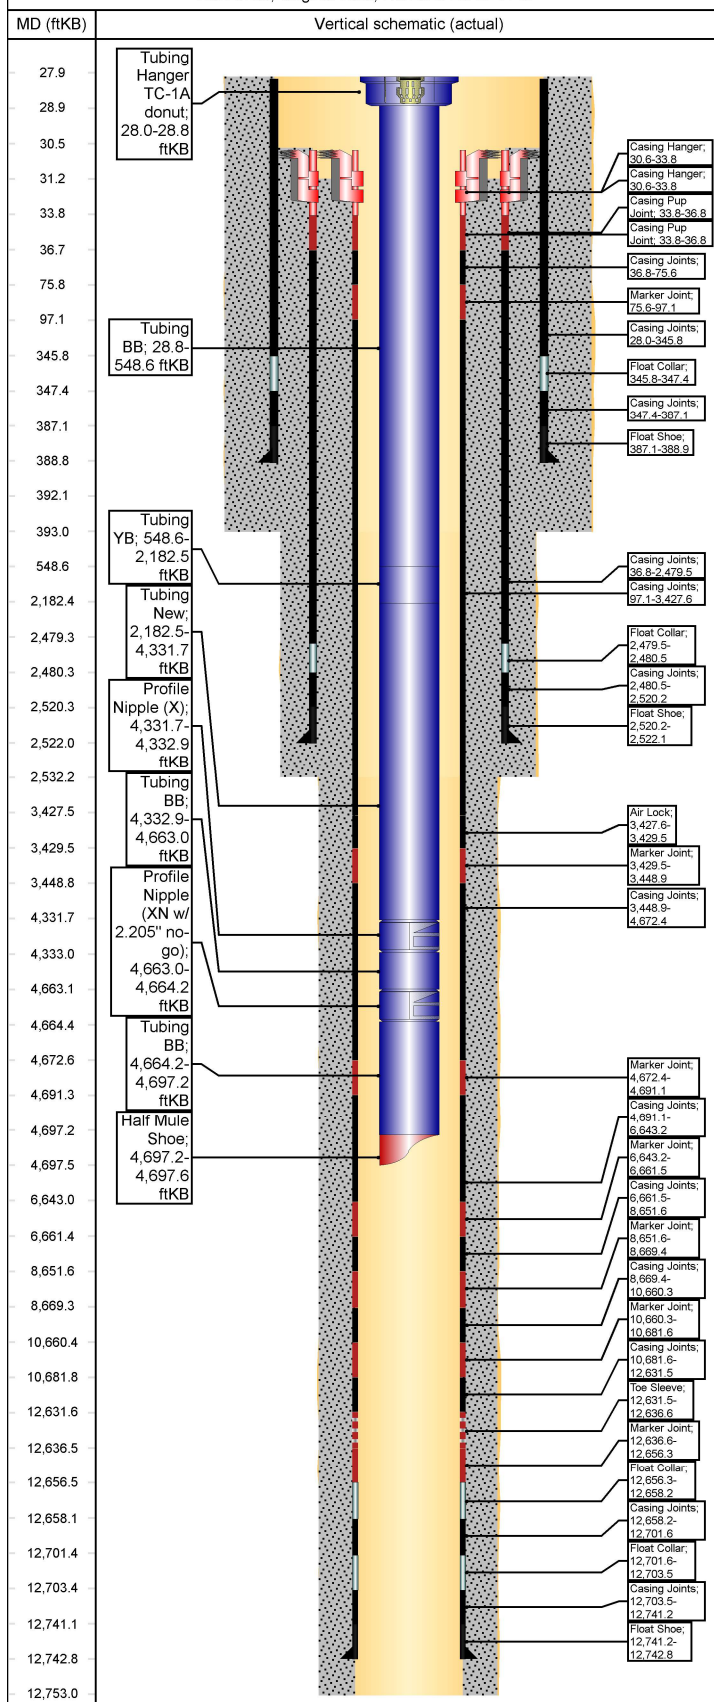**Casing Components**

Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)
Marker Joint	1	5 1/2	4.89	17.00	P-110	21.45
Casing Joints	82	5 1/2	4.89	17.00	P-110	3,330.50
Air Lock	1	5 1/2	4.89	17.00	P-110	1.92
Marker Joint	1	5 1/2	4.89	17.00	P-110	19.41
Casing Joints	29	5 1/2	4.89	17.00	P-110	1,223.50
Marker Joint	1	5 1/2	4.89	17.00	P-110	18.69
Casing Joints	47	5 1/2	4.89	17.00	P-110	1,952.09
Marker Joint	1	5 1/2	4.89	17.00	P-110	18.30
Casing Joints	49	5 1/2	4.89	17.00	P-110	1,990.11
Marker Joint	1	5 1/2	4.89	17.00	P-110	17.83
Casing Joints	48	5 1/2	4.89	17.00	P-110	1,990.89
Marker Joint	1	5 1/2	4.89	17.00	P-110	21.29
Casing Joints	48	5 1/2	4.89	17.00	P-110	1,949.92
Toe Sleeve	1	5 1/2	4.89	17.00	P-110	5.10
Marker Joint	1	5 1/2	4.89	17.00	P-110	19.71
Float Collar	1	5 1/2	4.89	17.00	P-110	1.90
Casing Joints	1	5 1/2	4.89	17.00	P-110	43.34
Float Collar	1	5 1/2	4.89	17.00	P-110	1.90
Casing Joints	1	5 1/2	4.89	17.00	P-110	37.68
Float Shoe	1	5 1/2	4.89	17.00	P-110	1.63

Cement**Surface Casing Cement, Casing, 2/9/2022 12:40**

Description	String	Cementing Start Date	Cementing End Date
Surface Casing Cement	Surface, 388.9ftKB	2/9/2022 12:40	2/9/2022 15:00

Cement Stages

Stg #	Top (ftKB)	Btm (ftKB)	Com
1	28.0	392.0	PJSM, test lines, pump 10 bbls FW spacer, 10 bbls Sapp sweep, 10 bbls FW spacer & 86 bbls Type III cmt (350 sxs) @ 14.6 PPG, drop plug & disp w/ 49 bbls H2O. Bump plug @ 530 psi, circ 49 bbls good cmt to surface

Intermediate Casing Cement, Casing, 3/19/2022 12:20

Description	String	Cementing Start Date	Cementing End Date
Intermediate Casing Cement	Intermediate, 2,522.1ftKB	3/19/2022 12:20	3/19/2022 16:20

Cement Stages


Stg #	Top (ftKB)	Btm (ftKB)	Com
1	30.6	2,532.0	Cement Offline as follows: PJSM with Drake Energy Services. Pressure tested lines to 2,000 psi. Pumped 10 bbls FW, 20 bbls D-Mud Breaker, & 10 bbls of FW. Pumped Lead Cement: 180.6 bbls (474 sx) 90:10 Poz:Type III at 12.5 ppg, 2.14 ft3/sk, 12.05 gal H2O/sk. Pumped Tail Cement: 33.4 bbls (136 sx) Type III Blend at 14.6 ppg, 1.38 ft3/sk, 6.64 gal H2O/sk. Dropped plug & began displacement. Displaced with 181 bbls FW. FCP at 700 psi Didnt Bumped Plug Left 650 psi On Well. Shut in. Maintained returns throughout job. Calculated 49 bbls to surface. Top of Lead to surface and top of tail at 1,946 ft MD. Released Rig @ 12:30 3/19/2022 to the W. Lybrook Unit 763 H. (Cement 13:20 Hour's To 16:20 Hour's on -3/19/2022)

Production Casing Cement, Casing, 4/5/2022 11:30

Description	String	Cementing Start Date	Cementing End Date
Production Casing Cement	Production, 12,742.8ftKB	4/5/2022 11:30	4/5/2022 14:48

Well Name: GREATER LYBROOK UNIT 830H (fka W LYBROOK)

Horizontal, Original Hole, 7/5/2023 2:04:25 PM

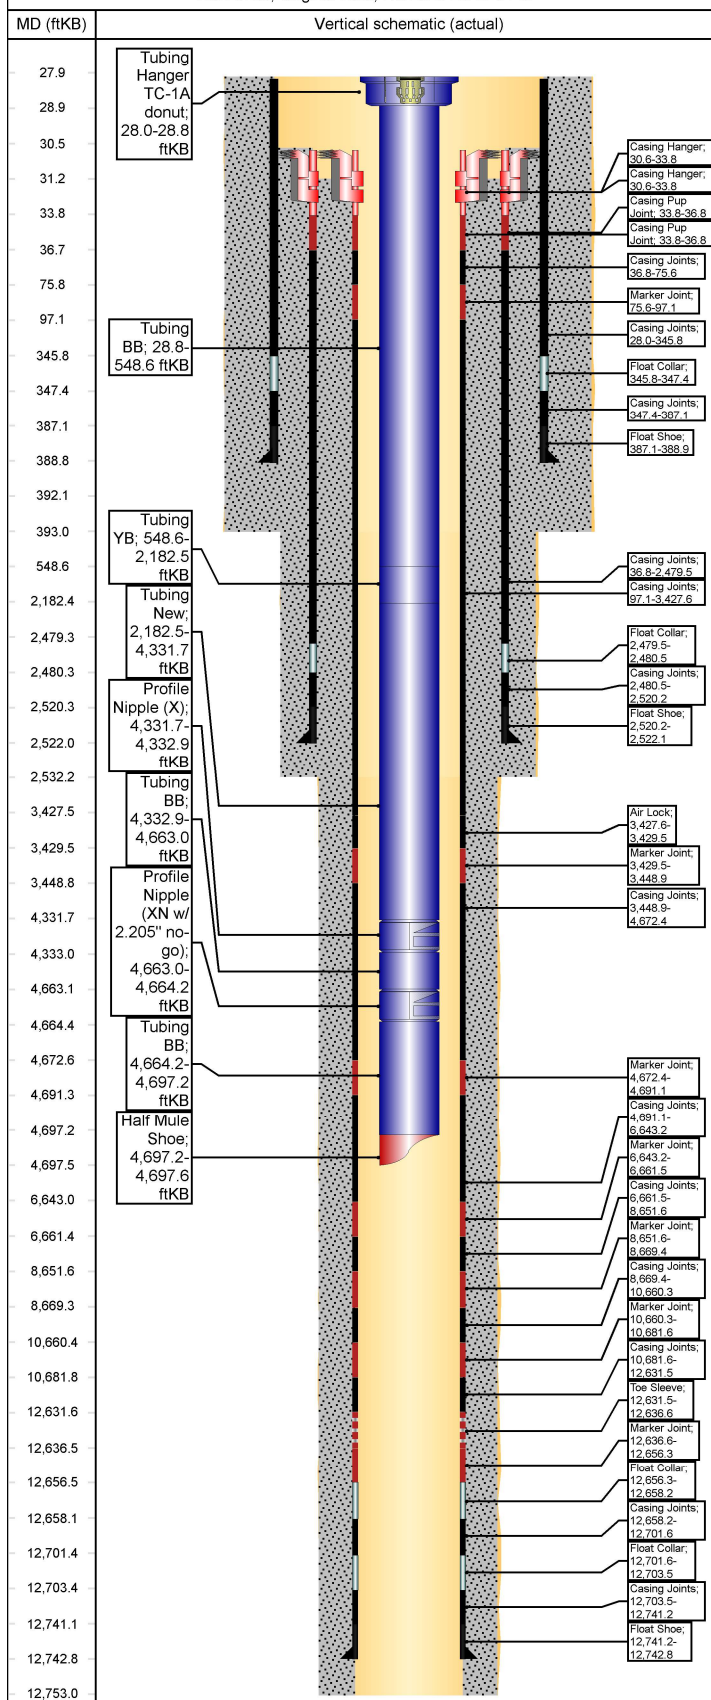

Cement Stages

Stg #	Top (ftKB)	Btm (ftKB)	Com
1	31.2	12,753.0	Cement Summary: PJSM with American Cementing. Pressure tested lines to 5000 psi. Pumped 60 bbls Intraguard Star @ 11.0 ppg. Pumped Lead Cement: 209.63. bbls (498 sx) ASTM Type I/II at 12.4 ppg, 2.36 ft3/sk, 13.4 gal H2O/sk. Pumped Tail Cement: 336.7 bbls (1209 sx) Class G Cement at 13.3 ppg, 1.56 ft3/sk, 7.7 gal H2O/sk. Washed lines, dropped plug & began displacement. Displaced with 262.8 bbls FW with cement retarder in 1st 50 bbls. FCP at 1,648 psi Didnt Bump Plug at 4.0 bpm to 1,648- psi. Bled back 1- Bbls and floats held. Top of Tail: Calculated 3863 ft MD. Tof of Lead: surface Cement Back 33- BBL, Calculated Back 60- bbl's Cement in place at 07:09- on 3/31/2022

Wellbores

Original Hole

Wellbore Name	Parent Wellbore
Original Hole	Original Hole

Wellbore Sections

Section Des	Size (in)	Act Top (ftKB)	Act Btm (ftKB)
Surface	17 1/2	28.0	393.0
Intermediate	12 1/4	393.0	2,532.0
Production	8 1/2	2,532.0	12,753.0

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 258677

CONDITIONS

Operator: ENDURING RESOURCES, LLC 6300 S Syracuse Way, Suite 525 Centennial, CO 80111	OGRID: 372286
	Action Number: 258677
	Action Type: [C-103] Sub. Workover (C-103R)

CONDITIONS

Created By	Condition	Condition Date
dmcclure	None	9/5/2023
