

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER		5. Lease Serial No.
1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		7. If Unit or CA Agreement, Name and No.
2. Name of Operator		8. Lease Name and Well No.
3a. Address		9. API Well No. 30-045-38385
3b. Phone No. (include area code)		10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
		13. State
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM. |

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



Approval Date: 08/16/2024

Additional Operator Remarks

Location of Well

0. SHL: SESE / 667 FSL / 1114 FEL / TWSP: 23N / RANGE: 10W / SECTION: 1 / LAT: 36.250546 / LONG: -107.842905 (TVD: 0 feet, MD: 0 feet)

PPP: NWNE / 448 FNL / 1480 FEL / TWSP: 23N / RANGE: 10W / SECTION: 12 / LAT: 36.247482 / LONG: -107.844137 (TVD: 4470 feet, MD: 4874 feet)

PPP: LOT 2 / 1900 FNL / 1 FWL / TWSP: 23N / RANGE: 9W / SECTION: 7 / LAT: 36.243504 / LONG: -107.839107 (TVD: 4472 feet, MD: 11382 feet)

BHL: SWSE / 335 FSL / 2160 FEL / TWSP: 23N / RANGE: 9W / SECTION: 7 / LAT: 36.235093 / LONG: -107.828474 (TVD: 4472 feet, MD: 11382 feet)

BLM Point of Contact

Name: CHRISTOPHER P WENMAN

Title: Natural Resource Specialist

Phone: (505) 564-7727

Email: cwenman@blm.gov

CONFIDENTIAL

C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024	
		Submittal Type:	☒ Initial Submittal ☐ Amended Report ☐ As Drilled

WELL LOCATION INFORMATION

API Number 30-045-38385	Pool Code 5860	Pool Name BISTI; S-GALLUP (O)
Property Code 336273 335196	Property Name ESCRITO P01 2310 FEDERAL COM	Well Number 134H
OGRID No. 371838	Operator Name DJR OPERATING, LLC	Ground Level Elevation 6857'
Surface Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal		Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal

Surface Location (SHL)

UL	Section	Township	Range	Lot	Ft from the N/S	Ft from the E/W	Latitude	Longitude	County
P	1	23N	10W		667' SOUTH	1114' EAST	36.250546° N	107.842905° W	SAN JUAN

Bottom Hole Location (BHL)

UL	Section	Township	Range	Lot	Ft from the N/S	Ft from the E/W	Latitude	Longitude	County
O	7	23N	9W		335' SOUTH	2160' EAST	36.235093° N	107.828474° W	SAN JUAN

Dedicated Acres PENETRATED SPACING UNIT; SEC 12: NW/NE, NE/NE, & SE/NE (120 AC.); SEC 7: LOT 2, LOT 3, NE/SW, SE/SW & SW/SE (200.36 AC.) = 320.36 ACRES	Infill or Defining Well	Defining Well API	Overlapping Spacing Unit (Y/N)	Consolidation Code
Order Numbers:	Well Setbacks are under Common Ownership: ☐ Yes ☐ No			

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Ft from the N/S	Ft from the E/W	Latitude	Longitude	County
B	12	23N	10W		448' NORTH	1480' EAST	36.247482° N	107.844137° W	SAN JUAN

Fist Take Point (FTP)

UL	Section	Township	Range	Lot	Ft from the N/S	Ft from the E/W	Latitude	Longitude	County
B	12	23N	10W		448' NORTH	1480' EAST	36.247482° N	107.844137° W	SAN JUAN

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Ft from the N/S	Ft from the E/W	Latitude	Longitude	County
O	7	23N	9W		335' SOUTH	2160' EAST	36.235093° N	107.828474° W	SAN JUAN

Unitized Area or Area of Uniform Interest	Spacing Unit Type ☒ Horizontal ☐ Vertical	Ground Floor Elevation
---	--	------------------------

OPERATOR CERTIFICATIONS

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.

Shaw-Marie Ford
Signature

9/9/2024
Date

Shaw-Marie Ford
Printed Name

sford@enduringresources.com
E-mail Address

SURVEYOR CERTIFICATIONS


I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.



Signature and Seal of Professional Surveyor:

Certificate Number 11393	Date of Survey MARCH 16, 2023
------------------------------------	---

Note: No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

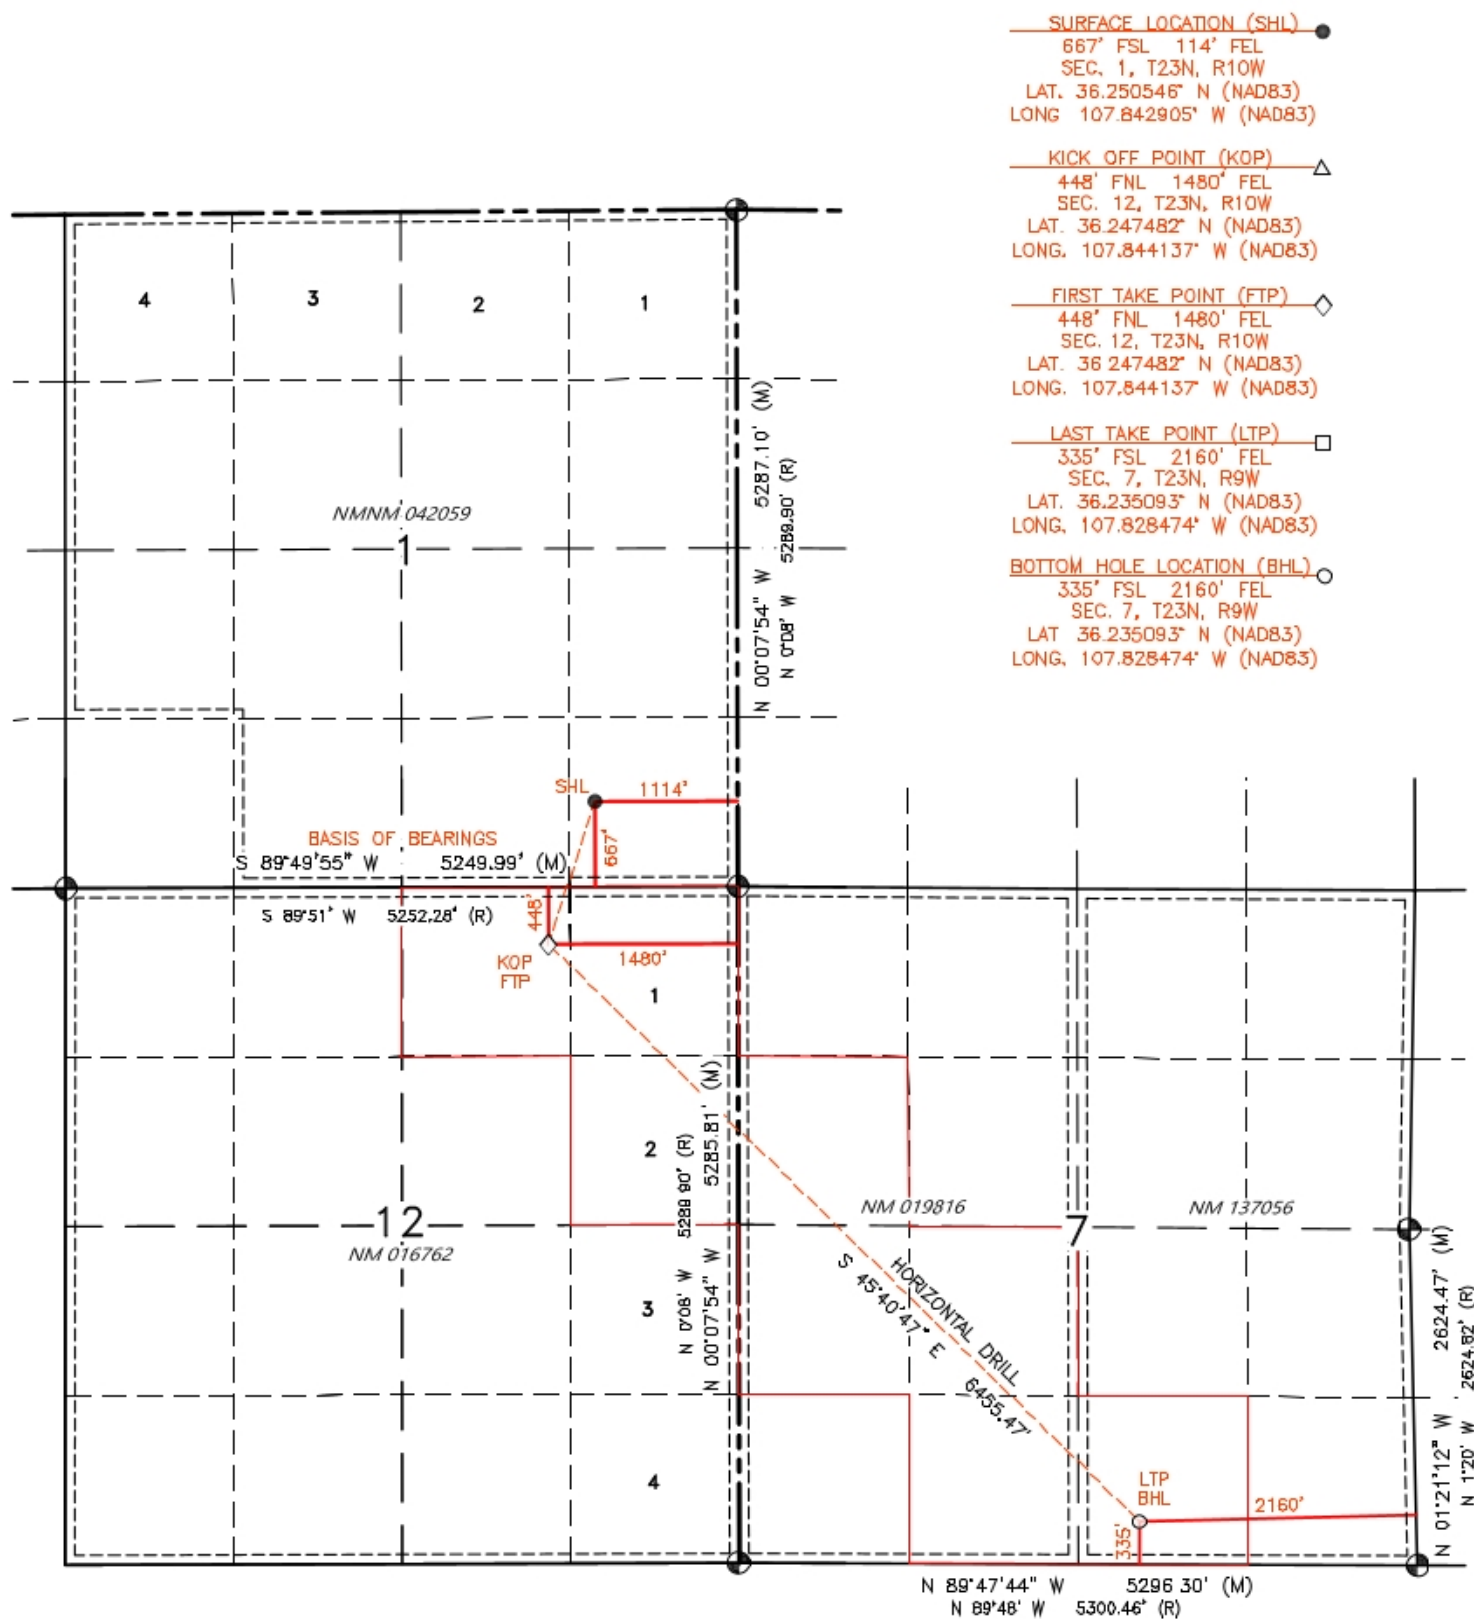

State of New Mexico
Energy, Minerals and Natural Resources DepartmentSubmit Electronically
Via E-permittingOil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505**NATURAL GAS MANAGEMENT PLAN**

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description
Effective May 25, 2021**I. Operator:** DJR Operating, LLC **OGRID:** 371838 **Date:** 09 / 09 / 2024**II. Type:** ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Escrito P01 2310 FED COM 106H	TBD	P-01-23N-10W	646' FSL x 1191' FEL	309	695	124
Escrito P01 2310 FED COM 108H	TBD	P-01-23N-10W	656' FSL x 1153' FEL	369	830	148
Escrito P01 2310 FED COM 133H	TBD	P-01-23N-10W	651' FSL x 1172' FEL	200	50	80
Escrito P01 2310 FED COM 134H	TBD	P-01-23N-10W	667' FSL x 1114' FEL	204	51	82
Escrito P01 2310 137H	TBD	P-01-23N-10W	661' FSL x 1133' FEL	208	52	83

IV. Central Delivery Point Name: Chaco Processing Plant [See 19.15.27.9(D)(1) NMAC]**V. Anticipated Schedule:** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Escrito P01 2310 FED COM 106H	TBD	7/11/2025	7/18/2025	8/26/2025	9/10/2025	9/13/2025
Escrito P01 2310 FED COM 108H	TBD	7/19/2025	7/27/2025	8/26/2025	9/15/2025	9/18/2025
Escrito P01 2310 FED COM 133H	TBD	7/28/2025	8/4/2025	8/26/2025	9/20/2025	9/23/2025
Escrito P01 2310 FED COM 134H	TBD	8/5/2025	8/12/2025	8/26/2025	9/25/2025	9/28/2025
Escrito P01 2310 137H	TBD	8/13/2025	8/21/2025	8/26/2025	9/30/2025	10/3/2025

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.**VII. Operational Practices:** ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.**VIII. Best Management Practices:** ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan**EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: <i>Shaw-Marie Ford</i>
Printed Name: Shaw-Marie Ford
Title: Regulatory Specialist
E-mail Address: sford@enduringresources.com
Date: 09/09/2024
Phone: 505-716-3297
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
Escrito P01 2310 FED COM 106H, 108H, 133H, 134H and Escrito P01 2310 137H
SESE P-01-23N-10W

SEPARATION EQUIPMENT

DJR Operating, LLC (DJR) has pulled representative pressurized samples from wells in the same producing formation. DJR has utilized these samples in process simulations to determine the amount of gas anticipated in each stage of the process and utilized this information with a safety factor to size the equipment listed below:

Separation equipment will be set as follows:

- Individual 3-phase separator will be set for the individual well.
- The separator will be sized based on the anticipated volume of the well and the pressure of the lines utilized for oil, gas, and water takeaway.
- The 3-phase production separator will be equipped with a 0.75 MMBtu/hr indirect fired heater.

Heater treaters will be set as follows:

- Individual heater treaters will be set for the individual well.
- The heater treaters are sized based on the anticipated combined volume of oil and produced water predicted to come from the initial 3-phase separator.
- Oil will be separated from the produced water and the oil/produced water will be sent to its respective tanks.
- The combined oil and natural gas stream is routed to the Vapor Recovery Tower.

Vapor Recovery Equipment will be set as follows:

- The Vapor Recovery Tower has been sized, based on the anticipated volume of gas from the heater treater and oil and water tanks.
- The Vapor Recovery Unit has been sized, based on the anticipated volume of gas from the heater treater and oil and water tanks. The Vapor Recovery Unit is utilized to push the recovered gas into the sales pipeline.

Production storage tanks will be set as follows:

- The oil and produced water tanks utilize a closed vent capture system to ensure all breathing, working, and flashing losses are routed to the Vapor Recovery Tower and Vapor Recovery Unit.
- Each of the production storage tanks will be equipped with a 0.5 MMBtu/hr indirect heater.



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
Escrito P01 2310 FED COM 106H, 108H, 133H, 134H and Escrito P01 2310 137H
SESE P-01-23N-10W

VENTING and FLARING

DJR Operating, LLC (DJR) has a natural gas system available prior to startup of completion operations. DJR utilizes a Vapor Recovery Unit System and sells all natural gas except during periods of startup, shutdown, maintenance, or malfunction for the gas capturing equipment, including the vapor recovery tower, vapor recovery unit, storage tanks, and pipelines.

Currently, DJR utilizes the following from list A-I of Section 3 for its operations to minimize flaring:

- a) DJR utilizes natural gas-powered generators to power its leases where grid power isn't available.
- b) When electrical grid power is unavailable, natural gas generators will be used for major equipment onsite.
- c) DJR's in service compression will be natural gas powered.
- d) Should liquids removal, such as dehydration be required, units will be powered by natural gas.

DJR will only flare gas during the following times:

- Scheduled maintenance for gas capturing equipment including:
 - Vapor Recovery Tower
 - Vapor Recovery Unit
 - Storage tanks
 - Pipelines
 - Emergency flaring



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
Escrito P01 2310 FED COM 106H, 108H, 133H, 134H and Escrito P01 2310 137H
SESE P-01-23N-10W

OPERATIONAL PRACTICES

19.15.27.8 A. Venting and Flaring of Natural Gas

DJR Operating, LLC (DJR) understands the requirements of NMAC 19.15.27.8 which states that the venting and flaring of natural gas during drilling, completion or production that constitutes waste as defined in 19.15.2 are prohibited.

19.15.27.8 B. Venting and flaring during drilling operations

- DJR shall capture or combust natural gas if technically feasible during drilling operations using best industry practices.
- A flare stack with a 100% capacity for expected volumes will be set on location of the facility at least 100 feet from the nearest surface hole location, well heads, and storage tanks.
- In the event of an emergency, DJR will vent natural gas in order to avoid substantial impact. DJR shall report the vented or flared gas to the NMOCD.

19.15.27.8 E. Venting and flaring during completion or recompletion operations

During Completion Operations, DJR utilizes the following:

- DJR facilities are built and ready from day 1 of Flowback.
- Individual well test separators will be set to properly separate gas and liquids. Temporary test separator will be utilized initially to process volumes. In addition, separators will be tied into flowback tanks which will be tied into the gas processing equipment for sales down a pipeline. See Separation Equipment for details.
- Should the facility not yet be capable of processing gas, or the gas does not meet quality standards, then storage tanks will be set that are tied into gas busters or temporary flare to manage natural gas. This flare would meet the following requirements:
 - 1) An appropriately sized flare stack with an automatic igniter.
 - 2) DJR analyzes the natural gas samples twice per week.
 - 3) DJR routes the natural gas into a gathering pipeline as soon as the pipeline specifications are met.
 - 4) DJR provides the NMOCD with pipeline specifications and natural gas data.



19.15.27.8 D. Venting and flaring during production operations

During Production Operations DJR will not vent or flare natural gas except under the following circumstances:

1. During an emergency or malfunction
2. To unload or clean-up liquid holdup in a well to atmospheric pressure, provided:
 - a. DJR does not vent after the well achieves a stabilized rate and pressure.
 - b. DJR will remain present on-site during liquids unloading by manual purging and take all reasonable actions to achieve a stabilized rate and pressure at the earliest practical time.
 - c. DJR will optimize the system to minimize natural gas venting on any well equipped with a plunger lift or auto control system.
 - d. Best Management Practices will be used during downhole well maintenance.
3. During the first year of production from an exploratory well provided:
 - a. DJR receives approval from the NMOCD.
 - b. DJR remains in compliance with the NM gas capture requirements.
 - c. DJR submits an updated C-129 form to the NMOCD.
4. During the following activities unless prohibited:
 - a. Gauging or sampling a storage tank or low-pressure production vessel.
 - b. Loading out liquids from a storage tank.
 - c. Repair and maintenance.
 - d. Normal operation of gas activated pneumatic controller or pump.
 - e. Normal operation of a storage tank but not including venting from a thief hatch.
 - f. Normal operation of dehydration units.
 - g. Normal operations of compressors, compressor engines, turbines, valves, flanges, and connectors.
 - h. During a bradenhead, packer leakage test, or production test lasting less than 24-hours.
 - i. When natural gas does not meet the gathering pipeline specifications.
 - j. Commissioning of pipelines, equipment, or facilities only for as long as necessary to purge introduced impurities.

19.15.27.8 E. Performance standards

1. DJR has utilized process simulations with a safety factor to design all separation and storage equipment. The equipment is routed to a Vapor Recovery System and utilizes a flare as back up for periods of startup, shutdown, maintenance, or malfunction of the VRU System.
2. DJR will install a flare that designed to handle the full volume of vapors from the facility in case of the VRU failure and it is designed with an auto ignition system.
3. Flare stacks will appropriately sized and designed to ensure proper combustion efficiency.



- a. Flare stacks installed or replaced will be equipped with an automatic ignitor or continuous pilot.
 - b. Previously installed flare stacks will be retrofitted with an automatic ignitor, continuous pilot, or technology that alerts DJR of flare malfunction within 18 months after May 25, 2021.
 - c. Flare stacks replaced after May 25, 2021, will be equipped with an automatic ignitor or continuous pilot if located at a well or facility with average daily production of 60,000 cubic feet of natural gas or less.
 - d. Flare stacks will be located at least 100 feet from the well and storage tanks and securely anchored.
4. DJR will conduct an AVO inspection on all components for leaks and defects on a weekly basis.
 5. DJR will make and keep records of AVO inspections which will be available to the NMOCD for at least 5 years.
 6. DJR may use a remote or automated monitoring technology to detect leaks and releases in lieu of AVO inspections with prior NMOCD approval.
 7. Facilities will be designed to minimize waste.
 8. DJR will resolve emergencies as promptly as possible.

19.15.27.8 F. Measurement or estimation of vented and flared natural gas

1. DJR will have meters on both the low- and high-pressure sides of the flares and the volumes will be recorded in DJR's SCADA system.
2. DJR will install equipment to measure the volume of flared natural gas that has an average daily production of 60,000 cubic feet or greater of natural gas.
3. DJR's measuring equipment will conform to the industry standards.
4. The measurement system is designed such that it cannot be bypassed except for inspections and servicing meters.
5. DJR will estimate the volume of vented or flared natural gas using a methodology that can be independently verified if metering is not practicable due to low flow rate or pressure.
6. DJR will estimate the volume of flared and vented natural gas based on the results of an annual GOR test for wells that do not require measuring equipment reported on Form C-116.
7. DJR will install measuring equipment whenever the NMOCD determines that metering is necessary.



DJR OPERATING, LLC.
OGRID NO: 371838
NATURAL GAS MANAGEMENT PLAN
Escrito P01 2310 FED COM 106H, 108H, 133H, 134H and Escrito P01 2310 137H
SESE P-01-23N-10W

BEST MANAGEMENT PRACTICES

DJR Operating, LLC (DJR) utilizes the following Best Management Practices to minimize venting during active and planned maintenance.

DJR has a closed vent capture system to route emissions from the heater treater, tanks, and vapor recovery to the vapor recovery unit with an enclosed combustion device (ECD) for backup. The system is designed such that if the vapor recovery unit is taken out of service for any reason, the vapors will be routed to the ECD for combustion.

DJR will isolate and attempt to route all vapors to the vapor recovery unit or ECD prior to opening any lines for maintenance to minimize venting from the equipment.

DJR shall notify the NMOCD of venting or flaring that exceeds 50 MCF but less than 500 MCF in volume that either resulted from an emergency or malfunction, or an event lasting over eight hours or more cumulatively within any 24-hour period from a single event by filing a form C-129 no later than 15 days following the discovery or commencement of venting or flaring.

DJR shall notify the NMOCD verbally or by e-mail within 24-hours following discovery or commencement of venting or flaring that exceeds 500 MCF in volume or otherwise qualifies as a major release as defined in 19.15.29.7 NMAC from a single event and provide the information required in form C-129 to the NMOCD no later than 15 days that verifies, updates, or corrects the verbal or e-mail notification.

DJR will install measuring equipment to conform to industry standards such as American Petroleum Institute (API) Manual of Petroleum Measurement Standards (MPMS) Chapter 14.10 Measurement of Flow to Flares.

DJR's measuring equipment shall not be designed or equipped with a manifold that allows the diversion of natural gas around the metering element except for the sole purpose of inspecting and servicing the measurement equipment.

DJR shall report the volume of vented and flared natural gas for each well or facility at which venting or flaring occurred on a monthly basis.

Rev 0



DRILLING AND CASING PLAN

Escrito P01 2310 Federal COM #134H

San Juan County, New Mexico

Surface Location

1114-ft FEL & 667-ft FSL
 Sec 1 T23N R10W
 Graded Elevation 6857' MSL
 RKB Elevation 6871' (14' KB)

SHL Geographical Coordinates (NAD-83)

Latitude 36.2505460° N
 Longitude 107.8429050° W

Kick Off Point for Horizontal Build Curve

4062-ft MD
 3942-ft TVD

Local Coordinates (from SHL)

626-ft South
 652-ft West

Heel Location (Pay zone entry)

1480-ft FEL & 448-ft FNL
 Sec 12 T23N R10W

Heel Geographical Coordinates (NAD-83)

Latitude 36.24748246° N
 Longitude 107.84413676° W

Bottom Hole Location (TD)

2160-ft FEL & 335-ft FSL
 Sec 7 T23N R9W

BHL Geographical Coordinates (NAD-83)

Latitude 36.23509284° N
 Longitude 107.8284741° W

Well objectives

This well is planned as a 6460-ft lateral in the Mancos Silt sand.

Bottom Hole temperature and pressure

The temperature in the Mancos Silt horizontal objective is 130°F. Bottom hole pressure in the Mancos Silt is forecast to be 1985 psi.

Formation Tops (Sd = Sand; Sh = Shale; Siltstone = Slt, Coal = C; W = water; O = oil; G = gas; NP = no penetration)

Name	MD (ft)	TVD (ft)	Lithology	Pore fluid	Expected Pore Pressure (ppg)	Planned Mud Weight (ppg)
Ojo Alamo	458	458	Sd	W	8.3	8.4 – 8.8
Kirtland	584	584	Sh	-	8.3	8.4 – 8.8
Fruitland	998	990	C	G	8.3	9.0 - 9.5
Pictured Cliffs	1257	1239	Sd	W	8.3	9.0 - 9.5
Lewis	1409	1386	Sh	-		9.0 - 9.5
Chacra	2067	2020	Sd	-	8.3	9.0 - 9.5
Menefee	2707	2637	Sd, C	G	8.3	9.0 - 9.5
Point Lookout	3731	3623	Sd	-	8.3	9.0 - 9.5
Mancos	3882	3769	Sh	-		9.0 - 9.5
Mancos Silt	4213	4086	Slt	O/G	6.6	9.0 - 9.5
Gallup A	NP	4598	Slt	O/G	6.6	9.0 - 9.5
Gallup B	NP	4654	Sd	O/G	6.6	8.8 - 9.0
Gallup C	NP	NP	Sd	O/G	6.6	8.8 - 9.0
Target	4926	4472	Sd	O/G	6.6	8.8 - 9.0

Casing Program

Casing OD	Hole Size	Weight (#/ft)	Grade	Coupling	MD Top	MD Bottom	TVD Top	TVD Bottom	Top of Cement
9-5/8"	12-1/4"	36	K-55	STC	surf	350	surf	350	surface
7"	8-3/4"	26	K-55	LTC	surf	4874	surf	4470	surface
4-1/2"	6-1/8"	11.6	P-110	BTC	4625	11382	4396	4435	4625

Note: all casing will be new

Rev 0



Casing Design Load Cases

		Casing String		
Description		9-5/8" Surface	7" Intermediate	4-1/2" Production Liner
Collapse	Full internal evacuation ¹	✓	✓	✓
	Cementing	✓	✓	✓
Burst	Pressure test	✓ ²	✓ ²	✓
	Gas kick		✓ ³	
	Fracture at shoe, 1/3 BHP at surface		✓ ⁴	
	Injection down casing			✓ ⁵
Axial	Dynamic load on casing coupling ⁶	✓	✓	✓
Axial	Overpull ⁷	✓	✓	✓

Note

- 1 Fluid level at shoe, air column to surface, pore pressure outside
- 2 Tested to 80% of minimum internal yield with freshwater inside, pore pressure outside
- 3 50 bbl kick at TD, 0.50 ppg intensity, 4" drill pipe, 9.0 ppg mud, fracture gradient at shoe
- 4 2060 psi BHP, 687 psi surface pressure, 12.5 ppg EMW shoe integrity
- 5 Surface stimulation pressure of 8000 psi on 8.3 ppg fluid column. Stimulation will be down frac string, so load does not apply to 7" intermediate casing.
- 6 Shock load from abrupt pipe deceleration, evaluated against coupling rating
- 7 Overpull values as follows: Surface casing 20,000 lbs, Intermediate & Production 100,000 lbs

Casing Design Factors

		Design Factors			
Casing string	Casing OD	Burst	Collapse	Axial	Triaxial
Surface	9-5/8"	1.25	13.38	8.16	1.56
Intermediate	7"	1.25	1.50	1.68	1.34
Production liner	4-1/2"	1.37	3.68	1.88	1.69

Cement Design

9-5/8" Surface Casing

	Lead
Name	Redi-Mix
Type	I-II
Planned top	Surface
Density (ppg)	14.50
Yield (cf/sx)	1.61
Mix water (gal/sx)	7.41
Volume (sx)	114
Volume (bbls)	33
Volume (cu. ft.)	185
Excess %	50

7" Intermediate Casing

	Lead	Tail
	American	American
Type	I/II	Poz/G
Planned top	Surface	3882-ft
Density (ppg)	12.30	13.50
Yield (cf/sx)	2.34	1.51
Mix water (gal/sx)	13.22	7.13
Volume (sx)	429	105
Volume (bbls)	179	28
Volume (cu.ft.)	1004	158
Excess %	78	0



Rev 0

4-1/2" Production Liner

Type	American
Planned top	Poz/G
Density (ppg)	4625-ft
Yield (cf/sx)	13.3
Mix water (gal/sx)	1.52
Volume (sx)	7.53
Volume (bbls)	584
Volume (cu.ft)	158
Excess %	888
	40

Wellhead & Pressure Control

The well head will be an 11" 5M multi-bowl system. A 3M BOPE conforming to Onshore Order #2 will be installed on the surface casing. The BOP and accumulator will meet API 16D and 16E respectively.

A PVT mud monitoring system and a trip tank will be rigged up and operational for all hole intervals. An electronic geolograph will be employed to monitor and record drilling data (ROP, WOB, SPM, Pressure, RPM and torque).

Mud Program

Surface hole will be drilled with a fresh water, native mud system. In intermediate hole, a low weight 7% KCl LSND drilling fluid will be used, with KCl providing chemical stability for the young shales and clays present in the interval. In production hole a LSND system with polymer and lubricant additives is programmed. Sufficient drill water and mud additives will be on hand to maintain adequate pit volumes and maintain well control.

Hole Section	Fluid type	Interval (MD)	Density (ppg)	Funnel Viscosity	Yield Point	Fluid Loss (cc/30 min)
Surface	Fresh water spud mud	0 – 350	8.4 – 8.8	32 – 44	2 – 12	NC
Intermediate	7% KCl Low solids, non-dispersed	350 – 4874	9.0 – 9.5	38 – 45	8 – 14	<20
Production	Low solids, non-dispersed	4874 – 11382	8.8 – 9.2	34 – 38	6 – 8	6 – 8

Cores, tests and logs

Wellbore surveying: Drift (inclination only) surveys will be obtained in surface hole. MWD directional surveys will be taken in intermediate and production hole.

Logging while drilling: None in surface hole. MWD GR in intermediate and production hole.

Mud logging: a two-person mud logging unit with C1 – C4 gas analysis will be operational in intermediate and production hole.

Electric logging: No open hole electric logs are programmed. A cased hole GR/CCL will be run during completions for perforating depth control.

Cuttings and drilling fluids management


A closed loop, steel tank-based circulating system will be used. In addition to the rig solids control equipment, a dewatering centrifuge and chemical flocculation system will be operational to strip solids from the whole mud. All solids will be collected in 3-sided bins and will then be put into transports with a bucket loader. Drying agents will be used if necessary. The solids will be taken to a licensed commercial disposal facility. Whole mud will be dewatered back to drill water and used as make up for subsequent wells or hauled off for disposal. A diagram of the closed loop system is included.

Completion

It is envisioned that this well will be completed with a multi-stage sand frac, using the plug and perf technique. After drilling out the plugs, the current plan is to install a 2-7/8" plunger-assisted gas lift tubing string. The stimulation and completion plan will be sundried at a later date.




Proposed BOP stack 11" 3M RRA

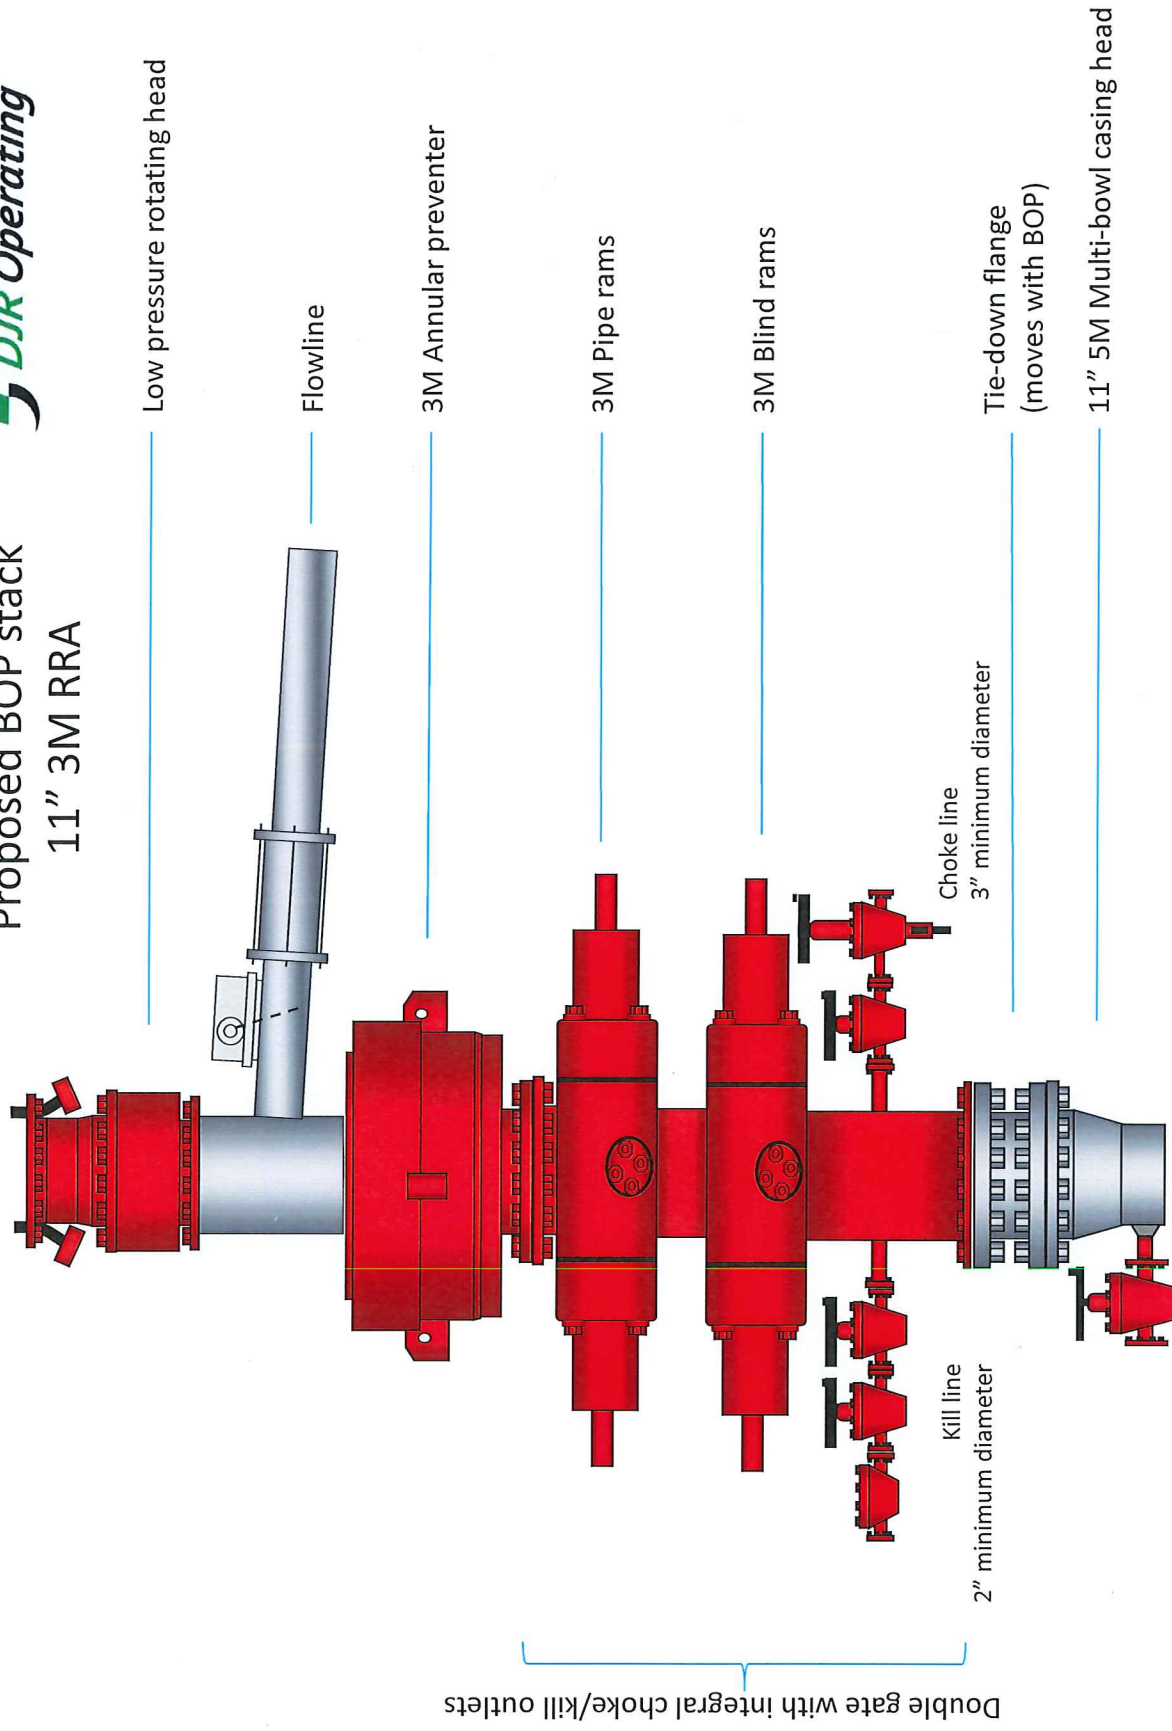



Choke Manifold

Actual system to conform with Onshore Order 2

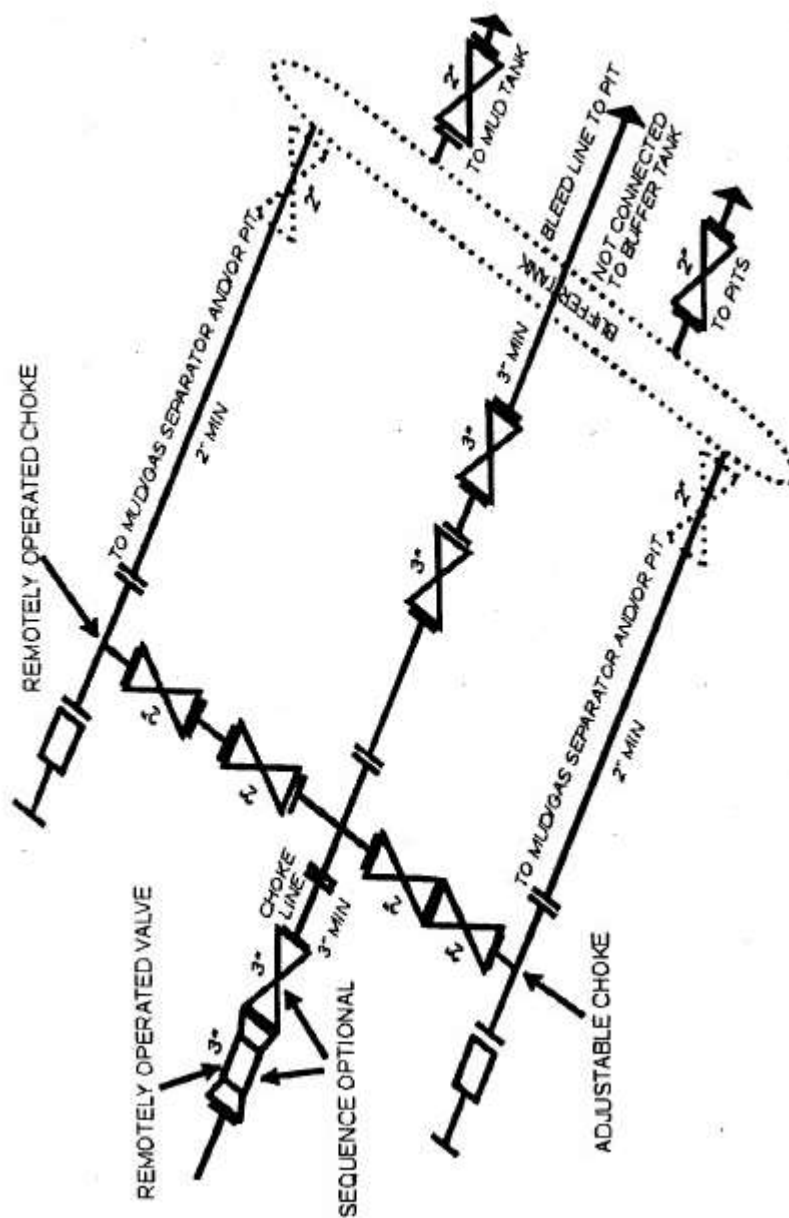



Company: DJR Operating
Project: Ponderosa Unit
Site: P01 2310 Pad
Well: Escrito P01 2310 Federal COM 134H
Wellbore: Original Drilling
Design: APD

WELL DETAILS: Escrito P01 2310 Federal COM 134H

+N/-S	+E/-W	Northing	Eastings	Latitude	Longitude
0.00	0.00	1910497.4087	2720269.4709	36.2505460	-107.8429050

Plan: APD (Escrito P01 2310 Federal COM 134H/Original Drilling)

Created By: Janie Collins Date: 16:26, September 11 2023

PROJECT DETAILS: Ponderosa Unit



Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Western Zone
System Datum: Mean Sea Level
Local North: True

DESIGN TARGET DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00
964.03	15.51	226.18	957.17	52.54	-54.75	2.75	226.18	18.86
4863.50	85.11	344.12	4863.50	-535.43	535.43	0.00	0.00	18.86
4926.00	90.33	134.31	4434.99	-1115.20	-5624.99	10.00	-91.71	670.20
11382.00	90.33	134.31	4434.99	-5624.99	4255.79	0.00	0.00	7053.53

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00
964.03	15.51	226.18	957.17	52.54	-54.75	2.75	226.18	18.86
4863.50	85.11	344.12	4863.50	-535.43	535.43	0.00	0.00	18.86
4926.00	90.33	134.31	4434.99	-1115.20	-5624.99	10.00	-91.71	670.20
11382.00	90.33	134.31	4434.99	-5624.99	4255.79	0.00	0.00	7053.53

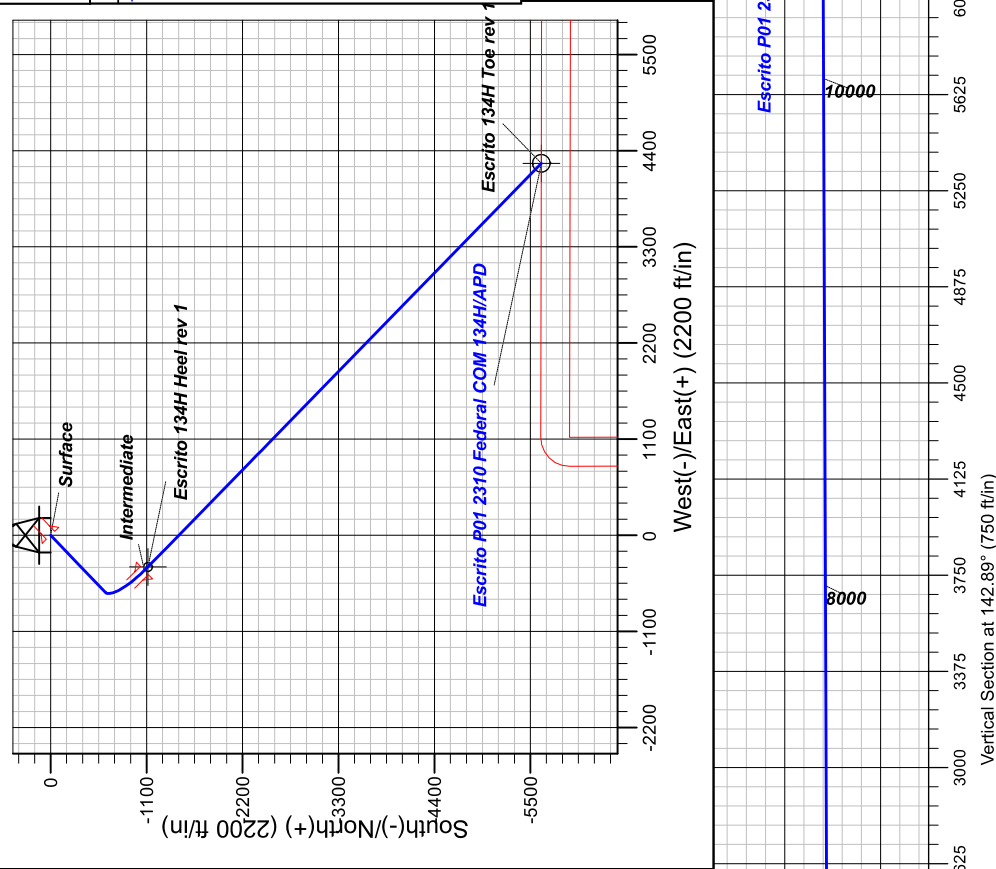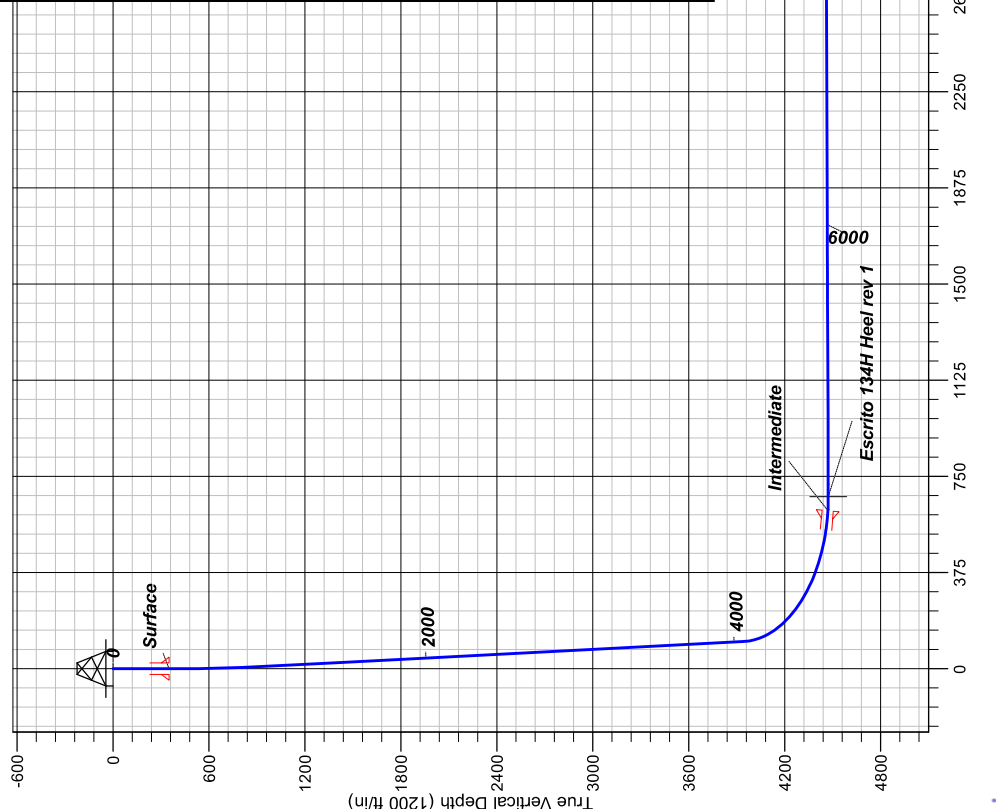

Azimuths to True North
Magnetic North: 8.8°
Magnetic Field
Strength: 49081.0 A/m
Dip Angle: 62.6°
Date: 1/9/2023
Model: HDGM2.3

CASING DETAILS

TVD	MD	Name
350.00	350.00	Surface
4469.69	4871.99	Intermediate

FORMATION DETAILS

TVDPath	MDPath	Formation
458.00	458.01	Ojo Alamo
584.00	584.24	Kirland
990.00	998.11	Fruiland
1239.00	1256.52	Pictured Cliffs
1386.00	1409.07	Lewis
2020.00	2067.04	Chacra
2637.00	2707.36	Menefee
3623.00	3730.62	Point Lookout
3769.00	3882.14	Mancos
4086.00	4212.89	Mancos Silt

Escrito 134H Toe rev 1
Escrito P01 2310 Federal COM 134H/APD



DJR Operating

Ponderosa Unit

P01 2310 Pad

Escrito P01 2310 Federal COM 134H - Slot 5

Original Drilling

Plan: APD

Standard Planning Report

11 September, 2023





Lonestar Consulting, LLC
Planning Report



Database:	Grand Junction	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Company:	DJR Operating	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Project:	Ponderosa Unit	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site:	P01 2310 Pad	North Reference:	True
Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Project	Ponderosa Unit		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Western Zone		

Site	P01 2310 Pad				
Site Position:		Northing:	1,910,476.6671 usft	Latitude:	36.2504890
From:	Lat/Long	Easting:	2,720,191.9235 usft	Longitude:	-107.8431680
Position Uncertainty:	0.00 ft	Slot Radius:	13.200 in		

Well	Escrito P01 2310 Federal COM 134H - Slot 5					
Well Position	+N/-S	0.00 ft	Northing:	1,910,497.4086 usft	Latitude:	36.2505460
	+E/-W	0.00 ft	Easting:	2,720,269.4709 usft	Longitude:	-107.8429050
Position Uncertainty		0.00 ft	Wellhead Elevation:	ft	Ground Level:	6,857.00 ft
Grid Convergence:		-0.01 °				

Wellbore	Original Drilling				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM2023	1/9/2023	8.62	62.67	49,081.00000000

Design	APD			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)
	0.00	0.00	0.00	142.89

Plan Survey Tool Program			Date	3/7/2023	
Depth From (ft)	Depth To (ft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.00	11,382.00	APD (Original Drilling)	MWD+HDGM	
				OWSG MWD + HDGM	

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00	
964.03	15.51	226.18	957.17	-52.54	-54.75	2.75	2.75	0.00	226.18	
4,061.50	15.51	226.18	3,941.82	-626.05	-652.43	0.00	0.00	0.00	0.00	
4,926.41	90.33	134.31	4,471.99	-1,115.20	-363.20	10.50	8.65	-10.62	-91.71	Escrito 134H Heel rev
11,382.00	90.33	134.31	4,434.99	-5,624.99	4,255.79	0.00	0.00	0.00	0.00	Escrito 134H Toe rev



Lonestar Consulting, LLC

Planning Report



Database:	Grand Junction	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Company:	DJR Operating	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Project:	Ponderosa Unit	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site:	P01 2310 Pad	North Reference:	True
Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	2.75	226.18	499.96	-1.66	-1.73	0.28	2.75	2.75	0.00
600.00	5.50	226.18	599.69	-6.64	-6.92	1.12	2.75	2.75	0.00
700.00	8.25	226.18	698.96	-14.93	-15.56	2.52	2.75	2.75	0.00
800.00	11.00	226.18	797.55	-26.50	-27.62	4.47	2.75	2.75	0.00
900.00	13.75	226.18	895.21	-41.34	-43.08	6.97	2.75	2.75	0.00
964.03	15.51	226.18	957.17	-52.54	-54.75	8.86	2.75	2.75	0.00
1,000.00	15.51	226.18	991.83	-59.20	-61.69	9.99	0.00	0.00	0.00
1,100.00	15.51	226.18	1,088.18	-77.71	-80.99	13.11	0.00	0.00	0.00
1,200.00	15.51	226.18	1,184.54	-96.23	-100.28	16.23	0.00	0.00	0.00
1,300.00	15.51	226.18	1,280.90	-114.74	-119.58	19.36	0.00	0.00	0.00
1,400.00	15.51	226.18	1,377.26	-133.26	-138.87	22.48	0.00	0.00	0.00
1,500.00	15.51	226.18	1,473.62	-151.77	-158.17	25.60	0.00	0.00	0.00
1,600.00	15.51	226.18	1,569.97	-170.29	-177.47	28.73	0.00	0.00	0.00
1,700.00	15.51	226.18	1,666.33	-188.81	-196.76	31.85	0.00	0.00	0.00
1,800.00	15.51	226.18	1,762.69	-207.32	-216.06	34.97	0.00	0.00	0.00
1,900.00	15.51	226.18	1,859.05	-225.84	-235.35	38.10	0.00	0.00	0.00
2,000.00	15.51	226.18	1,955.41	-244.35	-254.65	41.22	0.00	0.00	0.00
2,100.00	15.51	226.18	2,051.76	-262.87	-273.94	44.34	0.00	0.00	0.00
2,200.00	15.51	226.18	2,148.12	-281.38	-293.24	47.47	0.00	0.00	0.00
2,300.00	15.51	226.18	2,244.48	-299.90	-312.54	50.59	0.00	0.00	0.00
2,400.00	15.51	226.18	2,340.84	-318.41	-331.83	53.71	0.00	0.00	0.00
2,500.00	15.51	226.18	2,437.20	-336.93	-351.13	56.84	0.00	0.00	0.00
2,600.00	15.51	226.18	2,533.55	-355.44	-370.42	59.96	0.00	0.00	0.00
2,700.00	15.51	226.18	2,629.91	-373.96	-389.72	63.08	0.00	0.00	0.00
2,800.00	15.51	226.18	2,726.27	-392.48	-409.01	66.21	0.00	0.00	0.00
2,900.00	15.51	226.18	2,822.63	-410.99	-428.31	69.33	0.00	0.00	0.00
3,000.00	15.51	226.18	2,918.99	-429.51	-447.60	72.45	0.00	0.00	0.00
3,100.00	15.51	226.18	3,015.34	-448.02	-466.90	75.58	0.00	0.00	0.00
3,200.00	15.51	226.18	3,111.70	-466.54	-486.20	78.70	0.00	0.00	0.00
3,300.00	15.51	226.18	3,208.06	-485.05	-505.49	81.82	0.00	0.00	0.00
3,400.00	15.51	226.18	3,304.42	-503.57	-524.79	84.95	0.00	0.00	0.00
3,500.00	15.51	226.18	3,400.77	-522.08	-544.08	88.07	0.00	0.00	0.00
3,600.00	15.51	226.18	3,497.13	-540.60	-563.38	91.19	0.00	0.00	0.00
3,700.00	15.51	226.18	3,593.49	-559.11	-582.67	94.32	0.00	0.00	0.00
3,800.00	15.51	226.18	3,689.85	-577.63	-601.97	97.44	0.00	0.00	0.00
3,900.00	15.51	226.18	3,786.21	-596.15	-621.27	100.56	0.00	0.00	0.00
4,000.00	15.51	226.18	3,882.56	-614.66	-640.56	103.69	0.00	0.00	0.00
4,061.50	15.51	226.18	3,941.82	-626.05	-652.43	105.61	0.00	0.00	0.00
4,100.00	15.90	211.28	3,978.90	-634.12	-658.88	108.15	10.50	1.01	-38.72
4,200.00	20.82	181.26	4,073.99	-663.68	-666.40	127.19	10.50	4.92	-30.02
4,300.00	28.79	164.72	4,164.80	-704.79	-660.43	163.57	10.50	7.97	-16.53
4,400.00	37.94	155.25	4,248.29	-756.08	-641.16	216.10	10.50	9.14	-9.47
4,500.00	47.58	149.09	4,321.66	-815.83	-609.25	283.01	10.50	9.64	-6.16
4,600.00	57.46	144.60	4,382.45	-882.04	-565.75	362.06	10.50	9.88	-4.49
4,700.00	67.47	141.01	4,428.64	-952.50	-512.13	450.59	10.50	10.01	-3.59
4,800.00	77.55	137.92	4,458.66	-1,024.83	-450.18	545.66	10.50	10.08	-3.10
4,900.00	87.66	135.06	4,471.53	-1,096.63	-381.97	644.07	10.50	10.11	-2.86
4,926.41	90.33	134.31	4,471.99	-1,115.20	-363.20	670.20	10.50	10.12	-2.81



Lonestar Consulting, LLC

Planning Report



Database:	Grand Junction	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Company:	DJR Operating	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Project:	Ponderosa Unit	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site:	P01 2310 Pad	North Reference:	True
Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
5,000.00	90.33	134.31	4,471.57	-1,166.61	-310.55	742.96	0.00	0.00	0.00	
5,100.00	90.33	134.31	4,471.00	-1,236.46	-239.00	841.85	0.00	0.00	0.00	
5,200.00	90.33	134.31	4,470.42	-1,306.32	-167.45	940.73	0.00	0.00	0.00	
5,300.00	90.33	134.31	4,469.85	-1,376.18	-95.90	1,039.61	0.00	0.00	0.00	
5,400.00	90.33	134.31	4,469.28	-1,446.04	-24.35	1,138.49	0.00	0.00	0.00	
5,500.00	90.33	134.31	4,468.70	-1,515.90	47.20	1,237.37	0.00	0.00	0.00	
5,600.00	90.33	134.31	4,468.13	-1,585.76	118.75	1,336.25	0.00	0.00	0.00	
5,700.00	90.33	134.31	4,467.56	-1,655.62	190.30	1,435.13	0.00	0.00	0.00	
5,800.00	90.33	134.31	4,466.99	-1,725.48	261.86	1,534.01	0.00	0.00	0.00	
5,900.00	90.33	134.31	4,466.41	-1,795.33	333.41	1,632.89	0.00	0.00	0.00	
6,000.00	90.33	134.31	4,465.84	-1,865.19	404.96	1,731.77	0.00	0.00	0.00	
6,100.00	90.33	134.31	4,465.27	-1,935.05	476.51	1,830.65	0.00	0.00	0.00	
6,200.00	90.33	134.31	4,464.69	-2,004.91	548.06	1,929.53	0.00	0.00	0.00	
6,300.00	90.33	134.31	4,464.12	-2,074.77	619.61	2,028.41	0.00	0.00	0.00	
6,400.00	90.33	134.31	4,463.55	-2,144.63	691.16	2,127.29	0.00	0.00	0.00	
6,500.00	90.33	134.31	4,462.97	-2,214.49	762.71	2,226.17	0.00	0.00	0.00	
6,600.00	90.33	134.31	4,462.40	-2,284.34	834.26	2,325.05	0.00	0.00	0.00	
6,700.00	90.33	134.31	4,461.83	-2,354.20	905.81	2,423.94	0.00	0.00	0.00	
6,800.00	90.33	134.31	4,461.25	-2,424.06	977.36	2,522.82	0.00	0.00	0.00	
6,900.00	90.33	134.31	4,460.68	-2,493.92	1,048.91	2,621.70	0.00	0.00	0.00	
7,000.00	90.33	134.31	4,460.11	-2,563.78	1,120.46	2,720.58	0.00	0.00	0.00	
7,100.00	90.33	134.31	4,459.53	-2,633.64	1,192.01	2,819.46	0.00	0.00	0.00	
7,200.00	90.33	134.31	4,458.96	-2,703.50	1,263.56	2,918.34	0.00	0.00	0.00	
7,300.00	90.33	134.31	4,458.39	-2,773.36	1,335.11	3,017.22	0.00	0.00	0.00	
7,400.00	90.33	134.31	4,457.82	-2,843.21	1,406.66	3,116.10	0.00	0.00	0.00	
7,500.00	90.33	134.31	4,457.24	-2,913.07	1,478.21	3,214.98	0.00	0.00	0.00	
7,600.00	90.33	134.31	4,456.67	-2,982.93	1,549.76	3,313.86	0.00	0.00	0.00	
7,700.00	90.33	134.31	4,456.10	-3,052.79	1,621.31	3,412.74	0.00	0.00	0.00	
7,800.00	90.33	134.31	4,455.52	-3,122.65	1,692.86	3,511.62	0.00	0.00	0.00	
7,900.00	90.33	134.31	4,454.95	-3,192.51	1,764.41	3,610.50	0.00	0.00	0.00	
8,000.00	90.33	134.31	4,454.38	-3,262.37	1,835.96	3,709.38	0.00	0.00	0.00	
8,100.00	90.33	134.31	4,453.80	-3,332.23	1,907.51	3,808.26	0.00	0.00	0.00	
8,200.00	90.33	134.31	4,453.23	-3,402.08	1,979.06	3,907.14	0.00	0.00	0.00	
8,300.00	90.33	134.31	4,452.66	-3,471.94	2,050.61	4,006.03	0.00	0.00	0.00	
8,400.00	90.33	134.31	4,452.08	-3,541.80	2,122.16	4,104.91	0.00	0.00	0.00	
8,500.00	90.33	134.31	4,451.51	-3,611.66	2,193.71	4,203.79	0.00	0.00	0.00	
8,600.00	90.33	134.31	4,450.94	-3,681.52	2,265.26	4,302.67	0.00	0.00	0.00	
8,700.00	90.33	134.31	4,450.36	-3,751.38	2,336.81	4,401.55	0.00	0.00	0.00	
8,800.00	90.33	134.31	4,449.79	-3,821.24	2,408.36	4,500.43	0.00	0.00	0.00	
8,900.00	90.33	134.31	4,449.22	-3,891.09	2,479.91	4,599.31	0.00	0.00	0.00	
9,000.00	90.33	134.31	4,448.64	-3,960.95	2,551.46	4,698.19	0.00	0.00	0.00	
9,100.00	90.33	134.31	4,448.07	-4,030.81	2,623.01	4,797.07	0.00	0.00	0.00	
9,200.00	90.33	134.31	4,447.50	-4,100.67	2,694.56	4,895.95	0.00	0.00	0.00	
9,300.00	90.33	134.31	4,446.93	-4,170.53	2,766.11	4,994.83	0.00	0.00	0.00	
9,400.00	90.33	134.31	4,446.35	-4,240.39	2,837.66	5,093.71	0.00	0.00	0.00	
9,500.00	90.33	134.31	4,445.78	-4,310.25	2,909.21	5,192.59	0.00	0.00	0.00	
9,600.00	90.33	134.31	4,445.21	-4,380.11	2,980.76	5,291.47	0.00	0.00	0.00	
9,700.00	90.33	134.31	4,444.63	-4,449.96	3,052.31	5,390.35	0.00	0.00	0.00	
9,800.00	90.33	134.31	4,444.06	-4,519.82	3,123.86	5,489.23	0.00	0.00	0.00	
9,900.00	90.33	134.31	4,443.49	-4,589.68	3,195.41	5,588.11	0.00	0.00	0.00	
10,000.00	90.33	134.31	4,442.91	-4,659.54	3,266.97	5,687.00	0.00	0.00	0.00	
10,100.00	90.33	134.31	4,442.34	-4,729.40	3,338.52	5,785.88	0.00	0.00	0.00	
10,200.00	90.33	134.31	4,441.77	-4,799.26	3,410.07	5,884.76	0.00	0.00	0.00	



Lonestar Consulting, LLC
Planning Report



Database:	Grand Junction	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Company:	DJR Operating	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Project:	Ponderosa Unit	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site:	P01 2310 Pad	North Reference:	True
Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
10,300.00	90.33	134.31	4,441.19	-4,869.12	3,481.62	5,983.64	0.00	0.00	0.00	
10,400.00	90.33	134.31	4,440.62	-4,938.97	3,553.17	6,082.52	0.00	0.00	0.00	
10,500.00	90.33	134.31	4,440.05	-5,008.83	3,624.72	6,181.40	0.00	0.00	0.00	
10,600.00	90.33	134.31	4,439.47	-5,078.69	3,696.27	6,280.28	0.00	0.00	0.00	
10,700.00	90.33	134.31	4,438.90	-5,148.55	3,767.82	6,379.16	0.00	0.00	0.00	
10,800.00	90.33	134.31	4,438.33	-5,218.41	3,839.37	6,478.04	0.00	0.00	0.00	
10,900.00	90.33	134.31	4,437.76	-5,288.27	3,910.92	6,576.92	0.00	0.00	0.00	
11,000.00	90.33	134.31	4,437.18	-5,358.13	3,982.47	6,675.80	0.00	0.00	0.00	
11,100.00	90.33	134.31	4,436.61	-5,427.99	4,054.02	6,774.68	0.00	0.00	0.00	
11,200.00	90.33	134.31	4,436.04	-5,497.84	4,125.57	6,873.56	0.00	0.00	0.00	
11,300.00	90.33	134.31	4,435.46	-5,567.70	4,197.12	6,972.44	0.00	0.00	0.00	
11,382.00	90.33	134.31	4,434.99	-5,624.99	4,255.79	7,053.53	0.00	0.00	0.00	

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- hit/miss target									
- Shape									
Escrito 134H Toe rev 1	0.00	0.00	4,434.99	-5,624.99	4,255.79	1,904,872.0093	2,724,524.6993	36.2350928	-107.8284741
- plan hits target center									
- Circle (radius 100.00)									
Escrito 134H Heel rev 1	0.00	0.00	4,471.99	-1,115.20	-363.20	1,909,382.2487	2,719,906.1621	36.2474824	-107.8441368
- plan hits target center									
- Circle (radius 50.00)									

Casing Points					
Measured Depth (ft)	Vertical Depth (ft)	Name	Casing Diameter (in)	Hole Diameter (in)	
350.00	350.00	Surface	9.620	12.250	
4,871.99	4,469.69	Intermediate	7.000	8.750	

Formations						
Measured Depth (ft)	Vertical Depth (ft)	Name	Lithology	Dip (°)	Dip Direction (°)	
458.01	458.00	Ojo Alamo		0.00	0.00	
584.24	584.00	Kirtland		0.00	0.00	
998.11	990.00	Fruitland		0.00	0.00	
1,256.52	1,239.00	Pictured Cliffs		0.00	0.00	
1,409.07	1,386.00	Lewis		0.00	0.00	
2,067.04	2,020.00	Chacra		0.00	0.00	
2,707.36	2,637.00	Menefee		0.00	0.00	
3,730.62	3,623.00	Point Lookout		0.00	0.00	
3,882.14	3,769.00	Mancos		0.00	0.00	
4,212.89	4,086.00	Mancos Silt		0.00	0.00	



Database:	Grand Junction	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Company:	DJR Operating	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Project:	Ponderosa Unit	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site:	P01 2310 Pad	North Reference:	True
Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Original Drilling		
Design:	APD		



DJR Operating

Ponderosa Unit

P01 2310 Pad

Escrito P01 2310 Federal COM 134H

Original Drilling

APD

Anticollision Report

11 September, 2023





Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Reference	APD
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria
Interpolation Method:	Stations
Depth Range:	Unlimited
Results Limited by:	Maximum centre distance of 15,000.00ft
Warning Levels Evaluated at:	2.00 Sigma
Error Model:	ISCWSA
Scan Method:	Closest Approach 3D
Error Surface:	Pedal Curve
Casing Method:	Not applied

Survey Tool Program		Date	3/7/2023		
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description	
0.00	11,382.00	APD (Original Drilling)	MWD+HDGM	OWSG MWD + HDGM	

Summary						
Site Name	Reference Measured Depth (ft)	Offset Measured Depth (ft)	Distance Between Centres (ft)	Between Ellipses (ft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
P01 2310 Pad						
December Dream 002 - OH - OH	7,834.12	4,265.40	331.46	113.50	1.521 CC, ES, SF	
December Dream 003 - OH - OH	9,286.18	4,311.99	737.96	481.26	2.875 CC	
December Dream 003 - OH - OH	9,300.00	4,312.00	738.09	481.15	2.873 ES, SF	
Escrito P01 2310 137H - Original Drilling - APD	653.08	652.47	9.70	5.15	2.134 CC, ES, SF	
Escrito P01 2310 Federal COM 106H - Original Drilling -	914.92	902.60	65.45	59.08	10.273 CC, ES	
Escrito P01 2310 Federal COM 106H - Original Drilling -	1,100.00	1,082.75	73.43	65.49	9.253 SF	
Escrito P01 2310 Federal COM 108H - Original Drilling -	1,036.76	1,031.02	19.74	12.23	2.629 CC	
Escrito P01 2310 Federal COM 108H - Original Drilling -	1,100.00	1,094.14	20.23	12.17	2.511 ES	
Escrito P01 2310 Federal COM 108H - Original Drilling -	2,900.00	2,894.07	44.40	21.28	1.920 SF	
Escrito P01 2310 Federal COM 113H - Original Drilling -	400.00	400.00	19.83	17.22	7.589 CC, ES	
Escrito P01 2310 Federal COM 113H - Original Drilling -	11,382.00	10,689.73	963.51	623.92	2.837 SF	
Escrito P01 2310 Federal COM 133H - Original Drilling -	1,231.67	1,219.36	53.78	44.60	5.857 CC	
Escrito P01 2310 Federal COM 133H - Original Drilling -	1,300.00	1,287.48	54.04	44.18	5.480 ES	
Escrito P01 2310 Federal COM 133H - Original Drilling -	1,700.00	1,686.29	64.76	50.95	4.688 SF	
Witty 5 - OH - OH	5,465.28	4,440.86	335.87	170.57	2.032 CC, ES, SF	

Offset Design: P01 2310 Pad - December Dream 002 - OH - OH												Offset Site Error:	0.00 ft
Survey Program: 122-INCLINOMETER				Rule Assigned:				Offset Well Error:				0.00 ft	
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		Minimum Separation (ft)	Separation Factor	Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)		+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)			
0.00	0.00	0.00	0.00	0.00	0.00	146.18	-2,909.32	1,948.83	3,506.93				
100.00	100.00	0.00	0.00	0.31	0.00	146.18	-2,909.32	1,948.83	3,502.91	3,502.59	0.31	N/A	
200.00	200.00	9.00	9.00	0.67	0.27	146.18	-2,909.32	1,948.83	3,501.72	3,500.78	0.94	3,724.203	
300.00	300.00	109.00	109.00	1.03	3.31	146.18	-2,909.32	1,948.83	3,501.72	3,497.39	4.34	807.697	
361.20	361.20	169.09	169.08	1.24	5.14	146.18	-2,909.07	1,948.83	3,501.52	3,495.14	6.38	548.844	
400.00	400.00	191.95	191.94	1.38	5.83	146.18	-2,909.14	1,948.83	3,501.62	3,494.41	7.21	485.457	
500.00	499.96	308.99	308.96	1.73	9.38	-80.05	-2,909.32	1,948.83	3,501.31	3,490.20	11.11	315.092	
600.00	599.69	393.54	393.49	2.07	11.95	-80.18	-2,908.81	1,948.83	3,499.68	3,485.66	14.02	249.610	
700.00	698.96	508.08	507.96	2.43	15.43	-80.44	-2,909.32	1,948.83	3,498.04	3,480.19	17.86	195.892	
800.00	797.55	603.05	602.92	2.81	18.31	-80.78	-2,908.29	1,948.83	3,494.44	3,473.32	21.12	165.449	
900.00	895.21	676.85	676.71	3.22	20.55	-81.12	-2,908.69	1,948.83	3,491.45	3,467.67	23.77	146.880	
964.03	957.17	766.36	766.17	3.50	23.27	-81.54	-2,909.32	1,948.83	3,489.35	3,462.57	26.77	130.339	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - December Dream 002 - OH - OH												Offset Site Error:	0.00 ft
Survey Program: 122-INCLINOMETER												Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
1,000.00	991.83	801.02	800.83	3.67	24.33	-81.69	-2,909.32	1,948.83	3,487.89	3,459.90	27.99	124.621	
1,100.00	1,088.18	897.38	897.18	4.14	27.25	-82.11	-2,909.32	1,948.83	3,483.98	3,452.60	31.38	111.013	
1,200.00	1,184.54	992.24	992.03	4.62	30.13	-82.53	-2,908.23	1,948.83	3,479.40	3,444.65	34.75	100.133	
1,300.00	1,280.90	1,080.05	1,079.84	5.12	32.80	-82.92	-2,908.41	1,948.83	3,476.06	3,438.15	37.91	91.695	
1,400.00	1,377.26	1,167.98	1,167.77	5.62	35.47	-83.30	-2,908.86	1,948.83	3,473.16	3,432.08	41.08	84.543	
1,500.00	1,473.62	1,282.96	1,282.62	6.13	38.96	-83.80	-2,909.32	1,948.83	3,470.37	3,425.29	45.08	76.979	
1,600.00	1,569.97	1,379.32	1,378.97	6.64	41.89	-84.22	-2,909.32	1,948.83	3,467.48	3,418.96	48.52	71.463	
1,700.00	1,666.33	1,475.67	1,475.33	7.16	44.81	-84.65	-2,909.32	1,948.83	3,464.79	3,412.82	51.96	66.676	
1,800.00	1,762.69	1,558.50	1,558.12	7.68	47.33	-85.03	-2,907.62	1,948.83	3,461.00	3,406.00	55.00	62.928	
1,900.00	1,859.05	1,641.40	1,641.00	8.20	49.85	-85.39	-2,908.25	1,948.83	3,459.29	3,401.25	58.04	59.603	
2,000.00	1,955.41	1,764.95	1,764.41	8.73	53.60	-85.92	-2,909.32	1,948.83	3,457.94	3,395.62	62.32	55.490	
2,100.00	2,051.76	1,861.31	1,860.76	9.25	56.52	-86.35	-2,909.32	1,948.83	3,456.07	3,390.30	65.77	52.549	
2,200.00	2,148.12	1,957.67	1,957.12	9.78	59.45	-86.77	-2,909.32	1,948.83	3,454.41	3,385.18	69.22	49.903	
2,300.00	2,244.48	2,047.45	2,046.88	10.31	62.18	-87.19	-2,907.62	1,948.83	3,451.67	3,379.19	72.48	47.623	
2,400.00	2,340.84	2,133.12	2,132.54	10.84	64.78	-87.56	-2,908.01	1,948.83	3,450.76	3,375.15	75.61	45.639	
2,500.00	2,437.20	2,218.93	2,218.34	11.37	67.39	-87.94	-2,908.77	1,948.83	3,450.35	3,371.61	78.74	43.817	
2,600.00	2,533.55	2,343.25	2,342.55	11.90	71.16	-88.48	-2,909.32	1,948.83	3,449.81	3,366.76	83.05	41.537	
2,700.00	2,629.91	2,439.61	2,438.91	12.43	74.09	-88.91	-2,909.32	1,948.83	3,449.18	3,362.67	86.51	39.870	
2,800.00	2,726.27	2,533.95	2,533.23	12.96	76.95	-89.34	-2,907.96	1,948.83	3,447.77	3,357.86	89.91	38.347	
2,854.41	2,778.70	2,581.23	2,580.51	13.25	78.39	-89.55	-2,908.05	1,948.83	3,447.70	3,356.06	91.63	37.625	
2,900.00	2,822.63	2,620.89	2,620.17	13.49	79.59	-89.73	-2,908.19	1,948.83	3,447.74	3,354.66	93.08	37.040	
3,000.00	2,918.99	2,707.96	2,707.23	14.02	82.24	-90.11	-2,908.76	1,948.83	3,448.19	3,351.93	96.26	35.823	
3,100.00	3,015.34	2,825.16	2,824.34	14.55	85.80	-90.62	-2,909.32	1,948.83	3,448.73	3,348.38	100.35	34.367	
3,179.72	3,092.16	2,901.98	2,901.15	14.98	88.13	-90.97	-2,908.58	1,948.83	3,448.51	3,345.40	103.11	33.446	
3,200.00	3,111.70	2,918.32	2,917.49	15.09	88.62	-91.05	-2,908.59	1,948.83	3,448.62	3,344.91	103.71	33.252	
3,300.00	3,208.06	2,999.04	2,998.20	15.62	91.08	-91.40	-2,908.95	1,948.83	3,449.54	3,342.85	106.69	32.331	
3,400.00	3,304.42	3,114.29	3,113.42	16.15	94.58	-91.91	-2,909.32	1,948.83	3,450.57	3,339.84	110.73	31.162	
3,500.00	3,400.77	3,210.65	3,209.77	16.69	97.50	-92.33	-2,909.32	1,948.83	3,451.59	3,337.41	114.19	30.227	
3,600.00	3,497.13	3,305.47	3,304.59	17.22	100.38	-92.77	-2,908.24	1,948.83	3,452.09	3,334.49	117.60	29.355	
3,700.00	3,593.49	3,394.52	3,393.64	17.76	103.09	-93.16	-2,908.43	1,948.83	3,453.68	3,332.84	120.83	28.582	
3,800.00	3,689.85	3,483.69	3,482.80	18.29	105.79	-93.55	-2,908.91	1,948.83	3,455.68	3,331.60	124.07	27.852	
3,900.00	3,786.21	3,596.17	3,595.21	18.82	109.21	-94.04	-2,909.32	1,948.83	3,457.77	3,329.74	128.02	27.009	
4,000.00	3,882.56	3,692.53	3,691.56	19.36	112.14	-94.47	-2,909.32	1,948.83	3,459.83	3,328.35	131.48	26.315	
4,061.50	3,941.82	3,751.79	3,750.82	19.69	113.94	-94.73	-2,909.32	1,948.83	3,461.19	3,327.59	133.60	25.906	
4,100.00	3,978.90	3,788.87	3,787.90	19.89	115.06	-80.54	-2,909.32	1,948.83	3,460.73	3,325.80	134.93	25.648	
4,150.00	4,026.79	3,835.07	3,834.09	20.15	116.47	-64.52	-2,907.80	1,948.83	3,455.15	3,318.56	136.59	25.296	
4,200.00	4,073.99	3,878.50	3,877.52	20.39	117.78	-52.48	-2,907.87	1,948.83	3,446.14	3,307.98	138.15	24.944	
4,250.00	4,120.13	3,921.01	3,920.02	20.61	119.07	-43.99	-2,908.01	1,948.83	3,432.78	3,293.11	139.67	24.577	
4,300.00	4,164.80	3,962.25	3,961.26	20.83	120.33	-38.08	-2,908.21	1,948.83	3,415.18	3,274.04	141.14	24.197	
4,350.00	4,207.64	4,001.88	4,000.88	21.02	121.53	-33.95	-2,908.46	1,948.83	3,393.48	3,250.94	142.54	23.806	
4,400.00	4,248.29	4,039.58	4,038.57	21.21	122.68	-31.07	-2,908.77	1,948.83	3,367.86	3,223.98	143.88	23.408	
4,450.00	4,286.40	4,096.48	4,095.40	21.38	124.40	-29.26	-2,909.32	1,948.83	3,338.59	3,192.81	145.78	22.902	
4,500.00	4,321.66	4,131.73	4,130.66	21.54	125.47	-28.08	-2,909.32	1,948.83	3,305.52	3,158.51	147.01	22.485	
4,550.00	4,353.77	4,163.84	4,162.77	21.69	126.45	-27.54	-2,909.32	1,948.83	3,269.22	3,121.09	148.13	22.070	
4,600.00	4,382.45	4,192.53	4,191.45	21.83	127.32	-27.63	-2,909.32	1,948.83	3,230.01	3,080.87	149.14	21.658	
4,650.00	4,407.48	4,217.56	4,216.48	21.96	128.08	-28.41	-2,909.32	1,948.83	3,188.19	3,038.17	150.02	21.252	
4,700.00	4,428.64	4,238.71	4,237.64	22.10	128.72	-30.10	-2,909.32	1,948.83	3,144.11	2,993.35	150.77	20.854	
4,750.00	4,445.75	4,255.82	4,254.75	22.24	129.24	-33.15	-2,909.32	1,948.83	3,098.14	2,946.76	151.38	20.465	
4,800.00	4,458.66	4,268.74	4,267.66	22.40	129.63	-38.60	-2,909.32	1,948.83	3,050.66	2,898.80	151.86	20.088	
4,850.00	4,467.28	4,277.36	4,276.28	22.59	129.90	-49.13	-2,909.32	1,948.83	3,002.05	2,849.85	152.20	19.725	
4,900.00	4,471.53	4,281.60	4,280.53	22.83	130.03	-72.02	-2,909.32	1,948.83	2,952.71	2,800.32	152.39	19.376	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - December Dream 002 - OH - OH													Offset Site Error:	0.00 ft
Survey Program: 122-INCLINOMETER													Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		Minimum Separation		Separation Factor		Warning		
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
4,926.41	4,471.99	4,282.07	4,280.99	22.98	130.04	-92.88	-2,909.32	1,948.83	2,926.49	2,774.06	152.43	19.199		
5,000.00	4,471.57	4,281.65	4,280.57	23.54	130.03	-92.81	-2,909.32	1,948.83	2,853.39	2,700.90	152.49	18.712		
5,100.00	4,471.00	4,281.07	4,280.00	24.65	130.01	-92.71	-2,909.32	1,948.83	2,754.09	2,601.50	152.59	18.049		
5,200.00	4,470.42	4,280.50	4,279.42	26.13	129.99	-92.61	-2,909.32	1,948.83	2,654.85	2,502.15	152.70	17.386		
5,300.00	4,469.85	4,279.93	4,278.85	27.86	129.97	-92.51	-2,909.32	1,948.83	2,555.66	2,402.84	152.82	16.723		
5,400.00	4,469.28	4,279.35	4,278.28	29.77	129.96	-92.41	-2,909.32	1,948.83	2,456.54	2,303.57	152.97	16.059		
5,500.00	4,468.70	4,278.78	4,277.70	31.80	129.94	-92.31	-2,909.32	1,948.83	2,357.50	2,204.36	153.14	15.395		
5,600.00	4,468.13	4,278.21	4,277.13	33.92	129.92	-92.21	-2,909.32	1,948.83	2,258.54	2,105.20	153.33	14.730		
5,700.00	4,467.56	4,277.63	4,276.56	36.12	129.91	-92.11	-2,909.32	1,948.83	2,159.67	2,006.11	153.56	14.064		
5,800.00	4,466.99	4,277.06	4,275.99	38.37	129.89	-92.01	-2,909.32	1,948.83	2,060.91	1,907.10	153.82	13.398		
5,900.00	4,466.41	4,276.49	4,275.41	40.67	129.87	-91.92	-2,909.32	1,948.83	1,962.28	1,808.16	154.12	12.732		
6,000.00	4,465.84	4,275.92	4,274.84	43.00	129.85	-91.82	-2,909.32	1,948.83	1,863.80	1,709.32	154.48	12.065		
6,100.00	4,465.27	4,275.34	4,274.27	45.36	129.84	-91.72	-2,909.32	1,948.83	1,765.48	1,610.59	154.89	11.398		
6,200.00	4,464.69	4,274.77	4,273.69	47.76	129.82	-91.62	-2,909.32	1,948.83	1,667.37	1,511.98	155.39	10.730		
6,300.00	4,464.12	4,274.20	4,273.12	50.17	129.80	-91.52	-2,909.32	1,948.83	1,569.49	1,413.52	155.97	10.063		
6,400.00	4,463.55	4,273.62	4,272.55	52.60	129.78	-91.42	-2,909.32	1,948.83	1,471.90	1,315.23	156.67	9.395		
6,500.00	4,462.97	4,273.05	4,271.97	55.05	129.77	-91.32	-2,909.32	1,948.83	1,374.66	1,217.15	157.50	8.728		
6,600.00	4,462.40	4,272.48	4,271.40	57.51	129.75	-91.22	-2,909.32	1,948.83	1,277.84	1,119.32	158.51	8.061		
6,700.00	4,461.83	4,271.90	4,270.83	59.99	129.73	-91.12	-2,909.32	1,948.83	1,181.54	1,021.80	159.74	7.397		
6,800.00	4,461.25	4,271.33	4,270.25	62.47	129.71	-91.02	-2,909.32	1,948.83	1,085.92	924.67	161.26	6.734		
6,900.00	4,460.68	4,270.76	4,269.68	64.97	129.70	-90.93	-2,909.32	1,948.83	991.17	828.03	163.14	6.076		
7,000.00	4,460.11	4,270.18	4,269.11	67.47	129.68	-90.83	-2,909.32	1,948.83	897.55	732.06	165.49	5.424		
7,100.00	4,459.53	4,269.61	4,268.53	69.98	129.66	-90.73	-2,909.32	1,948.83	805.47	636.99	168.47	4.781		
7,200.00	4,458.96	4,269.04	4,267.96	72.50	129.64	-90.63	-2,909.32	1,948.83	715.51	543.23	172.28	4.153		
7,300.00	4,458.39	4,268.46	4,267.39	75.03	129.63	-90.53	-2,909.32	1,948.83	628.60	451.41	177.19	3.548		
7,400.00	4,457.82	4,267.89	4,266.82	77.55	129.61	-90.43	-2,909.32	1,948.83	546.19	362.69	183.50	2.977		
7,500.00	4,457.24	4,267.32	4,266.24	80.09	129.59	-90.33	-2,909.32	1,948.83	470.64	279.15	191.48	2.458		
7,600.00	4,456.67	4,266.75	4,265.67	82.63	129.57	-90.23	-2,909.32	1,948.83	405.80	204.80	201.01	2.019		
7,700.00	4,456.10	4,266.17	4,265.10	85.17	129.56	-90.13	-2,909.32	1,948.83	357.57	146.87	210.70	1.697		
7,800.00	4,455.52	4,265.60	4,264.52	87.72	129.54	-90.03	-2,909.32	1,948.83	333.21	116.02	217.19	1.534		
7,834.12	4,455.33	4,265.40	4,264.33	88.59	129.53	-90.00	-2,909.32	1,948.83	331.46	113.50	217.96	1.521 CC, ES, SF		
7,900.00	4,454.95	4,265.03	4,263.95	90.27	129.52	-89.93	-2,909.32	1,948.83	337.95	120.94	217.01	1.557		
8,000.00	4,454.38	4,264.45	4,263.38	92.82	129.50	-89.84	-2,909.32	1,948.83	370.65	159.98	210.68	1.759		
8,100.00	4,453.80	4,263.88	4,262.80	95.38	129.49	-89.74	-2,909.32	1,948.83	424.92	223.04	201.88	2.105		
8,200.00	4,453.23	4,263.31	4,262.23	97.94	129.47	-89.64	-2,909.32	1,948.83	493.69	300.26	193.44	2.552		
8,300.00	4,452.66	4,262.73	4,261.66	100.50	129.45	-89.54	-2,909.32	1,948.83	571.76	385.40	186.36	3.068		
8,400.00	4,452.08	4,262.16	4,261.08	103.06	129.44	-89.44	-2,909.32	1,948.83	655.80	475.11	180.69	3.629		
8,500.00	4,451.51	4,261.59	4,260.51	105.63	129.42	-89.34	-2,909.32	1,948.83	743.81	567.59	176.22	4.221		
8,600.00	4,450.94	4,261.01	4,259.94	108.19	129.40	-89.24	-2,909.32	1,948.83	834.52	661.85	172.67	4.833		
8,700.00	4,450.36	4,260.44	4,259.36	110.76	129.38	-89.14	-2,909.32	1,948.83	927.14	757.31	169.84	5.459		
8,800.00	4,449.79	4,259.87	4,258.79	113.33	129.37	-89.04	-2,909.32	1,948.83	1,021.16	853.61	167.55	6.095		
8,900.00	4,449.22	4,259.29	4,258.22	115.90	129.35	-88.94	-2,909.32	1,948.83	1,116.21	950.54	165.68	6.737		
9,000.00	4,448.64	4,258.72	4,257.64	118.48	129.33	-88.85	-2,909.32	1,948.83	1,212.07	1,047.93	164.13	7.385		
9,100.00	4,448.07	4,258.15	4,257.07	121.05	129.31	-88.75	-2,909.32	1,948.83	1,308.54	1,145.69	162.84	8.035		
9,200.00	4,447.50	4,257.57	4,256.50	123.63	129.30	-88.65	-2,909.32	1,948.83	1,405.50	1,243.74	161.76	8.689		
9,300.00	4,446.93	4,257.00	4,255.93	126.21	129.28	-88.55	-2,909.32	1,948.83	1,502.87	1,342.02	160.84	9.344		
9,400.00	4,446.35	4,256.43	4,255.35	128.79	129.26	-88.45	-2,909.32	1,948.83	1,600.55	1,440.49	160.06	10.000		
9,500.00	4,445.78	4,255.86	4,254.78	131.37	129.24	-88.35	-2,909.32	1,948.83	1,698.51	1,539.13	159.39	10.657		
9,600.00	4,445.21	4,255.28	4,254.21	133.95	129.23	-88.25	-2,909.32	1,948.83	1,796.69	1,637.89	158.80	11.314		
9,700.00	4,444.63	4,254.71	4,253.63	136.53	129.21	-88.15	-2,909.32	1,948.83	1,895.06	1,736.77	158.29	11.972		
9,800.00	4,444.06	4,254.14	4,253.06	139.11	129.19	-88.05	-2,909.32	1,948.83	1,993.60	1,835.75	157.85	12.630		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC
Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - December Dream 002 - OH - OH													Offset Site Error:	0.00 ft
Survey Program: 122-INCLINOMETER													Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Minimum	Separation	Warning		
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Separation (ft)			
9,900.00	4,443.49	4,253.56	4,252.49	141.69	129.17	-87.95	-2,909.32	1,948.83	2,092.27	1,934.81	157.46	13.288		
10,000.00	4,442.91	4,252.99	4,251.91	144.28	129.16	-87.86	-2,909.32	1,948.83	2,191.06	2,033.95	157.12	13.945		
10,100.00	4,442.34	4,252.42	4,251.34	146.86	129.14	-87.76	-2,909.32	1,948.83	2,289.96	2,133.15	156.81	14.603		
10,200.00	4,441.77	4,251.84	4,250.77	149.45	129.12	-87.66	-2,909.32	1,948.83	2,388.95	2,232.41	156.54	15.261		
10,300.00	4,441.19	4,251.27	4,250.19	152.04	129.10	-87.56	-2,909.32	1,948.83	2,488.02	2,331.72	156.30	15.918		
10,400.00	4,440.62	4,250.70	4,249.62	154.62	129.09	-87.46	-2,909.32	1,948.83	2,587.16	2,431.07	156.09	16.575		
10,500.00	4,440.05	4,250.12	4,249.05	157.21	129.07	-87.36	-2,909.32	1,948.83	2,686.37	2,530.47	155.90	17.231		
10,600.00	4,439.47	4,249.55	4,248.47	159.80	129.05	-87.26	-2,909.32	1,948.83	2,785.63	2,629.90	155.73	17.888		
10,700.00	4,438.90	4,248.98	4,247.90	162.39	129.03	-87.16	-2,909.32	1,948.83	2,884.94	2,729.37	155.57	18.544		
10,800.00	4,438.33	4,248.40	4,247.33	164.98	129.02	-87.06	-2,909.32	1,948.83	2,984.30	2,828.86	155.44	19.199		
10,900.00	4,437.76	4,247.83	4,246.75	167.57	129.00	-86.97	-2,909.32	1,948.83	3,083.70	2,928.38	155.31	19.855		
11,000.00	4,437.18	4,247.26	4,246.18	170.16	128.98	-86.87	-2,909.32	1,948.83	3,183.14	3,027.93	155.20	20.509		
11,100.00	4,436.61	4,246.68	4,245.61	172.75	128.97	-86.77	-2,909.32	1,948.83	3,282.61	3,127.50	155.10	21.164		
11,200.00	4,436.04	4,246.11	4,245.04	175.34	128.95	-86.67	-2,909.32	1,948.83	3,382.11	3,227.09	155.01	21.818		
11,300.00	4,435.46	4,245.54	4,244.46	177.93	128.93	-86.57	-2,909.32	1,948.83	3,481.64	3,326.70	154.94	22.472		
11,382.00	4,434.99	4,245.07	4,243.99	180.05	128.92	-86.49	-2,909.32	1,948.83	3,563.28	3,408.40	154.88	23.007		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - December Dream 003 - OH - OH													Offset Site Error:	0.00 ft
Survey Program: 92-INCLINOMETER													Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Distance Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
0.00	0.00	0.00	0.00	0.00	0.00	138.00	-3,634.08	3,271.77	4,891.92					
100.00	100.00	0.00	0.00	0.31	0.00	138.00	-3,634.08	3,271.77	4,890.06	4,889.75	0.31	N/A		
156.50	156.50	15.50	15.50	0.51	0.47	138.00	-3,634.08	3,271.77	4,889.89	4,888.91	0.98	4,981.468		
200.00	200.00	59.00	59.00	0.67	1.79	138.00	-3,634.08	3,271.77	4,889.89	4,887.43	2.46	1,988.904		
293.01	293.01	152.01	152.01	1.00	4.62	138.00	-3,634.01	3,271.77	4,889.84	4,884.22	5.62	870.622		
300.00	300.00	158.18	158.18	1.03	4.80	138.00	-3,634.01	3,271.77	4,889.84	4,884.01	5.83	838.879		
400.00	400.00	259.00	259.00	1.38	7.87	138.00	-3,634.08	3,271.77	4,889.89	4,880.64	9.25	528.678		
500.00	499.96	358.97	358.96	1.73	10.90	-88.21	-3,634.08	3,271.77	4,889.81	4,877.18	12.63	387.175		
600.00	599.69	458.46	458.45	2.07	13.92	-88.31	-3,633.28	3,271.77	4,889.00	4,873.01	15.99	305.717		
700.00	698.96	548.95	548.94	2.43	16.67	-88.44	-3,633.39	3,271.77	4,888.75	4,869.66	19.10	255.985		
800.00	797.55	638.88	638.86	2.81	19.40	-88.62	-3,633.73	3,271.77	4,888.59	4,866.39	22.21	220.120		
900.00	895.21	754.26	754.21	3.22	22.91	-88.91	-3,634.08	3,271.77	4,888.35	4,862.23	26.12	187.125		
964.03	957.17	816.22	816.17	3.50	24.79	-89.10	-3,634.08	3,271.77	4,888.06	4,859.78	28.29	172.800		
1,000.00	991.83	850.87	850.83	3.67	25.84	-89.21	-3,634.08	3,271.77	4,887.92	4,858.41	29.50	165.665		
1,100.00	1,088.18	947.23	947.18	4.14	28.77	-89.51	-3,634.08	3,271.77	4,887.61	4,854.71	32.90	148.549		
1,179.04	1,164.34	1,017.43	1,017.38	4.52	30.90	-89.74	-3,633.30	3,271.77	4,886.91	4,851.49	35.42	137.979		
1,200.00	1,184.54	1,035.94	1,035.89	4.62	31.46	-89.80	-3,633.34	3,271.77	4,886.92	4,850.84	36.08	135.439		
1,300.00	1,280.90	1,124.29	1,124.24	5.12	34.14	-90.07	-3,633.63	3,271.77	4,887.13	4,847.87	39.26	124.478		
1,400.00	1,377.26	1,236.35	1,236.26	5.62	37.55	-90.42	-3,634.08	3,271.77	4,887.56	4,844.39	43.17	113.222		
1,500.00	1,473.62	1,332.71	1,332.62	6.13	40.47	-90.72	-3,634.08	3,271.77	4,887.83	4,841.23	46.60	104.881		
1,600.00	1,569.97	1,429.06	1,428.97	6.64	43.40	-91.02	-3,634.08	3,271.77	4,888.26	4,838.21	50.04	97.680		
1,643.24	1,611.63	1,470.71	1,470.61	6.87	44.66	-91.16	-3,633.21	3,271.77	4,887.87	4,836.34	51.53	94.852		
1,700.00	1,666.33	1,521.12	1,521.03	7.16	46.19	-91.32	-3,633.24	3,271.77	4,888.24	4,834.88	53.36	91.615		
1,800.00	1,762.69	1,610.01	1,609.91	7.68	48.89	-91.59	-3,633.45	3,271.77	4,889.11	4,832.54	56.57	86.419		
1,900.00	1,859.05	1,698.97	1,698.87	8.20	51.60	-91.87	-3,633.85	3,271.77	4,890.28	4,830.48	59.80	81.780		
2,000.00	1,955.41	1,814.54	1,814.41	8.73	55.10	-92.23	-3,634.08	3,271.77	4,891.41	4,827.58	63.83	76.630		
2,100.00	2,051.76	1,910.90	1,910.76	9.25	58.03	-92.53	-3,634.08	3,271.77	4,892.56	4,825.28	67.28	72.717		
2,200.00	2,148.12	2,006.97	2,006.83	9.78	60.95	-92.84	-3,633.20	3,271.77	4,893.26	4,822.53	70.73	69.186		
2,300.00	2,244.48	2,096.07	2,095.92	10.31	63.65	-93.12	-3,633.31	3,271.77	4,894.78	4,820.83	73.96	66.183		
2,400.00	2,340.84	2,185.24	2,185.10	10.84	66.36	-93.39	-3,633.61	3,271.77	4,896.60	4,819.40	77.19	63.433		
2,500.00	2,437.20	2,296.47	2,296.20	11.37	69.74	-93.74	-3,634.08	3,271.77	4,898.63	4,817.53	81.10	60.403		
2,600.00	2,533.55	2,372.67	2,372.39	11.90	72.05	-93.98	-3,633.61	3,271.77	4,900.24	4,816.30	83.94	58.377		
2,700.00	2,629.91	2,489.23	2,488.91	12.43	75.59	-94.34	-3,634.08	3,271.77	4,902.54	4,814.53	88.01	55.704		
2,800.00	2,726.27	2,585.59	2,585.27	12.96	78.52	-94.64	-3,634.08	3,271.77	4,904.71	4,813.24	91.47	53.623		
2,900.00	2,822.63	2,679.84	2,679.51	13.49	81.38	-94.94	-3,632.72	3,271.77	4,906.13	4,811.28	94.86	51.721		
3,000.00	2,918.99	2,764.37	2,764.03	14.02	83.95	-95.20	-3,632.94	3,271.77	4,908.76	4,810.81	97.95	50.114		
3,100.00	3,015.34	2,849.03	2,848.68	14.55	86.52	-95.46	-3,633.46	3,271.77	4,911.76	4,810.71	101.05	48.607		
3,200.00	3,111.70	2,971.19	2,970.70	15.09	90.23	-95.84	-3,634.08	3,271.77	4,914.84	4,809.54	105.29	46.678		
3,300.00	3,208.06	3,067.55	3,067.06	15.62	93.15	-96.13	-3,634.08	3,271.77	4,917.73	4,808.98	108.75	45.221		
3,400.00	3,304.42	3,162.92	3,162.40	16.15	96.05	-96.45	-3,632.21	3,271.77	4,919.58	4,807.41	112.17	43.857		
3,500.00	3,400.77	3,243.62	3,243.08	16.69	98.50	-96.69	-3,632.44	3,271.77	4,922.94	4,807.79	115.15	42.752		
3,600.00	3,497.13	3,324.48	3,323.93	17.22	100.96	-96.94	-3,633.08	3,271.77	4,926.75	4,808.62	118.13	41.706		
3,700.00	3,593.49	3,453.21	3,452.49	17.76	104.87	-97.33	-3,634.08	3,271.77	4,930.73	4,808.16	122.57	40.227		
3,800.00	3,689.85	3,549.57	3,548.85	18.29	107.79	-97.62	-3,634.08	3,271.77	4,934.34	4,808.31	126.03	39.153		
3,900.00	3,786.21	3,645.93	3,645.21	18.82	110.72	-97.92	-3,634.08	3,271.77	4,938.09	4,808.61	129.48	38.137		
4,000.00	3,882.56	3,728.94	3,728.18	19.36	113.24	-98.19	-3,632.30	3,271.77	4,940.92	4,808.39	132.53	37.282		
4,061.50	3,941.82	3,779.18	3,778.42	19.69	114.76	-98.34	-3,632.60	3,271.77	4,943.60	4,809.23	134.38	36.789		
4,100.00	3,978.90	3,810.66	3,809.89	19.89	115.72	-98.08	-3,632.87	3,271.77	4,944.02	4,808.48	135.53	36.479		
4,150.00	4,026.79	3,851.38	3,850.60	20.15	116.96	-67.97	-3,633.30	3,271.77	4,940.63	4,803.60	137.02	36.057		
4,200.00	4,073.99	3,933.95	3,932.99	20.39	119.46	-56.04	-3,634.08	3,271.77	4,932.80	4,793.01	139.78	35.289		
4,250.00	4,120.13	3,980.08	3,979.13	20.61	120.87	-47.59	-3,634.08	3,271.77	4,920.23	4,778.81	141.42	34.792		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - December Dream 003 - OH - OH													Offset Site Error:	0.00 ft
Survey Program: 92-INCLINOMETER													Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Distance Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
4,300.00	4,164.80	4,024.76	4,023.80	20.83	122.22	-41.75	-3,634.08	3,271.77	4,903.36	4,760.36	143.00	34.290		
4,350.00	4,207.64	4,067.60	4,066.64	21.02	123.52	-37.73	-3,634.08	3,271.77	4,882.35	4,737.84	144.50	33.787		
4,400.00	4,248.29	4,108.24	4,107.29	21.21	124.76	-35.01	-3,634.08	3,271.77	4,857.36	4,711.43	145.93	33.285		
4,450.00	4,286.40	4,146.36	4,145.40	21.38	125.91	-33.26	-3,634.08	3,271.77	4,828.61	4,681.34	147.27	32.787		
4,500.00	4,321.66	4,178.29	4,177.30	21.54	126.88	-32.31	-3,632.18	3,271.77	4,795.22	4,646.81	148.41	32.311		
4,550.00	4,353.77	4,205.77	4,204.78	21.69	127.72	-32.04	-3,632.24	3,271.77	4,759.73	4,610.33	149.40	31.859		
4,600.00	4,382.45	4,230.42	4,229.43	21.83	128.47	-32.47	-3,632.32	3,271.77	4,721.31	4,571.01	150.29	31.414		
4,650.00	4,407.48	4,252.03	4,251.03	21.96	129.12	-33.72	-3,632.43	3,271.77	4,680.26	4,529.17	151.08	30.978		
4,700.00	4,428.64	4,270.40	4,269.40	22.10	129.68	-36.00	-3,632.55	3,271.77	4,636.91	4,485.14	151.76	30.553		
4,750.00	4,445.75	4,285.35	4,284.34	22.24	130.14	-39.81	-3,632.66	3,271.77	4,591.61	4,439.28	152.33	30.142		
4,800.00	4,458.66	4,296.74	4,295.73	22.40	130.48	-46.09	-3,632.75	3,271.77	4,544.73	4,391.95	152.78	29.747		
4,850.00	4,467.28	4,304.45	4,303.45	22.59	130.72	-56.83	-3,632.82	3,271.77	4,496.66	4,343.55	153.11	29.369		
4,900.00	4,471.53	4,308.41	4,307.40	22.83	130.84	-75.73	-3,632.85	3,271.77	4,447.79	4,294.47	153.31	29.011		
4,926.41	4,471.99	4,308.96	4,307.95	22.98	130.85	-90.15	-3,632.86	3,271.77	4,421.78	4,268.41	153.37	28.831		
5,000.00	4,471.57	4,309.00	4,307.99	23.54	130.85	-90.15	-3,632.86	3,271.77	4,349.24	4,195.76	153.48	28.337		
5,100.00	4,471.00	4,309.06	4,308.05	24.65	130.86	-90.16	-3,632.86	3,271.77	4,250.73	4,097.07	153.65	27.665		
5,200.00	4,470.42	4,309.12	4,308.11	26.13	130.86	-90.16	-3,632.86	3,271.77	4,152.28	3,998.44	153.84	26.991		
5,300.00	4,469.85	4,309.18	4,308.17	27.86	130.86	-90.17	-3,632.86	3,271.77	4,053.91	3,899.87	154.05	26.316		
5,400.00	4,469.28	4,309.24	4,308.23	29.77	130.86	-90.17	-3,632.86	3,271.77	3,955.62	3,801.35	154.27	25.640		
5,500.00	4,468.70	4,309.30	4,308.29	31.80	130.86	-90.18	-3,632.86	3,271.77	3,857.42	3,702.90	154.53	24.963		
5,600.00	4,468.13	4,309.36	4,308.35	33.92	130.86	-90.18	-3,632.86	3,271.77	3,759.32	3,604.51	154.81	24.284		
5,700.00	4,467.56	4,309.42	4,308.41	36.12	130.87	-90.19	-3,632.86	3,271.77	3,661.32	3,506.20	155.12	23.604		
5,800.00	4,466.99	4,309.48	4,308.48	38.37	130.87	-90.19	-3,632.86	3,271.77	3,563.43	3,407.97	155.46	22.922		
5,900.00	4,466.41	4,309.55	4,308.54	40.67	130.87	-90.20	-3,632.86	3,271.77	3,465.66	3,309.82	155.84	22.239		
6,000.00	4,465.84	4,309.61	4,308.60	43.00	130.87	-90.20	-3,632.86	3,271.77	3,368.02	3,211.77	156.25	21.555		
6,100.00	4,465.27	4,309.67	4,308.66	45.36	130.87	-90.21	-3,632.86	3,271.77	3,270.52	3,113.81	156.71	20.870		
6,200.00	4,464.69	4,309.74	4,308.73	47.76	130.88	-90.21	-3,632.86	3,271.77	3,173.18	3,015.96	157.22	20.183		
6,300.00	4,464.12	4,309.80	4,308.79	50.17	130.88	-90.22	-3,632.86	3,271.77	3,076.01	2,918.23	157.78	19.496		
6,400.00	4,463.55	4,309.87	4,308.86	52.60	130.88	-90.22	-3,632.86	3,271.77	2,979.03	2,820.63	158.40	18.807		
6,500.00	4,462.97	4,309.93	4,308.92	55.05	130.88	-90.23	-3,632.86	3,271.77	2,882.25	2,723.17	159.08	18.118		
6,600.00	4,462.40	4,310.00	4,308.99	57.51	130.88	-90.23	-3,632.87	3,271.77	2,785.70	2,625.87	159.83	17.429		
6,700.00	4,461.83	4,310.07	4,309.06	59.99	130.89	-90.24	-3,632.87	3,271.77	2,689.41	2,528.74	160.66	16.739		
6,800.00	4,461.25	4,310.13	4,309.12	62.47	130.89	-90.24	-3,632.87	3,271.77	2,593.39	2,431.81	161.58	16.050		
6,900.00	4,460.68	4,310.20	4,309.19	64.97	130.89	-90.25	-3,632.87	3,271.77	2,497.69	2,335.08	162.60	15.361		
7,000.00	4,460.11	4,310.27	4,309.26	67.47	130.89	-90.25	-3,632.87	3,271.77	2,402.33	2,238.60	163.73	14.673		
7,100.00	4,459.53	4,310.34	4,309.33	69.98	130.89	-90.26	-3,632.87	3,271.77	2,307.37	2,142.39	164.98	13.986		
7,200.00	4,458.96	4,310.41	4,309.40	72.50	130.90	-90.26	-3,632.87	3,271.77	2,212.85	2,046.49	166.36	13.301		
7,300.00	4,458.39	4,310.48	4,309.47	75.03	130.90	-90.27	-3,632.87	3,271.77	2,118.84	1,950.94	167.90	12.620		
7,400.00	4,457.82	4,310.55	4,309.54	77.55	130.90	-90.27	-3,632.87	3,271.77	2,025.40	1,855.79	169.61	11.941		
7,500.00	4,457.24	4,310.62	4,309.61	80.09	130.90	-90.28	-3,632.87	3,271.77	1,932.62	1,761.10	171.52	11.268		
7,600.00	4,456.67	4,310.69	4,309.68	82.63	130.91	-90.29	-3,632.87	3,271.77	1,840.59	1,666.95	173.64	10.600		
7,700.00	4,456.10	4,310.76	4,309.75	85.17	130.91	-90.29	-3,632.87	3,271.77	1,749.44	1,573.43	176.01	9.939		
7,800.00	4,455.52	4,310.83	4,309.82	87.72	130.91	-90.30	-3,632.87	3,271.77	1,659.31	1,480.65	178.66	9.287		
7,900.00	4,454.95	4,310.91	4,309.90	90.27	130.91	-90.30	-3,632.87	3,271.77	1,570.37	1,388.75	181.63	8.646		
8,000.00	4,454.38	4,310.98	4,309.97	92.82	130.91	-90.31	-3,632.87	3,271.77	1,482.85	1,297.89	184.95	8.017		
8,100.00	4,453.80	4,311.06	4,310.05	95.38	130.92	-90.31	-3,632.88	3,271.77	1,397.00	1,208.32	188.68	7.404		
8,200.00	4,453.23	4,311.13	4,310.12	97.94	130.92	-90.32	-3,632.88	3,271.77	1,313.15	1,120.29	192.86	6.809		
8,300.00	4,452.66	4,311.21	4,310.20	100.50	130.92	-90.33	-3,632.88	3,271.77	1,231.72	1,034.17	197.55	6.235		
8,400.00	4,452.08	4,311.28	4,310.27	103.06	130.92	-90.33	-3,632.88	3,271.77	1,153.21	950.44	202.77	5.687		
8,500.00	4,451.51	4,311.36	4,310.35	105.63	130.93	-90.34	-3,632.88	3,271.77	1,078.27	869.70	208.57	5.170		
8,600.00	4,450.94	4,311.44	4,310.43	108.19	130.93	-90.34	-3,632.88	3,271.77	1,007.68	792.75	214.94	4.688		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - December Dream 003 - OH - OH													Offset Site Error:	0.00 ft
Survey Program:		92-INCLINOMETER					Rule Assigned:		Offset Well Error:		0.00 ft			
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Distance		Warning						
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
8,700.00	4,450.36	4,311.52	4,310.51	110.76	130.93	-90.35	-3,632.88	3,271.77	942.44	720.62	221.82	4.249		
8,800.00	4,449.79	4,311.60	4,310.59	113.33	130.93	-90.36	-3,632.88	3,271.77	883.72	654.65	229.07	3.858		
8,900.00	4,449.22	4,311.67	4,310.67	115.90	130.94	-90.36	-3,632.88	3,271.77	832.90	596.48	236.42	3.523		
9,000.00	4,448.64	4,311.76	4,310.75	118.48	130.94	-90.37	-3,632.88	3,271.77	791.51	548.06	243.45	3.251		
9,100.00	4,448.07	4,311.84	4,310.83	121.05	130.94	-90.37	-3,632.88	3,271.77	761.08	511.48	249.60	3.049		
9,200.00	4,447.50	4,311.92	4,310.91	123.63	130.94	-90.38	-3,632.88	3,271.77	742.98	488.71	254.26	2.922		
9,286.18	4,447.00	4,311.99	4,310.98	125.85	130.94	-90.39	-3,632.88	3,271.77	737.96	481.26	256.70	2.875 CC		
9,300.00	4,446.93	4,312.00	4,310.99	126.21	130.95	-90.39	-3,632.88	3,271.77	738.09	481.15	256.94	2.873 ES, SF		
9,400.00	4,446.35	4,312.08	4,311.08	128.79	130.95	-90.39	-3,632.88	3,271.77	746.69	489.29	257.40	2.901		
9,500.00	4,445.78	4,312.17	4,311.16	131.37	130.95	-90.40	-3,632.89	3,271.77	768.31	512.55	255.76	3.004		
9,600.00	4,445.21	4,312.25	4,311.24	133.95	130.95	-90.41	-3,632.89	3,271.77	801.92	549.47	252.44	3.177		
9,700.00	4,444.63	4,312.34	4,311.33	136.53	130.96	-90.41	-3,632.89	3,271.77	846.07	598.10	247.97	3.412		
9,800.00	4,444.06	4,312.43	4,311.42	139.11	130.96	-90.42	-3,632.89	3,271.77	899.22	656.36	242.86	3.703		
9,900.00	4,443.49	4,312.51	4,311.50	141.69	130.96	-90.43	-3,632.89	3,271.77	959.88	722.34	237.53	4.041		
10,000.00	4,442.91	4,312.60	4,311.59	144.28	130.96	-90.43	-3,632.89	3,271.77	1,026.71	794.44	232.27	4.420		
10,100.00	4,442.34	4,312.69	4,311.68	146.86	130.97	-90.44	-3,632.89	3,271.77	1,098.59	871.34	227.24	4.834		
10,200.00	4,441.77	4,312.78	4,311.77	149.45	130.97	-90.45	-3,632.89	3,271.77	1,174.59	952.04	222.55	5.278		
10,300.00	4,441.19	4,312.87	4,311.86	152.04	130.97	-90.45	-3,632.89	3,271.77	1,253.96	1,035.74	218.22	5.746		
10,400.00	4,440.62	4,312.96	4,311.95	154.62	130.97	-90.46	-3,632.89	3,271.77	1,336.11	1,121.85	214.26	6.236		
10,500.00	4,440.05	4,313.05	4,312.04	157.21	130.98	-90.47	-3,632.89	3,271.77	1,420.55	1,209.89	210.66	6.743		
10,600.00	4,439.47	4,313.15	4,312.14	159.80	130.98	-90.48	-3,632.89	3,271.77	1,506.89	1,299.50	207.39	7.266		
10,700.00	4,438.90	4,313.24	4,312.23	162.39	130.98	-90.48	-3,632.90	3,271.77	1,594.83	1,390.41	204.42	7.802		
10,800.00	4,438.33	4,313.33	4,312.33	164.98	130.99	-90.49	-3,632.90	3,271.77	1,684.11	1,482.39	201.73	8.348		
10,900.00	4,437.76	4,313.43	4,312.42	167.57	130.99	-90.50	-3,632.90	3,271.77	1,774.54	1,575.26	199.28	8.905		
11,000.00	4,437.18	4,313.53	4,312.52	170.16	130.99	-90.51	-3,632.90	3,271.77	1,865.95	1,668.90	197.05	9.469		
11,100.00	4,436.61	4,313.62	4,312.62	172.75	130.99	-90.51	-3,632.90	3,271.77	1,958.20	1,763.17	195.02	10.041		
11,200.00	4,436.04	4,313.72	4,312.71	175.34	131.00	-90.52	-3,632.90	3,271.77	2,051.17	1,858.00	193.17	10.619		
11,300.00	4,435.46	4,313.82	4,312.81	177.93	131.00	-90.53	-3,632.90	3,271.77	2,144.78	1,953.31	191.47	11.202		
11,382.00	4,434.99	4,313.90	4,312.90	180.05	131.00	-90.54	-3,632.90	3,271.77	2,221.95	2,031.77	190.18	11.683		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 137H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Measured Depth (ft)	Reference Vertical Depth (ft)	Offset Measured Depth (ft)	Offset Vertical Depth (ft)	Semi Major Axis Reference (ft)	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	Offset Wellbore Centre +E/-W (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
0.00	0.00	0.00	0.00	0.00	0.00	-105.67	-5.46	-19.46	20.21					
100.00	100.00	100.00	100.00	0.31	0.31	-105.67	-5.46	-19.46	20.21	19.60	0.62	32.781		
200.00	200.00	200.00	200.00	0.67	0.67	-105.67	-5.46	-19.46	20.21	18.88	1.33	15.157		
300.00	300.00	300.00	300.00	1.03	1.03	-105.67	-5.46	-19.46	20.21	18.16	2.05	9.857		
400.00	400.00	400.00	400.00	1.38	1.38	-105.67	-5.46	-19.46	20.21	17.44	2.77	7.303		
500.00	499.96	499.96	499.96	1.73	1.74	31.75	-5.46	-19.46	18.13	14.66	3.47	5.224		
600.00	599.69	599.85	599.84	2.07	2.10	51.41	-5.06	-19.10	12.28	8.11	4.17	2.944		
653.08	652.45	652.47	652.43	2.26	2.29	88.89	-3.76	-17.93	9.70	5.15	4.54	2.134	CC, ES, SF	
700.00	698.96	698.47	698.37	2.43	2.45	130.24	-1.89	-16.24	13.07	8.18	4.88	2.676		
800.00	797.55	794.36	793.90	2.81	2.80	161.96	4.20	-10.74	35.23	29.64	5.59	6.302		
900.00	895.21	886.50	885.29	3.22	3.14	169.71	12.84	-2.93	68.16	61.89	6.27	10.873		
964.03	957.17	945.08	943.21	3.50	3.35	171.95	19.35	2.94	93.23	86.51	6.71	13.886		
1,000.00	991.83	977.91	975.67	3.67	3.47	172.84	23.00	6.24	107.86	100.90	6.96	15.499		
1,100.00	1,088.18	1,069.17	1,065.90	4.14	3.82	174.39	33.16	15.41	148.60	140.98	7.62	19.495		
1,200.00	1,184.54	1,160.44	1,156.14	4.62	4.18	175.28	43.32	24.59	189.40	181.11	8.29	22.842		
1,300.00	1,280.90	1,251.71	1,246.38	5.12	4.54	175.85	53.48	33.76	230.22	221.25	8.97	25.657		
1,400.00	1,377.26	1,342.98	1,336.61	5.62	4.90	176.25	63.64	42.93	271.06	261.40	9.66	28.067		
1,500.00	1,473.62	1,434.25	1,426.85	6.13	5.26	176.54	73.79	52.10	311.90	301.56	10.35	30.146		
1,600.00	1,569.97	1,525.52	1,517.09	6.64	5.62	176.77	83.95	61.28	352.75	341.71	11.04	31.957		
1,700.00	1,666.33	1,616.78	1,607.32	7.16	5.99	176.95	94.11	70.45	393.60	381.87	11.73	33.547		
1,800.00	1,762.69	1,708.05	1,697.56	7.68	6.36	177.09	104.27	79.62	434.46	422.03	12.43	34.952		
1,900.00	1,859.05	1,799.32	1,787.79	8.20	6.72	177.21	114.43	88.79	475.32	462.19	13.13	36.203		
2,000.00	1,955.41	1,890.59	1,878.03	8.73	7.09	177.32	124.58	97.97	516.18	502.35	13.83	37.323		
2,100.00	2,051.76	1,981.86	1,968.27	9.25	7.46	177.40	134.74	107.14	557.04	542.50	14.53	38.331		
2,200.00	2,148.12	2,073.13	2,058.50	9.78	7.83	177.48	144.90	116.31	597.90	582.66	15.24	39.243		
2,300.00	2,244.48	2,164.40	2,148.74	10.31	8.20	177.54	155.06	125.48	638.76	622.82	15.94	40.072		
2,400.00	2,340.84	2,255.66	2,238.98	10.84	8.57	177.60	165.22	134.66	679.62	662.97	16.65	40.829		
2,500.00	2,437.20	2,346.93	2,329.21	11.37	8.95	177.65	175.37	143.83	720.48	703.13	17.35	41.521		
2,600.00	2,533.55	2,438.20	2,419.45	11.90	9.32	177.70	185.53	153.00	761.35	743.29	18.06	42.158		
2,700.00	2,629.91	2,529.47	2,509.69	12.43	9.69	177.74	195.69	162.17	802.21	783.44	18.77	42.746		
2,800.00	2,726.27	2,620.74	2,599.92	12.96	10.06	177.77	205.85	171.35	843.07	823.60	19.48	43.289		
2,900.00	2,822.63	2,712.01	2,690.16	13.49	10.44	177.81	216.01	180.52	883.94	863.75	20.18	43.793		
3,000.00	2,918.99	2,803.27	2,780.39	14.02	10.81	177.84	226.16	189.69	924.80	903.91	20.89	44.261		
3,100.00	3,015.34	2,894.54	2,870.63	14.55	11.18	177.87	236.32	198.86	965.67	944.06	21.60	44.698		
3,200.00	3,111.70	2,985.81	2,960.87	15.09	11.56	177.89	246.48	208.04	1,006.53	984.22	22.31	45.106		
3,300.00	3,208.06	3,077.08	3,051.10	15.62	11.93	177.91	256.64	217.21	1,047.40	1,024.37	23.03	45.488		
3,400.00	3,304.42	3,168.35	3,141.34	16.15	12.30	177.94	266.80	226.38	1,088.26	1,064.52	23.74	45.847		
3,500.00	3,400.77	3,259.62	3,231.58	16.69	12.68	177.96	276.95	235.55	1,129.12	1,104.68	24.45	46.184		
3,600.00	3,497.13	3,350.88	3,321.81	17.22	13.05	177.98	287.11	244.73	1,169.99	1,144.83	25.16	46.501		
3,700.00	3,593.49	3,442.15	3,412.05	17.76	13.43	177.99	297.27	253.90	1,210.86	1,184.98	25.87	46.800		
3,800.00	3,689.85	3,533.42	3,502.29	18.29	13.80	178.01	307.43	263.07	1,251.72	1,225.13	26.59	47.083		
3,900.00	3,786.21	3,624.69	3,592.52	18.82	14.17	178.02	317.59	272.24	1,292.59	1,265.29	27.30	47.350		
4,000.00	3,882.56	3,715.96	3,682.76	19.36	14.55	178.04	327.74	281.42	1,333.45	1,305.44	28.01	47.603		
4,061.50	3,941.82	3,772.09	3,738.25	19.69	14.78	178.05	333.99	287.06	1,358.58	1,330.13	28.45	47.752		
4,100.00	3,978.90	3,807.20	3,772.97	19.89	14.92	-165.85	337.90	290.58	1,374.31	1,345.58	28.72	47.844		
4,150.00	4,026.79	3,852.52	3,817.77	20.15	15.11	-147.48	342.94	295.14	1,394.64	1,365.56	29.08	47.965		
4,200.00	4,073.99	3,897.17	3,861.92	20.39	15.29	-133.32	347.91	299.63	1,414.75	1,385.33	29.42	48.089		
4,250.00	4,120.13	3,940.78	3,905.03	20.61	15.47	-122.86	352.77	304.01	1,434.57	1,404.81	29.75	48.218		
4,300.00	4,164.80	3,982.98	3,946.76	20.83	15.64	-115.12	357.46	308.25	1,454.05	1,423.98	30.07	48.351		
4,350.00	4,207.64	4,020.30	3,983.65	21.02	15.80	-109.19	361.86	311.76	1,473.22	1,442.86	30.36	48.528		
4,400.00	4,248.29	4,050.00	4,012.94	21.21	15.92	-104.44	366.47	313.42	1,492.22	1,461.63	30.59	48.780		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 137H - Original Drilling - APD												Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM												Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Distance		Rule Assigned:					
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
4,450.00	4,286.40	4,076.81	4,039.24	21.38	16.03	-100.56	371.59	313.92	1,511.18	1,480.37	30.81	49.045	
4,500.00	4,321.66	4,100.00	4,061.85	21.54	16.12	-97.25	376.75	313.60	1,530.16	1,499.14	31.02	49.322	
4,550.00	4,353.77	4,113.78	4,075.20	21.69	16.17	-94.11	380.13	313.07	1,549.21	1,518.02	31.19	49.673	
4,600.00	4,382.45	4,125.72	4,086.71	21.83	16.22	-91.26	383.25	312.42	1,568.31	1,536.94	31.37	49.987	
4,650.00	4,407.48	4,133.91	4,094.57	21.96	16.25	-88.56	385.49	311.86	1,587.42	1,555.85	31.58	50.272	
4,700.00	4,428.64	4,138.83	4,099.28	22.10	16.27	-85.99	386.87	311.48	1,606.46	1,574.65	31.81	50.506	
4,750.00	4,445.75	4,150.00	4,109.92	22.24	16.32	-83.89	390.12	310.51	1,625.35	1,593.19	32.16	50.547	
4,800.00	4,458.66	4,150.00	4,109.92	22.40	16.32	-81.58	390.12	310.51	1,643.88	1,611.41	32.47	50.621	
4,850.00	4,467.28	4,150.00	4,109.92	22.59	16.32	-79.48	390.12	310.51	1,661.98	1,629.12	32.86	50.576	
4,900.00	4,471.53	4,133.77	4,094.43	22.83	16.25	-77.04	385.45	311.87	1,679.34	1,646.17	33.17	50.631	
4,926.41	4,471.99	4,130.87	4,091.65	22.98	16.24	-76.06	384.65	312.08	1,688.25	1,654.85	33.40	50.540	
5,000.00	4,471.57	4,122.71	4,083.81	23.54	16.21	-75.77	382.45	312.60	1,714.13	1,680.00	34.12	50.232	
5,100.00	4,471.00	4,100.00	4,061.85	24.65	16.12	-74.98	376.75	313.60	1,753.63	1,718.56	35.08	49.992	
5,200.00	4,470.42	4,100.00	4,061.85	26.13	16.12	-74.98	376.75	313.60	1,797.52	1,761.24	36.28	49.547	
5,300.00	4,469.85	4,100.00	4,061.85	27.86	16.12	-74.98	376.75	313.60	1,845.79	1,808.30	37.48	49.242	
5,400.00	4,469.28	4,100.00	4,061.85	29.77	16.12	-74.98	376.75	313.60	1,898.10	1,859.43	38.66	49.092	
5,500.00	4,468.70	4,100.00	4,061.85	31.80	16.12	-74.98	376.75	313.60	1,954.13	1,914.33	39.80	49.097	
5,600.00	4,468.13	4,080.49	4,042.84	33.92	16.04	-74.29	372.37	313.92	2,013.26	1,972.54	40.72	49.439	
5,700.00	4,467.56	4,075.99	4,038.45	36.12	16.02	-74.14	371.43	313.92	2,075.65	2,033.94	41.71	49.764	
5,800.00	4,466.99	4,071.95	4,034.49	38.37	16.01	-73.99	370.60	313.90	2,140.86	2,098.22	42.64	50.209	
5,900.00	4,466.41	4,050.00	4,012.94	40.67	15.92	-73.22	366.47	313.42	2,208.94	2,165.59	43.35	50.950	
6,000.00	4,465.84	4,050.00	4,012.94	43.00	15.92	-73.22	366.47	313.42	2,279.00	2,234.80	44.19	51.570	
6,100.00	4,465.27	4,050.00	4,012.94	45.36	15.92	-73.22	366.47	313.42	2,351.21	2,306.24	44.97	52.284	
6,200.00	4,464.69	4,050.00	4,012.94	47.76	15.92	-73.22	366.47	313.42	2,425.40	2,379.71	45.69	53.084	
6,300.00	4,464.12	4,050.00	4,012.94	50.17	15.92	-73.22	366.47	313.42	2,501.39	2,455.04	46.36	53.960	
6,400.00	4,463.55	4,050.00	4,012.94	52.60	15.92	-73.22	366.47	313.42	2,579.02	2,532.05	46.97	54.904	
6,500.00	4,462.97	4,050.00	4,012.94	55.05	15.92	-73.22	366.47	313.42	2,658.14	2,610.60	47.54	55.909	
6,600.00	4,462.40	4,050.00	4,012.94	57.51	15.92	-73.22	366.47	313.42	2,738.63	2,690.56	48.07	56.969	
6,700.00	4,461.83	4,050.00	4,012.94	59.99	15.92	-73.22	366.47	313.42	2,820.37	2,771.81	48.56	58.078	
6,800.00	4,461.25	4,050.00	4,012.94	62.47	15.92	-73.22	366.47	313.42	2,903.25	2,854.24	49.02	59.231	
6,900.00	4,460.68	4,050.00	4,012.94	64.97	15.92	-73.22	366.47	313.42	2,987.18	2,937.75	49.44	60.424	
7,000.00	4,460.11	4,050.00	4,012.94	67.47	15.92	-73.22	366.47	313.42	3,072.07	3,022.25	49.83	61.653	
7,100.00	4,459.53	4,050.00	4,012.94	69.98	15.92	-73.22	366.47	313.42	3,157.85	3,107.66	50.19	62.914	
7,200.00	4,458.96	4,050.00	4,012.94	72.50	15.92	-73.22	366.47	313.42	3,244.44	3,193.91	50.53	64.204	
7,300.00	4,458.39	4,050.00	4,012.94	75.03	15.92	-73.22	366.47	313.42	3,331.78	3,280.93	50.85	65.521	
7,400.00	4,457.82	4,050.00	4,012.94	77.55	15.92	-73.22	366.47	313.42	3,419.82	3,368.67	51.15	66.862	
7,500.00	4,457.24	4,050.00	4,012.94	80.09	15.92	-73.22	366.47	313.42	3,508.50	3,457.07	51.42	68.226	
7,600.00	4,456.67	4,050.00	4,012.94	82.63	15.92	-73.22	366.47	313.42	3,597.77	3,546.08	51.69	69.609	
7,700.00	4,456.10	4,050.00	4,012.94	85.17	15.92	-73.22	366.47	313.42	3,687.59	3,635.66	51.93	71.011	
7,800.00	4,455.52	4,050.00	4,012.94	87.72	15.92	-73.22	366.47	313.42	3,777.92	3,725.76	52.16	72.430	
7,900.00	4,454.95	4,050.00	4,012.94	90.27	15.92	-73.22	366.47	313.42	3,868.73	3,816.35	52.38	73.864	
8,000.00	4,454.38	4,050.00	4,012.94	92.82	15.92	-73.22	366.47	313.42	3,959.98	3,907.40	52.58	75.312	
8,100.00	4,453.80	4,050.00	4,012.94	95.38	15.92	-73.22	366.47	313.42	4,051.65	3,998.87	52.77	76.772	
8,200.00	4,453.23	4,050.00	4,012.94	97.94	15.92	-73.22	366.47	313.42	4,143.70	4,090.74	52.96	78.245	
8,300.00	4,452.66	4,050.00	4,012.94	100.50	15.92	-73.22	366.47	313.42	4,236.11	4,182.98	53.13	79.729	
8,400.00	4,452.08	4,028.27	3,991.53	103.06	15.83	-72.45	362.99	312.32	4,328.40	4,275.26	53.14	81.452	
8,500.00	4,451.51	4,027.56	3,990.82	105.63	15.83	-72.43	362.88	312.27	4,421.43	4,368.14	53.29	82.965	
8,600.00	4,450.94	4,026.87	3,990.14	108.19	15.82	-72.41	362.78	312.22	4,514.76	4,461.32	53.44	84.486	
8,700.00	4,450.36	4,026.21	3,989.49	110.76	15.82	-72.38	362.69	312.18	4,608.37	4,554.79	53.58	86.015	
8,800.00	4,449.79	4,025.58	3,988.87	113.33	15.82	-72.36	362.60	312.14	4,702.24	4,648.53	53.71	87.551	
8,900.00	4,449.22	4,024.97	3,988.27	115.90	15.82	-72.34	362.51	312.09	4,796.36	4,742.52	53.84	89.093	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 137H - Original Drilling - APD													Offset Site Error:	0.00 ft	
Survey Program:		0-MWD+HDGM		Offset		Semi Major Axis		Offset Wellbore Centre		Rule Assigned:				Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning		
9,000.00	4,448.64	4,024.39	3,987.69	118.48	15.81	-72.32	362.43	312.05	4,890.71	4,836.75	53.96	90.642			
9,100.00	4,448.07	4,023.83	3,987.14	121.05	15.81	-72.30	362.35	312.01	4,985.28	4,931.21	54.07	92.196			
9,200.00	4,447.50	4,023.29	3,986.60	123.63	15.81	-72.28	362.27	311.98	5,080.06	5,025.88	54.18	93.754			
9,300.00	4,446.93	4,000.93	3,964.51	126.21	15.72	-71.49	359.46	310.05	5,175.50	5,121.36	54.13	95.606			
9,400.00	4,446.35	4,000.93	3,964.51	128.79	15.72	-71.49	359.46	310.05	5,270.64	5,216.39	54.24	97.170			
9,500.00	4,445.78	4,000.93	3,964.51	131.37	15.72	-71.49	359.46	310.05	5,365.95	5,311.61	54.35	98.738			
9,600.00	4,445.21	4,000.93	3,964.51	133.95	15.72	-71.49	359.46	310.05	5,461.43	5,406.99	54.45	100.310			
9,700.00	4,444.63	4,000.93	3,964.51	136.53	15.72	-71.49	359.46	310.05	5,557.08	5,502.53	54.54	101.884			
9,800.00	4,444.06	4,000.93	3,964.51	139.11	15.72	-71.49	359.46	310.05	5,652.87	5,598.23	54.64	103.462			
9,900.00	4,443.49	4,000.93	3,964.51	141.69	15.72	-71.49	359.46	310.05	5,748.80	5,694.08	54.73	105.042			
10,000.00	4,442.91	4,000.93	3,964.51	144.28	15.72	-71.49	359.46	310.05	5,844.88	5,790.06	54.82	106.624			
10,100.00	4,442.34	4,000.93	3,964.51	146.86	15.72	-71.49	359.46	310.05	5,941.08	5,886.17	54.90	108.209			
10,200.00	4,441.77	4,000.93	3,964.51	149.45	15.72	-71.49	359.46	310.05	6,037.40	5,982.41	54.99	109.795			
10,300.00	4,441.19	4,000.93	3,964.51	152.04	15.72	-71.49	359.46	310.05	6,133.85	6,078.78	55.07	111.384			
10,400.00	4,440.62	4,000.93	3,964.51	154.62	15.72	-71.49	359.46	310.05	6,230.40	6,175.25	55.15	112.973			
10,500.00	4,440.05	4,000.93	3,964.51	157.21	15.72	-71.49	359.46	310.05	6,327.06	6,271.83	55.23	114.564			
10,600.00	4,439.47	4,000.93	3,964.51	159.80	15.72	-71.49	359.46	310.05	6,423.83	6,368.52	55.30	116.156			
10,700.00	4,438.90	4,000.93	3,964.51	162.39	15.72	-71.49	359.46	310.05	6,520.69	6,465.31	55.38	117.748			
10,800.00	4,438.33	4,000.93	3,964.51	164.98	15.72	-71.49	359.46	310.05	6,617.64	6,562.19	55.45	119.341			
10,900.00	4,437.76	4,000.93	3,964.51	167.57	15.72	-71.49	359.46	310.05	6,714.69	6,659.16	55.52	120.935			
11,000.00	4,437.18	4,000.93	3,964.51	170.16	15.72	-71.49	359.46	310.05	6,811.82	6,756.22	55.59	122.529			
11,100.00	4,436.61	4,000.93	3,964.51	172.75	15.72	-71.49	359.46	310.05	6,909.03	6,853.37	55.66	124.124			
11,200.00	4,436.04	4,000.93	3,964.51	175.34	15.72	-71.49	359.46	310.05	7,006.32	6,950.59	55.73	125.718			
11,300.00	4,435.46	4,000.93	3,964.51	177.93	15.72	-71.49	359.46	310.05	7,103.69	7,047.89	55.80	127.312			
11,382.00	4,434.99	4,000.93	3,964.51	180.05	15.72	-71.49	359.46	310.05	7,183.58	7,127.73	55.85	128.620			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 106H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Measured Depth (ft)	Reference Vertical Depth (ft)	Offset Measured Depth (ft)	Offset Vertical Depth (ft)	Semi Major Axis Reference (ft)	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	Offset Wellbore Centre +E/-W (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
0.00	0.00	0.00	0.00	0.00	0.00	-104.98	-20.75	-77.55	80.27					
100.00	100.00	100.00	100.00	0.31	0.31	-104.98	-20.75	-77.55	80.27	79.66	0.62	130.193		
200.00	200.00	200.00	200.00	0.67	0.67	-104.98	-20.75	-77.55	80.27	78.94	1.33	60.197		
300.00	300.00	300.00	300.00	1.03	1.03	-104.98	-20.75	-77.55	80.27	78.22	2.05	39.149		
400.00	400.00	400.00	400.00	1.38	1.38	-104.98	-20.75	-77.55	80.27	77.51	2.77	29.007		
500.00	499.96	499.30	499.30	1.73	1.74	29.70	-20.77	-77.65	78.29	74.82	3.47	22.591		
600.00	599.69	596.56	596.53	2.07	2.07	32.46	-21.33	-80.06	74.66	70.53	4.13	18.057		
700.00	698.96	693.82	693.60	2.43	2.41	37.45	-22.63	-85.68	70.75	65.93	4.82	14.690		
800.00	797.55	791.02	790.38	2.81	2.76	45.07	-24.68	-94.51	67.30	61.78	5.52	12.200		
900.00	895.21	888.13	886.70	3.22	3.12	55.44	-27.46	-106.51	65.49	59.23	6.26	10.470		
914.92	909.69	902.60	901.02	3.28	3.17	57.20	-27.94	-108.58	65.45	59.08	6.37	10.273 CC, ES		
964.03	957.17	950.24	948.07	3.50	3.35	63.27	-29.63	-115.86	65.89	59.13	6.76	9.740		
1,000.00	991.83	985.15	982.45	3.67	3.49	67.70	-30.98	-121.68	66.95	59.89	7.06	9.478		
1,100.00	1,088.18	1,082.75	1,078.21	4.14	3.89	77.86	-35.23	-140.04	73.43	65.49	7.94	9.253 SF		
1,200.00	1,184.54	1,181.77	1,175.16	4.62	4.30	85.70	-39.78	-159.68	82.48	73.63	8.85	9.319		
1,300.00	1,280.90	1,280.78	1,272.10	5.12	4.73	91.92	-44.33	-179.32	92.76	82.98	9.78	9.485		
1,400.00	1,377.26	1,379.80	1,369.05	5.62	5.16	96.85	-48.89	-198.96	103.91	93.20	10.71	9.700		
1,500.00	1,473.62	1,478.82	1,465.99	6.13	5.60	100.82	-53.44	-218.60	115.67	104.03	11.65	9.932		
1,600.00	1,569.97	1,577.84	1,562.93	6.64	6.04	104.04	-57.99	-238.24	127.89	115.31	12.58	10.165		
1,700.00	1,666.33	1,676.85	1,659.88	7.16	6.48	106.69	-62.54	-257.88	140.43	126.91	13.52	10.390		
1,800.00	1,762.69	1,775.87	1,756.82	7.68	6.93	108.91	-67.09	-277.52	153.22	138.77	14.45	10.604		
1,900.00	1,859.05	1,874.89	1,853.76	8.20	7.38	110.79	-71.64	-297.17	166.21	150.82	15.38	10.804		
2,000.00	1,955.41	1,973.91	1,950.71	8.73	7.83	112.39	-76.19	-316.81	179.34	163.02	16.32	10.991		
2,100.00	2,051.76	2,072.93	2,047.65	9.25	8.29	113.77	-80.75	-336.45	192.59	175.34	17.25	11.164		
2,200.00	2,148.12	2,171.94	2,144.59	9.78	8.74	114.98	-85.30	-356.09	205.94	187.76	18.18	11.325		
2,300.00	2,244.48	2,270.96	2,241.54	10.31	9.20	116.04	-89.85	-375.73	219.37	200.25	19.12	11.474		
2,400.00	2,340.84	2,369.98	2,338.48	10.84	9.66	116.97	-94.40	-395.37	232.86	212.81	20.05	11.613		
2,500.00	2,437.20	2,469.00	2,435.43	11.37	10.11	117.81	-98.95	-415.01	246.41	225.42	20.99	11.741		
2,600.00	2,533.55	2,568.02	2,532.37	11.90	10.57	118.55	-103.50	-434.65	260.00	238.08	21.92	11.861		
2,700.00	2,629.91	2,667.03	2,629.31	12.43	11.03	119.22	-108.05	-454.29	273.63	250.78	22.86	11.973		
2,800.00	2,726.27	2,766.05	2,726.26	12.96	11.49	119.83	-112.61	-473.93	287.30	263.51	23.79	12.077		
2,900.00	2,822.63	2,865.07	2,823.20	13.49	11.95	120.39	-117.16	-493.57	300.99	276.27	24.72	12.174		
3,000.00	2,918.99	2,964.09	2,920.14	14.02	12.41	120.89	-121.71	-513.21	314.71	289.06	25.66	12.265		
3,100.00	3,015.34	3,063.11	3,017.09	14.55	12.87	121.35	-126.26	-532.85	328.46	301.86	26.59	12.351		
3,200.00	3,111.70	3,162.12	3,114.03	15.09	13.33	121.78	-130.81	-552.49	342.22	314.69	27.53	12.431		
3,300.00	3,208.06	3,261.14	3,210.98	15.62	13.79	122.17	-135.36	-572.13	356.00	327.53	28.46	12.507		
3,400.00	3,304.42	3,360.16	3,307.92	16.15	14.25	122.54	-139.91	-591.77	369.79	340.39	29.40	12.578		
3,500.00	3,400.77	3,459.18	3,404.86	16.69	14.72	122.87	-144.47	-611.41	383.60	353.26	30.33	12.646		
3,600.00	3,497.13	3,558.19	3,501.81	17.22	15.18	123.19	-149.02	-631.05	397.42	366.15	31.27	12.709		
3,700.00	3,593.49	3,657.21	3,598.75	17.76	15.64	123.48	-153.57	-650.69	411.25	379.04	32.20	12.770		
3,800.00	3,689.85	3,756.23	3,695.69	18.29	16.10	123.75	-158.12	-670.33	425.08	391.94	33.14	12.827		
3,900.00	3,786.21	3,855.25	3,792.64	18.82	16.57	124.01	-162.67	-689.97	438.93	404.86	34.08	12.881		
4,000.00	3,882.56	3,954.27	3,889.58	19.36	17.03	124.25	-167.22	-709.61	452.79	417.78	35.01	12.933		
4,061.50	3,941.82	4,015.16	3,949.20	19.69	17.31	124.39	-170.02	-721.69	461.32	425.73	35.59	12.963		
4,100.00	3,978.90	4,053.12	3,986.36	19.89	17.49	124.44	-171.77	-729.22	467.74	431.79	35.95	13.012		
4,150.00	4,026.79	4,101.68	4,033.91	20.15	17.72	124.49	-174.00	-738.85	479.27	442.86	36.41	13.163		
4,200.00	4,073.99	4,149.06	4,080.30	20.39	17.94	124.54	-176.18	-748.25	494.37	457.50	36.87	13.409		
4,250.00	4,120.13	4,194.85	4,125.13	20.61	18.15	124.59	-178.28	-757.33	512.97	475.66	37.31	13.749		
4,300.00	4,164.80	4,238.67	4,168.03	20.83	18.36	124.64	-180.29	-766.03	535.03	497.29	37.74	14.178		
4,350.00	4,207.64	4,280.16	4,208.64	21.02	18.55	124.69	-182.20	-774.25	560.46	522.32	38.14	14.694		
4,400.00	4,248.29	4,318.95	4,246.62	21.21	18.73	124.74	-183.98	-781.95	589.16	550.64	38.52	15.294		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 106H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Measured Depth (ft)	Reference Vertical Depth (ft)	Offset Measured Depth (ft)	Offset Vertical Depth (ft)	Semi Major Axis Reference (ft)	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	Offset Wellbore Centre +E/-W (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
4,450.00	4,286.40	4,354.73	4,281.66	21.38	18.90	-162.49	-185.63	-789.05	620.99	582.12	38.87	15.976		
4,500.00	4,321.66	4,387.20	4,313.44	21.54	19.05	-158.88	-187.12	-795.49	655.76	616.58	39.18	16.735		
4,550.00	4,353.77	4,416.08	4,341.72	21.69	19.19	-155.05	-188.45	-801.22	693.25	653.79	39.46	17.567		
4,600.00	4,382.45	4,441.13	4,366.25	21.83	19.31	-150.66	-189.60	-806.18	733.18	693.47	39.70	18.467		
4,650.00	4,407.48	4,462.15	4,386.83	21.96	19.40	-145.30	-190.57	-810.35	775.24	735.34	39.90	19.430		
4,700.00	4,428.64	4,462.40	4,387.07	22.10	19.41	-136.46	-190.58	-810.40	819.28	779.37	39.91	20.530		
4,750.00	4,445.75	4,474.10	4,398.51	22.24	19.46	-127.02	-191.03	-812.81	864.70	824.68	40.02	21.606		
4,800.00	4,458.66	4,476.80	4,401.15	22.40	19.48	-114.17	-191.10	-813.39	911.23	871.17	40.05	22.750		
4,850.00	4,467.28	4,477.61	4,401.93	22.59	19.48	-99.42	-191.12	-813.56	958.31	918.23	40.08	23.912		
4,900.00	4,471.53	4,476.70	4,401.05	22.83	19.48	-84.58	-191.10	-813.37	1,005.51	965.42	40.09	25.081		
4,926.41	4,471.99	4,475.59	4,399.97	22.98	19.47	-77.40	-191.07	-813.13	1,030.36	990.26	40.10	25.698		
5,000.00	4,471.57	4,462.40	4,387.07	23.54	19.41	-75.48	-190.58	-810.40	1,099.83	1,059.80	40.03	27.478		
5,100.00	4,471.00	4,462.40	4,387.07	24.65	19.41	-75.48	-190.58	-810.40	1,194.75	1,154.66	40.09	29.802		
5,200.00	4,470.42	4,462.40	4,387.07	26.13	19.41	-75.48	-190.58	-810.40	1,290.44	1,250.29	40.14	32.146		
5,300.00	4,469.85	4,456.22	4,381.02	27.86	19.38	-74.59	-190.29	-809.18	1,386.72	1,346.57	40.14	34.543		
5,400.00	4,469.28	4,444.68	4,369.72	29.77	19.32	-72.98	-189.76	-806.89	1,483.41	1,443.31	40.11	36.987		
5,500.00	4,468.70	4,433.13	4,358.42	31.80	19.27	-71.42	-189.23	-804.60	1,580.43	1,540.36	40.07	39.442		
5,600.00	4,468.13	4,421.59	4,347.12	33.92	19.22	-69.89	-188.70	-802.31	1,677.73	1,637.69	40.04	41.906		
5,700.00	4,467.56	4,410.05	4,335.82	36.12	19.16	-68.42	-188.17	-800.02	1,775.24	1,735.24	40.00	44.380		
5,800.00	4,466.99	4,398.51	4,324.52	38.37	19.11	-66.99	-187.64	-797.73	1,872.95	1,832.98	39.97	46.860		
5,900.00	4,466.41	4,386.97	4,313.22	40.67	19.05	-65.60	-187.11	-795.44	1,970.82	1,930.88	39.94	49.347		
6,000.00	4,465.84	4,375.42	4,301.92	43.00	19.00	-64.26	-186.58	-793.15	2,068.83	2,028.92	39.91	51.840		
6,100.00	4,465.27	4,363.88	4,290.62	45.36	18.94	-62.96	-186.05	-790.86	2,166.96	2,127.08	39.88	54.337		
6,200.00	4,464.69	4,352.34	4,279.32	47.76	18.89	-61.70	-185.52	-788.57	2,265.20	2,225.35	39.85	56.839		
6,300.00	4,464.12	4,340.80	4,268.02	50.17	18.84	-60.49	-184.99	-786.28	2,363.52	2,323.70	39.83	59.345		
6,400.00	4,463.55	4,329.25	4,256.71	52.60	18.78	-59.32	-184.46	-783.99	2,461.93	2,422.13	39.80	61.854		
6,500.00	4,462.97	4,317.71	4,245.41	55.05	18.73	-58.18	-183.93	-781.70	2,560.41	2,520.63	39.78	64.365		
6,600.00	4,462.40	4,306.17	4,234.11	57.51	18.67	-57.09	-183.40	-779.41	2,658.95	2,619.20	39.76	66.880		
6,700.00	4,461.83	4,294.63	4,222.81	59.99	18.62	-56.03	-182.87	-777.12	2,757.55	2,717.82	39.74	69.396		
6,800.00	4,461.25	4,283.09	4,211.51	62.47	18.57	-55.01	-182.34	-774.84	2,856.20	2,816.48	39.72	71.914		
6,900.00	4,460.68	4,271.54	4,200.21	64.97	18.51	-54.03	-181.81	-772.55	2,954.90	2,915.20	39.70	74.433		
7,000.00	4,460.11	4,260.00	4,188.91	67.47	18.46	-53.07	-181.28	-770.26	3,053.63	3,013.95	39.68	76.953		
7,100.00	4,459.53	4,248.46	4,177.61	69.98	18.40	-52.16	-180.74	-767.97	3,152.41	3,112.74	39.67	79.473		
7,200.00	4,458.96	4,236.92	4,166.31	72.50	18.35	-51.27	-180.21	-765.68	3,251.22	3,211.56	39.65	81.995		
7,300.00	4,458.39	4,225.37	4,155.01	75.03	18.30	-50.41	-179.68	-763.39	3,350.05	3,310.42	39.64	84.516		
7,400.00	4,457.82	4,213.83	4,143.71	77.55	18.24	-49.58	-179.15	-761.10	3,448.92	3,409.30	39.63	87.036		
7,500.00	4,457.24	4,202.29	4,132.41	80.09	18.19	-48.78	-178.62	-758.81	3,547.81	3,508.20	39.62	89.557		
7,600.00	4,456.67	4,190.75	4,121.11	82.63	18.13	-48.01	-178.09	-756.52	3,646.73	3,607.13	39.61	92.076		
7,700.00	4,456.10	4,179.21	4,109.81	85.17	18.08	-47.26	-177.56	-754.23	3,745.67	3,706.07	39.60	94.595		
7,800.00	4,455.52	4,167.66	4,098.51	87.72	18.03	-46.54	-177.03	-751.94	3,844.63	3,805.04	39.59	97.112		
7,900.00	4,454.95	4,156.12	4,087.21	90.27	17.97	-45.84	-176.50	-749.65	3,943.61	3,904.02	39.58	99.628		
8,000.00	4,454.38	4,144.58	4,075.91	92.82	17.92	-45.16	-175.97	-747.36	4,042.60	4,003.02	39.58	102.142		
8,100.00	4,453.80	4,133.04	4,064.61	95.38	17.86	-44.50	-175.44	-745.07	4,141.61	4,102.04	39.57	104.654		
8,200.00	4,453.23	4,121.50	4,053.31	97.94	17.81	-43.87	-174.91	-742.78	4,240.64	4,201.07	39.57	107.164		
8,300.00	4,452.66	4,109.95	4,042.01	100.50	17.76	-43.26	-174.38	-740.49	4,339.68	4,300.11	39.57	109.672		
8,400.00	4,452.08	4,098.41	4,030.71	103.06	17.70	-42.66	-173.85	-738.20	4,438.73	4,399.17	39.57	112.177		
8,500.00	4,451.51	4,086.87	4,019.41	105.63	17.65	-42.09	-173.32	-735.92	4,537.80	4,498.23	39.57	114.679		
8,600.00	4,450.94	4,075.33	4,008.11	108.19	17.59	-41.53	-172.79	-733.63	4,636.88	4,597.31	39.57	117.177		
8,700.00	4,450.36	4,063.78	3,996.81	110.76	17.54	-40.99	-172.26	-731.34	4,735.96	4,696.39	39.57	119.673		
8,800.00	4,449.79	4,052.24	3,985.50	113.33	17.49	-40.47	-171.73	-729.05	4,835.06	4,795.48	39.58	122.165		
8,900.00	4,449.22	4,040.70	3,974.20	115.90	17.43	-39.96	-171.19	-726.76	4,934.17	4,894.59	39.58	124.654		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 106H - Original Drilling - APD													Offset Site Error:	0.00 ft	
Survey Program:		0-MWD+HDGM		Offset		Semi Major Axis		Offset Wellbore Centre		Rule Assigned:				Offset Well Error:	0.00 ft
Measured Depth	Vertical	Measured	Vertical	Reference	Offset	Highside Toolface	+N/-S	+E/-W	Between Centres	Between Ellipses	Minimum Separation	Separation Factor	Warning		
(ft)	(ft)	(ft)	(ft)	(ft)	(ft)	(°)	(ft)	(ft)	(ft)	(ft)	(ft)				
9,000.00	4,448.64	4,029.16	3,962.90	118.48	17.38	-39.46	-170.66	-724.47	5,033.29	4,993.70	39.59	127.139			
9,100.00	4,448.07	4,017.62	3,951.60	121.05	17.33	-38.99	-170.13	-722.18	5,132.41	5,092.81	39.60	129.619			
9,200.00	4,447.50	4,006.07	3,940.30	123.63	17.27	-38.52	-169.60	-719.89	5,231.54	5,191.94	39.60	132.096			
9,300.00	4,446.93	3,994.53	3,929.00	126.21	17.22	-38.07	-169.07	-717.60	5,330.68	5,291.07	39.61	134.568			
9,400.00	4,446.35	3,982.99	3,917.70	128.79	17.16	-37.63	-168.54	-715.31	5,429.83	5,390.20	39.62	137.036			
9,500.00	4,445.78	3,971.45	3,906.40	131.37	17.11	-37.20	-168.01	-713.02	5,528.98	5,489.35	39.63	139.499			
9,600.00	4,445.21	3,959.90	3,895.10	133.95	17.06	-36.79	-167.48	-710.73	5,628.14	5,588.49	39.65	141.957			
9,700.00	4,444.63	3,948.36	3,883.80	136.53	17.00	-36.39	-166.95	-708.44	5,727.31	5,687.65	39.66	144.410			
9,800.00	4,444.06	3,936.82	3,872.50	139.11	16.95	-36.00	-166.42	-706.15	5,826.48	5,786.80	39.67	146.857			
9,900.00	4,443.49	3,925.28	3,861.20	141.69	16.89	-35.62	-165.89	-703.86	5,925.65	5,885.96	39.69	149.300			
10,000.00	4,442.91	3,913.74	3,849.90	144.28	16.84	-35.25	-165.36	-701.57	6,024.83	5,985.13	39.71	151.737			
10,100.00	4,442.34	3,902.19	3,838.60	146.86	16.79	-34.88	-164.83	-699.28	6,124.02	6,084.30	39.72	154.168			
10,200.00	4,441.77	3,890.65	3,827.30	149.45	16.73	-34.53	-164.30	-697.00	6,223.21	6,183.47	39.74	156.593			
10,300.00	4,441.19	3,879.11	3,816.00	152.04	16.68	-34.19	-163.77	-694.71	6,322.41	6,282.65	39.76	159.013			
10,400.00	4,440.62	3,867.57	3,804.70	154.62	16.62	-33.86	-163.24	-692.42	6,421.61	6,381.83	39.78	161.426			
10,500.00	4,440.05	3,856.02	3,793.40	157.21	16.57	-33.53	-162.71	-690.13	6,520.81	6,481.01	39.80	163.834			
10,600.00	4,439.47	3,844.48	3,782.10	159.80	16.52	-33.22	-162.18	-687.84	6,620.02	6,580.20	39.82	166.235			
10,700.00	4,438.90	3,832.94	3,770.80	162.39	16.46	-32.91	-161.65	-685.55	6,719.23	6,679.38	39.85	168.629			
10,800.00	4,438.33	3,821.40	3,759.50	164.98	16.41	-32.61	-161.11	-683.26	6,818.44	6,778.57	39.87	171.017			
10,900.00	4,437.76	3,809.86	3,748.20	167.57	16.35	-32.31	-160.58	-680.97	6,917.66	6,877.77	39.89	173.398			
11,000.00	4,437.18	3,798.31	3,736.90	170.16	16.30	-32.03	-160.05	-678.68	7,016.88	6,976.96	39.92	175.773			
11,100.00	4,436.61	3,786.77	3,725.60	172.75	16.25	-31.75	-159.52	-676.39	7,116.11	7,076.16	39.95	178.140			
11,200.00	4,436.04	3,775.23	3,714.29	175.34	16.19	-31.48	-158.99	-674.10	7,215.34	7,175.36	39.97	180.501			
11,300.00	4,435.46	3,763.69	3,702.99	177.93	16.14	-31.21	-158.46	-671.81	7,314.57	7,274.56	40.00	182.854			
11,382.00	4,434.99	3,754.22	3,693.73	180.05	16.09	-30.99	-158.03	-669.93	7,395.94	7,355.92	40.03	184.779			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 108H - Original Drilling - APD												Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM												Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Offset		Highside Toolface (°)	Offset Wellbore Centre		Distance		Minimum Separation (ft)	Separation Factor	Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)		+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)			
0.00	0.00	0.00	0.00	0.00	0.00	-105.29	-10.56	-38.63	40.04				
100.00	100.00	100.00	100.00	0.31	0.31	-105.29	-10.56	-38.63	40.04	39.43	0.62	64.943	
200.00	200.00	200.00	200.00	0.67	0.67	-105.29	-10.56	-38.63	40.04	38.71	1.33	30.027	
300.00	300.00	300.00	300.00	1.03	1.03	-105.29	-10.56	-38.63	40.04	37.99	2.05	19.528	
400.00	400.00	400.00	400.00	1.38	1.38	-105.29	-10.56	-38.63	40.04	37.27	2.77	14.469	
500.00	499.96	498.93	498.92	1.73	1.73	29.17	-11.58	-39.71	39.27	35.82	3.45	11.376	
600.00	599.69	597.89	597.77	2.07	2.06	31.26	-14.65	-42.98	36.99	32.86	4.12	8.969	
700.00	698.96	696.89	696.49	2.43	2.41	35.36	-19.77	-48.42	33.31	28.50	4.81	6.922	
800.00	797.55	795.96	794.99	2.81	2.76	42.79	-26.94	-56.04	28.54	23.01	5.53	5.163	
900.00	895.21	895.11	893.23	3.22	3.13	56.43	-36.16	-65.84	23.43	17.13	6.30	3.718	
964.03	957.17	958.66	955.96	3.50	3.38	70.56	-43.13	-73.26	20.80	13.94	6.86	3.034	
1,000.00	991.83	994.41	991.15	3.67	3.52	79.79	-47.42	-77.82	19.98	12.80	7.18	2.784	
1,036.76	1,027.25	1,031.02	1,027.12	3.84	3.67	88.59	-52.09	-82.78	19.74	12.23	7.51	2.629 CC	
1,100.00	1,088.18	1,094.14	1,088.95	4.14	3.93	100.91	-60.78	-92.02	20.23	12.17	8.05	2.511 ES	
1,200.00	1,184.54	1,194.23	1,186.46	4.62	4.37	112.14	-76.23	-108.45	21.68	12.79	8.90	2.437	
1,300.00	1,280.90	1,294.30	1,283.38	5.12	4.82	116.35	-93.31	-126.61	22.69	12.91	9.78	2.321	
1,400.00	1,377.26	1,394.29	1,380.16	5.62	5.29	119.75	-110.51	-144.90	23.71	13.05	10.66	2.224	
1,500.00	1,473.62	1,494.27	1,476.94	6.13	5.77	122.85	-127.72	-163.19	24.80	13.27	11.53	2.150	
1,600.00	1,569.97	1,594.26	1,573.73	6.64	6.25	125.69	-144.92	-181.47	25.96	13.56	12.40	2.094	
1,700.00	1,666.33	1,694.24	1,670.51	7.16	6.74	128.28	-162.12	-199.76	27.18	13.92	13.26	2.050	
1,800.00	1,762.69	1,794.23	1,767.29	7.68	7.23	130.64	-179.32	-218.05	28.45	14.34	14.11	2.017	
1,900.00	1,859.05	1,894.21	1,864.07	8.20	7.73	132.80	-196.52	-236.34	29.76	14.81	14.95	1.991	
2,000.00	1,955.41	1,994.20	1,960.85	8.73	8.23	134.77	-213.72	-254.63	31.11	15.33	15.78	1.971	
2,100.00	2,051.76	2,094.18	2,057.64	9.25	8.73	136.57	-230.92	-272.91	32.50	15.88	16.61	1.956	
2,200.00	2,148.12	2,194.17	2,154.42	9.78	9.23	138.23	-248.12	-291.20	33.91	16.48	17.44	1.945	
2,300.00	2,244.48	2,294.16	2,251.20	10.31	9.74	139.75	-265.32	-309.49	35.35	17.10	18.26	1.936	
2,400.00	2,340.84	2,394.14	2,347.98	10.84	10.24	141.16	-282.52	-327.78	36.82	17.74	19.07	1.930	
2,500.00	2,437.20	2,494.13	2,444.76	11.37	10.75	142.45	-299.72	-346.07	38.30	18.41	19.89	1.926	
2,600.00	2,533.55	2,594.11	2,541.55	11.90	11.26	143.65	-316.92	-364.35	39.81	19.11	20.70	1.923	
2,700.00	2,629.91	2,694.10	2,638.33	12.43	11.77	144.76	-334.13	-382.64	41.32	19.82	21.51	1.921	
2,800.00	2,726.27	2,794.08	2,735.11	12.96	12.28	145.79	-351.33	-400.93	42.86	20.54	22.32	1.920	
2,900.00	2,822.63	2,894.07	2,831.89	13.49	12.79	146.75	-368.53	-419.22	44.40	21.28	23.12	1.920 SF	
3,000.00	2,918.99	2,994.05	2,928.67	14.02	13.30	147.64	-385.73	-437.50	45.96	22.03	23.93	1.921	
3,100.00	3,015.34	3,094.04	3,025.46	14.55	13.81	148.48	-402.93	-455.79	47.53	22.80	24.73	1.922	
3,200.00	3,111.70	3,194.02	3,122.24	15.09	14.32	149.26	-420.13	-474.08	49.11	23.57	25.53	1.923	
3,300.00	3,208.06	3,294.01	3,219.02	15.62	14.83	150.00	-437.37	-492.37	50.69	24.36	26.34	1.925	
3,400.00	3,304.42	3,393.99	3,315.80	16.15	15.35	150.68	-454.53	-510.66	52.29	25.15	27.14	1.927	
3,500.00	3,400.77	3,493.98	3,412.58	16.69	15.86	151.33	-471.73	-528.94	53.89	25.95	27.94	1.929	
3,600.00	3,497.13	3,593.97	3,509.37	17.22	16.37	151.94	-488.93	-547.23	55.50	26.75	28.74	1.931	
3,700.00	3,593.49	3,693.95	3,606.15	17.76	16.89	152.52	-506.13	-565.52	57.11	27.56	29.55	1.933	
3,800.00	3,689.85	3,793.94	3,702.93	18.29	17.40	153.06	-523.34	-583.81	58.73	28.38	30.35	1.935	
3,900.00	3,786.21	3,893.92	3,799.71	18.82	17.92	153.58	-540.54	-602.09	60.35	29.20	31.15	1.937	
4,000.00	3,882.56	3,993.91	3,896.49	19.36	18.43	154.07	-557.74	-620.38	61.98	30.03	31.95	1.940	
4,061.50	3,941.82	4,055.40	3,956.02	19.69	18.75	154.35	-568.32	-631.63	62.98	30.54	32.45	1.941	
4,100.00	3,978.90	4,093.86	3,993.24	19.89	18.94	167.89	-574.93	-638.66	64.17	31.30	32.87	1.952	
4,150.00	4,026.79	4,143.48	4,041.28	20.15	19.20	-179.74	-583.47	-647.74	67.60	33.84	33.76	2.002	
4,200.00	4,073.99	4,192.36	4,088.59	20.39	19.45	-173.59	-591.88	-656.68	73.91	38.90	35.01	2.111	
4,250.00	4,120.13	4,240.08	4,134.78	20.61	19.70	-171.81	-600.09	-665.41	84.07	47.61	36.46	2.306	
4,300.00	4,164.80	4,286.24	4,179.46	20.83	19.94	-172.23	-608.03	-673.85	98.78	60.92	37.86	2.609	
4,350.00	4,207.64	4,330.45	4,222.26	21.02	20.16	-173.34	-615.63	-681.94	118.30	79.25	39.06	3.029	
4,400.00	4,248.29	4,372.35	4,262.82	21.21	20.38	-174.41	-622.84	-689.60	142.51	102.50	40.01	3.562	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 108H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Reference	Vertical	Offset	Vertical	Reference	Semi Major Axis	Offset	Highside	Offset Wellbore Centre		Distance		Minimum	Separation	Warning
Measured Depth (ft)	Depth (ft)	Depth (ft)	Depth (ft)	Reference (ft)	Offset (ft)	Offset (ft)	Toolface (°)	+N/-S	+E/-W	Between Centres (ft)	Between Ellipses (ft)	Separation (ft)	Factor	
4,450.00	4,286.40	4,411.58	4,300.79	21.38	20.58	-175.14	-175.14	-629.59	-696.78	171.09	130.32	40.77	4.197	
4,500.00	4,321.66	4,456.63	4,344.39	21.54	20.81	-176.38	-176.38	-637.74	-704.61	203.29	161.91	41.38	4.913	
4,550.00	4,353.77	4,516.01	4,401.61	21.69	21.10	-178.24	-178.24	-652.06	-711.18	236.11	194.50	41.61	5.674	
4,600.00	4,382.45	4,583.54	4,465.56	21.83	21.42	-179.77	-179.77	-673.55	-712.91	268.38	227.16	41.23	6.510	
4,650.00	4,407.48	4,661.98	4,537.09	21.96	21.75	-178.88	-178.88	-705.07	-707.20	299.31	259.33	39.98	7.486	
4,700.00	4,428.64	4,754.96	4,616.12	22.10	22.10	-177.68	-177.68	-750.66	-689.89	327.85	290.35	37.50	8.742	
4,750.00	4,445.75	4,866.56	4,699.69	22.24	22.45	-176.65	-176.65	-815.38	-654.70	352.54	319.23	33.31	10.584	
4,752.25	4,446.42	4,872.07	4,703.44	22.25	22.47	-176.61	-176.61	-818.82	-652.57	353.53	320.46	33.07	10.690	
4,800.00	4,458.66	4,999.68	4,778.74	22.40	22.82	-175.88	-175.88	-903.25	-594.17	371.44	344.33	27.11	13.701	
4,802.25	4,459.15	5,006.17	4,781.94	22.41	22.84	-175.86	-175.86	-907.75	-590.76	372.11	345.32	26.79	13.890	
4,850.00	4,467.28	5,152.42	4,836.19	22.59	23.24	-175.50	-175.50	-1,011.94	-504.36	382.33	362.39	19.94	19.172	
4,900.00	4,471.53	5,302.97	4,853.96	22.83	23.89	-175.57	-175.57	-1,119.38	-401.10	383.59	367.07	16.52	23.217	
4,926.41	4,471.99	5,329.37	4,853.81	22.98	24.04	-175.59	-175.59	-1,137.82	-382.20	382.96	366.18	16.78	22.818	
5,000.00	4,471.57	5,402.96	4,853.39	23.54	24.72	-175.59	-175.59	-1,189.20	-329.52	382.96	365.45	17.51	21.873	
5,100.00	4,471.00	5,502.96	4,852.82	24.65	25.94	-175.60	-175.60	-1,259.02	-257.94	382.95	364.37	18.58	20.611	
5,200.00	4,470.42	5,602.96	4,852.24	26.13	27.47	-175.61	-175.61	-1,328.84	-186.35	382.95	363.22	19.73	19.413	
5,300.00	4,469.85	5,702.96	4,851.67	27.86	29.23	-175.62	-175.62	-1,398.66	-114.76	382.95	362.01	20.94	18.292	
5,400.00	4,469.28	5,802.96	4,851.10	29.77	31.14	-175.63	-175.63	-1,468.48	-43.17	382.94	360.75	22.20	17.253	
5,500.00	4,468.70	5,902.96	4,850.53	31.80	33.16	-175.63	-175.63	-1,538.30	28.42	382.94	359.44	23.50	16.295	
5,600.00	4,468.13	6,002.96	4,849.95	33.92	35.27	-175.64	-175.64	-1,608.12	100.00	382.93	358.09	24.84	15.416	
5,700.00	4,467.56	6,102.96	4,849.38	36.12	37.45	-175.65	-175.65	-1,677.94	171.59	382.93	356.72	26.21	14.609	
5,800.00	4,466.99	6,202.96	4,848.81	38.37	39.68	-175.66	-175.66	-1,747.76	243.18	382.93	355.32	27.61	13.869	
5,900.00	4,466.41	6,302.96	4,848.23	40.67	41.96	-175.67	-175.67	-1,817.58	314.77	382.92	353.89	29.03	13.191	
6,000.00	4,465.84	6,402.96	4,847.66	43.00	44.28	-175.67	-175.67	-1,887.40	386.35	382.92	352.45	30.47	12.568	
6,100.00	4,465.27	6,502.96	4,847.09	45.36	46.63	-175.68	-175.68	-1,957.22	457.94	382.92	350.99	31.92	11.994	
6,200.00	4,464.69	6,602.96	4,846.52	47.76	49.00	-175.69	-175.69	-2,027.04	529.53	382.91	349.52	33.40	11.466	
6,300.00	4,464.12	6,702.96	4,845.94	50.17	51.40	-175.70	-175.70	-2,096.86	601.12	382.91	348.03	34.88	10.978	
6,400.00	4,463.55	6,802.96	4,845.37	52.60	53.82	-175.71	-175.71	-2,166.68	672.71	382.90	346.53	36.37	10.527	
6,500.00	4,462.97	6,902.96	4,844.80	55.05	56.26	-175.71	-175.71	-2,236.50	744.29	382.90	345.03	37.88	10.110	
6,600.00	4,462.40	7,002.96	4,844.22	57.51	58.71	-175.72	-175.72	-2,306.32	815.88	382.90	343.51	39.39	9.721	
6,700.00	4,461.83	7,102.96	4,843.65	59.99	61.17	-175.73	-175.73	-2,376.14	887.47	382.89	341.99	40.91	9.360	
6,800.00	4,461.25	7,202.96	4,843.08	62.47	63.65	-175.74	-175.74	-2,445.96	959.06	382.89	340.46	42.43	9.024	
6,900.00	4,460.68	7,302.96	4,842.51	64.97	66.13	-175.75	-175.75	-2,515.78	1,030.65	382.89	338.92	43.96	8.709	
7,000.00	4,460.11	7,402.96	4,841.93	67.47	68.63	-175.75	-175.75	-2,585.60	1,102.23	382.88	337.38	45.50	8.415	
7,100.00	4,459.53	7,502.96	4,841.36	69.98	71.13	-175.76	-175.76	-2,655.42	1,173.82	382.88	335.83	47.04	8.139	
7,200.00	4,458.96	7,602.96	4,840.79	72.50	73.64	-175.77	-175.77	-2,725.24	1,245.41	382.87	334.28	48.59	7.880	
7,300.00	4,458.39	7,702.96	4,840.21	75.03	76.16	-175.78	-175.78	-2,795.06	1,317.00	382.87	332.73	50.14	7.636	
7,400.00	4,457.82	7,802.96	4,839.64	77.55	78.68	-175.79	-175.79	-2,864.88	1,388.59	382.87	331.17	51.69	7.407	
7,500.00	4,457.24	7,902.96	4,839.07	80.09	81.21	-175.80	-175.80	-2,934.70	1,460.17	382.86	329.61	53.25	7.190	
7,600.00	4,456.67	8,002.96	4,838.50	82.63	83.74	-175.80	-175.80	-3,004.52	1,531.76	382.86	328.05	54.81	6.985	
7,700.00	4,456.10	8,102.96	4,837.92	85.17	86.28	-175.81	-175.81	-3,074.34	1,603.35	382.86	326.49	56.37	6.792	
7,800.00	4,455.52	8,202.96	4,837.35	87.72	88.82	-175.82	-175.82	-3,144.16	1,674.94	382.85	324.92	57.94	6.608	
7,900.00	4,454.95	8,302.96	4,836.78	90.27	91.36	-175.83	-175.83	-3,213.98	1,746.52	382.85	323.35	59.50	6.434	
8,000.00	4,454.38	8,402.96	4,836.20	92.82	93.91	-175.84	-175.84	-3,283.80	1,818.11	382.85	321.77	61.07	6.269	
8,100.00	4,453.80	8,502.96	4,835.63	95.38	96.46	-175.84	-175.84	-3,353.62	1,889.70	382.84	320.20	62.64	6.112	
8,200.00	4,453.23	8,602.96	4,835.06	97.94	99.01	-175.85	-175.85	-3,423.44	1,961.29	382.84	318.63	64.21	5.962	
8,300.00	4,452.66	8,702.96	4,834.49	100.50	101.57	-175.86	-175.86	-3,493.26	2,032.88	382.83	317.05	65.79	5.819	
8,400.00	4,452.08	8,802.96	4,833.91	103.06	104.13	-175.87	-175.87	-3,563.08	2,104.46	382.83	315.47	67.36	5.683	
8,500.00	4,451.51	8,902.96	4,833.34	105.63	106.69	-175.88	-175.88	-3,632.90	2,176.05	382.83	313.89	68.94	5.553	
8,600.00	4,450.94	9,002.96	4,832.77	108.19	109.25	-175.88	-175.88	-3,702.72	2,247.64	382.82	312.31	70.51	5.429	
8,700.00	4,450.36	9,102.96	4,832.19	110.76	111.82	-175.89	-175.89	-3,772.54	2,319.23	382.82	310.73	72.09	5.310	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 108H - Original Drilling - APD												Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM												Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Minimum	Separation	Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Separation (ft)		
8,800.00	4,449.79	9,202.96	4,831.62	113.33	114.39	175.90	-3,842.36	2,390.82	382.82	309.15	73.67	5.196	
8,900.00	4,449.22	9,302.96	4,831.05	115.90	116.96	175.91	-3,912.18	2,462.40	382.81	307.56	75.25	5.087	
9,000.00	4,448.64	9,402.96	4,830.48	118.48	119.53	175.92	-3,982.00	2,533.99	382.81	305.98	76.83	4.982	
9,100.00	4,448.07	9,502.96	4,829.90	121.05	122.10	175.92	-4,051.82	2,605.58	382.81	304.39	78.41	4.882	
9,200.00	4,447.50	9,602.96	4,829.33	123.63	124.67	175.93	-4,121.64	2,677.17	382.80	302.81	80.00	4.785	
9,300.00	4,446.93	9,702.96	4,828.76	126.21	127.25	175.94	-4,191.46	2,748.76	382.80	301.22	81.58	4.692	
9,400.00	4,446.35	9,802.96	4,828.18	128.79	129.82	175.95	-4,261.28	2,820.34	382.80	299.63	83.16	4.603	
9,500.00	4,445.78	9,902.96	4,827.61	131.37	132.40	175.96	-4,331.10	2,891.93	382.79	298.05	84.75	4.517	
9,600.00	4,445.21	10,002.96	4,827.04	133.95	134.98	175.96	-4,400.92	2,963.52	382.79	296.46	86.33	4.434	
9,700.00	4,444.63	10,102.96	4,826.47	136.53	137.56	175.97	-4,470.74	3,035.11	382.79	294.87	87.91	4.354	
9,800.00	4,444.06	10,202.96	4,825.89	139.11	140.14	175.98	-4,540.56	3,106.70	382.78	293.28	89.50	4.277	
9,900.00	4,443.49	10,302.96	4,825.32	141.69	142.72	175.99	-4,610.38	3,178.28	382.78	291.69	91.09	4.202	
10,000.00	4,442.91	10,402.96	4,824.75	144.28	145.30	176.00	-4,680.20	3,249.87	382.77	290.10	92.67	4.130	
10,100.00	4,442.34	10,502.96	4,824.17	146.86	147.89	176.00	-4,750.02	3,321.46	382.77	288.51	94.26	4.061	
10,200.00	4,441.77	10,602.96	4,823.60	149.45	150.47	176.01	-4,819.84	3,393.05	382.77	286.92	95.84	3.994	
10,300.00	4,441.19	10,702.96	4,823.03	152.04	153.06	176.02	-4,889.66	3,464.63	382.76	285.33	97.43	3.929	
10,400.00	4,440.62	10,802.96	4,822.46	154.62	155.64	176.03	-4,959.48	3,536.22	382.76	283.74	99.02	3.866	
10,500.00	4,440.05	10,902.96	4,821.88	157.21	158.23	176.04	-5,029.30	3,607.81	382.76	282.15	100.61	3.805	
10,600.00	4,439.47	11,002.96	4,821.31	159.80	160.81	176.04	-5,099.12	3,679.40	382.75	280.56	102.19	3.745	
10,700.00	4,438.90	11,102.96	4,820.74	162.39	163.40	176.05	-5,168.94	3,750.99	382.75	278.97	103.78	3.688	
10,800.00	4,438.33	11,202.96	4,820.17	164.98	165.99	176.06	-5,238.76	3,822.57	382.75	277.38	105.37	3.632	
10,900.00	4,437.76	11,302.96	4,819.59	167.57	168.58	176.07	-5,308.58	3,894.16	382.74	275.79	106.96	3.579	
11,000.00	4,437.18	11,402.96	4,819.02	170.16	171.17	176.08	-5,378.40	3,965.75	382.74	274.20	108.54	3.526	
11,100.00	4,436.61	11,502.96	4,818.45	172.75	173.76	176.09	-5,448.22	4,037.34	382.74	272.61	110.13	3.475	
11,200.00	4,436.04	11,602.96	4,817.87	175.34	176.35	176.09	-5,518.04	4,108.93	382.73	271.01	111.72	3.426	
11,300.00	4,435.46	11,702.96	4,817.30	177.93	178.94	176.10	-5,587.86	4,180.51	382.73	269.42	113.31	3.378	
11,382.00	4,434.99	11,756.94	4,816.99	180.05	180.33	176.11	-5,625.55	4,219.16	383.75	269.31	114.44	3.353	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 113H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Measured Depth (ft)	Reference Vertical Depth (ft)	Offset Measured Depth (ft)	Offset Vertical Depth (ft)	Semi Major Axis Reference (ft)	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	Offset Wellbore Centre +E/-W (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
0.00	0.00	0.00	0.00	0.00	0.00	75.11	5.10	19.17	19.83					
100.00	100.00	100.00	100.00	0.31	0.15	75.11	5.10	19.17	19.83	19.37	0.46	42.885		
200.00	200.00	200.00	200.00	0.67	0.51	75.11	5.10	19.17	19.83	18.65	1.18	16.815		
300.00	300.00	300.00	300.00	1.03	0.87	75.11	5.10	19.17	19.83	17.93	1.90	10.458		
400.00	400.00	400.00	400.00	1.38	1.23	75.11	5.10	19.17	19.83	17.22	2.61	7.589 CC, ES		
500.00	499.96	499.61	499.59	1.73	1.57	-150.06	3.81	20.32	22.72	19.42	3.30	6.881		
600.00	599.69	598.77	598.61	2.07	1.91	-148.11	-0.04	23.76	31.41	27.42	3.99	7.881		
700.00	698.96	697.04	696.51	2.43	2.26	-146.44	-6.37	29.43	45.86	41.17	4.69	9.786		
800.00	797.55	793.98	792.74	2.81	2.61	-145.24	-15.05	37.21	66.01	60.61	5.40	12.218		
900.00	895.21	889.21	886.83	3.22	2.98	-144.36	-25.95	46.96	91.73	85.60	6.13	14.953		
964.03	957.17	949.11	945.75	3.50	3.22	-143.90	-33.99	54.16	111.07	104.45	6.62	16.785		
1,000.00	991.83	982.42	978.42	3.67	3.35	-143.77	-38.86	58.52	122.66	115.77	6.89	17.810		
1,100.00	1,088.18	1,074.23	1,068.02	4.14	3.74	-142.86	-53.74	71.85	156.01	148.38	7.64	20.433		
1,200.00	1,184.54	1,168.09	1,159.29	4.62	4.16	-141.84	-70.07	86.48	190.26	181.84	8.42	22.584		
1,300.00	1,280.90	1,262.00	1,250.60	5.12	4.59	-141.13	-86.42	101.11	224.55	215.32	9.23	24.319		
1,400.00	1,377.26	1,355.91	1,341.91	5.62	5.03	-140.61	-102.76	115.74	258.86	248.81	10.05	25.747		
1,500.00	1,473.62	1,449.82	1,433.22	6.13	5.47	-140.22	-119.10	130.38	293.19	282.31	10.88	26.937		
1,600.00	1,569.97	1,543.72	1,524.52	6.64	5.92	-139.90	-135.45	145.01	327.53	315.80	11.72	27.940		
1,700.00	1,666.33	1,637.63	1,615.83	7.16	6.37	-139.65	-151.79	159.65	361.87	349.30	12.57	28.795		
1,800.00	1,762.69	1,731.54	1,707.14	7.68	6.82	-139.44	-168.13	174.28	396.22	382.80	13.42	29.533		
1,900.00	1,859.05	1,825.44	1,798.45	8.20	7.28	-139.26	-184.48	188.92	430.57	416.30	14.27	30.173		
2,000.00	1,955.41	1,919.35	1,889.76	8.73	7.73	-139.11	-200.82	203.55	464.92	449.79	15.13	30.735		
2,100.00	2,051.76	2,013.26	1,981.07	9.25	8.19	-138.98	-217.16	218.19	499.28	483.29	15.99	31.231		
2,200.00	2,148.12	2,107.16	2,072.38	9.78	8.65	-138.86	-233.51	232.82	533.64	516.79	16.85	31.672		
2,300.00	2,244.48	2,201.07	2,163.69	10.31	9.11	-138.76	-249.85	247.46	568.00	550.28	17.71	32.066		
2,400.00	2,340.84	2,294.98	2,254.99	10.84	9.57	-138.68	-266.19	262.09	602.36	583.78	18.58	32.420		
2,500.00	2,437.20	2,388.89	2,346.30	11.37	10.04	-138.60	-282.54	276.72	636.72	617.28	19.45	32.740		
2,600.00	2,533.55	2,482.79	2,437.61	11.90	10.50	-138.53	-298.88	291.36	671.09	650.77	20.32	33.031		
2,700.00	2,629.91	2,576.70	2,528.92	12.43	10.96	-138.46	-315.22	305.99	705.45	684.27	21.19	33.296		
2,800.00	2,726.27	2,670.61	2,620.23	12.96	11.43	-138.40	-331.57	320.63	739.82	717.76	22.06	33.538		
2,900.00	2,822.63	2,764.51	2,711.54	13.49	11.89	-138.35	-347.91	335.26	774.18	751.25	22.93	33.761		
3,000.00	2,918.99	2,858.42	2,802.85	14.02	12.36	-138.30	-364.25	349.90	808.55	784.75	23.81	33.966		
3,100.00	3,015.34	2,952.33	2,894.15	14.55	12.82	-138.26	-380.60	364.53	842.92	818.24	24.68	34.155		
3,200.00	3,111.70	3,046.24	2,985.46	15.09	13.29	-138.22	-396.94	379.17	877.29	851.73	25.55	34.330		
3,300.00	3,208.06	3,140.14	3,076.77	15.62	13.76	-138.18	-413.28	393.80	911.65	885.22	26.43	34.493		
3,400.00	3,304.42	3,234.05	3,168.08	16.15	14.22	-138.14	-429.63	408.43	946.02	918.72	27.31	34.645		
3,500.00	3,400.77	3,327.96	3,259.39	16.69	14.69	-138.11	-445.97	423.07	980.39	952.21	28.18	34.787		
3,600.00	3,497.13	3,421.86	3,350.70	17.22	15.16	-138.08	-462.31	437.70	1,014.76	985.70	29.06	34.920		
3,700.00	3,593.49	3,515.77	3,442.01	17.76	15.63	-138.05	-478.66	452.34	1,049.13	1,019.19	29.94	35.044		
3,800.00	3,689.85	3,609.68	3,533.31	18.29	16.09	-138.03	-495.00	466.97	1,083.50	1,052.68	30.82	35.161		
3,900.00	3,786.21	3,703.58	3,624.62	18.82	16.56	-138.00	-511.34	481.61	1,117.87	1,086.17	31.69	35.270		
4,000.00	3,882.56	3,797.49	3,715.93	19.36	17.03	-137.98	-527.69	496.24	1,152.24	1,119.66	32.57	35.374		
4,061.50	3,941.82	3,855.24	3,772.09	19.69	17.32	-137.96	-537.74	505.24	1,173.38	1,140.26	33.11	35.435		
4,100.00	3,978.90	3,891.70	3,807.53	19.89	17.50	-137.96	-544.08	510.92	1,185.72	1,152.26	33.46	35.442		
4,150.00	4,026.79	3,939.71	3,854.22	20.15	17.74	-137.96	-552.44	518.41	1,199.02	1,165.11	33.91	35.359		
4,200.00	4,073.99	3,988.13	3,901.29	20.39	17.98	-92.84	-560.86	525.95	1,209.18	1,174.81	34.37	35.181		
4,250.00	4,120.13	4,036.53	3,948.35	20.61	18.22	-84.02	-569.29	533.49	1,216.16	1,181.33	34.83	34.916		
4,300.00	4,164.80	4,084.51	3,995.01	20.83	18.46	-78.08	-577.64	540.97	1,219.99	1,184.70	35.29	34.572		
4,350.00	4,207.64	4,131.67	4,040.86	21.02	18.70	-74.20	-585.84	548.32	1,220.73	1,184.99	35.74	34.155		
4,400.00	4,248.29	4,177.61	4,085.54	21.21	18.92	-71.83	-593.84	555.48	1,218.51	1,182.32	36.19	33.673		
4,450.00	4,286.40	4,221.96	4,128.65	21.38	19.15	-70.60	-601.56	562.39	1,213.48	1,176.86	36.63	33.129		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 113H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGDM													Offset Well Error:	0.00 ft
Measured Depth (ft)	Reference Vertical Depth (ft)	Offset Measured Depth (ft)	Offset Vertical Depth (ft)	Semi Major Axis Reference (ft)	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	Offset Wellbore Centre +E/-W (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
4,500.00	4,321.66	4,264.33	4,169.85	21.54	19.36	-70.27	-608.93	568.99	1,205.86	1,168.79	37.07	32.528		
4,550.00	4,353.77	4,304.37	4,208.78	21.69	19.56	-70.68	-615.90	575.23	1,195.88	1,158.36	37.52	31.874		
4,600.00	4,382.45	4,341.74	4,245.12	21.83	19.74	-71.68	-622.40	581.06	1,183.82	1,145.84	37.98	31.171		
4,650.00	4,407.48	4,359.76	4,262.64	21.96	19.83	-72.58	-625.54	583.87	1,170.11	1,131.81	38.29	30.556		
4,700.00	4,428.64	4,382.95	4,285.07	22.10	19.96	-74.08	-629.91	587.82	1,155.23	1,116.50	38.73	29.831		
4,750.00	4,445.75	4,399.99	4,301.38	22.24	20.05	-75.71	-633.55	591.15	1,139.60	1,100.44	39.16	29.101		
4,800.00	4,458.66	4,411.92	4,312.70	22.40	20.12	-77.41	-636.31	593.70	1,123.36	1,083.74	39.62	28.352		
4,850.00	4,467.28	4,425.20	4,325.20	22.59	20.21	-79.42	-639.59	596.74	1,106.73	1,066.54	40.19	27.540		
4,900.00	4,471.53	4,437.46	4,336.65	22.83	20.28	-81.60	-642.80	599.75	1,089.92	1,049.09	40.83	26.696		
4,926.41	4,471.99	4,449.99	4,348.24	22.98	20.36	-83.13	-646.27	603.00	1,081.09	1,039.81	41.28	26.190		
5,000.00	4,471.57	4,461.00	4,358.33	23.54	20.44	-83.70	-649.47	606.02	1,058.46	1,016.13	42.33	25.002		
5,100.00	4,471.00	4,489.74	4,384.24	24.65	20.65	-85.16	-658.50	614.57	1,034.48	990.34	44.13	23.439		
5,200.00	4,470.42	4,526.06	4,415.98	26.13	20.94	-86.95	-671.25	626.74	1,018.34	972.14	46.20	22.044		
5,300.00	4,469.85	4,572.89	4,455.06	27.86	21.34	-89.18	-689.84	644.62	1,009.78	961.29	48.49	20.824		
5,400.00	4,469.28	4,634.47	4,502.82	29.77	21.95	-91.90	-717.71	671.63	1,007.96	956.92	51.03	19.751		
5,404.45	4,469.25	4,637.64	4,505.15	29.86	21.98	-92.04	-719.25	673.13	1,008.01	956.86	51.15	19.705		
5,500.00	4,468.70	4,716.50	4,559.08	31.80	22.89	-95.12	-760.34	713.27	1,011.28	957.35	53.93	18.752		
5,504.45	4,468.68	4,720.73	4,561.73	31.89	22.94	-95.27	-762.70	715.58	1,011.51	957.44	54.07	18.708		
5,600.00	4,468.13	4,825.07	4,618.67	33.92	24.36	-98.51	-824.87	776.79	1,017.16	959.77	57.39	17.723		
5,604.45	4,468.11	4,830.59	4,621.21	34.02	24.45	-98.65	-828.36	780.23	1,017.43	959.86	57.56	17.675		
5,700.00	4,467.56	4,962.16	4,666.45	36.12	26.58	-101.22	-915.83	867.00	1,022.14	960.43	61.71	16.564		
5,704.45	4,467.53	4,968.82	4,667.94	36.22	26.70	-101.30	-920.43	871.58	1,022.28	960.35	61.92	16.508		
5,800.00	4,466.99	5,108.07	4,680.90	38.37	29.24	-102.07	-1,018.25	969.33	1,022.96	956.29	66.67	15.343		
5,822.61	4,466.86	5,130.68	4,680.78	38.89	29.68	-102.08	-1,034.22	985.34	1,022.72	955.11	67.61	15.126		
5,900.00	4,466.41	5,208.06	4,680.35	40.67	31.19	-102.09	-1,088.88	1,040.11	1,021.90	951.05	70.85	14.424		
5,922.61	4,466.28	5,230.67	4,680.23	41.19	31.64	-102.09	-1,104.85	1,056.11	1,021.66	949.84	71.81	14.226		
6,000.00	4,465.84	5,308.05	4,679.80	43.00	33.22	-102.10	-1,159.52	1,110.88	1,020.83	945.69	75.14	13.586		
6,022.61	4,465.71	5,330.66	4,679.68	43.53	33.69	-102.11	-1,175.48	1,126.89	1,020.59	944.46	76.13	13.406		
6,100.00	4,465.27	5,408.05	4,679.25	45.36	35.32	-102.12	-1,230.15	1,181.66	1,019.76	940.24	79.53	12.823		
6,122.61	4,465.14	5,430.65	4,679.13	45.90	35.81	-102.12	-1,246.12	1,197.66	1,019.52	938.99	80.54	12.659		
6,200.00	4,464.69	5,508.04	4,678.70	47.76	37.48	-102.13	-1,300.78	1,252.44	1,018.70	934.70	84.00	12.128		
6,222.60	4,464.56	5,530.64	4,678.58	48.30	37.98	-102.13	-1,316.75	1,268.43	1,018.46	933.43	85.02	11.979		
6,300.00	4,464.12	5,608.04	4,678.15	50.17	39.70	-102.15	-1,371.42	1,323.21	1,017.63	929.09	88.54	11.494		
6,322.60	4,463.99	5,630.64	4,678.03	50.72	40.21	-102.15	-1,387.38	1,339.21	1,017.39	927.81	89.58	11.358		
6,400.00	4,463.55	5,708.03	4,677.61	52.60	41.96	-102.16	-1,442.05	1,393.99	1,016.56	923.43	93.14	10.915		
6,422.60	4,463.42	5,730.63	4,677.48	53.15	42.47	-102.16	-1,458.02	1,409.98	1,016.32	922.14	94.18	10.791		
6,500.00	4,462.97	5,808.02	4,677.06	55.05	44.25	-102.17	-1,512.69	1,464.76	1,015.50	917.72	97.78	10.385		
6,522.60	4,462.84	5,830.62	4,676.93	55.61	44.78	-102.18	-1,528.65	1,480.76	1,015.26	916.42	98.84	10.272		
6,600.00	4,462.40	5,908.02	4,676.51	57.51	46.58	-102.19	-1,583.32	1,535.54	1,014.43	911.96	102.47	9.900		
6,622.60	4,462.27	5,930.61	4,676.38	58.07	47.11	-102.19	-1,599.28	1,551.53	1,014.19	910.65	103.54	9.795		
6,700.00	4,461.83	6,008.01	4,675.96	59.99	48.93	-102.20	-1,653.96	1,606.32	1,013.37	906.17	107.20	9.453		
6,722.60	4,461.70	6,030.60	4,675.83	60.55	49.46	-102.21	-1,669.92	1,622.31	1,013.12	904.85	108.27	9.357		
6,800.00	4,461.25	6,108.01	4,675.41	62.47	51.30	-102.22	-1,724.59	1,677.09	1,012.30	900.34	111.95	9.042		
6,822.59	4,461.12	6,130.60	4,675.29	63.04	51.84	-102.22	-1,740.55	1,693.08	1,012.06	899.02	113.04	8.953		
6,900.00	4,460.68	6,208.00	4,674.86	64.97	53.69	-102.23	-1,795.23	1,747.87	1,011.23	894.49	116.74	8.662		
6,922.59	4,460.55	6,230.59	4,674.74	65.53	54.24	-102.24	-1,811.18	1,763.86	1,010.99	893.17	117.83	8.580		
7,000.00	4,460.11	6,307.99	4,674.31	67.47	56.10	-102.25	-1,865.86	1,818.64	1,010.17	888.62	121.55	8.311		
7,022.59	4,459.98	6,330.58	4,674.19	68.04	56.65	-102.25	-1,881.82	1,834.63	1,009.93	887.29	122.64	8.235		
7,100.00	4,459.53	6,407.99	4,673.76	69.98	58.53	-102.26	-1,936.50	1,889.42	1,009.10	882.72	126.38	7.985		
7,122.59	4,459.41	6,430.57	4,673.64	70.55	59.08	-102.26	-1,952.45	1,905.41	1,008.86	881.38	127.47	7.914		
7,200.00	4,458.96	6,507.98	4,673.21	72.50	60.97	-102.28	-2,007.13	1,960.20	1,008.03	876.81	131.23	7.682		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 113H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Distance Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
7,222.59	4,458.83	6,530.57	4,673.09	73.07	61.52	-102.28	-2,023.08	1,976.18	1,007.79	875.47	132.33	7.616		
7,300.00	4,458.39	6,607.98	4,672.66	75.03	63.42	-102.29	-2,077.77	2,030.97	1,006.97	870.87	136.09	7.399		
7,322.58	4,458.26	6,630.56	4,672.54	75.60	63.98	-102.29	-2,093.72	2,046.96	1,006.73	869.53	137.20	7.338		
7,400.00	4,457.82	6,707.97	4,672.11	77.55	65.88	-102.31	-2,148.40	2,101.75	1,005.90	864.93	140.98	7.135		
7,422.58	4,457.69	6,730.55	4,671.99	78.13	66.44	-102.31	-2,164.35	2,117.73	1,005.66	863.58	142.08	7.078		
7,500.00	4,457.24	6,807.96	4,671.57	80.09	68.35	-102.32	-2,219.04	2,172.52	1,004.84	858.97	145.87	6.889		
7,522.58	4,457.11	6,830.54	4,671.44	80.66	68.91	-102.32	-2,234.98	2,188.51	1,004.60	857.62	146.98	6.835		
7,600.00	4,456.67	6,907.96	4,671.02	82.63	70.83	-102.33	-2,289.67	2,243.30	1,003.77	853.00	150.77	6.657		
7,622.58	4,456.54	6,930.53	4,670.89	83.20	71.39	-102.34	-2,305.62	2,259.28	1,003.53	851.65	151.88	6.607		
7,700.00	4,456.10	7,007.95	4,670.47	85.17	73.32	-102.35	-2,360.30	2,314.08	1,002.70	847.01	155.69	6.440		
7,722.58	4,455.97	7,030.53	4,670.34	85.75	73.88	-102.35	-2,376.25	2,330.05	1,002.46	845.66	156.80	6.393		
7,800.00	4,455.52	7,107.95	4,669.92	87.72	75.81	-102.36	-2,430.94	2,384.85	1,001.64	841.02	160.62	6.236		
7,822.57	4,455.39	7,130.52	4,669.79	88.29	76.37	-102.37	-2,446.88	2,400.83	1,001.40	839.67	161.73	6.192		
7,900.00	4,454.95	7,207.94	4,669.37	90.27	78.31	-102.38	-2,501.57	2,455.63	1,000.57	835.02	165.55	6.044		
7,922.57	4,454.82	7,230.51	4,669.24	90.84	78.87	-102.38	-2,517.52	2,471.60	1,000.33	833.67	166.67	6.002		
8,000.00	4,454.38	7,307.93	4,668.82	92.82	80.81	-102.39	-2,572.21	2,526.40	999.51	829.01	170.49	5.862		
8,022.57	4,454.25	7,330.50	4,668.70	93.40	81.38	-102.40	-2,588.15	2,542.38	999.27	827.66	171.61	5.823		
8,100.00	4,453.80	7,407.93	4,668.27	95.38	83.32	-102.41	-2,642.84	2,597.18	998.44	823.00	175.44	5.691		
8,122.57	4,453.67	7,430.49	4,668.15	95.95	83.89	-102.41	-2,658.78	2,613.15	998.20	821.64	176.56	5.654		
8,200.00	4,453.23	7,507.92	4,667.72	97.94	85.84	-102.42	-2,713.48	2,667.96	997.38	816.98	180.40	5.529		
8,222.57	4,453.10	7,530.49	4,667.60	98.51	86.41	-102.43	-2,729.42	2,683.93	997.14	815.62	181.52	5.493		
8,300.00	4,452.66	7,607.92	4,667.17	100.50	88.36	-102.44	-2,784.11	2,738.73	996.31	810.95	185.36	5.375		
8,322.56	4,452.53	7,630.48	4,667.05	101.08	88.93	-102.44	-2,800.05	2,754.70	996.07	809.59	186.48	5.341		
8,400.00	4,452.08	7,707.91	4,666.62	103.06	90.88	-102.45	-2,854.75	2,809.51	995.25	804.92	190.33	5.229		
8,422.56	4,451.95	7,730.47	4,666.50	103.64	91.45	-102.46	-2,870.68	2,825.48	995.01	803.56	191.45	5.197		
8,500.00	4,451.51	7,807.90	4,666.07	105.63	93.40	-102.47	-2,925.38	2,880.28	994.18	798.88	195.30	5.091		
8,522.56	4,451.38	7,830.46	4,665.95	106.20	93.97	-102.47	-2,941.32	2,896.25	993.94	797.52	196.42	5.060		
8,600.00	4,450.94	7,907.90	4,665.52	108.19	95.93	-102.48	-2,996.02	2,951.06	993.12	792.84	200.27	4.959		
8,622.56	4,450.81	7,930.45	4,665.40	108.77	96.50	-102.49	-3,011.95	2,967.03	992.88	791.48	201.40	4.930		
8,700.00	4,450.36	8,007.89	4,664.98	110.76	98.47	-102.50	-3,066.65	3,021.84	992.05	786.80	205.25	4.833		
8,722.56	4,450.23	8,030.45	4,664.85	111.34	99.04	-102.50	-3,082.58	3,037.80	991.81	785.43	206.38	4.806		
8,800.00	4,449.79	8,107.89	4,664.43	113.33	101.00	-102.51	-3,137.29	3,092.61	990.99	780.75	210.24	4.714		
8,822.56	4,449.66	8,130.44	4,664.30	113.91	101.57	-102.52	-3,153.22	3,108.58	990.75	779.38	211.36	4.687		
8,900.00	4,449.22	8,207.88	4,663.88	115.90	103.54	-102.53	-3,207.92	3,163.39	989.92	774.70	215.23	4.599		
8,922.55	4,449.09	8,230.43	4,663.75	116.49	104.11	-102.53	-3,223.85	3,179.35	989.68	773.33	216.35	4.574		
9,000.00	4,448.64	8,307.87	4,663.33	118.48	106.08	-102.54	-3,278.56	3,234.16	988.86	768.64	220.22	4.490		
9,022.55	4,448.52	8,330.42	4,663.20	119.06	106.65	-102.55	-3,294.48	3,250.12	988.62	767.27	221.34	4.466		
9,100.00	4,448.07	8,407.87	4,662.78	121.05	108.62	-102.56	-3,349.19	3,304.94	987.79	762.58	225.21	4.386		
9,122.55	4,447.94	8,430.42	4,662.66	121.63	109.19	-102.56	-3,365.12	3,320.90	987.55	761.21	226.34	4.363		
9,200.00	4,447.50	8,507.86	4,662.23	123.63	111.16	-102.57	-3,419.83	3,375.72	986.73	756.52	230.21	4.286		
9,222.55	4,447.37	8,530.41	4,662.11	124.21	111.74	-102.58	-3,435.75	3,391.67	986.49	755.15	231.33	4.264		
9,300.00	4,446.93	8,607.86	4,661.68	126.21	113.71	-102.59	-3,490.46	3,446.49	985.66	750.46	235.20	4.191		
9,322.55	4,446.80	8,630.40	4,661.56	126.79	114.29	-102.59	-3,506.38	3,462.45	985.42	749.09	236.33	4.170		
9,400.00	4,446.35	8,707.85	4,661.13	128.79	116.26	-102.60	-3,561.09	3,517.27	984.60	744.39	240.21	4.099		
9,422.54	4,446.22	8,730.39	4,661.01	129.37	116.83	-102.61	-3,577.02	3,533.22	984.36	743.02	241.33	4.079		
9,500.00	4,445.78	8,807.84	4,660.58	131.37	118.81	-102.62	-3,631.73	3,588.04	983.53	738.32	245.21	4.011		
9,522.54	4,445.65	8,830.38	4,660.46	131.95	119.38	-102.62	-3,647.65	3,604.00	983.29	736.96	246.34	3.992		
9,600.00	4,445.21	8,907.84	4,660.03	133.95	121.36	-102.63	-3,702.36	3,658.82	982.47	732.25	250.21	3.927		
9,622.54	4,445.08	8,930.38	4,659.91	134.53	121.94	-102.64	-3,718.29	3,674.77	982.23	730.89	251.34	3.908		
9,700.00	4,444.63	9,007.83	4,659.48	136.53	123.91	-102.65	-3,773.00	3,729.60	981.40	726.18	255.22	3.845		
9,722.54	4,444.50	9,030.37	4,659.36	137.11	124.49	-102.65	-3,788.92	3,745.55	981.16	724.82	256.35	3.827		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 113H - Original Drilling - APD												Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM												Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		Minimum Separation		Separation Factor		Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
9,800.00	4,444.06	9,107.83	4,658.94	139.11	126.47	-102.67	-3,843.63	3,800.37	980.34	720.11	260.23	3.767	
9,822.54	4,443.93	9,130.36	4,658.81	139.69	127.04	-102.67	-3,859.55	3,816.32	980.10	718.74	261.36	3.750	
9,900.00	4,443.49	9,207.82	4,658.39	141.69	129.02	-102.68	-3,914.27	3,871.15	979.28	714.04	265.24	3.692	
9,922.53	4,443.36	9,230.35	4,658.26	142.28	129.60	-102.68	-3,930.19	3,887.10	979.04	712.67	266.37	3.676	
10,000.00	4,442.91	9,307.81	4,657.84	144.28	131.58	-102.70	-3,984.90	3,941.92	978.21	707.96	270.25	3.620	
10,022.53	4,442.78	9,330.34	4,657.71	144.86	132.16	-102.70	-4,000.82	3,957.87	977.97	706.59	271.38	3.604	
10,100.00	4,442.34	9,407.81	4,657.29	146.86	134.14	-102.71	-4,055.54	4,012.70	977.15	701.89	275.26	3.550	
10,122.53	4,442.21	9,430.34	4,657.16	147.45	134.71	-102.72	-4,071.45	4,028.65	976.91	700.52	276.39	3.535	
10,200.00	4,441.77	9,507.80	4,656.74	149.45	136.70	-102.73	-4,126.17	4,083.48	976.08	695.81	280.28	3.483	
10,222.53	4,441.64	9,530.33	4,656.61	150.03	137.27	-102.73	-4,142.09	4,099.42	975.84	694.44	281.40	3.468	
10,300.00	4,441.19	9,607.79	4,656.19	152.04	139.26	-102.74	-4,196.81	4,154.25	975.02	689.73	285.29	3.418	
10,322.53	4,441.06	9,630.32	4,656.07	152.62	139.83	-102.75	-4,212.72	4,170.20	974.78	688.36	286.42	3.403	
10,400.00	4,440.62	9,707.79	4,655.64	154.62	141.82	-102.76	-4,267.44	4,225.03	973.96	683.65	290.31	3.355	
10,422.53	4,440.49	9,730.31	4,655.52	155.20	142.39	-102.76	-4,283.35	4,240.97	973.72	682.28	291.44	3.341	
10,500.00	4,440.05	9,807.78	4,655.09	157.21	144.38	-102.77	-4,338.08	4,295.80	972.89	677.57	295.32	3.294	
10,522.52	4,439.92	9,830.31	4,654.97	157.79	144.96	-102.78	-4,353.99	4,311.74	972.65	676.20	296.45	3.281	
10,600.00	4,439.47	9,907.78	4,654.54	159.80	146.94	-102.79	-4,408.71	4,366.58	971.83	671.49	300.34	3.236	
10,622.52	4,439.35	9,930.30	4,654.42	160.38	147.52	-102.79	-4,424.62	4,382.52	971.59	670.12	301.47	3.223	
10,700.00	4,438.90	10,007.77	4,653.99	162.39	149.51	-102.81	-4,479.35	4,437.36	970.76	665.41	305.36	3.179	
10,722.52	4,438.77	10,030.29	4,653.87	162.97	150.08	-102.81	-4,495.25	4,453.29	970.52	664.04	306.49	3.167	
10,800.00	4,438.33	10,107.76	4,653.44	164.98	152.07	-102.82	-4,549.98	4,508.13	969.70	659.33	310.38	3.124	
10,822.52	4,438.20	10,130.28	4,653.32	165.56	152.65	-102.83	-4,565.89	4,524.07	969.46	657.96	311.51	3.112	
10,900.00	4,437.76	10,207.76	4,652.89	167.57	154.63	-102.84	-4,620.61	4,578.91	968.64	653.24	315.39	3.071	
10,922.52	4,437.63	10,230.27	4,652.77	168.15	155.21	-102.84	-4,636.52	4,594.84	968.40	651.87	316.52	3.059	
11,000.00	4,437.18	10,307.75	4,652.35	170.16	157.20	-102.85	-4,691.25	4,649.68	967.57	647.16	320.41	3.020	
11,022.51	4,437.05	10,330.27	4,652.22	170.74	157.78	-102.86	-4,707.15	4,665.62	967.33	645.79	321.54	3.008	
11,100.00	4,436.61	10,407.75	4,651.80	172.75	159.77	-102.87	-4,761.88	4,720.46	966.51	641.08	325.43	2.970	
11,122.51	4,436.48	10,430.26	4,651.67	173.33	160.35	-102.87	-4,777.79	4,736.39	966.27	639.71	326.56	2.959	
11,200.00	4,436.04	10,507.74	4,651.25	175.34	162.33	-102.88	-4,832.52	4,791.24	965.45	634.99	330.45	2.922	
11,222.51	4,435.91	10,530.25	4,651.12	175.92	162.91	-102.89	-4,848.42	4,807.17	965.21	633.62	331.59	2.911	
11,300.00	4,435.46	10,607.73	4,650.70	177.93	164.90	-102.90	-4,903.15	4,862.01	964.38	628.91	335.48	2.875	
11,318.46	4,435.36	10,626.19	4,650.60	178.41	165.38	-102.90	-4,916.19	4,875.08	964.19	627.78	336.40	2.866	
11,382.00	4,434.99	10,689.73	4,650.25	180.05	167.01	-102.91	-4,961.08	4,920.05	963.51	623.92	339.59	2.837 SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 133H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Minimum	Separation	Warning		
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Separation (ft)			
0.00	0.00	0.00	0.00	0.00	0.00	-105.08	-15.65	-58.09	60.16					
100.00	100.00	100.00	100.00	0.31	0.31	-105.08	-15.65	-58.09	60.16	59.54	0.62	97.568		
200.00	200.00	200.00	200.00	0.67	0.67	-105.08	-15.65	-58.09	60.16	58.82	1.33	45.112		
300.00	300.00	300.00	300.00	1.03	1.03	-105.08	-15.65	-58.09	60.16	58.11	2.05	29.339		
400.00	400.00	400.00	400.00	1.38	1.38	-105.08	-15.65	-58.09	60.16	57.39	2.77	21.738		
500.00	499.96	497.58	497.55	1.73	1.72	29.16	-16.82	-59.80	60.06	56.62	3.45	17.418		
600.00	599.69	595.18	594.94	2.07	2.06	30.43	-20.34	-64.94	59.81	55.69	4.11	14.536		
700.00	698.96	692.80	692.00	2.43	2.40	32.57	-26.19	-73.51	59.44	54.65	4.79	12.404		
800.00	797.55	790.45	788.56	2.81	2.77	35.59	-34.37	-85.48	59.08	53.59	5.49	10.764		
900.00	895.21	888.61	884.94	3.22	3.16	39.58	-44.87	-100.85	58.78	52.56	6.22	9.447		
964.03	957.17	952.51	947.52	3.50	3.43	43.43	-52.17	-111.53	57.60	50.86	6.74	8.545		
1,000.00	991.83	988.37	982.64	3.67	3.58	46.04	-56.26	-117.53	56.66	49.62	7.04	8.046		
1,100.00	1,088.18	1,088.08	1,080.27	4.14	4.00	53.70	-67.65	-134.20	54.73	46.80	7.93	6.905		
1,197.44	1,182.07	1,185.23	1,175.41	4.61	4.43	61.55	-78.74	-150.44	53.84	45.00	8.85	6.086		
1,200.00	1,184.54	1,187.78	1,177.91	4.62	4.44	61.76	-79.03	-150.87	53.84	44.96	8.87	6.068		
1,231.67	1,215.06	1,219.36	1,208.83	4.78	4.58	64.35	-82.64	-156.15	53.78	44.60	9.18	5.857 CC		
1,300.00	1,280.90	1,287.48	1,275.55	5.12	4.88	69.93	-90.42	-167.54	54.04	44.18	9.86	5.480 ES		
1,400.00	1,377.26	1,387.19	1,373.19	5.62	5.32	77.87	-101.81	-184.20	55.32	44.45	10.87	5.089		
1,500.00	1,473.62	1,486.89	1,470.82	6.13	5.77	85.32	-113.20	-200.87	57.62	45.74	11.87	4.852		
1,600.00	1,569.97	1,586.59	1,568.46	6.64	6.22	92.10	-124.58	-217.54	60.81	47.95	12.86	4.729		
1,700.00	1,666.33	1,686.29	1,666.10	7.16	6.68	98.13	-135.97	-234.21	64.76	50.95	13.82	4.688 SF		
1,800.00	1,762.69	1,786.00	1,763.74	7.68	7.13	103.42	-147.36	-250.88	69.35	54.61	14.74	4.704		
1,900.00	1,859.05	1,885.70	1,861.38	8.20	7.59	108.02	-158.74	-267.55	74.45	58.81	15.65	4.758		
2,000.00	1,955.41	1,985.40	1,959.01	8.73	8.05	112.01	-170.13	-284.22	79.98	63.45	16.53	4.838		
2,100.00	2,051.76	2,085.11	2,056.65	9.25	8.51	115.47	-181.52	-300.88	85.83	68.44	17.40	4.933		
2,200.00	2,148.12	2,184.81	2,154.29	9.78	8.97	118.48	-192.90	-317.55	91.97	73.71	18.26	5.038		
2,300.00	2,244.48	2,284.51	2,251.93	10.31	9.43	121.11	-204.29	-334.22	98.32	79.22	19.10	5.147		
2,400.00	2,340.84	2,384.21	2,349.56	10.84	9.89	123.42	-215.68	-350.89	104.85	84.91	19.95	5.257		
2,500.00	2,437.20	2,483.92	2,447.20	11.37	10.35	125.45	-227.06	-367.56	111.54	90.75	20.78	5.366		
2,600.00	2,533.55	2,583.62	2,544.84	11.90	10.81	127.25	-238.45	-384.23	118.34	96.72	21.62	5.474		
2,700.00	2,629.91	2,683.32	2,642.48	12.43	11.27	128.86	-249.84	-400.90	125.26	102.80	22.45	5.578		
2,800.00	2,726.27	2,783.02	2,740.12	12.96	11.73	130.30	-261.23	-417.56	132.26	108.97	23.29	5.680		
2,900.00	2,822.63	2,882.73	2,837.75	13.49	12.20	131.59	-272.61	-434.23	139.33	115.21	24.12	5.777		
3,000.00	2,918.99	2,982.43	2,935.39	14.02	12.66	132.75	-284.00	-450.90	146.47	121.52	24.95	5.871		
3,100.00	3,015.34	3,082.13	3,033.03	14.55	13.12	133.81	-295.39	-467.57	153.66	127.88	25.78	5.960		
3,200.00	3,111.70	3,181.84	3,130.67	15.09	13.59	134.77	-306.77	-484.24	160.90	134.29	26.61	6.046		
3,300.00	3,208.06	3,281.54	3,228.31	15.62	14.05	135.65	-318.16	-500.91	168.18	140.74	27.44	6.129		
3,400.00	3,304.42	3,381.24	3,325.94	16.15	14.51	136.46	-329.55	-517.58	175.50	147.22	28.27	6.207		
3,500.00	3,400.77	3,480.94	3,423.58	16.69	14.98	137.20	-340.93	-534.25	182.85	153.74	29.10	6.282		
3,600.00	3,497.13	3,580.65	3,521.22	17.22	15.44	137.88	-352.32	-550.91	190.22	160.29	29.94	6.354		
3,700.00	3,593.49	3,680.35	3,618.86	17.76	15.91	138.52	-363.71	-567.58	197.62	166.86	30.77	6.423		
3,800.00	3,689.85	3,780.05	3,716.49	18.29	16.37	139.10	-375.09	-584.25	205.05	173.45	31.60	6.489		
3,900.00	3,786.21	3,879.76	3,814.13	18.82	16.84	139.65	-386.48	-600.92	212.49	180.06	32.43	6.552		
4,000.00	3,882.56	3,979.46	3,911.77	19.36	17.30	140.16	-397.87	-617.59	219.95	186.69	33.27	6.612		
4,061.50	3,941.82	4,035.87	3,967.00	19.69	17.56	140.37	-404.07	-627.25	224.81	191.06	33.75	6.661		
4,100.00	3,978.90	4,066.02	3,996.39	19.89	17.71	154.72	-406.16	-633.59	230.03	195.98	34.05	6.756		
4,150.00	4,026.79	4,100.00	4,029.28	20.15	17.87	170.60	-407.06	-642.08	241.36	206.97	34.39	7.017		
4,200.00	4,073.99	4,138.09	4,065.67	20.39	18.06	-178.19	-406.25	-653.26	257.90	222.99	34.91	7.388		
4,250.00	4,120.13	4,168.81	4,094.55	20.61	18.21	-170.16	-404.18	-663.53	279.86	244.60	35.26	7.938		
4,300.00	4,164.80	4,200.00	4,123.33	20.83	18.37	-164.65	-400.81	-675.05	307.14	271.47	35.67	8.610		
4,350.00	4,207.64	4,217.21	4,138.95	21.02	18.45	-158.88	-398.41	-681.87	339.19	303.58	35.62	9.523		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 133H - Original Drilling - APD													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
4,400.00	4,248.29	4,234.86	4,154.74	21.21	18.54	-153.64	-395.54	-689.20	375.56	339.91	35.65	10.535		
4,450.00	4,286.40	4,250.00	4,168.11	21.38	18.62	-147.94	-392.75	-695.74	415.48	379.79	35.69	11.642		
4,500.00	4,321.66	4,250.00	4,168.11	21.54	18.62	-138.45	-392.75	-695.74	458.31	423.06	35.25	13.000		
4,550.00	4,353.77	4,264.95	4,181.13	21.69	18.69	-130.58	-389.72	-702.44	502.96	467.42	35.54	14.151		
4,600.00	4,382.45	4,268.61	4,184.29	21.83	18.71	-118.09	-388.93	-704.11	549.16	513.64	35.52	15.461		
4,650.00	4,407.48	4,269.70	4,185.23	21.96	18.72	-102.94	-388.69	-704.61	596.19	560.67	35.52	16.783		
4,700.00	4,428.64	4,268.54	4,184.23	22.10	18.71	-86.76	-388.95	-704.08	643.56	608.00	35.56	18.097		
4,750.00	4,445.75	4,265.42	4,181.53	22.24	18.70	-72.02	-389.62	-702.65	690.81	655.18	35.63	19.386		
4,800.00	4,458.66	4,250.00	4,168.11	22.40	18.62	-58.65	-392.75	-695.74	737.73	702.29	35.44	20.816		
4,850.00	4,467.28	4,250.00	4,168.11	22.59	18.62	-50.91	-392.75	-695.74	783.48	747.72	35.76	21.907		
4,900.00	4,471.53	4,250.00	4,168.11	22.83	18.62	-45.15	-392.75	-695.74	828.22	792.10	36.12	22.928		
4,926.41	4,471.99	4,250.00	4,168.11	22.98	18.62	-42.73	-392.75	-695.74	851.38	815.06	36.32	23.441		
5,000.00	4,471.57	4,229.79	4,150.24	23.54	18.52	-41.47	-396.40	-687.06	915.55	879.14	36.41	25.147		
5,100.00	4,471.00	4,200.00	4,123.33	24.65	18.37	-39.74	-400.81	-675.05	1,004.65	968.20	36.45	27.561		
5,200.00	4,470.42	4,200.00	4,123.33	26.13	18.37	-39.74	-400.81	-675.05	1,094.57	1,057.57	37.00	29.583		
5,300.00	4,469.85	4,200.00	4,123.33	27.86	18.37	-39.74	-400.81	-675.05	1,186.10	1,148.67	37.43	31.686		
5,400.00	4,469.28	4,178.82	4,103.85	29.77	18.26	-38.60	-403.24	-667.11	1,278.32	1,240.83	37.49	34.098		
5,500.00	4,468.70	4,169.20	4,094.91	31.80	18.21	-38.10	-404.15	-663.67	1,371.51	1,333.83	37.68	36.400		
5,600.00	4,468.13	4,150.00	4,076.93	33.92	18.12	-37.15	-405.59	-657.11	1,465.54	1,427.82	37.72	38.853		
5,700.00	4,467.56	4,150.00	4,076.93	36.12	18.12	-37.15	-405.59	-657.11	1,559.89	1,521.93	37.96	41.088		
5,800.00	4,466.99	4,150.00	4,076.93	38.37	18.12	-37.15	-405.59	-657.11	1,654.91	1,616.74	38.17	43.355		
5,900.00	4,466.41	4,150.00	4,076.93	40.67	18.12	-37.15	-405.59	-657.11	1,750.49	1,712.14	38.35	45.646		
6,000.00	4,465.84	4,150.00	4,076.93	43.00	18.12	-37.15	-405.59	-657.11	1,846.53	1,808.03	38.50	47.958		
6,100.00	4,465.27	4,127.05	4,055.19	45.36	18.00	-36.09	-406.68	-649.85	1,942.36	1,903.91	38.44	50.523		
6,200.00	4,464.69	4,121.87	4,050.24	47.76	17.98	-35.86	-406.83	-648.29	2,038.84	2,000.31	38.53	52.911		
6,300.00	4,464.12	4,100.00	4,029.28	50.17	17.87	-34.92	-407.06	-642.08	2,135.93	2,097.45	38.48	55.504		
6,400.00	4,463.55	4,100.00	4,029.28	52.60	17.87	-34.92	-407.06	-642.08	2,232.77	2,194.17	38.60	57.850		
6,500.00	4,462.97	4,100.00	4,029.28	55.05	17.87	-34.92	-407.06	-642.08	2,329.87	2,291.17	38.70	60.205		
6,600.00	4,462.40	4,100.00	4,029.28	57.51	17.87	-34.92	-407.06	-642.08	2,427.21	2,388.42	38.79	62.568		
6,700.00	4,461.83	4,100.00	4,029.28	59.99	17.87	-34.92	-407.06	-642.08	2,524.76	2,485.88	38.88	64.937		
6,800.00	4,461.25	4,100.00	4,029.28	62.47	17.87	-34.92	-407.06	-642.08	2,622.49	2,583.53	38.96	67.312		
6,900.00	4,460.68	4,100.00	4,029.28	64.97	17.87	-34.92	-407.06	-642.08	2,720.39	2,681.36	39.03	69.691		
7,000.00	4,460.11	4,100.00	4,029.28	67.47	17.87	-34.92	-407.06	-642.08	2,818.44	2,779.33	39.10	72.074		
7,100.00	4,459.53	4,100.00	4,029.28	69.98	17.87	-34.92	-407.06	-642.08	2,916.62	2,877.44	39.17	74.459		
7,200.00	4,458.96	4,100.00	4,029.28	72.50	17.87	-34.92	-407.06	-642.08	3,014.91	2,975.68	39.23	76.845		
7,300.00	4,458.39	4,100.00	4,029.28	75.03	17.87	-34.92	-407.06	-642.08	3,113.32	3,074.03	39.29	79.233		
7,400.00	4,457.82	4,100.00	4,029.28	77.55	17.87	-34.92	-407.06	-642.08	3,211.82	3,172.47	39.35	81.620		
7,500.00	4,457.24	4,078.43	4,008.45	80.09	17.77	-34.06	-406.67	-636.53	3,309.92	3,270.63	39.29	84.235		
7,600.00	4,456.67	4,076.26	4,006.34	82.63	17.76	-33.97	-406.59	-636.00	3,408.50	3,369.16	39.34	86.645		
7,700.00	4,456.10	4,074.19	4,004.33	85.17	17.75	-33.89	-406.52	-635.50	3,507.14	3,467.76	39.38	89.053		
7,800.00	4,455.52	4,072.22	4,002.42	87.72	17.74	-33.82	-406.44	-635.03	3,605.85	3,566.43	39.43	91.459		
7,900.00	4,454.95	4,050.00	3,980.80	90.27	17.63	-33.00	-405.20	-630.08	3,705.06	3,665.69	39.37	94.105		
8,000.00	4,454.38	4,050.00	3,980.80	92.82	17.63	-33.00	-405.20	-630.08	3,803.82	3,764.39	39.42	96.484		
8,100.00	4,453.80	4,050.00	3,980.80	95.38	17.63	-33.00	-405.20	-630.08	3,902.64	3,863.16	39.48	98.862		
8,200.00	4,453.23	4,050.00	3,980.80	97.94	17.63	-33.00	-405.20	-630.08	4,001.51	3,961.99	39.53	101.237		
8,300.00	4,452.66	4,050.00	3,980.80	100.50	17.63	-33.00	-405.20	-630.08	4,100.45	4,060.87	39.58	103.609		
8,400.00	4,452.08	4,050.00	3,980.80	103.06	17.63	-33.00	-405.20	-630.08	4,199.43	4,159.80	39.63	105.978		
8,500.00	4,451.51	4,050.00	3,980.80	105.63	17.63	-33.00	-405.20	-630.08	4,298.46	4,258.78	39.67	108.344		
8,600.00	4,450.94	4,050.00	3,980.80	108.19	17.63	-33.00	-405.20	-630.08	4,397.53	4,357.81	39.72	110.706		
8,700.00	4,450.36	4,050.00	3,980.80	110.76	17.63	-33.00	-405.20	-630.08	4,496.65	4,456.88	39.77	113.065		
8,800.00	4,449.79	4,050.00	3,980.80	113.33	17.63	-33.00	-405.20	-630.08	4,595.80	4,555.98	39.82	115.419		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC
Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Escrito P01 2310 Federal COM 133H - Original Drilling - APD													Offset Site Error: 0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error: 0.00 ft
Measured Depth (ft)	Vertical Reference Depth (ft)	Measured Depth (ft)	Vertical Offset Depth (ft)	Semi Major Axis Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Distance Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
8,900.00	4,449.22	4,050.00	3,980.80	115.90	17.63	-33.00	-405.20	-630.08	4,694.99	4,655.12	39.87	117.769	
9,000.00	4,448.64	4,050.00	3,980.80	118.48	17.63	-33.00	-405.20	-630.08	4,794.21	4,754.30	39.91	120.114	
9,100.00	4,448.07	4,050.00	3,980.80	121.05	17.63	-33.00	-405.20	-630.08	4,893.47	4,853.50	39.96	122.455	
9,200.00	4,447.50	4,050.00	3,980.80	123.63	17.63	-33.00	-405.20	-630.08	4,992.75	4,952.74	40.01	124.791	
9,300.00	4,446.93	4,050.00	3,980.80	126.21	17.63	-33.00	-405.20	-630.08	5,092.06	5,052.01	40.06	127.122	
9,400.00	4,446.35	4,050.00	3,980.80	128.79	17.63	-33.00	-405.20	-630.08	5,191.40	5,151.30	40.10	129.448	
9,500.00	4,445.78	4,050.00	3,980.80	131.37	17.63	-33.00	-405.20	-630.08	5,290.76	5,250.61	40.15	131.768	
9,600.00	4,445.21	4,050.00	3,980.80	133.95	17.63	-33.00	-405.20	-630.08	5,390.15	5,349.95	40.20	134.083	
9,700.00	4,444.63	4,050.00	3,980.80	136.53	17.63	-33.00	-405.20	-630.08	5,489.56	5,449.31	40.25	136.392	
9,800.00	4,444.06	4,050.00	3,980.80	139.11	17.63	-33.00	-405.20	-630.08	5,588.99	5,548.69	40.30	138.695	
9,900.00	4,443.49	4,050.00	3,980.80	141.69	17.63	-33.00	-405.20	-630.08	5,688.44	5,648.09	40.35	140.993	
10,000.00	4,442.91	4,050.00	3,980.80	144.28	17.63	-33.00	-405.20	-630.08	5,787.91	5,747.52	40.39	143.284	
10,100.00	4,442.34	4,050.00	3,980.80	146.86	17.63	-33.00	-405.20	-630.08	5,887.40	5,846.95	40.44	145.569	
10,200.00	4,441.77	4,050.00	3,980.80	149.45	17.63	-33.00	-405.20	-630.08	5,986.90	5,946.41	40.49	147.848	
10,300.00	4,441.19	4,050.00	3,980.80	152.04	17.63	-33.00	-405.20	-630.08	6,086.42	6,045.88	40.54	150.120	
10,400.00	4,440.62	4,050.00	3,980.80	154.62	17.63	-33.00	-405.20	-630.08	6,185.96	6,145.36	40.59	152.386	
10,500.00	4,440.05	4,050.00	3,980.80	157.21	17.63	-33.00	-405.20	-630.08	6,285.51	6,244.86	40.64	154.645	
10,600.00	4,439.47	4,050.00	3,980.80	159.80	17.63	-33.00	-405.20	-630.08	6,385.07	6,344.38	40.70	156.897	
10,700.00	4,438.90	4,050.00	3,980.80	162.39	17.63	-33.00	-405.20	-630.08	6,484.65	6,443.90	40.75	159.143	
10,800.00	4,438.33	4,050.00	3,980.80	164.98	17.63	-33.00	-405.20	-630.08	6,584.24	6,543.44	40.80	161.381	
10,900.00	4,437.76	4,050.00	3,980.80	167.57	17.63	-33.00	-405.20	-630.08	6,683.85	6,642.99	40.85	163.613	
11,000.00	4,437.18	4,050.00	3,980.80	170.16	17.63	-33.00	-405.20	-630.08	6,783.46	6,742.56	40.90	165.837	
11,100.00	4,436.61	4,050.00	3,980.80	172.75	17.63	-33.00	-405.20	-630.08	6,883.09	6,842.13	40.96	168.055	
11,200.00	4,436.04	4,050.00	3,980.80	175.34	17.63	-33.00	-405.20	-630.08	6,982.72	6,941.71	41.01	170.264	
11,300.00	4,435.46	4,050.00	3,980.80	177.93	17.63	-33.00	-405.20	-630.08	7,082.37	7,041.31	41.07	172.467	
11,382.00	4,434.99	4,050.00	3,980.80	180.05	17.63	-33.00	-405.20	-630.08	7,164.09	7,122.98	41.11	174.268	



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Witty 5 - OH - OH													Offset Site Error:	0.00 ft
Survey Program: 224-INCLINOMETER													Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference	Semi Major Axis Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Distance Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
0.00	0.00	0.00	0.00	0.00	0.00	168.39	-1,251.33	257.00	1,277.78					
100.00	100.00	71.00	71.00	0.31	2.16	168.39	-1,251.33	257.00	1,277.45	1,274.98	2.46	518.319		
200.00	200.00	171.00	171.00	0.67	5.19	168.39	-1,251.33	257.00	1,277.45	1,271.59	5.86	218.000		
300.00	300.00	271.00	271.00	1.03	8.23	168.39	-1,251.33	257.00	1,277.45	1,268.19	9.26	138.025		
400.00	400.00	371.00	371.00	1.38	11.27	168.39	-1,251.33	257.00	1,277.45	1,264.80	12.65	100.980		
500.00	499.96	470.96	470.96	1.73	14.30	-57.91	-1,251.33	257.00	1,276.17	1,260.14	16.03	79.605		
600.00	599.69	568.99	568.99	2.07	17.28	-58.27	-1,250.81	257.00	1,271.86	1,252.51	19.35	65.726		
700.00	698.96	666.28	666.27	2.43	20.23	-58.86	-1,251.03	257.00	1,265.80	1,243.13	22.66	55.855		
800.00	797.55	768.60	768.55	2.81	23.34	-59.73	-1,251.33	257.00	1,257.46	1,231.32	26.15	48.095		
900.00	895.21	866.26	866.21	3.22	26.31	-60.83	-1,251.33	257.00	1,246.65	1,217.13	29.51	42.244		
964.03	957.17	928.22	928.17	3.50	28.19	-61.66	-1,251.33	257.00	1,238.67	1,207.00	31.67	39.118		
1,000.00	991.83	962.88	962.83	3.67	29.24	-62.04	-1,251.33	257.00	1,234.00	1,201.12	32.88	37.535		
1,100.00	1,088.18	1,056.80	1,056.74	4.14	32.09	-63.10	-1,250.31	257.00	1,220.34	1,184.16	36.18	33.733		
1,200.00	1,184.54	1,149.46	1,149.39	4.62	34.91	-64.15	-1,250.65	257.00	1,208.46	1,169.01	39.46	30.628		
1,300.00	1,280.90	1,252.07	1,251.90	5.12	38.02	-65.33	-1,251.33	257.00	1,197.35	1,154.30	43.05	27.813		
1,400.00	1,377.26	1,348.43	1,348.26	5.62	40.95	-66.47	-1,251.33	257.00	1,186.09	1,139.62	46.47	25.526		
1,500.00	1,473.62	1,443.98	1,443.79	6.13	43.85	-67.64	-1,250.11	257.00	1,174.18	1,124.32	49.87	23.547		
1,600.00	1,569.97	1,533.63	1,533.43	6.64	46.57	-68.73	-1,250.45	257.00	1,164.29	1,111.20	53.09	21.929		
1,700.00	1,666.33	1,637.63	1,637.33	7.16	49.73	-70.00	-1,251.33	257.00	1,155.36	1,098.60	56.77	20.353		
1,800.00	1,762.69	1,733.99	1,733.69	7.68	52.66	-71.22	-1,251.33	257.00	1,146.18	1,085.97	60.21	19.036		
1,900.00	1,859.05	1,830.35	1,830.05	8.20	55.58	-72.45	-1,251.33	257.00	1,137.56	1,073.90	63.66	17.869		
2,000.00	1,955.41	1,923.90	1,923.57	8.73	58.42	-73.70	-1,249.77	257.00	1,128.12	1,061.09	67.03	16.830		
2,100.00	2,051.76	2,015.60	2,015.27	9.25	61.21	-74.89	-1,250.25	257.00	1,121.11	1,050.76	70.35	15.937		
2,200.00	2,148.12	2,107.49	2,107.14	9.78	64.00	-76.09	-1,251.17	257.00	1,115.08	1,041.41	73.67	15.136		
2,300.00	2,244.48	2,215.98	2,215.48	10.31	67.29	-77.54	-1,251.33	257.00	1,108.87	1,031.36	77.51	14.307		
2,400.00	2,340.84	2,305.55	2,305.03	10.84	70.01	-78.78	-1,250.59	257.00	1,102.60	1,021.83	80.77	13.652		
2,500.00	2,437.20	2,408.80	2,408.20	11.37	73.15	-80.17	-1,251.33	257.00	1,098.16	1,013.71	84.44	13.004		
2,600.00	2,533.55	2,505.15	2,504.55	11.90	76.08	-81.50	-1,251.33	257.00	1,093.74	1,005.83	87.91	12.441		
2,700.00	2,629.91	2,601.51	2,600.91	12.43	79.00	-82.84	-1,251.33	257.00	1,089.97	998.58	91.38	11.927		
2,800.00	2,726.27	2,694.45	2,693.82	12.96	81.82	-84.19	-1,249.86	257.00	1,085.68	990.93	94.75	11.458		
2,900.00	2,822.63	2,786.83	2,786.19	13.49	84.63	-85.47	-1,250.46	257.00	1,083.70	985.61	98.10	11.047		
3,000.00	2,918.99	2,890.75	2,889.99	14.02	87.79	-86.91	-1,251.33	257.00	1,082.53	980.73	101.80	10.634		
3,100.00	3,015.34	2,987.11	2,986.34	14.55	90.71	-88.27	-1,251.33	257.00	1,081.36	976.10	105.26	10.273		
3,200.00	3,111.70	3,083.47	3,082.70	15.09	93.64	-89.64	-1,251.33	257.00	1,080.85	972.13	108.73	9.941		
3,234.40	3,144.84	3,116.53	3,115.74	15.27	94.64	-90.16	-1,249.70	257.00	1,079.66	969.75	109.91	9.823		
3,300.00	3,208.06	3,177.32	3,176.52	15.62	96.49	-91.02	-1,249.81	257.00	1,079.93	967.82	112.11	9.633		
3,400.00	3,304.42	3,270.13	3,269.32	16.15	99.31	-92.32	-1,250.34	257.00	1,081.16	965.70	115.46	9.364		
3,500.00	3,400.77	3,372.66	3,371.77	16.69	102.42	-93.73	-1,251.33	257.00	1,083.30	964.20	119.10	9.096		
3,600.00	3,497.13	3,469.02	3,468.13	17.22	105.35	-95.09	-1,251.33	257.00	1,085.43	962.88	122.55	8.857		
3,700.00	3,593.49	3,565.38	3,564.49	17.76	108.27	-96.44	-1,251.33	257.00	1,088.22	962.22	125.99	8.637		
3,800.00	3,689.85	3,660.46	3,659.56	18.29	111.16	-97.81	-1,250.32	257.00	1,091.03	961.63	129.39	8.432		
3,900.00	3,786.21	3,754.67	3,753.76	18.82	114.02	-99.10	-1,250.66	257.00	1,095.33	962.57	132.76	8.250		
4,000.00	3,882.56	3,854.50	3,853.56	19.36	117.05	-100.45	-1,251.33	257.00	1,100.44	964.14	136.30	8.074		
4,061.50	3,941.82	3,913.76	3,912.82	19.69	118.85	-101.26	-1,251.33	257.00	1,103.65	965.25	138.40	7.974		
4,100.00	3,978.90	3,950.84	3,949.90	19.89	119.98	-87.40	-1,251.33	257.00	1,104.44	964.72	139.72	7.905		
4,150.00	4,026.79	3,998.72	3,997.79	20.15	121.43	-71.88	-1,251.33	257.00	1,101.63	960.22	141.41	7.790		
4,200.00	4,073.99	4,045.92	4,044.99	20.39	122.87	-60.47	-1,251.33	257.00	1,094.54	951.46	143.08	7.650		
4,250.00	4,120.13	4,092.06	4,091.13	20.61	124.27	-52.73	-1,251.33	257.00	1,083.25	938.55	144.70	7.486		
4,300.00	4,164.80	4,136.46	4,135.52	20.83	125.62	-47.73	-1,250.78	257.00	1,067.61	921.36	146.25	7.300		
4,350.00	4,207.64	4,178.93	4,178.00	21.02	126.91	-44.66	-1,250.82	257.00	1,048.37	900.64	147.73	7.096		
4,400.00	4,248.29	4,219.27	4,218.34	21.21	128.13	-43.05	-1,250.88	257.00	1,025.44	876.30	149.14	6.876		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Witty 5 - OH - OH												Offset Site Error:	0.00 ft
Survey Program: 224-INCLINOMETER				Rule Assigned:					Offset Well Error:		0.00 ft		
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance			Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)		+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)		Separation Factor
4,450.00	4,286.40	4,257.14	4,256.20	21.38	129.28	-42.61	-1,250.97	257.00	999.04	848.58	150.46	6.640	
4,500.00	4,321.66	4,292.22	4,291.28	21.54	130.35	-43.21	-1,251.07	257.00	969.44	817.75	151.69	6.391	
4,550.00	4,353.77	4,324.21	4,323.27	21.69	131.32	-44.81	-1,251.18	257.00	936.92	784.11	152.82	6.131	
4,600.00	4,382.45	4,352.85	4,351.91	21.83	132.19	-47.43	-1,251.29	257.00	901.81	747.97	153.84	5.862	
4,650.00	4,407.48	4,379.43	4,378.48	21.96	132.99	-51.26	-1,251.33	257.00	864.42	709.61	154.81	5.584	
4,700.00	4,428.64	4,400.59	4,399.64	22.10	133.64	-56.19	-1,251.33	257.00	825.14	669.53	155.61	5.303	
4,750.00	4,445.75	4,417.70	4,416.75	22.24	134.16	-62.35	-1,251.33	257.00	784.39	628.08	156.30	5.018	
4,800.00	4,458.66	4,430.62	4,429.66	22.40	134.55	-69.64	-1,251.33	257.00	742.56	585.67	156.89	4.733	
4,850.00	4,467.28	4,439.23	4,438.28	22.59	134.81	-77.76	-1,251.33	257.00	700.10	542.73	157.38	4.449	
4,900.00	4,471.53	4,443.48	4,442.53	22.83	134.94	-86.17	-1,251.33	257.00	657.44	499.67	157.76	4.167	
4,926.41	4,471.99	4,443.94	4,442.99	22.98	134.95	-90.53	-1,251.33	257.00	634.97	477.03	157.94	4.020	
5,000.00	4,471.57	4,443.52	4,442.57	23.54	134.94	-90.45	-1,251.33	257.00	573.84	415.39	158.45	3.622	
5,100.00	4,471.00	4,442.95	4,442.00	24.65	134.92	-90.36	-1,251.33	257.00	496.22	336.78	159.44	3.112	
5,200.00	4,470.42	4,442.38	4,441.42	26.13	134.91	-90.26	-1,251.33	257.00	428.00	267.12	160.87	2.660	
5,300.00	4,469.85	4,441.80	4,440.85	27.86	134.89	-90.16	-1,251.33	257.00	374.33	211.62	162.72	2.301	
5,400.00	4,469.28	4,441.23	4,440.28	29.77	134.87	-90.06	-1,251.33	257.00	342.15	177.62	164.53	2.080	
5,465.28	4,468.90	4,440.86	4,439.90	31.09	134.86	-90.00	-1,251.33	257.00	335.87	170.57	165.30	2.032 CC, ES, SF	
5,500.00	4,468.70	4,440.66	4,439.70	31.80	134.85	-89.97	-1,251.33	257.00	337.66	172.17	165.48	2.040	
5,600.00	4,468.13	4,440.08	4,439.13	33.92	134.84	-89.87	-1,251.33	257.00	361.88	196.71	165.16	2.191	
5,700.00	4,467.56	4,439.51	4,438.56	36.12	134.82	-89.77	-1,251.33	257.00	409.75	245.70	164.05	2.498	
5,800.00	4,466.99	4,438.94	4,437.99	38.37	134.80	-89.67	-1,251.33	257.00	474.17	311.38	162.79	2.913	
5,900.00	4,466.41	4,438.36	4,437.41	40.67	134.78	-89.57	-1,251.33	257.00	549.34	387.66	161.68	3.398	
6,000.00	4,465.84	4,437.79	4,436.84	43.00	134.77	-89.48	-1,251.33	257.00	631.44	470.64	160.80	3.927	
6,100.00	4,465.27	4,437.22	4,436.27	45.36	134.75	-89.38	-1,251.33	257.00	718.09	557.98	160.12	4.485	
6,200.00	4,464.69	4,436.65	4,435.69	47.76	134.73	-89.28	-1,251.33	257.00	807.83	648.25	159.59	5.062	
6,300.00	4,464.12	4,436.07	4,435.12	50.17	134.71	-89.18	-1,251.33	257.00	899.74	740.57	159.17	5.653	
6,400.00	4,463.55	4,435.50	4,434.55	52.60	134.70	-89.09	-1,251.33	257.00	993.21	834.37	158.84	6.253	
6,500.00	4,462.97	4,434.93	4,433.97	55.05	134.68	-88.99	-1,251.33	257.00	1,087.85	929.27	158.58	6.860	
6,600.00	4,462.40	4,434.35	4,433.40	57.51	134.66	-88.89	-1,251.33	257.00	1,183.36	1,025.00	158.37	7.472	
6,700.00	4,461.83	4,433.78	4,432.83	59.99	134.64	-88.79	-1,251.33	257.00	1,279.56	1,121.37	158.19	8.089	
6,800.00	4,461.25	4,433.21	4,432.25	62.47	134.63	-88.70	-1,251.33	257.00	1,376.30	1,218.26	158.04	8.708	
6,900.00	4,460.68	4,432.63	4,431.68	64.97	134.61	-88.60	-1,251.33	257.00	1,473.48	1,315.56	157.92	9.331	
7,000.00	4,460.11	4,432.06	4,431.11	67.47	134.59	-88.50	-1,251.33	257.00	1,571.01	1,413.20	157.81	9.955	
7,100.00	4,459.53	4,431.49	4,430.53	69.98	134.57	-88.40	-1,251.33	257.00	1,668.84	1,511.11	157.73	10.581	
7,200.00	4,458.96	4,430.91	4,429.96	72.50	134.56	-88.30	-1,251.33	257.00	1,766.90	1,609.25	157.65	11.208	
7,300.00	4,458.39	4,430.34	4,429.39	75.03	134.54	-88.21	-1,251.33	257.00	1,865.17	1,707.59	157.58	11.836	
7,400.00	4,457.82	4,429.77	4,428.82	77.55	134.52	-88.11	-1,251.33	257.00	1,963.62	1,806.09	157.53	12.465	
7,500.00	4,457.24	4,429.19	4,428.24	80.09	134.50	-88.01	-1,251.33	257.00	2,062.22	1,904.74	157.48	13.095	
7,600.00	4,456.67	4,428.62	4,427.67	82.63	134.49	-87.91	-1,251.33	257.00	2,160.94	2,003.50	157.44	13.726	
7,700.00	4,456.10	4,428.05	4,427.10	85.17	134.47	-87.82	-1,251.33	257.00	2,259.78	2,102.38	157.40	14.357	
7,800.00	4,455.52	4,427.47	4,426.52	87.72	134.45	-87.72	-1,251.33	257.00	2,358.71	2,201.34	157.37	14.988	
7,900.00	4,454.95	4,426.90	4,425.95	90.27	134.44	-87.62	-1,251.33	257.00	2,457.73	2,300.39	157.34	15.620	
8,000.00	4,454.38	4,426.33	4,425.38	92.82	134.42	-87.52	-1,251.33	257.00	2,556.83	2,399.51	157.32	16.252	
8,100.00	4,453.80	4,425.76	4,424.80	95.38	134.40	-87.43	-1,251.33	257.00	2,655.99	2,498.69	157.30	16.885	
8,200.00	4,453.23	4,425.18	4,424.23	97.94	134.38	-87.33	-1,251.33	257.00	2,755.22	2,597.93	157.29	17.517	
8,300.00	4,452.66	4,424.61	4,423.66	100.50	134.37	-87.23	-1,251.33	257.00	2,854.50	2,697.23	157.27	18.150	
8,400.00	4,452.08	4,424.04	4,423.08	103.06	134.35	-87.13	-1,251.33	257.00	2,953.82	2,796.56	157.26	18.783	
8,500.00	4,451.51	4,423.46	4,422.51	105.63	134.33	-87.04	-1,251.33	257.00	3,053.20	2,895.94	157.25	19.416	
8,600.00	4,450.94	4,422.89	4,421.94	108.19	134.31	-86.94	-1,251.33	257.00	3,152.61	2,995.36	157.25	20.049	
8,700.00	4,450.36	4,422.32	4,421.36	110.76	134.30	-86.84	-1,251.33	257.00	3,252.05	3,094.81	157.24	20.682	
8,800.00	4,449.79	4,421.74	4,420.79	113.33	134.28	-86.74	-1,251.33	257.00	3,351.53	3,194.29	157.24	21.314	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report



Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Offset Design: P01 2310 Pad - Witty 5 - OH - OH													Offset Site Error:	0.00 ft
Survey Program: 224-INCLINOMETER													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis		Offset Wellbore Centre			Rule Assigned:				Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
8,900.00	4,449.22	4,421.17	4,420.22	115.90	134.26	-86.65	-1,251.33	257.00	3,451.04	3,293.80	157.24	21.947		
9,000.00	4,448.64	4,420.60	4,419.64	118.48	134.24	-86.55	-1,251.33	257.00	3,550.58	3,393.33	157.24	22.580		
9,100.00	4,448.07	4,420.02	4,419.07	121.05	134.23	-86.45	-1,251.33	257.00	3,650.14	3,492.89	157.25	23.213		
9,200.00	4,447.50	4,419.45	4,418.50	123.63	134.21	-86.35	-1,251.33	257.00	3,749.73	3,592.47	157.25	23.845		
9,300.00	4,446.93	4,418.88	4,417.93	126.21	134.19	-86.26	-1,251.33	257.00	3,849.33	3,692.07	157.26	24.477		
9,400.00	4,446.35	4,418.30	4,417.35	128.79	134.17	-86.16	-1,251.33	257.00	3,948.96	3,791.69	157.27	25.110		
9,500.00	4,445.78	4,417.73	4,416.78	131.37	134.16	-86.06	-1,251.33	257.00	4,048.60	3,891.33	157.28	25.742		
9,600.00	4,445.21	4,417.16	4,416.21	133.95	134.14	-85.96	-1,251.33	257.00	4,148.27	3,990.98	157.29	26.374		
9,700.00	4,444.63	4,416.59	4,415.63	136.53	134.12	-85.87	-1,251.33	257.00	4,247.94	4,090.64	157.30	27.005		
9,800.00	4,444.06	4,416.01	4,415.06	139.11	134.10	-85.77	-1,251.33	257.00	4,347.64	4,190.32	157.31	27.637		
9,900.00	4,443.49	4,415.44	4,414.49	141.69	134.09	-85.67	-1,251.33	257.00	4,447.34	4,290.02	157.33	28.268		
10,000.00	4,442.91	4,414.87	4,413.91	144.28	134.07	-85.58	-1,251.33	257.00	4,547.06	4,389.72	157.34	28.899		
10,100.00	4,442.34	4,414.29	4,413.34	146.86	134.05	-85.48	-1,251.33	257.00	4,646.79	4,489.43	157.36	29.530		
10,200.00	4,441.77	4,413.72	4,412.77	149.45	134.03	-85.38	-1,251.33	257.00	4,746.54	4,589.16	157.38	30.160		
10,300.00	4,441.19	4,413.15	4,412.19	152.04	134.02	-85.28	-1,251.33	257.00	4,846.29	4,688.89	157.40	30.791		
10,400.00	4,440.62	4,412.57	4,411.62	154.62	134.00	-85.19	-1,251.33	257.00	4,946.05	4,788.64	157.41	31.421		
10,500.00	4,440.05	4,412.00	4,411.05	157.21	133.98	-85.09	-1,251.33	257.00	5,045.82	4,888.39	157.44	32.050		
10,600.00	4,439.47	4,411.43	4,410.47	159.80	133.97	-84.99	-1,251.33	257.00	5,145.60	4,988.15	157.46	32.680		
10,700.00	4,438.90	4,410.85	4,409.90	162.39	133.95	-84.90	-1,251.33	257.00	5,245.39	5,087.91	157.48	33.309		
10,800.00	4,438.33	4,410.28	4,409.33	164.98	133.93	-84.80	-1,251.33	257.00	5,345.19	5,187.69	157.50	33.937		
10,900.00	4,437.76	4,409.71	4,408.75	167.57	133.91	-84.70	-1,251.33	257.00	5,444.99	5,287.47	157.53	34.566		
11,000.00	4,437.18	4,409.13	4,408.18	170.16	133.90	-84.60	-1,251.33	257.00	5,544.81	5,387.26	157.55	35.194		
11,100.00	4,436.61	4,408.56	4,407.61	172.75	133.88	-84.51	-1,251.33	257.00	5,644.62	5,487.05	157.58	35.821		
11,200.00	4,436.04	4,407.99	4,407.04	175.34	133.86	-84.41	-1,251.33	257.00	5,744.45	5,586.85	157.60	36.449		
11,300.00	4,435.46	4,407.41	4,406.46	177.93	133.84	-84.31	-1,251.33	257.00	5,844.28	5,686.65	157.63	37.076		
11,382.00	4,434.99	4,406.94	4,405.99	180.05	133.83	-84.23	-1,251.33	257.00	5,926.15	5,768.49	157.65	37.590		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report




Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Reference Depths are relative to GL 6857' & RKB14' @ 6871.00ft
 Offset Depths are relative to Offset Datum
 Central Meridian is -107.8333334

Coordinates are relative to: Escrito P01 2310 Federal COM 134H - Slot 5
 Coordinate System is US State Plane 1983, New Mexico Western Zone
 Grid Convergence at Surface is: -0.01°

Ladder Plot

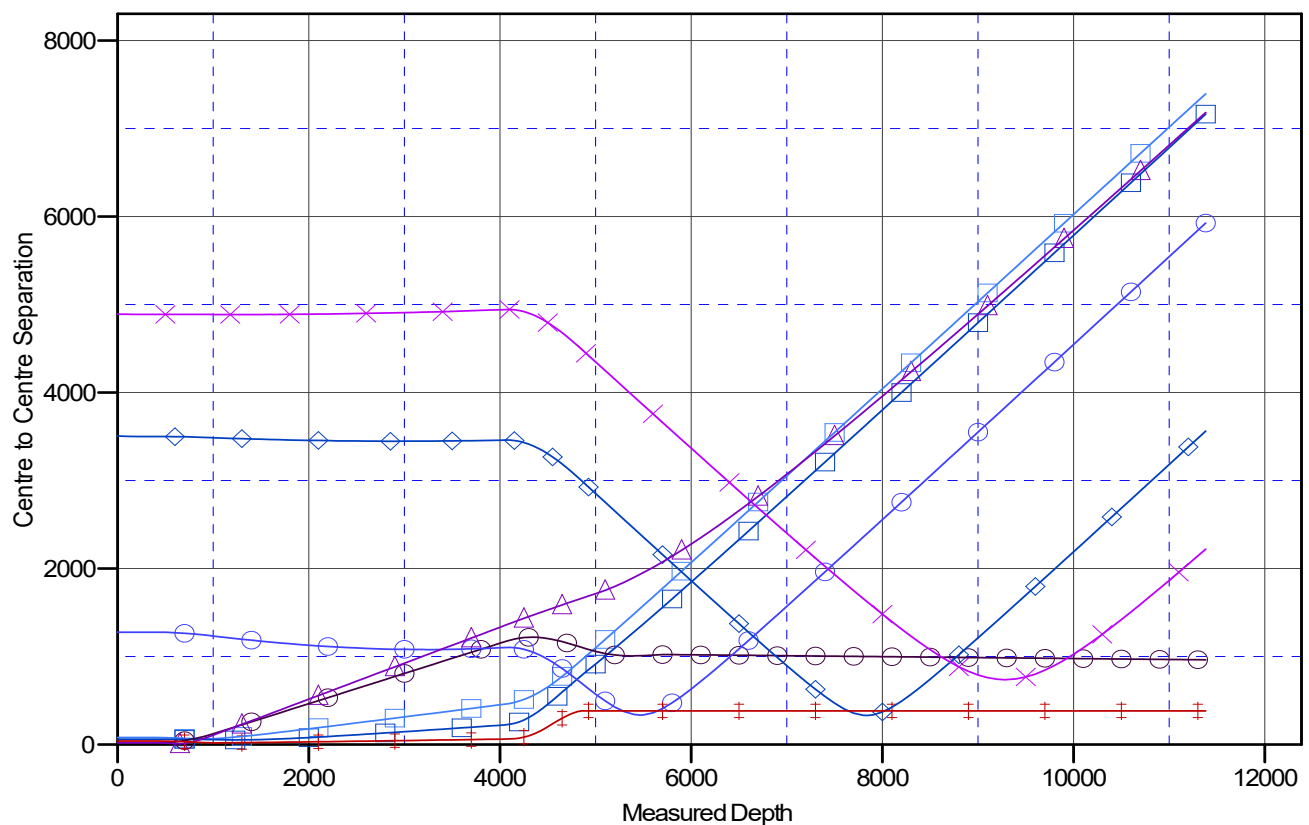

LEGEND

- Escrito P01 2310 Federal COM 108H Original Drilling, APDVO
- Escrito P01 2310 Federal COM 133H Original Drilling, APDVO
- Escrito P01 2310 Federal COM 113H Original Drilling, APDVO
- Well 5, OH, OHVO
- December Dream 002, OH, OHVO
- December Dream 003, OH, OHVO
- Escrito P01 2310 137H, Original Drilling, APDVO
- Escrito P01 2310 Federal COM 108H Original Drilling, APDVO

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Lonestar Consulting, LLC

Anticollision Report




Company:	DJR Operating	Local Co-ordinate Reference:	Well Escrito P01 2310 Federal COM 134H - Slot 5
Project:	Ponderosa Unit	TVD Reference:	GL 6857' & RKB14' @ 6871.00ft
Reference Site:	P01 2310 Pad	MD Reference:	GL 6857' & RKB14' @ 6871.00ft
Site Error:	0.00 ft	North Reference:	True
Reference Well:	Escrito P01 2310 Federal COM 134H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 ft	Output errors are at	2.00 sigma
Reference Wellbore	Original Drilling	Database:	Grand Junction
Reference Design:	APD	Offset TVD Reference:	Offset Datum

Reference Depths are relative to GL 6857' & RKB14' @ 6871.00ft
 Offset Depths are relative to Offset Datum
 Central Meridian is -107.8333334

Coordinates are relative to: Escrito P01 2310 Federal COM 134H - Slot 5
 Coordinate System is US State Plane 1983, New Mexico Western Zone
 Grid Convergence at Surface is: -0.01°

Separation Factor Plot

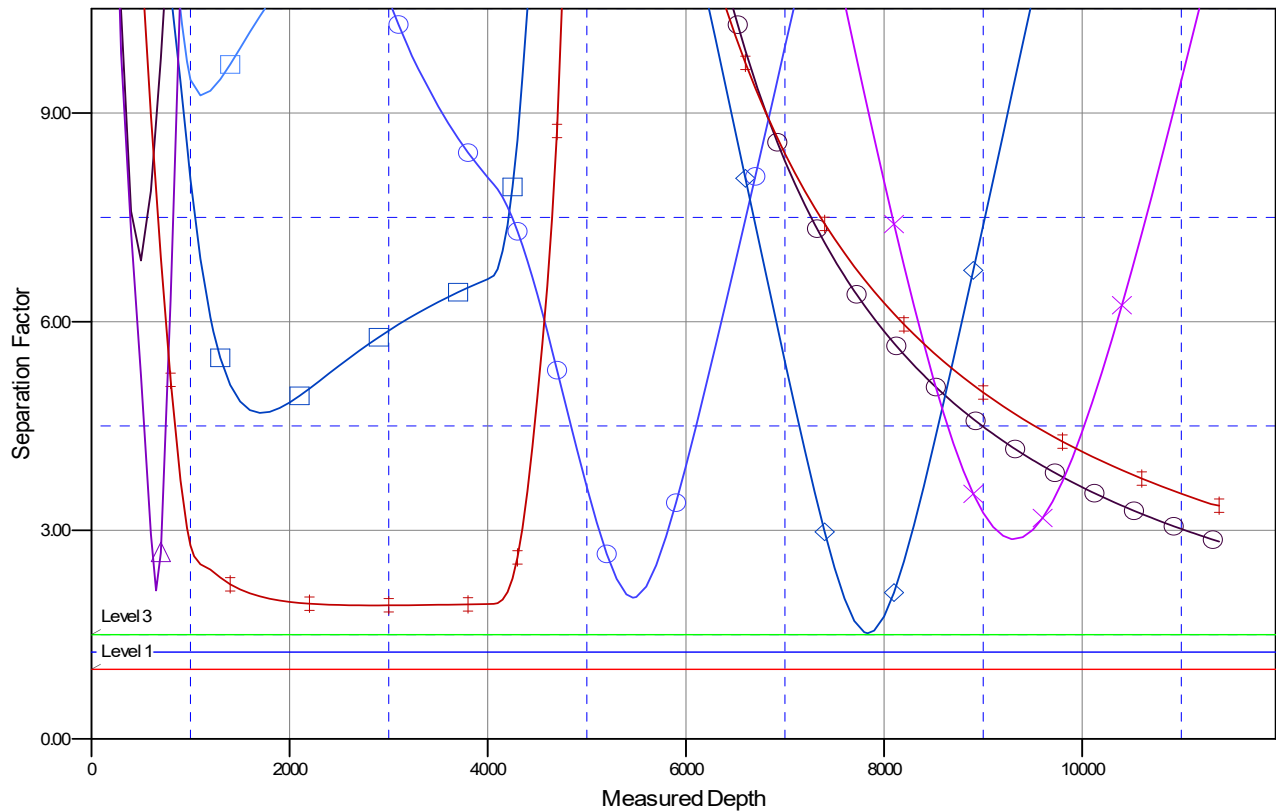

LEGEND

- Escrito P01 2310 Federal COM 106H Original Drilling, APDVO
- Escrito P01 2310 Federal COM 133H Original Drilling, APDVO
- Escrito P01 2310 Federal COM 113H Original Drilling, APDVO
- Well 5 OH OHVO
- December Dream 002 OH OHVO
- December Dream 003 OH OHVO
- Escrito P01 2310 137H Original Drilling, APDVO
- Escrito P01 2310 Federal COM 108H Original Drilling, APDVO

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



United States Department of the Interior

BUREAU OF LAND MANAGEMENT
Farmington District Office
6251 College Blvd, Suite A
Farmington, New Mexico 87402



In Reply Refer To:
3162.3-1(NMF0110)

* DJR OPERATING LLC

#134H ESCRITO P01 2310 FED COM

Lease: NMNM16762 Agreement: TBD
SH: SESE Section 1, T. 23 N., R. 10 W.
San Juan County, New Mexico
BH: SWSE Section 7, T.23 N., R. 9 W.
San Juan County, New Mexico

***Above Data Required on Well Sign**

GENERAL REQUIREMENTS FOR OIL AND GAS OPERATIONS ON FEDERAL AND INDIAN LEASES

The following special requirements apply and are effective when **checked**:

- A. ☒ Note all surface/drilling conditions of approval attached.
- B. ☒ The required wait on cement (WOC) time will be a minimum of 500 psi compressive strength at 60 degrees. Blowout preventor (BOP) nipple-up operations may then be initiated
- C. ☐ Test the surface casing to a minimum of _____ psi for 30 minutes.
- D. ☐ Test all casing strings below the surface casing to .22 psi/ft. of casing string length or 1500 psi, whichever is greater, but not to exceed 70% of the minimum internal yield burst) for a minimum of 30 minutes.
- E. ☒ Communitization Agreement covering the acreage dedicated to this well must be filed for approval with the Bureau of Land Management, New Mexico State Office, Reservoir Management Group, 301 Dinosaur Trail, Santa Fe, New Mexico 87508.
The effective date of the agreement must be **prior** to any sales.
- F. ☐ The use of co-flex hose is authorized contingent upon the following:
 1. From the BOP to the choke manifold: the co-flex hose must be hobbled on both ends and saddle to prevent whip.
 2. From the choke manifold to the discharge tank: the co-flex hoses must be as straight as practical, hobbled on both ends and anchored to prevent whip.
 3. The co-flex hose pressure rating must be at least commensurate with approved BOPE.

INTERIOR REGION 7 • UPPER COLORADO BASIN

COLORADO, NEW MEXICO, UTAH, WYOMING

I. GENERAL

- A. Full compliance with all applicable laws and regulations, with the approved Permit to drill, and with the approved Surface Use and Operations Plan is required. Lessees and/or operators are fully accountable for the actions of their contractors and subcontractors. Failure to comply with these requirements and the filing of required reports will result in strict enforcement pursuant to 43 CFR 3163.1 or 3163.2.
- B. Each well shall have a well sign in legible condition from spud date to final abandonment. The sign should show the operator's name, lease serial number, or unit name, well number, location of the well, and whether lease is Tribal or Allotted, (See 43 CFR 3162.6(b)).
- C. A complete copy of the approved Application for Permit to Drill, along with any conditions of approval, shall be available to authorized personnel at the drill site whenever active drilling operations are under way.
- D. For Wildcat wells only, a drilling operations progress report is to be submitted, to the BLM-Field Office, weekly from the spud date until the well is completed and the Well Completion Report is filed. The report should be on 8-1/2 x 11 inch paper, and each page should identify the well by; operator's name, well number, location and lease number.
- E. As soon as practical, notice is required of all blowouts, fires and accidents involving life-threatening injuries or loss of life. (See NTL-3A).
- F. Prior approval by the BLM-Authorized Office (Drilling and Production Section) is required for variance from the approved drilling program and before commencing plugging operations, plug back work, casing repair work, corrective cementing operations, or suspending drilling operations indefinitely. Emergency approval may be obtained orally, but such approval is contingent upon filing of a Notice of Intent sundry within three business days. **Any changes to the approved plan or any questions regarding drilling operations should be directed to BLM during regular business hours at 505-564-7600. Emergency program changes after hours should be directed to Virgil Lucero at 505-793-1836.**
- G. **The Inspection and Enforcement Section (I&E), phone number (505-564-7750) is to be notified at least 24 hours in advance of BOP test, spudding, cementing, or plugging operations so that a BLM representative may witness the operations.**
- H. From the time drilling operations are initiated and until drilling operations are completed, a member of the drilling crew or the tool pusher shall always maintain rig surveillance, unless the well is secured with blowout preventers or cement plugs.
- I. If for any reason, drilling operations are suspended for more than 90 days, a written notice must be provided to this office outlining your plans for this well.

II. REPORTING REQUIREMENTS

- A. For reporting purposes, all well Sundry notices, well completion and other well actions shall be referenced by the appropriate lease, communitization agreement and/or unit agreement numbers.
- B. The following reports shall be filed with the BLM-Authorized Officer within 30 days after the work is completed.
1. Original and three copies on Federal and an Original and five copies on Indian leases of Sundry Notice (Form 3150-5), giving complete information concerning.
 - a. Setting of each string of casing. Show size and depth of hole, grade and weight of casing, depth set, depth of any and all cementing tools that are used, amount (in cubic feet) and types of cement used, whether cement circulated to surface and all cement tops in the casing annulus, casing test method and results, and the date work was done. Show spud date on first report submitted.
 - b. Intervals tested, perforated (include; size, number and location of perforations), acidized, or fractured; and results obtained. Provide date work was done on well completion report and completion sundry notice.
 - c. Subsequent Report of Abandonment, show the manner in which the well was plugged, including depths where casing was cut and pulled, intervals (by depths) where cement plugs were replaced, and dates of the operations.
 2. Well Completion Report (Form 3160-4) will be submitted with 30 days after well has been completed.
 - a. Initial Bottom Hole Pressure (BHP) for the producing formations. Show the BHP on the completion report. The pressure may be: 1) measured with a bottom hole bomb, or; 2) calculated based on shut in surface pressures (minimum seven day buildup) and fluid level shot.
 3. Submit a cement evaluation log, if cement is not circulated to surface.

III. DRILLER'S LOG

The following shall be entered in the daily driller's log: 1) Blowout preventer pressures tests, including test pressures and results. 2) Blowout preventer tests for proper functioning, 3) Blowout prevention drills conducted, 4) Casing run, including size, grade, weight, and depth set, 5) How pipe was cemented, including amount of cement, type, whether cement circulated to surface, location of cementing tools, etc., 6) Waiting on cement time for each casing string, 7) Casing pressure tests after cementing, including test pressure and results and 8) Estimated amounts of oil and gas recovered and/or produced during drill stem test.

IV. GAS FLARING

Gas produced from this well may not be vented or flared beyond an initial, authorized test period of *** Days or 50 MMCF** following its (completion)(recompletion), whichever first occurs, without the prior, written approval of the authorized officer. Should gas be vented or flared without approval beyond the test period authorized above, you may be directed to shut-in the well until the gas can be captured or approval to continue venting or flaring as uneconomic is granted. You shall be required to compensate the lessor for the portion of the gas vented or flared without approval which is determined to have been avoidably lost.

***30 days**, unless a longer test period is specifically approved by the authorized officer. The 30-day period will commence upon the first gas to surface.

V. SAFETY

- A. All rig heating stoves are to be of the explosion-proof type.
- B. Rig safety lines are to be installed.
- C. Hard hats and other Personal Protective Equipment (PPE) must be utilized.

VI. CHANGE OF PLANS OR ABANDONMENT

- A. Any changes of plans required to mitigate unanticipated conditions encountered during drilling operations, will require approval as set forth in Section 1.F.
- B. If the well is dry, it is to be plugged in accordance with 43 CFR 3162.3-4, approval of the proposed plugging program is required as set forth in Section 1.F. The report should show the total depth reached, the reason for plugging, and the proposed intervals, by depths, where cement plugs are to be placed, type of plugging mud, etc. A Subsequent Report of Abandonment is required as set forth in Section II.B.1c.
- C. Unless a well has been properly cased and cemented, or properly plugged, the drilling rig must not be moved from the drill site without prior approval from the BLM-Authorized Officer.

VII. PHONE NUMBERS

- A. For BOPE tests, cementing, and plugging operations the phone number is 505-564-7750 and must be called 24 hours in advance in order that a BLM representative may witness the operations.

District I
1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720
District II
811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720
District III
1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170
District IV
1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 381791

CONDITIONS

Operator: DJR OPERATING, LLC 200 Energy Court Farmington, NM 87401	OGRID:
	371838
	Action Number:
	381791
Action Type:	
[C-101] BLM - Federal/Indian Land Lease (Form 3160-3)	

CONDITIONS

Created By	Condition	Condition Date
ward.rikala	Notify OCD 24 hours prior to casing & cement	9/18/2024
ward.rikala	Will require a File As Drilled C-102 and a Directional Survey with the C-104	9/18/2024
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string	9/18/2024
ward.rikala	Cement is required to circulate on both surface and intermediate1 strings of casing	9/18/2024
ward.rikala	If cement does not circulate on any string, a CBL is required for that string of casing	9/18/2024
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system	9/18/2024
ward.rikala	This well can not be produced until operator is in compliance with Rule 5.9.	9/18/2024
