

Form 3160-5
(June 2019)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: October 31, 2021

5. Lease Serial No.
NMNM26394

6. If Indian, Allottee or Tribe Name

SUBMIT IN TRIPLICATE - Other instructions on page 2

1. Type of Well
☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator
EOG RESOURCES INCORPORATED

3a. Address 1111 BAGBY SKY LOBBY 2, HOUSTON, TX 77030 3b. Phone No. (include area code)
(713) 651-7000

4. Location of Well (Footage, Sec., T.,R.,M., or Survey Description)
SEC 16/T25S/R33E/NMP

7. If Unit of CA/Agreement, Name and/or No.

8. Well Name and No.
GREEN DRAKE 16 FED COM/509H

9. API Well No. 30-025-51092

10. Field and Pool or Exploratory Area
WC-025 G-09 S253309P; Upper Wolfcamp

11. Country or Parish, State
LEA/NM

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | | | |
|--|--|---|--|---|--|
| <input checked="" type="checkbox"/> Notice of Intent | <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production (Start/Resume) | <input type="checkbox"/> Water Shut-Off | |
| <input type="checkbox"/> Subsequent Report | <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Hydraulic Fracturing | <input type="checkbox"/> Reclamation | <input type="checkbox"/> Well Integrity | |
| <input type="checkbox"/> Final Abandonment Notice | <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete | <input type="checkbox"/> Other | |
| | <input checked="" type="checkbox"/> Change Plans | <input type="checkbox"/> Plug and Abandon | <input type="checkbox"/> Temporarily Abandon | | |
| | <input type="checkbox"/> Convert to Injection | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal | | |

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has detennined that the site is ready for final inspection.)

EOG respectfully requests an amendment to our approved APD for this well to reflect the following changes:

- Green Drake 16 Fed Com 753H (FKA 509H) API #: 30-025-51092
- Change name from Green Drake 16 Fed Com 509H to Green Drake 16 Fed Com 753H.
- Change SHL from T-25-S, R-33-E, Sec 16, 2137' FSL, 1401' FWL, LEA Co., NM, to T-25-S, R-33-E, Sec 16, 2331' FSL, 737' FEL, LEA Co., N.M.
- Change BHL from T-25-S, R-33-E, Sec 21, 100' FSL, 680' FWL, LEA Co., NM, to T-25-S, R-33-E, Sec 21, 100' FSL, 495' FEL, LEA Co., N.M.

Continued on page 3 additional information

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed)
STAR HARRELL / Ph: (432) 848-9161

Title
Regulatory Specialist

(Electronic Submission)
Signature

Date
10/22/2024

THE SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by
CHRISTOPHER WALLS / Ph: (575) 234-2234 / Approved

Petroleum Engineer

Title

10/23/2024

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office
CARLSBAD

Title 18 U.S.C Section 1001 and Title 43 U.S.C Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

GENERAL INSTRUCTIONS

This form is designed for submitting proposals to perform certain well operations and reports of such operations when completed as indicated on Federal and Indian lands pursuant to applicable Federal law and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local area or regional procedures and practices, are either shown below, will be issued by or may be obtained from the local Federal office.

SPECIFIC INSTRUCTIONS

Item 4 - Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult the local Federal office for specific instructions.

Item 13: Proposals to abandon a well and subsequent reports of abandonment should include such special information as is required by the local Federal office. In addition, such proposals and reports should include reasons for the abandonment; data on any former or present productive zones or other zones with present significant fluid contents not sealed off by cement or otherwise; depths (top and bottom) and method of placement of cement plugs; mud or other material placed below, between and above plugs; amount, size, method of parting of any casing, liner or tubing pulled and the depth to the top of any tubing left in the hole; method of closing top of well and date well site conditioned for final inspection looking for approval of the abandonment. If the proposal will involve **hydraulic fracturing operations**, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The privacy Act of 1974 and the regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 351 et seq., 25 U.S.C. 396; 43 CFR 3160.

PRINCIPAL PURPOSE: The information is used to: (1) Evaluate, when appropriate, approve applications, and report completion of subsequent well operations, on a Federal or Indian lease; and (2) document for administrative use, information for the management, disposal and use of National Resource lands and resources, such as: (a) evaluating the equipment and procedures to be used during a proposed subsequent well operation and reviewing the completed well operations for compliance with the approved plan; (b) requesting and granting approval to perform those actions covered by 43 CFR 3162.3-2, 3162.3-3, and 3162.3-4; (c) reporting the beginning or resumption of production, as required by 43 CFR 3162.4-1(c) and (d) analyzing future applications to drill or modify operations in light of data obtained and methods used.

ROUTINE USES: Information from the record and/or the record will be transferred to appropriate Federal, State, local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecutions in connection with congressional inquiries or to consumer reporting agencies to facilitate collection of debts owed the Government.

EFFECT OF NOT PROVIDING THE INFORMATION: Filing of this notice and report and disclosure of the information is mandatory for those subsequent well operations specified in 43 CFR 3162.3-2, 3162.3-3, 3162.3-4.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM collects this information to evaluate proposed and/or completed subsequent well operations on Federal or Indian oil and gas leases.

Response to this request is mandatory.

The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Collection Clearance Officer (WO-630), 1849 C St., N.W., Mail Stop 401 LS, Washington, D.C. 20240

Additional Information

Additional Remarks

Change target formation to Wolfcamp M1.

Update casing and cement program to current design.

Update HSU to 480 acres.

Update the Pool as reflected in the C-102.

Location of Well

O. SHL: TR K / 2137 FSL / 1401 FWL / TWSP: 25S / RANGE: 33E / SECTION: 16 / LAT: 32.1292029 / LONG: -103.5812329 (TVD: 0 feet, MD: 0 feet)

PPP: TR L / 2540 FSL / 680 FWL / TWSP: 25S / RANGE: 33E / SECTION: 16 / LAT: 32.1303161 / LONG: -103.5835597 (TVD: 10237 feet, MD: 10346 feet)

BHL: TR M / 100 FSL / 680 FWL / TWSP: 25S / RANGE: 33E / SECTION: 21 / LAT: 32.1090899 / LONG: -103.5835725 (TVD: 10801 feet, MD: 18416 feet)

| | | | |
|--|--|-------------------------------------|--|
| C-102 Submit Electronically Via OCD Permitting | State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION | Revised July 9, 2024 | |
| | | Submittal Type: | <input type="checkbox"/> Initial Submittal |
| | | | <input checked="" type="checkbox"/> Amended Report |
| | | <input type="checkbox"/> As Drilled | |

WELL LOCATION AND ACREAGE DEDICATION PLAT

| | | |
|--|--|---|
| API Number 30-025-51092 | Pool Code 98180 | Pool Name WC-025 G-09 S253309P; Upper Wolfcamp |
| Property Code 328239 | Property Name GREEN DRAKE 16 FED COM | Well Number 753H |
| OGRID No. 7377 | Operator Name EOG RESOURCES, INC. | Ground Level Elevation 3385' |
| Surface Owner: <input checked="" type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input type="checkbox"/> Federal | | Mineral Owner: <input checked="" type="checkbox"/> State <input type="checkbox"/> Fee <input type="checkbox"/> Tribal <input checked="" type="checkbox"/> Federal |

Surface Location

| | | | | | | | | | |
|---------------|---------|----------|-------|---------|-------------------|-------------------|--------------|---------------|--------|
| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the N/S | Feet from the E/W | Latitude | Longitude | County |
| I | 16 | 25-S | 33-E | - | 2331' S | 737' E | N 32.1297149 | W 103.5711608 | LEA |

Bottom Hole Location

| | | | | | | | | | |
|---------------|---------|----------|-------|---------|-------------------|-------------------|--------------|---------------|--------|
| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the N/S | Feet from the E/W | Latitude | Longitude | County |
| P | 21 | 25-S | 33-E | - | 100' S | 495' E | N 32.1090645 | W 103.5703905 | LEA |

| | | | | |
|------------------------------------|--|--|--|-------------------------------|
| Dedicated Acres 480.00 | Infill or Defining Well INFILL | Defining Well API 30-025-47179 | Overlapping Spacing Unit (Y/N) Y | Consolidated Code C |
| Order Numbers NMMN139915 | | | Well Setbacks are under Common Ownership: <input type="checkbox"/> Yes <input type="checkbox"/> No | |

Kick Off Point (KOP)

| | | | | | | | | | |
|---------------|---------|----------|-------|---------|-------------------|-------------------|--------------|---------------|--------|
| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the N/S | Feet from the E/W | Latitude | Longitude | County |
| I | 16 | 25-S | 33-E | - | 2591' S | 495' E | N 32.1304275 | W 103.5703792 | LEA |


First Take Point (FTP)

| | | | | | | | | | |
|---------------|---------|----------|-------|---------|-------------------|-------------------|--------------|---------------|--------|
| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the N/S | Feet from the E/W | Latitude | Longitude | County |
| I | 16 | 25-S | 33-E | - | 2541' S | 495' E | N 32.1302901 | W 103.5703792 | LEA |

Last Take Point (LTP)

| | | | | | | | | | |
|---------------|---------|----------|-------|---------|-------------------|-------------------|--------------|---------------|--------|
| UL or lot no. | Section | Township | Range | Lot Idn | Feet from the N/S | Feet from the E/W | Latitude | Longitude | County |
| P | 21 | 25-S | 33-E | - | 100' S | 495' E | N 32.1090645 | W 103.5703905 | LEA |

| | | |
|---|--|--|
| Unitized Area or Area of Uniform Intrest COMM AGREEMENT | Spacing Unity Type <input checked="" type="checkbox"/> Horizontal <input type="checkbox"/> Vertical | Ground Floor Elevation 3410' |
|---|--|--|

| | | | |
|---|--|--|--|
| OPERATOR CERTIFICATION <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief; and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> <i>If this well is a horizontal well, I further certify that this organization has received The consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i> <i>Star L Harrell</i> Signature Star L Harrell Print Name star_harrell@eogresources.com E-mail Address 10/22/24 Date | | SURVEYORS CERTIFICATION <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</i>  9/18/2024 4:36:54 PM Signature and Seal of Professional Surveyor Date Certificate Number Date of Survey 08/29/2024 | |
|---|--|--|--|

C-102

Submit Electronically
Via OCD PermittingState of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION

Revised July 9, 2024

Submittal
Type:

- ☐ Initial Submittal
☒ Amended Report
☐ As Drilled

Property Name and Well Number

GREEN DRAKE 16 FED COM 753H

SURFACE LOCATION (SHL)

NEW MEXICO EAST
NAD 1983
X=777272 Y=411761
LAT.: N 32.1297149
LONG.: W 103.5711608
NAD 1927
X=736086 Y=411703
LAT.: N 32.1295904
LONG.: W 103.5706884
2331' FSL 737' FEL

KICK OFF POINT (KOP)

NEW MEXICO EAST
NAD 1983
X=777512 Y=412022
LAT.: N 32.1304275
LONG.: W 103.5703792
NAD 1927
X=736326 Y=411964
LAT.: N 32.1303030
LONG.: W 103.5699067
2591' FSL 495' FEL

UPPER MOST PERF. (UMP)



NEW MEXICO EAST
NAD 1983
X=777512 Y=411972
LAT.: N 32.1302901
LONG.: W 103.5703792
NAD 1927
X=736326 Y=411914
LAT.: N 32.1301655
LONG.: W 103.5699068
2541' FSL 495' FEL

FED PERF. POINT (FPP)

NEW MEXICO EAST
NAD 1983
X=777529 Y=409431
LAT.: N 32.1233068
LONG.: W 103.5703829
NAD 1927
X=736343 Y=409373
LAT.: N 32.1231822
LONG.: W 103.5699110
0' FSL 495' FEL

LOWER MOST PERF. (LMP)
BOTTOM HOLE LOCATION (BHL)

NEW MEXICO EAST
NAD 1983
X=777563 Y=404250
LAT.: N 32.1090645
LONG.: W 103.5703905
NAD 1927
X=736377 Y=404192
LAT.: N 32.1089398
LONG.: W 103.5699193
100' FSL 495' FEL

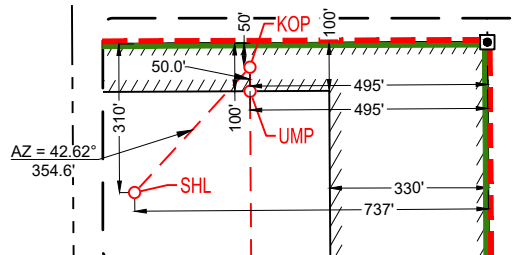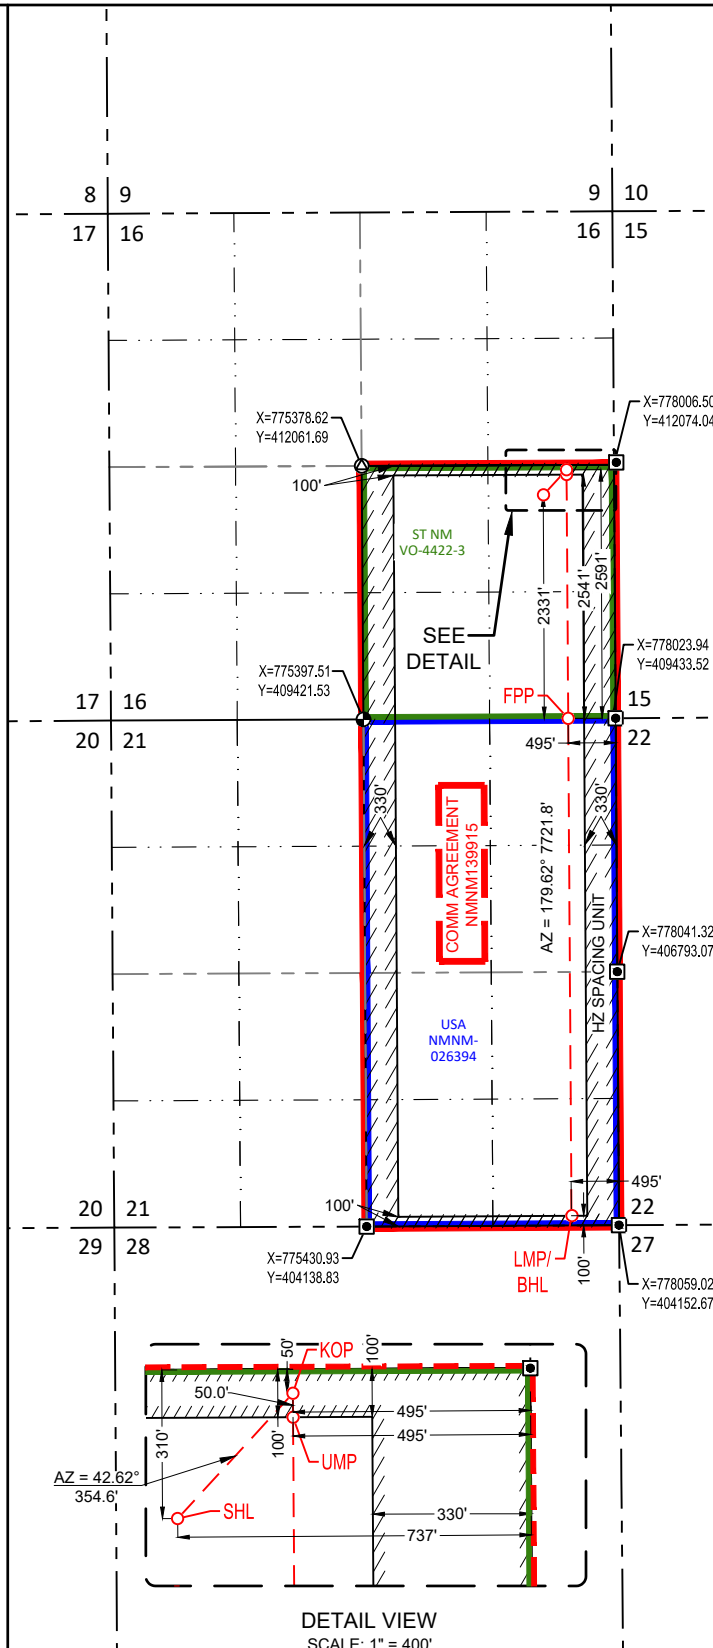

SURVEYORS CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.
08/29/2024

Date of Survey

Signature and Seal of Professional Surveyor:



PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

| | |
|------------------|-----------------------------|
| OPERATOR'S NAME: | EOG Resources Inc |
| WELL NAME & NO.: | GREEN DRAKE 16 FED COM 753H |
| LOCATION: | Section 16, T.25S., R.33E. |
| COUNTY: | Lea County, New Mexico |

COA

| | | | |
|----------------------------------|--|--|---|
| H2S | <input checked="" type="radio"/> Yes | <input type="radio"/> No | |
| Potash | <input checked="" type="radio"/> None | <input type="radio"/> Secretary | <input type="radio"/> R-111-P |
| Cave/Karst Potential | <input checked="" type="radio"/> Low | <input type="radio"/> Medium | <input type="radio"/> High |
| Cave/Karst Potential | <input type="radio"/> Critical | | |
| Variance | <input type="radio"/> None | <input checked="" type="radio"/> Flex Hose | <input type="radio"/> Other |
| Wellhead | <input type="radio"/> Conventional | <input checked="" type="radio"/> Multibowl | <input type="radio"/> Both |
| Wellhead Variance | <input type="radio"/> Diverter | | |
| Other | <input type="checkbox"/> 4 String | <input type="checkbox"/> Capitan Reef | <input type="checkbox"/> WIPP |
| Other | <input checked="" type="checkbox"/> Fluid Filled | <input type="checkbox"/> Pilot Hole | <input type="checkbox"/> Open Annulus |
| Cementing | <input type="checkbox"/> Contingency Cement Squeeze | <input checked="" type="checkbox"/> EchoMeter | <input checked="" type="checkbox"/> Primary Cement Squeeze |
| Special Requirements | <input type="checkbox"/> Water Disposal | <input checked="" type="checkbox"/> COM | <input type="checkbox"/> Unit |
| Special Requirements | <input type="checkbox"/> Batch Sundry | | |
| Special Requirements Variance | <input checked="" type="checkbox"/> Break Testing | <input checked="" type="checkbox"/> Offline Cementing | <input checked="" type="checkbox"/> Casing Clearance |

A. CASING

Primary Casing Design:

1. The **9-5/8** inch surface casing shall be set at approximately **1,137** feet (a minimum of 25 feet (Lea County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours

after bringing cement to surface or 500 pounds compressive strength, whichever is greater.

- d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The 7-5/8 inch intermediate casing shall be set at approximately **12,693 feet TVD**. The minimum required fill of cement behind the 7-5/8 inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

Option 2:

Operator has proposed to cement in two stages by conventionally cementing the first stage and performing a bradenhead squeeze on the second stage, contingent upon no returns to surface.

- a. First stage: Operator will cement with intent to reach the top of the **Brushy Canyon**
- b. Second stage:
 - Operator will perform bradenhead squeeze and top-out. Cement to surface. If cement does not reach surface, the appropriate BLM office shall be notified.

Operator has proposed to pump down 7-5/8" X 9-5/8" annulus. Operator must top out cement after the bradenhead squeeze and verify cement to surface. Operator can also check TOC with Echo-meter. CBL must be run from TD of the 7-5/8" casing to surface if confidence is lacking on the quality of the bradenhead squeeze cement job. Submit results to BLM.

If cement does not tie-back into the previous casing shoe, a third stage remediation BH may be performed. The appropriate BLM office shall be notified.

Bradenhead squeeze in the production interval is only as an edge case remediation measure and is NOT approved in this COA. If production cement job experiences losses and a bradenhead squeeze is needed for tie-back, BLM Engineering should be notified prior to job with volumes and planned wellbore schematic. CBL will be needed when this occurs.

If cement does not reach surface, the next casing string must come to surface.

Operator must use a limited flush fluid volume of 1 bbl following backside cementing procedures.

3. The **5-1/2** inch production casing shall be set at approximately **20,745** feet. The minimum required fill of cement behind the **5-1/2** inch production casing is:

Option 1 (Single Stage):

- Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

Alternate Casing Design:

1. The **10-3/4** inch surface casing shall be set at approximately **1,137** feet (a minimum of 25 feet (Lea County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
 - e. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - f. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - g. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - h. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The **8-3/4** inch intermediate casing shall be set at approximately **12,693 feet TVD**. The minimum required fill of cement behind the **8-3/4** inch intermediate casing is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

Option 2:

Operator has proposed to cement in two stages by conventionally cementing the first stage and performing a bradenhead squeeze on the second stage, contingent upon no returns to surface.

- c. First stage: Operator will cement with intent to reach the top of the **Brushy Canyon**
- d. Second stage:

- Operator will perform bradenhead squeeze and top-out. Cement to surface. If cement does not reach surface, the appropriate BLM office shall be notified.

Operator has proposed to pump down 10-3/4 X 8-3/4" annulus. Operator must top out cement after the bradenhead squeeze and verify cement to surface. Operator can also check TOC with Echo-meter. CBL must be run from TD of the 8-3/4" casing to surface if confidence is lacking on the quality of the bradenhead squeeze cement job. Submit results to BLM.

If cement does not tie-back into the previous casing shoe, a third stage remediation BH may be performed. The appropriate BLM office shall be notified.

Bradenhead squeeze in the production interval is only as an edge case remediation measure and is NOT approved in this COA. If production cement job experiences losses and a bradenhead squeeze is needed for tie-back, BLM Engineering should be notified prior to job with volumes and planned wellbore schematic. CBL will be needed when this occurs.

If cement does not reach surface, the next casing string must come to surface.

Operator must use a limited flush fluid volume of 1 bbl following backside cementing procedures.

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

3. The 6 inch production casing shall be set at approximately 20,745 feet. The minimum required fill of cement behind the 6 inch production casing is:

Option 1 (Single Stage):

- Cement should tie-back at least 200 feet into previous casing string. Operator shall provide method of verification.

Production casing must be kept fluid filled to meet BLM minimum collapse requirement.

NOTE ON PRODUCTION CASING FOR ALTERNATE DESIGN: OPERATOR HAS REQUESTED TO RUN 6" OR 5.5" OR A TAPERED STRING WITH BOTH. ALL THREE OPTIONS REVIEWED AND IS OK.

B. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 3500 (70% Working Pressure) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

(Note: For a minimum 5M BOPE or less (Utilizing a 10M BOPE system)

BOPE Break Testing Variance

- BOPE Break Testing is ONLY permitted for 5M BOPE or less. (**Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP**)
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer (**575-706-2779**) prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted (575-689-5981 Lea County) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per 43 CFR part 3170 Subpart 3172.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

Offline Cementing

Offline cementing approved for surface and intermediate intervals. Contact the BLM PETs prior to the commencement of any offline cementing procedure.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

Contact Eddy County Petroleum Engineering Inspection Staff:

Email or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220;
BLM_NM_CFO_DrillingNotifications@BLM.GOV; (575) 361-2822

Contact Lea County Petroleum Engineering Inspection Staff:

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - i. Notify the BLM when moving in and removing the Spudder Rig.
 - ii. Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - iii. BOP/BOPE test to be conducted per 43 CFR 3172 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area

immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

3. For intervals in which cement to surface is required, cement to surface should be verified with a visual check and density or pH check to differentiate cement from spacer and drilling mud. The results should be documented in the driller's log and daily reports.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.

2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.

3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.

4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.

5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.

6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.

7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-Q potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in 43 CFR 3172.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - i. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - ii. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - iii. Manufacturer representative shall install the test plug for the initial BOP test.
 - iv. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
 - v. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.

5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.

i. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

ii. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)

iii. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to 43 CFR 3172 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

iv. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.

v. The results of the test shall be reported to the appropriate BLM office.

vi. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.

vii. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.

viii. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate

casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per 43 CFR 3172.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

KPI 10/22/2024



Green Drake 16 Fed Com 753H

Revised Permit Information 08/20/2024:

Well Name: Green Drake 16 Fed Com 753H

Location: SHL: 2331' FSL & 737' FEL, Section 16, T-25-S, R-33-E, LEA Co., N.M.

BHL: 100' FSL & 495' FEL, Section 21, T-25-S, R-33-E, LEA Co., N.M.

CASING PROGRAM:

| Hole Size | Interval MD | | Interval TVD | | Csg OD | Weight | Grade | Conn |
|-----------|-------------|---------|--------------|---------|--------|--------|----------|---------------|
| | From (ft) | To (ft) | From (ft) | To (ft) | | | | |
| 12-1/4" | 0 | 1,137 | 0 | 1,140 | 9-5/8" | 36# | J-55 | LTC |
| 8-3/4" | 0 | 12,701 | 0 | 12,690 | 7-5/8" | 29.7# | ICYP-110 | MO FXL |
| 6-3/4" | 0 | 12,201 | 0 | 12,190 | 5-1/2" | 20# | P110-EC | DWC/C IS MS |
| 6-3/4" | 12,201 | 12,701 | 12,190 | 12,690 | 5-1/2" | 20# | P110-EC | VAM Sprint SF |
| 6-3/4" | 12,701 | 20,745 | 12,690 | 13,170 | 5-1/2" | 20# | P110-EC | DWC/C IS MS |

Variance is requested to waive the centralizer requirements for the 7-5/8" casing in the 8-3/4" hole size. An expansion additive will be utilized, in the cement slurry, for the entire length of the 8-3/4" hole interval to maximize cement bond and zonal isolation.

Variance is also requested to waive any centralizer requirements for the 5-1/2" casing in the 6-3/4" hole size. An expansion additive will be utilized, in the cement slurry, for the entire length of the 6-3/4" hole interval to maximize cement bond and zonal isolation.

Variance is also requested to waive the annular clearance requirements for the 5-1/2" casing by 7-5/8" casing annulus to the proposed top of cement.

EOG requests permission to allow deviation from the 0.422" annulus clearance requirement from Onshore Order #2 under the following conditions:

- Annular clearance to meet or exceed 0.422" between intermediate casing ID and production casing coupling only on the first 500' overlap between both casing strings.
- Annular clearance less than 0.422" is acceptable for the production open hole section.

CEMENTING PROGRAM:

| Depth | No. Sacks | Wt. ppg | Yld Ft3/sk | Slurry Description |
|-------------------|-----------|---------|------------|--|
| 1,140' 9-5/8" | 320 | 13.5 | 1.73 | Lead: Class C + 4.0% Bentonite Gel + 0.5% CaCl ₂ + 0.25 lb/sk Cello-Flake (TOC @ Surface) |
| | 80 | 14.8 | 1.34 | Tail: Class C + 0.6% FL-62 + 0.25 lb/sk Cello-Flake + 0.2% Sodium Metasilicate (TOC @ 937') |
| 12,690' 7-5/8" | 1460 | 14.2 | 1.11 | 1st Stage (Tail): Class C + 0.6% Halad-9 + 0.45% HR-601 + 3% Microbond (TOC @ 8,810') |
| | 1000 | 14.8 | 1.5 | 2nd Stage (Bradenhead squeeze): Class C + 3% Salt + 1% PreMag-M + 6% Bentonite Gel (TOC @ surface) |
| 20,745' 5-1/2" | 2208 | 12.5 | 2.05 | Lead: Class H + 0.4% Halad-344 + 0.35% HR-601 + 3% Microbond (TOC @ Surface) |
| | 2210 | 13.2 | 1.41 | Lead: Class H + 0.4% Halad-344 + 0.35% HR-601 + 3% Microbond (TOC @ 12,193') |



Green Drake 16 Fed Com 753H

| Additive | Purpose |
|---------------------|---|
| Bentonite Gel | Lightweight/Lost circulation prevention |
| Calcium Chloride | Accelerator |
| Cello-flake | Lost circulation prevention |
| Sodium Metasilicate | Accelerator |
| MagOx | Expansive agent |
| Pre-Mag-M | Expansive agent |
| Sodium Chloride | Accelerator |
| FL-62 | Fluid loss control |
| Halad-344 | Fluid loss control |
| Halad-9 | Fluid loss control |
| HR-601 | Retarder |
| Microbond | Expansive Agent |

EOG requests variance from minimum standards to pump a two stage cement job on the 7-5/8" intermediate casing string with the first stage being pumped conventionally with the calculated top of cement at the Brushy Canyon (9,007') and the second stage performed as a 1000 sack bradenhead squeeze with planned cement from the Brushy Canyon to surface. If necessary, a top out consisting of 100 sacks of Class C cement + 3% Salt + 1% PreMag-M + 6% Bentonite Gel (2.30 yld, 12.91 ppg) will be executed as a contingency. Top will be verified by Echo-meter.

EOG will include the Echo-meter verified fluid top and the volume of displacement fluid above the cement slurry in the annulus in all post-drill sundries on wells utilizing this cement program.

EOG will report to the BLM the volume of fluid (limited to 5 bbls) used to flush intermediate casing valves following backside cementing procedures.

EOG requests a variance to set the intermediate casing shoe in the Bone Spring formation OR the Wolfcamp formation, depending on depletion in the area and well conditions. EOG will monitor the well and ensure the well is static before casing operations begin.

MUD PROGRAM:

| Measured Depth | Type | Weight (ppg) | Viscosity | Water Loss |
|------------------------------|-------------|--------------|-----------|------------|
| 0 – 1,140' | Fresh - Gel | 8.6-8.8 | 28-34 | N/c |
| 1,140' – 12,690' | Brine | 9.0-10.5 | 28-34 | N/c |
| 12,690' – 12,701' | Oil Base | 8.7-9.4 | 58-68 | N/c - 6 |
| 12,701' – 20,745' Lateral | Oil Base | 10.0-14.0 | 58-68 | 4 - 6 |



Green Drake 16 Fed Com 753H

TUBING REQUIREMENTS

EOG respectfully requests an exception to the following NMOCD rule:

- 19.15.16.10 Casing AND TUBING REQUIREMENTS:
J (3): "The operator shall set tubing as near the bottom as practical and tubing perforations shall not be more than 250 feet above top of pay zone."

With horizontal flowing and gas lifted wells an end of tubing depth placed at or slightly above KOP is a conservative way to ensure the tubing stays clean from debris, plugging, and allows for fewer well interventions post offset completion. The deeper the tubulars are run into the curve, the higher the probability is that the tubing will become stuck in sand and or well debris as the well produces over time. An additional consideration for EOT placement during artificial lift installations is avoiding the high dog leg severity and inclinations found in the curve section of the wellbore to help improve reliability and performance. Dog leg severity and inclinations tend not to hamper gas lifted or flowing wells, but they do effect other forms of artificial lift like rod pump or ESP (electric submersible pump). Keeping the EOT above KOP is an industry best practice for those respective forms of artificial lift.




Green Drake 16 Fed Com 753H

2331' FSL
737' FEL
Section 16
T-25-S, R-33-E

Revised Wellbore

API: 30-025-51092

KB: 3410'
GL: 3385'

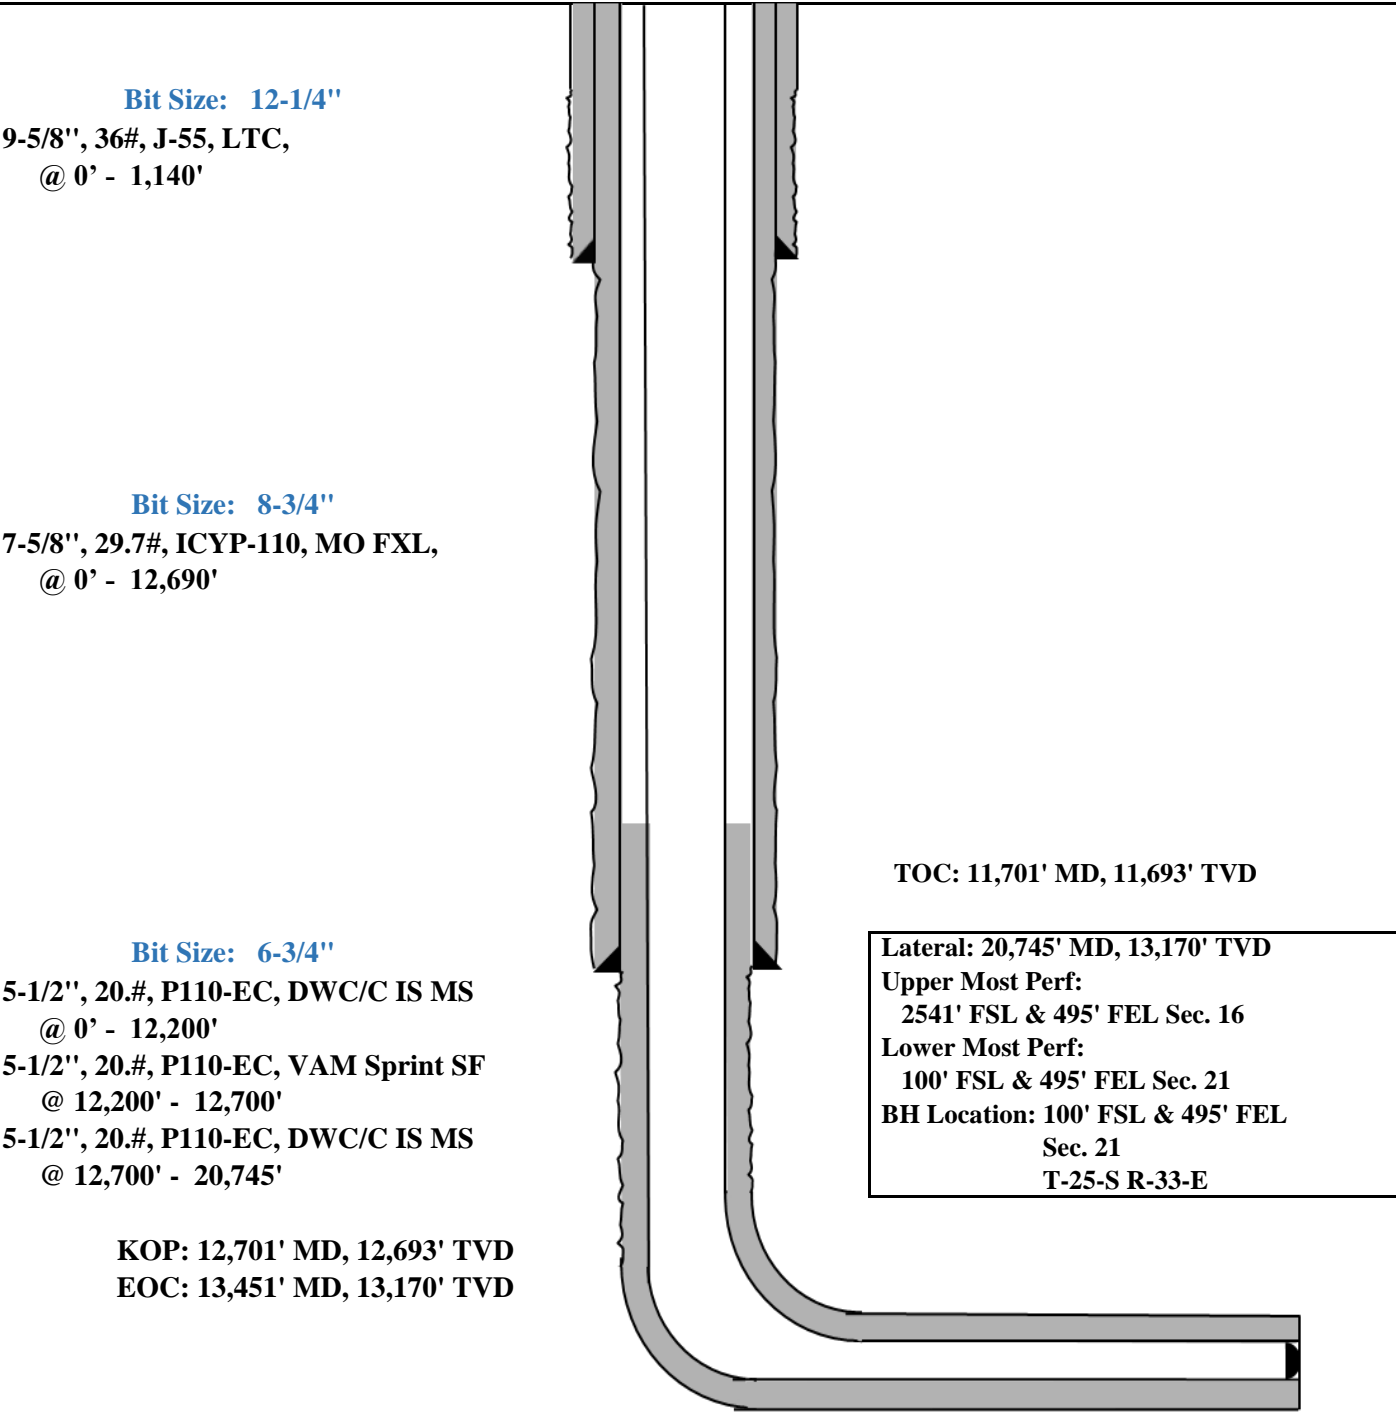



Green Drake 16 Fed Com 753H

Design B**CASING PROGRAM:**

| Hole Size | Interval MD | | Interval TVD | | Csg OD | Weight | Grade | Conn |
|-----------|-------------|---------|--------------|---------|---------|--------|---------|---------------|
| | From (ft) | To (ft) | From (ft) | To (ft) | | | | |
| 13" | 0 | 1,137 | 0 | 1,137 | 10-3/4" | 40.5# | J-55 | STC |
| 9-7/8" | 0 | 11,338 | 0 | 11,330 | 8-3/4" | 38.5# | P110-EC | VAM Sprint-SF |
| 7-7/8" | 0 | 12,701 | 0 | 12,693 | 6" | 22.3# | P110-EC | DWC/C IS |
| 6.75" | 12,701 | 20,745 | 12,693 | 13,170 | 5-1/2" | 20# | P110-EC | DWC/C IS MS |

**For highlighted rows above, variance is requested to run entire string of either 6" or 5-1/2" casing string above due to availability.

Variance is requested to waive the centralizer requirements for the 8-3/4" casing in the 9-7/8" hole size. An expansion additive will be utilized, in the cement slurry, for the entire length of the 9-7/8" hole interval to maximize cement bond and zonal isolation.

Variance is also requested to waive any centralizer requirements for the 6" and 5-1/2" casings in the 7-7/8" hole size. An expansion additive will be utilized, in the cement slurry, for the entire length of the 7-7/8" hole interval to maximize cement bond and zonal isolation.

Variance is also requested to waive the annular clearance requirements for the 6" and 5-1/2" casings by 8-3/4" casing annulus to the proposed top of cement.

EOG requests permission to allow deviation from the 0.422" annulus clearance requirement from Onshore Order #2 under the following conditions:

- Annular clearance to meet or exceed 0.422" between intermediate casing ID and production casing coupling only on the first 500' overlap between both casing strings.
- Annular clearance less than 0.422" is acceptable for the production open hole section.

CEMENTING PROGRAM:

| Depth | No. Sacks | Wt. ppg | Yld Ft3/sk | Slurry Description |
|-------------------|-----------|---------|------------|--|
| 1,137' 10-3/4" | 290 | 13.5 | 1.73 | Lead: Class C + 4.0% Bentonite Gel + 0.5% CaCl ₂ + 0.25 lb/sk Cello-Flake (TOC @ Surface) |
| | 70 | 14.8 | 1.34 | Tail: Class C + 0.6% FL-62 + 0.25 lb/sk Cello-Flake + 0.2% Sodium Metasilicate (TOC @ 937') |
| 12,693' 8-3/4" | 1650 | 14.2 | 1.11 | 1st Stage (Tail): Class C + 0.6% Halad-9 + 0.45% HR-601 + 3% Microbond (TOC @ 8,807') |
| | 1000 | 14.8 | 1.5 | 2nd Stage (Bradenhead squeeze): Class C + 3% Salt + 1% PreMag-M + 6% Bentonite Gel (TOC @ surface) |
| 20,745' 6" | 1210 | 13.2 | 1.31 | Lead: Class H + 0.4% Halad-344 + 0.35% HR-601 + 3% Microbond (TOC @ 12,193') |



Green Drake 16 Fed Com 753H

EOG requests variance from minimum standards to pump a two stage cement job on the 8-3/4" intermediate casing string with the first stage being pumped conventionally with the calculated top of cement at the Brushy Canyon (9,007') and the second stage performed as a 1000 sack bradenhead squeeze with planned cement from the Brushy Canyon to surface. If necessary, a top out consisting of -974 sacks of Class C cement + 3% Salt + 1% PreMag-M + 6% Bentonite Gel (2.30 yld, 12.91 ppg) will be executed as a contingency. Top will be verified by Echo-meter.

EOG will include the Echo-meter verified fluid top and the volume of displacement fluid above the cement slurry in the annulus in all post-drill sundries on wells utilizing this cement program.

EOG will report to the BLM the volume of fluid (limited to 5 bbls) used to flush intermediate casing valves following backside cementing procedures.

EOG requests a variance to set the intermediate casing shoe in the Bone Spring formation OR the Wolfcamp formation, depending on depletion in the area and well conditions. EOG will monitor the well and ensure the well is static before casing operations begin.

VARIANCE REQUESTS:

EOG requests the additional variance(s) in the attached document(s):

Variances requested include (supporting documents attached):


- BOP Break Testing for 5M Intermediate Intervals (EOG BLM Variance 3a_b)
- Offline Cementing for Surface and Intermediate Intervals (EOG BLM Variance 3a_b)
- Intermediate Bradenhead Cement (EOG BLM Variance 2a)
- Wolfcamp Intermediate Casing Setpoint (EOG BLM Varinace 2b)



Green Drake 16 Fed Com 753H

2331' FSL
737' FEL
Section 16
T-25-S, R-33-E

Proposed Wellbore
KB: 3410'
GL: 3385'
API: 30-025-51092

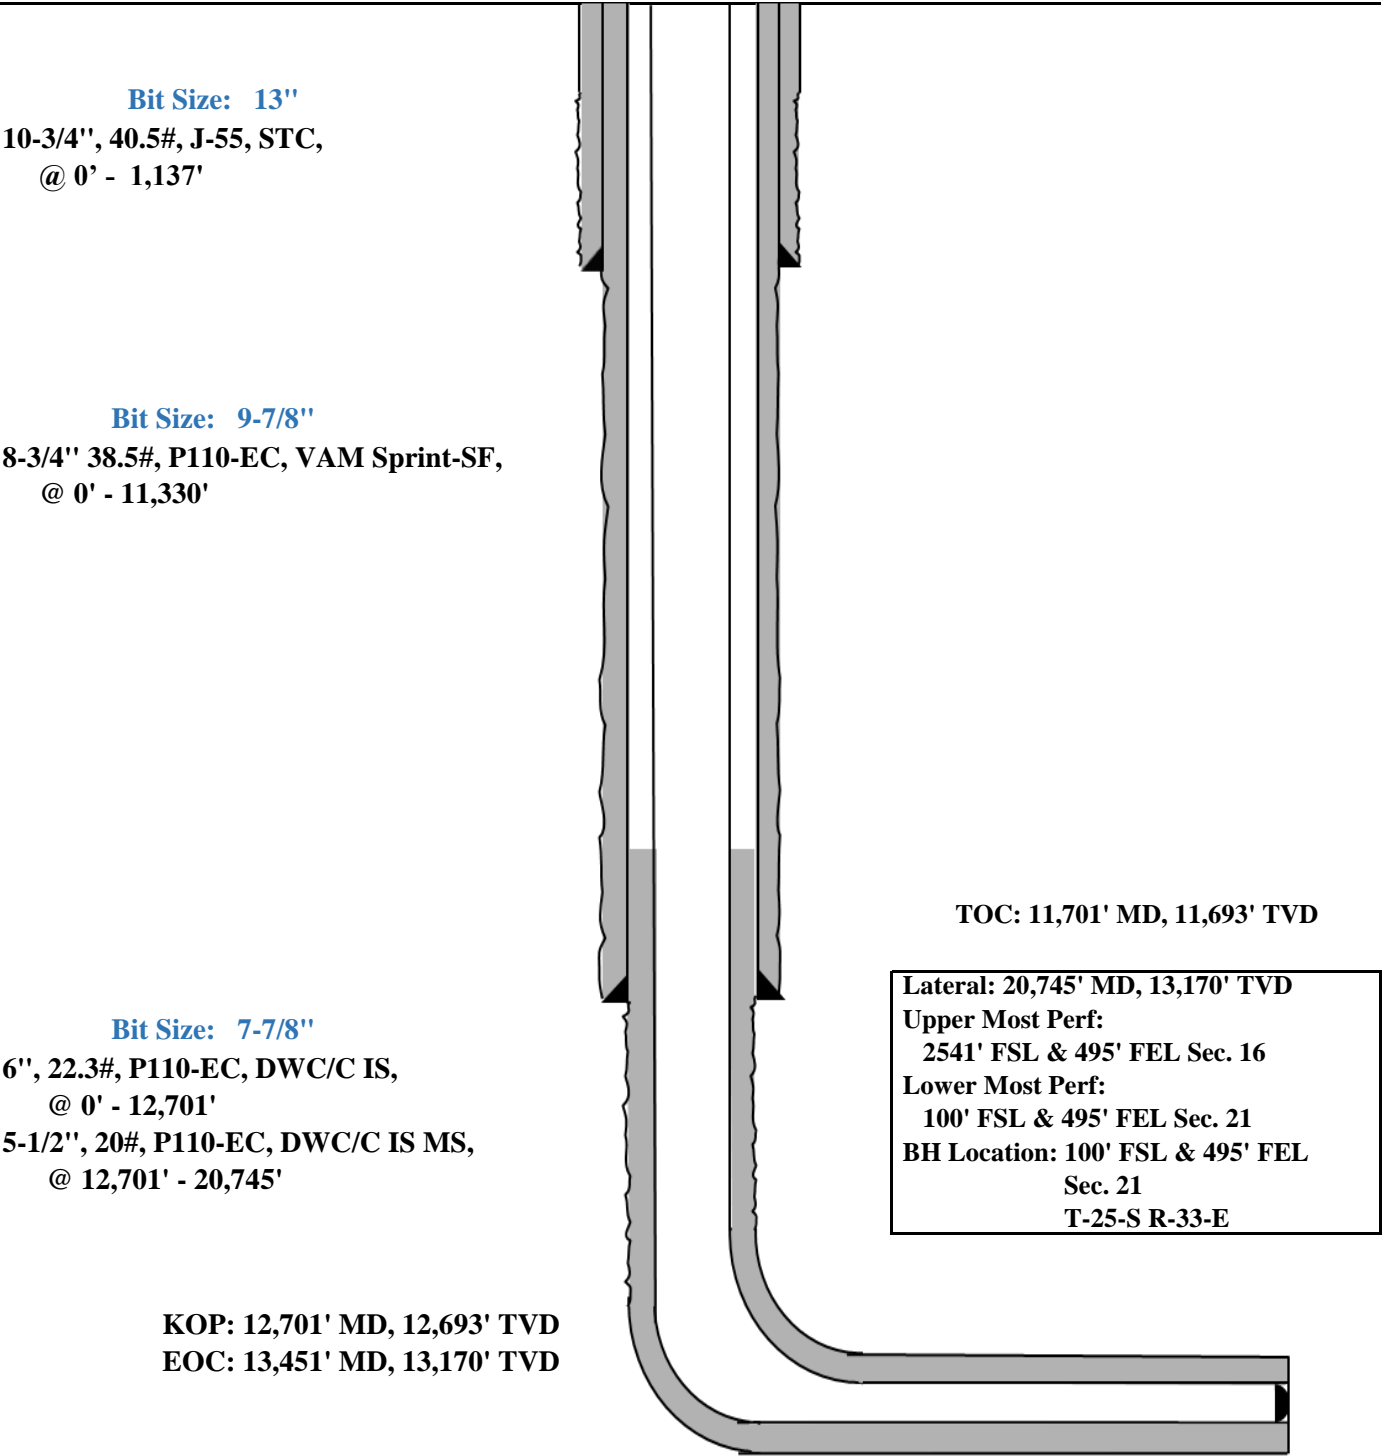



Green Drake 16 Fed Com 753H

GEOLOGIC NAME OF SURFACE FORMATION:

Permian

ESTIMATED TOPS OF IMPORTANT GEOLOGICAL MARKERS:

| | |
|------------------------|---------|
| Rustler | 1,014' |
| Tamarisk Anhydrite | 1,112' |
| Top of Salt | 1,321' |
| Base of Salt | 4,606' |
| Lamar | 4,972' |
| Bell Canyon | 5,024' |
| Cherry Canyon | 6,114' |
| Brushy Canyon | 9,007' |
| Bone Spring Lime | 9,190' |
| Leonard (Avalon) Shale | 9,248' |
| 1st Bone Spring Sand | 10,122' |
| 2nd Bone Spring Shale | 10,362' |
| 2nd Bone Spring Sand | 10,716' |
| 3rd Bone Spring Carb | 11,230' |
| 3rd Bone Spring Sand | 11,878' |
| Wolfcamp | 12,299' |
| TD | 13,170' |

ESTIMATED DEPTHS OF ANTICIPATED FRESH WATER, OIL OR GAS:

| | | |
|------------------------|---------|-------------|
| Upper Permian Sands | 0- 400' | Fresh Water |
| Bell Canyon | 5,024' | Oil |
| Cherry Canyon | 6,114' | Oil |
| Brushy Canyon | 9,007' | Oil |
| Leonard (Avalon) Shale | 9,248' | Oil |
| 1st Bone Spring Sand | 10,122' | Oil |
| 2nd Bone Spring Shale | 10,362' | Oil |
| 2nd Bone Spring Sand | 10,716' | Oil |



EOG Batch Casing

Pad Name: Green Drake 16 Fed Com DEEP
SHL: Section 16, Township 25-S, Range 33-E, LEA County, NM

| Well Name | API # | Surface | | Intermediate | | Production | |
|---|--------------|---------|-------|--------------|--------|------------|--------|
| | | MD | TVD | MD | TVD | MD | TVD |
| Green Drake 16 Fed Com #751H (FKA 405H) | 30-025-51086 | 1,137 | 1,137 | 12,824 | 12,693 | 20,864 | 13,170 |
| Green Drake 16 Fed Com #752H (FKA 603H) | 30-025-51997 | 1,137 | 1,137 | 12,717 | 12,693 | 20,762 | 13,170 |
| Green Drake 16 Fed Com #753H (FKA 509H) | 30-025-51092 | 1,137 | 1,137 | 12,701 | 12,693 | 20,745 | 13,170 |



EOG Batch Casing

Variances

EOG requests the additional variance(s) in the attached document(s):

- EOG BLM Variance 2a - Intermediate Bradenhead Cement
- EOG BLM Variance 2b - Wolfcamp Intermediate Casing Setpoint
- EOG BLM Variance 3a_b - BOP Break-test and Offline Intermediate Cement



EOG Batch Casing

GEOLOGIC NAME OF SURFACE FORMATION:

Permian

ESTIMATED TOPS OF IMPORTANT GEOLOGICAL MARKERS:

| | |
|------------------------|---------|
| Rustler | 1,014' |
| Tamarisk Anhydrite | 1,112' |
| Top of Salt | 1,321' |
| Base of Salt | 4,606' |
| Lamar | 4,972' |
| Bell Canyon | 5,024' |
| Cherry Canyon | 6,114' |
| Brushy Canyon | 9,007' |
| Bone Spring Lime | 9,190' |
| Leonard (Avalon) Shale | 9,248' |
| 1st Bone Spring Sand | 10,122' |
| 2nd Bone Spring Shale | 10,362' |
| 2nd Bone Spring Sand | 10,716' |
| 3rd Bone Spring Carb | 11,230' |
| 3rd Bone Spring Sand | 11,878' |
| Wolfcamp | 12,299' |

ESTIMATED DEPTHS OF ANTICIPATED FRESH WATER, OIL OR GAS:

| | | |
|------------------------|---------|-------------|
| Upper Permian Sands | 0- 400' | Fresh Water |
| Bell Canyon | 5,024' | Oil |
| Cherry Canyon | 6,114' | Oil |
| Brushy Canyon | 9,007' | Oil |
| Leonard (Avalon) Shale | 9,248' | Oil |
| 1st Bone Spring Sand | 10,122' | Oil |
| 2nd Bone Spring Shale | 10,362' | Oil |
| 2nd Bone Spring Sand | 10,716' | Oil |

No other Formations are expected to give up oil, gas or fresh water in measurable quantities. Surface fresh water sands will be protected by setting surface casing at 1,140' and circulating cement back to surface.

**Green Drake 16 Fed Com 753H (FKA 509H) API #: 30-025-51092 Variances**

EOG respectfully requests the below variances to be applied to the above well:

- Variance is requested to waive the centralizer requirements for the intermediate casing in the intermediate hole. An expansion additive will be utilized, in the cement slurry, for the entire length of the intermediate interval to maximize cement bond and zonal isolation.
- Variance is also requested to waive the centralizer requirements for the production casing in the production hole. An expansion additive will be utilized, in the cement slurry, for the entire length of the production interval to maximize cement bond and zonal isolation.
- EOG requests a variance to set the intermediate casing shoe in the Bone Spring formation or the Wolfcamp formation, depending on depletion in the area and well conditions. EOG will monitor the well and ensure the well is static before casing operations begin.
- Variance is requested to use a co-flex line between the BOP and choke manifold (instead of using a 4" OD steel line).
- Variance is requested to use a 5,000 psi annular BOP with the 10,000 psi BOP stack.
- EOG Resources requests the option to contract a Surface Rig to drill, set surface casing, and Cement on the subject well. After WOC 8 hours or 500 psi compressive strength (whichever is greater), the Surface Rig will move off so the wellhead can be installed. A welder will cut the casing to the proper height and weld on the wellhead (both "A" and "B" sections). The weld will be tested to 1,500 psi. All valves will be closed and a wellhead cap will be installed (diagram attached). If the timing between rigs is such that EOG Resources would not be able to preset the surface, the Primary Rig will MIRU and drill the well in its entirety per the APD.

EOG requests the additional variance(s) in the attached document(s):

- EOG BLM Variance 2a - Intermediate Bradenhead Cement
- EOG BLM Variance 3a_b - BOP Break-test and Offline Intermediate Cement



Intermediate Bradenhead Cement:

EOG requests variance from minimum standards to pump a two stage cement job on the intermediate casing string with the first stage being pumped conventionally with the calculated top of cement at the Brushy Canyon and the second stage performed as 1000 sack bradenhead squeeze with planned cement from the Brushy Canyon to surface. If necessary, a top out consisting of Class C cement + 3% Salt + 1% PreMag-M + 6% Bentonite Gel (2.30 yld, 12.91 ppg) will be executed as a contingency. Top of cement will be verified by Echo-meter.

EOG will include the Echo-meter verified fluid top and the volume of displacement fluid above the cement slurry in the annulus in all post-drill sundries on wells utilizing this cement program.

EOG will report to the BLM the volume of fluid (limited to 5 bbls) used to flush intermediate casing valves following backside cementing procedures.



Wolfcamp Intermediate Casing Setpoint:




EOG Resources Inc. (EOG) requests a variance to set the intermediate casing shoe in the Bone Spring formation OR the Wolfcamp formation, depending on depletion in the area and well conditions. EOG will monitor the well and ensure the well is static before casing operations begin.

**Break-test BOP & Offline Cementing:**

EOG Resources Inc. (EOG) respectfully requests a variance from the minimum standards for well control equipment testing of ECFR Title 43 Part 3172.6(b)(9)(iv) to allow a testing schedule of the blow out preventer (BOP) and blow out prevention equipment (BOPE) along with Batch Drilling & Offline cement operations to include the following:

- Full BOPE test at first installation on the pad.
- Full BOPE test every 21 days.
- This test will be conducted for 5M rated hole intervals only.
- Each rig requesting the break-test variance is capable of picking up the BOP without damaging components using winches, following API Standard 53, Well Control Equipment Systems for Drilling Wells (Fifth edition, December 2018, Annex C. Table C.4) which recognizes break testing as an acceptable practice.
- Function tests will be performed on the following BOP elements:
 - Annular ð during each full BOPE test
 - Upper Pipe Rams ð On trip ins where FIT required
 - Blind Rams ð Every trip
 - Lower Pipe Rams ð during each full BOPE test
- Break testing BOP and BOPE coupled with batch drilling operations and option to offline cement and/or remediate (if needed) any surface or intermediate sections, according to attached offline cementing support documentation.
- After the well section is secured, the BOP will be disconnected from the wellhead and walked with the rig to another well on the pad.
- TA cap will also be installed per Wellhead vendor procedure and pressure inside the casing will be monitored via the valve on the TA cap as per standard batch drilling ops.


Break Test Diagram (HCR valve)

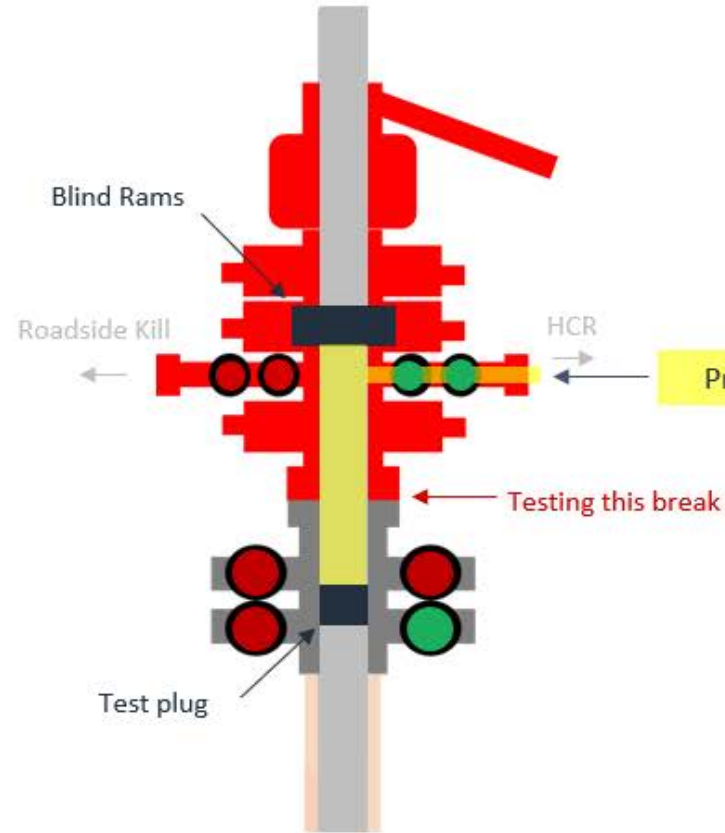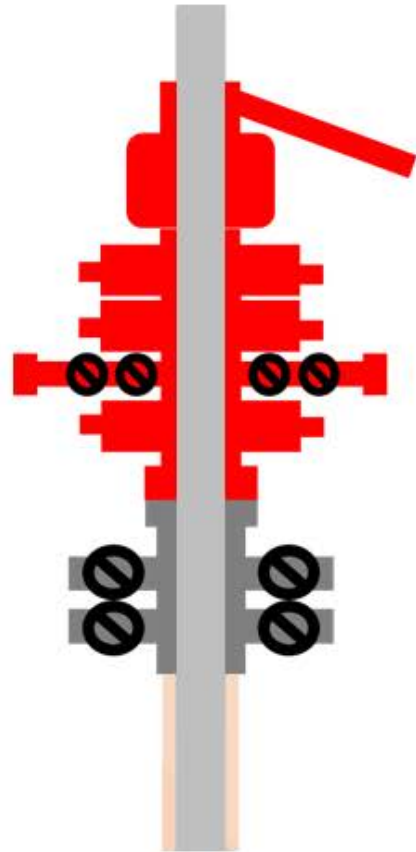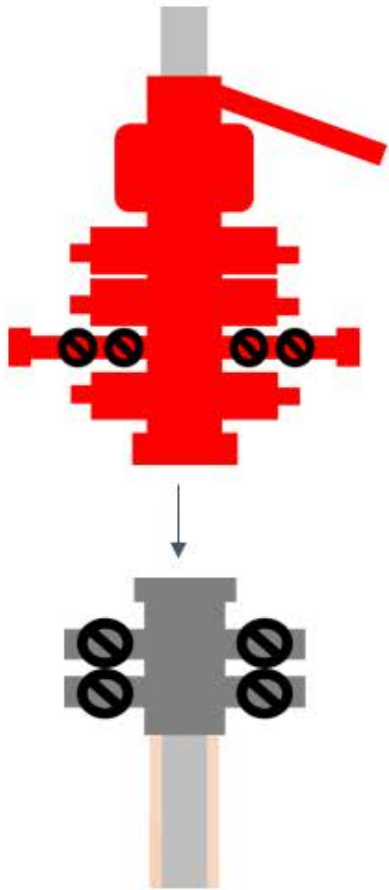

Steps

1. Set plug in wellhead (lower barrier)
2. Close Blind Rams (upper barrier)
3. Close roadside kill
4. Open HCR (pressure application)
5. Open wellhead valves below test plug to ensure if leak past test plug, pressure won't be applied to wellbore
6. Tie BOP testers high pressure line to main choke manifold crown valve
7. Pressure up to test break
8. Bleed test pressure from BOP testing unit

Break Test Diagram (Test Joint)

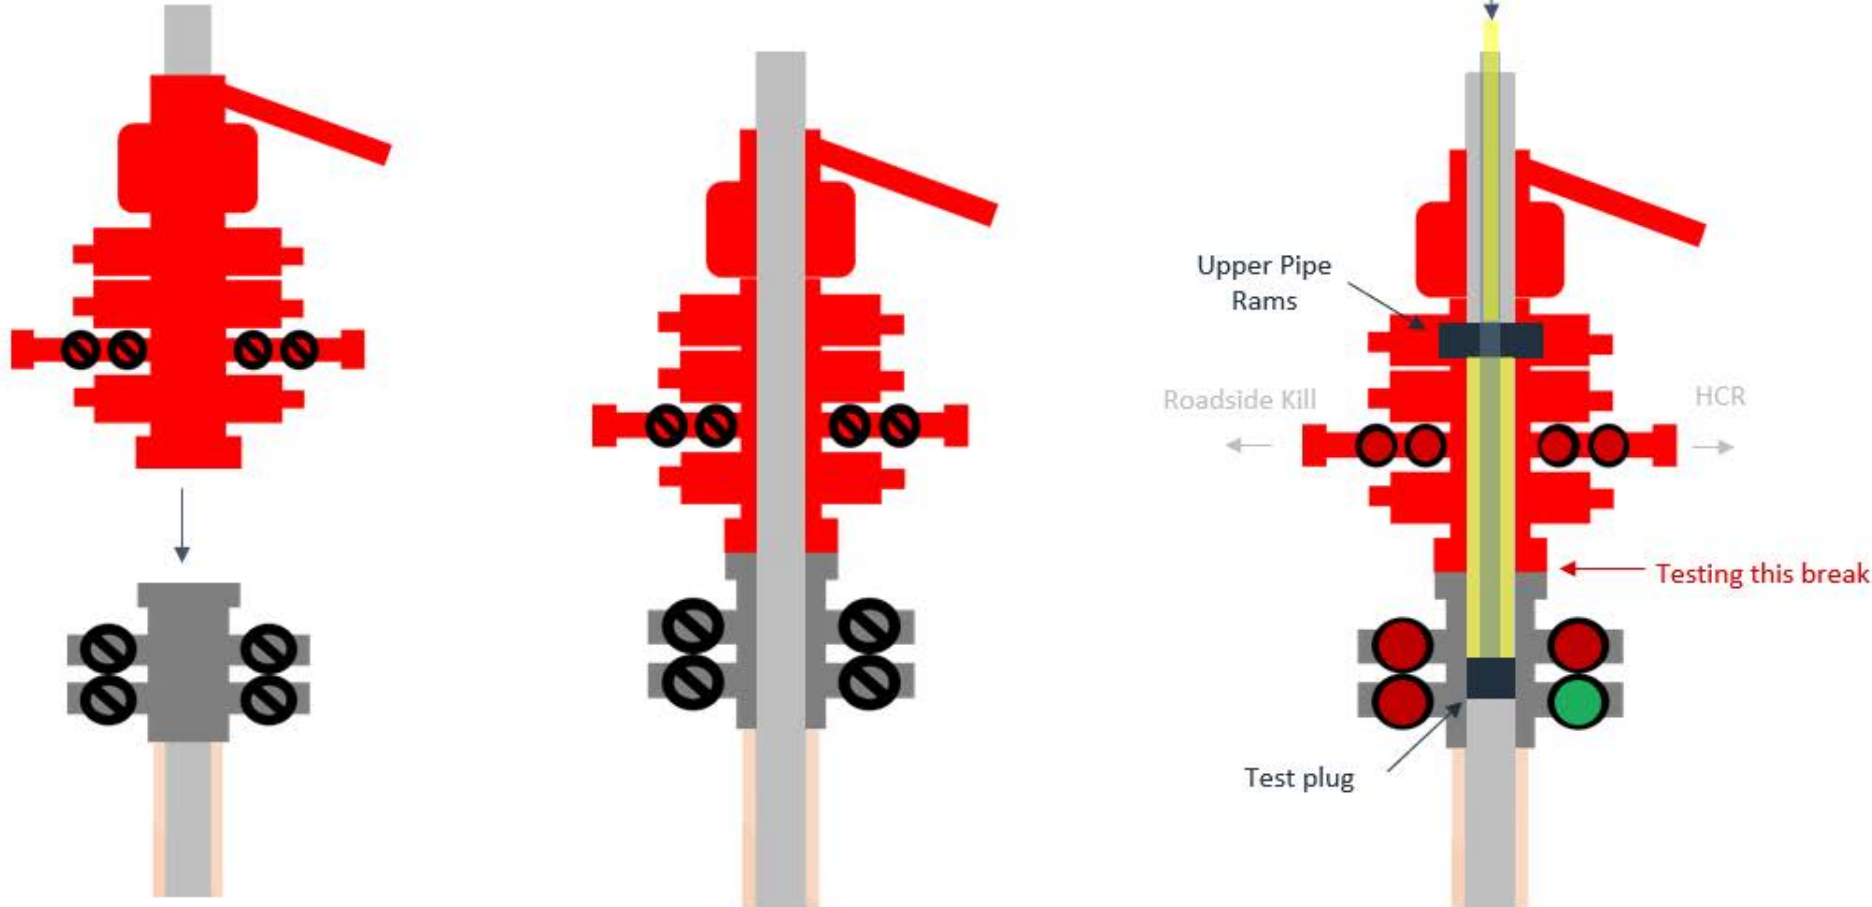

Steps

1. Set plug in with test joint wellhead (lower barrier)
2. Close Upper Pipe Rams (upper barrier)
3. Close roadside kill
4. Close HCR
5. Open wellhead valves below test plug to ensure if leak past test plug, pressure won't be applied to wellbore
6. Tie BOP testers high pressure line to top of test joint
7. Pressure up to test break
8. Bleed test pressure from BOP testing unit



Offline Intermediate Cementing Procedure

2/24/2022

Cement Program

1. No changes to the cement program will take place for offline cementing.

Summarized Operational Procedure for Intermediate Casing

1. Run casing as per normal operations. While running casing, conduct negative pressure test and confirm integrity of the float equipment back pressure valves.
 - a. Float equipment is equipped with two back pressure valves rated to a minimum of 5,000 psi.
2. Land production casing on mandrel hanger through BOP.
 - a. If casing is unable to be landed with a mandrel hanger, then the **casing will be cemented online**.
3. Break circulation and confirm no restrictions.
 - a. Ensure no blockage of float equipment and appropriate annular returns.
 - b. Perform flow check to confirm well is static.
4. Set pack-off
 - a. If utilizing a fluted/ported mandrel hanger, ensure well is static on the annulus and inside the casing by filling the pipe with kill weight fluid, remove landing joint, and set annular packoff through BOP. Pressure test to 5,000 psi for 10 min.
 - b. If utilizing a solid mandrel hanger, ensure well is static on the annulus and inside the casing by filling the pipe with kill weight fluid. Pressure test seals to 5,000 psi for 10 min. Remove landing joint through BOP.
5. After confirmation of both annular barriers and the two casing barriers, install TA plug and pressure test to 5,000 psi for 10 min. Notify the BLM with intent to proceed with nipple down and offline cementing.
 - a. Minimum 4 hrs notice.
6. With the well secured and BLM notified, nipple down BOP and secure on hydraulic carrier or cradle.
 - a. **Note, if any of the barriers fail to test, the BOP stack will not be nipped down until after the cement job has concluded and both lead and tail slurry have reached 500 psi.**
7. Skid/Walk rig off current well.
8. Confirm well is static before removing TA Plug.
 - a. Cementing operations will not proceed until well is under control. (If well is not static, notify BLM and proceed to kill)
 - b. Casing outlet valves will provide access to both the casing ID and annulus. Rig or third party pump truck will kill well prior to cementing.
 - c. Well control plan can be seen in Section B, Well Control Procedures.
 - d. If need be, rig can be moved back over well and BOP nipped back up for any further remediation.



Offline Intermediate Cementing Procedure

2/24/2022

- e. Diagram for rig positioning relative to offline cementing can be seen in Figure 4.
9. Rig up return lines to take returns from wellhead to pits and rig choke.
 - a. Test all connections and lines from wellhead to choke manifold to 5,000 psi high for 10 min.
 - b. If either test fails, perform corrections and retest before proceeding.
 - c. Return line schematics can be seen in Figure 3.
10. Remove TA Plug from the casing.
11. Install offline cement tool.
 - a. Current offline cement tool schematics can be seen in Figure 1 (Cameron) and Figure 2 (Cactus).
12. Rig up cement head and cementing lines.
 - a. Pressure test cement lines against cement head to 80% of casing burst for 10 min.
13. Break circulation on well to confirm no restrictions.
 - a. If gas is present on circulation, well will be shut in and returns rerouted through gas buster.
 - b. Max anticipated time before circulating with cement truck is 6 hrs.
14. Pump cement job as per plan.
 - a. At plug bump, test casing to 0.22 psi/ft or 1500 psi, whichever is greater.
 - b. If plug does not bump on calculated, shut down and wait 8 hrs or 500 psi compressive strength, whichever is greater before testing casing.
15. Confirm well is static and floats are holding after cement job.
 - a. With floats holding and backside static:
 - i. Remove cement head.
 - b. If floats are leaking:
 - i. Shut-in well and WOC (Wait on Cement) until tail slurry reaches 500 psi compressive strength and the casing is static prior to removing cement head.
 - c. If there is flow on the backside:
 - i. Shut in well and WOC until tail slurry reaches 500 psi compressive strength. Ensure that the casing is static prior to removing cement head.
16. Remove offline cement tool.
17. Install night cap with pressure gauge for monitoring.
18. Test night cap to 5,000 psi for 10 min.



Offline Intermediate Cementing Procedure

2/24/2022

Example Well Control Plan Content

A. Well Control Component Table

The table below, which covers the cementing of the **5M MASP (Maximum Allowable Surface Pressure) portion of the well**, outlines the well control component rating in use. This table, combined with the mud program, documents that two barriers to flow can be maintained at all times, independent of the BOP nipped up to the wellhead.

Intermediate hole section, 5M requirement

| Component | RWP |
|--------------------------|-----|
| Pack-off | 10M |
| Casing Wellhead Valves | 10M |
| Annular Wellhead Valves | 5M |
| TA Plug | 10M |
| Float Valves | 5M |
| 2" 1502 Lo-Torque Valves | 15M |

B. Well Control Procedures

Well control procedures are specific to the rig equipment and the operation at the time the kick occurs. Below are the minimal high-level tasks prescribed to assure a proper shut-in while circulating and cementing through the Offline Cement Adapter.

General Procedure While Circulating

1. Sound alarm (alert crew).
2. Shut down pumps.
3. Shut-in Well (close valves to rig pits and open valve to rig choke line. Rig choke will already be in the closed position).
4. Confirm shut-in.
5. Notify tool pusher/company representative.



Offline Intermediate Cementing Procedure

2/24/2022

6. Read and record the following:
 - a. SICP (Shut in Casing Pressure) and AP (Annular Pressure)
 - b. Pit gain
 - c. Time
 - d. Regroup and identify forward plan to continue circulating out kick via rig choke and mud/gas separator. Circulate and adjust mud density as needed to control well.

General Procedure While Cementing

1. Sound alarm (alert crew).
2. Shut down pumps.
3. Shut-in Well (close valves to rig pits and open valve to rig choke line. Rig choke will already be in the closed position).
4. Confirm shut-in.
5. Notify tool pusher/company representative.
6. Open rig choke and begin pumping again taking returns through choke manifold and mud/gas separator.
7. Continue to place cement until plug bumps.
8. At plug bump close rig choke and cement head.
9. Read and record the following
 - a. SICP and AP
 - b. Pit gain
 - c. Time
 - d. Shut-in annulus valves on wellhead

General Procedure After Cementing

1. Sound alarm (alert crew).
2. Shut-in Well (close valves to rig pits and open valve to rig choke line. Rig choke will already be in the closed position).
3. Confirm shut-in.
4. Notify tool pusher/company representative.
5. Read and record the following:
 - a. SICP and AP
 - b. Pit gain
 - c. Time
 - d. Shut-in annulus valves on wellhead



Offline Intermediate Cementing Procedure

2/24/2022

Figure 1: Cameron TA Plug and Offline Adapter Schematic






Offline Intermediate Cementing Procedure

2/24/2022

Figure 2: Cactus TA Plug and Offline Adapter Schematic

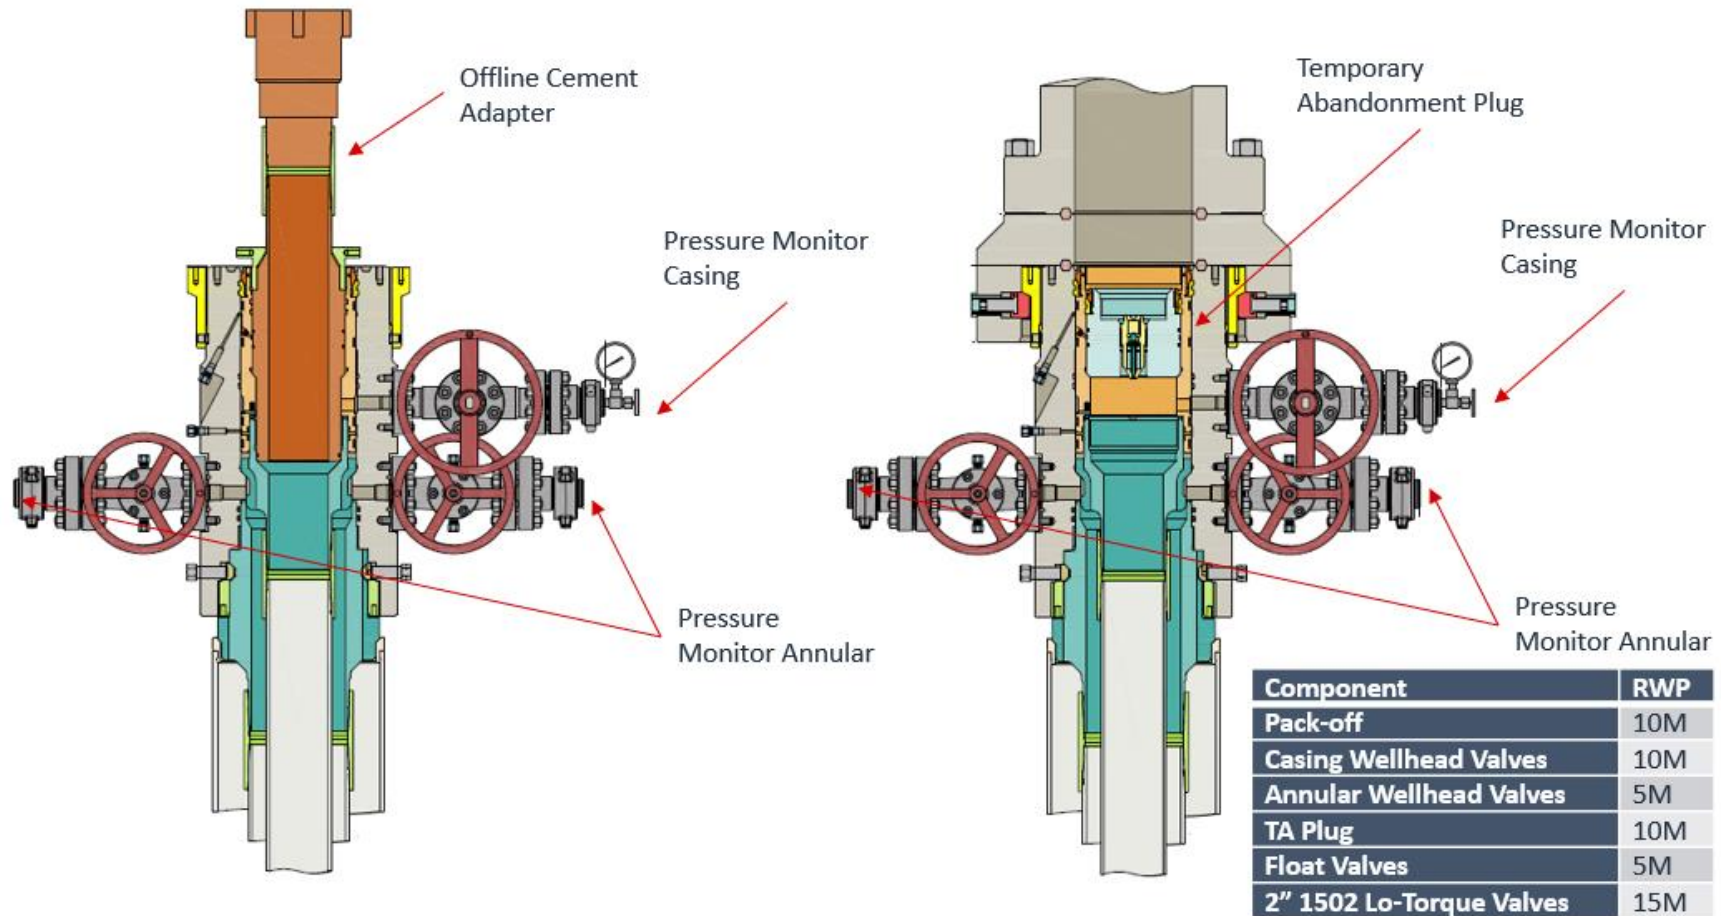




Offline Intermediate Cementing Procedure

2/24/2022

Figure 3: Back Yard Rig Up

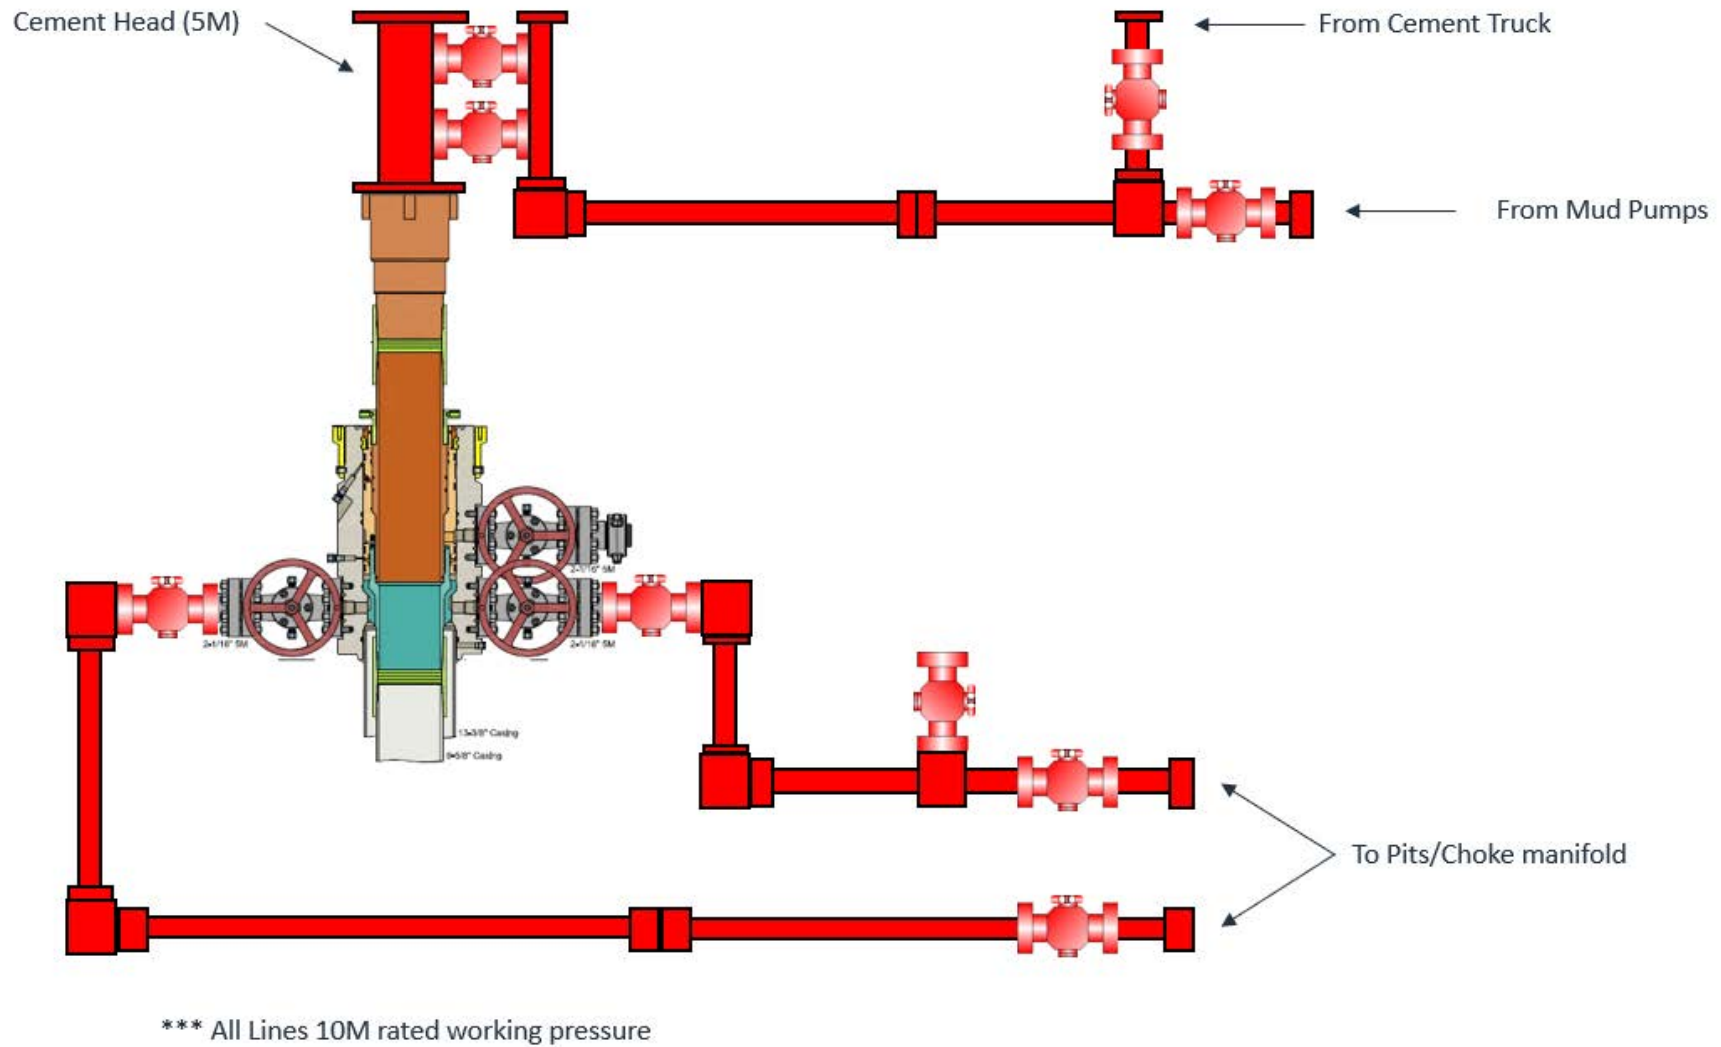



Offline Intermediate Cementing Procedure

2/24/2022

Figure 4: Rig Placement Diagram





Midland

**Lea County, NM (NAD 83 NME)
Green Drake 16 Fed Com
#753H**

OH

Plan: Plan #0.2

Standard Planning Report

24 September, 2024



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-------------------|
| Database: | PEDMB | Local Co-ordinate Reference: | Well #753H |
| Company: | Midland | TVD Reference: | 26 @ 3411.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | 26 @ 3411.0usft |
| Site: | Green Drake 16 Fed Com | North Reference: | Grid |
| Well: | #753H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| | | | |
|--------------------|-----------------------------|----------------------|----------------|
| Project | Lea County, NM (NAD 83 NME) | | |
| Map System: | US State Plane 1983 | System Datum: | Mean Sea Level |
| Geo Datum: | North American Datum 1983 | | |
| Map Zone: | New Mexico Eastern Zone | | |

| | | | | | |
|-----------------------|-----|------------------------|-----------------|------------|------------------|
| Site | | Green Drake 16 Fed Com | | | |
| Site Position: | | Northing: | 411,802.00 usft | Latitude: | 32° 7' 47.652 N |
| From: | Map | Easting: | 773,380.00 usft | Longitude: | 103° 35' 1.431 W |
| Position Uncertainty: | | 0.0 usft | Slot Radius: | 13-3/16 " | |

| Well | #753H | | | | | |
|----------------------|-------|----------|---------------------|-----------------|---------------|-------------------|
| Well Position | +N/-S | 0.0 usft | Northing: | 411,761.00 usft | Latitude: | 32° 7' 46.976 N |
| | +E/-W | 0.0 usft | Easting: | 777,272.00 usft | Longitude: | 103° 34' 16.175 W |
| Position Uncertainty | | 0.0 usft | Wellhead Elevation: | usft | Ground Level: | 3,385.0 usft |
| Grid Convergence: | | 0.41 ° | | | | |

| | | | | | |
|------------------|-------------------|--------------------|------------------------|----------------------|----------------------------|
| Wellbore | OH | | | | |
| Magnetics | Model Name | Sample Date | Declination (°) | Dip Angle (°) | Field Strength (nT) |
| | IGRF2020 | 7/13/2022 | 6.41 | 59.78 | 47,326.28724354 |

| | | | | | |
|--------------------------|--------------------------------|---------------------|---------------------|----------------------|-----|
| Design | Plan #0.2 | | | | |
| Audit Notes: | | | | | |
| Version: | | Phase: | PLAN | Tie On Depth: | 0.0 |
| Vertical Section: | Depth From (TVD) (usft) | +N/-S (usft) | +E/-W (usft) | Direction (°) | |
| | 0.0 | 0.0 | 0.0 | 177.78 | |

| | | | | | |
|---------------------------------|------------------------|--------------------------|------------------|----------------|--|
| Plan Survey Tool Program | Date | 9/24/2024 | | | |
| Depth From (usft) | Depth To (usft) | Survey (Wellbore) | Tool Name | Remarks | |
| 1 | 0.0 | 20,745.4 Plan #0.2 (OH) | EOG MWD+IFR1 | | |
| | | | MWD + IFR1 | | |



Planning Report

| | | | |
|-----------|-----------------------------|------------------------------|-------------------|
| Database: | PEDMB | Local Co-ordinate Reference: | Well #753H |
| Company: | Midland | TVD Reference: | 26 @ 3411.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | 26 @ 3411.0usft |
| Site: | Green Drake 16 Fed Com | North Reference: | Grid |
| Well: | #753H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Plan Sections | | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|------------------------|-----------------------|---------|----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) | TFO (°) | Target |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 1,300.0 | 0.00 | 0.00 | 1,300.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 1,434.0 | 2.68 | 42.60 | 1,434.0 | 2.3 | 2.1 | 2.00 | 2.00 | 0.00 | 42.60 | |
| 8,881.2 | 2.68 | 42.60 | 8,873.0 | 258.7 | 237.9 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 9,015.2 | 0.00 | 0.00 | 9,007.0 | 261.0 | 240.0 | 2.00 | -2.00 | 0.00 | 180.00 | |
| 12,700.7 | 0.00 | 0.00 | 12,692.5 | 261.0 | 240.0 | 0.00 | 0.00 | 0.00 | 0.00 | KOP(Green Drake 16 |
| 12,921.2 | 26.46 | 180.00 | 12,905.2 | 211.0 | 240.0 | 12.00 | 12.00 | 81.65 | 180.00 | FTP(Green Drake 16 |
| 13,450.7 | 90.00 | 179.60 | 13,169.9 | -216.4 | 242.1 | 12.00 | 12.00 | -0.08 | -0.45 | |
| 15,564.3 | 90.00 | 179.60 | 13,170.0 | -2,330.0 | 257.0 | 0.00 | 0.00 | 0.00 | 0.00 | Fed Perf 1(Green Dra |
| 20,745.4 | 90.00 | 179.65 | 13,170.0 | -7,511.0 | 291.0 | 0.00 | 0.00 | 0.00 | 87.00 | PBHL(Green Drake 16 |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-------------------|
| Database: | PEDMB | Local Co-ordinate Reference: | Well #753H |
| Company: | Midland | TVD Reference: | 26 @ 3411.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | 26 @ 3411.0usft |
| Site: | Green Drake 16 Fed Com | North Reference: | Grid |
| Well: | #753H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 100.0 | 0.00 | 0.00 | 100.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 200.0 | 0.00 | 0.00 | 200.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 300.0 | 0.00 | 0.00 | 300.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 400.0 | 0.00 | 0.00 | 400.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 500.0 | 0.00 | 0.00 | 500.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 700.0 | 0.00 | 0.00 | 700.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 800.0 | 0.00 | 0.00 | 800.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 900.0 | 0.00 | 0.00 | 900.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,000.0 | 0.00 | 0.00 | 1,000.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,100.0 | 0.00 | 0.00 | 1,100.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,200.0 | 0.00 | 0.00 | 1,200.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,300.0 | 0.00 | 0.00 | 1,300.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 1,400.0 | 2.00 | 42.60 | 1,400.0 | 1.3 | 1.2 | -1.2 | 2.00 | 2.00 | 0.00 |
| 1,434.0 | 2.68 | 42.60 | 1,434.0 | 2.3 | 2.1 | -2.2 | 2.00 | 2.00 | 0.00 |
| 1,500.0 | 2.68 | 42.60 | 1,499.9 | 4.6 | 4.2 | -4.4 | 0.00 | 0.00 | 0.00 |
| 1,600.0 | 2.68 | 42.60 | 1,599.8 | 8.0 | 7.4 | -7.7 | 0.00 | 0.00 | 0.00 |
| 1,700.0 | 2.68 | 42.60 | 1,699.7 | 11.5 | 10.5 | -11.0 | 0.00 | 0.00 | 0.00 |
| 1,800.0 | 2.68 | 42.60 | 1,799.6 | 14.9 | 13.7 | -14.4 | 0.00 | 0.00 | 0.00 |
| 1,900.0 | 2.68 | 42.60 | 1,899.4 | 18.3 | 16.9 | -17.7 | 0.00 | 0.00 | 0.00 |
| 2,000.0 | 2.68 | 42.60 | 1,999.3 | 21.8 | 20.0 | -21.0 | 0.00 | 0.00 | 0.00 |
| 2,100.0 | 2.68 | 42.60 | 2,099.2 | 25.2 | 23.2 | -24.3 | 0.00 | 0.00 | 0.00 |
| 2,200.0 | 2.68 | 42.60 | 2,199.1 | 28.7 | 26.4 | -27.6 | 0.00 | 0.00 | 0.00 |
| 2,300.0 | 2.68 | 42.60 | 2,299.0 | 32.1 | 29.5 | -31.0 | 0.00 | 0.00 | 0.00 |
| 2,400.0 | 2.68 | 42.60 | 2,398.9 | 35.6 | 32.7 | -34.3 | 0.00 | 0.00 | 0.00 |
| 2,500.0 | 2.68 | 42.60 | 2,498.8 | 39.0 | 35.9 | -37.6 | 0.00 | 0.00 | 0.00 |
| 2,600.0 | 2.68 | 42.60 | 2,598.7 | 42.4 | 39.0 | -40.9 | 0.00 | 0.00 | 0.00 |
| 2,700.0 | 2.68 | 42.60 | 2,698.6 | 45.9 | 42.2 | -44.2 | 0.00 | 0.00 | 0.00 |
| 2,800.0 | 2.68 | 42.60 | 2,798.5 | 49.3 | 45.4 | -47.5 | 0.00 | 0.00 | 0.00 |
| 2,900.0 | 2.68 | 42.60 | 2,898.3 | 52.8 | 48.5 | -50.9 | 0.00 | 0.00 | 0.00 |
| 3,000.0 | 2.68 | 42.60 | 2,998.2 | 56.2 | 51.7 | -54.2 | 0.00 | 0.00 | 0.00 |
| 3,100.0 | 2.68 | 42.60 | 3,098.1 | 59.7 | 54.9 | -57.5 | 0.00 | 0.00 | 0.00 |
| 3,200.0 | 2.68 | 42.60 | 3,198.0 | 63.1 | 58.0 | -60.8 | 0.00 | 0.00 | 0.00 |
| 3,300.0 | 2.68 | 42.60 | 3,297.9 | 66.5 | 61.2 | -64.1 | 0.00 | 0.00 | 0.00 |
| 3,400.0 | 2.68 | 42.60 | 3,397.8 | 70.0 | 64.4 | -67.4 | 0.00 | 0.00 | 0.00 |
| 3,500.0 | 2.68 | 42.60 | 3,497.7 | 73.4 | 67.5 | -70.8 | 0.00 | 0.00 | 0.00 |
| 3,600.0 | 2.68 | 42.60 | 3,597.6 | 76.9 | 70.7 | -74.1 | 0.00 | 0.00 | 0.00 |
| 3,700.0 | 2.68 | 42.60 | 3,697.5 | 80.3 | 73.9 | -77.4 | 0.00 | 0.00 | 0.00 |
| 3,800.0 | 2.68 | 42.60 | 3,797.4 | 83.8 | 77.0 | -80.7 | 0.00 | 0.00 | 0.00 |
| 3,900.0 | 2.68 | 42.60 | 3,897.3 | 87.2 | 80.2 | -84.0 | 0.00 | 0.00 | 0.00 |
| 4,000.0 | 2.68 | 42.60 | 3,997.1 | 90.6 | 83.4 | -87.4 | 0.00 | 0.00 | 0.00 |
| 4,100.0 | 2.68 | 42.60 | 4,097.0 | 94.1 | 86.5 | -90.7 | 0.00 | 0.00 | 0.00 |
| 4,200.0 | 2.68 | 42.60 | 4,196.9 | 97.5 | 89.7 | -94.0 | 0.00 | 0.00 | 0.00 |
| 4,300.0 | 2.68 | 42.60 | 4,296.8 | 101.0 | 92.9 | -97.3 | 0.00 | 0.00 | 0.00 |
| 4,400.0 | 2.68 | 42.60 | 4,396.7 | 104.4 | 96.0 | -100.6 | 0.00 | 0.00 | 0.00 |
| 4,500.0 | 2.68 | 42.60 | 4,496.6 | 107.9 | 99.2 | -103.9 | 0.00 | 0.00 | 0.00 |
| 4,600.0 | 2.68 | 42.60 | 4,596.5 | 111.3 | 102.3 | -107.3 | 0.00 | 0.00 | 0.00 |
| 4,700.0 | 2.68 | 42.60 | 4,696.4 | 114.7 | 105.5 | -110.6 | 0.00 | 0.00 | 0.00 |
| 4,800.0 | 2.68 | 42.60 | 4,796.3 | 118.2 | 108.7 | -113.9 | 0.00 | 0.00 | 0.00 |
| 4,900.0 | 2.68 | 42.60 | 4,896.2 | 121.6 | 111.8 | -117.2 | 0.00 | 0.00 | 0.00 |
| 5,000.0 | 2.68 | 42.60 | 4,996.0 | 125.1 | 115.0 | -120.5 | 0.00 | 0.00 | 0.00 |
| 5,100.0 | 2.68 | 42.60 | 5,095.9 | 128.5 | 118.2 | -123.8 | 0.00 | 0.00 | 0.00 |
| 5,200.0 | 2.68 | 42.60 | 5,195.8 | 132.0 | 121.3 | -127.2 | 0.00 | 0.00 | 0.00 |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-------------------|
| Database: | PEDMB | Local Co-ordinate Reference: | Well #753H |
| Company: | Midland | TVD Reference: | 26 @ 3411.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | 26 @ 3411.0usft |
| Site: | Green Drake 16 Fed Com | North Reference: | Grid |
| Well: | #753H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 5,300.0 | 2.68 | 42.60 | 5,295.7 | 135.4 | 124.5 | -130.5 | 0.00 | 0.00 | 0.00 |
| 5,400.0 | 2.68 | 42.60 | 5,395.6 | 138.8 | 127.7 | -133.8 | 0.00 | 0.00 | 0.00 |
| 5,500.0 | 2.68 | 42.60 | 5,495.5 | 142.3 | 130.8 | -137.1 | 0.00 | 0.00 | 0.00 |
| 5,600.0 | 2.68 | 42.60 | 5,595.4 | 145.7 | 134.0 | -140.4 | 0.00 | 0.00 | 0.00 |
| 5,700.0 | 2.68 | 42.60 | 5,695.3 | 149.2 | 137.2 | -143.8 | 0.00 | 0.00 | 0.00 |
| 5,800.0 | 2.68 | 42.60 | 5,795.2 | 152.6 | 140.3 | -147.1 | 0.00 | 0.00 | 0.00 |
| 5,900.0 | 2.68 | 42.60 | 5,895.1 | 156.1 | 143.5 | -150.4 | 0.00 | 0.00 | 0.00 |
| 6,000.0 | 2.68 | 42.60 | 5,995.0 | 159.5 | 146.7 | -153.7 | 0.00 | 0.00 | 0.00 |
| 6,100.0 | 2.68 | 42.60 | 6,094.8 | 162.9 | 149.8 | -157.0 | 0.00 | 0.00 | 0.00 |
| 6,200.0 | 2.68 | 42.60 | 6,194.7 | 166.4 | 153.0 | -160.3 | 0.00 | 0.00 | 0.00 |
| 6,300.0 | 2.68 | 42.60 | 6,294.6 | 169.8 | 156.2 | -163.7 | 0.00 | 0.00 | 0.00 |
| 6,400.0 | 2.68 | 42.60 | 6,394.5 | 173.3 | 159.3 | -167.0 | 0.00 | 0.00 | 0.00 |
| 6,500.0 | 2.68 | 42.60 | 6,494.4 | 176.7 | 162.5 | -170.3 | 0.00 | 0.00 | 0.00 |
| 6,600.0 | 2.68 | 42.60 | 6,594.3 | 180.2 | 165.7 | -173.6 | 0.00 | 0.00 | 0.00 |
| 6,700.0 | 2.68 | 42.60 | 6,694.2 | 183.6 | 168.8 | -176.9 | 0.00 | 0.00 | 0.00 |
| 6,800.0 | 2.68 | 42.60 | 6,794.1 | 187.0 | 172.0 | -180.2 | 0.00 | 0.00 | 0.00 |
| 6,900.0 | 2.68 | 42.60 | 6,894.0 | 190.5 | 175.2 | -183.6 | 0.00 | 0.00 | 0.00 |
| 7,000.0 | 2.68 | 42.60 | 6,993.9 | 193.9 | 178.3 | -186.9 | 0.00 | 0.00 | 0.00 |
| 7,100.0 | 2.68 | 42.60 | 7,093.8 | 197.4 | 181.5 | -190.2 | 0.00 | 0.00 | 0.00 |
| 7,200.0 | 2.68 | 42.60 | 7,193.6 | 200.8 | 184.7 | -193.5 | 0.00 | 0.00 | 0.00 |
| 7,300.0 | 2.68 | 42.60 | 7,293.5 | 204.3 | 187.8 | -196.8 | 0.00 | 0.00 | 0.00 |
| 7,400.0 | 2.68 | 42.60 | 7,393.4 | 207.7 | 191.0 | -200.1 | 0.00 | 0.00 | 0.00 |
| 7,500.0 | 2.68 | 42.60 | 7,493.3 | 211.1 | 194.2 | -203.5 | 0.00 | 0.00 | 0.00 |
| 7,600.0 | 2.68 | 42.60 | 7,593.2 | 214.6 | 197.3 | -206.8 | 0.00 | 0.00 | 0.00 |
| 7,700.0 | 2.68 | 42.60 | 7,693.1 | 218.0 | 200.5 | -210.1 | 0.00 | 0.00 | 0.00 |
| 7,800.0 | 2.68 | 42.60 | 7,793.0 | 221.5 | 203.6 | -213.4 | 0.00 | 0.00 | 0.00 |
| 7,900.0 | 2.68 | 42.60 | 7,892.9 | 224.9 | 206.8 | -216.7 | 0.00 | 0.00 | 0.00 |
| 8,000.0 | 2.68 | 42.60 | 7,992.8 | 228.4 | 210.0 | -220.1 | 0.00 | 0.00 | 0.00 |
| 8,100.0 | 2.68 | 42.60 | 8,092.7 | 231.8 | 213.1 | -223.4 | 0.00 | 0.00 | 0.00 |
| 8,200.0 | 2.68 | 42.60 | 8,192.5 | 235.2 | 216.3 | -226.7 | 0.00 | 0.00 | 0.00 |
| 8,300.0 | 2.68 | 42.60 | 8,292.4 | 238.7 | 219.5 | -230.0 | 0.00 | 0.00 | 0.00 |
| 8,400.0 | 2.68 | 42.60 | 8,392.3 | 242.1 | 222.6 | -233.3 | 0.00 | 0.00 | 0.00 |
| 8,500.0 | 2.68 | 42.60 | 8,492.2 | 245.6 | 225.8 | -236.6 | 0.00 | 0.00 | 0.00 |
| 8,600.0 | 2.68 | 42.60 | 8,592.1 | 249.0 | 229.0 | -240.0 | 0.00 | 0.00 | 0.00 |
| 8,700.0 | 2.68 | 42.60 | 8,692.0 | 252.5 | 232.1 | -243.3 | 0.00 | 0.00 | 0.00 |
| 8,800.0 | 2.68 | 42.60 | 8,791.9 | 255.9 | 235.3 | -246.6 | 0.00 | 0.00 | 0.00 |
| 8,881.2 | 2.68 | 42.60 | 8,873.0 | 258.7 | 237.9 | -249.3 | 0.00 | 0.00 | 0.00 |
| 8,900.0 | 2.30 | 42.60 | 8,891.8 | 259.3 | 238.4 | -249.9 | 2.00 | -2.00 | 0.00 |
| 9,000.0 | 0.30 | 42.60 | 8,991.8 | 261.0 | 240.0 | -251.5 | 2.00 | -2.00 | 0.00 |
| 9,015.2 | 0.00 | 0.00 | 9,007.0 | 261.0 | 240.0 | -251.5 | 2.00 | -2.00 | 0.00 |
| 9,100.0 | 0.00 | 0.00 | 9,091.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,200.0 | 0.00 | 0.00 | 9,191.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,300.0 | 0.00 | 0.00 | 9,291.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,400.0 | 0.00 | 0.00 | 9,391.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,500.0 | 0.00 | 0.00 | 9,491.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,600.0 | 0.00 | 0.00 | 9,591.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,700.0 | 0.00 | 0.00 | 9,691.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,800.0 | 0.00 | 0.00 | 9,791.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 9,900.0 | 0.00 | 0.00 | 9,891.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,000.0 | 0.00 | 0.00 | 9,991.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,100.0 | 0.00 | 0.00 | 10,091.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,200.0 | 0.00 | 0.00 | 10,191.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,300.0 | 0.00 | 0.00 | 10,291.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,400.0 | 0.00 | 0.00 | 10,391.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-------------------|
| Database: | PEDMB | Local Co-ordinate Reference: | Well #753H |
| Company: | Midland | TVD Reference: | 26 @ 3411.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | 26 @ 3411.0usft |
| Site: | Green Drake 16 Fed Com | North Reference: | Grid |
| Well: | #753H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 10,500.0 | 0.00 | 0.00 | 10,491.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,600.0 | 0.00 | 0.00 | 10,591.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,700.0 | 0.00 | 0.00 | 10,691.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,800.0 | 0.00 | 0.00 | 10,791.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 10,900.0 | 0.00 | 0.00 | 10,891.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,000.0 | 0.00 | 0.00 | 10,991.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,100.0 | 0.00 | 0.00 | 11,091.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,200.0 | 0.00 | 0.00 | 11,191.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,300.0 | 0.00 | 0.00 | 11,291.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,400.0 | 0.00 | 0.00 | 11,391.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,500.0 | 0.00 | 0.00 | 11,491.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,600.0 | 0.00 | 0.00 | 11,591.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,700.0 | 0.00 | 0.00 | 11,691.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,800.0 | 0.00 | 0.00 | 11,791.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 11,900.0 | 0.00 | 0.00 | 11,891.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,000.0 | 0.00 | 0.00 | 11,991.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,100.0 | 0.00 | 0.00 | 12,091.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,200.0 | 0.00 | 0.00 | 12,191.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,300.0 | 0.00 | 0.00 | 12,291.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,400.0 | 0.00 | 0.00 | 12,391.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,500.0 | 0.00 | 0.00 | 12,491.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,600.0 | 0.00 | 0.00 | 12,591.8 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,700.7 | 0.00 | 0.00 | 12,692.5 | 261.0 | 240.0 | -251.5 | 0.00 | 0.00 | 0.00 |
| 12,725.0 | 2.91 | 180.00 | 12,716.7 | 260.4 | 240.0 | -250.9 | 12.00 | 12.00 | 0.00 |
| 12,750.0 | 5.91 | 180.00 | 12,741.7 | 258.5 | 240.0 | -249.0 | 12.00 | 12.00 | 0.00 |
| 12,775.0 | 8.91 | 180.00 | 12,766.5 | 255.2 | 240.0 | -245.8 | 12.00 | 12.00 | 0.00 |
| 12,800.0 | 11.91 | 180.00 | 12,791.0 | 250.7 | 240.0 | -241.2 | 12.00 | 12.00 | 0.00 |
| 12,825.0 | 14.91 | 180.00 | 12,815.4 | 244.9 | 240.0 | -235.4 | 12.00 | 12.00 | 0.00 |
| 12,850.0 | 17.91 | 180.00 | 12,839.3 | 237.9 | 240.0 | -228.4 | 12.00 | 12.00 | 0.00 |
| 12,875.0 | 20.91 | 180.00 | 12,862.9 | 229.6 | 240.0 | -220.1 | 12.00 | 12.00 | 0.00 |
| 12,900.0 | 23.91 | 180.00 | 12,886.0 | 220.0 | 240.0 | -210.6 | 12.00 | 12.00 | 0.00 |
| 12,921.2 | 26.46 | 180.00 | 12,905.2 | 211.0 | 240.0 | -201.6 | 12.00 | 12.00 | 0.00 |
| 12,925.0 | 26.91 | 179.99 | 12,908.6 | 209.3 | 240.0 | -199.8 | 12.00 | 12.00 | -0.21 |
| 12,950.0 | 29.91 | 179.95 | 12,930.6 | 197.4 | 240.0 | -188.0 | 12.00 | 12.00 | -0.19 |
| 12,975.0 | 32.91 | 179.91 | 12,951.9 | 184.4 | 240.0 | -174.9 | 12.00 | 12.00 | -0.16 |
| 13,000.0 | 35.91 | 179.87 | 12,972.5 | 170.2 | 240.1 | -160.8 | 12.00 | 12.00 | -0.13 |
| 13,025.0 | 38.91 | 179.84 | 12,992.4 | 155.1 | 240.1 | -145.6 | 12.00 | 12.00 | -0.11 |
| 13,050.0 | 41.91 | 179.82 | 13,011.4 | 138.9 | 240.1 | -129.4 | 12.00 | 12.00 | -0.10 |
| 13,075.0 | 44.91 | 179.80 | 13,029.6 | 121.7 | 240.2 | -112.3 | 12.00 | 12.00 | -0.09 |
| 13,100.0 | 47.91 | 179.78 | 13,046.8 | 103.6 | 240.3 | -94.2 | 12.00 | 12.00 | -0.08 |
| 13,125.0 | 50.91 | 179.76 | 13,063.1 | 84.6 | 240.3 | -75.2 | 12.00 | 12.00 | -0.07 |
| 13,150.0 | 53.91 | 179.74 | 13,078.3 | 64.8 | 240.4 | -55.4 | 12.00 | 12.00 | -0.07 |
| 13,175.0 | 56.91 | 179.73 | 13,092.5 | 44.2 | 240.5 | -34.9 | 12.00 | 12.00 | -0.06 |
| 13,200.0 | 59.91 | 179.71 | 13,105.6 | 22.9 | 240.6 | -13.6 | 12.00 | 12.00 | -0.06 |
| 13,225.0 | 62.91 | 179.70 | 13,117.6 | 1.0 | 240.7 | 8.4 | 12.00 | 12.00 | -0.05 |
| 13,250.0 | 65.91 | 179.69 | 13,128.4 | -21.6 | 240.9 | 30.9 | 12.00 | 12.00 | -0.05 |
| 13,275.0 | 68.91 | 179.67 | 13,138.0 | -44.7 | 241.0 | 54.0 | 12.00 | 12.00 | -0.05 |
| 13,300.0 | 71.91 | 179.66 | 13,146.4 | -68.2 | 241.1 | 77.5 | 12.00 | 12.00 | -0.05 |
| 13,325.0 | 74.91 | 179.65 | 13,153.5 | -92.2 | 241.3 | 101.5 | 12.00 | 12.00 | -0.05 |
| 13,350.0 | 77.91 | 179.64 | 13,159.4 | -116.5 | 241.4 | 125.7 | 12.00 | 12.00 | -0.04 |
| 13,375.0 | 80.91 | 179.63 | 13,164.0 | -141.0 | 241.6 | 150.3 | 12.00 | 12.00 | -0.04 |
| 13,400.0 | 83.91 | 179.62 | 13,167.3 | -165.8 | 241.7 | 175.1 | 12.00 | 12.00 | -0.04 |
| 13,425.0 | 86.91 | 179.61 | 13,169.3 | -190.7 | 241.9 | 200.0 | 12.00 | 12.00 | -0.04 |
| 13,450.7 | 90.00 | 179.60 | 13,169.9 | -216.4 | 242.1 | 225.7 | 12.00 | 12.00 | -0.04 |



Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-------------------|
| Database: | PEDMB | Local Co-ordinate Reference: | Well #753H |
| Company: | Midland | TVD Reference: | 26 @ 3411.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | 26 @ 3411.0usft |
| Site: | Green Drake 16 Fed Com | North Reference: | Grid |
| Well: | #753H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 13,500.0 | 90.00 | 179.60 | 13,169.9 | -265.7 | 242.4 | 274.9 | 0.00 | 0.00 | 0.00 |
| 13,600.0 | 90.00 | 179.60 | 13,169.9 | -365.7 | 243.1 | 374.9 | 0.00 | 0.00 | 0.00 |
| 13,700.0 | 90.00 | 179.60 | 13,170.0 | -465.7 | 243.8 | 474.8 | 0.00 | 0.00 | 0.00 |
| 13,800.0 | 90.00 | 179.60 | 13,170.0 | -565.7 | 244.6 | 574.8 | 0.00 | 0.00 | 0.00 |
| 13,900.0 | 90.00 | 179.60 | 13,170.0 | -665.7 | 245.3 | 674.7 | 0.00 | 0.00 | 0.00 |
| 14,000.0 | 90.00 | 179.60 | 13,170.0 | -765.7 | 246.0 | 774.7 | 0.00 | 0.00 | 0.00 |
| 14,100.0 | 90.00 | 179.60 | 13,170.0 | -865.7 | 246.7 | 874.6 | 0.00 | 0.00 | 0.00 |
| 14,200.0 | 90.00 | 179.60 | 13,170.0 | -965.7 | 247.4 | 974.6 | 0.00 | 0.00 | 0.00 |
| 14,300.0 | 90.00 | 179.60 | 13,170.0 | -1,065.7 | 248.1 | 1,074.5 | 0.00 | 0.00 | 0.00 |
| 14,400.0 | 90.00 | 179.60 | 13,170.0 | -1,165.7 | 248.8 | 1,174.5 | 0.00 | 0.00 | 0.00 |
| 14,500.0 | 90.00 | 179.60 | 13,170.0 | -1,265.7 | 249.5 | 1,274.4 | 0.00 | 0.00 | 0.00 |
| 14,600.0 | 90.00 | 179.60 | 13,170.0 | -1,365.7 | 250.2 | 1,374.4 | 0.00 | 0.00 | 0.00 |
| 14,700.0 | 90.00 | 179.60 | 13,170.0 | -1,465.7 | 250.9 | 1,474.3 | 0.00 | 0.00 | 0.00 |
| 14,800.0 | 90.00 | 179.60 | 13,170.0 | -1,565.7 | 251.6 | 1,574.3 | 0.00 | 0.00 | 0.00 |
| 14,900.0 | 90.00 | 179.60 | 13,170.0 | -1,665.7 | 252.3 | 1,674.2 | 0.00 | 0.00 | 0.00 |
| 15,000.0 | 90.00 | 179.60 | 13,170.0 | -1,765.7 | 253.0 | 1,774.2 | 0.00 | 0.00 | 0.00 |
| 15,100.0 | 90.00 | 179.60 | 13,170.0 | -1,865.7 | 253.7 | 1,874.1 | 0.00 | 0.00 | 0.00 |
| 15,200.0 | 90.00 | 179.60 | 13,170.0 | -1,965.7 | 254.4 | 1,974.1 | 0.00 | 0.00 | 0.00 |
| 15,300.0 | 90.00 | 179.60 | 13,170.0 | -2,065.7 | 255.1 | 2,074.0 | 0.00 | 0.00 | 0.00 |
| 15,400.0 | 90.00 | 179.60 | 13,170.0 | -2,165.7 | 255.8 | 2,174.0 | 0.00 | 0.00 | 0.00 |
| 15,500.0 | 90.00 | 179.60 | 13,170.0 | -2,265.7 | 256.5 | 2,273.9 | 0.00 | 0.00 | 0.00 |
| 15,564.3 | 90.00 | 179.60 | 13,170.0 | -2,330.0 | 257.0 | 2,338.2 | 0.00 | 0.00 | 0.00 |
| 15,600.0 | 90.00 | 179.60 | 13,170.0 | -2,365.7 | 257.3 | 2,373.9 | 0.00 | 0.00 | 0.00 |
| 15,700.0 | 90.00 | 179.60 | 13,170.0 | -2,465.7 | 258.0 | 2,473.8 | 0.00 | 0.00 | 0.00 |
| 15,800.0 | 90.00 | 179.60 | 13,170.0 | -2,565.7 | 258.7 | 2,573.8 | 0.00 | 0.00 | 0.00 |
| 15,900.0 | 90.00 | 179.60 | 13,170.0 | -2,665.7 | 259.4 | 2,673.7 | 0.00 | 0.00 | 0.00 |
| 16,000.0 | 90.00 | 179.60 | 13,170.0 | -2,765.7 | 260.1 | 2,773.7 | 0.00 | 0.00 | 0.00 |
| 16,100.0 | 90.00 | 179.60 | 13,170.0 | -2,865.7 | 260.8 | 2,873.6 | 0.00 | 0.00 | 0.00 |
| 16,200.0 | 90.00 | 179.60 | 13,170.0 | -2,965.7 | 261.4 | 2,973.6 | 0.00 | 0.00 | 0.00 |
| 16,300.0 | 90.00 | 179.60 | 13,170.0 | -3,065.7 | 262.1 | 3,073.5 | 0.00 | 0.00 | 0.00 |
| 16,400.0 | 90.00 | 179.60 | 13,170.0 | -3,165.7 | 262.8 | 3,173.5 | 0.00 | 0.00 | 0.00 |
| 16,500.0 | 90.00 | 179.61 | 13,170.0 | -3,265.7 | 263.5 | 3,273.4 | 0.00 | 0.00 | 0.00 |
| 16,600.0 | 90.00 | 179.61 | 13,170.0 | -3,365.7 | 264.2 | 3,373.4 | 0.00 | 0.00 | 0.00 |
| 16,700.0 | 90.00 | 179.61 | 13,170.0 | -3,465.6 | 264.9 | 3,473.3 | 0.00 | 0.00 | 0.00 |
| 16,800.0 | 90.00 | 179.61 | 13,170.0 | -3,565.6 | 265.6 | 3,573.3 | 0.00 | 0.00 | 0.00 |
| 16,900.0 | 90.00 | 179.61 | 13,170.0 | -3,665.6 | 266.3 | 3,673.2 | 0.00 | 0.00 | 0.00 |
| 17,000.0 | 90.00 | 179.61 | 13,170.0 | -3,765.6 | 266.9 | 3,773.2 | 0.00 | 0.00 | 0.00 |
| 17,100.0 | 90.00 | 179.61 | 13,170.0 | -3,865.6 | 267.6 | 3,873.1 | 0.00 | 0.00 | 0.00 |
| 17,200.0 | 90.00 | 179.61 | 13,170.0 | -3,965.6 | 268.3 | 3,973.1 | 0.00 | 0.00 | 0.00 |
| 17,300.0 | 90.00 | 179.61 | 13,170.0 | -4,065.6 | 269.0 | 4,073.0 | 0.00 | 0.00 | 0.00 |
| 17,400.0 | 90.00 | 179.62 | 13,170.0 | -4,165.6 | 269.6 | 4,172.9 | 0.00 | 0.00 | 0.00 |
| 17,500.0 | 90.00 | 179.62 | 13,170.0 | -4,265.6 | 270.3 | 4,272.9 | 0.00 | 0.00 | 0.00 |
| 17,600.0 | 90.00 | 179.62 | 13,170.0 | -4,365.6 | 271.0 | 4,372.8 | 0.00 | 0.00 | 0.00 |
| 17,700.0 | 90.00 | 179.62 | 13,170.0 | -4,465.6 | 271.6 | 4,472.8 | 0.00 | 0.00 | 0.00 |
| 17,800.0 | 90.00 | 179.62 | 13,170.0 | -4,565.6 | 272.3 | 4,572.7 | 0.00 | 0.00 | 0.00 |
| 17,900.0 | 90.00 | 179.62 | 13,170.0 | -4,665.6 | 273.0 | 4,672.7 | 0.00 | 0.00 | 0.00 |
| 18,000.0 | 90.00 | 179.62 | 13,170.0 | -4,765.6 | 273.6 | 4,772.6 | 0.00 | 0.00 | 0.00 |
| 18,100.0 | 90.00 | 179.62 | 13,170.0 | -4,865.6 | 274.3 | 4,872.6 | 0.00 | 0.00 | 0.00 |
| 18,200.0 | 90.00 | 179.62 | 13,170.0 | -4,965.6 | 274.9 | 4,972.5 | 0.00 | 0.00 | 0.00 |
| 18,300.0 | 90.00 | 179.63 | 13,170.0 | -5,065.6 | 275.6 | 5,072.5 | 0.00 | 0.00 | 0.00 |
| 18,400.0 | 90.00 | 179.63 | 13,170.0 | -5,165.6 | 276.2 | 5,172.4 | 0.00 | 0.00 | 0.00 |
| 18,500.0 | 90.00 | 179.63 | 13,170.0 | -5,265.6 | 276.9 | 5,272.4 | 0.00 | 0.00 | 0.00 |
| 18,600.0 | 90.00 | 179.63 | 13,170.0 | -5,365.6 | 277.5 | 5,372.3 | 0.00 | 0.00 | 0.00 |
| 18,700.0 | 90.00 | 179.63 | 13,170.0 | -5,465.6 | 278.2 | 5,472.3 | 0.00 | 0.00 | 0.00 |




Planning Report

| | | | |
|------------------|-----------------------------|-------------------------------------|-------------------|
| Database: | PEDMB | Local Co-ordinate Reference: | Well #753H |
| Company: | Midland | TVD Reference: | 26 @ 3411.0usft |
| Project: | Lea County, NM (NAD 83 NME) | MD Reference: | 26 @ 3411.0usft |
| Site: | Green Drake 16 Fed Com | North Reference: | Grid |
| Well: | #753H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | OH | | |
| Design: | Plan #0.2 | | |

| Planned Survey | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|--------------|--------------|-------------------------|-------------------------|------------------------|-----------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Vertical Section (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) |
| 18,800.0 | 90.00 | 179.63 | 13,170.0 | -5,565.6 | 278.8 | 5,572.2 | 0.00 | 0.00 | 0.00 |
| 18,900.0 | 90.00 | 179.63 | 13,170.0 | -5,665.6 | 279.5 | 5,672.2 | 0.00 | 0.00 | 0.00 |
| 19,000.0 | 90.00 | 179.63 | 13,170.0 | -5,765.6 | 280.1 | 5,772.1 | 0.00 | 0.00 | 0.00 |
| 19,100.0 | 90.00 | 179.63 | 13,170.0 | -5,865.6 | 280.8 | 5,872.1 | 0.00 | 0.00 | 0.00 |
| 19,200.0 | 90.00 | 179.64 | 13,170.0 | -5,965.6 | 281.4 | 5,972.0 | 0.00 | 0.00 | 0.00 |
| 19,300.0 | 90.00 | 179.64 | 13,170.0 | -6,065.6 | 282.0 | 6,072.0 | 0.00 | 0.00 | 0.00 |
| 19,400.0 | 90.00 | 179.64 | 13,170.0 | -6,165.6 | 282.7 | 6,171.9 | 0.00 | 0.00 | 0.00 |
| 19,500.0 | 90.00 | 179.64 | 13,170.0 | -6,265.6 | 283.3 | 6,271.9 | 0.00 | 0.00 | 0.00 |
| 19,600.0 | 90.00 | 179.64 | 13,170.0 | -6,365.6 | 283.9 | 6,371.8 | 0.00 | 0.00 | 0.00 |
| 19,700.0 | 90.00 | 179.64 | 13,170.0 | -6,465.6 | 284.6 | 6,471.8 | 0.00 | 0.00 | 0.00 |
| 19,800.0 | 90.00 | 179.64 | 13,170.0 | -6,565.6 | 285.2 | 6,571.7 | 0.00 | 0.00 | 0.00 |
| 19,900.0 | 90.00 | 179.64 | 13,170.0 | -6,665.6 | 285.8 | 6,671.6 | 0.00 | 0.00 | 0.00 |
| 20,000.0 | 90.00 | 179.64 | 13,170.0 | -6,765.6 | 286.4 | 6,771.6 | 0.00 | 0.00 | 0.00 |
| 20,100.0 | 90.00 | 179.65 | 13,170.0 | -6,865.6 | 287.0 | 6,871.5 | 0.00 | 0.00 | 0.00 |
| 20,200.0 | 90.00 | 179.65 | 13,170.0 | -6,965.6 | 287.7 | 6,971.5 | 0.00 | 0.00 | 0.00 |
| 20,300.0 | 90.00 | 179.65 | 13,170.0 | -7,065.6 | 288.3 | 7,071.4 | 0.00 | 0.00 | 0.00 |
| 20,400.0 | 90.00 | 179.65 | 13,170.0 | -7,165.6 | 288.9 | 7,171.4 | 0.00 | 0.00 | 0.00 |
| 20,500.0 | 90.00 | 179.65 | 13,170.0 | -7,265.6 | 289.5 | 7,271.3 | 0.00 | 0.00 | 0.00 |
| 20,600.0 | 90.00 | 179.65 | 13,170.0 | -7,365.6 | 290.1 | 7,371.3 | 0.00 | 0.00 | 0.00 |
| 20,700.0 | 90.00 | 179.65 | 13,170.0 | -7,465.6 | 290.7 | 7,471.2 | 0.00 | 0.00 | 0.00 |
| 20,745.4 | 90.00 | 179.65 | 13,170.0 | -7,511.0 | 291.0 | 7,516.6 | 0.00 | 0.00 | 0.00 |

| Design Targets | | | | | | | | | |
|--|---------------|--------------|------------|--------------|--------------|-----------------|----------------|-----------------|-------------------|
| Target Name - hit/miss target - Shape | Dip Angle (°) | Dip Dir. (°) | TVD (usft) | +N/-S (usft) | +E/-W (usft) | Northing (usft) | Easting (usft) | Latitude | Longitude |
| KOP(Green Drake 16 Fe - plan hits target center - Point | 0.00 | 0.00 | 12,692.5 | 261.0 | 240.0 | 412,022.00 | 777,512.00 | 32° 7' 49.542 N | 103° 34' 13.363 W |
| FTP(Green Drake 16 Fe - plan hits target center - Point | 0.00 | 0.00 | 12,905.2 | 211.0 | 240.0 | 411,972.00 | 777,512.00 | 32° 7' 49.047 N | 103° 34' 13.367 W |
| PBHL(Green Drake 16 F - plan hits target center - Point | 0.00 | 0.00 | 13,170.0 | -7,511.0 | 291.0 | 404,250.00 | 777,563.00 | 32° 6' 32.632 N | 103° 34' 13.410 W |
| Fed Perf 1(Green Drake - plan hits target center - Point | 0.00 | 0.00 | 13,170.0 | -2,330.0 | 257.0 | 409,431.00 | 777,529.00 | 32° 7' 23.902 N | 103° 34' 13.379 W |

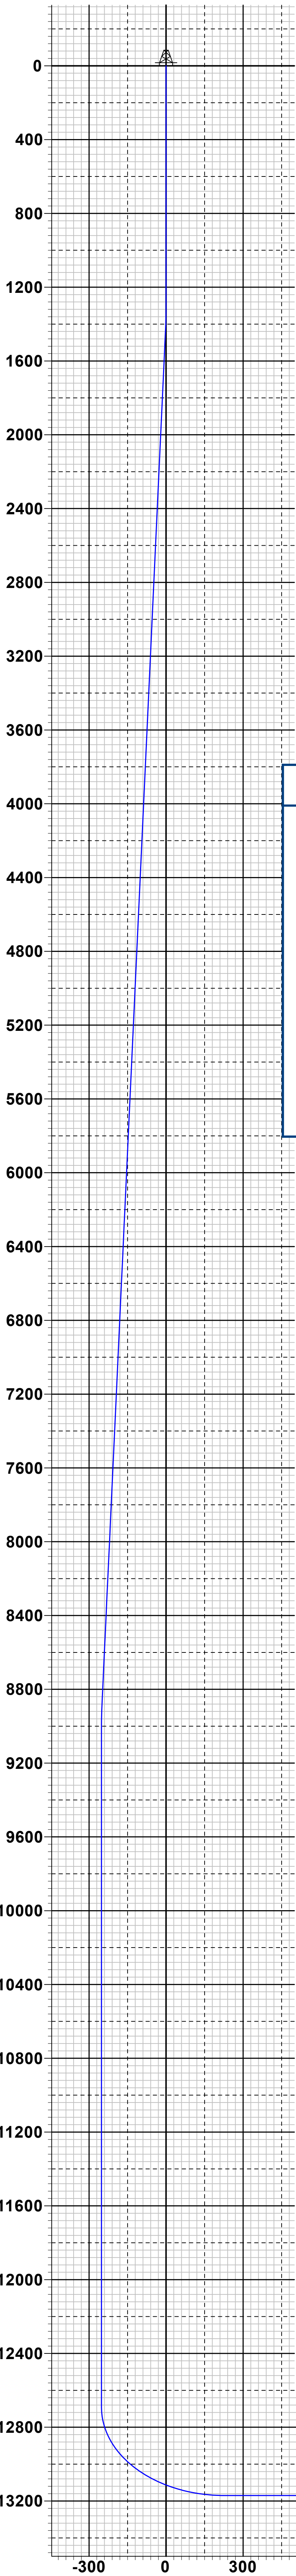


To convert a Magnetic Direction to a Grid Direction, Add 6.01°
To convert a Magnetic Direction to a True Direction, Add 6.41° East
To convert a True Direction to a Grid Direction, Subtract 0.41°

| WELL DETAILS: #753H | | | |
|------------------------|-----------|-----------------|-------------------|
| 26 @ 3411.0usft 3385.0 | | | |
| Northing | Easting | Latitude | Longitude |
| 411761.00 | 777272.00 | 32° 7' 46.976 N | 103° 34' 16.175 W |

| SECTION DETAILS | | | | | | | | | | |
|-----------------|---------|-------|--------|---------|---------|-------|-------|--------|--------|--|
| Sec | MD | Inc | Azi | TVD | +N/-S | +E/-W | Dleg | TFace | VSect | Target |
| 1 | 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 2 | 1300.0 | 0.00 | 0.00 | 1300.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 3 | 1434.0 | 2.68 | 42.60 | 1434.0 | 2.3 | 2.1 | 2.00 | 42.60 | -2.2 | |
| 4 | 8881.2 | 2.68 | 42.60 | 8873.0 | 258.7 | 237.9 | 0.00 | 0.00 | -249.3 | |
| 5 | 9015.2 | 0.00 | 0.00 | 9007.0 | 261.0 | 240.0 | 2.00 | 180.00 | -251.5 | |
| 6 | 12700.7 | 0.00 | 0.00 | 12692.5 | 261.0 | 240.0 | 0.00 | 0.00 | -251.5 | KOP(Green Drake 16 Fed Com #509H) |
| 7 | 12921.2 | 26.46 | 180.00 | 12905.2 | 211.0 | 240.0 | 12.00 | 180.00 | -201.6 | FTP(Green Drake 16 Fed Com #509H) |
| 8 | 13450.7 | 90.00 | 179.60 | 13169.9 | -216.4 | 242.1 | 12.00 | -0.45 | 225.7 | |
| 9 | 15564.3 | 90.00 | 179.60 | 13170.0 | -2330.0 | 257.0 | 0.00 | 0.00 | 2338.2 | Fed Perf 1(Green Drake 16 Fed Com #509H) |
| 10 | 20745.4 | 90.00 | 179.65 | 13170.0 | -7511.0 | 291.0 | 0.00 | 87.00 | 7516.6 | PBHL(Green Drake 16 Fed Com #509H) |

| CASING DETAILS |
|-----------------------------|
| No casing data is available |

| WELLBORE TARGET DETAILS (MAP CO-ORDINATES) | | | | | |
|--|---------|---------|-------|-----------|-----------|
| Name | TVD | +N/-S | +E/-W | Northing | Easting |
| KOP(Green Drake 16 Fed Com #509H) | 12692.5 | 261.0 | 240.0 | 412022.00 | 777512.00 |
| FTP(Green Drake 16 Fed Com #509H) | 12905.2 | 211.0 | 240.0 | 411972.00 | 777512.00 |
| Fed Perf 1(Green Drake 16 Fed Com #509H) | 13170.0 | -2330.0 | 257.0 | 409431.00 | 777529.00 |
| PBHL(Green Drake 16 Fed Com #509H) | 13170.0 | -7511.0 | 291.0 | 404250.00 | 777563.00 |

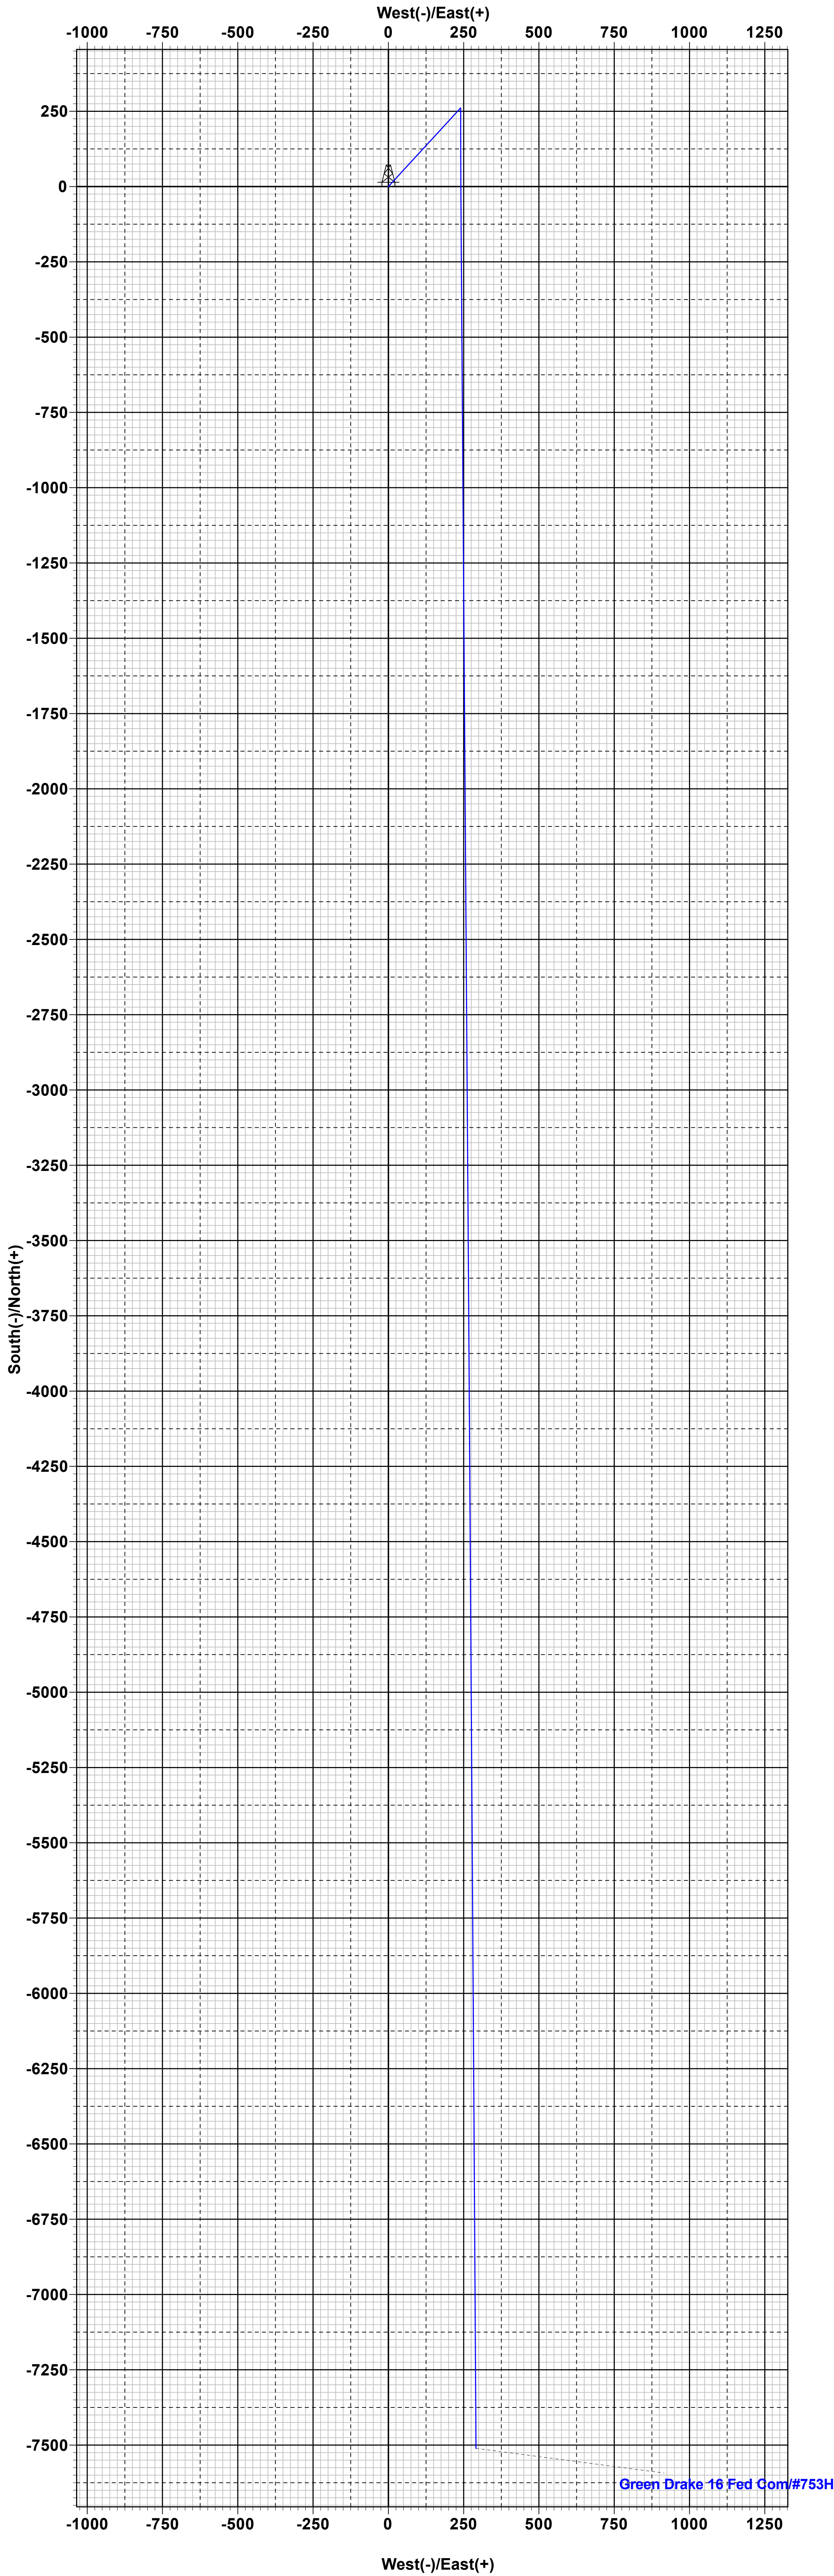

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 395335

CONDITIONS

| | |
|---|--|
| Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706 | OGRID: 7377 |
| | Action Number: 395335 |
| | Action Type: [C-103] NOI Change of Plans (C-103A) |

CONDITIONS

| Created By | Condition | Condition Date |
|------------|--|----------------|
| pkautz | If cement is not circulated to surface during cementing operations, a Cement Bond Log (CBL) is required. | 2/18/2025 |
| pkautz | Cement is required to circulate on both surface and intermediate1 strings of casing. | 2/18/2025 |
