

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER 1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other 1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-025-54627
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.



(Continued on page 2)

*(Instructions on page 2)

Additional Operator Remarks

Location of Well

0. SHL: SESE / 480 FSL / 1185 FEL / TWSP: 20S / RANGE: 33E / SECTION: 15 / LAT: 32.567215 / LONG: -103.646362 (TVD: 0 feet, MD: 0 feet)
PPP: NWNE / 100 FNL / 1640 FEL / TWSP: 20S / RANGE: 33E / SECTION: 22 / LAT: 32.565618 / LONG: -103.64784 (TVD: 10393 feet, MD: 10500 feet)
PPP: NWNE / 1 FNL / 1640 FEL / TWSP: 20S / RANGE: 33E / SECTION: 27 / LAT: 32.551379 / LONG: -103.647832 (TVD: 10575 feet, MD: 15681 feet)
PPP: SWNE / 1321 FNL / 1640 FEL / TWSP: 20S / RANGE: 33E / SECTION: 22 / LAT: 32.562268 / LONG: -103.647838 (TVD: 10575 feet, MD: 11721 feet)
PPP: NWNE / 1 FNL / 1640 FEL / TWSP: 20S / RANGE: 33E / SECTION: 34 / LAT: 32.536861 / LONG: -103.647819 (TVD: 10575 feet, MD: 20961 feet)
BHL: SWSE / 50 FSL / 1640 FEL / TWSP: 20S / RANGE: 33E / SECTION: 34 / LAT: 32.522482 / LONG: -103.647815 (TVD: 10575 feet, MD: 26040 feet)

BLM Point of Contact

Name: JANET D ESTES
Title: ADJUDICATOR
Phone: (575) 234-6233
Email: JESTES@BLM.GOV

C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024	
		Submittal Type:	☒ Initial Submittal
			☐ Amended Report
		☐ As Drilled	

WELL LOCATION INFORMATION

API Number 30-025-54627	Pool Code 58960	Pool Name Teas; Bone Spring
Property Code 337204	Property Name DONKEY POTROAST FEDERAL COM	Well Number 503H
OGRID No. 229137	Operator Name COG OPERATING LLC	Ground Level Elevation 3590.5'
Surface Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal		Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal

Surface Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
P	15	20-S	33-E		480 FSL	1185 FEL	32.567215°N	103.646362°W	LEA

Bottom Hole Location

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
O	34	20-S	33-E		50 FSL	1640 FEL	32.522482°N	103.647815°W	LEA

Dedicated Acres 1920	Infill or Defining Well Defining	Defining Well API Pending 503H	Overlapping Spacing Unit (Y/N)	Consolidation Code Com
Order Numbers.			Well setbacks are under Common Ownership: ☒ Yes ☐ No	

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
P	15	20-S	33-E		480 FSL	1185 FEL	32.567215°N	103.646362°W	LEA



First Take Point (FTP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
B	22	20-S	33-E		100 FNL	1640 FEL	32.565618°N	103.647840°W	LEA

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Ft. from N/S	Ft. from E/W	Latitude	Longitude	County
O	34	20-S	33-E		100 FSL	1640 FEL	32.522620°N	103.647815°W	LEA


Unitized Area or Area of Uniform Interest	Spacing Unit Type ☒ Horizontal ☐ Vertical	Ground Floor Elevation:
---	--	-------------------------

OPERATOR CERTIFICATIONS <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> <i>If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i>  8/29/24		SURVEYOR CERTIFICATIONS <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.</i>  8/8/24	
Signature	Date	Signature and Seal of Professional Surveyor	
Printed Name Stan Wagner		Certificate Number 17777	Date of Survey JULY 31, 2024
Email Address		W.O.#24-664	DRAWN BY: WN
		PAGE 1 OF 2	


Note: No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

This grid represents a standard section. You may superimpose a non-standard section, or larger area, over this grid. Operators must outline the dedicated acreage in a red box, clearly show the well surface location and bottom hole location, if it is directionally drilled, with the dimensions from the section lines in the cardinal directions. If this is a horizontal wellbore show on this plat the location of the First Take Point and Last Take Point, and the point within the Completed interval (other than the First Take Point or Last Take Point) that is closest to any outer boundary of the tract.


Surveyors shall use the latest United States government survey or dependent resurvey. Well locations will be in reference to the New Mexico Principal Meridian. If the land is not surveyed, contact the OCD Engineering Bureau. Independent subdivision surveys will not be acceptable.

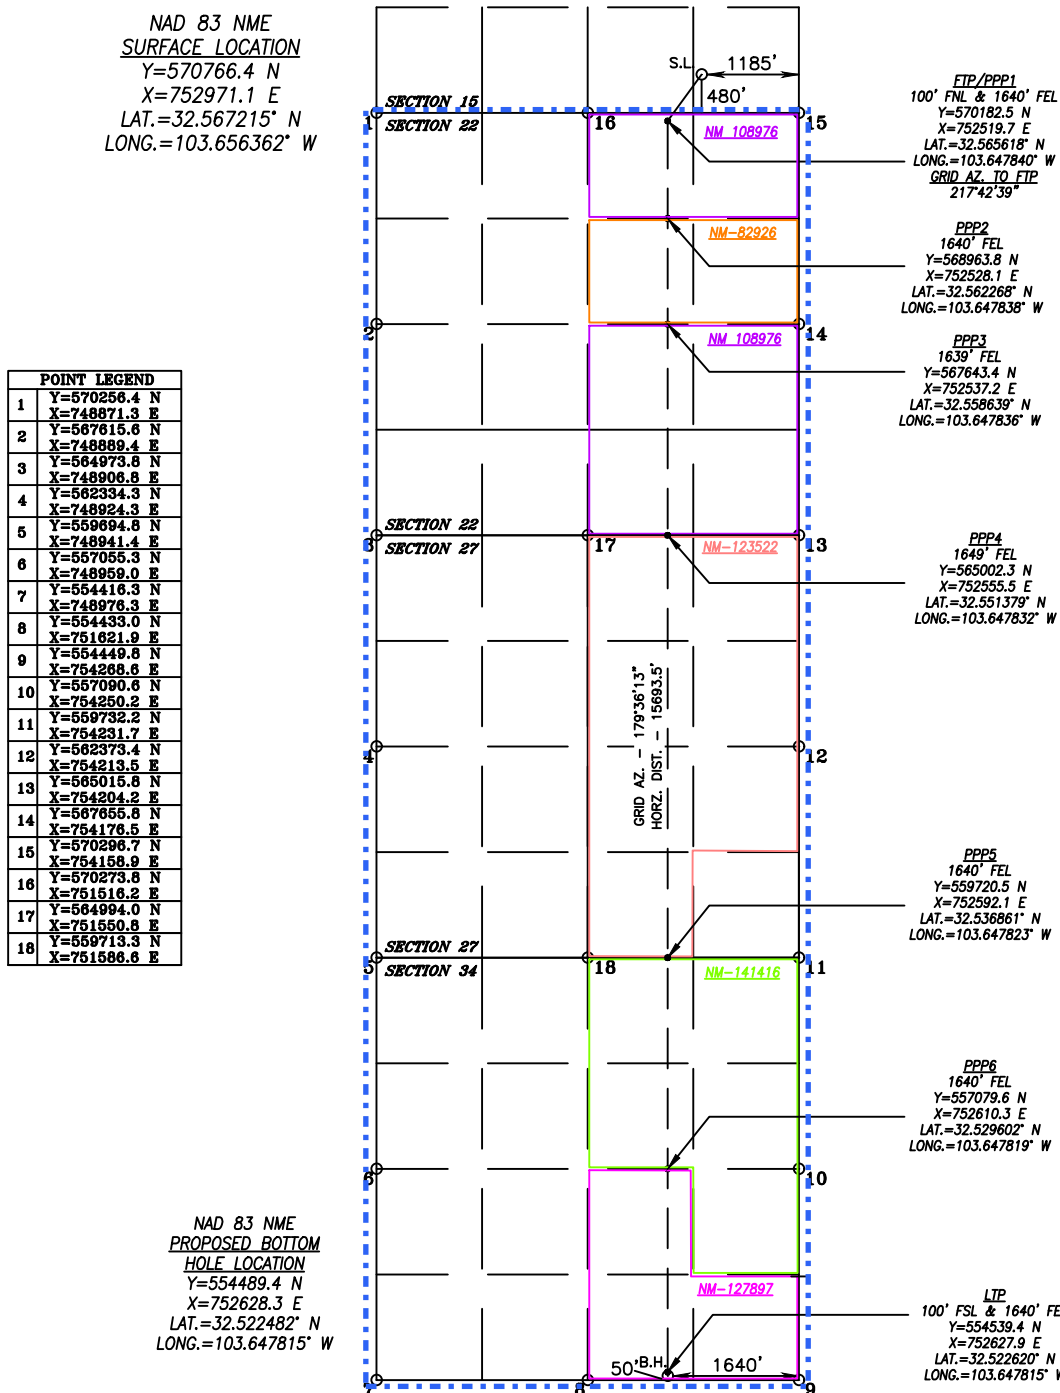

10M CHOKE MANIFOLD CONFIGURATION

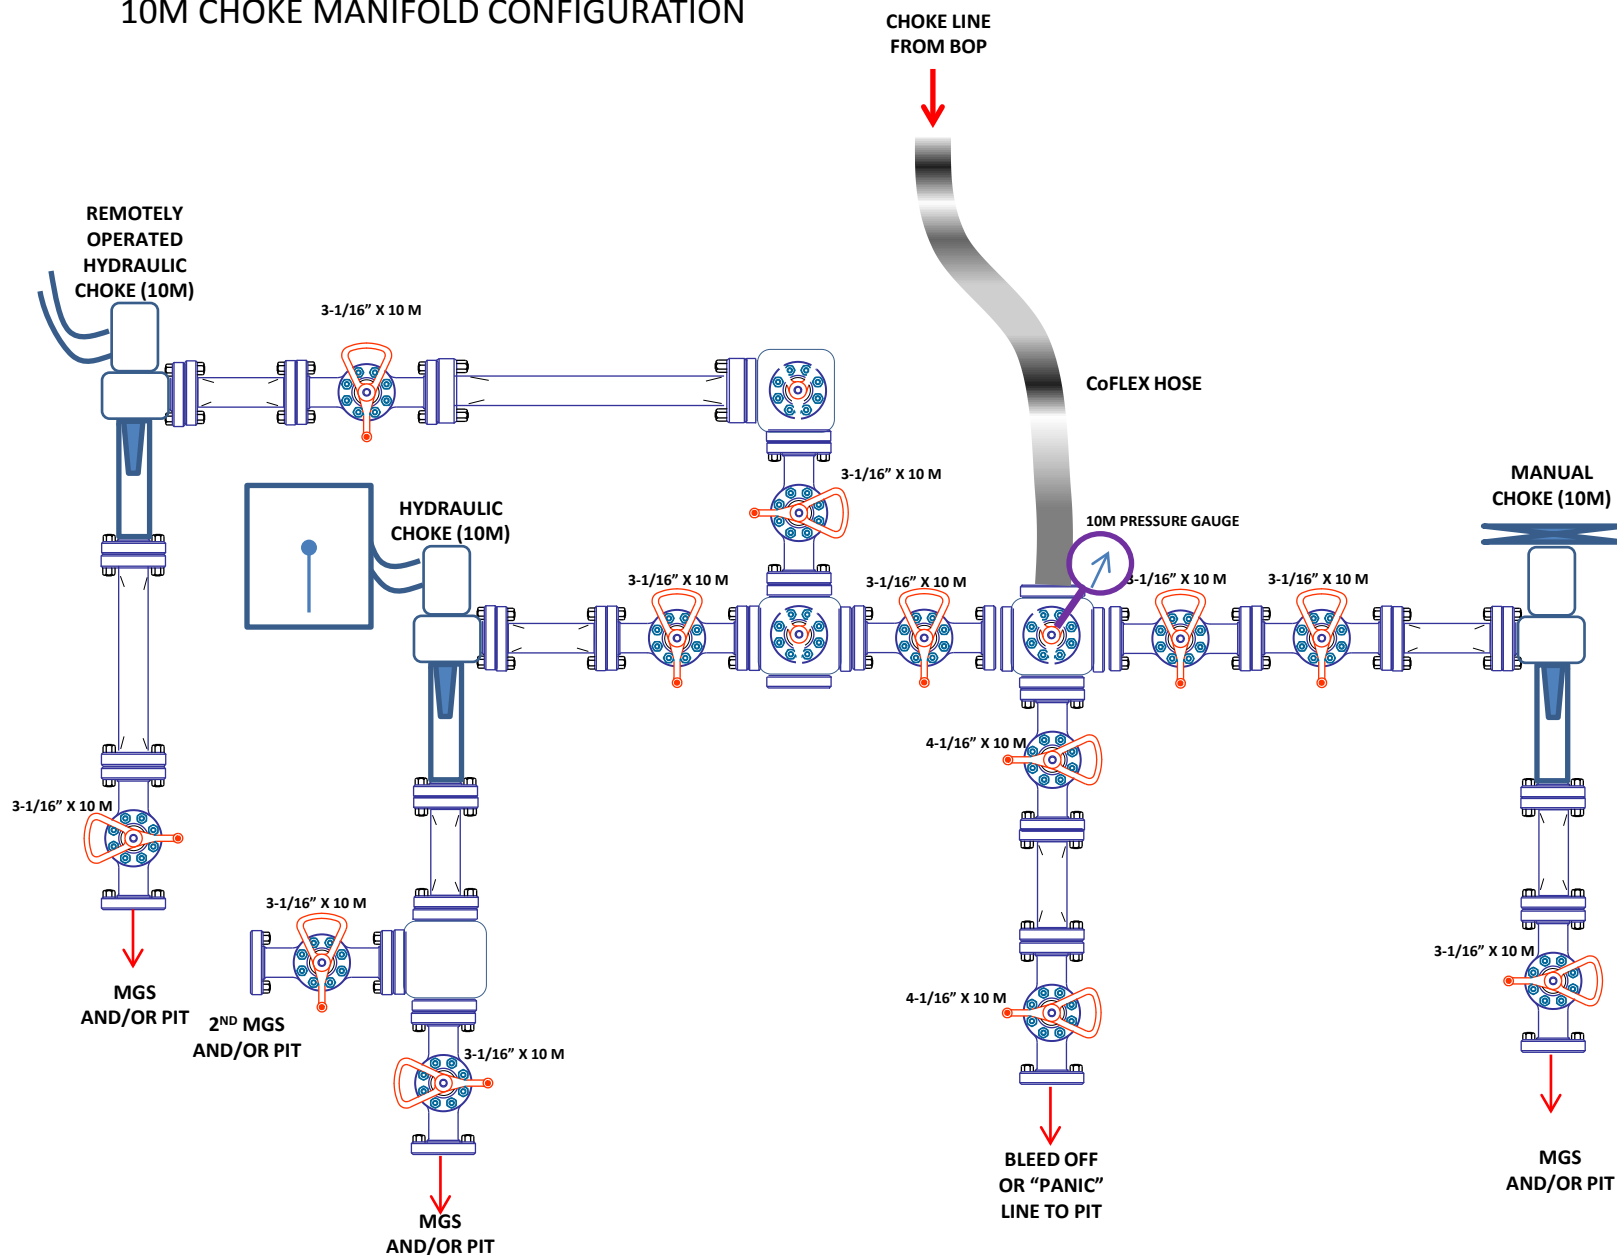

10M REMOTE KILL SCHEMATIC

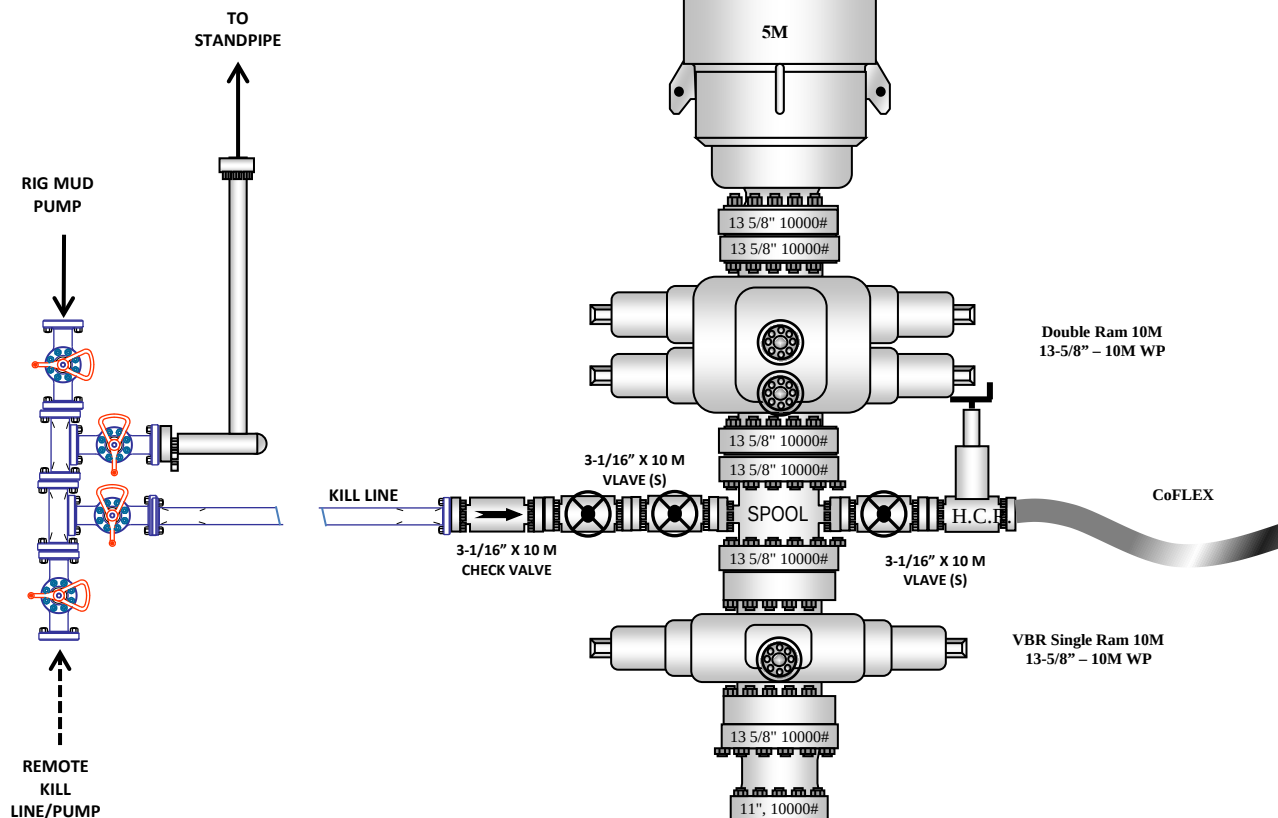

COG Operating, LLC - Donkey Potroast Fed Com 503H

1. Geologic Formations

TVD of target	10,600' EOL	Pilot hole depth	NA
MD at TD:	26,040'	Deepest expected fresh water:	325'

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Quaternary Fill	Surface	Water	
Rustler	1334	Water	
Top of Salt	1729	Salt	
USGS Marker Bed 126	2803	Salt	
Base of Salt	3037	Salt Water	
Capitan Reef	3604	Salt Water	
Lamar	5138	Oil/Gas	
Brushy Canyon	6635	Oil/Gas	
Bone Spring	8321	Oil/Gas	
Avalon	8682	Oil/Gas	
1st Bone Spring Sand	9404	Oil/Gas	
1st Bone Spring Shale	9681	Oil/Gas	
2nd Bone Spring Sand	9927	Target Oil/Gas	
3rd Bone Spring Carb	10449	Not Penetrated	

Potash/Reef well archetype: 5-String Design Open 2nd Int x 3rd Int Annulus w/ ICP 3 below relief zone (Figure D). Sundry aims to comply with R-111-Q as passed on 5/10/2024.

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Body	SF Joint
	From	To								
26.00"	0	1434	20.000"	106.5	J55	ER	1.17	1.77	11.03	11.03
17.50"	0	3237	13.375"	54.5	L80-IC	BTC	1.25	1.84	7.03	6.98
12.25"	0	5138	9.625"	40	L80-IC	BTC	2.17	1.54	4.46	4.61
8.750"	0	9740	7.625"	29.7	P110-ICY	W513	1.56	1.96	3.17	3.27
6.75"	0	9540	5.5"	23	P110-CY	BTC	2.17	2.28	3.32	3.30
6.75"	9540	26,040	5.5"	23	P110-CY	W441	1.95	2.28	2.99	2.90
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet	1.6 Dry 1.8 Wet

Intermediate casing will be kept at least 1/3 full while running casing to mitigate collapse. Surface burst based on 0.7 frac gradient at the shoe with Gas Gradient 0.1 psi/ft to surface and
All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

The 5 1/2" wedge casing will be run back 200' above KOP to ensure the coupling OD clearance is greater than .422" for the cement bond tie in.

Intend to use new casing meeting API standards.

COG Operating, LLC - Donkey Potroast Fed Com 503H

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	Y
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	Y
If yes, does production casing cement tie back a minimum of 50' above the Reef?	N
Is well within the designated 4 string boundary?	Y
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	Y
If yes, are the first three strings cemented to surface?	Y
Is 2 nd string set 100' to 600' below the base of salt?	Y
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

COG Operating, LLC - Donkey Potroast Fed Com 503H

3. Cementing Program

Casing	# Sks	Wt. lb/ gal	Yld ft3/ sack	H ₂ O gal/sk	500# Comp. Strength (hours)	Slurry Description
Surf	808	13.5	1.75	9	12	Lead: Class C + 4% Gel + 1% CaCl ₂
	565	14.8	1.34	6.34	8	Tail: Class C + 2% CaCl ₂
Inter 1	846	12.8	2.26	12.84	12	Lead: Class C + 5% Gel + 1% CaCl ₂
	291	14.8	1.2	5.35	10	50:50 Class H Premium
Inter 2	576	12.8	2.26	12.84	12	Lead: Class C + 5% Gel + 1% CaCl ₂
	262	14.8	1.2	5.35	10	50:50 Class H Premium
Inter 3	157	14.8	1.35	6.6	10	Tail: Class H - Single Slurry
Prod						
	1297	13.2	1.24	5.7	19	Tail: 50:50:2 Class H Blend Single Slurry

Intermediate #1 Salt string cemented to surface. Drill out to wait for 500PSI compressive strength.

Intermediate #2 Reef string will be cemented to surface. Drill out to wait for 500PSI compressive strength.

Intermediate #3 long string cemented Tail single slurry leaving Delaware Mountain group open as a relief zone. Section to be monitored during completions, and then Bradenhead cemented after completion is complete within 180 days to tie back. Drill out of intermediate to wait for 500psi compressive strength.

Production cement tied back 1000' into intermediate 3 string with minimal excess to ensure annulus remains open.

Volumes Subject to Observed Hole Conditions and/or Fluid Caliper Results

Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

Casing String	TOC	% Excess
Surface	0'	50%
1st Intermediate	0'	50%
2nd Intermediate	0'	50%
3rd Intermediate	7,635'	0%
Production	8,540'	10% OH in Lateral (KOP to EOL)

COG Operating, LLC - Donkey Potroast Fed Com 503H

4. Pressure Control Equipment

N	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
Y	A variance is requested for the use of BOPE break testing on intermediate skids (in accordance with the 30 day full BOPE test requirements).

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	x	Tested to:
17-1/2"	20"	5M	Annular	x	2500psi
			Blind Ram		5000psi
			Pipe Ram		
			Double Ram		
			Other*		
12 1/4"	13-3/8"	5M	Annular	x	2500psi
			Blind Ram	x	5000psi
			Pipe Ram	x	
			Double Ram	x	
			Other*		
8-3/4"	13-3/8"	5M	Annular	x	2500psi
			Blind Ram	x	5000psi
			Pipe Ram	x	
			Double Ram	x	
			Other*		
6-3/4"	13-3/8"	10M	5M Annular	x	5000psi
			Blind Ram	x	10000psi
			Pipe Ram	x	
			Double Ram	x	
			Other*		

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

Y	Formation integrity test will be performed per Onshore Order #2.
Y	On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
N	Are anchors required by manufacturer?
Y	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

COG Operating, LLC - Donkey Potroast Fed Com 503H

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	Surf. Shoe	FW Gel	8.6 - 8.8	28-34	N/C
Surf csg	13.375" Int 1 shoe	Saturated Brine	9 - 10	28-34	N/C
13.375" shoe	9.625" Int 2 shoe	Saturated Brine	9 - 10	28-34	N/C
9.625" Int 2 shoe	7-5/8" Int 3 shoe	Diesel/Brine	8.4 - 9.3	28-34	N/C
7-5/8" Int 3 shoe	Lateral TD	OBM	9.6 - 13.5	35-45	<20

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
Y	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
Y	No Logs are planned based on well control or offset log information.
N	Drill stem test? If yes, explain.
Y	Coring? If yes, explain.

Sidewall coring will be performed for pilot hole operations from Avalon to Strawn.

Additional logs planned		Interval
Y	Resistivity	Pilot Hole TD to ICP
Y	Density	Pilot Hole TD to ICP
Y	CBL	Production casing (If cement not circulated to surface)
Y	Mud log	Intermediate shoe to TD
N	PEX	

COG Operating, LLC - Donkey Potroast Fed Com 503H**7. Drilling Conditions**

Condition	Specify what type and where?
BH Pressure at deepest TVD	7445 psi at 10600' TVD
Abnormal Temperature	NO 165 Deg. F.

No abnormal pressure or temperature conditions are anticipated. Sufficient mud materials to maintain mud properties and weight increase requirements will be kept on location at all times.

Sufficient supplies of Paper/LCM for periodic sweeps to control seepage and losses will be maintained on location.

Hydrogen Sulfide (H₂S) monitors will be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

N H₂S is present

Y H₂S Plan attached

8. Other Facets of Operation

Y	Is it a walking operation?
Y	Is casing pre-set?

x	H ₂ S Plan.
x	BOP & Choke Schematics.
x	Directional Plan

COG OPERATING LLC
HYDROGEN SULFIDE DRILLING OPERATIONS PLAN

1. HYDROGEN SULFIDE TRAINING

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

- a. The hazards and characteristics of hydrogen sulfide (H₂S).
- b. The proper use and maintenance of personal protective equipment and life support systems.
- c. The proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
- d. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

- a. The effects of H₂S on metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
- b. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
- c. The contents and requirements of the H₂S Drilling Operations Plan and the Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H₂S zone (within 3 days or 500 feet) and weekly H₂S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H₂S Drilling Operations Plan and the Public Protection Plan. This plan shall be available at the well site. All personnel will be required to carry documentation that they have received the proper training.

2. H₂S SAFETY EQUIPMENT AND SYSTEMS

Note: All H₂S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H₂S. If H₂S greater than 100 ppm is encountered in the gas stream we will shut in and install H₂S equipment.

- a. Well Control Equipment:
 - Flare line.
 - Choke manifold with remotely operated choke.
 - Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit.
 - Auxiliary equipment to include: annular preventer, mud-gas separator, rotating head.

- b. Protective equipment for essential personnel:
Mark II Surviveair 30-minute units located in the dog house and at briefing areas.
- c. H2S detection and monitoring equipment:
2 - portable H2S monitor positioned on location for best coverage and response. These units have warning lights and audible sirens when H2S levels of 20 ppm are reached.
- d. Visual warning systems:
Caution/Danger signs shall be posted on roads providing direct access to location. Signs will be painted a high visibility yellow with black lettering of sufficient size to be readable at a reasonable distance from the immediate location. Bilingual signs will be used, when appropriate. See example attached.
- e. Mud Program:
The mud program has been designed to minimize the volume of H2S circulated to the surface.
- f. Metallurgy:
All drill strings, casings, tubing, wellhead, blowout preventers, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service.
- g. Communication:
Company vehicles equipped with cellular telephone.

COG OPERATING LLC has conducted a review to determine if an H2S contingency plan is required for the above referenced well. We were able to conclude that any potential hazardous volume would be minimal. H2S concentrations of wells in this area from surface to TD are low enough; therefore, we do not believe that an H2S contingency plan is necessary.

W A R N I N G

**YOU ARE ENTERING AN H₂S AREA
AUTHORIZED PERSONNEL ONLY**

- 1. BEARDS OR CONTACT LENSES NOT ALLOWED**
- 2. HARD HATS REQUIRED**
- 3. SMOKING IN DESIGNATED AREAS ONLY**
- 4. BE WIND CONSCIOUS AT ALL TIMES**
- 5. CK WITH COG OPERATING LLC FOREMAN AT MAIN OFFICE**

COG OPERATING LLC

1-575-748-6940

EMERGENCY CALL LIST


	<u>OFFICE</u>	<u>MOBILE</u>
Jenaya Rohlfing	432-683-7443	713-478-0376
Chad Gregory		432-238-5840

EMERGENCY RESPONSE NUMBERS

	<u>OFFICE</u>
STATE POLICE	575-748-9718
EDDY COUNTY SHERIFF	575-746-2701
EMERGENCY MEDICAL SERVICES (AMBULANCE)	911 or 575-746-2701
EDDY COUNTY EMERGENCY MANAGEMENT (HARRY BURGESS)	575-887-9511
STATE EMERGENCY RESPONSE CENTER (SERC)	575-476-9620
CARLSBAD POLICE DEPARTMENT	575-885-2111
CARLSBAD FIRE DEPARTMENT	575-885-3125
NEW MEXICO OIL CONSERVATION DIVISION	575-748-1283
INDIAN FIRE & SAFETY	800-530-8693
HALLIBURTON SERVICES	800-844-8451

COG Operating LLC
H₂S Equipment Schematic
Terrain: Shinnery sand hills.

Well pad will be 400' x 400'
with cellar in center of pad

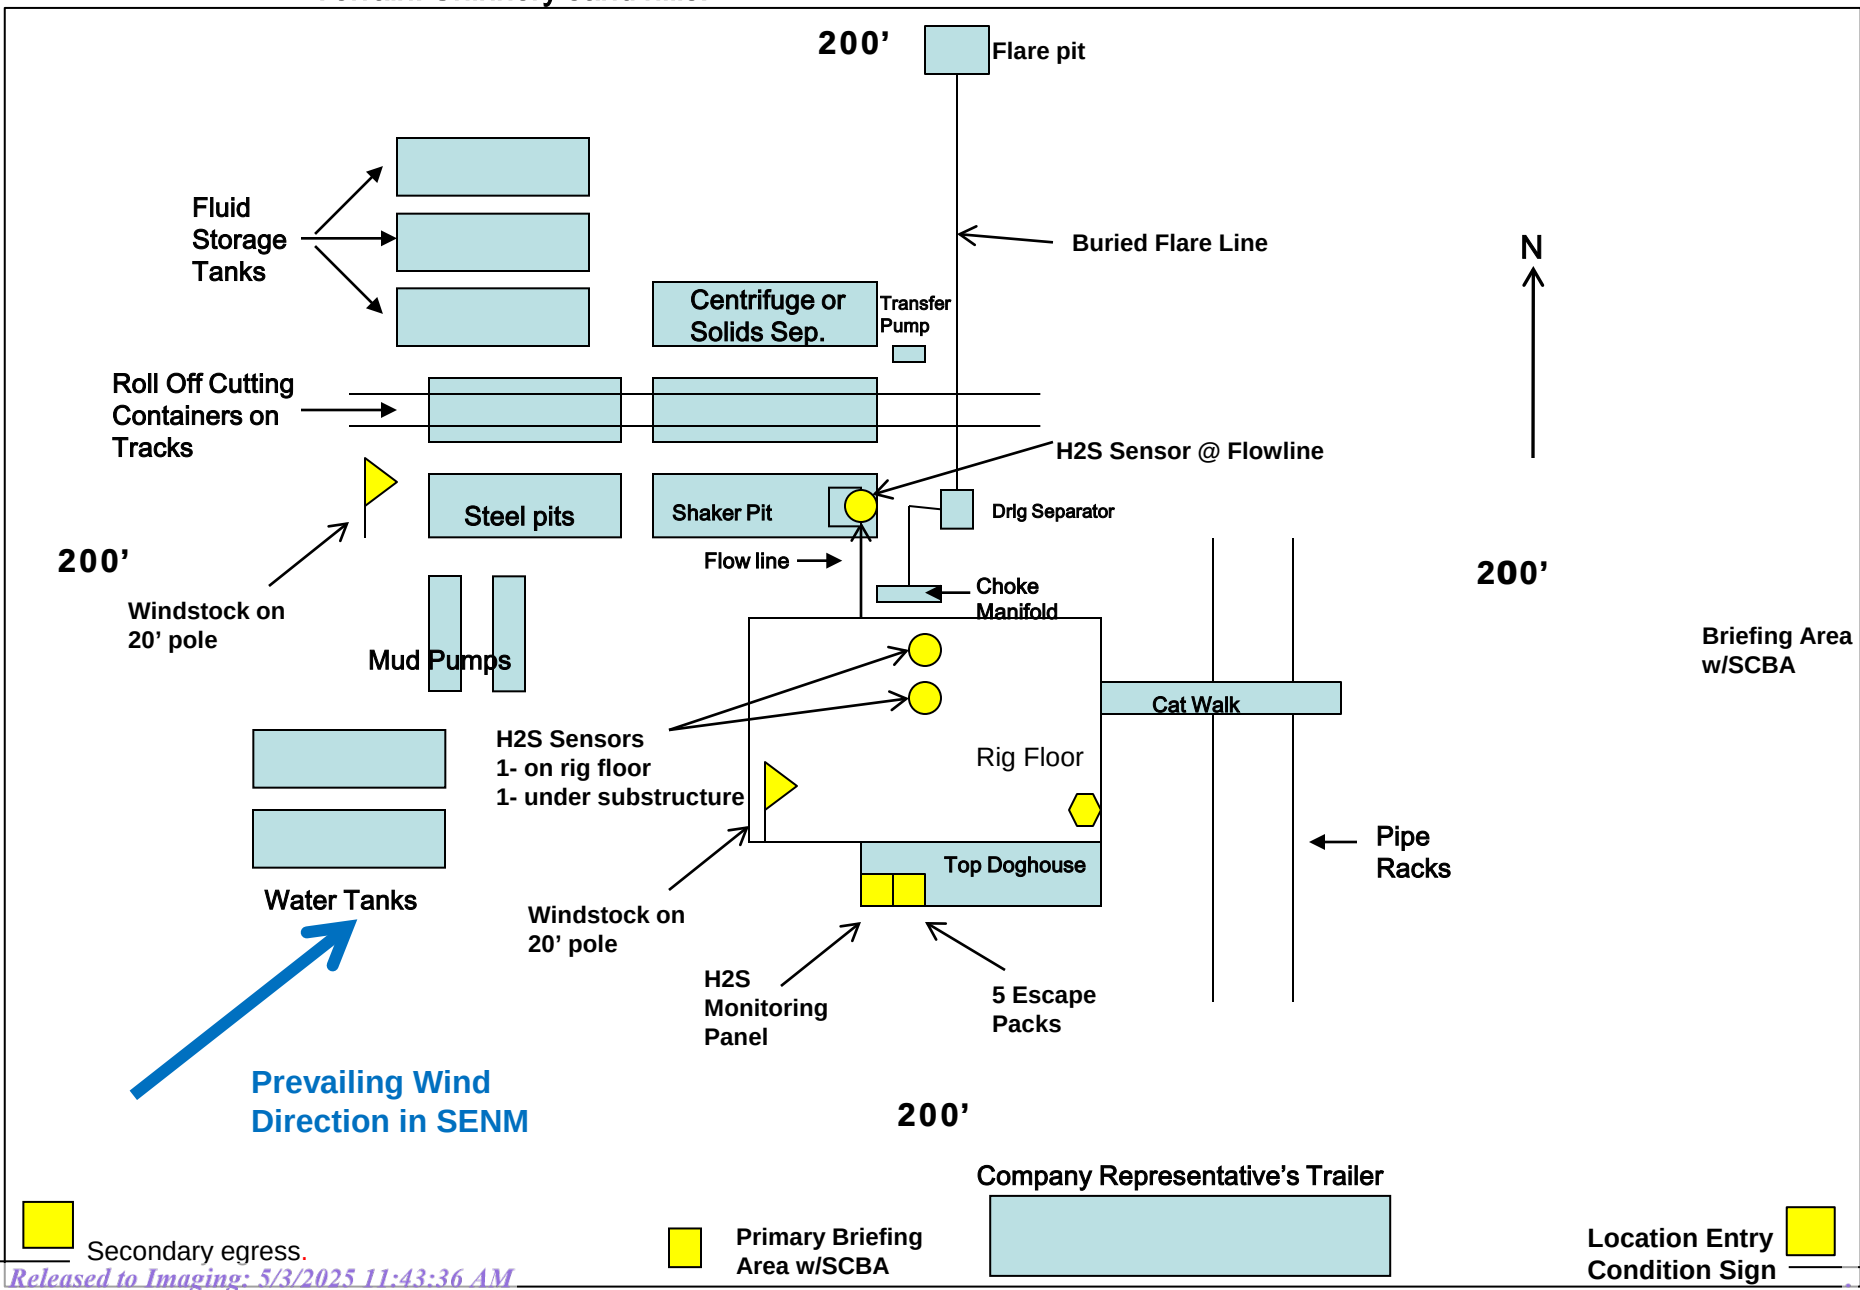

DELAWARE BASIN EAST

ZEUS_NME

TARHEEL_DONKEY POTROAST PROJECT

_DONKEY POTROAST FED COM 503H

OWB

PWP0

Anticollision Report

22 July, 2024

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 504H - OWB - PWP0A													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1+MS													Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (")	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
25,300.0	10,575.0	10,400.0	10,294.5	151.8	27.9	-33.47	-16,419.7	-110.8	978.6	871.9	106.70	9.171		
25,400.0	10,575.0	10,411.5	10,305.2	152.8	27.9	-34.40	-16,423.8	-109.8	889.1	777.0	112.06	7.934		
25,500.0	10,575.0	10,425.0	10,317.6	153.7	28.0	-35.54	-16,429.0	-108.6	801.5	683.2	118.35	6.773		
25,600.0	10,575.0	10,441.5	10,332.6	154.7	28.0	-37.00	-16,435.8	-107.0	716.3	590.6	125.69	5.699		
25,700.0	10,575.0	10,460.1	10,349.1	155.7	28.0	-38.74	-16,444.1	-105.0	634.3	499.7	134.52	4.715		
25,800.0	10,575.0	10,481.8	10,368.0	156.6	28.0	-40.88	-16,454.5	-102.5	556.4	411.3	145.11	3.835		
25,900.0	10,575.0	10,507.4	10,389.5	157.6	28.0	-43.56	-16,467.9	-99.3	484.4	326.6	157.71	3.071		
26,000.0	10,575.0	10,537.8	10,414.2	158.6	28.0	-46.94	-16,485.2	-95.1	420.1	247.8	172.32	2.438	Caution - Monitor Closely	
26,040.2	10,575.0	10,550.0	10,423.7	159.0	28.0	-48.34	-16,492.5	-93.3	397.2	218.4	178.81	2.221	Caution - Monitor Closely, CC, ES, SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 505H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1+MS											Offset Well Error:	0.0 usft
Reference	Vertical	Offset	Vertical	Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Rule Assigned:		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Depth (usft)	Measured Depth (usft)	Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
25,600.0	10,575.0	10,350.0	10,327.7	154.7	16.2	64.38	-16,436.6	-1,003.9	944.4	770.2	174.25	5.420	
25,700.0	10,575.0	10,375.0	10,350.0	155.7	16.2	65.99	-16,447.9	-1,004.6	884.1	700.5	183.66	4.814	
25,800.0	10,575.0	10,400.0	10,371.7	156.6	16.1	67.60	-16,460.3	-1,005.4	830.4	637.1	193.35	4.295	
25,900.0	10,575.0	10,425.0	10,392.6	157.6	16.1	69.19	-16,473.9	-1,006.2	784.2	581.2	202.92	3.864	
26,000.0	10,575.0	10,450.0	10,412.9	158.6	16.0	70.76	-16,488.6	-1,007.1	746.3	534.6	211.78	3.524	
26,040.2	10,575.0	10,468.4	10,427.3	159.0	16.0	71.89	-16,500.0	-1,007.8	733.6	519.0	214.61	3.418 CC, ES, SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 704H - OWB - PWP0A												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1+MS												Offset Well Error:	0.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Rule Assigned:		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
25,200.0	10,575.0	10,723.7	10,645.0	150.8	25.9	-90.00	-16,383.2	-256.3	950.4	886.9	63.45	14.978	
25,300.0	10,575.0	10,723.7	10,645.0	151.8	25.9	-90.00	-16,383.2	-256.3	850.8	786.4	64.46	13.199	
25,400.0	10,575.0	10,723.7	10,645.0	152.8	25.9	-90.00	-16,383.2	-256.3	751.4	685.6	65.79	11.421	
25,500.0	10,575.0	10,723.7	10,645.0	153.7	25.9	-90.00	-16,383.2	-256.3	652.2	584.6	67.62	9.645	
25,600.0	10,575.0	10,723.7	10,645.0	154.7	25.9	-90.00	-16,383.2	-256.3	553.2	482.9	70.29	7.871	
25,700.0	10,575.0	10,723.7	10,645.0	155.7	25.9	-90.00	-16,383.2	-256.3	454.7	380.2	74.49	6.104	
25,800.0	10,575.0	10,723.7	10,645.0	156.6	25.9	-90.00	-16,383.2	-256.3	357.0	275.3	81.75	4.368	
25,900.0	10,575.0	10,723.7	10,645.0	157.6	25.9	-90.00	-16,383.2	-256.3	261.1	165.3	95.89	2.723	Normal Operations
26,000.0	10,575.0	10,723.7	10,645.0	158.6	25.9	-90.00	-16,383.2	-256.3	170.0	42.0	128.08	1.328	Take Immediate Action
26,040.2	10,575.0	10,723.7	10,645.0	159.0	25.9	-90.00	-16,383.2	-256.3	137.0	-15.1	152.02	0.901	STOP Drilling, CC, ES, SF

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	GRIZZOUGAR FEDERAL PROJECT - _GRIZZOUGAR FED COM 705H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1+MS											Offset Well Error:	0.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	
25,600.0	10,575.0	10,645.5	10,645.0	154.7	14.7	90.00	-16,446.5	-1,123.3	987.2	813.2	174.00	5.673	
25,700.0	10,575.0	10,645.5	10,645.0	155.7	14.7	90.00	-16,446.5	-1,123.3	929.4	744.4	185.00	5.024	
25,800.0	10,575.0	10,645.5	10,645.0	156.6	14.7	90.00	-16,446.5	-1,123.3	879.2	683.2	195.98	4.486	
25,900.0	10,575.0	10,645.5	10,645.0	157.6	14.7	90.00	-16,446.5	-1,123.3	838.0	631.6	206.32	4.061	
26,000.0	10,575.0	10,645.5	10,645.0	158.6	14.7	90.00	-16,446.5	-1,123.3	807.1	591.9	215.20	3.750	
26,040.2	10,575.0	10,645.5	10,645.0	159.0	14.7	90.00	-16,446.5	-1,123.3	797.9	579.7	218.16	3.657 CC, ES, SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #403H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		Warning					
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	
0.0	0.0	0.0	0.0	3.0	3.0	-31.06	150.2	-90.5	175.3	168.9	6.43	27.272	
100.0	100.0	100.0	100.0	3.2	3.2	-31.06	150.2	-90.5	175.3	168.4	6.89	25.438	
200.0	200.0	200.0	200.0	3.5	3.5	-31.06	150.2	-90.5	175.3	168.0	7.33	23.925	
300.0	300.0	300.0	300.0	3.7	3.7	-31.06	150.2	-90.5	175.3	167.6	7.74	22.648	
400.0	400.0	400.0	400.0	3.9	3.9	-31.06	150.2	-90.5	175.3	167.2	8.14	21.551	
500.0	500.0	500.0	500.0	4.1	4.1	-31.06	150.2	-90.5	175.3	166.8	8.51	20.594	
600.0	600.0	600.0	600.0	4.2	4.2	-31.06	150.2	-90.5	175.3	166.5	8.88	19.749	
700.0	700.0	700.0	700.0	4.4	4.4	-31.06	150.2	-90.5	175.3	166.1	9.23	18.997	
800.0	800.0	800.0	800.0	4.6	4.6	-31.06	150.2	-90.5	175.3	165.8	9.57	18.320	
900.0	900.0	900.0	900.0	4.8	4.8	-31.06	150.2	-90.5	175.3	165.4	9.90	17.706	
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-31.06	150.2	-90.5	175.3	165.1	10.22	17.148	
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-31.06	150.2	-90.5	175.3	164.8	10.54	16.635	
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-31.06	150.2	-90.5	175.3	164.5	10.85	16.163	
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-31.06	150.2	-90.5	175.3	164.2	11.15	15.726	
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-31.06	150.2	-90.5	175.3	163.9	11.44	15.320	
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-31.06	150.2	-90.5	175.3	163.6	11.73	14.941 CC	
1,600.0	1,600.0	1,602.1	1,602.0	5.9	5.9	113.63	148.8	-91.6	175.4	163.4	12.01	14.604 ES	
1,700.0	1,699.8	1,704.1	1,703.9	6.1	6.1	113.54	144.6	-95.1	175.8	163.5	12.26	14.338	
1,800.0	1,799.5	1,806.1	1,805.6	6.3	6.4	113.39	137.6	-100.9	176.4	163.8	12.51	14.097	
1,900.0	1,898.7	1,908.2	1,906.8	6.6	6.6	113.18	127.9	-109.0	177.2	164.4	12.76	13.879	
2,000.0	1,997.5	2,009.8	2,007.1	6.9	6.8	112.95	115.5	-119.3	178.2	165.2	13.01	13.697	
2,021.2	2,018.4	2,031.0	2,028.0	6.9	6.9	112.95	112.7	-121.6	178.5	165.5	13.06	13.667	
2,100.0	2,095.8	2,109.8	2,105.6	7.0	7.1	113.09	102.4	-130.2	179.9	166.5	13.31	13.513	
2,200.0	2,194.2	2,209.8	2,204.2	7.3	7.4	113.26	89.3	-141.1	181.5	167.9	13.59	13.357	
2,300.0	2,292.5	2,309.7	2,302.7	7.5	7.6	113.42	76.2	-152.0	183.2	169.3	13.88	13.194	
2,400.0	2,390.9	2,409.7	2,401.2	7.8	7.9	113.58	63.1	-162.8	184.9	170.7	14.19	13.027	
2,500.0	2,489.2	2,509.7	2,499.7	8.1	8.2	113.74	50.0	-173.7	186.5	172.0	14.51	12.857	
2,600.0	2,587.6	2,609.7	2,598.3	8.4	8.5	113.90	36.9	-184.6	188.2	173.4	14.84	12.685	
2,700.0	2,685.9	2,709.7	2,696.8	8.8	8.8	114.05	23.9	-195.5	189.9	174.7	15.17	12.512	
2,800.0	2,784.3	2,809.7	2,795.3	9.1	9.1	114.20	10.8	-206.4	191.5	176.0	15.52	12.338	
2,900.0	2,882.6	2,909.7	2,893.9	9.4	9.5	114.35	-2.3	-217.2	193.2	177.3	15.88	12.165	
3,000.0	2,981.0	3,009.6	2,992.4	9.8	9.8	114.50	-15.4	-228.1	194.9	178.6	16.25	11.993	
3,100.0	3,079.3	3,109.6	3,090.9	10.2	10.2	114.64	-28.5	-239.0	196.6	179.9	16.63	11.822	
3,200.0	3,177.7	3,209.6	3,189.4	10.5	10.6	114.78	-41.6	-249.9	198.2	181.2	17.01	11.653	
3,300.0	3,276.0	3,309.6	3,288.0	10.9	10.9	114.92	-54.7	-260.7	199.9	182.5	17.41	11.486	
3,400.0	3,374.4	3,409.6	3,386.5	11.3	11.3	115.06	-67.7	-271.6	201.6	183.8	17.81	11.322	
3,500.0	3,472.7	3,509.6	3,485.0	11.7	11.7	115.19	-80.8	-282.5	203.3	185.1	18.21	11.161	
3,600.0	3,571.1	3,609.5	3,583.5	12.1	12.1	115.32	-93.9	-293.4	205.0	186.3	18.63	11.003	
3,700.0	3,669.4	3,709.5	3,682.1	12.5	12.5	115.45	-107.0	-304.3	206.7	187.6	19.05	10.848	
3,800.0	3,767.8	3,809.5	3,780.6	12.9	12.9	115.58	-120.1	-315.1	208.3	188.9	19.48	10.697	
3,900.0	3,866.1	3,909.5	3,879.1	13.3	13.3	115.71	-133.2	-326.0	210.0	190.1	19.91	10.549	
4,000.0	3,964.5	4,009.5	3,977.6	13.7	13.7	115.83	-146.3	-336.9	211.7	191.4	20.35	10.404	
4,100.0	4,062.8	4,109.5	4,076.2	14.1	14.1	115.95	-159.3	-347.8	213.4	192.6	20.79	10.263	
4,200.0	4,161.2	4,209.5	4,174.7	14.5	14.5	116.07	-172.4	-358.6	215.1	193.9	21.24	10.126	
4,300.0	4,259.5	4,309.4	4,273.2	15.0	14.9	116.19	-185.5	-369.5	216.8	195.1	21.70	9.991	
4,400.0	4,357.9	4,409.4	4,371.7	15.4	15.3	116.31	-198.6	-380.4	218.5	196.3	22.16	9.861	
4,500.0	4,456.2	4,509.4	4,470.3	15.8	15.7	116.42	-211.7	-391.3	220.2	197.6	22.62	9.734	
4,600.0	4,554.6	4,608.8	4,568.2	16.2	16.1	116.57	-224.6	-402.0	221.9	198.9	23.06	9.624	
4,700.0	4,652.9	4,707.2	4,665.5	16.7	16.5	117.06	-236.2	-411.7	224.2	200.6	23.60	9.502	
4,800.0	4,751.3	4,805.6	4,762.9	17.1	16.9	117.93	-246.6	-420.3	227.3	203.0	24.22	9.384	
4,900.0	4,849.6	4,903.8	4,860.4	17.5	17.3	119.15	-255.7	-427.8	231.0	206.1	24.93	9.269	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #403H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (")	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
5,000.0	4,948.0	5,001.8	4,957.9	17.9	17.7	120.70	-263.4	-434.3	235.7	210.0	25.73	9.161		
5,100.0	5,046.3	5,100.0	5,055.7	18.4	18.1	122.55	-269.9	-439.7	241.3	214.7	26.63	9.062		
5,200.0	5,144.7	5,196.8	5,152.3	18.8	18.4	124.62	-275.1	-444.0	248.0	220.4	27.61	8.984		
5,300.0	5,243.0	5,293.7	5,249.1	19.3	18.7	126.89	-279.0	-447.2	255.9	227.3	28.67	8.927		
5,400.0	5,341.4	5,390.2	5,345.5	19.7	19.0	129.30	-281.6	-449.4	265.2	235.4	29.80	8.902		
5,500.0	5,439.7	5,486.2	5,441.4	20.1	19.3	131.81	-283.0	-450.5	276.0	245.0	30.96	8.916		
5,524.0	5,463.3	5,509.1	5,464.3	20.2	19.3	132.42	-283.1	-450.7	278.8	247.6	31.22	8.930		
5,600.0	5,538.1	5,582.9	5,538.1	20.6	19.4	134.37	-283.2	-450.7	287.9	255.9	32.02	8.991		
5,700.0	5,636.9	5,681.6	5,636.9	21.0	19.4	136.62	-283.2	-450.7	299.4	266.4	33.01	9.070		
5,800.0	5,735.9	5,780.6	5,735.9	21.4	19.4	138.48	-283.2	-450.7	309.9	276.0	33.89	9.144		
5,900.0	5,835.1	5,879.8	5,835.1	21.8	19.4	140.02	-283.2	-450.7	319.4	284.7	34.68	9.209		
6,000.0	5,934.5	5,979.2	5,934.5	22.2	19.5	141.28	-283.2	-450.7	327.7	292.3	35.39	9.260		
6,100.0	6,034.1	6,078.8	6,034.1	22.6	19.5	142.28	-283.2	-450.7	334.8	298.8	36.02	9.294		
6,200.0	6,133.8	6,178.5	6,133.8	22.9	19.6	143.07	-283.2	-450.7	340.6	304.0	36.58	9.309		
6,300.0	6,233.7	6,278.4	6,233.7	23.3	19.6	143.64	-283.2	-450.7	345.0	307.9	37.07	9.306		
6,400.0	6,333.6	6,378.3	6,333.6	23.6	19.6	144.03	-283.2	-450.7	348.0	310.5	37.49	9.284		
6,500.0	6,433.6	6,478.3	6,433.6	23.9	19.7	144.23	-283.2	-450.7	349.7	311.9	37.82	9.245		
6,566.4	6,500.0	6,544.7	6,500.0	24.0	19.7	-0.45	-283.2	-450.7	350.0	312.1	37.93	9.227		
6,600.0	6,533.6	6,578.3	6,533.6	24.0	19.7	-0.45	-283.2	-450.7	350.0	312.1	37.95	9.224		
6,700.0	6,633.6	6,678.3	6,633.6	24.0	19.7	-0.45	-283.2	-450.7	350.0	312.0	38.01	9.207		
6,800.0	6,733.6	6,778.3	6,733.6	24.0	19.8	-0.45	-283.2	-450.7	350.0	311.9	38.08	9.190		
6,900.0	6,833.6	6,878.3	6,833.6	24.0	19.8	-0.45	-283.2	-450.7	350.0	311.8	38.15	9.173		
7,000.0	6,933.6	6,978.3	6,933.6	24.0	19.8	-0.45	-283.2	-450.7	350.0	311.8	38.23	9.156		
7,100.0	7,033.6	7,078.3	7,033.6	24.1	19.9	-0.45	-283.2	-450.7	350.0	311.7	38.30	9.139		
7,200.0	7,133.6	7,178.3	7,133.6	24.1	19.9	-0.45	-283.2	-450.7	350.0	311.6	38.37	9.122		
7,300.0	7,233.6	7,278.3	7,233.6	24.1	19.9	-0.45	-283.2	-450.7	350.0	311.6	38.44	9.105		
7,400.0	7,333.6	7,378.3	7,333.6	24.2	20.0	-0.45	-283.2	-450.7	350.0	311.5	38.51	9.088		
7,500.0	7,433.6	7,478.3	7,433.6	24.2	20.0	-0.45	-283.2	-450.7	350.0	311.4	38.59	9.070		
7,600.0	7,533.6	7,578.3	7,533.6	24.2	20.1	-0.45	-283.2	-450.7	350.0	311.3	38.66	9.053		
7,700.0	7,633.6	7,678.3	7,633.6	24.2	20.1	-0.45	-283.2	-450.7	350.0	311.3	38.74	9.035		
7,800.0	7,733.6	7,778.3	7,733.6	24.3	20.1	-0.45	-283.2	-450.7	350.0	311.2	38.81	9.018		
7,900.0	7,833.6	7,878.3	7,833.6	24.3	20.2	-0.45	-283.2	-450.7	350.0	311.1	38.89	9.000		
8,000.0	7,933.6	7,978.3	7,933.6	24.3	20.2	-0.45	-283.2	-450.7	350.0	311.0	38.96	8.983		
8,100.0	8,033.6	8,078.3	8,033.6	24.3	20.3	-0.45	-283.2	-450.7	350.0	311.0	39.04	8.965		
8,200.0	8,133.6	8,178.3	8,133.6	24.4	20.3	-0.45	-283.2	-450.7	350.0	310.9	39.12	8.947		
8,300.0	8,233.6	8,278.3	8,233.6	24.4	20.3	-0.45	-283.2	-450.7	350.0	310.8	39.20	8.930		
8,400.0	8,333.6	8,378.3	8,333.6	24.4	20.4	-0.45	-283.2	-450.7	350.0	310.7	39.27	8.912		
8,500.0	8,433.6	8,478.3	8,433.6	24.5	20.4	-0.45	-283.2	-450.7	350.0	310.6	39.35	8.894		
8,600.0	8,533.6	8,578.3	8,533.6	24.5	20.5	-0.45	-283.2	-450.7	350.0	310.6	39.43	8.876		
8,700.0	8,633.6	8,678.3	8,633.6	24.5	20.5	-0.45	-283.2	-450.7	350.0	310.5	39.51	8.858		
8,800.0	8,733.6	8,778.3	8,733.6	24.5	20.5	-0.45	-283.2	-450.7	350.0	310.4	39.59	8.840		
8,900.0	8,833.6	8,878.3	8,833.6	24.6	20.6	-0.45	-283.2	-450.7	350.0	310.3	39.67	8.822		
9,000.0	8,933.6	8,978.3	8,933.6	24.6	20.6	-0.45	-283.2	-450.7	350.0	310.2	39.75	8.804		
9,010.0	8,943.6	8,988.3	8,943.6	24.6	20.6	-0.45	-283.2	-450.7	350.0	310.2	39.76	8.802 SF		
9,100.0	9,033.6	9,050.0	9,005.3	24.6	20.6	-0.45	-282.1	-450.7	352.3	312.9	39.40	8.940		
9,200.0	9,133.6	9,109.0	9,063.7	24.7	20.5	-0.45	-274.4	-450.8	365.5	326.8	38.70	9.444		
9,300.0	9,233.6	9,163.1	9,116.2	24.7	20.3	-0.45	-261.1	-450.9	390.2	352.3	37.91	10.293		
9,400.0	9,333.6	9,213.7	9,163.5	24.7	20.2	-0.45	-243.4	-451.1	425.3	388.2	37.14	11.452		
9,500.0	9,433.6	9,259.9	9,204.9	24.7	20.0	-0.45	-222.8	-451.2	469.8	433.3	36.48	12.877		
9,600.0	9,533.6	9,300.0	9,239.0	24.8	19.9	-0.45	-201.9	-451.4	522.3	486.3	35.95	14.528		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #403H - OWB - PWP0										Offset Site Error:		0.0 usft	
Survey Program:		0-r.5 MWD+IFR1					Rule Assigned:					Offset Well Error:		3.0 usft	
Reference		Offset		Semi Major Axis		Offset Wellbore Centre		Distance							
Measured	Vertical	Measured	Vertical	Reference	Offset	Highside			Between	Between	No-Go	Separation	Warning		
Depth	Depth	Depth	Depth			Toolface	+N/-S	+E/-W	Centres	Ellipses	Distance	Factor			
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)				
9,700.0	9,633.6	9,339.1	9,270.5	24.8	19.8	-0.46	-178.8	-451.6	581.6	546.0	35.61	16.335			
9,800.0	9,733.6	9,375.0	9,297.7	24.8	19.7	-0.46	-155.3	-451.8	646.8	611.4	35.41	18.265			
9,900.0	9,833.6	9,400.0	9,315.6	24.9	19.7	-0.46	-137.8	-452.0	716.7	681.4	35.32	20.293			
10,000.0	9,933.6	9,425.0	9,332.5	24.9	19.6	-0.46	-119.4	-452.1	790.8	755.4	35.36	22.365			
10,068.4	10,002.0	9,450.0	9,348.4	24.9	19.6	-0.46	-100.1	-452.3	843.4	808.0	35.44	23.802			
10,100.0	10,033.6	9,450.0	9,348.4	25.0	19.6	179.92	-100.1	-452.3	868.6	833.1	35.50	24.469			
10,150.0	10,083.3	9,459.9	9,354.4	25.1	19.6	179.90	-92.3	-452.3	911.1	875.5	35.66	25.553			
10,200.0	10,132.4	9,475.0	9,363.3	25.3	19.5	179.89	-80.1	-452.4	956.2	920.4	35.82	26.692			

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #404H - OWB - PWP0											Offset Site Error:		0.0 usft	
Survey Program:		0-r.5 MWD+IFR1						Rule Assigned:						Offset Well Error:		3.0 usft
Measured Depth	Vertical Reference	Measured Depth	Vertical Offset	Semi Major Axis Reference	Semi Major Axis Offset	Highside Toolface	Offset Wellbore Centre		Distance		No-Go Distance	Separation Factor	Warning			
Depth (usft)	Depth (usft)	Depth (usft)	Depth (usft)	(usft)	(usft)	(°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	(usft)					
0.0	0.0	0.0	0.0	3.0	3.0	21.38	151.3	59.3	162.5	156.1	6.43	25.277				
100.0	100.0	100.0	100.0	3.2	3.2	21.38	151.3	59.3	162.5	155.6	6.89	23.578				
200.0	200.0	200.0	200.0	3.5	3.5	21.38	151.3	59.3	162.5	155.2	7.33	22.175				
300.0	300.0	300.0	300.0	3.7	3.7	21.38	151.3	59.3	162.5	154.8	7.74	20.992				
400.0	400.0	400.0	400.0	3.9	3.9	21.38	151.3	59.3	162.5	154.4	8.14	19.975				
500.0	500.0	500.0	500.0	4.1	4.1	21.38	151.3	59.3	162.5	154.0	8.51	19.088				
600.0	600.0	600.0	600.0	4.2	4.2	21.38	151.3	59.3	162.5	153.6	8.88	18.305				
700.0	700.0	700.0	700.0	4.4	4.4	21.38	151.3	59.3	162.5	153.3	9.23	17.607				
800.0	800.0	800.0	800.0	4.6	4.6	21.38	151.3	59.3	162.5	152.9	9.57	16.980				
900.0	900.0	900.0	900.0	4.8	4.8	21.38	151.3	59.3	162.5	152.6	9.90	16.412				
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	21.38	151.3	59.3	162.5	152.3	10.22	15.893				
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	21.38	151.3	59.3	162.5	152.0	10.54	15.418				
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	21.38	151.3	59.3	162.5	151.7	10.85	14.981				
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	21.38	151.3	59.3	162.5	151.4	11.15	14.576				
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	21.38	151.3	59.3	162.5	151.1	11.44	14.200				
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	21.38	151.3	59.3	162.5	150.8	11.73	13.849 CC, ES				
1,600.0	1,600.0	1,600.6	1,600.6	5.9	5.9	166.86	150.5	60.8	164.0	151.9	12.07	13.583 SF				
1,700.0	1,699.8	1,700.8	1,700.6	6.1	6.1	169.02	148.0	65.5	168.7	156.3	12.40	13.609				
1,800.0	1,799.5	1,800.1	1,799.5	6.3	6.4	172.34	144.0	73.1	177.0	164.3	12.74	13.895				
1,900.0	1,898.7	1,898.2	1,896.9	6.6	6.6	176.44	138.4	83.7	189.5	176.4	13.11	14.460				
2,000.0	1,997.5	1,994.8	1,992.3	6.9	6.9	-179.08	131.3	96.9	206.8	193.3	13.50	15.318				
2,021.2	2,018.4	2,015.0	2,012.3	6.9	6.9	-178.12	129.7	100.0	211.1	197.6	13.56	15.572				
2,100.0	2,095.8	2,089.6	2,085.4	7.0	7.1	-174.60	123.0	112.7	228.2	214.4	13.82	16.515				
2,200.0	2,194.2	2,184.4	2,178.0	7.3	7.3	-170.29	113.4	130.7	251.6	237.5	14.15	17.788				
2,300.0	2,292.5	2,279.8	2,271.2	7.5	7.6	-166.63	103.7	149.1	276.3	261.8	14.54	19.001				
2,400.0	2,390.9	2,375.3	2,364.3	7.8	7.9	-163.56	93.9	167.5	301.9	286.9	14.97	20.168				
2,500.0	2,489.2	2,470.8	2,457.5	8.1	8.2	-160.97	84.1	185.9	328.2	312.8	15.42	21.283				
2,600.0	2,587.6	2,566.3	2,550.7	8.4	8.5	-158.76	74.4	204.3	355.0	339.1	15.89	22.339				
2,700.0	2,685.9	2,661.7	2,643.9	8.8	8.8	-156.86	64.6	222.7	382.3	365.9	16.39	23.332				
2,800.0	2,784.3	2,757.2	2,737.0	9.1	9.1	-155.21	54.8	241.1	409.9	393.0	16.90	24.261				
2,900.0	2,882.6	2,852.7	2,830.2	9.4	9.4	-153.77	45.1	259.5	437.8	420.4	17.42	25.127				
3,000.0	2,981.0	2,948.2	2,923.4	9.8	9.8	-152.49	35.3	277.9	465.9	448.0	17.97	25.934				
3,100.0	3,079.3	3,043.7	3,016.6	10.2	10.2	-151.37	25.5	296.3	494.2	475.7	18.52	26.684				
3,200.0	3,177.7	3,139.1	3,109.8	10.5	10.5	-150.36	15.8	314.7	522.7	503.6	19.09	27.380				
3,300.0	3,276.0	3,234.6	3,202.9	10.9	10.9	-149.46	6.0	333.1	551.3	531.6	19.67	28.027				
3,400.0	3,374.4	3,330.1	3,296.1	11.3	11.3	-148.64	-3.7	351.5	580.0	559.8	20.26	28.628				
3,500.0	3,472.7	3,425.6	3,389.3	11.7	11.7	-147.90	-13.5	369.9	608.8	588.0	20.86	29.186				
3,600.0	3,571.1	3,521.0	3,482.5	12.1	12.0	-147.23	-23.3	388.3	637.7	616.3	21.47	29.705				
3,700.0	3,669.4	3,616.5	3,575.6	12.5	12.4	-146.62	-33.0	406.7	666.7	644.6	22.08	30.188				
3,800.0	3,767.8	3,712.0	3,668.8	12.9	12.8	-146.05	-42.8	425.1	695.7	673.0	22.71	30.637				
3,900.0	3,866.1	3,807.5	3,762.0	13.3	13.2	-145.54	-52.6	443.5	724.8	701.5	23.34	31.057				
4,000.0	3,964.5	3,902.9	3,855.2	13.7	13.7	-145.06	-62.3	461.9	754.0	730.0	23.98	31.448				
4,100.0	4,062.8	3,998.4	3,948.3	14.1	14.1	-144.62	-72.1	480.3	783.1	758.5	24.62	31.813				
4,200.0	4,161.2	4,093.9	4,041.5	14.5	14.5	-144.21	-81.9	498.7	812.4	787.1	25.26	32.155				
4,300.0	4,259.5	4,189.4	4,134.7	15.0	14.9	-143.82	-91.6	517.1	841.6	815.7	25.92	32.475				
4,400.0	4,357.9	4,284.9	4,227.9	15.4	15.3	-143.47	-101.4	535.5	870.9	844.4	26.57	32.775				
4,500.0	4,456.2	4,380.3	4,321.1	15.8	15.7	-143.13	-111.1	553.9	900.3	873.0	27.23	33.056				
4,600.0	4,554.6	4,475.8	4,414.2	16.2	16.1	-142.82	-120.9	572.3	929.6	901.7	27.90	33.321				
4,700.0	4,652.9	4,571.3	4,507.4	16.7	16.6	-142.53	-130.7	590.7	959.0	930.4	28.57	33.570				
4,800.0	4,751.3	4,666.8	4,600.6	17.1	17.0	-142.25	-140.4	609.1	988.4	959.1	29.24	33.804				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #503H - OWB - PWP0											Offset Site Error:		0.0 usft
Survey Program:		0-r.5 MWD+IFR1+MS					Rule Assigned:				Offset Well Error:		3.0 usft		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning		
							+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)					
0.0	0.0	0.0	0.0	3.0	3.0	-21.98	150.2	-60.6	162.0	155.5	6.43	25.193			
100.0	100.0	100.0	100.0	3.2	3.2	-21.98	150.2	-60.6	162.0	155.1	6.89	23.499			
200.0	200.0	200.0	200.0	3.5	3.5	-21.98	150.2	-60.6	162.0	154.6	7.33	22.102			
300.0	300.0	300.0	300.0	3.7	3.7	-21.98	150.2	-60.6	162.0	154.2	7.74	20.922			
400.0	400.0	400.0	400.0	3.9	3.9	-21.98	150.2	-60.6	162.0	153.8	8.14	19.908			
500.0	500.0	500.0	500.0	4.1	4.1	-21.98	150.2	-60.6	162.0	153.5	8.51	19.024			
600.0	600.0	600.0	600.0	4.2	4.2	-21.98	150.2	-60.6	162.0	153.1	8.88	18.244			
700.0	700.0	700.0	700.0	4.4	4.4	-21.98	150.2	-60.6	162.0	152.7	9.23	17.549			
800.0	800.0	800.0	800.0	4.6	4.6	-21.98	150.2	-60.6	162.0	152.4	9.57	16.923			
900.0	900.0	900.0	900.0	4.8	4.8	-21.98	150.2	-60.6	162.0	152.1	9.90	16.357			
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-21.98	150.2	-60.6	162.0	151.7	10.22	15.841			
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-21.98	150.2	-60.6	162.0	151.4	10.54	15.367			
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-21.98	150.2	-60.6	162.0	151.1	10.85	14.931			
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-21.98	150.2	-60.6	162.0	150.8	11.15	14.527			
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-21.98	150.2	-60.6	162.0	150.5	11.44	14.152			
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-21.98	150.2	-60.6	162.0	150.2	11.73	13.802 CC			
1,600.0	1,600.0	1,602.9	1,602.9	5.9	5.9	122.70	148.7	-61.8	162.0	150.0	12.04	13.459			
1,700.0	1,699.8	1,705.8	1,705.6	6.1	6.1	122.61	144.4	-65.2	162.1	149.8	12.31	13.172			
1,800.0	1,799.5	1,808.7	1,808.1	6.3	6.4	122.45	137.1	-70.9	162.4	149.8	12.59	12.898 ES			
1,900.0	1,898.7	1,911.6	1,910.2	6.6	6.6	122.22	126.9	-78.8	162.7	149.8	12.87	12.640			
2,000.0	1,997.5	2,013.4	2,010.7	6.9	6.8	122.02	114.2	-88.7	163.2	150.1	13.12	12.441			
2,021.2	2,018.4	2,034.6	2,031.6	6.9	6.8	122.06	111.4	-90.9	163.5	150.3	13.16	12.420			
2,100.0	2,095.8	2,113.4	2,109.3	7.0	7.0	122.32	101.2	-98.9	164.7	151.3	13.39	12.296			
2,200.0	2,194.2	2,213.4	2,207.9	7.3	7.3	122.65	88.2	-109.0	166.2	152.5	13.71	12.121			
2,300.0	2,292.5	2,313.3	2,306.5	7.5	7.5	122.97	75.1	-119.2	167.7	153.7	14.05	11.938			
2,400.0	2,390.9	2,413.3	2,405.1	7.8	7.8	123.28	62.1	-129.4	169.2	154.8	14.41	11.749			
2,500.0	2,489.2	2,513.3	2,503.7	8.1	8.1	123.59	49.1	-139.5	170.8	156.0	14.78	11.556			
2,600.0	2,587.6	2,613.3	2,602.4	8.4	8.4	123.90	36.1	-149.7	172.3	157.2	15.17	11.360			
2,700.0	2,685.9	2,713.3	2,701.0	8.8	8.7	124.20	23.0	-159.8	173.9	158.3	15.57	11.163			
2,800.0	2,784.3	2,813.3	2,799.6	9.1	9.1	124.49	10.0	-170.0	175.4	159.4	16.00	10.966			
2,900.0	2,882.6	2,913.3	2,898.2	9.4	9.4	124.78	-3.0	-180.2	177.0	160.5	16.43	10.770			
3,000.0	2,981.0	3,013.2	2,996.8	9.8	9.8	125.06	-16.1	-190.3	178.5	161.6	16.88	10.576			
3,100.0	3,079.3	3,113.2	3,095.4	10.2	10.1	125.34	-29.1	-200.5	180.1	162.7	17.34	10.384			
3,200.0	3,177.7	3,213.2	3,194.0	10.5	10.5	125.61	-42.1	-210.7	181.6	163.8	17.82	10.195			
3,300.0	3,276.0	3,313.2	3,292.6	10.9	10.9	125.88	-55.1	-220.8	183.2	164.9	18.30	10.009			
3,400.0	3,374.4	3,413.2	3,391.2	11.3	11.2	126.15	-68.2	-231.0	184.8	166.0	18.80	9.827			
3,500.0	3,472.7	3,513.2	3,489.8	11.7	11.6	126.41	-81.2	-241.2	186.4	167.0	19.31	9.650			
3,600.0	3,571.1	3,613.1	3,588.4	12.1	12.0	126.66	-94.2	-251.3	187.9	168.1	19.83	9.476			
3,700.0	3,669.4	3,713.1	3,687.1	12.5	12.4	126.91	-107.2	-261.5	189.5	169.2	20.36	9.308			
3,800.0	3,767.8	3,813.1	3,785.7	12.9	12.8	127.16	-120.3	-271.6	191.1	170.2	20.90	9.143			
3,900.0	3,866.1	3,913.1	3,884.3	13.3	13.2	127.40	-133.3	-281.8	192.7	171.3	21.45	8.984			
4,000.0	3,964.5	4,013.1	3,982.9	13.7	13.6	127.64	-146.3	-292.0	194.3	172.3	22.01	8.829			
4,100.0	4,062.8	4,113.1	4,081.5	14.1	14.0	127.88	-159.3	-302.1	195.9	173.3	22.57	8.679			
4,200.0	4,161.2	4,213.0	4,180.1	14.5	14.4	128.11	-172.4	-312.3	197.5	174.4	23.14	8.533			
4,300.0	4,259.5	4,313.0	4,278.7	15.0	14.8	128.34	-185.4	-322.5	199.1	175.4	23.72	8.392			
4,400.0	4,357.9	4,413.0	4,377.3	15.4	15.2	128.56	-198.4	-332.6	200.7	176.4	24.31	8.256			
4,500.0	4,456.2	4,513.0	4,475.9	15.8	15.6	128.78	-211.5	-342.8	202.3	177.4	24.91	8.123			
4,600.0	4,554.6	4,613.0	4,574.5	16.2	16.1	129.00	-224.5	-352.9	203.9	178.4	25.51	7.995			
4,700.0	4,652.9	4,713.0	4,673.2	16.7	16.5	129.21	-237.5	-363.1	205.6	179.4	26.12	7.871			
4,800.0	4,751.3	4,812.9	4,771.8	17.1	16.9	129.42	-250.5	-373.3	207.2	180.4	26.73	7.751			
4,900.0	4,849.6	4,912.9	4,870.4	17.5	17.3	129.63	-263.6	-383.4	208.8	181.4	27.35	7.635			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #503H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Rule Assigned:							
Measured	Vertical	Measured	Vertical	Reference	Offset	Highside	Offset Wellbore Centre	Between	Between	No-Go	Separation	Warning	
Depth	Depth	Depth	Depth			Toolface	+N/-S	+E/-W	Centres	Ellipses	Distance	Factor	
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	(usft)	(usft)	(usft)	(usft)	(usft)		
5,000.0	4,948.0	5,012.9	4,969.0	17.9	17.8	129.83	-276.6	-393.6	210.4	182.4	27.97	7.523	
5,100.0	5,046.3	5,112.6	5,067.3	18.4	18.2	130.04	-289.6	-403.7	212.1	183.4	28.63	7.408	
5,200.0	5,144.7	5,210.3	5,163.8	18.8	18.7	130.46	-301.4	-413.0	214.4	184.9	29.50	7.267	
5,300.0	5,243.0	5,307.9	5,260.5	19.3	19.1	131.21	-312.0	-421.3	217.7	187.5	30.28	7.192	
5,400.0	5,341.4	5,405.4	5,357.3	19.7	19.5	132.28	-321.3	-428.5	222.2	191.1	31.14	7.135	
5,500.0	5,439.7	5,502.6	5,454.0	20.1	19.9	133.61	-329.3	-434.7	227.9	195.8	32.10	7.100	
5,524.0	5,463.3	5,525.9	5,477.1	20.2	20.0	133.97	-331.0	-436.0	229.5	197.1	32.33	7.097	
5,600.0	5,538.1	5,600.0	5,551.0	20.6	20.3	135.13	-335.9	-439.9	234.5	201.4	33.09	7.087	
5,700.0	5,636.9	5,696.4	5,647.2	21.0	20.6	136.58	-341.2	-444.0	241.2	207.1	34.06	7.082	
5,800.0	5,735.9	5,793.1	5,743.7	21.4	20.9	137.96	-345.3	-447.2	247.9	212.9	34.99	7.086	
5,900.0	5,835.1	5,889.7	5,840.2	21.8	21.2	139.27	-348.1	-449.4	254.7	218.8	35.88	7.100	
6,000.0	5,934.5	5,986.1	5,936.6	22.2	21.5	140.52	-349.5	-450.5	261.5	224.8	36.70	7.125	
6,100.0	6,034.1	6,083.6	6,034.1	22.6	21.6	141.70	-349.8	-450.7	268.2	230.8	37.40	7.172	
6,200.0	6,133.8	6,183.3	6,133.8	22.9	21.6	142.68	-349.8	-450.7	274.0	236.0	38.02	7.207	
6,300.0	6,233.7	6,283.1	6,233.7	23.3	21.6	143.39	-349.8	-450.7	278.4	239.9	38.54	7.223	
6,400.0	6,333.6	6,383.1	6,333.6	23.6	21.7	143.87	-349.8	-450.7	281.4	242.5	38.98	7.220	
6,500.0	6,433.6	6,483.0	6,433.6	23.9	21.7	144.12	-349.8	-450.7	283.1	243.8	39.32	7.200	
6,566.4	6,500.0	6,549.5	6,500.0	24.0	21.7	-0.55	-349.8	-450.7	283.4	244.0	39.42	7.189	
6,600.0	6,533.6	6,583.0	6,533.6	24.0	21.7	-0.55	-349.8	-450.7	283.4	244.0	39.44	7.186	
6,700.0	6,633.6	6,683.0	6,633.6	24.0	21.7	-0.55	-349.8	-450.7	283.4	243.9	39.50	7.175	
6,800.0	6,733.6	6,783.0	6,733.6	24.0	21.8	-0.55	-349.8	-450.7	283.4	243.8	39.56	7.163	
6,900.0	6,833.6	6,883.0	6,833.6	24.0	21.8	-0.55	-349.8	-450.7	283.4	243.8	39.63	7.152	
7,000.0	6,933.6	6,983.0	6,933.6	24.0	21.8	-0.55	-349.8	-450.7	283.4	243.7	39.69	7.140	
7,100.0	7,033.6	7,083.0	7,033.6	24.1	21.9	-0.55	-349.8	-450.7	283.4	243.6	39.76	7.128	
7,200.0	7,133.6	7,183.0	7,133.6	24.1	21.9	-0.55	-349.8	-450.7	283.4	243.6	39.82	7.116	
7,300.0	7,233.6	7,283.0	7,233.6	24.1	21.9	-0.55	-349.8	-450.7	283.4	243.5	39.89	7.104	
7,400.0	7,333.6	7,383.0	7,333.6	24.2	22.0	-0.55	-349.8	-450.7	283.4	243.4	39.96	7.093	
7,500.0	7,433.6	7,483.0	7,433.6	24.2	22.0	-0.55	-349.8	-450.7	283.4	243.4	40.03	7.081	
7,600.0	7,533.6	7,583.0	7,533.6	24.2	22.0	-0.55	-349.8	-450.7	283.4	243.3	40.09	7.068	
7,700.0	7,633.6	7,683.0	7,633.6	24.2	22.0	-0.55	-349.8	-450.7	283.4	243.2	40.16	7.056	
7,800.0	7,733.6	7,783.0	7,733.6	24.3	22.1	-0.55	-349.8	-450.7	283.4	243.2	40.23	7.044	
7,900.0	7,833.6	7,883.0	7,833.6	24.3	22.1	-0.55	-349.8	-450.7	283.4	243.1	40.30	7.032	
8,000.0	7,933.6	7,983.0	7,933.6	24.3	22.1	-0.55	-349.8	-450.7	283.4	243.0	40.37	7.020	
8,100.0	8,033.6	8,083.0	8,033.6	24.3	22.2	-0.55	-349.8	-450.7	283.4	243.0	40.44	7.007	
8,200.0	8,133.6	8,183.0	8,133.6	24.4	22.2	-0.55	-349.8	-450.7	283.4	242.9	40.51	6.995	
8,300.0	8,233.6	8,283.0	8,233.6	24.4	22.2	-0.55	-349.8	-450.7	283.4	242.8	40.59	6.983	
8,400.0	8,333.6	8,383.0	8,333.6	24.4	22.3	-0.55	-349.8	-450.7	283.4	242.7	40.66	6.970	
8,500.0	8,433.6	8,483.0	8,433.6	24.5	22.3	-0.55	-349.8	-450.7	283.4	242.7	40.73	6.958	
8,600.0	8,533.6	8,583.0	8,533.6	24.5	22.4	-0.55	-349.8	-450.7	283.4	242.6	40.81	6.945	
8,700.0	8,633.6	8,683.0	8,633.6	24.5	22.4	-0.55	-349.8	-450.7	283.4	242.5	40.88	6.933	
8,800.0	8,733.6	8,783.0	8,733.6	24.5	22.4	-0.55	-349.8	-450.7	283.4	242.4	40.95	6.920	
8,900.0	8,833.6	8,883.0	8,833.6	24.6	22.5	-0.55	-349.8	-450.7	283.4	242.4	41.03	6.907	
9,000.0	8,933.6	8,983.0	8,933.6	24.6	22.5	-0.55	-349.8	-450.7	283.4	242.3	41.10	6.895	
9,100.0	9,033.6	9,083.0	9,033.6	24.6	22.5	-0.55	-349.8	-450.7	283.4	242.2	41.18	6.882	
9,200.0	9,133.6	9,183.0	9,133.6	24.7	22.6	-0.55	-349.8	-450.7	283.4	242.1	41.26	6.869	
9,300.0	9,233.6	9,283.0	9,233.6	24.7	22.6	-0.55	-349.8	-450.7	283.4	242.1	41.33	6.856	
9,400.0	9,333.6	9,383.0	9,333.6	24.7	22.6	-0.55	-349.8	-450.7	283.4	242.0	41.41	6.843	
9,500.0	9,433.6	9,483.0	9,433.6	24.7	22.7	-0.55	-349.8	-450.7	283.4	241.9	41.49	6.831	
9,600.0	9,533.6	9,583.0	9,533.6	24.8	22.7	-0.55	-349.8	-450.7	283.4	241.8	41.57	6.818	
9,700.0	9,633.6	9,683.0	9,633.6	24.8	22.7	-0.55	-349.8	-450.7	283.4	241.8	41.65	6.805	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #503H - OWB - PWP0											Offset Site Error:		0.0 usft	
Survey Program:		0-r.5 MWD+IFR1+MS							Rule Assigned:					Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)						
9,800.0	9,733.6	9,783.0	9,733.6	24.8	22.8	-0.55	-349.8	-450.7	283.4	241.7	41.73	6.792				
9,810.0	9,743.6	9,793.0	9,743.6	24.8	22.8	-0.55	-349.8	-450.7	283.4	241.7	41.73	6.791 SF				
9,900.0	9,833.6	9,867.7	9,818.2	24.9	22.8	-0.55	-349.1	-450.7	284.5	243.0	41.52	6.853				
10,000.0	9,933.6	9,925.0	9,875.1	24.9	22.6	-0.55	-342.6	-450.8	296.4	255.7	40.74	7.276				
10,068.4	10,002.0	9,975.0	9,923.8	24.9	22.5	-0.55	-331.4	-450.9	311.8	271.4	40.35	7.727				
10,100.0	10,033.6	9,988.3	9,936.6	25.0	22.5	179.83	-327.6	-450.9	321.5	281.4	40.10	8.018				
10,150.0	10,083.3	10,015.1	9,961.8	25.1	22.4	179.83	-318.8	-451.0	342.5	302.6	39.94	8.574				
10,200.0	10,132.4	10,039.1	9,984.1	25.3	22.3	179.82	-309.7	-451.1	369.6	329.8	39.85	9.276				
10,250.0	10,180.5	10,060.1	10,003.1	25.5	22.2	179.82	-300.8	-451.1	402.2	362.4	39.80	10.105				
10,300.0	10,227.3	10,075.0	10,016.4	25.8	22.2	179.80	-294.1	-451.2	439.3	399.5	39.76	11.047				
10,350.0	10,272.4	10,092.6	10,031.8	26.0	22.1	179.78	-285.5	-451.3	480.1	440.3	39.81	12.060				
10,400.0	10,315.4	10,100.0	10,038.1	26.2	22.1	179.75	-281.8	-451.3	524.1	484.2	39.83	13.158				
10,450.0	10,356.0	10,113.1	10,049.3	26.4	22.1	179.71	-274.9	-451.4	570.3	530.3	39.92	14.284				
10,500.0	10,393.9	10,125.0	10,059.2	26.6	22.0	179.63	-268.4	-451.4	618.3	578.2	40.03	15.445				
10,550.0	10,428.8	10,125.0	10,059.2	26.8	22.0	179.41	-268.4	-451.4	667.3	627.2	40.09	16.645				
10,600.0	10,460.5	10,125.0	10,059.2	27.0	22.0	178.41	-268.4	-451.4	717.1	676.9	40.17	17.851				
10,650.0	10,488.7	10,125.0	10,059.2	27.2	22.0	1.90	-268.4	-451.4	767.0	726.8	40.25	19.055				
10,700.0	10,513.2	10,125.0	10,059.2	27.3	22.0	0.57	-268.4	-451.4	816.9	776.5	40.35	20.247				
10,750.0	10,533.8	10,125.0	10,059.2	27.5	22.0	0.33	-268.4	-451.4	866.2	825.8	40.44	21.420				
10,800.0	10,550.4	10,125.0	10,059.2	27.6	22.0	0.23	-268.4	-451.4	914.8	874.3	40.53	22.571				
10,850.0	10,562.8	10,111.5	10,048.0	27.7	22.1	0.16	-275.7	-451.4	962.2	921.6	40.57	23.715				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #504H - OWB - PWP0											Offset Site Error:		0.0 usft	
Survey Program:		0-r.5 MWD+IFR1						Rule Assigned:						Offset Well Error:		3.0 usft
Measured Depth	Vertical Reference	Measured Depth	Vertical Offset	Reference	Offset	Highside Toolface	Offset Wellbore Centre		Distance		No-Go Distance	Separation Factor	Warning			
Depth (usft)	Depth (usft)	Depth (usft)	Depth (usft)	(usft)	(usft)	(°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	(usft)					
0.0	0.0	0.0	0.0	3.0	3.0	11.06	151.1	29.5	154.0	147.5	6.43	23.949				
100.0	100.0	100.0	100.0	3.2	3.2	11.06	151.1	29.5	154.0	147.1	6.89	22.338				
200.0	200.0	200.0	200.0	3.5	3.5	11.06	151.1	29.5	154.0	146.6	7.33	21.010				
300.0	300.0	300.0	300.0	3.7	3.7	11.06	151.1	29.5	154.0	146.2	7.74	19.889				
400.0	400.0	400.0	400.0	3.9	3.9	11.06	151.1	29.5	154.0	145.8	8.14	18.925				
500.0	500.0	500.0	500.0	4.1	4.1	11.06	151.1	29.5	154.0	145.5	8.51	18.085				
600.0	600.0	600.0	600.0	4.2	4.2	11.06	151.1	29.5	154.0	145.1	8.88	17.343				
700.0	700.0	700.0	700.0	4.4	4.4	11.06	151.1	29.5	154.0	144.7	9.23	16.682				
800.0	800.0	800.0	800.0	4.6	4.6	11.06	151.1	29.5	154.0	144.4	9.57	16.087				
900.0	900.0	900.0	900.0	4.8	4.8	11.06	151.1	29.5	154.0	144.1	9.90	15.549				
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	11.06	151.1	29.5	154.0	143.7	10.22	15.058				
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	11.06	151.1	29.5	154.0	143.4	10.54	14.608				
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	11.06	151.1	29.5	154.0	143.1	10.85	14.193				
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	11.06	151.1	29.5	154.0	142.8	11.15	13.810				
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	11.06	151.1	29.5	154.0	142.5	11.44	13.453				
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	11.06	151.1	29.5	154.0	142.2	11.73	13.121 CC, ES				
1,600.0	1,600.0	1,601.8	1,601.8	5.9	5.9	156.67	150.2	31.1	155.0	142.9	12.07	12.834				
1,700.0	1,699.8	1,703.2	1,703.0	6.1	6.1	159.25	147.4	35.7	158.2	145.8	12.39	12.763 SF				
1,800.0	1,799.5	1,803.8	1,803.2	6.3	6.4	163.28	142.8	43.3	164.2	151.5	12.73	12.897				
1,900.0	1,898.7	1,903.2	1,901.9	6.6	6.6	168.34	136.5	53.8	173.9	160.8	13.10	13.278				
2,000.0	1,997.5	2,001.0	1,998.5	6.9	6.9	173.94	128.5	67.0	188.2	174.7	13.49	13.945				
2,021.2	2,018.4	2,021.6	2,018.7	6.9	6.9	175.16	126.7	70.1	191.8	178.3	13.55	14.157				
2,100.0	2,095.8	2,097.2	2,092.9	7.0	7.2	179.63	119.1	82.7	206.5	192.7	13.81	14.954				
2,200.0	2,194.2	2,192.0	2,185.3	7.3	7.4	-174.88	108.2	100.8	227.2	213.0	14.16	16.045				
2,300.0	2,292.5	2,287.2	2,277.8	7.5	7.7	-169.97	96.5	120.1	249.9	235.4	14.58	17.138				
2,400.0	2,390.9	2,382.5	2,370.3	7.8	8.0	-165.87	84.8	139.5	274.2	259.2	15.01	18.269				
2,500.0	2,489.2	2,477.7	2,462.8	8.1	8.3	-162.43	73.2	158.8	299.6	284.2	15.45	19.389				
2,600.0	2,587.6	2,572.9	2,555.3	8.4	8.6	-159.52	61.5	178.2	325.9	310.0	15.92	20.473				
2,700.0	2,685.9	2,668.1	2,647.8	8.8	8.9	-157.04	49.9	197.5	352.9	336.5	16.41	21.511				
2,800.0	2,784.3	2,763.4	2,740.3	9.1	9.2	-154.91	38.2	216.9	380.4	363.5	16.91	22.497				
2,900.0	2,882.6	2,858.6	2,832.8	9.4	9.6	-153.06	26.5	236.3	408.4	391.0	17.43	23.428				
3,000.0	2,981.0	2,953.8	2,925.3	9.8	9.9	-151.45	14.9	255.6	436.7	418.7	17.97	24.302				
3,100.0	3,079.3	3,049.0	3,017.9	10.2	10.3	-150.03	3.2	275.0	465.3	446.8	18.52	25.123				
3,200.0	3,177.7	3,144.3	3,110.4	10.5	10.6	-148.78	-8.5	294.3	494.1	475.0	19.08	25.890				
3,300.0	3,276.0	3,239.5	3,202.9	10.9	11.0	-147.66	-20.1	313.7	523.1	503.4	19.66	26.608				
3,400.0	3,374.4	3,334.7	3,295.4	11.3	11.4	-146.66	-31.8	333.0	552.3	532.0	20.24	27.279				
3,500.0	3,472.7	3,429.9	3,387.9	11.7	11.8	-145.76	-43.5	352.4	581.6	560.7	20.84	27.906				
3,600.0	3,571.1	3,525.2	3,480.4	12.1	12.2	-144.95	-55.1	371.7	611.0	589.6	21.44	28.492				
3,700.0	3,669.4	3,620.4	3,572.9	12.5	12.6	-144.21	-66.8	391.1	640.5	618.5	22.06	29.039				
3,800.0	3,767.8	3,715.6	3,665.4	12.9	13.0	-143.53	-78.4	410.4	670.2	647.5	22.68	29.551				
3,900.0	3,866.1	3,810.8	3,757.9	13.3	13.4	-142.92	-90.1	429.8	699.9	676.6	23.30	30.031				
4,000.0	3,964.5	3,906.1	3,850.4	13.7	13.8	-142.35	-101.8	449.2	729.6	705.7	23.94	30.480				
4,100.0	4,062.8	4,001.3	3,942.9	14.1	14.2	-141.83	-113.4	468.5	759.5	734.9	24.58	30.901				
4,200.0	4,161.2	4,096.5	4,035.4	14.5	14.6	-141.34	-125.1	487.9	789.3	764.1	25.22	31.296				
4,300.0	4,259.5	4,191.7	4,127.9	15.0	15.1	-140.89	-136.8	507.2	819.3	793.4	25.87	31.668				
4,400.0	4,357.9	4,287.0	4,220.4	15.4	15.5	-140.47	-148.4	526.6	849.2	822.7	26.53	32.017				
4,500.0	4,456.2	4,382.2	4,312.9	15.8	15.9	-140.09	-160.1	545.9	879.3	852.1	27.18	32.345				
4,600.0	4,554.6	4,477.4	4,405.4	16.2	16.3	-139.72	-171.8	565.3	909.3	881.5	27.85	32.655				
4,700.0	4,652.9	4,572.6	4,497.9	16.7	16.8	-139.38	-183.4	584.6	939.4	910.9	28.51	32.948				
4,800.0	4,751.3	4,667.9	4,590.4	17.1	17.2	-139.06	-195.1	604.0	969.5	940.3	29.18	33.224				
4,900.0	4,849.6	4,763.1	4,682.9	17.5	17.6	-138.76	-206.7	623.3	999.6	969.8	29.85	33.485				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #504H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:							
Measured	Vertical	Measured	Vertical	Reference	Offset	Highside		Between	Between	No-Go	Separation	Warning	
Depth	Depth	Depth	Depth			Toolface		Centres	Ellipses	Distance	Factor		
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	+N/-S (usft)	+E/-W (usft)	(usft)	(usft)	(usft)		

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #703H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		Warning						
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor		
0.0	0.0	0.0	0.0	3.0	3.0	-11.43	150.6	-30.5	153.7	147.3	6.43	23.907		
100.0	100.0	100.0	100.0	3.2	3.2	-11.43	150.6	-30.5	153.7	146.8	6.89	22.299		
200.0	200.0	200.0	200.0	3.5	3.5	-11.43	150.6	-30.5	153.7	146.4	7.33	20.973		
300.0	300.0	300.0	300.0	3.7	3.7	-11.43	150.6	-30.5	153.7	146.0	7.74	19.854		
400.0	400.0	400.0	400.0	3.9	3.9	-11.43	150.6	-30.5	153.7	145.6	8.14	18.892		
500.0	500.0	500.0	500.0	4.1	4.1	-11.43	150.6	-30.5	153.7	145.2	8.51	18.053		
600.0	600.0	600.0	600.0	4.2	4.2	-11.43	150.6	-30.5	153.7	144.8	8.88	17.313		
700.0	700.0	700.0	700.0	4.4	4.4	-11.43	150.6	-30.5	153.7	144.5	9.23	16.653		
800.0	800.0	800.0	800.0	4.6	4.6	-11.43	150.6	-30.5	153.7	144.1	9.57	16.059		
900.0	900.0	900.0	900.0	4.8	4.8	-11.43	150.6	-30.5	153.7	143.8	9.90	15.522		
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-11.43	150.6	-30.5	153.7	143.5	10.22	15.032		
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-11.43	150.6	-30.5	153.7	143.2	10.54	14.583		
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-11.43	150.6	-30.5	153.7	142.8	10.85	14.169		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-11.43	150.6	-30.5	153.7	142.5	11.15	13.786		
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-11.43	150.6	-30.5	153.7	142.3	11.44	13.430		
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-11.43	150.6	-30.5	153.7	142.0	11.73	13.098		
1,600.0	1,600.0	1,603.8	1,603.8	5.9	5.9	133.27	149.1	-31.6	153.7	141.6	12.07	12.729		
1,700.0	1,699.8	1,707.6	1,707.4	6.1	6.1	133.20	144.5	-34.9	153.6	141.2	12.38	12.404		
1,800.0	1,799.5	1,811.3	1,810.7	6.3	6.4	133.09	136.9	-40.3	153.4	140.7	12.70	12.078		
1,900.0	1,898.7	1,915.1	1,913.6	6.6	6.6	132.93	126.3	-48.0	153.1	140.1	13.04	11.748		
2,000.0	1,997.5	2,018.8	2,016.0	6.9	6.9	132.74	112.6	-57.8	152.8	139.5	13.38	11.427		
2,021.2	2,018.4	2,040.8	2,037.6	6.9	6.9	132.69	109.3	-60.2	152.8	139.4	13.41	11.393		
2,100.0	2,095.8	2,120.1	2,115.4	7.0	7.1	132.40	97.0	-69.1	152.3	138.6	13.62	11.179		
2,200.0	2,194.2	2,220.1	2,213.6	7.3	7.3	132.03	81.3	-80.4	151.6	137.6	13.98	10.843		
2,300.0	2,292.5	2,320.1	2,311.7	7.5	7.6	131.66	65.7	-91.6	150.9	136.5	14.36	10.509		
2,400.0	2,390.9	2,420.1	2,409.8	7.8	7.9	131.28	50.1	-102.9	150.2	135.5	14.76	10.180		
2,500.0	2,489.2	2,520.1	2,507.9	8.1	8.2	130.90	34.4	-114.1	149.6	134.4	15.17	9.859		
2,600.0	2,587.6	2,620.1	2,606.0	8.4	8.5	130.51	18.8	-125.4	148.9	133.3	15.60	9.548		
2,700.0	2,685.9	2,720.1	2,704.2	8.8	8.8	130.12	3.2	-136.6	148.3	132.2	16.03	9.247		
2,800.0	2,784.3	2,820.1	2,802.3	9.1	9.2	129.73	-12.5	-147.9	147.6	131.1	16.48	8.957		
2,900.0	2,882.6	2,920.1	2,900.4	9.4	9.5	129.33	-28.1	-159.1	147.0	130.0	16.93	8.680		
3,000.0	2,981.0	3,020.1	2,998.5	9.8	9.9	128.94	-43.7	-170.4	146.4	129.0	17.39	8.414		
3,100.0	3,079.3	3,120.0	3,096.6	10.2	10.3	128.53	-59.3	-181.6	145.7	127.9	17.86	8.160		
3,200.0	3,177.7	3,220.0	3,194.8	10.5	10.6	128.13	-75.0	-192.9	145.1	126.8	18.33	7.918		
3,300.0	3,276.0	3,320.0	3,292.9	10.9	11.0	127.72	-90.6	-204.1	144.5	125.7	18.80	7.687		
3,400.0	3,374.4	3,420.0	3,391.0	11.3	11.4	127.30	-106.2	-215.4	143.9	124.6	19.27	7.468		
3,500.0	3,472.7	3,520.0	3,489.1	11.7	11.8	126.89	-121.9	-226.7	143.3	123.6	19.74	7.259		
3,600.0	3,571.1	3,620.0	3,587.2	12.1	12.2	126.47	-137.5	-237.9	142.7	122.5	20.22	7.060		
3,700.0	3,669.4	3,720.0	3,685.4	12.5	12.6	126.05	-153.1	-249.2	142.2	121.5	20.69	6.872		
3,800.0	3,767.8	3,820.0	3,783.5	12.9	13.0	125.62	-168.8	-260.4	141.6	120.4	21.16	6.692		
3,900.0	3,866.1	3,920.0	3,881.6	13.3	13.5	125.19	-184.4	-271.7	141.0	119.4	21.63	6.522		
4,000.0	3,964.5	4,020.0	3,979.7	13.7	13.9	124.76	-200.0	-282.9	140.5	118.4	22.09	6.360		
4,100.0	4,062.8	4,120.0	4,077.8	14.1	14.3	124.32	-215.7	-294.2	139.9	117.4	22.55	6.206		
4,200.0	4,161.2	4,220.0	4,176.0	14.5	14.7	123.88	-231.3	-305.4	139.4	116.4	23.01	6.059		
4,300.0	4,259.5	4,320.0	4,274.1	15.0	15.1	123.44	-246.9	-316.7	138.9	115.4	23.46	5.919		
4,400.0	4,357.9	4,420.0	4,372.2	15.4	15.6	122.99	-262.6	-327.9	138.4	114.5	23.91	5.787		
4,500.0	4,456.2	4,519.9	4,470.3	15.8	16.0	122.54	-278.2	-339.2	137.9	113.5	24.35	5.660		
4,600.0	4,554.6	4,619.9	4,568.4	16.2	16.4	122.09	-293.8	-350.4	137.3	112.6	24.79	5.540		
4,700.0	4,652.9	4,719.9	4,666.6	16.7	16.9	121.63	-309.5	-361.7	136.9	111.6	25.22	5.426		
4,800.0	4,751.3	4,819.9	4,764.7	17.1	17.3	121.17	-325.1	-372.9	136.4	110.7	25.65	5.316		
4,900.0	4,849.6	4,919.9	4,862.8	17.5	17.7	120.71	-340.7	-384.2	135.9	109.8	26.07	5.214		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #703H - OWB - PWP0													Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)				
4,988.2	4,936.4	5,007.5	4,948.8	17.9	18.1	120.39	-354.2	-393.9	135.6	109.2	26.43	5.131	CC	
5,000.0	4,948.0	5,019.1	4,960.2	17.9	18.2	120.38	-355.9	-395.2	135.6	109.1	26.49	5.120		
5,100.0	5,046.3	5,118.0	5,057.6	18.4	18.6	120.64	-369.8	-405.1	136.1	109.1	27.07	5.030	ES	
5,200.0	5,144.7	5,216.7	5,155.1	18.8	19.0	121.51	-382.3	-414.1	137.6	109.8	27.81	4.947		
5,300.0	5,243.0	5,315.4	5,252.8	19.3	19.4	122.95	-393.4	-422.1	139.9	111.2	28.71	4.874		
5,400.0	5,341.4	5,413.9	5,350.6	19.7	19.8	124.90	-403.2	-429.2	143.4	113.6	29.77	4.815		
5,500.0	5,439.7	5,512.1	5,448.3	20.1	20.2	127.29	-411.5	-435.2	148.0	117.0	30.99	4.774		
5,524.0	5,463.3	5,535.6	5,471.7	20.2	20.3	127.91	-413.3	-436.5	149.3	118.0	31.30	4.769		
5,600.0	5,538.1	5,610.1	5,545.9	20.6	20.6	129.90	-418.5	-440.2	153.6	121.3	32.28	4.758		
5,700.0	5,636.9	5,708.0	5,643.5	21.0	20.9	132.33	-424.1	-444.2	159.5	126.0	33.53	4.757		
5,800.0	5,735.9	5,805.7	5,741.1	21.4	21.2	134.59	-428.4	-447.3	165.6	130.9	34.71	4.771		
5,900.0	5,835.1	5,903.3	5,838.6	21.8	21.5	136.67	-431.3	-449.4	172.0	136.1	35.83	4.800		
6,000.0	5,934.5	6,000.0	5,935.3	22.2	21.8	138.59	-432.9	-450.5	178.5	141.6	36.84	4.845		
6,100.0	6,034.1	6,098.8	6,034.1	22.6	21.9	140.38	-433.2	-450.7	185.1	147.4	37.71	4.907		
6,200.0	6,133.8	6,198.5	6,133.8	22.9	21.9	141.81	-433.2	-450.7	190.7	152.3	38.45	4.960		
6,300.0	6,233.7	6,298.4	6,233.7	23.3	21.9	142.84	-433.2	-450.7	195.1	156.0	39.06	4.995		
6,400.0	6,333.6	6,398.3	6,333.6	23.6	22.0	143.51	-433.2	-450.7	198.1	158.6	39.55	5.009		
6,500.0	6,433.6	6,498.3	6,433.6	23.9	22.0	143.87	-433.2	-450.7	199.8	159.8	39.91	5.005		
6,566.4	6,500.0	6,564.7	6,500.0	24.0	22.0	-0.78	-433.2	-450.7	200.1	160.0	40.02	4.999		
6,600.0	6,533.6	6,598.3	6,533.6	24.0	22.0	-0.78	-433.2	-450.7	200.1	160.0	40.03	4.998		
6,700.0	6,633.6	6,698.3	6,633.6	24.0	22.1	-0.78	-433.2	-450.7	200.1	160.0	40.09	4.990		
6,800.0	6,733.6	6,798.3	6,733.6	24.0	22.1	-0.78	-433.2	-450.7	200.1	159.9	40.16	4.982		
6,900.0	6,833.6	6,898.3	6,833.6	24.0	22.1	-0.78	-433.2	-450.7	200.1	159.8	40.22	4.974		
7,000.0	6,933.6	6,998.3	6,933.6	24.0	22.1	-0.78	-433.2	-450.7	200.1	159.8	40.28	4.967		
7,100.0	7,033.6	7,098.3	7,033.6	24.1	22.2	-0.78	-433.2	-450.7	200.1	159.7	40.35	4.959		
7,200.0	7,133.6	7,198.3	7,133.6	24.1	22.2	-0.78	-433.2	-450.7	200.1	159.7	40.41	4.951		
7,300.0	7,233.6	7,298.3	7,233.6	24.1	22.2	-0.78	-433.2	-450.7	200.1	159.6	40.48	4.943		
7,400.0	7,333.6	7,398.3	7,333.6	24.2	22.3	-0.78	-433.2	-450.7	200.1	159.5	40.54	4.935		
7,500.0	7,433.6	7,498.3	7,433.6	24.2	22.3	-0.78	-433.2	-450.7	200.1	159.5	40.61	4.926		
7,600.0	7,533.6	7,598.3	7,533.6	24.2	22.3	-0.78	-433.2	-450.7	200.1	159.4	40.68	4.918		
7,700.0	7,633.6	7,698.3	7,633.6	24.2	22.4	-0.78	-433.2	-450.7	200.1	159.3	40.74	4.910		
7,800.0	7,733.6	7,798.3	7,733.6	24.3	22.4	-0.78	-433.2	-450.7	200.1	159.3	40.81	4.902		
7,900.0	7,833.6	7,898.3	7,833.6	24.3	22.4	-0.78	-433.2	-450.7	200.1	159.2	40.88	4.894		
8,000.0	7,933.6	7,998.3	7,933.6	24.3	22.5	-0.78	-433.2	-450.7	200.1	159.1	40.95	4.886		
8,100.0	8,033.6	8,098.3	8,033.6	24.3	22.5	-0.78	-433.2	-450.7	200.1	159.0	41.02	4.877		
8,200.0	8,133.6	8,198.3	8,133.6	24.4	22.5	-0.78	-433.2	-450.7	200.1	159.0	41.09	4.869		
8,300.0	8,233.6	8,298.3	8,233.6	24.4	22.6	-0.78	-433.2	-450.7	200.1	158.9	41.16	4.861		
8,400.0	8,333.6	8,398.3	8,333.6	24.4	22.6	-0.78	-433.2	-450.7	200.1	158.8	41.23	4.852		
8,500.0	8,433.6	8,498.3	8,433.6	24.5	22.6	-0.78	-433.2	-450.7	200.1	158.8	41.30	4.844		
8,600.0	8,533.6	8,598.3	8,533.6	24.5	22.7	-0.78	-433.2	-450.7	200.1	158.7	41.38	4.835		
8,700.0	8,633.6	8,698.3	8,633.6	24.5	22.7	-0.78	-433.2	-450.7	200.1	158.6	41.45	4.827		
8,800.0	8,733.6	8,798.3	8,733.6	24.5	22.7	-0.78	-433.2	-450.7	200.1	158.5	41.52	4.818		
8,900.0	8,833.6	8,898.3	8,833.6	24.6	22.8	-0.78	-433.2	-450.7	200.1	158.5	41.60	4.810		
9,000.0	8,933.6	8,998.3	8,933.6	24.6	22.8	-0.78	-433.2	-450.7	200.1	158.4	41.67	4.801		
9,100.0	9,033.6	9,098.3	9,033.6	24.6	22.8	-0.78	-433.2	-450.7	200.1	158.3	41.75	4.793		
9,200.0	9,133.6	9,198.3	9,133.6	24.7	22.9	-0.78	-433.2	-450.7	200.1	158.2	41.82	4.784		
9,300.0	9,233.6	9,298.3	9,233.6	24.7	22.9	-0.78	-433.2	-450.7	200.1	158.2	41.90	4.775		
9,400.0	9,333.6	9,398.3	9,333.6	24.7	22.9	-0.78	-433.2	-450.7	200.1	158.1	41.97	4.767		
9,500.0	9,433.6	9,498.3	9,433.6	24.7	23.0	-0.78	-433.2	-450.7	200.1	158.0	42.05	4.758		
9,600.0	9,533.6	9,598.3	9,533.6	24.8	23.0	-0.78	-433.2	-450.7	200.1	157.9	42.13	4.749		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #703H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Rule Assigned:		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
9,700.0	9,633.6	9,698.3	9,633.6	24.8	23.0	-0.78	-433.2	-450.7	200.1	157.9	42.20	4.740	
9,800.0	9,733.6	9,798.3	9,733.6	24.8	23.1	-0.78	-433.2	-450.7	200.1	157.8	42.28	4.732	
9,900.0	9,833.6	9,898.3	9,833.6	24.9	23.1	-0.78	-433.2	-450.7	200.1	157.7	42.36	4.723	
10,000.0	9,933.6	9,998.3	9,933.6	24.9	23.1	-0.78	-433.2	-450.7	200.1	157.6	42.44	4.714	
10,068.4	10,002.0	10,066.7	10,002.0	24.9	23.2	-0.78	-433.2	-450.7	200.1	157.6	42.48	4.709 SF	
10,100.0	10,033.6	10,098.3	10,033.6	25.0	23.2	179.60	-433.2	-450.7	200.9	158.4	42.55	4.722	
10,150.0	10,083.3	10,148.0	10,083.3	25.1	23.2	179.61	-433.2	-450.7	205.9	163.1	42.78	4.812	
10,200.0	10,132.4	10,197.1	10,132.4	25.3	23.2	179.62	-433.2	-450.7	215.1	172.1	43.05	4.997	
10,250.0	10,180.5	10,245.2	10,180.5	25.5	23.2	179.63	-433.2	-450.7	228.6	185.3	43.33	5.276	
10,300.0	10,227.3	10,292.0	10,227.3	25.8	23.3	179.65	-433.2	-450.7	246.2	202.6	43.62	5.645	
10,350.0	10,272.4	10,337.1	10,272.4	26.0	23.3	179.66	-433.2	-450.7	267.9	224.0	43.91	6.100	
10,400.0	10,315.4	10,380.1	10,315.4	26.2	23.3	179.67	-433.2	-450.7	293.4	249.1	44.21	6.636	
10,450.0	10,356.0	10,420.7	10,356.0	26.4	23.3	179.68	-433.2	-450.7	322.5	278.0	44.49	7.248	
10,500.0	10,393.9	10,458.6	10,393.9	26.6	23.3	179.69	-433.2	-450.7	355.1	310.3	44.77	7.931	
10,550.0	10,428.8	10,493.5	10,428.8	26.8	23.3	179.69	-433.2	-450.7	390.8	345.8	45.03	8.680	
10,600.0	10,460.5	10,525.2	10,460.5	27.0	23.3	179.69	-433.2	-450.7	429.5	384.2	45.27	9.487	
10,650.0	10,488.7	10,553.4	10,488.7	27.2	23.4	179.68	-433.2	-450.7	470.7	425.2	45.48	10.349	
10,700.0	10,513.2	10,577.9	10,513.2	27.3	23.4	179.65	-433.2	-450.7	514.3	468.6	45.68	11.259	
10,750.0	10,533.8	10,598.5	10,533.8	27.5	23.4	179.62	-433.2	-450.7	559.8	514.0	45.84	12.212	
10,800.0	10,550.4	10,615.1	10,550.4	27.6	23.4	179.54	-433.2	-450.7	607.0	561.0	45.98	13.201	
10,850.0	10,562.8	10,627.5	10,562.8	27.7	23.4	179.40	-433.2	-450.7	655.4	609.3	46.09	14.222	
10,900.0	10,570.9	10,635.6	10,570.9	27.7	23.4	179.05	-433.2	-450.7	704.8	658.6	46.16	15.268	
10,950.0	10,574.7	10,639.4	10,574.7	27.8	23.4	176.70	-433.2	-450.7	754.6	708.4	46.20	16.333	
10,968.4	10,575.0	10,639.7	10,575.0	27.8	23.4	90.09	-433.2	-450.7	773.0	726.8	46.21	16.729	
11,000.0	10,575.0	10,639.7	10,575.0	27.8	23.4	90.09	-433.2	-450.7	804.6	758.4	46.22	17.409	
11,100.0	10,575.0	10,639.7	10,575.0	27.9	23.4	90.10	-433.2	-450.7	904.6	858.3	46.24	19.562	

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #704H - OWB - PWP0											Offset Site Error:		0.0 usft	
Survey Program:		0-r.5 MWD+IFR1						Rule Assigned:						Offset Well Error:		3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning			
0.0	0.0	0.0	0.0	3.0	3.0	-0.03	150.6	-0.1	150.6	144.2	6.43	23.433				
100.0	100.0	100.0	100.0	3.2	3.2	-0.03	150.6	-0.1	150.6	143.8	6.89	21.857				
200.0	200.0	200.0	200.0	3.5	3.5	-0.03	150.6	-0.1	150.6	143.3	7.33	20.557				
300.0	300.0	300.0	300.0	3.7	3.7	-0.03	150.6	-0.1	150.6	142.9	7.74	19.460				
400.0	400.0	400.0	400.0	3.9	3.9	-0.03	150.6	-0.1	150.6	142.5	8.14	18.517				
500.0	500.0	500.0	500.0	4.1	4.1	-0.03	150.6	-0.1	150.6	142.1	8.51	17.695				
600.0	600.0	600.0	600.0	4.2	4.2	-0.03	150.6	-0.1	150.6	141.8	8.88	16.969				
700.0	700.0	700.0	700.0	4.4	4.4	-0.03	150.6	-0.1	150.6	141.4	9.23	16.322				
800.0	800.0	800.0	800.0	4.6	4.6	-0.03	150.6	-0.1	150.6	141.1	9.57	15.741				
900.0	900.0	900.0	900.0	4.8	4.8	-0.03	150.6	-0.1	150.6	140.7	9.90	15.214				
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-0.03	150.6	-0.1	150.6	140.4	10.22	14.734				
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-0.03	150.6	-0.1	150.6	140.1	10.54	14.293				
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-0.03	150.6	-0.1	150.6	139.8	10.85	13.888				
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-0.03	150.6	-0.1	150.6	139.5	11.15	13.512				
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-0.03	150.6	-0.1	150.6	139.2	11.44	13.163				
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-0.03	150.6	-0.1	150.6	138.9	11.73	12.838 CC, ES				
1,600.0	1,600.0	1,602.9	1,602.9	5.9	5.9	145.66	149.6	1.4	151.1	139.0	12.08	12.511				
1,700.0	1,699.8	1,705.5	1,705.3	6.1	6.1	148.52	146.6	6.0	152.7	140.3	12.40	12.316				
1,800.0	1,799.5	1,807.2	1,806.6	6.3	6.4	153.07	141.5	13.6	156.1	143.4	12.74	12.260 SF				
1,900.0	1,898.7	1,907.8	1,906.4	6.6	6.6	158.97	134.6	24.0	162.5	149.4	13.10	12.407				
2,000.0	1,997.5	2,006.9	2,004.2	6.9	6.9	165.70	125.8	37.1	173.1	159.6	13.49	12.825				
2,021.2	2,018.4	2,027.7	2,024.7	6.9	7.0	167.18	123.7	40.2	175.9	162.4	13.55	12.983				
2,100.0	2,095.8	2,104.3	2,099.8	7.0	7.2	172.68	115.4	52.7	187.7	173.9	13.81	13.592				
2,200.0	2,194.2	2,200.3	2,193.5	7.3	7.4	179.28	103.7	70.3	204.9	190.7	14.13	14.503				
2,300.0	2,292.5	2,296.1	2,286.9	7.5	7.6	-175.10	91.8	88.0	224.4	209.9	14.52	15.453				
2,400.0	2,390.9	2,391.9	2,380.3	7.8	7.9	-170.38	80.0	105.7	245.7	230.8	14.94	16.451				
2,500.0	2,489.2	2,487.7	2,473.6	8.1	8.2	-166.41	68.2	123.4	268.4	253.0	15.37	17.462				
2,600.0	2,587.6	2,583.4	2,567.0	8.4	8.5	-163.06	56.4	141.1	292.2	276.4	15.83	18.460				
2,700.0	2,685.9	2,679.2	2,660.4	8.8	8.8	-160.21	44.6	158.8	316.8	300.5	16.30	19.430				
2,800.0	2,784.3	2,775.0	2,753.8	9.1	9.2	-157.76	32.7	176.5	342.0	325.2	16.80	20.362				
2,900.0	2,882.6	2,870.8	2,847.2	9.4	9.5	-155.65	20.9	194.2	367.8	350.5	17.31	21.251				
3,000.0	2,981.0	2,966.6	2,940.6	9.8	9.9	-153.81	9.1	211.9	394.0	376.1	17.83	22.094				
3,100.0	3,079.3	3,062.3	3,034.0	10.2	10.2	-152.20	-2.7	229.6	420.5	402.1	18.37	22.890				
3,200.0	3,177.7	3,158.1	3,127.3	10.5	10.6	-150.78	-14.5	247.3	447.3	428.4	18.92	23.640				
3,300.0	3,276.0	3,253.9	3,220.7	10.9	11.0	-149.52	-26.4	265.0	474.3	454.8	19.48	24.345				
3,400.0	3,374.4	3,349.7	3,314.1	11.3	11.3	-148.39	-38.2	282.7	501.5	481.4	20.05	25.007				
3,500.0	3,472.7	3,445.5	3,407.5	11.7	11.7	-147.38	-50.0	300.4	528.9	508.2	20.64	25.629				
3,600.0	3,571.1	3,541.2	3,500.9	12.1	12.1	-146.47	-61.8	318.1	556.4	535.1	21.23	26.212				
3,700.0	3,669.4	3,637.0	3,594.3	12.5	12.5	-145.65	-73.7	335.8	584.0	562.2	21.82	26.760				
3,800.0	3,767.8	3,732.8	3,687.7	12.9	12.9	-144.89	-85.5	353.5	611.7	589.3	22.43	27.274				
3,900.0	3,866.1	3,828.6	3,781.0	13.3	13.3	-144.21	-97.3	371.2	639.5	616.5	23.04	27.757				
4,000.0	3,964.5	3,924.4	3,874.4	13.7	13.7	-143.58	-109.1	388.9	667.4	643.8	23.66	28.211				
4,100.0	4,062.8	4,020.1	3,967.8	14.1	14.2	-143.00	-120.9	406.6	695.4	671.1	24.28	28.638				
4,200.0	4,161.2	4,115.9	4,061.2	14.5	14.6	-142.46	-132.8	424.3	723.4	698.5	24.91	29.040				
4,300.0	4,259.5	4,211.7	4,154.6	15.0	15.0	-141.97	-144.6	442.0	751.5	726.0	25.55	29.418				
4,400.0	4,357.9	4,307.5	4,248.0	15.4	15.4	-141.51	-156.4	459.7	779.6	753.4	26.18	29.776				
4,500.0	4,456.2	4,403.3	4,341.4	15.8	15.8	-141.08	-168.2	477.4	807.8	781.0	26.83	30.113				
4,600.0	4,554.6	4,499.1	4,434.7	16.2	16.3	-140.68	-180.0	495.1	836.0	808.5	27.47	30.431				
4,700.0	4,652.9	4,594.8	4,528.1	16.7	16.7	-140.31	-191.9	512.9	864.3	836.1	28.12	30.732				
4,800.0	4,751.3	4,690.6	4,621.5	17.1	17.1	-139.96	-203.7	530.6	892.5	863.8	28.78	31.017				
4,900.0	4,849.6	4,786.4	4,714.9	17.5	17.6	-139.63	-215.5	548.3	920.8	891.4	29.43	31.287				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - *TARHEEL FED COM #704H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:									
Measured Depth	Vertical Depth	Measured Depth	Vertical Depth	Reference	Offset	Highside Toolface	Offset Wellbore Centre		Distance		No-Go Distance	Separation Factor	Warning
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	(usft)		
5,000.0	4,948.0	4,882.2	4,808.3	17.9	18.0	-139.32	-227.3	566.0	949.2	919.1	30.09	31.543	
5,100.0	5,046.3	4,978.0	4,901.7	18.4	18.4	-139.03	-239.2	583.7	977.5	946.8	30.75	31.786	

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 504H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1+MS												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		No-Go		Separation		Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Distance (usft)	Factor	
0.0	0.0	0.0	0.0	3.0	3.0	89.16	0.4	30.1	30.1	23.7	6.43	4.680	
100.0	100.0	100.0	100.0	3.2	3.2	89.16	0.4	30.1	30.1	23.2	6.89	4.366	
200.0	200.0	200.0	200.0	3.5	3.5	89.16	0.4	30.1	30.1	22.8	7.33	4.106	
300.0	300.0	300.0	300.0	3.7	3.7	89.16	0.4	30.1	30.1	22.3	7.74	3.887	
400.0	400.0	400.0	400.0	3.9	3.9	89.16	0.4	30.1	30.1	22.0	8.14	3.698	
500.0	500.0	500.0	500.0	4.1	4.1	89.16	0.4	30.1	30.1	21.6	8.51	3.534	
600.0	600.0	600.0	600.0	4.2	4.2	89.16	0.4	30.1	30.1	21.2	8.88	3.389	
700.0	700.0	700.0	700.0	4.4	4.4	89.16	0.4	30.1	30.1	20.9	9.23	3.260	
800.0	800.0	800.0	800.0	4.6	4.6	89.16	0.4	30.1	30.1	20.5	9.57	3.144	
900.0	900.0	900.0	900.0	4.8	4.8	89.16	0.4	30.1	30.1	20.2	9.90	3.039	
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	89.16	0.4	30.1	30.1	19.9	10.22	2.943 Normal Operations	
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	89.16	0.4	30.1	30.1	19.5	10.54	2.855 Normal Operations	
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	89.16	0.4	30.1	30.1	19.2	10.85	2.774 Normal Operations	
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	89.16	0.4	30.1	30.1	18.9	11.15	2.699 Normal Operations	
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	89.16	0.4	30.1	30.1	18.6	11.44	2.629 Normal Operations	
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	89.16	0.4	30.1	30.1	18.4	11.73	2.564 Normal Operations, CC, ES, SF	
1,600.0	1,600.0	1,599.1	1,599.1	5.9	5.9	-126.70	-0.6	31.5	32.5	20.4	12.07	2.692 Normal Operations	
1,700.0	1,699.8	1,697.9	1,697.7	6.1	6.1	-127.99	-3.7	35.5	39.7	27.3	12.37	3.208	
1,800.0	1,799.5	1,796.0	1,795.4	6.3	6.3	-129.31	-8.7	42.3	51.7	39.0	12.69	4.073	
1,900.0	1,898.7	1,893.0	1,891.8	6.6	6.6	-130.32	-15.7	51.6	68.4	55.4	13.02	5.257	
2,000.0	1,997.5	1,988.8	1,986.4	6.9	6.8	-130.99	-24.5	63.4	89.9	76.5	13.36	6.725	
2,021.2	2,018.4	2,008.9	2,006.2	6.9	6.9	-131.10	-26.6	66.1	95.0	81.6	13.41	7.082	
2,100.0	2,095.8	2,083.1	2,079.1	7.0	7.1	-131.31	-35.1	77.4	115.2	101.5	13.66	8.431	
2,200.0	2,194.2	2,176.2	2,169.9	7.3	7.4	-130.69	-47.2	93.6	142.8	128.8	13.97	10.221	
2,300.0	2,292.5	2,271.6	2,262.6	7.5	7.6	-129.84	-60.8	111.6	171.8	157.4	14.35	11.970	
2,400.0	2,390.9	2,367.2	2,355.6	7.8	7.9	-129.23	-74.4	129.7	200.8	186.0	14.76	13.604	
2,500.0	2,489.2	2,462.9	2,448.5	8.1	8.2	-128.77	-87.9	147.8	229.8	214.6	15.18	15.136	
2,600.0	2,587.6	2,558.6	2,541.5	8.4	8.5	-128.42	-101.5	165.9	258.8	243.2	15.63	16.564	
2,700.0	2,685.9	2,654.3	2,634.5	8.8	8.8	-128.13	-115.1	184.0	287.9	271.8	16.09	17.892	
2,800.0	2,784.3	2,750.0	2,727.5	9.1	9.1	-127.90	-128.7	202.1	316.9	300.3	16.57	19.126	
2,900.0	2,882.6	2,845.7	2,820.4	9.4	9.5	-127.71	-142.2	220.2	346.0	328.9	17.07	20.271	
3,000.0	2,981.0	2,941.3	2,913.4	9.8	9.8	-127.55	-155.8	238.2	375.0	357.4	17.58	21.335	
3,100.0	3,079.3	3,037.0	3,006.4	10.2	10.2	-127.41	-169.4	256.3	404.1	386.0	18.10	22.322	
3,200.0	3,177.7	3,132.7	3,099.3	10.5	10.6	-127.29	-183.0	274.4	433.1	414.5	18.64	23.238	
3,300.0	3,276.0	3,228.4	3,192.3	10.9	11.0	-127.18	-196.6	292.5	462.2	443.0	19.18	24.090	
3,400.0	3,374.4	3,324.1	3,285.3	11.3	11.3	-127.09	-210.1	310.6	491.2	471.5	19.74	24.882	
3,500.0	3,472.7	3,419.8	3,378.3	11.7	11.7	-127.01	-223.7	328.7	520.3	500.0	20.31	25.618	
3,600.0	3,571.1	3,515.4	3,471.2	12.1	12.1	-126.93	-237.3	346.8	549.3	528.5	20.88	26.304	
3,700.0	3,669.4	3,611.1	3,564.2	12.5	12.5	-126.87	-250.9	364.9	578.4	556.9	21.47	26.944	
3,800.0	3,767.8	3,706.8	3,657.2	12.9	12.9	-126.81	-264.5	383.0	607.5	585.4	22.06	27.540	
3,900.0	3,866.1	3,802.5	3,750.1	13.3	13.3	-126.75	-278.0	401.0	636.5	613.9	22.65	28.098	
4,000.0	3,964.5	3,898.2	3,843.1	13.7	13.8	-126.70	-291.6	419.1	665.6	642.3	23.26	28.619	
4,100.0	4,062.8	3,993.9	3,936.1	14.1	14.2	-126.66	-305.2	437.2	694.6	670.8	23.86	29.107	
4,200.0	4,161.2	4,089.5	4,029.1	14.5	14.6	-126.62	-318.8	455.3	723.7	699.2	24.48	29.565	
4,300.0	4,259.5	4,185.2	4,122.0	15.0	15.0	-126.58	-332.4	473.4	752.8	727.7	25.10	29.994	
4,400.0	4,357.9	4,280.9	4,215.0	15.4	15.4	-126.54	-345.9	491.5	781.8	756.1	25.72	30.398	
4,500.0	4,456.2	4,376.6	4,308.0	15.8	15.9	-126.51	-359.5	509.6	810.9	784.5	26.35	30.777	
4,600.0	4,554.6	4,472.3	4,400.9	16.2	16.3	-126.48	-373.1	527.7	839.9	813.0	26.98	31.135	
4,700.0	4,652.9	4,567.9	4,493.9	16.7	16.7	-126.45	-386.7	545.7	869.0	841.4	27.61	31.472	
4,800.0	4,751.3	4,663.6	4,586.9	17.1	17.2	-126.42	-400.2	563.8	898.1	869.8	28.25	31.790	
4,900.0	4,849.6	4,759.3	4,679.8	17.5	17.6	-126.40	-413.8	581.9	927.1	898.2	28.89	32.091	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 504H - OWB - PWP0											Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1+MS											Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:									
Measured	Vertical	Measured	Vertical	Reference	Offset	Highside	Offset Wellbore Centre	Distance		No-Go	Separation	Warning	
Depth	Depth	Depth	Depth			Toolface	+N/-S	+E/-W	Between	Distance	Factor		
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	(usft)	(usft)	Centres	Ellipses			
									(usft)	(usft)	(usft)		
5,000.0	4,948.0	4,855.0	4,772.8	17.9	18.0	-126.37	-427.4	600.0	956.2	926.7	29.54	32.375	
5,100.0	5,046.3	4,950.7	4,865.8	18.4	18.5	-126.35	-441.0	618.1	985.3	955.1	30.18	32.644	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Semi Reference (usft)	Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre		Distance Between Centres (usft)		No-Go Distance (usft)	Separation Factor	Warning
							+N/-S (usft)	+E/-W (usft)					
0.0	0.0	0.0	0.0	3.0	3.0	-90.00	0.0	-29.9	29.9	23.5	6.43	4.653	
100.0	100.0	100.0	100.0	3.2	3.2	-90.00	0.0	-29.9	29.9	23.0	6.89	4.340	
200.0	200.0	200.0	200.0	3.5	3.5	-90.00	0.0	-29.9	29.9	22.6	7.33	4.082	
300.0	300.0	300.0	300.0	3.7	3.7	-90.00	0.0	-29.9	29.9	22.2	7.74	3.864	
400.0	400.0	400.0	400.0	3.9	3.9	-90.00	0.0	-29.9	29.9	21.8	8.14	3.677	
500.0	500.0	500.0	500.0	4.1	4.1	-90.00	0.0	-29.9	29.9	21.4	8.51	3.514	
600.0	600.0	600.0	600.0	4.2	4.2	-90.00	0.0	-29.9	29.9	21.0	8.88	3.369	
700.0	700.0	700.0	700.0	4.4	4.4	-90.00	0.0	-29.9	29.9	20.7	9.23	3.241	
800.0	800.0	800.0	800.0	4.6	4.6	-90.00	0.0	-29.9	29.9	20.3	9.57	3.126	
900.0	900.0	900.0	900.0	4.8	4.8	-90.00	0.0	-29.9	29.9	20.0	9.90	3.021	
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	-90.00	0.0	-29.9	29.9	19.7	10.22	2.926 Normal Operations	
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	-90.00	0.0	-29.9	29.9	19.4	10.54	2.838 Normal Operations	
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	-90.00	0.0	-29.9	29.9	19.1	10.85	2.758 Normal Operations	
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	-90.00	0.0	-29.9	29.9	18.8	11.15	2.683 Normal Operations	
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	-90.00	0.0	-29.9	29.9	18.5	11.44	2.614 Normal Operations	
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	-90.00	0.0	-29.9	29.9	18.2	11.73	2.549 Normal Operations, CC	
1,600.0	1,600.0	1,599.4	1,599.3	5.9	5.9	54.84	-1.4	-31.0	30.0	17.9	12.05	2.489 Caution - Monitor Closely	
1,700.0	1,699.8	1,698.7	1,698.6	6.1	6.1	55.18	-5.4	-34.2	30.2	17.8	12.32	2.448 Caution - Monitor Closely	
1,800.0	1,799.5	1,798.1	1,797.5	6.3	6.3	55.74	-12.2	-39.5	30.5	17.9	12.61	2.419 Caution - Monitor Closely	
1,900.0	1,898.7	1,897.4	1,896.2	6.6	6.6	56.51	-21.6	-46.9	30.9	18.1	12.89	2.401 Caution - Monitor Closely	
2,000.0	1,997.5	1,997.1	1,994.7	6.9	6.7	58.18	-33.5	-56.2	31.3	18.2	13.10	2.388 Caution - Monitor Closely	
2,021.2	2,018.4	2,018.4	2,015.7	6.9	6.8	59.11	-36.0	-58.2	31.2	18.0	13.12	2.374 Caution - Monitor Closely	
2,100.0	2,095.8	2,097.1	2,093.5	7.0	6.9	63.08	-45.6	-65.8	30.7	17.4	13.27	2.312 Caution - Monitor Closely	
2,200.0	2,194.2	2,197.1	2,192.2	7.3	7.2	68.28	-57.8	-75.3	30.3	16.8	13.46	2.249 Caution - Monitor Closely	
2,300.0	2,292.5	2,297.0	2,291.0	7.5	7.4	73.56	-69.9	-84.9	30.2	16.5	13.65	2.209 Caution - Monitor Closely	
2,304.4	2,296.9	2,301.5	2,295.4	7.6	7.4	73.80	-70.5	-85.3	30.2	16.5	13.66	2.207 Caution - Monitor Closely	
2,400.0	2,390.9	2,397.0	2,389.7	7.8	7.7	78.85	-82.1	-94.5	30.3	16.4	13.84	2.188 Caution - Monitor Closely, ES	
2,500.0	2,489.2	2,496.9	2,488.5	8.1	8.0	84.05	-94.2	-104.0	30.6	16.6	14.04	2.183 Caution - Monitor Closely, SF	
2,600.0	2,587.6	2,596.9	2,587.3	8.4	8.3	89.08	-106.4	-113.6	31.3	17.0	14.27	2.192 Caution - Monitor Closely	
2,700.0	2,685.9	2,696.9	2,686.0	8.8	8.6	93.89	-118.6	-123.1	32.1	17.6	14.54	2.209 Caution - Monitor Closely	
2,800.0	2,784.3	2,796.8	2,784.8	9.1	8.9	98.41	-130.7	-132.7	33.2	18.3	14.87	2.232 Caution - Monitor Closely	
2,900.0	2,882.6	2,896.8	2,883.5	9.4	9.3	102.63	-142.9	-142.3	34.4	19.2	15.26	2.257 Caution - Monitor Closely	
3,000.0	2,981.0	2,996.7	2,982.3	9.8	9.6	106.53	-155.0	-151.8	35.9	20.2	15.71	2.284 Caution - Monitor Closely	
3,100.0	3,079.3	3,096.7	3,081.0	10.2	10.0	110.12	-167.2	-161.4	37.5	21.2	16.22	2.309 Caution - Monitor Closely	
3,200.0	3,177.7	3,196.7	3,179.8	10.5	10.3	113.41	-179.4	-170.9	39.2	22.4	16.79	2.334 Caution - Monitor Closely	
3,300.0	3,276.0	3,296.6	3,278.6	10.9	10.7	116.40	-191.5	-180.5	41.0	23.6	17.40	2.357 Caution - Monitor Closely	
3,400.0	3,374.4	3,396.6	3,377.3	11.3	11.1	119.14	-203.7	-190.1	43.0	24.9	18.06	2.379 Caution - Monitor Closely	
3,500.0	3,472.7	3,496.5	3,476.1	11.7	11.5	121.63	-215.8	-199.6	45.0	26.3	18.75	2.400 Caution - Monitor Closely	
3,600.0	3,571.1	3,596.5	3,574.8	12.1	11.8	123.91	-228.0	-209.2	47.1	27.6	19.47	2.420 Caution - Monitor Closely	
3,700.0	3,669.4	3,696.5	3,673.6	12.5	12.2	125.99	-240.1	-218.7	49.3	29.1	20.21	2.439 Caution - Monitor Closely	
3,800.0	3,767.8	3,796.4	3,772.3	12.9	12.6	127.88	-252.3	-228.3	51.5	30.6	20.97	2.457 Caution - Monitor Closely	
3,900.0	3,866.1	3,896.4	3,871.1	13.3	13.0	129.62	-264.5	-237.9	53.8	32.1	21.75	2.474 Caution - Monitor Closely	
4,000.0	3,964.5	3,996.4	3,969.9	13.7	13.4	131.22	-276.6	-247.4	56.1	33.6	22.54	2.491 Caution - Monitor Closely	
4,100.0	4,062.8	4,096.3	4,068.6	14.1	13.8	132.69	-288.8	-257.0	58.5	35.2	23.34	2.507 Normal Operations	
4,200.0	4,161.2	4,196.3	4,167.4	14.5	14.2	134.04	-300.9	-266.5	60.9	36.8	24.16	2.522 Normal Operations	
4,300.0	4,259.5	4,296.2	4,266.1	15.0	14.6	135.29	-313.1	-276.1	63.4	38.4	24.97	2.537 Normal Operations	
4,400.0	4,357.9	4,396.2	4,364.9	15.4	15.0	136.45	-325.2	-285.7	65.8	40.0	25.80	2.552 Normal Operations	
4,500.0	4,456.2	4,496.2	4,463.6	15.8	15.4	137.52	-337.4	-295.2	68.3	41.7	26.63	2.566 Normal Operations	
4,600.0	4,554.6	4,596.1	4,562.4	16.2	15.8	138.51	-349.6	-304.8	70.8	43.4	27.46	2.580 Normal Operations	
4,700.0	4,652.9	4,696.1	4,661.2	16.7	16.2	139.44	-361.7	-314.3	73.4	45.1	28.30	2.593 Normal Operations	
4,800.0	4,751.3	4,796.0	4,759.9	17.1	16.7	140.31	-373.9	-323.9	75.9	46.8	29.14	2.606 Normal Operations	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0													Offset Site Error: 0.0 usft	
Survey Program: 0-r.5 MWD+IFR1				Offset					Rule Assigned:				Offset Well Error: 3.0 usft	
Reference		Offset		Semi Major Axis		Offset Wellbore Centre			Distance		Rule Assigned:		Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor		
4,900.0	4,849.6	4,896.0	4,858.7	17.5	17.1	141.12	-386.0	-333.5	78.5	48.5	29.98	2.618	Normal Operations	
5,000.0	4,948.0	4,996.0	4,957.4	17.9	17.5	141.87	-398.2	-343.0	81.1	50.3	30.83	2.630	Normal Operations	
5,100.0	5,046.3	5,095.9	5,056.2	18.4	17.9	142.58	-410.4	-352.6	83.7	52.0	31.67	2.642	Normal Operations	
5,200.0	5,144.7	5,195.9	5,154.9	18.8	18.3	143.25	-422.5	-362.2	86.3	53.8	32.52	2.653	Normal Operations	
5,300.0	5,243.0	5,295.8	5,253.7	19.3	18.8	143.88	-434.7	-371.7	88.9	55.5	33.37	2.664	Normal Operations	
5,400.0	5,341.4	5,395.8	5,352.5	19.7	19.2	144.47	-446.8	-381.3	91.5	57.3	34.22	2.675	Normal Operations	
5,500.0	5,439.7	5,495.8	5,451.2	20.1	19.6	145.03	-459.0	-390.8	94.2	59.1	35.08	2.685	Normal Operations	
5,524.0	5,463.3	5,519.7	5,474.9	20.2	19.7	145.16	-461.9	-393.1	94.8	59.5	35.27	2.688	Normal Operations	
5,600.0	5,538.1	5,595.7	5,550.0	20.6	20.0	145.40	-471.1	-400.4	96.4	60.5	35.87	2.688	Normal Operations	
5,700.0	5,636.9	5,695.3	5,648.3	21.0	20.4	145.23	-483.2	-409.8	97.3	60.8	36.51	2.666	Normal Operations	
5,800.0	5,735.9	5,793.9	5,746.0	21.4	20.8	144.96	-494.0	-418.4	97.9	60.8	37.11	2.639	Normal Operations	
5,900.0	5,835.1	5,892.6	5,843.9	21.8	21.2	144.73	-503.6	-425.9	98.4	60.7	37.69	2.611	Normal Operations	
6,000.0	5,934.5	5,991.3	5,942.0	22.2	21.6	144.54	-511.8	-432.4	98.9	60.6	38.24	2.585	Normal Operations	
6,100.0	6,034.1	6,089.9	6,040.3	22.6	22.0	144.38	-518.7	-437.8	99.2	60.5	38.77	2.559	Normal Operations	
6,200.0	6,133.8	6,188.6	6,138.7	22.9	22.4	144.25	-524.2	-442.1	99.5	60.3	39.27	2.534	Normal Operations	
6,300.0	6,233.7	6,287.2	6,237.2	23.3	22.7	144.15	-528.5	-445.5	99.8	60.0	39.73	2.510	Normal Operations	
6,400.0	6,333.6	6,385.9	6,335.8	23.6	23.0	144.08	-531.4	-447.7	99.9	59.8	40.15	2.488	Caution - Monitor Closely	
6,500.0	6,433.6	6,484.6	6,434.5	23.9	23.3	144.04	-532.9	-449.0	100.0	59.5	40.51	2.468	Caution - Monitor Closely	
6,566.4	6,500.0	6,550.1	6,500.0	24.0	23.4	-0.68	-533.2	-449.2	100.0	59.4	40.60	2.463	Caution - Monitor Closely	
6,600.0	6,533.6	6,583.7	6,533.6	24.0	23.4	-0.68	-533.2	-449.2	100.0	59.4	40.60	2.463	Caution - Monitor Closely	
6,700.0	6,633.6	6,683.7	6,633.6	24.0	23.4	-0.68	-533.2	-449.2	100.0	59.3	40.66	2.460	Caution - Monitor Closely	
6,800.0	6,733.6	6,783.7	6,733.6	24.0	23.4	-0.68	-533.2	-449.2	100.0	59.3	40.72	2.456	Caution - Monitor Closely	
6,900.0	6,833.6	6,883.7	6,833.6	24.0	23.4	-0.68	-533.2	-449.2	100.0	59.2	40.78	2.452	Caution - Monitor Closely	
7,000.0	6,933.6	6,983.7	6,933.6	24.0	23.5	-0.68	-533.2	-449.2	100.0	59.2	40.84	2.449	Caution - Monitor Closely	
7,100.0	7,033.6	7,083.7	7,033.6	24.1	23.5	-0.68	-533.2	-449.2	100.0	59.1	40.90	2.445	Caution - Monitor Closely	
7,200.0	7,133.6	7,183.7	7,133.6	24.1	23.5	-0.68	-533.2	-449.2	100.0	59.0	40.96	2.442	Caution - Monitor Closely	
7,300.0	7,233.6	7,283.7	7,233.6	24.1	23.5	-0.68	-533.2	-449.2	100.0	59.0	41.02	2.438	Caution - Monitor Closely	
7,400.0	7,333.6	7,383.7	7,333.6	24.2	23.6	-0.68	-533.2	-449.2	100.0	58.9	41.09	2.434	Caution - Monitor Closely	
7,500.0	7,433.6	7,483.7	7,433.6	24.2	23.6	-0.68	-533.2	-449.2	100.0	58.9	41.15	2.430	Caution - Monitor Closely	
7,600.0	7,533.6	7,583.7	7,533.6	24.2	23.6	-0.68	-533.2	-449.2	100.0	58.8	41.21	2.427	Caution - Monitor Closely	
7,700.0	7,633.6	7,683.7	7,633.6	24.2	23.6	-0.68	-533.2	-449.2	100.0	58.7	41.28	2.423	Caution - Monitor Closely	
7,800.0	7,733.6	7,783.7	7,733.6	24.3	23.7	-0.68	-533.2	-449.2	100.0	58.7	41.34	2.419	Caution - Monitor Closely	
7,900.0	7,833.6	7,883.7	7,833.6	24.3	23.7	-0.68	-533.2	-449.2	100.0	58.6	41.41	2.415	Caution - Monitor Closely	
8,000.0	7,933.6	7,983.7	7,933.6	24.3	23.7	-0.68	-533.2	-449.2	100.0	58.5	41.47	2.411	Caution - Monitor Closely	
8,100.0	8,033.6	8,083.7	8,033.6	24.3	23.8	-0.68	-533.2	-449.2	100.0	58.5	41.54	2.408	Caution - Monitor Closely	
8,200.0	8,133.6	8,183.7	8,133.6	24.4	23.8	-0.68	-533.2	-449.2	100.0	58.4	41.61	2.404	Caution - Monitor Closely	
8,300.0	8,233.6	8,283.7	8,233.6	24.4	23.8	-0.68	-533.2	-449.2	100.0	58.3	41.67	2.400	Caution - Monitor Closely	
8,400.0	8,333.6	8,383.7	8,333.6	24.4	23.8	-0.68	-533.2	-449.2	100.0	58.3	41.74	2.396	Caution - Monitor Closely	
8,500.0	8,433.6	8,483.7	8,433.6	24.5	23.9	-0.68	-533.2	-449.2	100.0	58.2	41.81	2.392	Caution - Monitor Closely	
8,600.0	8,533.6	8,583.7	8,533.6	24.5	23.9	-0.68	-533.2	-449.2	100.0	58.1	41.88	2.388	Caution - Monitor Closely	
8,700.0	8,633.6	8,683.7	8,633.6	24.5	23.9	-0.68	-533.2	-449.2	100.0	58.1	41.95	2.384	Caution - Monitor Closely	
8,800.0	8,733.6	8,783.7	8,733.6	24.5	24.0	-0.68	-533.2	-449.2	100.0	58.0	42.02	2.380	Caution - Monitor Closely	
8,900.0	8,833.6	8,883.7	8,833.6	24.6	24.0	-0.68	-533.2	-449.2	100.0	57.9	42.09	2.376	Caution - Monitor Closely	
9,000.0	8,933.6	8,983.7	8,933.6	24.6	24.0	-0.68	-533.2	-449.2	100.0	57.8	42.16	2.372	Caution - Monitor Closely	
9,100.0	9,033.6	9,083.7	9,033.6	24.6	24.1	-0.68	-533.2	-449.2	100.0	57.8	42.23	2.368	Caution - Monitor Closely	
9,200.0	9,133.6	9,183.7	9,133.6	24.7	24.1	-0.68	-533.2	-449.2	100.0	57.7	42.30	2.364	Caution - Monitor Closely	
9,300.0	9,233.6	9,283.7	9,233.6	24.7	24.1	-0.68	-533.2	-449.2	100.0	57.6	42.38	2.360	Caution - Monitor Closely	
9,400.0	9,333.6	9,383.7	9,333.6	24.7	24.1	-0.68	-533.2	-449.2	100.0	57.6	42.45	2.356	Caution - Monitor Closely	
9,500.0	9,433.6	9,483.7	9,433.6	24.7	24.2	-0.68	-533.2	-449.2	100.0	57.5	42.52	2.352	Caution - Monitor Closely	
9,600.0	9,533.6	9,583.7	9,533.6	24.8	24.2	-0.68	-533.2	-449.2	100.0	57.4	42.60	2.348	Caution - Monitor Closely	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0													Offset Site Error: 0.0 usft	
Survey Program: 0-r.5 MWD+IFR1		Offset		Semi Major Axis		Offset Wellbore Centre		Rule Assigned:			Offset Well Error: 3.0 usft			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning	
9,700.0	9,633.6	9,683.7	9,633.6	24.8	24.2	-0.68	-533.2	-449.2	100.0	57.3	42.67	2.344	Caution - Monitor Closely	
9,800.0	9,733.6	9,783.7	9,733.6	24.8	24.3	-0.68	-533.2	-449.2	100.0	57.3	42.74	2.340	Caution - Monitor Closely	
9,900.0	9,833.6	9,883.7	9,833.6	24.9	24.3	-0.68	-533.2	-449.2	100.0	57.2	42.82	2.336	Caution - Monitor Closely	
10,000.0	9,933.6	9,983.7	9,933.6	24.9	24.3	-0.68	-533.2	-449.2	100.0	57.1	42.90	2.331	Caution - Monitor Closely	
10,068.4	10,002.0	10,052.1	10,002.0	24.9	24.4	-0.68	-533.2	-449.2	100.0	57.1	42.94	2.329	Caution - Monitor Closely	
10,100.0	10,033.6	10,083.7	10,033.6	25.0	24.4	179.70	-533.2	-449.2	100.9	57.9	43.00	2.346	Caution - Monitor Closely	
10,150.0	10,083.3	10,133.4	10,083.3	25.1	24.4	179.71	-533.2	-449.2	105.8	62.6	43.23	2.447	Caution - Monitor Closely	
10,200.0	10,132.4	10,182.5	10,132.4	25.3	24.4	179.73	-533.2	-449.2	115.0	71.6	43.50	2.645	Normal Operations	
10,250.0	10,180.5	10,230.6	10,180.5	25.5	24.4	179.75	-533.2	-449.2	128.5	84.8	43.78	2.936	Normal Operations	
10,300.0	10,227.3	10,277.4	10,227.3	25.8	24.4	179.78	-533.2	-449.2	146.2	102.1	44.06	3.317		
10,350.0	10,272.4	10,322.5	10,272.4	26.0	24.5	179.80	-533.2	-449.2	167.8	123.5	44.36	3.783		
10,400.0	10,315.4	10,365.5	10,315.4	26.2	24.5	179.81	-533.2	-449.2	193.3	148.7	44.65	4.330		
10,450.0	10,356.0	10,406.1	10,356.0	26.4	24.5	179.83	-533.2	-449.2	222.4	177.5	44.93	4.951		
10,500.0	10,393.9	10,444.0	10,393.9	26.6	24.5	179.84	-533.2	-449.2	255.0	209.8	45.20	5.642		
10,550.0	10,428.8	10,478.9	10,428.8	26.8	24.5	179.85	-533.2	-449.2	290.7	245.3	45.45	6.397		
10,600.0	10,460.5	10,510.6	10,460.5	27.0	24.5	179.85	-533.2	-449.2	329.4	283.7	45.69	7.210		
10,650.0	10,488.7	10,538.8	10,488.7	27.2	24.5	179.85	-533.2	-449.2	370.7	324.8	45.90	8.075		
10,700.0	10,513.2	10,563.3	10,513.2	27.3	24.5	179.84	-533.2	-449.2	414.2	368.2	46.09	8.987		
10,750.0	10,533.8	10,583.9	10,533.8	27.5	24.5	179.82	-533.2	-449.2	459.8	413.5	46.25	9.940		
10,800.0	10,550.4	10,600.5	10,550.4	27.6	24.5	179.80	-533.2	-449.2	506.9	460.6	46.39	10.928		
10,850.0	10,562.8	10,612.9	10,562.8	27.7	24.6	179.74	-533.2	-449.2	555.4	508.9	46.49	11.946		
10,900.0	10,570.9	10,621.0	10,570.9	27.7	24.6	179.58	-533.2	-449.2	604.7	558.1	46.56	12.987		
10,950.0	10,574.7	10,624.8	10,574.7	27.8	24.6	178.58	-533.2	-449.2	654.5	607.9	46.60	14.045		
10,968.4	10,575.0	10,625.1	10,575.0	27.8	24.6	90.21	-533.2	-449.2	673.0	626.4	46.61	14.438		
11,000.0	10,575.0	10,625.1	10,575.0	27.8	24.6	90.22	-533.2	-449.2	704.5	657.9	46.62	15.113		
11,100.0	10,575.0	10,625.1	10,575.0	27.9	24.6	90.25	-533.2	-449.2	804.5	757.9	46.64	17.249		
11,200.0	10,575.0	10,625.1	10,575.0	28.0	24.6	90.28	-533.2	-449.2	904.5	857.9	46.67	19.383		
11,300.0	10,575.0	12,358.7	11,550.0	28.1	27.9	179.97	-1,537.7	-442.4	975.0	925.1	49.88	19.545		
11,400.0	10,575.0	12,458.7	11,550.0	28.2	28.1	179.97	-1,637.7	-441.8	975.0	924.5	50.54	19.291		
11,500.0	10,575.0	12,558.7	11,550.0	28.4	28.3	179.97	-1,737.7	-441.1	975.0	923.8	51.24	19.029		
11,600.0	10,575.0	12,658.7	11,550.0	28.6	28.5	179.97	-1,837.7	-440.4	975.0	923.0	51.97	18.761		
11,700.0	10,575.0	12,758.7	11,550.0	28.8	28.8	179.97	-1,937.7	-439.8	975.0	922.3	52.74	18.488		
11,800.0	10,575.0	12,858.7	11,550.0	29.1	29.1	179.97	-2,037.7	-439.1	975.0	921.5	53.54	18.210		
11,900.0	10,575.0	12,958.7	11,550.0	29.4	29.5	179.97	-2,137.7	-438.4	975.0	920.6	54.38	17.931		
12,000.0	10,575.0	13,058.7	11,550.0	29.8	29.9	179.97	-2,237.7	-437.7	975.0	919.8	55.24	17.650		
12,100.0	10,575.0	13,158.7	11,550.0	30.2	30.4	179.97	-2,337.7	-437.1	975.0	918.9	56.14	17.368		
12,200.0	10,575.0	13,258.7	11,550.0	30.7	30.9	179.97	-2,437.7	-436.4	975.0	917.9	57.06	17.087		
12,300.0	10,575.0	13,358.7	11,550.0	31.2	31.5	179.97	-2,537.7	-435.7	975.0	917.0	58.01	16.807		
12,400.0	10,575.0	13,458.7	11,550.0	31.8	32.1	179.97	-2,637.7	-435.1	975.0	916.0	58.99	16.529		
12,500.0	10,575.0	13,558.7	11,550.0	32.4	32.7	179.97	-2,737.7	-434.4	975.0	915.0	59.99	16.253		
12,600.0	10,575.0	13,658.7	11,550.0	33.0	33.4	179.97	-2,837.7	-433.7	975.0	914.0	61.01	15.980		
12,700.0	10,575.0	13,758.7	11,550.0	33.7	34.1	179.97	-2,937.7	-433.0	975.0	912.9	62.06	15.711		
12,800.0	10,575.0	13,858.7	11,550.0	34.5	34.8	179.97	-3,037.7	-432.4	975.0	911.9	63.13	15.445		
12,900.0	10,575.0	13,958.7	11,550.0	35.2	35.5	179.97	-3,137.7	-431.7	975.0	910.8	64.21	15.184		
13,000.0	10,575.0	14,058.7	11,550.0	36.0	36.3	179.97	-3,237.7	-431.0	975.0	909.7	65.32	14.927		
13,100.0	10,575.0	14,158.7	11,550.0	36.7	37.1	179.97	-3,337.7	-430.4	975.0	908.6	66.44	14.675		
13,200.0	10,575.0	14,258.7	11,550.0	37.5	37.9	179.97	-3,437.7	-429.7	975.0	907.4	67.58	14.427		
13,300.0	10,575.0	14,358.7	11,550.0	38.4	38.7	179.98	-3,537.7	-429.0	975.0	906.3	68.74	14.185		
13,400.0	10,575.0	14,458.7	11,550.0	39.2	39.5	179.98	-3,637.7	-428.4	975.0	905.1	69.91	13.947		
13,500.0	10,575.0	14,558.7	11,550.0	40.0	40.3	179.98	-3,737.7	-427.7	975.0	903.9	71.09	13.715		
13,600.0	10,575.0	14,658.7	11,550.0	40.9	41.2	179.98	-3,837.7	-427.0	975.0	902.7	72.29	13.487		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:		TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0											Offset Site Error:		0.0 usft	
Survey Program:		0-r.5 MWD+IFR1						Rule Assigned:						Offset Well Error:		3.0 usft
Measured Depth	Vertical	Measured	Vertical	Semi Major Axis		Highside Toolface	Offset Wellbore Centre		Distance			Separation Factor	Warning			
Depth (usft)	Depth (usft)	Depth (usft)	Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)					
13,700.0	10,575.0	14,758.7	11,550.0	41.7	42.0	179.98	-3,937.7	-426.3	975.0	901.5	73.50	13.264				
13,800.0	10,575.0	14,858.7	11,550.0	42.6	42.9	179.98	-4,037.7	-425.7	975.0	900.3	74.73	13.047				
13,900.0	10,575.0	14,958.7	11,550.0	43.4	43.7	179.98	-4,137.6	-425.0	975.0	899.0	75.97	12.835				
14,000.0	10,575.0	15,058.7	11,550.0	44.3	44.6	179.98	-4,237.6	-424.3	975.0	897.8	77.22	12.627				
14,100.0	10,575.0	15,158.7	11,550.0	45.2	45.5	179.98	-4,337.6	-423.7	975.0	896.5	78.47	12.424				
14,200.0	10,575.0	15,258.7	11,550.0	46.1	46.4	179.98	-4,437.6	-423.0	975.0	895.3	79.74	12.227				
14,300.0	10,575.0	15,358.7	11,550.0	47.0	47.2	179.98	-4,537.6	-422.3	975.0	894.0	81.02	12.034				
14,400.0	10,575.0	15,458.7	11,550.0	47.9	48.1	179.98	-4,637.6	-421.6	975.0	892.7	82.31	11.845				
14,500.0	10,575.0	15,558.7	11,550.0	48.8	49.0	179.98	-4,737.6	-421.0	975.0	891.4	83.61	11.661				
14,600.0	10,575.0	15,658.7	11,550.0	49.7	49.9	179.98	-4,837.6	-420.3	975.0	890.1	84.91	11.482				
14,700.0	10,575.0	15,758.7	11,550.0	50.6	50.8	179.98	-4,937.6	-419.6	975.0	888.8	86.23	11.307				
14,800.0	10,575.0	15,858.7	11,550.0	51.5	51.7	179.98	-5,037.6	-419.0	975.0	887.5	87.55	11.137				
14,900.0	10,575.0	15,958.7	11,550.0	52.4	52.6	179.98	-5,137.6	-418.3	975.0	886.1	88.88	10.970				
15,000.0	10,575.0	16,058.7	11,550.0	53.3	53.5	179.98	-5,237.6	-417.6	975.0	884.8	90.21	10.808				
15,100.0	10,575.0	16,158.7	11,550.0	54.2	54.5	179.98	-5,337.6	-416.9	975.0	883.4	91.56	10.649				
15,200.0	10,575.0	16,258.7	11,550.0	55.2	55.4	179.98	-5,437.6	-416.3	975.0	882.1	92.91	10.494				
15,300.0	10,575.0	16,358.7	11,550.0	56.1	56.3	179.98	-5,537.6	-415.6	975.0	880.7	94.26	10.344				
15,400.0	10,575.0	16,458.7	11,550.0	57.0	57.2	179.98	-5,637.6	-414.9	975.0	879.4	95.62	10.196				
15,500.0	10,575.0	16,558.7	11,550.0	57.9	58.1	179.98	-5,737.6	-414.3	975.0	878.0	96.99	10.053				
15,600.0	10,575.0	16,658.7	11,550.0	58.9	59.1	179.98	-5,837.6	-413.6	975.0	876.6	98.36	9.912				
15,700.0	10,575.0	16,758.7	11,550.0	59.8	60.0	179.98	-5,937.6	-412.9	975.0	875.3	99.74	9.775				
15,800.0	10,575.0	16,858.7	11,550.0	60.7	60.9	179.98	-6,037.6	-412.2	975.0	873.9	101.12	9.642				
15,900.0	10,575.0	16,958.7	11,550.0	61.6	61.8	179.98	-6,137.6	-411.6	975.0	872.5	102.51	9.511				
16,000.0	10,575.0	17,058.7	11,550.0	62.6	62.8	179.98	-6,237.6	-410.9	975.0	871.1	103.90	9.384				
16,100.0	10,575.0	17,158.7	11,550.0	63.5	63.7	179.98	-6,337.6	-410.2	975.0	869.7	105.30	9.260				
16,200.0	10,575.0	17,258.7	11,550.0	64.4	64.6	179.98	-6,437.6	-409.6	975.0	868.3	106.70	9.138				
16,300.0	10,575.0	17,358.7	11,550.0	65.4	65.6	179.98	-6,537.6	-408.9	975.0	866.9	108.10	9.019				
16,400.0	10,575.0	17,458.7	11,550.0	66.3	66.5	179.98	-6,637.6	-408.2	975.0	865.5	109.51	8.903				
16,500.0	10,575.0	17,558.7	11,550.0	67.3	67.4	179.98	-6,737.6	-407.5	975.0	864.1	110.92	8.790				
16,600.0	10,575.0	17,658.7	11,550.0	68.2	68.4	179.98	-6,837.6	-406.9	975.0	862.7	112.34	8.679				
16,700.0	10,575.0	17,758.7	11,550.0	69.1	69.3	179.98	-6,937.6	-406.2	975.0	861.2	113.76	8.571				
16,800.0	10,575.0	17,858.7	11,550.0	70.1	70.3	179.98	-7,037.6	-405.5	975.0	859.8	115.18	8.465				
16,900.0	10,575.0	17,958.7	11,550.0	71.0	71.2	179.98	-7,137.6	-404.9	975.0	858.4	116.61	8.362				
17,000.0	10,575.0	18,058.7	11,550.0	72.0	72.1	179.98	-7,237.6	-404.2	975.0	857.0	118.03	8.260				
17,100.0	10,575.0	18,158.7	11,550.0	72.9	73.1	179.98	-7,337.6	-403.5	975.0	855.5	119.47	8.161				
17,200.0	10,575.0	18,258.7	11,550.0	73.9	74.0	179.98	-7,437.6	-402.8	975.0	854.1	120.90	8.064				
17,300.0	10,575.0	18,358.7	11,550.0	74.8	75.0	179.98	-7,537.6	-402.2	975.0	852.7	122.34	7.970				
17,400.0	10,575.0	18,458.7	11,550.0	75.8	75.9	179.98	-7,637.6	-401.5	975.0	851.2	123.78	7.877				
17,500.0	10,575.0	18,558.7	11,550.0	76.7	76.9	179.98	-7,737.6	-400.8	975.0	849.8	125.22	7.786				
17,600.0	10,575.0	18,658.7	11,550.0	77.7	77.8	179.98	-7,837.6	-400.2	975.0	848.3	126.67	7.697				
17,700.0	10,575.0	18,758.7	11,550.0	78.6	78.8	179.98	-7,937.6	-399.5	975.0	846.9	128.11	7.610				
17,800.0	10,575.0	18,858.7	11,550.0	79.6	79.7	179.98	-8,037.6	-398.8	975.0	845.4	129.56	7.525				
17,900.0	10,575.0	18,958.7	11,550.0	80.5	80.7	179.98	-8,137.6	-398.1	975.0	844.0	131.02	7.442				
18,000.0	10,575.0	19,058.7	11,550.0	81.5	81.6	179.98	-8,237.6	-397.5	975.0	842.5	132.47	7.360				
18,100.0	10,575.0	19,158.7	11,550.0	82.4	82.6	179.98	-8,337.6	-396.8	975.0	841.1	133.93	7.280				
18,200.0	10,575.0	19,258.7	11,550.0	83.4	83.5	179.98	-8,437.6	-396.1	975.0	839.6	135.39	7.202				
18,300.0	10,575.0	19,358.7	11,550.0	84.3	84.5	179.98	-8,537.5	-395.5	975.0	838.2	136.85	7.125				
18,400.0	10,575.0	19,458.7	11,550.0	85.3	85.4	179.99	-8,637.5	-394.8	975.0	836.7	138.31	7.049				
18,500.0	10,575.0	19,558.7	11,550.0	86.2	86.4	179.99	-8,737.5	-394.1	975.0	835.2	139.77	6.976				
18,600.0	10,575.0	19,658.7	11,550.0	87.2	87.3	179.99	-8,837.5	-393.4	975.0	833.8	141.24	6.903				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0													Offset Site Error: 0.0 usft	
Survey Program: 0-r.5 MWD+IFR1				Rule Assigned:									Offset Well Error: 3.0 usft	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning	
18,700.0	10,575.0	19,758.7	11,550.0	88.1	88.3	179.99	-8,937.5	-392.8	975.0	832.3	142.71	6.832		
18,800.0	10,575.0	19,858.7	11,550.0	89.1	89.2	179.99	-9,037.5	-392.1	975.0	830.8	144.18	6.763		
18,900.0	10,575.0	19,958.7	11,550.0	90.1	90.2	179.99	-9,137.5	-391.4	975.0	829.4	145.65	6.694		
19,000.0	10,575.0	20,058.7	11,550.0	91.0	91.1	179.99	-9,237.5	-390.8	975.0	827.9	147.12	6.627		
19,100.0	10,575.0	20,158.7	11,550.0	92.0	92.1	179.99	-9,337.5	-390.1	975.0	826.4	148.60	6.561		
19,200.0	10,575.0	20,258.7	11,550.0	92.9	93.1	179.99	-9,437.5	-389.4	975.0	824.9	150.07	6.497		
19,300.0	10,575.0	20,358.7	11,550.0	93.9	94.0	179.99	-9,537.5	-388.7	975.0	823.5	151.55	6.434		
19,400.0	10,575.0	20,458.7	11,550.0	94.8	95.0	179.99	-9,637.5	-388.1	975.0	822.0	153.03	6.371		
19,500.0	10,575.0	20,558.7	11,550.0	95.8	95.9	179.99	-9,737.5	-387.4	975.0	820.5	154.51	6.310		
19,600.0	10,575.0	20,658.7	11,550.0	96.8	96.9	179.99	-9,837.5	-386.7	975.0	819.0	155.99	6.250		
19,700.0	10,575.0	20,758.7	11,550.0	97.7	97.8	179.99	-9,937.5	-386.1	975.0	817.5	157.47	6.192		
19,800.0	10,575.0	20,858.7	11,550.0	98.7	98.8	179.99	-10,037.5	-385.4	975.0	816.0	158.96	6.134		
19,900.0	10,575.0	20,958.7	11,550.0	99.6	99.8	179.99	-10,137.5	-384.7	975.0	814.6	160.44	6.077		
20,000.0	10,575.0	21,058.7	11,550.0	100.6	100.7	179.99	-10,237.5	-384.0	975.0	813.1	161.93	6.021		
20,100.0	10,575.0	21,158.7	11,550.0	101.6	101.7	179.99	-10,337.5	-383.4	975.0	811.6	163.41	5.966		
20,200.0	10,575.0	21,258.7	11,550.0	102.5	102.6	179.99	-10,437.5	-382.7	975.0	810.1	164.90	5.913		
20,300.0	10,575.0	21,358.7	11,550.0	103.5	103.6	179.99	-10,537.5	-382.0	975.0	808.6	166.39	5.860		
20,400.0	10,575.0	21,458.7	11,550.0	104.5	104.6	179.99	-10,637.5	-381.4	975.0	807.1	167.88	5.808		
20,500.0	10,575.0	21,558.7	11,550.0	105.4	105.5	179.99	-10,737.5	-380.7	975.0	805.6	169.38	5.756		
20,600.0	10,575.0	21,658.7	11,550.0	106.4	106.5	179.99	-10,837.5	-380.0	975.0	804.1	170.87	5.706		
20,700.0	10,575.0	21,758.7	11,550.0	107.3	107.4	179.99	-10,937.5	-379.3	975.0	802.6	172.36	5.657		
20,800.0	10,575.0	21,858.7	11,550.0	108.3	108.4	179.99	-11,037.5	-378.7	975.0	801.1	173.86	5.608		
20,900.0	10,575.0	21,958.7	11,550.0	109.3	109.4	179.99	-11,137.5	-378.0	975.0	799.6	175.35	5.560		
21,000.0	10,575.0	22,058.7	11,550.0	110.2	110.3	179.99	-11,237.5	-377.3	975.0	798.2	176.85	5.513		
21,100.0	10,575.0	22,158.7	11,550.0	111.2	111.3	179.99	-11,337.5	-376.7	975.0	796.7	178.35	5.467		
21,200.0	10,575.0	22,258.7	11,550.0	112.2	112.2	179.99	-11,437.5	-376.0	975.0	795.2	179.84	5.421		
21,300.0	10,575.0	22,358.7	11,550.0	113.1	113.2	179.99	-11,537.5	-375.3	975.0	793.7	181.34	5.377		
21,400.0	10,575.0	22,458.7	11,550.0	114.1	114.2	179.99	-11,637.5	-374.6	975.0	792.2	182.84	5.332		
21,500.0	10,575.0	22,558.7	11,550.0	115.0	115.1	179.99	-11,737.5	-374.0	975.0	790.7	184.34	5.289		
21,600.0	10,575.0	22,658.7	11,550.0	116.0	116.1	179.99	-11,837.5	-373.3	975.0	789.2	185.85	5.246		
21,700.0	10,575.0	22,758.7	11,550.0	117.0	117.1	179.99	-11,937.5	-372.6	975.0	787.7	187.35	5.204		
21,800.0	10,575.0	22,858.7	11,550.0	117.9	118.0	179.99	-12,037.5	-372.0	975.0	786.1	188.85	5.163		
21,900.0	10,575.0	22,958.7	11,550.0	118.9	119.0	179.99	-12,137.5	-371.3	975.0	784.6	190.36	5.122		
22,000.0	10,575.0	23,058.7	11,550.0	119.9	120.0	179.99	-12,237.5	-370.6	975.0	783.1	191.86	5.082		
22,100.0	10,575.0	23,158.7	11,550.0	120.8	120.9	179.99	-12,337.5	-369.9	975.0	781.6	193.37	5.042		
22,200.0	10,575.0	23,258.7	11,550.0	121.8	121.9	179.99	-12,437.5	-369.3	975.0	780.1	194.87	5.003		
22,300.0	10,575.0	23,358.7	11,550.0	122.8	122.9	179.99	-12,537.5	-368.6	975.0	778.6	196.38	4.965		
22,400.0	10,575.0	23,458.7	11,550.0	123.7	123.8	179.99	-12,637.5	-367.9	975.0	777.1	197.89	4.927		
22,500.0	10,575.0	23,558.7	11,550.0	124.7	124.8	179.99	-12,737.5	-367.3	975.0	775.6	199.39	4.890		
22,600.0	10,575.0	23,658.7	11,550.0	125.7	125.7	179.99	-12,837.5	-366.6	975.0	774.1	200.90	4.853		
22,700.0	10,575.0	23,758.7	11,550.0	126.6	126.7	179.99	-12,937.4	-365.9	975.0	772.6	202.41	4.817		
22,800.0	10,575.0	23,858.7	11,550.0	127.6	127.7	179.99	-13,037.4	-365.2	975.0	771.1	203.92	4.781		
22,900.0	10,575.0	23,958.7	11,550.0	128.6	128.6	179.99	-13,137.4	-364.6	975.0	769.6	205.43	4.746		
23,000.0	10,575.0	24,058.7	11,550.0	129.5	129.6	179.99	-13,237.4	-363.9	975.0	768.1	206.94	4.711		
23,100.0	10,575.0	24,158.7	11,550.0	130.5	130.6	179.99	-13,337.4	-363.2	975.0	766.5	208.45	4.677		
23,200.0	10,575.0	24,258.7	11,550.0	131.5	131.5	179.99	-13,437.4	-362.6	975.0	765.0	209.96	4.644		
23,300.0	10,575.0	24,358.7	11,550.0	132.4	132.5	179.99	-13,537.4	-361.9	975.0	763.5	211.48	4.610		
23,400.0	10,575.0	24,458.7	11,550.0	133.4	133.5	179.99	-13,637.4	-361.2	975.0	762.0	212.99	4.578		
23,500.0	10,575.0	24,558.7	11,550.0	134.4	134.4	180.00	-13,737.4	-360.5	975.0	760.5	214.50	4.545		
23,600.0	10,575.0	24,658.7	11,550.0	135.3	135.4	180.00	-13,837.4	-359.9	975.0	759.0	216.02	4.514		
23,700.0	10,575.0	24,758.7	11,550.0	136.3	136.4	180.00	-13,937.4	-359.2	975.0	757.5	217.53	4.482		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 703H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Rule Assigned:		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
23,800.0	10,575.0	24,858.7	11,550.0	137.3	137.3	180.00	-14,037.4	-358.5	975.0	756.0	219.05	4.451	
23,900.0	10,575.0	24,958.7	11,550.0	138.2	138.3	180.00	-14,137.4	-357.9	975.0	754.4	220.56	4.421	
24,000.0	10,575.0	25,058.7	11,550.0	139.2	139.3	180.00	-14,237.4	-357.2	975.0	752.9	222.08	4.390	
24,100.0	10,575.0	25,158.7	11,550.0	140.2	140.2	180.00	-14,337.4	-356.5	975.0	751.4	223.59	4.361	
24,200.0	10,575.0	25,258.7	11,550.0	141.1	141.2	180.00	-14,437.4	-355.9	975.0	749.9	225.11	4.331	
24,300.0	10,575.0	25,358.7	11,550.0	142.1	142.2	180.00	-14,537.4	-355.2	975.0	748.4	226.63	4.302	
24,400.0	10,575.0	25,458.7	11,550.0	143.1	143.1	180.00	-14,637.4	-354.5	975.0	746.9	228.15	4.274	
24,500.0	10,575.0	25,558.7	11,550.0	144.0	144.1	180.00	-14,737.4	-353.8	975.0	745.3	229.66	4.245	
24,600.0	10,575.0	25,658.7	11,550.0	145.0	145.1	180.00	-14,837.4	-353.2	975.0	743.8	231.18	4.217	
24,700.0	10,575.0	25,758.7	11,550.0	146.0	146.1	180.00	-14,937.4	-352.5	975.0	742.3	232.70	4.190	
24,800.0	10,575.0	25,858.7	11,550.0	147.0	147.0	180.00	-15,037.4	-351.8	975.0	740.8	234.22	4.163	
24,900.0	10,575.0	25,958.7	11,550.0	147.9	148.0	180.00	-15,137.4	-351.2	975.0	739.3	235.74	4.136	
25,000.0	10,575.0	26,058.7	11,550.0	148.9	149.0	180.00	-15,237.4	-350.5	975.0	737.7	237.26	4.109	
25,100.0	10,575.0	26,158.7	11,550.0	149.9	149.9	180.00	-15,337.4	-349.8	975.0	736.2	238.78	4.083	
25,200.0	10,575.0	26,258.7	11,550.0	150.8	150.9	180.00	-15,437.4	-349.1	975.0	734.7	240.30	4.057	
25,300.0	10,575.0	26,358.7	11,550.0	151.8	151.9	180.00	-15,537.4	-348.5	975.0	733.2	241.82	4.032	
25,400.0	10,575.0	26,458.7	11,550.0	152.8	152.8	180.00	-15,637.4	-347.8	975.0	731.7	243.34	4.007	
25,500.0	10,575.0	26,558.7	11,550.0	153.7	153.8	180.00	-15,737.4	-347.1	975.0	730.1	244.86	3.982	
25,600.0	10,575.0	26,658.7	11,550.0	154.7	154.8	180.00	-15,837.4	-346.5	975.0	728.6	246.39	3.957	
25,700.0	10,575.0	26,758.7	11,550.0	155.7	155.7	180.00	-15,937.4	-345.8	975.0	727.1	247.91	3.933	
25,800.0	10,575.0	26,858.7	11,550.0	156.6	156.7	180.00	-16,037.4	-345.1	975.0	725.6	249.43	3.909	
25,900.0	10,575.0	26,958.7	11,550.0	157.6	157.7	180.00	-16,137.4	-344.4	975.0	724.0	250.95	3.885	
26,000.0	10,575.0	27,058.7	11,550.0	158.6	158.6	180.00	-16,237.4	-343.8	975.0	722.5	252.48	3.862	
26,040.2	10,575.0	27,098.9	11,550.0	159.0	159.0	180.00	-16,277.6	-343.5	975.0	721.9	253.09	3.852	

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program: 0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Rule Assigned:		Distance		No-Go		Separation		Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Distance (usft)	Factor	
0.0	0.0	0.0	0.0	3.0	3.0	89.31	0.7	60.1	60.1	53.7	6.43	9.347	
100.0	100.0	100.0	100.0	3.2	3.2	89.31	0.7	60.1	60.1	53.2	6.89	8.718	
200.0	200.0	200.0	200.0	3.5	3.5	89.31	0.7	60.1	60.1	52.8	7.33	8.200	
300.0	300.0	300.0	300.0	3.7	3.7	89.31	0.7	60.1	60.1	52.3	7.74	7.762	
400.0	400.0	400.0	400.0	3.9	3.9	89.31	0.7	60.1	60.1	52.0	8.14	7.386	
500.0	500.0	500.0	500.0	4.1	4.1	89.31	0.7	60.1	60.1	51.6	8.51	7.058	
600.0	600.0	600.0	600.0	4.2	4.2	89.31	0.7	60.1	60.1	51.2	8.88	6.769	
700.0	700.0	700.0	700.0	4.4	4.4	89.31	0.7	60.1	60.1	50.9	9.23	6.511	
800.0	800.0	800.0	800.0	4.6	4.6	89.31	0.7	60.1	60.1	50.5	9.57	6.279	
900.0	900.0	900.0	900.0	4.8	4.8	89.31	0.7	60.1	60.1	50.2	9.90	6.068	
1,000.0	1,000.0	1,000.0	1,000.0	4.9	4.9	89.31	0.7	60.1	60.1	49.9	10.22	5.877	
1,100.0	1,100.0	1,100.0	1,100.0	5.1	5.1	89.31	0.7	60.1	60.1	49.5	10.54	5.701	
1,200.0	1,200.0	1,200.0	1,200.0	5.2	5.2	89.31	0.7	60.1	60.1	49.2	10.85	5.539	
1,300.0	1,300.0	1,300.0	1,300.0	5.4	5.4	89.31	0.7	60.1	60.1	48.9	11.15	5.390	
1,400.0	1,400.0	1,400.0	1,400.0	5.5	5.5	89.31	0.7	60.1	60.1	48.6	11.44	5.250	
1,500.0	1,500.0	1,500.0	1,500.0	5.7	5.7	89.31	0.7	60.1	60.1	48.4	11.73	5.121 CC, ES, SF	
1,600.0	1,600.0	1,598.2	1,598.2	5.9	5.9	-126.34	-0.2	61.5	62.5	50.5	12.07	5.181	
1,700.0	1,699.8	1,696.1	1,695.9	6.1	6.1	-127.29	-2.9	65.7	69.9	57.5	12.38	5.645	
1,800.0	1,799.5	1,793.2	1,792.7	6.3	6.3	-128.47	-7.5	72.6	82.2	69.5	12.70	6.468	
1,900.0	1,898.7	1,889.3	1,888.1	6.6	6.6	-129.59	-13.7	82.2	99.3	86.2	13.03	7.617	
2,000.0	1,997.5	1,984.0	1,981.7	6.9	6.8	-130.51	-21.6	94.2	121.2	107.8	13.38	9.056	
2,021.2	2,018.4	2,003.9	2,001.3	6.9	6.9	-130.67	-23.5	97.1	126.5	113.0	13.44	9.411	
2,100.0	2,095.8	2,077.2	2,073.3	7.0	7.1	-131.20	-31.0	108.6	147.2	133.5	13.69	10.748	
2,200.0	2,194.2	2,169.2	2,163.1	7.3	7.3	-131.10	-41.8	125.2	175.5	161.5	14.00	12.536	
2,300.0	2,292.5	2,264.3	2,255.6	7.5	7.6	-130.69	-54.0	143.8	205.3	190.9	14.38	14.281	
2,400.0	2,390.9	2,359.7	2,348.4	7.8	7.9	-130.38	-66.2	162.5	235.1	220.3	14.79	15.889	
2,500.0	2,489.2	2,455.2	2,441.2	8.1	8.1	-130.15	-78.4	181.2	264.8	249.6	15.23	17.386	
2,600.0	2,587.6	2,550.7	2,534.0	8.4	8.4	-129.96	-90.6	199.9	294.6	278.9	15.69	18.773	
2,700.0	2,685.9	2,646.1	2,626.8	8.8	8.8	-129.80	-102.9	218.6	324.4	308.2	16.17	20.056	
2,800.0	2,784.3	2,741.6	2,719.6	9.1	9.1	-129.67	-115.1	237.3	354.1	337.5	16.67	21.241	
2,900.0	2,882.6	2,837.0	2,812.4	9.4	9.4	-129.56	-127.3	256.0	383.9	366.7	17.19	22.337	
3,000.0	2,981.0	2,932.5	2,905.2	9.8	9.8	-129.47	-139.5	274.7	413.7	396.0	17.72	23.349	
3,100.0	3,079.3	3,028.0	2,998.1	10.2	10.1	-129.39	-151.7	293.4	443.5	425.2	18.26	24.283	
3,200.0	3,177.7	3,123.4	3,090.9	10.5	10.5	-129.32	-163.9	312.1	473.2	454.4	18.82	25.147	
3,300.0	3,276.0	3,218.9	3,183.7	10.9	10.9	-129.26	-176.2	330.8	503.0	483.6	19.39	25.946	
3,400.0	3,374.4	3,314.4	3,276.5	11.3	11.3	-129.20	-188.4	349.5	532.8	512.8	19.97	26.686	
3,500.0	3,472.7	3,409.8	3,369.3	11.7	11.7	-129.15	-200.6	368.2	562.6	542.0	20.55	27.371	
3,600.0	3,571.1	3,505.3	3,462.1	12.1	12.1	-129.11	-212.8	386.9	592.4	571.2	21.15	28.006	
3,700.0	3,669.4	3,600.7	3,554.9	12.5	12.5	-129.07	-225.0	405.6	622.1	600.4	21.76	28.596	
3,800.0	3,767.8	3,696.2	3,647.7	12.9	12.9	-129.03	-237.2	424.4	651.9	629.5	22.37	29.145	
3,900.0	3,866.1	3,791.7	3,740.6	13.3	13.3	-129.00	-249.5	443.1	681.7	658.7	22.99	29.655	
4,000.0	3,964.5	3,887.1	3,833.4	13.7	13.7	-128.97	-261.7	461.8	711.5	687.9	23.61	30.131	
4,100.0	4,062.8	3,982.6	3,926.2	14.1	14.1	-128.94	-273.9	480.5	741.3	717.0	24.24	30.575	
4,200.0	4,161.2	4,078.1	4,019.0	14.5	14.5	-128.91	-286.1	499.2	771.0	746.2	24.88	30.990	
4,300.0	4,259.5	4,173.5	4,111.8	15.0	14.9	-128.89	-298.3	517.9	800.8	775.3	25.52	31.379	
4,400.0	4,357.9	4,269.0	4,204.6	15.4	15.4	-128.87	-310.5	536.6	830.6	804.4	26.17	31.743	
4,500.0	4,456.2	4,364.4	4,297.4	15.8	15.8	-128.85	-322.7	555.3	860.4	833.6	26.82	32.084	
4,600.0	4,554.6	4,459.9	4,390.2	16.2	16.2	-128.83	-335.0	574.0	890.2	862.7	27.47	32.404	
4,700.0	4,652.9	4,555.4	4,483.1	16.7	16.6	-128.81	-347.2	592.7	919.9	891.8	28.13	32.706	
4,800.0	4,751.3	4,650.8	4,575.9	17.1	17.1	-128.79	-359.4	611.4	949.7	920.9	28.79	32.989	
4,900.0	4,849.6	4,746.3	4,668.7	17.5	17.5	-128.78	-371.6	630.1	979.5	950.1	29.45	33.257	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design:	TARHEEL_DONKEY POTROAST PROJECT - _DONKEY POTROAST FED COM 704H - OWB - PWP0												Offset Site Error:	0.0 usft
Survey Program:	0-r.5 MWD+IFR1												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre				Rule Assigned:				Offset Well Error:		
Measured Vertical	Measured Vertical	Reference	Offset	Highside			Distance							
Depth Depth	Depth Depth	Reference	Offset	Toolface			Between	Between	No-Go	Separation				
(usft) (usft)	(usft) (usft)	(usft)	(usft)	(°)			Centres	Ellipses	Distance	Factor				
							(usft)	(usft)	(usft)					
							+N/-S	+E/-W						
							(usft)	(usft)						

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - OUTLAW 22 FEDERAL COM #1H - OWB - AWP													Offset Site Error:	0.0 usft
Survey Program: 100-r.5 GYRO-NS													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Distance		Rule Assigned:		Warning				
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor		
3,700.0	3,669.4	3,680.1	3,678.8	12.5	13.5	-4.90	-1,147.9	-709.8	1,000.0	973.8	26.10	38.308		
3,800.0	3,767.8	3,773.1	3,771.7	12.9	13.8	-5.04	-1,146.0	-707.7	979.1	952.3	26.81	36.514		
3,900.0	3,866.1	3,866.7	3,865.3	13.3	14.2	-5.20	-1,144.6	-705.6	958.7	931.1	27.53	34.822		
4,000.0	3,964.5	3,960.8	3,959.4	13.7	14.5	-5.36	-1,143.4	-703.8	938.7	910.4	28.25	33.225		
4,100.0	4,062.8	4,061.1	4,059.6	14.1	14.8	-5.52	-1,142.3	-702.1	918.9	889.9	28.99	31.701		
4,200.0	4,161.2	4,165.5	4,164.0	14.5	15.2	-5.69	-1,140.6	-700.1	898.5	868.8	29.73	30.225		
4,300.0	4,259.5	4,260.5	4,259.0	15.0	15.5	-5.85	-1,138.5	-698.3	877.8	847.3	30.46	28.817		
4,400.0	4,357.9	4,351.1	4,349.6	15.4	15.8	-5.99	-1,137.2	-697.1	857.8	826.6	31.19	27.499		
4,500.0	4,456.2	4,444.9	4,443.3	15.8	16.1	-6.13	-1,136.3	-696.3	838.6	806.7	31.93	26.260		
4,600.0	4,554.6	4,541.9	4,540.4	16.2	16.5	-6.26	-1,135.4	-695.8	819.6	786.9	32.68	25.080		
4,700.0	4,652.9	4,640.2	4,638.7	16.7	16.8	-6.39	-1,134.5	-695.5	800.7	767.3	33.43	23.953		
4,800.0	4,751.3	4,740.1	4,738.6	17.1	17.2	-6.54	-1,133.6	-694.9	781.6	747.5	34.18	22.869		
4,900.0	4,849.6	4,837.7	4,836.1	17.5	17.5	-6.74	-1,132.8	-693.9	762.5	727.6	34.93	21.829		
5,000.0	4,948.0	4,933.0	4,931.4	17.9	17.8	-6.93	-1,132.2	-693.1	743.6	707.9	35.68	20.840		
5,100.0	5,046.3	5,029.1	5,027.6	18.4	18.1	-7.12	-1,131.9	-692.7	725.1	688.7	36.44	19.900		
5,200.0	5,144.7	5,126.9	5,125.3	18.8	18.5	-7.32	-1,131.7	-692.2	706.7	669.5	37.19	19.002		
5,300.0	5,243.0	5,225.1	5,223.5	19.3	18.8	-7.55	-1,131.6	-691.7	688.5	650.5	37.95	18.143		
5,400.0	5,341.4	5,325.3	5,323.7	19.7	19.2	-7.79	-1,131.3	-691.1	670.0	631.3	38.70	17.312		
5,500.0	5,439.7	5,422.5	5,420.9	20.1	19.5	-8.01	-1,130.7	-690.7	651.4	611.9	39.46	16.507		
5,524.0	5,463.3	5,443.9	5,442.4	20.2	19.6	-8.06	-1,130.7	-690.6	647.0	607.4	39.64	16.323		
5,600.0	5,538.1	5,514.4	5,512.8	20.6	19.8	-8.22	-1,130.9	-690.6	634.1	593.9	40.21	15.771		
5,700.0	5,636.9	5,618.7	5,617.1	21.0	20.2	-8.39	-1,130.8	-690.8	618.3	577.4	40.95	15.099		
5,800.0	5,735.9	5,717.1	5,715.6	21.4	20.5	-8.52	-1,130.3	-691.1	604.0	562.3	41.69	14.486		
5,900.0	5,835.1	5,815.9	5,814.3	21.8	20.9	-8.65	-1,130.0	-691.3	591.4	549.0	42.43	13.939		
6,000.0	5,934.5	5,915.2	5,913.6	22.2	21.2	-8.74	-1,129.6	-691.6	580.6	537.4	43.15	13.456		
6,100.0	6,034.1	6,014.0	6,012.4	22.6	21.5	-8.80	-1,129.1	-692.2	571.5	527.7	43.86	13.032		
6,200.0	6,133.8	6,112.2	6,110.6	22.9	21.9	-8.80	-1,128.8	-693.1	564.4	519.9	44.55	12.669		
6,300.0	6,233.7	6,210.2	6,208.6	23.3	22.2	-8.76	-1,128.6	-694.3	559.4	514.2	45.23	12.368		
6,400.0	6,333.6	6,311.2	6,309.6	23.6	22.6	-8.68	-1,128.5	-695.6	556.1	510.2	45.87	12.123		
6,500.0	6,433.6	6,412.0	6,410.4	23.9	22.9	-8.58	-1,128.2	-696.9	554.4	507.9	46.48	11.927		
6,552.6	6,486.2	6,464.5	6,462.9	23.9	23.1	-8.52	-1,128.0	-697.5	554.1	507.4	46.72	11.860		
6,566.4	6,500.0	6,478.3	6,476.6	24.0	23.1	-153.22	-1,127.9	-697.6	554.2	507.4	46.79	11.844		
6,600.0	6,533.6	6,511.8	6,510.1	24.0	23.3	-153.18	-1,127.8	-698.0	554.2	507.3	46.90	11.817		
6,700.0	6,633.6	6,611.5	6,609.9	24.0	23.6	-153.06	-1,127.6	-699.2	554.5	507.2	47.27	11.731		
6,800.0	6,733.6	6,710.9	6,709.2	24.0	23.9	-152.96	-1,127.4	-700.2	554.9	507.2	47.64	11.647		
6,900.0	6,833.6	6,811.0	6,809.3	24.0	24.3	-152.89	-1,127.5	-701.0	555.3	507.3	48.01	11.566		
7,000.0	6,933.6	6,912.2	6,910.5	24.0	24.6	-152.84	-1,127.5	-701.7	555.6	507.2	48.38	11.484		
7,100.0	7,033.6	7,013.0	7,011.4	24.1	25.0	-152.79	-1,127.4	-702.1	555.7	507.0	48.75	11.398		
7,200.0	7,133.6	7,113.4	7,111.8	24.1	25.3	-152.75	-1,127.2	-702.5	555.7	506.6	49.13	11.311		
7,300.0	7,233.6	7,214.1	7,212.4	24.1	25.7	-152.68	-1,126.8	-703.0	555.6	506.1	49.51	11.223		
7,400.0	7,333.6	7,314.9	7,313.3	24.2	26.0	-152.60	-1,126.3	-703.6	555.4	505.5	49.89	11.132		
7,500.0	7,433.6	7,415.5	7,413.8	24.2	26.4	-152.52	-1,125.6	-704.1	555.0	504.7	50.27	11.040		
7,600.0	7,533.6	7,514.3	7,512.6	24.2	26.7	-152.44	-1,125.0	-704.7	554.7	504.1	50.66	10.949		
7,700.0	7,633.6	7,613.5	7,611.8	24.2	27.1	-152.37	-1,124.6	-705.2	554.6	503.6	51.05	10.864		
7,800.0	7,733.6	7,713.7	7,712.1	24.3	27.4	-152.31	-1,124.2	-705.7	554.5	503.1	51.44	10.780		
7,900.0	7,833.6	7,813.9	7,812.2	24.3	27.8	-152.25	-1,123.8	-706.2	554.4	502.6	51.83	10.696		
8,000.0	7,933.6	7,913.7	7,912.0	24.3	28.1	-152.19	-1,123.5	-706.6	554.3	502.1	52.23	10.614		
8,100.0	8,033.6	8,013.4	8,011.8	24.3	28.5	-152.14	-1,123.2	-707.0	554.3	501.7	52.62	10.533		
8,146.2	8,079.8	8,059.4	8,057.8	24.4	28.6	-152.12	-1,123.1	-707.2	554.3	501.5	52.81	10.497		
8,200.0	8,133.6	8,113.0	8,111.3	24.4	28.8	-152.10	-1,123.0	-707.4	554.3	501.3	53.02	10.454		
8,300.0	8,233.6	8,212.3	8,210.6	24.4	29.1	-152.04	-1,122.9	-707.9	554.4	501.0	53.42	10.378		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - OUTLAW 22 FEDERAL COM #1H - OWB - AWP												Offset Site Error:	0.0 usft
Survey Program: 100-r.5 GYRO-NS												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
8,400.0	8,333.6	8,310.8	8,309.2	24.4	29.5	-152.01	-1,123.0	-708.3	554.7	500.9	53.82	10.307	
8,500.0	8,433.6	8,411.8	8,410.1	24.5	29.8	-152.02	-1,123.4	-708.4	555.0	500.8	54.22	10.238	
8,600.0	8,533.6	8,511.3	8,509.6	24.5	30.2	-152.04	-1,123.7	-708.4	555.4	500.7	54.62	10.168	
8,700.0	8,633.6	8,611.0	8,609.3	24.5	30.5	-152.03	-1,124.0	-708.7	555.7	500.7	55.02	10.100	
8,800.0	8,733.6	8,706.9	8,705.2	24.5	30.9	-152.05	-1,124.7	-708.8	556.5	501.1	55.42	10.041	
8,900.0	8,833.6	8,809.9	8,808.2	24.6	31.2	-152.20	-1,126.2	-708.0	557.4	501.6	55.82	9.985	
9,000.0	8,933.6	8,916.9	8,915.2	24.6	31.6	-152.43	-1,127.3	-706.0	557.4	501.1	56.22	9.913	
9,100.0	9,033.6	9,022.4	9,020.6	24.6	32.0	-152.64	-1,127.2	-703.6	556.2	499.6	56.62	9.823	
9,200.0	9,133.6	9,128.5	9,126.7	24.7	32.3	-152.79	-1,125.7	-701.3	554.0	497.0	57.02	9.715	
9,300.0	9,233.6	9,232.1	9,230.3	24.7	32.7	-152.79	-1,122.9	-699.8	550.9	493.5	57.43	9.593	
9,400.0	9,333.6	9,334.9	9,332.9	24.7	33.0	-152.71	-1,119.2	-698.7	547.3	489.4	57.84	9.461	
9,500.0	9,433.6	9,434.5	9,432.5	24.7	33.4	-152.57	-1,115.0	-698.0	543.2	485.0	58.27	9.323	
9,600.0	9,533.6	9,529.3	9,527.3	24.8	33.7	-152.46	-1,111.7	-697.5	539.8	481.1	58.70	9.197	
9,700.0	9,633.6	9,625.4	9,623.3	24.8	34.1	-152.37	-1,109.2	-697.1	537.4	478.2	59.13	9.088	
9,800.0	9,733.6	9,724.3	9,722.2	24.8	34.4	-152.38	-1,107.4	-696.1	535.2	475.7	59.55	8.988	
9,900.0	9,833.6	9,821.4	9,819.3	24.9	34.7	-152.49	-1,106.3	-694.5	533.5	473.6	59.97	8.897	
10,000.0	9,933.6	9,919.6	9,917.4	24.9	35.1	-152.63	-1,105.8	-692.7	532.3	471.9	60.39	8.814	
10,068.4	10,002.0	9,986.7	9,984.6	24.9	35.3	-152.73	-1,105.7	-691.6	531.6	470.9	60.67	8.762	
10,100.0	10,033.6	10,017.2	10,015.0	25.0	35.4	27.69	-1,105.7	-691.1	530.6	469.8	60.83	8.722	
10,150.0	10,083.3	10,064.7	10,062.5	25.1	35.6	28.07	-1,105.8	-690.4	526.0	464.8	61.18	8.598	
10,200.0	10,132.4	10,111.8	10,109.6	25.3	35.7	28.86	-1,106.1	-689.8	517.8	456.3	61.55	8.413	
10,250.0	10,180.5	10,158.5	10,156.3	25.5	35.9	30.09	-1,106.5	-689.3	506.1	444.2	61.93	8.172	
10,300.0	10,227.3	10,204.2	10,202.0	25.8	36.1	31.85	-1,107.0	-689.0	491.0	428.7	62.32	7.879	
10,350.0	10,272.4	10,249.8	10,247.6	26.0	36.2	34.24	-1,107.5	-688.7	472.6	409.9	62.70	7.539	
10,400.0	10,315.4	10,293.5	10,291.3	26.2	36.4	37.33	-1,108.0	-688.3	451.2	388.2	63.05	7.156	
10,450.0	10,356.0	10,335.2	10,333.0	26.4	36.5	41.27	-1,108.5	-687.8	427.1	363.7	63.38	6.739	
10,500.0	10,393.9	10,374.2	10,372.0	26.6	36.7	46.16	-1,109.0	-687.2	400.8	337.1	63.65	6.297	
10,550.0	10,428.8	10,410.0	10,407.8	26.8	36.8	52.04	-1,109.4	-686.6	372.9	309.0	63.84	5.841	
10,600.0	10,460.5	10,441.9	10,439.7	27.0	36.9	58.78	-1,109.7	-686.1	344.2	280.3	63.91	5.386	
10,650.0	10,488.7	10,470.4	10,468.1	27.2	37.0	66.11	-1,110.0	-685.7	316.0	252.2	63.80	4.953	
10,700.0	10,513.2	10,495.1	10,492.9	27.3	37.1	73.49	-1,110.2	-685.4	289.6	226.1	63.44	4.564	
10,750.0	10,533.8	10,516.0	10,513.8	27.5	37.2	80.25	-1,110.4	-685.1	266.7	204.0	62.74	4.252	
10,800.0	10,550.4	10,532.9	10,530.6	27.6	37.2	85.76	-1,110.6	-684.9	249.7	188.1	61.67	4.049	
10,850.0	10,562.8	10,545.6	10,543.3	27.7	37.3	89.59	-1,110.7	-684.7	240.8	180.4	60.38	3.989 SF	
10,871.4	10,566.8	10,549.7	10,547.5	27.7	37.3	90.66	-1,110.7	-684.7	239.9	180.1	59.82	4.010 CC, ES	
10,900.0	10,570.9	10,554.0	10,551.8	27.7	37.3	91.51	-1,110.7	-684.6	241.6	182.4	59.17	4.083	
10,950.0	10,574.7	10,558.2	10,555.9	27.8	37.3	91.38	-1,110.8	-684.6	252.3	194.0	58.38	4.322	
10,968.4	10,575.0	10,558.6	10,556.4	27.8	37.3	90.82	-1,110.8	-684.6	258.7	200.4	58.23	4.442	
11,000.0	10,575.0	10,558.9	10,556.6	27.8	37.3	90.88	-1,110.8	-684.6	272.1	213.9	58.13	4.681	
11,100.0	10,575.0	10,559.7	10,557.4	27.9	37.3	91.07	-1,110.8	-684.6	331.3	272.6	58.65	5.648	
11,200.0	10,575.0	10,560.5	10,558.2	28.0	37.3	91.26	-1,110.8	-684.6	406.7	347.2	59.54	6.831	
11,300.0	10,575.0	10,561.3	10,559.1	28.1	37.3	91.46	-1,110.8	-684.6	491.1	430.7	60.32	8.141	
11,400.0	10,575.0	10,562.1	10,559.9	28.2	37.3	91.65	-1,110.8	-684.5	580.4	519.5	60.92	9.526	
11,500.0	10,575.0	10,562.9	10,560.7	28.4	37.3	91.84	-1,110.8	-684.5	672.7	611.3	61.39	10.958	
11,600.0	10,575.0	10,563.7	10,561.4	28.6	37.3	92.03	-1,110.8	-684.5	767.0	705.2	61.75	12.420	
11,700.0	10,575.0	10,564.5	10,562.2	28.8	37.3	92.22	-1,110.8	-684.5	862.5	800.5	62.05	13.901	
11,800.0	10,575.0	10,565.3	10,563.0	29.1	37.3	92.41	-1,110.8	-684.5	959.0	896.7	62.28	15.397	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - OUTLAW 22 FEDERAL COM #1H - ST01 - ST01 AWP													Offset Site Error: 0.0 usft	
Survey Program: 100-r.5 GYRO-NS, 10661-r.5 MWD									Rule Assigned:				Offset Well Error: 3.0 usft	
Reference		Offset		Semi Major Axis		Offset Wellbore Centre			Distance					
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	No-Go Distance (usft)	Separation Factor	Warning	
3,700.0	3,669.4	3,680.1	3,678.8	12.5	13.5	-4.90	-1,147.9	-709.8	1,000.0	973.8	26.10	38.308		
3,800.0	3,767.8	3,773.1	3,771.7	12.9	13.8	-5.04	-1,146.0	-707.7	979.1	952.3	26.81	36.514		
3,900.0	3,866.1	3,866.7	3,865.3	13.3	14.2	-5.20	-1,144.6	-705.6	958.7	931.1	27.53	34.822		
4,000.0	3,964.5	3,960.8	3,959.4	13.7	14.5	-5.36	-1,143.4	-703.8	938.7	910.4	28.25	33.225		
4,100.0	4,062.8	4,061.1	4,059.6	14.1	14.8	-5.52	-1,142.3	-702.1	918.9	889.9	28.99	31.701		
4,200.0	4,161.2	4,165.5	4,164.0	14.5	15.2	-5.69	-1,140.6	-700.1	898.5	868.8	29.73	30.225		
4,300.0	4,259.5	4,260.5	4,259.0	15.0	15.5	-5.85	-1,138.5	-698.3	877.8	847.3	30.46	28.817		
4,400.0	4,357.9	4,351.1	4,349.6	15.4	15.8	-5.99	-1,137.2	-697.1	857.8	826.6	31.19	27.499		
4,500.0	4,456.2	4,444.9	4,443.3	15.8	16.1	-6.13	-1,136.3	-696.3	838.6	806.7	31.93	26.260		
4,600.0	4,554.6	4,541.9	4,540.4	16.2	16.5	-6.26	-1,135.4	-695.8	819.6	786.9	32.68	25.080		
4,700.0	4,652.9	4,640.2	4,638.7	16.7	16.8	-6.39	-1,134.5	-695.5	800.7	767.3	33.43	23.953		
4,800.0	4,751.3	4,740.1	4,738.6	17.1	17.2	-6.54	-1,133.6	-694.9	781.6	747.5	34.18	22.869		
4,900.0	4,849.6	4,837.7	4,836.1	17.5	17.5	-6.74	-1,132.8	-693.9	762.5	727.6	34.93	21.829		
5,000.0	4,948.0	4,933.0	4,931.4	17.9	17.8	-6.93	-1,132.2	-693.1	743.6	707.9	35.68	20.840		
5,100.0	5,046.3	5,029.1	5,027.6	18.4	18.1	-7.12	-1,131.9	-692.7	725.1	688.7	36.44	19.900		
5,200.0	5,144.7	5,126.9	5,125.3	18.8	18.5	-7.32	-1,131.7	-692.2	706.7	669.5	37.19	19.002		
5,300.0	5,243.0	5,225.1	5,223.5	19.3	18.8	-7.55	-1,131.6	-691.7	688.5	650.5	37.95	18.143		
5,400.0	5,341.4	5,325.3	5,323.7	19.7	19.2	-7.79	-1,131.3	-691.1	670.0	631.3	38.70	17.312		
5,500.0	5,439.7	5,422.5	5,420.9	20.1	19.5	-8.01	-1,130.7	-690.7	651.4	611.9	39.46	16.507		
5,524.0	5,463.3	5,443.9	5,442.4	20.2	19.6	-8.06	-1,130.7	-690.6	647.0	607.4	39.64	16.323		
5,600.0	5,538.1	5,514.4	5,512.8	20.6	19.8	-8.22	-1,130.9	-690.6	634.1	593.9	40.21	15.771		
5,700.0	5,636.9	5,618.7	5,617.1	21.0	20.2	-8.39	-1,130.8	-690.8	618.3	577.4	40.95	15.099		
5,800.0	5,735.9	5,717.1	5,715.6	21.4	20.5	-8.52	-1,130.3	-691.1	604.0	562.3	41.69	14.486		
5,900.0	5,835.1	5,815.9	5,814.3	21.8	20.9	-8.65	-1,130.0	-691.3	591.4	549.0	42.43	13.939		
6,000.0	5,934.5	5,915.2	5,913.6	22.2	21.2	-8.74	-1,129.6	-691.6	580.6	537.4	43.15	13.456		
6,100.0	6,034.1	6,014.0	6,012.4	22.6	21.5	-8.80	-1,129.1	-692.2	571.5	527.7	43.86	13.032		
6,200.0	6,133.8	6,112.2	6,110.6	22.9	21.9	-8.80	-1,128.8	-693.1	564.4	519.9	44.55	12.669		
6,300.0	6,233.7	6,210.2	6,208.6	23.3	22.2	-8.76	-1,128.6	-694.3	559.4	514.2	45.23	12.368		
6,400.0	6,333.6	6,311.2	6,309.6	23.6	22.6	-8.68	-1,128.5	-695.6	556.1	510.2	45.87	12.123		
6,500.0	6,433.6	6,412.0	6,410.4	23.9	22.9	-8.58	-1,128.2	-696.9	554.4	507.9	46.48	11.927		
6,552.6	6,486.2	6,464.5	6,462.9	23.9	23.1	-8.52	-1,128.0	-697.5	554.1	507.4	46.72	11.860		
6,566.4	6,500.0	6,478.3	6,476.6	24.0	23.1	-153.22	-1,127.9	-697.6	554.2	507.4	46.79	11.844		
6,600.0	6,533.6	6,511.8	6,510.1	24.0	23.3	-153.18	-1,127.8	-698.0	554.2	507.3	46.90	11.817		
6,700.0	6,633.6	6,611.5	6,609.9	24.0	23.6	-153.06	-1,127.6	-699.2	554.5	507.2	47.27	11.731		
6,800.0	6,733.6	6,710.9	6,709.2	24.0	23.9	-152.96	-1,127.4	-700.2	554.9	507.2	47.64	11.647		
6,900.0	6,833.6	6,811.0	6,809.3	24.0	24.3	-152.89	-1,127.5	-701.0	555.3	507.3	48.01	11.566		
7,000.0	6,933.6	6,912.2	6,910.5	24.0	24.6	-152.84	-1,127.5	-701.7	555.6	507.2	48.38	11.484		
7,100.0	7,033.6	7,013.0	7,011.4	24.1	25.0	-152.79	-1,127.4	-702.1	555.7	507.0	48.75	11.398		
7,200.0	7,133.6	7,113.4	7,111.8	24.1	25.3	-152.75	-1,127.2	-702.5	555.7	506.6	49.13	11.311		
7,300.0	7,233.6	7,214.1	7,212.4	24.1	25.7	-152.68	-1,126.8	-703.0	555.6	506.1	49.51	11.223		
7,400.0	7,333.6	7,314.9	7,313.3	24.2	26.0	-152.60	-1,126.3	-703.6	555.4	505.5	49.89	11.132		
7,500.0	7,433.6	7,415.5	7,413.8	24.2	26.4	-152.52	-1,125.6	-704.1	555.0	504.7	50.27	11.040		
7,600.0	7,533.6	7,514.3	7,512.6	24.2	26.7	-152.44	-1,125.0	-704.7	554.7	504.1	50.66	10.949		
7,700.0	7,633.6	7,613.5	7,611.8	24.2	27.1	-152.37	-1,124.6	-705.2	554.6	503.6	51.05	10.864		
7,800.0	7,733.6	7,713.7	7,712.1	24.3	27.4	-152.31	-1,124.2	-705.7	554.5	503.1	51.44	10.780		
7,900.0	7,833.6	7,813.9	7,812.2	24.3	27.8	-152.25	-1,123.8	-706.2	554.4	502.6	51.83	10.696		
8,000.0	7,933.6	7,913.7	7,912.0	24.3	28.1	-152.19	-1,123.5	-706.6	554.3	502.1	52.23	10.614		
8,100.0	8,033.6	8,013.4	8,011.8	24.3	28.5	-152.14	-1,123.2	-707.0	554.3	501.7	52.62	10.533		
8,146.2	8,079.8	8,059.4	8,057.8	24.4	28.6	-152.12	-1,123.1	-707.2	554.3	501.5	52.81	10.497		
8,200.0	8,133.6	8,113.0	8,111.3	24.4	28.8	-152.10	-1,123.0	-707.4	554.3	501.3	53.02	10.454		
8,300.0	8,233.6	8,212.3	8,210.6	24.4	29.1	-152.04	-1,122.9	-707.9	554.4	501.0	53.42	10.378		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - OUTLAW 22 FEDERAL COM #1H - ST01 - ST01 AWP												Offset Site Error:	0.0 usft
Survey Program: 100-r.5 GYRO-NS, 10661-r.5 MWD												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (")	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
8,400.0	8,333.6	8,310.8	8,309.2	24.4	29.5	-152.01	-1,123.0	-708.3	554.7	500.9	53.82	10.307	
8,500.0	8,433.6	8,411.8	8,410.1	24.5	29.8	-152.02	-1,123.4	-708.4	555.0	500.8	54.22	10.238	
8,600.0	8,533.6	8,511.3	8,509.6	24.5	30.2	-152.04	-1,123.7	-708.4	555.4	500.7	54.62	10.168	
8,700.0	8,633.6	8,611.0	8,609.3	24.5	30.5	-152.03	-1,124.0	-708.7	555.7	500.7	55.02	10.100	
8,800.0	8,733.6	8,706.9	8,705.2	24.5	30.9	-152.05	-1,124.7	-708.8	556.5	501.1	55.42	10.041	
8,900.0	8,833.6	8,809.9	8,808.2	24.6	31.2	-152.20	-1,126.2	-708.0	557.4	501.6	55.82	9.985	
9,000.0	8,933.6	8,916.9	8,915.2	24.6	31.6	-152.43	-1,127.3	-706.0	557.4	501.1	56.22	9.913	
9,100.0	9,033.6	9,022.4	9,020.6	24.6	32.0	-152.64	-1,127.2	-703.6	556.2	499.6	56.62	9.823	
9,200.0	9,133.6	9,128.5	9,126.7	24.7	32.3	-152.79	-1,125.7	-701.3	554.0	497.0	57.02	9.715	
9,300.0	9,233.6	9,232.1	9,230.3	24.7	32.7	-152.79	-1,122.9	-699.8	550.9	493.5	57.43	9.593	
9,400.0	9,333.6	9,334.9	9,332.9	24.7	33.0	-152.71	-1,119.2	-698.7	547.3	489.4	57.84	9.461	
9,500.0	9,433.6	9,434.5	9,432.5	24.7	33.4	-152.57	-1,115.0	-698.0	543.2	485.0	58.27	9.323	
9,600.0	9,533.6	9,529.3	9,527.3	24.8	33.7	-152.46	-1,111.7	-697.5	539.8	481.1	58.70	9.197	
9,700.0	9,633.6	9,625.4	9,623.3	24.8	34.1	-152.37	-1,109.2	-697.1	537.4	478.2	59.13	9.088	
9,800.0	9,733.6	9,724.3	9,722.2	24.8	34.4	-152.38	-1,107.4	-696.1	535.2	475.7	59.55	8.988	
9,900.0	9,833.6	9,821.4	9,819.3	24.9	34.7	-152.49	-1,106.3	-694.5	533.5	473.6	59.97	8.897	
10,000.0	9,933.6	9,919.6	9,917.4	24.9	35.1	-152.63	-1,105.8	-692.7	532.3	471.9	60.39	8.814	
10,068.4	10,002.0	9,986.7	9,984.6	24.9	35.3	-152.73	-1,105.7	-691.6	531.6	470.9	60.67	8.762	
10,100.0	10,033.6	10,017.2	10,015.0	25.0	35.4	27.69	-1,105.7	-691.1	530.6	469.8	60.83	8.722	
10,150.0	10,083.3	10,064.7	10,062.5	25.1	35.6	28.07	-1,105.8	-690.4	526.0	464.8	61.18	8.598	
10,200.0	10,132.4	10,111.8	10,109.6	25.3	35.7	28.86	-1,106.1	-689.8	517.8	456.3	61.55	8.413	
10,250.0	10,180.5	10,158.5	10,156.3	25.5	35.9	30.09	-1,106.5	-689.3	506.1	444.2	61.93	8.172	
10,300.0	10,227.3	10,204.2	10,202.0	25.8	36.1	31.85	-1,107.0	-689.0	491.0	428.7	62.32	7.879	
10,350.0	10,272.4	10,249.8	10,247.6	26.0	36.2	34.24	-1,107.5	-688.7	472.6	409.9	62.70	7.539	
10,400.0	10,315.4	10,293.5	10,291.3	26.2	36.4	37.33	-1,108.0	-688.3	451.2	388.2	63.05	7.156	
10,450.0	10,356.0	10,335.2	10,333.0	26.4	36.5	41.27	-1,108.5	-687.8	427.1	363.7	63.38	6.739	
10,500.0	10,393.9	10,374.2	10,372.0	26.6	36.7	46.16	-1,109.0	-687.2	400.8	337.1	63.65	6.297	
10,550.0	10,428.8	10,410.0	10,407.8	26.8	36.8	52.04	-1,109.4	-686.6	372.9	309.0	63.84	5.841	
10,600.0	10,460.5	10,441.9	10,439.7	27.0	36.9	58.78	-1,109.7	-686.1	344.2	280.3	63.91	5.386	
10,650.0	10,488.7	10,470.4	10,468.1	27.2	37.0	66.11	-1,110.0	-685.7	316.0	252.2	63.80	4.953	
10,700.0	10,513.2	10,495.1	10,492.9	27.3	37.1	73.49	-1,110.2	-685.4	289.6	226.1	63.44	4.564	
10,750.0	10,533.8	10,516.0	10,513.8	27.5	37.2	80.25	-1,110.4	-685.1	266.7	204.0	62.74	4.252	
10,800.0	10,550.4	10,532.9	10,530.6	27.6	37.2	85.76	-1,110.6	-684.9	249.7	188.1	61.67	4.049	
10,850.0	10,562.8	10,545.6	10,543.3	27.7	37.3	89.59	-1,110.7	-684.7	240.8	180.4	60.38	3.989 SF	
10,871.4	10,566.8	10,549.7	10,547.5	27.7	37.3	90.66	-1,110.7	-684.7	239.9	180.1	59.82	4.010 CC, ES	
10,900.0	10,570.9	10,554.0	10,551.8	27.7	37.3	91.51	-1,110.7	-684.6	241.6	182.4	59.17	4.083	
10,950.0	10,574.7	10,558.2	10,555.9	27.8	37.3	91.38	-1,110.8	-684.6	252.3	194.0	58.38	4.322	
10,968.4	10,575.0	10,558.6	10,556.4	27.8	37.3	90.82	-1,110.8	-684.6	258.7	200.4	58.23	4.442	
11,000.0	10,575.0	10,558.9	10,556.6	27.8	37.3	90.88	-1,110.8	-684.6	272.1	213.9	58.13	4.681	
11,100.0	10,575.0	10,559.7	10,557.4	27.9	37.3	91.07	-1,110.8	-684.6	331.3	272.6	58.65	5.648	
11,200.0	10,575.0	10,560.5	10,558.2	28.0	37.3	91.26	-1,110.8	-684.6	406.7	347.2	59.54	6.831	
11,300.0	10,575.0	10,561.3	10,559.1	28.1	37.3	91.46	-1,110.8	-684.6	491.1	430.7	60.32	8.141	
11,400.0	10,575.0	10,562.1	10,559.9	28.2	37.3	91.65	-1,110.8	-684.5	580.4	519.5	60.92	9.526	
11,500.0	10,575.0	11,534.0	11,121.5	28.4	39.0	157.61	-1,723.0	-675.0	615.2	566.7	48.42	12.703	
11,600.0	10,575.0	11,625.8	11,123.0	28.6	39.4	157.31	-1,814.7	-678.4	618.3	569.2	49.08	12.598	
11,700.0	10,575.0	11,732.6	11,125.2	28.8	40.0	156.98	-1,921.4	-682.6	622.0	572.3	49.73	12.508	
11,800.0	10,575.0	11,822.5	11,126.8	29.1	40.5	156.66	-2,011.2	-686.4	625.6	575.1	50.52	12.385	
11,900.0	10,575.0	11,920.6	11,130.1	29.4	41.2	156.44	-2,109.1	-689.8	630.4	579.0	51.30	12.287	
12,000.0	10,575.0	12,026.2	11,134.8	29.8	41.9	156.54	-2,214.6	-690.0	634.7	582.7	52.04	12.197	
12,100.0	10,575.0	12,136.2	11,139.2	30.2	42.7	156.84	-2,324.6	-687.5	637.8	585.0	52.76	12.089	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Offset Design: TARHEEL_DONKEY POTROAST PROJECT - OUTLAW 22 FEDERAL COM #1H - ST01 - ST01 AWP												Offset Site Error:	0.0 usft
Survey Program: 100-r.5 GYRO-NS, 10661-r.5 MWD												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		No-Go Distance (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
12,200.0	10,575.0	12,238.5	11,142.7	30.7	43.6	157.21	-2,426.7	-683.8	639.8	586.3	53.53	11.951	
12,300.0	10,575.0	12,337.5	11,145.5	31.2	44.4	157.40	-2,525.7	-682.0	641.9	587.5	54.41	11.799	
12,400.0	10,575.0	12,439.8	11,148.0	31.8	45.4	157.57	-2,627.9	-680.3	643.9	588.6	55.31	11.642	
12,500.0	10,575.0	12,541.4	11,150.6	32.4	46.3	157.81	-2,729.4	-677.8	645.5	589.3	56.23	11.481	
12,600.0	10,575.0	12,645.3	11,152.9	33.0	47.4	158.06	-2,833.3	-675.0	646.8	589.7	57.17	11.314	
12,700.0	10,575.0	12,750.3	11,154.5	33.7	48.4	158.30	-2,938.2	-671.9	647.4	589.2	58.13	11.136	
12,800.0	10,575.0	12,858.4	11,155.0	34.5	49.6	158.54	-3,046.3	-668.6	647.0	587.9	59.11	10.945	
12,872.0	10,575.0	12,923.5	11,155.0	35.0	50.3	158.65	-3,111.3	-666.8	646.4	586.5	59.92	10.789	
12,900.0	10,575.0	12,947.5	11,155.1	35.2	50.6	158.66	-3,135.4	-666.5	646.5	586.3	60.24	10.732	
13,000.0	10,575.0	13,048.5	11,155.9	36.0	51.7	158.67	-3,236.3	-666.1	647.3	586.0	61.38	10.547	
13,100.0	10,575.0	13,138.2	11,156.8	36.7	52.7	158.66	-3,326.1	-665.9	648.4	585.8	62.61	10.357	
13,200.0	10,575.0	13,238.5	11,158.6	37.5	53.9	158.60	-3,426.3	-666.7	650.6	586.8	63.82	10.195	
13,300.0	10,575.0	13,337.6	11,160.1	38.4	55.1	158.50	-3,525.4	-667.8	652.6	587.6	65.08	10.028	
13,400.0	10,575.0	13,445.9	11,160.8	39.2	56.4	158.30	-3,633.7	-669.9	654.2	587.9	66.36	9.859	
13,500.0	10,575.0	13,539.3	11,160.8	40.0	57.6	158.01	-3,727.1	-672.8	655.6	587.8	67.77	9.674	
13,600.0	10,575.0	13,644.7	11,160.0	40.9	58.9	157.55	-3,832.3	-677.5	656.8	587.6	69.22	9.488	
13,700.0	10,575.0	13,729.1	11,160.2	41.7	60.0	157.20	-3,916.7	-681.3	659.1	588.4	70.77	9.313	
13,800.0	10,575.0	13,834.5	11,161.2	42.6	61.3	156.78	-4,021.9	-686.3	662.0	589.8	72.28	9.159	
13,900.0	10,575.0	13,917.0	11,162.0	43.4	62.4	156.46	-4,104.3	-690.2	665.3	591.4	73.87	9.006	
14,000.0	10,575.0	14,011.0	11,165.5	44.3	63.7	156.18	-4,198.1	-694.6	670.8	595.4	75.43	8.893	
14,100.0	10,575.0	14,108.2	11,170.6	45.2	65.0	155.95	-4,295.1	-699.1	677.8	600.9	76.97	8.807	
14,200.0	10,575.0	14,214.6	11,175.0	46.1	66.4	155.68	-4,401.3	-704.0	683.7	605.2	78.53	8.707	
14,300.0	10,575.0	14,303.8	11,179.2	47.0	67.6	155.46	-4,490.3	-708.2	690.2	610.0	80.12	8.614	
14,400.0	10,575.0	14,412.0	11,184.4	47.9	69.1	155.21	-4,598.3	-713.1	696.7	615.0	81.71	8.527	
14,500.0	10,575.0	14,520.6	11,188.1	48.8	70.6	154.94	-4,706.7	-717.7	701.9	618.6	83.33	8.424	
14,600.0	10,575.0	14,625.3	11,190.8	49.7	72.1	154.66	-4,811.3	-722.2	706.3	621.3	84.99	8.310	
14,700.0	10,575.0	14,731.0	11,193.0	50.6	73.6	154.42	-4,916.9	-725.8	709.9	623.3	86.65	8.193	
14,800.0	10,575.0	14,833.0	11,194.6	51.5	75.0	154.22	-5,018.9	-728.7	712.9	624.6	88.31	8.072	
14,900.0	10,575.0	14,930.0	11,196.1	52.4	76.4	154.03	-5,115.8	-731.4	715.8	625.8	90.01	7.953	
15,000.0	10,575.0	14,930.0	11,196.1	53.3	76.4	154.03	-5,115.8	-731.4	726.1	634.7	91.40	7.944	
15,100.0	10,575.0	14,930.0	11,196.1	54.2	76.4	154.03	-5,115.8	-731.4	749.6	657.7	91.98	8.150	
15,200.0	10,575.0	14,930.0	11,196.1	55.2	76.4	154.03	-5,115.8	-731.4	785.3	693.5	91.85	8.551	
15,300.0	10,575.0	14,930.0	11,196.1	56.1	76.4	154.03	-5,115.8	-731.4	831.6	740.4	91.18	9.120	
15,400.0	10,575.0	14,930.0	11,196.1	57.0	76.4	154.03	-5,115.8	-731.4	886.8	796.6	90.18	9.833	
15,500.0	10,575.0	14,930.0	11,196.1	57.9	76.4	154.03	-5,115.8	-731.4	949.3	860.3	89.01	10.664	

ConocoPhillips

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 3630.0usft (Original Well Ele

Offset Depths are relative to Offset Datum


Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: _DONKEY POTROAST FED COM 503H - Slot DONK

Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30

Grid Convergence at Surface is: 0.37°

Ladder Plot

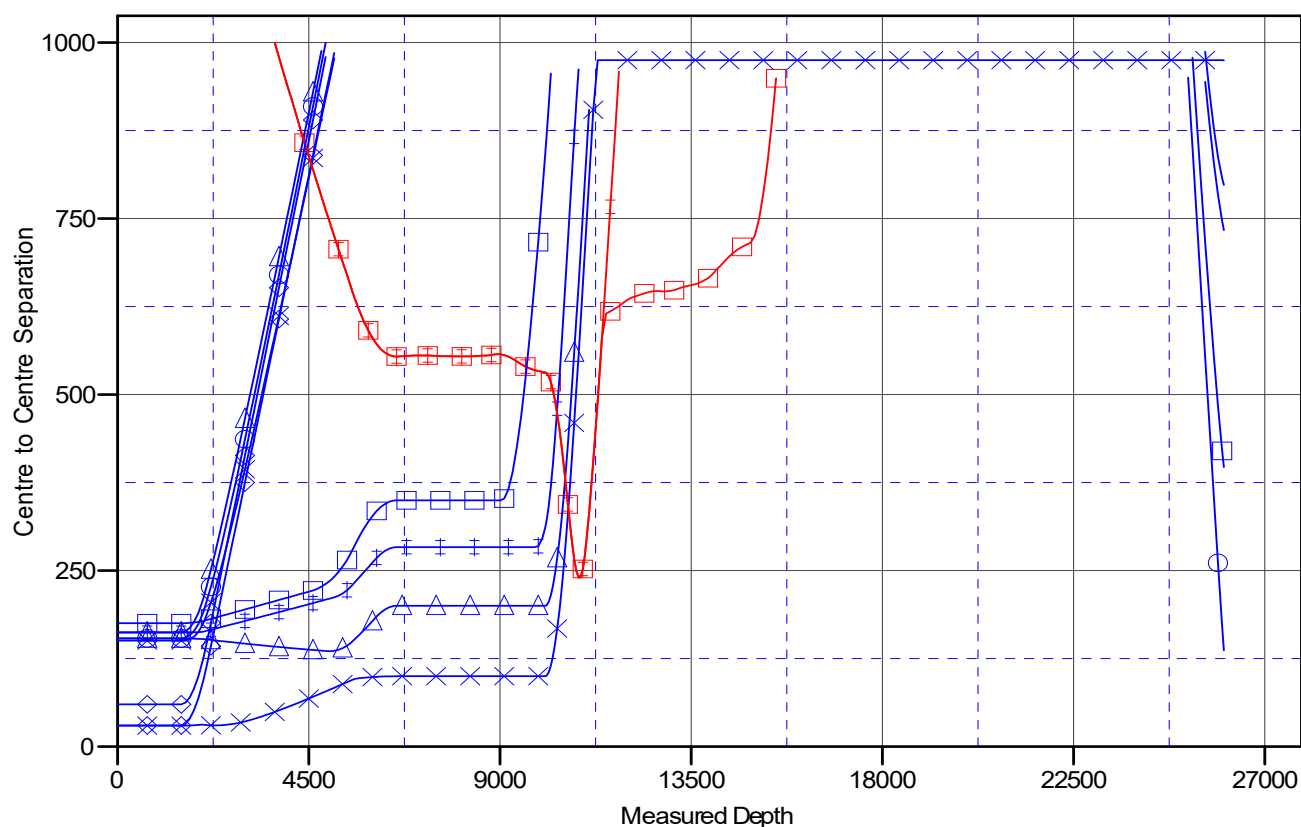

LEGEND

*GRIZZOGAR FED COM 503H, OWB, PWP0 V0	*TARHEEL FED COM #704H, OWB, PWP0 V0	*TARHEEL FED COM #604H, OWB, PWP0 V0
*GRIZZOGAR FED COM 705H, OWB, PWP0 V0	*DONKEY POTROAST FED COM 504H, OWB, PWP0 V0	OUTLAW 22 FEDERAL COM #H, OWB, AWP V0
*GRIZZOGAR FED COM 504H, OWB, PWP0A V0	*DONKEY POTROAST FED COM 703H, OWB, PWP0 V0	OUTLAW 22 FEDERAL COM #H, ST01, ST01 AWP V0
*GRIZZOGAR FED COM 704H, OWB, PWP0A V0	*TARHEEL FED COM #703H, OWB, PWP0 V0	*TARHEEL FED COM #604H, OWB, PWP0 V0
*DONKEY POTROAST FED COM 704H, OWB, PWP0 V0	*TARHEEL FED COM #503H, OWB, PWP0 V0	*TARHEEL FED COM #603H, OWB, PWP0 V0


CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

ConocoPhillips
Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Project:	ZEUS_NME	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Reference Site:	TARHEEL_DONKEY POTROAST PROJECT	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site Error:	0.0 usft	North Reference:	Grid
Reference Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	EDT 17 Permian Prod
Reference Design:	PWP0	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 3630.0usft (Original Well Ele
Offset Depths are relative to Offset Datum
Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: _DONKEY POTROAST FED COM 503H - Slot DONK
Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30
Grid Convergence at Surface is: 0.37°

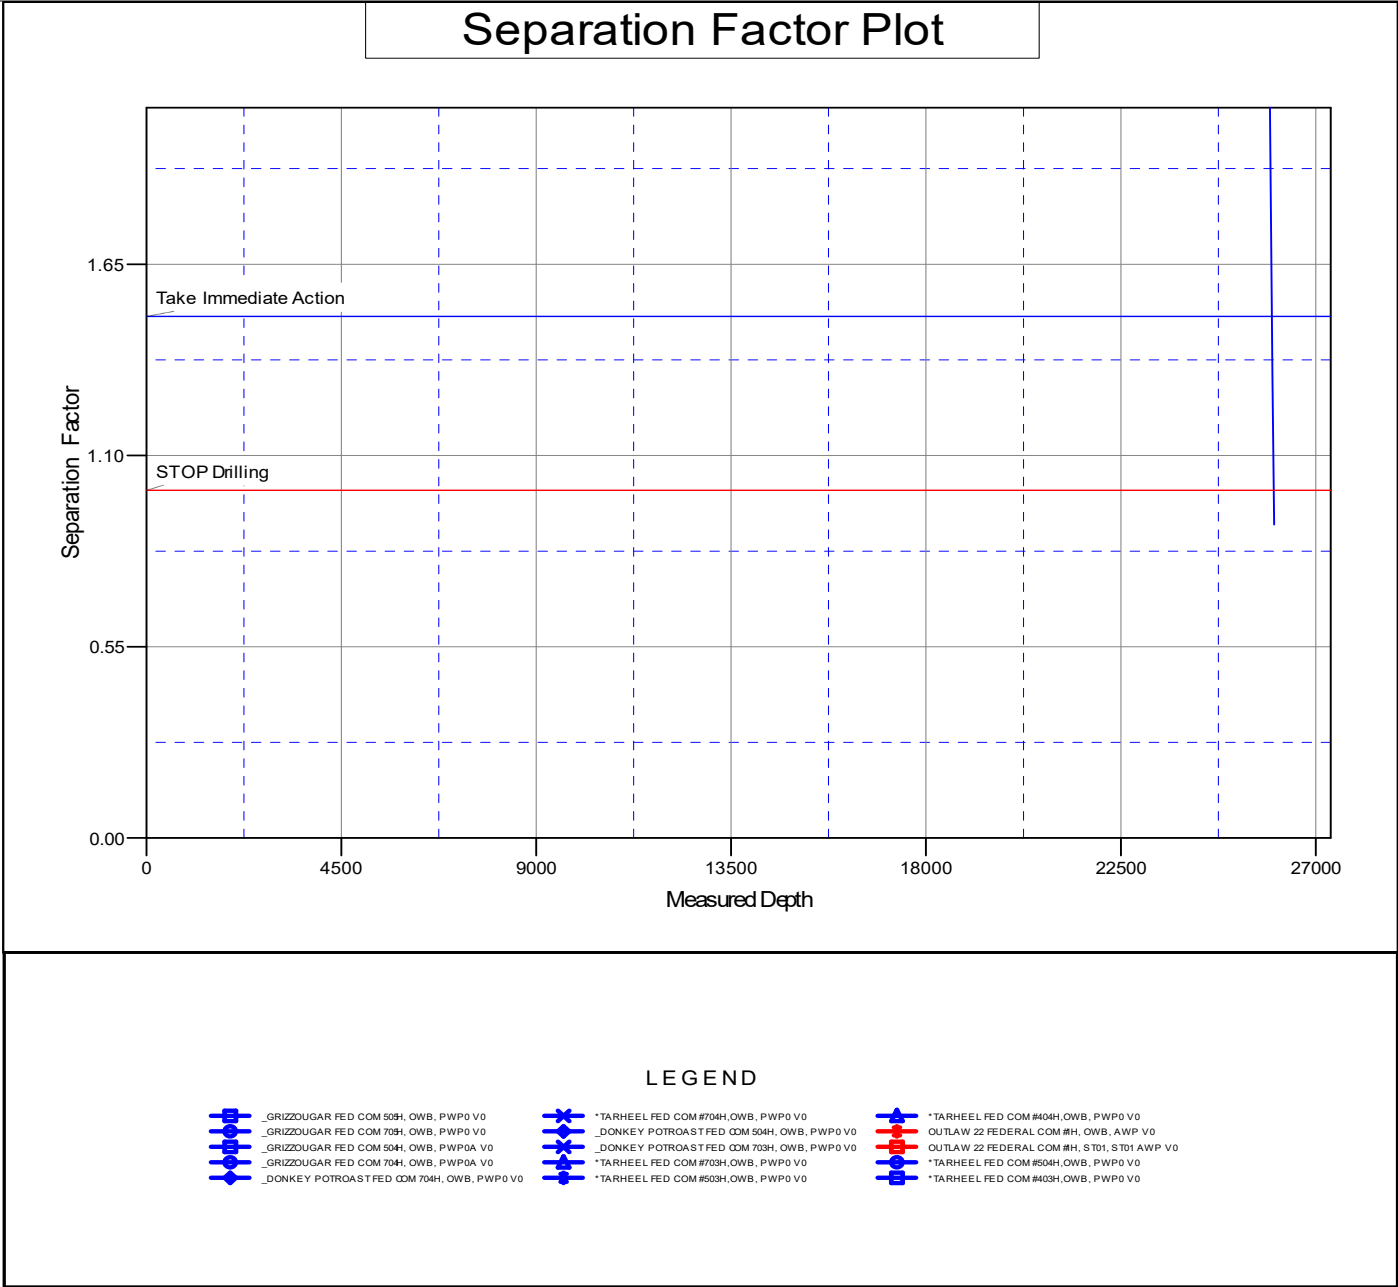

DELAWARE BASIN EAST

ZEUS_NME

TARHEEL_DONKEY POTROAST PROJECT

**_DONKEY POTROAST FED COM 503H - Slot DONKEY
POTROAST #503H**

OWB

Plan: PWP0

Standard Planning Report

22 July, 2024

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Project	ZEUS_NME		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Site	TARHEEL_DONKEY POTROAST PROJECT		
Site Position:		Northing:	567,544.34 usft
From:	Map	Easting:	710,351.32 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 33' 30.358 N
		Longitude:	103° 39' 2.181 W

Well	_DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H		
Well Position	+N/-S	0.0 usft	Northing:
	+E/-W	0.0 usft	Easting:
Position Uncertainty		3.0 usft	Wellhead Elevation:
Grid Convergence:		0.37 °	
			Latitude:
			Longitude:
			Ground Level:

Wellbore	OWB				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	BGGM2022	9/14/2023	6.55	60.36	47,636.75594949

Design	PWP0			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	181.21

Plan Survey Tool Program	Date	7/22/2024		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	26,040.2 PWP0 (OWB)	r.5 MWD+IFR1	
			OWSG MWD + IFR1 rev.5	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,021.2	10.42	215.28	2,018.4	-38.6	-27.3	2.00	2.00	0.00	215.28	
5,524.0	10.42	215.28	5,463.3	-556.0	-393.4	0.00	0.00	0.00	0.00	
6,566.4	0.00	0.00	6,500.0	-633.2	-448.0	1.00	-1.00	0.00	180.00	
10,068.4	0.00	0.00	10,002.0	-633.2	-448.0	0.00	0.00	0.00	0.00	
10,968.4	90.00	179.62	10,575.0	-1,206.1	-444.2	10.00	10.00	19.96	179.62	
26,040.2	90.00	179.62	10,575.0	-16,277.6	-343.5	0.00	0.00	0.00	0.00	

ConocoPhillips

Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00	
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00	
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00	
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00	
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00	
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00	
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00	
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00	
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00	
1,600.0	2.00	215.28	1,600.0	-1.4	-1.0	1.4	2.00	2.00	0.00	
1,700.0	4.00	215.28	1,699.8	-5.7	-4.0	5.8	2.00	2.00	0.00	
1,800.0	6.00	215.28	1,799.5	-12.8	-9.1	13.0	2.00	2.00	0.00	
1,900.0	8.00	215.28	1,898.7	-22.8	-16.1	23.1	2.00	2.00	0.00	
2,000.0	10.00	215.28	1,997.5	-35.5	-25.1	36.1	2.00	2.00	0.00	
2,021.2	10.42	215.28	2,018.4	-38.6	-27.3	39.2	2.00	2.00	0.00	
2,100.0	10.42	215.28	2,095.8	-50.2	-35.5	51.0	0.00	0.00	0.00	
2,200.0	10.42	215.28	2,194.2	-65.0	-46.0	66.0	0.00	0.00	0.00	
2,300.0	10.42	215.28	2,292.5	-79.8	-56.4	81.0	0.00	0.00	0.00	
2,400.0	10.42	215.28	2,390.9	-94.6	-66.9	95.9	0.00	0.00	0.00	
2,500.0	10.42	215.28	2,489.2	-109.3	-77.3	110.9	0.00	0.00	0.00	
2,600.0	10.42	215.28	2,587.6	-124.1	-87.8	125.9	0.00	0.00	0.00	
2,700.0	10.42	215.28	2,685.9	-138.9	-98.2	140.9	0.00	0.00	0.00	
2,800.0	10.42	215.28	2,784.3	-153.6	-108.7	155.9	0.00	0.00	0.00	
2,900.0	10.42	215.28	2,882.6	-168.4	-119.2	170.9	0.00	0.00	0.00	
3,000.0	10.42	215.28	2,981.0	-183.2	-129.6	185.9	0.00	0.00	0.00	
3,100.0	10.42	215.28	3,079.3	-197.9	-140.1	200.9	0.00	0.00	0.00	
3,200.0	10.42	215.28	3,177.7	-212.7	-150.5	215.8	0.00	0.00	0.00	
3,300.0	10.42	215.28	3,276.0	-227.5	-161.0	230.8	0.00	0.00	0.00	
3,400.0	10.42	215.28	3,374.4	-242.3	-171.4	245.8	0.00	0.00	0.00	
3,500.0	10.42	215.28	3,472.7	-257.0	-181.9	260.8	0.00	0.00	0.00	
3,600.0	10.42	215.28	3,571.1	-271.8	-192.3	275.8	0.00	0.00	0.00	
3,700.0	10.42	215.28	3,669.4	-286.6	-202.8	290.8	0.00	0.00	0.00	
3,800.0	10.42	215.28	3,767.8	-301.3	-213.2	305.8	0.00	0.00	0.00	
3,900.0	10.42	215.28	3,866.1	-316.1	-223.7	320.8	0.00	0.00	0.00	
4,000.0	10.42	215.28	3,964.5	-330.9	-234.1	335.8	0.00	0.00	0.00	
4,100.0	10.42	215.28	4,062.8	-345.7	-244.6	350.7	0.00	0.00	0.00	
4,200.0	10.42	215.28	4,161.2	-360.4	-255.0	365.7	0.00	0.00	0.00	
4,300.0	10.42	215.28	4,259.5	-375.2	-265.5	380.7	0.00	0.00	0.00	
4,400.0	10.42	215.28	4,357.9	-390.0	-275.9	395.7	0.00	0.00	0.00	
4,500.0	10.42	215.28	4,456.2	-404.7	-286.4	410.7	0.00	0.00	0.00	
4,600.0	10.42	215.28	4,554.6	-419.5	-296.8	425.7	0.00	0.00	0.00	
4,700.0	10.42	215.28	4,652.9	-434.3	-307.3	440.7	0.00	0.00	0.00	
4,800.0	10.42	215.28	4,751.3	-449.1	-317.7	455.7	0.00	0.00	0.00	
4,900.0	10.42	215.28	4,849.6	-463.8	-328.2	470.6	0.00	0.00	0.00	
5,000.0	10.42	215.28	4,948.0	-478.6	-338.6	485.6	0.00	0.00	0.00	
5,100.0	10.42	215.28	5,046.3	-493.4	-349.1	500.6	0.00	0.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,200.0	10.42	215.28	5,144.7	-508.1	-359.5	515.6	0.00	0.00	0.00	
5,300.0	10.42	215.28	5,243.0	-522.9	-370.0	530.6	0.00	0.00	0.00	
5,400.0	10.42	215.28	5,341.4	-537.7	-380.4	545.6	0.00	0.00	0.00	
5,500.0	10.42	215.28	5,439.7	-552.5	-390.9	560.6	0.00	0.00	0.00	
5,524.0	10.42	215.28	5,463.3	-556.0	-393.4	564.2	0.00	0.00	0.00	
5,600.0	9.66	215.28	5,538.1	-566.8	-401.0	575.2	1.00	-1.00	0.00	
5,700.0	8.66	215.28	5,636.9	-579.8	-410.2	588.3	1.00	-1.00	0.00	
5,800.0	7.66	215.28	5,735.9	-591.4	-418.4	600.1	1.00	-1.00	0.00	
5,900.0	6.66	215.28	5,835.1	-601.6	-425.6	610.4	1.00	-1.00	0.00	
6,000.0	5.66	215.28	5,934.5	-610.4	-431.8	619.3	1.00	-1.00	0.00	
6,100.0	4.66	215.28	6,034.1	-617.7	-437.0	626.8	1.00	-1.00	0.00	
6,200.0	3.66	215.28	6,133.8	-623.6	-441.2	632.8	1.00	-1.00	0.00	
6,300.0	2.66	215.28	6,233.7	-628.1	-444.4	637.4	1.00	-1.00	0.00	
6,400.0	1.66	215.28	6,333.6	-631.2	-446.6	640.5	1.00	-1.00	0.00	
6,500.0	0.66	215.28	6,433.6	-632.9	-447.8	642.2	1.00	-1.00	0.00	
6,566.4	0.00	0.00	6,500.0	-633.2	-448.0	642.5	1.00	-1.00	0.00	
6,600.0	0.00	0.00	6,533.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
6,700.0	0.00	0.00	6,633.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
6,800.0	0.00	0.00	6,733.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
6,900.0	0.00	0.00	6,833.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,000.0	0.00	0.00	6,933.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,100.0	0.00	0.00	7,033.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,200.0	0.00	0.00	7,133.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,300.0	0.00	0.00	7,233.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,400.0	0.00	0.00	7,333.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,500.0	0.00	0.00	7,433.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,600.0	0.00	0.00	7,533.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,700.0	0.00	0.00	7,633.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,800.0	0.00	0.00	7,733.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
7,900.0	0.00	0.00	7,833.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,000.0	0.00	0.00	7,933.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,100.0	0.00	0.00	8,033.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,200.0	0.00	0.00	8,133.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,300.0	0.00	0.00	8,233.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,400.0	0.00	0.00	8,333.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,500.0	0.00	0.00	8,433.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,600.0	0.00	0.00	8,533.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,700.0	0.00	0.00	8,633.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,800.0	0.00	0.00	8,733.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
8,900.0	0.00	0.00	8,833.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,000.0	0.00	0.00	8,933.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,100.0	0.00	0.00	9,033.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,200.0	0.00	0.00	9,133.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,300.0	0.00	0.00	9,233.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,400.0	0.00	0.00	9,333.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,500.0	0.00	0.00	9,433.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,600.0	0.00	0.00	9,533.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,700.0	0.00	0.00	9,633.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,800.0	0.00	0.00	9,733.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
9,900.0	0.00	0.00	9,833.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
10,000.0	0.00	0.00	9,933.6	-633.2	-448.0	642.5	0.00	0.00	0.00	
10,068.4	0.00	0.00	10,002.0	-633.2	-448.0	642.5	0.00	0.00	0.00	
10,100.0	3.16	179.62	10,033.6	-634.1	-448.0	643.4	10.00	10.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
10,150.0	8.16	179.62	10,083.3	-639.0	-448.0	648.3	10.00	10.00	0.00	
10,200.0	13.16	179.62	10,132.4	-648.2	-447.9	657.5	10.00	10.00	0.00	
10,250.0	18.16	179.62	10,180.5	-661.7	-447.8	671.0	10.00	10.00	0.00	
10,300.0	23.16	179.62	10,227.3	-679.4	-447.7	688.7	10.00	10.00	0.00	
10,350.0	28.16	179.62	10,272.4	-701.0	-447.5	710.3	10.00	10.00	0.00	
10,400.0	33.16	179.62	10,315.4	-726.5	-447.4	735.8	10.00	10.00	0.00	
10,450.0	38.16	179.62	10,356.0	-755.6	-447.2	764.9	10.00	10.00	0.00	
10,500.0	43.16	179.62	10,393.9	-788.2	-447.0	797.4	10.00	10.00	0.00	
10,550.0	48.16	179.62	10,428.8	-823.9	-446.7	833.2	10.00	10.00	0.00	
10,600.0	53.16	179.62	10,460.5	-862.6	-446.5	871.8	10.00	10.00	0.00	
10,650.0	58.16	179.62	10,488.7	-903.9	-446.2	913.1	10.00	10.00	0.00	
10,700.0	63.16	179.62	10,513.2	-947.4	-445.9	956.6	10.00	10.00	0.00	
10,750.0	68.16	179.62	10,533.8	-993.0	-445.6	1,002.2	10.00	10.00	0.00	
10,800.0	73.16	179.62	10,550.4	-1,040.1	-445.3	1,049.3	10.00	10.00	0.00	
10,850.0	78.16	179.62	10,562.8	-1,088.6	-445.0	1,097.7	10.00	10.00	0.00	
10,900.0	83.16	179.62	10,570.9	-1,137.9	-444.6	1,147.0	10.00	10.00	0.00	
10,950.0	88.16	179.62	10,574.7	-1,187.7	-444.3	1,196.8	10.00	10.00	0.00	
10,968.4	90.00	179.62	10,575.0	-1,206.1	-444.2	1,215.2	10.00	10.00	0.00	
11,000.0	90.00	179.62	10,575.0	-1,237.7	-444.0	1,246.8	0.00	0.00	0.00	
11,100.0	90.00	179.62	10,575.0	-1,337.7	-443.3	1,346.8	0.00	0.00	0.00	
11,200.0	90.00	179.62	10,575.0	-1,437.7	-442.6	1,446.7	0.00	0.00	0.00	
11,300.0	90.00	179.62	10,575.0	-1,537.7	-442.0	1,546.7	0.00	0.00	0.00	
11,400.0	90.00	179.62	10,575.0	-1,637.7	-441.3	1,646.6	0.00	0.00	0.00	
11,500.0	90.00	179.62	10,575.0	-1,737.7	-440.6	1,746.6	0.00	0.00	0.00	
11,600.0	90.00	179.62	10,575.0	-1,837.7	-440.0	1,846.6	0.00	0.00	0.00	
11,700.0	90.00	179.62	10,575.0	-1,937.7	-439.3	1,946.5	0.00	0.00	0.00	
11,800.0	90.00	179.62	10,575.0	-2,037.7	-438.6	2,046.5	0.00	0.00	0.00	
11,900.0	90.00	179.62	10,575.0	-2,137.7	-438.0	2,146.5	0.00	0.00	0.00	
12,000.0	90.00	179.62	10,575.0	-2,237.7	-437.3	2,246.4	0.00	0.00	0.00	
12,100.0	90.00	179.62	10,575.0	-2,337.7	-436.6	2,346.4	0.00	0.00	0.00	
12,200.0	90.00	179.62	10,575.0	-2,437.7	-435.9	2,446.3	0.00	0.00	0.00	
12,300.0	90.00	179.62	10,575.0	-2,537.7	-435.3	2,546.3	0.00	0.00	0.00	
12,400.0	90.00	179.62	10,575.0	-2,637.7	-434.6	2,646.3	0.00	0.00	0.00	
12,500.0	90.00	179.62	10,575.0	-2,737.7	-433.9	2,746.2	0.00	0.00	0.00	
12,600.0	90.00	179.62	10,575.0	-2,837.7	-433.3	2,846.2	0.00	0.00	0.00	
12,700.0	90.00	179.62	10,575.0	-2,937.7	-432.6	2,946.1	0.00	0.00	0.00	
12,800.0	90.00	179.62	10,575.0	-3,037.7	-431.9	3,046.1	0.00	0.00	0.00	
12,900.0	90.00	179.62	10,575.0	-3,137.7	-431.3	3,146.1	0.00	0.00	0.00	
13,000.0	90.00	179.62	10,575.0	-3,237.7	-430.6	3,246.0	0.00	0.00	0.00	
13,100.0	90.00	179.62	10,575.0	-3,337.7	-429.9	3,346.0	0.00	0.00	0.00	
13,200.0	90.00	179.62	10,575.0	-3,437.7	-429.3	3,446.0	0.00	0.00	0.00	
13,300.0	90.00	179.62	10,575.0	-3,537.7	-428.6	3,545.9	0.00	0.00	0.00	
13,400.0	90.00	179.62	10,575.0	-3,637.7	-427.9	3,645.9	0.00	0.00	0.00	
13,500.0	90.00	179.62	10,575.0	-3,737.7	-427.3	3,745.8	0.00	0.00	0.00	
13,600.0	90.00	179.62	10,575.0	-3,837.7	-426.6	3,845.8	0.00	0.00	0.00	
13,700.0	90.00	179.62	10,575.0	-3,937.7	-425.9	3,945.8	0.00	0.00	0.00	
13,800.0	90.00	179.62	10,575.0	-4,037.7	-425.3	4,045.7	0.00	0.00	0.00	
13,900.0	90.00	179.62	10,575.0	-4,137.6	-424.6	4,145.7	0.00	0.00	0.00	
14,000.0	90.00	179.62	10,575.0	-4,237.6	-423.9	4,245.6	0.00	0.00	0.00	
14,100.0	90.00	179.62	10,575.0	-4,337.6	-423.3	4,345.6	0.00	0.00	0.00	
14,200.0	90.00	179.62	10,575.0	-4,437.6	-422.6	4,445.6	0.00	0.00	0.00	
14,300.0	90.00	179.62	10,575.0	-4,537.6	-421.9	4,545.5	0.00	0.00	0.00	
14,400.0	90.00	179.62	10,575.0	-4,637.6	-421.3	4,645.5	0.00	0.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,500.0	90.00	179.62	10,575.0	-4,737.6	-420.6	4,745.5	0.00	0.00	0.00
14,600.0	90.00	179.62	10,575.0	-4,837.6	-419.9	4,845.4	0.00	0.00	0.00
14,700.0	90.00	179.62	10,575.0	-4,937.6	-419.2	4,945.4	0.00	0.00	0.00
14,800.0	90.00	179.62	10,575.0	-5,037.6	-418.6	5,045.3	0.00	0.00	0.00
14,900.0	90.00	179.62	10,575.0	-5,137.6	-417.9	5,145.3	0.00	0.00	0.00
15,000.0	90.00	179.62	10,575.0	-5,237.6	-417.2	5,245.3	0.00	0.00	0.00
15,100.0	90.00	179.62	10,575.0	-5,337.6	-416.6	5,345.2	0.00	0.00	0.00
15,200.0	90.00	179.62	10,575.0	-5,437.6	-415.9	5,445.2	0.00	0.00	0.00
15,300.0	90.00	179.62	10,575.0	-5,537.6	-415.2	5,545.1	0.00	0.00	0.00
15,400.0	90.00	179.62	10,575.0	-5,637.6	-414.6	5,645.1	0.00	0.00	0.00
15,500.0	90.00	179.62	10,575.0	-5,737.6	-413.9	5,745.1	0.00	0.00	0.00
15,600.0	90.00	179.62	10,575.0	-5,837.6	-413.2	5,845.0	0.00	0.00	0.00
15,700.0	90.00	179.62	10,575.0	-5,937.6	-412.6	5,945.0	0.00	0.00	0.00
15,800.0	90.00	179.62	10,575.0	-6,037.6	-411.9	6,045.0	0.00	0.00	0.00
15,900.0	90.00	179.62	10,575.0	-6,137.6	-411.2	6,144.9	0.00	0.00	0.00
16,000.0	90.00	179.62	10,575.0	-6,237.6	-410.6	6,244.9	0.00	0.00	0.00
16,100.0	90.00	179.62	10,575.0	-6,337.6	-409.9	6,344.8	0.00	0.00	0.00
16,200.0	90.00	179.62	10,575.0	-6,437.6	-409.2	6,444.8	0.00	0.00	0.00
16,300.0	90.00	179.62	10,575.0	-6,537.6	-408.6	6,544.8	0.00	0.00	0.00
16,400.0	90.00	179.62	10,575.0	-6,637.6	-407.9	6,644.7	0.00	0.00	0.00
16,500.0	90.00	179.62	10,575.0	-6,737.6	-407.2	6,744.7	0.00	0.00	0.00
16,600.0	90.00	179.62	10,575.0	-6,837.6	-406.6	6,844.6	0.00	0.00	0.00
16,700.0	90.00	179.62	10,575.0	-6,937.6	-405.9	6,944.6	0.00	0.00	0.00
16,800.0	90.00	179.62	10,575.0	-7,037.6	-405.2	7,044.6	0.00	0.00	0.00
16,900.0	90.00	179.62	10,575.0	-7,137.6	-404.6	7,144.5	0.00	0.00	0.00
17,000.0	90.00	179.62	10,575.0	-7,237.6	-403.9	7,244.5	0.00	0.00	0.00
17,100.0	90.00	179.62	10,575.0	-7,337.6	-403.2	7,344.5	0.00	0.00	0.00
17,200.0	90.00	179.62	10,575.0	-7,437.6	-402.5	7,444.4	0.00	0.00	0.00
17,300.0	90.00	179.62	10,575.0	-7,537.6	-401.9	7,544.4	0.00	0.00	0.00
17,400.0	90.00	179.62	10,575.0	-7,637.6	-401.2	7,644.3	0.00	0.00	0.00
17,500.0	90.00	179.62	10,575.0	-7,737.6	-400.5	7,744.3	0.00	0.00	0.00
17,600.0	90.00	179.62	10,575.0	-7,837.6	-399.9	7,844.3	0.00	0.00	0.00
17,700.0	90.00	179.62	10,575.0	-7,937.6	-399.2	7,944.2	0.00	0.00	0.00
17,800.0	90.00	179.62	10,575.0	-8,037.6	-398.5	8,044.2	0.00	0.00	0.00
17,900.0	90.00	179.62	10,575.0	-8,137.6	-397.9	8,144.1	0.00	0.00	0.00
18,000.0	90.00	179.62	10,575.0	-8,237.6	-397.2	8,244.1	0.00	0.00	0.00
18,100.0	90.00	179.62	10,575.0	-8,337.6	-396.5	8,344.1	0.00	0.00	0.00
18,200.0	90.00	179.62	10,575.0	-8,437.6	-395.9	8,444.0	0.00	0.00	0.00
18,300.0	90.00	179.62	10,575.0	-8,537.6	-395.2	8,544.0	0.00	0.00	0.00
18,400.0	90.00	179.62	10,575.0	-8,637.5	-394.5	8,643.9	0.00	0.00	0.00
18,500.0	90.00	179.62	10,575.0	-8,737.5	-393.9	8,743.9	0.00	0.00	0.00
18,600.0	90.00	179.62	10,575.0	-8,837.5	-393.2	8,843.9	0.00	0.00	0.00
18,700.0	90.00	179.62	10,575.0	-8,937.5	-392.5	8,943.8	0.00	0.00	0.00
18,800.0	90.00	179.62	10,575.0	-9,037.5	-391.9	9,043.8	0.00	0.00	0.00
18,900.0	90.00	179.62	10,575.0	-9,137.5	-391.2	9,143.8	0.00	0.00	0.00
19,000.0	90.00	179.62	10,575.0	-9,237.5	-390.5	9,243.7	0.00	0.00	0.00
19,100.0	90.00	179.62	10,575.0	-9,337.5	-389.9	9,343.7	0.00	0.00	0.00
19,200.0	90.00	179.62	10,575.0	-9,437.5	-389.2	9,443.6	0.00	0.00	0.00
19,300.0	90.00	179.62	10,575.0	-9,537.5	-388.5	9,543.6	0.00	0.00	0.00
19,400.0	90.00	179.62	10,575.0	-9,637.5	-387.9	9,643.6	0.00	0.00	0.00
19,500.0	90.00	179.62	10,575.0	-9,737.5	-387.2	9,743.5	0.00	0.00	0.00
19,600.0	90.00	179.62	10,575.0	-9,837.5	-386.5	9,843.5	0.00	0.00	0.00
19,700.0	90.00	179.62	10,575.0	-9,937.5	-385.8	9,943.4	0.00	0.00	0.00

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
19,800.0	90.00	179.62	10,575.0	-10,037.5	-385.2	10,043.4	0.00	0.00	0.00	
19,900.0	90.00	179.62	10,575.0	-10,137.5	-384.5	10,143.4	0.00	0.00	0.00	
20,000.0	90.00	179.62	10,575.0	-10,237.5	-383.8	10,243.3	0.00	0.00	0.00	
20,100.0	90.00	179.62	10,575.0	-10,337.5	-383.2	10,343.3	0.00	0.00	0.00	
20,200.0	90.00	179.62	10,575.0	-10,437.5	-382.5	10,443.3	0.00	0.00	0.00	
20,300.0	90.00	179.62	10,575.0	-10,537.5	-381.8	10,543.2	0.00	0.00	0.00	
20,400.0	90.00	179.62	10,575.0	-10,637.5	-381.2	10,643.2	0.00	0.00	0.00	
20,500.0	90.00	179.62	10,575.0	-10,737.5	-380.5	10,743.1	0.00	0.00	0.00	
20,600.0	90.00	179.62	10,575.0	-10,837.5	-379.8	10,843.1	0.00	0.00	0.00	
20,700.0	90.00	179.62	10,575.0	-10,937.5	-379.2	10,943.1	0.00	0.00	0.00	
20,800.0	90.00	179.62	10,575.0	-11,037.5	-378.5	11,043.0	0.00	0.00	0.00	
20,900.0	90.00	179.62	10,575.0	-11,137.5	-377.8	11,143.0	0.00	0.00	0.00	
21,000.0	90.00	179.62	10,575.0	-11,237.5	-377.2	11,242.9	0.00	0.00	0.00	
21,100.0	90.00	179.62	10,575.0	-11,337.5	-376.5	11,342.9	0.00	0.00	0.00	
21,200.0	90.00	179.62	10,575.0	-11,437.5	-375.8	11,442.9	0.00	0.00	0.00	
21,300.0	90.00	179.62	10,575.0	-11,537.5	-375.2	11,542.8	0.00	0.00	0.00	
21,400.0	90.00	179.62	10,575.0	-11,637.5	-374.5	11,642.8	0.00	0.00	0.00	
21,500.0	90.00	179.62	10,575.0	-11,737.5	-373.8	11,742.8	0.00	0.00	0.00	
21,600.0	90.00	179.62	10,575.0	-11,837.5	-373.2	11,842.7	0.00	0.00	0.00	
21,700.0	90.00	179.62	10,575.0	-11,937.5	-372.5	11,942.7	0.00	0.00	0.00	
21,800.0	90.00	179.62	10,575.0	-12,037.5	-371.8	12,042.6	0.00	0.00	0.00	
21,900.0	90.00	179.62	10,575.0	-12,137.5	-371.2	12,142.6	0.00	0.00	0.00	
22,000.0	90.00	179.62	10,575.0	-12,237.5	-370.5	12,242.6	0.00	0.00	0.00	
22,100.0	90.00	179.62	10,575.0	-12,337.5	-369.8	12,342.5	0.00	0.00	0.00	
22,200.0	90.00	179.62	10,575.0	-12,437.5	-369.1	12,442.5	0.00	0.00	0.00	
22,300.0	90.00	179.62	10,575.0	-12,537.5	-368.5	12,542.4	0.00	0.00	0.00	
22,400.0	90.00	179.62	10,575.0	-12,637.5	-367.8	12,642.4	0.00	0.00	0.00	
22,500.0	90.00	179.62	10,575.0	-12,737.5	-367.1	12,742.4	0.00	0.00	0.00	
22,600.0	90.00	179.62	10,575.0	-12,837.5	-366.5	12,842.3	0.00	0.00	0.00	
22,700.0	90.00	179.62	10,575.0	-12,937.5	-365.8	12,942.3	0.00	0.00	0.00	
22,800.0	90.00	179.62	10,575.0	-13,037.4	-365.1	13,042.3	0.00	0.00	0.00	
22,900.0	90.00	179.62	10,575.0	-13,137.4	-364.5	13,142.2	0.00	0.00	0.00	
23,000.0	90.00	179.62	10,575.0	-13,237.4	-363.8	13,242.2	0.00	0.00	0.00	
23,100.0	90.00	179.62	10,575.0	-13,337.4	-363.1	13,342.1	0.00	0.00	0.00	
23,200.0	90.00	179.62	10,575.0	-13,437.4	-362.5	13,442.1	0.00	0.00	0.00	
23,300.0	90.00	179.62	10,575.0	-13,537.4	-361.8	13,542.1	0.00	0.00	0.00	
23,400.0	90.00	179.62	10,575.0	-13,637.4	-361.1	13,642.0	0.00	0.00	0.00	
23,500.0	90.00	179.62	10,575.0	-13,737.4	-360.5	13,742.0	0.00	0.00	0.00	
23,600.0	90.00	179.62	10,575.0	-13,837.4	-359.8	13,841.9	0.00	0.00	0.00	
23,700.0	90.00	179.62	10,575.0	-13,937.4	-359.1	13,941.9	0.00	0.00	0.00	
23,800.0	90.00	179.62	10,575.0	-14,037.4	-358.5	14,041.9	0.00	0.00	0.00	
23,900.0	90.00	179.62	10,575.0	-14,137.4	-357.8	14,141.8	0.00	0.00	0.00	
24,000.0	90.00	179.62	10,575.0	-14,237.4	-357.1	14,241.8	0.00	0.00	0.00	
24,100.0	90.00	179.62	10,575.0	-14,337.4	-356.5	14,341.7	0.00	0.00	0.00	
24,200.0	90.00	179.62	10,575.0	-14,437.4	-355.8	14,441.7	0.00	0.00	0.00	
24,300.0	90.00	179.62	10,575.0	-14,537.4	-355.1	14,541.7	0.00	0.00	0.00	
24,400.0	90.00	179.62	10,575.0	-14,637.4	-354.5	14,641.6	0.00	0.00	0.00	
24,500.0	90.00	179.62	10,575.0	-14,737.4	-353.8	14,741.6	0.00	0.00	0.00	
24,600.0	90.00	179.62	10,575.0	-14,837.4	-353.1	14,841.6	0.00	0.00	0.00	
24,700.0	90.00	179.62	10,575.0	-14,937.4	-352.4	14,941.5	0.00	0.00	0.00	
24,800.0	90.00	179.62	10,575.0	-15,037.4	-351.8	15,041.5	0.00	0.00	0.00	
24,900.0	90.00	179.62	10,575.0	-15,137.4	-351.1	15,141.4	0.00	0.00	0.00	
25,000.0	90.00	179.62	10,575.0	-15,237.4	-350.4	15,241.4	0.00	0.00	0.00	

ConocoPhillips
Planning Report

Database:	EDT 17 Permian Prod	Local Co-ordinate Reference:	Well _DONKEY POTROAST FED COM 503H - Slot DONKEY POTROAST #503H
Company:	DELAWARE BASIN EAST	TVD Reference:	WELL @ 3630.0usft (Original Well Elev)
Project:	ZEUS_NME	MD Reference:	WELL @ 3630.0usft (Original Well Elev)
Site:	TARHEEL_DONKEY POTROAST PROJECT	North Reference:	Grid
Well:	_DONKEY POTROAST FED COM 503H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OWB		
Design:	PWP0		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
25,100.0	90.00	179.62	10,575.0	-15,337.4	-349.8	15,341.4	0.00	0.00	0.00	
25,200.0	90.00	179.62	10,575.0	-15,437.4	-349.1	15,441.3	0.00	0.00	0.00	
25,300.0	90.00	179.62	10,575.0	-15,537.4	-348.4	15,541.3	0.00	0.00	0.00	
25,400.0	90.00	179.62	10,575.0	-15,637.4	-347.8	15,641.2	0.00	0.00	0.00	
25,500.0	90.00	179.62	10,575.0	-15,737.4	-347.1	15,741.2	0.00	0.00	0.00	
25,600.0	90.00	179.62	10,575.0	-15,837.4	-346.4	15,841.2	0.00	0.00	0.00	
25,700.0	90.00	179.62	10,575.0	-15,937.4	-345.8	15,941.1	0.00	0.00	0.00	
25,800.0	90.00	179.62	10,575.0	-16,037.4	-345.1	16,041.1	0.00	0.00	0.00	
25,900.0	90.00	179.62	10,575.0	-16,137.4	-344.4	16,141.1	0.00	0.00	0.00	
26,000.0	90.00	179.62	10,575.0	-16,237.4	-343.8	16,241.0	0.00	0.00	0.00	
26,040.2	90.00	179.62	10,575.0	-16,277.6	-343.5	16,281.2	0.00	0.00	0.00	

Design Targets										
Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude	
FTP (DONKEY POTROAST) - plan misses target center by 273.6usft at 10500.0usft MD (10393.9 TVD, -788.2 N, -447.0 E) - Circle (radius 50.0)	0.00	0.00	10,575.0	-583.2	-449.2	570,121.92	711,339.07	32° 33' 55.801 N	103° 38' 50.446 W	
PBHL (DONKEY POTROAST) - plan hits target center - Rectangle (sides W100.0 H15,700.0 D20.0)	0.00	359.62	10,575.0	-16,277.6	-343.5	554,427.53	711,444.77	32° 31' 20.496 N	103° 38' 50.392 W	
LTP (DONKEY POTROAST) - plan hits target center - Circle (radius 50.0)	90.00	179.65	10,575.0	-16,227.6	-343.8	554,477.53	711,444.45	32° 31' 20.990 N	103° 38' 50.392 W	





Casing Points					
Measured Depth (usft)	Vertical Depth (usft)	Name		Casing Diameter (")	Hole Diameter (")
26,040.2	10,575.0	5-1/2" Production Casing		5-1/2	6-3/4



Project: ZEUS_NME
Site: TARHEEL_DONKEY POTROAST PROJECT
Well: DONKEY POTROAST FED COM 503H
Wellbore: OWB
Design: PWP0

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0
1500.0	0.00	0.00	1500.0	0.0	0.0	0.00	0.00	0.0
2021.2	10.42	215.28	2018.4	-38.6	-27.3	2.00	215.28	39.2
5524.0	10.42	215.28	5463.3	-556.0	-393.4	0.00	0.00	564.2
6566.4	0.00	0.00	6500.0	-633.2	-448.0	1.00	180.00	642.5
10068.4	0.00	0.00	10002.0	-633.2	-448.0	0.00	0.00	642.5
10968.4	90.00	179.62	10575.0	-1206.1	-444.2	10.00	179.62	1215.2
26040.2	90.00	179.62	10575.0	-16277.6	-343.5	0.00	0.00	16281.2

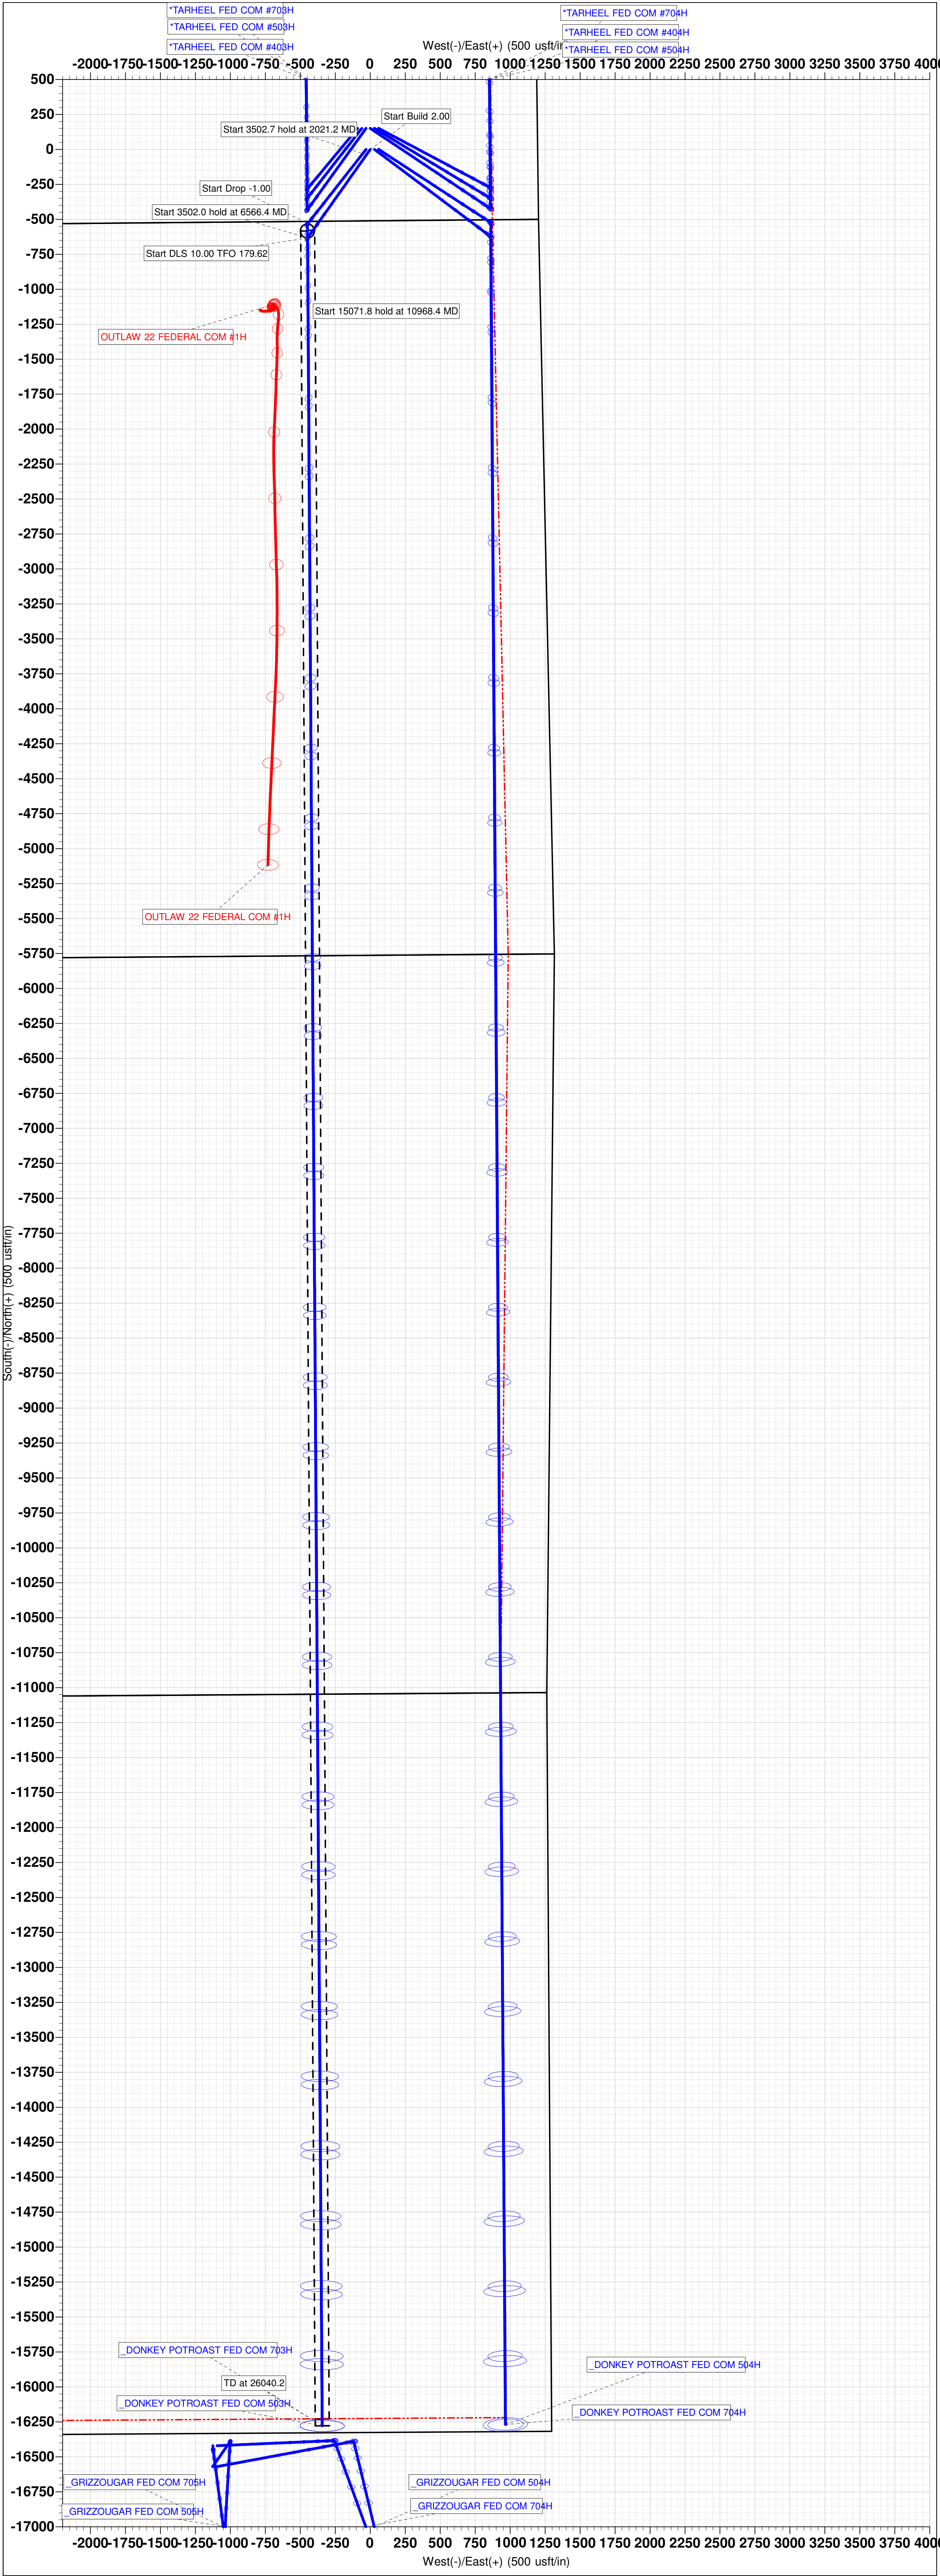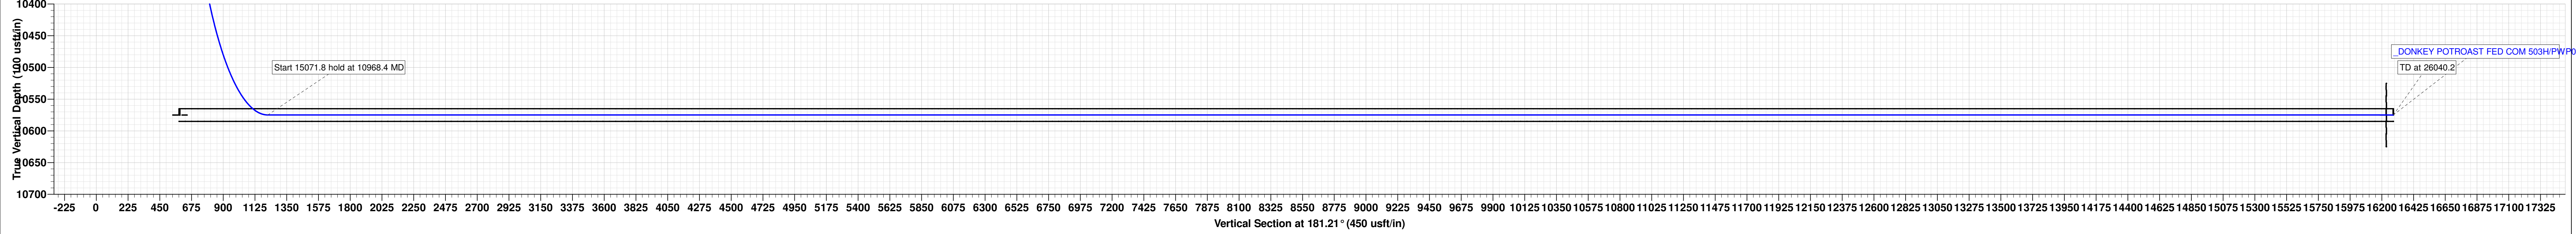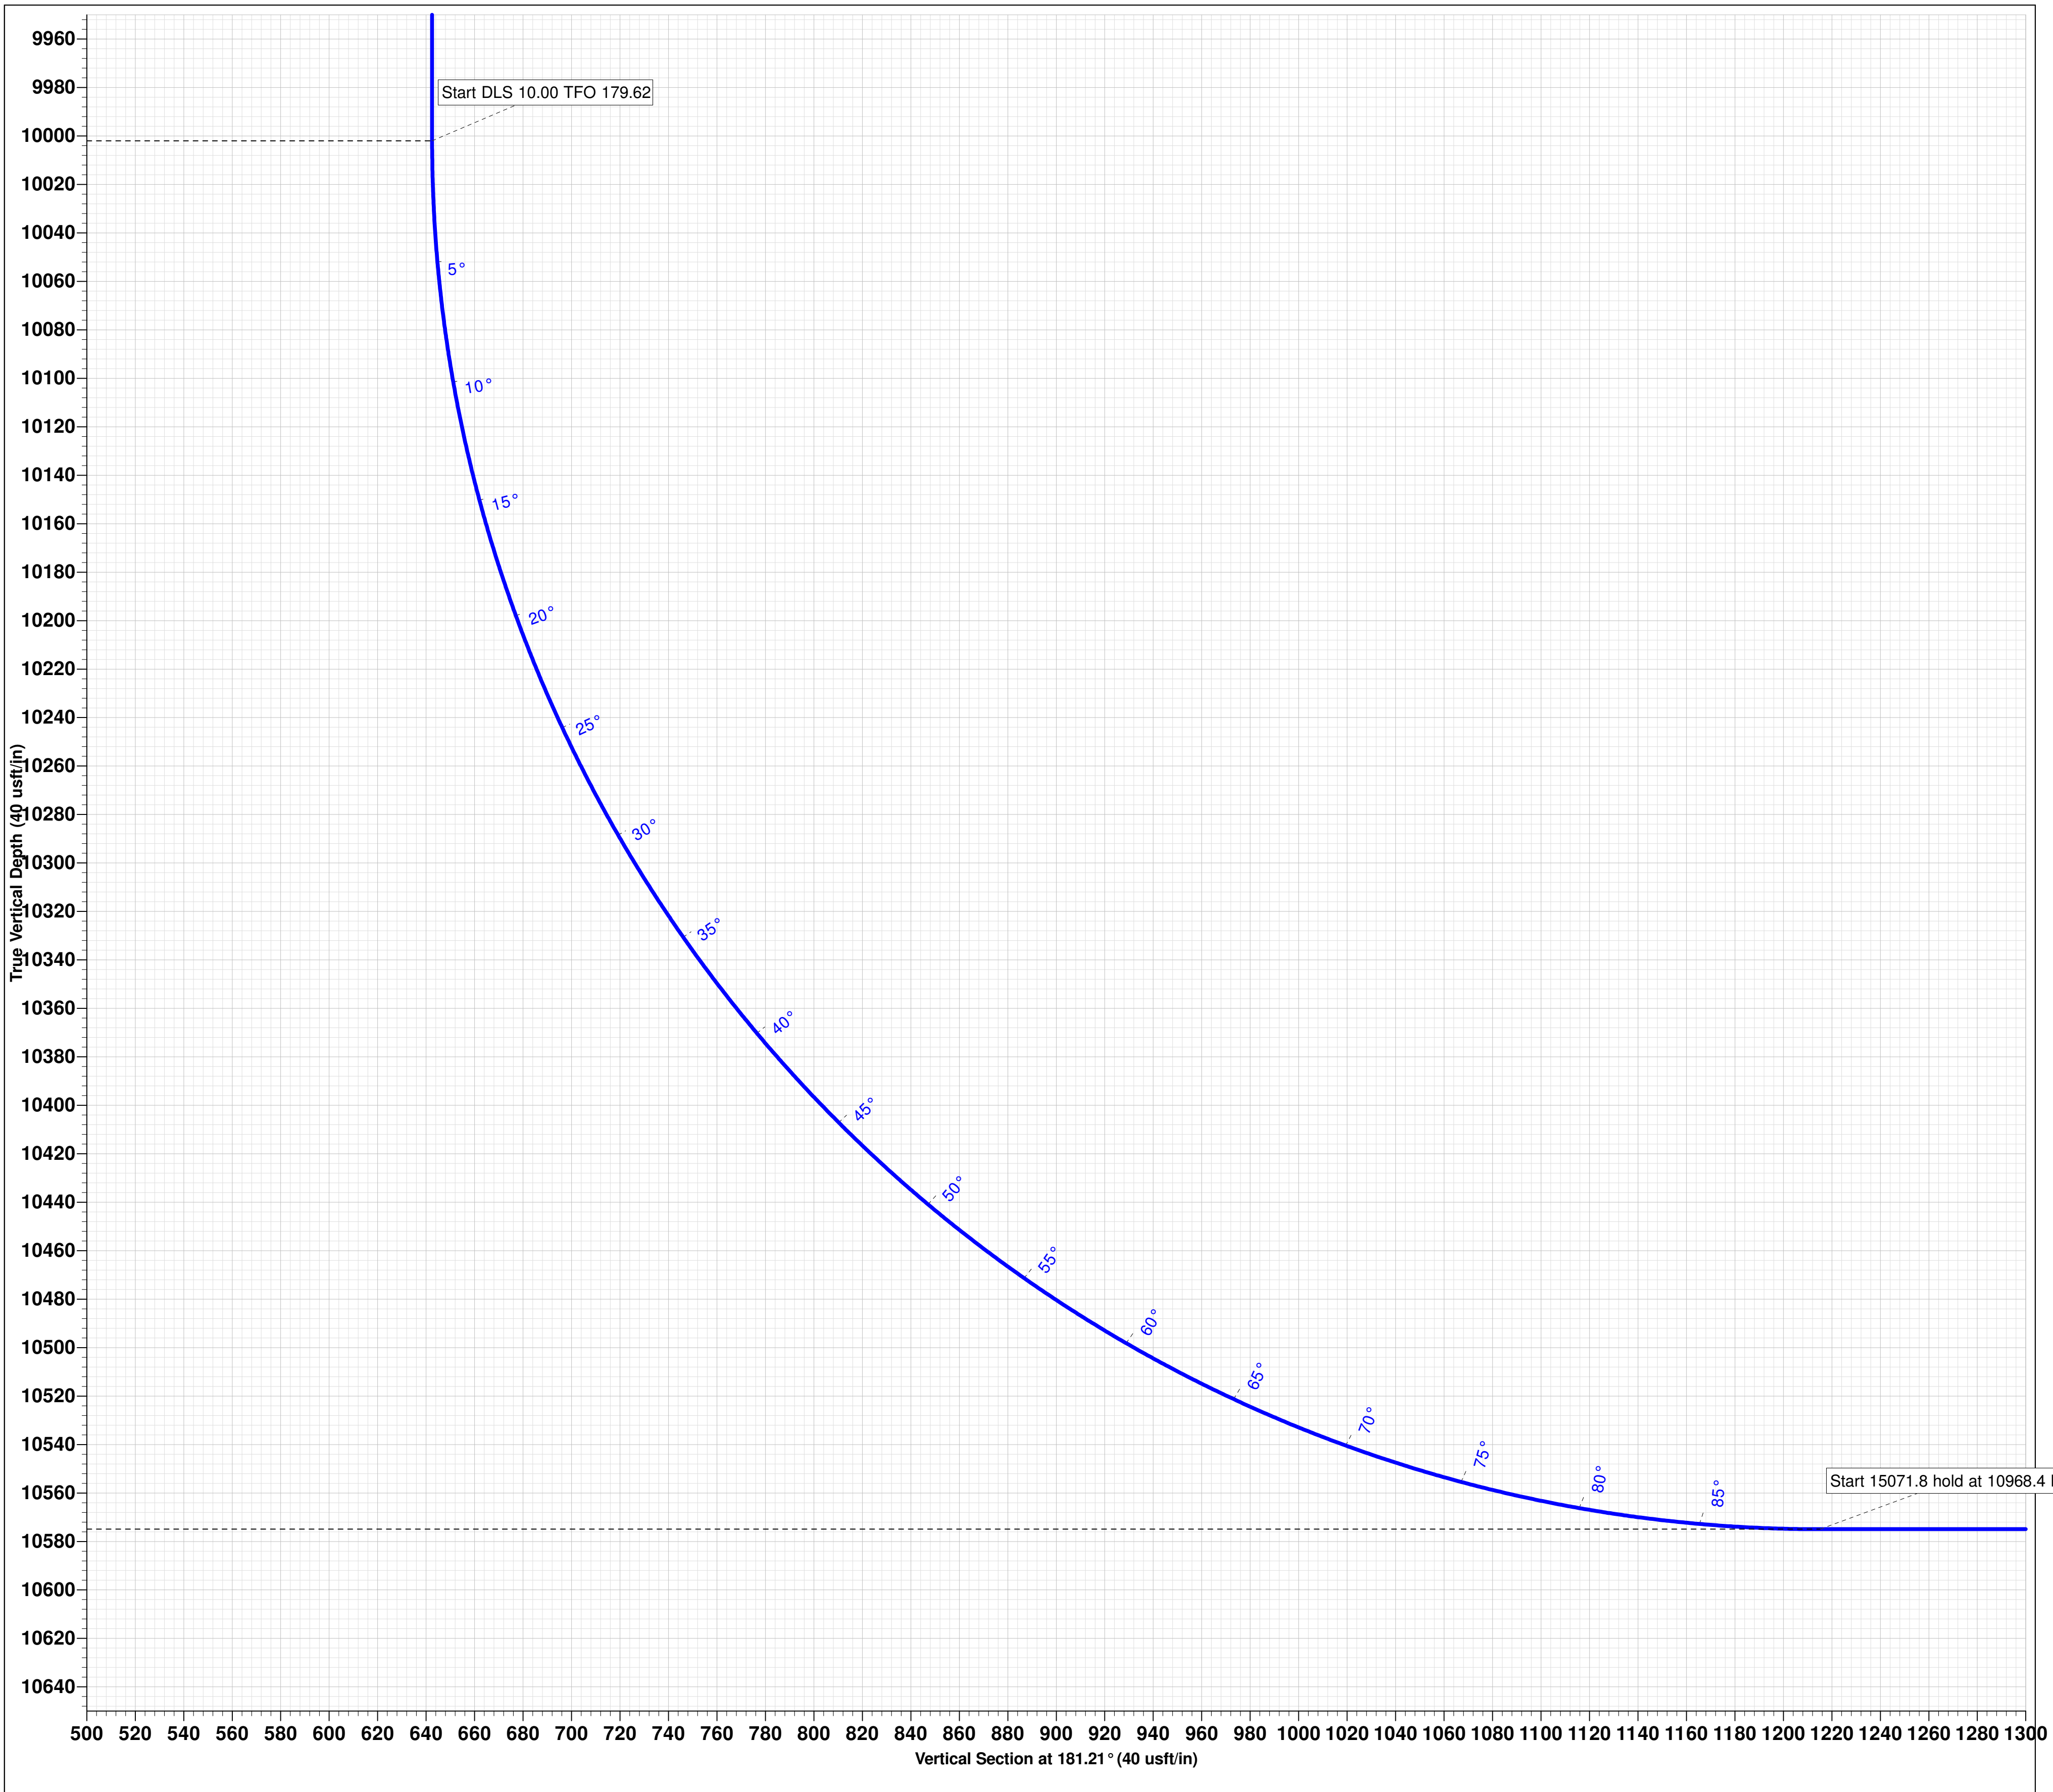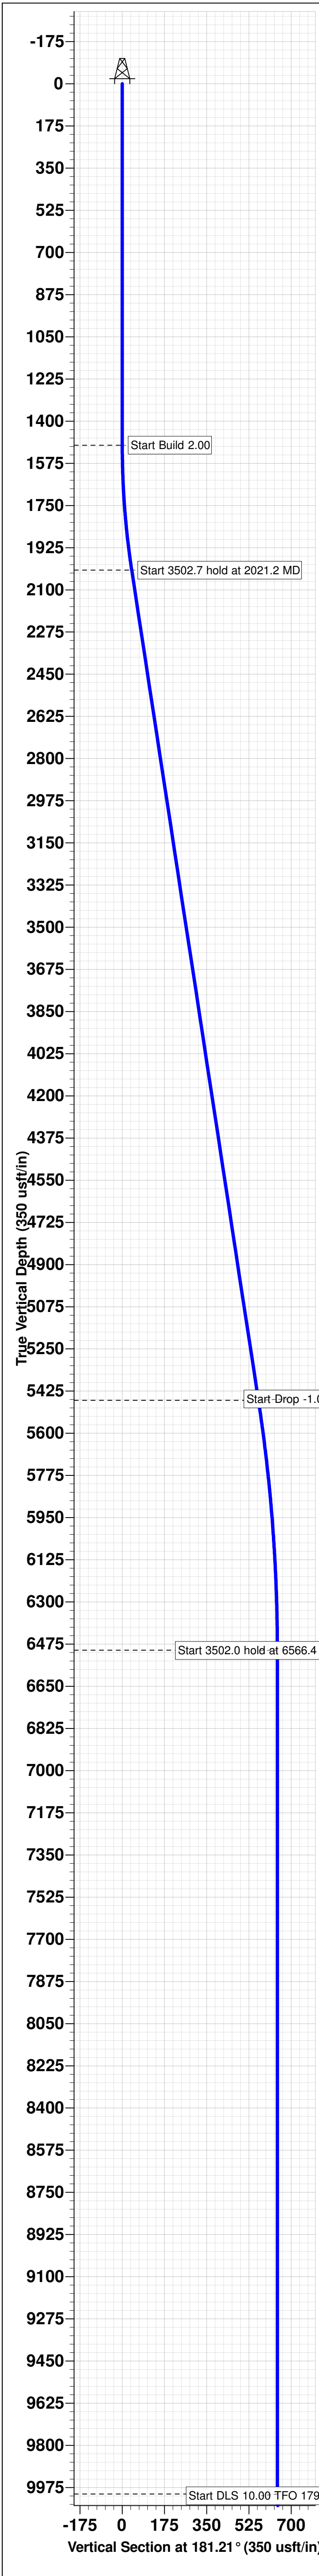

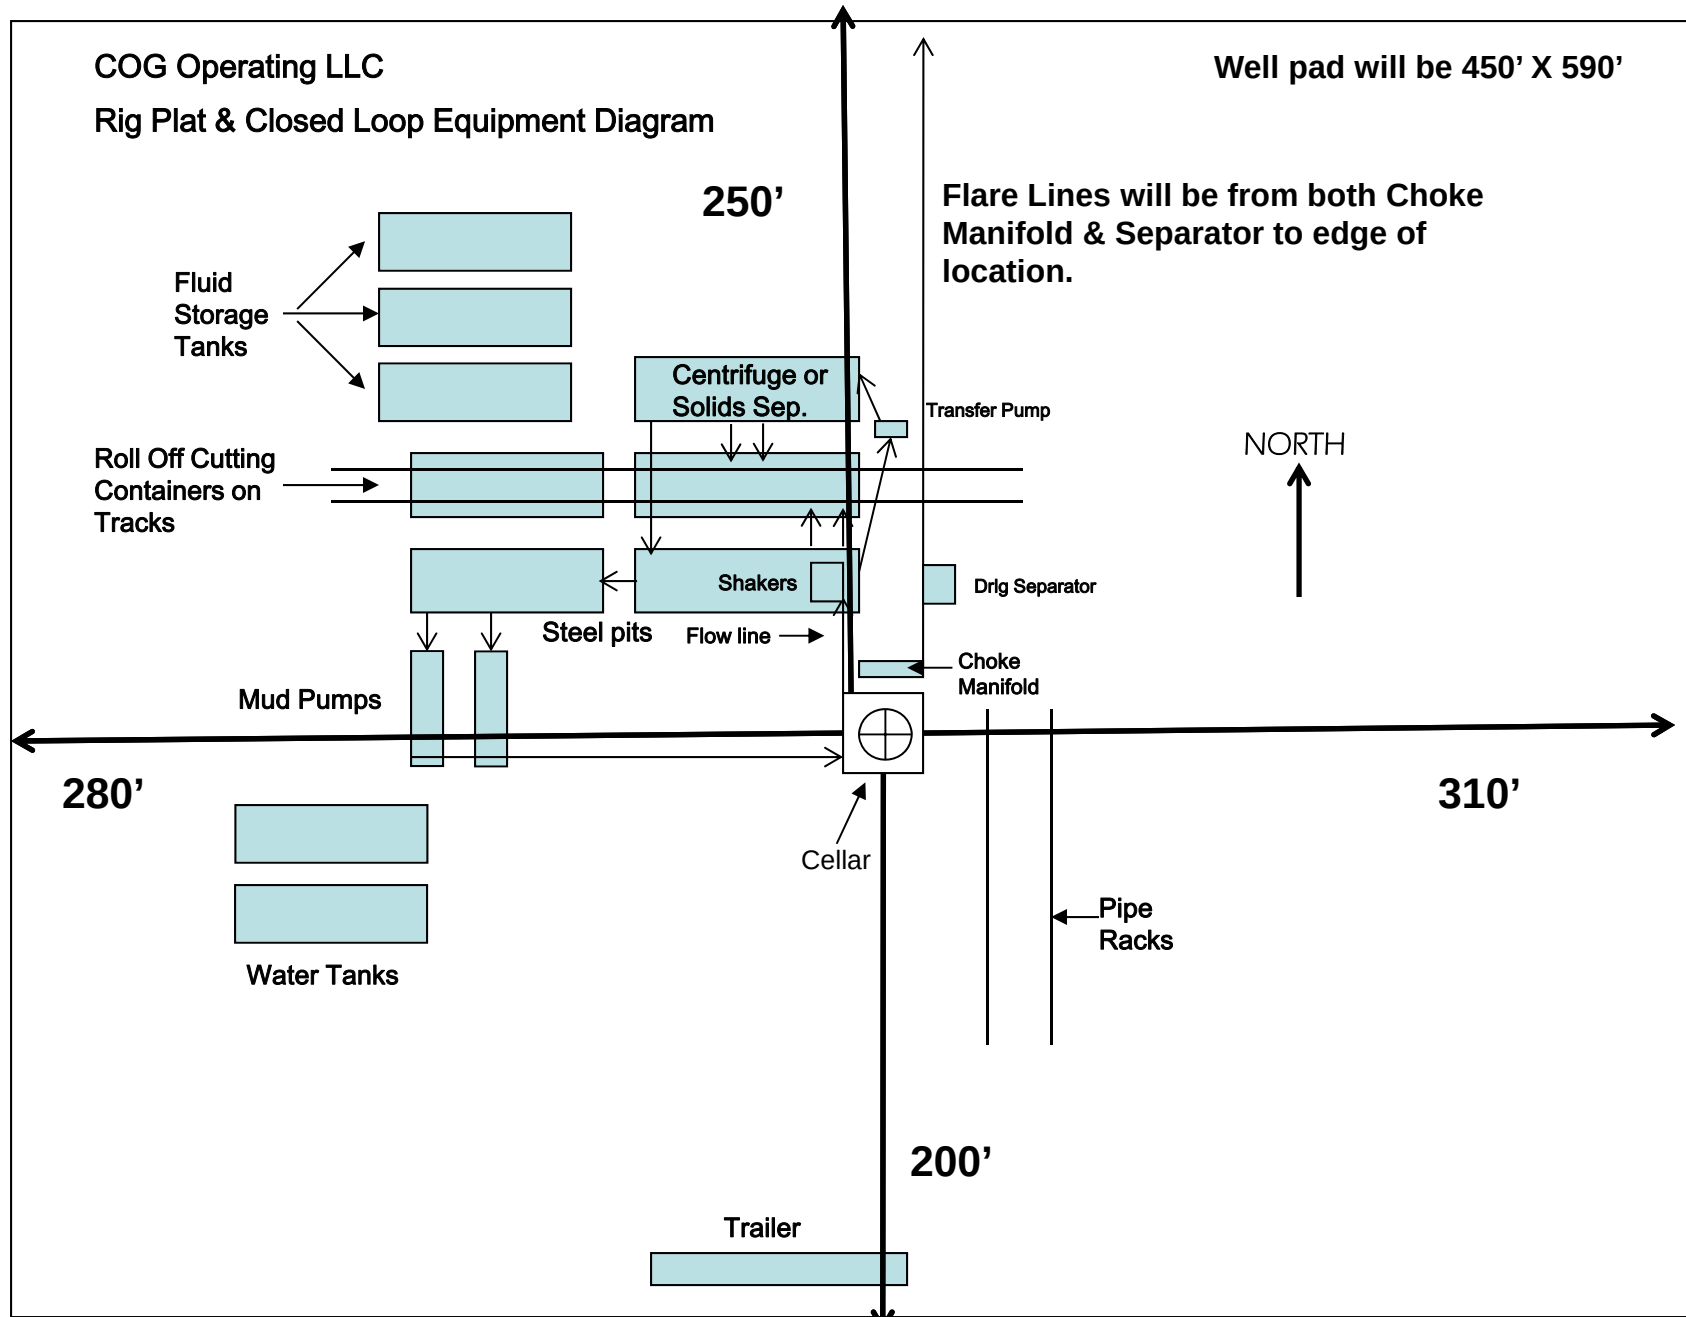


Exhibit 1

"I further certify that COG will comply with Rule 19.15.17 NMAC by using a Closed Loop System."

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit Electronically
Via E-permitting

NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description

Effective May 25, 2021

I. Operator: COG Operating LLC

OGRID: 229137

Date: 08/26/2024

II. Type: ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Donkey Potroast Federal Com 503H	30-025-	P-15-20S-33E	480 FSL & 1185 FEL	± 1687	± 1510	± 4527
Donkey Potroast Federal Com 504H	30-025-	P-15-20S-33E	480 FSL & 1155 FEL	± 1687	± 1510	± 4527
Donkey Potroast Federal Com 703H	30-025-	P-15-20S-33E	480 FSL & 1215 FEL	± 1680	± 2071	± 4785
Donkey Potroast Federal Com 704H	30-025-	P-15-20S-33E	480 FSL & 1125 FEL	± 1680	± 2071	± 4785

IV. Central Delivery Point Name: 22 C CTB NENE 22-20S-33E [See 19.15.27.9(D)(1) NMAC]

V. Anticipated Schedule: Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Donkey Potroast Federal Com	Pending	± 06/01/2025	± 25 days from spud	TBD	TBD	TBD
503H, 504H, 703H, 704H,						

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

VII. Operational Practices: ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

VIII. Best Management Practices: ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices


1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name: Stan Wagner
Title: Regulatory Advisor
E-mail Address: stan.s.wagner@conocophillips.com
Date: 08/29/2024
Phone: 432-253-9685
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)
Approved By:
Title:
Approval Date:
Conditions of Approval:

VI. Separation Equipment

How Operator will size separation equipment to optimize gas capture:

All ConocoPhillips production facility equipment will be sized per industry standards (API 12J) with adequate retention time to effectively separate all phases of production. Each project will take into consideration the number of wells and type curves for each formation pool to ensure adequate facility capacity. Design considerations will also include review of all piping, tanks, VRU's and associated equipment to ensure optimized gas capture minimized risk of release.

VII. Operational Practices

Actions Operator will take to comply with the requirements below:

B. Drilling Operations

- During drilling, flare stacks will be located a minimum of 100 feet from the nearest surface hole location. All gas is captured or combusted. If an emergency or malfunction occurs, gas will be flared or vented for public health, safety, and the environment and be properly reported to the NMOCD pursuant to 19.15.27.8.G.
- Measure or estimate the volume of natural gas that is vented, flared or beneficially used during drilling, completion and production operations, regardless of the reason or authorization for such venting or flaring.

C. Completion Operations

- During completion operations, operator does not produce oil or gas but maintains adequate well control through completion operations.
- Individual well test separators will be set to properly separate gas and liquids. A temporary test separator will be utilized initially to process volumes. In addition, separators will be tied into flowback tanks which will be tied into the gas processing equipment for sales down a pipeline.

D. Venting and flaring during production operations

- During each phase of well life (drilling, completion and production) of a ConocoPhillips well, COP personnel will follow all necessary procedures to ensure both the operation and the equipment are within the NMAC 19.15.27.8 Subsection D guidelines.
- During well operations that require unloading of the well to atmospheric pressure, all reasonable actions will be taken to minimize vented gas
- Through the life of the well all flaring shall be measured, and venting events quantified using the data available and industry best practice.

E. Performance standards for separation, storage tank and flare equipment

- All storage tanks and separation equipment are designed minimize risk of liquid or vapor release and optimize gas capture. This includes automation for automatic gauging and pressure monitoring.

- All flare stacks are equipped with auto ignition devices and/or continuous pilots and are designed to operate at maximum combustion efficiency pursuant NMAC 19.15.27.8 Subsection E. Flares will follow COP spacing guidelines to ensure they are a safe distance from combustibles and operations equipment.
- COP personnel will conduct routine AVO inspections on a regular basis per NMAC 19.15.27.8 Subsection E guidelines.

F. Measurement of vented and flared natural gas.

- Measurement equipment will be installed to quantify gas flared during drilling, completion and production of the well.
- All measurement devices installed will meet accuracy ratings per AGA and API standards.
- Measurement devices will be installed without manifolds that allow diversion of gas around the metering element, except for the sole purpose of inspection of servicing the measurement device.

VIII. Best Management Practices



- Operator will curtail or shut in production, within reasonable limits, during upset conditions to minimize venting and flaring.
- When feasible, Operator will use equipment to capture gas that would otherwise be vented or flared.
- During completions and production operations Operator will minimize blowdowns to atmosphere
- When feasible, Operator will use electric or air actuated equipment to reduce bleed emissions

Waste Minimization Plan



Per § 3162.3-1 Drilling applications and plans. Part J:

- (1) The anticipated initial oil production rate from the oil well and the anticipated production decline over the first 3 years of production.
 - a. See attached Anticipated Production & Decline Curve
- (2) The anticipated initial oil-well gas production rate from the oil well and the anticipated production decline over the first 3 years of production.
 - a. See attached Anticipated Production & Decline Curve
- (3) Certification that the operator has a valid, executed gas sales contract to sell to a purchaser 100 percent of the produced oil-well gas, less gas anticipated for use on-lease pursuant to 43 CFR subpart 3178.
 - a. See attached NMOCD – Natural Gas Management Plan
- (4) Any other information demonstrating the operator's plans to avoid the waste of gas production from any source, including, as appropriate, from pneumatic equipment, storage tanks, and leaks.
 - a. This location will comply with NSPS OOOOb which will include reduced associated gas flaring, non-emitting pneumatic equipment, storage tanks that are controlled and a rigorous leak detection and repair program. In addition, this facility complies with 20.2.50 NMAC (Ozone Precursor Pollutants) which also imposes standards on pneumatic equipment, tank controls, and leak detection and repair. Finally, this facility must comply with 19.15.27 NMAC (Venting and Flaring of Natural Gas) which significantly reduces instances of flaring.


Anticipated Production Decline Curve

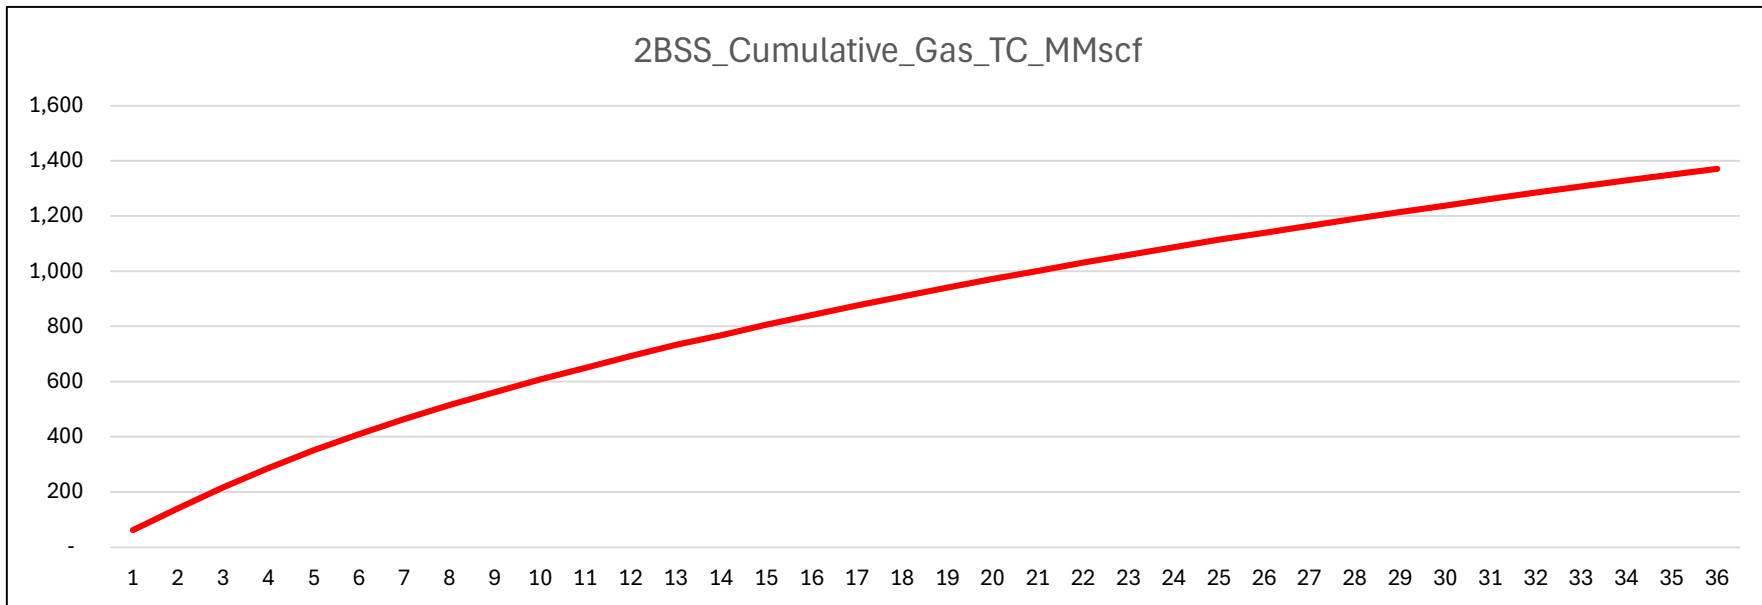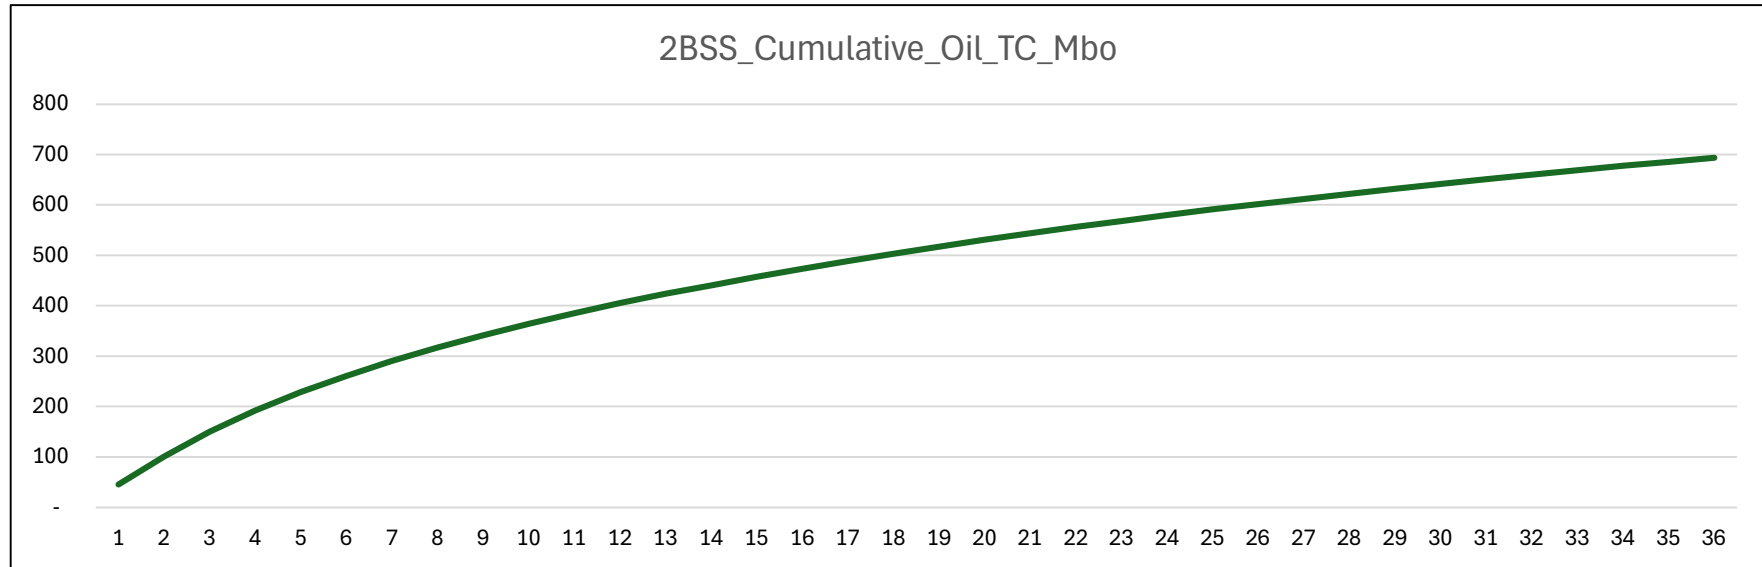

Anticipated Production Decline Curve

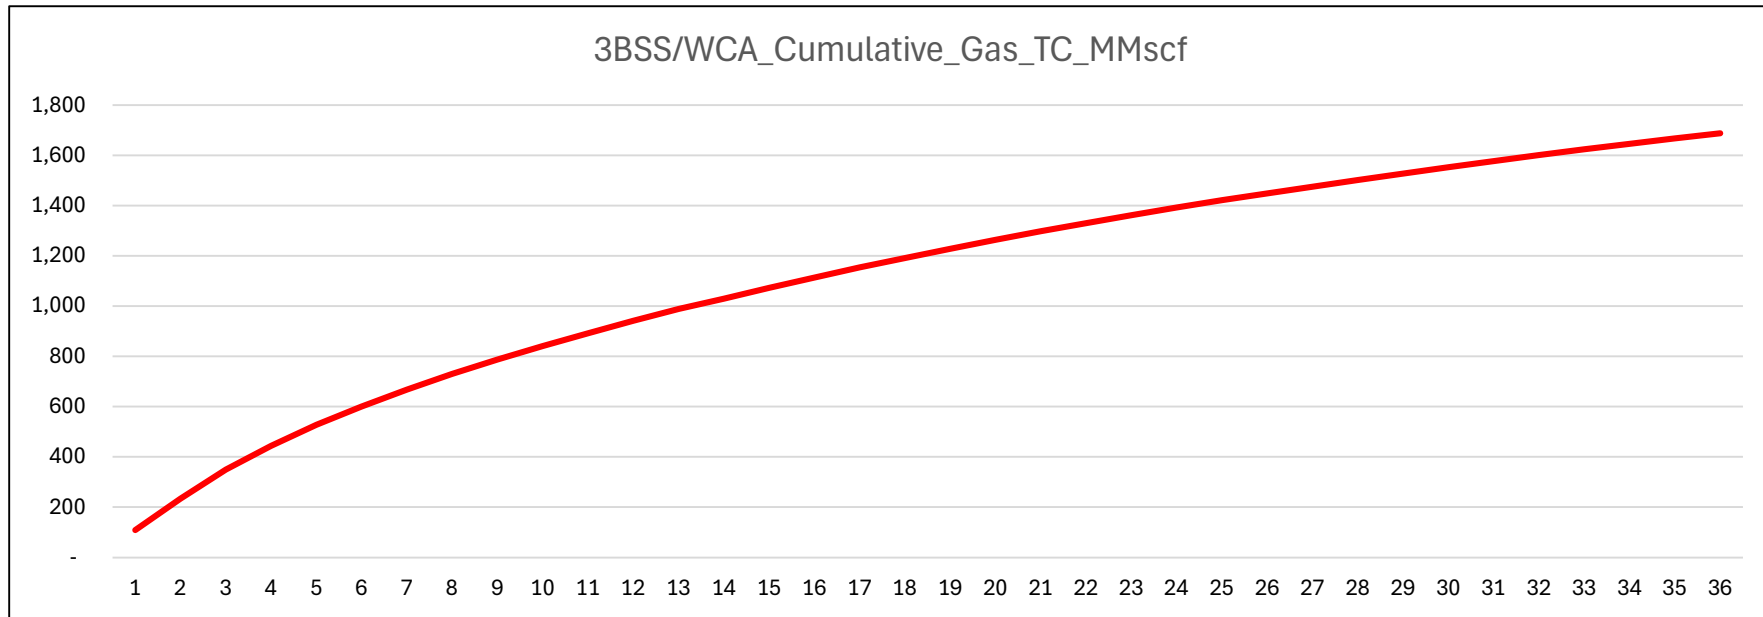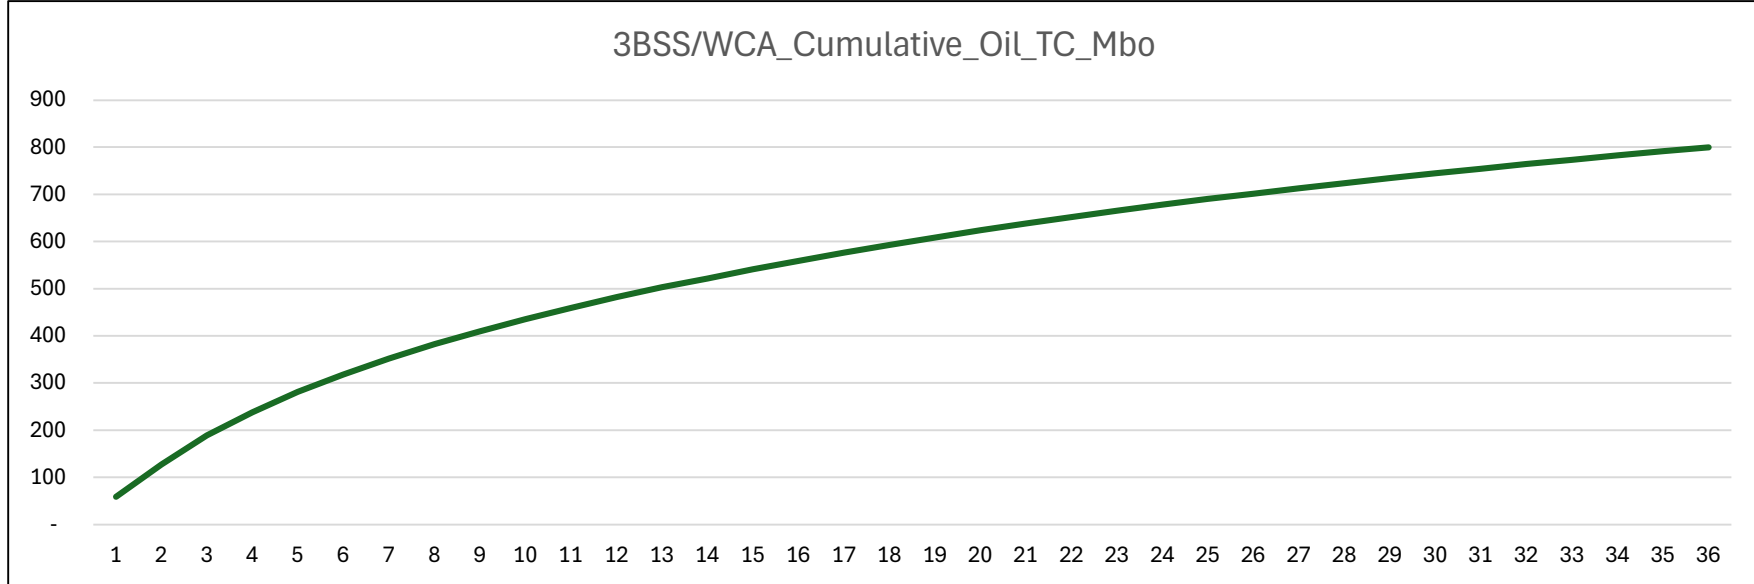

4-String Design – Open 1st Int x 2nd Int Annulus (ICP 2 below relief zone)

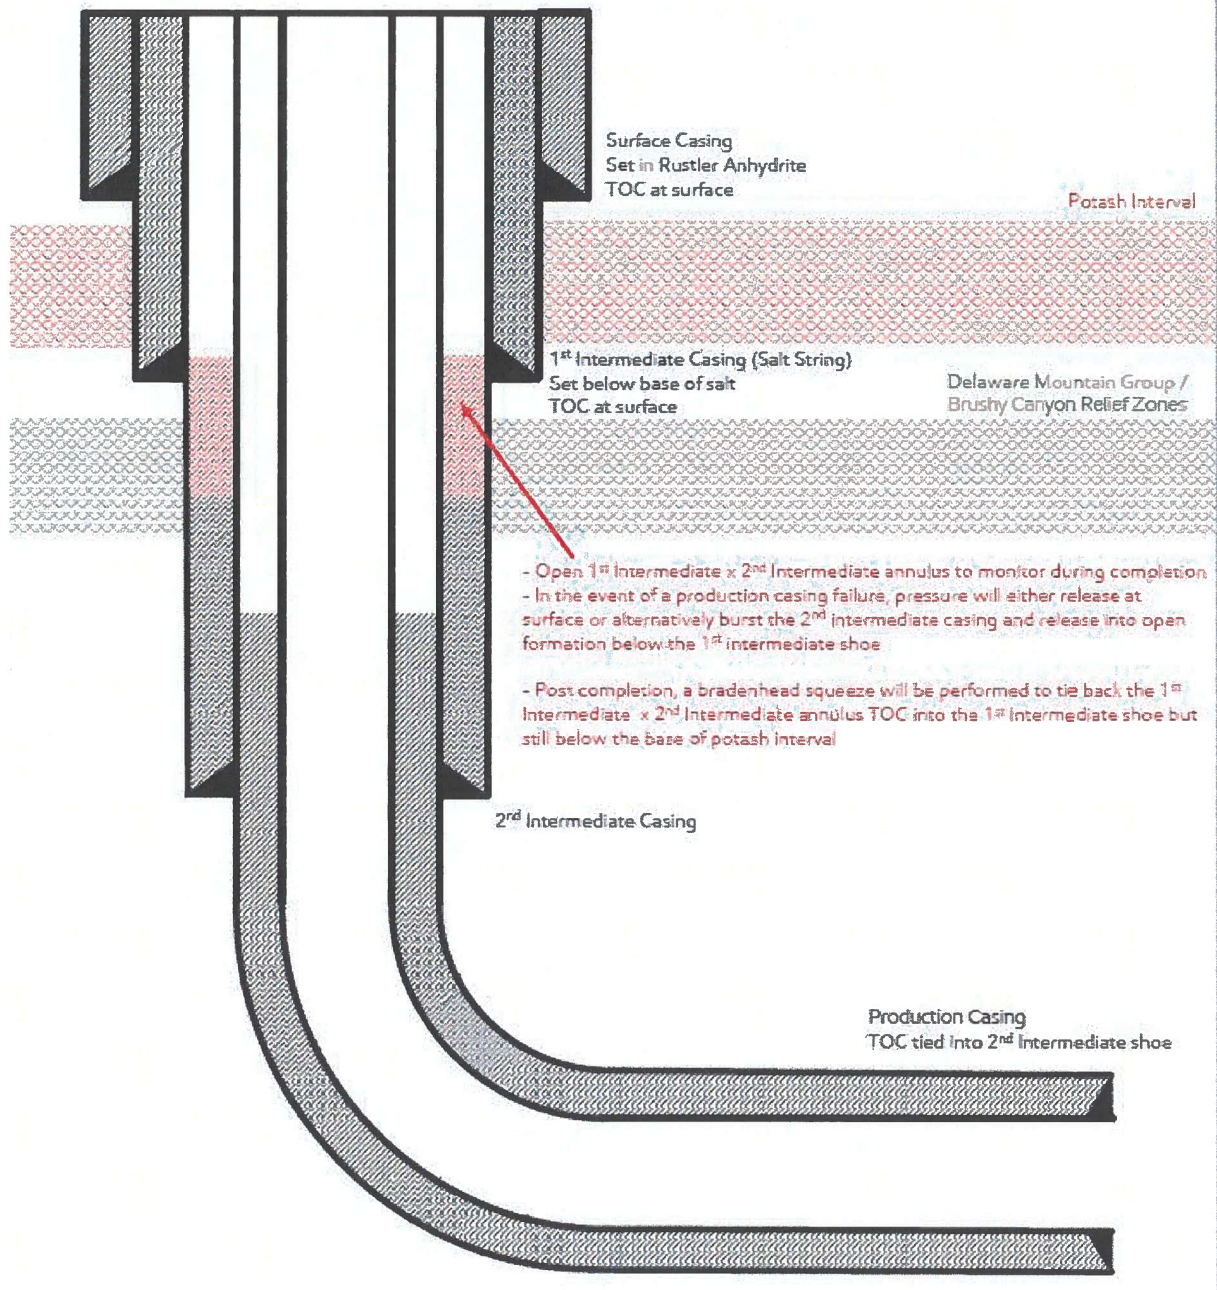

[Figure D] 4 String – Uncemented annulus between 1st and 2nd Intermediate casing strings

ConocoPhillips is aware of R111Q order update and proposed well complies with the requirements in the order

Uses above figure from R111Q as design

All casing ran will be new that meets API standards

Fluids will be diverted away from the salt interval via the open 1st intermediate x 2nd intermediate annulus in case of production casing failure and the annulus will be monitored during frac

As in above schematic, Intermediate 2 cement and production cement will not be brought to surface (0% excess on intermediate 2 with TOC 1000' below previous shoe, 10% excess on production with enough to tie back 1000' into previous casing)

Completions will Bradenhead 1st intermediate x 2nd intermediate annulus within 180 days of frac tying back at minimum 500' into previous casing but not above Marker Bed 126

No anticollision risks < 1.5 SF will be present in salt interval

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	COG OPERATING LLC
WELL NAME & NO.:	DONKEY POTROAST FED COM 503H
SURFACE HOLE FOOTAGE:	480'S & 1185'E
BOTTOM HOLE FOOTAGE:	50'S & 1640'E
LOCATION:	Section 15, T.20 S., R.33 E., NMP
COUNTY:	Lea County, New Mexico

COA

H ₂ S	☐ No	☒ Yes
Potash / WIPP	☐ None ☐ Secretary ☒ R-111-Q ☐ Open Annulus	☐ WIPP
	5-String Design: Open 2nd Int x 3rd Int Annulus (ICP 2 below Relief Zone)	
Cave / Karst	☒ Low ☐ Medium ☐ High ☐ Critical	
Wellhead	☐ Conventional ☒ Multibowl ☐ Both ☐ Diverter	
Cementing	☐ Primary Squeeze ☐ Cont. Squeeze ☒ EchoMeter ☐ DV Tool	
Special Req	☒ Capitan Reef ☐ Water Disposal ☒ COM ☐ Unit	
Waste Prev.	☐ Self-Certification ☒ Waste Min. Plan ☐ APD Submitted prior to 06/10/2024	
Additional Language	☒ Flex Hose ☒ Casing Clearance ☐ Pilot Hole ☒ Break Testing	
	☒ Five-String ☐ Offline Cementing ☒ Fluid-Filled	

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H₂S) Drilling Plan shall be activated AT SPUD. As a result, the Hydrogen Sulfide area must meet 43 CFR part 3170 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

APD is within the R-111-Q defined boundary. Operator must follow all procedures and requirements listed within the updated order.

B. CASING

1. The **20** inch surface casing shall be set at approximately **1465 feet per BLM Geologist** (a minimum of 25 feet (Lea County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping

- cement and ideally between 8-10 hours after completing the cement job.
- b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or **500 pounds compressive strength**, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
- **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

2. The **13-3/8** inch intermediate 1 casing shall be set at approximately **3575 feet per BLM Geologist**. The minimum required fill of cement behind the **13-3/8** inch intermediate 1 casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
 - **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

3. Intermediate 2 should be set prior to entering Delaware group to facilitate monitoring during hydraulic fracturing, and post-frac bradenhead cementing. The **9-5/8** inch intermediate 2 casing shall be set at approximately **5135 feet**. The minimum required fill of cement behind the **9-5/8** inch intermediate 2 casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
 - **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**
4. The minimum required fill of cement behind the **7-5/8** inch intermediate 3 casing is:

(Primary + Post Frac Bradenhead):

- **A monitored open annulus will be incorporated during completion by leaving the Intermediate 2 x Intermediate 3 annulus un-cemented and monitored inside the Intermediate String.** Operator must follow monitoring requirements listed within R-111-Q. Tieback requirements shall be met within **180 days**.

Operator has proposed to pump down **intermediate 2 x intermediate 3** annulus post completion. **Operator must run Echo-meter to verify Cement Slurry/Fluid top in the annulus OR operator shall run a CBL from TD of the intermediate 2/intermediate 3 casing to surface after the second stage BH to verify TOC.** Submit results to the BLM. No displacement fluid/wash out shall be utilized at the top of the cement slurry during second stage bradenhead when running Echo-meter if cement is required to surface. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.

Operator has proposed an open annulus completion in R-111-Q. Operator shall provide a method of verification pre-completion top of cement. **Submit results to the BLM. Pressure monitoring device and Pressure Safety Valves must be installed at surface on both the intermediate annulus and the production annulus for the life of the well.**

In the event of a casing failure during completion, the operator must contact the BLM at (575-706-2779) and (575-361-2822 Eddy County).

- **After bradenhead mentioned above Cement should tie-back 500 feet or 50 feet on top of the Capitan Reef, whichever is closer to surface into the previous casing but not higher than USGS Marker Bed No. 126. Operator must verify top of cement per R-111-Q requirements.** Submit results to the BLM. If cement does not circulate, contact the appropriate BLM office. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
- **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

5. The minimum required fill of cement behind the 5-1/2 inch production casing is:

- **Cement should tie-back 500 feet into the previous casing but not higher than USGS Marker Bed No. 126. Operator must verify top of cement per R-111-Q requirements.** Submit results to the BLM. If cement does not circulate, contact the appropriate BLM office. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**

- **Cement excess is less than 25%, more cement is required if washout occurs. Adjust cement volume and excess based on a fluid caliper or similar method that reflects the as-drilled size of the wellbore.**

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
2. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the **20** inch surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 3500 (70% Working Pressure) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in 43 CFR 3171 and 3172.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.

- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

BOPE Break Testing Variance

- BOPE Break Testing is ONLY permitted for intervals utilizing a 5M BOPE or less. **(Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP.)**
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer **(575-706-2779)** prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted (575-689-5981 Lea County) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per **43 CFR 3172**.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

Casing Clearance

- **The W441 connection should tie back 500'+ into the W513 intermediate casing for clearance overlap.**

Operator shall clean up cycles until wellbore is clear of cuttings and any large debris, ensure cutting sizes are adequate "coffee ground or less" before cementing.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

Contact Petroleum Engineering Inspection Staff:

☒ Eddy County

EMAIL or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
BLM_NM_CFO_DrillingNotifications@BLM.GOV
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240,

(575) 689-5981

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - i. Notify the BLM when moving in and removing the Spudder Rig.
 - ii. Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - iii. BOP/BOPE test to be conducted per **43 CFR 3172** as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. For intervals in which cement to surface is required, cement to surface should be verified with a visual check and density or pH check to differentiate cement from spacer and drilling mud. The results should be documented in the driller's log and daily reports.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.

3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-Q potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR 3172**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - i. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - ii. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - iii. Manufacturer representative shall install the test plug for the initial BOP test.
 - iv. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
 - v. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - i. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - ii. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
 - iii. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an

independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- iv. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- v. The results of the test shall be reported to the appropriate BLM office.
- vi. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- vii. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- viii. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR 3172**.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JS 11/20/2024

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 450254

CONDITIONS

Operator: COG OPERATING LLC 600 W Illinois Ave Midland, TX 79701	OGRID: 229137
	Action Number: 450254
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
stanwagner	Cement is required to circulate on both surface and intermediate1 strings of casing.	4/9/2025
stanwagner	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	4/9/2025
matthew.gomez	Administrative order required for non-standard spacing unit prior to production.	5/3/2025
matthew.gomez	Notify the OCD 24 hours prior to casing & cement.	5/3/2025
matthew.gomez	A [C-103] Sub. Drilling (C-103N) is required within (10) days of spud.	5/3/2025
matthew.gomez	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	5/3/2025
matthew.gomez	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	5/3/2025
matthew.gomez	File As Drilled C-102 and a directional Survey with C-104 completion packet.	5/3/2025
matthew.gomez	This well is within the R-111-Q defined boundary. Operator must follow all procedures and requirements listed within the order.	5/3/2025
matthew.gomez	This well is within the Capitan Reef. The first intermediate casing string shall be sat and cemented back to surface immediately above the Capitan Reef. The second intermediate string shall be set and cemented back to surface immediately below the base of the Capitan Reef.	5/3/2025
matthew.gomez	Brine water shall not be used in the Capitan Reef. Only fresh water shall be utilized until the Capitan Reef is cased and cemented.	5/3/2025
