

Form 3160-3  
(June 2015)FORM APPROVED  
OMB No. 1004-0137  
Expires: January 31, 2018

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
**APPLICATION FOR PERMIT TO DRILL OR REENTER**

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone			5. Lease Serial No. <b>NMNM103597</b> 6. If Indian, Allottee or Tribe Name  7. If Unit or CA Agreement, Name and No.  8. Lease Name and Well No.  <b>COORS FED COM</b>  <b>213H</b>
2. Name of Operator <b>TAP ROCK OPERATING LLC</b>			9. API Well No. <b>30-015-56869</b>
3a. Address <b>602 PARK POINT DRIVE SUITE 200, GOLDEN, CO 8040</b>		3b. Phone No. (include area code) <b>(720) 460-3316</b>	10. Field and Pool, or Exploratory <b>PURPLE SAGE/WOLFCAMP</b>
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface <b>SWSW / 933 FSL / 1297 FWL / LAT 32.0230655 / LONG -104.3193838</b> At proposed prod. zone <b>NWNE / 5 FNL / 1650 FEL / LAT 32.0497811 / LONG -104.3289342</b>			11. Sec., T. R. M. or Blk. and Survey or Area <b>SEC 20/T26S/R26E/NMP</b>
14. Distance in miles and direction from nearest town or post office* <b>11 miles</b>		12. County or Parish <b>EDDY</b>	13. State <b>NM</b>
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) <b>933 feet</b>	16. No of acres in lease  	17. Spacing Unit dedicated to this well  <b>1280.0</b>	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. <b>25 feet</b>	19. Proposed Depth <b>8293 feet / 19093 feet</b>	20. BLM/BIA Bond No. in file <b>FED: NMB105800930</b>	
21. Elevations (Show whether DF, KDB, RT, GL, etc.) <b>3462 feet</b>	22. Approximate date work will start* <b>11/01/2025</b>	23. Estimated duration <b>60 days</b>	
24. Attachments			

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- |   |   |
|---|---|
| 1. Well plat certified by a registered surveyor.<br>2. A Drilling Plan.<br>3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).<br>5. Operator certification.<br>6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature (Electronic Submission)  Title <b>Permitting Agent</b>	Name (Printed/Typed) <b>BRIAN WOOD / Ph: (720) 460-3316</b>	Date <b>09/12/2024</b>
Approved by (Signature) (Electronic Submission)  Title <b>Assistant Field Manager Lands &amp; Minerals</b>	Name (Printed/Typed) <b>CODY LAYTON / Ph: (575) 234-5959</b>	Date <b>05/19/2025</b>
Office <b>Carlsbad Field Office</b>		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

\*(Instructions on page 2)



C-102  Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024	
		Submittal Type:	<input type="checkbox"/> Initial Submittal
			<input checked="" type="checkbox"/> Amended Report
		<input type="checkbox"/> As Drilled	

30-015-56869 WELL LOCATION AND ACREAGE DEDICATION PLAT

API Number <del>30-025</del>	Pool Code 98220	Pool Name PURPLE SAGE; WOLFCAMP (GAS)
Property Code 337360	Property Name COORS FED COM	Well Number 213H
OGRID No. #372043	Operator Name TAP ROCK OPERATING, LLC.	Ground Level Elevation 3462'
Surface Owner: <input type="checkbox"/> State <input checked="" type="checkbox"/> Fee <input type="checkbox"/> Tribal <input type="checkbox"/> Federal		Mineral Owner: <input type="checkbox"/> State <input checked="" type="checkbox"/> Fee <input type="checkbox"/> Tribal <input checked="" type="checkbox"/> Federal

Surface Location

UL or lot no. M	Section 20	Township 26-S	Range 26-E	Lot Idn -	Feet from the N/S 933' S	Feet from the E/W 1297' W	Latitude N 32.0230655	Longitude W 104.3193838	County EDDY
--------------------	---------------	------------------	---------------	--------------	-----------------------------	------------------------------	--------------------------	----------------------------	----------------

Bottom Hole Location

UL or lot no. B	Section 18	Township 26-S	Range 26-E	Lot Idn -	Feet from the N/S 5' N	Feet from the E/W 1650' E	Latitude N 32.0497811	Longitude W 104.3289342	County EDDY
--------------------	---------------	------------------	---------------	--------------	---------------------------	------------------------------	--------------------------	----------------------------	----------------

Dedicated Acres 1280	Infill or Defining Well Infill	Defining Well API 214H (30-015-xxxxx)	Overlapping Spacing Unit (Y/N) N	Consolidated Code C
Order Numbers			Well Setbacks are under Common Ownership: <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	

Kick Off Point (KOP)

UL or lot no. O	Section 19	Township 26-S	Range 26-E	Lot Idn -	Feet from the N/S 50' S	Feet from the E/W 1650' E	Latitude N 32.0206528	Longitude W 104.3288897	County EDDY
--------------------	---------------	------------------	---------------	--------------	----------------------------	------------------------------	--------------------------	----------------------------	----------------



First Take Point (FTP)

UL or lot no. O	Section 19	Township 26-S	Range 26-E	Lot Idn -	Feet from the N/S 330' S	Feet from the E/W 1650' E	Latitude N 32.0214225	Longitude W 104.3288909	County EDDY
--------------------	---------------	------------------	---------------	--------------	-----------------------------	------------------------------	--------------------------	----------------------------	----------------

Last Take Point (LTP)

UL or lot no. B	Section 18	Township 26-S	Range 26-E	Lot Idn -	Feet from the N/S 330' N	Feet from the E/W 1650' E	Latitude N 32.0488877	Longitude W 104.3289325	County EDDY
--------------------	---------------	------------------	---------------	--------------	-----------------------------	------------------------------	--------------------------	----------------------------	----------------

Unitized Area or Area of Uniform Interest	Spacing Unity Type <input checked="" type="checkbox"/> Horizontal <input type="checkbox"/> Vertical	Ground Floor Elevation
---	--	------------------------

<b>OPERATOR CERTIFICATION</b> <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief; and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> <i>If this well is a horizontal well, I further certify that this organization has received The consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i>  Signature Cory Walk Date 03-20-25 Print Name cory@permitswest.com E-mail Address		<b>SURVEYORS CERTIFICATION</b> <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision and that the same is true and correct to the best of my belief.</i>  3/4/2025 2:53:28 PM Signature and Seal of Professional Surveyor Date Certificate Number Date of Survey 02/20/2025	
---	--	--	--

C-102

Submit Electronically  
Via OCD PermittingState of New Mexico  
Energy, Minerals & Natural Resources Department  
OIL CONSERVATION DIVISION

Revised July 9, 2024

Submittal  
Type:

- ☐ Initial Submittal
- ☒ Amended Report
- ☐ As Drilled

Property Name and Well Number

COORS FED COM 213H

## SURFACE LOCATION (SHL)

NEW MEXICO EAST  
NAD 1983  
X=545661 Y=372130  
LAT.: N 32.0230655  
LONG.: W 104.3193838  
NAD 1927  
X=504477 Y=372074  
LAT.: N 32.0229450  
LONG.: W 104.3188867  
933' FSL 1297' FWL

## KICK OFF POINT (KOP)

NEW MEXICO EAST  
NAD 1983  
X=542715 Y=371252  
LAT.: N 32.0206528  
LONG.: W 104.3288897  
NAD 1927  
X=501531 Y=371196  
LAT.: N 32.0205324  
LONG.: W 104.3283924  
50' FSL 1650' FEL

## FIRST TAKE POINT (FTP)

NEW MEXICO EAST  
NAD 1983  
X=542714 Y=371532  
LAT.: N 32.0214225  
LONG.: W 104.3288909  
NAD 1927  
X=501531 Y=371476  
LAT.: N 32.0213021  
LONG.: W 104.3283936  
330' FSL 1650' FEL

## FED PERF. POINT (FPP1)

NEW MEXICO EAST  
NAD 1983  
X=542711 Y=373867  
LAT.: N 32.02778400  
LONG.: W 104.3289008  
NAD 1927  
X=501528 Y=373811  
LAT.: N 32.0277198  
LONG.: W 104.3284033  
2662' FNL 1650' FEL

## FED PERF. POINT (FPP2)


NEW MEXICO EAST  
NAD 1983  
X=542708 Y=376529  
LAT.: N 32.0351568  
LONG.: W 104.3289117  
NAD 1927  
X=501524 Y=376472  
LAT.: N 32.0350367  
LONG.: W 104.3284140  
0' FNL 1653' FEL

## LAST TAKE POINT (LTP)

NEW MEXICO EAST  
NAD 1983  
X=542701 Y=381523  
LAT.: N 32.0488877  
LONG.: W 104.3289325  
NAD 1927  
X=501518 Y=381467  
LAT.: N 32.0487678  
LONG.: W 104.3284345  
330' FNL 1650' FEL

## BOTTOM HOLE LOCATION (BHL)

NEW MEXICO EAST  
NAD 1983  
X=542700 Y=381848  
LAT.: N 32.0497811  
LONG.: W 104.3289342  
NAD 1927  
X=501517 Y=381792  
LAT.: N 32.0496613  
LONG.: W 104.3284362  
5' FNL 1650' FEL

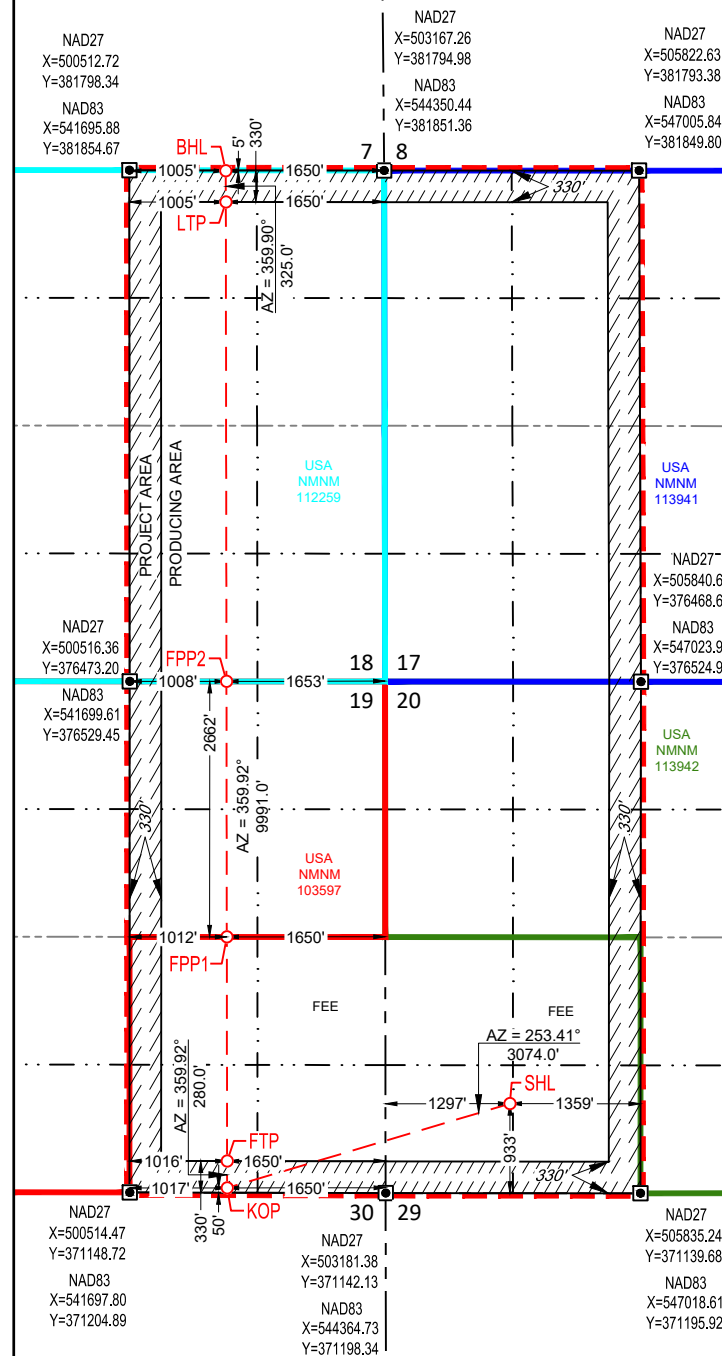

## SURVEYORS CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.  
02/20/2025

Date of Survey


Signature and Seal of Professional Surveyor:



3/4/2025 2:53:28 PM



SECTION 20, TOWNSHIP 26-S, RANGE 26-E, N.M.P.M.  
EDDY COUNTY, NEW MEXICO

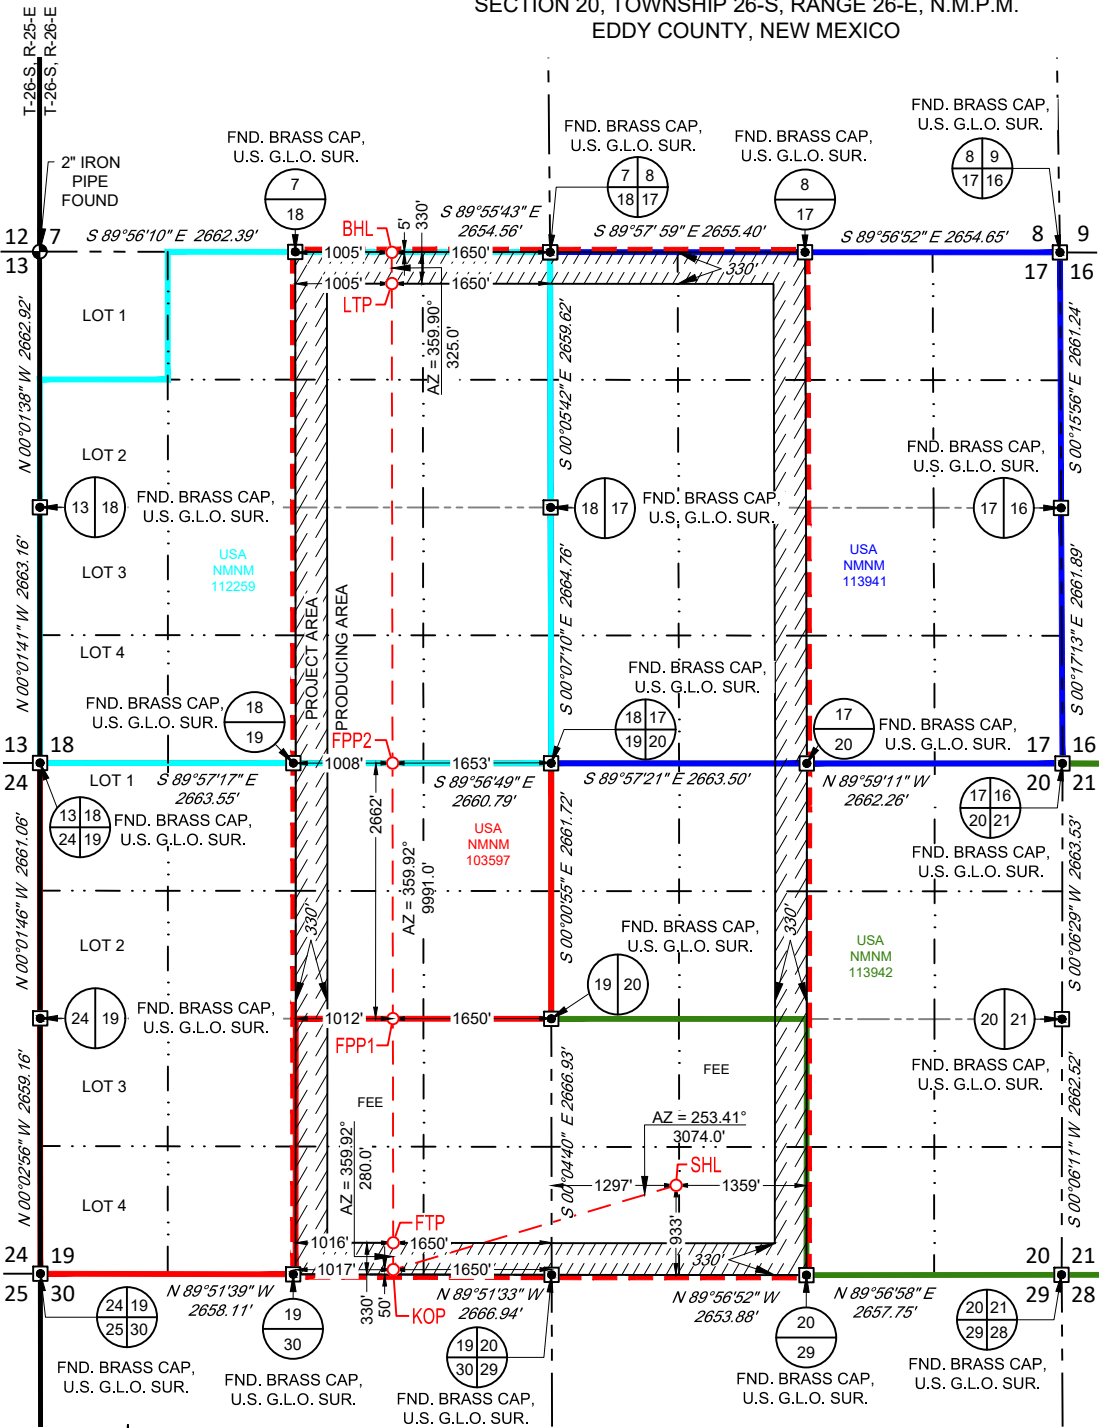

**SURFACE LOCATION (SHL)**  
NEW MEXICO EAST  
NAD 1983  
X=545661 Y=372130  
LAT.: N 32.0230655  
LONG.: W 104.3193838  
933' FSL 1297' FWL

**KICK OFF POINT (KOP)**  
NEW MEXICO EAST  
NAD 1983  
X=542715 Y=371252  
LAT.: N 32.0206528  
LONG.: W 104.3288897  
50' FSL 1650' FEL

**FIRST TAKE POINT (FTP)**  
NEW MEXICO EAST  
NAD 1983  
X=542714 Y=371532  
LAT.: N 32.0214225  
LONG.: W 104.3288909  
330' FSL 1650' FEL

**FED PERF. POINT (FPP1)**  
NEW MEXICO EAST  
NAD 1983  
X=542711 Y=373867  
LAT.: N 32.0278400  
LONG.: W 104.3289008  
2662' FNL 1650' FEL

**FED PERF. POINT (FPP2)**  
NEW MEXICO EAST  
NAD 1983  
X=542708 Y=376529  
LAT.: N 32.0351568  
LONG.: W 104.3289117  
0' FNL 1653' FEL

**LAST TAKE POINT (LTP)**  
NEW MEXICO EAST  
NAD 1983  
X=542701 Y=381523  
LAT.: N 32.0488877  
LONG.: W 104.3289325  
330' FNL 1650' FEL

**BOTTOM HOLE LOCATION (BHL)**  
NEW MEXICO EAST  
NAD 1983  
X=542700 Y=381848  
LAT.: N 32.0497811  
LONG.: W 104.3289342  
5' FNL 1650' FEL


LEASE NAME & WELL NO.: \_\_\_\_\_ COORS FED COM 213H

SECTION 20 TWP 26-S RGE 26-E SURVEY N.M.P.M.  
COUNTY EDDY STATE NM  
DESCRIPTION 933' FSL & 1297' FWL

DISTANCE & DIRECTION  
FROM INT. OF US-180 E/US-62 E AND BLACK ROVER VILLAGE RD., GO  
SOUTHWEST ON US-180 E/US-62 E ±11.9 MILES, THENCE SOUTHEAST  
(LEFT) ON DILLAHUNTY RD. ±10.1 MILES, THENCE EAST (LEFT) ON A  
LEASE RD. ±0.4 MILES, THENCE CONTINUE EAST (LEFT) ON A LEASE RD.  
±200 FEET, THENCE NORTH (LEFT) ON A PROPOSED RD. ±1106 FEET,  
THENCE NORTH (RIGHT) ON A PROPOSED RD. ±361 FEET TO A POINT  
±975 FEET NORTHEAST OF THE LOCATION.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID  
BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY  
FEET.

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND  
UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF  
SURVEY, AND DATA PROVIDED BY TAP ROCK OPERATING, LLC THIS CERTIFICATION IS MADE AND  
LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS  
NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.



3/4/2025 2:53:29 PM

Ramon A. Dominguez, P.S. No. 24508



481 WINSOTT ROAD, Ste. 200 • BENBROOK, TEXAS 76126  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM

State of New Mexico  
Energy, Minerals and Natural Resources Department

Submit Electronically  
Via E-permitting

Oil Conservation Division  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

## NATURAL GAS MANAGEMENT PLAN

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

### Section 1 – Plan Description

Effective May 25, 2021

**I. Operator:** \_\_\_\_\_ Tap Rock Operating LLC \_\_\_\_\_ **OGRID:** \_\_\_\_\_ 372043 \_\_\_\_\_ **Date:** \_\_\_\_\_ 2/20/2025

**II. Type:** ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: \_\_\_\_\_

**III. Well(s):** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	A PI	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
Coors Fed Com 211H		N, 20, 26S, 26E	933' FSL, 1347' FWL	939	3571	5149
Coors Fed Com 212H		N, 20, 26S, 26E	933' FSL, 1372' FWL	939	3571	5149
Coors Fed Com 213H		M, 20, 26S, 26E	933' FSL, 1297' FWL	939	3571	5149
Coors Fed Com 214H		M, 20, 26S, 26E	933' FSL, 1322' FWL	939	3571	5149

**IV. Central Delivery Point Name:** \_\_\_\_\_ Coors Fed Com CDP \_\_\_\_\_ [See 19.15.27.9(D)(1) NMAC]

**V. Anticipated Schedule:** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
Coors Fed Com 211H		12/1/2025	2/20/2026	3/1/2026	4/1/2026	4/1/2026
Coors Fed Com 212H		12/1/2025	2/20/2026	3/1/2026	4/1/2026	4/1/2026
Coors Fed Com 213H		12/1/2025	2/20/2026	3/1/2026	4/1/2026	4/1/2026
Coors Fed Com 214H		12/1/2025	2/20/2026	3/1/2026	4/1/2026	4/1/2026

**VI. Separation Equipment:** ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.

**VII. Operational Practices:** ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.

**VIII. Best Management Practices:** ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.



## **Section 2 – Enhanced Plan**

### **EFFECTIVE APRIL 1, 2022**

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

#### **IX. Anticipated Natural Gas Production:**

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

#### **X. Natural Gas Gathering System (NGGS):**

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

**XI. Map.** ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

**XII. Line Capacity.** The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

**XIII. Line Pressure.** Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

**XIV. Confidentiality:** ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

### **Section 3 - Certifications**

**Effective May 25, 2021**

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

***If Operator checks this box, Operator will select one of the following:***

**Well Shut-In.** ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

**Venting and Flaring Plan.** ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

### **Section 4 - Notices**

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature: 
Printed Name: Bill Ramsey
Title: Sr. Environmental and Regulatory Specialist
E-mail Address: <a href="mailto:brmasey@taprk.com">brmasey@taprk.com</a>
Date: 3/12/2025
Phone: 720-238-2787
<b>OIL CONSERVATION DIVISION</b> <b>(Only applicable when submitted as a standalone form)</b>
Approved By:
Title:
Approval Date:
Conditions of Approval:





U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

# Drilling Plan Data Report

05/19/2025

APD ID: 10400100982

Submission Date: 09/12/2024

Highlighted data  
reflects the most  
recent changes

Operator Name: TAP ROCK OPERATING LLC

Well Name: COORS FED COM

Well Number: 213H

Well Type: CONVENTIONAL GAS WELL

Well Work Type: Drill

[Show Final Text](#)

## Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
15647053	QUATERNARY	3462	0	0	OTHER : None	NONE	N
15647054	RUSTLER ANHYDRITE	3326	136	136	ANHYDRITE	NONE	N
15647055	TOP OF SALT	3055	407	407	SALT	OTHER : Salt	N
15647056	BASE OF SALT	2072	1390	1394	SALT	OTHER : Salt	N
15647057	DELAWARE	1866	1596	1603	OTHER, SANDSTONE : Mountain Group	NONE	N
15647058	LAMAR	1861	1601	1608	SANDSTONE	NATURAL GAS, OIL	N
15647059	BELL CANYON	1845	1617	1624	SANDSTONE	NATURAL GAS, OIL	N
15647070	RAMSEY SAND	1837	1625	1632	SANDSTONE	NATURAL GAS, OIL	N
15647060	CHERRY CANYON	868	2594	2643	LIMESTONE	NATURAL GAS, OIL	N
15647061	BRUSHY CANYON	-52	3514	3622	SANDSTONE	NATURAL GAS, OIL	N
15647062	BONE SPRING LIME	-1563	5025	5230	OTHER : Carbonate	NATURAL GAS, OIL	N
15647063	AVALON SAND	-1668	5130	5342	OTHER : Upper - Carbonate	NATURAL GAS, OIL	N
15647064	AVALON SAND	-1969	5431	5662	OTHER : Middle - Carbonate	NATURAL GAS, OIL	N
15647065	BONE SPRING 1ST	-2404	5866	6125	SANDSTONE	NATURAL GAS, OIL	N
15647066	BONE SPRING 2ND	-2636	6098	6372	OTHER : Carbonate	NATURAL GAS, OIL	N
15647067	BONE SPRING 2ND	-3126	6588	6893	SANDSTONE	NATURAL GAS, OIL	N
15647068	BONE SPRING 3RD	-4110	7572	7940	SANDSTONE	NATURAL GAS, OIL	N

**Operator Name:** TAP ROCK OPERATING LLC**Well Name:** COORS FED COM**Well Number:** 213H

Formation ID	Formation Name	Elevation	True Vertical	Measured Depth	Lithologies	Mineral Resources	Producing Formatio
15647069	WOLFCAMP	-4431	7893	8319	OTHER : A	NATURAL GAS, OIL	Y

## Section 2 - Blowout Prevention

**Pressure Rating (PSI):** 5M**Rating Depth:** 20000

**Equipment:** At 19,093', a 5M pressure control system is required. The BOP stack consisting of 3 rams with 2 pipe rams, 1 blind ram, and 1 annular preventer will be used below surface casing to TD. Also present will be an accumulator that meets the requirements of 43 CFR 3172 for the pressure rating of the BOP stack. A rotating head will also be installed as needed. BOP will be inspected and operated as recommended in 43 CFR 3172. A top drive check valve and sub equipped with a full opening valve sized to fit the drill pipe and collars will be available on the rig floor in the open position. The wellhead will be a multi-bowl speed head.

**Requesting Variance?** YES

**Variance request:** Tap Rock requests a variance to run a multi-bowl speed head for setting the Intermediate and Production Strings. Tap Rock requests a variance to drill this well using a co-flex line between the BOP and choke manifold. Certification for proposed co-flex hose is attached. The hose is not required by the manufacturer to be anchored. In the event the specific hose is not available, one of equal or higher rating will be used. Tap Rock requests a variance to have the option of batch drilling this well with other wells on the same pad. If this well is batch drilled, after cementing a casing string, a 5M dry hole cap with bleed off valve will be installed. The rig will then walk to another well on the pad. Tap Rock Operating requests to only test BOP connection breaks after rig walks per the procedures and stipulations set forth in the "BOP Shell Test Procedure" document emailed to the BLM on 8/11/22.

**Testing Procedure:** After surface casing is set and the BOP is nipped up, the BOP pressure tests will be made with a third party tester to 250 psi low, 5000 psi high, and the annular preventer will be tested to 250 psi low, 2500 psi high.

**Choke Diagram Attachment:**

5M\_Choke\_Diagram\_20250325085429.pdf

**BOP Diagram Attachment:**

5M\_BOP\_Diagram\_20250325085438.pdf

## Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	14.75	11.75	NEW	API	N	0	400	0	400	3462	3062	400	J-55	42	BUTT	1.13	1.15	DRY	1.6	DRY	1.6
2	INTERMEDIATE	11	8.625	NEW	API	N	0	1658	0	1651	3543	1811	1658	J-55	32	BUTT	1.13	1.15	DRY	1.6	DRY	1.6

Operator Name: TAP ROCK OPERATING LLC

Well Name: COORS FED COM

Well Number: 213H

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
3	PRODUCTI ON	7.87 5	5.5	NEW	NON API	N	0	19106	0	8218	3543	-4756	19106	P- 110	20	OTHER - TXP	1.13	1.15	DRY	1.6	DRY	1.6

Casing Attachments

Casing ID: 1StringSURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Casing\_Design\_Assumptions\_20250325085517.pdf

Casing ID: 2StringINTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Casing\_Design\_Assumptions\_20250325085554.pdf

Operator Name: TAP ROCK OPERATING LLC

Well Name: COORS FED COM

Well Number: 213H

Casing Attachments

Casing ID: 3StringPRODUCTION

Inspection Document:

Spec Document:  
5.5in\_TXP\_Casing\_Spec\_20250325085630.PDF

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):  
Casing\_Design\_Assumptions\_20250325085643.pdf

Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	0	0	0	0	0	0	None	None
SURFACE	Tail		0	400	418	1.33	14.8	556	100	Class C	5% NCI + LCM
INTERMEDIATE	Lead		0	1158	164	2.7	11	443	75	Class C	Bentonite + 1% CaCL2 + 8% NaCl + LCM
INTERMEDIATE	Tail		1158	1658	124	1.33	14.8	165	30	Class C	5% NaCl + LCM
PRODUCTION	Lead		1458	7953	402	3.35	10.5	1346	20	Class C	Fluid Loss + Dispersant + Retarder + LCM
PRODUCTION	Tail		7953	19093	2227	1.63	13.2	3630	20	Class H	Fluid Loss + Dispersant + Retarder + LCM

Operator Name: TAP ROCK OPERATING LLC

Well Name: COORS FED COM

Well Number: 213H

## Section 5 - Circulating Medium

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with 43 CFR 3172:

Diagram of the equipment for the circulating system in accordance with 43 CFR 3172:

**Describe what will be on location to control well or mitigate other conditions:** All necessary mud products (i.e., barite, pac) for weight addition and fluid loss control will always be on site. Mud program is subject to change due to hole conditions. A closed loop system will be used.

**Describe the mud monitoring system utilized:** Electronic Pason mud monitor system complying with 43 CFR 3172 will be used.

## Circulating Medium Table

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	400	OTHER : Fresh Water Spud Mud	8.4	8.4							
400	1658	OTHER : Salt Saturated Mud	10	10							
1658	1909 3	OTHER : Fresh Water/Cut Brine	9	9							

## Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

Electric Logging Program: No open-hole logs are planned at this time. GR will be collected while drilling through the MWD tools from KOP to TD. A 2-person mud logging program will be used from KOP to TD. CBL w/ CCL from as far as gravity will let it fall to TOC.

List of open and cased hole logs run in the well:

CEMENT BOND LOG, GAMMA RAY LOG,

Coring operation description for the well:

No DSTs or cores are planned at this time.

**Operator Name:** TAP ROCK OPERATING LLC**Well Name:** COORS FED COM**Well Number:** 213H

## Section 7 - Pressure

**Anticipated Bottom Hole Pressure:** 3881**Anticipated Surface Pressure:** 2056**Anticipated Bottom Hole Temperature(F):** 160**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO**Describe:****Contingency Plans geohazards description:****Contingency Plans geohazards****Hydrogen Sulfide drilling operations plan required?** YES**Hydrogen sulfide drilling operations**

Coors\_H2S\_Plan\_20250325085923.pdf

## Section 8 - Other Information

**Proposed horizontal/directional/multi-lateral plan submission:**

Coors\_213H\_Directional\_Plan\_20250325085945.pdf

**Other proposed operations facets description:****Other proposed operations facets attachment:**

BOP\_Shell\_Test\_Procedure\_20240912101941.pdf

CoFlex\_Certs\_20240912101952.pdf

Coors\_213H\_Drill\_Plan\_20250325085953.pdf

Coors\_213H\_Anticollision\_Report\_20250325090005.pdf

Wellhead\_Diagram\_3T\_20250325090014.pdf

Coors\_WMP\_20250325090025.pdf

**Other Variance request(s)?:** N**Other Variance attachment:**







Company: Tap Rock Operating  
Well: Coors Fed Com 213H  
County: Eddy County, New Mexico (NAD 83)  
Rig: H&P 466  
Wellbore: Wellbore #1  
Design: Design #1  
Date: 13:27, March 12 2025

Geodetic System: US State Plane 1983  
Datum: North American Datum 1983  
Ellipsoid: GRS 1980  
Zone: New Mexico Eastern Zone  
System Datum: Mean Sea Level

WELL DETAILS: Coors Fed Com 213H						SURVEY PROGRAM			
+N/-S	+E/-W	GL @	Well @	GL @	Well @	Depth From	Depth To	Survey/Plan	Tool
0.00	0.00	Northing	Easting	Latitude	Longitude	0.00	19093.06	Design #1 (Wellbore #1)	MWD+HRGM+SAG+FDIR
372130.32	545660.61	32° 1' 23.036 N	104° 19' 9.782 W						
DESIGN TARGET DETAILS									
Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude		
FPP1_Coors 213H	0.00	1736.57	-2949.49	373866.88	542711.12	32° 1' 40.224 N	104° 19' 44.043 W		
FPP2_Coors 213H	0.00	4398.20	-2952.98	376528.52	542707.63	32° 2' 6.564 N	104° 19' 44.082 W		
FTP_Coors 213H	0.00	-597.92	-2946.32	371532.39	542714.28	32° 1' 17.121 N	104° 19' 44.007 W		
KOP_Coors 213H	0.00	-877.92	-2945.94	371252.40	542714.66	32° 1' 14.350 N	104° 19' 44.003 W		
LTP_Coors 213H	0.00	9393.09	-2959.62	381523.41	542700.98	32° 2' 55.996 N	104° 19' 44.157 W		
PBHL_Coors 213H	8293.00	9718.09	-2960.16	381848.40	542700.44	32° 2' 59.212 N	104° 19' 44.163 W		

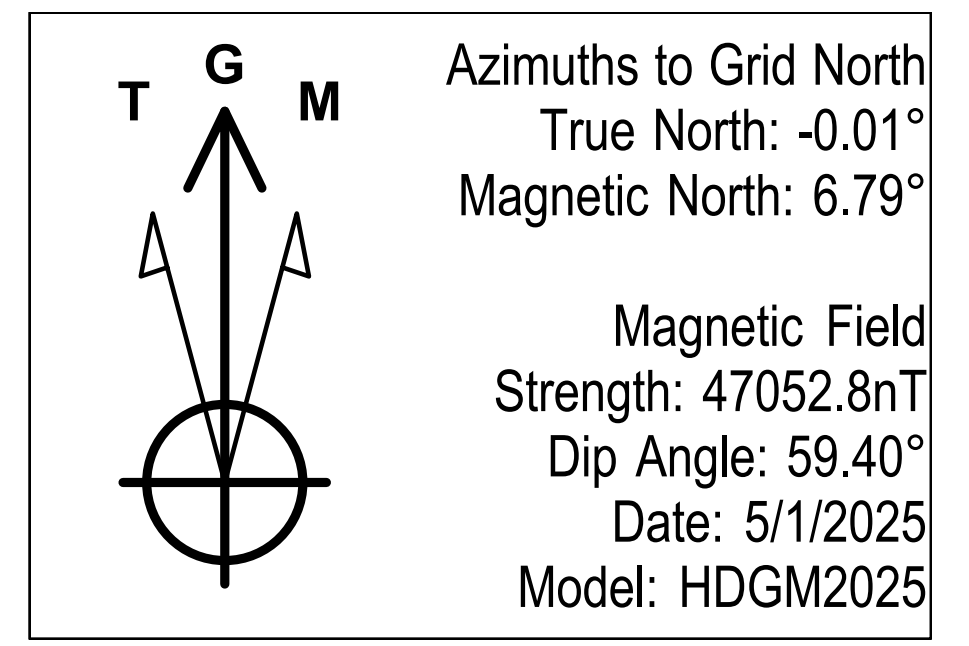

To convert a Magnetic Direction to a Grid Direction, Add 6.793°  
To convert a Magnetic Direction to a True Direction, Add 6.800° East  
To convert a True Direction to a Grid Direction, Subtract 0.007°

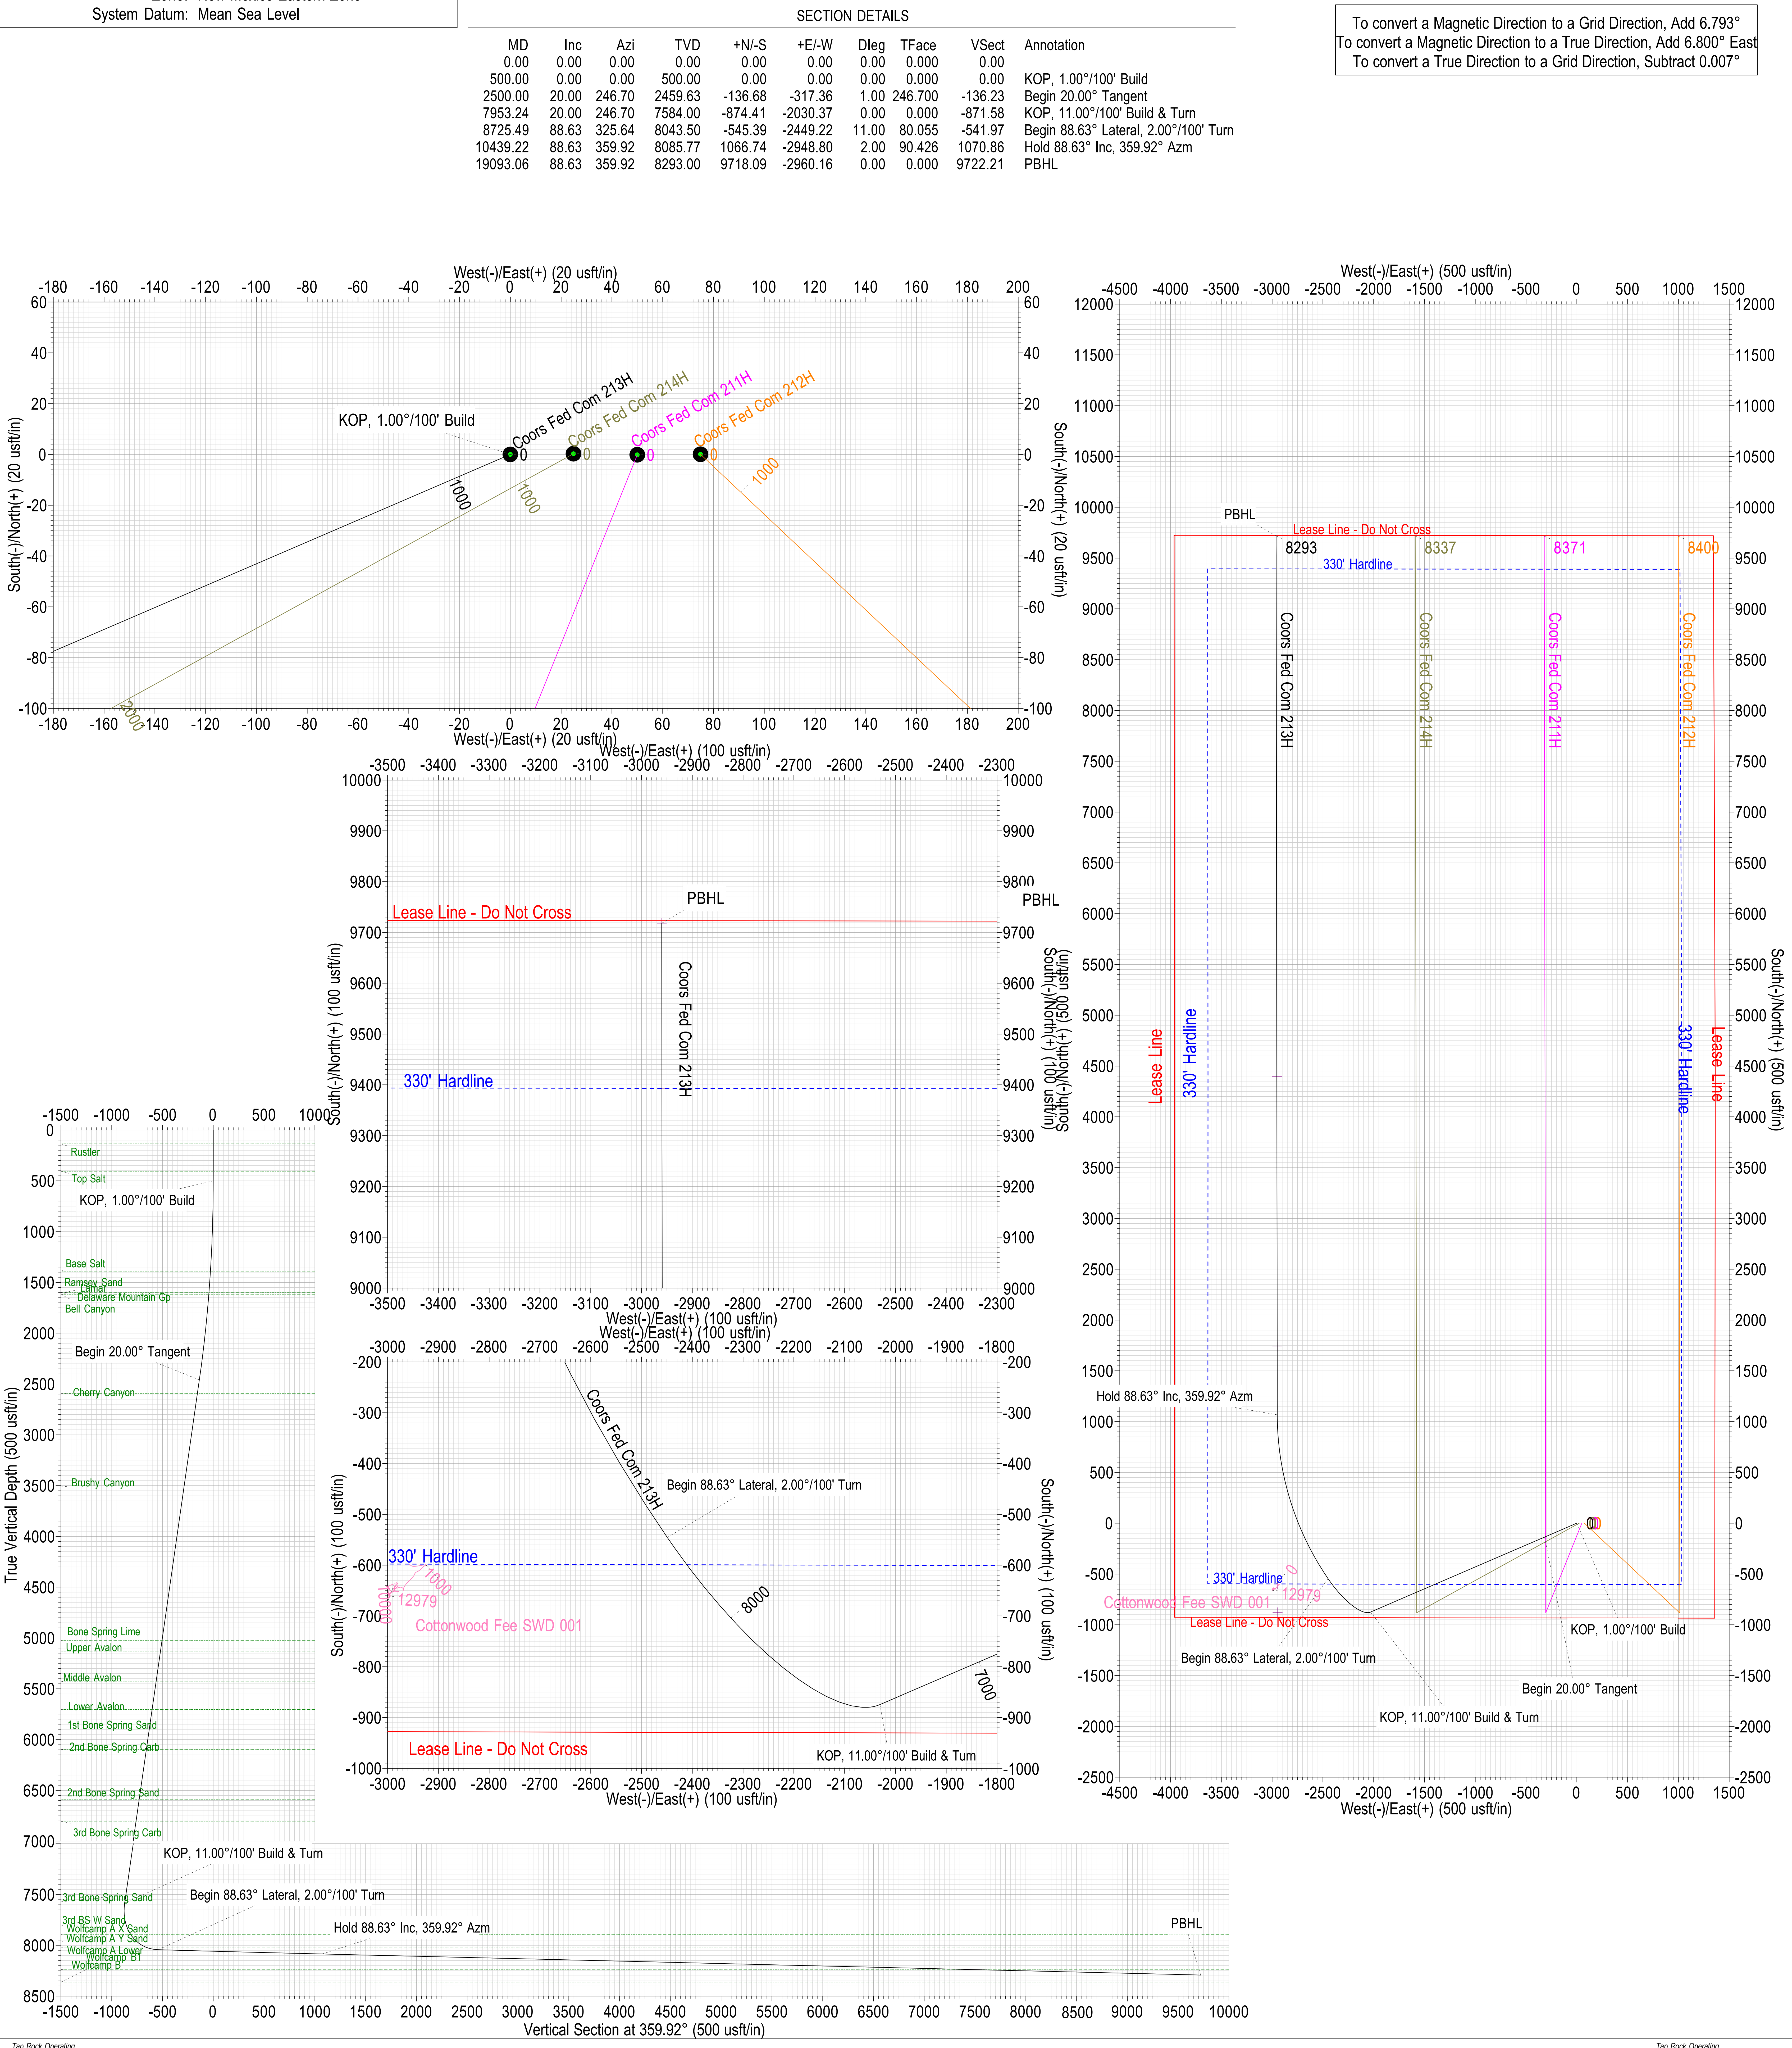





## **Tap Rock Operating**

**Eddy County, New Mexico (NAD 83)**

**Coors Fed Com (211H, 211H, 213H, 214H)**

**Coors Fed Com 213H**

**Wellbore #1**

**Plan: Design #1**

## **Standard Planning Report**

**12 March, 2025**





## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

<b>Project</b>	Eddy County, New Mexico (NAD 83)		
<b>Map System:</b>	US State Plane 1983	<b>System Datum:</b>	Mean Sea Level
<b>Geo Datum:</b>	North American Datum 1983		
<b>Map Zone:</b>	New Mexico Eastern Zone		

Site	Coors Fed Com (211H, 211H, 213H, 214H)				
Site Position:		Northing:	372,130.18 usft	Latitude:	32° 1' 23.034 N
From:	Lat/Long	Easting:	545,710.63 usft	Longitude:	104° 19' 9.201 W
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "		

Well		Coors Fed Com 213H				
Well Position	+N/-S	0.00 usft	Northing:	372,130.32 usft	Latitude:	32° 1' 23.036 N
	+E/-W	0.00 usft	Easting:	545,660.61 usft	Longitude:	104° 19' 9.782 W
Position Uncertainty		0.00 usft	Wellhead Elevation:	usft	Ground Level:	3,462.00 usft
Grid Convergence:		0.007 °				

<b>Wellbore</b>	Wellbore #1				
<b>Magnetics</b>	<b>Model Name</b>	<b>Sample Date</b>	<b>Declination (°)</b>	<b>Dip Angle (°)</b>	<b>Field Strength (nT)</b>
	HDGM2025	5/1/2025	6.800	59.400	47,052.80

<b>Design</b>	Design #1				
<b>Audit Notes:</b>					
<b>Version:</b>		<b>Phase:</b>	PLAN	<b>Tie On Depth:</b>	0.00
<b>Vertical Section:</b>	<b>Depth From (TVD) (usft)</b>	<b>+N/-S (usft)</b>	<b>+E/-W (usft)</b>	<b>Direction (°)</b>	
	0.00	0.00	0.00	359.92	

<b>Plan Survey Tool Program</b>	<b>Date</b>	3/12/2025			
<b>Depth From (usft)</b>	<b>Depth To (usft)</b>	<b>Survey (Wellbore)</b>	<b>Tool Name</b>	<b>Remarks</b>	
1	0.00	19,093.06	Design #1 (Wellbore #1)	MWD+HRGM+SAG+FDIR	
				OWSG MWD + HRGM + SAG	

<b>Plan Sections</b>										
<b>Measured Depth (usft)</b>	<b>Inclination (°)</b>	<b>Azimuth (°)</b>	<b>Vertical Depth (usft)</b>	<b>+N/-S (usft)</b>	<b>+E/-W (usft)</b>	<b>Dogleg Rate (°/100usft)</b>	<b>Build Rate (°/100usft)</b>	<b>Turn Rate (°/100usft)</b>	<b>TFO (°)</b>	<b>Target</b>
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.000	
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.000	
2,500.00	20.00	246.70	2,459.63	-136.68	-317.36	1.00	1.00	0.00	246.700	
7,953.24	20.00	246.70	7,584.00	-874.41	-2,030.37	0.00	0.00	0.00	0.000	
8,725.49	88.63	325.64	8,043.50	-545.39	-2,449.22	11.00	8.89	10.22	80.055	
10,439.22	88.63	359.92	8,085.77	1,066.74	-2,948.80	2.00	0.00	2.00	90.426	
19,093.06	88.63	359.92	8,293.00	9,718.09	-2,960.16	0.00	0.00	0.00	0.000	PBHL_Coors 213H



## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
136.00	0.00	0.00	136.00	0.00	0.00	0.00	0.00	0.00	0.00
<b>Rustler</b>									
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
407.00	0.00	0.00	407.00	0.00	0.00	0.00	0.00	0.00	0.00
<b>Top Salt</b>									
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
<b>KOP, 1.00°/100' Build</b>									
600.00	1.00	246.70	599.99	-0.35	-0.80	-0.34	1.00	1.00	0.00
700.00	2.00	246.70	699.96	-1.38	-3.21	-1.38	1.00	1.00	0.00
800.00	3.00	246.70	799.86	-3.11	-7.21	-3.10	1.00	1.00	0.00
900.00	4.00	246.70	899.68	-5.52	-12.82	-5.50	1.00	1.00	0.00
1,000.00	5.00	246.70	999.37	-8.62	-20.02	-8.60	1.00	1.00	0.00
1,100.00	6.00	246.70	1,098.90	-12.42	-28.83	-12.37	1.00	1.00	0.00
1,200.00	7.00	246.70	1,198.26	-16.89	-39.22	-16.84	1.00	1.00	0.00
1,300.00	8.00	246.70	1,297.40	-22.06	-51.21	-21.98	1.00	1.00	0.00
1,393.62	8.94	246.70	1,390.00	-27.51	-63.87	-27.42	1.00	1.00	0.00
<b>Base Salt</b>									
1,400.00	9.00	246.70	1,396.30	-27.90	-64.79	-27.81	1.00	1.00	0.00
1,500.00	10.00	246.70	1,494.93	-34.43	-79.95	-34.32	1.00	1.00	0.00
1,600.00	11.00	246.70	1,593.26	-41.64	-96.68	-41.50	1.00	1.00	0.00
1,602.80	11.03	246.70	1,596.00	-41.85	-97.17	-41.71	1.00	1.00	0.00
<b>Delaware Mountain Gp</b>									
1,607.89	11.08	246.70	1,601.00	-42.24	-98.07	-42.10	1.00	1.00	0.00
<b>Lamar</b>									
1,624.20	11.24	246.70	1,617.00	-43.48	-100.97	-43.34	1.00	1.00	0.00
<b>Bell Canyon</b>									
1,632.36	11.32	246.70	1,625.00	-44.12	-102.44	-43.97	1.00	1.00	0.00
<b>Ramsey Sand</b>									
1,700.00	12.00	246.70	1,691.25	-49.52	-114.99	-49.36	1.00	1.00	0.00
1,800.00	13.00	246.70	1,788.87	-58.09	-134.87	-57.90	1.00	1.00	0.00
1,900.00	14.00	246.70	1,886.11	-67.32	-156.31	-67.10	1.00	1.00	0.00
2,000.00	15.00	246.70	1,982.92	-77.22	-179.31	-76.97	1.00	1.00	0.00
2,100.00	16.00	246.70	2,079.29	-87.79	-203.85	-87.51	1.00	1.00	0.00
2,200.00	17.00	246.70	2,175.17	-99.03	-229.94	-98.71	1.00	1.00	0.00
2,300.00	18.00	246.70	2,270.54	-110.92	-257.56	-110.56	1.00	1.00	0.00
2,400.00	19.00	246.70	2,365.37	-123.47	-286.70	-123.07	1.00	1.00	0.00
2,500.00	20.00	246.70	2,459.63	-136.68	-317.36	-136.23	1.00	1.00	0.00
<b>Begin 20.00° Tangent</b>									
2,600.00	20.00	246.70	2,553.60	-150.20	-348.77	-149.72	0.00	0.00	0.00
2,642.99	20.00	246.70	2,594.00	-156.02	-362.27	-155.51	0.00	0.00	0.00
<b>Cherry Canyon</b>									
2,700.00	20.00	246.70	2,647.57	-163.73	-380.18	-163.20	0.00	0.00	0.00
2,800.00	20.00	246.70	2,741.54	-177.26	-411.59	-176.69	0.00	0.00	0.00
2,900.00	20.00	246.70	2,835.51	-190.79	-443.01	-190.17	0.00	0.00	0.00
3,000.00	20.00	246.70	2,929.48	-204.32	-474.42	-203.65	0.00	0.00	0.00
3,100.00	20.00	246.70	3,023.45	-217.85	-505.83	-217.14	0.00	0.00	0.00
3,200.00	20.00	246.70	3,117.42	-231.37	-537.25	-230.62	0.00	0.00	0.00
3,300.00	20.00	246.70	3,211.39	-244.90	-568.66	-244.11	0.00	0.00	0.00
3,400.00	20.00	246.70	3,305.35	-258.43	-600.07	-257.59	0.00	0.00	0.00



## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
3,500.00	20.00	246.70	3,399.32	-271.96	-631.48	-271.08	0.00	0.00	0.00
3,600.00	20.00	246.70	3,493.29	-285.49	-662.90	-284.56	0.00	0.00	0.00
3,622.04	20.00	246.70	3,514.00	-288.47	-669.82	-287.53	0.00	0.00	0.00
<b>Brushy Canyon</b>									
3,700.00	20.00	246.70	3,587.26	-299.02	-694.31	-298.05	0.00	0.00	0.00
3,800.00	20.00	246.70	3,681.23	-312.55	-725.72	-311.53	0.00	0.00	0.00
3,900.00	20.00	246.70	3,775.20	-326.07	-757.13	-325.02	0.00	0.00	0.00
4,000.00	20.00	246.70	3,869.17	-339.60	-788.55	-338.50	0.00	0.00	0.00
4,100.00	20.00	246.70	3,963.14	-353.13	-819.96	-351.99	0.00	0.00	0.00
4,200.00	20.00	246.70	4,057.11	-366.66	-851.37	-365.47	0.00	0.00	0.00
4,300.00	20.00	246.70	4,151.08	-380.19	-882.79	-378.95	0.00	0.00	0.00
4,400.00	20.00	246.70	4,245.05	-393.72	-914.20	-392.44	0.00	0.00	0.00
4,500.00	20.00	246.70	4,339.02	-407.24	-945.61	-405.92	0.00	0.00	0.00
4,600.00	20.00	246.70	4,432.99	-420.77	-977.02	-419.41	0.00	0.00	0.00
4,700.00	20.00	246.70	4,526.95	-434.30	-1,008.44	-432.89	0.00	0.00	0.00
4,800.00	20.00	246.70	4,620.92	-447.83	-1,039.85	-446.38	0.00	0.00	0.00
4,900.00	20.00	246.70	4,714.89	-461.36	-1,071.26	-459.86	0.00	0.00	0.00
5,000.00	20.00	246.70	4,808.86	-474.89	-1,102.67	-473.35	0.00	0.00	0.00
5,100.00	20.00	246.70	4,902.83	-488.41	-1,134.09	-486.83	0.00	0.00	0.00
5,200.00	20.00	246.70	4,996.80	-501.94	-1,165.50	-500.32	0.00	0.00	0.00
5,230.01	20.00	246.70	5,025.00	-506.00	-1,174.93	-504.36	0.00	0.00	0.00
<b>Bone Spring Lime</b>									
5,300.00	20.00	246.70	5,090.77	-515.47	-1,196.91	-513.80	0.00	0.00	0.00
5,341.75	20.00	246.70	5,130.00	-521.12	-1,210.03	-519.43	0.00	0.00	0.00
<b>Upper Avalon</b>									
5,400.00	20.00	246.70	5,184.74	-529.00	-1,228.32	-527.28	0.00	0.00	0.00
5,500.00	20.00	246.70	5,278.71	-542.53	-1,259.74	-540.77	0.00	0.00	0.00
5,600.00	20.00	246.70	5,372.68	-556.06	-1,291.15	-554.25	0.00	0.00	0.00
5,662.06	20.00	246.70	5,431.00	-564.45	-1,310.65	-562.62	0.00	0.00	0.00
<b>Middle Avalon</b>									
5,700.00	20.00	246.70	5,466.65	-569.59	-1,322.56	-567.74	0.00	0.00	0.00
5,800.00	20.00	246.70	5,560.62	-583.11	-1,353.98	-581.22	0.00	0.00	0.00
5,900.00	20.00	246.70	5,654.59	-596.64	-1,385.39	-594.71	0.00	0.00	0.00
5,952.59	20.00	246.70	5,704.00	-603.76	-1,401.91	-601.80	0.00	0.00	0.00
<b>Lower Avalon</b>									
6,000.00	20.00	246.70	5,748.56	-610.17	-1,416.80	-608.19	0.00	0.00	0.00
6,100.00	20.00	246.70	5,842.52	-623.70	-1,448.21	-621.68	0.00	0.00	0.00
6,124.98	20.00	246.70	5,866.00	-627.08	-1,456.06	-625.05	0.00	0.00	0.00
<b>1st Bone Spring Sand</b>									
6,200.00	20.00	246.70	5,936.49	-637.23	-1,479.63	-635.16	0.00	0.00	0.00
6,300.00	20.00	246.70	6,030.46	-650.76	-1,511.04	-648.65	0.00	0.00	0.00
6,371.87	20.00	246.70	6,098.00	-660.48	-1,533.62	-658.34	0.00	0.00	0.00
<b>2nd Bone Spring Carb</b>									
6,400.00	20.00	246.70	6,124.43	-664.28	-1,542.45	-662.13	0.00	0.00	0.00
6,500.00	20.00	246.70	6,218.40	-677.81	-1,573.86	-675.62	0.00	0.00	0.00
6,600.00	20.00	246.70	6,312.37	-691.34	-1,605.28	-689.10	0.00	0.00	0.00
6,700.00	20.00	246.70	6,406.34	-704.87	-1,636.69	-702.58	0.00	0.00	0.00
6,800.00	20.00	246.70	6,500.31	-718.40	-1,668.10	-716.07	0.00	0.00	0.00
6,893.32	20.00	246.70	6,588.00	-731.02	-1,697.42	-728.65	0.00	0.00	0.00
<b>2nd Bone Spring Sand</b>									
6,900.00	20.00	246.70	6,594.28	-731.93	-1,699.52	-729.55	0.00	0.00	0.00
7,000.00	20.00	246.70	6,688.25	-745.46	-1,730.93	-743.04	0.00	0.00	0.00
7,100.00	20.00	246.70	6,782.22	-758.98	-1,762.34	-756.52	0.00	0.00	0.00



## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
7,123.18	20.00	246.70	6,804.00	-762.12	-1,769.62	-759.65	0.00	0.00	0.00
<b>3rd Bone Spring Carb</b>									
7,200.00	20.00	246.70	6,876.19	-772.51	-1,793.75	-770.01	0.00	0.00	0.00
7,300.00	20.00	246.70	6,970.16	-786.04	-1,825.17	-783.49	0.00	0.00	0.00
7,400.00	20.00	246.70	7,064.13	-799.57	-1,856.58	-796.98	0.00	0.00	0.00
7,500.00	20.00	246.70	7,158.09	-813.10	-1,887.99	-810.46	0.00	0.00	0.00
7,600.00	20.00	246.70	7,252.06	-826.63	-1,919.40	-823.95	0.00	0.00	0.00
7,700.00	20.00	246.70	7,346.03	-840.15	-1,950.82	-837.43	0.00	0.00	0.00
7,800.00	20.00	246.70	7,440.00	-853.68	-1,982.23	-850.91	0.00	0.00	0.00
7,900.00	20.00	246.70	7,533.97	-867.21	-2,013.64	-864.40	0.00	0.00	0.00
7,940.47	20.00	246.70	7,572.00	-872.69	-2,026.36	-869.86	0.00	0.00	0.00
<b>3rd Bone Spring Sand</b>									
7,953.24	20.00	246.70	7,584.00	-874.41	-2,030.37	-871.58	0.00	0.00	0.00
<b>KOP, 11.00°/100' Build &amp; Turn</b>									
8,000.00	21.47	260.66	7,627.76	-878.97	-2,046.17	-876.11	11.00	3.14	29.86
8,050.00	24.13	273.12	7,673.87	-879.90	-2,065.41	-877.01	11.00	5.32	24.92
8,100.00	27.60	282.94	7,718.88	-876.74	-2,086.92	-873.83	11.00	6.94	19.63
8,150.00	31.61	290.58	7,762.36	-869.54	-2,110.50	-866.59	11.00	8.02	15.28
8,200.00	35.98	296.60	7,803.91	-858.35	-2,135.91	-855.37	11.00	8.74	12.04
8,207.55	36.66	297.40	7,810.00	-856.32	-2,139.90	-853.33	11.00	9.05	10.56
<b>3rd BS W Sand</b>									
8,250.00	40.59	301.45	7,843.16	-843.28	-2,162.94	-840.25	11.00	9.25	9.54
8,300.00	45.37	305.45	7,879.74	-824.46	-2,191.34	-821.40	11.00	9.56	8.00
8,319.20	47.24	306.81	7,893.00	-816.27	-2,202.55	-813.20	11.00	9.73	7.09
<b>Wolfcamp A X Sand</b>									
8,350.00	50.27	308.83	7,913.31	-802.07	-2,220.83	-798.97	11.00	9.83	6.56
8,400.00	55.25	311.76	7,943.56	-776.32	-2,251.15	-773.17	11.00	9.96	5.86
8,441.59	59.44	313.93	7,966.00	-752.50	-2,276.81	-749.32	11.00	10.08	5.23
<b>Wolfcamp A Y Sand</b>									
8,450.00	60.29	314.35	7,970.22	-747.44	-2,282.03	-744.25	11.00	10.13	4.95
8,500.00	65.38	316.69	7,993.04	-715.69	-2,313.17	-712.46	11.00	10.18	4.69
8,550.00	70.50	318.85	8,011.82	-681.38	-2,344.29	-678.11	11.00	10.25	4.32
8,569.50	72.51	319.66	8,018.00	-667.37	-2,356.35	-664.08	11.00	10.28	4.12
<b>Wolfcamp A Lower</b>									
8,600.00	75.65	320.88	8,026.37	-644.82	-2,375.10	-641.50	11.00	10.30	4.01
8,650.00	80.82	322.81	8,036.56	-606.33	-2,405.32	-602.98	11.00	10.33	3.87
8,700.00	85.99	324.69	8,042.30	-566.29	-2,434.67	-562.89	11.00	10.35	3.76
8,725.49	88.63	325.64	8,043.50	-545.39	-2,449.22	-541.97	11.00	10.36	3.71
<b>Begin 88.63° Lateral, 2.00°/100' Turn</b>									
8,800.00	88.62	327.13	8,045.29	-483.36	-2,490.45	-479.88	2.00	-0.01	2.00
8,900.00	88.61	329.13	8,047.71	-398.47	-2,543.23	-394.91	2.00	-0.01	2.00
9,000.00	88.60	331.13	8,050.15	-311.78	-2,593.01	-308.16	2.00	-0.01	2.00
9,100.00	88.59	333.13	8,052.61	-223.41	-2,639.74	-219.72	2.00	-0.01	2.00
9,200.00	88.58	335.13	8,055.08	-133.46	-2,683.35	-129.71	2.00	-0.01	2.00
9,300.00	88.57	337.13	8,057.57	-42.04	-2,723.80	-38.24	2.00	-0.01	2.00
9,400.00	88.57	339.13	8,060.06	50.73	-2,761.03	54.58	2.00	0.00	2.00
9,500.00	88.57	341.13	8,062.57	144.74	-2,795.00	148.65	2.00	0.00	2.00
9,600.00	88.57	343.14	8,065.07	239.89	-2,825.67	243.83	2.00	0.00	2.00
9,700.00	88.57	345.14	8,067.57	336.04	-2,852.99	340.03	2.00	0.00	2.00
9,800.00	88.57	347.14	8,070.07	433.09	-2,876.95	437.11	2.00	0.00	2.00
9,900.00	88.57	349.14	8,072.57	530.92	-2,897.50	534.97	2.00	0.00	2.00
10,000.00	88.58	351.14	8,075.05	629.41	-2,914.62	633.48	2.00	0.01	2.00
10,100.00	88.59	353.14	8,077.52	728.43	-2,928.29	732.52	2.00	0.01	2.00





## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
10,200.00	88.60	355.14	8,079.98	827.88	-2,938.50	831.98	2.00	0.01	2.00
10,300.00	88.61	357.14	8,082.41	927.62	-2,945.23	931.73	2.00	0.01	2.00
10,400.00	88.62	359.14	8,084.83	1,027.53	-2,948.48	1,031.64	2.00	0.01	2.00
10,439.22	88.63	359.92	8,085.77	1,066.74	-2,948.80	1,070.86	2.00	0.01	2.00
<b>Hold 88.63° Inc, 359.92° Azm</b>									
10,500.00	88.63	359.92	8,087.23	1,127.50	-2,948.88	1,131.61	0.00	0.00	0.00
10,600.00	88.63	359.92	8,089.62	1,227.47	-2,949.01	1,231.59	0.00	0.00	0.00
10,700.00	88.63	359.92	8,092.02	1,327.44	-2,949.14	1,331.56	0.00	0.00	0.00
10,800.00	88.63	359.92	8,094.41	1,427.41	-2,949.27	1,431.53	0.00	0.00	0.00
10,900.00	88.63	359.92	8,096.81	1,527.38	-2,949.40	1,531.50	0.00	0.00	0.00
11,000.00	88.63	359.92	8,099.20	1,627.35	-2,949.53	1,631.47	0.00	0.00	0.00
11,100.00	88.63	359.92	8,101.60	1,727.33	-2,949.67	1,731.44	0.00	0.00	0.00
11,200.00	88.63	359.92	8,103.99	1,827.30	-2,949.80	1,831.41	0.00	0.00	0.00
11,300.00	88.63	359.92	8,106.38	1,927.27	-2,949.93	1,931.38	0.00	0.00	0.00
11,400.00	88.63	359.92	8,108.78	2,027.24	-2,950.06	2,031.36	0.00	0.00	0.00
11,500.00	88.63	359.92	8,111.17	2,127.21	-2,950.19	2,131.33	0.00	0.00	0.00
11,600.00	88.63	359.92	8,113.57	2,227.18	-2,950.32	2,231.30	0.00	0.00	0.00
11,700.00	88.63	359.92	8,115.96	2,327.15	-2,950.45	2,331.27	0.00	0.00	0.00
11,800.00	88.63	359.92	8,118.36	2,427.12	-2,950.58	2,431.24	0.00	0.00	0.00
11,900.00	88.63	359.92	8,120.75	2,527.10	-2,950.72	2,531.21	0.00	0.00	0.00
12,000.00	88.63	359.92	8,123.15	2,627.07	-2,950.85	2,631.18	0.00	0.00	0.00
12,100.00	88.63	359.92	8,125.54	2,727.04	-2,950.98	2,731.16	0.00	0.00	0.00
12,200.00	88.63	359.92	8,127.94	2,827.01	-2,951.11	2,831.13	0.00	0.00	0.00
12,300.00	88.63	359.92	8,130.33	2,926.98	-2,951.24	2,931.10	0.00	0.00	0.00
12,400.00	88.63	359.92	8,132.73	3,026.95	-2,951.37	3,031.07	0.00	0.00	0.00
12,500.00	88.63	359.92	8,135.12	3,126.92	-2,951.50	3,131.04	0.00	0.00	0.00
12,600.00	88.63	359.92	8,137.51	3,226.89	-2,951.64	3,231.01	0.00	0.00	0.00
12,700.00	88.63	359.92	8,139.91	3,326.86	-2,951.77	3,330.98	0.00	0.00	0.00
12,800.00	88.63	359.92	8,142.30	3,426.84	-2,951.90	3,430.95	0.00	0.00	0.00
12,900.00	88.63	359.92	8,144.70	3,526.81	-2,952.03	3,530.93	0.00	0.00	0.00
13,000.00	88.63	359.92	8,147.09	3,626.78	-2,952.16	3,630.90	0.00	0.00	0.00
13,100.00	88.63	359.92	8,149.49	3,726.75	-2,952.29	3,730.87	0.00	0.00	0.00
13,200.00	88.63	359.92	8,151.88	3,826.72	-2,952.42	3,830.84	0.00	0.00	0.00
13,300.00	88.63	359.92	8,154.28	3,926.69	-2,952.56	3,930.81	0.00	0.00	0.00
13,400.00	88.63	359.92	8,156.67	4,026.66	-2,952.69	4,030.78	0.00	0.00	0.00
13,500.00	88.63	359.92	8,159.07	4,126.63	-2,952.82	4,130.75	0.00	0.00	0.00
13,600.00	88.63	359.92	8,161.46	4,226.61	-2,952.95	4,230.73	0.00	0.00	0.00
13,700.00	88.63	359.92	8,163.86	4,326.58	-2,953.08	4,330.70	0.00	0.00	0.00
13,800.00	88.63	359.92	8,166.25	4,426.55	-2,953.21	4,430.67	0.00	0.00	0.00
13,900.00	88.63	359.92	8,168.65	4,526.52	-2,953.34	4,530.64	0.00	0.00	0.00
14,000.00	88.63	359.92	8,171.04	4,626.49	-2,953.47	4,630.61	0.00	0.00	0.00
14,100.00	88.63	359.92	8,173.43	4,726.46	-2,953.61	4,730.58	0.00	0.00	0.00
14,200.00	88.63	359.92	8,175.83	4,826.43	-2,953.74	4,830.55	0.00	0.00	0.00
14,300.00	88.63	359.92	8,178.22	4,926.40	-2,953.87	4,930.52	0.00	0.00	0.00
14,400.00	88.63	359.92	8,180.62	5,026.38	-2,954.00	5,030.50	0.00	0.00	0.00
14,500.00	88.63	359.92	8,183.01	5,126.35	-2,954.13	5,130.47	0.00	0.00	0.00
14,600.00	88.63	359.92	8,185.41	5,226.32	-2,954.26	5,230.44	0.00	0.00	0.00
14,700.00	88.63	359.92	8,187.80	5,326.29	-2,954.39	5,330.41	0.00	0.00	0.00
14,800.00	88.63	359.92	8,190.20	5,426.26	-2,954.53	5,430.38	0.00	0.00	0.00
14,900.00	88.63	359.92	8,192.59	5,526.23	-2,954.66	5,530.35	0.00	0.00	0.00
15,000.00	88.63	359.92	8,194.99	5,626.20	-2,954.79	5,630.32	0.00	0.00	0.00
15,100.00	88.63	359.92	8,197.38	5,726.17	-2,954.92	5,730.30	0.00	0.00	0.00
15,200.00	88.63	359.92	8,199.78	5,826.15	-2,955.05	5,830.27	0.00	0.00	0.00



## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
15,300.00	88.63	359.92	8,202.17	5,926.12	-2,955.18	5,930.24	0.00	0.00	0.00	
15,400.00	88.63	359.92	8,204.56	6,026.09	-2,955.31	6,030.21	0.00	0.00	0.00	
15,500.00	88.63	359.92	8,206.96	6,126.06	-2,955.44	6,130.18	0.00	0.00	0.00	
15,600.00	88.63	359.92	8,209.35	6,226.03	-2,955.58	6,230.15	0.00	0.00	0.00	
15,700.00	88.63	359.92	8,211.75	6,326.00	-2,955.71	6,330.12	0.00	0.00	0.00	
15,800.00	88.63	359.92	8,214.14	6,425.97	-2,955.84	6,430.09	0.00	0.00	0.00	
15,900.00	88.63	359.92	8,216.54	6,525.94	-2,955.97	6,530.07	0.00	0.00	0.00	
16,000.00	88.63	359.92	8,218.93	6,625.92	-2,956.10	6,630.04	0.00	0.00	0.00	
16,100.00	88.63	359.92	8,221.33	6,725.89	-2,956.23	6,730.01	0.00	0.00	0.00	
16,200.00	88.63	359.92	8,223.72	6,825.86	-2,956.36	6,829.98	0.00	0.00	0.00	
16,300.00	88.63	359.92	8,226.12	6,925.83	-2,956.50	6,929.95	0.00	0.00	0.00	
16,400.00	88.63	359.92	8,228.51	7,025.80	-2,956.63	7,029.92	0.00	0.00	0.00	
16,500.00	88.63	359.92	8,230.91	7,125.77	-2,956.76	7,129.89	0.00	0.00	0.00	
16,600.00	88.63	359.92	8,233.30	7,225.74	-2,956.89	7,229.86	0.00	0.00	0.00	
16,700.00	88.63	359.92	8,235.70	7,325.71	-2,957.02	7,329.84	0.00	0.00	0.00	
16,800.00	88.63	359.92	8,238.09	7,425.69	-2,957.15	7,429.81	0.00	0.00	0.00	
16,879.78	88.63	359.92	8,240.00	7,505.45	-2,957.26	7,509.57	0.00	0.00	0.00	
<b>Wolfcamp B</b>										
16,900.00	88.63	359.92	8,240.48	7,525.66	-2,957.28	7,529.78	0.00	0.00	0.00	
17,000.00	88.63	359.92	8,242.88	7,625.63	-2,957.42	7,629.75	0.00	0.00	0.00	
17,100.00	88.63	359.92	8,245.27	7,725.60	-2,957.55	7,729.72	0.00	0.00	0.00	
17,200.00	88.63	359.92	8,247.67	7,825.57	-2,957.68	7,829.69	0.00	0.00	0.00	
17,300.00	88.63	359.92	8,250.06	7,925.54	-2,957.81	7,929.66	0.00	0.00	0.00	
17,400.00	88.63	359.92	8,252.46	8,025.51	-2,957.94	8,029.64	0.00	0.00	0.00	
17,500.00	88.63	359.92	8,254.85	8,125.48	-2,958.07	8,129.61	0.00	0.00	0.00	
17,600.00	88.63	359.92	8,257.25	8,225.46	-2,958.20	8,229.58	0.00	0.00	0.00	
17,700.00	88.63	359.92	8,259.64	8,325.43	-2,958.33	8,329.55	0.00	0.00	0.00	
17,800.00	88.63	359.92	8,262.04	8,425.40	-2,958.47	8,429.52	0.00	0.00	0.00	
17,900.00	88.63	359.92	8,264.43	8,525.37	-2,958.60	8,529.49	0.00	0.00	0.00	
18,000.00	88.63	359.92	8,266.83	8,625.34	-2,958.73	8,629.46	0.00	0.00	0.00	
18,100.00	88.63	359.92	8,269.22	8,725.31	-2,958.86	8,729.43	0.00	0.00	0.00	
18,200.00	88.63	359.92	8,271.61	8,825.28	-2,958.99	8,829.41	0.00	0.00	0.00	
18,300.00	88.63	359.92	8,274.01	8,925.25	-2,959.12	8,929.38	0.00	0.00	0.00	
18,400.00	88.63	359.92	8,276.40	9,025.23	-2,959.25	9,029.35	0.00	0.00	0.00	
18,500.00	88.63	359.92	8,278.80	9,125.20	-2,959.39	9,129.32	0.00	0.00	0.00	
18,600.00	88.63	359.92	8,281.19	9,225.17	-2,959.52	9,229.29	0.00	0.00	0.00	
18,700.00	88.63	359.92	8,283.59	9,325.14	-2,959.65	9,329.26	0.00	0.00	0.00	
18,800.00	88.63	359.92	8,285.98	9,425.11	-2,959.78	9,429.23	0.00	0.00	0.00	
18,900.00	88.63	359.92	8,288.38	9,525.08	-2,959.91	9,529.21	0.00	0.00	0.00	
19,000.00	88.63	359.92	8,290.77	9,625.05	-2,960.04	9,629.18	0.00	0.00	0.00	
19,093.06	88.63	359.92	8,293.00	9,718.09	-2,960.16	9,722.21	0.00	0.00	0.00	
<b>PBHL</b>										



## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

## Design Targets

Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
FPP2_Coors 213H - plan misses target center by 5297.57usft at 0.00usft MD (0.00 TVD, 0.00 N, 0.00 E) - Point	0.00	0.00	0.00	4,398.20	-2,952.98	376,528.51	542,707.63	32° 2' 6.564 N	104° 19' 44.082 W
LTP_Coors 213H - plan misses target center by 8282.84usft at 18569.57usft MD (8280.46 TVD, 9194.75 N, -2959.48 E) - Point	0.00	0.00	0.00	9,393.09	-2,959.62	381,523.41	542,700.98	32° 2' 55.996 N	104° 19' 44.157 W
FPP1_Coors 213H - plan misses target center by 3422.74usft at 0.00usft MD (0.00 TVD, 0.00 N, 0.00 E) - Point	0.00	0.00	0.00	1,736.57	-2,949.49	373,866.88	542,711.12	32° 1' 40.224 N	104° 19' 44.043 W
KOP_Coors 213H - plan misses target center by 3073.97usft at 0.00usft MD (0.00 TVD, 0.00 N, 0.00 E) - Point	0.00	0.00	0.00	-877.92	-2,945.94	371,252.40	542,714.67	32° 1' 14.350 N	104° 19' 44.003 W
FTP_Coors 213H - plan misses target center by 3006.38usft at 0.00usft MD (0.00 TVD, 0.00 N, 0.00 E) - Point	0.00	0.00	0.00	-597.92	-2,946.33	371,532.39	542,714.28	32° 1' 17.121 N	104° 19' 44.007 W
PBHL_Coors 213H - plan hits target center - Point	0.00	0.00	8,293.00	9,718.09	-2,960.16	381,848.40	542,700.44	32° 2' 59.212 N	104° 19' 44.163 W

## Formations

Measured Depth (usft)	Vertical Depth (usft)	Name	Lithology	Dip (°)	Dip Direction (°)
136.00	136.00	Rustler			
407.00	407.00	Top Salt			
1,393.62	1,390.00	Base Salt			
1,602.80	1,596.00	Delaware Mountain Gp			
1,607.89	1,601.00	Lamar			
1,624.20	1,617.00	Bell Canyon			
1,632.36	1,625.00	Ramsey Sand			
2,642.99	2,594.00	Cherry Canyon			
3,622.04	3,514.00	Brushy Canyon			
5,230.01	5,025.00	Bone Spring Lime			
5,341.75	5,130.00	Upper Avalon			
5,662.06	5,431.00	Middle Avalon			
5,952.59	5,704.00	Lower Avalon			
6,124.98	5,866.00	1st Bone Spring Sand			
6,371.87	6,098.00	2nd Bone Spring Carb			
6,893.32	6,588.00	2nd Bone Spring Sand			
7,123.18	6,804.00	3rd Bone Spring Carb			
7,940.47	7,572.00	3rd Bone Spring Sand			
8,207.55	7,810.00	3rd BS W Sand			
8,319.20	7,893.00	Wolfcamp A X Sand			
8,441.59	7,966.00	Wolfcamp A Y Sand			
8,569.50	8,018.00	Wolfcamp A Lower			
16,879.78	8,240.00	Wolfcamp B			



## Planning Report



<b>Database:</b>	TRG_EDMConroe	<b>Local Co-ordinate Reference:</b>	Well Coors Fed Com 213H
<b>Company:</b>	Tap Rock Operating	<b>TVD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Project:</b>	Eddy County, New Mexico (NAD 83)	<b>MD Reference:</b>	Well @ 3488.00usft (H&P 466)
<b>Site:</b>	Coors Fed Com (211H, 211H, 213H, 214H)	<b>North Reference:</b>	Grid
<b>Well:</b>	Coors Fed Com 213H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

## Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
500.00	500.00	0.00	0.00	KOP, 1.00°/100' Build
2,500.00	2,459.63	-136.68	-317.36	Begin 20.00° Tangent
7,953.24	7,584.00	-874.41	-2,030.37	KOP, 11.00°/100' Build & Turn
8,725.49	8,043.50	-545.39	-2,449.22	Begin 88.63° Lateral, 2.00°/100' Turn
10,439.22	8,085.77	1,066.74	-2,948.80	Hold 88.63° Inc, 359.92° Azm
19,093.06	8,293.00	9,718.09	-2,960.16	PBHL

## PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

<b>OPERATOR'S NAME:</b>	Tap Rock Operating LLC
<b>WELL NAME &amp; NO.:</b>	Coors Fed Com 213H
<b>LOCATION:</b>	Sec 20-26S-26E-NMP
<b>COUNTY:</b>	Eddy County, New Mexico <span style="border: 1px solid black; padding: 2px;">▼</span>

COA

<b>H<sub>2</sub>S</b>	<input type="radio"/> No <span style="margin-left: 100px;"><input checked="" type="radio"/> Yes</span>			
<b>Potash / WIPP</b>	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-Q	<input type="checkbox"/> Open Annulus <input type="checkbox"/> WIPP
<b>Cave / Karst</b>	<input type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High	<input checked="" type="radio"/> Critical
<b>Wellhead</b>	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both	<input type="radio"/> Diverter
<b>Cementing</b>	<input type="checkbox"/> Primary Squeeze	<input type="checkbox"/> Cont. Squeeze	<input type="checkbox"/> EchoMeter	<input type="checkbox"/> DV Tool
<b>Special Req</b>	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> Water Disposal	<input checked="" type="checkbox"/> COM	<input type="checkbox"/> Unit
<b>Waste Prev.</b>	<input type="radio"/> Self-Certification	<input checked="" type="radio"/> Waste Min. Plan	<input type="radio"/> APD Submitted prior to 06/10/2024	
<b>Additional Language</b>	<input checked="" type="checkbox"/> Flex Hose <input type="checkbox"/> Four-String	<input type="checkbox"/> Casing Clearance <input type="checkbox"/> Offline Cementing	<input type="checkbox"/> Pilot Hole <input type="checkbox"/> Fluid-Filled	<input checked="" type="checkbox"/> Break Testing

### A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H<sub>2</sub>S) Drilling Plan shall be activated 500 feet prior to drilling into the **Delaware and Bone Springs** formations. As a result, the Hydrogen Sulfide area must meet all requirements from 43 CFR 3176, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

### B. CASING

1. The **11-3/4** inch surface casing shall be set at approximately **350** feet (a minimum of 70 feet (Eddy County) into the Rustler Anhydrite, above the salt, and below usable fresh water) and cemented to the surface. ***Set depth adjusted per BLM geologist.***
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or **500 pounds compressive strength**, whichever is greater. (This is to include the lead cement)
  - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
  - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

2. The minimum required fill of cement behind the **8-5/8** inch intermediate casing is:
  - Cement to surface. If cement does not circulate see B.1.a, c-d above. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**
- ❖ In Critical Cave/Karst Areas cement must come to surface on the first three casing strings.
3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
  - Cement to surface. If cement does not circulate, contact the appropriate BLM office. **Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry due to cave/karst, Capitan Reef, or potash.**

### C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
2. Operator has proposed a multi-bowl wellhead assembly. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. If the cement does not circulate and one-inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
  - e. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172 must be followed.

### D. SPECIAL REQUIREMENT (S)

#### Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in 43 CFR 3171 and 3172.



- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

#### **BOPE Break Testing Variance**

- BOPE Break Testing is ONLY permitted for intervals utilizing a 5M BOPE or less. (**Annular preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP.**)
- BOPE Break Testing is NOT permitted to drilling the production hole section.
- Variance only pertains to the intermediate hole-sections and no deeper than the Bone Springs formation.
- While in transfer between wells, the BOPE shall be secured by the hydraulic carrier or cradle.
- Any well control event while drilling require notification to the BLM Petroleum Engineer (**575-706-2779**) prior to the commencement of any BOPE Break Testing operations.
- A full BOPE test is required prior to drilling the first deep intermediate hole section. If any subsequent hole interval is deeper than the first, a full BOPE test will be required. (200' TVD tolerance between intermediate shoes is allowable).
- The BLM is to be contacted (575-361-2822 Eddy County) 4 hours prior to BOPE tests.
- As a minimum, a full BOPE test shall be performed at 21-day intervals.
- In the event any repairs or replacement of the BOPE is required, the BOPE shall test as per **43 CFR 3172**.
- If in the event break testing is not utilized, then a full BOPE test would be conducted.

## GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

### Contact Eddy County Petroleum Engineering Inspection Staff:

Email or call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220;

**BLM NM CFO DrillingNotifications@BLM.GOV**; (575) 361-2822

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig
    - i. Notify the BLM when moving in and removing the Spudder Rig.
    - ii. Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
    - iii. BOP/BOPE test to be conducted per **43 CFR 3172** as soon as 2<sup>nd</sup> Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. For intervals in which cement to surface is required, cement to surface should be verified with a visual check and density or pH check to differentiate cement from spacer and drilling mud. The results should be documented in the driller's log and daily reports.

### A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following

- conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends of both lead and tail cement, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
  4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
  5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
  6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
  7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
  8. Whenever a casing string is cemented in the R-111-Q potash area, the NMOCD requirements shall be followed.

## **B. PRESSURE CONTROL**

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in **43 CFR 3172**.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - i. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - ii. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - iii. Manufacturer representative shall install the test plug for the initial BOP test.
  - iv. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172.6(b)(9) must be followed.
  - v. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
  - i. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead cement), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
  - ii. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the cement plug. The BOPE test can be initiated after bumping the cement plug with the casing valve open. (only applies to single stage cement jobs, prior to the cement setting up.)
  - iii. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to **43 CFR 3172** with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for 8 hours or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- iv. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- v. The results of the test shall be reported to the appropriate BLM office.
- vi. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- vii. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- viii. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per **43 CFR 3172**.

### **C. DRILLING MUD**

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

### **D. WASTE MATERIAL AND FLUIDS**

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.



## Hydrogen Sulfide Drilling

### Operations Plan

#### Tap Rock Resources

#### 1 H2S safety instructions to the following:

- Characteristics of H2S
- Physical effects and hazards
- Principal and operation of H2S detectors, warning system and briefing areas
- Evacuation procedures, routes and first aid
- Proper use of safety equipment & life support systems
- Essential personnel meeting medical evaluation criteria will receive additional training on the proper use of 30min pressure demand air packs

#### 2 H2S Detection and Alarm Systems:

- H2S sensor/detectors to be located on the drilling rig floor, in the base of the sub structure / cellar area, on the mud pits in the shale shaker area. Additional H2S detectors may be placed as deemed necessary
- An audio alarm system will be installed on the derrick floor and in the doghouse

#### 3 Windssocks and / Wind Streamers:

- Windssocks at mud pit area should be high enough to be visible
- Windssock on the rig floor and / top of doghouse should be high enough to be visible

#### 4 Condition Flags and Signs:

- Warning sign on access road to location
- Flags to be displayed on sign at entrance to location
  - Green Flag – Normal Safe Operation Condition
  - Yellow Flag – Potential Pressure and Danger
  - Red Flag – Danger (H2S present in dangerous concentrations) Only H2S trained personnel admitted on location

#### 5 Well Control Equipment:

- See Drilling Operations Plan Schematics

#### 6 Communication:

- While working under masks chalkboards will be used for communications
- Hand signals will be used where chalk board is inappropriate
- Two way radio will be used to communicate off location in case of emergency help is required. In most cases cellular telephones will be available at most drilling foreman's trailer or living quarters.





#### 7 Drilling Stem Testing:

- No DST cores are planned at this time

8 Drilling contractor supervisor will be required to be familiar with the effects H<sub>2</sub>S has on tubulars good and other mechanical equipment

9 If H<sub>2</sub>S is encountered, mud system will be altered if necessary to maintain control of formation. A mud gas separator will be brought into service along with H<sub>2</sub>S scavengers if necessary

#### 11 Emergency Contacts


<b>Emergency Contacts</b>		
Carlsbad Police Department	575.887.7551	911
Carlsbad Medical Center	575.887.4100	911
Eddy County Fire Service	575.628.5450	911
Eddy County Sherriff	575.887.7551	911
Lea County Fire Service	575.391.2983	911
Lea County Sherriff	575.396.3611	911
Jal Police Department	575.395.2121	911
Jal Fire Department	575.395.2221	911
Tap Rock Resources	720.772.5090	



# Tap Rock Operating, LLC


Coors Fed Com  
H2S Contingency Plan:  
2 Mile Radius Map

Eddy County, New Mexico



Pad Center



1:27,000



NAD 1983 New Mexico State Plane East  
FIPS 3001 Feet



Prepared by Permits West, Inc., Feb 28, 2025  
for Tap Rock Operating, LLC

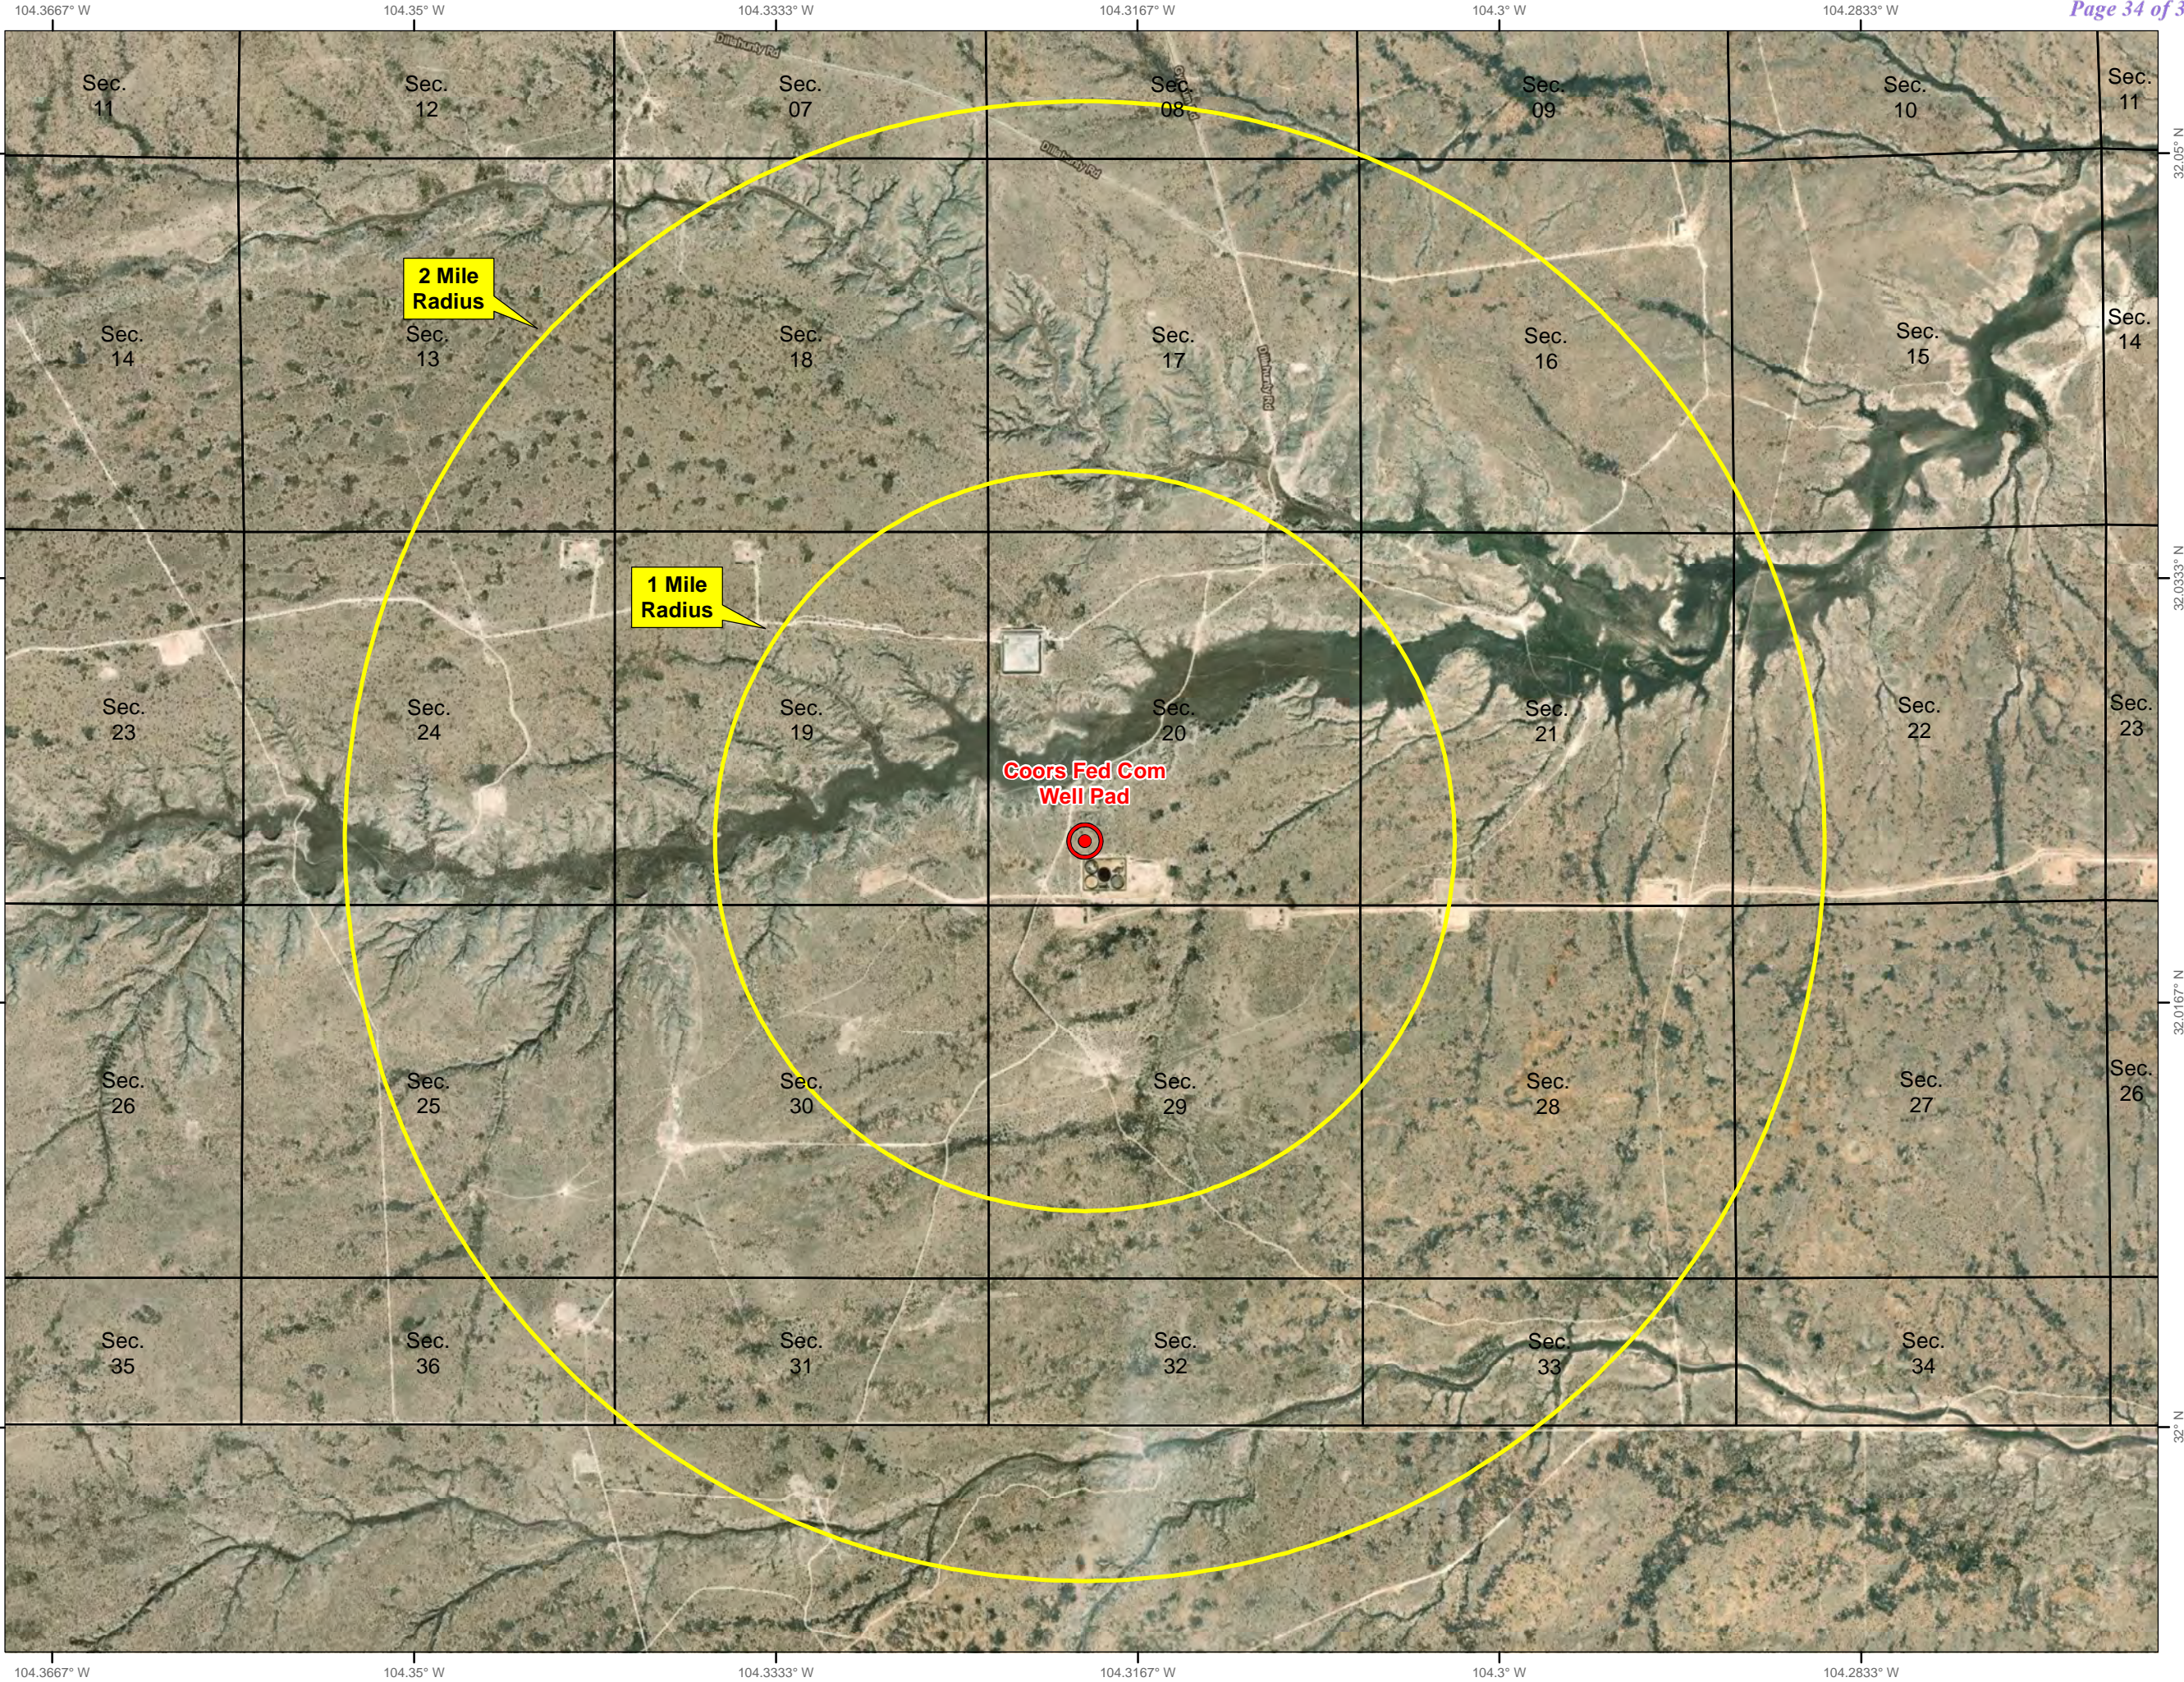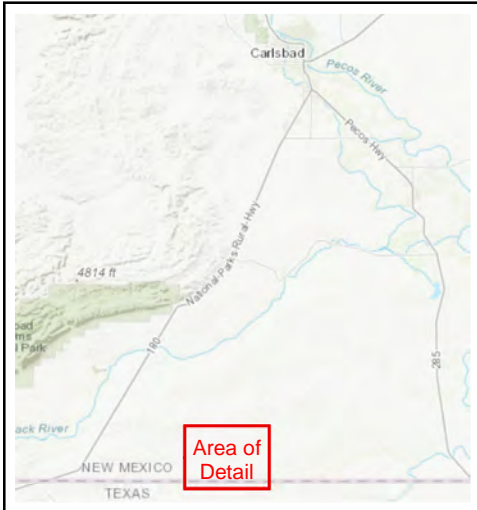



Rig Diagram  
Coors Fed Com  
Well Pad  
Tap Rock Operating, LLC  
20-26S-26E  
Eddy County, NM

N

↑

○

Briefing Area

○

Current Well

△

Flare Stack

◇


H2S Monitor

⤿


Wind Indicator

○

Mud Gas Separator

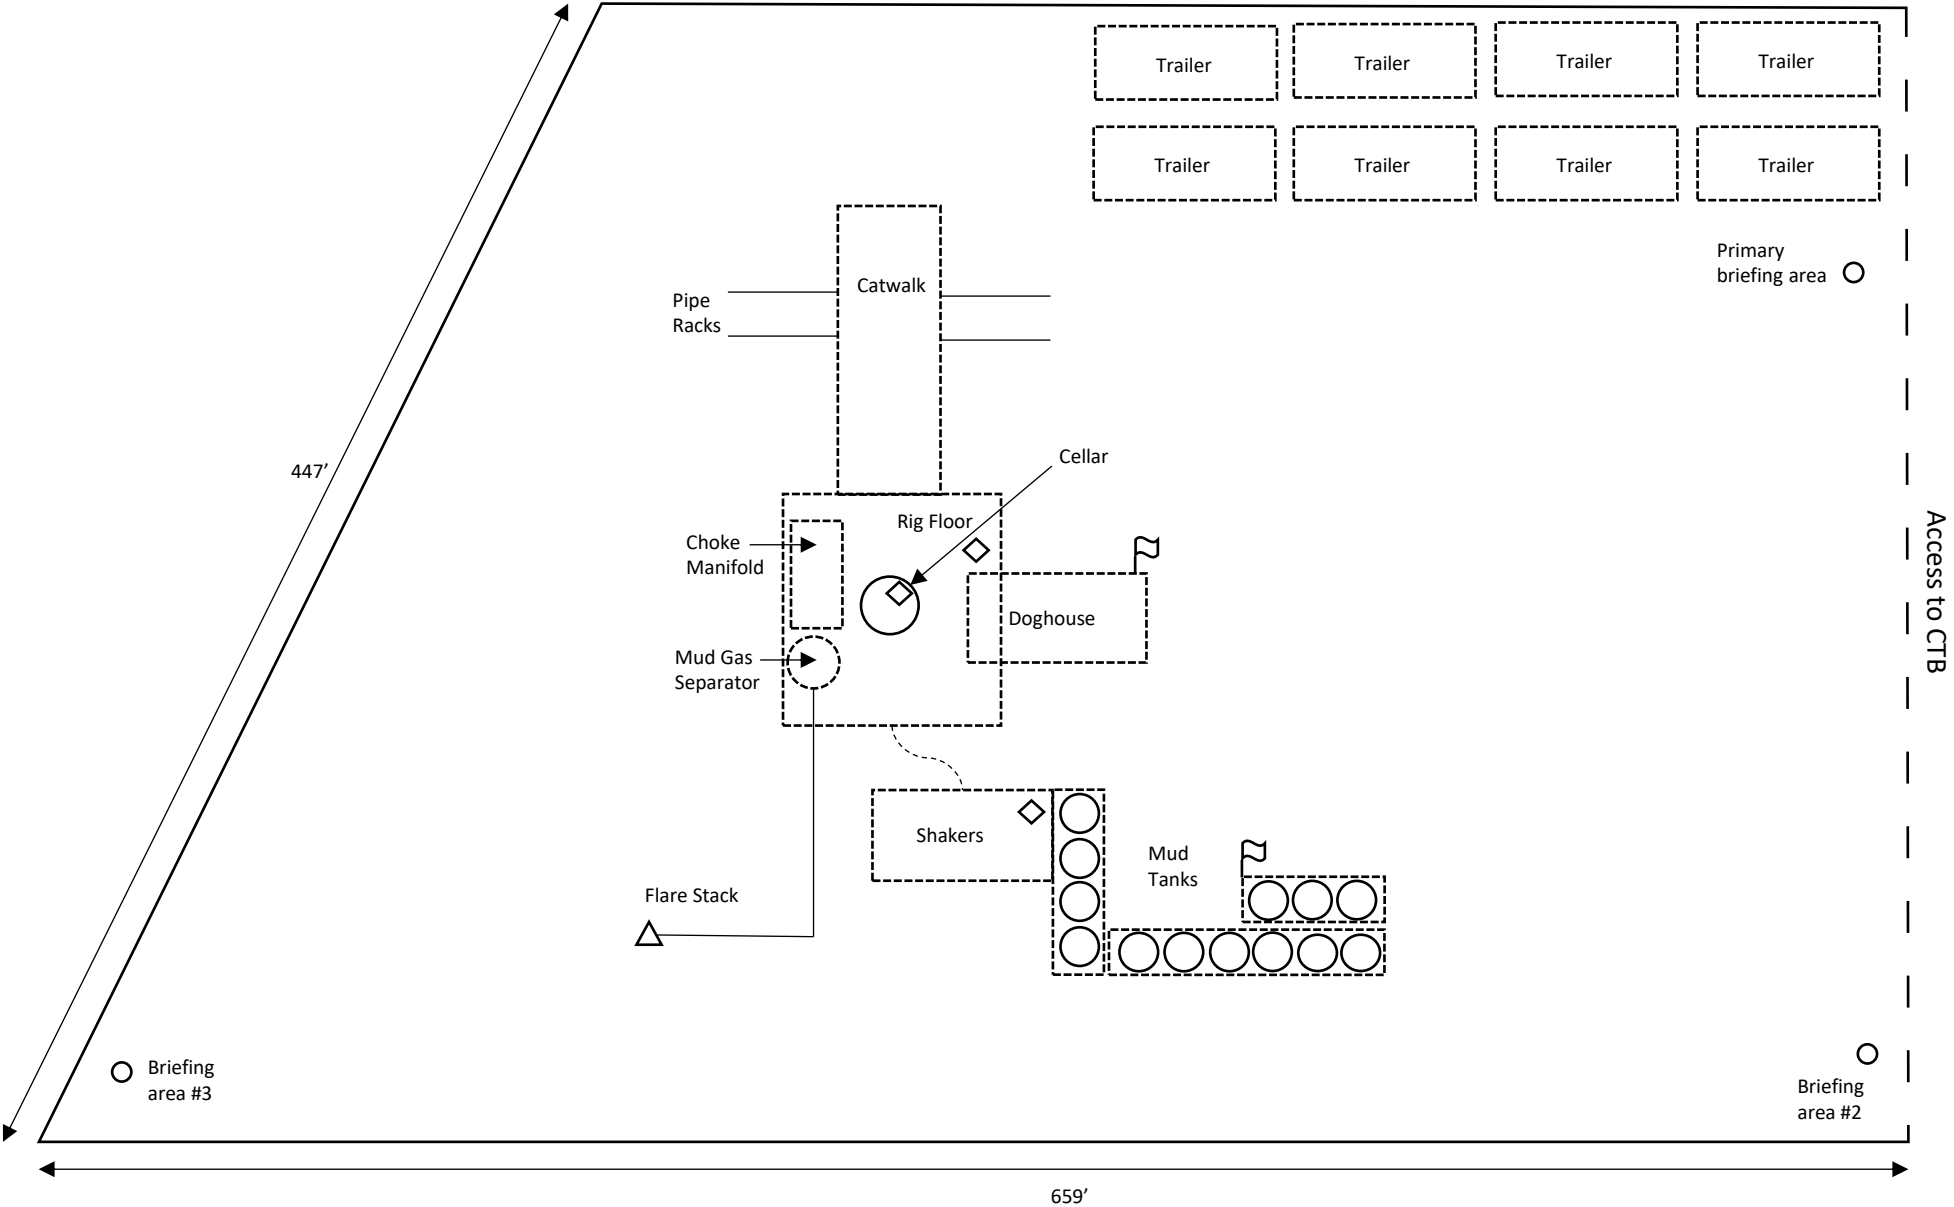

## Avant Natural Resources Closed Loop Mud System Schematic

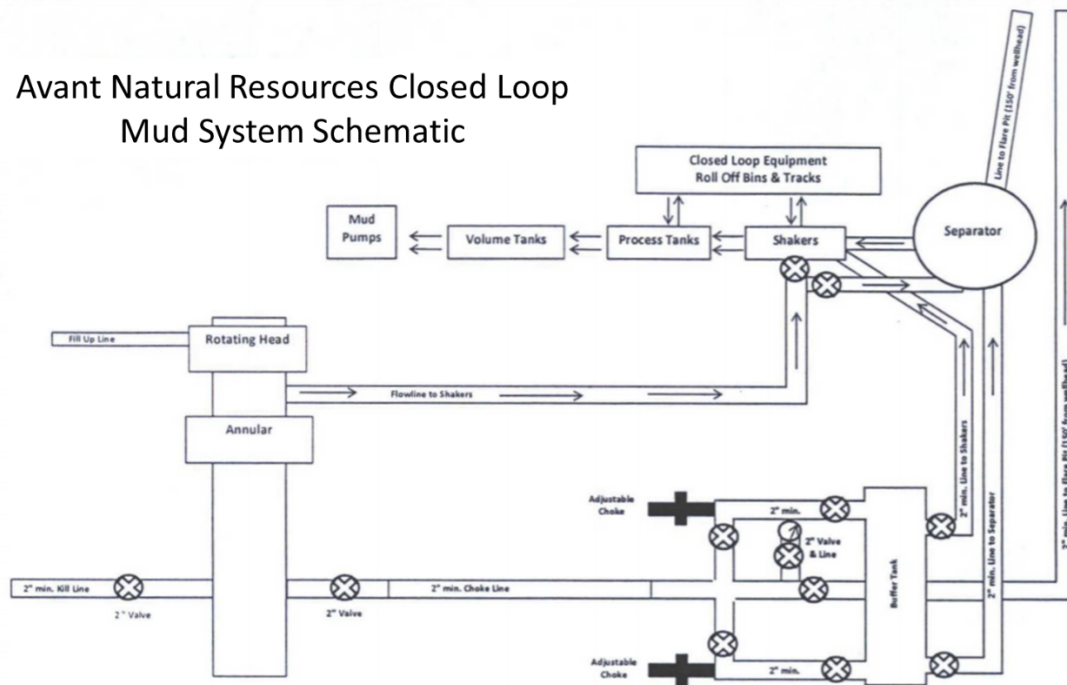

Sante Fe Main Office  
Phone: (505) 476-3441

General Information  
Phone: (505) 629-6116

Online Phone Directory  
<https://www.emnrd.nm.gov/oed/contact-us>

**State of New Mexico**  
**Energy, Minerals and Natural Resources**  
**Oil Conservation Division**  
**1220 S. St Francis Dr.**  
**Santa Fe, NM 87505**

CONDITIONS

Action 464878

**CONDITIONS**

Operator: TAP ROCK OPERATING, LLC 1700 Lincoln St Denver, CO 80203	OGRID: 372043
	Action Number: 464878
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

**CONDITIONS**

Created By	Condition	Condition Date
bwood	Cement is required to circulate on both surface and intermediate1 strings of casing.	5/19/2025
bwood	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	5/19/2025
ward.rikala	Notify the OCD 24 hours prior to casing & cement.	6/21/2025
ward.rikala	File As Drilled C-102 and a directional Survey with C-104 completion packet.	6/21/2025
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	6/21/2025
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	6/21/2025
ward.rikala	Administrative order required for non-standard location prior to production.	6/21/2025
ward.rikala	Administrative order required for non-standard spacing unit prior to production.	6/21/2025
