

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER 1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other 1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No.
2. Name of Operator		9. API Well No. 30-015-57208
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish
13. State		
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)



Approval Date: 08/08/2025

C-102 Submit Electronically Via OCD Permitting	State of New Mexico Energy, Minerals & Natural Resources Department OIL CONSERVATION DIVISION	Revised July 9, 2024	
		Submittal Type:	☒ Initial Submittal
			☐ Amended Report
			☐ As Drilled

WELL LOCATION INFORMATION

API Number 30-015-57208	Pool Code 50270	Pool Name PENASCO DRAW; SA-YESO
Property Code 337736	Property Name FRIESIAN 3 FEDERAL COM	Well Number 10H
OGRID No. 328947	Operator Name SPUR ENERGY PARTNERS LLC.	Ground Level Elevation 3472'
Surface Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal		Mineral Owner: ☐ State ☐ Fee ☐ Tribal ☒ Federal

Surface Location

UL M	Section 2	Township 19S	Range 25E	Lot	Ft. from N/S 1300 FSL	Ft. from E/W 630 FWL	Latitude 32.6863479°N	Longitude 104.4620059°W	County EDDY
----------------	---------------------	------------------------	---------------------	-----	---------------------------------	--------------------------------	---------------------------------	-----------------------------------	-----------------------

Bottom Hole Location

UL M	Section 3	Township 19S	Range 25E	Lot	Ft. from N/S 775 FSL	Ft. from E/W 50 FWL	Latitude 32.6852041°N	Longitude 104.4813800°W	County EDDY
----------------	---------------------	------------------------	---------------------	-----	--------------------------------	-------------------------------	---------------------------------	-----------------------------------	-----------------------

Dedicated Acres 320	Infill or Defining Well INFILL	Defining Well API PENDING	Overlapping Spacing Unit (Y/N) N	Consolidation Code C & F
Order Numbers. PENDING			Well setbacks are under Common Ownership: ☒ Yes ☐ No	

Kick Off Point (KOP)

UL M	Section 2	Township 19S	Range 25E	Lot	Ft. from N/S 957 FSL	Ft. from E/W 751 FWL	Latitude 32.6853963°N	Longitude 104.4615958°W	County EDDY
----------------	---------------------	------------------------	---------------------	-----	--------------------------------	--------------------------------	---------------------------------	-----------------------------------	-----------------------


First Take Point (FTP)

UL P	Section 3	Township 19S	Range 25E	Lot	Ft. from N/S 775 FSL	Ft. from E/W 100 FEL	Latitude 32.6849614°N	Longitude 104.4643500°W	County EDDY
----------------	---------------------	------------------------	---------------------	-----	--------------------------------	--------------------------------	---------------------------------	-----------------------------------	-----------------------

Last Take Point (LTP)

UL M	Section 3	Township 19S	Range 25E	Lot	Ft. from N/S 775 FSL	Ft. from E/W 100 FWL	Latitude 32.6852019°N	Longitude 104.4812176°W	County EDDY
----------------	---------------------	------------------------	---------------------	-----	--------------------------------	--------------------------------	---------------------------------	-----------------------------------	-----------------------

Unitized Area or Area of Uniform Interest Y	Spacing Unit Type ☒ Horizontal ☐ Vertical	Ground Floor Elevation: 3472' GF
---	--	--

OPERATOR CERTIFICATIONS <i>I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and, if the well is a vertical or directional well, that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of a working interest or unleased mineral interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.</i> <i>If this well is a horizontal well, I further certify that this organization has received the consent of at least one lessee or owner of a working interest or unleased mineral interest in each tract (in the target pool or formation) in which any part of the well's completed interval will be located or obtained a compulsory pooling order from the division.</i> Sarah Chapman 12/30/2024 Signature Date		SURVEYOR CERTIFICATIONS <i>I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me under my supervision, and that the same is true and correct to the best of my belief.</i>  Signature and Seal of Professional Surveyor	
SARAH CHAPMAN Printed Name		14400 Certificate Number	
SCHAPMAN@SPURENERGY.COM Email Address		10/14/2024 Date of Survey	


Note: No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

ACREAGE DEDICATION PLATS

This grid represents a standard section. You may superimpose a non-standard section, or larger area, over this grid. Operators must outline the dedicated acreage in a red box, clearly show the well surface location and bottom hole location, if it is a directionally drilled, with the dimensions from the section lines in the cardinal directions. If this is a horizontal wellbore show on this plat the location of the First Take Point and Last Take Point, and the point within the Completed interval (other than the First Take Point or Last Take Point) that is closest to any outer boundary of the tract.

Surveyors shall use the latest United States government survey or dependent resurvey. Well locations will be in reference to the New Mexico Principal Meridian. If the land is not surveyed, contact the OCD Engineering Bureau. Independent subdivision surveys will not be acceptable.

FRIESIAN 3 FEDERAL COM #10H

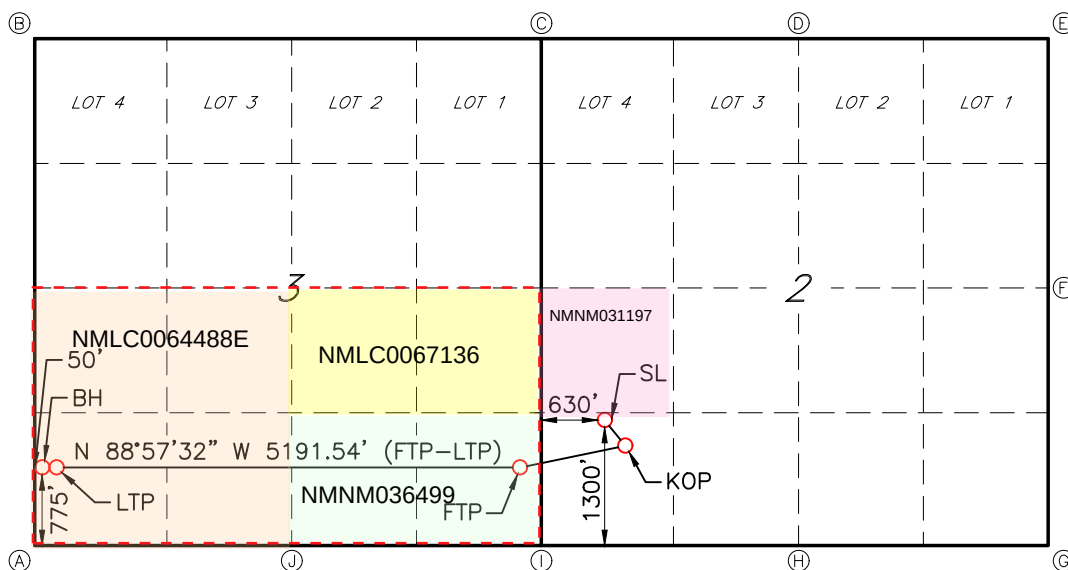

11/07/2024

GEODETIC DATA

NAD 83 GRID - NM EAST

SURFACE LOCATION (SL)

N: 613448.6 - E: 501750.5

LAT: 32.6863479° N
LONG: 104.4620059° W

KICK OFF POINT (KOP)

957' FSL & 751' FWL (SEC.2)
N: 613102.2 - E: 501876.3LAT: 32.6853963° N
LONG: 104.4615958° W

FIRST TAKE POINT (FTP)

775' FSL & 100' FEL (SEC.3)
N: 612945.0 - E: 501028.7LAT: 32.6849614° N
LONG: 104.4643500° W

LAST TAKE POINT (LTP)

775' FSL & 100' FWL (SEC.3)
N: 613039.3 - E: 495839.3LAT: 32.6852019° N
LONG: 104.4812176° W

BOTTOM HOLE (BH)

N: 613040.2 - E: 495789.3

LAT: 32.6852041° N
LONG: 104.4813800° W


CORNER DATA

NAD 83 GRID - NM EAST


A: FOUND MOUND OF STONES
N: 612266.3 - E: 495736.5B: CALCULATED CORNER
N: 617562.6 - E: 495756.1C: FOUND 3" PIPE
N: 617517.7 - E: 501061.4D: FOUND 3/8" REBAR
N: 617459.6 - E: 503718.1E: FOUND 1/2" REBAR
N: 617394.9 - E: 506366.1F: FOUND 1/2" REBAR
N: 614647.4 - E: 506352.6G: FOUND 1/2" REBAR
N: 612008.3 - E: 506339.4H: FOUND 1" BOLT
N: 612088.5 - E: 503739.5I: FOUND 1-1/2" PIPE
N: 612168.4 - E: 501140.0J: FOUND MOUND OF STONES
N: 612218.7 - E: 498438.8

JOB #: LS24090798D1

Dagger Draw Paddock Type Curve

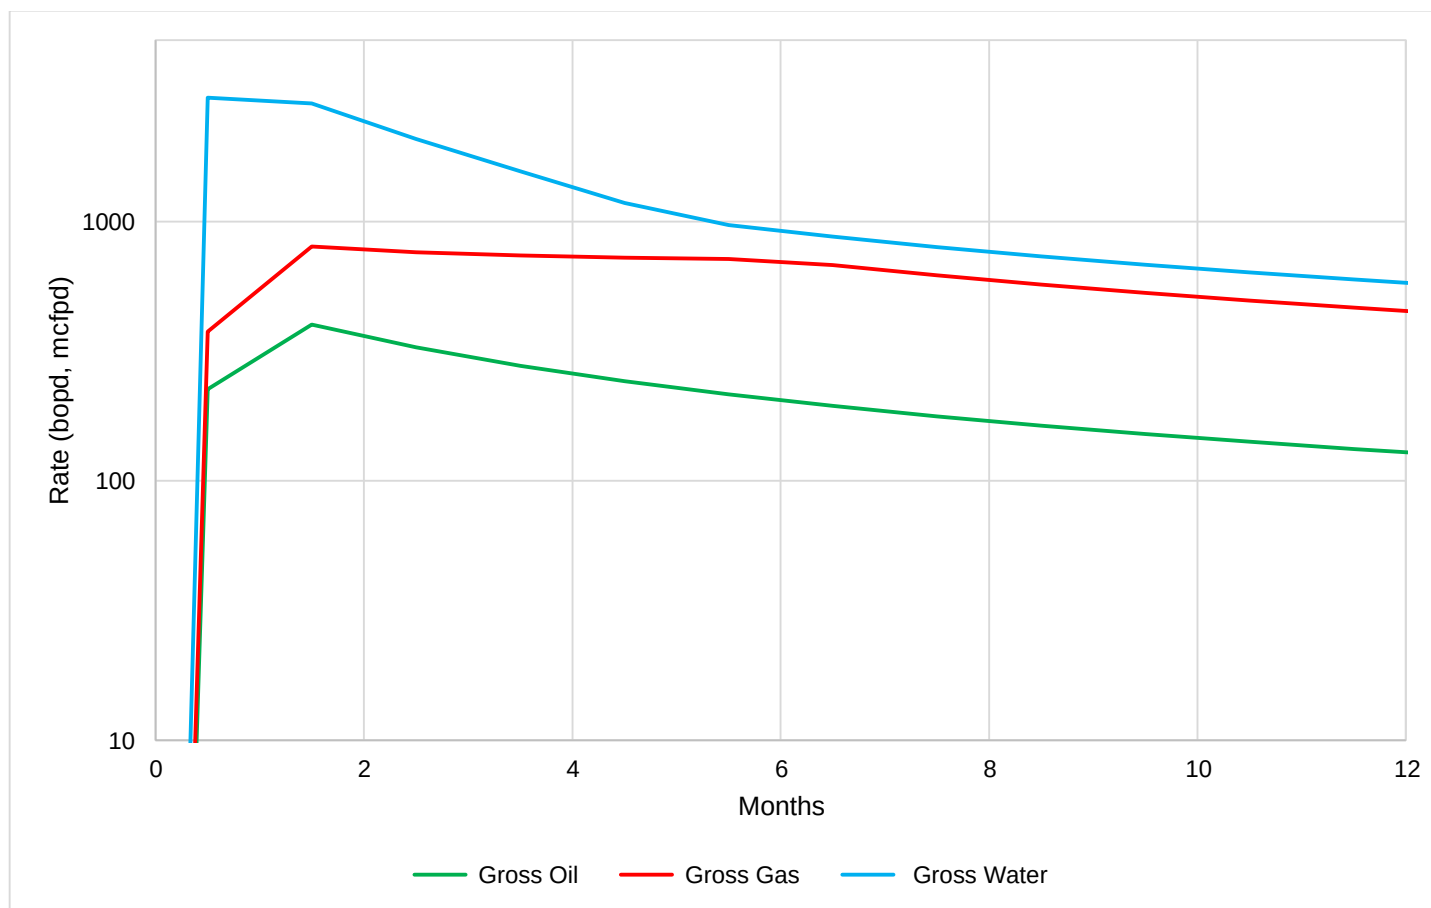

Dagger Draw Blinebry Type Curve

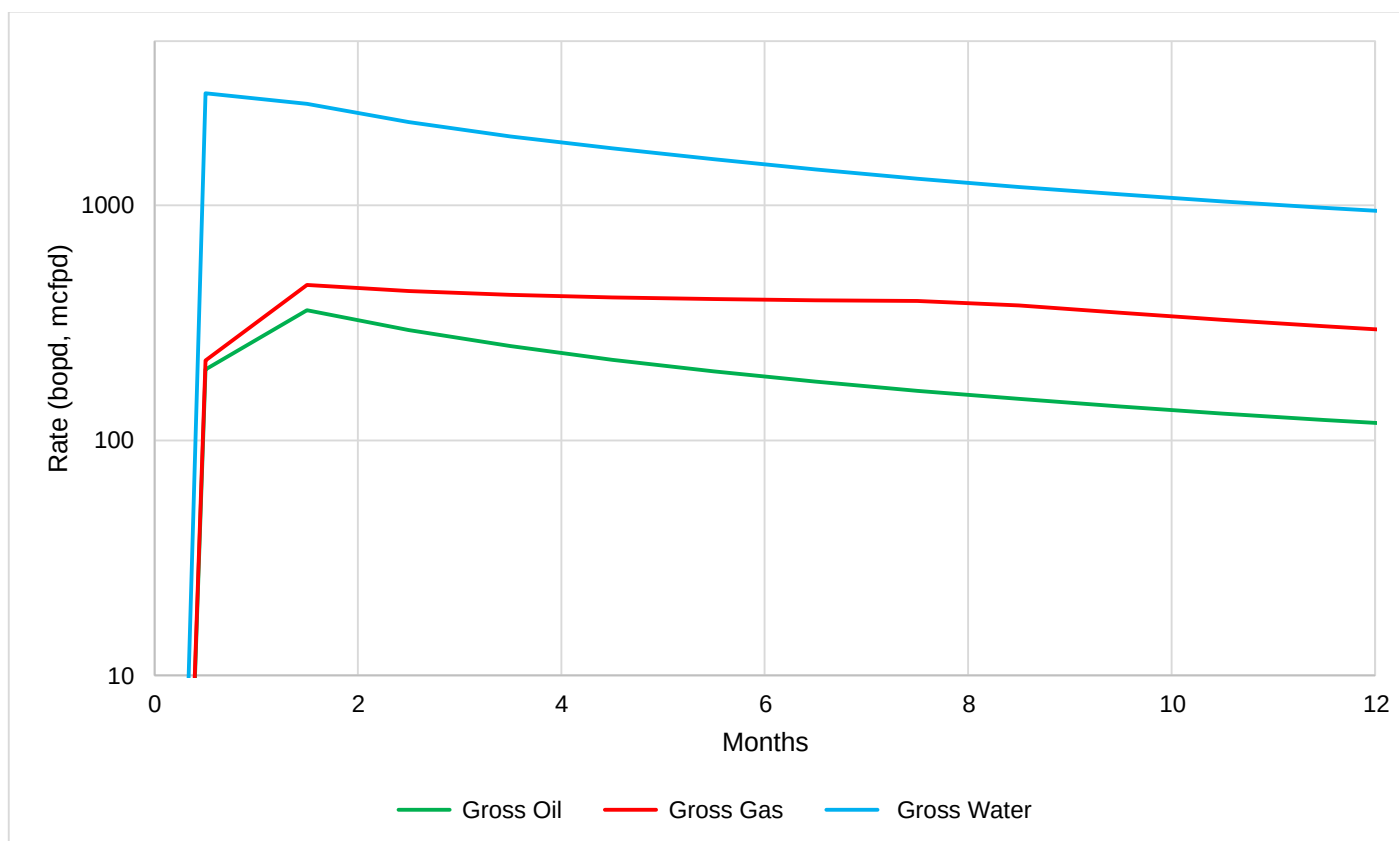

State of New Mexico
Energy, Minerals and Natural Resources DepartmentSubmit Electronically
Via E-permittingOil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505**NATURAL GAS MANAGEMENT PLAN**

This Natural Gas Management Plan must be submitted with each Application for Permit to Drill (APD) for a new or recompleted well.

Section 1 – Plan Description
Effective May 25, 2021**I. Operator:** SPUR ENERGY PARTNERS LLC **OGRID:** 328947 **Date:** 12 / 19 / 2024**II. Type:** ☒ Original ☐ Amendment due to ☐ 19.15.27.9.D(6)(a) NMAC ☐ 19.15.27.9.D(6)(b) NMAC ☐ Other.

If Other, please describe: _____

III. Well(s): Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	ULSTR	Footages	Anticipated Oil BBL/D	Anticipated Gas MCF/D	Anticipated Produced Water BBL/D
FRESIAN 3 FEDERAL COM 1H	30-015-	L-2-19S-25E	1320' FSL 630' FWL	293 BBL/D	557 MCF/D	1172 BBL/D
FRESIAN 3 FEDERAL COM 10H	30-015-	M-2-19S-25E	1300' FSL 630' FWL	393 BBL/D	430 MCF/D	1672 BBL/D
FRESIAN 3 FEDERAL COM 11H	30-015-	L-2-19S-25E	1360' FSL 630' FWL	393 BBL/D	430 MCF/D	1672 BBL/D
FRESIAN 3 FEDERAL COM 70H	30-015-	M-2-19S-25E	1280' FSL 630' FWL	279 BBL/D	447 MCF/D	558 BBL/D
FRESIAN 3 FEDERAL COM 71H	30-015-	L-2-19S-25E	1340' FSL 630' FWL	279 BBL/D	447 MCF/D	558 BBL/D

IV. Central Delivery Point Name: FRESIAN 3 FEDERAL COM TANK BATTERY [See 19.15.27.9(D)(1) NMAC]**V. Anticipated Schedule:** Provide the following information for each new or recompleted well or set of wells proposed to be drilled or proposed to be recompleted from a single well pad or connected to a central delivery point.

Well Name	API	Spud Date	TD Reached Date	Completion Commencement Date	Initial Flow Back Date	First Production Date
FRESIAN 3 FEDERAL COM 1H	30-015-	09/24/2025	09/29/2025	12/05/2025	01/01/2026	01/09/2026
FRESIAN 3 FEDERAL COM 10H	30-015-	09/29/2025	10/05/2025	12/05/2025	01/01/2026	01/09/2026
FRESIAN 3 FEDERAL COM 11H	30-015-	10/05/2025	10/13/2025	12/05/2025	01/01/2026	01/09/2026
FRESIAN 3 FEDERAL COM 70H	30-015-	10/13/2025	10/21/2025	12/05/2025	01/01/2026	01/09/2026
FRESIAN 3 FEDERAL COM 71H	30-015-	10/21/2025	10/29/2025	12/05/2025	01/01/2026	01/09/2026

VI. Separation Equipment: ☒ Attach a complete description of how Operator will size separation equipment to optimize gas capture.**VII. Operational Practices:** ☒ Attach a complete description of the actions Operator will take to comply with the requirements of Subsection A through F of 19.15.27.8 NMAC.**VIII. Best Management Practices:** ☒ Attach a complete description of Operator's best management practices to minimize venting during active and planned maintenance.

Section 2 – Enhanced Plan

EFFECTIVE APRIL 1, 2022

Beginning April 1, 2022, an operator that is not in compliance with its statewide natural gas capture requirement for the applicable reporting area must complete this section.

☒ Operator certifies that it is not required to complete this section because Operator is in compliance with its statewide natural gas capture requirement for the applicable reporting area.

IX. Anticipated Natural Gas Production:

Well	API	Anticipated Average Natural Gas Rate MCF/D	Anticipated Volume of Natural Gas for the First Year MCF

X. Natural Gas Gathering System (NGGS):

Operator	System	ULSTR of Tie-in	Anticipated Gathering Start Date	Available Maximum Daily Capacity of System Segment Tie-in

XI. Map. ☐ Attach an accurate and legible map depicting the location of the well(s), the anticipated pipeline route(s) connecting the production operations to the existing or planned interconnect of the natural gas gathering system(s), and the maximum daily capacity of the segment or portion of the natural gas gathering system(s) to which the well(s) will be connected.

XII. Line Capacity. The natural gas gathering system ☐ will ☐ will not have capacity to gather 100% of the anticipated natural gas production volume from the well prior to the date of first production.

XIII. Line Pressure. Operator ☐ does ☐ does not anticipate that its existing well(s) connected to the same segment, or portion, of the natural gas gathering system(s) described above will continue to meet anticipated increases in line pressure caused by the new well(s).

☐ Attach Operator's plan to manage production in response to the increased line pressure.

XIV. Confidentiality: ☐ Operator asserts confidentiality pursuant to Section 71-2-8 NMSA 1978 for the information provided in Section 2 as provided in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and attaches a full description of the specific information for which confidentiality is asserted and the basis for such assertion.

Section 3 - Certifications

Effective May 25, 2021

Operator certifies that, after reasonable inquiry and based on the available information at the time of submittal:

☒ Operator will be able to connect the well(s) to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system; or

☐ Operator will not be able to connect to a natural gas gathering system in the general area with sufficient capacity to transport one hundred percent of the anticipated volume of natural gas produced from the well(s) commencing on the date of first production, taking into account the current and anticipated volumes of produced natural gas from other wells connected to the pipeline gathering system.

If Operator checks this box, Operator will select one of the following:

Well Shut-In. ☐ Operator will shut-in and not produce the well until it submits the certification required by Paragraph (4) of Subsection D of 19.15.27.9 NMAC; or

Venting and Flaring Plan. ☐ Operator has attached a venting and flaring plan that evaluates and selects one or more of the potential alternative beneficial uses for the natural gas until a natural gas gathering system is available, including:

- (a) power generation on lease;
- (b) power generation for grid;
- (c) compression on lease;
- (d) liquids removal on lease;
- (e) reinjection for underground storage;
- (f) reinjection for temporary storage;
- (g) reinjection for enhanced oil recovery;
- (h) fuel cell production; and
- (i) other alternative beneficial uses approved by the division.

Section 4 - Notices

1. If, at any time after Operator submits this Natural Gas Management Plan and before the well is spud:

(a) Operator becomes aware that the natural gas gathering system it planned to connect the well(s) to has become unavailable or will not have capacity to transport one hundred percent of the production from the well(s), no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised venting and flaring plan containing the information specified in Paragraph (5) of Subsection D of 19.15.27.9 NMAC; or

(b) Operator becomes aware that it has, cumulatively for the year, become out of compliance with its baseline natural gas capture rate or natural gas capture requirement, no later than 20 days after becoming aware of such information, Operator shall submit for OCD's approval a new or revised Natural Gas Management Plan for each well it plans to spud during the next 90 days containing the information specified in Paragraph (2) of Subsection D of 19.15.27.9 NMAC, and shall file an update for each Natural Gas Management Plan until Operator is back in compliance with its baseline natural gas capture rate or natural gas capture requirement.

2. OCD may deny or conditionally approve an APD if Operator does not make a certification, fails to submit an adequate venting and flaring plan which includes alternative beneficial uses for the anticipated volume of natural gas produced, or if OCD determines that Operator will not have adequate natural gas takeaway capacity at the time a well will be spud.

I certify that, after reasonable inquiry, the statements in and attached to this Natural Gas Management Plan are true and correct to the best of my knowledge and acknowledge that a false statement may be subject to civil and criminal penalties under the Oil and Gas Act.

Signature:	<i>Sarah Chapman</i>
Printed Name:	SARAH CHAPMAN
Title:	REGULATORY DIRECTOR
E-mail Address:	SCHAPMAN@SPUREENERGY.COM
Date:	DECEMBER 19, 2024
Phone:	832-930-8613
OIL CONSERVATION DIVISION (Only applicable when submitted as a standalone form)	
Approved By:	
Title:	
Approval Date:	
Conditions of Approval:	



Natural Gas Management Plan – Attachment

VI. Separation equipment will be sized by construction engineering staff based on anticipated daily production to ensure adequate capacity.

VII. Spur Energy Partners LLC (“Spur”) will take the following actions to comply with the regulations listed in 19.15.27.8:

- A. Spur will maximize the recovery of natural gas by minimizing waste, as defined by 19.15.2 NMAC, of natural gas through venting and flaring. Spur will ensure that our wells will be connected to a natural gas gathering system with sufficient capacity to transport natural gas.
- B. All drilling operations will be equipped with a rig flare at least 100 feet from the nearest surface hole location. Rig flare will be utilized to combust any natural gas that is brought to surface during normal operations. In the case of emergency, flaring volumes will be reported appropriately.
- C. During completion operations any natural gas brought to surface will be flared. Immediately following completion operations, wells will flow to permanent separation equipment. Produced natural gas from separation equipment will be sent to sales. If natural gas does not meet gathering pipeline specifications, Spur will flare for 60 days or until natural gas meets the pipeline specifications. Spur will ensure flare is properly sized and is equipped with an automatic igniter or continuous pilot. Gas samples will be taken twice per week and natural gas will be routed into a gathering system as soon as the pipeline specifications are met.
- D. Natural gas will not be flared with the exception of 19.15.27.8(D)(1-4). If there is no adequate takeaway for the separator gas, wells will be shut-in until that natural gas gathering system is available with exception of emergency or malfunction situations. Volumes will be reported appropriately.
- E. Spur will comply with performance standards pursuant to 19.15.27.8(E)(1-8). All equipment will be designed and sized to handle maximum pressures to minimize waste. Storage tanks constructed after May 25, 2021 will be equipped with an automatic gauging system that reduces venting of natural gas. Flare stacks installed or replaced after May 25, 2021 will be equipped with an automatic igniter or continuous pilot. Spur will conduct AVO inspections as described in 19.15.27.8(E)(5)(a) with frequencies specified in 19.15.27.8(E)(5)(b) and (c). All emergencies or malfunctions will be resolved as quickly and safely as possible to minimize waste.
- F. The volume of natural gas that is vented or flared as the result of an emergency or malfunction during drilling and/or completion operations will be estimated and reported accordingly. The volume of natural gas that is vented, flared or beneficially used during production operations, will be measured and reported accordingly. Spur will install equipment to measure the volume of natural gas flared from existing piping or a flowline piped from equipment such as high-pressure separators, heater treaters, or VRUs associated with a well or facility associated with a well authorized by an APD after May 25, 2021 that has an average daily production of less than 60,000 cubic feet of natural gas. If metering is not practicable due to circumstances such as low flow rate or low pressure venting or flaring, Spur will estimate the volume of flared or vented natural gas. Measuring equipment will conform to industry standards and will not be equipped with a manifold



that allows the diversion of natural gas around the metering element except for the sole purpose of inspecting and servicing equipment.

VIII. For maintenance activities involving production equipment and compression, venting be limited to the depressurization of the subject equipment to ensure safe working conditions. For maintenance of production equipment, the associated producing wells will be shut-in to eliminate venting. For maintenance of VRUs, all natural gas normally routed to the VRU will be routed to flare.

Spur Energy Partners LLC – Friesian 3 Federal Com 10H

1. Geologic Formations

TVD of Target	2,475'
MD at TD	8,464'

Formation	Depth	Lithology	Expected Fluids
Quaternary	0'	Dolomite, other: Caliche	Useable Water
Rustler		Not Present	
Top Salt		Not Present	
Base Salt		Not Present	
Yates		Not Present	
Seven Rivers		Not Present	
Queen		Not Present	
Grayburg	585'	Dolomite, Sandstone, Anhydrite	Natural Gas, Oil
San Andres	745'	Dolomite, Limestone	Natural Gas, Oil
Middle San Andres	1050'	Dolomite, Limestone	Natural Gas, Oil
Glorieta	2230'	Dolomite, Siltstone	Natural Gas, Oil
Paddock	2340'	Dolomite, Limestone	Natural Gas, Oil
Blinebry	3000'	Dolomite, Limestone	Natural Gas, Oil
Tubb	4050'	Dolomite, Limestone	Natural Gas, Oil

*H₂S, water flows, loss of circulation, abnormal pressures, etc.

2. Casing Program

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

Casing Formation Set Interval	Hole Size (in)	Casing Interval		Csg. Size (in)	Weight (lbs)	Grade	Conn.	SF	SF Burst	Body SF Tension	Joint SF Tension
		From (ft)	To (ft)					Collapse			
San Andres	12.25	0	1200	9.625	36	J-55	BTC	1.125	1.2	1.4	1.4
N/A	8.75	0	2950	7	32	L-80	BK-HT	1.125	1.2	1.4	1.4
Yeso	8.75	2950	8464	5.5	20	L-80	BK-HT	1.125	1.2	1.4	1.4
SF Values will meet or Exceed											

Spur Energy Partners LLC – Friesian 3 Federal Com 10H

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

3. Cementing Program

Casing String	Top (ft)	Bottom (ft)	% Excess
Surface (Lead)	0	950	100%
Surface (Tail)	950	1200	100%
Production (Lead)	0	1950	100%
Production (Tail)	1950	8464	25%

Casing String	# Sks	Wt. (lb/gal)	Yld (ft ³ /sack)	H ₂ O (gal/sk)	500# Comp. Strength (hours)	Slurry Description
Surface (Lead)	259	12	2.4	13.48	08:12	Clas C Premium Plus Cement
Surface (Tail)	94	13.2	1.87	9.92	06:59	Clas C Premium Plus Cement
Production (Lead)	176	11.4	2.42	15.29	N/A	Clas C Premium Plus Cement
Production (Tail)	1240	13.2	1.56	9.81	N/A	Clas C Premium Plus Cement

Spur Energy Partners LLC – Friesian 3 Federal Com 10H

4. Pressure Control Equipment

Spur Energy Partners LLC variance for flex hose

Spur requests a variance to use a flex line from the BOP to the choke manifold. Documentation will be attached in the APD and be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no bends).

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
12.25" Hole	13-5/8"	5M	Annular	✓	70% of working pressure
		5M	Blind Ram	✓	250 psi / 3000 psi
			Pipe Ram	✓	
			Double Ram		
			Other*		
8.75" Hole	13-5/8"	5M	Annular	✓	70% of working pressure
		5M	Blind Ram	✓	250 psi / 3000 psi
			Pipe Ram	✓	
			Double Ram		
			Other*		

Spur Energy Partners LLC will be utilizing a 5M BOP

Condition	Specify what type and where?
BH Pressure at deepest TVD	1146 psi
Abnormal Temperature	No
BH Temperature at deepest TVD	100°F

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

Formation integrity test will be performed per Onshore Order #2.
--

Spur Energy Partners LLC – Friesian 3 Federal Com 10H

	On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	Are anchors required by manufacturer?
	A conventional wellhead system will be employed. The wellhead and connection to the BOPE will meet all API 6A requirements. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. See attached schematics.

5. BOP Break Testing Request

Spur Energy Partners LLC requests permission to adjust the BOP break testing requirements as follows:

BOP break test under the following conditions:

- After a full BOP test is conducted
- When skidding to drill the production section, where the surface casing point is shallower than the 3 Bone Spring or 10,000 TVD.
- When skidding to drill a production section that does not penetrate the 3rd Bone Spring or deeper.

If the kill line is broken prior to skid, four tests will be performed.

- 1) The void between the wellhead and the spool (this consists of two tests)
- 2) The spool between the kill lines and the choke manifold (this consists of two tests)

If the kill line is not broken prior to skid, two tests will be performed.

- 1) The void between the wellhead and the pipe rams

6. Mud Program

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times. The following is a general list of products: Barite, Bentonite, Gypsum, Lime, Soda Ash, Caustic Soda, Nut Plug, Cedar Fiber, Cotton Seed Hulls, Drilling Paper, Salt Water Clay, CACL2. Spur will use a closed mud system.

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From (ft)	To (ft)				
0	1200	Water-Based Mud	8.6-8.9	32-36	N/C
1200	8464	Water-Based Mud	8.6-8.9	32-36	N/C

What will be used to monitor the loss or gain of fluid?	PVT/PASON/Visual Monitoring
---	-----------------------------

Spur Energy Partners LLC – Friesian 3 Federal Com 10H

7. Logging and Testing Procedures

Logging, Coring and Testing.		
Yes	Will run GR from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.	
No	Logs are planned based on well control or offset log information.	
No	Drill stem test? If yes, explain	
No	Coring? If yes, explain	
Additional logs planned		Interval
No	Resistivity	
No	Density	
No	CBL	
Yes	Mud log	SCP - TD
No	PEX	

8. Drilling Conditions

Pump high viscosity sweeps as needed for hole cleaning. The mud system will be monitored visually/manually as well as with an electronic PVT. The necessary mud products for additional weight and fluid loss control will be on location at all times. Appropriately weighted mud will be used to isolate potential gas, oil, and water zones until such time as casing can be cemented into place for zonal isolation.

Hydrogen Sulfide (H ₂ S) monitors will be installed prior to drilling out the surface shoe. If H ₂ S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.	
N	H ₂ S is present
Y	H ₂ S Plan attached

Total estimated cuttings volume: 804.4 bbls.

Spur Energy Partners LLC – Friesian 3 Federal Com 10H**9. Other facets of operation**

	Yes/No
Will more than one drilling rig be used for drilling operations? If yes, describe. Spur Energy Partners LLC. requests the option to contract a Surface Rig to drill, set surface casing, and cement for this well. If the timing between rigs is such that Spur Energy Partners LLC. would not be able to preset surface, the Primary Rig will MIRU and drill the well in its entirety per the APD. Please see the attached document for information on the spudder rig.	Yes

Attachments

- ☒ Directional Plan
☒ H2S Contingency Plan
☒ Akita 57 Attachments
☒ BOP Schematics
☒ Transcend Spudder Rig Attachments

10. Company Personnel

Name	Title	Office Phone	Mobile Phone
Christopher Hollis	D&C Manager	832-930-8629	713-380-7754
Ryan Barber	Senior D&C Engineer	832-930-8502	832-544-9267
Johnny Nabors	EVP Operations	832-930-8502	281-904-8811






Spur Energy Partners
Well Name: Friesian 3 Federal Com 10H
Project: Eddy County, NM
Wellbore: Wellbore #1
Plan: Plan #1
Rig: Akita 57




SURFACE LOCATION		Ground Elevation: 3472.00 KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))			
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.00	0.00	613448.60	501750.50	32.68634801	-104.46200593

TARGET LOCATIONS						
Name	TVD	+N/-S	+E/-W	Northing	Easting	
PBHL (Friesian 3 Federal Com 10H)	2475.00	-408.40	-5961.20	613040.20	495789.30	
LTP (Friesian 3 Federal Com 10H)	2476.76	-409.30	-5911.20	613039.30	495839.30	
FTP (Friesian 3 Federal Com 10H)	2660.00	-503.60	-721.80	612945.00	501028.70	

SECTION DETAILS:										
Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect	Annotation
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2	300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	KOP - Start Build @ 2°/100'
3	1390.43	21.81	160.05	1364.29	-192.72	69.97	2.00	160.05	-73.46	EOB @ 1390.43' MD, 1364.29' TVD, 21.81° INC
4	1830.50	21.81	160.05	1772.86	-346.40	125.77	0.00	0.00	-132.03	Start Build & Turn @ 8°/100'
5	2700.22	60.00	271.04	2483.60	-512.32	-241.98	8.00	120.37	232.64	EOB & T @ 2700.22' MD, 2483.60' TVD, 60.00° INC, 271.04° Azi
6	2900.22	60.00	271.04	2583.59	-509.17	-415.16	0.00	0.00	405.85	Start Build @ 10°/100'
7	3220.44	92.02	271.04	2660.00	-503.60	-721.80	10.00	0.00	712.54	Landing Point @ 3220.44' MD, 2660.00' TVD, 92.02° INC, 271.04° Azi
8	8463.97	92.02	271.04	2475.00	-408.40	-5961.20	0.00	0.00	5952.81	TD @ 8463.97' MD, 2475.00' TVD

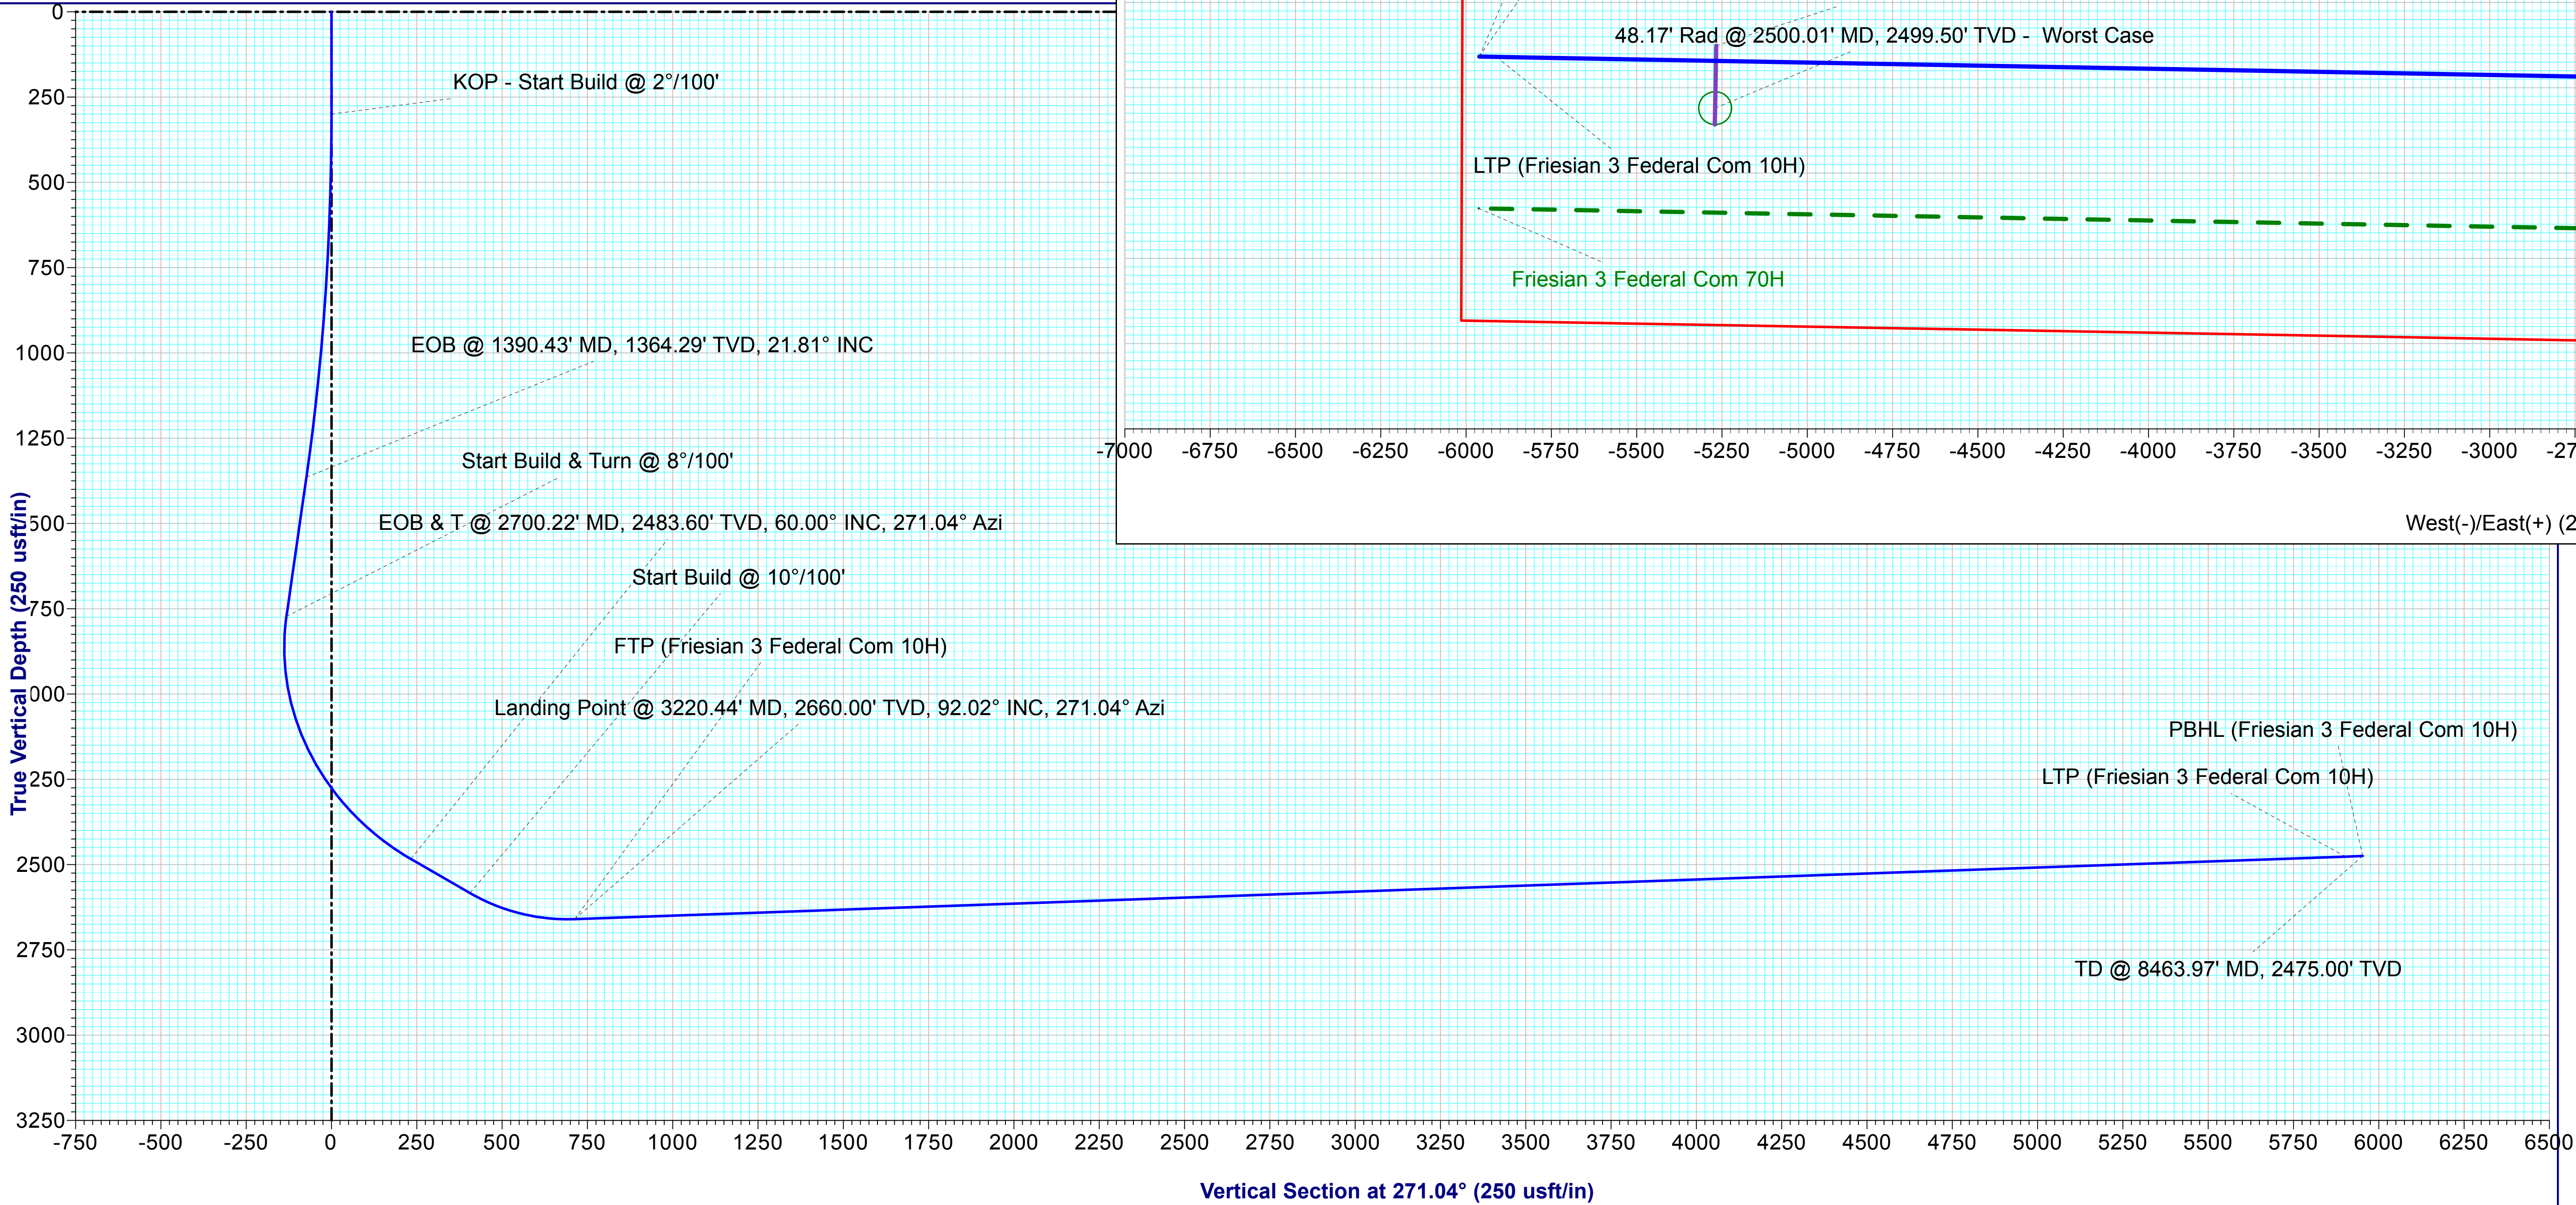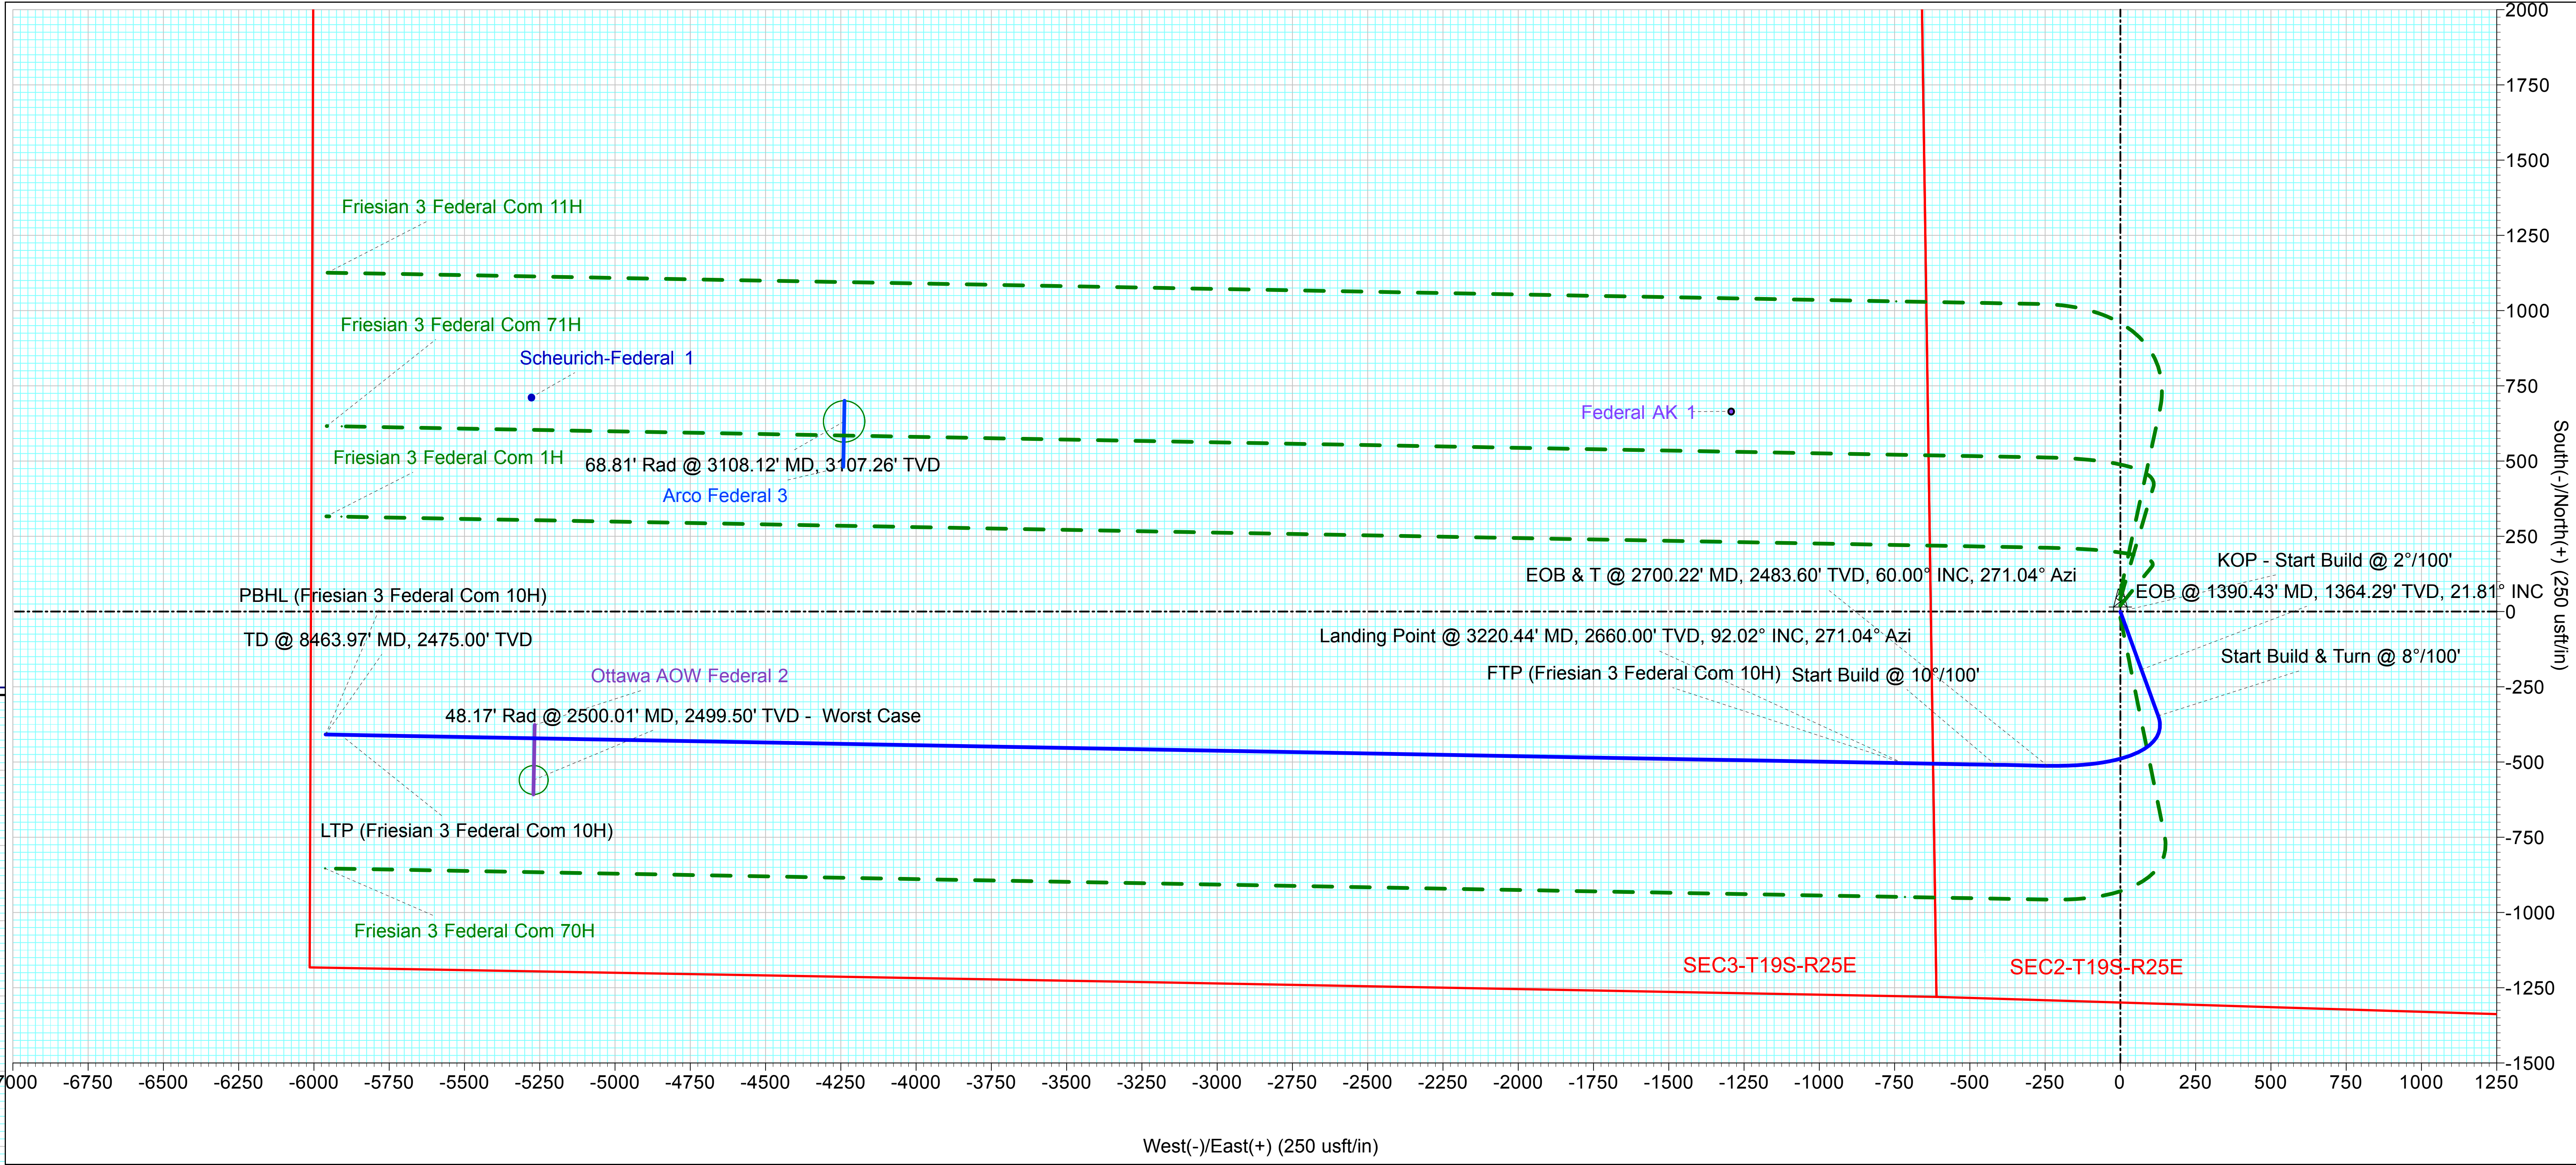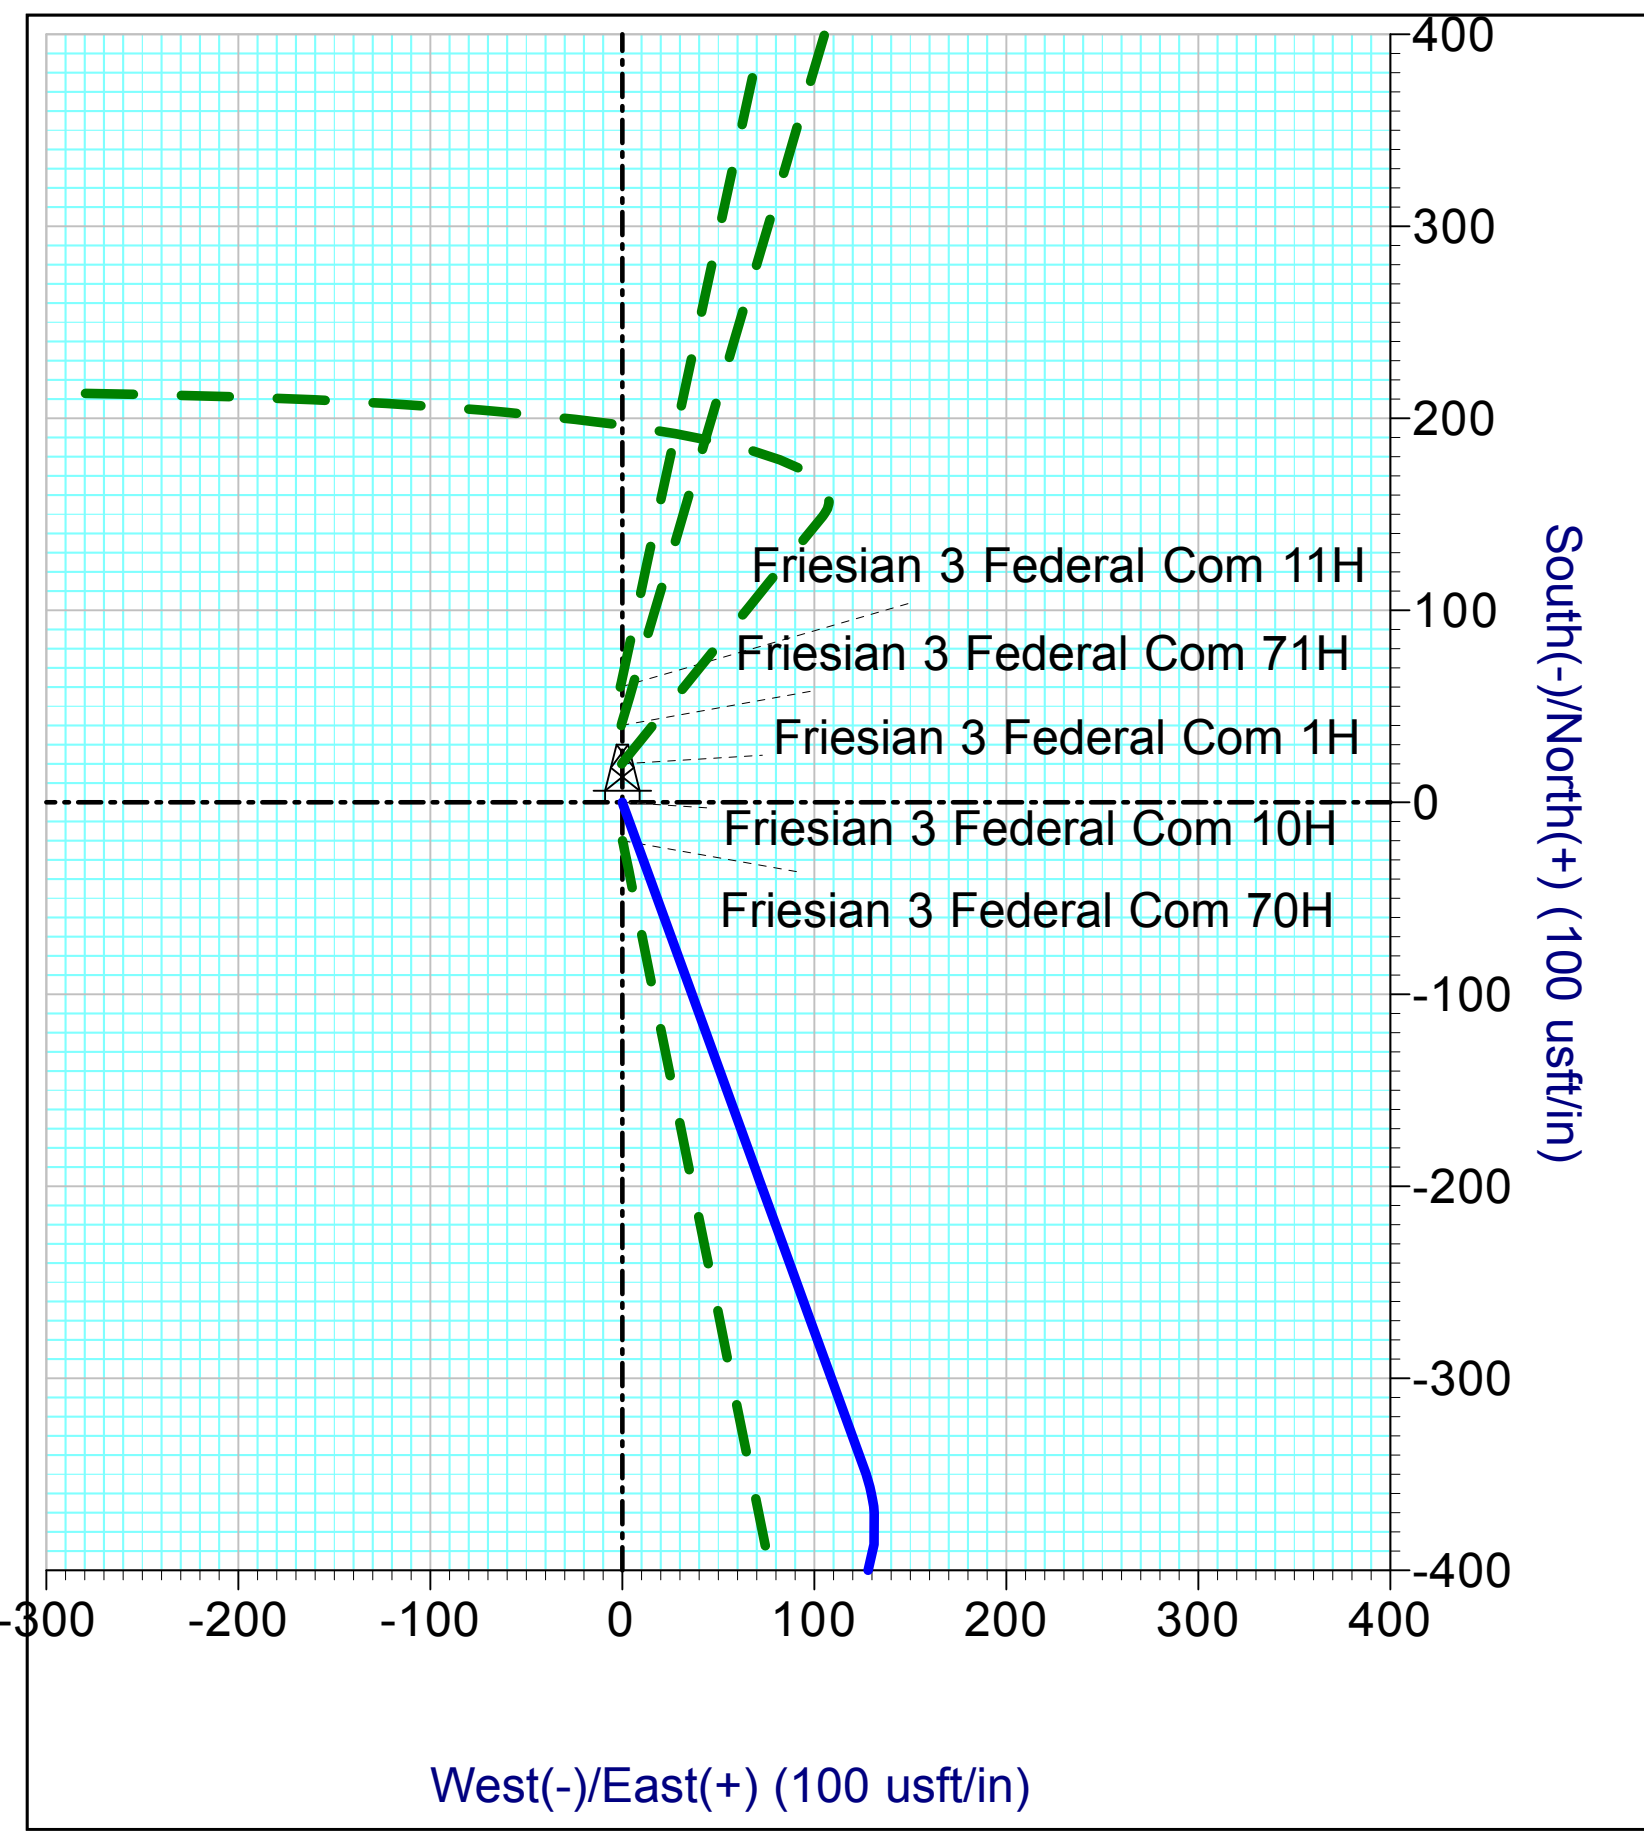

Map System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone Name: New Mexico Eastern Zone
Latitude: 32.68634801
Longitude: -104.46200593
Grid East: 501750.50
Grid North: 613448.60
Scale Factor: 1.000
Geomagnetic Model: IGRF2020
Sample Date: 02-Dec-24
Magnetic Declination: 6.59°
Dip Angle from Horizontal: 60.08°
Magnetic Field Strength: 47314.11914446nT
To convert a Magnetic Direction to a Grid Direction, Add 6.66°

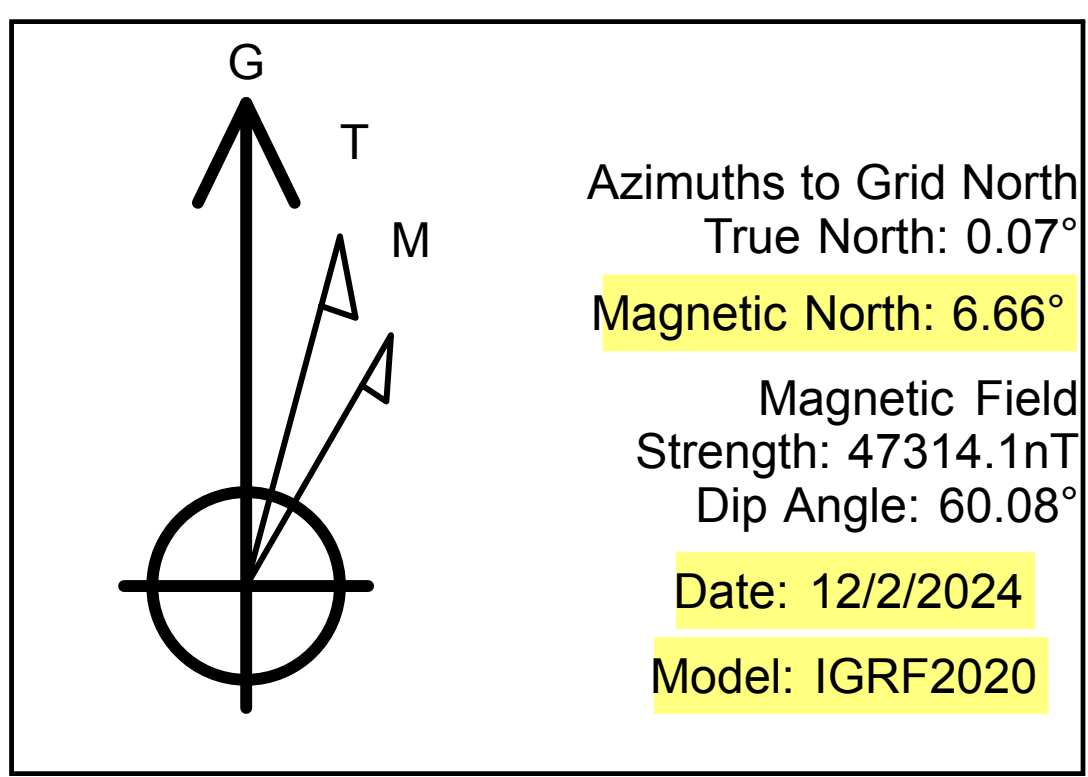

Well Planning: Chris Thomas
21:45, December 02 2024



Spur Energy Partners

Eddy County, NM

Friesian 3 Federal Com

Friesian 3 Federal Com 10H

Wellbore #1

Plan: Plan #1

Standard Planning Report

02 December, 2024





Patriot Drilling Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Company:	Spur Energy Partners	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Project:	Eddy County, NM	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site:	Friesian 3 Federal Com	North Reference:	Grid
Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan #1		

Project	Eddy County, NM		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site		Friesian 3 Federal Com			
Site Position:		Northing:	613,468.60 usft	Latitude:	32.68640298
From:	Map	Easting:	501,750.20 usft	Longitude:	-104.46200699
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "	Grid Convergence:	-0.07 °

Well	Friesian 3 Federal Com 10H					
Well Position	+N/-S	-20.00 usft	Northing:	613,448.60 usft	Latitude:	32.68634801
	+E/-W	0.30 usft	Easting:	501,750.50 usft	Longitude:	-104.46200594
Position Uncertainty		0.00 usft	Wellhead Elevation:		Ground Level:	3,472.00 usft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	12/2/2024	6.59	60.08	47,314.11914446

Design	Plan #1				
Audit Notes:					
Version:		Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.00	0.00	0.00	271.04	

Plan Survey Tool Program	Date	12/2/2024			
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks	
1	0.00	8,463.97	Plan #1 (Wellbore #1)	MWD+IFR1+MS	
				OWSG Rev. 2 MWD + IFR1 + I	



Patriot Drilling Services
Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Company:	Spur Energy Partners	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Project:	Eddy County, NM	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site:	Friesian 3 Federal Com	North Reference:	Grid
Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan #1		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,390.43	21.81	160.05	1,364.29	-192.72	69.97	2.00	2.00	0.00	160.05	
1,830.50	21.81	160.05	1,772.86	-346.40	125.77	0.00	0.00	0.00	0.00	
2,700.22	60.00	271.04	2,483.59	-512.32	-241.98	8.00	4.39	12.76	120.37	
2,900.22	60.00	271.04	2,583.59	-509.17	-415.16	0.00	0.00	0.00	0.00	
3,220.44	92.02	271.04	2,660.00	-503.60	-721.80	10.00	10.00	0.00	0.00	FTP (Friesian 3 Federal Com 10H)
8,463.97	92.02	271.04	2,475.00	-408.40	-5,961.20	0.00	0.00	0.00	0.00	PBHL (Friesian 3 Federal Com 10H)



Patriot Drilling Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Company:	Spur Energy Partners	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Project:	Eddy County, NM	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site:	Friesian 3 Federal Com	North Reference:	Grid
Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
KOP - Start Build @ 2°/100'									
400.00	2.00	160.05	399.98	-1.64	0.60	-0.63	2.00	2.00	0.00
500.00	4.00	160.05	499.84	-6.56	2.38	-2.50	2.00	2.00	0.00
600.00	6.00	160.05	599.45	-14.75	5.36	-5.62	2.00	2.00	0.00
700.00	8.00	160.05	698.70	-26.21	9.51	-9.99	2.00	2.00	0.00
800.00	10.00	160.05	797.47	-40.91	14.85	-15.59	2.00	2.00	0.00
900.00	12.00	160.05	895.62	-58.84	21.36	-22.43	2.00	2.00	0.00
1,000.00	14.00	160.05	993.06	-79.99	29.04	-30.49	2.00	2.00	0.00
1,100.00	16.00	160.05	1,089.64	-104.31	37.87	-39.76	2.00	2.00	0.00
1,200.00	18.00	160.05	1,185.27	-131.80	47.85	-50.23	2.00	2.00	0.00
1,300.00	20.00	160.05	1,279.82	-162.40	58.96	-61.90	2.00	2.00	0.00
1,390.43	21.81	160.05	1,364.29	-192.72	69.97	-73.46	2.00	2.00	0.00
EOB @ 1390.43' MD, 1364.29' TVD, 21.81° INC									
1,400.00	21.81	160.05	1,373.17	-196.07	71.19	-74.73	0.00	0.00	0.00
1,500.00	21.81	160.05	1,466.02	-230.99	83.86	-88.04	0.00	0.00	0.00
1,600.00	21.81	160.05	1,558.86	-265.91	96.54	-101.35	0.00	0.00	0.00
1,700.00	21.81	160.05	1,651.70	-300.83	109.22	-114.66	0.00	0.00	0.00
1,800.00	21.81	160.05	1,744.55	-335.75	121.90	-127.97	0.00	0.00	0.00
1,830.50	21.81	160.05	1,772.86	-346.40	125.77	-132.03	0.00	0.00	0.00
Start Build & Turn @ 8°/100'									
1,900.00	19.57	174.50	1,837.92	-370.13	131.29	-137.99	8.00	-3.23	20.80
2,000.00	18.81	198.90	1,932.52	-402.10	127.67	-134.94	8.00	-0.75	24.40
2,100.00	21.17	221.42	2,026.63	-430.95	110.47	-118.27	8.00	2.36	22.52
2,200.00	25.81	237.90	2,118.41	-456.09	80.03	-88.29	8.00	4.64	16.48
2,300.00	31.74	249.14	2,206.09	-477.06	36.94	-45.60	8.00	5.93	11.23
2,400.00	38.36	256.99	2,287.96	-493.44	-17.95	8.99	8.00	6.62	7.85
2,500.00	45.37	262.79	2,362.42	-504.90	-83.59	74.41	8.00	7.01	5.80
2,600.00	52.60	267.32	2,428.02	-511.24	-158.69	149.39	8.00	7.24	4.53
2,700.00	59.98	271.03	2,483.49	-512.32	-241.79	232.45	8.00	7.38	3.72
2,700.22	60.00	271.04	2,483.59	-512.32	-241.98	232.64	8.00	7.43	3.42
EOB & T @ 2700.22' MD, 2483.60' TVD, 60.00° INC, 271.04° Azi									
2,800.00	60.00	271.04	2,533.49	-510.75	-328.38	319.06	0.00	0.00	0.00
2,900.00	60.00	271.04	2,583.49	-509.18	-414.97	405.66	0.00	0.00	0.00
2,900.22	60.00	271.04	2,583.59	-509.17	-415.16	405.85	0.00	0.00	0.00
Start Build @ 10°/100'									
3,000.00	69.98	271.04	2,625.73	-507.53	-505.45	496.16	10.00	10.00	0.00
3,100.00	79.98	271.04	2,651.61	-505.78	-601.90	592.62	10.00	10.00	0.00
3,200.00	89.98	271.04	2,660.36	-503.97	-701.37	692.11	10.00	10.00	0.00
3,220.44	92.02	271.04	2,660.00	-503.60	-721.80	712.54	10.00	10.00	0.00
Landing Point @ 3220.44' MD, 2660.00' TVD, 92.02° INC, 271.04° Azi - FTP (Friesian 3 Federal Com 10H)									
3,300.00	92.02	271.04	2,657.19	-502.16	-801.30	792.05	0.00	0.00	0.00
3,400.00	92.02	271.04	2,653.66	-500.34	-901.22	891.99	0.00	0.00	0.00
3,500.00	92.02	271.04	2,650.14	-498.52	-1,001.14	991.93	0.00	0.00	0.00
3,600.00	92.02	271.04	2,646.61	-496.71	-1,101.06	1,091.87	0.00	0.00	0.00
3,700.00	92.02	271.04	2,643.08	-494.89	-1,200.99	1,191.81	0.00	0.00	0.00
3,800.00	92.02	271.04	2,639.55	-493.08	-1,300.91	1,291.74	0.00	0.00	0.00
3,900.00	92.02	271.04	2,636.02	-491.26	-1,400.83	1,391.68	0.00	0.00	0.00



Patriot Drilling Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Company:	Spur Energy Partners	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Project:	Eddy County, NM	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site:	Friesian 3 Federal Com	North Reference:	Grid
Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,000.00	92.02	271.04	2,632.50	-489.45	-1,500.75	1,491.62	0.00	0.00	0.00
4,100.00	92.02	271.04	2,628.97	-487.63	-1,600.67	1,591.56	0.00	0.00	0.00
4,200.00	92.02	271.04	2,625.44	-485.82	-1,700.59	1,691.49	0.00	0.00	0.00
4,300.00	92.02	271.04	2,621.91	-484.00	-1,800.51	1,791.43	0.00	0.00	0.00
4,400.00	92.02	271.04	2,618.38	-482.18	-1,900.43	1,891.37	0.00	0.00	0.00
4,500.00	92.02	271.04	2,614.86	-480.37	-2,000.36	1,991.31	0.00	0.00	0.00
4,600.00	92.02	271.04	2,611.33	-478.55	-2,100.28	2,091.25	0.00	0.00	0.00
4,700.00	92.02	271.04	2,607.80	-476.74	-2,200.20	2,191.18	0.00	0.00	0.00
4,800.00	92.02	271.04	2,604.27	-474.92	-2,300.12	2,291.12	0.00	0.00	0.00
4,900.00	92.02	271.04	2,600.74	-473.11	-2,400.04	2,391.06	0.00	0.00	0.00
5,000.00	92.02	271.04	2,597.21	-471.29	-2,499.96	2,491.00	0.00	0.00	0.00
5,100.00	92.02	271.04	2,593.69	-469.48	-2,599.88	2,590.93	0.00	0.00	0.00
5,200.00	92.02	271.04	2,590.16	-467.66	-2,699.80	2,690.87	0.00	0.00	0.00
5,300.00	92.02	271.04	2,586.63	-465.84	-2,799.73	2,790.81	0.00	0.00	0.00
5,400.00	92.02	271.04	2,583.10	-464.03	-2,899.65	2,890.75	0.00	0.00	0.00
5,500.00	92.02	271.04	2,579.57	-462.21	-2,999.57	2,990.68	0.00	0.00	0.00
5,600.00	92.02	271.04	2,576.05	-460.40	-3,099.49	3,090.62	0.00	0.00	0.00
5,700.00	92.02	271.04	2,572.52	-458.58	-3,199.41	3,190.56	0.00	0.00	0.00
5,800.00	92.02	271.04	2,568.99	-456.77	-3,299.33	3,290.50	0.00	0.00	0.00
5,900.00	92.02	271.04	2,565.46	-454.95	-3,399.25	3,390.44	0.00	0.00	0.00
6,000.00	92.02	271.04	2,561.93	-453.14	-3,499.17	3,490.37	0.00	0.00	0.00
6,100.00	92.02	271.04	2,558.40	-451.32	-3,599.10	3,590.31	0.00	0.00	0.00
6,200.00	92.02	271.04	2,554.88	-449.50	-3,699.02	3,690.25	0.00	0.00	0.00
6,300.00	92.02	271.04	2,551.35	-447.69	-3,798.94	3,790.19	0.00	0.00	0.00
6,400.00	92.02	271.04	2,547.82	-445.87	-3,898.86	3,890.12	0.00	0.00	0.00
6,500.00	92.02	271.04	2,544.29	-444.06	-3,998.78	3,990.06	0.00	0.00	0.00
6,600.00	92.02	271.04	2,540.76	-442.24	-4,098.70	4,090.00	0.00	0.00	0.00
6,700.00	92.02	271.04	2,537.24	-440.43	-4,198.62	4,189.94	0.00	0.00	0.00
6,800.00	92.02	271.04	2,533.71	-438.61	-4,298.54	4,289.88	0.00	0.00	0.00
6,900.00	92.02	271.04	2,530.18	-436.79	-4,398.47	4,389.81	0.00	0.00	0.00
7,000.00	92.02	271.04	2,526.65	-434.98	-4,498.39	4,489.75	0.00	0.00	0.00
7,100.00	92.02	271.04	2,523.12	-433.16	-4,598.31	4,589.69	0.00	0.00	0.00
7,200.00	92.02	271.04	2,519.59	-431.35	-4,698.23	4,689.63	0.00	0.00	0.00
7,300.00	92.02	271.04	2,516.07	-429.53	-4,798.15	4,789.56	0.00	0.00	0.00
7,400.00	92.02	271.04	2,512.54	-427.72	-4,898.07	4,889.50	0.00	0.00	0.00
7,500.00	92.02	271.04	2,509.01	-425.90	-4,997.99	4,989.44	0.00	0.00	0.00
7,600.00	92.02	271.04	2,505.48	-424.09	-5,097.91	5,089.38	0.00	0.00	0.00
7,700.00	92.02	271.04	2,501.95	-422.27	-5,197.84	5,189.32	0.00	0.00	0.00
7,800.00	92.02	271.04	2,498.43	-420.45	-5,297.76	5,289.25	0.00	0.00	0.00
7,900.00	92.02	271.04	2,494.90	-418.64	-5,397.68	5,389.19	0.00	0.00	0.00
8,000.00	92.02	271.04	2,491.37	-416.82	-5,497.60	5,489.13	0.00	0.00	0.00
8,100.00	92.02	271.04	2,487.84	-415.01	-5,597.52	5,589.07	0.00	0.00	0.00
8,200.00	92.02	271.04	2,484.31	-413.19	-5,697.44	5,689.00	0.00	0.00	0.00
8,300.00	92.02	271.04	2,480.79	-411.38	-5,797.36	5,788.94	0.00	0.00	0.00
8,400.00	92.02	271.04	2,477.26	-409.56	-5,897.28	5,888.88	0.00	0.00	0.00
LTP (Friesian 3 Federal Com 10H)									
8,463.97	92.02	271.04	2,475.00	-408.40	-5,961.20	5,952.81	0.00	0.00	0.00
TD @ 8463.97' MD, 2475.00' TVD - PBHL (Friesian 3 Federal Com 10H)									



Patriot Drilling Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Company:	Spur Energy Partners	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Project:	Eddy County, NM	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site:	Friesian 3 Federal Com	North Reference:	Grid
Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Plan #1		

Design Targets

Target Name

- hit/miss target	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- Shape									
PBHL (Friesian 3 Federal Com 10H) - plan hits target center - Point	0.00	0.00	2,475.00	-408.40	-5,961.20	613,040.20	495,789.30	32.68520407	-104.48138017
LTP (Friesian 3 Federal Com 10H) - plan misses target center by 13.93usft at 8400.00usft MD (2477.26 TVD, -409.56 N, -5897.28 E) - Point	0.00	360.00	2,476.76	-409.30	-5,911.20	613,039.30	495,839.30	32.68520179	-104.48121765
FTP (Friesian 3 Federal Com 10H) - plan hits target center - Point	0.00	360.00	2,660.00	-503.60	-721.80	612,945.00	501,028.70	32.68496133	-104.46435003

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
300.00	300.00	0.00	0.00	KOP - Start Build @ 2°/100'
1,390.43	1,364.29	-192.72	69.97	EOB @ 1390.43' MD, 1364.29' TVD, 21.81° INC
1,830.50	1,772.86	-346.40	125.77	Start Build & Turn @ 8°/100'
2,700.22	2,483.59	-512.32	-241.98	EOB & T @ 2700.22' MD, 2483.60' TVD, 60.00° INC, 271.04° Azi
2,900.22	2,583.59	-509.17	-415.16	Start Build @ 10°/100'
3,220.44	2,660.00	-503.60	-721.80	Landing Point @ 3220.44' MD, 2660.00' TVD, 92.02° INC, 271.04° Azi
8,463.97	2,475.00	-408.40	-5,961.20	TD @ 8463.97' MD, 2475.00' TVD



Spur Energy Partners

Eddy County, NM

Friesian 3 Federal Com

Friesian 3 Federal Com 10H

Wellbore #1

Plan #1

Anticollision Report

02 December, 2024





Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Reference	Plan #1		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	Stations	Error Model:	ISCWSA
Depth Range:	Unlimited	Scan Method:	Closest Approach 3D
Results Limited by:	Max. Cent. Dist. of 1,000.00usft or Max. SF of 55	Error Surface:	Pedal Curve
Warning Levels Evaluated at:	2.00 Sigma	Casing Method:	Not applied

Survey Tool Program	Date	12/2/2024		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description
0.00	8,463.97	Plan #1 (Wellbore #1)	MWD+IFR1+MS	OWSG Rev. 2 MWD + IFR1 + Multi-Station Correction

Summary						
Site Name	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
Friesian 3 Federal Com						
Friesian 3 Federal Com 11H - Wellbore #1 - Plan #1	215.28	219.28	60.01	58.88	53.218	CC
Friesian 3 Federal Com 11H - Wellbore #1 - Plan #1	300.00	303.88	60.01	58.28	34.595	ES
Friesian 3 Federal Com 11H - Wellbore #1 - Plan #1	8,463.97	8,545.40	1,536.19	1,400.84	11.350	SF
Friesian 3 Federal Com 1H - Wellbore #1 - Plan #1	215.99	217.99	20.00	18.88	17.772	CC
Friesian 3 Federal Com 1H - Wellbore #1 - Plan #1	300.00	301.99	20.00	18.28	11.577	ES
Friesian 3 Federal Com 1H - Wellbore #1 - Plan #1	8,463.97	8,142.06	762.32	631.09	5.809	SF
Friesian 3 Federal Com 70H - Wellbore #1 - Plan #1	330.22	329.02	20.00	18.07	10.389	CC
Friesian 3 Federal Com 70H - Wellbore #1 - Plan #1	700.00	696.26	21.15	16.69	4.741	ES
Friesian 3 Federal Com 70H - Wellbore #1 - Plan #1	1,100.00	1,093.33	28.28	20.91	3.836	SF
Friesian 3 Federal Com 71H - Wellbore #1 - Plan #1	215.64	218.64	40.00	38.88	35.510	CC
Friesian 3 Federal Com 71H - Wellbore #1 - Plan #1	300.00	302.96	40.01	38.27	23.107	ES
Friesian 3 Federal Com 71H - Wellbore #1 - Plan #1	8,463.97	9,031.36	1,161.65	1,034.47	9.134	SF
Ottawa AOW Federal 2 - Wellbore #1 - Wellbore #1	7,769.55	2,532.91	137.88	69.45	2.015	CC, ES, SF

Offset Design:	Friesian 3 Federal Com - Friesian 3 Federal Com 11H - Wellbore #1 - Plan #1											Offset Site Error:	0.00 usft
Survey Program:	0-MWD+IFR1+MS											Offset Well Error:	0.00 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Semi Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	Offset Wellbore Centre +E/-W (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.00	0.00	4.00	4.00	0.00	0.01	-0.95	60.00	-1.00	60.01	59.71	0.30	199.286	
100.00	100.00	104.00	104.00	0.14	0.16	-0.95	60.00	-1.00	60.01	58.99	1.02	58.944	
200.00	200.00	204.00	204.00	0.50	0.52	-0.95	60.00	-1.00	60.01	58.88	1.13	53.218	CC
215.28	215.28	219.28	219.28	0.56	0.57	-0.95	60.00	-1.00	60.01	58.28	1.73	34.595	ES
300.00	300.00	303.88	303.88	0.86	0.87	-0.95	60.00	-1.00	60.01	58.28	1.73	34.595	ES
400.00	399.98	400.00	399.95	1.20	1.22	-160.92	62.56	-0.45	64.33	61.90	2.44	26.405	
500.00	499.84	496.50	496.15	1.55	1.58	-160.80	69.87	1.14	76.83	73.69	3.14	24.472	
600.00	599.45	590.22	589.10	1.90	1.93	-160.66	81.51	3.66	97.34	93.50	3.84	25.351	
700.00	698.70	680.98	678.46	2.26	2.27	-160.51	97.02	7.02	125.61	121.08	4.52	27.762	
800.00	797.47	768.04	763.37	2.62	2.60	-160.33	115.77	11.08	161.29	156.10	5.19	31.095	
900.00	895.62	850.78	843.17	2.99	2.92	-160.13	137.08	15.69	203.98	198.15	5.82	35.033	
1,000.00	993.06	928.74	917.45	3.36	3.22	-159.90	160.24	20.71	253.21	246.78	6.43	39.393	
1,100.00	1,089.64	1,000.00	984.43	3.74	3.50	-159.61	183.98	25.85	308.52	301.54	6.98	44.190	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 11H - Wellbore #1 - Plan #1												Offset Site Error:	0.00 usft
Survey Program: 0-MWD+IFR1+MS												Offset Well Error:	0.00 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Semi Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Distance Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
1,200.00	1,185.27	1,069.30	1,048.67	4.13	3.78	-159.29	209.39	31.35	369.39	361.87	7.52	49.098	
1,300.00	1,279.82	1,131.70	1,105.66	4.53	4.02	-158.89	234.21	36.73	435.35	427.32	8.04	54.176	
1,390.43	1,364.29	1,183.62	1,152.44	4.90	4.23	-158.48	256.24	41.50	498.97	490.51	8.46	58.955	
1,400.00	1,373.17	1,188.88	1,157.14	4.94	4.25	-158.50	258.54	42.00	505.90	497.39	8.51	59.418	
1,500.00	1,466.02	1,242.11	1,204.37	5.36	4.47	-158.70	282.53	47.19	579.33	570.39	8.94	64.806	
1,600.00	1,558.86	1,300.00	1,254.93	5.79	4.70	-158.82	310.08	53.16	654.57	645.15	9.42	69.491	
1,700.00	1,651.70	1,339.75	1,289.15	6.21	4.86	-158.85	329.85	57.44	731.30	721.57	9.73	75.140	
1,800.00	1,744.55	1,384.53	1,327.17	6.64	5.04	-158.86	352.95	62.44	809.57	799.46	10.10	80.144	
1,830.50	1,772.86	1,400.00	1,340.18	6.77	5.11	-158.86	361.14	64.21	833.71	823.48	10.23	81.468	
1,850.00	1,791.02	1,400.00	1,340.18	6.86	5.11	-164.36	361.14	64.21	849.22	839.00	10.22	83.121	
1,900.00	1,837.92	1,427.07	1,362.78	7.07	5.22	-179.17	375.70	67.37	888.78	878.33	10.45	85.072	
1,950.00	1,885.17	1,447.69	1,379.86	7.27	5.30	165.11	387.01	69.82	928.14	917.53	10.61	87.508	
2,000.00	1,932.52	1,467.79	1,396.37	7.48	5.39	149.33	398.20	72.24	967.12	956.36	10.76	89.920	
2,050.00	1,979.75	1,500.00	1,422.59	7.67	5.53	134.94	416.49	76.20	1,005.74	994.71	11.03	91.218	
2,100.00	2,026.63	1,500.00	1,422.59	7.85	5.53	120.96	416.49	76.20	1,043.56	1,032.61	10.96	95.239	
2,150.00	2,072.92	1,524.17	1,442.05	8.03	5.64	109.91	430.49	79.23	1,080.80	1,069.66	11.14	97.013	
2,200.00	2,118.41	1,541.47	1,455.87	8.20	5.72	100.44	440.66	81.44	1,117.34	1,106.09	11.25	99.322	
2,250.00	2,162.87	1,557.94	1,468.94	8.36	5.80	92.54	450.46	83.56	1,153.10	1,141.75	11.35	101.600	
2,300.00	2,206.09	1,573.55	1,481.25	8.51	5.87	85.94	459.85	85.59	1,188.02	1,176.58	11.44	103.835	
2,350.00	2,247.85	1,600.00	1,501.91	8.65	6.00	80.95	475.98	89.08	1,222.14	1,210.49	11.65	104.885	
2,400.00	2,287.96	1,600.00	1,501.91	8.79	6.00	75.54	475.98	89.08	1,255.14	1,243.56	11.59	108.330	
2,450.00	2,326.21	1,614.99	1,513.53	8.91	6.07	71.58	485.24	91.09	1,287.26	1,275.57	11.69	110.114	
2,500.00	2,362.42	1,626.95	1,522.74	9.03	6.12	68.07	492.70	92.70	1,318.36	1,306.59	11.77	111.989	
2,550.00	2,396.41	1,637.96	1,531.17	9.14	6.17	65.01	499.61	94.20	1,348.41	1,336.55	11.86	113.716	
2,600.00	2,428.02	1,648.99	1,539.58	9.24	6.23	62.38	506.58	95.71	1,377.36	1,365.40	11.96	115.166	
2,650.00	2,457.09	1,663.08	1,550.31	9.37	6.29	60.25	515.52	97.65	1,405.15	1,393.03	12.11	115.989	
2,700.22	2,483.59	1,677.47	1,561.25	9.57	6.36	58.43	524.65	99.62	1,431.82	1,419.53	12.29	116.472	
2,800.00	2,533.49	1,704.55	1,581.85	10.03	6.49	59.63	541.83	103.34	1,485.78	1,473.06	12.72	116.850	
2,900.22	2,583.59	3,025.32	2,514.21	10.55	11.82	86.84	1,025.14	-429.47	1,536.13	1,513.93	22.20	69.180	
2,950.00	2,606.58	3,069.84	2,535.50	10.83	12.06	86.87	1,025.86	-468.56	1,536.09	1,513.35	22.74	67.561	
3,000.00	2,625.73	3,113.49	2,553.42	11.13	12.30	86.93	1,026.58	-508.33	1,536.01	1,512.72	23.29	65.945	
3,050.00	2,640.78	3,157.23	2,568.29	11.45	12.57	87.01	1,027.33	-549.46	1,535.91	1,512.04	23.87	64.334	
3,100.00	2,651.61	3,200.00	2,579.75	11.78	12.84	87.10	1,028.09	-590.64	1,535.78	1,511.31	24.47	62.757	
3,150.00	2,658.16	3,245.16	2,588.49	12.12	13.13	87.22	1,028.90	-634.93	1,535.63	1,510.53	25.10	61.177	
3,200.00	2,660.36	3,289.40	2,593.64	12.46	13.44	87.36	1,029.70	-678.86	1,535.47	1,509.73	25.74	59.660	
3,220.44	2,660.00	3,307.56	2,594.76	12.61	13.56	87.42	1,030.03	-696.97	1,535.40	1,509.40	26.00	59.053	
3,271.14	2,658.21	3,352.84	2,595.08	12.98	13.88	87.49	1,030.86	-742.23	1,535.31	1,508.63	26.68	57.544	
3,300.00	2,657.19	3,381.44	2,594.04	13.20	14.09	87.49	1,031.38	-770.81	1,535.31	1,508.22	27.09	56.667	
3,400.00	2,653.66	3,481.44	2,590.39	13.99	14.85	87.49	1,033.21	-870.72	1,535.33	1,506.71	28.62	53.652	
3,500.00	2,650.14	3,581.44	2,586.75	14.82	15.64	87.48	1,035.04	-970.64	1,535.34	1,505.12	30.23	50.791	
3,600.00	2,646.61	3,681.44	2,583.11	15.69	16.47	87.48	1,036.86	-1,070.56	1,535.36	1,503.44	31.92	48.104	
3,700.00	2,643.08	3,781.44	2,579.47	16.58	17.34	87.47	1,038.69	-1,170.47	1,535.38	1,501.71	33.67	45.598	
3,800.00	2,639.55	3,881.44	2,575.82	17.51	18.22	87.47	1,040.52	-1,270.39	1,535.40	1,499.91	35.48	43.273	
3,900.00	2,636.02	3,981.44	2,572.18	18.45	19.14	87.47	1,042.35	-1,370.31	1,535.41	1,498.07	37.34	41.121	
4,000.00	2,632.50	4,081.44	2,568.54	19.41	20.07	87.46	1,044.17	-1,470.22	1,535.43	1,496.19	39.24	39.132	
4,100.00	2,628.97	4,181.44	2,564.89	20.39	21.02	87.46	1,046.00	-1,570.14	1,535.45	1,494.27	41.17	37.294	
4,200.00	2,625.44	4,281.44	2,561.25	21.39	21.98	87.45	1,047.83	-1,670.06	1,535.46	1,492.33	43.14	35.597	
4,300.00	2,621.91	4,381.44	2,557.61	22.39	22.96	87.45	1,049.66	-1,769.98	1,535.48	1,490.35	45.13	34.027	
4,400.00	2,618.38	4,481.44	2,553.96	23.41	23.95	87.44	1,051.48	-1,869.89	1,535.50	1,488.36	47.14	32.574	
4,500.00	2,614.86	4,581.44	2,550.32	24.44	24.96	87.44	1,053.31	-1,969.81	1,535.51	1,486.34	49.17	31.227	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 11H - Wellbore #1 - Plan #1												Offset Site Error:	0.00 usft
Survey Program: 0-MWD+IFR1+MS												Offset Well Error:	0.00 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Semi Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Distance Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
4,600.00	2,611.33	4,681.44	2,546.68	25.47	25.97	87.44	1,055.14	-2,069.73	1,535.53	1,484.31	51.22	29.976	
4,700.00	2,607.80	4,781.44	2,543.03	26.51	26.99	87.43	1,056.96	-2,169.64	1,535.55	1,482.26	53.29	28.814	
4,800.00	2,604.27	4,881.44	2,539.39	27.56	28.02	87.43	1,058.79	-2,269.56	1,535.56	1,480.19	55.37	27.731	
4,900.00	2,600.74	4,981.44	2,535.75	28.61	29.05	87.42	1,060.62	-2,369.48	1,535.58	1,478.11	57.47	26.721	
5,000.00	2,597.21	5,081.44	2,532.11	29.67	30.09	87.42	1,062.45	-2,469.39	1,535.60	1,476.03	59.57	25.777	
5,100.00	2,593.69	5,181.44	2,528.46	30.73	31.14	87.41	1,064.27	-2,569.31	1,535.61	1,473.93	61.69	24.893	
5,200.00	2,590.16	5,281.44	2,524.82	31.80	32.19	87.41	1,066.10	-2,669.23	1,535.63	1,471.82	63.81	24.065	
5,300.00	2,586.63	5,381.44	2,521.18	32.87	33.25	87.41	1,067.93	-2,769.14	1,535.65	1,469.70	65.94	23.287	
5,400.00	2,583.10	5,481.44	2,517.53	33.94	34.31	87.40	1,069.76	-2,869.06	1,535.67	1,467.58	68.08	22.555	
5,500.00	2,579.57	5,581.44	2,513.89	35.02	35.37	87.40	1,071.58	-2,968.98	1,535.68	1,465.45	70.23	21.866	
5,600.00	2,576.05	5,681.44	2,510.25	36.10	36.44	87.39	1,073.41	-3,068.89	1,535.70	1,463.32	72.38	21.216	
5,700.00	2,572.52	5,781.44	2,506.60	37.18	37.51	87.39	1,075.24	-3,168.81	1,535.72	1,461.17	74.54	20.602	
5,800.00	2,568.99	5,881.44	2,502.96	38.27	38.58	87.38	1,077.06	-3,268.73	1,535.73	1,459.03	76.71	20.021	
5,900.00	2,565.46	5,981.44	2,499.32	39.36	39.66	87.38	1,078.89	-3,368.65	1,535.75	1,456.88	78.87	19.471	
6,000.00	2,561.93	6,081.44	2,495.68	40.45	40.74	87.38	1,080.72	-3,468.56	1,535.77	1,454.72	81.05	18.949	
6,100.00	2,558.40	6,181.44	2,492.03	41.54	41.82	87.37	1,082.55	-3,568.48	1,535.78	1,452.56	83.22	18.454	
6,200.00	2,554.88	6,281.44	2,488.39	42.63	42.90	87.37	1,084.37	-3,668.40	1,535.80	1,450.40	85.40	17.983	
6,300.00	2,551.35	6,381.44	2,484.75	43.72	43.99	87.36	1,086.20	-3,768.31	1,535.82	1,448.23	87.59	17.535	
6,400.00	2,547.82	6,481.44	2,481.10	44.82	45.08	87.36	1,088.03	-3,868.23	1,535.84	1,446.06	89.77	17.108	
6,500.00	2,544.29	6,581.44	2,477.46	45.92	46.16	87.35	1,089.86	-3,968.15	1,535.85	1,443.89	91.96	16.701	
6,600.00	2,540.76	6,681.44	2,473.82	47.02	47.26	87.35	1,091.68	-4,068.06	1,535.87	1,441.71	94.16	16.312	
6,700.00	2,537.24	6,781.44	2,470.17	48.11	48.35	87.35	1,093.51	-4,167.98	1,535.89	1,439.54	96.35	15.941	
6,800.00	2,533.71	6,881.44	2,466.53	49.22	49.44	87.34	1,095.34	-4,267.90	1,535.90	1,437.36	98.55	15.585	
6,900.00	2,530.18	6,981.44	2,462.89	50.32	50.54	87.34	1,097.16	-4,367.81	1,535.92	1,435.17	100.75	15.245	
7,000.00	2,526.65	7,081.44	2,459.25	51.42	51.63	87.33	1,098.99	-4,467.73	1,535.94	1,432.99	102.95	14.919	
7,100.00	2,523.12	7,181.44	2,455.60	52.52	52.73	87.33	1,100.82	-4,567.65	1,535.96	1,430.80	105.15	14.607	
7,200.00	2,519.59	7,281.44	2,451.96	53.63	53.83	87.32	1,102.65	-4,667.56	1,535.97	1,428.61	107.36	14.307	
7,300.00	2,516.07	7,381.44	2,448.32	54.73	54.93	87.32	1,104.47	-4,767.48	1,535.99	1,426.42	109.57	14.019	
7,400.00	2,512.54	7,481.44	2,444.67	55.84	56.03	87.32	1,106.30	-4,867.40	1,536.01	1,424.23	111.77	13.742	
7,500.00	2,509.01	7,581.44	2,441.03	56.95	57.13	87.31	1,108.13	-4,967.31	1,536.02	1,422.04	113.98	13.476	
7,600.00	2,505.48	7,681.44	2,437.39	58.05	58.23	87.31	1,109.96	-5,067.23	1,536.04	1,419.84	116.20	13.219	
7,700.00	2,501.95	7,781.44	2,433.74	59.16	59.33	87.30	1,111.78	-5,167.15	1,536.06	1,417.65	118.41	12.972	
7,800.00	2,498.43	7,881.44	2,430.10	60.27	60.44	87.30	1,113.61	-5,267.07	1,536.08	1,415.45	120.62	12.734	
7,900.00	2,494.90	7,981.44	2,426.46	61.38	61.54	87.29	1,115.44	-5,366.98	1,536.09	1,413.25	122.84	12.505	
8,000.00	2,491.37	8,081.44	2,422.81	62.49	62.65	87.29	1,117.26	-5,466.90	1,536.11	1,411.05	125.06	12.283	
8,100.00	2,487.84	8,181.44	2,419.17	63.60	63.75	87.29	1,119.09	-5,566.82	1,536.13	1,408.85	127.27	12.070	
8,200.00	2,484.31	8,281.44	2,415.53	64.71	64.86	87.28	1,120.92	-5,666.73	1,536.14	1,406.65	129.49	11.863	
8,300.00	2,480.79	8,381.44	2,411.89	65.82	65.96	87.28	1,122.75	-5,766.65	1,536.16	1,404.45	131.71	11.663	
8,400.00	2,477.26	8,481.44	2,408.24	66.93	67.07	87.27	1,124.57	-5,866.57	1,536.18	1,402.25	133.93	11.470	
8,463.97	2,475.00	8,545.40	2,405.91	67.64	67.78	87.27	1,125.74	-5,930.48	1,536.19	1,400.84	135.35	11.350 SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 1H - Wellbore #1 - Plan #1												Offset Site Error:	0.00 usft
Survey Program:		0-MWD+IFR1+MS					Rule Assigned:		Offset Well Error:		0.00 usft		
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Distance		Minimum		Separation	Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)			
0.00	0.00	2.00	2.00	0.00	0.00	-0.86	20.00	-0.30	20.00				
100.00	100.00	102.00	102.00	0.14	0.15	-0.86	20.00	-0.30	20.00	19.71	0.29	68.047	
200.00	200.00	202.00	202.00	0.50	0.51	-0.86	20.00	-0.30	20.00	18.99	1.01	19.787	
215.99	215.99	217.99	217.99	0.56	0.57	-0.86	20.00	-0.30	20.00	18.88	1.13	17.772 CC	
300.00	300.00	301.99	301.99	0.86	0.87	-0.86	20.00	-0.30	20.00	18.28	1.73	11.577 ES	
400.00	399.98	401.36	401.34	1.20	1.22	-159.43	21.39	0.83	23.04	20.61	2.43	9.482	
500.00	499.84	500.00	499.84	1.55	1.58	-156.83	25.42	4.10	32.09	28.95	3.13	10.235	
600.00	599.45	597.93	597.39	1.90	1.94	-154.70	32.02	9.45	47.12	43.28	3.84	12.262	
700.00	698.70	694.09	692.84	2.26	2.29	-153.26	41.02	16.75	68.06	63.52	4.55	14.963	
800.00	797.47	789.27	786.94	2.62	2.64	-152.37	52.15	25.79	94.54	89.29	5.25	18.004	
900.00	895.62	884.69	881.19	2.99	2.98	-152.36	63.73	35.18	124.44	118.48	5.96	20.884	
1,000.00	993.06	979.12	974.45	3.36	3.33	-152.83	75.19	44.48	157.30	150.63	6.67	23.591	
1,100.00	1,089.64	1,072.43	1,066.63	3.74	3.67	-153.49	86.51	53.67	193.11	185.73	7.37	26.189	
1,200.00	1,185.27	1,164.53	1,157.59	4.13	4.00	-154.22	97.69	62.74	231.87	223.79	8.08	28.692	
1,300.00	1,279.82	1,255.30	1,247.25	4.53	4.34	-154.95	108.70	71.67	273.59	264.80	8.79	31.137	
1,390.43	1,364.29	1,336.14	1,327.09	4.90	4.64	-155.59	118.51	79.63	313.84	304.42	9.42	33.305	
1,400.00	1,373.17	1,344.63	1,335.48	4.94	4.67	-155.69	119.54	80.47	318.23	308.73	9.50	33.514	
1,500.00	1,466.02	1,433.34	1,423.10	5.36	4.99	-156.63	130.30	89.20	364.11	353.92	10.19	35.747	
1,600.00	1,558.86	1,522.06	1,510.73	5.79	5.32	-157.36	141.07	97.93	410.05	399.17	10.88	37.684	
1,700.00	1,651.70	1,611.45	1,599.06	6.21	5.65	-158.00	151.90	106.32	456.02	444.44	11.58	39.363	
1,800.00	1,744.55	1,701.47	1,688.40	6.64	5.97	-159.59	162.44	106.47	501.80	489.52	12.29	40.844	
1,830.50	1,772.86	1,728.26	1,714.93	6.77	6.06	-160.28	165.46	104.34	515.80	503.31	12.49	41.293	
1,850.00	1,791.02	1,745.25	1,731.71	6.86	6.12	-165.01	167.34	102.47	524.73	512.11	12.62	41.579	
1,900.00	1,837.92	1,788.76	1,774.45	7.07	6.27	-178.05	172.05	95.87	547.27	534.33	12.94	42.285	
1,950.00	1,885.17	1,832.23	1,816.69	7.27	6.41	-167.90	176.57	86.68	569.18	555.93	13.25	42.942	
2,000.00	1,932.52	1,875.71	1,858.33	7.48	6.56	-153.62	180.90	74.92	590.32	576.76	13.56	43.542	
2,050.00	1,979.75	1,919.25	1,899.24	7.67	6.70	-140.08	185.01	60.64	610.55	596.70	13.85	44.078	
2,100.00	2,026.63	1,962.86	1,939.30	7.85	6.84	-128.05	188.89	43.85	629.77	615.64	14.14	44.546	
2,150.00	2,072.92	2,006.57	1,978.36	8.03	6.98	-117.81	192.54	24.61	647.88	633.46	14.42	44.940	
2,200.00	2,118.41	2,050.00	2,015.97	8.20	7.13	-109.30	195.90	3.15	664.77	650.08	14.69	45.263	
2,250.00	2,162.87	2,094.26	2,052.90	8.36	7.28	-102.28	199.05	-21.02	680.36	665.41	14.96	45.482	
2,300.00	2,206.09	2,138.22	2,088.06	8.51	7.43	-96.49	201.89	-47.24	694.60	679.37	15.23	45.614	
2,350.00	2,247.85	2,182.23	2,121.60	8.65	7.59	-91.69	204.43	-75.62	707.39	691.90	15.50	45.646	
2,400.00	2,287.96	2,226.27	2,153.38	8.79	7.75	-87.68	206.66	-106.01	718.71	702.93	15.77	45.566	
2,450.00	2,326.21	2,270.29	2,183.24	8.91	7.92	-84.31	208.57	-138.29	728.48	712.43	16.05	45.376	
2,500.00	2,362.42	2,314.26	2,211.05	9.03	8.11	-81.48	210.15	-172.30	736.68	720.33	16.35	45.060	
2,550.00	2,396.41	2,358.12	2,236.68	9.14	8.30	-79.09	211.40	-207.86	743.27	726.61	16.66	44.622	
2,600.00	2,428.02	2,401.83	2,260.04	9.24	8.50	-77.08	212.31	-244.79	748.22	731.24	16.98	44.058	
2,650.00	2,457.09	2,450.57	2,284.44	9.37	8.76	-75.44	213.08	-286.98	751.38	733.99	17.39	43.213	
2,700.22	2,483.59	2,500.75	2,309.53	9.57	9.02	-74.33	213.88	-330.42	752.45	734.61	17.84	42.182	
2,800.00	2,533.49	2,600.53	2,359.42	10.03	9.61	-74.33	215.45	-416.82	752.45	733.58	18.87	39.879	
2,900.22	2,583.59	2,676.41	2,393.85	10.55	10.09	-74.04	216.68	-484.37	753.93	734.19	19.75	38.181	
2,950.00	2,606.58	2,712.57	2,407.07	10.83	10.33	-73.62	217.29	-518.01	755.41	735.22	20.19	37.424	
3,000.00	2,625.73	2,750.00	2,418.50	11.13	10.59	-73.28	217.94	-553.64	756.58	735.91	20.67	36.609	
3,050.00	2,640.78	2,784.84	2,427.02	11.45	10.83	-73.06	218.56	-587.41	757.41	736.26	21.15	35.804	
3,100.00	2,651.61	2,820.86	2,433.65	11.78	11.09	-72.92	219.20	-622.81	757.90	736.22	21.68	34.958	
3,150.00	2,658.16	2,850.00	2,437.38	12.12	11.30	-72.88	219.73	-651.70	758.08	735.91	22.17	34.201	
3,200.00	2,660.36	2,892.85	2,440.19	12.46	11.62	-72.95	220.51	-694.44	757.81	735.01	22.80	33.232	
3,220.44	2,660.00	2,907.57	2,440.42	12.61	11.72	-73.01	220.77	-709.16	757.61	734.57	23.04	32.877	
3,252.14	2,658.88	2,930.92	2,440.00	12.84	11.90	-73.03	221.20	-732.50	757.45	734.02	23.43	32.326	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 1H - Wellbore #1 - Plan #1												Offset Site Error:	0.00 usft
Survey Program: 0-MWD+IFR1+MS												Offset Well Error:	0.00 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Distance		Minimum	Separation	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Separation (usft)	Factor	
3,300.00	2,657.19	2,978.12	2,438.20	13.20	12.26	73.02	222.06	-779.65	757.49	733.36	24.13	31.386	
3,400.00	2,653.66	3,078.12	2,434.37	13.99	13.08	73.00	223.88	-879.56	757.58	731.88	25.70	29.476	
3,500.00	2,650.14	3,178.12	2,430.55	14.82	13.93	72.98	225.70	-979.47	757.67	730.32	27.36	27.697	
3,600.00	2,646.61	3,278.11	2,426.72	15.69	14.82	72.96	227.52	-1,079.38	757.77	728.68	29.08	26.055	
3,700.00	2,643.08	3,378.11	2,422.90	16.58	15.74	72.94	229.34	-1,179.29	757.86	726.99	30.87	24.550	
3,800.00	2,639.55	3,478.11	2,419.08	17.51	16.69	72.92	231.16	-1,279.20	757.95	725.24	32.71	23.173	
3,900.00	2,636.02	3,578.11	2,415.25	18.45	17.65	72.90	232.98	-1,379.11	758.04	723.45	34.59	21.916	
4,000.00	2,632.50	3,678.11	2,411.43	19.41	18.64	72.88	234.80	-1,479.02	758.13	721.63	36.50	20.768	
4,100.00	2,628.97	3,778.11	2,407.61	20.39	19.64	72.85	236.62	-1,578.93	758.22	719.77	38.45	19.719	
4,200.00	2,625.44	3,878.11	2,403.78	21.39	20.65	72.83	238.44	-1,678.84	758.31	717.89	40.42	18.760	
4,300.00	2,621.91	3,978.11	2,399.96	22.39	21.67	72.81	240.26	-1,778.75	758.41	715.99	42.42	17.880	
4,400.00	2,618.38	4,078.11	2,396.14	23.41	22.70	72.79	242.08	-1,878.66	758.50	714.07	44.43	17.071	
4,500.00	2,614.86	4,178.11	2,392.31	24.44	23.74	72.77	243.90	-1,978.57	758.59	712.13	46.46	16.327	
4,600.00	2,611.33	4,278.11	2,388.49	25.47	24.79	72.75	245.72	-2,078.48	758.68	710.17	48.51	15.641	
4,700.00	2,607.80	4,378.11	2,384.67	26.51	25.84	72.73	247.54	-2,178.39	758.77	708.21	50.56	15.006	
4,800.00	2,604.27	4,478.11	2,380.84	27.56	26.90	72.71	249.36	-2,278.30	758.87	706.23	52.63	14.418	
4,900.00	2,600.74	4,578.11	2,377.02	28.61	27.97	72.68	251.18	-2,378.21	758.96	704.25	54.71	13.872	
5,000.00	2,597.21	4,678.11	2,373.19	29.67	29.04	72.66	253.00	-2,478.12	759.05	702.25	56.80	13.363	
5,100.00	2,593.69	4,778.11	2,369.37	30.73	30.11	72.64	254.82	-2,578.03	759.14	700.25	58.90	12.889	
5,200.00	2,590.16	4,878.11	2,365.55	31.80	31.19	72.62	256.64	-2,677.94	759.24	698.24	61.00	12.447	
5,300.00	2,586.63	4,978.11	2,361.72	32.87	32.27	72.60	258.46	-2,777.85	759.33	696.22	63.11	12.032	
5,400.00	2,583.10	5,078.11	2,357.90	33.94	33.35	72.58	260.28	-2,877.76	759.42	694.20	65.22	11.644	
5,500.00	2,579.57	5,178.11	2,354.08	35.02	34.44	72.56	262.10	-2,977.67	759.51	692.17	67.34	11.278	
5,600.00	2,576.05	5,278.11	2,350.25	36.10	35.52	72.54	263.92	-3,077.58	759.61	690.14	69.47	10.935	
5,700.00	2,572.52	5,378.11	2,346.43	37.18	36.61	72.52	265.74	-3,177.49	759.70	688.11	71.60	10.611	
5,800.00	2,568.99	5,478.11	2,342.61	38.27	37.71	72.49	267.56	-3,277.40	759.79	686.07	73.73	10.305	
5,900.00	2,565.46	5,578.10	2,338.78	39.36	38.80	72.47	269.38	-3,377.31	759.89	684.02	75.86	10.016	
6,000.00	2,561.93	5,678.10	2,334.96	40.45	39.90	72.45	271.20	-3,477.22	759.98	681.98	78.00	9.743	
6,100.00	2,558.40	5,778.10	2,331.14	41.54	40.99	72.43	273.02	-3,577.13	760.07	679.93	80.14	9.484	
6,200.00	2,554.88	5,878.10	2,327.31	42.63	42.09	72.41	274.84	-3,677.04	760.17	677.88	82.29	9.238	
6,300.00	2,551.35	5,978.10	2,323.49	43.72	43.19	72.39	276.66	-3,776.95	760.26	675.83	84.44	9.004	
6,400.00	2,547.82	6,078.10	2,319.66	44.82	44.29	72.37	278.48	-3,876.86	760.36	673.77	86.58	8.782	
6,500.00	2,544.29	6,178.10	2,315.84	45.92	45.39	72.35	280.30	-3,976.77	760.45	671.71	88.74	8.570	
6,600.00	2,540.76	6,278.10	2,312.02	47.02	46.50	72.32	282.12	-4,076.68	760.54	669.66	90.89	8.368	
6,700.00	2,537.24	6,378.10	2,308.19	48.11	47.60	72.30	283.94	-4,176.59	760.64	667.60	93.04	8.175	
6,800.00	2,533.71	6,478.10	2,304.37	49.22	48.71	72.28	285.76	-4,276.50	760.73	665.53	95.20	7.991	
6,900.00	2,530.18	6,578.10	2,300.55	50.32	49.81	72.26	287.58	-4,376.41	760.83	663.47	97.36	7.815	
7,000.00	2,526.65	6,678.10	2,296.72	51.42	50.92	72.24	289.40	-4,476.32	760.92	661.41	99.52	7.646	
7,100.00	2,523.12	6,778.10	2,292.90	52.52	52.03	72.22	291.22	-4,576.23	761.02	659.34	101.68	7.485	
7,200.00	2,519.59	6,878.10	2,289.08	53.63	53.13	72.20	293.04	-4,676.14	761.11	657.27	103.84	7.330	
7,300.00	2,516.07	6,978.10	2,285.25	54.73	54.24	72.18	294.86	-4,776.04	761.21	655.21	106.00	7.181	
7,400.00	2,512.54	7,078.10	2,281.43	55.84	55.35	72.16	296.68	-4,875.95	761.30	653.14	108.16	7.038	
7,500.00	2,509.01	7,178.10	2,277.61	56.95	56.46	72.14	298.50	-4,975.86	761.40	651.07	110.33	6.901	
7,600.00	2,505.48	7,278.10	2,273.78	58.05	57.57	72.11	300.32	-5,075.77	761.49	649.00	112.49	6.769	
7,700.00	2,501.95	7,378.10	2,269.96	59.16	58.68	72.09	302.14	-5,175.68	761.59	646.93	114.66	6.642	
7,800.00	2,498.43	7,478.10	2,266.13	60.27	59.80	72.07	303.96	-5,275.59	761.68	644.85	116.83	6.520	
7,900.00	2,494.90	7,578.10	2,262.31	61.38	60.91	72.05	305.78	-5,375.50	761.78	642.78	119.00	6.402	
8,000.00	2,491.37	7,678.10	2,258.49	62.49	62.02	72.03	307.60	-5,475.41	761.87	640.71	121.16	6.288	
8,100.00	2,487.84	7,778.10	2,254.66	63.60	63.13	72.01	309.42	-5,575.32	761.97	638.64	123.33	6.178	
8,200.00	2,484.31	7,878.09	2,250.84	64.71	64.25	71.99	311.24	-5,675.23	762.06	636.56	125.50	6.072	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 1H - Wellbore #1 - Plan #1													Offset Site Error: 0.00 usft
Survey Program: 0-MWD+IFR1+MS													Offset Well Error: 0.00 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		Rule Assigned:		Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
8,300.00	2,480.79	7,978.09	2,247.02	65.82	65.36	71.97	313.06	-5,775.14	762.16	634.49	127.67	5.970	
8,400.00	2,477.26	8,078.09	2,243.19	66.93	66.47	71.95	314.88	-5,875.05	762.26	632.42	129.84	5.871	
8,463.97	2,475.00	8,142.06	2,240.75	67.64	67.18	71.93	316.04	-5,938.96	762.32	631.09	131.23	5.809 SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 70H - Wellbore #1 - Plan #1												Offset Site Error:	0.00 usft
Survey Program: 0-MWD+IFR1+MS												Offset Well Error:	0.00 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Semi Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Distance Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.00	0.00	0.00	0.00	0.00	0.00	179.43	-20.00	0.20	20.03				
100.00	100.00	99.00	99.00	0.14	0.14	179.43	-20.00	0.20	20.00	19.72	0.29	70.094	
200.00	200.00	199.00	199.00	0.50	0.50	179.43	-20.00	0.20	20.00	19.00	1.00	19.998	
300.00	300.00	299.00	299.00	0.86	0.86	179.43	-20.00	0.20	20.00	18.28	1.72	11.648	
330.22	330.22	329.02	329.02	0.96	0.96	19.45	-20.14	0.23	20.00	18.07	1.92	10.389 CC	
400.00	399.98	398.33	398.31	1.20	1.20	20.12	-21.65	0.53	20.02	17.62	2.40	8.336	
500.00	499.84	497.64	497.49	1.55	1.54	22.26	-26.68	1.55	20.18	17.11	3.08	6.561	
600.00	599.45	596.96	596.42	1.90	1.89	25.74	-35.07	3.25	20.53	16.77	3.76	5.454	
700.00	698.70	696.26	695.00	2.26	2.25	30.36	-46.82	5.63	21.15	16.69	4.46	4.741 ES	
800.00	797.47	795.55	793.08	2.62	2.61	35.85	-61.90	8.68	22.14	16.98	5.17	4.285	
900.00	895.62	894.83	890.57	2.99	2.97	41.84	-80.31	12.40	23.61	17.73	5.89	4.011	
1,000.00	993.06	994.09	987.32	3.36	3.34	47.93	-102.01	16.79	25.64	19.02	6.62	3.873	
1,100.00	1,089.64	1,093.33	1,083.23	3.74	3.71	53.76	-126.98	21.84	28.28	20.91	7.37	3.836 SF	
1,200.00	1,185.27	1,192.55	1,178.18	4.13	4.10	59.10	-155.18	27.55	31.56	23.42	8.14	3.875	
1,300.00	1,279.82	1,291.75	1,272.06	4.53	4.49	63.82	-186.58	33.90	35.48	26.54	8.94	3.969	
1,390.43	1,364.29	1,381.42	1,355.92	4.90	4.86	67.54	-217.69	40.20	39.55	29.88	9.67	4.089	
1,400.00	1,373.17	1,390.92	1,364.74	4.94	4.90	67.89	-221.14	40.89	40.02	30.27	9.75	4.104	
1,500.00	1,466.02	1,490.02	1,456.09	5.36	5.32	69.02	-258.79	48.51	45.85	35.28	10.57	4.337	
1,600.00	1,558.86	1,588.86	1,545.82	5.79	5.75	66.65	-299.41	56.73	53.41	42.03	11.38	4.694	
1,700.00	1,651.70	1,687.66	1,634.13	6.21	6.18	62.42	-342.81	65.51	62.84	50.66	12.18	5.159	
1,800.00	1,744.55	1,787.06	1,722.67	6.64	6.63	58.85	-387.09	74.47	72.95	59.94	13.01	5.606	
1,830.50	1,772.86	1,817.37	1,749.68	6.77	6.76	57.96	-400.59	77.20	76.08	62.81	13.27	5.734	
1,850.00	1,791.02	1,836.76	1,766.95	6.86	6.85	53.89	-409.23	78.95	77.97	64.54	13.43	5.805	
1,900.00	1,837.92	1,886.39	1,811.16	7.07	7.08	40.93	-431.33	83.42	81.86	68.03	13.83	5.919	
1,950.00	1,885.17	1,935.75	1,855.12	7.27	7.30	24.80	-453.32	87.87	84.78	70.58	14.21	5.968	
2,000.00	1,932.52	1,984.57	1,898.62	7.48	7.53	6.48	-475.06	92.27	87.51	72.95	14.56	6.009	
2,050.00	1,979.75	2,032.63	1,941.43	7.67	7.75	-12.72	-496.47	96.60	91.10	76.19	14.91	6.109	
2,100.00	2,026.63	2,079.70	1,983.35	7.85	7.96	-31.47	-517.43	100.84	96.75	81.48	15.27	6.338	
2,150.00	2,072.92	2,125.53	2,024.18	8.03	8.18	-48.72	-537.85	104.97	105.59	89.95	15.64	6.751	
2,200.00	2,118.41	2,169.92	2,063.72	8.20	8.38	-63.81	-557.62	108.97	118.44	102.40	16.04	7.385	
2,250.00	2,162.87	2,212.63	2,101.77	8.36	8.58	-76.49	-576.65	112.82	135.63	119.18	16.44	8.247	
2,300.00	2,206.09	2,253.48	2,138.15	8.51	8.77	-86.83	-594.84	116.50	157.10	140.26	16.84	9.327	
2,350.00	2,247.85	2,292.24	2,172.69	8.65	8.95	-95.09	-612.10	119.99	182.60	165.38	17.22	10.602	
2,400.00	2,287.96	2,328.75	2,205.20	8.79	9.12	-101.55	-628.36	123.28	211.75	194.17	17.58	12.047	
2,450.00	2,326.21	2,362.81	2,235.54	8.91	9.28	-106.49	-643.54	126.35	244.18	226.28	17.90	13.638	
2,500.00	2,362.42	2,394.27	2,263.57	9.03	9.43	-110.11	-657.55	129.19	279.55	261.35	18.20	15.357	
2,550.00	2,396.41	2,422.96	2,289.13	9.14	9.56	-112.55	-670.33	131.77	317.53	299.05	18.48	17.185	
2,600.00	2,428.02	2,448.76	2,312.11	9.24	9.68	-113.87	-681.82	134.10	357.81	339.08	18.72	19.110	
2,650.00	2,457.09	2,471.53	2,332.39	9.37	9.79	-114.05	-691.96	136.15	400.10	381.16	18.94	21.122	
2,700.22	2,483.59	2,491.24	2,349.95	9.57	9.88	-112.92	-700.74	137.93	444.33	425.19	19.14	23.220	
2,800.00	2,533.49	2,527.20	2,381.98	10.03	10.05	-118.29	-716.76	141.17	534.38	514.92	19.47	27.449	
2,900.22	2,583.59	2,563.31	2,414.15	10.55	10.22	-122.48	-732.84	144.42	625.72	605.93	19.79	31.619	
2,950.00	2,606.58	2,579.45	2,428.53	10.83	10.30	-113.79	-740.03	145.87	671.74	651.80	19.94	33.686	
3,000.00	2,625.73	2,591.98	2,439.68	11.13	10.35	-102.70	-745.61	147.00	718.77	698.69	20.07	35.809	
3,050.00	2,640.78	3,495.57	3,144.43	11.45	13.07	-141.70	-956.47	-269.85	732.96	716.69	16.28	45.034	
3,100.00	2,651.61	3,543.25	3,168.27	11.78	13.14	-141.64	-955.72	-311.14	744.95	728.26	16.70	44.617	
3,150.00	2,658.16	3,589.43	3,191.36	12.12	13.23	-141.51	-955.00	-351.13	760.38	743.26	17.11	44.434	
3,200.00	2,660.36	3,633.78	3,213.53	12.46	13.37	-141.27	-954.30	-389.53	779.20	761.68	17.53	44.456	
3,220.44	2,660.00	4,014.80	3,298.52	12.61	15.39	-145.21	-947.69	-754.22	779.26	763.95	15.32	50.882	
3,300.00	2,657.19	4,094.37	3,295.49	13.20	15.91	-145.20	-946.25	-833.71	779.08	762.69	16.39	47.538	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 70H - Wellbore #1 - Plan #1												Offset Site Error:	0.00 usft
Survey Program: 0-MWD+IFR1+MS												Offset Well Error:	0.00 usft
Rule Assigned:												Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Semi Major Axis Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
3,400.00	2,653.66	4,194.36	3,291.68	13.99	16.62	-145.19	-944.44	-933.63	778.86	761.04	17.82	43.710	
3,500.00	2,650.14	4,294.36	3,287.87	14.82	17.36	-145.18	-942.63	-1,033.54	778.63	759.31	19.32	40.309	
3,600.00	2,646.61	4,394.36	3,284.06	15.69	18.14	-145.17	-940.82	-1,133.45	778.40	757.53	20.87	37.302	
3,700.00	2,643.08	4,494.36	3,280.26	16.58	18.96	-145.15	-939.01	-1,233.36	778.17	755.71	22.46	34.645	
3,800.00	2,639.55	4,594.36	3,276.45	17.51	19.80	-145.14	-937.20	-1,333.27	777.95	753.86	24.09	32.295	
3,900.00	2,636.02	4,694.36	3,272.64	18.45	20.67	-145.13	-935.39	-1,433.18	777.72	751.98	25.74	30.210	
4,000.00	2,632.50	4,794.36	3,268.83	19.41	21.56	-145.12	-933.58	-1,533.09	777.49	750.07	27.42	28.354	
4,100.00	2,628.97	4,894.36	3,265.02	20.39	22.47	-145.11	-931.77	-1,633.00	777.27	748.15	29.12	26.694	
4,200.00	2,625.44	4,994.36	3,261.22	21.39	23.40	-145.09	-929.96	-1,732.91	777.04	746.21	30.83	25.204	
4,300.00	2,621.91	5,094.36	3,257.41	22.39	24.35	-145.08	-928.15	-1,832.82	776.81	744.26	32.56	23.861	
4,400.00	2,618.38	5,194.36	3,253.60	23.41	25.31	-145.07	-926.34	-1,932.73	776.59	742.29	34.29	22.646	
4,500.00	2,614.86	5,294.36	3,249.79	24.44	26.28	-145.06	-924.53	-2,032.64	776.36	740.32	36.04	21.542	
4,600.00	2,611.33	5,394.36	3,245.98	25.47	27.27	-145.04	-922.72	-2,132.55	776.13	738.34	37.79	20.536	
4,700.00	2,607.80	5,494.36	3,242.18	26.51	28.26	-145.03	-920.90	-2,232.46	775.91	736.35	39.56	19.615	
4,800.00	2,604.27	5,594.36	3,238.37	27.56	29.26	-145.02	-919.09	-2,332.37	775.68	734.35	41.33	18.770	
4,900.00	2,600.74	5,694.36	3,234.56	28.61	30.28	-145.01	-917.28	-2,432.29	775.45	732.35	43.10	17.992	
5,000.00	2,597.21	5,794.36	3,230.75	29.67	31.29	-145.00	-915.47	-2,532.20	775.23	730.34	44.88	17.273	
5,100.00	2,593.69	5,894.36	3,226.94	30.73	32.32	-144.98	-913.66	-2,632.11	775.00	728.33	46.67	16.608	
5,200.00	2,590.16	5,994.36	3,223.14	31.80	33.35	-144.97	-911.85	-2,732.02	774.77	726.32	48.45	15.990	
5,300.00	2,586.63	6,094.36	3,219.33	32.87	34.39	-144.96	-910.04	-2,831.93	774.55	724.30	50.25	15.415	
5,400.00	2,583.10	6,194.36	3,215.52	33.94	35.43	-144.95	-908.23	-2,931.84	774.32	722.28	52.04	14.879	
5,500.00	2,579.57	6,294.36	3,211.71	35.02	36.48	-144.94	-906.42	-3,031.75	774.09	720.25	53.84	14.378	
5,600.00	2,576.05	6,394.36	3,207.90	36.10	37.53	-144.92	-904.61	-3,131.66	773.87	718.23	55.64	13.908	
5,700.00	2,572.52	6,494.36	3,204.10	37.18	38.59	-144.91	-902.80	-3,231.57	773.64	716.20	57.44	13.468	
5,800.00	2,568.99	6,594.36	3,200.29	38.27	39.65	-144.90	-900.99	-3,331.48	773.41	714.16	59.25	13.053	
5,900.00	2,565.46	6,694.36	3,196.48	39.36	40.71	-144.89	-899.18	-3,431.39	773.19	712.13	61.06	12.663	
6,000.00	2,561.93	6,794.36	3,192.67	40.45	41.78	-144.87	-897.37	-3,531.30	772.96	710.09	62.87	12.295	
6,100.00	2,558.40	6,894.36	3,188.86	41.54	42.84	-144.86	-895.56	-3,631.21	772.73	708.05	64.68	11.947	
6,200.00	2,554.88	6,994.36	3,185.06	42.63	43.92	-144.85	-893.74	-3,731.12	772.51	706.01	66.49	11.618	
6,300.00	2,551.35	7,094.36	3,181.25	43.72	44.99	-144.84	-891.93	-3,831.04	772.28	703.97	68.31	11.306	
6,400.00	2,547.82	7,194.36	3,177.44	44.82	46.07	-144.83	-890.12	-3,930.95	772.06	701.93	70.13	11.010	
6,500.00	2,544.29	7,294.36	3,173.63	45.92	47.15	-144.81	-888.31	-4,030.86	771.83	699.89	71.94	10.728	
6,600.00	2,540.76	7,394.36	3,169.83	47.02	48.23	-144.80	-886.50	-4,130.77	771.60	697.84	73.76	10.461	
6,700.00	2,537.24	7,494.36	3,166.02	48.11	49.31	-144.79	-884.69	-4,230.68	771.38	695.79	75.58	10.206	
6,800.00	2,533.71	7,594.36	3,162.21	49.22	50.39	-144.78	-882.88	-4,330.59	771.15	693.75	77.41	9.962	
6,900.00	2,530.18	7,694.36	3,158.40	50.32	51.48	-144.76	-881.07	-4,430.50	770.93	691.70	79.23	9.730	
7,000.00	2,526.65	7,794.36	3,154.59	51.42	52.57	-144.75	-879.26	-4,530.41	770.70	689.65	81.05	9.509	
7,100.00	2,523.12	7,894.36	3,150.79	52.52	53.66	-144.74	-877.45	-4,630.32	770.47	687.60	82.88	9.296	
7,200.00	2,519.59	7,994.36	3,146.98	53.63	54.75	-144.73	-875.64	-4,730.23	770.25	685.54	84.70	9.093	
7,300.00	2,516.07	8,094.36	3,143.17	54.73	55.84	-144.71	-873.83	-4,830.14	770.02	683.49	86.53	8.899	
7,400.00	2,512.54	8,194.36	3,139.36	55.84	56.93	-144.70	-872.02	-4,930.05	769.80	681.44	88.36	8.712	
7,500.00	2,509.01	8,294.36	3,135.55	56.95	58.03	-144.69	-870.21	-5,029.96	769.57	679.38	90.19	8.533	
7,600.00	2,505.48	8,394.36	3,131.75	58.05	59.12	-144.68	-868.40	-5,129.87	769.34	677.33	92.02	8.361	
7,700.00	2,501.95	8,494.36	3,127.94	59.16	60.22	-144.67	-866.58	-5,229.78	769.12	675.27	93.85	8.195	
7,800.00	2,498.43	8,594.36	3,124.13	60.27	61.31	-144.65	-864.77	-5,329.70	768.89	673.21	95.68	8.036	
7,900.00	2,494.90	8,694.36	3,120.32	61.38	62.41	-144.64	-862.96	-5,429.61	768.67	671.16	97.51	7.883	
8,000.00	2,491.37	8,794.36	3,116.51	62.49	63.51	-144.63	-861.15	-5,529.52	768.44	669.10	99.34	7.735	
8,100.00	2,487.84	8,894.36	3,112.71	63.60	64.61	-144.62	-859.34	-5,629.43	768.22	667.04	101.18	7.593	
8,200.00	2,484.31	8,994.36	3,108.90	64.71	65.71	-144.60	-857.53	-5,729.34	767.99	664.98	103.01	7.455	
8,300.00	2,480.79	9,094.36	3,105.09	65.82	66.81	-144.59	-855.72	-5,829.25	767.77	662.92	104.85	7.323	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 70H - Wellbore #1 - Plan #1													Offset Site Error: 0.00 usft
Survey Program: 0-MWD+IFR1+MS													Offset Well Error: 0.00 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		Rule Assigned:		Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
8,400.00	2,477.26	9,194.35	3,101.28	66.93	67.92	-144.58	-853.91	-5,929.16	767.54	660.86	106.68	7.195	
8,435.41	2,476.01	9,228.02	3,100.00	67.32	68.29	-144.57	-853.30	-5,962.80	767.46	660.13	107.33	7.151	
8,463.97	2,475.00	9,228.02	3,100.00	67.64	68.29	-144.57	-853.30	-5,962.80	767.99	660.22	107.78	7.126	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 71H - Wellbore #1 - Plan #1													Offset Site Error: 0.00 usft	
Survey Program: 0-MWD+IFR1+MS							Offset Wellbore Centre		Rule Assigned:				Offset Well Error: 0.00 usft	
Reference	Offset	Semi Major Axis							Distance				Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.00	0.00	3.00	3.00	0.00	0.00	-0.86	40.00	-0.60	40.00					
100.00	100.00	103.00	103.00	0.14	0.15	-0.86	40.00	-0.60	40.00	39.71	0.30	134.455		
200.00	200.00	203.00	203.00	0.50	0.51	-0.86	40.00	-0.60	40.00	38.99	1.01	39.434		
215.64	215.64	218.64	218.64	0.56	0.57	-0.86	40.00	-0.60	40.00	38.88	1.13	35.510 CC		
300.00	300.00	302.96	302.96	0.86	0.87	-0.86	40.00	-0.60	40.01	38.27	1.73	23.107 ES		
400.00	399.98	401.53	401.51	1.20	1.23	-160.92	41.73	-0.09	43.40	40.96	2.43	17.834		
500.00	499.84	500.00	499.84	1.55	1.58	-161.02	46.69	1.37	53.35	50.21	3.14	17.006		
600.00	599.45	596.12	595.59	1.90	1.93	-161.11	54.67	3.72	69.78	65.93	3.84	18.149		
700.00	698.70	690.93	689.72	2.26	2.28	-161.16	65.55	6.92	92.57	88.03	4.55	20.365		
800.00	797.47	783.35	781.06	2.62	2.62	-161.16	79.02	10.88	121.56	116.32	5.24	23.219		
900.00	895.62	872.90	869.09	2.99	2.96	-161.10	94.77	15.51	156.54	150.63	5.91	26.486		
1,000.00	993.06	962.91	957.15	3.36	3.29	-161.07	112.64	20.77	196.69	190.10	6.59	29.839		
1,100.00	1,089.64	1,053.02	1,045.28	3.74	3.62	-161.21	130.67	26.08	240.00	232.72	7.28	32.980		
1,200.00	1,185.27	1,141.64	1,131.95	4.13	3.94	-161.44	148.40	31.29	286.28	278.31	7.97	35.939		
1,300.00	1,279.82	1,228.64	1,217.03	4.53	4.27	-161.70	165.81	36.41	335.49	326.84	8.65	38.786		
1,390.43	1,364.29	1,305.83	1,292.53	4.90	4.55	-161.94	181.25	40.96	382.47	373.21	9.26	41.282		
1,400.00	1,373.17	1,313.93	1,300.45	4.94	4.58	-162.00	182.87	41.43	387.57	378.24	9.34	41.515		
1,500.00	1,466.02	1,398.49	1,383.15	5.36	4.90	-162.56	199.79	46.41	440.84	430.84	10.00	44.086		
1,600.00	1,558.86	1,483.05	1,465.85	5.79	5.21	-163.00	216.71	51.39	494.14	483.47	10.67	46.316		
1,700.00	1,651.70	1,567.61	1,548.55	6.21	5.53	-163.35	233.63	56.37	547.45	536.11	11.34	48.263		
1,800.00	1,744.55	1,652.17	1,631.26	6.64	5.84	-163.64	250.54	61.34	600.77	588.75	12.02	49.976		
1,830.50	1,772.86	1,677.96	1,656.48	6.77	5.94	-163.72	255.70	62.86	617.04	604.81	12.23	50.458		
1,850.00	1,791.02	1,694.49	1,672.64	6.86	6.00	-168.17	259.01	63.84	627.38	615.02	12.36	50.758		
1,900.00	1,837.92	1,737.17	1,714.38	7.07	6.16	-179.64	267.55	66.35	653.35	640.66	12.70	51.459		
1,950.00	1,885.17	1,780.10	1,756.37	7.27	6.33	-166.62	276.14	68.87	678.46	665.43	13.03	52.070		
2,000.00	1,932.52	1,823.07	1,798.40	7.48	6.49	-153.52	284.74	71.40	702.65	689.29	13.36	52.595		
2,050.00	1,979.75	1,865.89	1,840.27	7.67	6.65	-141.29	293.30	73.92	725.92	712.23	13.68	53.047		
2,100.00	2,026.63	1,908.33	1,881.78	7.85	6.81	-130.63	301.79	76.42	748.28	734.28	14.00	53.439		
2,150.00	2,072.92	1,950.19	1,922.72	8.03	6.96	-121.83	310.17	78.89	769.79	755.48	14.31	53.781		
2,200.00	2,118.41	1,991.27	1,962.90	8.20	7.12	-114.77	318.39	81.30	790.54	775.92	14.62	54.085		
2,250.00	2,162.87	2,031.37	2,002.12	8.36	7.27	-109.19	326.41	83.67	810.60	795.69	14.91	54.360		
2,300.00	2,206.09	2,070.29	2,040.18	8.51	7.42	-104.81	334.20	85.96	830.10	814.90	15.20	54.615		
2,350.00	2,247.85	2,107.85	2,076.91	8.65	7.56	-101.35	341.71	88.17	849.16	833.68	15.48	54.860		
2,400.00	2,287.96	2,143.85	2,112.12	8.79	7.70	-98.60	348.91	90.29	867.90	852.15	15.75	55.101		
2,450.00	2,326.21	2,178.13	2,145.65	8.91	7.82	-96.37	355.77	92.30	886.46	870.44	16.02	55.345		
2,500.00	2,362.42	2,210.51	2,177.32	9.03	7.95	-94.54	362.25	94.21	904.96	888.68	16.28	55.599		
2,550.00	2,396.41	2,240.85	2,206.99	9.14	8.06	-92.98	368.32	96.00	923.53	907.00	16.53	55.869		
2,600.00	2,428.02	2,268.99	2,234.51	9.24	8.17	-91.61	373.95	97.65	942.28	925.50	16.78	56.161		
2,650.00	2,457.09	2,294.79	2,259.74	9.37	8.26	-90.35	379.11	99.17	961.31	944.29	17.02	56.479		
2,700.22	2,483.59	2,318.22	2,282.66	9.57	8.35	-89.14	383.80	100.55	980.79	963.53	17.26	56.832		
2,800.00	2,533.49	2,362.25	2,325.72	10.03	8.52	-91.57	392.61	103.14	1,023.08	1,005.33	17.75	57.643		
2,900.22	2,583.59	2,406.46	2,368.96	10.55	8.69	-93.96	401.45	105.74	1,071.42	1,053.16	18.26	58.682		
2,950.00	2,606.58	2,426.51	2,388.56	10.83	8.76	-91.99	405.46	106.92	1,097.52	1,079.02	18.50	59.324		
3,000.00	2,625.73	2,442.68	2,404.38	11.13	8.82	-89.60	408.70	107.88	1,125.16	1,106.44	18.72	60.103		
3,050.00	2,640.78	2,454.77	2,416.20	11.45	8.87	-86.76	411.12	108.59	1,154.11	1,135.19	18.91	61.021		
3,100.00	2,651.61	3,343.15	3,132.17	11.78	12.05	-116.84	513.26	-307.53	1,163.25	1,140.81	22.44	51.838		
3,150.00	2,658.16	3,389.34	3,155.27	12.12	12.26	-116.79	513.99	-347.52	1,172.44	1,149.57	22.87	51.276		
3,200.00	2,660.36	3,433.69	3,177.44	12.46	12.48	-116.66	514.69	-385.92	1,183.84	1,160.56	23.28	50.856		
3,220.44	2,660.00	3,451.20	3,186.20	12.61	12.57	-116.57	514.97	-401.09	1,189.15	1,165.71	23.44	50.727		
3,300.00	2,657.19	3,879.07	3,271.41	13.20	15.08	-120.85	522.47	-811.87	1,193.13	1,167.65	25.48	46.827		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 71H - Wellbore #1 - Plan #1												Offset Site Error:	0.00 usft
Survey Program: 0-MWD+IFR1+MS												Offset Well Error:	0.00 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Warning					
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
3,400.00	2,653.66	3,979.06	3,266.63	13.99	15.79	120.80	524.29	-911.73	1,192.49	1,165.59	26.90	44.325	
3,500.00	2,650.14	4,079.05	3,261.85	14.82	16.54	120.75	526.11	-1,011.59	1,191.86	1,163.45	28.41	41.953	
3,600.00	2,646.61	4,179.05	3,257.06	15.69	17.33	120.70	527.94	-1,111.45	1,191.22	1,161.24	29.99	39.725	
3,700.00	2,643.08	4,279.04	3,252.28	16.58	18.15	120.64	529.76	-1,211.31	1,190.59	1,158.96	31.62	37.649	
3,800.00	2,639.55	4,379.03	3,247.50	17.51	19.01	120.59	531.58	-1,311.17	1,189.96	1,156.64	33.31	35.721	
3,900.00	2,636.02	4,479.02	3,242.72	18.45	19.89	120.54	533.41	-1,411.03	1,189.33	1,154.28	35.05	33.937	
4,000.00	2,632.50	4,579.01	3,237.93	19.41	20.79	120.49	535.23	-1,510.89	1,188.70	1,151.88	36.82	32.287	
4,100.00	2,628.97	4,679.01	3,233.15	20.39	21.72	120.44	537.05	-1,610.75	1,188.07	1,149.44	38.62	30.762	
4,200.00	2,625.44	4,779.00	3,228.37	21.39	22.66	120.38	538.88	-1,710.62	1,187.44	1,146.98	40.45	29.353	
4,300.00	2,621.91	4,878.99	3,223.59	22.39	23.62	120.33	540.70	-1,810.48	1,186.81	1,144.50	42.31	28.049	
4,400.00	2,618.38	4,978.98	3,218.81	23.41	24.59	120.28	542.52	-1,910.34	1,186.18	1,141.99	44.19	26.841	
4,500.00	2,614.86	5,078.97	3,214.02	24.44	25.57	120.23	544.34	-2,010.20	1,185.56	1,139.47	46.09	25.721	
4,600.00	2,611.33	5,178.97	3,209.24	25.47	26.57	120.17	546.17	-2,110.06	1,184.93	1,136.93	48.01	24.681	
4,700.00	2,607.80	5,278.96	3,204.46	26.51	27.57	120.12	547.99	-2,209.92	1,184.31	1,134.37	49.94	23.714	
4,800.00	2,604.27	5,378.95	3,199.68	27.56	28.59	120.07	549.81	-2,309.78	1,183.69	1,131.80	51.89	22.812	
4,900.00	2,600.74	5,478.94	3,194.90	28.61	29.61	120.01	551.64	-2,409.64	1,183.07	1,129.22	53.85	21.971	
5,000.00	2,597.21	5,578.94	3,190.11	29.67	30.64	119.96	553.46	-2,509.50	1,182.45	1,126.63	55.82	21.184	
5,100.00	2,593.69	5,678.93	3,185.33	30.73	31.67	119.91	555.28	-2,609.37	1,181.83	1,124.03	57.80	20.448	
5,200.00	2,590.16	5,778.92	3,180.55	31.80	32.71	119.86	557.10	-2,709.23	1,181.21	1,121.42	59.79	19.757	
5,300.00	2,586.63	5,878.91	3,175.77	32.87	33.76	119.80	558.93	-2,809.09	1,180.59	1,118.81	61.79	19.108	
5,400.00	2,583.10	5,978.90	3,170.98	33.94	34.81	119.75	560.75	-2,908.95	1,179.98	1,116.19	63.79	18.497	
5,500.00	2,579.57	6,078.90	3,166.20	35.02	35.86	119.70	562.57	-3,008.81	1,179.36	1,113.56	65.80	17.922	
5,600.00	2,576.05	6,178.89	3,161.42	36.10	36.92	119.64	564.40	-3,108.67	1,178.75	1,110.92	67.82	17.380	
5,700.00	2,572.52	6,278.88	3,156.64	37.18	37.99	119.59	566.22	-3,208.53	1,178.14	1,108.29	69.85	16.867	
5,800.00	2,568.99	6,378.87	3,151.86	38.27	39.05	119.54	568.04	-3,308.39	1,177.52	1,105.64	71.88	16.382	
5,900.00	2,565.46	6,478.86	3,147.07	39.36	40.12	119.48	569.87	-3,408.25	1,176.91	1,102.99	73.92	15.922	
6,000.00	2,561.93	6,578.86	3,142.29	40.45	41.19	119.43	571.69	-3,508.12	1,176.30	1,100.34	75.96	15.486	
6,100.00	2,558.40	6,678.85	3,137.51	41.54	42.27	119.38	573.51	-3,607.98	1,175.69	1,097.69	78.01	15.072	
6,200.00	2,554.88	6,778.84	3,132.73	42.63	43.34	119.32	575.33	-3,707.84	1,175.09	1,095.03	80.06	14.678	
6,300.00	2,551.35	6,878.83	3,127.95	43.72	44.42	119.27	577.16	-3,807.70	1,174.48	1,092.37	82.11	14.304	
6,400.00	2,547.82	6,978.83	3,123.16	44.82	45.50	119.22	578.98	-3,907.56	1,173.87	1,089.70	84.17	13.947	
6,500.00	2,544.29	7,078.82	3,118.38	45.92	46.59	119.16	580.80	-4,007.42	1,173.27	1,087.04	86.23	13.606	
6,600.00	2,540.76	7,178.81	3,113.60	47.02	47.67	119.11	582.63	-4,107.28	1,172.66	1,084.37	88.30	13.281	
6,700.00	2,537.24	7,278.80	3,108.82	48.11	48.76	119.05	584.45	-4,207.14	1,172.06	1,081.69	90.37	12.970	
6,800.00	2,533.71	7,378.79	3,104.03	49.22	49.85	119.00	586.27	-4,307.00	1,171.46	1,079.02	92.44	12.673	
6,900.00	2,530.18	7,478.79	3,099.25	50.32	50.94	118.95	588.10	-4,406.86	1,170.86	1,076.34	94.51	12.388	
7,000.00	2,526.65	7,578.78	3,094.47	51.42	52.03	118.89	589.92	-4,506.73	1,170.26	1,073.67	96.59	12.115	
7,100.00	2,523.12	7,678.77	3,089.69	52.52	53.12	118.84	591.74	-4,606.59	1,169.66	1,070.99	98.67	11.854	
7,200.00	2,519.59	7,778.76	3,084.91	53.63	54.22	118.78	593.56	-4,706.45	1,169.06	1,068.30	100.76	11.603	
7,300.00	2,516.07	7,878.75	3,080.12	54.73	55.31	118.73	595.39	-4,806.31	1,168.47	1,065.62	102.84	11.362	
7,400.00	2,512.54	7,978.75	3,075.34	55.84	56.41	118.68	597.21	-4,906.17	1,167.87	1,062.94	104.93	11.130	
7,500.00	2,509.01	8,078.74	3,070.56	56.95	57.51	118.62	599.03	-5,006.03	1,167.28	1,060.25	107.02	10.907	
7,600.00	2,505.48	8,178.73	3,065.78	58.05	58.60	118.57	600.86	-5,105.89	1,166.68	1,057.56	109.12	10.692	
7,700.00	2,501.95	8,278.72	3,061.00	59.16	59.70	118.51	602.68	-5,205.75	1,166.09	1,054.88	111.21	10.485	
7,800.00	2,498.43	8,378.71	3,056.21	60.27	60.80	118.46	604.50	-5,305.61	1,165.50	1,052.19	113.31	10.286	
7,900.00	2,494.90	8,478.71	3,051.43	61.38	61.90	118.40	606.32	-5,405.48	1,164.91	1,049.50	115.41	10.094	
8,000.00	2,491.37	8,578.70	3,046.65	62.49	63.01	118.35	608.15	-5,505.34	1,164.32	1,046.81	117.51	9.908	
8,100.00	2,487.84	8,678.69	3,041.87	63.60	64.11	118.29	609.97	-5,605.20	1,163.73	1,044.11	119.62	9.729	
8,200.00	2,484.31	8,778.68	3,037.08	64.71	65.21	118.24	611.79	-5,705.06	1,163.14	1,041.42	121.72	9.556	
8,300.00	2,480.79	8,878.68	3,032.30	65.82	66.32	118.19	613.62	-5,804.92	1,162.56	1,038.73	123.83	9.388	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Friesian 3 Federal Com 71H - Wellbore #1 - Plan #1													Offset Site Error: 0.00 usft
Survey Program: 0-MWD+IFR1+MS													Offset Well Error: 0.00 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		Rule Assigned:		Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
8,400.00	2,477.26	8,978.67	3,027.52	66.93	67.42	118.13	615.44	-5,904.78	1,161.97	1,036.03	125.94	9.226	
8,459.10	2,475.17	9,031.36	3,025.00	67.59	68.00	118.10	616.40	-5,957.40	1,161.64	1,034.52	127.13	9.138	
8,463.97	2,475.00	9,031.36	3,025.00	67.64	68.00	118.10	616.40	-5,957.40	1,161.65	1,034.47	127.18	9.134 SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Ottawa AOW Federal 2 - Wellbore #1 - Wellbore #1													Offset Site Error: 0.00 usft
Survey Program: 260-MWD													Offset Well Error: 0.00 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Rule Assigned:		Warning					
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
0.00	0.00	31.10	31.10	0.00	0.05	-96.58	-607.67	-5,270.82	5,305.73				
100.00	100.00	134.77	134.77	0.14	0.23	-96.57	-607.23	-5,270.81	5,305.68	5,305.31	0.37	N/A	
200.00	200.00	238.43	238.43	0.50	0.40	-96.56	-606.26	-5,270.79	5,305.55	5,304.65	0.90	5,896.060	
300.00	300.00	341.57	341.55	0.86	0.73	-96.55	-604.78	-5,270.77	5,305.36	5,303.78	1.59	3,342.754	
328.89	328.88	371.32	371.30	0.96	0.83	103.42	-604.27	-5,270.76	5,305.33	5,303.54	1.79	2,959.035	
400.00	399.98	444.51	444.47	1.20	1.10	103.45	-602.86	-5,270.73	5,305.52	5,303.22	2.30	2,307.413	
500.00	499.84	543.42	543.37	1.55	1.45	103.50	-600.80	-5,270.70	5,306.47	5,303.48	2.99	1,772.986	
600.00	599.45	640.89	640.82	1.90	1.80	103.58	-599.03	-5,270.66	5,308.28	5,304.59	3.69	1,438.112	
700.00	698.70	738.01	737.93	2.26	2.15	103.66	-597.55	-5,270.64	5,310.98	5,306.58	4.40	1,208.298	
800.00	797.47	839.36	839.26	2.62	2.51	103.78	-596.02	-5,270.61	5,314.54	5,309.42	5.12	1,037.636	
900.00	895.62	941.42	941.30	2.99	2.88	103.92	-593.83	-5,270.57	5,318.93	5,313.07	5.86	908.040	
1,000.00	993.06	1,041.50	1,041.34	3.36	3.24	104.08	-591.02	-5,270.52	5,324.17	5,317.58	6.59	807.475	
1,100.00	1,089.64	1,135.56	1,135.37	3.74	3.58	104.24	-588.33	-5,270.47	5,330.39	5,323.07	7.32	728.558	
1,200.00	1,185.27	1,229.57	1,229.35	4.13	3.92	104.41	-585.88	-5,270.42	5,337.64	5,329.60	8.05	663.306	
1,300.00	1,279.82	1,322.86	1,322.60	4.53	4.25	104.59	-583.54	-5,270.38	5,345.97	5,337.19	8.78	608.601	
1,390.43	1,364.29	1,406.18	1,405.90	4.90	4.55	104.76	-581.51	-5,270.34	5,354.46	5,345.01	9.45	566.324	
1,400.00	1,373.17	1,414.95	1,414.66	4.94	4.58	104.79	-581.30	-5,270.34	5,355.41	5,345.89	9.53	562.186	
1,500.00	1,466.02	1,506.56	1,506.25	5.36	4.91	105.17	-579.16	-5,270.30	5,365.48	5,355.21	10.27	522.302	
1,600.00	1,558.86	1,598.23	1,597.89	5.79	5.24	105.54	-577.09	-5,270.26	5,375.83	5,364.81	11.02	487.657	
1,700.00	1,651.70	1,689.97	1,689.62	6.21	5.57	105.91	-575.11	-5,270.23	5,386.44	5,374.66	11.78	457.330	
1,800.00	1,744.55	1,781.78	1,781.41	6.64	5.90	106.28	-573.19	-5,270.19	5,397.32	5,384.79	12.53	430.584	
1,830.50	1,772.86	1,809.80	1,809.42	6.77	6.00	106.39	-572.62	-5,270.18	5,400.69	5,387.93	12.77	423.068	
1,850.00	1,791.02	1,827.76	1,827.38	6.86	6.07	103.01	-572.26	-5,270.18	5,402.61	5,389.69	12.91	418.417	
1,900.00	1,837.92	1,874.19	1,873.80	7.07	6.23	93.19	-571.34	-5,270.16	5,405.20	5,391.91	13.29	406.801	
1,950.00	1,885.17	1,920.99	1,920.59	7.27	6.40	82.04	-570.43	-5,270.14	5,404.46	5,390.81	13.66	395.643	
2,000.00	1,932.52	1,967.92	1,967.51	7.48	6.57	70.36	-569.54	-5,270.13	5,400.39	5,386.37	14.03	384.969	
2,050.00	1,979.75	2,014.76	2,014.34	7.67	6.74	59.13	-568.66	-5,270.11	5,393.00	5,378.61	14.39	374.798	
2,100.00	2,026.63	2,061.27	2,060.85	7.85	6.91	49.12	-567.82	-5,270.10	5,382.31	5,367.57	14.74	365.125	
2,150.00	2,072.92	2,107.23	2,106.80	8.03	7.07	40.65	-567.00	-5,270.08	5,368.36	5,353.28	15.08	355.927	
2,200.00	2,118.41	2,152.53	2,152.08	8.20	7.23	33.64	-566.20	-5,270.07	5,351.23	5,335.82	15.41	347.165	
2,250.00	2,162.87	2,196.85	2,196.41	8.36	7.39	27.88	-565.41	-5,270.05	5,330.98	5,315.25	15.73	338.818	
2,300.00	2,206.09	2,239.95	2,239.49	8.51	7.55	23.08	-564.62	-5,270.04	5,307.70	5,291.66	16.04	330.867	
2,350.00	2,247.85	2,281.59	2,281.13	8.65	7.70	19.02	-563.85	-5,270.02	5,281.51	5,265.17	16.34	323.293	
2,400.00	2,287.96	2,321.59	2,321.12	8.79	7.84	15.48	-563.09	-5,270.01	5,252.52	5,235.90	16.62	316.082	
2,450.00	2,326.21	2,359.76	2,359.28	8.91	7.98	12.30	-562.35	-5,270.00	5,220.87	5,203.98	16.88	309.224	
2,500.00	2,362.42	2,395.89	2,395.41	9.03	8.11	9.33	-561.64	-5,269.98	5,186.70	5,169.57	17.13	302.712	
2,550.00	2,396.41	2,429.83	2,429.34	9.14	8.23	6.45	-560.96	-5,269.97	5,150.19	5,132.82	17.37	296.542	
2,600.00	2,428.02	2,461.41	2,460.91	9.24	8.34	3.51	-560.32	-5,269.96	5,111.51	5,093.92	17.58	290.713	
2,650.00	2,457.09	2,490.47	2,489.97	9.37	8.45	0.38	-559.72	-5,269.95	5,070.83	5,053.05	17.78	285.225	
2,700.22	2,483.59	2,516.99	2,516.48	9.57	8.54	-3.15	-559.17	-5,269.94	5,028.18	5,010.22	17.95	280.054	
2,800.00	2,533.49	2,566.93	2,566.41	10.03	8.72	-3.18	-558.12	-5,269.92	4,941.77	4,923.50	18.26	270.568	
2,900.22	2,583.59	2,617.09	2,616.55	10.55	8.90	-3.21	-557.04	-5,269.90	4,854.98	4,836.40	18.58	261.299	
2,950.00	2,606.58	2,640.06	2,639.52	10.83	8.99	-3.82	-556.54	-5,269.89	4,810.84	4,792.11	18.74	256.758	
3,000.00	2,625.73	2,659.18	2,658.63	11.13	9.05	-4.75	-556.12	-5,269.88	4,764.68	4,745.80	18.88	252.414	
3,050.00	2,640.78	2,674.20	2,673.66	11.45	9.11	-6.31	-555.80	-5,269.88	4,717.02	4,698.04	18.99	248.450	
3,100.00	2,651.61	2,685.02	2,684.48	11.78	9.15	-9.44	-555.57	-5,269.87	4,668.24	4,649.18	19.06	244.866	
3,150.00	2,658.16	2,691.56	2,691.01	12.12	9.17	-18.52	-555.43	-5,269.87	4,618.71	4,599.59	19.11	241.658	
3,200.00	2,660.36	2,693.75	2,693.20	12.46	9.18	-90.47	-555.39	-5,269.87	4,568.79	4,549.66	19.13	238.814	
3,220.44	2,660.00	2,693.40	2,692.85	12.61	9.18	-140.53	-555.39	-5,269.87	4,548.37	4,529.24	19.13	237.751	
3,300.00	2,657.19	2,690.60	2,690.05	13.20	9.17	-140.03	-555.45	-5,269.87	4,468.89	4,449.77	19.12	233.746	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design:		Friesian 3 Federal Com - Ottawa AOW Federal 2 - Wellbore #1 - Wellbore #1											Offset Site Error:		0.00 usft		
Survey Program:		260-MWD		Offset		Semi Major Axis		Offset Wellbore Centre		Rule Assigned:				Offset Well Error:		0.00 usft	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning				
3,400.00	2,653.66	2,687.07	2,686.52	13.99	9.15	-139.39	-555.53	-5,269.87	4,369.00	4,349.90	19.10	228.688					
3,500.00	2,650.14	2,683.55	2,683.00	14.82	9.14	-138.73	-555.60	-5,269.87	4,269.11	4,250.02	19.09	223.607					
3,600.00	2,646.61	2,680.03	2,679.48	15.69	9.13	-138.06	-555.68	-5,269.88	4,169.23	4,150.15	19.08	218.504					
3,700.00	2,643.08	2,676.50	2,675.96	16.58	9.12	-137.36	-555.75	-5,269.88	4,069.35	4,050.28	19.07	213.380					
3,800.00	2,639.55	2,672.98	2,672.43	17.51	9.10	-136.65	-555.83	-5,269.88	3,969.47	3,950.41	19.06	208.237					
3,900.00	2,636.02	2,669.46	2,668.91	18.45	9.09	-135.92	-555.90	-5,269.88	3,869.59	3,850.54	19.06	203.075					
4,000.00	2,632.50	2,665.93	2,665.39	19.41	9.08	-135.17	-555.98	-5,269.88	3,769.72	3,750.67	19.05	197.895					
4,100.00	2,628.97	2,662.41	2,661.87	20.39	9.07	-134.40	-556.05	-5,269.88	3,669.85	3,650.81	19.04	192.698					
4,200.00	2,625.44	2,658.89	2,658.34	21.39	9.05	-133.62	-556.13	-5,269.88	3,569.99	3,550.94	19.04	187.485					
4,300.00	2,621.91	2,655.36	2,654.82	22.39	9.04	-132.81	-556.21	-5,269.89	3,470.12	3,451.09	19.04	182.258					
4,400.00	2,618.38	2,651.84	2,651.30	23.41	9.03	-131.98	-556.28	-5,269.89	3,370.27	3,351.23	19.04	177.016					
4,500.00	2,614.86	2,648.32	2,647.78	24.44	9.02	-131.13	-556.36	-5,269.89	3,270.42	3,251.38	19.04	171.761					
4,600.00	2,611.33	2,644.79	2,644.26	25.47	9.00	-130.26	-556.43	-5,269.89	3,170.57	3,151.53	19.04	166.494					
4,700.00	2,607.80	2,641.27	2,640.73	26.51	8.99	-129.36	-556.51	-5,269.89	3,070.73	3,051.68	19.05	161.216					
4,800.00	2,604.27	2,637.75	2,637.21	27.56	8.98	-128.44	-556.59	-5,269.89	2,970.90	2,951.84	19.05	155.926					
4,900.00	2,600.74	2,634.22	2,633.69	28.61	8.96	-127.50	-556.66	-5,269.89	2,871.07	2,852.01	19.06	150.627					
5,000.00	2,597.21	2,630.70	2,630.17	29.67	8.95	-126.54	-556.74	-5,269.90	2,771.25	2,752.18	19.07	145.318					
5,100.00	2,593.69	2,627.18	2,626.64	30.73	8.94	-125.56	-556.82	-5,269.90	2,671.44	2,652.36	19.08	140.000					
5,200.00	2,590.16	2,623.66	2,623.12	31.80	8.93	-124.55	-556.89	-5,269.90	2,571.64	2,552.55	19.10	134.673					
5,300.00	2,586.63	2,620.13	2,619.59	32.87	8.91	-123.51	-556.97	-5,269.90	2,471.86	2,452.74	19.11	129.338					
5,400.00	2,583.10	2,616.59	2,616.06	33.94	8.90	-122.45	-557.05	-5,269.90	2,372.08	2,352.95	19.13	123.995					
5,500.00	2,579.57	2,613.06	2,612.53	35.02	8.89	-121.36	-557.12	-5,269.90	2,272.32	2,253.17	19.15	118.643					
5,600.00	2,576.05	2,609.53	2,609.00	36.10	8.88	-120.25	-557.20	-5,269.90	2,172.57	2,153.40	19.18	113.282					
5,700.00	2,572.52	2,606.00	2,605.47	37.18	8.86	-119.12	-557.28	-5,269.90	2,072.85	2,053.64	19.21	107.912					
5,800.00	2,568.99	2,602.47	2,601.94	38.27	8.85	-117.96	-557.35	-5,269.91	1,973.14	1,953.90	19.24	102.532					
5,900.00	2,565.46	2,598.94	2,598.41	39.36	8.84	-116.78	-557.43	-5,269.91	1,873.46	1,854.18	19.29	97.141					
6,000.00	2,561.93	2,595.41	2,594.88	40.45	8.83	-115.58	-557.51	-5,269.91	1,773.81	1,754.47	19.34	91.736					
6,100.00	2,558.40	2,591.87	2,591.35	41.54	8.81	-114.35	-557.58	-5,269.91	1,674.19	1,654.80	19.40	86.315					
6,200.00	2,554.88	2,588.34	2,587.82	42.63	8.80	-113.10	-557.66	-5,269.91	1,574.62	1,555.15	19.47	80.877					
6,300.00	2,551.35	2,584.81	2,584.29	43.72	8.79	-111.82	-557.73	-5,269.91	1,475.09	1,455.53	19.56	75.416					
6,400.00	2,547.82	2,581.28	2,580.76	44.82	8.77	-110.53	-557.81	-5,269.91	1,375.62	1,355.95	19.67	69.929					
6,500.00	2,544.29	2,577.75	2,577.22	45.92	8.76	-109.21	-557.88	-5,269.92	1,276.22	1,256.41	19.81	64.410					
6,600.00	2,540.76	2,574.22	2,573.69	47.02	8.75	-107.87	-557.96	-5,269.92	1,176.92	1,156.92	20.00	58.854					
6,700.00	2,537.24	2,570.68	2,570.16	48.11	8.74	-106.52	-558.04	-5,269.92	1,077.74	1,057.50	20.24	53.254					
6,800.00	2,533.71	2,567.15	2,566.63	49.22	8.72	-105.14	-558.11	-5,269.92	978.70	958.14	20.56	47.603					
6,900.00	2,530.18	2,563.62	2,563.10	50.32	8.71	-103.75	-558.19	-5,269.92	879.87	858.87	21.00	41.898					
7,000.00	2,526.65	2,560.09	2,559.57	51.42	8.70	-102.35	-558.26	-5,269.92	781.33	759.71	21.62	36.142					
7,100.00	2,523.12	2,556.56	2,556.04	52.52	8.69	-100.93	-558.34	-5,269.92	683.19	660.68	22.51	30.352					
7,200.00	2,519.59	2,553.03	2,552.51	53.63	8.67	-99.50	-558.41	-5,269.93	585.65	561.82	23.83	24.573					
7,300.00	2,516.07	2,549.50	2,548.98	54.73	8.66	-98.06	-558.49	-5,269.93	489.09	463.22	25.87	18.902					
7,400.00	2,512.54	2,545.96	2,545.45	55.84	8.65	-96.61	-558.56	-5,269.93	394.22	365.05	29.17	13.515					
7,500.00	2,509.01	2,542.43	2,541.92	56.95	8.63	-95.15	-558.64	-5,269.93	302.62	267.85	34.77	8.704					
7,600.00	2,505.48	2,538.90	2,538.39	58.05	8.62	-93.69	-558.71	-5,269.93	218.45	173.70	44.75	4.882					
7,700.00	2,501.95	2,535.37	2,534.86	59.16	8.61	-92.23	-558.78	-5,269.93	154.41	93.70	60.71	2.543					
7,769.55	2,499.50	2,532.91	2,532.40	59.93	8.60	-91.21	-558.84	-5,269.93	137.88	69.45	68.43	2.015	CC, ES, SF				
7,800.00	2,498.43	2,531.84	2,531.32	60.27	8.60	-90.76	-558.86	-5,269.93	141.20	73.38	67.83	2.082					
7,900.00	2,494.90	2,528.31	2,527.79	61.38	8.58	-89.29	-558.93	-5,269.94	189.76	134.62	55.14	3.441					
8,000.00	2,491.37	2,524.77	2,524.26	62.49	8.57	-87.83	-559.01	-5,269.94	268.43	224.69	43.74	6.137					
8,100.00	2,487.84	2,521.24	2,520.73	63.60	8.56	-86.37	-559.08	-5,269.94	357.88	320.93	36.95	9.686					
8,200.00	2,484.31	2,517.71	2,517.20	64.71	8.55	-84.92	-559.15	-5,269.94	451.74	418.90	32.84	13.755					

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report



Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design: Friesian 3 Federal Com - Ottawa AOW Federal 2 - Wellbore #1 - Wellbore #1													Offset Site Error: 0.00 usft
Survey Program: 260-MWD													Offset Well Error: 0.00 usft
Reference	Offset	Semi Major Axis		Offset Wellbore Centre		Distance		Rule Assigned:		Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	+N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
8,300.00	2,480.79	2,514.18	2,513.67	65.82	8.53	-83.47	-559.23	-5,269.94	547.76	517.55	30.21	18.133	
8,400.00	2,477.26	2,510.65	2,510.14	66.93	8.52	-82.04	-559.30	-5,269.94	644.97	616.55	28.42	22.692	
8,463.97	2,475.00	2,508.39	2,507.88	67.64	8.51	-81.13	-559.35	-5,269.94	707.55	679.98	27.57	25.665	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report




Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to KB @ 3492.00usft (GL: 3472.00' + 20'
 Offset Depths are relative to Offset Datum
 Central Meridian is -104.33333334

Coordinates are relative to: Friesian 3 Federal Com 10H
 Coordinate System is US State Plane 1983, New Mexico Eastern Zone
 Grid Convergence at Surface is: -0.07°

Ladder Plot

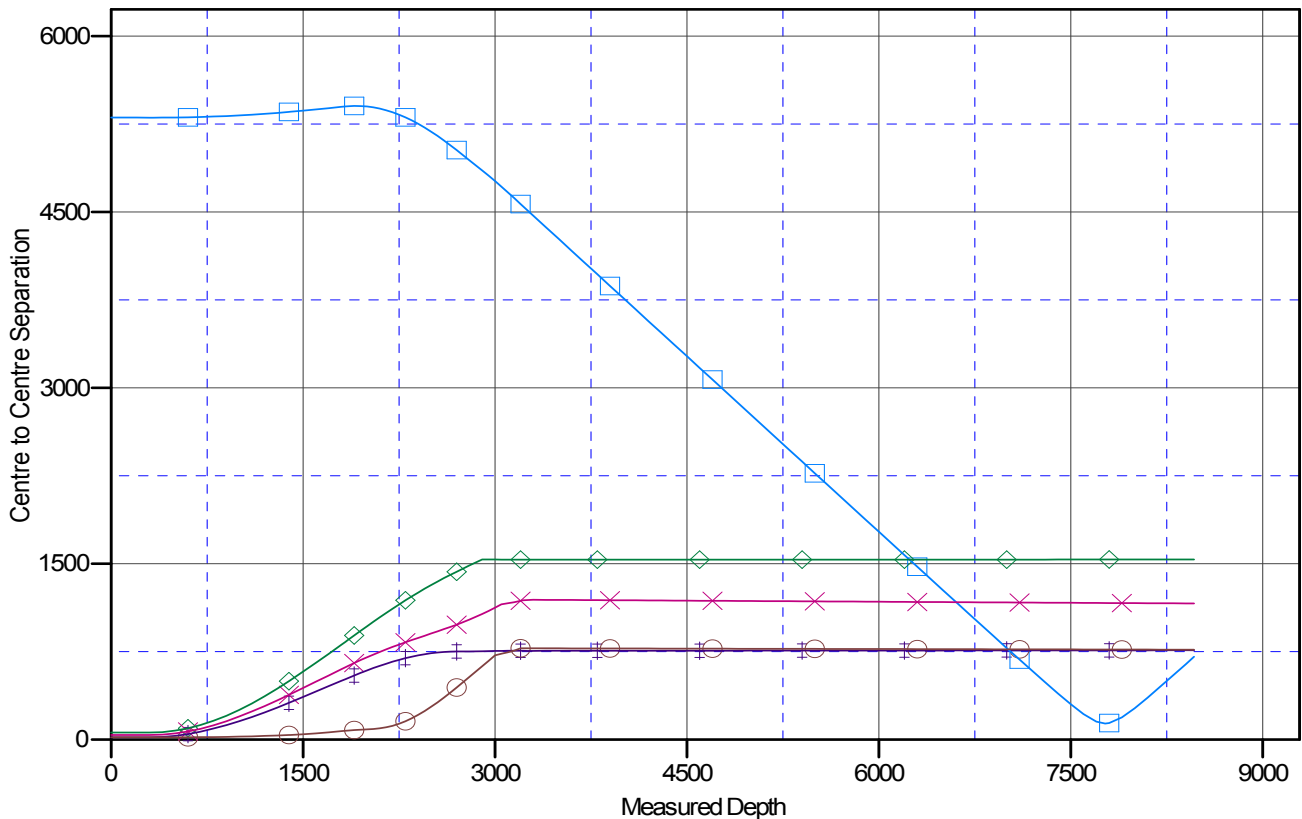

LEGEND

Friesian 3 Federal Com 1H, Wellbore #1, Plan #1 V0
 Friesian 3 Federal Com 70H, Wellbore #1, Plan #1 V0
 Friesian 3 Federal Com 71H, Wellbore #1, Plan #1 V0
 Ottawa AOW Federal 2, Wellbore #1, Wellbore #1 V0
 Friesian 3 Federal Com 11H, Wellbore #1, Plan #1 V0

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Patriot Drilling Services

Anticollision Report




Company:	Spur Energy Partners	Local Co-ordinate Reference:	Well Friesian 3 Federal Com 10H
Project:	Eddy County, NM	TVD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Reference Site:	Friesian 3 Federal Com	MD Reference:	KB @ 3492.00usft (GL: 3472.00' + 20' KB (Akita 57))
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Friesian 3 Federal Com 10H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to KB @ 3492.00usft (GL: 3472.00' + 20'
 Offset Depths are relative to Offset Datum
 Central Meridian is -104.33333334

Coordinates are relative to: Friesian 3 Federal Com 10H
 Coordinate System is US State Plane 1983, New Mexico Eastern Zone
 Grid Convergence at Surface is: -0.07°

Separation Factor Plot

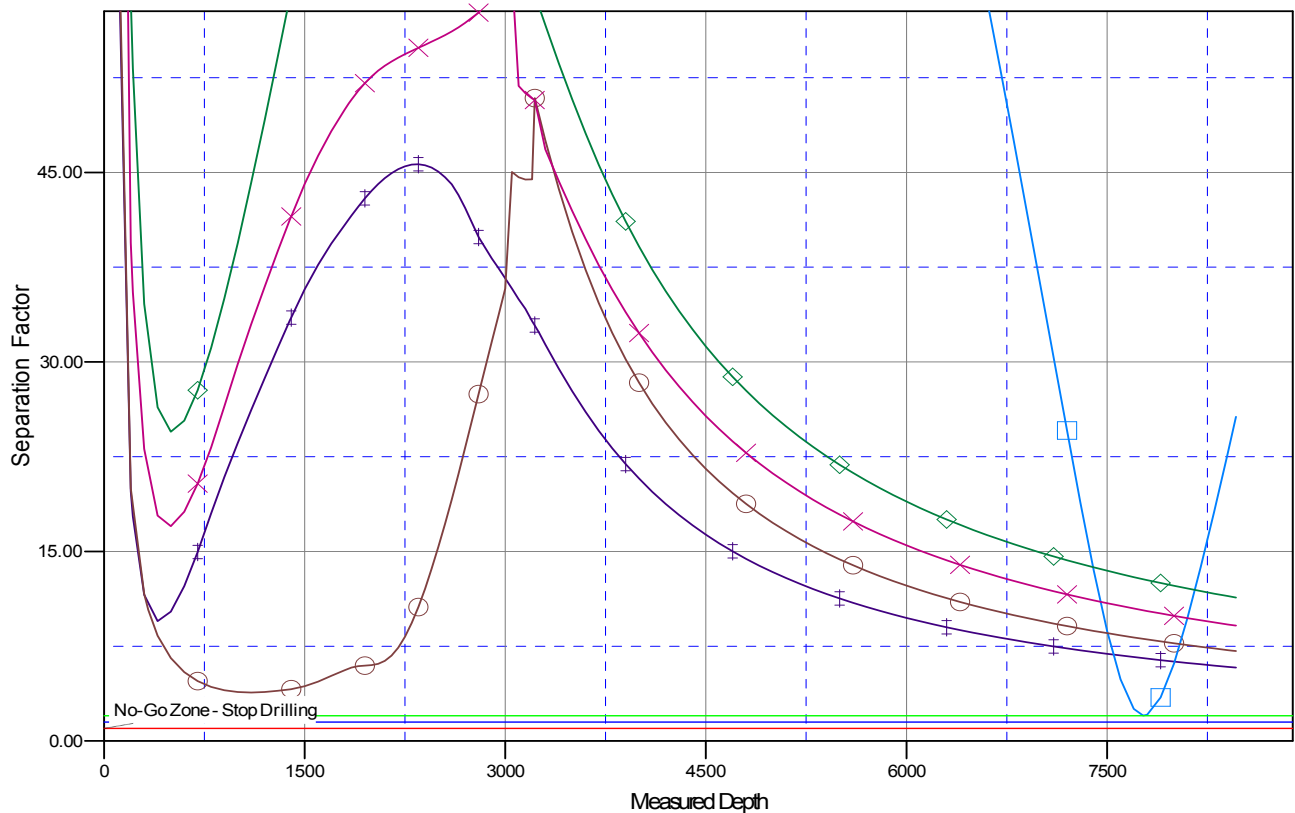

LEGEND

Friesian3Fedral/Com 11H, Wellbore#1, Plan#1 V0
 Friesian3Fedral/Com 70H, Wellbore#1, Plan#1 V0
 Friesian3Fedral/Com 71H, Wellbore#1, Plan#1 V0
 Friesian3Fedral/Com 11H, Wellbore#1, Plan#1 V0
 Ottawa AOW Fedral 2, Wellbore #1, Wellbore#1 V0

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Pecos District

Application for Permit to Drill

Conditions of Approval

Geology Concerns

Potash	☒ None	☐ Secretary	☐ R-111-P
Cave/Karst	☒ Medium	☐ High	☐ Critical
H2S	☒ None	☐ Below 100 PPM	☐ Above 100 PPM
Other	☐ 4 String Area	☐ Capitan Reef	☐ SWD Well

Note: The geology of the area where the well is being drilled determines the COAs that apply, not the above table.

Additional Engineering Requirements

Surface casing must be set at: 1,185 feet

Intermediate casing must be set at: No change from drill plan

General Requirements

1. Changes to the approved APD casing program need prior approval.
2. The Bureau of Land Management (BLM) will be notified in advance for a representative to witness:
 - a. Well spudding (minimum of 24 hours notice)
 - b. Setting and/or cementing of all casing strings (minimum of 4 hours notice)
 - c. BOPE tests (minimum of 4 hours notice)

Eddy County

620 East Greene Street, Carlsbad, NM 88220

(575) 361-2822

BLM_NM_CFO_DrillingNotifications@BLM.GOV

Lea County

414 West Taylor, Hobbs, NM 88240

(575) 689-5981

3. The initial wellhead installed on the well will remain on the well with spools used as needed.
4. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.

- a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig:
 - i. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with a Spudder Rig:
 - i. Notify the BLM when moving in and removing the Spudder Rig.
 - ii. Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - iii. BOP/BOPE test to be conducted per 43 CFR 3172.6 as soon as 2nd Rig is rigged up on well.
5. Floor controls are required for 3M or greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller, and will always be operational during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table or the area immediately above the substructure on which the draw works are located (this does not include the doghouse or stairway area).
6. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

Pressure Control

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in 43 CFR 3172.6 and API STD 53 Sec. 5.3.
2. 5M or higher systems require an HCR valve, remote kill line, and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
3. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE, and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
 - b. The results of the test shall be reported to the appropriate BLM office.
 - c. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.

- d. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
 - e. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per 43 CFR 3172.6(b)(9).
 - f. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - g. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, no tests shall commence until the cement has had a minimum of 24 hours setup time.
 - h. The tests shall be done by an independent service company utilizing a test plug, not a cup or J-packer and can be initiated immediately with the casing valve open. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to 43 CFR 3172 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
4. If the operator has proposed using a 5,000 (5M) Annular on a 10M BOP:
- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 10,000 (10M) psi.
5. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
- a. Wellhead shall be installed by manufacturer's representatives (submit documentation with subsequent sundry).

- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in 43 CFR 3172 must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed, and another wellhead installed.
6. If a variance is approved for break testing the BOPE, the following requirements apply:
- a. BOPE break testing is only approved for a BOP rated at 5M or less.
 - b. Approval is only for the intermediate hole sections, so long as those sections do not go deeper than the Bone Springs formation.
 - c. The Annular Preventer must be tested to a minimum of 70% of BOPE working pressure and shall be higher than the MASP.
 - d. A full BOP test shall be performed every 21 days (at a minimum).
 - e. A full BOP test is required prior to drilling the first intermediate hole section (if applicable). If any subsequent intermediate hole interval is deeper than the first, a full BOP test shall be required (a maximum 200 foot difference in true vertical depth (TVD) is allowed).
 - f. BOPE break testing is not permitted for drilling the production hole section.
 - g. While in transfer, the BOP shall be secured by the hydraulic carrier or cradle.
 - h. If any repairs or replacements of the BOPE is required, the BOPE shall be tested as required by 43 CFR 3172.
 - i. Pressure tests shall be performed on any BOPE components that have been disconnected. A low pressure (250-300 psi) and a high pressure (BOP max pressure rating) test are required.
 - j. If a testing plug is used, pressure shall be maintained for at least 10 minutes. If there is any bleed off in pressure, the test shall be considered to have failed.
 - k. If no testing plug is used, pressure shall be maintained for at least 30 minutes. If there is a decline in pressure of more than 10 percent, the test shall be considered to have failed.
 - l. The appropriate Bureau of Land Management (BLM) office shall be notified a minimum of 4 hours before testing occurs.
 - m. Any well control event while drilling require notification to the BLM Petroleum Engineer (575-706-2779) prior to the commencement of any BOPE Break Testing operations.
 - n. If break testing is not used, then a full BOPE test shall be conducted.
7. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply:
- a. The flex line must meet the requirements of API 16C.

- b. Check condition of flexible line from BOP to choke manifold (replace if exterior is damaged or if line fails test).
- c. Line is to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements.
- d. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating.
- e. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, shall be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.

Casing and Cement

1. Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.).
2. On any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. The formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
3. Provide compressive strengths (including hours to reach required 500 pounds compressive strength) prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
4. The surface casing shall be set at a minimum of 25 feet into the Rustler Anhydrite and 80 feet above the salt and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of 8 hours (or 24 hours in the Potash Area) or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

5. Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.
6. Intermediate casing must be cemented to surface. For medium/high cave/karst, potash, and Capitan Reef, wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
7. The production cement should tie-back at least 200 feet (500 feet in Secretary Potash, surface in R-111-P potash) into previous casing string. Operator shall provide method of verification.
8. Production liner cement should tie-back at least 100 feet into previous casing string. Operator shall provide verification of cement top.
9. In WIPP Areas, cement must come to surface on the first three casing strings.
10. If cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
11. No pea gravel permitted for remedial cement or fall back remedial cement without prior authorization from a BLM petroleum engineer.
12. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
13. DV tools:
 - a. First stage to DV tool (The DV tool may be cancelled if cement circulates to surface on the first stage):
 - i. Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
 - b. Second stage above DV tool:
 - i. For intermediate casing, cement to surface.
 - ii. For production casing, cement should tie-back at least 200 feet (500 feet in Secretary Potash, surface in R-111-P potash) into previous casing string. Operator shall provide method of verification.
 - iii. If cement does not circulate, contact the appropriate BLM office.

14. Potash Areas:

- a. Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
- b. After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met:
 - i. Cement reaches a minimum compressive strength of 500 psi for all cement blends
 - ii. Until cement has been in place at least 24 hours.
- c. WOC time will be recorded in the driller's log.
- d. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.
- e. In R111 Potash Areas, if cement does not circulate to surface on the first two salt protection casing strings, the cement on the 3rd casing salt string must come to surface.
- f. In Secretary Potash Areas, if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.

15. Wait on cement (WOC) for Water Basin:

- a. After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met:
 - i. Cement reaches a minimum compressive strength of 500 psi at the shoe
 - ii. Until cement has been in place at least 8 hours.
- b. WOC time will be recorded in the driller's log.

16. Medium/High/Critical Cave/Karst Areas:

- a. Wait on cement (WOC) time for a primary cement job is to include the lead cement slurry.
- b. In Critical Cave/Karst Areas cement must come to surface on the first three casing strings.
- c. In Medium and High Cave/Karst Areas, if cement does not circulate to surface on the first two casing strings, the cement on the 3rd casing string must come to surface.
- d. In Critical Cave/Karst Areas, if cement does not circulate to surface on the first three casing strings, the cement on the 4th casing string must come to surface.

Drilling Mud

1. Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation and shall be used until production casing is run and cemented.

Waste Material and Fluids

1. All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and

disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

2. Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

Special Requirements

1. Communitization Agreement

- a. The operator will submit a Communitization Agreement to the Santa Fe Office (301 Dinosaur Trail, Santa Fe, NM 87508), at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division.
- b. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
 - i. The operator will submit an as-drilled survey well plat of the well completion, but are not limited to, those specified in 43 CFR 3171 and 3172.
 - ii. If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- c. In addition, the well sign shall include the surface and bottom hole lease numbers.
 - i. When the Communitization Agreement number is known, it shall also be on the sign.

2. Unit Wells

- a. The well sign for a unit well shall include the unit number in addition to the surface and bottom hole lease numbers. This also applies to participating area numbers.
 - i. If a participating area has not been established, the operator can use the general unit designation, but will replace the unit number with the participating area number when the sign is replaced.
- b. Commercial Well Determination
 - i. A commercial well determination shall be submitted after production has been established for at least six months (this is not necessary for secondary recovery unit wells).

3. Hydrogen Sulfide (H₂S)

- a. If H₂S is encountered, provide measured values and formations to the BLM.
- b. An H₂S area must meet 43 CFR 3176 requirements, which includes equipment and personnel/public protection items.

- c. An H2S Drilling Plan shall be activated 500 feet prior to drilling into any formation designated as having H2S.
 - d. Hydrogen Sulfide monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet 43 CFR 3176 requirements, which includes equipment and personnel/public protection items.
- 4. Capitan Reef
 - a. If lost circulation (50% or greater) occurs below the Base of the Salt, the operator shall do the following (Use this for 3 string wells in the Capitan Reef, if it is a 4 string well ensure fresh water based mud is used across the Capitan interval):
 - i. Switch to fresh water mud to protect the Capitan Reef and use fresh water mud until setting the intermediate casing. The appropriate BLM office is to be notified for a PET to witness the switch to fresh water.
 - ii. Daily drilling reports from the Base of the Salt to the setting of the intermediate casing are to be submitted to the BLM CFO engineering staff via e-mail by 0800 hours each morning. Any lost circulation encountered is to be recorded on these drilling reports.
 - iii. The daily drilling report should show mud volume per shift/tour.
 - iv. Failure to submit these reports will result in an Incidence of Non-Compliance being issued for failure to comply with the Conditions of Approval.
 - v. If not already planned, the operator shall run a caliper survey for the intermediate well bore and submit to the appropriate BLM office.
- 5. Salt Water Disposal Wells
 - a. The operator shall supply the BLM with a copy of a mudlog over the permitted disposal interval and estimated in situ water salinity based on open-hole logs.
 - b. If hydrocarbons are encountered while drilling, the operator shall notify the BLM.
 - c. The operator shall provide to the BLM a summary of formation depth picks based on mudlog and geophysical logs along with a copy of the mudlog and open-hole logs from total depth to top of Devonian.
 - d. An NOI sundry with the completion procedure for this well shall be submitted and approved prior to commencing completion work. The procedure will be reviewed to verify that the completion proposal will allow the operator to:
 - i. Properly evaluate the injection zone utilizing open-hole logs, swab testing and/or any other method to confirm that hydrocarbons cannot be produced in paying quantities. This evaluation shall be reviewed by the BLM prior to injection commencing.
 - ii. Restrict the injection fluid to the approved formation.
 - iii. If a step rate test will be run, an NOI sundry shall be submitted to the BLM for approval.

- e. If off-lease water will be disposed in this well, the operator shall provide proof of right-of-way approval.

6. WIPP Requirements

- a. If the proposed surface well or bottom hole is located within 330 feet of the WIPP Land Withdrawal Area boundary:
 - i. Daily drilling reports, logs, and deviation survey information are required to be submitted to the Bureau of Land Management Engineering Department and the U.S. Department of Energy (per requirements of the Joint Powers Agreement) until a total vertical depth of 7,000 feet is reached. These reports will have at a minimum the rate of penetration and a clearly marked section showing the deviation for each 500-foot interval. Operator may be required to do more frequent deviation surveys based on the daily information submitted and may be required to take other corrective measures.
 - ii. Information will also be provided to the New Mexico Oil Conservation Division after drilling activities have been completed.
 - iii. Upon completion of the well, the operator shall submit a complete directional survey.
 - iv. Any future entry into the well for purposes of completing additional drilling will require supplemental information.
- b. Required information shall be emailed to OilGasReports@wipp.ws.
 - i. Attached files must not be greater than 20 MB.
 - ii. Call WIPP Tech Support at 575-234-7422, during the hours of 7:00am to 4:30pm, if there are any issues sending to this address.




Permian Drilling Hydrogen Sulfide Drilling Operations Plan Fresian 3 Federal Com Development

Open drill site. No homes or buildings are near the proposed location.

1. Escape


Personnel shall escape upwind of wellbore in the event of an emergency gas release. Escape can take place through the lease road on the Southeast side of the location. Personnel need to move to a safe distance and block the entrance to location. If the primary route is not an option due to the wind direction, then a secondary egress route should be taken.

Secondary Briefing Area

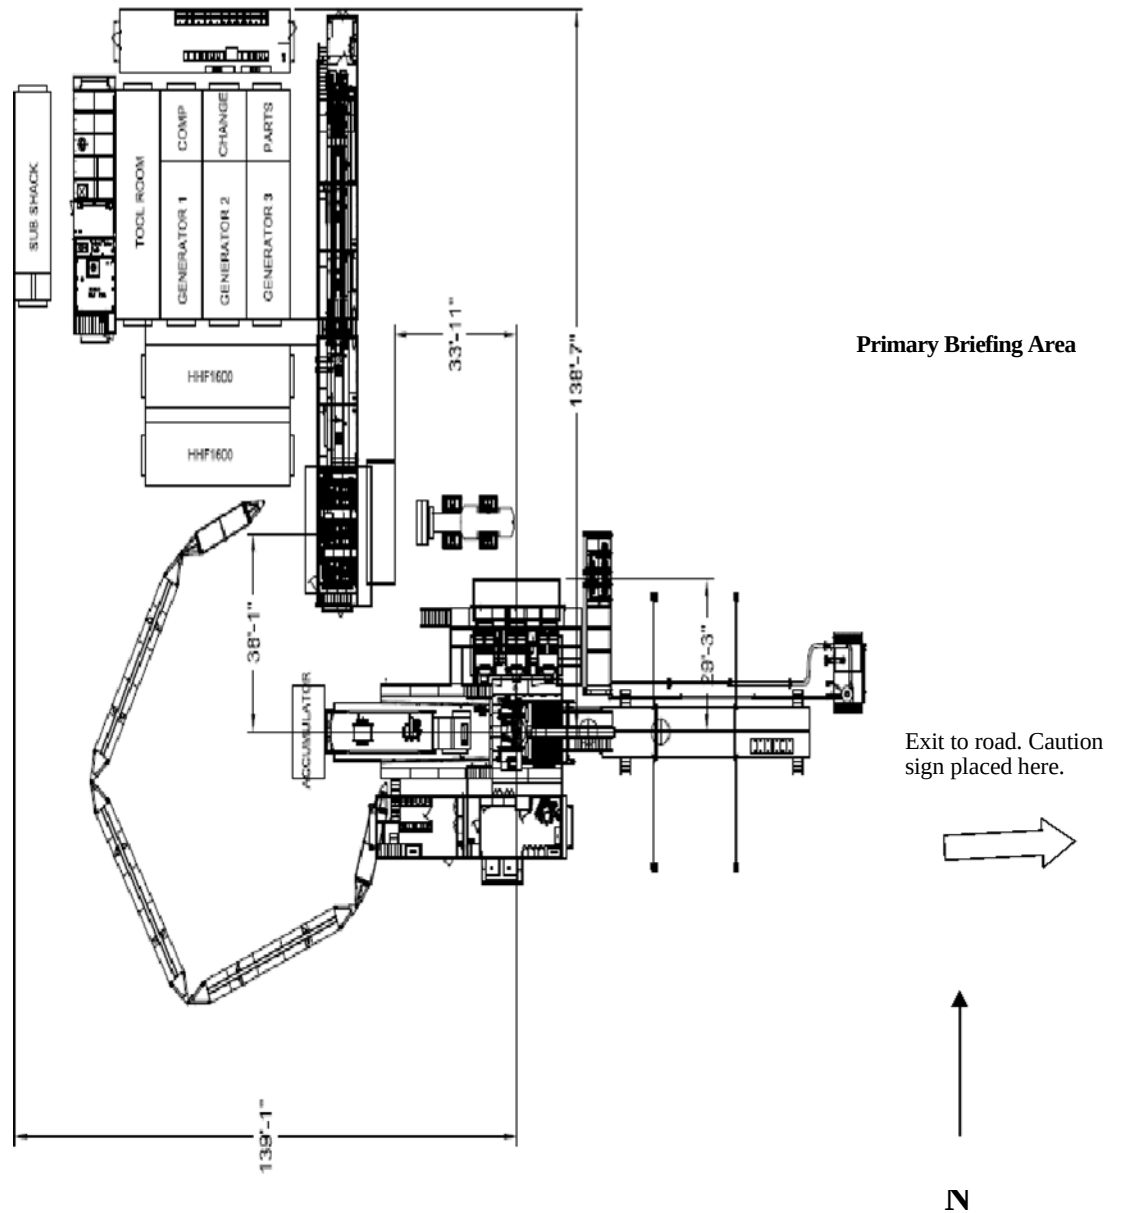

WIND: Prevailing winds are from the Southwest

Secondary Egress

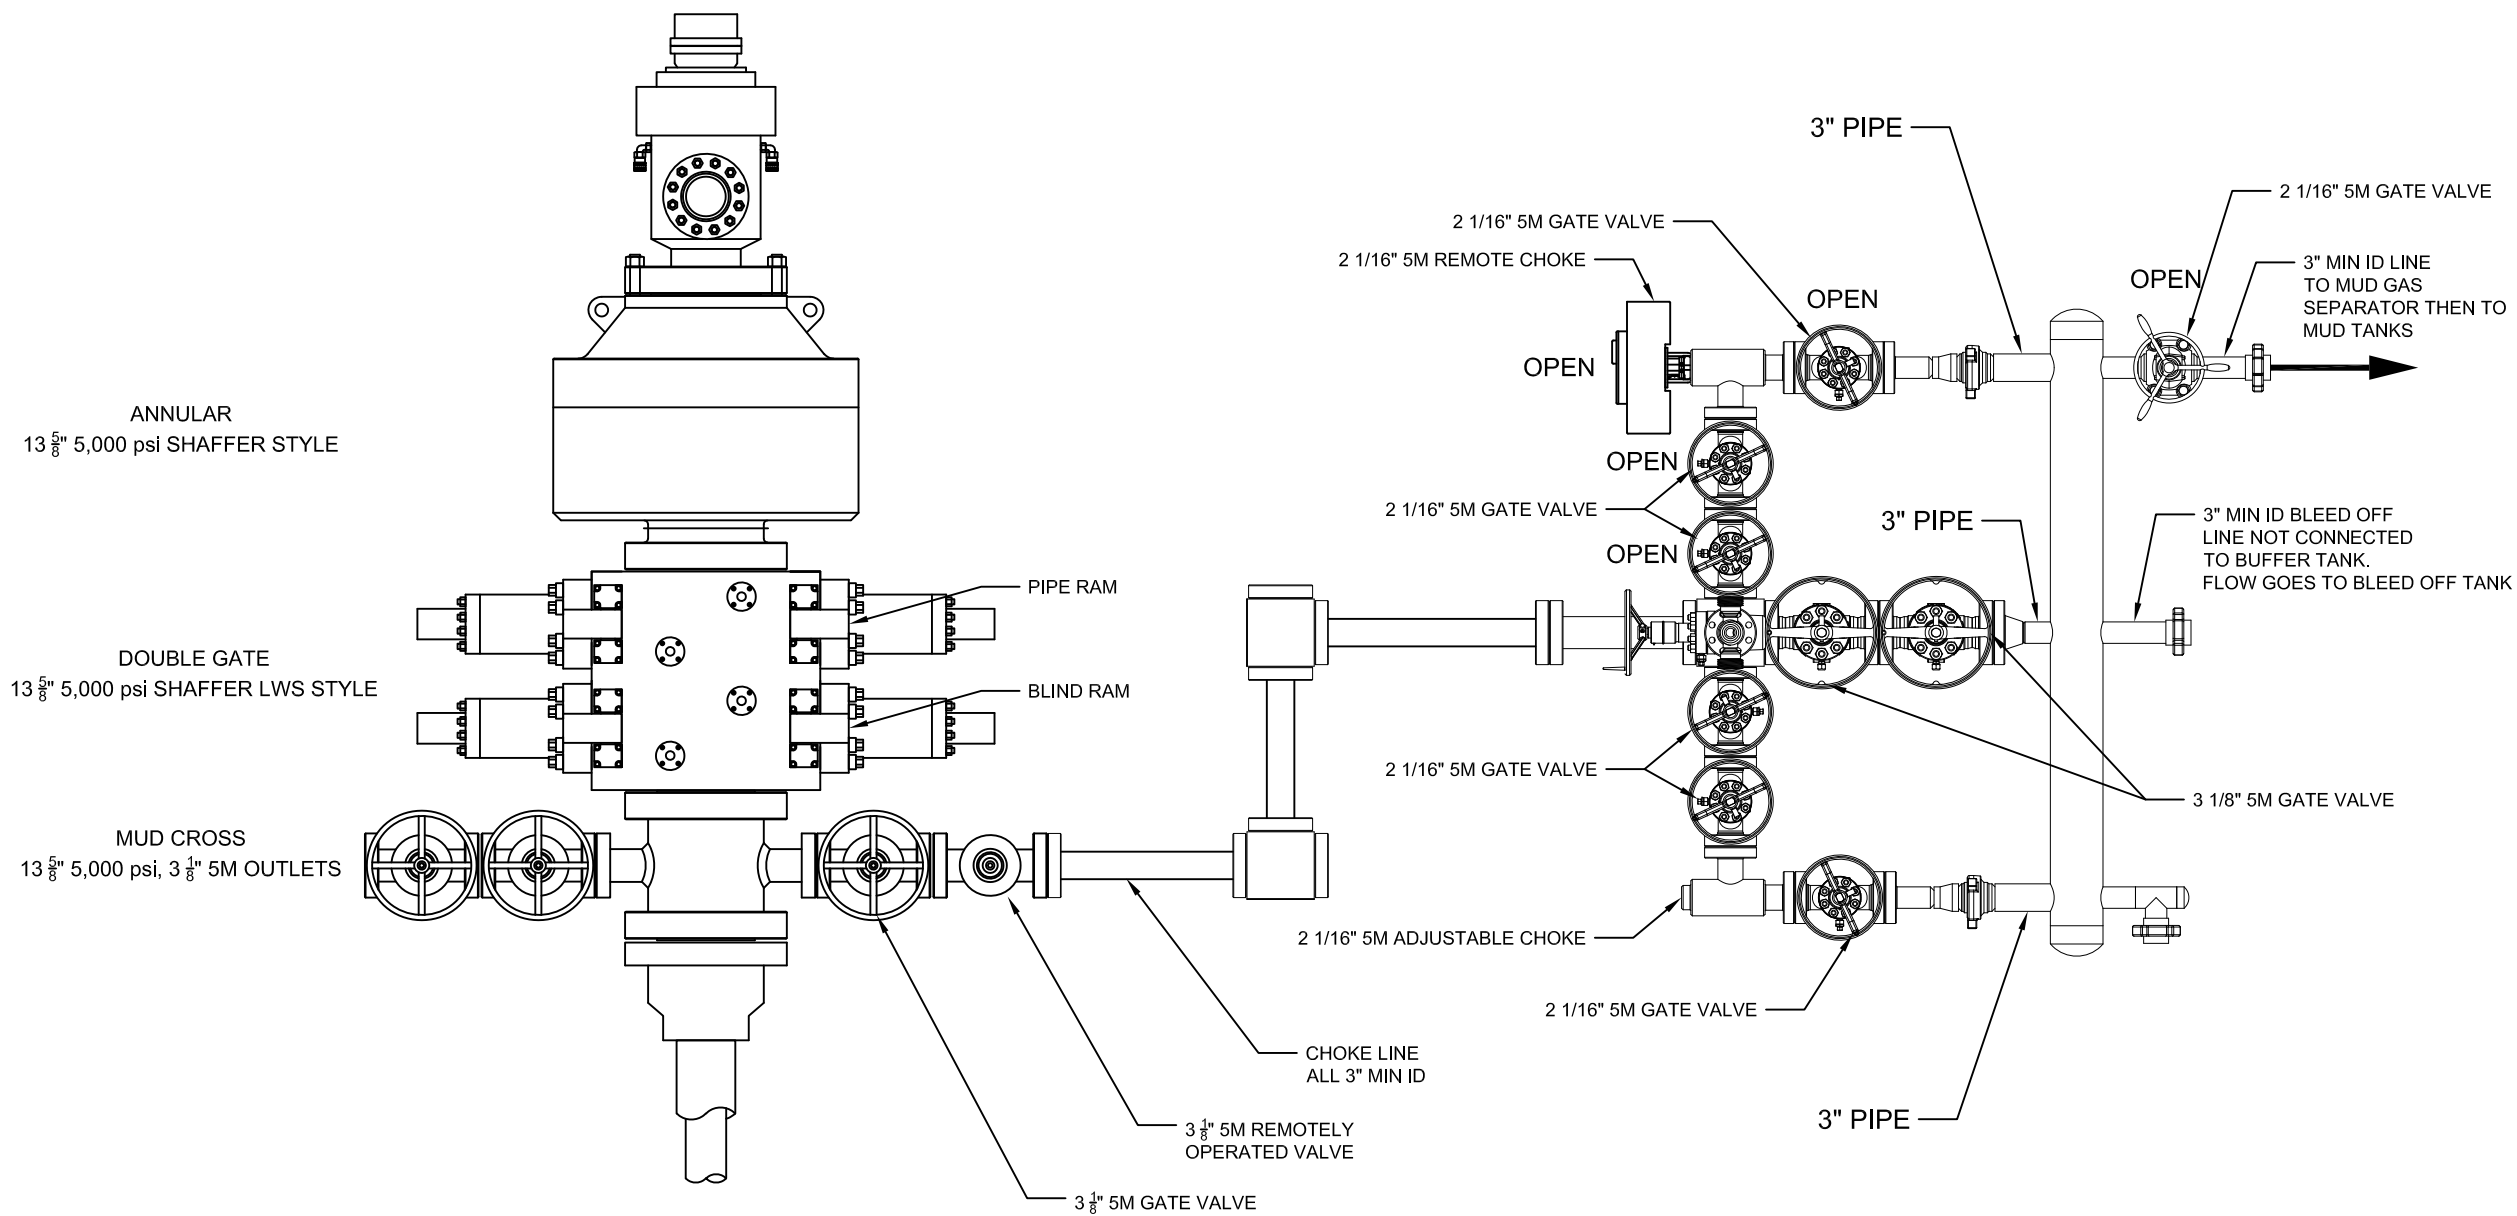

Notes
-
-
-

No.	Revision	Date
-----	----------	------



AKITA
DRILLING LTD.
2302 8th Street, Nisku Alberta
T9E 7Z2 Tel: (780) 955-6700

The information contained in this drawing is the sole property of AKITA Drilling Ltd. Any reproduction in whole or part without the express written consent of AKITA Drilling Ltd. is prohibited.

Date	5-6-2021	Scale	NTS
Des / Chk'd By	BG	File Name	R57 13 5M dou..
Project	R57		

RIG 57 BOP SCHEMATIC



POWERING PROGRESS™

MTR DATA BOOK

CL2013

CUSTOMER: GATES CANADA INC**DATE:** 12/19/2017**Purchase Order:** D235455 (PO 45750)**Sales Order #:** 509128**Product Description:** 5K 3 1/2 in. 17 FT. Fire Rated Choke & Kill Gates Hose Assembly c/w 3 1/8
5K Flange with Safety Clamps & Slings Attached**Hose S/N:** H-121917-14**PART NUMBER:** FR5K3.517.0CK31/85KFLG S/C**CONTENTS INCLUDED****GMCO FITTINGS**

17-309-1

INSERT STEM

15-095-1A

FERRULE

3 1/8 in. 5K FIXED FLANGE X 3 1/8 in. 5K FLOAT FLANGE

V4131

FIXED FLANGE

V5054

FLOAT FLANGE

WELDING SPECIFICATIONS

Certification and Procedure for welding

NDE RESULTS

1622371-03/1622371-01 Ultrasonic Test Results and Imaging

Safety Clamps

34145/34144

TEST CHART

Chart Recording of Hydrostatic Test

TEST CERTIFICATE

Document Product Details & Positive Results of Hydrostatic Testing

CERTIFICATE OF CONFORMANCE

A Declaration of the conformity with the type approval

IMAGES

Images of the product prior to shipping.

PACKING LIST

Details of Shipping Contents, Dimensions and Weights



GATES ENGINEERING & SERVICES NORTH AMERICA
7603 Prairie Oak Dr. Suite 190
Houston, TX. 77086

PHONE: +1 (281) 602-4100
FAX: +1 (281) 602-4147
EMAIL: gesna.quality@gates.com
WEB: www.gates.com/ollandgas

PRESSURE TEST CERTIFICATE

Customer:	GATES CANADA INC	Test Date:	12/19/2017
Customer Ref.:	D235455 (PO 45750)	Hose Serial No.:	H-121917-14
Invoice No.:	509128	Created By:	Cristian Rivera

Product Description: 5K 3 1/2 in. 17 FT. Fire Rated Choke & Kill c/w 3 1/8 5K Flange with Safety Clamps & Slings Attached

End Fitting 1:	3 1/8 in. 5K FIXED FLG	End Fitting 2:	3 1/8 in. 5K FLOAT FLG
Oracle Star No.:	68903550-9725917	Assembly Code:	15M5019042016H-121917-14
CUSTOMER P/N:	FR5K3.517.0CK31/85KFLG S/C	Test Pressure:	7,500 psi.
		Working Pressure:	5,000 psi.

Gates Engineering & Services North America certifies that:

The following hose assembly has successfully passed all pressure testing requirements set forth in Gates specifications: GTS-04-052 (for 5K assemblies) or GTS-04-053 (10K assemblies) or GTS-04-048 (15K assemblies), which include reference to Specification API 16C (2nd Edition); sections 7.5.4, 7.5.9, and 10.8.7. A test graph will accompany this test certificate to illustrate conformity to test requirements. This hose assembly was pressure tested using equipment and instrumentation that has been calibrated in accordance with the requirements set-forth in the GESNA management system.

Quality: QUALITY
 Date : 8/5/2021
 Signature :

Production: PRODUCTION
 Date : 8/5/2021
 Signature :

F-PRD-005B

Revision 6_05032021

**BLACK GOLD®**

GATES ENGINEERING & SERVICES NORTH AMERICA
7603 Prairie Oak Dr.
Houston, TX. 77086

PHONE: +1 (281) 602-4100
FAX: +1 (281) 602-4147
EMAIL: gesna.quality@gates.com
WEB: www.gates.com/ollandgas

CERTIFICATE OF CONFORMANCE

This is to certify that all parts and materials included in this shipment have manufactured and/or processed in accordance with various Gates and API assembly and test specifications. Records of required tests are on-file and subject to examination. Test reports and subsequent test graphs have been made available with this shipment. Additional supporting documentation related to materials, welding, weld inspections, and heat-treatment activities are available upon request.

CUSTOMER: GATES CANADA INC
CUSTOMER P.O.#: D235455 (PO 45750)
PART DESCRIPTION: FR5K3.517.0CK31/85KFLG S/C

PART DESCRIPTION: 5K 3 1/2 in. 17 FT. Fire Rated Choke & Kill c/w 3 1/8 5K Flange with Safety Clamps & Slings Attached

SALES ORDER #: 509128
QUANTITY: 1
SERIAL #: H-121917-14

SIGNATURE: _____

A handwritten signature in black ink, appearing to read "O. Rivera", written over a horizontal line.

TITLE: _____

QUALITY ASSURANCE

DATE: _____

8/5/2021

Hydrostatic Test

Technician= CHRIS OLIVO

17:55:52





1385 Hwy. 35 Bypass S. O: (361) 790-7910
 P.O. Box 2350 F: (361) 790-7927
 Rockport, TX 78381

tedwards@edwardsfabrication.com
 www.edwardsfabrication.com

CERTIFICATE OF TEST

Client:
 Gates E & S North America
 134 44th Street
 Corpus Christi, TX 78405

Purchase Order: 1592198/0

Certificate Number			Date of Examination	
34145			04/27/17	
ID#	Part Number	Description	SWL*	Proofload
34145	E3.5S	3.5" E Safety Clamp	6016 lbs.	12031 lbs.


The Safety Clamp unit identified on this certificate has been load tested completely assembled; including the clamp body, (2) 3/4" shackles, 5/8" x 48" wire rope sling and anchor tab. Thus, all components are tested at the "Proof" load. Do not disassemble. Do not interchange any part or parts of this tested unit with parts of other Safety Clamp units. DO NOT WELD, CUT, ADD-TO, TAKE AWAY ANY COMPONENTS OR MAKE ANY MODIFICATION TO THIS CLAMP UNIT. Doing so voids this test certificate.

Cutting/Removing either one or both stainless steel Tamper-proof hardware cables renders this Test Certificate VOID.

* Safe Work Load

THIS PRODUCT IS MANUFACTURED IN THE U.S.A.

We hereby verify that the above information is correct
 as contained in the records of Edwards Fabrication L.L.C.



Edwards Fabrication L.L.C. is certified as
 having a Quality Management System.

Thomas F. Edwards
 President
 Edwards Fabrication L.L.C.



1385 Hwy. 35 Bypass S. O: (361) 790-7910
 P.O. Box 2350 F: (361) 790-7927
 Rockport, TX 78381

tedwards@edwardsfabrication.com
 www.edwardsfabrication.com

CERTIFICATE OF TEST

Client:
 Gates E & S North America
 134 44th Street
 Corpus Christi, TX 78405

Purchase Order: 1592198/0

Certificate Number				Date of Examination	
34144				04/27/17	
ID#	Part Number	Description	SWL*	Proofload	
34144	E3.5S	3.5" E Safety Clamp	6014 lbs.	12027 lbs.	

The Safety Clamp unit identified on this certificate has been load tested completely assembled; including the clamp body, (2) 3/4" shackles, 5/8" x 48" wire rope sling and anchor tab. Thus, all components are tested at the "Proof" load. Do not disassemble. Do not interchange any part or parts of this tested unit with parts of other Safety Clamp units. DO NOT WELD, CUT, ADD-TO, TAKE AWAY ANY COMPONENTS OR MAKE ANY MODIFICATION TO THIS CLAMP UNIT. Doing so voids this test certificate.

Cutting/Removing either one or both stainless steel Tamper-proof hardware cables renders this Test Certificate VOID.

* Safe Work Load

THIS PRODUCT IS MANUFACTURED IN THE U.S.A.

We hereby verify that the above information is correct
 as contained in the records of Edwards Fabrication L.L.C.



Edwards Fabrication L.L.C. is certified as
 having a Quality Management System.

Thomas F. Edwards
 President
 Edwards Fabrication L.L.C.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 494189

ACKNOWLEDGMENTS

Operator: Spur Energy Partners LLC 9655 Katy Freeway Houston, TX 77024	OGRID: 328947
	Action Number: 494189
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

ACKNOWLEDGMENTS

☐	I hereby certify that no additives containing PFAS chemicals will be added to the completion or recompletion of this well.
--------------------------	--

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oecd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 494189

CONDITIONS

Operator: Spur Energy Partners LLC 9655 Katy Freeway Houston, TX 77024	OGRID: 328947
	Action Number: 494189
	Action Type: [C-101] BLM - Federal/Indian Land Lease (Form 3160-3)

CONDITIONS

Created By	Condition	Condition Date
schapman01	Cement is required to circulate on both surface and intermediate1 strings of casing.	8/11/2025
schapman01	If cement does not circulate on any string, a Cement Bond Log (CBL) is required for that string of casing.	8/11/2025
ward.rikala	Notify the OCD 24 hours prior to casing & cement.	9/4/2025
ward.rikala	File As Drilled C-102 and a directional Survey with C-104 completion packet.	9/4/2025
ward.rikala	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string.	9/4/2025
ward.rikala	Oil base muds are not to be used until fresh water zones are cased and cemented providing isolation from the oil or diesel. This includes synthetic oils. Oil based mud, drilling fluids and solids must be contained in a steel closed loop system.	9/4/2025
ward.rikala	No additives containing PFAS chemicals will be added to the drilling fluids or completion fluids used during drilling, completions, or recompletions operations.	9/4/2025
