

I. REQUEST FOR ALLOWABLE MINERAL AUTHORIZATION TO TRANSPORT

¹ Operator name and Address EOG RESOURCES INC PO BOX 2267 MIDLAND, TEXAS 79702		² OGRID Number 7377
		³ Reason for Filing Code/ Effective Date NW 05/12/2023
⁴ API Number 30 - 025-50931	⁵ Pool Name WC025 G08 S253235G; LOWER BONE SPRING	⁶ Pool Code 97903
⁷ Property Code 328894	⁸ Property Name MERCILESS 13 FEDERAL COM	⁹ Well Number 511H

II. ¹⁰ Surface Location

UI or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South Line	Feet from the	East/West line	County
A	13	25S	32E		310'	NORTH	563'	EAST	LEA

¹¹ Bottom Hole Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
H	24	25S	32E		2531'	NORTH	489'	EAST	LEA
¹² Lse Code	¹³ Producing Method Code FLOWING	¹⁴ Gas Connection Date	¹⁵ C-129 Permit Number		¹⁶ C-129 Effective Date		¹⁷ C-129 Expiration Date		

III. Oil and Gas Transporters

¹⁸ Transporter OGRID	¹⁹ Transporter Name and Address	²⁰ O/G/W
372812	EOGRM	OIL
151618	ENTERPRISE FIELD SERVICES	GAS
298751	REGENCY FIELD SERVICES	GAS
36785	DCP MIDSTREAM	GAS


IV. Well Completion Data

²¹ Spud Date 01/20/2023	²² Ready Date 05/12/2023	²³ TD 18,139'	²⁴ PBTD 18,108'	²⁵ Perforations 10,788 - 18,108'	²⁶ DHC, MC
²⁷ Hole Size		²⁸ Casing & Tubing Size		²⁹ Depth Set	
16"		13 3/8"		1128'	
11"		9 5/8"		4848'	
7 7/8"		5 1/2"		18,116'	
				1745 SXS CL C&H TOC 1608' CBL	

V. Well Test Data

³¹ Date New Oil 05/12/2023	³² Gas Delivery Date 05/12/2023	³³ Test Date 05/18/2023	³⁴ Test Length 24 HRS	³⁵ Tbg. Pressure	³⁶ Csg. Pressure 791
³⁷ Choke Size	³⁸ Oil 2324	³⁹ Water 10,315	⁴⁰ Gas 3497		⁴¹ Test Method
⁴² I hereby certify that the rules of the Oil Conservation Division have been complied with and that the information given above is true and complete to the best of my knowledge and belief. Signature: Kay Maddox			OIL CONSERVATION DIVISION Approved by: Title: Approval Date: 		
Printed name: Kay Maddox					
Title: SENIOR REGULATORY SPECIALIST					
E-mail Address: kay_maddox@eogresources.com					
Date: 06/05/2023		Phone: 432-638-8475			

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office
☐ AMENDED REPORT
AS-COMPLETED

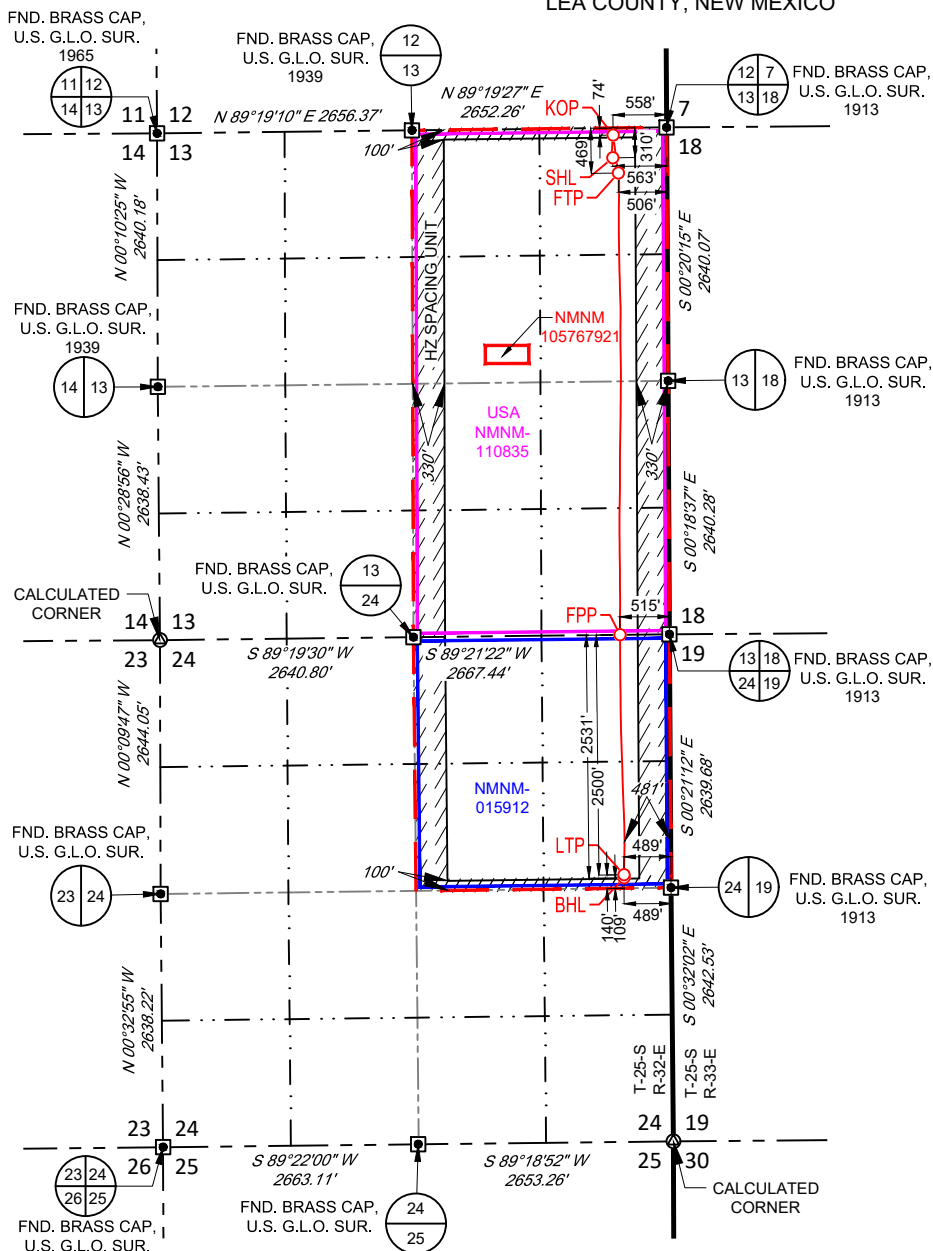SECTION 13, TOWNSHIP 25-S, RANGE 32-E, N.M.P.M.
LEA COUNTY, NEW MEXICO**SURFACE LOCATION (SHL)**NEW MEXICO EAST
NAD 1983X=761606 Y=414303
LAT.: N 32.1369972
LONG.: W 103.6217094**KICK OFF POINT (KOP)**NEW MEXICO EAST
NAD 1983X=761610 Y=414539
LAT.: N 32.1376464
LONG.: W 103.6216932
74' FNL 558' FEL
MD=10086' TVD=10075'**FIRST TAKE POINT (FTP)**NEW MEXICO EAST
NAD 1983X=761665 Y=414145
LAT.: N 32.1365614
LONG.: W 103.6215241
469' FNL 506' FEL
MD=10788' TVD=10606'**FED PERF. POINT (FPP)**NEW MEXICO EAST
NAD 1983X=761682 Y=409334
LAT.: N 32.1233375
LONG.: W 103.6215710
0' FNL 515' FEL
MD=15607' TVD=10677'**LAST TAKE POINT (LTP)**NEW MEXICO EAST
NAD 1983X=761724 Y=406834
LAT.: N 32.1164652
LONG.: W 103.6214887
2500' FNL 489' FEL
MD=18108' TVD=10680'**BOTTOM HOLE LOCATION (BHL)**NEW MEXICO EAST
NAD 1983X=761724 Y=406803
LAT.: N 32.1163800
LONG.: W 103.6214906
2531' FNL 489' FEL
MD=18139' TVD=10679'

LEASE NAME & WELL NO.: _____ MERCILESS 13 FED COM 511H
 SECTION 13 TWP 25-S RGE 32-E SURVEY N.M.P.M.
 COUNTY LEA STATE NM ELEVATION 3493'
 DESCRIPTION 310' FNL & 563' FEL

SCALE: 1" = 2000'
 0' 1000' 2000'



481 WINSOTT ROAD, Ste. 200 • BENBROOK, TEXAS 76126
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705
 TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743
 WWW.TOPOGRAPHIC.COM

5/17/2023 4:57:24 PM

Ramon A. Dominguez, P.S. No. 24508

eog resources, inc.

MERCILESS 13 FED COM
511H
AS-DRILLED

DATE: 05/12/2023

FILE:AD_MERCILESS_13_FED_COM_511H

DRAWN BY: IMU

SHEET: 2 OF 2

REVISION:

NOTES:

1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
3. THIS WELL LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY EOG RESOURCES, INC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.





Midland

Lea County, NM (NAD 83 NME)

Merciless 13 Fed Com

#511H

OH

Survey: Taktikal MWD

Final PVA

09 March, 2023





Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Project	Lea County, NM (NAD 83 NME)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Merciless 13 Fed Com		
Site Position:		Northing:	414,304.00 usft
From:	Map	Easting:	757,406.00 usft
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "
		Latitude:	32° 8' 13.472 N
		Longitude:	103° 38' 7.002 W
		Grid Convergence:	0.37 °

Well		#511H				
Well Position	+N/-S	0.0 usft	Northing:	414,303.00 usft	Latitude:	32° 8' 13.191 N
	+E/-W	0.0 usft	Easting:	761,606.00 usft	Longitude:	103° 37' 18.157 W
Position Uncertainty		0.0 usft	Wellhead Elevation:	usft	Ground Level:	3,494.0 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	3/4/2023	6.36	59.76	47,257.87948279

Design	OH				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)	
	0.0	0.0	0.0	179.22	

Survey Program	Date	3/9/2023			
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
188.0	18,139.0	Taktikal MWD (OH)	EOG MWD+IFR1	MWD + IFR1	



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.0	0.0	
188.0	1.14	336.21	188.0	1.7	-0.8	0.61	0.61	0.00	-1.9	0.0	
217.0	0.92	340.60	217.0	2.2	-0.9	0.81	-0.76	15.14	-2.4	0.2	
391.0	1.05	318.63	391.0	4.7	-2.5	0.23	0.07	-12.63	-5.2	-1.3	
476.0	0.84	314.41	475.9	5.7	-3.4	0.26	-0.25	-4.96	-6.5	-1.7	
561.0	0.53	342.27	560.9	6.5	-4.0	0.53	-0.36	32.78	-7.4	1.8	
746.0	1.01	280.57	745.9	7.7	-5.9	0.48	0.26	-33.35	-7.2	-6.5	
841.0	1.05	278.46	840.9	7.9	-7.5	0.06	0.04	-2.22	-8.6	-6.7	
935.0	1.27	294.20	934.9	8.5	-9.3	0.41	0.23	16.74	-12.0	-3.9	
1,030.0	1.67	353.43	1,029.9	10.3	-10.5	1.57	0.42	62.35	-11.4	9.2	
1,080.0	2.07	358.09	1,079.8	11.9	-10.6	0.86	0.80	9.32	-12.3	10.2	
1,208.0	1.85	351.59	1,207.8	16.3	-11.0	0.24	-0.17	-5.08	-17.7	8.5	
1,302.0	1.80	347.55	1,301.7	19.2	-11.5	0.15	-0.05	-4.30	-21.2	7.1	
1,396.0	1.54	341.31	1,395.7	21.9	-12.2	0.34	-0.28	-6.64	-23.1	5.0	
1,491.0	1.49	337.44	1,490.6	24.2	-13.1	0.12	-0.05	-4.07	-21.3	4.9	
1,585.0	1.27	340.43	1,584.6	26.3	-13.9	0.25	-0.23	3.18	-16.8	7.9	
1,678.0	2.55	1.08	1,677.6	29.4	-14.2	1.54	1.38	22.20	-9.2	13.0	
1,773.0	4.04	7.23	1,772.4	34.8	-13.8	1.61	1.57	6.47	-6.5	12.8	
1,867.0	4.00	9.34	1,866.2	41.3	-12.8	0.16	-0.04	2.24	-5.9	11.6	
2,055.0	3.12	4.77	2,053.8	52.9	-11.3	0.49	-0.47	-2.43	-5.0	8.5	
2,149.0	4.04	3.98	2,147.6	58.7	-10.9	0.98	0.98	-0.84	-4.2	7.5	
2,243.0	4.97	7.41	2,241.3	66.1	-10.1	1.03	0.99	3.65	-4.4	6.5	
2,337.0	5.01	8.11	2,335.0	74.2	-9.0	0.08	0.04	0.74	-5.8	5.2	
2,431.0	4.88	8.11	2,428.6	82.2	-7.9	0.14	-0.14	0.00	-7.3	3.8	
2,525.0	4.75	3.89	2,522.3	90.0	-7.0	0.40	-0.14	-4.49	-8.6	2.0	
2,619.0	4.44	2.40	2,616.0	97.6	-6.6	0.35	-0.33	-1.59	-9.4	1.0	
2,713.0	4.40	0.82	2,709.7	104.8	-6.4	0.14	-0.04	-1.68	-9.9	0.0	



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
2,808.0	4.18	4.07	2,804.4	111.9	-6.1	0.35	-0.23	3.42	-10.1	-0.2	
2,902.0	4.18	1.17	2,898.2	118.7	-5.8	0.22	0.00	-3.09	-10.2	-1.5	
2,996.0	4.04	2.05	2,992.0	125.5	-5.6	0.16	-0.15	0.94	-10.1	-2.0	
3,090.0	3.91	2.57	3,085.7	132.0	-5.4	0.14	-0.14	0.55	-9.9	-2.6	
3,185.0	3.96	0.64	3,180.5	138.5	-5.2	0.15	0.05	-2.03	-9.4	-3.6	
3,279.0	3.56	0.20	3,274.3	144.7	-5.1	0.43	-0.43	-0.47	-8.8	-4.2	
3,373.0	3.96	2.57	3,368.1	150.8	-5.0	0.46	0.43	2.52	-8.3	-4.5	
3,467.0	5.63	359.41	3,461.8	158.7	-4.9	1.80	1.78	-3.36	-9.1	-5.5	
3,562.0	5.10	0.38	3,556.4	167.6	-4.9	0.57	-0.56	1.02	-11.2	-5.8	
3,656.0	4.53	358.88	3,650.0	175.4	-4.9	0.62	-0.61	-1.60	-12.1	-6.5	
3,751.0	4.00	0.64	3,744.8	182.5	-5.0	0.57	-0.56	1.85	-12.5	-6.6	
3,845.0	3.91	7.58	3,838.5	189.0	-4.5	0.52	-0.10	7.38	-12.9	-6.0	
3,940.0	5.36	0.11	3,933.2	196.6	-4.1	1.65	1.53	-7.86	-12.8	-8.6	
4,034.0	4.66	356.16	4,026.9	204.8	-4.3	0.83	-0.74	-4.20	-13.6	-9.7	
4,128.0	3.69	354.75	4,120.6	211.6	-4.9	1.04	-1.03	-1.50	-13.3	-10.0	
4,222.0	2.95	358.18	4,214.5	217.1	-5.2	0.81	-0.79	3.65	-12.5	-9.3	
4,317.0	1.89	19.89	4,309.4	221.0	-4.8	1.46	-1.12	22.85	-12.6	-5.9	
4,411.0	2.59	10.13	4,403.3	224.5	-3.9	0.85	0.74	-10.38	-8.4	-9.8	
4,505.0	2.73	11.10	4,497.2	228.8	-3.1	0.16	0.15	1.03	-6.4	-11.4	
4,599.0	1.63	40.54	4,591.1	232.0	-1.8	1.63	-1.17	31.32	-9.6	-10.5	
4,694.0	1.80	51.53	4,686.1	234.0	0.3	0.39	0.18	11.57	-10.3	-13.9	
4,788.0	2.86	7.14	4,780.0	237.2	1.7	2.14	1.13	-47.22	5.7	-19.5	
4,907.0	2.77	4.51	4,898.9	243.0	2.3	0.13	-0.08	-2.21	9.3	-20.6	
5,001.0	2.42	6.00	4,992.8	247.3	2.7	0.38	-0.37	1.59	9.5	-21.7	
5,095.0	4.53	12.24	5,086.6	252.9	3.7	2.28	2.24	6.64	3.3	-22.9	
5,189.0	4.88	13.21	5,180.3	260.4	5.4	0.38	0.37	1.03	-4.8	-22.9	
5,283.0	4.84	12.77	5,273.9	268.2	7.2	0.06	-0.04	-0.47	-12.5	-23.0	



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
5,377.0	4.66	9.96	5,367.6	275.8	8.7	0.31	-0.19	-2.99	-19.2	-23.8	
5,472.0	4.31	4.60	5,462.3	283.2	9.7	0.57	-0.37	-5.64	-24.3	-25.9	
5,566.0	2.59	3.89	5,556.2	288.8	10.1	1.83	-1.83	-0.76	-29.6	-26.2	
5,660.0	1.41	15.14	5,650.1	292.0	10.6	1.32	-1.26	11.97	-37.4	-19.5	
5,754.0	1.41	8.02	5,744.1	294.3	11.0	0.19	0.00	-7.57	-37.0	-24.1	
5,848.0	1.49	3.45	5,838.0	296.7	11.3	0.15	0.09	-4.86	-37.3	-27.1	
5,943.0	1.36	1.96	5,933.0	299.0	11.4	0.14	-0.14	-1.57	-39.0	-28.1	
6,037.0	0.26	264.40	6,027.0	300.1	11.2	1.51	-1.17	-103.79	32.9	-36.1	
6,131.0	0.40	271.17	6,121.0	300.1	10.7	0.15	0.15	7.20	27.9	-39.7	
6,225.0	0.44	304.04	6,215.0	300.3	10.0	0.26	0.04	34.97	1.2	-48.3	
6,319.0	0.48	306.06	6,309.0	300.7	9.4	0.05	0.04	2.15	-1.2	-48.3	
6,413.0	0.62	330.85	6,403.0	301.4	8.8	0.29	0.15	26.37	-22.2	-43.1	
6,508.0	0.53	343.06	6,498.0	302.3	8.5	0.16	-0.09	12.85	-31.8	-37.3	
6,602.0	0.84	172.47	6,592.0	302.0	8.4	1.45	0.33	-181.48	37.2	31.6	
6,696.0	1.05	165.52	6,686.0	300.5	8.7	0.25	0.22	-7.39	31.6	35.8	
6,790.0	1.19	171.85	6,779.9	298.7	9.1	0.20	0.15	6.73	33.5	32.2	
6,885.0	1.19	172.29	6,874.9	296.7	9.4	0.01	0.00	0.46	31.7	31.9	
6,979.0	1.27	183.37	6,968.9	294.7	9.4	0.27	0.09	11.79	35.3	25.4	
7,073.0	1.32	186.09	7,062.9	292.6	9.3	0.08	0.05	2.89	34.3	23.8	
7,168.0	1.36	191.63	7,157.9	290.4	8.9	0.14	0.04	5.83	34.2	20.4	
7,262.0	1.36	189.06	7,251.8	288.2	8.5	0.06	0.00	-2.73	31.1	21.9	
7,356.0	1.23	194.42	7,345.8	286.2	8.1	0.19	-0.14	5.70	30.9	19.0	
7,450.0	1.23	185.63	7,439.8	284.2	7.7	0.20	0.00	-9.35	25.6	23.3	
7,545.0	1.45	177.37	7,534.8	282.0	7.7	0.31	0.23	-8.69	19.8	26.6	
7,639.0	1.58	188.44	7,628.7	279.5	7.6	0.34	0.14	11.78	22.0	22.6	
7,733.0	1.85	185.37	7,722.7	276.7	7.2	0.30	0.29	-3.27	18.0	23.6	
7,828.0	1.71	181.50	7,817.6	273.8	7.0	0.19	-0.15	-4.07	13.4	24.7	



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
7,923.0	2.07	177.99	7,912.6	270.6	7.1	0.40	0.38	-3.69	8.7	25.4	
8,017.0	2.20	190.11	8,006.5	267.1	6.8	0.50	0.14	12.89	10.4	23.3	
8,111.0	2.15	156.28	8,100.5	263.8	7.2	1.35	-0.05	-35.99	-7.6	24.2	
8,206.0	3.16	140.72	8,195.4	260.1	9.6	1.30	1.06	-16.38	-18.1	20.8	
8,300.0	1.01	99.50	8,289.3	258.0	12.0	2.65	-2.29	-43.85	-30.1	2.0	
8,394.0	0.79	112.95	8,383.3	257.6	13.4	0.32	-0.23	14.31	-30.3	9.1	
8,488.0	0.84	132.72	8,477.3	256.8	14.6	0.30	0.05	21.03	-26.7	19.0	
8,582.0	0.84	155.22	8,571.3	255.8	15.3	0.35	0.00	23.94	-18.7	28.1	
8,676.0	0.57	165.94	8,665.3	254.7	15.7	0.32	-0.29	11.40	-14.3	31.2	
8,770.0	0.66	194.60	8,759.2	253.7	15.7	0.34	0.10	30.49	1.4	34.5	
8,864.0	0.84	212.09	8,853.2	252.6	15.2	0.31	0.19	18.61	10.5	32.6	
8,959.0	0.92	221.31	8,948.2	251.4	14.3	0.17	0.08	9.71	14.2	30.6	
9,053.0	1.10	220.17	9,042.2	250.2	13.3	0.19	0.19	-1.21	11.9	30.9	
9,147.0	1.19	223.60	9,136.2	248.8	12.0	0.12	0.10	3.65	11.8	30.2	
9,241.0	0.84	220.96	9,230.2	247.5	10.9	0.38	-0.37	-2.81	8.8	30.6	
9,336.0	0.48	193.19	9,325.2	246.6	10.3	0.50	-0.38	-29.23	-7.5	30.9	
9,430.0	0.79	214.99	9,419.2	245.7	9.9	0.41	0.33	23.19	3.5	31.6	
9,563.0	1.27	209.10	9,552.1	243.7	8.6	0.37	0.36	-4.43	-2.2	31.7	
9,658.0	1.05	212.17	9,647.1	242.0	7.7	0.24	-0.23	3.23	-2.4	31.8	
9,752.0	0.66	198.64	9,741.1	240.8	7.0	0.46	-0.41	-14.39	-11.2	30.2	
9,846.0	0.48	236.96	9,835.1	240.1	6.5	0.44	-0.19	40.77	9.1	30.9	
9,940.0	1.05	227.99	9,929.1	239.3	5.6	0.62	0.61	-9.54	3.0	31.9	
10,034.0	0.97	223.86	10,023.1	238.1	4.4	0.12	-0.09	-4.39	-1.0	32.0	
10,086.0	3.75	201.20	10,075.0	236.2	3.4	5.53	5.34	-43.59	-15.3	29.0	
KOP (MD=10086.0', TVD=10075.0')											
10,129.0	6.11	198.29	10,117.9	232.7	2.2	5.53	5.50	-6.76	-20.0	27.8	
10,223.0	17.71	173.85	10,209.7	213.7	2.2	13.19	12.34	-26.00	-36.3	14.9	



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
10,233.6	18.77	172.86	10,219.8	210.4	2.6	10.44	10.02	-9.34	-37.5	14.3	
HL Crossing (MD:10233.6', TVD:10219.8', N/S:210.4', E/W:2.6', INC:18.77)											
10,317.0	27.25	167.70	10,296.5	178.4	8.3	10.44	10.16	-6.19	-45.7	12.4	
10,411.0	33.63	168.58	10,377.5	131.8	18.1	6.80	6.79	0.94	-49.9	17.1	
10,505.0	41.67	176.23	10,451.9	75.0	25.3	9.88	8.55	8.14	-47.2	22.7	
10,600.0	53.89	171.39	10,515.7	5.2	33.1	13.40	12.86	-5.09	-47.4	19.4	
10,694.0	61.80	170.69	10,565.6	-73.3	45.5	8.44	8.41	-0.74	-46.3	22.3	
10,788.0	68.26	172.01	10,605.3	-157.5	58.3	6.99	6.87	1.40	-39.7	25.7	
10,882.0	72.88	177.72	10,636.6	-245.8	66.2	7.55	4.91	6.07	-25.6	23.7	
10,976.0	86.51	181.76	10,653.4	-338.0	66.5	15.10	14.50	4.30	-12.4	12.8	
11,070.0	88.22	180.62	10,657.7	-431.9	64.6	2.19	1.82	-1.21	-7.3	4.4	
11,165.0	87.52	180.09	10,661.2	-526.8	64.0	0.92	-0.74	-0.56	-3.1	2.7	
11,259.0	89.98	180.01	10,663.3	-620.8	63.9	2.62	2.62	-0.09	-0.3	2.0	
11,353.0	89.49	180.09	10,663.7	-714.8	63.8	0.53	-0.52	0.09	0.8	1.4	
11,447.0	89.32	179.48	10,664.7	-808.8	64.2	0.67	-0.18	-0.65	2.5	1.2	
11,541.0	88.66	179.21	10,666.3	-902.8	65.3	0.76	-0.70	-0.29	4.9	1.7	
11,636.0	88.13	178.60	10,669.0	-997.7	67.1	0.85	-0.56	-0.64	8.3	3.0	
11,730.0	90.90	179.74	10,669.8	-1,091.7	68.4	3.19	2.95	1.21	9.8	3.8	
11,824.0	89.89	178.25	10,669.2	-1,185.7	70.1	1.91	-1.07	-1.59	9.8	4.9	
11,918.0	89.45	178.16	10,669.7	-1,279.6	73.0	0.48	-0.47	-0.10	11.1	7.3	
12,012.0	89.19	178.34	10,670.8	-1,373.6	75.9	0.34	-0.28	0.19	12.9	9.6	
12,107.0	88.84	178.34	10,672.4	-1,468.5	78.7	0.37	-0.37	0.00	14.9	11.8	
12,201.0	88.53	178.51	10,674.6	-1,562.4	81.2	0.38	-0.33	0.18	17.3	13.9	
12,295.0	92.09	180.80	10,674.1	-1,656.4	81.8	4.50	3.79	2.44	17.2	13.9	
12,389.0	91.34	180.36	10,671.3	-1,750.4	80.9	0.92	-0.80	-0.47	14.7	12.4	
12,483.0	90.99	180.01	10,669.4	-1,844.3	80.6	0.53	-0.37	-0.37	13.1	11.5	
12,577.0	90.20	179.74	10,668.4	-1,938.3	80.8	0.89	-0.84	-0.29	12.5	11.2	



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey											
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)	
12,671.0	89.14	179.21	10,668.9	-2,032.3	81.6	1.26	-1.13	-0.56	13.4	11.5	
12,765.0	89.01	178.78	10,670.4	-2,126.3	83.3	0.48	-0.14	-0.46	15.2	12.6	
12,860.0	88.18	178.69	10,672.8	-2,221.3	85.4	0.88	-0.87	-0.09	17.9	14.1	
12,954.0	90.33	181.06	10,674.0	-2,315.2	85.6	3.40	2.29	2.52	19.4	13.8	
13,048.0	90.29	180.88	10,673.5	-2,409.2	84.0	0.20	-0.04	-0.19	19.3	11.7	
13,142.0	89.85	180.36	10,673.4	-2,503.2	83.0	0.72	-0.47	-0.55	19.5	10.1	
13,237.0	89.32	180.09	10,674.1	-2,598.2	82.6	0.63	-0.56	-0.28	20.5	9.2	
13,331.0	91.08	181.15	10,673.7	-2,692.2	81.6	2.19	1.87	1.13	20.5	7.6	
13,425.0	90.77	181.24	10,672.2	-2,786.2	79.6	0.34	-0.33	0.10	19.2	5.1	
13,519.0	90.77	181.06	10,671.0	-2,880.1	77.7	0.19	0.00	-0.19	18.0	2.7	
13,614.0	90.42	180.97	10,670.0	-2,975.1	76.0	0.38	-0.37	-0.09	17.0	0.4	
13,708.0	89.85	180.01	10,669.7	-3,069.1	75.2	1.19	-0.61	-1.02	16.8	-0.9	
13,802.0	89.85	180.01	10,670.0	-3,163.1	75.2	0.00	0.00	0.00	17.0	-1.5	
13,896.0	89.41	180.09	10,670.6	-3,257.1	75.1	0.48	-0.47	0.09	17.6	-2.1	
13,990.0	89.10	179.92	10,671.8	-3,351.1	75.1	0.38	-0.33	-0.18	18.8	-2.7	
14,084.0	91.34	180.97	10,671.5	-3,445.1	74.4	2.63	2.38	1.12	18.5	-3.9	
14,178.0	90.95	180.71	10,669.6	-3,539.1	73.0	0.50	-0.41	-0.28	16.6	-5.8	
14,272.0	90.73	180.71	10,668.2	-3,633.0	71.9	0.23	-0.23	0.00	15.2	-7.6	
14,366.0	91.12	180.45	10,666.7	-3,727.0	70.9	0.50	0.41	-0.28	13.7	-9.1	
14,461.0	90.73	180.01	10,665.2	-3,822.0	70.5	0.62	-0.41	-0.46	12.2	-10.0	
14,555.0	90.77	179.83	10,663.9	-3,916.0	70.7	0.20	0.04	-0.19	10.9	-10.4	
14,650.0	90.55	179.39	10,662.8	-4,011.0	71.3	0.52	-0.23	-0.46	9.8	-10.3	
14,744.0	90.55	179.21	10,661.9	-4,105.0	72.5	0.19	0.00	-0.19	8.9	-9.7	
14,839.0	87.96	179.39	10,663.2	-4,200.0	73.6	2.73	-2.73	0.19	10.2	-9.1	
14,933.0	88.00	179.65	10,666.5	-4,293.9	74.4	0.28	0.04	0.28	13.5	-8.9	
15,027.0	87.87	179.57	10,669.9	-4,387.8	75.0	0.16	-0.14	-0.09	16.9	-8.8	
15,121.0	87.82	179.65	10,673.4	-4,481.8	75.7	0.10	-0.05	0.09	20.4	-8.7	



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
15,215.0	87.69	179.57	10,677.1	-4,575.7	76.3	0.16	-0.14	-0.09	24.1	-8.6
15,309.0	90.11	180.45	10,678.9	-4,669.7	76.3	2.74	2.57	0.94	25.9	-9.1
15,403.0	90.11	180.27	10,678.7	-4,763.7	75.7	0.19	0.00	-0.19	25.7	-10.3
15,497.0	90.46	180.09	10,678.2	-4,857.7	75.4	0.42	0.37	-0.19	25.2	-11.1
15,592.0	90.77	179.74	10,677.2	-4,952.7	75.6	0.49	0.33	-0.37	24.2	-11.5
15,686.0	91.65	179.48	10,675.2	-5,046.6	76.2	0.98	0.94	-0.28	22.2	-11.4
15,780.0	89.76	179.65	10,674.1	-5,140.6	76.9	2.02	-2.01	0.18	20.9	-11.2
15,874.0	90.42	179.65	10,673.9	-5,234.6	77.5	0.70	0.70	0.00	20.5	-11.2
15,968.0	88.18	179.65	10,675.1	-5,328.6	78.1	2.38	-2.38	0.00	21.4	-11.2
16,062.0	88.35	179.39	10,677.9	-5,422.6	78.8	0.33	0.18	-0.28	24.0	-11.0
16,156.0	89.54	179.30	10,679.7	-5,516.5	79.9	1.27	1.27	-0.10	25.4	-10.4
16,251.0	90.55	179.13	10,679.6	-5,611.5	81.2	1.08	1.06	-0.18	25.1	-9.7
16,345.0	89.23	179.48	10,679.8	-5,705.5	82.4	1.45	-1.40	0.37	25.0	-9.1
16,439.0	89.41	179.30	10,680.9	-5,799.5	83.4	0.27	0.19	-0.19	25.9	-8.7
16,533.0	89.93	178.95	10,681.4	-5,893.5	84.8	0.67	0.55	-0.37	26.1	-7.8
16,628.0	89.67	178.51	10,681.7	-5,988.5	86.9	0.54	-0.27	-0.46	26.2	-6.2
16,722.0	89.49	178.25	10,682.4	-6,082.4	89.6	0.34	-0.19	-0.28	26.6	-4.1
16,816.0	90.20	177.81	10,682.7	-6,176.4	92.8	0.89	0.76	-0.47	26.6	-1.4
16,911.0	90.81	177.46	10,681.9	-6,271.3	96.7	0.74	0.64	-0.37	25.5	1.9
17,005.0	89.67	178.86	10,681.5	-6,365.2	99.7	1.92	-1.21	1.49	24.9	4.4
17,099.0	89.05	178.25	10,682.5	-6,459.2	102.1	0.93	-0.66	-0.65	25.7	6.2
17,194.0	89.41	178.34	10,683.8	-6,554.1	104.9	0.39	0.38	0.09	26.7	8.5
17,288.0	89.89	177.90	10,684.4	-6,648.1	108.0	0.69	0.51	-0.47	27.0	11.0
17,382.0	90.64	177.63	10,683.9	-6,742.0	111.7	0.85	0.80	-0.29	26.3	14.1
17,476.0	91.03	177.02	10,682.6	-6,835.9	116.1	0.77	0.41	-0.65	24.7	17.9
17,571.0	90.51	178.86	10,681.3	-6,930.8	119.5	2.01	-0.55	1.94	23.2	20.8
17,665.0	90.20	178.16	10,680.7	-7,024.8	121.9	0.81	-0.33	-0.74	22.5	22.7



Final PVA



Company:	Midland	Local Co-ordinate Reference:	Well #511H
Project:	Lea County, NM (NAD 83 NME)	TVD Reference:	kb = 26' @ 3520.0usft
Site:	Merciless 13 Fed Com	MD Reference:	kb = 26' @ 3520.0usft
Well:	#511H	North Reference:	Grid
Wellbore:	OH	Survey Calculation Method:	Minimum Curvature
Design:	OH	Database:	PEDM

Survey										
MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	N/S (usft)	E/W (usft)	DLeg (°/100usft)	Build (°/100usft)	Turn (°/100usft)	High to Plan (usft)	Right to Plan (usft)
17,759.0	89.49	180.53	10,681.0	-7,118.8	123.0	2.63	-0.76	2.52	22.6	23.2
17,854.0	89.80	181.15	10,681.5	-7,213.8	121.6	0.73	0.33	0.65	23.0	21.3
17,948.0	90.37	180.97	10,681.4	-7,307.8	119.9	0.64	0.61	-0.19	22.7	19.0
18,042.0	90.77	180.71	10,680.5	-7,401.7	118.5	0.51	0.43	-0.28	21.6	17.1
Final MWD Survey (MD=18042.0')										
18,139.0	90.77	180.71	10,679.2	-7,498.7	117.3	0.00	0.00	0.00	20.2	15.3
Final Projection to Bit (MD=18139.0')										

Survey Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment	
		+N/-S (usft)	+E/-W (usft)		
10,086.0	10,075.0	236.2	3.4	KOP (MD=10086.0', TVD:10075.0')	
10,233.6	10,219.8	210.4	2.6	HL Crossing (MD:10233.6', TVD:10219.8', N/S:210.4', E/W:2.6', INC:18.77)	
18,042.0	10,680.5	-7,401.7	118.5	Final MWD Survey (MD=18042.0')	
18,139.0	10,679.2	-7,498.7	117.3	Final Projection to Bit (MD=18139.0')	

Checked By: _____	Approved By: _____	Date: _____
-------------------	--------------------	-------------

I CERTIFY THIS SURVEY TO BE TRUE AND CORRECT TO THE BEST OF MY BELIEF AND KNOWLEDGE
KAY MADDOX 06/01/2023



Lea County, NM (NAD 83 NME)

Merciless 13 Fed Com #511H

OH

PROJECT DETAILS: Lea County, NM (NAD 83 NME)

Geodetic System: US State Plane 1983
Datum: North American Datum 1983
Ellipsoid: GRS 1980
Zone: New Mexico Eastern Zone
System Datum: Mean Sea Level

WELL DETAILS: #511H










3494.0			
Northings	kb = 26' @ 3520.0usft	Latitude	Longitude
414303.00	761606.00	32° 8' 13.191 N	103° 37' 18.157 W



Azimuths to Grid North
True North: -0.38°
Magnetic North: 5.98°

Magnetic Field
Strength: 47257.9nT
Dip Angle: 59.76°
Date: 3/4/2023
Model: IGRF2020

To convert a Magnetic Direction to a Grid Direction, Add 5.98°
To convert a Magnetic Direction to a True Direction, Add 6.36° East
To convert a True Direction to a Grid Direction, Subtract 0.38°

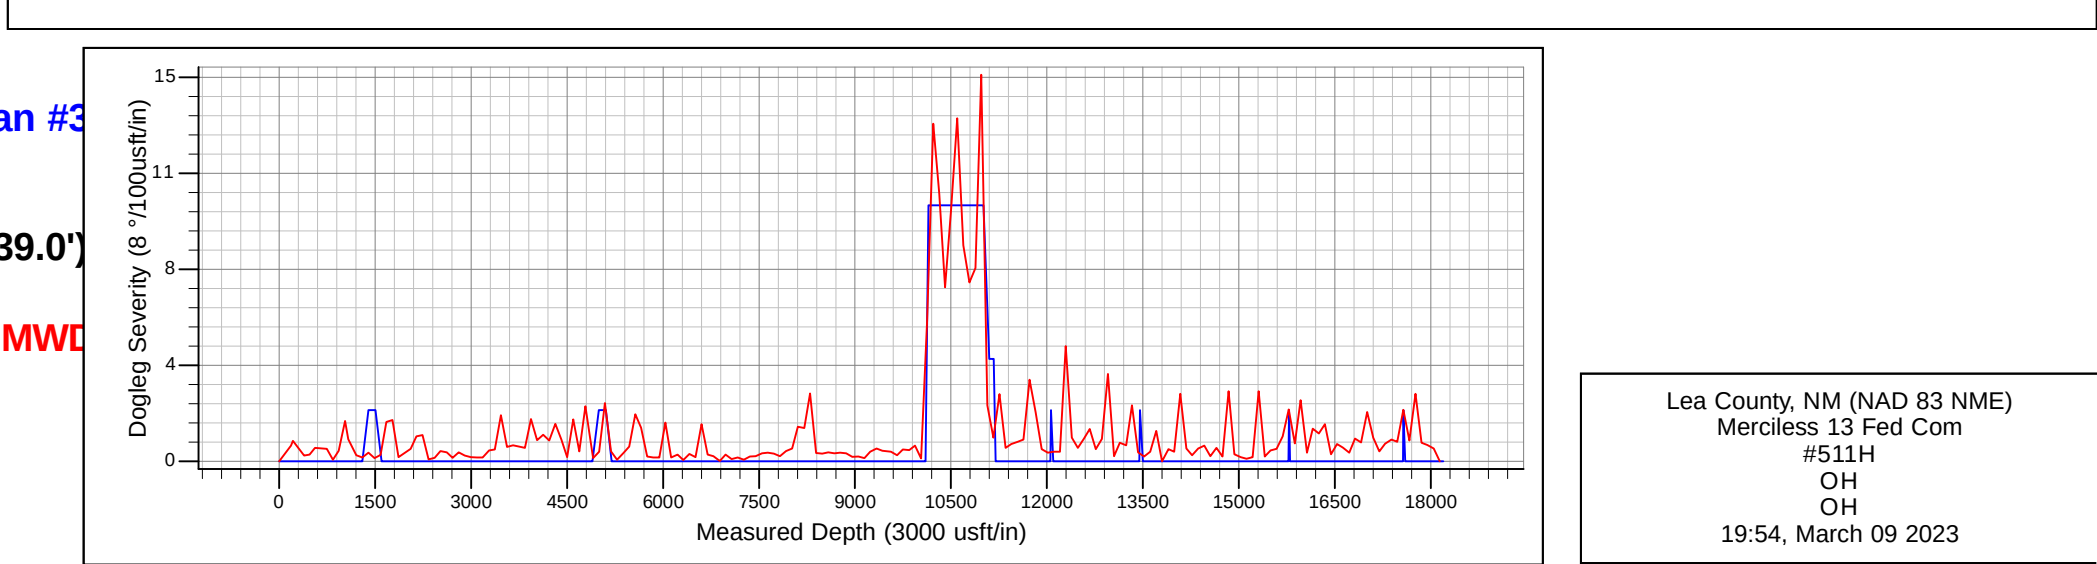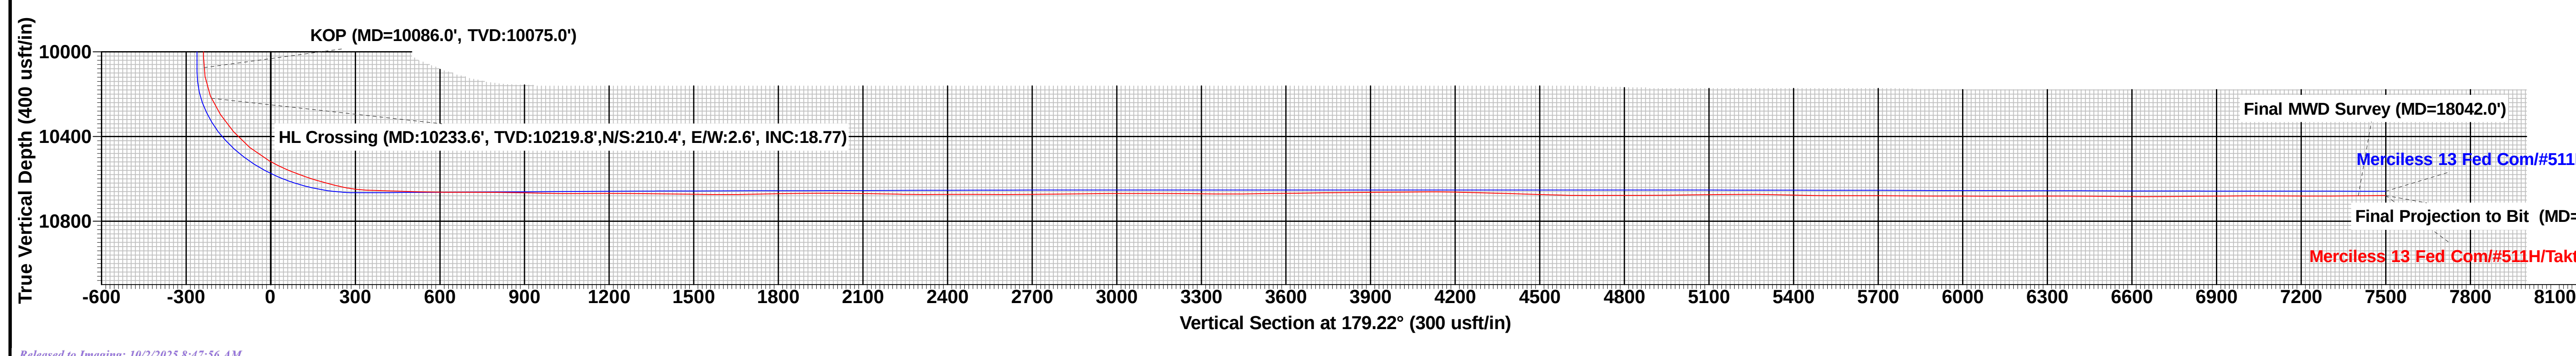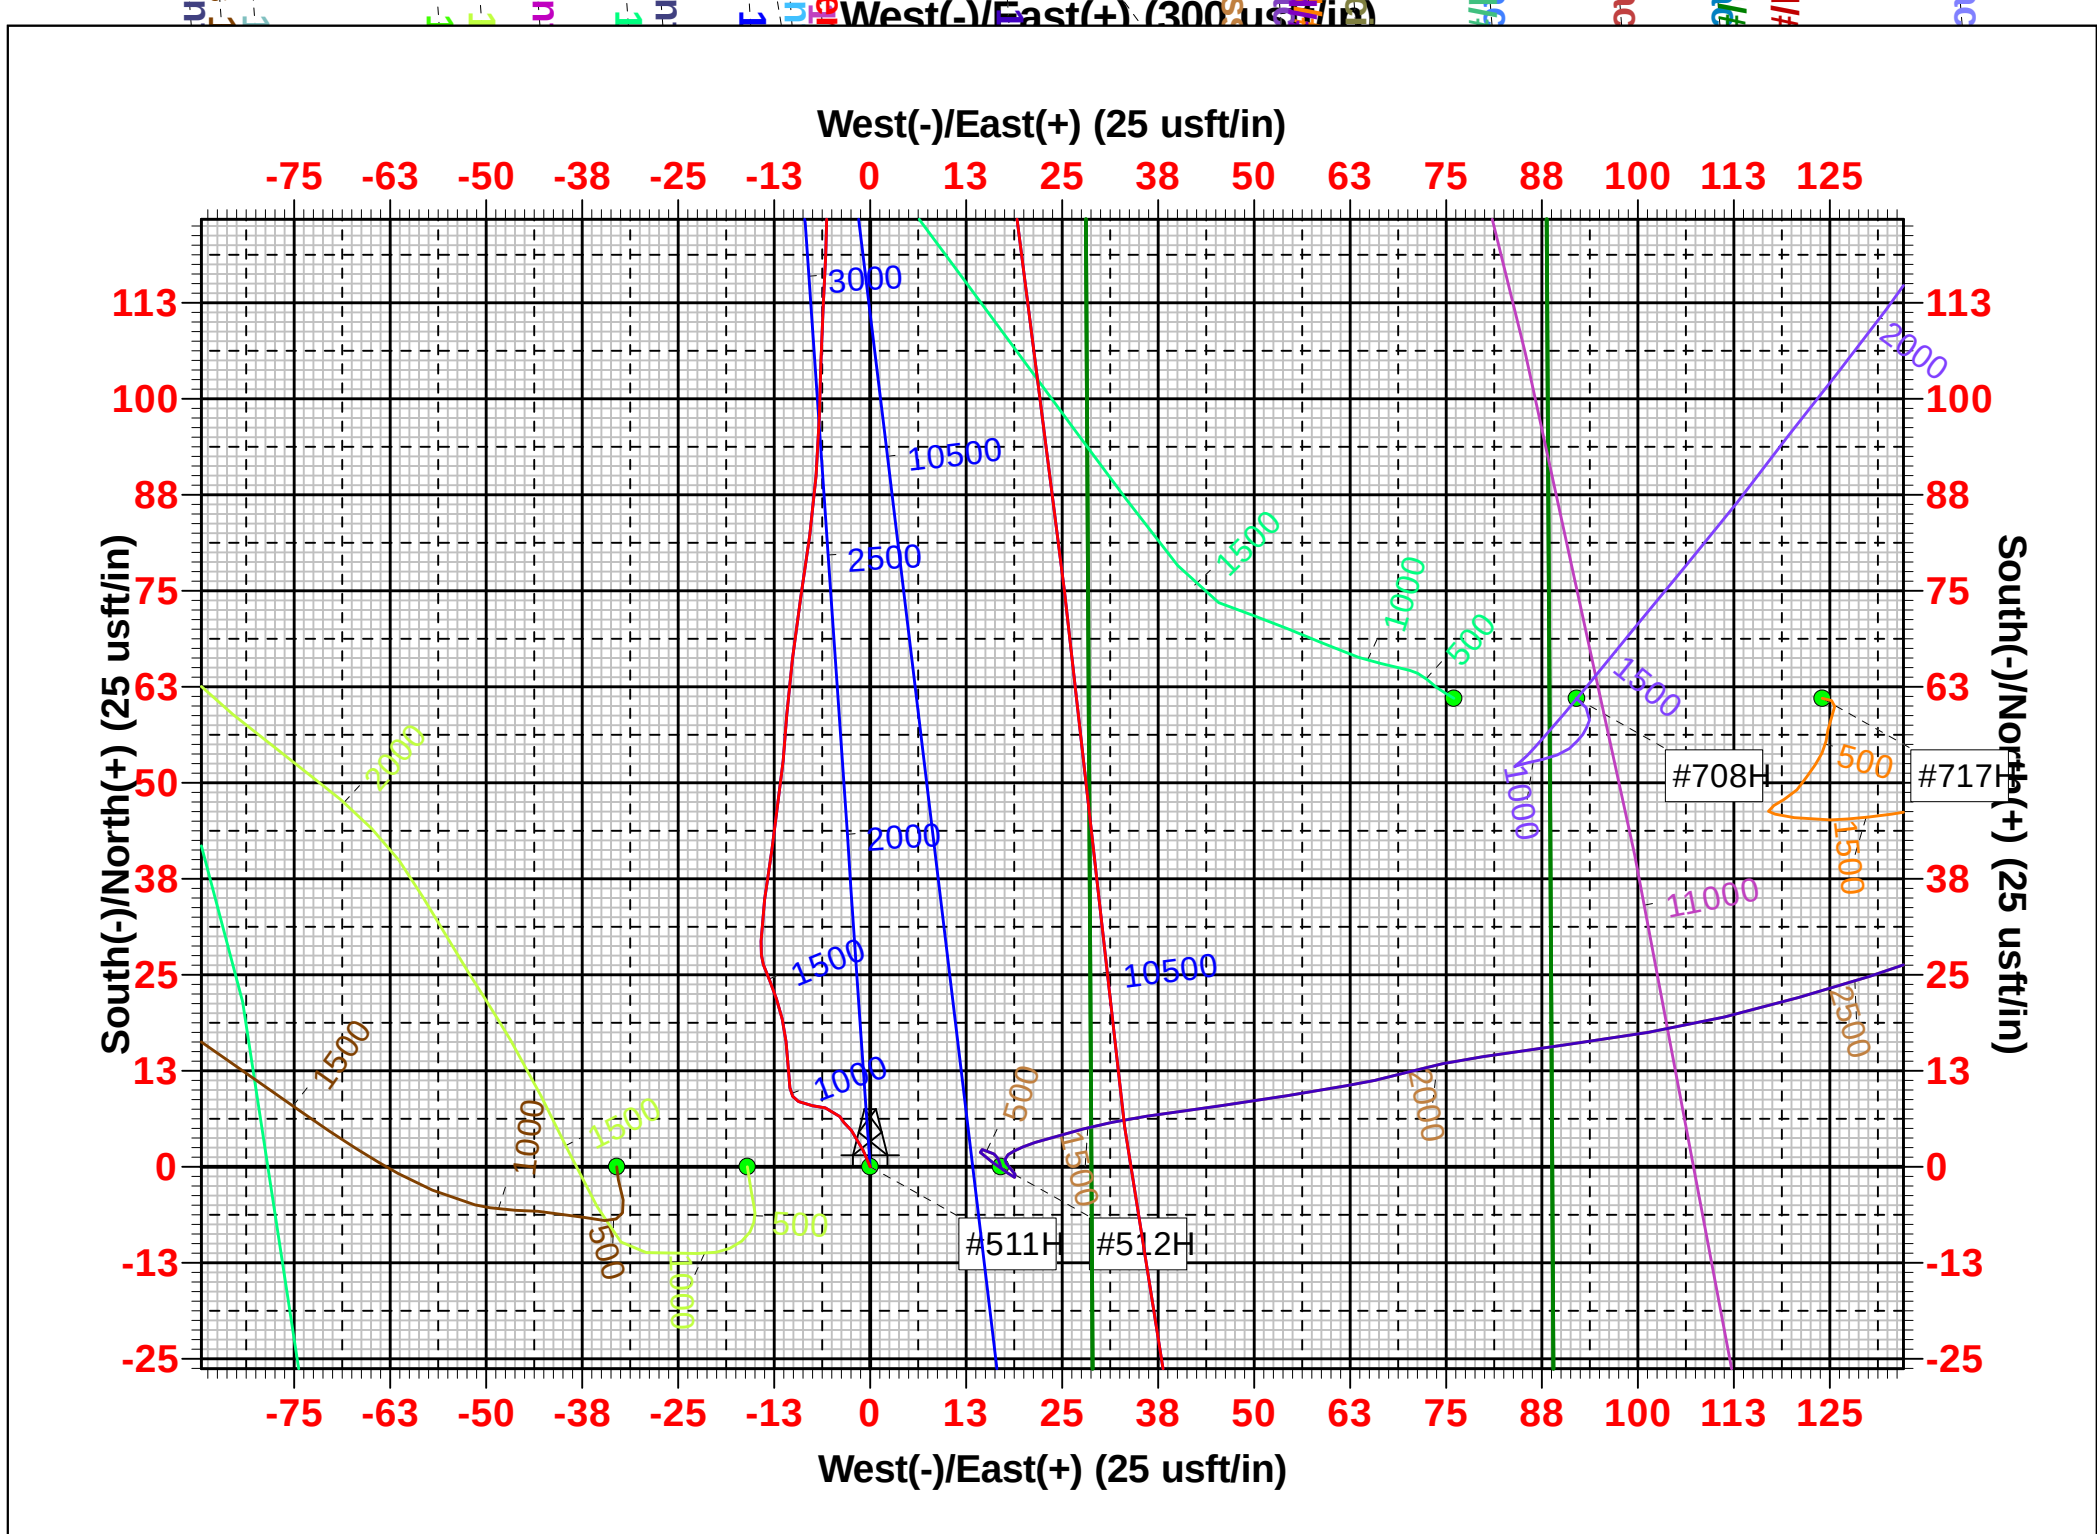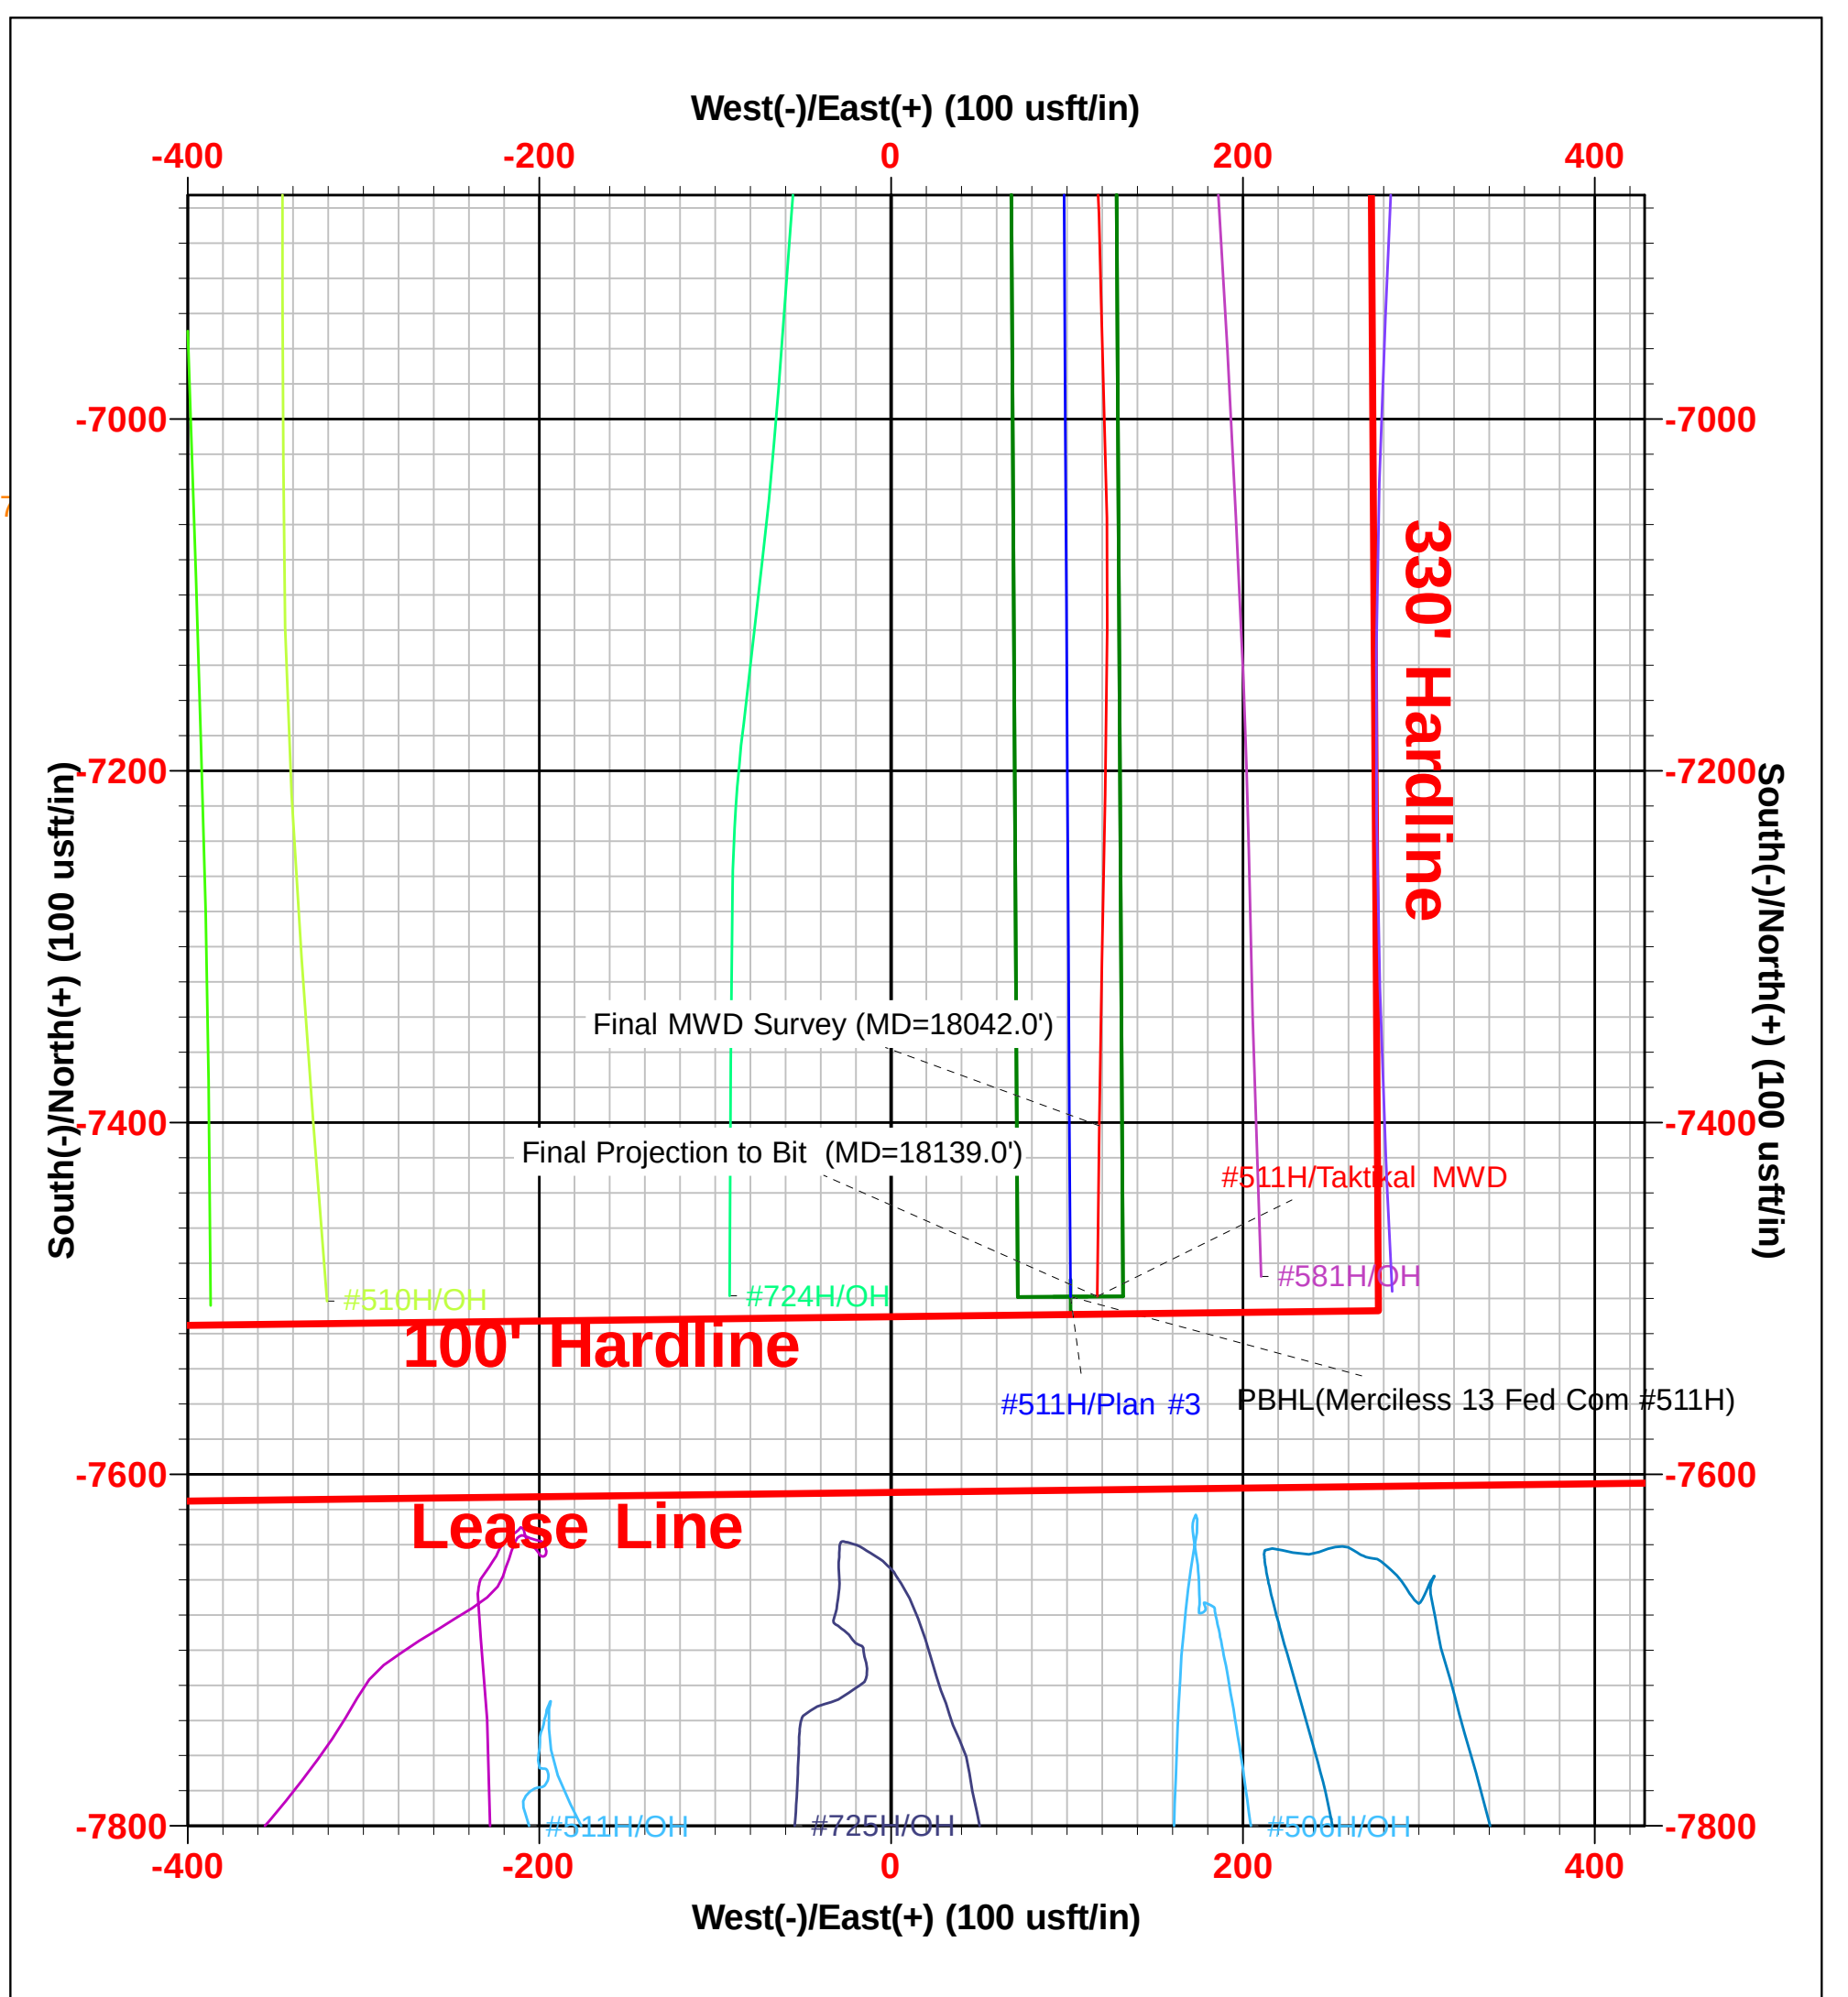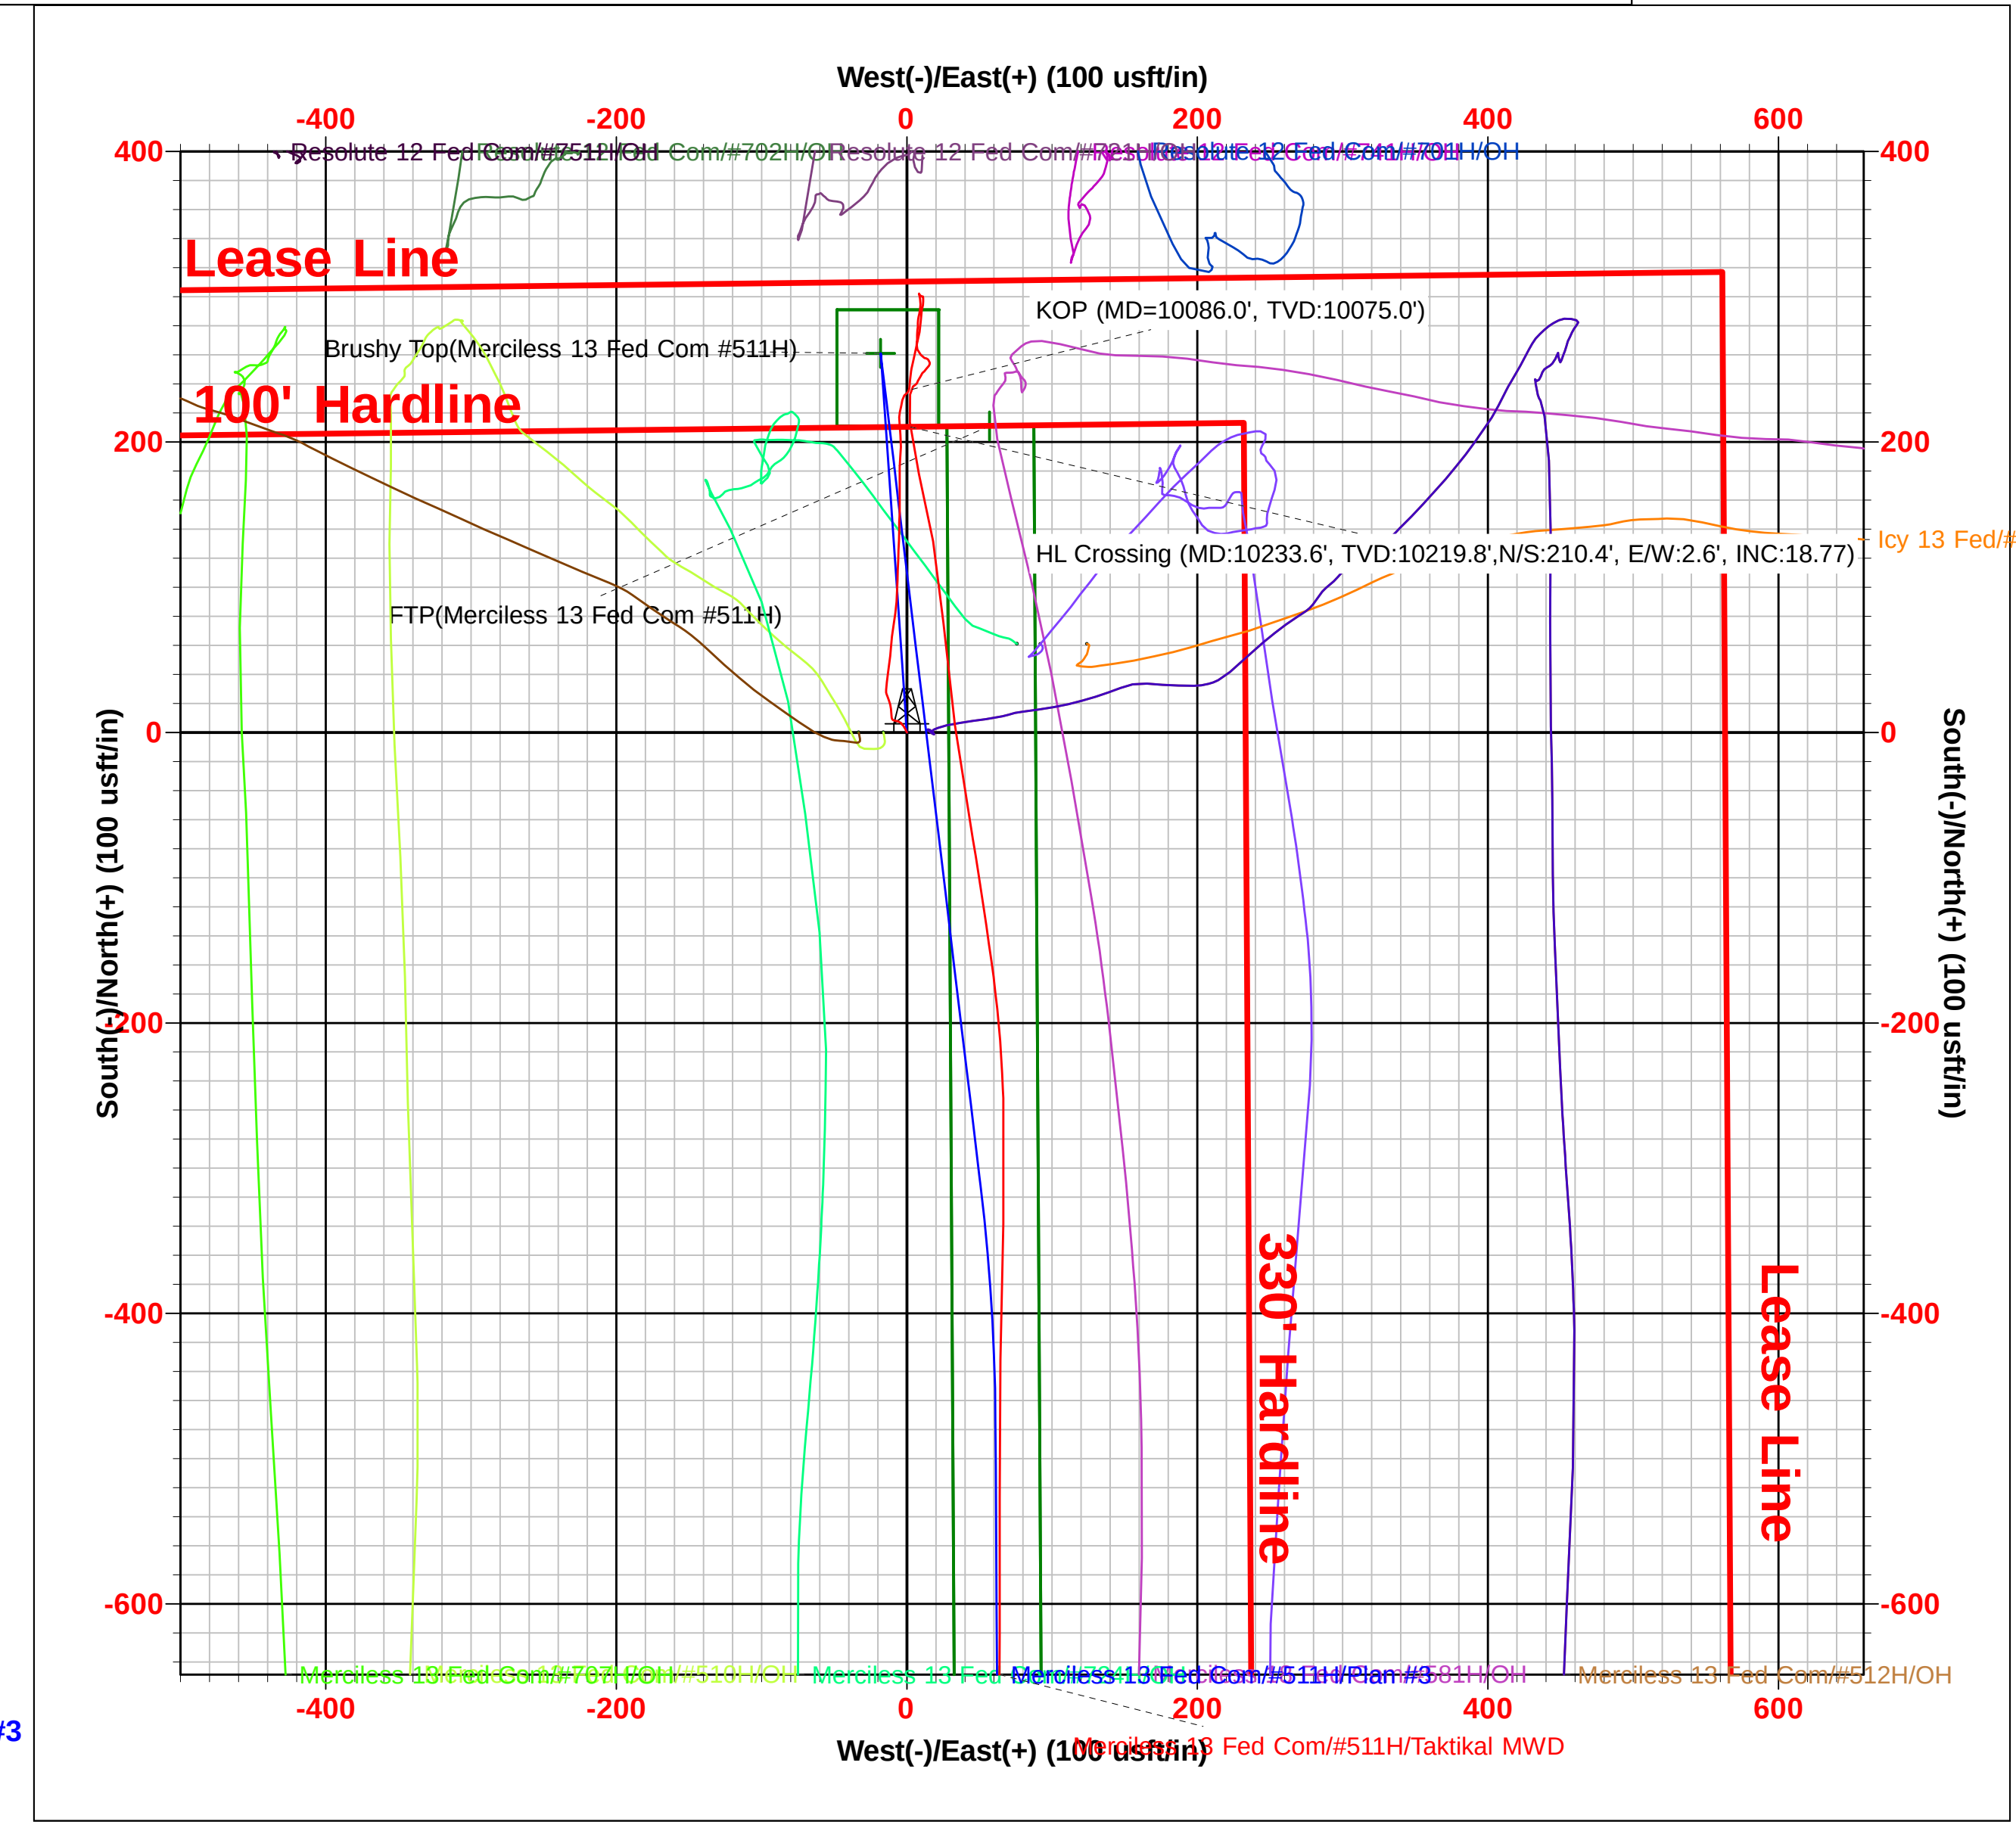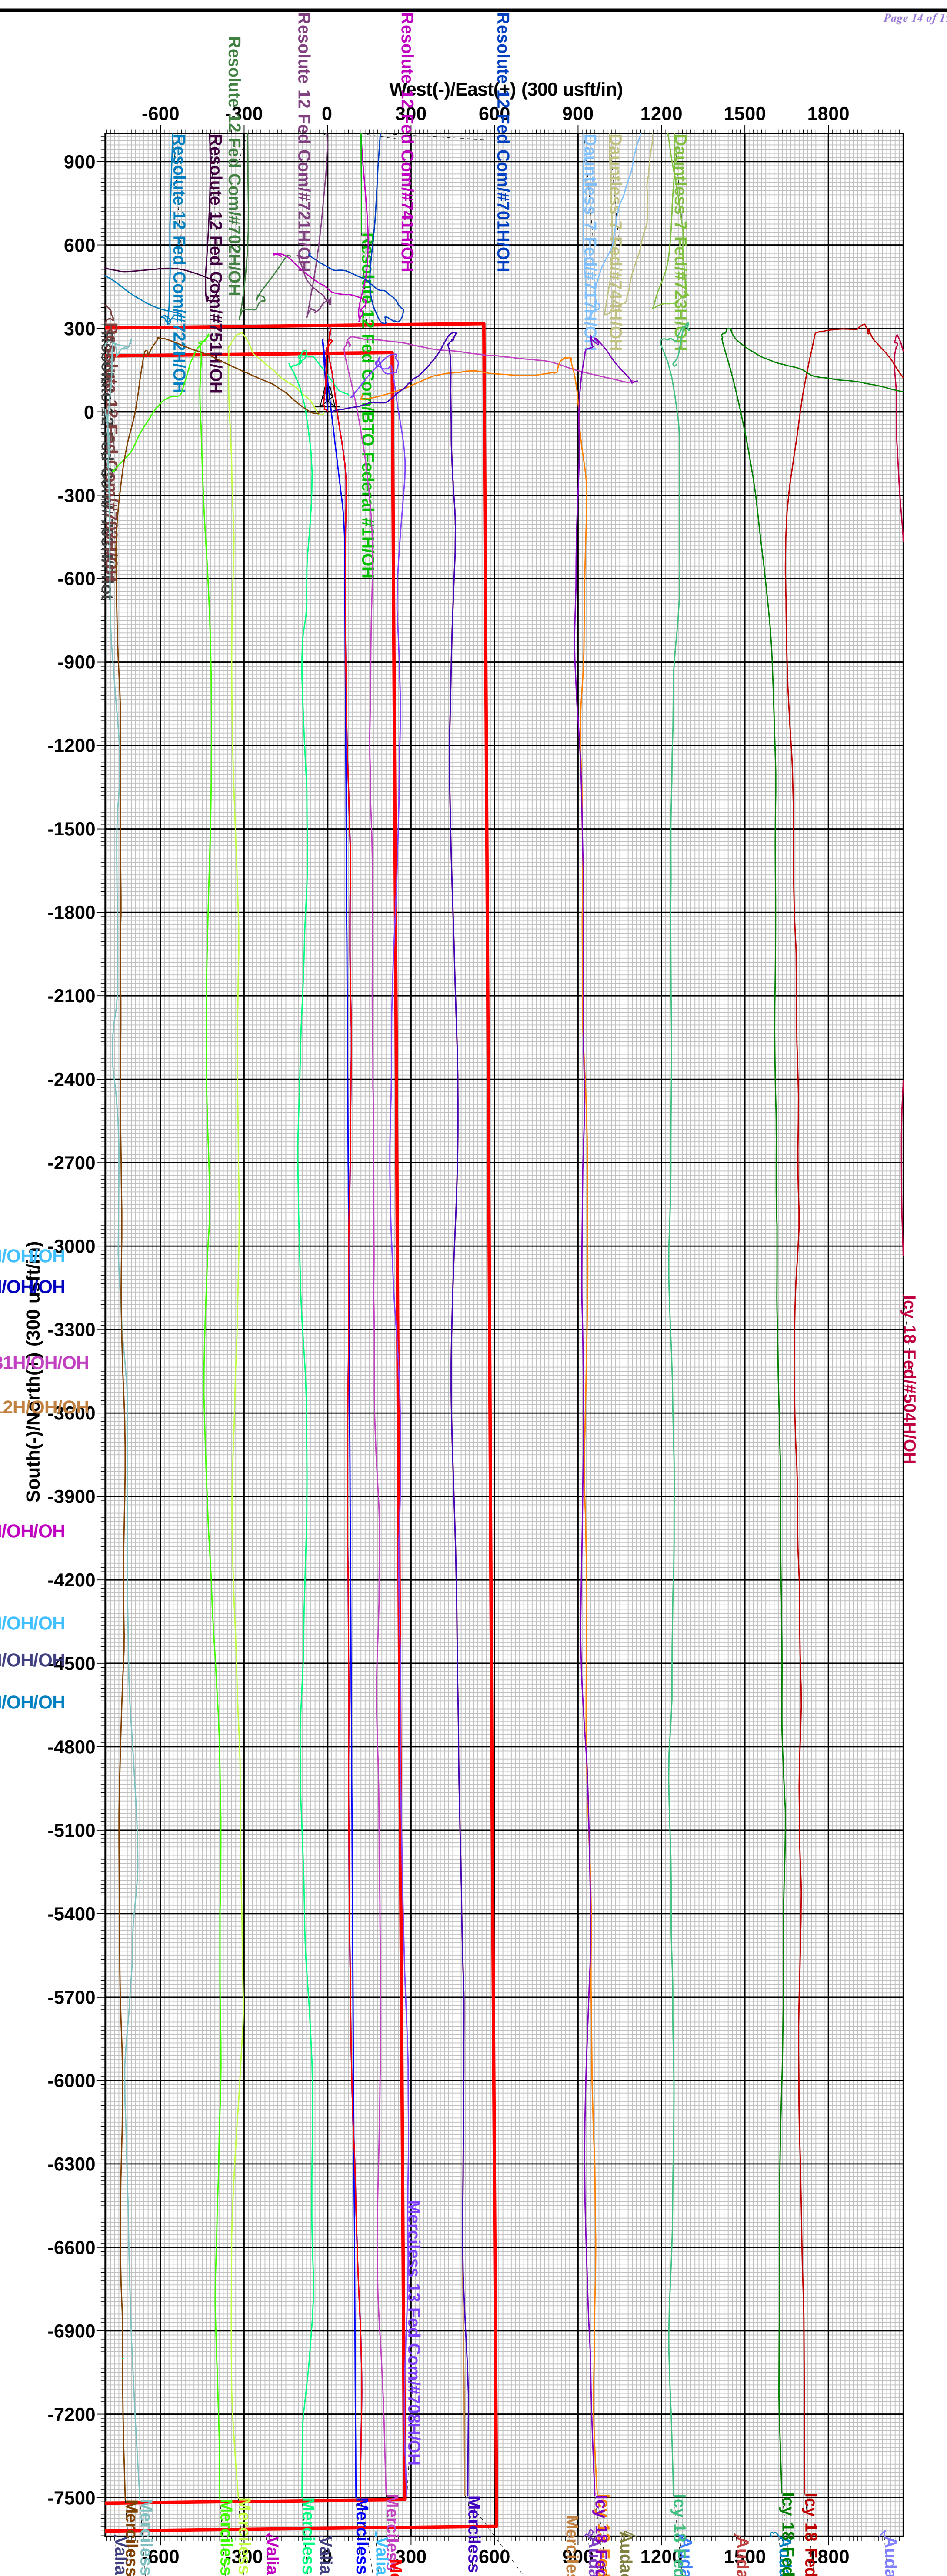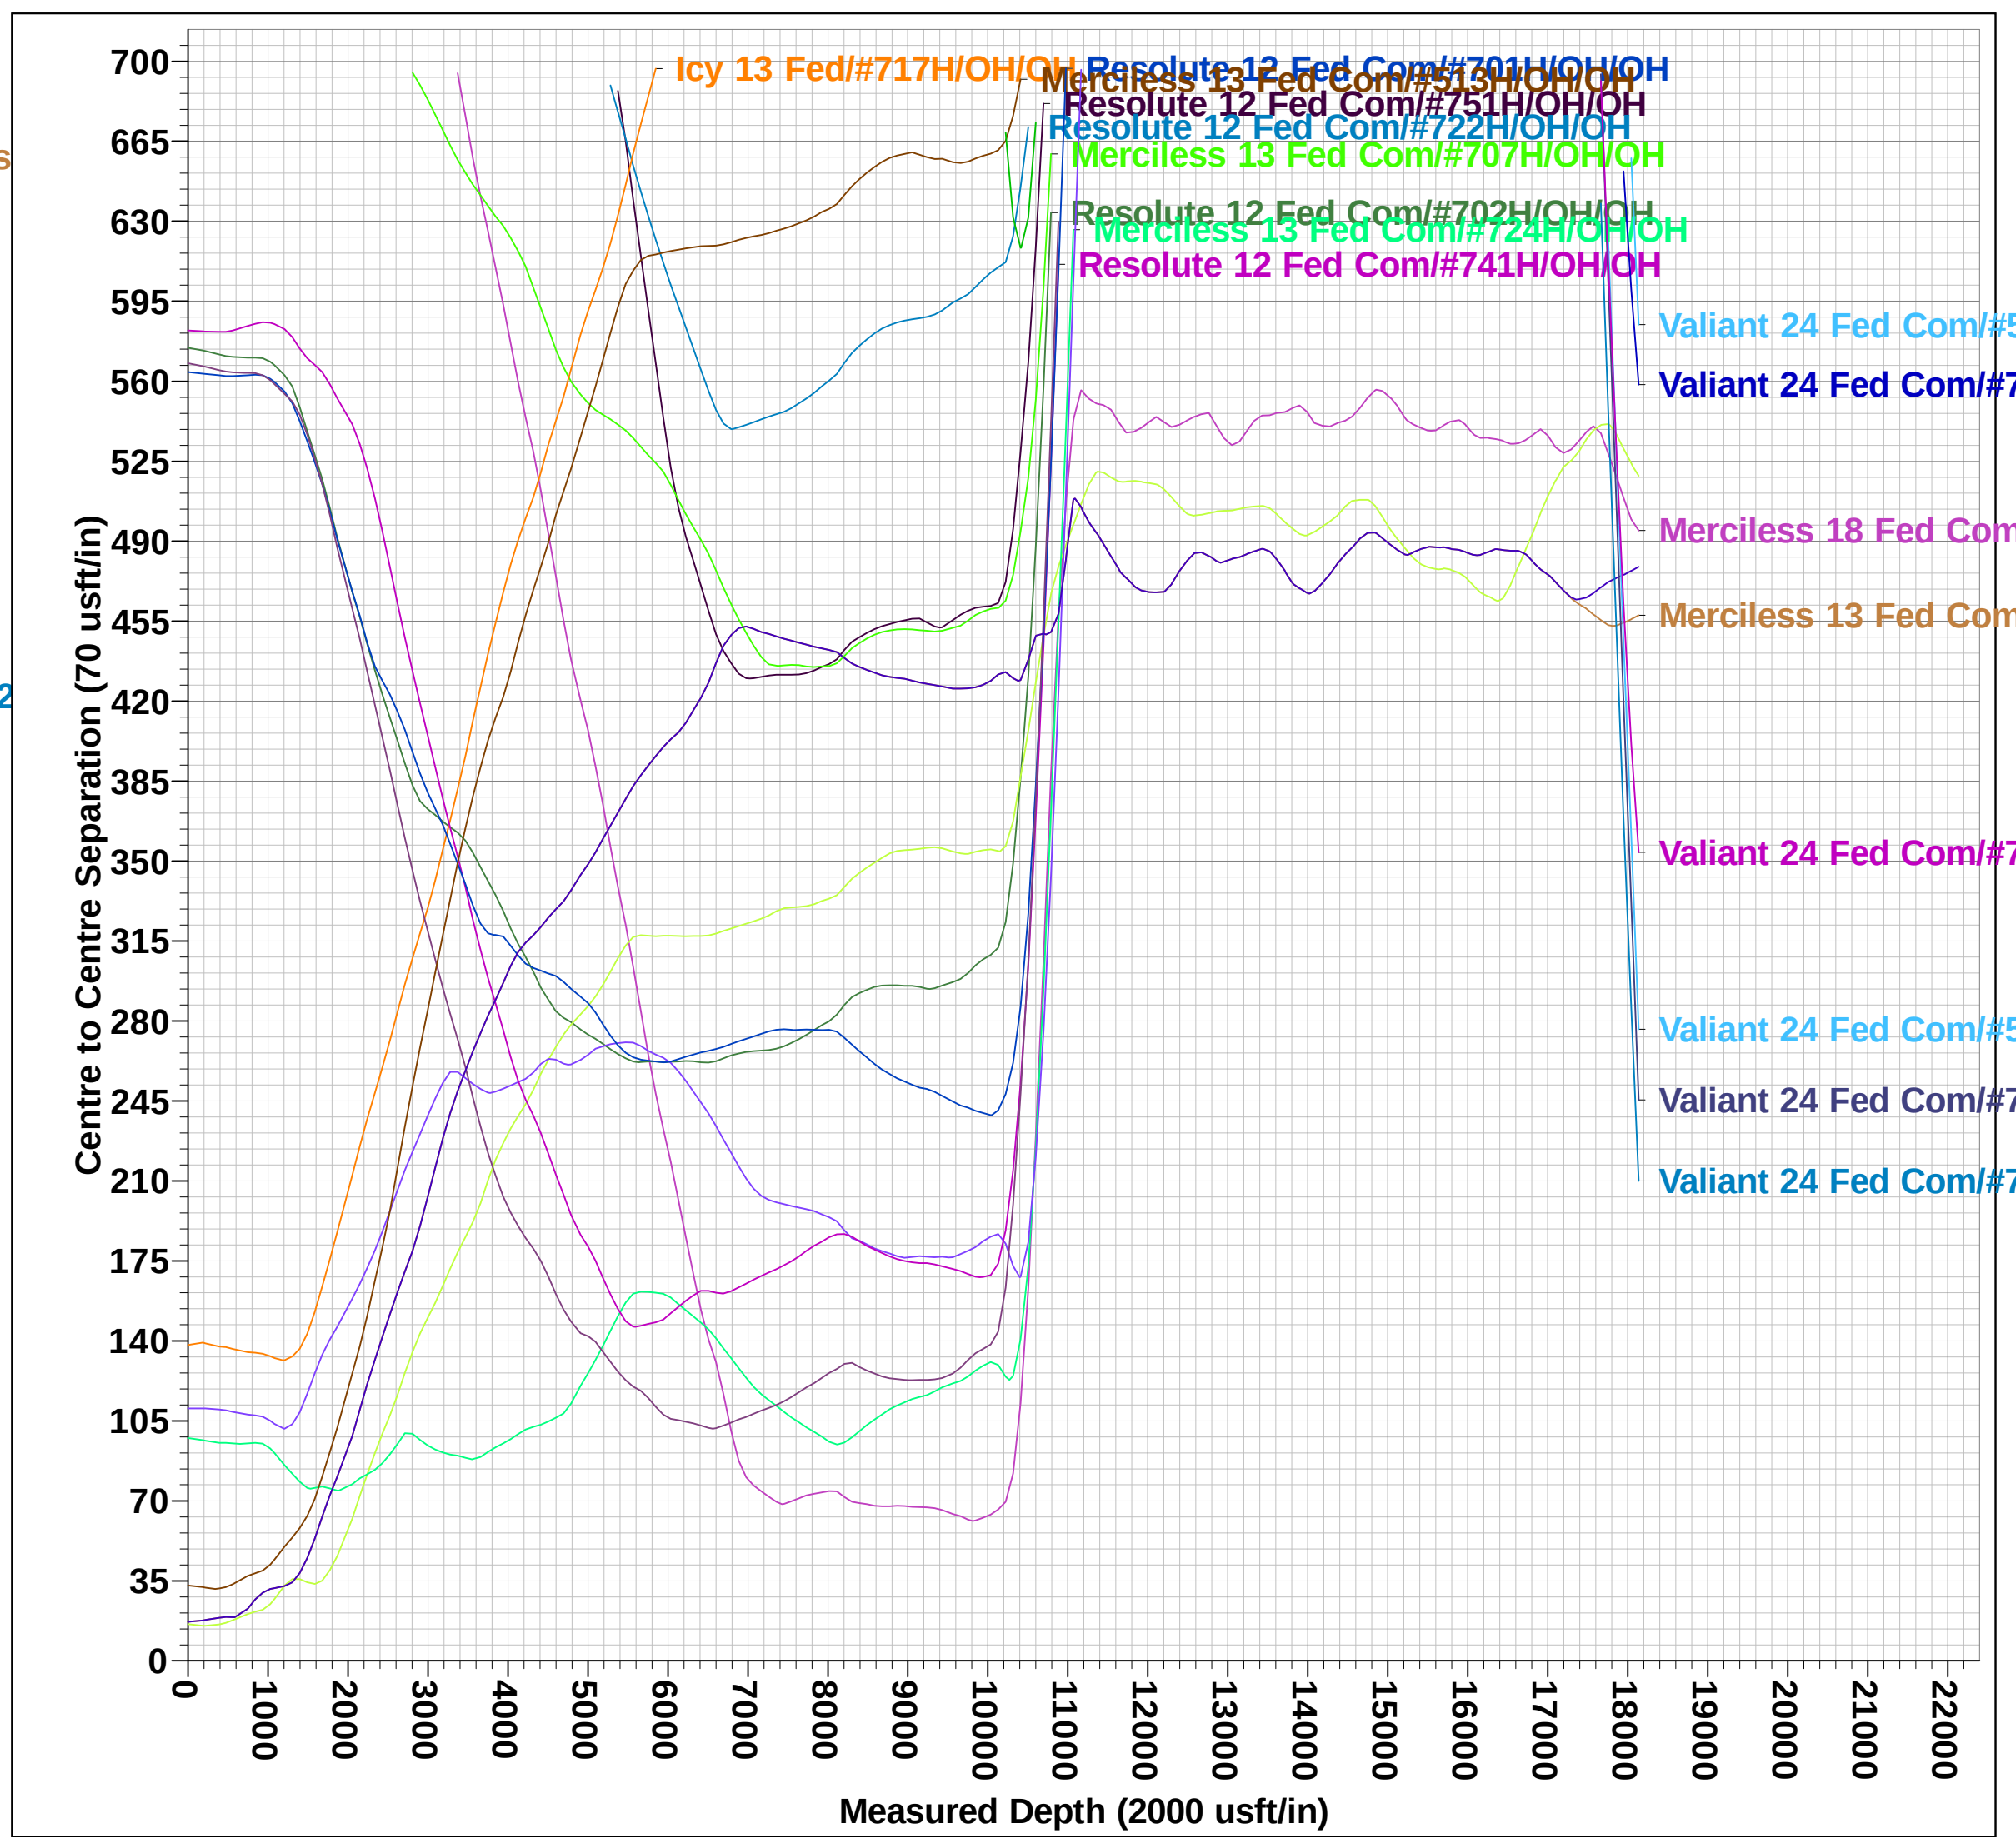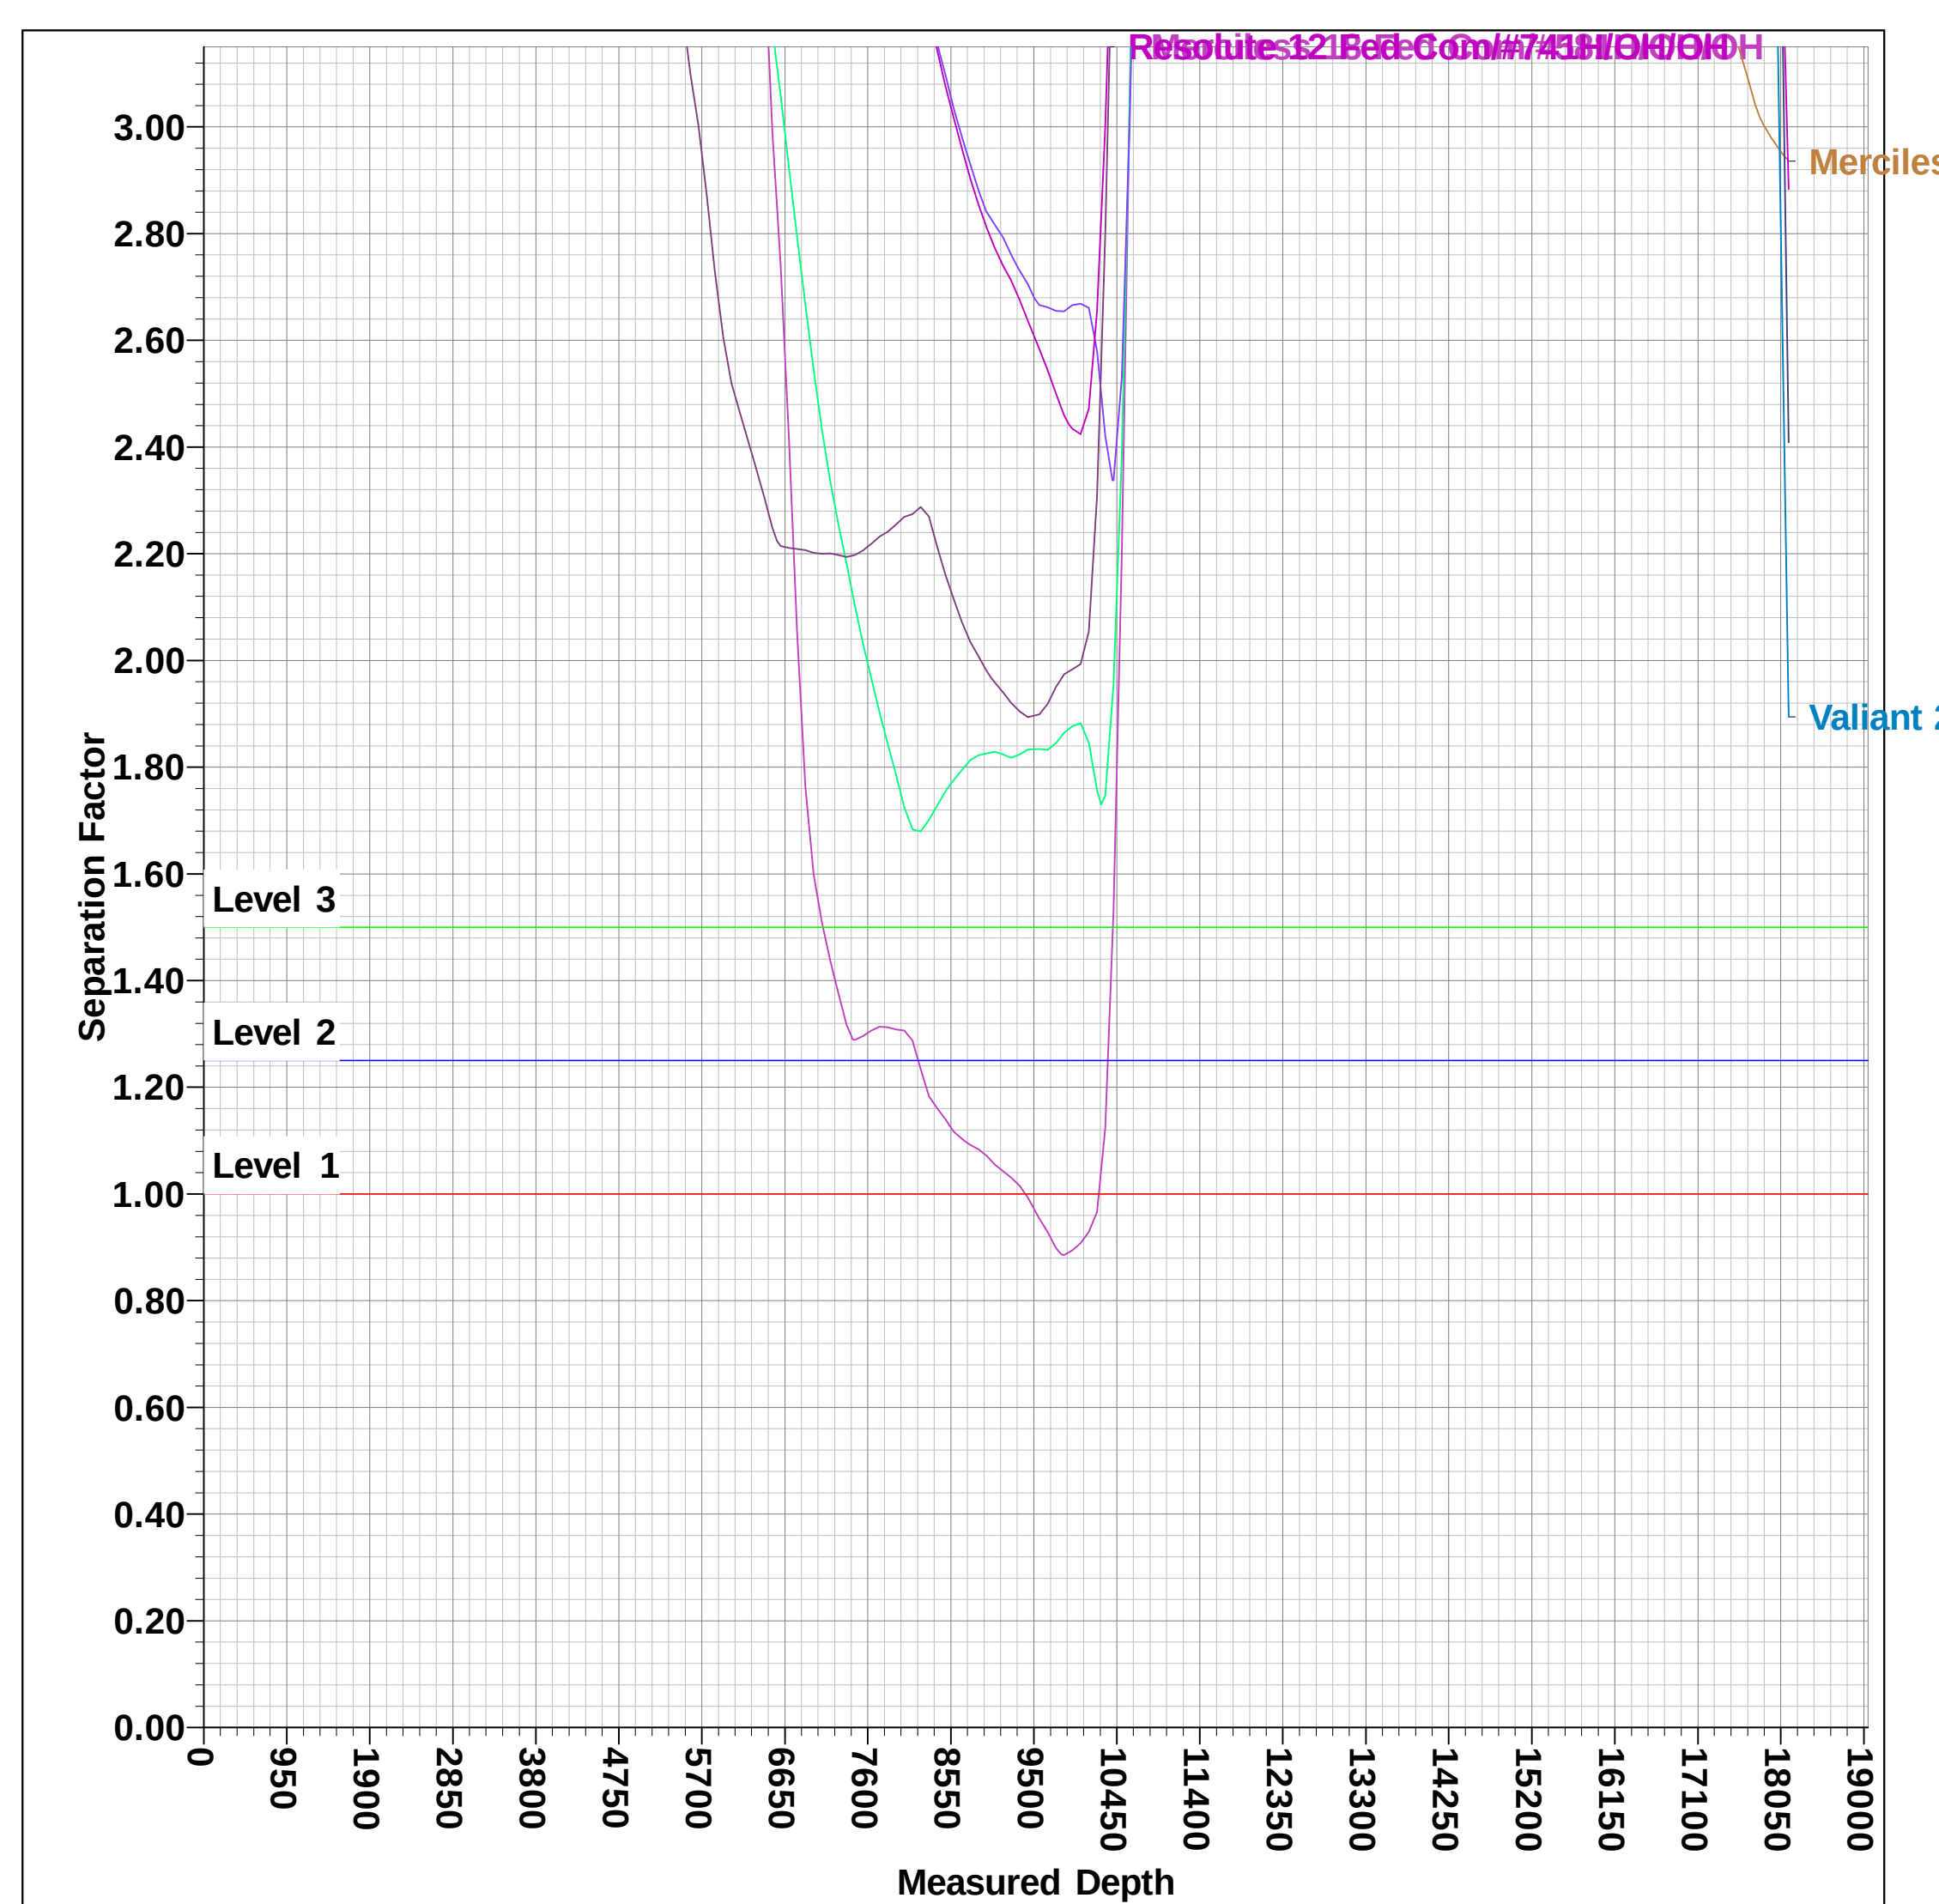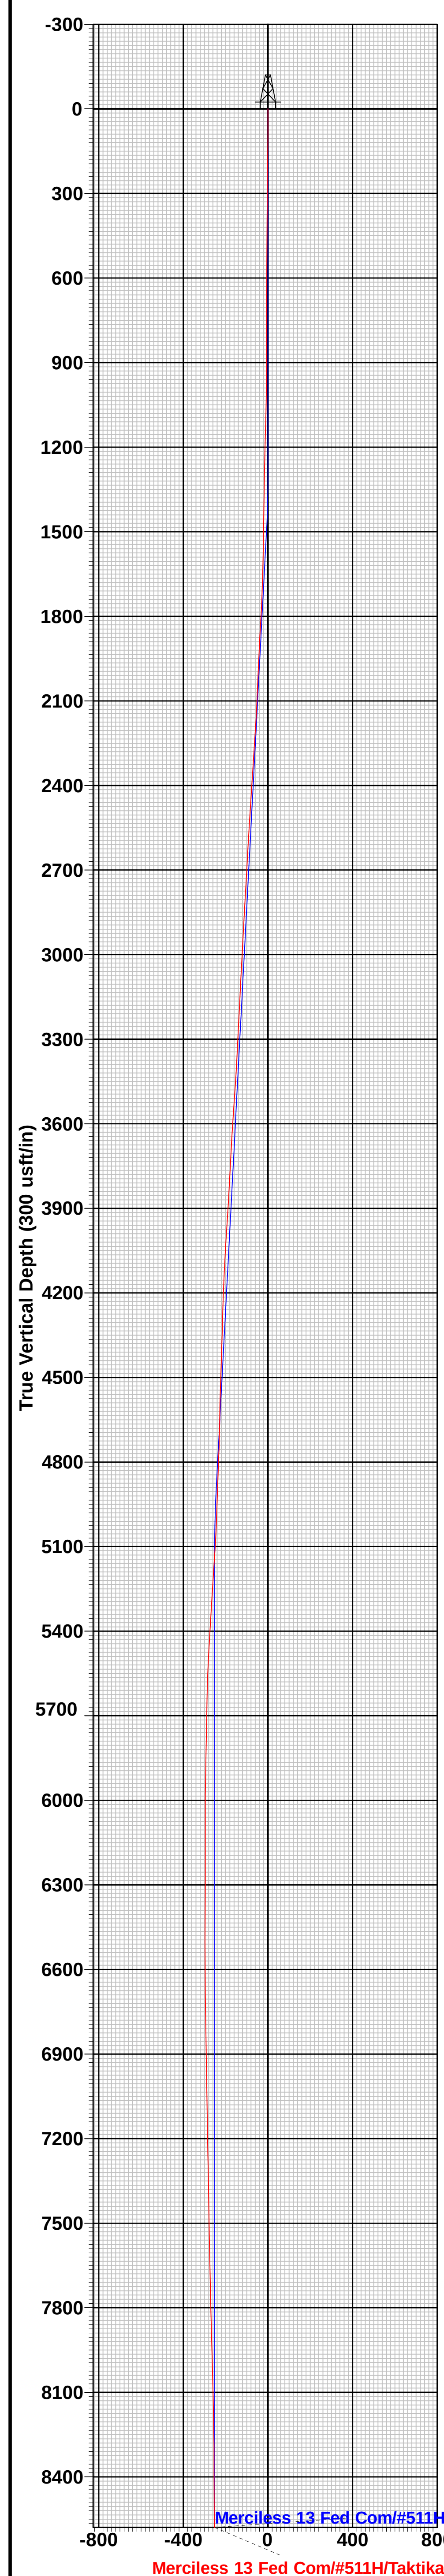

Intent ☐ As Drilled ☐

API #		
Operator Name:	Property Name:	Well Number

Kick Off Point (KOP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

First Take Point (FTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Last Take Point (LTP)

UL	Section	Township	Range	Lot	Feet	From N/S	Feet	From E/W	County
Latitude					Longitude				NAD

Is this well the defining well for the Horizontal Spacing Unit? ☐Is this well an infill well? ☐

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

Submit To Appropriate District Office Two Copies <u>District I</u> 1625 N. French Dr., Hobbs, NM 88240 <u>District II</u> 811 S. First St., Artesia, NM 88210 <u>District III</u> 1000 Rio Brazos Rd., Aztec, NM 87410 <u>District IV</u> 1220 S. St. Francis Dr., Santa Fe, NM 87505		State of New Mexico Energy, Minerals and Natural Resources Oil Conservation Division 1220 South St. Francis Dr. Santa Fe, NM 87505			Form C-105 Revised August 1, 2011					
WELL COMPLETION OR RECOMPLETION REPORT AND LOG										
4. Reason for filing: ☒ COMPLETION REPORT (Fill in boxes #1 through #31 for State and Fee wells only) ☐ C-144 CLOSURE ATTACHMENT (Fill in boxes #1 through #9, #15 Date Rig Released and #32 and/or #33; attach this and the plat to the C-144 closure report in accordance with 19.15.17.13.K NMAC)								5. Lease Name or Unit Agreement Name MERCILESS 13 FEDERAL COM		
								6. Well Number: 511H		
7. Type of Completion: ☒ NEW WELL ☐ WORKOVER ☐ DEEPENING ☐ PLUGBACK ☐ DIFFERENT RESERVOIR ☐ OTHER _____										
8. Name of Operator EOG RESOURCES INC							9. OGRID 7377			
10. Address of Operator PO BOX 2267 MIDLAND, TEXAS 79702							11. Pool name or Wildcat WC025 G08 S253235G; LOWER BONE SPRING			
12. Location	Unit Ltr	Section	Township	Range	Lot	Feet from the	N/S Line	Feet from the	E/W Line	County
Surface:	A	13	25S	32E		310	NORTH	563	EAST	LEA
BH:	H	24	25S	32E		2531	NORTH	489	EAST	LEA
13. Date Spudded 01/20/2023	14. Date T.D. Reached 02/26/2023		15. Date Rig Released 02/27/2023			16. Date Completed (Ready to Produce) 05/12/2023		17. Elevations (DF and RKB, RT, GR, etc.) 3494' GL		
18. Total Measured Depth of Well MD 18,139' TVD 10,679'			19. Plug Back Measured Depth MD 18,108' TVD 10,679'			20. Was Directional Survey Made? YES		21. Type Electric and Other Logs Run None		
22. Producing Interval(s), of this completion - Top, Bottom, Name BONE SPRING 10,788 - 18,108'										
23. CASING RECORD (Report all strings set in well)										
CASING SIZE		WEIGHT LB./FT.		DEPTH SET		HOLE SIZE		CEMENTING RECORD		AMOUNT PULLED
13 3/8"		54.5# J-55		1128'		16"		555 CL C/CIRC		
9 5/8"		40# J-55		4848'		11"		845 CL C/CIRC		
5 1/2"		20# ICYP 110		18,116'		7 7/8"		1745 CL C&H, TOC 1608'		CBL
24. LINER RECORD						25. TUBING RECORD				
SIZE	TOP	BOTTOM	SACKS CEMENT	SCREEN	SIZE	DEPTH SET	PACKER SET			
26. Perforation record (interval, size, and number) 10,788 - 18,108' 3 1/8", 1485 holes					27. ACID, SHOT, FRACTURE, CEMENT, SQUEEZE, ETC.					
					DEPTH INTERVAL		AMOUNT AND KIND MATERIAL USED			
					10,788 - 18,108		FRAC W/18,004,240 lbs proppant, 295,671 bbls load fld			
28. PRODUCTION										
Date First Production 05/12/2023		Production Method (<i>Flowing, gas lift, pumping - Size and type pump</i>) Flowing				Well Status (<i>Prod. or Shut-in</i>) Producing				
Date of Test 05/18/2023	Hours Tested 24	Choke Size	Prod'n For Test Period	Oil - Bbl 2324	Gas - MCF 3497	Water - Bbl. 10,315	Gas - Oil Ratio 1504			
Flow Tubing Press.	Casing Pressure 791	Calculated 24-Hour Rate	Oil - Bbl.	Gas - MCF	Water - Bbl.	Oil Gravity - API - (<i>Corr.</i>) 49				
29. Disposition of Gas (<i>Sold, used for fuel, vented, etc.</i>) SOLD							30. Test Witnessed By			
31. List Attachments C-102, C-104, C-103, Directional Survey, H spacing										
32. If a temporary pit was used at the well, attach a plat with the location of the temporary pit.										
33. If an on-site burial was used at the well, report the exact location of the on-site burial:										
Latitude _____ Longitude _____ NAD 1927 1983										
I hereby certify that the information shown on both sides of this form is true and complete to the best of my knowledge and belief Printed Signature Kay Maddox Name Kay Maddox Title Senior Regulatory Specialist Date 06/05/2023 E-mail Address kay_maddox@eogresources.com										

This form is to be filed with the appropriate District Office of the Division not later than 20 days after the completion of any newly-drilled or deepened well and not later than 60 days after completion of closure. When submitted as a completion report, this shall be accompanied by one copy of all electrical and radio-activity logs run on the well and a summary of all special tests conducted, including drill stem tests. All depths reported shall be measured depths. In the case of directionally drilled wells, true vertical depths shall also be reported. For multiple completions, items 11, 12 and 26-31 shall be reported for each zone.

Southeastern New Mexico		Northwestern New Mexico	
T. Anhy Rustler 966'	T. Canyon Brushy 7243'	T. Ojo Alamo	T. Penn A"
T. Salt 1237'	T. Strawn	T. Kirtland	T. Penn. "B"
B. Salt 4652'	T. Atoka	T. Fruitland	T. Penn. "C"
T. Yates	T. Miss	T. Pictured Cliffs	T. Penn. "D"
T. 7 Rivers	T. Devonian	T. Cliff House	T. Leadville
T. Queen	T. Silurian	T. Menefee	T. Madison
T. Grayburg	T. Montoya	T. Point Lookout	T. Elbert
T. San Andres	T. Simpson	T. Mancos	T. McCracken
T. Glorieta	T. McKee	T. Gallup	T. Ignacio Otzte
T. Paddock	T. Ellenburger	Base Greenhorn	T. Granite
T. Blinebry	T. Gr. Wash	T. Dakota	
T. Tubb	T. Delaware Sand	T. Morrison	
T. Drinkard	T. Bone Springs	T. Todilto	
T. Abo	T. 1st BS Sand 10,028	T. Entrada	
T. Wolfcamp	T. 2nd BS Sand 10,514'	T. Wingate	
T. Penn	T.	T. Chinle	
T. Cisco (Bough C)	T.	T. Permian	

No. 1, from.....to.....
No. 2, from.....to.....
No. 3, from.....to.....
No. 4, from.....to.....

Include data on rate of water inflow and elevation to which water rose in hole.

No. 1, from.....to.....feet.....
 No. 2, from.....to.....feet.....
 No. 3, from.....to.....feet.....

From	To	Thickness In Feet	Lithology

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

ACKNOWLEDGMENTS

Action 224109

ACKNOWLEDGMENTS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 224109
	Action Type: [C-104] Completion Packet (C-104C)

ACKNOWLEDGMENTS

☒	I hereby certify that the required Water Use Report has been, or will be, submitted for this wells completion.
☒	I hereby certify that the required FracFocus disclosure has been, or will be, submitted for this wells completion.

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/ocd/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 224109

CONDITIONS

Operator: EOG RESOURCES INC 5509 Champions Drive Midland, TX 79706	OGRID: 7377
	Action Number: 224109
	Action Type: [C-104] Completion Packet (C-104C)

CONDITIONS

Created By	Condition	Condition Date
plmartinez	File 3160-4 Completion Report within 10 days of BLM approval.	10/2/2025
