

Form 3160-5 (June 2019)		UNITED STATES DEPARTMENT OF THE INTERIOR BUREAU OF LAND MANAGEMENT		FORM APPROVED OMB No. 1004-0137 Expires: October 31, 2021	
SUNDRY NOTICES AND REPORTS ON WELLS <i>Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.</i>				5. Lease Serial No. NMNM121961	
				6. If Indian, Allottee or Tribe Name EASTERN NAVAJO	
				7. If Unit of CA/Agreement, Name and/or No. Greater Lybrook/NMNM144419X	
SUBMIT IN TRIPLICATE - Other instructions on page 2				8. Well Name and No. GREATER LYBROOK UNIT/761H	
1. Type of Well ☒ Oil Well ☐ Gas Well ☐ Other				9. API Well No. 3004538269	
2. Name of Operator ENDURING RESOURCES LLC				10. Field and Pool or Exploratory Area BASIN MANCOS/LYBROOK MANCOS W	
3a. Address 1050 17TH STREET SUITE 2500, DENVER, CO		3b. Phone No. (include area code) (303) 573-1222		11. Country or Parish, State SAN JUAN/NM	
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) SEC 23/T23N/R09W/NMP					

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA					
TYPE OF SUBMISSION		TYPE OF ACTION			
☐ Notice of Intent	☐ Acidize	☐ Deepen	☐ Production (Start/Resume)	☐ Water Shut-Off	
☒ Subsequent Report	☐ Alter Casing	☐ Hydraulic Fracturing	☐ Reclamation	☐ Well Integrity	
☐ Final Abandonment Notice	☐ Casing Repair	☐ New Construction	☐ Recomplete	☒ Other	
	☐ Change Plans	☐ Plug and Abandon	☐ Temporarily Abandon		
	☐ Convert to Injection	☐ Plug Back	☐ Water Disposal		

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has detennined that the site is ready for final inspection.)

Enduring Resources performed a workover for wellbore cleanout and gas lift re-installation. No changes to production tubing string design. An updated well schematic is attached.

EOT: 5,256 MD
Packer: None
GLVs: 4336, 3810, 3158, 2370
Orifice Valve: None End of Tubing
Job Start: 1.3.2023
Job End: 1.9.2023

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed) HEATHER HUNTINGTON / Ph: (505) 636-9751		Title Permitting Technician	
Signature		Date 01/30/2023	

THE SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by KENNETH G RENNICK / Ph: (505) 564-7742 / Accepted		Title Petroleum Engineer		Date 01/31/2023	
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.		Office FARMINGTON			

Title 18 U.S.C Section 1001 and Title 43 U.S.C Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

WellView®

Wellbore Schematic - Components and Cement

Well Name: GREATER LYBROOK UNIT 761H (fka W LYBROOK)

API/UWI 30-045-38269		County SAN JUAN		State/Province NEW MEXICO		Surface Legal Location Unit (M), SW/4, SW/4, SEC 23, T23N, R09W	
Spud Date 12/29/2021		On Production Date		Abandon Date		Ground Elevation (ft) 6,748.00	
						Original KB Elevation (ft) 6,776.00	
						Total Depth (All) (ftKB) Original Hole - 12,833.0	
						PBDT (All) (ftKB)	

[illegible]

Wellbore Schematic - Components and Cement

Released to Imaging: 12/5/2025 1:35:01 PM

Horizontal, Original Hole, 1/23/2023 8:34:45 AM

Casing Components

Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)
Marker Joint	1	5 1/2	4.89	17.00	P-110	21.57
Casing Joints	43	5 1/2	4.89	17.00	P-110	1,850.40
Toe Sleeve	1	5 1/2	4.89	17.00	P-110	5.10
Marker Joint	1	5 1/2	4.89	17.00	P-110	21.65
Float Collar	1	5 1/2	4.89	17.00	P-110	1.92
Casing Joints	1	5 1/2	4.89	17.00	P-110	43.92
Float Collar	1	5 1/2	4.89	17.00	P-110	1.92
Casing Joints	1	5 1/2	4.89	17.00	P-110	43.65
Float Shoe	1	5 1/2	4.89	17.00	P-110	1.63

Intermediate, 2,677.2ftKB

Casing Description	OD (in)	Wt/Len (lb/ft)	String Grade	Top (ftKB)	Set Depth...	Depth C...	ID (in)
Intermediate	9 5/8	36.00	J-55	30.8	2,677.2		8.92

Casing Components

Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)
Casing Joints	0	9 5/8	8.92	36.00	J-55	0.00
Landing Joint	0	9 5/8	8.92	36.00	J-55	0.00
Casing Hanger	1	9 5/8	8.92	36.00	J-55	3.20
Casing Pup Joint	1	9 5/8	8.92	36.00	J-55	3.00
Casing Joints	65	9 5/8	8.92	36.00	J-55	2,596.98
Float Collar	1	9 5/8	8.92	36.00	J-55	1.35
Casing Joints	1	9 5/8	8.92	36.00	J-55	40.23
Float Shoe	1	9 5/8	8.92	36.00	J-55	1.60

Surface, 388.7ftKB

Casing Description	OD (in)	Wt/Len (lb/ft)	String Grade	Top (ftKB)	Set Depth...	Depth C...	ID (in)
Surface	13 3/8	54.50	J-55	28.0	388.7		12.62

Casing Components

Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)
Casing Joints	8	13 3/8	12.62	54.50	J-55	317.55
Float Collar	1	13 3/8	12.62	54.50	J-55	1.62
Casing Joints	1	13 3/8	12.62	54.50	J-55	39.70
Float Shoe	1	13 3/8	12.62	54.50	J-55	1.84

Cement

Surface Casing Cement, Casing, 12/30/2021 16:00

Description	String	Cementing Start Date	Cementing End Date
Surface Casing Cement	Surface, 388.7ftKB	12/30/2021 16:00	12/30/2021 18:54

Cement Stages

Stg #	Top (ftKB)	Btm (ftKB)	Com
1	28.0	393.0	

Intermediate Casing Cement, Casing, 1/23/2022 17:00

Description	String	Cementing Start Date	Cementing End Date
Intermediate Casing Cement	Intermediate, 2,677.2ftKB	1/23/2022 17:00	1/23/2022 20:00

Cement Stages

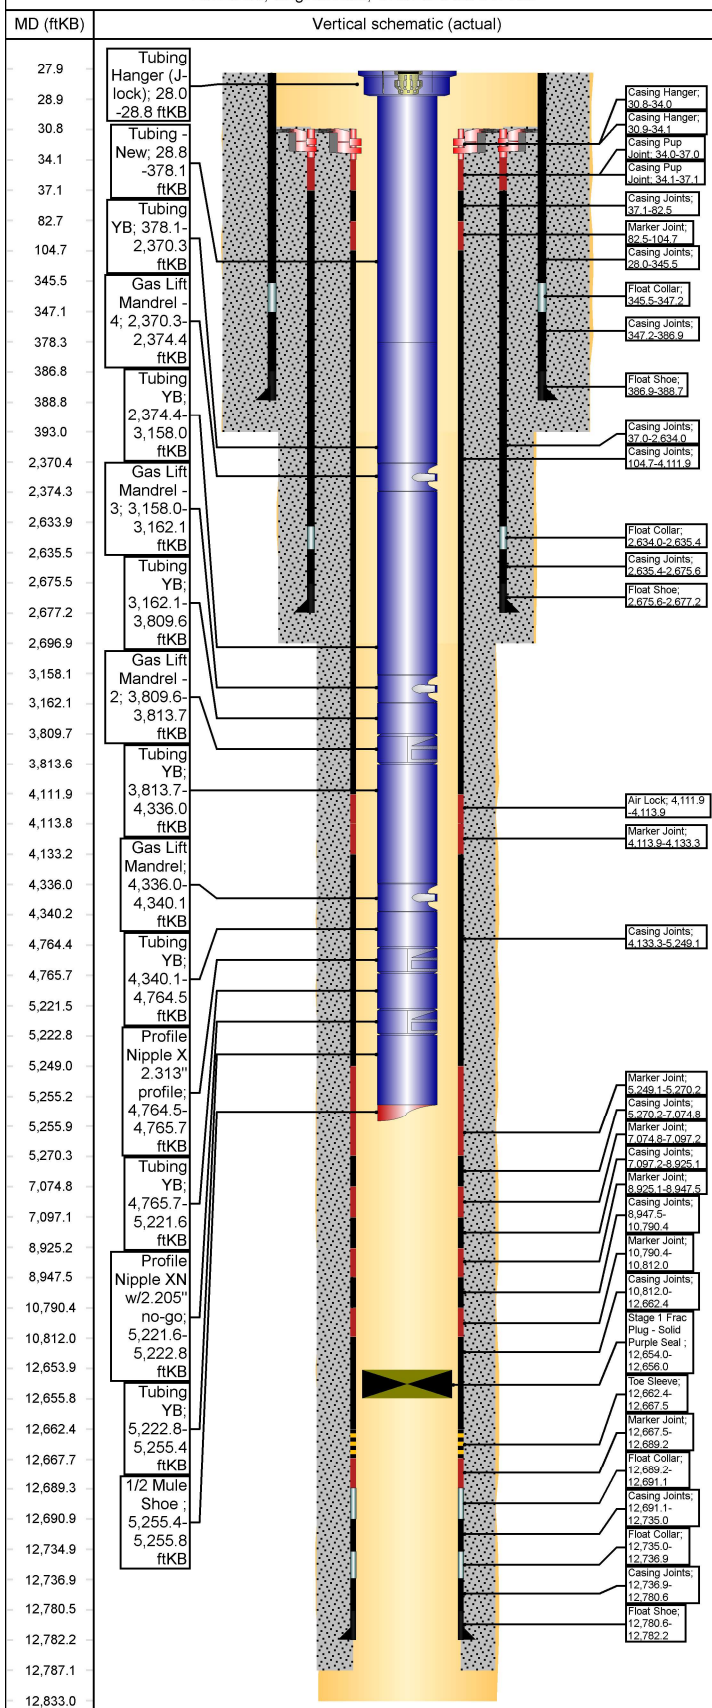
Stg #	Top (ftKB)	Btm (ftKB)	Com
1	30.8	2,697.0	Cement Offline as follows: PJSM with Drake Energy Services. Pressure tested lines to 2500 psi. Pumped 10 bbls FW, 10 bbls D-Mud Breaker, & 10 bbls of FW. Pumped Lead Cement: 193 bbls (506 sx) 90:10 Poz:Type III at 12.5 ppg, 2.14 ft3/sk, 12.05 gal H2O/sk. Pumped Tail Cement: 33 bbls (136 sx) Type III Blend at 14.6 ppg, 1.38 ft3/sk, 6.64 gal H2O/sk. Dropped plug & began displacement. Displaced with 203.6 bbls FW. FCP at 800 psi and plug bumped floats held, bleed 1.0 bbl back. Maintained returns throughout job. Calculated 43 bbls to surface and got 40 bbls of good cement to surface. Top of Lead to surface and top of tail at 2,477 ft MD. Released Rig @ 13:30 1/23/2022 to the W. Lybrook Unit 729 H. (Cement 17:00 Hour,s To 20:00 Hour,s on -1/23/2022)

Page 2/3

Report Printed: 1/23/2023

WellView®**Wellbore Schematic - Components and Cement****Well Name: GREATER LYBROOK UNIT 761H (fka W LYBROOK)**

Horizontal, Original Hole, 1/23/2023 8:34:47 AM

**Cement****Production Casing Cement, Casing, 2/8/2022 21:55**

Description	String	Cementing Start Date	Cementing End Date
Production	Production, 12,782.2ftKB	2/8/2022 21:55	2/9/2022 01:23
Casing Cement			

Cement Stages

Stg #	Top (ftKB)	Btm (ftKB)	Com
1	30.9	12,787.2	Cement Summary: PJSM with American Cementing. Pressure tested lines to 5000 psi. Pumped 60 bbls Intraguard Star @ 11.0 ppg. Pumped Lead Cement: 200 bbls (476 sx) ASTM Type I/II at 12.4 ppg, 2.36 ft³/sk, 13.4 gal H₂O/sk. Pumped Tail Cement: 403.3 bbls (1448 sx) Class G Cement at 13.3 ppg, 1.56 ft³/sk, 7.69 gal H₂O/sk. Washed lines, dropped plug & began displacement. Displaced with 394 bbls FW with cement retarder in 1st 50 bbls. FCP at 1,980 psi and plug bumped at 4.0 bpm to 2900 psi. Bled back 1.0 Bbls and floats held. Pressured up to 2900 psi 3 times bumping plug & pressure bled off each time. Checked floats and floats held. Top of Tail: Calculated 3,937 ft MD. Top of Lead: surface Cement Back 55 BBL, Cement in place at 01:30 on 02/09/2022

Wellbores**Original Hole**

Wellbore Name	Parent Wellbore
Original Hole	Original Hole

Wellbore Sections

Section Des	Size (in)	Act Top (ftKB)	Act Btm (ftKB)
Surface	17 1/2	28.0	393.0
Intermediate	12 1/4	393.0	2,697.0
Production	8 1/2	2,697.0	12,833.0

Sante Fe Main Office
Phone: (505) 476-3441

General Information
Phone: (505) 629-6116

Online Phone Directory
<https://www.emnrd.nm.gov/oed/contact-us>

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 227747

CONDITIONS

Operator: ENDURING RESOURCES, LLC 6300 S Syracuse Way Centennial, CO 80111	OGRID: 372286
	Action Number: 227747
	Action Type: [C-103] Sub. Workover (C-103R)

CONDITIONS

Created By	Condition	Condition Date
andrew.fordyce	Accepted for record.	12/5/2025
