

12/17/03 112 211 PWV 0334147806 5/12/00
 Federal 30-015-05384 1980 FSL 660 FWL 35-8065 WFX-761
 R-2239

Company: Hudson & Hudson		Company Representative: John Smith		Com: 253	
Lease: Puckett A #8		Test Date & Time: 5/16/03			
State: NM	County: Eddy	Elevation:			
Formation: Maljamar Grayburg	Unit:	Section: 24			
Township: 17S	Range: 31E				
Test Crew: David Bump					
TD@		PSTD@ 3894'			
Packer Set @: 3234'		FL			
Casing Size: 4 1/2 J55		Casing Wt:			
Casing Dia:		Casing Set @: 3287'			
Tubing Size: 2 3/8 plastic coated		Tubing Wt:			
Tubing Dia:		Tubing Set @: 3234'			
Perforations From: 3287		To: 3894'			
Time	EIapse Time	Tubing Pressure	Tubing Pressure Less Friction	BHP	Rate BPD
2:20		490			0
2:25		615			60
2:30		630			60
2:35	15	635			60
2:40		760			140
2:45		775			140
2:50	30	780			140
2:55		885			210
3:00		895			210
3:05	45	900			210
3:10		1190			310
3:15		1100			310
3:20	1	1110			310
3:25		1140			410
3:30		1140			410
3:35	1:15	1140			410
3:40		1170			510
3:45		1170			510
3:50	1:30	1170			510
3:55		1220			630
4:00		1220			630
4:05	1:45	1220			630

Test Conducted By: David Bump/Signal Wireline & Testing


Toll Free
866-766-SWAT

Signal Wireline And Testing

KANDAL HUDSON Office
616 TEXAS ST. 505-392-2048
FORT WORTH, TX
76102-4612

817-336-7109

Hudson & Hudson
Puckett A #8
5/16/03

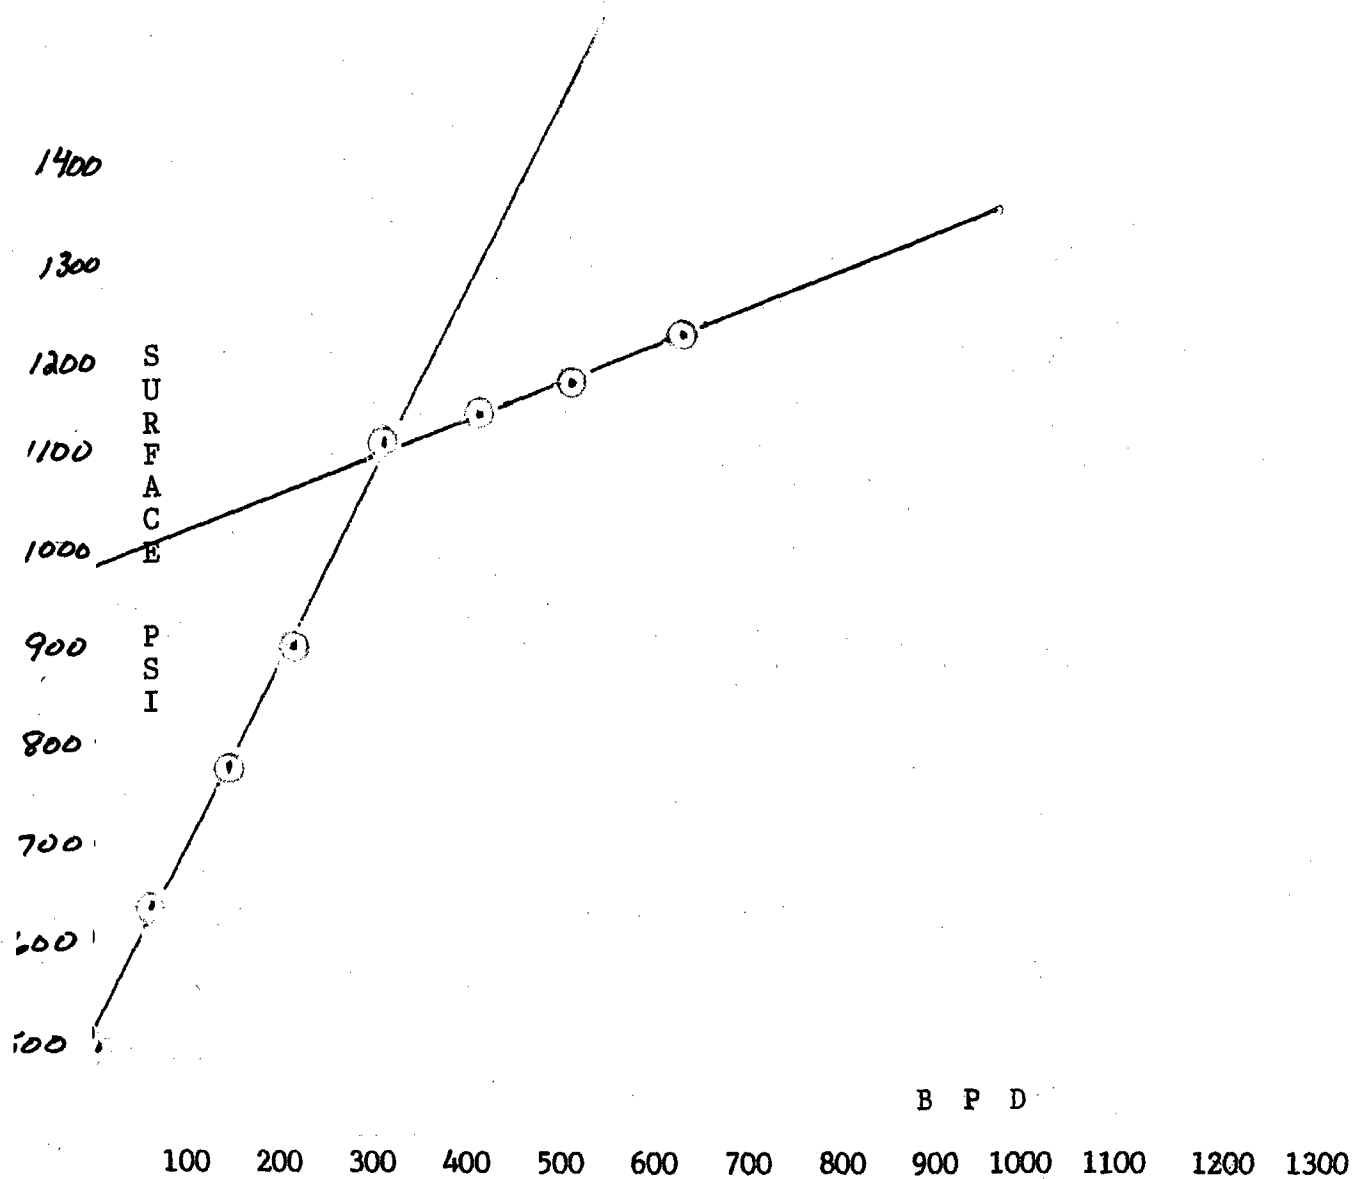

Parting point appears
to be 1100 PSI
