

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED  
OMB No. 1004-0137  
Expires: January 31, 2018

F/P  
(H)

HOBBS OCD  
JUL 10 2019  
RECEIVED

1a. Type of work: ☒ DRILL ☐ REENTER  
1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other  
1c. Type of Completion: ☐ Hydraulic Fracturing ☒ Single Zone ☐ Multiple Zone

5. Lease Serial No.  
NMNM137809  
6. If Indian, Allottee or Tribe Name

7. If Unit or CA Agreement, Name and No.

8. Lease Name and Well No.  
GREEN JACKET FED COM 26 36 29  
101H (325940)

2. Name of Operator  
AMEREDEV OPERATING LLC (372224)

9. API Well No.  
30-025-46204

3a. Address  
5707 Southwest Parkway, Building 1, Suite 275 Austin TX  
3b. Phone No. (include area code)  
(737)300-4700

10. Field and Pool, or Exploratory  
JAC 7 WOLF CAMP WEST NC; WOLF CAMP

4. Location of Well (Report location clearly and in accordance with any State requirements. \*)  
At surface LOT D / 262 FNL / 792 FWL / LAT 32.02078 / LONG -103.29303  
At proposed prod. zone LOT 4 / 50 FSL / 380 FWL / LAT 32.0004449 / LONG -103.2943253

11. Sec., T. R. M. or Blk. and Survey or Area  
SEC 29 / T26S / R36E / NMP

14. Distance in miles and direction from nearest town or post office\*  
10.5 miles

12. County or Parish  
LEA  
13. State  
NM

15. Distance from proposed\* location to nearest property or lease line, ft.  
(Also to nearest drig. unit line, if any)  
262 feet

16. No of acres in lease  
1264.15

17. Spacing Unit dedicated to this well  
467.17

18. Distance from proposed location\* to nearest well, drilling, completed, applied for, on this lease, ft.  
5320 feet

19. Proposed Depth  
12049 feet / 19490 feet

20. BLM/BIA Bond No. in file  
FED: NMB001478

21. Elevations (Show whether DF, KDB, RT, GL, etc.)  
2924 feet

22. Approximate date work will start\*  
09/15/2019

23. Estimated duration  
90 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- |  |   |
|--|---|
| 1. Well plat certified by a registered surveyor.   | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan.  | 5. Operator certification.  |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM.            |

25. Signature (Electronic Submission)	Name (Printed/Typed) Christie Hanna / Ph: (737)300-4723	Date 09/27/2018
--	--	--------------------

Title  
Senior Engineering Technician

Approved by (Signature) (Electronic Submission)	Name (Printed/Typed) Cody Layton / Ph: (575)234-5959	Date 07/05/2019
--	---	--------------------

Title  
Assistant Field Manager Lands & Minerals  
Office  
CARLSBAD

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

GCP Rec 07/10/19

KAC  
07/11/19

APPROVED WITH CONDITIONS  
Approval Date: 07/05/2019

## INSTRUCTIONS

**GENERAL:** This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

**ITEM 1:** If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

**ITEM 4:** Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

**ITEM 14:** Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

**ITEMS 15 AND 18:** If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

**ITEM 22:** Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

**ITEM 24:** If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

## NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48( d) provide that you be furnished the following information in connection with information required by this application.

**AUTHORITY:** 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

**PRINCIPAL PURPOSES:** The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

**ROUTINE USE:** Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

**EFFECT OF NOT PROVIDING INFORMATION:** Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

**BURDEN HOURS STATEMENT:** Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

## **Additional Operator Remarks**

### **Location of Well**

1. SHL: LOT D / 262 FNL / 792 FWL / TWSP: 26S / RANGE: 36E / SECTION: 29 / LAT: 32.02078 / LONG: -103.29303 ( TVD: 0 feet, MD: 0 feet )

PPP: NWNW / 214 FNL / 412 FWL / TWSP: 26S / RANGE: 36E / SECTION: 29 / LAT: 32.02122 / LONG: -103.29436 ( TVD: 11916 feet, MD: 12003 feet )

BHL: LOT 4 / 50 FSL / 380 FWL / TWSP: 26S / RANGE: 36E / SECTION: 32 / LAT: 32.0004449 / LONG: -103.2943253 ( TVD: 12049 feet, MD: 19490 feet )

### **BLM Point of Contact**

Name: Linda (Cathleen) Queen

Title: Project Manager-Carlsbad Field Office

Phone: 5752345962

Email: cqueen@blm.gov

---

(Form 3160-3, page 3)

**Approval Date: 07/05/2019**

## **Review and Appeal Rights**

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

# PECOS DISTRICT

## DRILLING CONDITIONS OF APPROVAL

<b>OPERATOR'S NAME:</b>	AMEREDEV OPERATING LLC
<b>LEASE NO.:</b>	NMNM137809
<b>WELL NAME &amp; NO.:</b>	101H – GREEN JACKET FED COM 26 36 29
<b>SURFACE HOLE FOOTAGE:</b>	262'/S & 792'/W
<b>BOTTOM HOLE FOOTAGE:</b>	50'/N & 380'/W
<b>LOCATION:</b>	SECTION 29, T26S, R36E, NMPM
<b>COUNTY:</b>	LEA

COA

H2S	<input type="radio"/> Yes	<input checked="" type="radio"/> No	
Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	<input type="radio"/> Both
Other	<input type="checkbox"/> 4 String Area	<input checked="" type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP

### A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

### B. CASING

#### Primary Casing Design:

1. The 13-3/8 inch surface casing shall be set at approximately **1109** feet (a minimum of 25 feet into the Rustler Anhydrite and above the salt) and cemented to the surface.
  - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
  - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
  - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours

after bringing cement to surface or 500 pounds compressive strength, whichever is greater.

- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

❖ **Special Capitan Reef requirements.** If lost circulation (50% or greater) occurs below the Base of the Salt, the operator shall do the following:

- Switch to fresh water mud to protect the Capitan Reef and use fresh water mud until setting the intermediate casing. The appropriate BLM office is to be notified for a PET to witness the switch to fresh water.
- Daily drilling reports from the Base of the Salt to the setting of the intermediate casing are to be submitted to the BLM CFO engineering staff via e-mail by 0800 hours each morning. Any lost circulation encountered is to be recorded on these drilling reports. The daily drilling report should show mud volume per shift/tour. Failure to submit these reports will result in an Incidence of Non-Compliance being issued for failure to comply with the Conditions of Approval. If not already planned, the operator shall run a caliper survey for the intermediate well bore and submit to the appropriate BLM office.

**Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.**

2. The minimum required fill of cement behind the 9-5/8 inch 1<sup>st</sup> intermediate casing is:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
  - b. Second stage above DV tool:
    - Cement to surface. If cement does not circulate, contact the appropriate BLM office. **Excess calculates to 22% - additional cement might be required.**
3. The minimum required fill of cement behind the 5-1/2 inch production casing is:
- Cement should tie-back at least 50 feet on top of Capitan Reef Top. Operator shall provide method of verification. **Excess calculates to 16% - additional cement might be required.**

### **Alternate Casing Design:**

**2<sup>nd</sup> Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.**

3. The minimum required fill of cement behind the 7-5/8 inch 2<sup>nd</sup> intermediate casing is:
  - Cement to surface. If cement does not circulate see B.1.a, c-d above. Excess calculates to 14% - additional cement might be required.

**In the case of lost circulation, operator has proposed to pump down 9 5/8" X 7 5/8" annulus. Operator must run a CBL from TD of the 7 5/8" casing to surface. Submit results to the BLM.**

**Pilot hole is required to have a plug at the bottom of the hole. If two plugs are set, the BLM is to be contacted (575-361-2822) prior to tag of bottom plug, which must be a minimum of 200' in length. Operator can set one plug from bottom of pilot hole to kick-off point and save the WOC time for tagging the first plug. Note plug tops on subsequent drilling report.**

4. The minimum required fill of cement behind the 5-1/2 inch production casing is:
  - Cement should tie-back at least 50 feet on top of Capitan Reef Top. Operator shall provide method of verification.

### **C. PRESSURE CONTROL**

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).'
- 2.

#### **Option 1:**

Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 10,000 (10M) psi.

#### **Option 2:**

**Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 10,000 (10M) psi.**

- a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
- b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- c. Manufacturer representative shall install the test plug for the initial BOP test.
- d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
- e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

**Variance approved to use a 5M annular. The annular must be tested to full working pressure (5000 psi.)**

#### **D. SPECIAL REQUIREMENT(S)**

##### **Communitization Agreement**

- The operator will submit a Communitization Agreement to the Carlsbad Field Office, 620 E Greene St. Carlsbad, New Mexico 88220, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.



## GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Chaves and Roosevelt Counties  
Call the Roswell Field Office, 2909 West Second St., Roswell NM 88201.  
During office hours call (575) 627-0272.  
After office hours call (575)

☒ Eddy County  
Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,  
(575) 361-2822

☒ Lea County  
Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)  
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
  - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
  - b. When the operator proposes to set surface casing with Spudder Rig
    - Notify the BLM when moving in and removing the Spudder Rig.
    - Notify the BLM when moving in the 2<sup>nd</sup> Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
    - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log (one log per well pad is acceptable) run from TD to surface (horizontal well – vertical portion of hole) shall

be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

#### A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.

7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

#### B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
  - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
  - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
  - c. Manufacturer representative shall install the test plug for the initial BOP test.
  - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
  - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.

- a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
- c. The tests shall be done by an independent service company utilizing a test plug. The results of the test shall be reported to the appropriate BLM office.
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes. This test shall be performed prior to the test at full stack pressure.
- g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

### **C. DRILLING MUD**

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

### **D. WASTE MATERIAL AND FLUIDS**

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

#### **Waste Minimization Plan (WMP)**

In the interest of resource development, submission of additional well gas capture development plan information is deferred but may be required by the BLM Authorized Officer at a later date.

**NMK6242019**

**PECOS DISTRICT  
SURFACE USE  
CONDITIONS OF APPROVAL**

**Green Jacket Federal Com 26 36 29 101H  
Green Jacket Federal Com 26 36 29 111H  
Green Jacket Federal Com 26 36 29 121H**

**Lease Number NMNM137809  
Ameredev Operating LLC**

**TABLE OF CONTENTS**

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
  - Wildlife**
- ☐ **Construction**
  - Notification
  - Topsoil
  - Closed Loop System
  - Federal Mineral Material Pits
  - Well Pads
  - Roads
- ☐ **Road Section Diagram**
- ☐ **Production (Post Drilling)**
  - Well Structures & Facilities
  - Pipelines
  - Electric Lines
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**

## **I. GENERAL PROVISIONS**

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

## **II. PERMIT EXPIRATION**

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

## **III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES**

Any cultural and/or paleontological resource discovered by the operator or by any person working on the operator's behalf shall immediately report such findings to the Authorized Officer. The operator is fully accountable for the actions of their contractors and subcontractors. The operator shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery shall be made by the Authorized Officer to determine the appropriate actions that shall be required to prevent the loss of significant cultural or scientific values of the discovery. The operator shall be held responsible for the cost of the proper mitigation measures that the Authorized Officer assesses after consultation with the operator on the evaluation and decisions of the discovery. Any unauthorized collection or disturbance of cultural or paleontological resources may result in a shutdown order by the Authorized Officer.

## **IV. NOXIOUS WEEDS**

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

## **V. SPECIAL REQUIREMENT(S)**

### **Avian Power line Protection**

Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006. The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all power line structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. The holder without liability or expense shall make such modifications and/or additions to the United States.



## **VI. CONSTRUCTION**

### **A. NOTIFICATION**

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

### **B. TOPSOIL**

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

### **C. CLOSED LOOP SYSTEM**

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

### **D. FEDERAL MINERAL MATERIALS PIT**

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

### **E. WELL PAD SURFACING**

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

### **F. EXCLOSURE FENCING (CELLARS & PITS)**

**Exclosure Fencing**

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

**G. ON LEASE ACCESS ROADS****Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

**Surfacing**

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

**Crowning**

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

**Ditching**

Ditching shall be required on both sides of the road.

**Turnouts**


Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

**Drainage**

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill out sloping and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

#### **Cross Section of a Typical Lead-off Ditch**



All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

#### **Formula for Spacing Interval of Lead-off Ditches**

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

#### **Cattle guards**

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

#### **Fence Requirement**

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

#### **Public Access**

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

### Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes

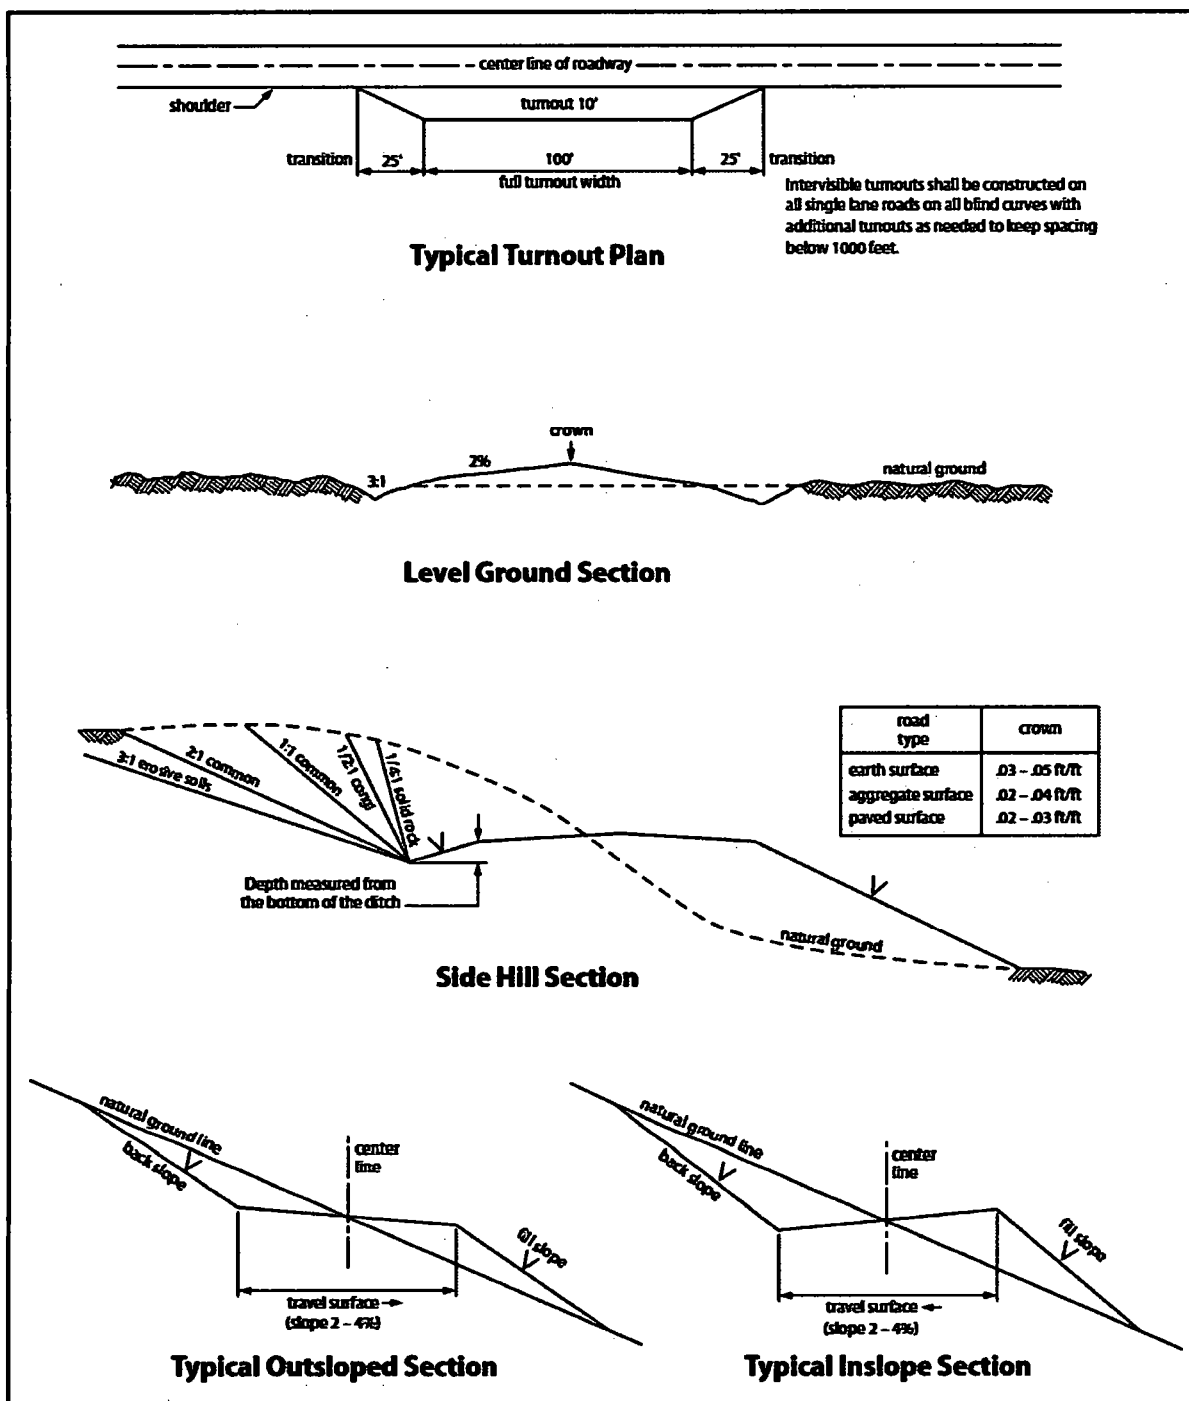


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

## **VII. PRODUCTION (POST DRILLING)**

### **A. WELL STRUCTURES & FACILITIES**

#### **Placement of Production Facilities**

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

#### **Exclosure Netting (Open-top Tanks)**

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

#### **Chemical and Fuel Secondary Containment and Exclosure Screening**

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

#### **Open-Vent Exhaust Stack Exclosures**

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

#### **Containment Structures**

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

#### **Painting Requirement**

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

#### **B. PIPELINES**

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.
4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting

Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.

5. All construction and maintenance activity will be confined to the authorized right-of-way.
6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.
7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:
- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 30 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
  - Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
  - The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)
8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.
9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.
10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.
11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.



12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- |  |  |
|--|--|
| <input type="checkbox"/> seed mixture 1            | <input type="checkbox"/> seed mixture 3          |
| <input checked="" type="checkbox"/> seed mixture 2 | <input type="checkbox"/> seed mixture 4          |
| <input type="checkbox"/> seed mixture 2/LPC        | <input type="checkbox"/> Aplomado Falcon Mixture |

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural and/or paleontological resources (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

17. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

18. Escape Ramps - The operator will construct and maintain pipeline/utility trenches [that are not otherwise fenced, screened, or netted] to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps,

ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.
- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

### **C. ELECTRIC LINES**

**A copy of the grant and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.**

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.
4. There will be no clearing or blading of the right-of-way unless otherwise agreed to in writing by the Authorized Officer.

5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the holder without liability or expense to the United States.

Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.

6. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

7. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.

8. Upon cancellation, relinquishment, or expiration of this grant, the holder shall comply with those abandonment procedures as prescribed by the Authorized Officer.

9. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this grant, whichever comes first. This will not apply where the power line extends service to an active, adjoining facility or facilities.

10. Any cultural and/or paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

11. Special Stipulations:

- For reclamation remove poles, lines, transformer, etc. and dispose of properly.
- Fill in any holes from the poles removed.

## **VIII. INTERIM RECLAMATION**

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

## **IX. FINAL ABANDONMENT & RECLAMATION**

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

#### Seed Mixture 2, for Sandy Sites

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)\* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law (s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed\* per acre:

<u>Species</u>	<u>lb/acre</u>
Sand dropseed ( <i>Sporobolus cryptandrus</i> )	1.0
Sand love grass ( <i>Eragrostis trichodes</i> )	1.0
Plains bristlegrass ( <i>Setaria macrostachya</i> )	2.0

\*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed



U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## Operator Certification Data Report

07/08/2019

### Operator Certification

*I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.*

**NAME:** Christie Hanna

**Signed on:** 05/16/2019

**Title:** Senior Engineering Technician

**Street Address:** 5707 Southwest Parkway, Building 1, Suite 275

**City:** Austin

**State:** TX

**Zip:** 78735

**Phone:** (737)300-4723

**Email address:** channa@ameredev.com

### Field Representative

**Representative Name:** ZACHARY BOYD

**Street Address:** 5707 SOUTHWEST PARKWAY, BLDG 1, STE. 275

**City:** AUSTIN

**State:** TX

**Zip:** 78735

**Phone:** (737)300-4725

**Email address:** zboyd@ameredev.com



U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## Application Data Report

07/08/2019

APD ID: 10400034498

Submission Date: 09/27/2018

Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

Well Type: OIL WELL

Well Work Type: Drill



[Show Final Text](#)

### Section 1 - General

APD ID: 10400034498

Tie to previous NOS? 10400032176 Submission Date: 09/27/2018

BLM Office: CARLSBAD

User: Christie Hanna

Title: Senior Engineering Technician

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMNM137809

Lease Acres: 1264.15

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? NO

Federal or Indian agreement:

Agreement number:

Agreement name:

Keep application confidential? NO

Permitting Agent? NO

APD Operator: AMEREDEV OPERATING LLC

Operator letter of designation:

### Operator Info

Operator Organization Name: AMEREDEV OPERATING LLC

Operator Address: 5707 Southwest Parkway, Building 1, Suite 275

Zip: 78735

Operator PO Box:

Operator City: Austin

State: TX

Operator Phone: (737)300-4700

Operator Internet Address:

### Section 2 - Well Information

Well in Master Development Plan? NO

Master Development Plan name:

Well in Master SUPO? NO

Master SUPO name:

Well in Master Drilling Plan? NO

Master Drilling Plan name:

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

Well API Number:

Field/Pool or Exploratory? Field and Pool

Field Name: GREEN JACKET FED COM 26 36 29  
Pool Name: GREEN JACKET FED COM 26 36 29  
Well

Is the proposed well in an area containing other mineral resources? USEABLE WATER,NATURAL GAS,CO2,OIL

Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

Describe other minerals:

Is the proposed well in a Helium production area? N Use Existing Well Pad? NO New surface disturbance?

Type of Well Pad: MULTIPLE WELL

Multiple Well Pad? YES Number of Legs: 1

Well Class: HORIZONTAL

Number of Legs: 1

Well Work Type: Drill

Well Type: OIL WELL

Describe Well Type:

Well sub-Type: INFILL

Describe sub-type:

Distance to town: 10.5 Miles

Distance to nearest well: 5320 FT

Distance to town by road: 232 FT

Estimated well spacing on 1000 ft x 1000 ft block: 467.17 Acres

Well plat: JEFF\_20190516153041.pdf

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_BLM\_LEASES\_REV\_20190516153125.pdf

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_EXHIBIT\_2A\_\_2B\_REV\_20190516153127.pdf

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_VICINITY\_MAP\_REV\_20190516153127.pdf

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_GAS\_CAPTURE\_PLAN\_20190516153137.pdf

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_C\_102\_REV\_SIG\_20190516153423.pdf

Well work start Date: 09/15/2019

Duration: 90 DAYS

### Section 3 - Well Location Table

Survey Type: RECTANGULAR

Describe Survey Type:

Datum: NAD83

Vertical Datum: NAVD88

Survey number: 11401

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
SHL Leg #1	262	FNL	792	FWL	26S	36E	29	Lot D	32.02073	-103.20303	LEA	NEW MEXI CO	NEW MEXI CO		NMNM 137809	2924	0	0




Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
KOP Leg #1		FNL	76	FWL	26S	36E		Aliquot NWN W	36.1474	105.0919	LEA	NEW MEXI CO	NEW MEXI CO		NMNM 137809	3576	1.52	11300
PPP Leg #1		FNL	100	FWL	26S	36E		Aliquot NWN W	36.1474	105.0919	LEA	NEW MEXI CO	NEW MEXI CO		NMNM 137809	3999	1.03	11913
EXIT Leg #1		FSL	100	FWL	26S	36E		Lot 4	36.1474	105.0919	LEA	NEW MEXI CO	NEW MEXI CO		STATE	3915	1.02	12010
BHL Leg #1		FSL	100	FWL	26S	36E		Lot 4	36.1474	105.0919	LEA	NEW MEXI CO	NEW MEXI CO		STATE	3915	1.01	12040


Ameredev Operating, LLC  
Green Jacket Fed Com 26 36 29 101H  
Section 29, Township 26S, Range 36E  
Lea County, New Mexico

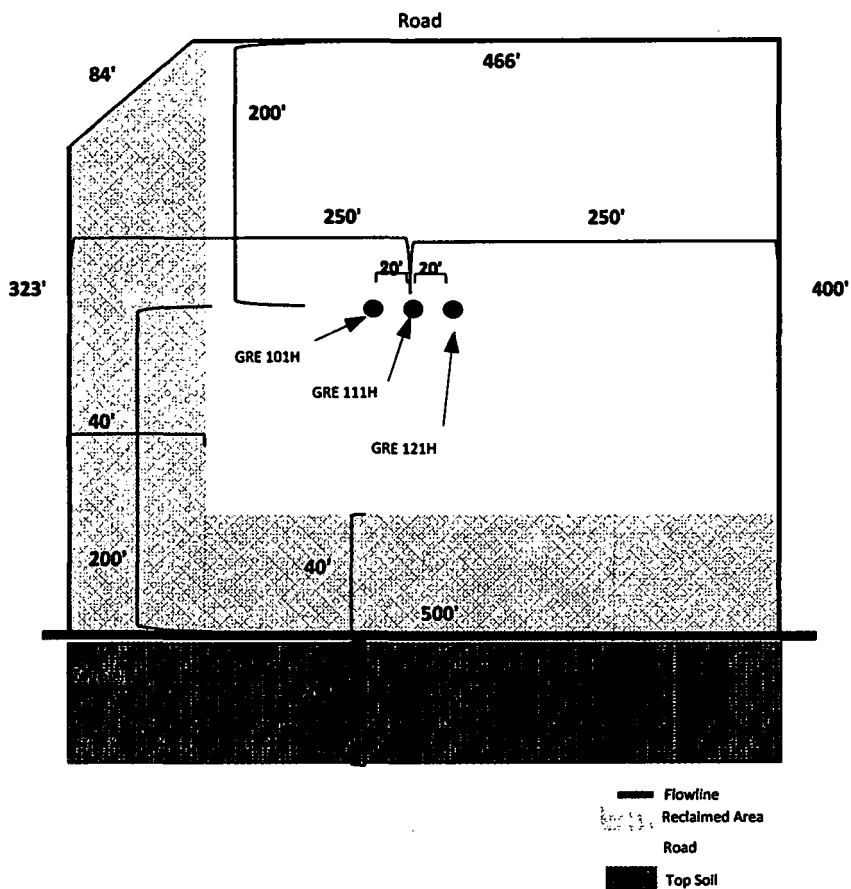

Green Jacket Fed Com 26 36 29 101H SHL: 26S 36E 262' FNL 752' FWL  
Green Jacket Fed Com 26 36 29 111H SHL: 26S 36E 262' FNL 772' FWL  
Green Jacket Fed Com 26 36 29 121H SHL: 26S 36E 262' FNL 792' FWL

**Exhibit 3 – Well Site Diagram**

# LOCATION & ELEVATION VERIFICATION MAP

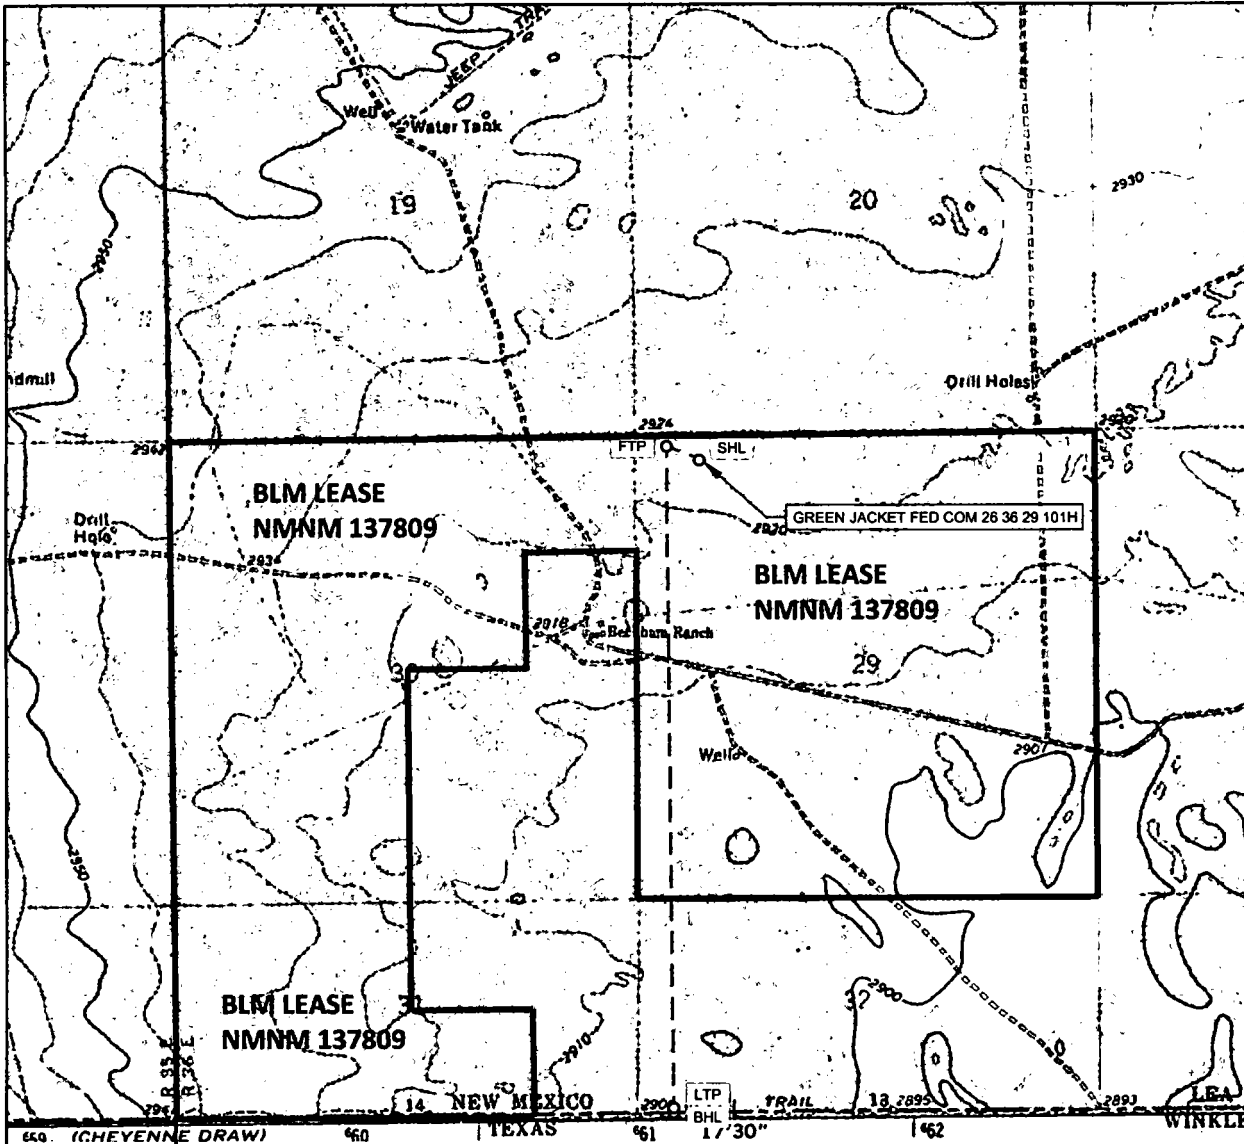

## AMEREDEV

AMEREDEV OPERATING, LLC

LEASE NAME & WELL NO.: GREEN JACKET FED COM 26 36 29 101H

SECTION 29 TWP 26-S RGE 36-E SURVEY N.M.P.M.  
 COUNTY LEA STATE NM ELEVATION 2924'  
 DESCRIPTION 262' FNL & 792' FWL

LATITUDE N 32.0207848 LONGITUDE W 103.2930300



SCALE: 1" = 2000'  
 0' 1000' 2000'

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY AMEREDEV OPERATING LLC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.



**TOPOGRAPHIC**  
 LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
 TELEPHONE: (432) 682-1653 OR (800) 787-1653 • FAX (432) 682-1743  
 WWW.TOPOGRAPHIC.COM

**AMEREDEV OPERATING, LLC**  
**EXHIBIT 2A**

LEASE NAME & WELL NO.: GREEN JACKET FED COM 26 36 29 101H

SECTION 29 TWP 26-S RGE 36-E SURVEY N.M.P.M.  
COUNTY \_\_\_\_\_ LEA \_\_\_\_\_ STATE \_\_\_\_\_ NM \_\_\_\_\_  
DESCRIPTION \_\_\_\_\_ 262' FNL & 792' FWL \_\_\_\_\_

**DISTANCE & DIRECTION**  
FROM INT. OF NM-205 & NM-128 HEAD SOUTH ON NM-205




# EXHIBIT 2B

## AMEREDEV

AMEREDEV OPERATING, LLC


SECTION 29, TOWNSHIP 26-S, RANGE 36-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

DETAIL VIEW  
SCALE: 1" = 100'  
SECTION LINE

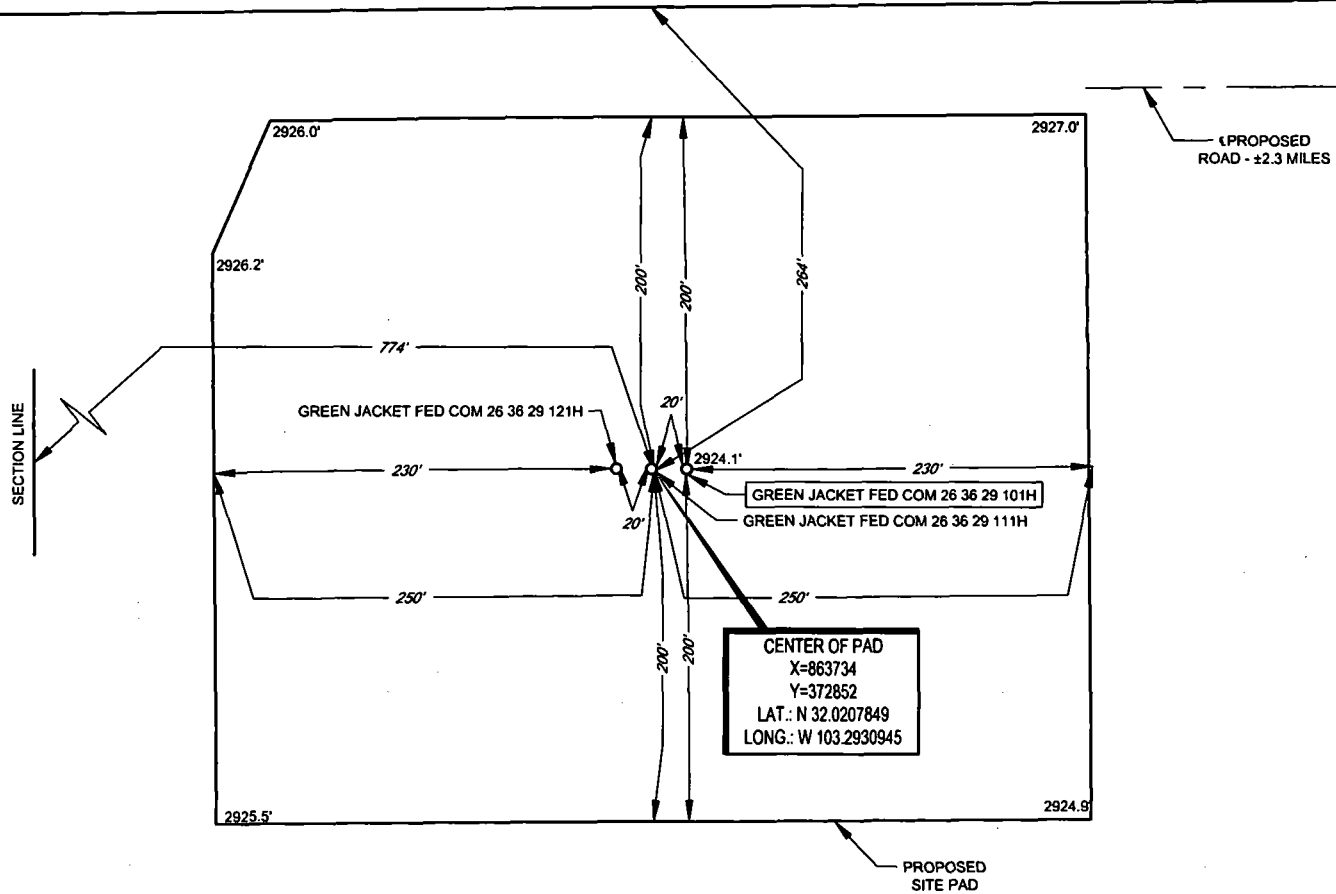

LEASE NAME & WELL NO.: GREEN JACKET FED COM 26 36 29 101H  
101H LATITUDE N 32.0207848 101H LONGITUDE W 103.2930300

CENTER OF PAD IS 264' FNL & 774' FWL



ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID  
BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY  
FEET.

THIS PROPOSED PAD SITE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER  
MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY,  
AND DATA PROVIDED BY AMEREDEV OPERATING LLC. THIS CERTIFICATION IS MADE AND LIMITED TO  
THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS  
SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

ORIGINAL DOCUMENT SIZE: 8.5" X 11"


S:\SURVEY\AMEREDEV\_OPERATING\_LLC\GREEN\_JACKET\_FED\_COM\FINAL\_PRODUCTS\LO\_GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_REV2.DWG 4/26/2019 11:01:00 AM cccan



**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM

# EXHIBIT 2 VICINITY MAP

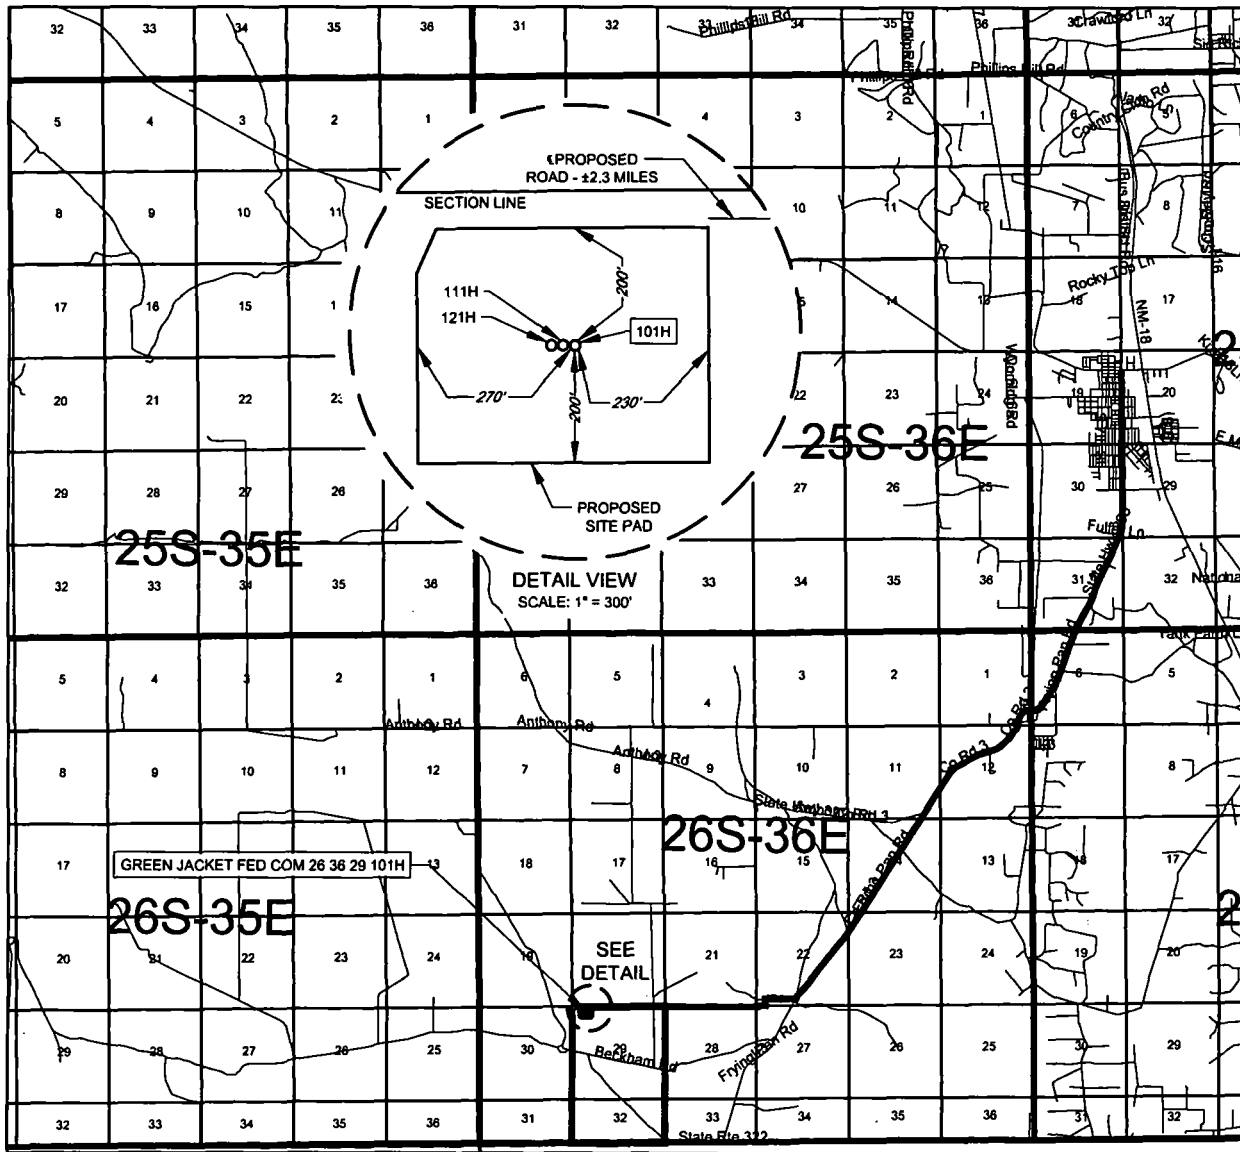

## AMEREDEV

AMEREDEV OPERATING, LLC

LEASE NAME & WELL NO.: GREEN JACKET FED COM 26 36 29 101H

SECTION 29 TWP 26-S RGE 36-E SURVEY N.M.P.M.

COUNTY LEA STATE NM


DESCRIPTION 262' FNL & 792' FWL

### DISTANCE & DIRECTION

FROM INT. OF NM-205 & NM-128, HEAD SOUTH ON NM-205  
±8.0 MILES, THENCE WEST (RIGHT) ON PROPOSED RD. ±2.3  
MILES TO A POINT ±314 FEET NORTHEAST OF THE  
LOCATION.

THIS EASEMENT/SERVITUDE LOCATION SHOWN HEREON HAS BEEN SURVEYED ON THE GROUND UNDER MY SUPERVISION AND PREPARED ACCORDING TO THE EVIDENCE FOUND AT THE TIME OF SURVEY, AND DATA PROVIDED BY AMEREDEV OPERATING LLC. THIS CERTIFICATION IS MADE AND LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE. THIS SURVEY IS CERTIFIED FOR THIS TRANSACTION ONLY.

ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREON ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.



**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
 TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
 2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
 TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
 WWW.TOPOGRAPHIC.COM



U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## Drilling Plan Data Report

07/08/2019

APD ID: 10400034498

Submission Date: 09/27/2018

Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

[Show Final Text](#)

Well Type: OIL WELL

Well Work Type: Drill



### Section 1 - Geologic Formations

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
1	RUSTLER ANHYDRITE	2924	1659	1659	ANHYDRITE	NONE	No
2	SALADO	852	2072	2072	SALT	NONE	No
3	TANSILL	-331	3255	3255	LIMESTONE	NONE	No
4	CAPITAN REEF	-586	3510	3510	LIMESTONE	USEABLE WATER	No
5	LAMAR	-2056	4980	4980	LIMESTONE	NONE	No
6	BELL CANYON	-2127	5051	5051	SANDSTONE	NATURAL GAS,OIL	No
7	BRUSHY CANYON	-4356	7280	7280	SANDSTONE	NATURAL GAS,OIL	No
8	BONE SPRING LIME	-5536	8460	8460	LIMESTONE	NONE	No
9	BONE SPRING 1ST	-6960	9884	9884	SANDSTONE	NATURAL GAS,OIL	No
10	BONE SPRING 2ND	-7552	10476	10476	SANDSTONE	NATURAL GAS,OIL	No
11	BONE SPRING 3RD	-8114	11038	11038	LIMESTONE	NATURAL GAS,OIL	No
12	BONE SPRING 3RD	-8721	11645	11645	SANDSTONE	NATURAL GAS,OIL	No
13	WOLFCAMP	-8975	11899	11899	SHALE	NATURAL GAS,OIL	Yes

### Section 2 - Blowout Prevention

Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

Pressure Rating (PSI): 10M

Rating Depth: 15000



Requesting Variance? YES



Choke Diagram Attachment:

10M\_Choke\_Manifold\_REV\_20190516154143.pdf

BOP Diagram Attachment:

5M\_Annular\_Preventer\_Variance\_and\_Well\_Control\_Plan\_20190516154152.pdf

5M\_BOP\_System\_20190516154153.pdf

Pressure\_Control\_Plan\_Single\_Well\_MB4\_3String\_Big\_Hole\_BLM\_20190516154153.pdf

4\_String\_MB\_Ameredev\_Wellhead\_Drawing\_net\_REV\_20190516154206.pdf

### Section 3 - Casing

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE																					
2	INTERMEDIATE																					
3	PRODUCTION																					

Casing Attachments



**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

#### Casing Attachments

---

**Casing ID:** 1      **String Type:** SURFACE

**Inspection Document:**

**Spec Document:**

**Tapered String Spec:**

**Casing Design Assumptions and Worksheet(s):**

13.375\_68.00\_\_J55\_BTC\_20190516154319.pdf

Green\_Jacket\_Fed\_Com\_26\_36\_29\_101H\_\_Wellbore\_Diagram\_and\_CDA\_20190516154330.pdf

---

**Casing ID:** 2      **String Type:** INTERMEDIATE

**Inspection Document:**

**Spec Document:**

**Tapered String Spec:**

**Casing Design Assumptions and Worksheet(s):**

Green\_Jacket\_Fed\_Com\_26\_36\_29\_101H\_\_Wellbore\_Diagram\_and\_CDA\_20190516154430.pdf

9.625\_40\_SeAH80HC\_4100\_Collapse\_20190516154439.pdf

---

**Casing ID:** 3      **String Type:** PRODUCTION

**Inspection Document:**

**Spec Document:**

**Tapered String Spec:**

**Casing Design Assumptions and Worksheet(s):**

5.50\_20\_USS\_P110\_HC\_BTC\_API\_20190516154806.pdf

Green\_Jacket\_Fed\_Com\_26\_36\_29\_101H\_\_Wellbore\_Diagram\_and\_CDA\_20190516154825.pdf

---

Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

#### Section 4 - Cement

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
101H-001	Lead		0	100	500	1.76	1.76	100	0	100	100
101H-002	Tail		100	100	500						
101H-003	Lead		0	100	500	2.47	2.47	100	0	100	100
101H-004	Tail		100	100	500						
101H-005	Lead		0	100	500	2.47	2.47	100	0	100	100
101H-006	Tail		100	100	500						
101H-007	Lead		0	100	500	1.34	1.34	100	0	100	100

#### Section 5 - Circulating Medium

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

Describe what will be on location to control well or mitigate other conditions: All necessary supplies (e.g. bentonite, cedar bark) for fluid control will be on site.

Describe the mud monitoring system utilized: An electronic pit volume totalizer (PVT) will be utilized on the circulating system to monitor pit volume, flow rate, pump pressure, and pump rate.

#### Circulating Medium Table

**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	1784	WATER-BASED MUD	8.4	8.6							
1784	1116 3	OTHER : Diesel Brine Emulsion	8.5	9.4							
1116 3	1204 9	OIL-BASED MUD	10.5	12.5							

### Section 6 - Test, Logging, Coring

**List of production tests including testing procedures, equipment and safety measures:**

A directional survey, measurement while drilling and a mudlog/geologic lithology log will all be run from surface to TD.

**List of open and cased hole logs run in the well:**

DS,MWD,MUDLOG

**Coring operation description for the well:**

No coring will be done on this well.

### Section 7 - Pressure

**Anticipated Bottom Hole Pressure:** 5000

**Anticipated Surface Pressure:** 2349.21

**Anticipated Bottom Hole Temperature(F):** 160

**Anticipated abnormal pressures, temperatures, or potential geologic hazards?** NO

**Describe:**

**Contingency Plans geohazards description:**

**Contingency Plans geohazards attachment:**

**Hydrogen Sulfide drilling operations plan required?** YES

**Hydrogen sulfide drilling operations plan:**

H2S\_Plan\_20180924122653.pdf

**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

## Section 8 - Other Information

### Proposed horizontal/directional/multi-lateral plan submission:

GJ101\_DR\_20190516155628.pdf

GJ101\_LLR\_20190516155629.pdf

5M\_Annular\_Preventer\_Variance\_and\_Well\_Control\_Plan\_20190516155718.pdf

Pressure\_Control\_Plan\_Single\_Well\_MB4\_3String\_Big\_Hole\_BLM\_20190516155718.pdf

### Other proposed operations facets description:

4-STRING CONTINGENCY PLAN ATTACHED



### Other proposed operations facets attachment:

CAPITAN\_PROTECTION\_CONTINGENCY\_PLAN\_20190516155817.pdf


### Other Variance attachment:

R616\_\_CoC\_for\_hoses\_12\_18\_17\_20190516155905.pdf




Requested\_Exceptions\_\_3\_String\_Revised\_01312019\_20190516155905.pdf

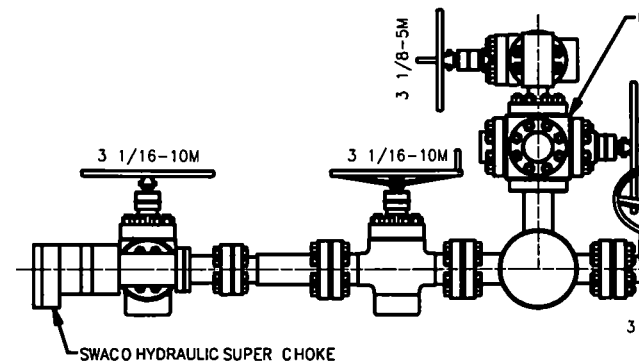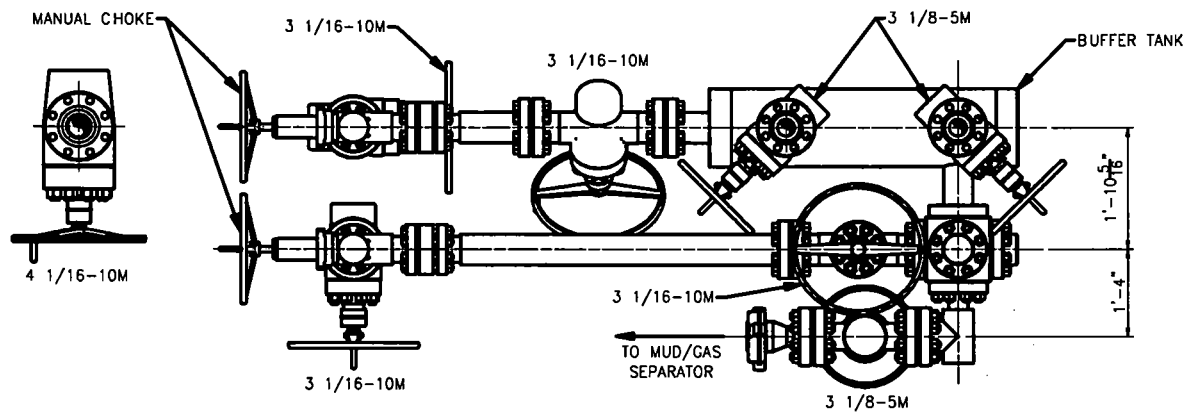

VIEW A-A

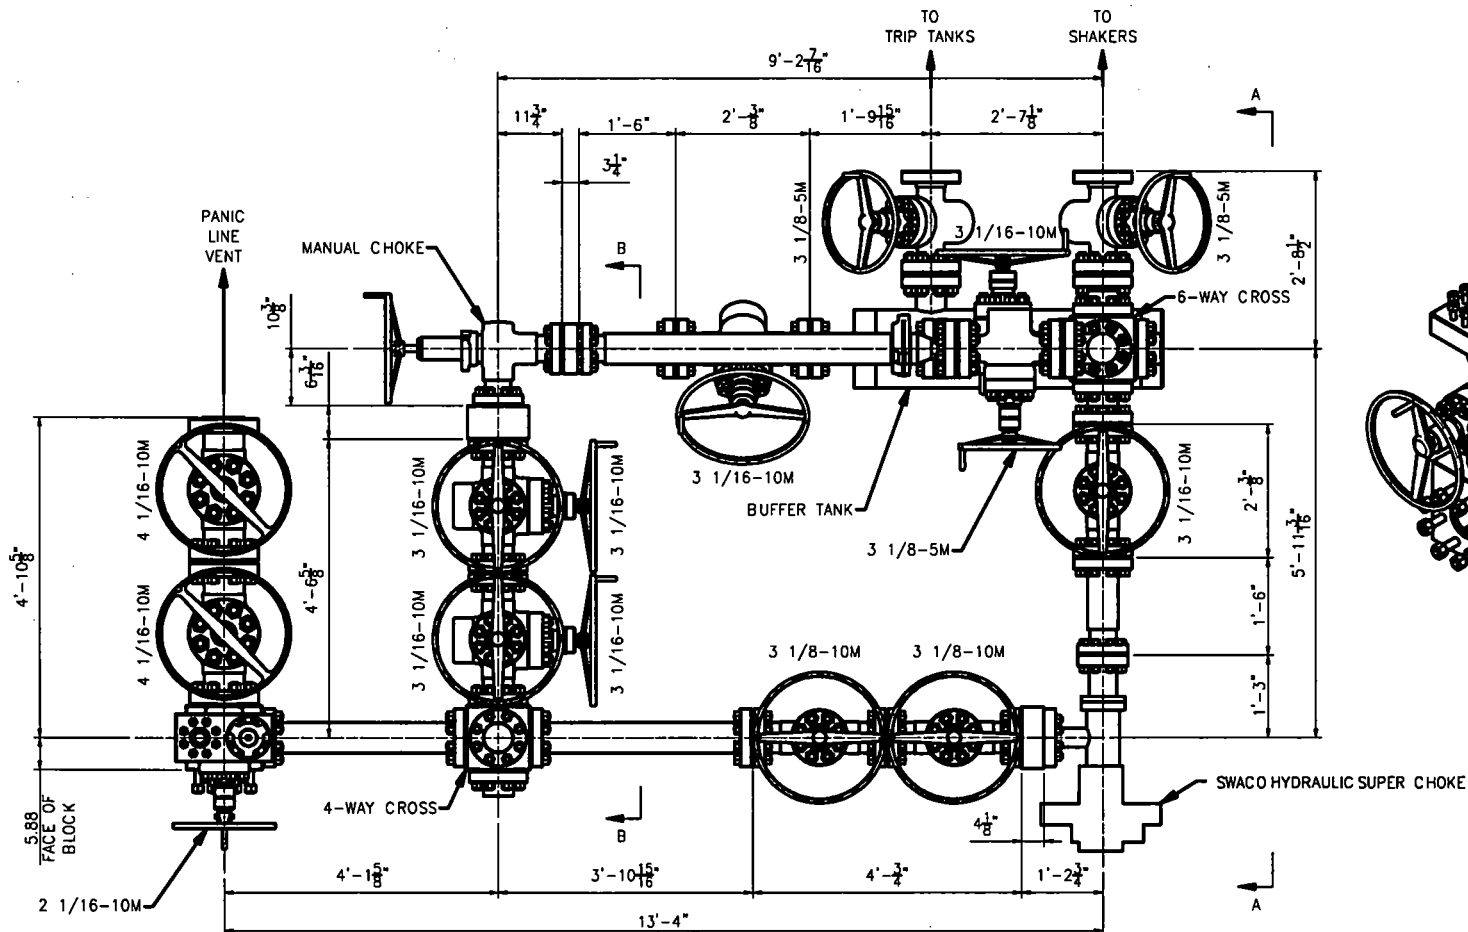

PLAN VIEW

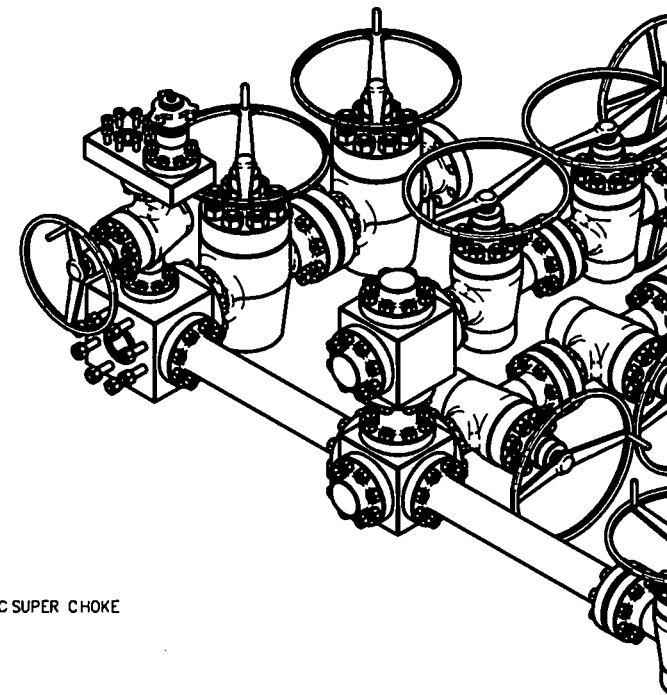

# 5M Annular Preventer Variance Request and Well Control Procedures

Note: A copy of the Well Control Plan must be available at multiple locations on the rig for review by rig personnel, as well as review by the BLM PET/PE, and a copy must be maintained on the rig floor.

## Dual Isolation Design for 5M Annular Exception

Ameredev will utilize 13-5/8" 10M (5M Annular) BOPE System consisting of:

- 13-5/8" 5M Annular
- 13-5/8" 10M Upper Pipe Rams
  - 3-1/2" – 5-1/2" Variable Bore Ram
- 13-5/8" 10M Blind Rams
- 13-5/8" 10M Drilling Spool /w 2 - 4" 10M Outlets Double 10M Isolation Valves
- 13-5/8" 10M Lower Blind Rams
  - 3-1/2" – 5-1/2" Variable Bore Ram

All drilling components and casing associated to exposure > 5000 psi BHP requiring a 10M system will have a double isolation (secondary barrier) below the 5M Annular that would provide a barrier to flow. The mud system will always be primary barrier, it will be maintained by adjusting values based on tourly mud tests and monitoring a PVT System to maintain static wellbore conditions, displacement procedures will be followed and recorded on daily drilling reports during tripping operations. Surge and swab pressure values will be calculated and maintained and static flow check will be monitored at previous casing shoe and verified static well conditions prior to tripping out of hole and again prior to pulling last joint of drill pipe through BOPE. The below table, documents that two barriers to flow can be maintained at all times, independent of the rating of the annular preventer.

Drill Components	Size	Primary Barrier	Secondary Barrier	Third Barrier
Drillpipe	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
HWDP Drillpipe	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
Drill Collars	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
Production Casing	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
Open Hole	13-5/8	Drilling Fluid	Blind Rams	

All Drilling Components in 10M Environment will have OD that will allow full Operational RATED WORKING PRESSURE for system design. Kill line with minimum 2" ID will be available outside substructure with 10M Check Valve for OOH Kill Operations

# Well Control Procedures

Proper well control procedures are dependent to differentiating well conditions, to cover the basic well control operations there are will be standard drilling ahead, tripping pipe, tripping BHA, running casing, and pipe out of the hole/open hole scenarios that will be defined by procedures below. Initial Shut In Pressure can be taken against the Uppermost BOPE component the 5M Annular, pressure control can be transferred from the lesser 5M Annular to the 10M Upper Pipe Rams if needed. Shut In Pressures may be equal to or less than the Rated Working Pressure but at no time will the pressure on the annular preventer exceed the Rated Working Pressure of the annular. The annular will be tested to 5,000 psi. This will be the Rated Working Pressure of the annular preventer. All scenarios will be written such as shut in will be performed by closing the 10,000 psi Upper Pipe Rams for faster Accumulator pressure recovery to allow safer reaction to controlling wellbore pressure.

## Shutting In While Drilling

1. Sound alarm signaling well control event to Rig Crew
2. Space out drill string to allow FOSV installation
3. Shut down pumps
4. Shut in Upper Pipe Rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
5. Install open, full open safety valve and close valve, Close Chokes
6. Verify well is shut-in and flow has stopped
7. Notify supervisory personnel
8. Record data (SIDP, SICP, Pit Gain, and Time)
9. Hold pre-job safety meeting and discuss kill procedure

## Shutting In While Tripping

1. Sound alarm signaling well control event to Rig Crew
2. Space out drill string to allow FOSV installation
3. Shut in Upper Pipe Rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
4. Install open, full open safety valve and close valve, Close Chokes
5. Verify well is shut-in and flow has stopped
6. Notify supervisory personnel
7. Record data (SIDP, SICP, Pit Gain, and Time)
8. Hold pre-job safety meeting and discuss kill procedure

### **Shutting In While Running Casing**

1. Sound alarm signaling well control event to Rig Crew
2. Space out casing to allow circulating swedge installation
3. Shut in Upper Pipe Rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
4. Install circulating swedge, Close high pressure, low torque valves, Close Chokes
5. Verify well is shut-in and flow has stopped
6. Notify supervisory personnel
7. Record data (SIDP, SICP, Pit Gain, and Time)
8. Hold Pre-job safety meeting and discuss kill procedure

### **Shutting in while out of hole**

1. Sound alarm signaling well control event to Rig Crew
2. Shut-in well: close blind rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
3. Close Chokes, Verify well is shut-in and monitor pressures
4. Notify supervisory personnel
5. Record data (SIDP, SICP, Pit Gain, and Time)
6. Hold Pre-job safety meeting and discuss kill procedure

### **Shutting in prior to pulling BHA through stack**

Prior to pulling last joint of drill pipe thru the stack space out and check flow  
If flowing see steps below.

1. Sound alarm signaling well control event to Rig Crew
2. Shut in upper pipe ram and open HCR against Open Chokes and Valves Open  
to working pressure gauge
3. Install open, full open safety valve and close valve, Close Chokes
4. Verify well is shut-in and flow has stopped
5. Notify supervisory personnel
6. Record data (SIDP, SICP, Pit Gain, and Time)
7. Hold pre-job safety meeting and discuss kill procedure



**Shutting in while BHA is in the stack and ram preventer and combo immediately available**

1. Sound alarm signaling well control event to Rig Crew
2. Space out BHA with upset just beneath the compatible pipe ram
3. Shut in upper compatible pipe ram and open HCR against Open Chokes and Valves Open to working pressure gauge
4. Install open, full open safety valve and close valve, Close Chokes
5. Verify well is shut-in and flow has stopped
6. Notify supervisory personnel
7. Record data (SIDP, SICP, Pit Gain, and Time)
8. Hold pre-job safety meeting and discuss kill procedure

\*FOSV will be on rig floor in open position with operating handle for each type of connection utilized and tested to 10,000 psi

**Shutting in while BHA is in the stack and no ram preventer or combo immediately available**

1. Sound alarm signaling well control event to Rig Crew
2. If possible pick up high enough, to pull string clear and follow "Open Hole" scenario

If not possible to pick up high enough:

3. Stab Crossover, make up one joint/stand of drill pipe, and install open, full open safety valve (Leave Open)
4. Space out drill string with upset just beneath the compatible pipe ram.
5. Shut in upper compatible pipe ram and open HCR against Open Chokes and Valves Open to working pressure gauge
6. Close FOSV, Close Chokes, Verify well is shut-in and flow has stopped
7. Notify supervisory personnel
8. Record data (SIDP, SICP, Pit Gain, and Time)
9. Hold pre-job safety meeting and discuss kill procedure


13 5/8" 5M BOP  
Configuration

CO-FLEX LINE TO  
CHOKE MANIFOLD

2" KILL LINE

4" 10M VALVES &

10M Check Valve

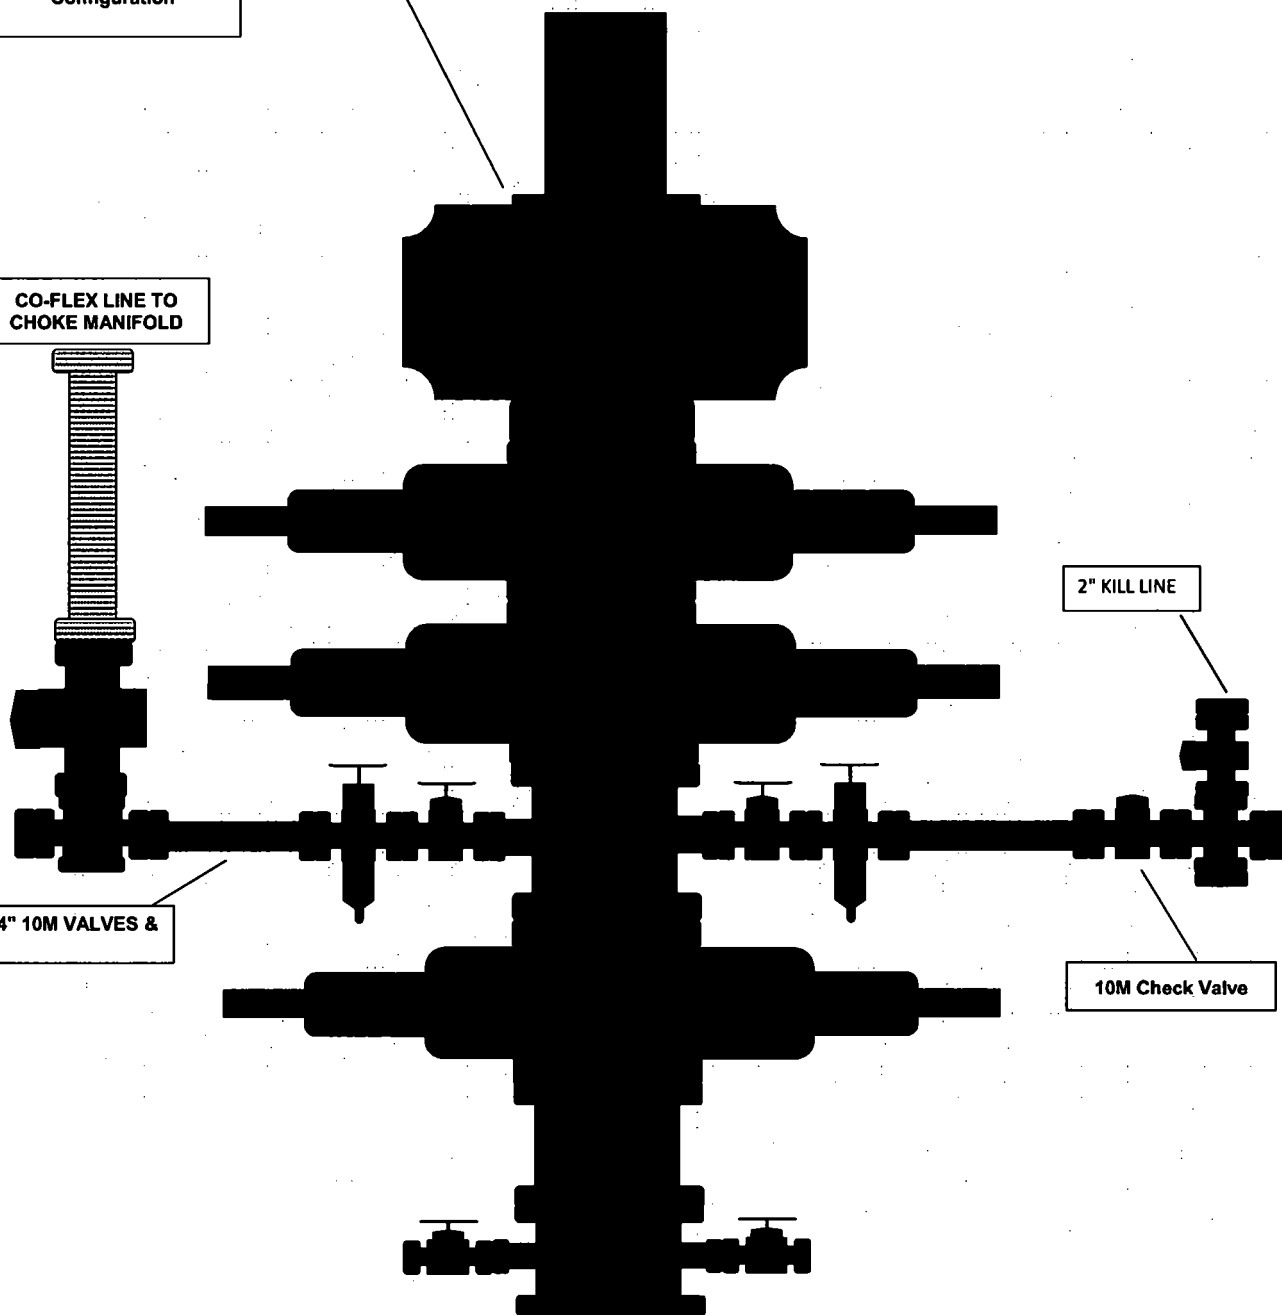


## Pressure Control Plan

### Pressure Control Equipment

- Following setting of 13-3/8" Surface Casing Ameredev will install 13-5/8 MB4 Multi Bowl Casing Head by welding on a 13-5/8 SOW x 13-5/8" 5M in combination with 13-5/8 5M x 13-5/8 10M B-Sec to Land Intm #1 and a 13-5/8 10M x 13-5/8 10M shouldered to land C-Sec to Land Intm #2 (Installation procedure witnessed and verified by a manufacturer's representative).
- Casing will be tested to 1500 psi or .22 psi/ft whichever is greater for 30 minutes with <10% leak off, but will not exceed 70% of the burst rating per Onshore Order No. 2.
- Ameredev will install a 5M System Blowout Preventer (BOPE) with a 5M Annular Preventer and related equipment (BOPE). Full testing will be performed utilizing a full isolation test plug and limited to 5,000 psi MOP of MB4 Multi Bowl Casing Head. Pressure will be held for 10 min or until provisions of test are met on all valves and rams. The 5M Annular Preventer will be tested to 50% of approved working pressure (2,500 psi). Casing will be tested to 1500 psi or .22 psi/ft whichever is greater for 30 minutes with <10% leak off, but will not exceed 70% of the burst rating per Onshore Order No. 2.
- Setting of 9-5/8" Intermediate will be done by landing a wellhead hanger in the 13-5/8" 5M Bowl, Cementing and setting Well Head Packing seals and testing same. (Installation procedure witnessed and verified by a manufacturer's representative) Casing will be tested to 1500 psi or .22 psi/ft whichever is greater for 30 minutes with <10% leak off, but will not exceed 70% of the burst rating per Onshore Order No. 2.
- Full testing will be performed utilizing a full isolation test plug to 10,000 psi MOP of MB4 Multi Bowl B-Section. Pressure will be held for 10 min or until provisions of test are met on all valves and rams. The 5M Annular Preventer will be tested to 100% of approved working pressure (5,000 psi).
- Before drilling >20ft of new formation under the 9-5/8" Casing Shoe a pressure integrity test of the Casing Shoe will be performed to minimum of the MWE anticipated to control formation pressure to the next casing depth.
- Following setting of 5-1/2" Production Casing and adequate WOC time Ameredev will break 10M System Blowout Preventer (BOP) from 10M DOL-2 Casing Head, install annulus casing slips and test same (Installation procedure witnessed and verified by a manufacturer's representative) and install 11" 10M x 5-1/8" 15M Tubing Head (Installation procedure witnessed and verified by a manufacturer's representative). Ameredev will test head to 70% casing design and install Dry Hole cap with needle valve and pressure gauge to monitor well awaiting completion.

## Pressure Control Plan

- Slow pump speeds will be taken daily by each crew and recorded on Daily Drilling Report after mudding up.
- A choke manifold and accumulator with floor and remote operating stations will be functional and in place after installation of BOPE, as well as full functioning mud gas separator.
- Weekly BOPE pit level drills will be conducted by each crew and recorded on Daily Drilling Report.
- BOP will be fully operated when out of hole and will be documented on the daily drilling log.
- All B.O.P.s and associated equipment will be tested in accordance with Onshore Order #2
- All B.O.P. testing will be done by an independent service company.
- The B.O.P. will be tested within 21 days of the original test if drilling takes more time than planned.
- Ameredev requests a variance to connect the B.O.P. choke outlet to the choke manifold using a co-flex hose with a 10,000 psi working pressure that has been tested to 15,000psi and is built to API Spec 16C. Once the flex line is installed it will be tied down with safety clamps. (certifications will be sent to Carlsbad BLM Office prior to install)
- Ameredev requests a variance to install a 5M Annular Preventer on the 10M System to drill the Production Hole below the 9-5/8" Intermediate Section. 5M Annular will be tested to 100% working pressure (5,000 psi). A full well control procedure will be included to isolate well bore.

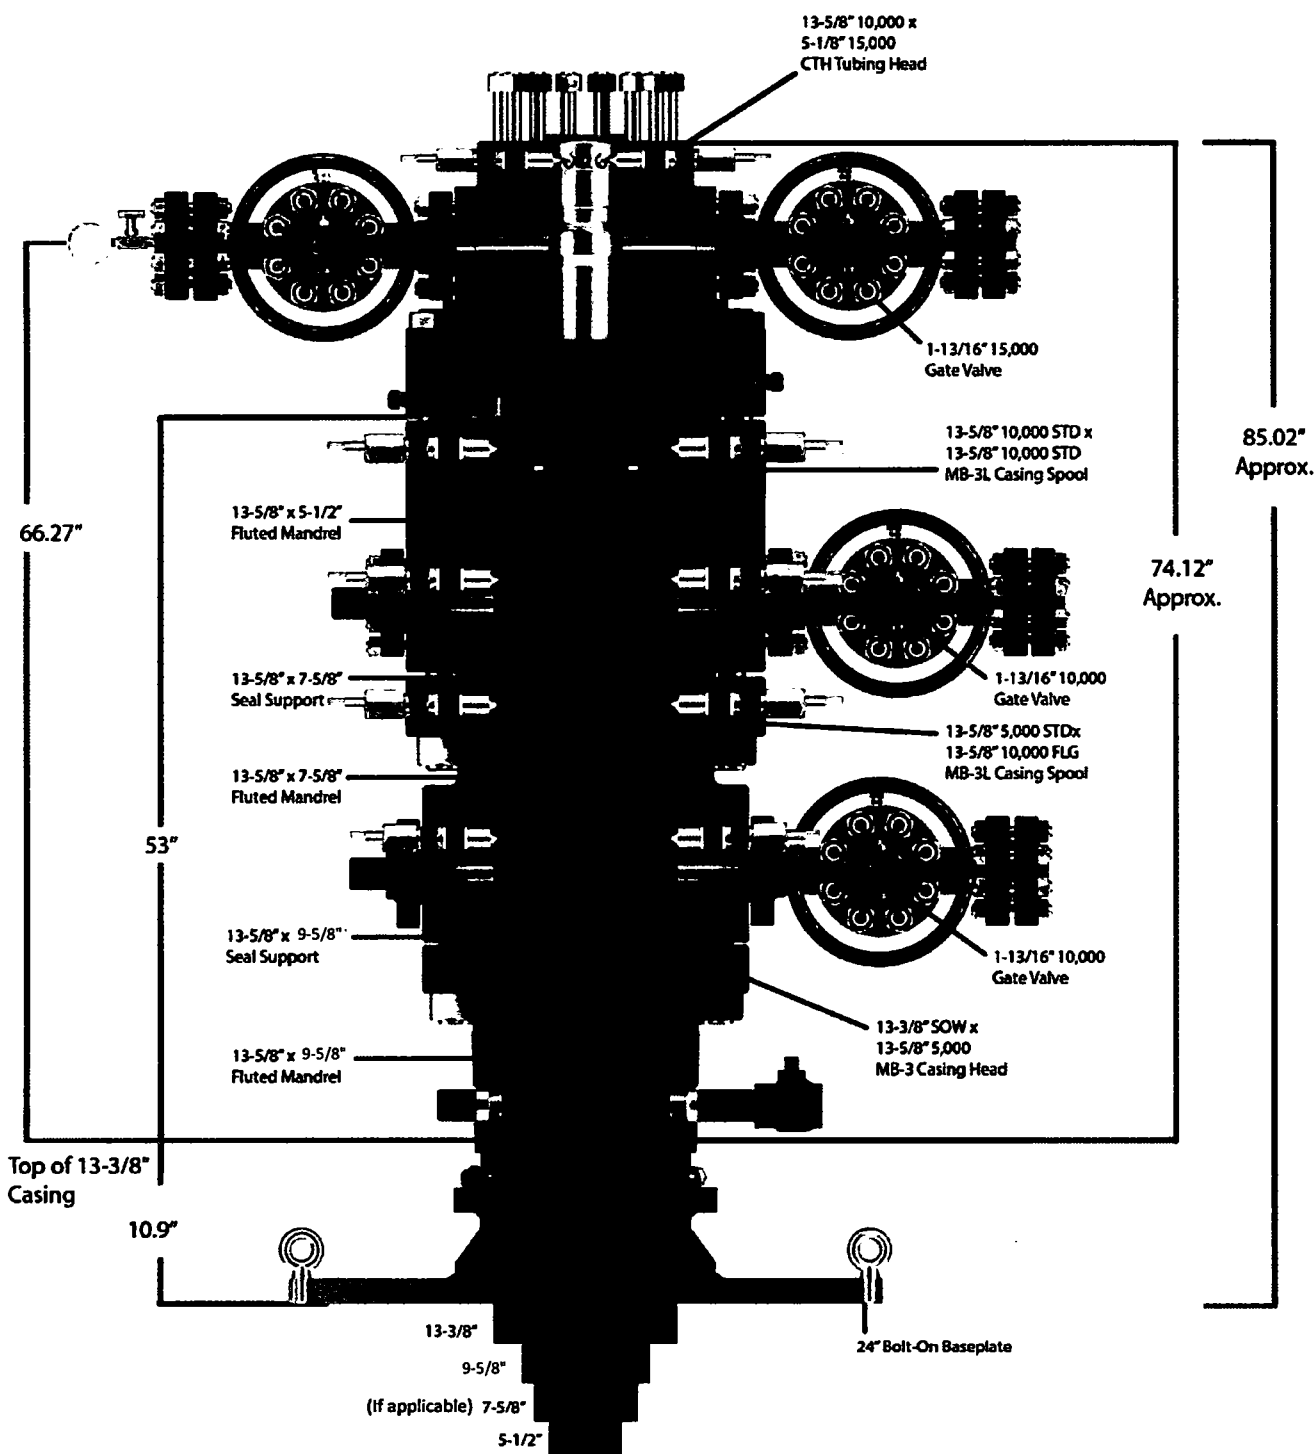

## Quotation

## Downing Wellhead Equipment

Oklahoma City,  
Oklahoma - USA

### Reference Data:

16925 AMEREDEV

### Proprietary and Confidential

The information contained in this drawing is the sole property of Downing Wellhead Equipment, any reproduction in part or in whole without the written permission of Downing Wellhead Equipment is prohibited.

### TITLE:

AMEREDEV

DRAWN

CHECKED

APPROVED

SIZE

A

DWG. NO.

REV.

Scale:

Weight:

Sheet:

# PERFORMANCE DATA

API BTC

13.375 in

68.00 lbs/ft

J-55

## Technical Data Sheet

### Tubular Parameters

Size	13.375	in	Minimum Yield	55,000	psi
Nominal Weight	68.00	lbs/ft	Minimum Tensile	75,000	psi
Grade	J-55		Yield Load	1,069,000	lbs
PE Weight	66.10	lbs/ft	Tensile Load	1,458,000	lbs
Wall Thickness	0.480	in	Min. Internal Yield Pressure	3,500	psi
Nominal ID	12.415	in	Collapse Pressure	1,950	psi
Drift Diameter	12.259	in			
Nom. Pipe Body Area	19.445	in <sup>2</sup>			

### Connection Parameters

Connection OD	14.375	in
Coupling Length	10.625	in
Threads Per Inch	5.000	in
Standoff Thread Turns	1.000	
Make-Up Loss	4.513	in
Yield Load In Tension	—	lbs
Min. Internal Yield Pressure	3,500	psi

Printed on: February-13-2015

#### NOTE:

The content of this Technical Data Sheet is for general information only and does not guarantee performance or imply fitness for a particular purpose, which only a competent drilling professional can determine considering the specific installation and operation parameters. Information that is printed or downloaded is no longer controlled by TMK IPSCO and might not be the latest information. Anyone using the information herein does so at their own risk. To verify that you have the latest TMK IPSCO technical information, please contact TMK IPSCO Technical Sales toll-free at 1-888-258-2000.



**Wellbore Schematic**

Well: Green Jacket Fed Com 26-36-29 101H  
 SHL: Sec. 29 26S-36E 262' FNL & 792' FWL  
 BHL: Sec. 32 26S-36E 50' FSL & 380' FWL  
 Lea, NM  
 Wellhead: A - 13-5/8" 10M x 13-5/8" SOW  
 B - 13-5/8" 10M x 13-5/8" 10M  
 C - 13-5/8" 10M x 13-5/8" 10M  
 Tubing Spool - 5-1/8" 15M x 13-3/8" 10M  
 Xmas Tree: 2-9/16" 10M  
 Tubing: 2-7/8" L-80 6.5# 8rd EUE

Co. Well ID: xxxxxx  
 AFE No.: xxxx-xxx  
 API No.: xxxxxxxxxxxx  
 GL: 2,924'  
 Field: Delaware  
 Objective: Wolfcamp A  
 TVD: 12,049'  
 MD: 19,490'  
 Rig: TBD KB: 27'  
 E-Mail: [Wellsite2@ameredev.com](mailto:Wellsite2@ameredev.com)

Hole Size	Formation Tops	Logs Cement	Mud Weight
17.5"	Rustler 1,659'	1,103 Sacks TOC 0'	8.4-8.6 ppg WBM
	13.375" 68# J-55 BTC 1,784'		
12.25"	Salado 2,072'		
	Tansill 3,255'		
	Capitan Reef 3,510'		
	Lamar 4,980'	889 Sacks TOC 0'	50% Excess
	DV Tool 5,030'		
	Bell Canyon 5,051'		
	Brushy Canyon 7,280'		
	Bone Spring Lime 8,460'		
	First Bone Spring 9,884'		
	Second Bone Spring 10,476'		
	Third Bone Spring Upper 11,038'		
	9.625" 40# L-80HC BTC 11,163'	1,723 Sacks TOC 0'	50% Excess
8.5"	Third Bone Spring 11,645'		
12° Build @ 11,522' MD thru 12,375' MD	Wolfcamp A 11,899'		
	5.5" 20# P-110CYHP BTC 19,490'	4,161 Sacks TOC 0'	25% Excess
	Target Wolfcamp A 12049 TVD // 19490 MD		10.5 - 12.5 ppg OBM

## Casing Design and Safety Factor Check

<b>Casing Specifications</b>						
Segment	Hole ID	Depth	OD	Weight	Grade	Coupling
Surface	17.5	1,784'	13.375	68	J-55	BTC
Intermediate	12.25	11,163'	9.625	40	HCL-80	BTC
Prod Segment A	8.5	11,522'	5.5	20	CYHP-110	BTC
Prod Segment B	8.5	19,490'	5.5	20	CYHP-110	BTC

<b>Check Surface Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
14.375	1,069	915	4,100	3,450
<b>Safety Factors</b>				
1.56	8.82	7.54	5.14	0.63
<b>Check Intermediate Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
7.625	940	558	6700	9460
<b>Safety Factors</b>				
2.31	2.11	2.10	1.23	1.21
<b>Check Prod Casing, Segment A</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
5.777	728	655	12780	14360
<b>Safety Factors</b>				
1.36	3.02	2.72	1.71	1.84
<b>Check Prod Casing, Segment B</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
5.777	728	655	12780	14360
<b>Safety Factors</b>				
1.36	69.07	62.14	1.63	1.84



## Wellbore Schematic

**Well:** Green Jacket Fed Com 26-36-29 101H  
**SHL:** Sec. 29 26S-36E 262' FNL & 792' FWL  
**BHL:** Sec. 32 26S-36E 50' FSL & 380' FWL  
 Lea, NM  
**Wellhead:** A - 13-5/8" 10M x 13-5/8" SOW  
 B - 13-5/8" 10M x 13-5/8" 10M  
 C - 13-5/8" 10M x 13-5/8" 10M  
 Tubing Spool - 5-1/8" 15M x 13-3/8" 10M  
**Xmas Tree:** 2-9/16" 10M  
**Tubing:** 2-7/8" L-80 6.5# 8rd EUE

**Co. Well ID:** xxxxxx  
**AFE No.:** xxxx-xxx  
**API No.:** xxxxxxxxxxxx  
**GL:** 2,924'  
**Field:** Delaware  
**Objective:** Wolfcamp A  
**TVD:** 12,049'  
**MD:** 19,490'  
**Rig:** TBD **KB:** 27'  
**E-Mail:** Wellsite2@ameredev.com

Hole Size	Formation Tops	Logs Cement	Mud Weight
17.5"	Rustler 1,659' 13.375" 68# J-55 BTC 1,784'	1,103 Sacks TOC 0' 100% Excess	8.4-8.6 ppg WBM
12.25"	Salado 2,072' Tansill 3,255' Capitan Reef 3,510' Lamar 4,980' DV Tool 5,030' Bell Canyon 5,051' Brushy Canyon 7,280' Bone Spring Lime 8,460' First Bone Spring 9,884' Second Bone Spring 10,476' Third Bone Spring Upper 11,038' 9.625" 40# L-80HC BTC 11,163'	889 Sacks TOC 0' 50% Excess 1,723 Sacks TOC 0' 50% Excess	8.5 - 9.4 ppg Diesel Brine Emulsion
8.5"	Third Bone Spring 11,645' Wolfcamp A 11,899' 5.5" 20# P-110CYHP BTC 19,490' Target Wolfcamp A 12049 TVD // 19490 MD	4,161 Sacks TOC 0' 25% Excess	10.5 - 12.5 ppg OBM

12° Build  
 @  
 11,522' MD  
 thru  
 12,375' MD

## Casing Design and Safety Factor Check

<b>Casing Specifications</b>						
Segment	Hole ID	Depth	OD	Weight	Grade	Coupling
Surface	17.5	1,784'	13.375	68	J-55	BTC
Intermediate	12.25	11,163'	9.625	40	HCL-80	BTC
Prod Segment A	8.5	11,522'	5.5	20	CYHP-110	BTC
Prod Segment B	8.5	19,490'	5.5	20	CYHP-110	BTC

<b>Check Surface Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
14.375	1,069	915	4,100	3,450
<b>Safety Factors</b>				
1.56	8.82	7.54	5.14	0.63
<b>Check Intermediate Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
7.625	940	558	6700	9460
<b>Safety Factors</b>				
2.31	2.11	2.10	1.23	1.21
<b>Check Prod Casing, Segment A</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
5.777	728	655	12780	14360
<b>Safety Factors</b>				
1.36	3.02	2.72	1.71	1.84
<b>Check Prod Casing, Segment B</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
5.777	728	655	12780	14360
<b>Safety Factors</b>				
1.36	69.07	62.14	1.63	1.84

# SeAH

9.625"

40#

.395"

SEAH-80 HIGH COLLAPSE

(SEAH-80 IS A NON HEAT TREATED PRODUCT)

## Dimensions (Nominal)

Outside Diameter	9.625	in.
Wall	0.395	in.
Inside Diameter	8.835	in.
Drift	8.750	in.
Weight, T&C	40.000	lbs./ft.
Weight, PE	38.970	lbs./ft.

## Performance Properties

Collapse	4100	psi
Internal Yield Pressure at Minimum Yield		
PE	5750	psi
LTC	5750	psi
BTC	5750	psi
Yield Strength, Pipe Body	916	1000 lbs.
Joint Strength		
LTC	717	1000 lbs.
BTC	915	1000 lbs.

Note: SeAH Steel has produced this specification sheet for general information only. SeAH does not assume liability or responsibility for any loss or injury resulting from the use of information or data contained herein. All applications for the material described are at the customer's own risk and responsibility.

**U.S. Steel Tubular Products**  
**Product Information**  
**5.5 in. 20 lb/ft (0.361 in. wall) P-110 HC Casing**  
**STAR SEAL - CDC™**

Grade(s)		P-110 HC	
MECHANICAL PROPERTIES			
	Yield Strength		
	Minimum	110	ksi
	Maximum	140	ksi
	Tensile Strength		
	Minimum	125	ksi
PIPE PROPERTIES			
Dimensions, Nominal	Pipe Outside Diameter	5.500	in.
	Wall	0.361	in.
	Pipe Inside Diameter	4.778	in.
	Pipe Drift		
	API	4.653	in.
	Special (If Applicable)	N/A	in.
	Weight, T&C	20.00	lbs/ft
	Weight, Plain End	19.83	lbs/ft
	Pipe Cross Sectional Area	5.828	sq. in.
Performance Properties	Minimum Pipe Body Yield Strength	641	1,000 lbs
	Minimum Collapse Pressure	12,200	psi
	Minimum Internal Yield Pressure	12,640	psi
CONNECTION PROPERTIES			
Dimensions, Nominal	Connection Outside Diameter	6.050	in.
	Connection Inside Diameter	4.778	in.
	Connection Drift		
	API	4.653	in.
	Special (If Applicable)	N/A	in.
	Makeup Loss	4.63	in.
	Critical Area	5.828	in.
	Joint Efficiency	100	%
	Performance Properties	Joint Strength	667
Compression Rating		400	1,000 lbs
API Collapse Pressure Rating		12,200	psi
API Internal Pressure Resistance		12,360	psi
Maximum Uniaxial Bend Rating		57.2	deg/100 ft
Recommended Torque Values	Minimum Shoulder Torque	5,000	ft-lbs
	Maximum Shoulder Torque	7,500	ft-lbs
	Connection Yield Torque	16,100	ft-lbs

\* STAR SEAL - CDC (Casing Drilling Connection) is a Modified API Buttress threaded and coupled connection designed for field proven in drilling with casing applications. Star Seal is a registered trademark of U. S. Steel Corporation. All material contained in this publication is for general information only. This material should not therefore, be used or relied upon for any specific application without independent competent professional examination and verification of its accuracy, suitability and applicability. Anyone making use of this material does so at their own risk and assumes any and all liability resulting from such use. U. S. Steel disclaims any and all expressed or implied warranties of fitness for any general or particular application.



**U.S. Steel Tubular Products, Inc.**  
**600 Grant Street**  
**Pittsburgh, PA 15219**

6/9/2009

## Wellbore Schematic

**Well:** Green Jacket Fed Com 26-36-29 101H  
**SHL:** Sec. 29 26S-36E 262' FNL & 792' FWL  
**BHL:** Sec. 32 26S-36E 50' FSL & 380' FWL  
 Lea, NM  
**Wellhead:** A - 13-5/8" 10M x 13-5/8" SOW  
 B - 13-5/8" 10M x 13-5/8" 10M  
 C - 13-5/8" 10M x 13-5/8" 10M  
 Tubing Spool - 5-1/8" 15M x 13-3/8" 10M  
**Xmas Tree:** 2-9/16" 10M  
**Tubing:** 2-7/8" L-80 6.5# 8rd EUE

**Co. Well ID:** xxxxxx  
**AFE No.:** xxxx-xxxx  
**API No.:** xxxxxxxxxxxx  
**GL:** 2,924'  
**Field:** Delaware  
**Objective:** Wolfcamp A  
**TVD:** 12,049'  
**MD:** 19,490'  
**Rig:** TBD **KB:** 27'  
**E-Mail:** Wellsite2@ameredev.com

Hole Size	Formation Tops	Logs Cement	Mud Weight
17.5"	Rustler 1,659' 13.375" 68# J-55 BTC 1,784'	1,103 Sacks TOC 0' 100% Excess	8.4-8.6 ppg WBM
12.25"	Salado 2,072' Tansill 3,255' Capitan Reef 3,510' Lamar 4,980' DV Tool 5,030' Bell Canyon 5,051' Brushy Canyon 7,280' Bone Spring Lime 8,460' First Bone Spring 9,884' Second Bone Spring 10,476' Third Bone Spring Upper 11,038' 9.625" 40# L-80HC BTC 11,163'	889 Sacks TOC 0' 50% Excess 1,723 Sacks TOC 0' 50% Excess	8.5 - 9.4 ppg Diesel Brine Emulsion
8.5"	Third Bone Spring 11,645' Wolfcamp A 11,899' 5.5" 20# P-110CYHP BTC 19,490' Target Wolfcamp A 12049 TVD // 19490 MD	4,161 Sacks TOC 0' 25% Excess	10.5 - 12.5 ppg OBM

12° Build  
 @  
 11,522' MD  
 thru  
 12,375' MD

## Casing Design and Safety Factor Check

<b>Casing Specifications</b>						
Segment	Hole ID	Depth	OD	Weight	Grade	Coupling
Surface	17.5	1,784'	13.375	68	J-55	BTC
Intermediate	12.25	11,163'	9.625	40	HCL-80	BTC
Prod Segment A	8.5	11,522'	5.5	20	CYHP-110	BTC
Prod Segment B	8.5	19,490'	5.5	20	CYHP-110	BTC

<b>Check Surface Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
14.375	1,069	915	4,100	3,450
<b>Safety Factors</b>				
1.56	8.82	7.54	5.14	0.63
<b>Check Intermediate Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
7.625	940	558	6700	9460
<b>Safety Factors</b>				
2.31	2.11	2.10	1.23	1.21
<b>Check Prod Casing, Segment A</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
5.777	728	655	12780	14360
<b>Safety Factors</b>				
1.36	3.02	2.72	1.71	1.84
<b>Check Prod Casing, Segment B</b>				
OD Cplg	Body	Joint	Collapse	Burst
<i>inches</i>	<i>1000 lbs</i>	<i>1000 lbs</i>	<i>psi</i>	<i>psi</i>
5.777	728	655	12780	14360
<b>Safety Factors</b>				
1.36	69.07	62.14	1.63	1.84

## H<sub>2</sub>S Drilling Operation Plan

**1. All Company and Contract personnel admitted on location must be trained by a qualified H<sub>2</sub>S safety instructor to the following:**

- a. Characteristics of H<sub>2</sub>S
- b. Physical effects and hazards
- c. Principal and operation of H<sub>2</sub>S detectors, warning system and briefing areas
- d. Evacuation procedure, routes and first aid
- e. Proper use of safety equipment and life support systems
- f. Essential personnel meeting Medical Evaluation criteria will receive additional training on the proper use of 30 minute pressure demand air packs.

**2. Briefing Area:**

- a. Two perpendicular areas will be designated by signs and readily accessible.
- b. Upon location entry there will be a designated area to establish all safety compliance criteria (1.) has been met.

**3. H<sub>2</sub>S Detection and Alarm Systems:**

- a. H<sub>2</sub>S sensors/detectors shall be located on the drilling rig floor, in the base of the sub structure/cellar area, and on the mud pits in the shale shaker area. Additional H<sub>2</sub>S detectors may be placed as deemed necessary. All detectors will be set to initiate visual alarm at 10 ppm and visual with audible at 14 ppm and all equipment will be calibrated every 30 days or as needed.
- b. An audio alarm will be installed on the derrick floor and in the top doghouse.

**4. Protective Equipment for Essential Personnel:**

- a. **Breathing Apparatus:**
  - i. Rescue Packs (SCBA) - 1 Unit shall be placed at each briefing area.
  - ii. Two (SCBA) Units will be stored in safety trailer on location.
  - iii. Work/Escapes packs - 1 Unit will be available on rig floor in doghouse for emergency evacuation for driller.
- b. **Auxiliary Rescue Equipment:**
  - i. Stretcher
  - ii. 2 - OSHA full body harnesses
  - iii. 100 ft. 5/8" OSHA approved rope
  - iv. 1 - 20# class ABC fire extinguisher

**5. Windsock and/or Wind Streamers:**

- a. Windsock at mud pit area should be high enough to be visible.
- b. Windsock on the rig floor should be high enough to be visible.

**6. Communication:**

- a. While working under mask scripting boards will be used for communication where applicable.
- b. Hand signals will be used when script boards are not applicable.

## H<sub>2</sub>S Drilling Operation Plan

- c. Two way radios will be used to communicate off location in case of emergency help is required. In most cases cellular telephones will be available at Drilling Foreman's Office.

7. **Drill Stem Testing:** - No Planned DST at this time.

8. **Mud program:**

- a. If H<sub>2</sub>S is encountered, mud system will be altered if necessary to maintain control of formation. A mud gas separator will be brought into service along with H<sub>2</sub>S scavengers if necessary.

9. **Metallurgy:**

- a. All drill strings, casing, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H<sub>2</sub>S service.
- b. Drilling Contractor supervisor will be required to be familiar with the effect H<sub>2</sub>S has on tubular goods and other mechanical equipment provided through contractor.



## H<sub>2</sub>S Contingency Plan

### Emergency Procedures

In the event of a release of H<sub>2</sub>S, the first responder(s) must:

- Isolate the area and prevent entry by other persons into the 100 ppm ROE.
- Evacuate any public places encompassed by the 100 ppm ROE.
- Be equipped with H<sub>2</sub>S monitors and air packs in order to control the release.
- Use the "buddy system" to ensure no injuries occur during the response.
- Take precautions to avoid personal injury during this operation.
- Contact Operator and/or local officials the aid in operation. See list of phone numbers attached.
- Have received training in the:
  - Detection of H<sub>2</sub>S and
  - Measures for protection against the gas,
  - Equipment used for protection and emergency response.

### Ignition of Gas Source

Should control of the well be considered lost and ignition considered, take care to protect against exposure to Sulfur Dioxide (SO<sub>2</sub>). Intentional ignition must be coordinated with the NMOC and local officials. Additionally, the NM State Police may become involved. NM State Police shall be the Incident Command on scene of any major release. Take care to protect downwind whenever there is an ignition of the gas.

### Characteristics of H<sub>2</sub>S and SO<sub>2</sub>

Common Name	Chemical Formula	Specific Gravity	Threshold Limit	Hazardous Limit	Lethal Concentration
Hydrogen Sulfide	H <sub>2</sub> S	1.189 Air=1	10 ppm	100 ppm/hr	600 ppm
Sulfur Dioxide	SO <sub>2</sub>	2.21 Air=1	2 ppm	N/A	1000 ppm

### Contacting Authorities

Ameredev Operating LLC personnel must liaise with local and state agencies to ensure a proper response to a major release. Additionally, the OCD must be notified of the release as soon as possible but no later than 4 hours. Agencies will ask for information such as type and volume of release, wind direction, location of release, etc. Be prepared with all information available including direction to site. The following call list of essential and potential responders has been prepared for use during a release. Ameredev Operating LLC's response must be in coordination with the State of New Mexico's "Hazardous Materials Emergency Response Plan" (HMER)

**H<sub>2</sub>S Contingency Plan**

<b>Amerdev Operating LLC – Emergency Phone 737-300-4799</b>			
<b>Key Personnel:</b>			
<b>Name</b>	<b>Title</b>	<b>Office</b>	<b>Mobile</b>
Floyd Hammond	Chief Operating officer	737-300-4724	512-783-6810
Zachary Boyd	Operations Superintendent	737-300-4725	432-385-6996
Blake Estrada	Construction Foreman		432-385-5831

<b><u>Artesia</u></b>			
Ambulance			911
State Police			575-746-2703
City Police			575-746-2703
Sheriff's Office			575-746-9888
Fire Department			575-746-2701
Local Emergency Planning Committee			575-746-2122
New Mexico Oil Conservation Division			575-748-1283
<b><u>Carlsbad</u></b>			
Ambulance			911
State Police			575-885-3137
City Police			575-885-2111
Sheriff's Office			575-887-7551
Fire Department			575-887-3798
Local Emergency Planning Committee			575-887-6544
US Bureau of Land Management			575-887-6544
<b><u>Santa Fe</u></b>			
New Mexico Emergency Response Commission (Santa Fe)			505-476-9600
New Mexico Emergency Response Commission (Santa Fe) 24 Hrs			505-827-9126
New Mexico State Emergency Operations Center			505-476-9635
<b><u>National</u></b>			
National Emergency Response Center (Washington, D.C.)			800-424-8802
<b><u>Medical</u></b>			
Flight for Life - 4000 24th St.; Lubbock, TX			806-743-9911
Aerocare - R3, Box 49F; Lubbock, TX			806-747-8923
Med Flight Air Amb - 2301 Yale Blvd S.E., #D3; Albuquerque, NM			505-842-4433
'SB Air Med Service - 2505 Clark Carr Loop S.E.; Albuquerque, NM			505-842-4949

# ***AMEREDEV***

## **Ameredev Operating, LLC.**

**Green Jacket**

**Green Jacket WC1's**

**Green Jacket 101H**

**Wellbore #1**

**Plan: Design #1**

## **Standard Planning Report**

**01 May, 2019**

Database:	EDM5000	Local Co-ordinate Reference:	Well Green Jacket 101H
Company:	Ameredev Operating, LLC.	TVD Reference:	KB @ 2951.0usft
Project:	Green Jacket	MD Reference:	KB @ 2951.0usft
Site:	Green Jacket WC1's	North Reference:	Grid
Well:	Green Jacket 101H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Project	Green Jacket		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Green Jacket WC1's				
Site Position:		Northing:	372,852.16 usft	Latitude:	32° 1' 14.826 N
From:	Lat/Long	Easting:	863,714.12 usft	Longitude:	103° 17' 35.373 W
Position Uncertainty:	0.0 usft	Slot Radius:	13-3/16 "	Grid Convergence:	0.55 °

Well	Green Jacket 101H					
Well Position	+N/-S	0.3 usft	Northing:	372,852.48 usft	Latitude:	32° 1' 14.825 N
	+E/-W	40.0 usft	Easting:	863,754.16 usft	Longitude:	103° 17' 34.908 W
Position Uncertainty	0.0 usft	Wellhead Elevation:		Ground Level:	2,924.0 usft	

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2015	4/22/2019	6.61	59.89	47,660.18024870

Design	Design #1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	182.56

Plan Survey Tool Program	Date	5/1/2019		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.0	19,490.3	Design #1 (Wellbore #1)	MWD
				OWSG MWD - Standard

Database:	EDM5000	Local Co-ordinate Reference:	Well Green Jacket 101H
Company:	Ameredev Operating, LLC.	TVD Reference:	KB @ 2951.0usft
Project:	Green Jacket	MD Reference:	KB @ 2951.0usft
Site:	Green Jacket WC1's	North Reference:	Grid
Well:	Green Jacket 101H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.00	0.00	0.00	0.00	
2,300.0	6.00	324.00	2,299.5	12.7	-9.2	2.00	2.00	0.00	324.00	
4,613.2	6.00	324.00	4,600.0	208.3	-151.3	0.00	0.00	0.00	0.00	
4,913.2	0.00	0.00	4,899.5	221.0	-160.6	2.00	-2.00	0.00	180.00	
8,513.8	0.00	0.00	8,500.0	221.0	-160.6	0.00	0.00	0.00	0.00	
8,813.8	6.00	280.00	8,799.5	223.7	-176.0	2.00	2.00	0.00	280.00	
10,020.9	6.00	280.00	10,000.0	245.6	-300.3	0.00	0.00	0.00	0.00	
10,320.9	0.00	0.00	10,299.5	248.4	-315.7	2.00	-2.00	0.00	180.00	
11,521.5	0.00	0.00	11,500.0	248.4	-315.7	0.00	0.00	0.00	0.00	
11,862.6	40.93	198.29	11,812.8	137.5	-352.4	12.00	12.00	0.00	198.29	
11,943.8	40.93	198.29	11,874.2	87.0	-369.1	0.00	0.00	0.00	0.00	
12,374.7	90.00	179.33	12,049.0	-288.3	-414.0	12.00	11.39	-4.40	-24.45	GJ101 FTP2
19,490.3	90.00	179.33	12,049.0	-7,403.4	-330.9	0.00	0.00	0.00	0.00	GJ101 BHL

Database:	EDM5000	Local Co-ordinate Reference:	Well Green Jacket 101H
Company:	Ameredev Operating, LLC.	TVD Reference:	KB @ 2951.0usft
Project:	Green Jacket	MD Reference:	KB @ 2951.0usft
Site:	Green Jacket WC1's	North Reference:	Grid
Well:	Green Jacket 101H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

### Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	2.00	324.00	2,100.0	1.4	-1.0	-1.4	2.00	2.00	0.00
2,200.0	4.00	324.00	2,199.8	5.6	-4.1	-5.5	2.00	2.00	0.00
2,300.0	6.00	324.00	2,299.5	12.7	-9.2	-12.3	2.00	2.00	0.00
2,400.0	6.00	324.00	2,398.9	21.2	-15.4	-20.4	0.00	0.00	0.00
2,500.0	6.00	324.00	2,498.4	29.6	-21.5	-28.6	0.00	0.00	0.00
2,600.0	6.00	324.00	2,597.8	38.1	-27.7	-36.8	0.00	0.00	0.00
2,700.0	6.00	324.00	2,697.3	46.5	-33.8	-45.0	0.00	0.00	0.00
2,800.0	6.00	324.00	2,796.7	55.0	-39.9	-53.1	0.00	0.00	0.00
2,900.0	6.00	324.00	2,896.2	63.4	-46.1	-61.3	0.00	0.00	0.00
3,000.0	6.00	324.00	2,995.6	71.9	-52.2	-69.5	0.00	0.00	0.00
3,100.0	6.00	324.00	3,095.1	80.3	-58.4	-77.7	0.00	0.00	0.00
3,200.0	6.00	324.00	3,194.5	88.8	-64.5	-85.8	0.00	0.00	0.00
3,300.0	6.00	324.00	3,294.0	97.3	-70.7	-94.0	0.00	0.00	0.00
3,400.0	6.00	324.00	3,393.4	105.7	-76.8	-102.2	0.00	0.00	0.00
3,500.0	6.00	324.00	3,492.9	114.2	-83.0	-110.4	0.00	0.00	0.00
3,600.0	6.00	324.00	3,592.3	122.6	-89.1	-118.5	0.00	0.00	0.00
3,700.0	6.00	324.00	3,691.8	131.1	-95.2	-126.7	0.00	0.00	0.00
3,800.0	6.00	324.00	3,791.2	139.5	-101.4	-134.9	0.00	0.00	0.00
3,900.0	6.00	324.00	3,890.7	148.0	-107.5	-143.1	0.00	0.00	0.00
4,000.0	6.00	324.00	3,990.1	156.5	-113.7	-151.2	0.00	0.00	0.00
4,100.0	6.00	324.00	4,089.6	164.9	-119.8	-159.4	0.00	0.00	0.00
4,200.0	6.00	324.00	4,189.0	173.4	-126.0	-167.6	0.00	0.00	0.00
4,300.0	6.00	324.00	4,288.5	181.8	-132.1	-175.7	0.00	0.00	0.00
4,400.0	6.00	324.00	4,387.9	190.3	-138.2	-183.9	0.00	0.00	0.00
4,500.0	6.00	324.00	4,487.4	198.7	-144.4	-192.1	0.00	0.00	0.00
4,600.0	6.00	324.00	4,586.9	207.2	-150.5	-200.3	0.00	0.00	0.00
4,613.2	6.00	324.00	4,600.0	208.3	-151.3	-201.3	0.00	0.00	0.00
4,700.0	4.26	324.00	4,686.4	214.6	-155.9	-207.4	2.00	-2.00	0.00
4,800.0	2.26	324.00	4,786.3	219.2	-159.3	-211.9	2.00	-2.00	0.00
4,900.0	0.26	324.00	4,886.2	221.0	-160.6	-213.6	2.00	-2.00	0.00
4,913.2	0.00	0.00	4,899.5	221.0	-160.6	-213.6	2.00	-2.00	0.00
5,000.0	0.00	0.00	4,986.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,100.0	0.00	0.00	5,086.2	221.0	-160.6	-213.6	0.00	0.00	0.00

Database:	EDM5000	Local Co-ordinate Reference:	Well Green Jacket 101H
Company:	Ameredev Operating, LLC.	TVD Reference:	KB @ 2951.0usft
Project:	Green Jacket	MD Reference:	KB @ 2951.0usft
Site:	Green Jacket WC1's	North Reference:	Grid
Well:	Green Jacket 101H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

### Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,200.0	0.00	0.00	5,186.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,300.0	0.00	0.00	5,286.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,400.0	0.00	0.00	5,386.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,500.0	0.00	0.00	5,486.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,600.0	0.00	0.00	5,586.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,700.0	0.00	0.00	5,686.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,800.0	0.00	0.00	5,786.2	221.0	-160.6	-213.6	0.00	0.00	0.00
5,900.0	0.00	0.00	5,886.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,000.0	0.00	0.00	5,986.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,100.0	0.00	0.00	6,086.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,200.0	0.00	0.00	6,186.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,300.0	0.00	0.00	6,286.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,400.0	0.00	0.00	6,386.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,500.0	0.00	0.00	6,486.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,600.0	0.00	0.00	6,586.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,700.0	0.00	0.00	6,686.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,800.0	0.00	0.00	6,786.2	221.0	-160.6	-213.6	0.00	0.00	0.00
6,900.0	0.00	0.00	6,886.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,000.0	0.00	0.00	6,986.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,100.0	0.00	0.00	7,086.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,200.0	0.00	0.00	7,186.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,300.0	0.00	0.00	7,286.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,400.0	0.00	0.00	7,386.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,500.0	0.00	0.00	7,486.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,600.0	0.00	0.00	7,586.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,700.0	0.00	0.00	7,686.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,800.0	0.00	0.00	7,786.2	221.0	-160.6	-213.6	0.00	0.00	0.00
7,900.0	0.00	0.00	7,886.2	221.0	-160.6	-213.6	0.00	0.00	0.00
8,000.0	0.00	0.00	7,986.2	221.0	-160.6	-213.6	0.00	0.00	0.00
8,100.0	0.00	0.00	8,086.2	221.0	-160.6	-213.6	0.00	0.00	0.00
8,200.0	0.00	0.00	8,186.2	221.0	-160.6	-213.6	0.00	0.00	0.00
8,300.0	0.00	0.00	8,286.2	221.0	-160.6	-213.6	0.00	0.00	0.00
8,400.0	0.00	0.00	8,386.2	221.0	-160.6	-213.6	0.00	0.00	0.00
8,500.0	0.00	0.00	8,486.2	221.0	-160.6	-213.6	0.00	0.00	0.00
8,513.8	0.00	0.00	8,500.0	221.0	-160.6	-213.6	0.00	0.00	0.00
8,600.0	1.72	280.00	8,586.2	221.2	-161.9	-213.8	2.00	2.00	0.00
8,700.0	3.72	280.00	8,686.1	222.1	-166.5	-214.4	2.00	2.00	0.00
8,800.0	5.72	280.00	8,785.8	223.5	-174.6	-215.5	2.00	2.00	0.00
8,813.8	6.00	280.00	8,799.5	223.7	-176.0	-215.7	2.00	2.00	0.00
8,900.0	6.00	280.00	8,885.2	225.3	-184.9	-216.8	0.00	0.00	0.00
9,000.0	6.00	280.00	8,984.7	227.1	-195.2	-218.2	0.00	0.00	0.00
9,100.0	6.00	280.00	9,084.1	228.9	-205.5	-219.5	0.00	0.00	0.00
9,200.0	6.00	280.00	9,183.6	230.7	-215.8	-220.9	0.00	0.00	0.00
9,300.0	6.00	280.00	9,283.0	232.6	-226.1	-222.2	0.00	0.00	0.00
9,400.0	6.00	280.00	9,382.5	234.4	-236.4	-223.6	0.00	0.00	0.00
9,500.0	6.00	280.00	9,481.9	236.2	-246.7	-224.9	0.00	0.00	0.00
9,600.0	6.00	280.00	9,581.4	238.0	-257.0	-226.3	0.00	0.00	0.00
9,700.0	6.00	280.00	9,680.8	239.8	-267.3	-227.6	0.00	0.00	0.00
9,800.0	6.00	280.00	9,780.3	241.6	-277.6	-229.0	0.00	0.00	0.00
9,900.0	6.00	280.00	9,879.7	243.5	-287.8	-230.4	0.00	0.00	0.00
10,000.0	6.00	280.00	9,979.2	245.3	-298.1	-231.7	0.00	0.00	0.00
10,020.9	6.00	280.00	10,000.0	245.6	-300.3	-232.0	0.00	0.00	0.00
10,100.0	4.42	280.00	10,078.7	246.9	-307.4	-232.9	2.00	-2.00	0.00
10,200.0	2.42	280.00	10,178.6	247.9	-313.2	-233.7	2.00	-2.00	0.00

Database:	EDM5000	Local Co-ordinate Reference:	Well Green Jacket 101H
Company:	Ameredev Operating, LLC.	TVD Reference:	KB @ 2951.0usft
Project:	Green Jacket	MD Reference:	KB @ 2951.0usft
Site:	Green Jacket WC1's	North Reference:	Grid
Well:	Green Jacket 101H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

### Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
10,300.0	0.42	280.00	10,278.5	248.4	-315.7	-234.0	2.00	-2.00	0.00
10,320.9	0.00	0.00	10,299.5	248.4	-315.7	-234.0	2.00	-2.00	0.00
10,400.0	0.00	0.00	10,378.5	248.4	-315.7	-234.0	0.00	0.00	0.00
10,500.0	0.00	0.00	10,478.5	248.4	-315.7	-234.0	0.00	0.00	0.00
10,600.0	0.00	0.00	10,578.5	248.4	-315.7	-234.0	0.00	0.00	0.00
10,700.0	0.00	0.00	10,678.5	248.4	-315.7	-234.0	0.00	0.00	0.00
10,800.0	0.00	0.00	10,778.5	248.4	-315.7	-234.0	0.00	0.00	0.00
10,900.0	0.00	0.00	10,878.5	248.4	-315.7	-234.0	0.00	0.00	0.00
11,000.0	0.00	0.00	10,978.5	248.4	-315.7	-234.0	0.00	0.00	0.00
11,100.0	0.00	0.00	11,078.5	248.4	-315.7	-234.0	0.00	0.00	0.00
11,200.0	0.00	0.00	11,178.5	248.4	-315.7	-234.0	0.00	0.00	0.00
11,300.0	0.00	0.00	11,278.5	248.4	-315.7	-234.0	0.00	0.00	0.00
11,400.0	0.00	0.00	11,378.5	248.4	-315.7	-234.0	0.00	0.00	0.00
11,500.0	0.00	0.00	11,478.5	248.4	-315.7	-234.0	0.00	0.00	0.00
11,521.5	0.00	0.00	11,500.0	248.4	-315.7	-234.0	0.00	0.00	0.00
<b>GJ101 KOP</b>									
11,600.0	9.42	198.29	11,578.2	242.3	-317.8	-227.8	12.00	12.00	0.00
11,700.0	21.42	198.29	11,674.4	217.1	-326.1	-202.3	12.00	12.00	0.00
11,800.0	33.42	198.29	11,763.0	173.4	-340.5	-158.0	12.00	12.00	0.00
11,862.6	40.93	198.29	11,812.8	137.5	-352.4	-121.7	12.00	12.00	0.00
11,900.0	40.93	198.29	11,841.1	114.2	-360.1	-98.1	0.00	0.00	0.00
11,943.8	40.93	198.29	11,874.2	87.0	-369.1	-70.4	0.00	0.00	0.00
12,000.0	47.14	194.49	11,914.6	49.5	-380.0	-32.5	12.00	11.04	-6.77
12,002.5	47.41	194.34	11,916.2	47.8	-380.5	-30.7	12.00	11.15	-6.03
<b>GJ101 FTP</b>									
12,100.0	58.41	189.31	11,975.0	-28.3	-396.1	45.9	12.00	11.28	-5.16
12,200.0	69.85	185.26	12,018.6	-117.4	-407.4	135.4	12.00	11.44	-4.04
12,300.0	81.37	181.78	12,043.4	-213.9	-413.2	232.1	12.00	11.52	-3.48
12,374.7	90.00	179.33	12,049.0	-288.3	-414.0	306.5	12.00	11.55	-3.28
<b>GJ101 FTP2</b>									
12,400.0	90.00	179.33	12,049.0	-313.6	-413.7	331.7	0.00	0.00	0.00
12,500.0	90.00	179.33	12,049.0	-413.6	-412.5	431.6	0.00	0.00	0.00
12,600.0	90.00	179.33	12,049.0	-513.6	-411.3	531.4	0.00	0.00	0.00
12,700.0	90.00	179.33	12,049.0	-613.6	-410.2	631.3	0.00	0.00	0.00
12,800.0	90.00	179.33	12,049.0	-713.5	-409.0	731.1	0.00	0.00	0.00
12,900.0	90.00	179.33	12,049.0	-813.5	-407.8	830.9	0.00	0.00	0.00
13,000.0	90.00	179.33	12,049.0	-913.5	-406.7	930.8	0.00	0.00	0.00
13,100.0	90.00	179.33	12,049.0	-1,013.5	-405.5	1,030.6	0.00	0.00	0.00
13,200.0	90.00	179.33	12,049.0	-1,113.5	-404.3	1,130.5	0.00	0.00	0.00
13,300.0	90.00	179.33	12,049.0	-1,213.5	-403.2	1,230.3	0.00	0.00	0.00
13,400.0	90.00	179.33	12,049.0	-1,313.5	-402.0	1,330.1	0.00	0.00	0.00
13,500.0	90.00	179.33	12,049.0	-1,413.5	-400.8	1,430.0	0.00	0.00	0.00
13,600.0	90.00	179.33	12,049.0	-1,513.5	-399.7	1,529.8	0.00	0.00	0.00
13,700.0	90.00	179.33	12,049.0	-1,613.5	-398.5	1,629.7	0.00	0.00	0.00
13,800.0	90.00	179.33	12,049.0	-1,713.5	-397.3	1,729.5	0.00	0.00	0.00
13,900.0	90.00	179.33	12,049.0	-1,813.5	-396.2	1,829.4	0.00	0.00	0.00
14,000.0	90.00	179.33	12,049.0	-1,913.5	-395.0	1,929.2	0.00	0.00	0.00
14,100.0	90.00	179.33	12,049.0	-2,013.5	-393.8	2,029.0	0.00	0.00	0.00
14,200.0	90.00	179.33	12,049.0	-2,113.5	-392.7	2,128.9	0.00	0.00	0.00
14,300.0	90.00	179.33	12,049.0	-2,213.4	-391.5	2,228.7	0.00	0.00	0.00
14,400.0	90.00	179.33	12,049.0	-2,313.4	-390.3	2,328.6	0.00	0.00	0.00
14,500.0	90.00	179.33	12,049.0	-2,413.4	-389.2	2,428.4	0.00	0.00	0.00
14,600.0	90.00	179.33	12,049.0	-2,513.4	-388.0	2,528.2	0.00	0.00	0.00



Database:	EDM5000	Local Co-ordinate Reference:	Well Green Jacket 101H
Company:	Ameredev Operating, LLC.	TVD Reference:	KB @ 2951.0usft
Project:	Green Jacket	MD Reference:	KB @ 2951.0usft
Site:	Green Jacket WC1's	North Reference:	Grid
Well:	Green Jacket 101H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

### Planned Survey

Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,700.0	90.00	179.33	12,049.0	-2,613.4	-386.8	2,628.1	0.00	0.00	0.00
14,800.0	90.00	179.33	12,049.0	-2,713.4	-385.7	2,727.9	0.00	0.00	0.00
14,900.0	90.00	179.33	12,049.0	-2,813.4	-384.5	2,827.8	0.00	0.00	0.00
15,000.0	90.00	179.33	12,049.0	-2,913.4	-383.3	2,927.6	0.00	0.00	0.00
15,100.0	90.00	179.33	12,049.0	-3,013.4	-382.2	3,027.5	0.00	0.00	0.00
15,200.0	90.00	179.33	12,049.0	-3,113.4	-381.0	3,127.3	0.00	0.00	0.00
15,300.0	90.00	179.33	12,049.0	-3,213.4	-379.8	3,227.1	0.00	0.00	0.00
15,400.0	90.00	179.33	12,049.0	-3,313.4	-378.7	3,327.0	0.00	0.00	0.00
15,500.0	90.00	179.33	12,049.0	-3,413.4	-377.5	3,426.8	0.00	0.00	0.00
15,600.0	90.00	179.33	12,049.0	-3,513.4	-376.3	3,526.7	0.00	0.00	0.00
15,700.0	90.00	179.33	12,049.0	-3,613.4	-375.2	3,626.5	0.00	0.00	0.00
15,800.0	90.00	179.33	12,049.0	-3,713.3	-374.0	3,726.3	0.00	0.00	0.00
15,900.0	90.00	179.33	12,049.0	-3,813.3	-372.8	3,826.2	0.00	0.00	0.00
16,000.0	90.00	179.33	12,049.0	-3,913.3	-371.7	3,926.0	0.00	0.00	0.00
16,100.0	90.00	179.33	12,049.0	-4,013.3	-370.5	4,025.9	0.00	0.00	0.00
16,200.0	90.00	179.33	12,049.0	-4,113.3	-369.3	4,125.7	0.00	0.00	0.00
16,300.0	90.00	179.33	12,049.0	-4,213.3	-368.1	4,225.5	0.00	0.00	0.00
16,400.0	90.00	179.33	12,049.0	-4,313.3	-367.0	4,325.4	0.00	0.00	0.00
16,500.0	90.00	179.33	12,049.0	-4,413.3	-365.8	4,425.2	0.00	0.00	0.00
16,600.0	90.00	179.33	12,049.0	-4,513.3	-364.6	4,525.1	0.00	0.00	0.00
16,700.0	90.00	179.33	12,049.0	-4,613.3	-363.5	4,624.9	0.00	0.00	0.00
16,800.0	90.00	179.33	12,049.0	-4,713.3	-362.3	4,724.8	0.00	0.00	0.00
16,900.0	90.00	179.33	12,049.0	-4,813.3	-361.1	4,824.6	0.00	0.00	0.00
17,000.0	90.00	179.33	12,049.0	-4,913.3	-360.0	4,924.4	0.00	0.00	0.00
17,100.0	90.00	179.33	12,049.0	-5,013.3	-358.8	5,024.3	0.00	0.00	0.00
17,200.0	90.00	179.33	12,049.0	-5,113.2	-357.6	5,124.1	0.00	0.00	0.00
17,300.0	90.00	179.33	12,049.0	-5,213.2	-356.5	5,224.0	0.00	0.00	0.00
17,400.0	90.00	179.33	12,049.0	-5,313.2	-355.3	5,323.8	0.00	0.00	0.00
17,500.0	90.00	179.33	12,049.0	-5,413.2	-354.1	5,423.6	0.00	0.00	0.00
17,600.0	90.00	179.33	12,049.0	-5,513.2	-353.0	5,523.5	0.00	0.00	0.00
17,700.0	90.00	179.33	12,049.0	-5,613.2	-351.8	5,623.3	0.00	0.00	0.00
17,800.0	90.00	179.33	12,049.0	-5,713.2	-350.6	5,723.2	0.00	0.00	0.00
17,900.0	90.00	179.33	12,049.0	-5,813.2	-349.5	5,823.0	0.00	0.00	0.00
18,000.0	90.00	179.33	12,049.0	-5,913.2	-348.3	5,922.8	0.00	0.00	0.00
18,100.0	90.00	179.33	12,049.0	-6,013.2	-347.1	6,022.7	0.00	0.00	0.00
18,200.0	90.00	179.33	12,049.0	-6,113.2	-346.0	6,122.5	0.00	0.00	0.00
18,300.0	90.00	179.33	12,049.0	-6,213.2	-344.8	6,222.4	0.00	0.00	0.00
18,400.0	90.00	179.33	12,049.0	-6,313.2	-343.6	6,322.2	0.00	0.00	0.00
18,500.0	90.00	179.33	12,049.0	-6,413.2	-342.5	6,422.1	0.00	0.00	0.00
18,600.0	90.00	179.33	12,049.0	-6,513.2	-341.3	6,521.9	0.00	0.00	0.00
18,700.0	90.00	179.33	12,049.0	-6,613.1	-340.1	6,621.7	0.00	0.00	0.00
18,800.0	90.00	179.33	12,049.0	-6,713.1	-339.0	6,721.6	0.00	0.00	0.00
18,900.0	90.00	179.33	12,049.0	-6,813.1	-337.8	6,821.4	0.00	0.00	0.00
19,000.0	90.00	179.33	12,049.0	-6,913.1	-336.6	6,921.3	0.00	0.00	0.00
19,100.0	90.00	179.33	12,049.0	-7,013.1	-335.5	7,021.1	0.00	0.00	0.00
19,200.0	90.00	179.33	12,049.0	-7,113.1	-334.3	7,120.9	0.00	0.00	0.00
19,300.0	90.00	179.33	12,049.0	-7,213.1	-333.1	7,220.8	0.00	0.00	0.00
19,400.0	90.00	179.33	12,049.0	-7,313.1	-332.0	7,320.6	0.00	0.00	0.00
GJ101 LTP									
19,490.3	90.00	179.33	12,049.0	-7,403.4	-330.9	7,410.8	0.00	0.00	0.00
GJ101 BHL									

<b>Database:</b>	EDM5000	<b>Local Co-ordinate Reference:</b>	Well Green Jacket 101H
<b>Company:</b>	Ameredev Operating, LLC.	<b>TVD Reference:</b>	KB @ 2951.0usft
<b>Project:</b>	Green Jacket	<b>MD Reference:</b>	KB @ 2951.0usft
<b>Site:</b>	Green Jacket WC1's	<b>North Reference:</b>	Grid
<b>Well:</b>	Green Jacket 101H	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

**Design Targets**

Target Name - hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
GJ101 KOP - plan hits target center - Point	0.00	0.00	11,500.0	248.4	-315.7	373,100.85	863,438.41	32° 1' 17.313 N	103° 17' 38.547 W
GJ101 LTP - plan misses target center by 136.6usft at 19400.0usft MD (12049.0 TVD, -7313.1 N, -332.0 E) - Point	0.00	0.00	12,049.0	-7,354.7	-462.0	365,497.78	863,292.13	32° 0' 2.096 N	103° 17' 41.095 W
GJ101 FTP - plan misses target center by 175.6usft at 12002.5usft MD (11916.2 TVD, 47.8 N, -380.5 E) - Point	0.00	0.00	12,049.0	157.8	-414.0	373,010.29	863,340.20	32° 1' 16.426 N	103° 17' 39.698 W
GJ101 BHL - plan misses target center by 0.6usft at 19490.3usft MD (12049.0 TVD, -7403.4 N, -330.9 E) - Point	0.00	0.00	12,049.0	-7,403.4	-330.3	365,449.06	863,423.83	32° 0' 1.602 N	103° 17' 39.571 W
GJ101 FTP2 - plan hits target center - Point	0.00	0.01	12,049.0	-288.3	-414.0	372,564.16	863,340.20	32° 1' 12.012 N	103° 17' 39.748 W

# ***AMEREDEV***

## **Ameredev Operating, LLC.**

**Green Jacket**

**Green Jacket WC1's**

**Green Jacket 101H**

**Wellbore #1**

**Plan: Design #1**

## **Lease Penetration Section Line Foot**

**01 May, 2019**

<b>Company:</b>	Ameredev Operating, LLC.	<b>Local Co-ordinate Reference:</b>	Well Green Jacket 101H
<b>Project:</b>	Green Jacket	<b>TVD Reference:</b>	KB @ 2951.0usft
<b>Site:</b>	Green Jacket WC1's	<b>MD Reference:</b>	KB @ 2951.0usft
<b>Well:</b>	Green Jacket 101H	<b>North Reference:</b>	Grid
<b>Wellbore:</b>	Wellbore #1	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Design:</b>	Design #1	<b>Database:</b>	EDM5000

<b>Project</b>	Green Jacket		
<b>Map System:</b>	US State Plane 1983	<b>System Datum:</b>	Mean Sea Level
<b>Geo Datum:</b>	North American Datum 1983		
<b>Map Zone:</b>	New Mexico Eastern Zone		

<b>Site</b>	Green Jacket WC1's				
<b>Site Position:</b>		<b>Northing:</b>	372,852.16 usft	<b>Latitude:</b>	32° 1' 14.826 N
<b>From:</b>	Lat/Long	<b>Easting:</b>	863,714.12 usft	<b>Longitude:</b>	103° 17' 35.373 W
<b>Position Uncertainty:</b>	0.0 usft	<b>Spot Radius:</b>	13-3/16"	<b>Grid Convergence:</b>	0.55 °

<b>Well</b>	Green Jacket 101H					
<b>Well Position</b>	+N/-S	0.0 usft	<b>Northing:</b>	372,852.48 usft	<b>Latitude:</b>	32° 1' 14.825 N
	+E/-W	0.0 usft	<b>Easting:</b>	863,754.17 usft	<b>Longitude:</b>	103° 17' 34.908 W
<b>Position Uncertainty</b>	0.0 usft	<b>Wellhead Elevation:</b>	usft	<b>Ground Level:</b>	2,924.0 usft	

<b>Wellbore</b>	Wellbore #1				
<b>Magnetics</b>	<b>Model Name</b>	<b>Sample Date</b>	<b>Declination (°)</b>	<b>Dip Angle (°)</b>	<b>Field Strength (nT)</b>
	IGRF2015	4/22/2019	6.61	59.89	47,660.18024869

<b>Design</b>	Design #1			
<b>Audit Notes:</b>				
<b>Version:</b>	<b>Phase:</b>	PROTOTYPE	<b>Tie On Depth:</b>	0.0
<b>Vertical Section:</b>	<b>Depth From (TVD) (usft)</b>	<b>+N/-S (usft)</b>	<b>+E/-W (usft)</b>	<b>Direction (°)</b>
	0.0	0.0	0.0	182.56

<b>Survey Tool Program</b>	<b>Date</b> 5/1/2019			
<b>From (usft)</b>	<b>To (usft)</b>	<b>Survey (Wellbore)</b>	<b>Tool Name</b>	<b>Description</b>
0.0	19,490.3	Design #1 (Wellbore #1)	MWD	OWSG MWD - Standard

<b>Planned Survey</b>							
<b>MD (usft)</b>	<b>Inc (°)</b>	<b>Azi (azimuth) (°)</b>	<b>TVD (usft)</b>	<b>+FSL/-FNL (usft)</b>	<b>+FWL/-FEL (usft)</b>	<b>Latitude</b>	<b>Longitude</b>
0.0	0.00	0.00	0.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
100.0	0.00	0.00	100.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
200.0	0.00	0.00	200.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
300.0	0.00	0.00	300.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
400.0	0.00	0.00	400.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
500.0	0.00	0.00	500.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
600.0	0.00	0.00	600.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
700.0	0.00	0.00	700.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
800.0	0.00	0.00	800.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
900.0	0.00	0.00	900.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,000.0	0.00	0.00	1,000.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,100.0	0.00	0.00	1,100.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W

Company:	Ameredev Operating, LLC.	Local Co-ordinate Reference:	Well Green Jacket 101H
Project:	Green Jacket	TVD Reference:	KB @ 2951.0usft
Site:	Green Jacket WC1's	MD Reference:	KB @ 2951.0usft
Well:	Green Jacket 101H	North Reference:	Grid
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Design #1	Database:	EDM5000

**Planned Survey**

MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	+FSL/-FNL (usft)	+FWL/-FEL (usft)	Latitude	Longitude
1,200.0	0.00	0.00	1,200.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,300.0	0.00	0.00	1,300.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,400.0	0.00	0.00	1,400.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,500.0	0.00	0.00	1,500.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,600.0	0.00	0.00	1,600.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,700.0	0.00	0.00	1,700.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,800.0	0.00	0.00	1,800.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
1,900.0	0.00	0.00	1,900.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
2,000.0	0.00	0.00	2,000.0	-261.7	792.0	32° 1' 14.825 N	103° 17' 34.908 W
2,100.0	2.00	324.00	2,100.0	-260.3	791.0	32° 1' 14.839 N	103° 17' 34.920 W
2,200.0	4.00	324.00	2,199.8	-256.0	787.9	32° 1' 14.882 N	103° 17' 34.955 W
2,300.0	6.00	324.00	2,299.5	-249.0	782.8	32° 1' 14.952 N	103° 17' 35.014 W
2,400.0	6.00	324.00	2,398.9	-240.5	776.7	32° 1' 15.036 N	103° 17' 35.084 W
2,500.0	6.00	324.00	2,498.4	-232.1	770.5	32° 1' 15.120 N	103° 17' 35.155 W
2,600.0	6.00	324.00	2,597.8	-223.6	764.4	32° 1' 15.205 N	103° 17' 35.225 W
2,700.0	6.00	324.00	2,697.3	-215.2	758.2	32° 1' 15.289 N	103° 17' 35.295 W
2,800.0	6.00	324.00	2,796.7	-206.7	752.1	32° 1' 15.373 N	103° 17' 35.366 W
2,900.0	6.00	324.00	2,896.2	-198.3	746.0	32° 1' 15.457 N	103° 17' 35.436 W
3,000.0	6.00	324.00	2,995.6	-189.8	739.8	32° 1' 15.542 N	103° 17' 35.507 W
3,100.0	6.00	324.00	3,095.1	-181.3	733.7	32° 1' 15.626 N	103° 17' 35.577 W
3,200.0	6.00	324.00	3,194.5	-172.9	727.5	32° 1' 15.710 N	103° 17' 35.647 W
3,300.0	6.00	324.00	3,294.0	-164.4	721.4	32° 1' 15.794 N	103° 17' 35.718 W
3,400.0	6.00	324.00	3,393.4	-156.0	715.2	32° 1' 15.879 N	103° 17' 35.788 W
3,500.0	6.00	324.00	3,492.9	-147.5	709.1	32° 1' 15.963 N	103° 17' 35.859 W
3,600.0	6.00	324.00	3,592.3	-139.1	702.9	32° 1' 16.047 N	103° 17' 35.929 W
3,700.0	6.00	324.00	3,691.8	-130.6	696.8	32° 1' 16.131 N	103° 17' 35.999 W
3,800.0	6.00	324.00	3,791.2	-122.1	690.7	32° 1' 16.216 N	103° 17' 36.070 W
3,900.0	6.00	324.00	3,890.7	-113.7	684.5	32° 1' 16.300 N	103° 17' 36.140 W
4,000.0	6.00	324.00	3,990.1	-105.2	678.4	32° 1' 16.384 N	103° 17' 36.211 W
4,100.0	6.00	324.00	4,089.6	-96.8	672.2	32° 1' 16.468 N	103° 17' 36.281 W
4,200.0	6.00	324.00	4,189.0	-88.3	666.1	32° 1' 16.553 N	103° 17' 36.352 W
4,300.0	6.00	324.00	4,288.5	-79.9	659.9	32° 1' 16.637 N	103° 17' 36.422 W
4,400.0	6.00	324.00	4,387.9	-71.4	653.8	32° 1' 16.721 N	103° 17' 36.492 W
4,500.0	6.00	324.00	4,487.4	-62.9	647.7	32° 1' 16.806 N	103° 17' 36.563 W
4,600.0	6.00	324.00	4,586.9	-54.5	641.5	32° 1' 16.890 N	103° 17' 36.633 W
4,613.2	6.00	324.00	4,600.0	-53.4	640.7	32° 1' 16.901 N	103° 17' 36.642 W
4,700.0	4.26	324.00	4,686.4	-47.1	636.1	32° 1' 16.963 N	103° 17' 36.695 W
4,800.0	2.26	324.00	4,786.3	-42.5	632.8	32° 1' 17.009 N	103° 17' 36.733 W
4,900.0	0.26	324.00	4,886.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
4,913.2	0.00	0.00	4,899.5	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,000.0	0.00	0.00	4,986.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,100.0	0.00	0.00	5,086.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,200.0	0.00	0.00	5,186.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,300.0	0.00	0.00	5,286.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W

<b>Company:</b>	Ameredev Operating, LLC.	<b>Local Co-ordinate Reference:</b>	Well Green Jacket 101H
<b>Project:</b>	Green Jacket	<b>TVD Reference:</b>	KB @ 2951.0usft
<b>Site:</b>	Green Jacket WC1's	<b>MD Reference:</b>	KB @ 2951.0usft
<b>Well:</b>	Green Jacket 101H	<b>North Reference:</b>	Grid
<b>Wellbore:</b>	Wellbore #1	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Design:</b>	Design #1	<b>Database:</b>	EDM5000

**Planned Survey**

MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	+FSL/-FNL (usft)	+FWL/-FEL (usft)	Latitude	Longitude
5,400.0	0.00	0.00	5,386.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,500.0	0.00	0.00	5,486.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,600.0	0.00	0.00	5,586.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,700.0	0.00	0.00	5,686.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,800.0	0.00	0.00	5,786.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
5,900.0	0.00	0.00	5,886.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,000.0	0.00	0.00	5,986.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,100.0	0.00	0.00	6,086.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,200.0	0.00	0.00	6,186.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,300.0	0.00	0.00	6,286.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,400.0	0.00	0.00	6,386.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,500.0	0.00	0.00	6,486.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,600.0	0.00	0.00	6,586.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,700.0	0.00	0.00	6,686.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,800.0	0.00	0.00	6,786.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
6,900.0	0.00	0.00	6,886.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,000.0	0.00	0.00	6,986.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,100.0	0.00	0.00	7,086.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,200.0	0.00	0.00	7,186.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,300.0	0.00	0.00	7,286.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,400.0	0.00	0.00	7,386.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,500.0	0.00	0.00	7,486.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,600.0	0.00	0.00	7,586.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,700.0	0.00	0.00	7,686.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,800.0	0.00	0.00	7,786.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
7,900.0	0.00	0.00	7,886.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,000.0	0.00	0.00	7,986.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,100.0	0.00	0.00	8,086.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,200.0	0.00	0.00	8,186.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,300.0	0.00	0.00	8,286.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,400.0	0.00	0.00	8,386.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,500.0	0.00	0.00	8,486.2	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,513.8	0.00	0.00	8,500.0	-40.7	631.5	32° 1' 17.027 N	103° 17' 36.748 W
8,600.0	1.72	280.00	8,586.2	-40.5	630.2	32° 1' 17.030 N	103° 17' 36.763 W
8,700.0	3.72	280.00	8,686.1	-39.6	625.5	32° 1' 17.038 N	103° 17' 36.817 W
8,800.0	5.72	280.00	8,785.8	-38.2	617.4	32° 1' 17.053 N	103° 17' 36.911 W
8,813.8	6.00	280.00	8,799.5	-38.0	616.0	32° 1' 17.056 N	103° 17' 36.927 W
8,900.0	6.00	280.00	8,885.2	-36.4	607.1	32° 1' 17.072 N	103° 17' 37.030 W
9,000.0	6.00	280.00	8,984.7	-34.6	596.8	32° 1' 17.091 N	103° 17' 37.150 W
9,100.0	6.00	280.00	9,084.1	-32.8	586.6	32° 1' 17.110 N	103° 17' 37.269 W
9,200.0	6.00	280.00	9,183.6	-30.9	576.3	32° 1' 17.129 N	103° 17' 37.388 W
9,300.0	6.00	280.00	9,283.0	-29.1	566.0	32° 1' 17.148 N	103° 17' 37.508 W
9,400.0	6.00	280.00	9,382.5	-27.3	555.7	32° 1' 17.167 N	103° 17' 37.627 W
9,500.0	6.00	280.00	9,481.9	-25.5	545.4	32° 1' 17.186 N	103° 17' 37.746 W

<b>Company:</b>	Ameredev Operating, LLC.	<b>Local Co-ordinate Reference:</b>	Well Green Jacket 101H
<b>Project:</b>	Green Jacket	<b>TVD Reference:</b>	KB @ 2951.0usft
<b>Site:</b>	Green Jacket WC1's	<b>MD Reference:</b>	KB @ 2951.0usft
<b>Well:</b>	Green Jacket 101H	<b>North Reference:</b>	Grid
<b>Wellbore:</b>	Wellbore #1	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Design:</b>	Design #1	<b>Database:</b>	EDM5000

**Planned Survey**

MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	+FSL/-FNL (usft)	+FWL/-FEL (usft)	Latitude	Longitude
9,600.0	6.00	280.00	9,581.4	-23.7	535.1	32° 1' 17.205 N	103° 17' 37.866 W
9,700.0	6.00	280.00	9,680.8	-21.9	524.8	32° 1' 17.224 N	103° 17' 37.985 W
9,800.0	6.00	280.00	9,780.3	-20.0	514.5	32° 1' 17.243 N	103° 17' 38.105 W
9,900.0	6.00	280.00	9,879.7	-18.2	504.2	32° 1' 17.262 N	103° 17' 38.224 W
10,000.0	6.00	280.00	9,979.2	-16.4	493.9	32° 1' 17.281 N	103° 17' 38.343 W
10,020.9	6.00	280.00	10,000.0	-16.0	491.8	32° 1' 17.284 N	103° 17' 38.368 W
10,100.0	4.42	280.00	10,078.7	-14.8	484.7	32° 1' 17.298 N	103° 17' 38.450 W
10,200.0	2.42	280.00	10,178.6	-13.8	478.8	32° 1' 17.308 N	103° 17' 38.518 W
10,300.0	0.42	280.00	10,278.5	-13.3	476.4	32° 1' 17.313 N	103° 17' 38.547 W
10,320.9	0.00	0.00	10,299.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
10,400.0	0.00	0.00	10,378.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
10,500.0	0.00	0.00	10,478.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
10,600.0	0.00	0.00	10,578.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
10,700.0	0.00	0.00	10,678.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
10,800.0	0.00	0.00	10,778.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
10,900.0	0.00	0.00	10,878.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
11,000.0	0.00	0.00	10,978.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
11,100.0	0.00	0.00	11,078.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
11,200.0	0.00	0.00	11,178.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
11,300.0	0.00	0.00	11,278.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
11,400.0	0.00	0.00	11,378.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
11,500.0	0.00	0.00	11,478.5	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
11,521.5	0.00	0.00	11,500.0	-13.3	476.3	32° 1' 17.313 N	103° 17' 38.547 W
<b>GJ101 KOP</b>							
11,600.0	9.42	198.29	11,578.2	-19.4	474.3	32° 1' 17.253 N	103° 17' 38.572 W
11,700.0	21.42	198.29	11,674.4	-44.6	465.9	32° 1' 17.004 N	103° 17' 38.671 W
11,800.0	33.42	198.29	11,763.0	-88.3	451.5	32° 1' 16.573 N	103° 17' 38.844 W
11,862.6	40.93	198.29	11,812.8	-124.2	439.7	32° 1' 16.220 N	103° 17' 38.985 W
11,900.0	40.93	198.29	11,841.1	-147.4	432.0	32° 1' 15.990 N	103° 17' 39.077 W
11,943.8	40.93	198.29	11,874.2	-174.7	423.0	32° 1' 15.721 N	103° 17' 39.185 W
12,000.0	47.14	194.49	11,914.6	-212.2	412.0	32° 1' 15.352 N	103° 17' 39.316 W
12,002.5	47.41	194.34	11,916.2	-213.9	411.6	32° 1' 15.334 N	103° 17' 39.322 W
<b>GJ101 FTP</b>							
12,100.0	58.41	189.31	11,975.0	-290.0	395.9	32° 1' 14.583 N	103° 17' 39.512 W
12,200.0	69.85	185.26	12,018.6	-379.1	384.7	32° 1' 13.703 N	103° 17' 39.652 W
12,300.0	81.37	181.78	12,043.4	-475.6	378.8	32° 1' 12.748 N	103° 17' 39.731 W
12,374.7	90.00	179.33	12,049.0	-550.0	378.1	32° 1' 12.012 N	103° 17' 39.748 W
<b>GJ101 FTP2</b>							
12,400.0	90.00	179.33	12,049.0	-575.3	378.4	32° 1' 11.762 N	103° 17' 39.747 W
12,500.0	90.00	179.33	12,049.0	-675.3	379.5	32° 1' 10.772 N	103° 17' 39.745 W
12,600.0	90.00	179.33	12,049.0	-775.2	380.7	32° 1' 9.783 N	103° 17' 39.743 W
12,700.0	90.00	179.33	12,049.0	-875.2	381.9	32° 1' 8.793 N	103° 17' 39.740 W
12,800.0	90.00	179.33	12,049.0	-975.2	383.0	32° 1' 7.804 N	103° 17' 39.738 W
12,900.0	90.00	179.33	12,049.0	-1,075.2	384.2	32° 1' 6.814 N	103° 17' 39.735 W
13,000.0	90.00	179.33	12,049.0	-1,175.2	385.4	32° 1' 5.825 N	103° 17' 39.733 W

<b>Company:</b>	Ameredev Operating, LLC.	<b>Local Co-ordinate Reference:</b>	Well Green Jacket 101H
<b>Project:</b>	Green Jacket	<b>TVD Reference:</b>	KB @ 2951.0usft
<b>Site:</b>	Green Jacket WC1's	<b>MD Reference:</b>	KB @ 2951.0usft
<b>Well:</b>	Green Jacket 101H	<b>North Reference:</b>	Grid
<b>Wellbore:</b>	Wellbore #1	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Design:</b>	Design #1	<b>Database:</b>	EDM5000

### Planned Survey

MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	+FSL/-FNL (usft)	+FWL/-FEL (usft)	Latitude	Longitude
13,100.0	90.00	179.33	12,049.0	-1,275.2	386.5	32° 1' 4.835 N	103° 17' 39.731 W
13,200.0	90.00	179.33	12,049.0	-1,375.2	387.7	32° 1' 3.846 N	103° 17' 39.728 W
13,300.0	90.00	179.33	12,049.0	-1,475.2	388.9	32° 1' 2.856 N	103° 17' 39.726 W
13,400.0	90.00	179.33	12,049.0	-1,575.2	390.0	32° 1' 1.867 N	103° 17' 39.723 W
13,500.0	90.00	179.33	12,049.0	-1,675.2	391.2	32° 1' 0.877 N	103° 17' 39.721 W
13,600.0	90.00	179.33	12,049.0	-1,775.2	392.4	32° 0' 59.888 N	103° 17' 39.719 W
13,700.0	90.00	179.33	12,049.0	-1,875.2	393.6	32° 0' 58.898 N	103° 17' 39.716 W
13,800.0	90.00	179.33	12,049.0	-1,975.2	394.7	32° 0' 57.909 N	103° 17' 39.714 W
13,900.0	90.00	179.33	12,049.0	-2,075.2	395.9	32° 0' 56.919 N	103° 17' 39.712 W
14,000.0	90.00	179.33	12,049.0	-2,175.2	397.1	32° 0' 55.930 N	103° 17' 39.709 W
14,100.0	90.00	179.33	12,049.0	-2,275.1	398.2	32° 0' 54.940 N	103° 17' 39.707 W
14,200.0	90.00	179.33	12,049.0	-2,375.1	399.4	32° 0' 53.951 N	103° 17' 39.704 W
14,300.0	90.00	179.33	12,049.0	-2,475.1	400.6	32° 0' 52.961 N	103° 17' 39.702 W
14,400.0	90.00	179.33	12,049.0	-2,575.1	401.7	32° 0' 51.972 N	103° 17' 39.700 W
14,500.0	90.00	179.33	12,049.0	-2,675.1	402.9	32° 0' 50.982 N	103° 17' 39.697 W
14,600.0	90.00	179.33	12,049.0	-2,775.1	404.1	32° 0' 49.992 N	103° 17' 39.695 W
14,700.0	90.00	179.33	12,049.0	-2,875.1	405.2	32° 0' 49.003 N	103° 17' 39.692 W
14,800.0	90.00	179.33	12,049.0	-2,975.1	406.4	32° 0' 48.013 N	103° 17' 39.690 W
14,900.0	90.00	179.33	12,049.0	-3,075.1	407.6	32° 0' 47.024 N	103° 17' 39.688 W
15,000.0	90.00	179.33	12,049.0	-3,175.1	408.7	32° 0' 46.034 N	103° 17' 39.685 W
15,100.0	90.00	179.33	12,049.0	-3,275.1	409.9	32° 0' 45.045 N	103° 17' 39.683 W
15,200.0	90.00	179.33	12,049.0	-3,375.1	411.1	32° 0' 44.055 N	103° 17' 39.680 W
15,300.0	90.00	179.33	12,049.0	-3,475.1	412.2	32° 0' 43.066 N	103° 17' 39.678 W
15,400.0	90.00	179.33	12,049.0	-3,575.1	413.4	32° 0' 42.076 N	103° 17' 39.676 W
15,500.0	90.00	179.33	12,049.0	-3,675.1	414.6	32° 0' 41.087 N	103° 17' 39.673 W
15,600.0	90.00	179.33	12,049.0	-3,775.0	415.7	32° 0' 40.097 N	103° 17' 39.671 W
15,700.0	90.00	179.33	12,049.0	-3,875.0	416.9	32° 0' 39.108 N	103° 17' 39.669 W
15,800.0	90.00	179.33	12,049.0	-3,975.0	418.1	32° 0' 38.118 N	103° 17' 39.666 W
15,900.0	90.00	179.33	12,049.0	-4,075.0	419.2	32° 0' 37.129 N	103° 17' 39.664 W
16,000.0	90.00	179.33	12,049.0	-4,175.0	420.4	32° 0' 36.139 N	103° 17' 39.661 W
16,100.0	90.00	179.33	12,049.0	-4,275.0	421.6	32° 0' 35.150 N	103° 17' 39.659 W
16,200.0	90.00	179.33	12,049.0	-4,375.0	422.7	32° 0' 34.160 N	103° 17' 39.657 W
16,300.0	90.00	179.33	12,049.0	-4,475.0	423.9	32° 0' 33.171 N	103° 17' 39.654 W
16,400.0	90.00	179.33	12,049.0	-4,575.0	425.1	32° 0' 32.181 N	103° 17' 39.652 W
16,500.0	90.00	179.33	12,049.0	-4,675.0	426.2	32° 0' 31.192 N	103° 17' 39.649 W
16,600.0	90.00	179.33	12,049.0	-4,775.0	427.4	32° 0' 30.202 N	103° 17' 39.647 W
16,700.0	90.00	179.33	12,049.0	-4,875.0	428.6	32° 0' 29.213 N	103° 17' 39.645 W
16,800.0	90.00	179.33	12,049.0	-4,975.0	429.7	32° 0' 28.223 N	103° 17' 39.642 W
16,900.0	90.00	179.33	12,049.0	-5,075.0	430.9	32° 0' 27.234 N	103° 17' 39.640 W
17,000.0	90.00	179.33	12,049.0	-5,174.9	432.1	32° 0' 26.244 N	103° 17' 39.637 W
17,100.0	90.00	179.33	12,049.0	-5,274.9	433.2	32° 0' 25.254 N	103° 17' 39.635 W
17,200.0	90.00	179.33	12,049.0	-5,374.9	434.4	32° 0' 24.265 N	103° 17' 39.633 W
17,300.0	90.00	179.33	12,049.0	-5,474.9	435.6	32° 0' 23.275 N	103° 17' 39.630 W
17,400.0	90.00	179.33	12,049.0	-5,574.9	436.7	32° 0' 22.286 N	103° 17' 39.628 W



**Company:** Ameredev Operating, LLC.  
**Project:** Green Jacket  
**Site:** Green Jacket WC1's  
**Well:** Green Jacket 101H  
**Wellbore:** Wellbore #1  
**Design:** Design #1

**Local Co-ordinate Reference:** Well Green Jacket 101H  
**TVD Reference:** KB @ 2951.0usft  
**MD Reference:** KB @ 2951.0usft  
**North Reference:** Grid  
**Survey Calculation Method:** Minimum Curvature  
**Database:** EDM5000

**Planned Survey**

MD (usft)	Inc (°)	Azi (azimuth) (°)	TVD (usft)	+FSL/-FNL (usft)	+FWL/-FEL (usft)	Latitude	Longitude
17,500.0	90.00	179.33	12,049.0	-5,674.9	437.9	32° 0' 21.296 N	103° 17' 39.625 W
17,600.0	90.00	179.33	12,049.0	-5,774.9	439.1	32° 0' 20.307 N	103° 17' 39.623 W
17,700.0	90.00	179.33	12,049.0	-5,874.9	440.2	32° 0' 19.317 N	103° 17' 39.621 W
17,800.0	90.00	179.33	12,049.0	-5,974.9	441.4	32° 0' 18.328 N	103° 17' 39.618 W
17,900.0	90.00	179.33	12,049.0	-6,074.9	442.6	32° 0' 17.338 N	103° 17' 39.616 W
18,000.0	90.00	179.33	12,049.0	-6,174.9	443.7	32° 0' 16.349 N	103° 17' 39.614 W
18,100.0	90.00	179.33	12,049.0	-6,274.9	444.9	32° 0' 15.359 N	103° 17' 39.611 W
18,200.0	90.00	179.33	12,049.0	-6,374.9	446.1	32° 0' 14.370 N	103° 17' 39.609 W
18,300.0	90.00	179.33	12,049.0	-6,474.9	447.2	32° 0' 13.380 N	103° 17' 39.606 W
18,400.0	90.00	179.33	12,049.0	-6,574.9	448.4	32° 0' 12.391 N	103° 17' 39.604 W
18,500.0	90.00	179.33	12,049.0	-6,674.8	449.6	32° 0' 11.401 N	103° 17' 39.602 W
18,600.0	90.00	179.33	12,049.0	-6,774.8	450.7	32° 0' 10.412 N	103° 17' 39.599 W
18,700.0	90.00	179.33	12,049.0	-6,874.8	451.9	32° 0' 9.422 N	103° 17' 39.597 W
18,800.0	90.00	179.33	12,049.0	-6,974.8	453.1	32° 0' 8.433 N	103° 17' 39.594 W
18,900.0	90.00	179.33	12,049.0	-7,074.8	454.2	32° 0' 7.443 N	103° 17' 39.592 W
19,000.0	90.00	179.33	12,049.0	-7,174.8	455.4	32° 0' 6.454 N	103° 17' 39.590 W
19,100.0	90.00	179.33	12,049.0	-7,274.8	456.6	32° 0' 5.464 N	103° 17' 39.587 W
19,200.0	90.00	179.33	12,049.0	-7,374.8	457.7	32° 0' 4.475 N	103° 17' 39.585 W
19,300.0	90.00	179.33	12,049.0	-7,474.8	458.9	32° 0' 3.485 N	103° 17' 39.582 W
19,400.0	90.00	179.33	12,049.0	-7,574.8	460.1	32° 0' 2.495 N	103° 17' 39.580 W
GJ101 LTP							
19,490.3	90.00	179.33	12,049.0	-7,665.1	461.1	32° 0' 1.602 N	103° 17' 39.578 W
GJ101 BHL							

Checked By: \_\_\_\_\_ Approved By: \_\_\_\_\_ Date: \_\_\_\_\_

# 5M Annular Preventer Variance Request and Well Control Procedures

Note: A copy of the Well Control Plan must be available at multiple locations on the rig for review by rig personnel, as well as review by the BLM PET/PE, and a copy must be maintained on the rig floor.

## Dual Isolation Design for 5M Annular Exception

Ameredev will utilize 13-5/8" 10M (5M Annular) BOPE System consisting of:

- 13-5/8" 5M Annular
- 13-5/8" 10M Upper Pipe Rams
  - 3-1/2" – 5-1/2" Variable Bore Ram
- 13-5/8" 10M Blind Rams
- 13-5/8" 10M Drilling Spool /w 2 - 4" 10M Outlets Double 10M Isolation Valves
- 13-5/8" 10M Lower Blind Rams
  - 3-1/2" – 5-1/2" Variable Bore Ram

All drilling components and casing associated to exposure > 5000 psi BHP requiring a 10M system will have a double isolation (secondary barrier) below the 5M Annular that would provide a barrier to flow. The mud system will always be primary barrier, it will be maintained by adjusting values based on tourly mud tests and monitoring a PVT System to maintain static wellbore conditions, displacement procedures will be followed and recorded on daily drilling reports during tripping operations. Surge and swab pressure values will be calculated and maintained and static flow check will be monitored at previous casing shoe and verified static well conditions prior to tripping out of hole and again prior to pulling last joint of drill pipe through BOPE. The below table, documents that two barriers to flow can be maintained at all times, independent of the rating of the annular preventer.

Drill Components	Size	Primary Barrier	Secondary Barrier	Third Barrier
Drillpipe	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
HWDP Drillpipe	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
Drill Collars	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
Production Casing	3-1/2"-5-1/2"	Drilling Fluid	Upper Pipe Rams	Lower Pipe Rams
Open Hole	13-5/8	Drilling Fluid	Blind Rams	
All Drilling Components in 10M Environment will have OD that will allow full Operational RATED WORKING PRESSURE for system design. Kill line with minimum 2" ID will be available outside substructure with 10M Check Valve for OOH Kill Operations				

# Well Control Procedures

Proper well control procedures are dependent to differentiating well conditions, to cover the basic well control operations there are will be standard drilling ahead, tripping pipe, tripping BHA, running casing, and pipe out of the hole/open hole scenarios that will be defined by procedures below. Initial Shut In Pressure can be taken against the Uppermost BOPE component the 5M Annular, pressure control can be transferred from the lesser 5M Annular to the 10M Upper Pipe Rams if needed. Shut In Pressures may be equal to or less than the Rated Working Pressure but at no time will the pressure on the annular preventer exceed the Rated Working Pressure of the annular. The annular will be tested to 5,000 psi. This will be the Rated Working Pressure of the annular preventer. All scenarios will be written such as shut in will be performed by closing the 10,000 psi Upper Pipe Rams for faster Accumulator pressure recovery to allow safer reaction to controlling wellbore pressure.

## Shutting In While Drilling

1. Sound alarm signaling well control event to Rig Crew
2. Space out drill string to allow FOSV installation
3. Shut down pumps
4. Shut in Upper Pipe Rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
5. Install open, full open safety valve and close valve, Close Chokes
6. Verify well is shut-in and flow has stopped
7. Notify supervisory personnel
8. Record data (SIDP, SICP, Pit Gain, and Time)
9. Hold pre-job safety meeting and discuss kill procedure

## Shutting In While Tripping

1. Sound alarm signaling well control event to Rig Crew
2. Space out drill string to allow FOSV installation
3. Shut in Upper Pipe Rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
4. Install open, full open safety valve and close valve, Close Chokes
5. Verify well is shut-in and flow has stopped
6. Notify supervisory personnel
7. Record data (SIDP, SICP, Pit Gain, and Time)
8. Hold pre-job safety meeting and discuss kill procedure

### **Shutting In While Running Casing**

1. Sound alarm signaling well control event to Rig Crew
2. Space out casing to allow circulating swedge installation
3. Shut in Upper Pipe Rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
4. Install circulating swedge, Close high pressure, low torque valves, Close Chokes
5. Verify well is shut-in and flow has stopped
6. Notify supervisory personnel
7. Record data (SIDP, SICP, Pit Gain, and Time)
8. Hold Pre-job safety meeting and discuss kill procedure

### **Shutting in while out of hole**

1. Sound alarm signaling well control event to Rig Crew
2. Shut-in well: close blind rams and open HCR against Open Chokes and Valves  
Open to working pressure gauge
3. Close Chokes, Verify well is shut-in and monitor pressures
4. Notify supervisory personnel
5. Record data (SIDP, SICP, Pit Gain, and Time)
6. Hold Pre-job safety meeting and discuss kill procedure

### **Shutting in prior to pulling BHA through stack**

Prior to pulling last joint of drill pipe thru the stack space out and check flow  
If flowing see steps below.

1. Sound alarm signaling well control event to Rig Crew
2. Shut in upper pipe ram and open HCR against Open Chokes and Valves Open  
to working pressure gauge
3. Install open, full open safety valve and close valve, Close Chokes
4. Verify well is shut-in and flow has stopped
5. Notify supervisory personnel
6. Record data (SIDP, SICP, Pit Gain, and Time)
7. Hold pre-job safety meeting and discuss kill procedure

**Shutting in while BHA is in the stack and ram preventer and combo immediately available**

1. Sound alarm signaling well control event to Rig Crew
2. Space out BHA with upset just beneath the compatible pipe ram
3. Shut in upper compatible pipe ram and open HCR against Open Chokes and Valves Open to working pressure gauge
4. Install open, full open safety valve and close valve, Close Chokes
5. Verify well is shut-in and flow has stopped
6. Notify supervisory personnel
7. Record data (SIDP, SICP, Pit Gain, and Time)
8. Hold pre-job safety meeting and discuss kill procedure

\*FOSV will be on rig floor in open position with operating handle for each type of connection utilized and tested to 10,000 psi

**Shutting in while BHA is in the stack and no ram preventer or combo immediately available**

1. Sound alarm signaling well control event to Rig Crew
2. If possible pick up high enough, to pull string clear and follow "Open Hole" scenario

If not possible to pick up high enough:

3. Stab Crossover, make up one joint/stand of drill pipe, and install open, full open safety valve (Leave Open)
4. Space out drill string with upset just beneath the compatible pipe ram.
5. Shut in upper compatible pipe ram and open HCR against Open Chokes and Valves Open to working pressure gauge
6. Close FOSV, Close Chokes, Verify well is shut-in and flow has stopped
7. Notify supervisory personnel
8. Record data (SIDP, SICP, Pit Gain, and Time)
9. Hold pre-job safety meeting and discuss kill procedure

## Pressure Control Plan

### Pressure Control Equipment

- Following setting of 13-3/8" Surface Casing Ameredev will install 13-5/8 MB4 Multi Bowl Casing Head by welding on a 13-5/8 SOW x 13-5/8" 5M in combination with 13-5/8 5M x 13-5/8 10M B-Sec to Land Intm #1 and a 13-5/8 10M x 13-5/8 10M shouldered to land C-Sec to Land Intm #2 (Installation procedure witnessed and verified by a manufacturer's representative).
- Casing will be tested to 1500 psi or .22 psi/ft whichever is greater for 30 minutes with <10% leak off, but will not exceed 70% of the burst rating per Onshore Order No. 2.
- Ameredev will install a 5M System Blowout Preventer (BOPE) with a 5M Annular Preventer and related equipment (BOPE). Full testing will be performed utilizing a full isolation test plug and limited to 5,000 psi MOP of MB4 Multi Bowl Casing Head. Pressure will be held for 10 min or until provisions of test are met on all valves and rams. The 5M Annular Preventer will be tested to 50% of approved working pressure (2,500 psi). Casing will be tested to 1500 psi or .22 psi/ft whichever is greater for 30 minutes with <10% leak off, but will not exceed 70% of the burst rating per Onshore Order No. 2.
- Setting of 9-5/8" Intermediate will be done by landing a wellhead hanger in the 13-5/8" 5M Bowl, Cementing and setting Well Head Packing seals and testing same. (Installation procedure witnessed and verified by a manufacturer's representative) Casing will be tested to 1500 psi or .22 psi/ft whichever is greater for 30 minutes with <10% leak off, but will not exceed 70% of the burst rating per Onshore Order No. 2.
- Full testing will be performed utilizing a full isolation test plug to 10,000 psi MOP of MB4 Multi Bowl B-Section. Pressure will be held for 10 min or until provisions of test are met on all valves and rams. The 5M Annular Preventer will be tested to 100% of approved working pressure (5,000 psi).
- Before drilling >20ft of new formation under the 9-5/8" Casing Shoe a pressure integrity test of the Casing Shoe will be performed to minimum of the MWE anticipated to control formation pressure to the next casing depth.
- Following setting of 5-1/2" Production Casing and adequate WOC time Ameredev will break 10M System Blowout Preventer (BOP) from 10M DOL-2 Casing Head, install annulus casing slips and test same (Installation procedure witnessed and verified by a manufacturer's representative) and install 11" 10M x 5-1/8" 15M Tubing Head (Installation procedure witnessed and verified by a manufacturer's representative). Ameredev will test head to 70% casing design and install Dry Hole cap with needle valve and pressure gauge to monitor well awaiting completion.

## Pressure Control Plan

- Slow pump speeds will be taken daily by each crew and recorded on Daily Drilling Report after mudding up.
- A choke manifold and accumulator with floor and remote operating stations will be functional and in place after installation of BOPE, as well as full functioning mud gas separator.
- Weekly BOPE pit level drills will be conducted by each crew and recorded on Daily Drilling Report.
- BOP will be fully operated when out of hole and will be documented on the daily drilling log.
- All B.O.P.s and associated equipment will be tested in accordance with Onshore Order #2
- All B.O.P. testing will be done by an independent service company.
- The B.O.P. will be tested within 21 days of the original test if drilling takes more time than planned.
- Ameredev requests a variance to connect the B.O.P. choke outlet to the choke manifold using a co-flex hose with a 10,000 psi working pressure that has been tested to 15,000psi and is built to API Spec 16C. Once the flex line is installed it will be tied down with safety clamps. (certifications will be sent to Carlsbad BLM Office prior to install)
- Ameredev requests a variance to install a 5M Annular Preventer on the 10M System to drill the Production Hole below the 9-5/8" Intermediate Section. 5M Annular will be tested to 100% working pressure (5,000 psi). A full well control procedure will be included to isolate well bore.

## **Ameredev Drilling Plan: 3 String with 4 String Contingency**

- Contingency Plan If Losses Exceed 50% in Intermediate Interval
  - We will utilize a MB4 wellhead that will enable us to convert a 3 string design to a 4 string design. (Schematic Attached)
  - We will displace well with FW and drill or condition to run 9-5/8" Casing at the Lamar Limestone, we will utilize DV Tool w/ ACP @ the Tansill to Isolate Capitan Reef and cement to surface.
  - Casing will be tested to 1500 psi or .22 psi/ft whichever is greater for 30 minutes with <10% leak off, but will not exceed 70% of the burst rating per Onshore Order No. 2.
- 7.625 Casing will be Additional 4<sup>th</sup> String
  - Drill remaining hole section to 10,670'
  - Run 7.625 29.7# HCL80 FJM Casing



# 4-String Contingency Wellbore Schematic

<b>Well:</b>	(Well Name)	<b>Co. Well ID:</b>	xxxxxx
<b>SHL:</b>	(SHL)	<b>AFE No.:</b>	xxxx-xxx
<b>BHL:</b>	(BHL)	<b>API No.:</b>	xxxxxxxxxxx
	Lea, NM	<b>GL:</b>	(Elevation)'
<b>Wellhead:</b>	A - 13-5/8" 10M x 13-5/8" SOW	<b>Field:</b>	Delaware
	B - 13-5/8" 10M x 13-5/8" 10M	<b>Objective:</b>	Wolfcamp B
	C - 13-5/8" 10M x 13-5/8" 10M	<b>TVD:</b>	(TVD)'
	Tubing Spool - 5-1/8" 15M x 13-3/8" 10M	<b>MD:</b>	(MD)'
<b>Xmas Tree:</b>	2-9/16" 10M	<b>Rig:</b>	TBD KB 27'
<b>Tubing:</b>	2-7/8" L-80 6.5# 8rd EUE	<b>E-Mail:</b>	Wellsite2@ameredev.com


Hole Size	Formation Tops	Logs	Cement	Mud Weight
17.5"	Rustler 125' below Rustler 13.375" 54.5# J-55 BTC		TOC 0' 100% Excess	8.4-8.6 ppg WBM
12.25"	Salado DV Tool with ACP At Tansill Tansill Capitan Reef Lamar 50' below Lamar 9.625" 40# L-80HC BTC		TOC 0' 50% Excess TOC 0' 50% Excess	8.3-10.2 Fresh Water
8.75"	Bell Canyon Brushy Canyon Bone Spring Lime First Bone Spring Second Bone Spring Third Bone Spring Upper 125' below TBSG Upper 7.625" 29.7# L-80HC FJM		TOC 0' 25% Excess	8.5-9.4 Diesel Brine Emulsion
6.75" 12° Build @ KOP	Third Bone Spring Wolfcamp Wolfcamp B (If Applicable) 5.5" 20# P-110CYHP TMK UP SF TORQ (MD) Target Wolfcamp B TVD // MD		TOC 0' 25% Excess	10.5-14 ppg OBM

**\*\*EXAMPLE ONLY - NOT FOR CONSTRUCTION\*\***

**Contingency Casing Design and Safety Factor Check**

<b>Casing Specifications</b>						
<b>Segment</b>	<b>Hole ID</b>	<b>Depth</b>	<b>OD</b>	<b>Weight</b>	<b>Grade</b>	<b>Coupling</b>
Surface	17.5	1,888'	13.375	54.5	J-55	BTC
Int #1	12.25	5,013'	9.625	40	HCL-80	BTC
Int #2	8.75	11,147'	7.625	29.7	HCL-80	FJM
Prod Segment A	6.75	11,147'	5.5	20	CYHP-110	TMK UPSF
Prod Segment B	6.75	22,496'	5.5	20	CYHP-110	TMK UPSF

<b>Check Surface Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
inches	1000 lbs	1000 lbs	psi	psi
14.38	853	909	1,130	2,730
<b>Safety Factors</b>				
1.56	8.29	8.83	1.15	0.91
<b>Check Int #1 Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
inches	1000 lbs	1000 lbs	psi	psi
10.625	916	1042	4230	5750
<b>Safety Factors</b>				
0.81	4.57	5.20	1.41	0.95
<b>Check Int #2 Casing</b>				
OD Cplg	Body	Joint	Collapse	Burst
inches	1000 lbs	1000 lbs	psi	psi
7.625	940	558	6700	9460
<b>Safety Factors</b>				
0.56	2.84	1.96	1.10	1.24
<b>Check Prod Casing, Segment A</b>				
OD Cplg	Body	Joint	Collapse	Burst
inches	1000 lbs	1000 lbs	psi	psi
5.777	728	655	12780	14360
<b>Safety Factors</b>				
0.49	3.11	2.79	1.77	1.89
<b>Check Prod Casing, Segment B</b>				
OD Cplg	Body	Joint	Collapse	Burst
inches	1000 lbs	1000 lbs	psi	psi
5.777	728	655	12780	14360
<b>Safety Factors</b>				
0.49	63.53	57.16	1.68	1.89

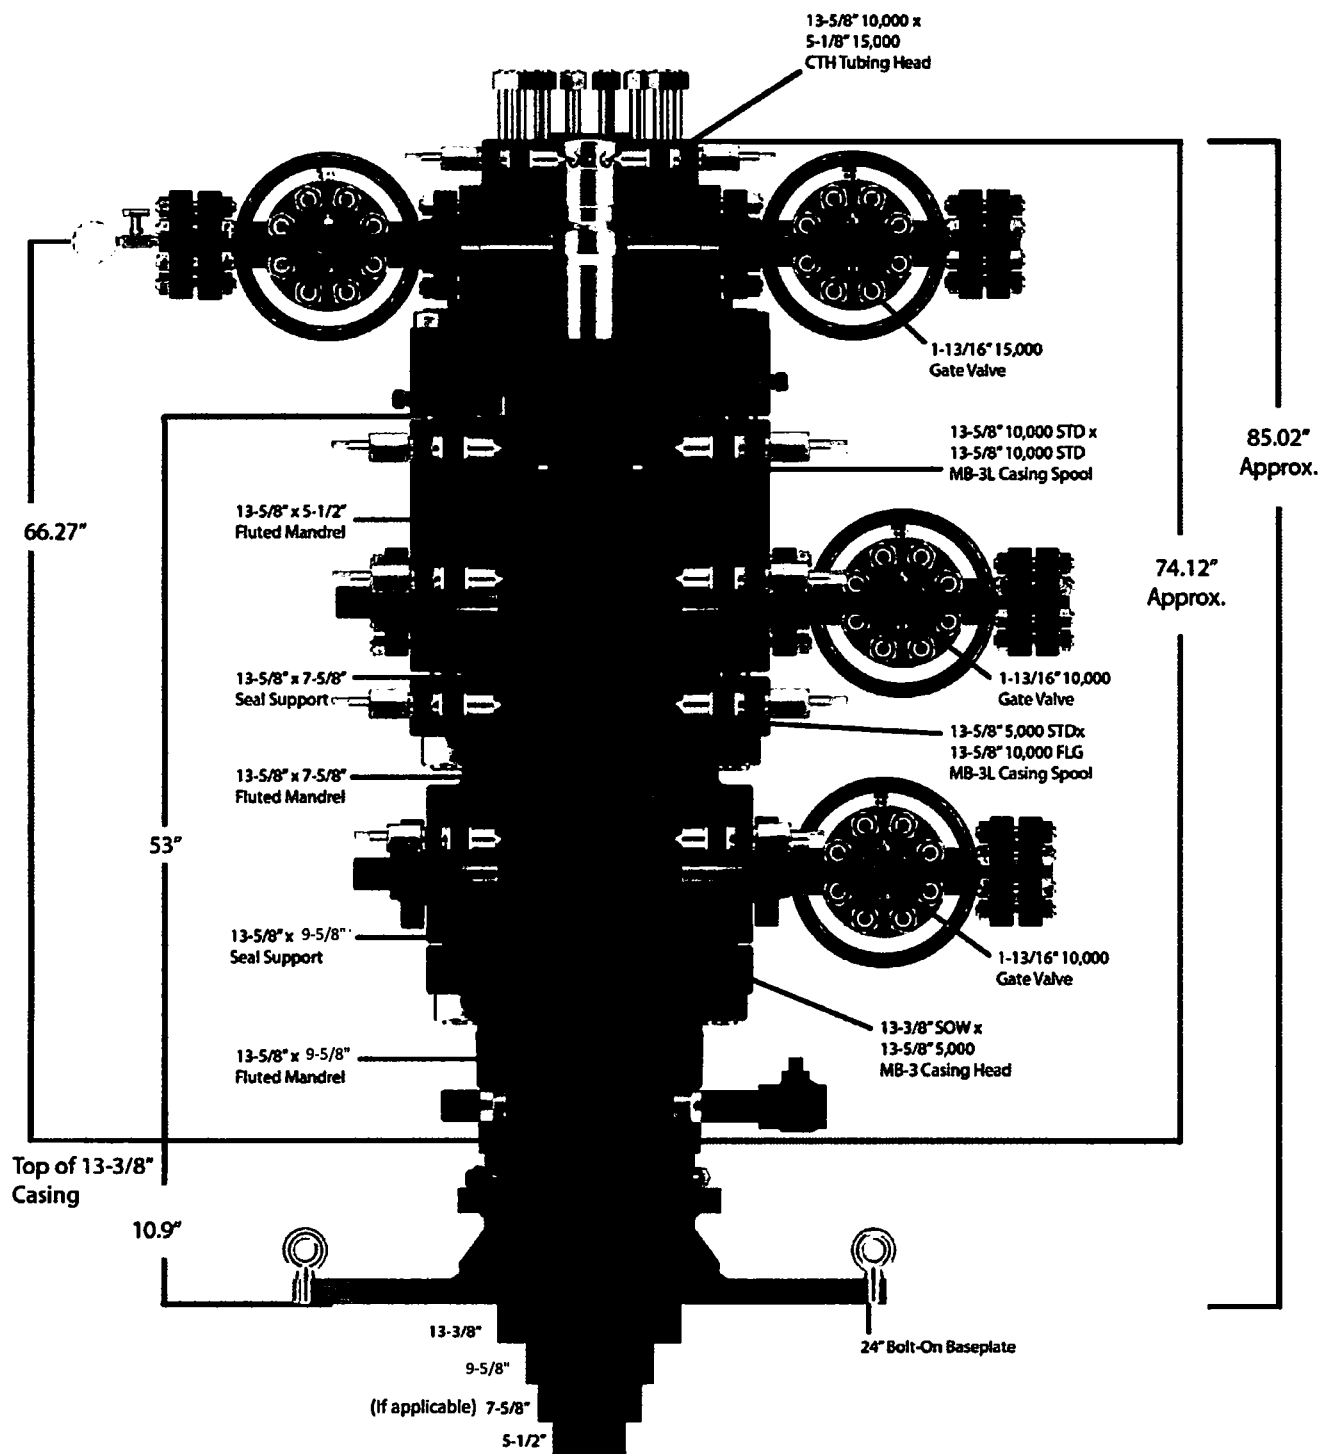

## Quotation

## Downing Wellhead Equipment

Oklahoma City,  
Oklahoma - USA

### Reference Data:

16925 AMEREDEV

### Proprietary and Confidential

The information contained in this drawing is the sole property of Downing Wellhead Equipment, any reproduction in part or in whole without the written permission of Downing Wellhead Equipment is prohibited.

### TITLE:

AMEREDEV

DRAWN

CHECKED

APPROVED

SIZE

A

DWG. NO.

Scale:

Weight:

REV

Sheet:

**\*\*EXAMPLE ONLY - NOT FOR CONSTRUCTION\*\***

Stage 1 Lead	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th style="width:15%;">Hole Size</th> <th style="width:15%;">Casing Size</th> <th style="width:15%;">Depth</th> <th style="width:15%;">Sacks</th> <th style="width:15%;">Yield</th> <th style="width:15%;">Density</th> </tr> <tr> <td align="center">17.5</td> <td align="center">13.375</td> <td align="center">1888</td> <td align="center">1,337</td> <td align="center">1.76</td> <td align="center">13.5</td> </tr> </table>						Hole Size	Casing Size	Depth	Sacks	Yield	Density	17.5	13.375	1888	1,337	1.76	13.5
	Hole Size	Casing Size	Depth	Sacks	Yield	Density												
	17.5	13.375	1888	1,337	1.76	13.5												
	Bbl/Sk 0.31372549																	
	bbls 419.402246																	
	Stage Tool Depth N/A																	
	Top MD of Segment 0																	
	Bottom MD of Segment 1502																	
	Cement Type C																	
	Additives Bentonite, Accelerator, Kolseal, Defoamer, Celloflake																	
	Quantity (sks) 1,337																	
	Yield (cu ft/sk) 1.76																	
	Density (lbs/gal) 13.5																	
	Volume (cu ft) 2,352.85																	
Percent Excess 100%																		
Column Height 3,389.88																		
<div style="display: flex; justify-content: space-between;"> <div> <b>Target TOC</b> 0            Calc TOC -1888            calc vol 0.12372195         </div> <div> <table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th style="width:15%;">Sacks</th> <th style="width:15%;">Yield</th> <th style="width:15%;">Density</th> </tr> <tr> <td align="center">233.587041</td> <td align="center">291.9838012</td> <td align="center">14.8</td> </tr> </table> </div> <div>           25% Excess 100%            467.174082         </div> </div>						Sacks	Yield	Density	233.587041	291.9838012	14.8							
Sacks	Yield	Density																
233.587041	291.9838012	14.8																
Stage 1 Tail	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th style="width:15%;">Hole Size</th> <th style="width:15%;">Casing Size</th> <th style="width:15%;">Depth</th> <th style="width:15%;">Sacks</th> <th style="width:15%;">Yield</th> <th style="width:15%;">Density</th> </tr> <tr> <td align="center">17.5</td> <td align="center">13.375</td> <td align="center">1888</td> <td align="center">200</td> <td align="center">1.34</td> <td align="center">14.8</td> </tr> </table>						Hole Size	Casing Size	Depth	Sacks	Yield	Density	17.5	13.375	1888	200	1.34	14.8
	Hole Size	Casing Size	Depth	Sacks	Yield	Density												
	17.5	13.375	1888	200	1.34	14.8												
	Bbl/Sk 0.23885918																	
	bbls 47.77183601																	
	Top MD of Segment 1502																	
	Bottom MD of Segment 1888																	
	Cement Type C																	
	Additives																	
	Quantity (sks) 200																	
	Yield (cu ft/sk) 1.34																	
	Density (lbs/gal) 14.8																	
	Volume (cu ft) 268																	
	Percent Excess 100%																	
Column Height 386.1225606																		

**SURFACE CEMENT**

**\*\*EXAMPLE ONLY - NOT FOR CONSTRUCTION\*\***

Stage 1	Lead	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th>Hole Size</th><th>Casing Size</th><th>Depth</th><th>Sacks</th><th>Yield</th><th>Density</th></tr> <tr> <td>12.25</td><td>9.625</td><td>5013</td><td>0.623885918</td><td>3.5</td><td>9</td></tr> </table>	Hole Size	Casing Size	Depth	Sacks	Yield	Density	12.25	9.625	5013	0.623885918	3.5	9				
		Hole Size	Casing Size	Depth	Sacks	Yield	Density											
12.25	9.625	5013	0.623885918	3.5	9													
<div style="display: flex; justify-content: space-between;"> <div>             Bbl/Sk 0.623885918              bbls 372.0365733              Stage Tool Depth N/A              Top MD of Segment 0              Bottom MD of Segment 4163              Cement Type C              Additives Bentonite,Salt,Kolseal,Defoamer,Celloclake           </div> <div>             Quantity (sks) 596              Yield (cu ft/sk) 3.5              Density (lbs/gal) 9              Volume (cu ft) 2,087.13              Percent Excess 50%              Column Height 6,669.49           </div> <div>             Target % 50%           </div> </div>																		
<div style="display: flex; justify-content: space-between;"> <div> <b>Target TOC</b> 0              Calc TOC -2506.5              calc vol 0.055781888           </div> <div>             bbl 279.6346021              25% Excess 349.5432526              50% 419.4519031           </div> </div>																		
Stage 1	Tail	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th>Hole Size</th><th>Casing Size</th><th>Depth</th><th>Sacks</th><th>Yield</th><th>Density</th></tr> <tr> <td>12.25</td><td>9.625</td><td>5013</td><td>0.237076649</td><td>1.33</td><td>14.8</td></tr> </table>	Hole Size	Casing Size	Depth	Sacks	Yield	Density	12.25	9.625	5013	0.237076649	1.33	14.8				
		Hole Size	Casing Size	Depth	Sacks	Yield	Density											
12.25	9.625	5013	0.237076649	1.33	14.8													
<div style="display: flex; justify-content: space-between;"> <div>             Bbl/Sk 0.237076649              bbls 47.41532977              Top MD of Segment 4163              Bottom MD of Segment 5013              Cement Type C              Additives           </div> <div>             Quantity (sks) 200              Yield (cu ft/sk) 1.33              Density (lbs/gal) 14.8              Volume (cu ft) 266              Percent Excess 25%              Column Height 850.013004           </div> </div>																		

INTERMEDIATE 1 CEMENT - STAGE 1

**\*\*EXAMPLE ONLY - NOT FOR CONSTRUCTION\*\***

Stage 2

Lead

Hole Size	Casing Size	Depth	Sacks	Yield	Density
12.25	9.625	3262	981	3.5	9

Bbl/Sk

0.623885918

bbls

225.5254458

Stage Tool Depth

N/A

Top MD of Segment

0

Bottom MD of Segment

2412

Cement Type

C

Additives

Bentonite, Salt, Kolseal, Defoamer, Cellocake

Quantity (sks)

361

Yield (cu ft/sk)

3.5

Density (lbs/gal)

9

Volume (cu ft)

1,265.20

Percent Excess

50%

Column Height

4,042.99

Target %

50%

Target TOC

0

Calc TOC

-1631

calc vol

0.055781888

bbl

181.960517

25% Excess

227.4506463

50%

272.9407756

Stage 2

Tail

Hole Size	Casing Size	Depth	Sacks	Yield	Density
12.25	9.625	3262	981	1.33	14.8

Bbl/Sk

0.237076649

bbls

47.41532977

Top MD of Segment

2412

Bottom MD of Segment

3262

Cement Type

C

Additives

Quantity (sks)

200

Yield (cu ft/sk)

1.33

Density (lbs/gal)

14.8

Volume (cu ft)

266

Percent Excess

25%

Column Height

850.013004

INTERMEDIATE 1 CEMENT - STAGE 2

**\*\*EXAMPLE ONLY - NOT FOR CONSTRUCTION\*\***

<div>Stage 1</div> <div>Lead</div>	<table border="1"> <tr> <th>Hole Size</th><th>Casing Size</th><th>Depth</th><th>Sacks</th><th>Yield</th><th>Density</th></tr> <tr> <td>8.75</td><td>7.625</td><td>10670</td><td>131</td><td>2.47</td><td>9</td></tr> </table> <div> <div>Bbl/Sk0.440285205</div> <div>bbls168.6309595</div> <div>Stage Tool DepthN/A</div> <div>Top MD of Segment0</div> <div>Bottom MD of Segment6755</div> <div>Cement TypeH</div> <div>AdditivesBentonite, Retarder, Kolseal, Defoamer, Celloflake, Anti-Settling</div> <div>Expansion Additive</div> </div> <div> <div>Quantity (sks)383</div> <div>Yield (cu ft/sk)2.47</div> <div>Density (lbs/gal)9</div> <div>Volume (cu ft)946.02</div> <div>Percent Excess25%</div> <div>Column Height9,422.97</div> </div> <div> <div>Target %25%</div> <div>Target TOC0</div> <div>Calc TOC-2667.5</div> <div>calc vol0.01789574</div> <div> <table border="1"> <tr> <th>bbl</th><th>25% Excess</th></tr> <tr> <td>190.9475483</td><td>238.6844354</td></tr> </table> </div> <div>238.6844354</div> </div>	Hole Size	Casing Size	Depth	Sacks	Yield	Density	8.75	7.625	10670	131	2.47	9	bbl	25% Excess	190.9475483	238.6844354
	Hole Size	Casing Size	Depth	Sacks	Yield	Density											
	8.75	7.625	10670	131	2.47	9											
	bbl	25% Excess															
	190.9475483	238.6844354															
	<div>Stage 1</div> <div>Tail</div>	<table border="1"> <tr> <th>Hole Size</th><th>Casing Size</th><th>Depth</th><th>Sacks</th><th>Yield</th><th>Density</th></tr> <tr> <td>8.75</td><td>7.625</td><td>10670</td><td>131</td><td>1.31</td><td>14.2</td></tr> </table> <div> <div>Bbl/Sk0.233511586</div> <div>bbls70.05347594</div> <div>Top MD of Segment6755</div> <div>Bottom MD of Segment10670</div> <div>Cement TypeH</div> <div>AdditivesSalt, Bentonite, Retarder, Dispersant, Fluid Loss</div> </div> <div> <div>Quantity (sks)300</div> <div>Yield (cu ft/sk)1.31</div> <div>Density (lbs/gal)14.2</div> <div>Volume (cu ft)393</div> <div>Percent Excess25%</div> <div>Column Height3914.533571</div> </div>	Hole Size	Casing Size	Depth	Sacks	Yield	Density	8.75	7.625	10670	131	1.31	14.2			
		Hole Size	Casing Size	Depth	Sacks	Yield	Density										
		8.75	7.625	10670	131	1.31	14.2										

INTERMEDIATE 2 CEMENT

**\*\*EXAMPLE ONLY - NOT FOR CONSTRUCTION\*\***

Stage 1 Lead	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th style="width:15%;">Hole Size</th> <th style="width:15%;">Casing Size</th> <th style="width:15%;">Depth</th> <th style="width:15%;">Sacks</th> <th style="width:15%;">Yield</th> <th style="width:15%;">Density</th> </tr> <tr> <td align="center">6.75</td> <td align="center">5.5</td> <td align="center">22496</td> <td align="center">1.751</td> <td align="center">1.34</td> <td align="center">14.2</td> </tr> </table>						Hole Size	Casing Size	Depth	Sacks	Yield	Density	6.75	5.5	22496	1.751	1.34	14.2
	Hole Size	Casing Size	Depth	Sacks	Yield	Density												
	6.75	5.5	22496	1.751	1.34	14.2												
	Bbl/Sk 0.23885918																	
	bbls 418.2897805																	
	Stage Tool Depth N/A																	
	Top MD of Segment 0																	
	Bottom MD of Segment 22496																	
	Cement Type H																	
	Additives Salt, Bentonite, Fluid Loss, Dispersant, Retarder, Defoamer																	
	Quantity (sks) 1,751																	
	Yield (cu ft/sk) 1.34																	
	Density (lbs/gal) 14.2																	
	Volume (cu ft) 2,346.61																	
	Percent Excess 25%																	
	Column Height 28,120.00																	
	<div style="display: flex; justify-content: space-between;"> <div> <b>Target TOC</b> 0            Calc TOC -5624            calc vol 0.01487517         </div> <div> <table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th style="width:15%;">bbl</th> <th style="width:15%;">25% Excess</th> <th style="width:15%;">25%</th> </tr> <tr> <td align="center">334.6318244</td> <td align="center">418.2897805</td> <td align="center">418.2897805</td> </tr> </table> </div> </div>						bbl	25% Excess	25%	334.6318244	418.2897805	418.2897805						
	bbl	25% Excess	25%															
	334.6318244	418.2897805	418.2897805															
Stage 1 Tail	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <th style="width:15%;">Hole Size</th> <th style="width:15%;">Casing Size</th> <th style="width:15%;">Depth</th> <th style="width:15%;">Sacks</th> <th style="width:15%;">Yield</th> <th style="width:15%;">Density</th> </tr> <tr> <td align="center">6.75</td> <td align="center">5.5</td> <td align="center">22496</td> <td align="center">0</td> <td align="center">0</td> <td align="center">0</td> </tr> </table>						Hole Size	Casing Size	Depth	Sacks	Yield	Density	6.75	5.5	22496	0	0	0
	Hole Size	Casing Size	Depth	Sacks	Yield	Density												
	6.75	5.5	22496	0	0	0												
	Bbl/Sk 0																	
	bbls 0																	
	Top MD of Segment 22496																	
	Bottom MD of Segment 22496																	
	Cement Type H																	
	Additives																	
	Quantity (sks) 0																	
	Yield (cu ft/sk) 0																	
	Density (lbs/gal) 0																	
	Volume (cu ft) 0																	
	Percent Excess																	
	Column Height 0																	

PRODUCTION CEMENT



# HALLIBURTON

Permian Basin, Ft Stockton

Lab Results- Lead

## Job Information

Request/Slurry	2488456/2	Rig Name		Date	18/DEC/2018
Submitted By	Dillon Briers	Job Type	Intermediate Casing	Bulk Plant	
Customer	Ameredev	Location	Lea	Well	

## Well Information

Casing/Liner Size	7.625 in	Depth MD	5013 ft	BHST	165°F
Hole Size	8.75 in	Depth TVD	5013 ft	BHCT	130°F

## Cement Information - Lead Design

Conc	UOM	Cement/Additive	Cement Properties		
100	% BWOC	NeoCem	Slurry Density	9	lbm/gal
14.68	gal/sack	Heated Fresh Water	Slurry Yield	3.5	ft <sup>3</sup> /sack
			Water Requirement	14.68	gal/sack

## Pilot Test Results Request ID 2488456/1

### API Rheology, Request Test ID:35665340

Temp (degF)	300	200	100	60	30	6	3	Cond Time (min)
-------------	-----	-----	-----	----	----	---	---	-----------------

80 (up)	82	67	49	42	39	36	28	0
80 (down)	82	59	35	26	18	10	9	0
80 (avg.)	82	63	42	34	29	23	19	0

PV (cP) & YP (lbs/100ft<sup>2</sup>): 61.73 22.32 (Least-squares method)

PV (cP) & YP (lbs/100ft<sup>2</sup>): 60 22 (Traditional method (300 & 100 rpm based))

Generalized Herschel-Bulkley 4: YP(lbf/100ft<sup>2</sup>)=20.33 MuInf(cP)=52.39 m=0.81 n=0.81

### API Rheology, Request Test ID:35665341

Temp (degF)	300	200	100	60	30	6	3	Cond Time (min)	Cond Temp (degF)
-------------	-----	-----	-----	----	----	---	---	-----------------	------------------

134 (up)	63	47	29	21	15	7	6	30	134
134 (down)	63	46	29	21	14	7	4	30	134
134 (avg.)	63	47	29	21	15	7	5	30	134

PV (cP) & YP (lbs/100ft<sup>2</sup>): 57.12 7.98 (Least-squares method)

PV (cP) & YP (lbs/100ft<sup>2</sup>): 51 12 (Traditional method (300 & 100 rpm based))

Generalized Herschel-Bulkley 4: YP(lbf/100ft<sup>2</sup>)=2.26 MuInf(cP)=30.64 m=0.41 n=0.41

### API Fluid Loss, Request Test ID:35665342

Test Temp (degF)	Test Pressure (psi)	Test Time (min)	Meas. Vol.	Calculated FL (<30 min)	Conditioning time (min)	Conditioning Temp (degF)
134	1000	9.12	52	189	30	134

This report is the property of Halliburton Energy Services and neither it nor any part thereof, nor a copy thereof, is to be published or disclosed without first securing the expressed written approval of Halliburton. It may however be used in the course of regular business operations by any person or concern receiving such report from Halliburton. This report is for information purposes only and the content is limited to the sample described. Halliburton makes no warranties, expressed or implied, as to the accuracy of the contents or results. Any user of this report agrees Halliburton shall not be liable for any loss or damage regardless of cause, including any act or omission of Halliburton, resulting from the use hereof.

**Free Fluid API 10B-2, Request Test ID:35665343**

Con. Temp (degF)	Cond. Time (min)	Static T. (F)	Static time (min)	Incl. (deg)	% Fluid
134	30	80	120	0	0

**Pilot Test Results Request ID 2504116/5****Thickening Time - ON-OFF-ON, Request Test ID:35852392**

Test Temp (degF)	Pressure (psi)	Reached in (min)	70 Bc (hh:mm)	Start Bc
126	5800	40	6:18	16

**UCA Comp. Strength, Request Test ID:35852394**

End Temp (degF)	Pressure (psi)	50 psi (hh:mm)	500 psi (hh:mm)	12 hr CS (psi)	24 hr CS (psi)	48 hr CS (psi)
159	4000	8:55	12:23	456	749	681


This report is the property of Halliburton Energy Services and neither it nor any part thereof, nor a copy thereof, is to be published or disclosed without first securing the expressed written approval of Halliburton. It may however be used in the course of regular business operations by any person or concern receiving such report from Halliburton. This report is for information purposes only and the content is limited to the sample described. Halliburton makes no warranties, expressed or implied, as to the accuracy of the contents or results. Any user of this report agrees Halliburton shall not be liable for any loss or damage regardless of cause, including any act or omission of Halliburton, resulting from the use hereof.



# U. S. Steel Tubular Products

6/8/2017 6:18:53 PM

7.625" 29.70lbs/ft (0.375" Wall) HCL80 USS-LIBERTY FJM®



MECHANICAL PROPERTIES	Pipe	USS-LIBERTY FJM®	
Minimum Yield Strength	110,000	--	psi
Maximum Yield Strength	140,000	--	psi
Minimum Tensile Strength	125,000	--	psi

DIMENSIONS	Pipe	USS-LIBERTY FJM®	
Outside Diameter	7.625	7.625	in.
Wall Thickness	0.375	--	in.
Inside Diameter	6.875	6.789	in.
Standard Drift	6.750	6.750	in.
Alternate Drift	--	--	in.
Nominal Linear Weight, T&C	29.70	--	lbs/ft
Plain End Weight	29.06	--	lbs/ft

SECTION AREA	Pipe	USS-LIBERTY FJM®	
Critical Area	8.541	5.074	sq. in.
Joint Efficiency	--	59.4	%

PERFORMANCE	Pipe	USS-LIBERTY FJM®	
Minimum Collapse Pressure	6,700	6,700	psi
Minimum Internal Yield Pressure	9,460	9,460	psi
Minimum Pipe Body Yield Strength	940,000	--	lbs
Joint Strength	--	558,000	lbs
Compression Rating	--	558,000	lbs
Reference Length	--	12,810	ft
Maximum Uniaxial Bend Rating	--	39.3	deg/100 ft

	Pipe	USS-LIBERTY FJM®	
Make-Up Loss	--	3.92	in.
Minimum Make-Up Torque	--	10,800	ft-lbs
Maximum Make-Up Torque	--	15,250	ft-lbs

1. Other than proprietary collapse and connection values, performance properties have been calculated using standard equations defined by API 5C3 and do not incorporate any additional design or safety factors. Calculations assume nominal pipe OD, nominal wall thickness and Specified Minimum Yield Strength (SMYS).
2. Compressive & Tensile Connection Efficiencies are calculated by dividing the connection critical area by the pipe body area.
3. Uniaxial bending rating shown is structural only, and equal to compression efficiency.
4. USS-LIBERTY FJM™ connections are optimized for each combination of OD and wall thickness and cannot be interchanged.
5. Torques have been calculated assuming a thread compound friction factor of 1.0 and are recommended only. Field make-up torques may require adjustment based on actual field conditions (e.g. make-up speed, temperature, thread compound, etc.).
6. Reference length is calculated by joint strength divided by nominal plain end weight with 1.5 safety factor.
7. Connection external pressure leak resistance has been verified to 100% API pipe body collapse pressure following the guidelines of API 5C5 Cal III.

## Legal Notice

USS-LIBERTY FJM® is a trademark of U. S. Steel Corporation. All material contained in this publication is for general information only. This material should not therefore be used or relied upon for any specific application without independent competent professional examination and verification of accuracy, suitability and applicability. Anyone making use of this material does so at their own risk and assumes any and all liability resulting from such use. U.S. Steel disclaims any and all expressed or implied warranties of fitness for any general or particular application.

U. S. Steel Tubular Products  
10343 Sam Houston Park Dr., #120  
Houston, TX 77064

1-877-893-9461  
connections@uss.com  
www.usstubular.com



## U. S. Steel Tubular Products

5 1/2 20.00 lb (0.361) P110 HP

USS-EAGLE SFH™

	PIPE	CONNECTION	
<b>MECHANICAL PROPERTIES</b>			
Minimum Yield Strength	125,000	125,000	psi
Maximum Yield Strength	140,000	140,000	psi
Minimum Tensile Strength	130,000	130,000	psi
<b>DIMENSIONS</b>			
Outside Diameter	5.500	5.830	in.
Wall Thickness	0.361		in.
Inside Diameter	4.778	4.693	in.
Drift - API	4.653	4.653	in.
Nominal Linear Weight, T&C	19.83		lbs/ft
Plain End Weight	19.83	19.83	lbs/ft
<b>SECTION AREA</b>			
Cross Sectional Area   Critical Area	5.828	5.054	sq. in.
Joint Efficiency		86.25	%
<b>PERFORMANCE</b>			
Minimum Collapse Pressure	13,150	13,150	psi
External Pressure Leak Resistance		10,000	psi
Minimum Internal Yield Pressure	14,360	14,360	psi
Minimum Pipe Body Yield Strength	729,000		lbs
Joint Strength		631,750	lbs
Compression Rating		631,750	lbs
Reference Length		21,240	ft
Maximum Uniaxial Bend Rating		89.9	deg/100 ft
<b>MAKE-UP</b>			
Minimum Make-Up Torque		14,000	ft-lbs
Maximum Make-Up Torque		16,900	ft-lbs
Maximum Operating Torque		25,000	ft-lbs
Make-Up Loss		5.92	in.

## Notes:

- 1) Other than proprietary collapse and connection values, performance properties have been calculated using standard equations defined by API 5C3 and do not incorporate any additional design or safety factors. Calculations assume nominal pipe OD, nominal wall thickness, and Specified Minimum Yield Strength (SMYS).
- 2) Compressive & Tensile Connection Efficiencies are calculated by dividing the connection critical area by the pipe body area.
- 3) Uniaxial bending rating shown is structural only, and equal to compression efficiency.
- 4) Torques have been calculated assuming a thread compound friction factor of 1.0 and are recommended only. Field make-up torques may require adjustment based on actual field conditions (e.g. make-up speed, temperature, thread compound, etc.).
- 5) Reference length is calculated by joint strength divided by plain end weight with 1.5 safety factor.
- 6) Connection external pressure resistance has been verified to 10,000 psi (Application specific testing).

Legal Notice: All material contained in this publication is for general information only. This material should not therefore be used or relied upon for any specific application without independent competent professional examination and verification of accuracy, suitability, and applicability. Anyone making use of this material does so at their own risk and assumes any and all liability resulting from such use. U. S. Steel disclaims any and all expressed or implied warranties of fitness for any general or particular application.  
Manuel USS Product Data Sheet 2017 rev25 (April)

U. S. Steel Tubular Products  
10343 Sam Houston Park Dr., #120  
Houston, TX 77064

1-877-893-9461  
connections@uss.com  
www.usstubular.com

QUALITY CONTROL	No.: QC-DB- 651 / 2013
	Page : 1 / 44
Hose No.: 66551, 66552, 66553, 66554	Revision : 0
	Date: 14. November 2013.
	Prepared by : <i>Scalá Sándor</i>
	Appr. by: <i>Scalá Sándor</i>

# CHOKE AND KILL HOSES

id.: 3" 69 MPa x 35 ft (10,67 m)

## DATA BOOK

Purchaser: H&P STOCK

Purchaser Order No.:

ContiTech Rubber Order No.: 537587

ContiTech Oil & Marine Corp. Order No.:  
4500370505

**NOT DESIGNED FOR WELL TESTING**

## CONTENT

	<u>Page</u>
1. API QMS Certificate (No.: 0760 )	3.
2. American Petroleum Institute Certificate of Authority To Use the Official API Monogram (No.: 16C-0004 )	4.
3. Quality Control Inspection and Test Certificates (No.: 1905, 1906, 1907, 1908 )	5-8.
4. Hose Data Sheet	9.
5. Metal Parts	
5.1. Raw Material Quality Certificates (No.: TR070687, EUR-265844, 86989/13-0)	10-13.
5.2. Hardness Test Reports (No.: 561/13, 562/13 )	14-15.
5.3. Ultrasonic Test Reports (No.: 513/13, 514/13, 515/13 )	16-18.
5.4. NDT Examiner Certificate (Name: Tóth Ákos József )	19-20.
5.5. Welding Procedure Specification (No.: 140-71 )	21-24.
5.6. Welding Procedure Qualification Record (No.: BUD 0700002/1 )	25-26.
5.7. Welder's Approval Test Certificate (No.: RK1825997.R1 )	27-28.
5.8. Welding Log Sheet (No.: 2013/2898 )	29.
5.9. Visual Examination Record (No.: 813/13 )	30.
5.10. NDT Examiner Certificate (Name: Kis Gábor Balázs )	31-32.
5.11. Radiographic Test Certificates (No.: 2431/13, 2430/13 )	33-34.
5.12. NDT Examiner Certificate (Name: Ménesi István )	35-36.
5.13. MP Examination Record (No.: 1222/13 )	37.
5.14. NDT Examiner Certificate (Name: Oravecz Gábor )	38-39.
6. Steel Cord	
6.1. Inspection Certificate (No.: 4046181212 )	40.
7. Outside Stripwound Tube	
7.1. Inspection Certificate (No.: 63892/2012 )	41.
8. Certificate of Calibration (Manometer Serial No.: 1518086 )	42-44.



ContiTech Rubber  
Industrial Kft.  
Quality Control Dept.  
(1)



U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## SUPO Data Report

07/08/2019

APD ID: 10400034498

Submission Date: 09/27/2018

Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

### Section 1 - Existing Roads

Will existing roads be used? YES

Existing Road Map:

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_WELL\_PAD\_ACCESS\_MAP\_REV\_20190516160010.pdf

Existing Road Purpose: ACCESS

Row(s) Exist? NO

ROW ID(s)

ID:

Do the existing roads need to be improved? NO

Existing Road Improvement Description:

Existing Road Improvement Attachment:

### Section 2 - New or Reconstructed Access Roads

Will new roads be needed? YES

New Road Map:

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_WELL\_PAD\_ACCESS\_MAP\_REV\_20190516160056.pdf

Green\_Jacket\_Road\_20190516160105.pdf

New road type: RESOURCE

Length: 4604

Feet

Width (ft.): 30

Max slope (%): 2

Max grade (%): 2

Army Corp of Engineers (ACOE) permit required? NO

ACOE Permit Number(s):

New road travel width: 20

New road access erosion control: Crowned and Ditched

New road access plan or profile prepared? NO

New road access plan attachment:

**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

**Access road engineering design?** NO

**Access road engineering design attachment:**

**Access surfacing type:** OTHER

**Access topsoil source:** ONSITE

**Access surfacing type description:** CALICHE

**Access onsite topsoil source depth:** 6

**Offsite topsoil source description:**

**Onsite topsoil removal process:** GRADER

**Access other construction information:** NM One Call (811) will be notified before construction start.

**Access miscellaneous information:**

**Number of access turnouts:**

**Access turnout map:**

### **Drainage Control**

**New road drainage crossing:** OTHER

**Drainage Control comments:** Crowned and Ditched

**Road Drainage Control Structures (DCS) description:** NONE

**Road Drainage Control Structures (DCS) attachment:**

### **Access Additional Attachments**

**Additional Attachment(s):**

### **Section 3 - Location of Existing Wells**

**Existing Wells Map?** YES

**Attach Well map:**

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_1\_MI\_RADIUS\_WELLS\_20180924124806.pdf

**Existing Wells description:**

### **Section 4 - Location of Existing and/or Proposed Production Facilities**

**Submit or defer a Proposed Production Facilities plan?** SUBMIT

**Production Facilities description:** Production will be transported via a buried 4" poly flowline, run approximately 13,281' from the Green Jacket Fed Com 26 36 29 101H to the existing Amen Corner CTB, northeast of the well pad. Should any type of production facilities be located on the well pad itself, they will be strategically placed to allow for maximum interim reclamation, re-contouring, and revegetation of the well location.

**Production Facilities map:**



**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

BO\_AMEN\_CORNER\_BATTERY\_SITE\_20190516160343.PDF

Green\_Jacket\_Flowline\_20190516160345.pdf

## Section 5 - Location and Types of Water Supply

### Water Source Table

**Water source use type:** DUST CONTROL,  
INTERMEDIATE/PRODUCTION CASING, STIMULATION, SURFACE  
CASING

**Water source type:** GW WELL

**Describe type:**

**Source longitude:**

**Source latitude:**

**Source datum:**

**Water source permit type:** PRIVATE CONTRACT

**Source land ownership:** PRIVATE

**Water source transport method:** PIPELINE,TRUCKING

**Source transportation land ownership:** FEDERAL

**Water source volume (barrels):** 20000

**Source volume (acre-feet):** 2.577862

**Source volume (gal):** 840000

**Water source and transportation map:**

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_WATER\_MAP\_REV\_20190516160444.pdf

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_WATER\_WELL\_LIST\_20190516160445.pdf

**Water source comments:** Water will be trucked or surface piped from existing water wells on private land. See attached list of available wells.

**New water well?** NO

### New Water Well Info

**Well latitude:**

**Well Longitude:**

**Well datum:**

**Well target aquifer:**

**Est. depth to top of aquifer(ft):**

**Est thickness of aquifer:**

**Aquifer comments:**

**Aquifer documentation:**

**Well depth (ft):**

**Well casing type:**

**Well casing outside diameter (in.):**

**Well casing inside diameter (in.):**

**New water well casing?**

**Used casing source:**

**Drilling method:**

**Drill material:**

**Grout material:**

**Grout depth:**

**Casing length (ft.):**

**Casing top depth (ft.):**

Operator Name: AMEREDEV OPERATING LLC

Well Name: GREEN JACKET FED COM 26 36 29

Well Number: 101H

Well Production type:

Completion Method:

Water well additional information:

State appropriation permit:

Additional information attachment:

### Section 6 - Construction Materials

Construction Materials source location attachment:

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_CALICHE\_MAP\_REV\_20190516160530.pdf

### Section 7 - Methods for Handling Waste

Waste type: DRILLING

Amount of waste: 2000 barrels

Waste disposal frequency : Daily

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY Disposal location ownership: COMMERCIAL

Disposal type description:

### Reserve Pit

Reserve Pit being used? NO

Temporary disposal of produced water into reserve pit?

Reserve pit length (ft.) Reserve pit width (ft.)

Reserve pit depth (ft.) Reserve pit volume (cu. yd.)

Is at least 50% of the reserve pit in cut?

Reserve pit liner

Reserve pit liner specifications and installation description

### Cuttings Area

**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

**Cuttings Area being used?** NO

**Are you storing cuttings on location?** YES

**Description of cuttings location** Steel tanks on pad

**Cuttings area length (ft.)**

**Cuttings area width (ft.)**

**Cuttings area depth (ft.)**

**Cuttings area volume (cu. yd.)**

**Is at least 50% of the cuttings area in cut?**

**WCuttings area liner**

**Cuttings area liner specifications and installation description**

### Section 8 - Ancillary Facilities

**Are you requesting any Ancillary Facilities?:** NO

**Ancillary Facilities attachment:**

**Comments:**

### Section 9 - Well Site Layout

**Well Site Layout Diagram:**

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_WELL\_SITE\_DIAGRAM\_REV\_20190516160743.pdf

BO\_GREEN\_JACKET\_SL1\_PAD\_SITE\_S\_20190516160804.pdf

**Comments:**

### Section 10 - Plans for Surface Reclamation

**Recontouring attachment:**

GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_WELL\_SITE\_DIAGRAM\_REV\_20190516160857.pdf

**Drainage/Erosion control construction:** Crowned and ditched

**Drainage/Erosion control reclamation:** Harrowed on the contour

**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

**Well pad proposed disturbance**  
(acres): 4.56

**Road proposed disturbance** (acres):  
3.17

**Powerline proposed disturbance**  
(acres): 0

**Pipeline proposed disturbance**  
(acres): 9.15

**Other proposed disturbance** (acres): 0

**Total proposed disturbance:** 16.88

**Well pad interim reclamation** (acres):  
0.75

**Road interim reclamation** (acres): 0

**Powerline interim reclamation** (acres):  
0

**Pipeline interim reclamation** (acres): 0

**Other interim reclamation** (acres): 0

**Total interim reclamation:** 0.75

**Well pad long term disturbance**  
(acres): 3.81


**Road long term disturbance** (acres):  
3.17

**Powerline long term disturbance**  
(acres): 0

**Pipeline long term disturbance**  
(acres): 9.15

**Other long term disturbance** (acres): 0

**Total long term disturbance:** 16.13



**Topsoil redistribution:** Enough stockpiled topsoil will be retained to cover the remainder of the pad when the well is plugged. New road will be similarly reclaimed within 6 months of plugging. Noxious weeds will be controlled.

**Soil treatment:** None

**Existing Vegetation at the well pad:**

**Existing Vegetation at the well pad attachment:**

**Existing Vegetation Community at the road:**

**Existing Vegetation Community at the road attachment:**

**Existing Vegetation Community at the pipeline:**

**Existing Vegetation Community at the pipeline attachment:**

**Existing Vegetation Community at other disturbances:**

**Existing Vegetation Community at other disturbances attachment:**

**Non native seed used?** NO

**Non native seed description:**

**Seedling transplant description:**

**Will seedlings be transplanted for this project?** NO

**Seedling transplant description attachment:**

**Will seed be harvested for use in site reclamation?** NO

**Seed harvest description:**

**Operator Name:** AMEREDEV OPERATING LLC  
**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

**Seed harvest description attachment:**

### Seed Management

#### Seed Table

**Seed type:**

**Seed source:**

**Seed name:**

**Source name:**

**Source address:**

**Source phone:**

**Seed cultivar:**

**Seed use location:**

**PLS pounds per acre:**

**Proposed seeding season:**

#### Seed Summary

**Total pounds/Acre:**

Seed Type	Pounds/Acre
-----------	-------------

**Seed reclamation attachment:**

#### Operator Contact/Responsible Official Contact Info

**First Name:** Zachary

**Last Name:** Boyd

**Phone:** (580)940-5054

**Email:** zboyd@ameredev.com

**Seedbed prep:**

**Seed BMP:**

**Seed method:**

**Existing invasive species?** NO

**Existing invasive species treatment description:**

**Existing invasive species treatment attachment:**

**Weed treatment plan description:** To BLM standards

**Weed treatment plan attachment:**

**Monitoring plan description:** To BLM standards

**Monitoring plan attachment:**

**Success standards:** To BLM satisfaction

**Pit closure description:** No pit

**Pit closure attachment:**


**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

### **Section 11 - Surface Ownership**


**Disturbance type:** NEW ACCESS ROAD




**USFS Region:**

**USFS Forest/Grassland:**

**USFS Ranger District:**



**Surface use plan certification document:**




**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H


**Disturbance type:** WELL PAD




**USFS Region:**

**USFS Forest/Grassland:**


**USFS Ranger District:**



**Surface use plan certification document:**




**Disturbance type:** PIPELINE



**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H




**USFS Region:**

**USFS Forest/Grassland:**

**USFS Ranger District:**



**Surface use plan certification document:**



## **Section 12 - Other Information**

**Right of Way needed?** NO

**Use APD as ROW?**

**ROW Type(s):**

### **ROW Applications**

**SUPO Additional Information:**

**Use a previously conducted onsite?** YES





**Operator Name:** AMEREDEV OPERATING LLC

**Well Name:** GREEN JACKET FED COM 26 36 29

**Well Number:** 101H

**Other SUPO Attachment**


GREEN\_JACKET\_FED\_COM\_26\_36\_29\_101H\_\_SURFACE\_USE\_PLAN\_REV\_20190516161521.pdf

Green Jacket Fed Com  
26 36 29 101H Well Pad  
(GJ #1S)

New Road:  
4,604 ft

Existing  
Amen Corner  
CTB

Route Into Location  
on Existing Roads

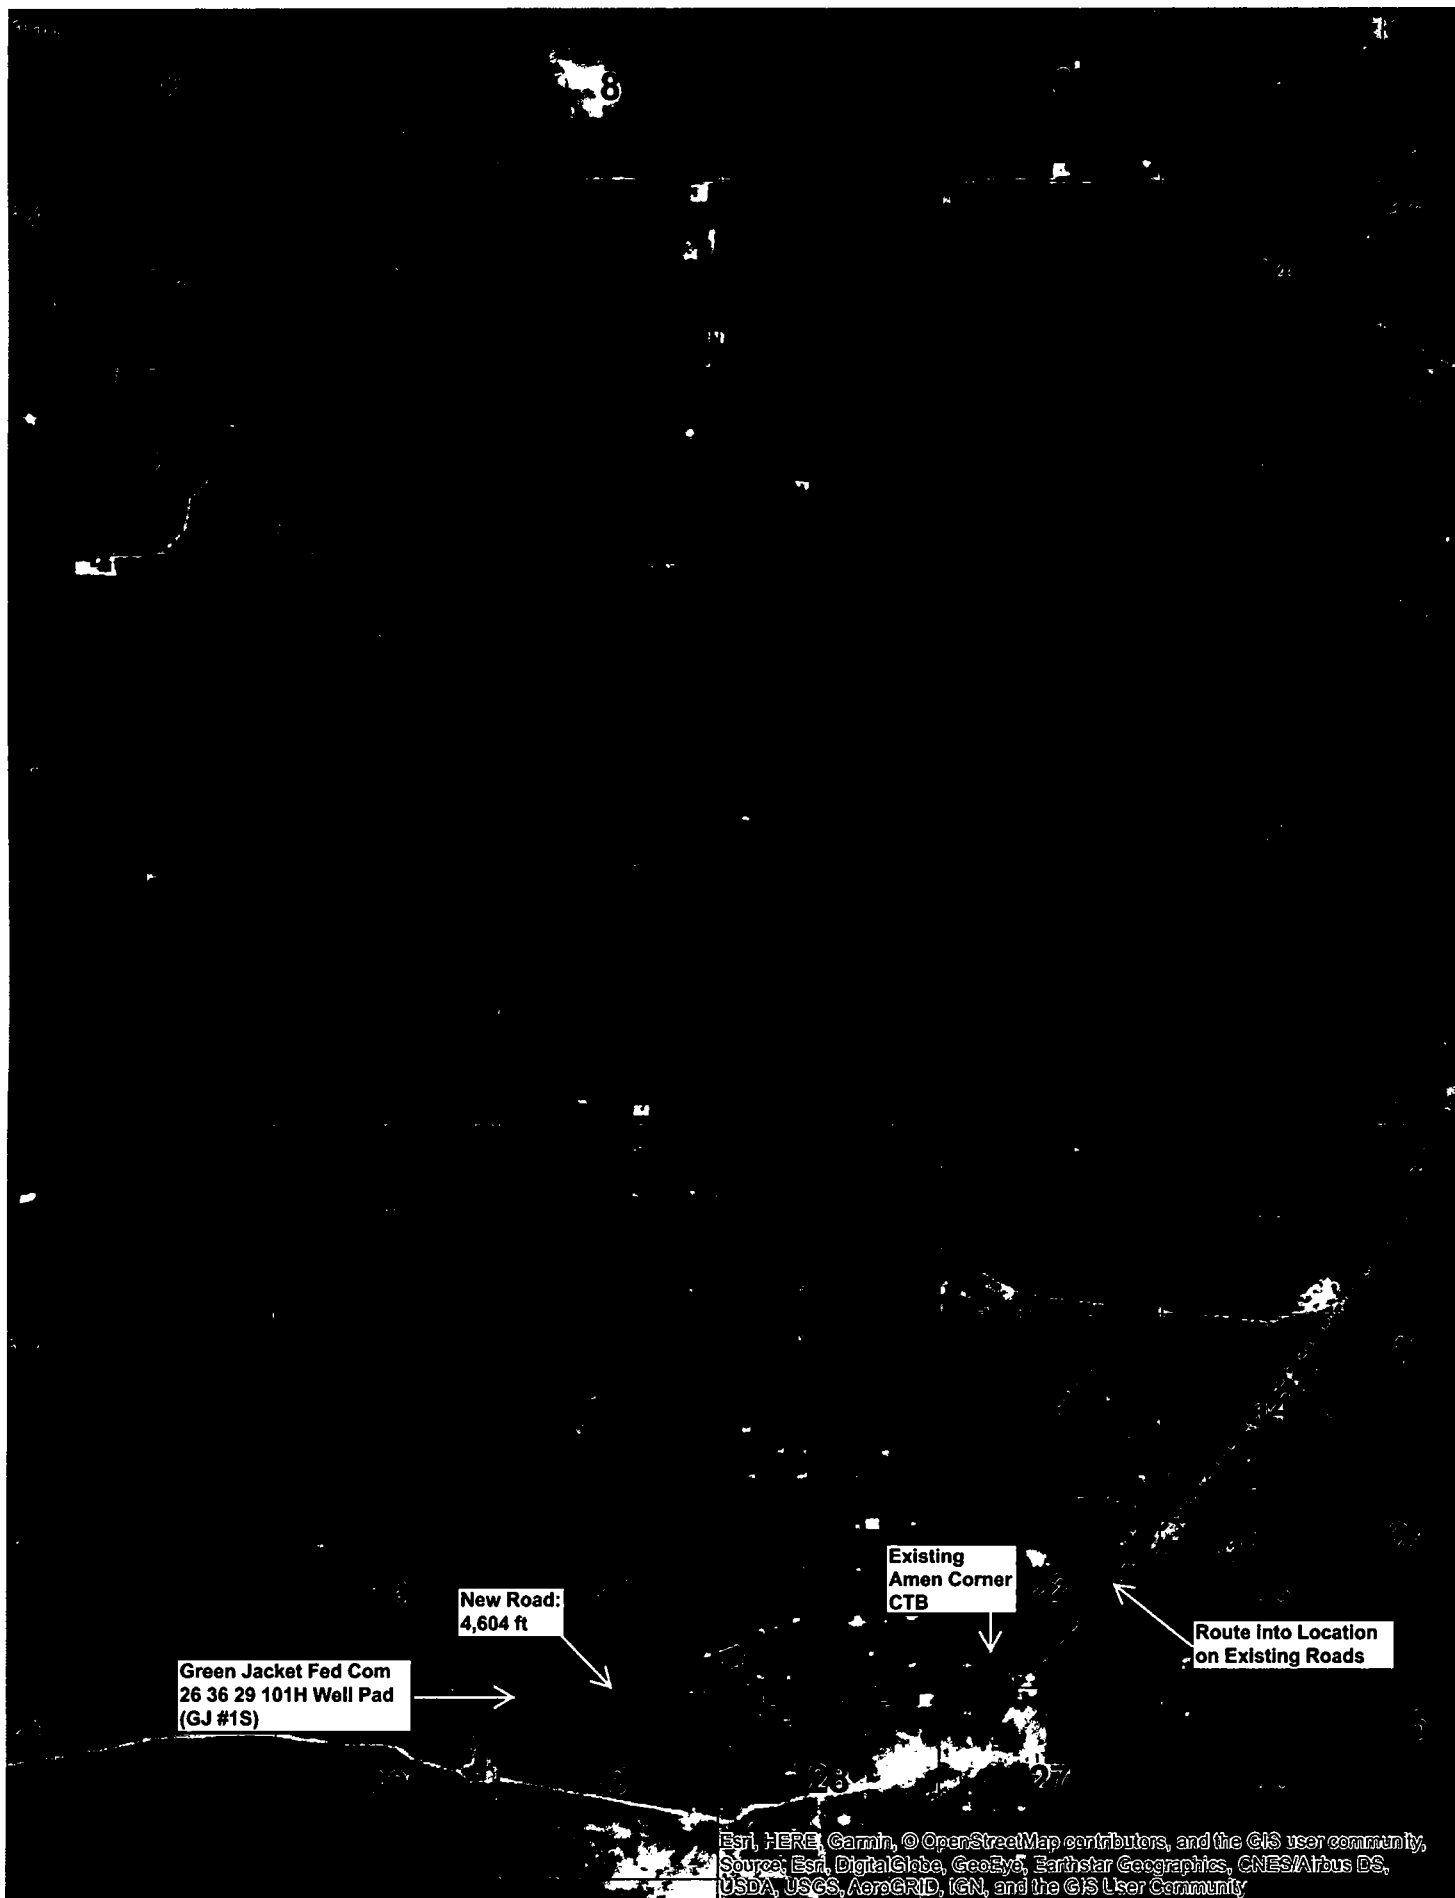

Green Jacket Fed Com  
26 36 29 101H Well Pad  
(GJ #1S)


New Road:  
4,604 ft

Existing  
Amen Corner  
CTB


Route into Location  
on Existing Roads

Esri, HERE, Garmin, © OpenStreetMap contributors, and the GIS user community,  
Source: Esri, DigitalGlobe, GeoEye, Earthstar Geographics, CNES/Airbus DS,  
USDA, USGS, AeroGRID, IGN, and the GIS User Community

SECTION 29, TOWNSHIP 26-S, RANGE 36-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

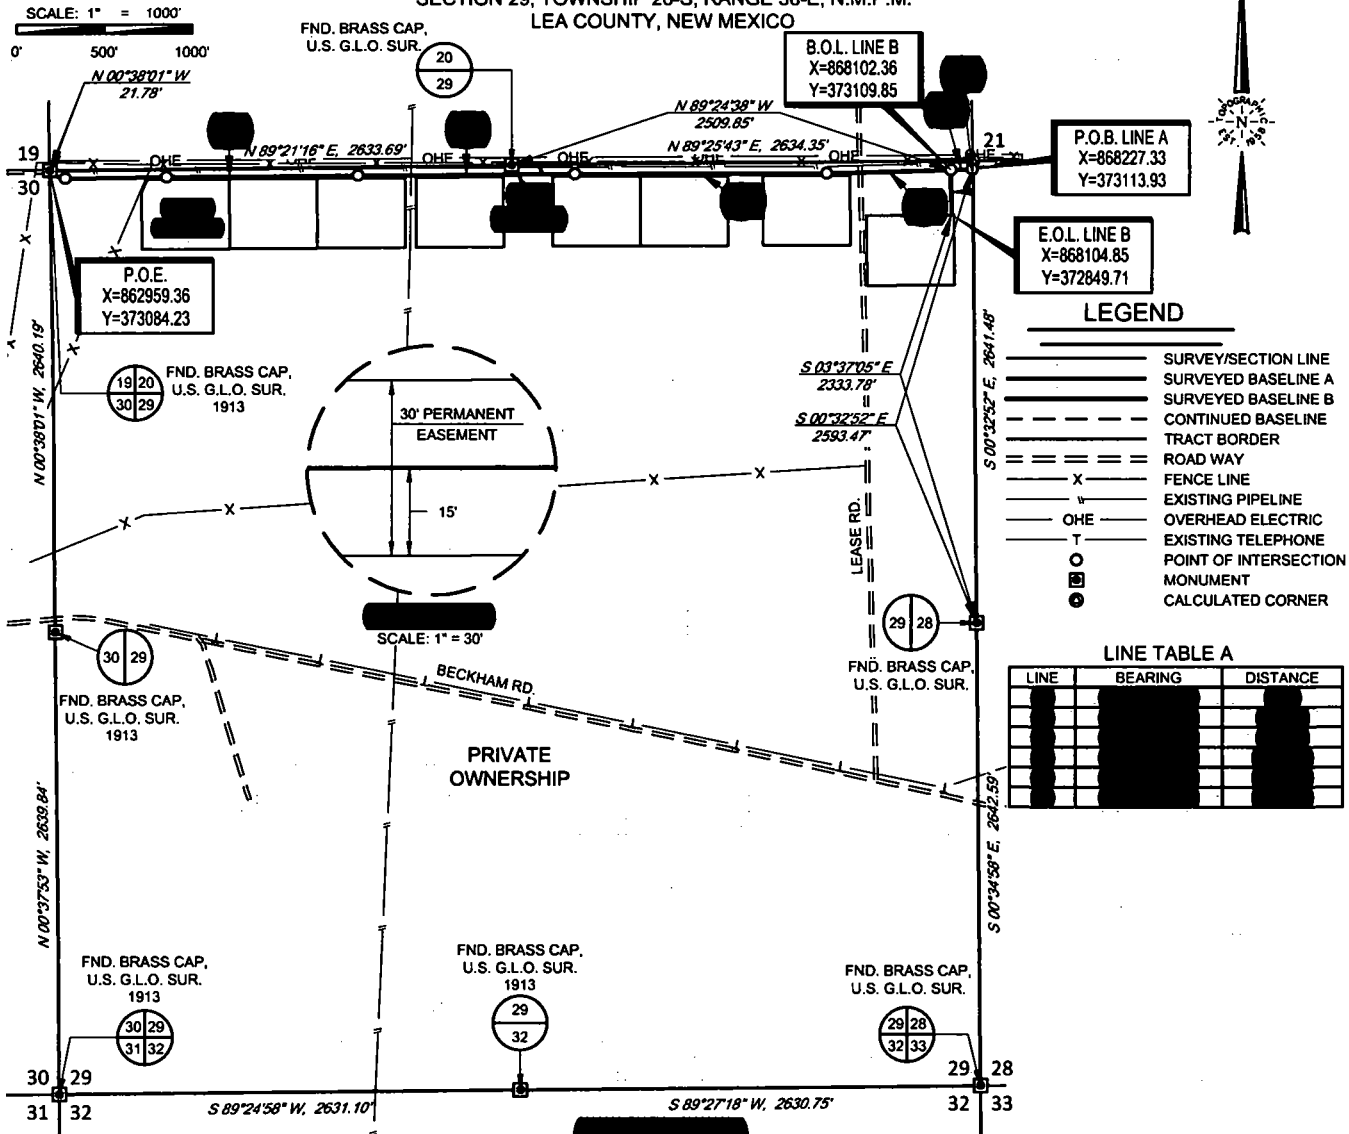

Being a proposed road easement being 30 feet in width, 15 feet left and right of the above platted centerline total line footage containing 5532.59 feet or 335.31 rods, containing 3.81 acres more or less.



"PRELIMINARY SURVEY DOCUMENT SHALL NOT BE USED FOR ANY PURPOSE"

Stan W. Lloyd, P.S. No. 19642  
JULY 30, 2018

**AMEREDEV**  
AMEREDEV OPERATING, LLC

**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY  
1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 787-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM

SOUTH ROAD EASEMENT	REVISION:	
	INT	DATE
DATE: 07/30/18		
FILE: EP_SOUTH_ROAD_EASEMENTS_SEC_29		
DRAWN BY: EAH		
SHEET: 1 OF 1		

- NOTES:
1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
  2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
  3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER MY SUPERVISION, AND USING DOCUMENTATION PROVIDED BY AMEREDEV OPERATING LLC. ONLY UTILITIES/EASEMENTS THAT WERE VISIBLE ON THE DATE OF THIS SURVEY, WITHIN/ADJOINING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREON OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY.
  4. B.O.L./P.O.B. = BEGINNING OF LINE/POINT OF BEGINNING
  5. E.O.L./P.O.E. = END OF LINE/POINT OF EXIT


Ameredev Operating, LLC  
Green Jacket Fed Com 26 36 29 101H  
Section 29, Township 26S, Range 36E  
Lea County, New Mexico

**AMEREDEV**

Ameredev, LLC

**Section 3 – Location of Existing Wells**

*Exhibit 2 – One Mile Radius Existing Wells* depicts all known wells within a one mile radius of the Green Jacket Fed Com 26 36 29 101H. See *Exhibit 2a – One Mile Radius Wells List* for a list of wells depicted.

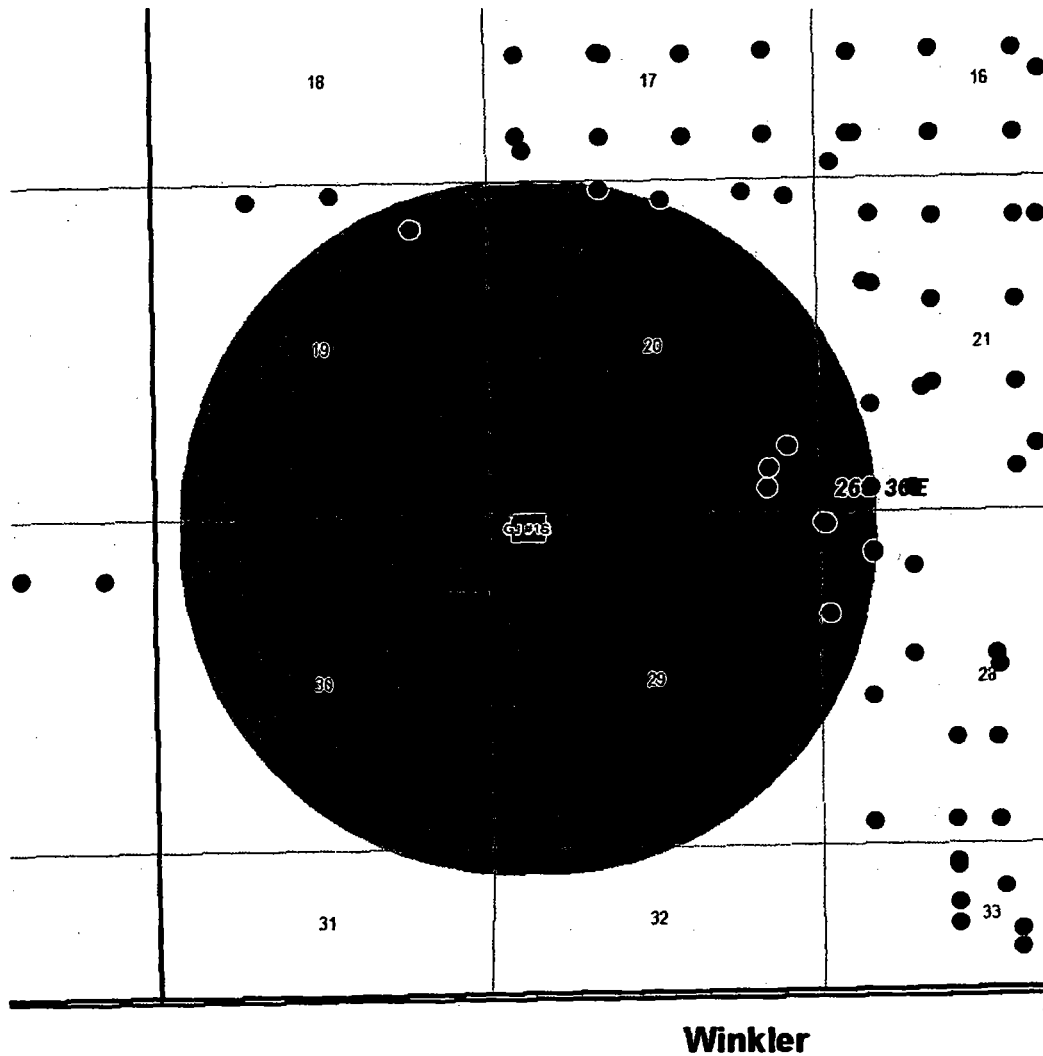

***Exhibit 2 – One Mile Radius Existing Wells***

Ameredev Operating, LLC  
Green Jacket Fed Com 26 36 29 101H  
Section 29, Township 26S, Range 36E  
Lea County, New Mexico

**AMEREDEV**


Ameredev, LLC

API	WELL NAME	STATUS	TD
30025441050100	AZALEA 26-36-28 STATE #121H	OIL	17550
30025442290000	AZALEA 26-36-28 STATE #121Y	PILOT	13600
30025442290100	AZALEA 26-36-28 STATE #121Y	OIL	19469
30025441040000	AZALEA STATE 26-36-28 #111H	OIL	18993
30025259570000	LEA #WD-1	INJECTION	3420
30025260560000	LEA 7406-JV-S #9	DRY	1406
30025260680000	LEA 7406-JV-S #9-Y	OIL	3270
30025259200000	LEA 7406 JV-S #7	OIL	3270
30025441110000	PRIZEHOG BWZ STATE COM #002H	OIL	17188
30025098560000	SAND HILLS UNIT #6	ABDNLOC	1257
30025098570000	SAND HILLS UNIT A #1	DRY	3349
30025427330000	WILDHOG BWX STATE COM #001H	OIL	17244
30025261320000	WILSON /21/ FED #2	OIL	3500

**Exhibit 2a – One Mile Radius Existing Wells List**

SCALE: 1" = 1000'

SECTION 22, TOWNSHIP 26-S, RANGE 36-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

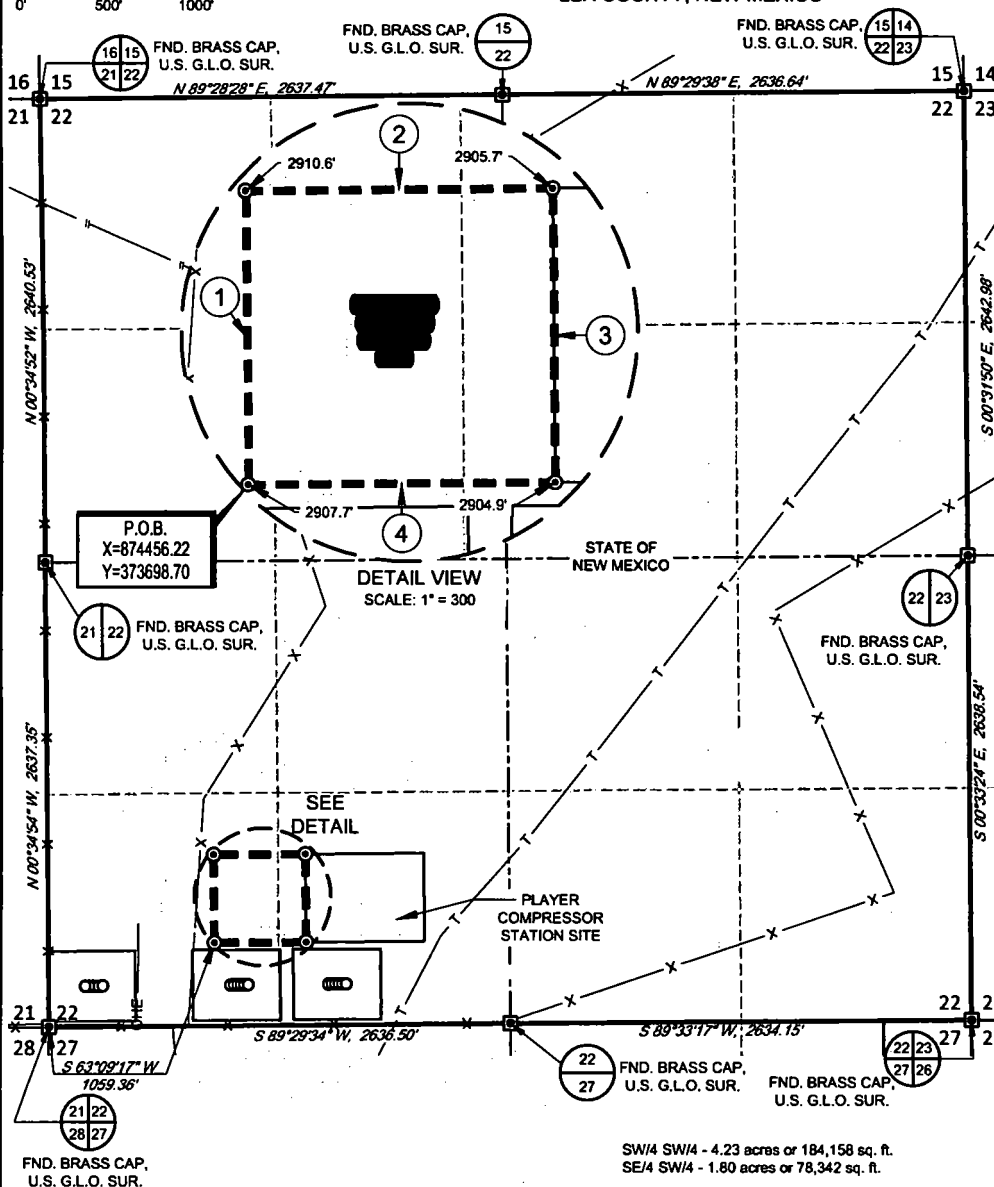

AMEN CORNER  
BATTERY SITE

Meters and Bounds Description of a proposed 6.03 acre battery site located within the Southwest quarter of the Southwest quarter and the Southeast quarter of the Southwest quarter of Section 22, Township 26 South, Range 36 East, N.M.P.M., in Lea County, New Mexico.

BEGINNING at a 1/2" iron rod with cap stamped "Topographic" set for the Southwest corner of this site, from whence a brass cap found for the Southwest corner of said Section 22, bears: S 63°09'17" W, a distance of 1059.36 feet;

Thence N 00°34'54" W, a distance of 500.00 feet to a 1/2" iron rod with cap stamped "Topographic" set for the Northwest corner of this site;

Thence N 89°29'34" E, a distance of 525.00 feet to a 1/2" iron rod with cap stamped "Topographic" set for the Northeast corner of this site;

Thence S 00°34'54" E, a distance of 500.00 feet to a 1/2" iron rod with cap stamped "Topographic" set for the Southeast corner of this site;

Thence S 89°29'34" W, a distance of 525.00 feet to the Point of Beginning.

LEGEND

- SECTION LINE
- QUARTER SECTION LINE
- SIXTEENTH SECTION LINE
- PROPOSED SITE
- TRACT BORDER
- ROAD WAY
- EXISTING PIPELINE
- OHE
- OVERHEAD ELECTRIC
- EXISTING TELEPHONE
- FENCE LINE
- MONUMENT
- IRON ROD SET

LINE TABLE

LINE	BEARING	DISTANCE
1	N 00°34'54" W	500.00'
2	N 89°29'34" E	525.00'
3	S 00°34'54" E	500.00'
4	S 89°29'34" W	525.00'



Stan W. Lloyd, P.S. No. 19642

JANUARY 31, 2018

AMEREDEV



TOPOGRAPHIC  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, S.E. 146 - FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 882-1653 OR (800) 787-1653 • FAX (432) 882-1743  
WWW.TOPOGRAPHIC.COM

NOTES:

1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER MY SUPERVISION, AND USING DOCUMENTATION PROVIDED BY AMEREDEV OPERATING LLC. ONLY UTILITIES/EASEMENTS THAT WERE VISIBLE ON THE DATE OF THIS SURVEY, WITHIN/ADJOINING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREON OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY.
4. P.O.B. = POINT OF BEGINNING

AMEN CORNER  
BATTERY SITE

REVISION:

INT DATE

DATE: 1/31/2018


FILE:BO\_AMEN\_CORNER\_BATTERY\_SITE

DRAWN BY: EAH

SHEET: 1 OF 1

SECTION 29, TOWNSHIP 26-S, RANGE 36-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

SCALE: 1" = 1000'  
0' 500' 1000'

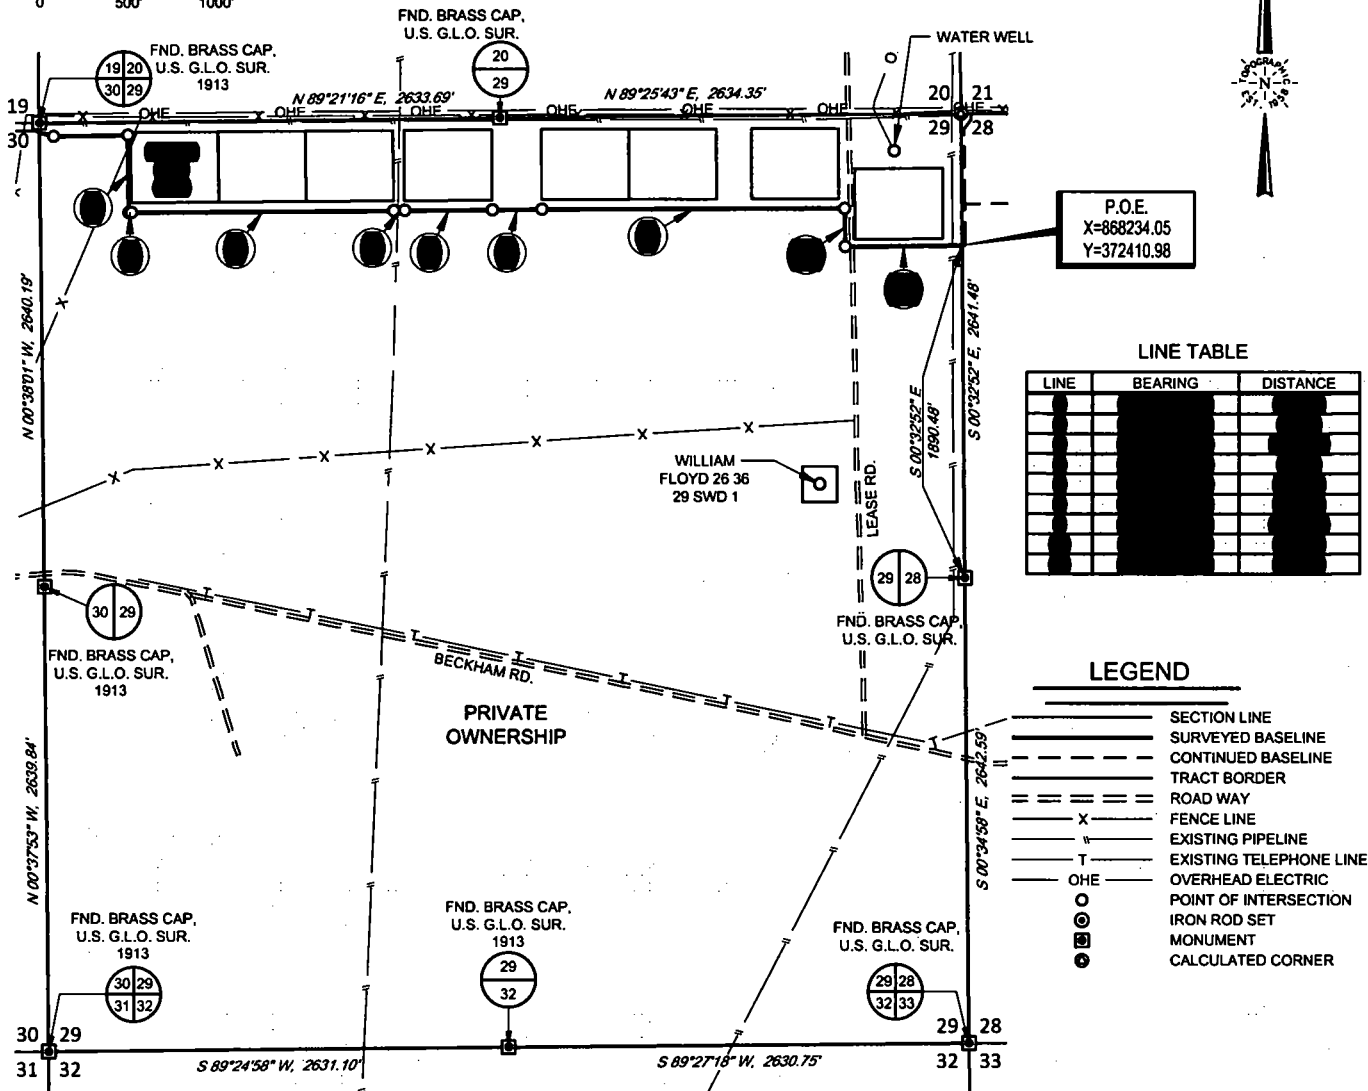

LINE TABLE


LINE	BEARING	DISTANCE
1		
2		
3		
4		
5		
6		
7		
8		
9		
10		
11		
12		
13		
14		
15		
16		
17		
18		
19		
20		
21		
22		
23		
24		
25		
26		
27		
28		
29		
30		
31		
32		
33		

LEGEND

—	SECTION LINE
—	SURVEYED BASELINE
—	CONTINUED BASELINE
—	TRACT BORDER
—	ROAD WAY
—	FENCE LINE
—	EXISTING PIPELINE
—	EXISTING TELEPHONE LINE
—	OVERHEAD ELECTRIC
○	POINT OF INTERSECTION
⊙	IRON ROD SET
⊙	MONUMENT
⊙	CALCULATED CORNER

GREEN JACKET TO AMEN CORNER  
FLOWLINE EASEMENT

Being a proposed flowline easement being 30 feet in width, 15 feet left and right of the above platted centerline total line footage containing 5926.71 feet or 359.19 rods, containing 4.08 acres more or less.



John Trevor Carnegie, P.S. No. 11401  
MARCH 4, 2019

**AMEREDEV**  
AMEREDEV OPERATING, LLC

**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY  
1400 EVERMAN PARKWAY, Ste. 148 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM

NOTES:

1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER MY SUPERVISION, AND USING DOCUMENTATION PROVIDED BY AMEREDEV OPERATING LLC. ONLY UTILITIES/EASEMENTS THAT WERE VISIBLE ON THE DATE OF THIS SURVEY, WITHIN/ADJOINING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREON OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY.
4. B.O.L./P.O.B. = BEGINNING OF LINE/POINT OF BEGINNING
5. E.O.L./P.O.E. = END OF LINE/POINT OF EXIT


GREEN JACKET TO CAM/AZE FLOWLINE EASEMENT	REVISION:	
	AMD	02/28/2019
	ACC	03/04/2019
DATE: 01/14/2019		
FILE: EP_CAM_AZE_1N_TO_GJ_CTB_FL_SEC_29_REV2		
DRAWN BY: AMD		
SHEET: 1 OF 1		



SECTION 28, TOWNSHIP 26-S, RANGE 36-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

FND. BRASS CAP.  
U.S. G.L.O. SUR.

SCALE: 1" = 1000'  
0' 500' 1000'

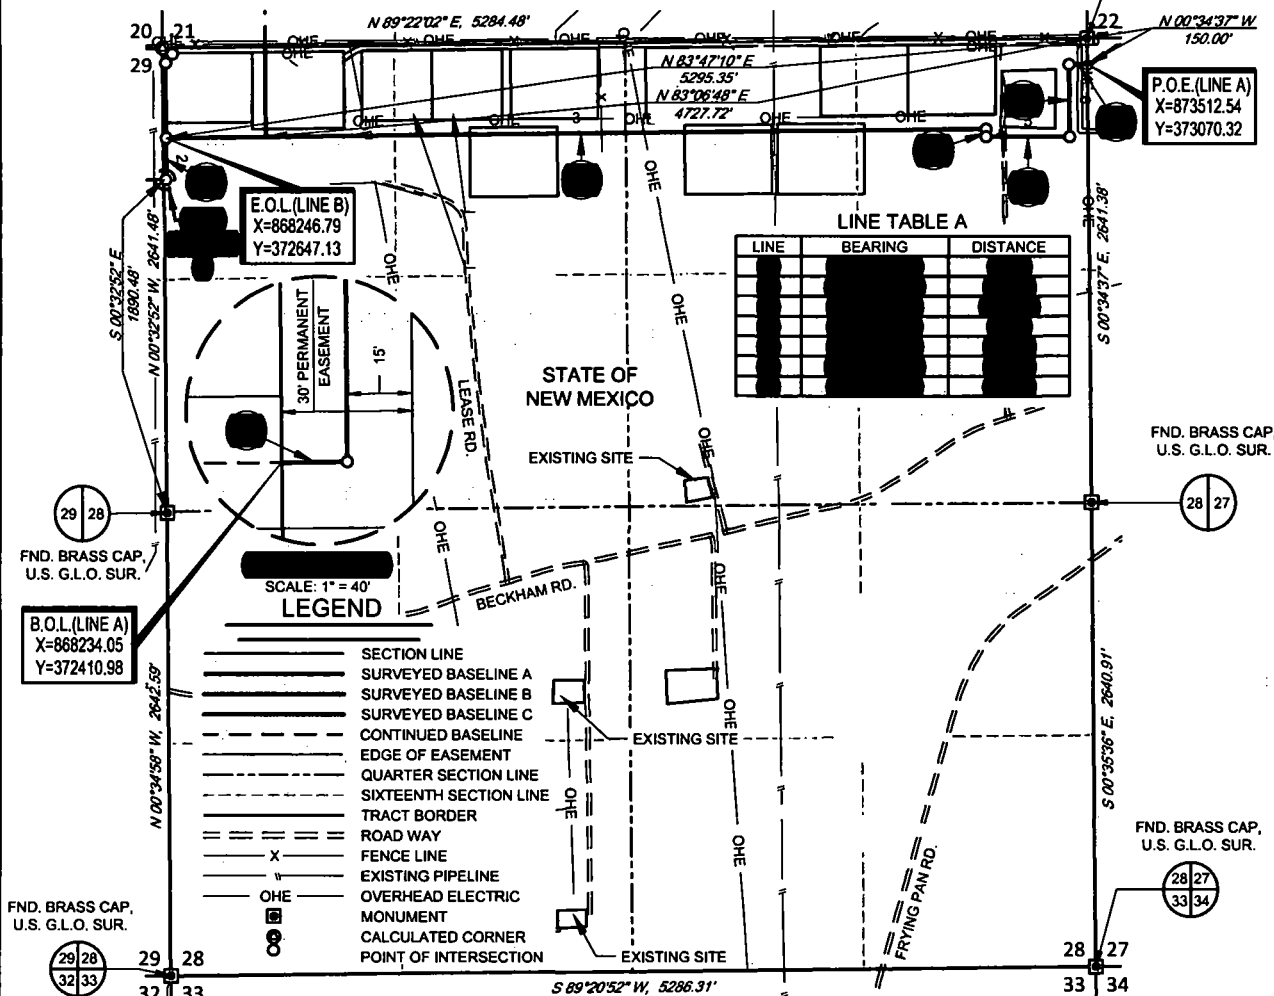

GREEN JACKET TO AMEN CORNER BATTERY SITE  
FLOWLINE EASEMENT

Being a flowline easement being 30 feet in width, 15 feet left and right of the above platted centerline total line footage containing 7019.70 feet or 425.44 rods, containing 4.83 acres more or less and being allocated by quarter quarters as follows:

NW1/4 NW1/4 - 2600.68 feet or 157.62 rods, containing 1.79 acres  
NE1/4 NW1/4 - 1321.17 feet or 80.07 rods, containing 0.91 acres  
NW1/4 NE1/4 - 1321.13 feet or 80.07 rods, containing 0.91 acres  
NE1/4 NE1/4 - 1776.72 feet or 107.68 rods, containing 1.22 acres



John Trevor Carnegie, P.S. No. 11401  
MARCH 4, 2019

**AMEREDEV**  
AMEREDEV OPERATING, LLC

**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY  
1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM

NOTES:

1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER MY SUPERVISION, AND USING DOCUMENTATION PROVIDED BY AMEREDEV OPERATING LLC. ONLY UTILITIES/EASEMENTS THAT WERE VISIBLE ON THE DATE OF THIS SURVEY, WITHIN/ADJOINING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREON OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY.
4. B.O.L./P.O.B. = BEGINNING OF LINE/POINT OF BEGINNING
5. E.O.L./P.O.E. = END OF LINE/POINT OF EXIT
6. P.I. = POINT OF INTERSECTION

CAM/AZE TO AMEN CORNER BATTERY SITE FLOWLINE EASEMENT	REVISION:	
	AMD	02/28/19
DATE: 02/19/19	ACC	03/04/19
FILE: IP CAM/AZE TO AMEN CORNER BATTERY SITE R. SEC. 28 REV2		
DRAWN BY: AMD		
SHEET: 1 OF 1		

S:\SURVEY\AMEREDEV\_OPERATING\_LLCAZALEA\_STATE\_COMFINAL\_PRODUCTS\SEP\_CAM\_AZE\_TO\_AMEN\_CORNER\_BATTERY\_SITE\_FL\_SEC\_28\_REV2.DWG 3/5/2019 8:48:19 AM cccaston

SECTION 27, TOWNSHIP 26-S, RANGE 36-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

SCALE: 1" = 1000'

0' 500' 1000'

FND. BRASS CAP,  
U.S. G.L.O. SUR.

FND. BRASS CAP,  
U.S. G.L.O. SUR.

P.O.E.  
X=874043.72  
Y=373225.03

P.O.B.  
X=873512.54  
Y=373070.32

N 00°34'37" W  
150.00'

N 89°29'34" E  
2103.78'

N 89°29'34" E, 2636.50'

N 89°33'17" E, 2634.15'

N 89°33'17" E, 2634.15'

S 00°33'13" E, 2641.32'

S 00°31'42" E, 2640.23'

S 89°30'09" W, 2630.21'

S 89°31'45" W, 2636.36'

LINE TABLE

LINE	BEARING	DISTANCE
1		
2		
3		
4		
5		
6		
7		
8		
9		
10		
11		
12		
13		
14		
15		
16		
17		
18		
19		
20		
21		
22		
23		
24		
25		
26		
27		
28		
29		
30		
31		
32		
33		
34		
35		

LEGEND

- SURVEY/SECTION LINE
- QUARTER SECTION LINE
- SIXTEENTH SECTION LINE
- SURVEYED BASELINE
- CONTINUED BASELINE
- TRACT BORDER
- == ROAD WAY
- X FENCE LINE
- EXISTING PIPELINE
- OHE OVERHEAD ELECTRIC
- T TELEPHONE LINE
- MONUMENT
- O POINT OF INTERSECTION

GREEN JACKET TO AMEN CORNER  
BATTERY SITE  
FLOWLINE EASEMENT

Being a proposed crude system easement being 30 feet in width, 15 feet left, and 15 feet right of the above platted centerline total line footage containing 609.46 feet or 36.94 rods, containing 0.42 acres more or less.



Michael Blake Brown, P.S. No. 18329  
FEBRUARY 20, 2019

**AMEREDEV**

AMEREDEV OPERATING, LLC



**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 148 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 787-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM

NOTES:

1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER MY SUPERVISION, AND USING DOCUMENTATION PROVIDED BY AMEREDEV OPERATING LLC. ONLY UTILITIES/EASEMENTS THAT WERE VISIBLE ON THE DATE OF THIS SURVEY, WITHIN/ADJOINING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREON OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY.
4. B.O.L./P.O.B. = BEGINNING OF LINE/POINT OF BEGINNING
5. E.O.L./P.O.E. = END OF LINE/POINT OF EXIT

CAM/AZE TO AMEN  
CORNER BATTERY SITE  
FLOWLINE EASEMENT

REVISION:

INT DATE

DATE: 02/20/2019

FILE: P CAM/AZE TO AMEN CORNER BATTERY SITE FL SEC 27


DRAWN BY: AMD

SHEET: 1 OF 1

S:\SURVEY\AMEREDEV\_OPERATING\_LLCAZALEA\_STATE\_COM\FINAL\_PRODUCTS\SEP\_CAM\_AZE\_TO\_AMEN\_CORNER\_BATTERY\_SITE\_FL\_SEC\_27.DWG 2/25/2019 8:17:52 AM ccession

0' 500' 1000'

SECTION 22, TOWNSHIP 26-S, RANGE 36-E, N.M.P.M.  
LEA COUNTY, NEW MEXICO

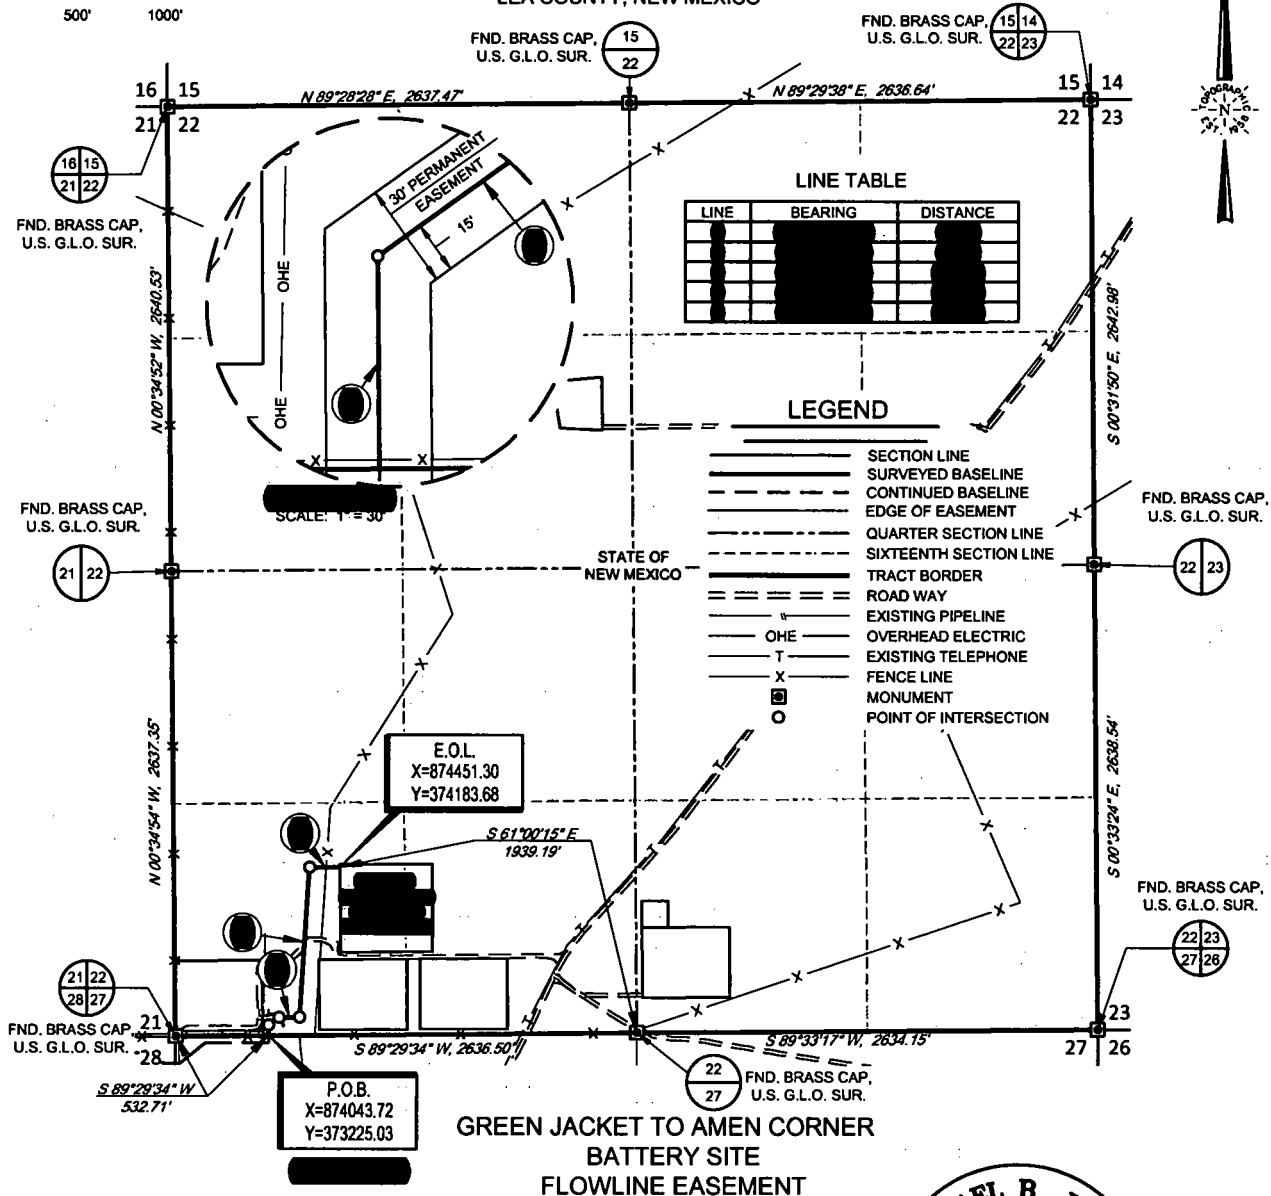

**SW/4 SW/4 - 1279.63 feet or 77.55 rods, containing 0.88 acres**



Michael Blake Brown, P.S. No. 18329  
FEBRUARY 20, 2019




**TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, Ste. 146 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 682-1653 OR (800) 767-1653 • FAX (432) 682-1743  
WWW.TOPOGRAPHIC.COM

CAM/AZE TO AMEN CORNER BATTERY SITE FLOWLINE EASEMENT	REVISION:	
	INT	DATE
DATE: 02/20/19		
FILE: P:\CAM_AZE TO AMEN CORNER BATTERY SITE FL SEC 22		
DRAWN BY: AMD		
SHEET: 1 OF 1		

**NOTES:**

1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER MY SUPERVISION, AND USING DOCUMENTATION PROVIDED BY AMERIDEAD OPERATING LLC. ONLY UTILITIES/EASEMENTS THAT WERE VISIBLE ON THE DATE OF THIS SURVEY, WITHIN/ADJOINING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREON OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES SHOWN ON THE FACE OF THIS PLAT AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY.
4. B.O.L./P.O.B. = BEGINNING OF LINE/POINT OF BEGINNING
5. E.O.L./P.O.E. = END OF LINE/POINT OF EXIT

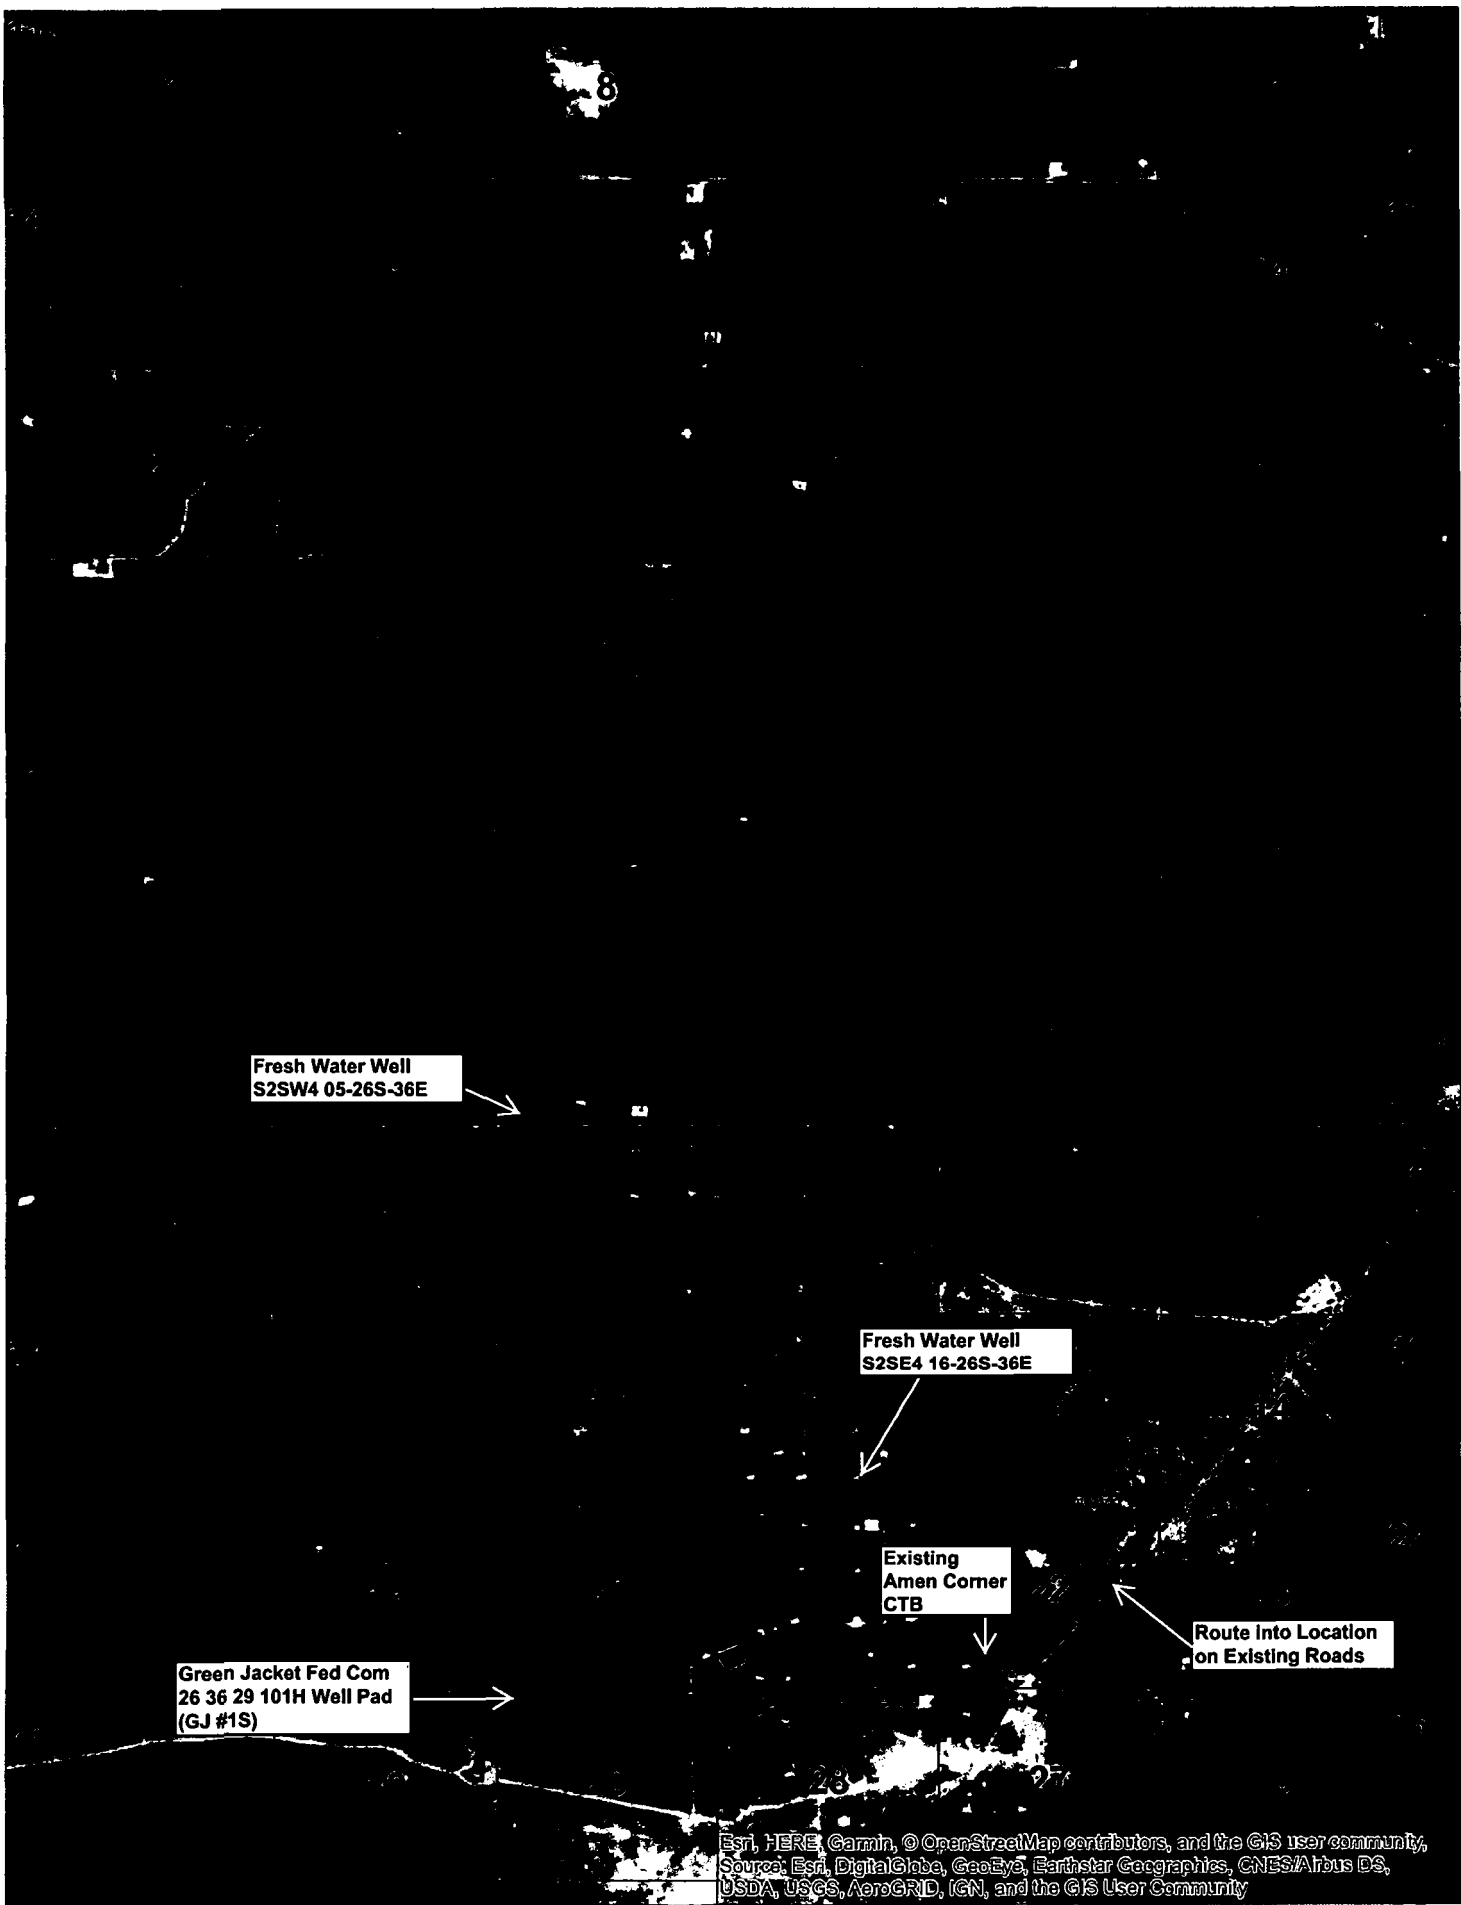

Esri, HERE, Garmin, © OpenStreetMap contributors, and the GIS user community,  
Source: Esri, DigitalGlobe, GeoEye, Earthstar Geographics, CNES/Airbus DS,  
USDA, USGS, AeroGRID, IGN, and the GIS User Community

**Section 5 - Location and Types of Water Supply**

- A. This location will be drilled using a combination of water and mud systems (outlined in the Drilling Program). The water will be obtained from preexisting water wells, by running a pump directly to the drilling rig. See *Exhibit 4 - Water Wells*, for a list of available water wells. In cases where a polyline is used to transport water for drilling or completion purposes, the existing and proposed roads into location will be utilized.

<u>Permit #</u>	<u>Well Name</u>	<u>Location (Lat/Lon)</u>
CP 1049 POD 2	Bennett	32°04'14.32" N, 103°12'32.30" W
CP 1378	S. Eppenour	32°05'40.62" N, 103°13' 35.26" W
CP 1285	Sec. 5	32°03'56.50" N, 103°17'37.04" W
CP 857	Capped	32°04'39.70" N, 103°16'51.13" W
C 2287	#1	32°03'59.0" N, 103°33'16.8" W
C 2286	#2	32°03'59.2" N, 103°33'15.2" W
C 2290	#3	32°04'1.0" N, 103°33' 12.6" W
C 2285	#4	32°04'3.7" N, 103°33'9.7" W
C 2288	#5	32°04'0.5" N, 103°33'8.4" W
C 2294	Garden	32°03'3.2" N, 103°32'38.1" W
C 2293	House	32°03'2.3" N, 103°32'36.8" W
J-11-S-3	Farm Well #2	32°03'08.4" N, 103°16'35.2" W
J-11-S-2	Farm Well #3	32°03'11.5" N, 103°17'02.0" W
J-11-S	Farm Well #4	32°03'24.6" N, 103°17'02.1" W
CP 1170 POD 1	CB 1	32°03'57.2" N, 103°18'45.3" W
CP 1170 POD 5		32°07'17.1" N, 103°17'48.0" W
CP 1263 POD 5	CB 2	32°03'56.27" N, 103°18'27.4" W
CP 1263 POD 3	CB 3	32°03'54.90" N, 103°18'16.74" W
CP 1351 POD 1	CB 4	32°03'57.16" N, 103°17'45.13" W
CP 1351 POD 2	CB 5	32°03'30.70" N, 103°17'45.70" W
J 26	Ryan	32°01'20.41" N, 103°15'49.46" W
J 3		32°02'41.5" N, 103°18'55.8" W

**Exhibit 4 – Water Wells**



Existing Caliche Pit  
E2 17-25S-36E

Existing Caliche Pit  
E2 11-26S-36E


Existing  
Amen Corner  
CTB

Green Jacket Fed Com  
26 36 29 101H Well Pad  
(GJ #1S)

Route into Location  
on Existing Roads

Esri, HERE, Garmin, © OpenStreetMap contributors, and the GIS user community,  
Source: Esri, DigitalGlobe, GeoEye, Earthstar Geographics, CNES/Airbus DS,  
USDA, USGS, AeroGRID, IGN, and the GIS User Community


Ameredev Operating, LLC  
Green Jacket Fed Com 26 36 29 101H  
Section 29, Township 26S, Range 36E  
Lea County, New Mexico

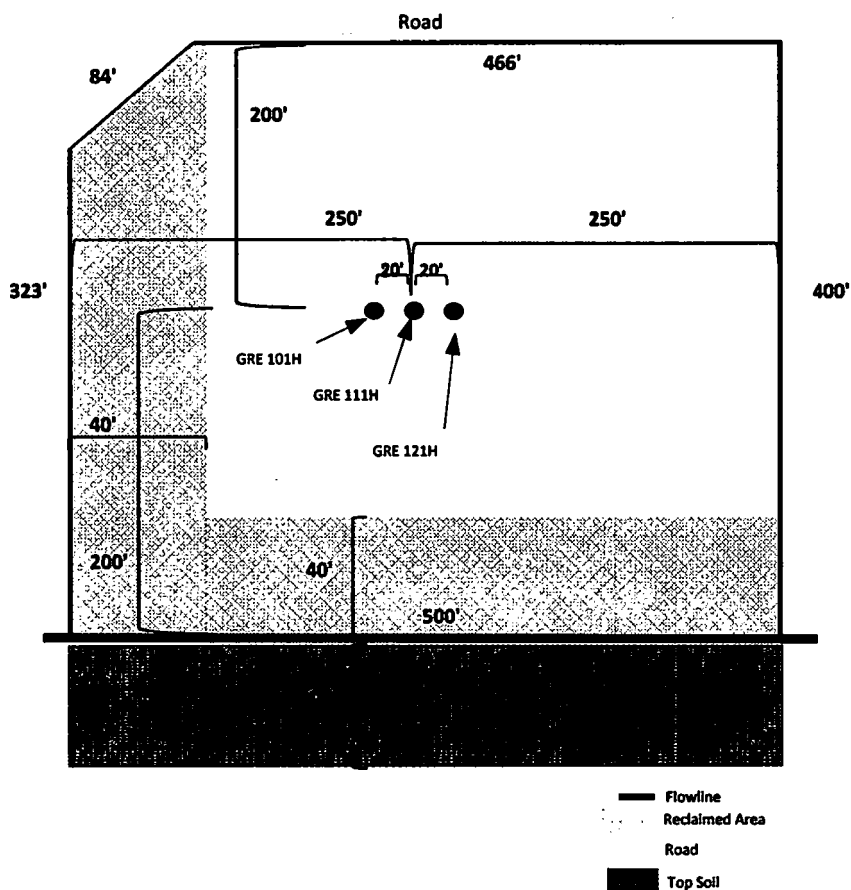


Green Jacket Fed Com 26 36 29 101H SHL: 26S 36E 262' FNL 752' FWL  
Green Jacket Fed Com 26 36 29 111H SHL: 26S 36E 262' FNL 772' FWL  
Green Jacket Fed Com 26 36 29 121H SHL: 26S 36E 262' FNL 792' FWL

**Exhibit 3 – Well Site Diagram**

SCALE: 1" = 1000'



0' 500' 1000'



 **TOPOGRAPHIC**  
LOYALTY INNOVATION LEGACY

1400 EVERMAN PARKWAY, STE. 146 • FT. WORTH, TEXAS 76140  
TELEPHONE: (817) 744-7512 • FAX (817) 744-7554  
2903 NORTH BIG SPRING • MIDLAND, TEXAS 79705  
TELEPHONE: (432) 882-1653 OR (800) 787-1653 • FAX (432) 882-1743  
[WWW.TOPOGRAPHIC.COM](http://WWW.TOPOGRAPHIC.COM)

A circular professional seal for Stan W. Lloyd, a Professional Surveyor in New Mexico. The seal features the text "STAN W. LLOYD" at the top, "NEW MEXICO" in the middle, and "19842" in the center. The words "PROFESSIONAL SURVEYOR" are written along the bottom arc of the seal. There are handwritten initials "SWL" and a date "1/28" over the seal.


Stan W. Lloyd  
Stan W. Lloyd, P.S. No. 19642  
AUGUST 2, 2018

**NOTES:**

1. ORIGINAL DOCUMENT SIZE: 8.5" X 11"
2. ALL BEARINGS, DISTANCES, AND COORDINATE VALUES CONTAINED HEREIN ARE GRID BASED UPON THE NEW MEXICO COORDINATE SYSTEM OF 1983, EAST ZONE, U.S. SURVEY FEET.
3. CERTIFICATION IS MADE ONLY TO THE LOCATION OF THIS EASEMENT, IN RELATION TO THE EVIDENCE FOUND DURING A FIELD SURVEY, MADE ON THE GROUND, UNDER SUPERVISION, AND USING DOCUMENTATION PROVIDED BY AMERDEEV OPERATING LLC. ONLY THE EASEMENT THAT IS THERE VERIFIED ON THE DATE OF THIS SURVEY, WITHIN A JOBING THIS EASEMENT, HAVE BEEN LOCATED AS SHOWN HEREOF, OF WHICH I HAVE KNOWLEDGE. THIS CERTIFICATION IS LIMITED TO THOSE PERSONS OR ENTITIES WHOSE NAMES ARE SHOWN ON THIS PLAN AND IS NON-TRANSFERABLE, AND MADE FOR THIS TRANSACTION ONLY.
4. P.O.B. = POINT OF BEGINNING



Ameredev Operating, LLC  
 Green Jacket Fed Com 26 36 29 101H  
 Section 29, Township 26S, Range 36E  
 Lea County, New Mexico

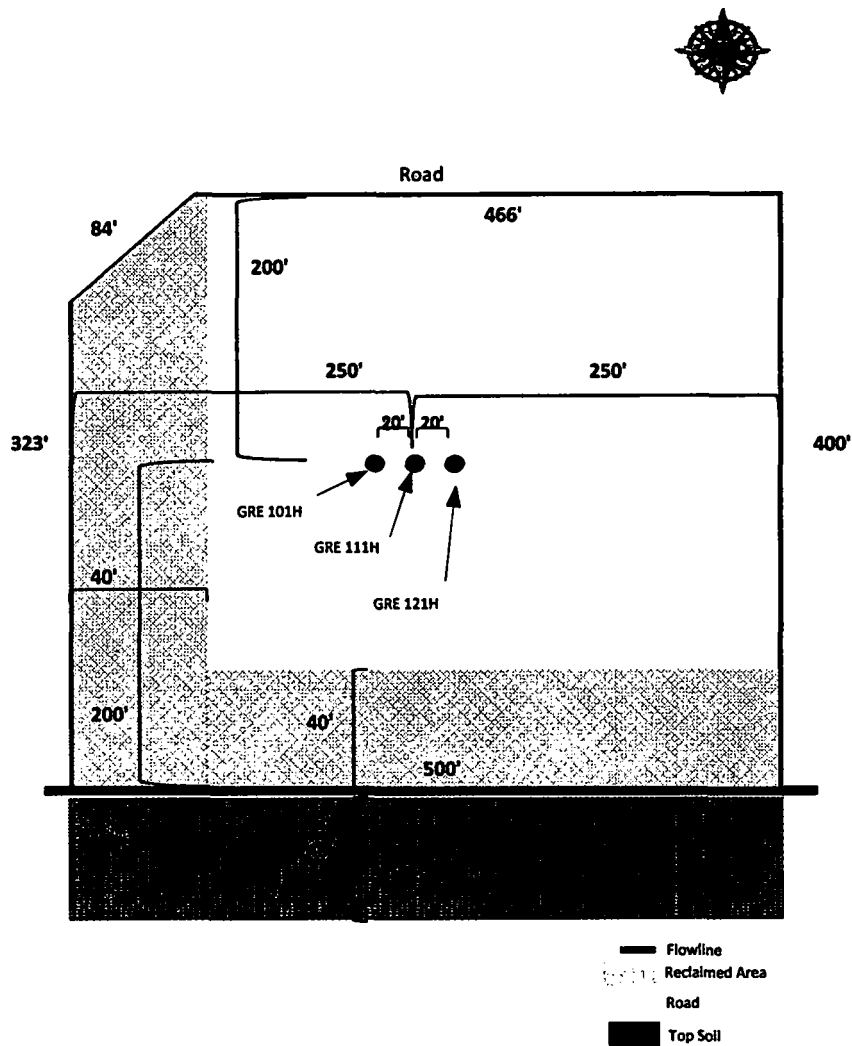

Green Jacket Fed Com 26 36 29 101H SHL: 26S 36E 262' FNL 752' FWL  
 Green Jacket Fed Com 26 36 29 111H SHL: 26S 36E 262' FNL 772' FWL  
 Green Jacket Fed Com 26 36 29 121H SHL: 26S 36E 262' FNL 792' FWL

**Exhibit 3 – Well Site Diagram**

## Surface Use Plan of Operations

### Introduction

The following Surface Use Plan of Operations will be implemented by Ameredev Operating, LLC (Ameredev), after APD approval. No disturbance will be created other than those described in this surface use plan. If any additional surface disturbance becomes necessary after APD approval, the appropriate BLM approved sundry notice or right of way application will be acquired prior to such disturbance. This Surface Use Plan includes Ameredev's well pad, battery site, electrical, water and flow lines, and access roads.

Before any surface disturbance is created, stakes or flagging will be installed to mark boundaries of permitted areas of disturbance, including soil storage areas. As necessary, slope, grade, and other construction control stakes will be placed to ensure construction is in accordance with the surface use plan. All boundary markers will be maintained in place until final construction cleanup is completed. If disturbance boundary markers are displaced, they will be replaced before construction proceeds. Adjacent operators will be contacted before construction starts to mark adjacent pipelines.

### Directions to proposed pad:

At the intersection of NM-205 & 3<sup>rd</sup> St/NM-128/Frying Pan Rd, Head south on NM-205 approximately 8 miles. Turn west (right) on proposed road and proceed approximately 2.3 miles, to the northeast side of the location. See *Exhibit 1 – Well Pad Access* for a map of the route.




- A.** The existing access road route to the proposed project is depicted on *Exhibit 1 – Well Pad Access*. Improvements to the driving surface will be done where necessary. No new surface disturbance will be done, unless otherwise noted in the New or Reconstructed Access Roads section of this surface use plan.
- B.** Right-Of-Way will be acquired before construction begins.
- C.** The operator will improve or maintain existing roads in a condition the same as or better than before operations begin. The operator will repair pot holes, clear ditches, repair the crown, etc.

All existing structures on the entire access route such as cattle guards, other range improvement projects, culverts, etc. will be properly repaired or replaced if they are damaged or have deteriorated beyond practical use.

- D. Operator will prevent and abate fugitive dust as needed, whether created by vehicular traffic, equipment operations, or wind events. BLM written approval will be acquired before application of surfactants, binding agents, or other dust suppression chemicals on roadways.

## **Section 2 – New or Reconstructed Access Roads**

- A. Sections of new access road will be needed for this proposed project. See *Exhibit 1 – Well Pad Access*, for locations.
- B. The total length of new access road needed to be constructed for this proposed project is approximately 4,604 feet.
- C. New access roads will be constructed with 6 inches of compacted caliche.
- D. The maximum driving width of the access road will be 20 feet. The maximum width of surface disturbance when constructing the access road will not exceed 30 feet. All areas outside of the driving surface will be revegetated.
- E. When the road travels on fairly level ground, the road will be crowned and ditched with a maximum 2% slope from the tip of the road crown to the edge of the driving surface. Ditches will be constructed on each side of the road. The ditches will be 3 feet wide with 3:1 slopes. See road cross section diagram below:




- F. No turnouts will be constructed on the new portions of access road.
- G. No cattle guards will be installed on the new portions of access road.
- H. Right-of-way will be acquired before construction begins.
- I. No culverts or low water crossings will be constructed for the new portions of access road.
- J. Since the access road is on level ground, no lead-off ditches will be constructed for the new portions of access road.
- K. Any sharp turns in the in the new road will be rounded to facilitate turning by trucks.
- L. Newly constructed or reconstructed roads, on surface under the jurisdiction of the Bureau of Land Management, will be constructed as outlined in the BLM "Gold Book" and to meet the standards of the anticipated traffic flow and all anticipated weather requirements as needed. Construction will include ditching, draining, crowning and capping or sloping and dipping the roadbed as necessary to provide a well-constructed and safe road.
- M. All topsoil and fragmented rock removed in excavation will be used as directed in approved plan.

Ameredev Operating, LLC  
Green Jacket Fed Com 26 36 29 101H  
Section 29, Township 26S, Range 36E  
Lea County, New Mexico

**AMEREDEV**

**Section 3 – Location of Existing Wells**

*Exhibit 2 – One Mile Radius Existing Wells* depicts all known wells within a one mile radius of the Green Jacket Fed Com 26 36 29 101H. See *Exhibit 2a – One Mile Radius Wells List* for a list of wells depicted.

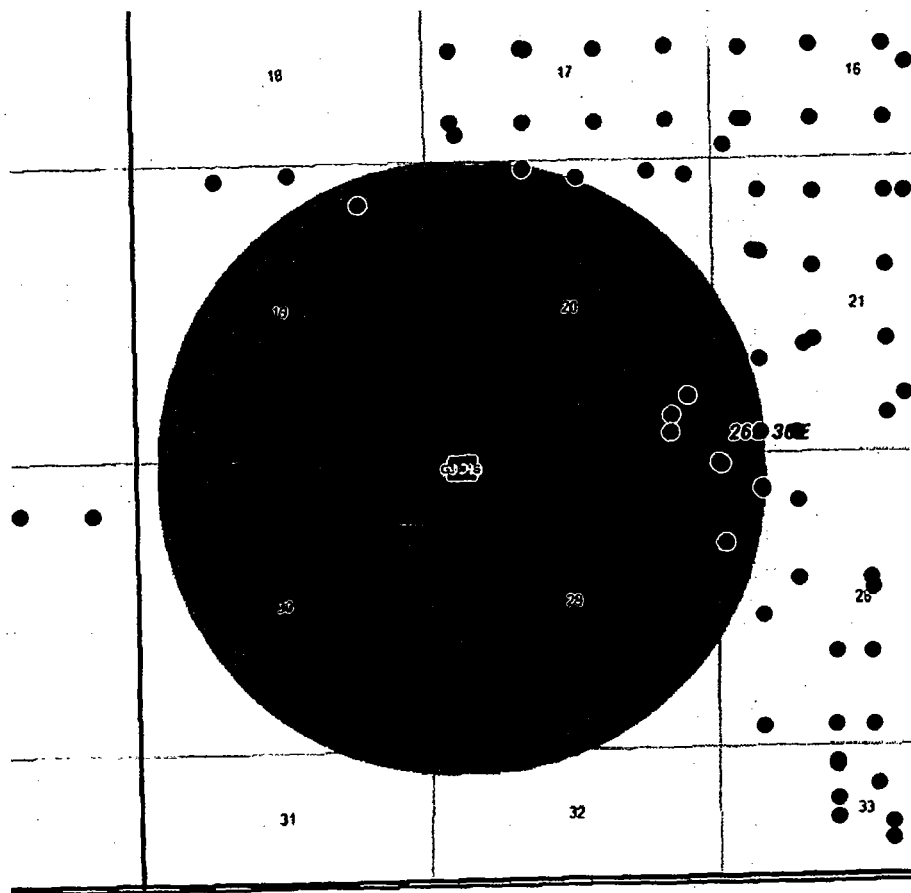


***Exhibit 2 – One Mile Radius Existing Wells***

API	WELL NAME	STATUS	TD
30025441050100	AZALEA 26-36-28 STATE #121H	OIL	17550
30025442290000	AZALEA 26-36-28 STATE #121Y	PILOT	13600
30025442290100	AZALEA 26-36-28 STATE #121Y	OIL	19469
30025441040000	AZALEA STATE 26-36-28 #111H	OIL	18993
30025259570000	LEA #WD-1	INJECTION	3420
30025260560000	LEA 7406-JV-S #9	DRY	1406
30025260680000	LEA 7406-JV-S #9-Y	OIL	3270
30025259200000	LEA 7406 JV-S #7	OIL	3270
30025441110000	PRIZEHOG BWZ STATE COM #002H	OIL	17188
30025098560000	SAND HILLS UNIT #6	ABDNLOC	1257
30025098570000	SAND HILLS UNIT A #1	DRY	3349
30025427330000	WILDHOG BWX STATE COM #001H	OIL	17244
30025261320000	WILSON /21/ FED #2	OIL	3500

**Exhibit 2a – One Mile Radius Existing Wells List**

**Section 4 – Location of Existing and/or Proposed Well Pad and Production Facilities**

- A. The multiple well pad will be located on Section 29, and will measure 466' x 400' x 500' x 323' x 84' (See *Exhibit 3 – Well Site Diagram*). Should any type of production facilities be located on the well pad, they will be strategically placed to allow for maximum interim reclamation, re-contouring, and revegetation of the well location.
- B. Production from the proposed well will be transported to an existing production facility named Amen Corner CTB, northeast of the well pad.
- C. A buried 4" poly flowline will be run approximately 13,281' from the Green Jacket Fed Com 26 36 29 101H to the existing Amen Corner CTB.
- D. All permanent (lasting more than six months) above ground structures including but not limited to pump jacks, storage tanks, barrels, pipeline risers, meter housing, etc., that are not subject to safety requirements will be painted a non-reflective paint color, Shale Green, from the BLM Standard Environmental Colors chart, unless another color is required in the APD Conditions of Approval.
- E. If any plans change regarding the production facility or other infrastructure (pipeline, electrical lines, etc.), Ameredev will submit a sundry notice or right-of-way (if applicable) prior to installation or construction.

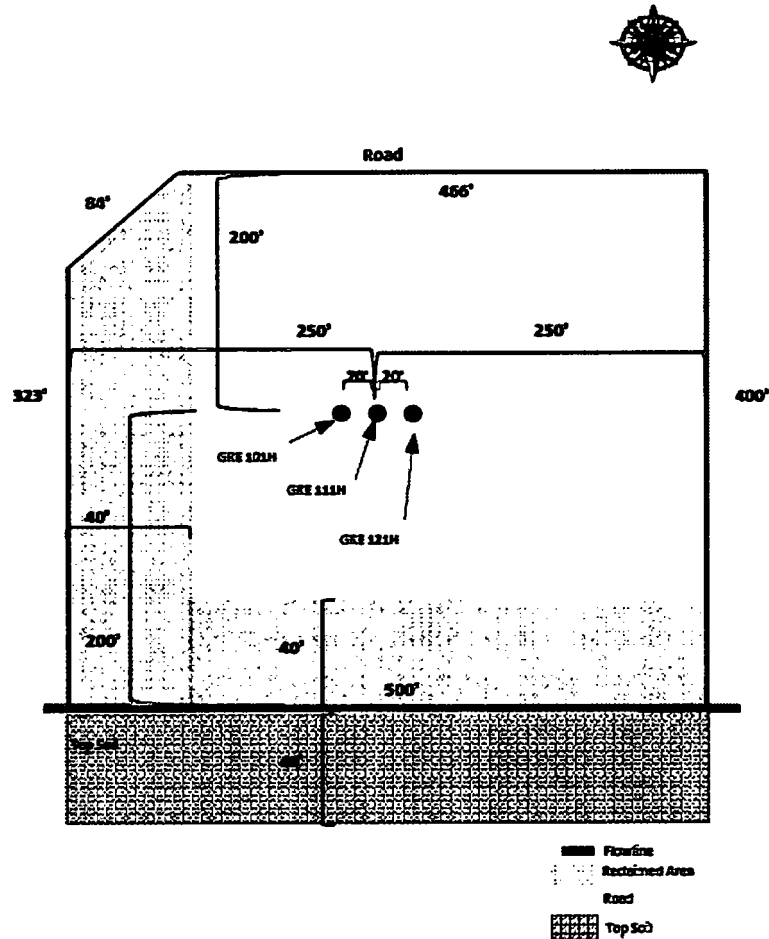

Green Jacket Fed Com 26 36 29 101H SHL: 26S 36E 262' FNL 752' FWL  
 Green Jacket Fed Com 26 36 29 111H SHL: 26S 36E 262' FNL 772' FWL  
 Green Jacket Fed Com 26 36 29 121H SHL: 26S 36E 262' FNL 792' FWL

*Exhibit 3 – Well Site Diagram*

**Section 5 - Location and Types of Water Supply**

- A. This location will be drilled using a combination of water and mud systems (outlined in the Drilling Program). The water will be obtained from preexisting water wells, by running a pump directly to the drilling rig. See *Exhibit 4 - Water Wells*, for a list of available water wells. In cases where a polyline is used to transport water for drilling or completion purposes, the existing and proposed roads into location will be utilized.

<u>Permit #</u>	<u>Well Name</u>	<u>Location (Lat/Lon)</u>
CP 1049 POD 2	Bennett	32°04'14.32" N, 103°12'32.30" W
CP 1378	S. Eppenour	32°05'40.62" N, 103°13' 35.26" W
CP 1285	Sec. 5	32°03'56.50" N, 103°17'37.04" W
CP 857	Capped	32°04'39.70" N, 103°16'51.13" W
C 2287	#1	32°03'59.0" N, 103°33'16.8" W
C 2286	#2	32°03'59.2" N, 103°33'15.2" W
C 2290	#3	32°04'1.0" N, 103°33' 12.6" W
C 2285	#4	32°04'3.7" N, 103°33'9.7" W
C 2288	#5	32°04'0.5" N, 103°33'8.4" W
C 2294	Garden	32°03'3.2" N, 103°32'38.1" W
C 2293	House	32°03'2.3" N, 103°32'36.8" W
J-11-S-3	Farm Well #2	32°03'08.4" N, 103°16'35.2" W
J-11-S-2	Farm Well #3	32°03'11.5" N, 103°17'02.0" W
J-11-S	Farm Well #4	32°03'24.6" N, 103°17'02.1" W
CP 1170 POD 1	CB 1	32°03'57.2" N, 103°18'45.3" W
CP 1170 POD 5		32°07'17.1" N, 103°17'48.0" W
CP 1263 POD 5	CB 2	32°03'56.27" N, 103°18'27.4" W
CP 1263 POD 3	CB 3	32°03'54.90" N, 103°18'16.74" W
CP 1351 POD 1	CB 4	32°03'57.16" N, 103°17'45.13" W
CP 1351 POD 2	CB 5	32°03'30.70" N, 103°17'45.70" W
J 26	Ryan	32°01'20.41" N, 103°15'49.46" W
J 3		32°02'41.5" N, 103°18'55.8" W

***Exhibit 4 – Water Wells***



**Section 6 – Construction/Construction Materials**

- A. Caliche will be obtained from the caliche pit located at Lat: 32° 6'28.78"N, Long: 103°16'58.77"W, the caliche pit at Lat: 32° 6'33.14"N, Long: 103°18'44.16"W, or the caliche pit at Lat: 32° 3'8.30"N, Long: 103°13'57.00"W.
- B. Caliche utilized for the drilling pad will be obtained either from the locations listed above, an existing approved mineral pit, or by benching into a hill, which will allow the pad to be level with existing caliche from the cut, or extracted by "flipping" the well location. A mineral material permit will be obtained from the BLM prior to excavating any caliche on Federal Lands. Amount will vary for each pad. The procedure for "flipping" a well location is as follows:
1. An adequate amount of topsoil/root zone (usually top 6 inches of soil) will be stripped from the proposed well location and stockpiled along the side of the well location as depicted on the *Exhibit 3 - Well Site Diagram*.
  2. An area will be used within the proposed well site dimensions to excavate caliche.
  3. Subsoil will be removed and stockpiled within the surveyed well pad dimensions.
  4. Once caliche/surfacing mineral is found, the mineral material will be excavated and stock piled within the approved drilling pad dimensions.
  5. Subsoil will then be pushed back in the excavated hole and caliche will be spread accordingly across the entire well pad and road (if available).
  6. Neither caliche, nor subsoil will be stockpiled outside of the well pad dimensions. Topsoil will be stockpiled along the edge of the pad as depicted in *Exhibit 3 – Well Site Diagram*.
  7. In the event that no caliche is found onsite, caliche will be hauled in from a BLM approved caliche pit or other established mineral pit. A BLM mineral material permit will be acquired prior to obtaining any mineral material from BLM pits or federal land.

**Section 7 - Methods of Handling Waste**

- A. Drill cuttings, mud, salts and other chemicals will be properly disposed of into steel tanks on site and hauled to a State approved commercial disposal facility.
- B. Garbage and trash produced during drilling and completion operations will be collected in a portable metal trash container and disposed of properly at a state approved disposal facility. All trash on and around the well site will be collected for disposal.
- C. Human waste and grey water will be properly contained and disposed of properly at a state approved disposal facility.
- D. After drilling and completion operations, trash, chemicals, salts, frac sand and other waste material will be removed and disposed of properly at a State approved commercial disposal facility.

**Section 8 - Ancillary Facilities**

- A. No ancillary facilities will be needed for the proposed project.

**Section 9 - Well Site Layout**

- A. See *Exhibit 3 - Well Site Diagram*. The following information is presented:
1. Reasonable scale
  2. Well pad dimensions/orientation
  3. Proposed access road
  4. Topsoil stockpile
- B. The proposed drilling pad was staked and surveyed by a professional surveyor. The attached survey plat of the well site depicts the drilling pad layout as staked.
- C. Topsoil salvaging
1. Grass, forbs, and small woody vegetation such as mesquite will be excavated as the topsoil is removed. Large woody vegetation will be stripped and stored separately and re-spread evenly on the site following topsoil re-spreading. Topsoil depth is defined as the top layer of soil that contains 80% of the roots. In areas to be heavily disturbed, the top 6 inches of soil material will be stripped and stockpiled on the perimeter of the well location and along the perimeter of the access road to control run-on and run-off, to keep topsoil viable, and to make redistribution of topsoil more efficient during interim reclamation. Stockpiled topsoil should include vegetative material. Topsoil will be clearly segregated and stored separately from subsoils. Contaminated soil will not be stockpiled, but properly treated and handled prior to topsoil salvaging.

**Section 10 - Plans for Final Surface Reclamation**

**Reclamation Objectives**

- A. The objective of interim reclamation is to restore vegetative cover and a portion of the landform sufficient to maintain healthy, biologically active topsoil, to control erosion, and to minimize habitat and forage loss, visual impact, and weed infestation during the life of the well or facilities.
- B. The long-term objective of final reclamation is to return the land to a condition similar to what existed prior to disturbance. This includes restoration of the landform and natural vegetative community, hydrologic systems, visual resources, and wildlife habitats. To ensure that the long-term objective will be reached through human and natural processes, actions will be taken to ensure standards are met for site stability, visual quality, hydrological functioning, and vegetative productivity.
- C. The BLM will be notified at least 3 days prior to the commencement of any reclamation procedures.

- D. If circumstances allow, interim reclamation and/or final reclamation actions will be completed no later than 6 months from when the final well on location has been completed or plugged. Ameredev will gain written permission from the BLM if more time is needed.
- E. Interim reclamation will be performed on the well site after the well is drilled and completed. *Exhibit 3 – Well Site Diagram* depicts the location and dimension of the planned interim reclamation for the well site.

**Interim Reclamation Procedures (if performed)**

- A. Within 30 days of well completion, the well location and surrounding areas will be cleared of, and maintained free of, all materials, trash, and equipment not required for production.
- B. In areas planned for interim reclamation, all the surfacing material will be removed and returned to the original mineral pit or recycled to repair or build roads and well pads.
- C. The areas planned for interim reclamation will then be contoured to the original contour if feasible, or if not feasible, to an interim contour that blends with the surrounding topography as much as possible. Where applicable, the fill material of the well pad will be backfilled into the cut to bring the area back to the original contour. The interim cut and fill slopes prior to re-seeding will not be steeper than a 3:1 Ratio, unless the adjacent native topography is steeper. Note: Constructed slopes may be much steeper during drilling, but will be re-contoured to the above ratios during interim reclamation.
- D. Topsoil will be evenly re-spread and aggressively revegetated over the entire disturbed area not needed for all-weather operations, including cuts and fills. To seed the area, the proper BLM mixture, free of noxious weeds, will be used. Final seedbed preparation will consist of contour cultivating to a depth of 4 to 6 inches within 24 hours prior to seeding, dozer tracking, or other imprinting, in order to break the soil crust and create seed germination micro-sites.
- E. Proper erosion control methods will be used on the area to control erosion, runoff, and siltation of the surrounding area.
- F. The interim reclamation will be monitored periodically to ensure that vegetation has reestablished and that erosion is controlled.

**Final Reclamation Procedures (well pad, buried pipelines, etc.)**

- A. Prior to final reclamation procedures, the well pad, road, and surrounding area will be cleared of material, trash, and equipment.
- B. All surfacing material will be removed and returned to the original mineral pit or recycled to repair or build roads and well pads.
- C. All disturbed areas, including roads, pipelines, pads, production facilities, and interim reclaimed areas will be re-contoured to the contour existing prior to initial construction or a contour that blends indistinguishably with the surrounding landscape. Topsoil that was spread over the interim reclamation areas will be stockpiled prior to re-contouring. The topsoil will be redistributed evenly over the entire disturbed site to ensure successful revegetation.
- D. After all the disturbed areas have been properly prepared, the areas will be seeded with the proper BLM seed mixture, free of noxious weeds. Final seedbed preparation will consist of

contour cultivating to a depth of 4 to 6 inches within 24 hours prior to seeding, dozer tracking, or other imprinting, in order to break the soil crust and create seed germination micro-sites.

- E. Proper erosion control methods will be used on the area to control erosion, runoff, and siltation of the surrounding area.
- F. All unused equipment and structures including pipelines, electric line poles, tanks, etc. that serviced the well will be removed.
- G. All reclaimed areas will be monitored periodically to ensure that revegetation occurs, that the area is not re-disturbed, and that erosion is controlled.

#### **Section 11 - Surface Ownership**

- A. BLM has surface ownership for proposed project area.

#### **Section 12 - Other Information**

- A. There are no dwellings within 1 mile of this location.
- B. An on-site meeting for Ameredev's Green Jacket Fed Com 26 36 29 101H well was held on July 23, 2018. (NOS ID#: 10400032176). Attendees included Jeff Robertson (BLM), Shane McNeely (Ameredev), and Ged Adams (Topographic).
- C. The well pad described in this document – Green Jacket #1S (GJ #1S) - will contain 3 wells that produce into an existing central tank battery (CTB) located northeast of the well pad. The wells share a common pad access road. Each well will have its own flowline. The three flowlines will share a common corridor that will terminate at the existing Amen Corner CTB. The wells that share the well pad are:
  - Green Jacket Fed Com 26 36 29 101H, APD ID#: 10400034498
  - Green Jacket Fed Com 26 36 29 111H, APD ID#: 10400034496
  - Green Jacket Fed Com 26 36 29 121H, APD ID#: 10400033661

#### **Ameredev field representative:**

Zac Boyd, Operations Supervisor

Cell: (432) 385-6996

Email: [zboyd@ameredev.com](mailto:zboyd@ameredev.com)

#### **Ameredev office contact:**

Christie Hanna, Regulatory Coordinator

Direct: (737) 300-4723

Email: [channa@ameredev.com](mailto:channa@ameredev.com)

**Ameredev Operating, LLC Address:** 5707 Southwest Parkway Building 1, Suite 275 Austin, Texas 78735



U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT

## PWD Data Report

07/08/2019

### Section 1 - General

Would you like to address long-term produced water disposal? NO

### Section 2 - Lined Pits

Would you like to utilize Lined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Lined pit PWD on or off channel:

Lined pit PWD discharge volume (bbl/day):

Lined pit specifications:

Pit liner description:

Pit liner manufacturers information:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Lined pit precipitated solids disposal schedule:

Lined pit precipitated solids disposal schedule attachment:

Lined pit reclamation description:

Lined pit reclamation attachment:

Leak detection system description:

Leak detection system attachment:

Lined pit Monitor description:

Lined pit Monitor attachment:

Lined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Lined pit bond number:

Lined pit bond amount:

Additional bond information attachment:

### **Section 3 - Unlined Pits**

Would you like to utilize Unlined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Unlined pit PWD on or off channel:

Unlined pit PWD discharge volume (bbl/day):

Unlined pit specifications:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Unlined pit precipitated solids disposal schedule:

Unlined pit precipitated solids disposal schedule attachment:

Unlined pit reclamation description:

Unlined pit reclamation attachment:

Unlined pit Monitor description:

Unlined pit Monitor attachment:

Do you propose to put the produced water to beneficial use?

Beneficial use user confirmation:

Estimated depth of the shallowest aquifer (feet):

Does the produced water have an annual average Total Dissolved Solids (TDS) concentration equal to or less than that of the existing water to be protected?

TDS lab results:

Geologic and hydrologic evidence:

State authorization:

Unlined Produced Water Pit Estimated percolation:

Unlined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Unlined pit bond number:

Unlined pit bond amount:

Additional bond information attachment:

### **Section 4 - Injection**

Would you like to utilize Injection PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Injection PWD discharge volume (bbl/day):

Injection well mineral owner:

**Injection well type:**

**Injection well number:**

**Injection well name:**

**Assigned injection well API number?**

**Injection well API number:**

**Injection well new surface disturbance (acres):**

**Minerals protection information:**

**Mineral protection attachment:**

**Underground Injection Control (UIC) Permit?**

**UIC Permit attachment:**

### **Section 5 - Surface Discharge**

**Would you like to utilize Surface Discharge PWD options? NO**

**Produced Water Disposal (PWD) Location:**

**PWD surface owner:**

**PWD disturbance (acres):**

**Surface discharge PWD discharge volume (bbl/day):**

**Surface Discharge NPDES Permit?**

**Surface Discharge NPDES Permit attachment:**

**Surface Discharge site facilities information:**

**Surface discharge site facilities map:**

### **Section 6 - Other**

**Would you like to utilize Other PWD options? NO**

**Produced Water Disposal (PWD) Location:**

**PWD surface owner:**

**PWD disturbance (acres):**

**Other PWD discharge volume (bbl/day):**

**Other PWD type description:**

**Other PWD type attachment:**

**Have other regulatory requirements been met?**

**Other regulatory requirements attachment:**



**U.S. Department of the Interior  
BUREAU OF LAND MANAGEMENT**

## **Bond Info Data Report**

07/08/2019

### **Bond Information**

**Federal/Indian APD:** FED

**BLM Bond number:** NMB001478

**BIA Bond number:**

**Do you have a reclamation bond?** NO

**Is the reclamation bond a rider under the BLM bond?**

**Is the reclamation bond BLM or Forest Service?**

**BLM reclamation bond number:**

**Forest Service reclamation bond number:**

**Forest Service reclamation bond attachment:**

**Reclamation bond number:**

**Reclamation bond amount:**

**Reclamation bond rider amount:**

**Additional reclamation bond information attachment:**
