

DISTRICT I
P.O. Box 1980, Hobbs, NM 88240

DISTRICT II
P.O. Drawer DD, Artesia, NM 88210

DISTRICT III
1000 Rio Brazos Rd., Aztec, NM 87410

OIL CONSERVATION DIVISION
P.O. Box 2088
Santa Fe, New Mexico 87504-2088

WELL API NO. 30-025-05757 ✓
5. Indicate Type of Lease STATE ☒ FEE ☐
6. State Oil & Gas Lease No. B-5553
7. Lease Name or Unit Agreement Name NORTH MONUMENT G/SA UNIT BLK. 10
8. Well No. 16
9. Pool name or Wildcat EUNICE MONUMENT G/SA

SUNDRY NOTICES AND REPORTS ON WELLS
(DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A
DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT"
(FORM C-101) FOR SUCH PROPOSALS.)

1. Type of Well: OIL WELL ☒ GAS WELL ☐ OTHER ☐	2. Name of Operator AMERADA HESS CORPORATION
3. Address of Operator DRAWER D, MONUMENT, NM 88265	4. Well Location Unit Letter P : 790 Feet From The SOUTH Line and 990 Feet From The EAST Line

Section 30	Township 19S	Range 37E	NMPM	LEA	County
10. Elevation (Show whether DF, RKB, RT, GR, etc.)					

11. Check Appropriate Box to Indicate Nature of Notice, Report, or Other Data	
NOTICE OF INTENTION TO:	SUBSEQUENT REPORT OF:
PERFORM REMEDIAL WORK ☐	REMEDIAL WORK ☐
TEMPORARILY ABANDON ☐	ALTERING CASING ☐
PULL OR ALTER CASING ☐	COMMENCE DRILLING OPNS. ☐
OTHER: ☐	PLUG AND ABANDONMENT ☐
	CASING TEST AND CEMENT JOB ☐
	OTHER: CASING TEST ☒

12. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work) SEE RULE 1103.
5-7 THRU 5-10-93

MIRU X-PERT WELL SERVICE PULLING UNIT & TOH W/RODS, & PUMP. REMOVED 6" 600 TUBINGHEAD FLANGE & INSTALLED A 6" 600 MANUAL BOP & TOH W/TBG. TIH W/A 4-3/4" DRILL BIT TAGGED AT 3,912', & TOH. TIH W/A 5-1/2" ELDER LOK-SET RETRIEVABLE BRIDGE PLUG, SET AT 3,750'. REVERSED CASING W/100 BBLs. FRESH WATER & PRESSURE TESTED CASING FROM 0' TO 3,750'. PRESSURE INCREASED FROM 560 PSI TO 570 PSI IN 30 MIN. RELEASED RBP & TOH W/RBP. TIH W/5-1/2" BAKER TAC, W/35,000# SHEAR PINS ON 2-3/8" H-40 TBG. REMOVED 6" 600 MANUAL BOP & INSTALLED A 6" 600 SLIP TYPE TUBING HANGER FLANGE. SET TAC AT 3,750', W/12,000# TENSION & SN AT 3,845'. TIH W/PUMP & RODS. LOADED TUBING & CHECKED PUMP ACTION. RIGGED DOWN PULLING UNIT, CLEANED LOCATION & RESUMED PROD. WELL.

TEST OF 5-16-93: PROD. 21 B.O., 67 B.W. & 17 MCFGPD IN 24 HRS.

I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE R. L. Wheeler, Jr. TITLE SUPV. ADM. SVC. DATE 5-21-93
TYPE OR PRINT NAME R.L. WHEELER, JR. (505)
TELEPHONE NO. 393-2144


(This space for State Use)

APPROVED BY _____ TITLE _____ DATE MAY 27 1993

CONDITIONS OF APPROVAL, IF ANY:

RECEIVED
MAY 2 - 1993
OCD HOBBS OFFICE

RECEIVED
MAY 2 - 1993
OCD HOBBS OFFICE

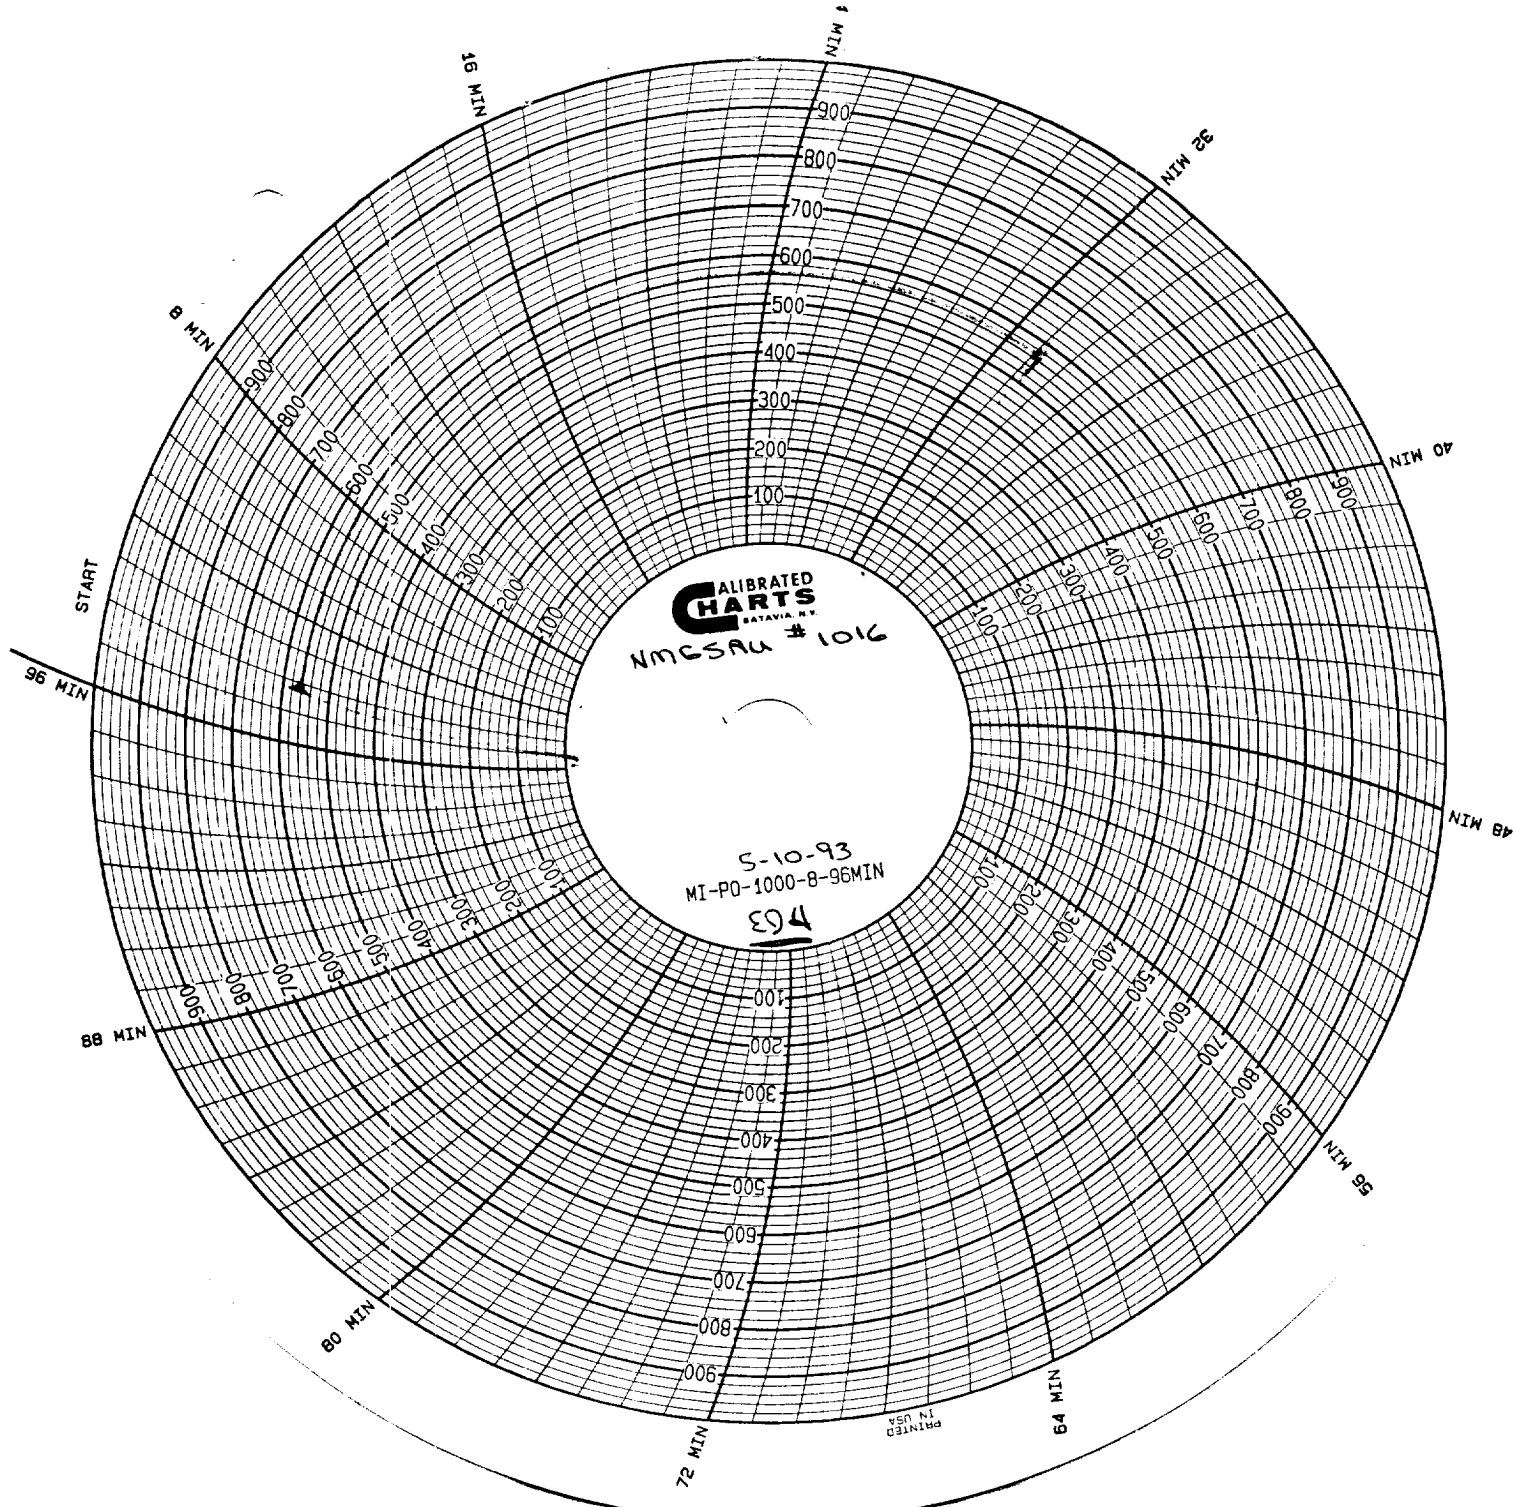

CALIBRATED
CHARTS
BATAVIA, N.Y.
NMCSAU # 1016

5-10-93
MI-PO-1000-8-96MIN
764

PRINTED
IN USA

RECEIVED
MAY 20 1990
OCD HOBBS OFFICE

RECEIVED
MAY 20 1990
OCD HOBBS OFFICE
