

CONTINENTAL OIL COMPANY  
 ACTUAL METHOD OF DUAL COMPLETION  
 LOCKHART B-11 NO. 15 TB-D

11-21-37

13-3/8" set at  
 307' (Cement  
 circulated).


9-5/8" set at  
 2995' (Cement  
 to 2000').

Blinebry  
 Perforations  
 5752'-5856'

Packer (detail  
 at right).

Drinkard Perforations  
 6589'-6665'

7" set at 6750'  
 (Cement to 3000').

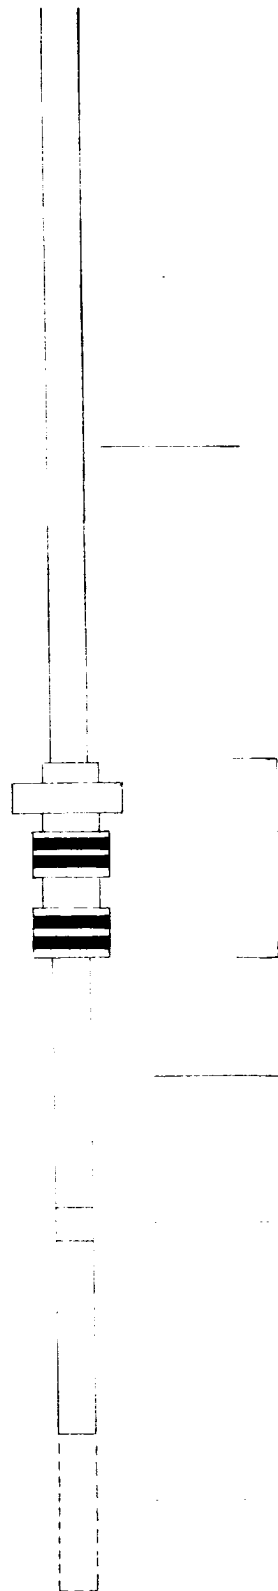

2" EUE tubing  
 to surface.

Baker Model "E" Anchor  
 Tubing Seal Assembly  
 and Baker Model "D"  
 Retainer Production  
 Packer set at 6540'.

2" EUE Tubing

Otis Type "J"  
 Seating Nipple

Baker Production  
 Tube at 6635'.
