

Submit 1 Copy To Appropriate District
Office
District I
1625 N. French Dr., Hobbs, NM 88240
District II
1301 W. Grand Ave., Artesia, NM 88210
District III
1000 Rio Brazos Rd., Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM
87505

State of New Mexico
Energy, Minerals and Natural Resources

Form C-103
October 13, 2009

OIL CONSERVATION DIVISION

1220 South St. Francis Dr.
Santa Fe, NM 87505

HOBBS OCD

MAY 28 2013

SUNDRY NOTICES AND REPORTS ON WELLS (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)		WELL API NO. 30-025-34197
1. Type of Well: Oil Well <input type="checkbox"/> Gas Well <input checked="" type="checkbox"/> Other SWD <input type="checkbox"/>		5. Indicate Type of Lease STATE <input checked="" type="checkbox"/> FEE <input type="checkbox"/>
2. Name of Operator D.K.D., L.L.C.		6. State Oil & Gas Lease No. 29221
3. Address of Operator PO Box 682, Tatum, NM 88267		7. Lease Name or Unit Agreement Name Watson 6
4. Well Location Unit Letter <u>2857</u> feet from the <u>S</u> line and <u>1417</u> feet from the <u>W</u> line Section <u>6</u> Township <u>16</u> Range <u>36</u> NMPM County <u>Lea</u>		8. Well Number <u>1</u>
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 3974		9. OGRID Number 210091
		10. Pool name or Wildcat Upper Permo Penn

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:

PERFORM REMEDIAL WORK ☐ PLUG AND ABANDON ☐
TEMPORARILY ABANDON ☐ CHANGE PLANS ☐
PULL OR ALTER CASING ☐ MULTIPLE COMPL ☐
DOWNHOLE COMMINGLE ☐

SUBSEQUENT REPORT OF:

REMEDIAL WORK ☐ ALTERING CASING ☐
COMMENCE DRILLING OPNS. ☐ P AND A ☐
CASING/CEMENT JOB ☐

OTHER: ☐

OTHER: SWD ☒

13. Describe proposed or completed operations. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work). SEE RULE 19.15.7.14 NMAC. For Multiple Completions: Attach wellbore diagram of proposed completion or recompletion.

5/14/13: Rig up pulling unit. Packer stuck and tubing parted. Pull out of hole; laid down all tubing; found part @ 6,824. Unloaded work-string.

5/15/13: Picked up work-string with over-shot; fished tubing; unseat packer; pulled out and laid down bad tubing.

5/16/13: Run bit & scraper; pulled back out. Shut down overnight and weekend.

5/20/13: Run in hole bridge plug and packer. Tested casing. Found to test okay.

5/21/13: Pull out of hole; lay down bp & packer; shut down waiting on new tubing and new packer.

5/22/13: Run new tubing and packer (model R); packer set at 10,262 ft; top perforation at 10,340. Load casing. Shut down overnight.

5/23/13: Run chart with Maxey/OCD present. Tested okay.

Spud Date:

Rig Release Date:

I hereby certify that the information above is true and complete to the best of my knowledge and belief.


SIGNATURE Danny R. Watson TITLE Owner DATE 12/16/2011

Type or print name Danny R. Watson E-mail address: dkdlle@leaco.net PHONE: (575)398-3490

For State Use Only

APPROVED BY
Conditions of Approval (if any)

TITLE DEPT. MGR DATE 6-20-2013

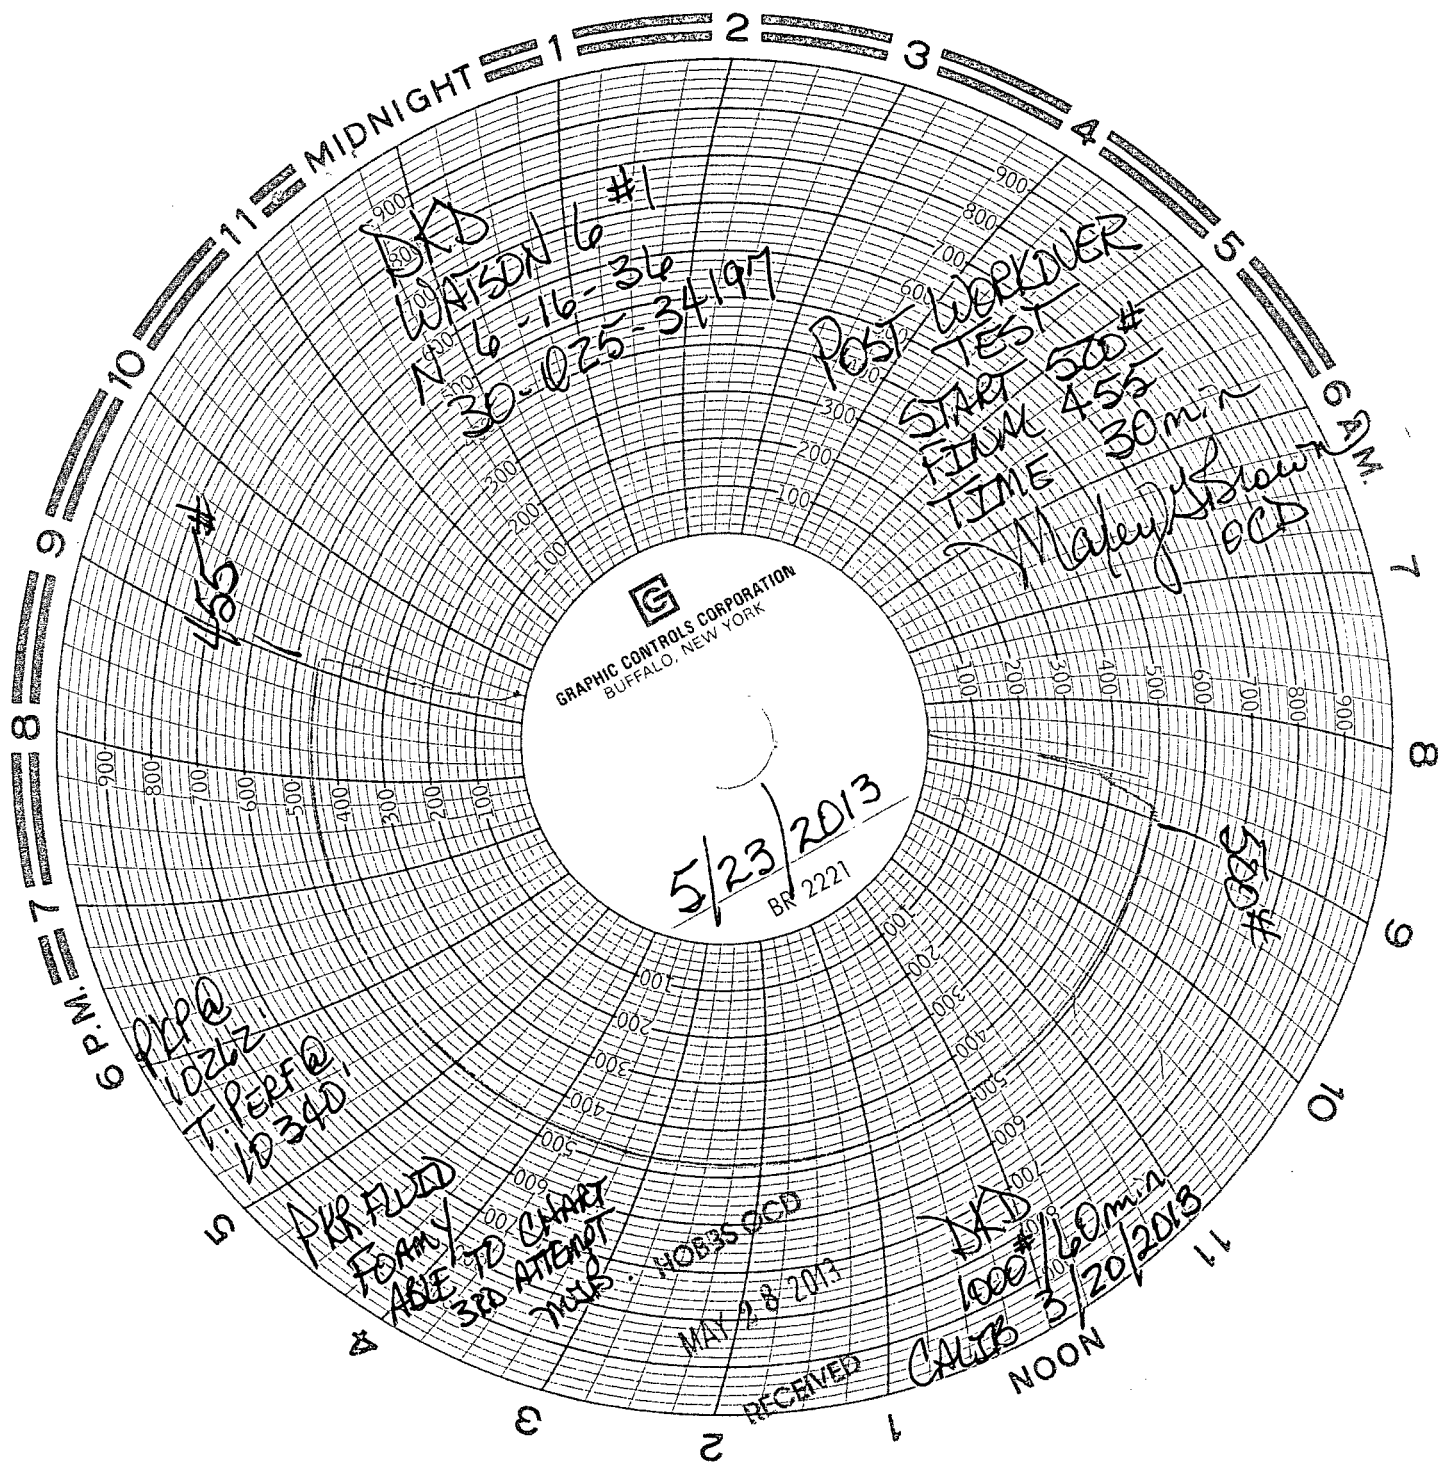

DKD
WATSON #1
N 16-16-36
30-025-34/197

POST WORKOVER
TEST
START 500#
FINISH 455
TIME 30 min
Malay Brown
OCD

PRP@
1026Z
T. PERF@
10340

PR FILLED
FOAM
ABLE TO CHART
3RD ATTEMPT
MUR

HOBBS OCD
MAY 28 2013

DKD
1000 #1
CALIB 5/20/2013
NOON

GRAPHIC CONTROLS CORPORATION
BUFFALO, NEW YORK

5/23/2013
BR 2221

RECEIVED
