

OCD Hobbs

ATS-15-472

FORM APPROVED  
OMB No. 1004-0137  
Expires October 31, 2014

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

HOBBS OCD

APPLICATION FOR PERMIT TO DRILL OR REENTER

APR 9 2016

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		RECEIVED
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		
2. Name of Operator Devon Energy Production Company, L.P. 6137/		
3a. Address 333 W. Sheridan Oklahoma City, OK 73102-5010	3b. Phone No. (include area code) 405.228.7203	5. Lease Serial No. NMNM98192
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface 2590 FNL & 614 FWL, Unit E Sec.16 PP: 2590 FNL & 660 FWL At proposed prod. zone 330 FNL & 660 FWL, Unit D Sec. 9		6. If Indian, Allottee or Tribe Name
14. Distance in miles and direction from nearest town or post office* Approximately 23.21 miles NE of Malaga, NM		7. If Unit or CA Agreement, Name and No.
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) See attached map	16. No. of acres in lease NMNM98192 - 640 ac	8. Lease Name and Well No. Big Cat 16-9 State Fed Com 1H 316163
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. See attached map	19. Proposed Depth TVD: 10,618' MD: 17,912'	9. API Well No. 30-025-43196
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3670.9' GL	22. Approximate date work will start* 09/15/2015	10. Field and Pool, or Exploratory WC-025 G-07 S233204D; Bone Spring
23. Estimated duration 45 Days		11. Sec., T. R. M. or Blk. and Survey or Area Sec. 16 T23S R32E 9933
24. Attachments		12. County or Parish Lea County
		13. State NM

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification
6. Such other site specific information and/or plans as may be required by the BLM.

25. Signature <i>Trina C. Couch</i>	Name (Printed/Typed) Trina C. Couch	Date 03/03/2015
Title Regulatory Analyst		
Approved by (Signature) <i>/s/George MacDonell</i>	Name (Printed/Typed)	Date APR 26 2016
Title FIELD MANAGER		Office CARLSBAD FIELD OFFICE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.

APPROVAL FOR TWO YEARS

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

See attached NMOCD  
Conditions of Approval

Carlsbad Controlled Water Basin

Ka  
04/02/16

SECRET

Approval Subject to General Requirements  
& Special Stipulations Attached

SEE ATTACHED FOR  
CONDITIONS OF APPROVAL

MAY 03 2016

## Devon Energy, Big Cat 16-9 State Fed Com 1H

## 1. Geologic Formations

TVD of target	10,618'	Pilot hole depth	N/A
MD at TD:	17,912'	Deepest expected fresh water:	400'

## Basin

[illegible]

\*H<sub>2</sub>S, water flows, loss of circulation, abnormal pressures, etc.

## Devon Energy, Big Cat 16-9 State Fed Com 1H

### 2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn	SF Collapse	SF Burst	SF Tension
	From	To							
17.5"	0	1,245'	13.375"	48	H-40	STC	1.38	3.11	9.05
12.25"	0	4,750'	9.625"	40	HCK-55	BTC	1.557	1.45	4.87
8.75"	0	17,912'	5.5"	17	HCP-110	BTC	1.55	1.93	3.15
BLM Minimum Safety Factor							1.125	1.00	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 <sup>rd</sup> string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 <sup>nd</sup> string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

## Devon Energy, Big Cat 16-9 State Fed Com 1H

### 3. Cementing Program

Casing	# Sks	Wt. lb/ gal	H <sub>2</sub> O gal/sk	Yld ft <sup>3</sup> / sack	500# Comp. Strength (hours)	Slurry Description
13-3/8" Surface	1320	14.8	6.32	1.33	6	Tail: Class C Cement + 0.125 lbs/sack Poly-E-Flake
9-5/8" Inter.	970	12.9	9.81	1.85	14	Lead: (65:35) Class C Cement: Poz (Fly Ash): 6% BWOC Bentonite + 5% BWOW Sodium Chloride + 0.125 lbs/sack Poly-E-Flake
	430	14.8	6.32	1.33	6	Tail: Class C Cement + 0.125 lbs/sack Poly-E-Flake
5-1/2" Prod	510	11.9	12.89	2.31	n/a	1 <sup>st</sup> Lead: (50:50) Class H Cement: Poz (Fly Ash) + 10% BWOC Bentonite + 1 lb/sk of Kol-Seal + 0.3% BWOC HR-601 + 0.5lb/sk D-Air 5000
	330	12.5	10.86	1.96	30	2 <sup>nd</sup> Lead: (65:35) Class H Cement: Poz (Fly Ash) + 6% BWOC Bentonite + 0.25% BWOC HR-601 + 0.125 lbs/sack Poly-E-Flake
	2080	14.5	5.31	1.2	25	Tail: (50:50) Class H Cement: Poz (Fly Ash) + 0.5% bwoc HALAD-344 + 0.4% bwoc CFR-3 + 0.2% BWOC HR-601 + 2% bwoc Bentonite

Casing String	TOC	% Excess
13-3/8" Surface	0'	100%
9-5/8" Intermediate	0'	75%
5-1/2" Production Casing	4250'	25%

## Devon Energy, Big Cat 16-9 State Fed Com 1H

### 4. Pressure Control Equipment

N	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
---	--

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
12-1/4"	13-5/8"	3M	Annular	x	50% of working pressure
			Blind Ram		3M
			Pipe Ram		
			Double Ram	x	
			Other*		
8-3/4"	13-5/8"	3M	Annular	x	50% testing pressure
			Blind Ram		3M
			Pipe Ram		
			Double Ram	x	
			Other *		
			Annular	x	
			Blind Ram		
			Pipe Ram		
			Double Ram	x	
			Other *		

\*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

Y	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
---	---

## Devon Energy, Big Cat 16-9 State Fed Com 1H

Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
Y	Are anchors required by manufacturer?
Y	<p>A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.</p> <p>Devon proposes using a multi-bowl wellhead assembly (FMC Uni-head). This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 3000 (3M) psi.</p> <ul style="list-style-type: none"> <li>Wellhead will be installed by FMC's representatives.</li> <li>If the welding is performed by a third party, the FMC's representative will monitor the temperature to verify that it does not exceed the maximum temperature of the seal.</li> <li>FMC representative will install the test plug for the initial BOP test.</li> <li>FMC will install a solid steel body pack-off to completely isolate the lower head after cementing intermediate casing. After installation of the pack-off, the pack-off and the lower flange will be tested to 3M, as shown on the attached schematic. Everything above the pack-off will not have been altered whatsoever from the initial nipple up. Therefore the BOP components will not be retested at that time.</li> <li>If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head will be cut and top out operations will be conducted.</li> <li>Devon will pressure test all seals above and below the mandrel (but still above the casing) to full working pressure rating.</li> <li>Devon will test the casing to 0.22 psi/ft or 1500 psi, whichever is greater, as per Onshore Order #2.</li> </ul> <p>After running the 13-3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 3M will be installed on the FMC Uni-head wellhead system and will undergo a 250 psi low pressure test followed by a 3,000 psi high pressure test. The 3,000 psi high and 250 psi low test will cover testing requirements a maximum of 30 days, as per Onshore Order #2. If the well is not complete within 30 days of this BOP test, another full BOP test will be conducted, as per Onshore Order #2.</p> <p>After running the 9-5/8' intermediate casing with a mandrel hanger, the 13-5/8" BOP/BOPE system with a minimum rating of 3M will already be installed on the FMC Uni-head.</p> <p>The pipe rams will be operated and checked each 24 hour period and each time the drill pipe is out of the hole. These tests will be logged in the daily driller's log. A 2" kill line and 3" choke line will be incorporated into the drilling spool below the ram BOP. In addition to the rams and annular preventer, additional BOP accessories include a kelly cock, floor safety valve, choke lines, and choke manifold rated at 3,000 psi WP.</p>

## Devon Energy, Big Cat 16-9 State Fed Com 1H

	Devon requests a variance to use a flexible line with flanged ends between the BOP and the choke manifold (choke line). The line will be kept as straight as possible with minimal turns
	See attached schematic.

### 5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	1,245'	FW Gel	8.6-8.8	28-34	N/C
1,245'	4,750'	Saturated Brine	10.0-10.2	28-34	N/C
4,750'	17,912'	Cut Brine	8.5-9.3	28-34	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

### 6. Logging and Testing Procedures

Logging, Coring and Testing	
x	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No Logs are planned based on well control or offset log information.
	Drill stem test? If yes, explain
	Coring? If yes, explain

Additional logs planned	Interval
Resistivity	Int. shoe to KOP
Density	Int. shoe to KOP
X CBL	Production casing
X Mud log	Intermediate shoe to TD
PEX	

## Devon Energy, Big Cat 16-9 State Fed Com 1H

### 7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	2799 psi
Abnormal Temperature	No

Mitigation measure for abnormal conditions. Describe. Lost circulation material/sweeps/mud scavengers.

Hydrogen Sulfide (H <sub>2</sub> S) monitors will be installed prior to drilling out the surface shoe. If H <sub>2</sub> S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.	
N	H <sub>2</sub> S is present
Y	H <sub>2</sub> S Plan attached

### 8. Other facets of operation

Is this a walking operation? No.


Will be pre-setting casing? No.

Attachments

☒ Directional Plan

☐ Other, describe



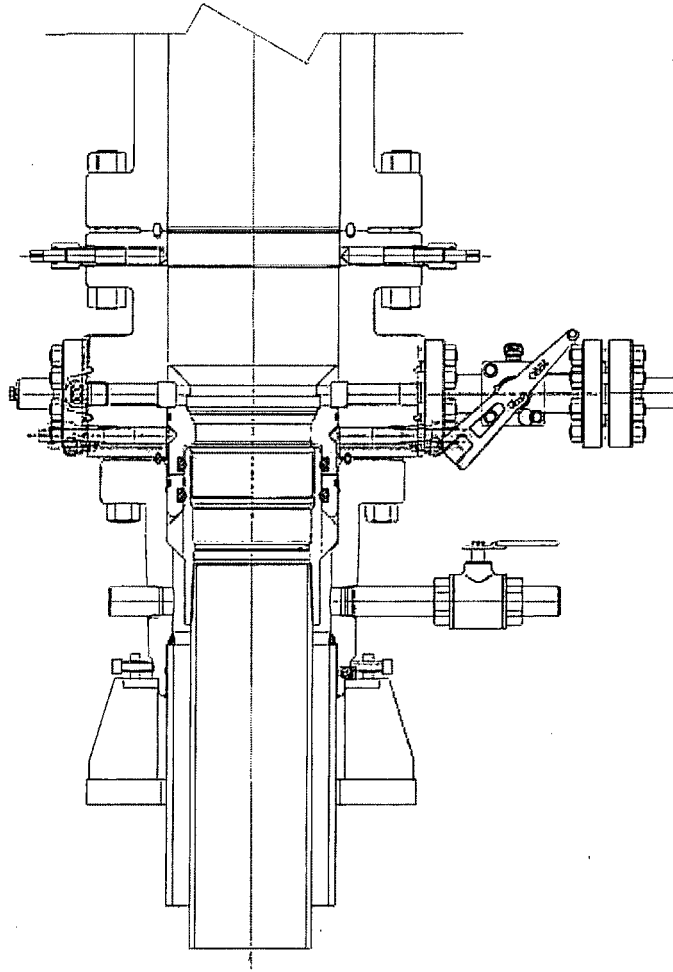


PRIMARY MODE

**DEVON ENERGY**  
**ARTESIA**  
**S.E.N.M**  
**13 3/8 X 9 5/8**

QUOTE LAYOUT  
F18648  
REF: DM100161737  
DM100151315


<b>PRIVATE AND CONFIDENTIAL</b> <small>THIS DOCUMENT AND ALL THE INFORMATION CONTAINED HEREIN ARE THE CONFIDENTIAL AND EXCLUSIVE PROPERTY OF FMC TECHNOLOGIES AND MAY NOT BE REPRODUCED, USED, DISCLOSED, OR MADE PUBLIC IN ANY MANNER PRIOR TO EXPRESS WRITTEN AUTHORIZATION BY FMC TECHNOLOGIES. THIS DOCUMENT IS ACCEPTED BY RECIPIENT PURSUANT TO AGREEMENT TO THE FOREGOING, AND MUST BE RETURNED UPON DEMAND.</small> <small>MANUFACTURER AGREES THAT ARTICLES MADE IN ACCORDANCE WITH THIS DOCUMENT SHALL BE CONSIDERED FMC TECHNOLOGIES' DESIGN AND THAT IDENTICAL ARTICLES OR PARTS THEREOF SHALL NOT BE MANUFACTURED FOR THE USE OR SALE BY MANUFACTURER OR ANY OTHER PERSON WITHOUT THE PRIOR EXPRESS WRITTEN AUTHORIZATION BY FMC TECHNOLOGIES</small>	REVISIONS	DESCRIPTION	DATE	BY
	A	05-08-13		
	B	1-22-14		
	C	5-13-14		
		SURFACE WELLHEAD LAYOUT UNIHEAD, UH-1, SOW, DEVON ENERGY, ODESSA		
			05-08-13	K. VU
			05-08-13	Z. MARQUEZ
			05-08-13	K. TAHA
			05-08-13	R. HAMILTON
				<b>FMC Technologies</b>
				DRAWING NUMBER DM100161771-2A

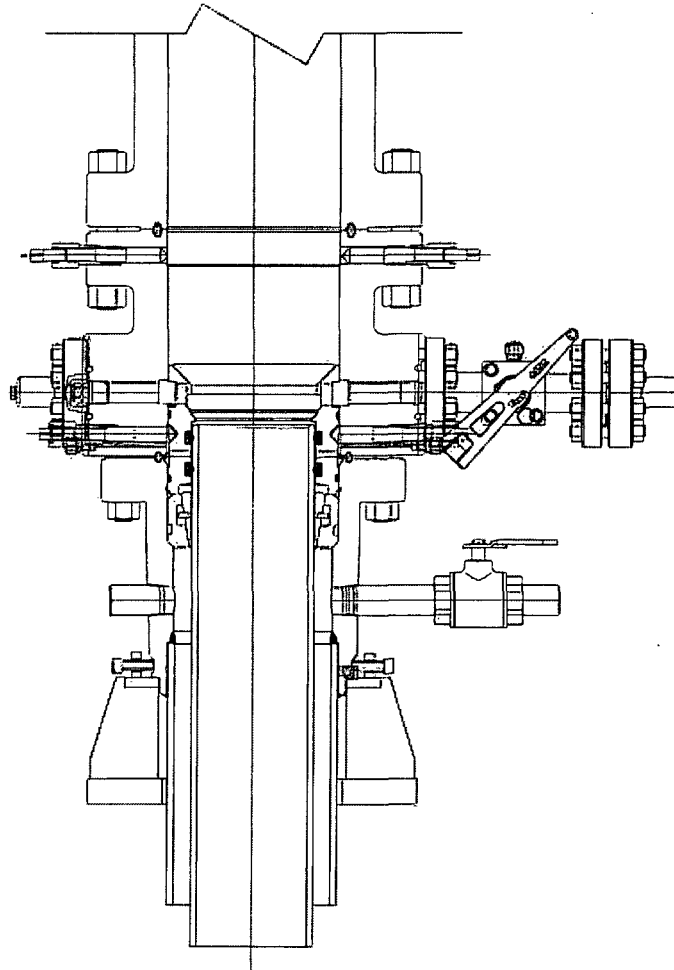

CONTINGENCY MODE


DEVON ENERGY  
ARTESIA  
S.E.N.M  
13 3/8 X 9 5/8

QUOTE LAYOUT  
F18648  
REF: DM100161737  
DM100151315

PRIVATE AND CONFIDENTIAL		REVISIONS	DESCRIPTION			DM100151315
THIS DOCUMENT AND ALL THE INFORMATION CONTAINED HEREIN ARE THE CONFIDENTIAL AND EXCLUSIVE PROPERTY OF FMC TECHNOLOGIES AND MAY NOT BE REPRODUCED, USED, DISCLOSED, OR MADE PUBLIC IN ANY MANNER PRIOR TO EXPRESS WRITTEN AUTHORIZATION BY FMC TECHNOLOGIES. THIS DOCUMENT IS ACCEPTED BY RECIPIENT PURSUANT TO AGREEMENT TO THE FOREGOING AND MUST BE RETURNED UPON DEMAND.		A 05-08-13	SURFACE WELLHEAD LAYOUT UNIHEAD, UH-1, SOW, DEVON ENERGY, ODESSA	DESIGNED BY		
		B 1-22-14		K. VU	05-08-13	
		C 5-13-14		Z. MARQUEZ	05-08-13	
				K. TAHA	05-08-13	
MANUFACTURER AGREES THAT ARTICLES MADE IN ACCORDANCE WITH THIS DOCUMENT SHALL BE CONSIDERED FMC TECHNOLOGIES' DESIGN AND THAT IDENTICAL ARTICLES OR PARTS THEREOF SHALL NOT BE MANUFACTURED FOR THE USE OR SALE BY MANUFACTURER OR ANY OTHER PERSON WITHOUT THE PRIOR EXPRESS WRITTEN AUTHORIZATION BY FMC TECHNOLOGIES				DESIGN REVIEW		
				APPROVED BY	R. HAMILTON	05-08-13


# DEVON ENERGY

Project: Lea County, NM (NAD-83)  
 Site: Big Cat 16-9 State Fed Com  
 Well: 1H  
 Wellbore: OH  
 Design: Plan #1



Azimuths to Grid North  
 True North: -0.35°  
 Magnetic North: 7.02°  
 Magnetic Field  
 Strength: 48230.7 nT  
 Dip Angle: 60.14°  
 Date: 2/23/2015  
 Model: BGGM2014

PROJECT DETAILS: Lea County, NM (NAD-83)  
 Geodetic System: US State Plane 1983  
 Datum: North American Datum 1983  
 Ellipsoid: GRS 1980  
 Zone: New Mexico Eastern Zone

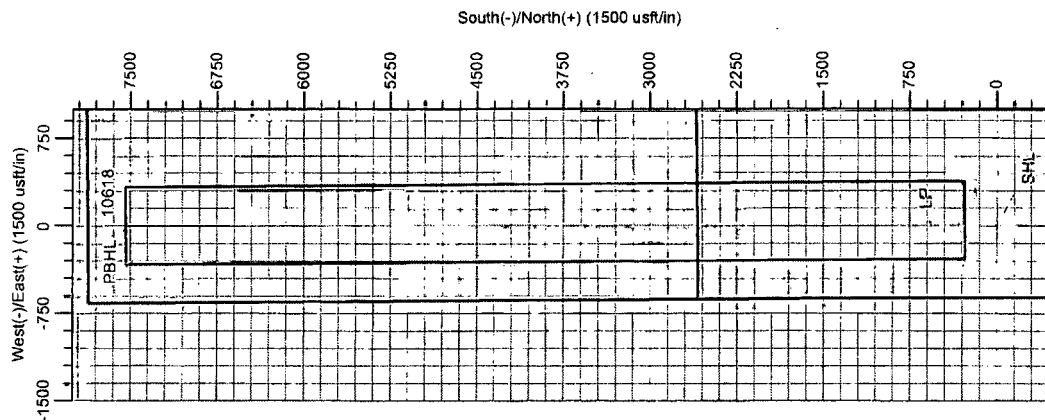

## DESIGN TARGET DETAILS


Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
SHL (BC169SFC 1H)	0.00	0.00	0.00	475196.92	741283.92	32° 18' 17.030 N	103° 41' 10.235 W
PBHL (BC169SFC 1H)	0618.00	7540.24	-2.98	482737.16	741280.94	32° 19' 31.643 N	103° 41' 9.739 W

## SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSeet	Annotation
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	KOP 10° DLS
2	10945.04	0.00	0.00	10045.04	0.00	0.00	0.00	0.00	0.00	LP
3	10945.04	90.00	359.98	10618.00	572.96	10.00	359.98	572.96	572.96	TD
4	17912.32	90.00	359.98	10618.00	7540.24	-2.98	0.00	0.00	7540.24	

## FORMATION TOP DETAILS

Formation	DipAngle	DipDir
Rustler	0.00	
Base Salt	0.00	
Lamar	0.00	
Delaware	0.00	
Bone Spring	0.00	
2nd BS SS	0.00	

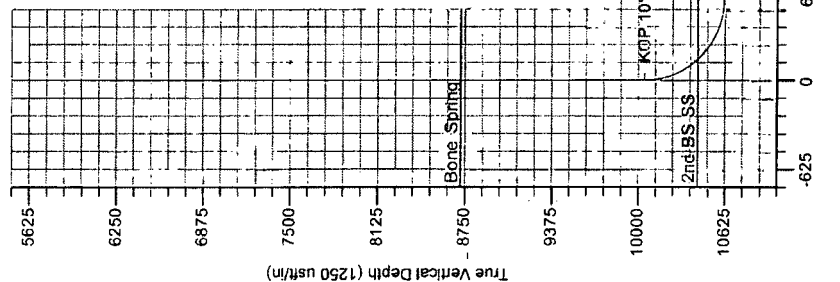

LEAM DRILLING SYSTEMS LLC  
 2010 East Davis, Conroe, Texas 77301  
 Phone: 936/756-7577, Fax 936/756-7595

Plan: Plan #1 (1H/CH)  
 Big Cat 16-9 State Fed Com  
 Created By: Brady Deaver  
 Date: 14.05, February 23 2015  
 Approved: \_\_\_\_\_  
 Date: \_\_\_\_\_
