

15-780

Form 3160-3
(March 2012)

OCD Hobbs
HOBBS OCD

FORM APPROVED
OMB No. 1004-0137
Expires October 31, 2014

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

JUN 28 2016

APPLICATION FOR PERMIT TO DRILL OR REENTER

5a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. NMLC057210	
1b. Type of Well: <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input checked="" type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name N/A	
2. Name of Operator ConocoPhillips Company (217817)		7. If Unit or CA Agreement, Name and No. N/A	
3a. Address 600 N. Dairy Ashford Rd.; P10-3096 Houston, TX 77079-1175		8. Lease Name and Well No. (31422) MCA Unit 548	
3b. Phone No. (include area code) 281-206-5281		9. API Well No. 30-025- 43323	
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface 1040' FNL and 457' FWL; <u>UL D</u> , Sec. 27, T17S, R32E At proposed prod. zone 1352' FNL and 700' FWL; <u>UL E</u> , Sec. 27, T17S, R32E		10. Field and Pool, or Exploratory Maljamar; Grayburg, San Andres (43329)	
11. Sec., T. R. M. or Blk. and Survey or Area Sec. 27, T17S, R32E		12. County or Parish Lea County	
13. State NM		14. Distance in miles and direction from nearest town or post office* Approximately 3.5 miles south east of Maljamar; New Mexico	
15. Distance from proposed* 32' to UL line location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No. of acres in lease 1200.00	17. Spacing Unit dedicated to this well 40	
18. Distance from proposed location* approx. 525' at surface to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth 4574' MD/4539' TVD	20. BLM/BIA Bond No. on file ES0085	
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 4025' GL	22. Approximate date work will start* 01/01/2016	23. Estimated duration 7 days	
24. Attachments			

UNORTHODOX LOCATION

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the BLM.

25. Signature <i>Susan B. Maunder</i>	Name (Printed/Typed) Susan B. Maunder	Date 6/5/15
Title Senior Regulatory Specialist		
Approved by (Signature) James A. Amos	Name (Printed/Typed)	JUN 20 2016
Title FIELD MANAGER	Office CARLSBAD FIELD OFFICE	

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

APPROVAL FOR TWO YEARS

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section States any false, fictitious or fraudulent statements or

See attached NMOCD
Conditions of Approval

make to any department or agency of the United

(Continued on page 2)

*(Instructions on page 2)

Roswell Controlled Water Basin

Kc
06/29/16

**Approval Subject to General Requirements
& Special Stipulations Attached**

**SEE ATTACHED FOR
CONDITIONS OF APPROVAL**

Kc

ConocoPhillips, MCA UNIT 548

1. Geologic Formations

TVD of target	4539'	Pilot hole depth	NA
MD at TD:	4574'	Deepest expected fresh water:	899'

Basin

Formation	TVD (ft)
Rustler	899
Salado	1079
Tansill	2049
Yates	2194
Seven Rivers	2529
Queen	3159
Grayburg	3519
San Andres	3909
TD	4539

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Tension
	From	To							
12.25"	0	934 955	8.625"	24	J55	STC	3.32	7.15	10.9
7.875"	0	4564	5.5"	17	J55	LTC	2.07	2.24	3.18
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

Must have table for contingency casing

ConocoPhillips, MCA UNIT 548

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	YES
Does casing meet API specifications? If no, attach casing specification sheet.	YES
Is premium or uncommon casing planned? If yes attach casing specification sheet.	NO
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	YES
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	N/A
Is well located within Capitan Reef?	NO
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	NO
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	NO
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	NO
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	NO
If yes, are there three strings cemented to surface?	

3. Cementing Program

Casing	# Skis	Wt. lb/ gal	Yld ft3/ sack	H ₂ O gal/sk	500# Comp. Strength (hours)	Slurry Description
Surf.	350	13.5	1.75	9.17	15.75	Lead: Class C + 4% Bentonite + 2% CaCl ₂ + 0.25% Cello Flake (LCM)
	250	14.8	1.34	6.36	8	Tail: Class C + 2% CaCl ₂
DV Tool- Contin gency DV tool @ 3519	450	11.5	3.22	19.06	29	Lead: Class C + 3% MPA-5 (strength enhancement) + 10% extender + .005 lbs/sx Static Free + .005 gps defoamer + .125 lb/sx Cello Flake + 3 lbs/sx LCM + 2% extender + 1% bonding improver + 6% Bentonite
	320	14.0	1.37	6.17	5.5	Tail: (35:65) Poz: Class C + 1% Extender + 1.5% Fluid Loss Add. + .125 lbs/sx Cello Flake + 3 lbs/sx LCM
	250	14.8	1.34	6.36	8	Stage 2: Class C + 2% CaCl ₂

ConocoPhillips, MCA UNIT 548

Prod.	450	11.5	3.21	19.34	29	Lead: Class C +10% Gas Migration Add.+2% Extender+3% MPA-5 (strength enhancement) +1% BA-10A (Bonding improver)+6% Bentonite
	320	14.0	1.37	6.48	5.5	Tail: (35:65) Poz:Class C+1% Extender+1.5% Fluid Loss Add.

Lab reports with recipe and the 500 psi compressive strength time for the cement will be onsite for review.

DV tool to be run and two stage cement job to be performed as contingency in the event of flows or severe losses while drilling and running casing. DV tool depth will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe.

Casing String	TOC	% Excess
Surface	0'	157% lead, 107% tail
Production	0'	262% lead, 81% tail

4. Pressure Control Equipment

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
7-7/8"	11"	3M	Annular	x	70% of working pressure
			Blind Ram		3M
			Pipe Ram		
			Double Ram	x	
			Other*		
			Pipe Ram		
			Double Ram		
			Other *		

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

ConocoPhillips, MCA UNIT 548

X	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
	Y/N Are anchors required by manufacturer?
	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.
	See attached schematic.

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss	PH
From	To					
0	Surf. shoe	FW Gel	8.5-9.0	28-40	N/C	N.C.
Surf. Shoe	TD	Saturated Brine	10.0	29	N/C	10-11

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
NO	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No Logs are planned based on well control or offset log information.
NO	Drill stem test? If yes, explain
NO	Coring? If yes, explain

Additional logs planned	Interval
Resistivity	
Density, GR, BHC	
CBL	
Mud log	
PEX	

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	1860 psi
Abnormal Temperature	No

- Mitigation measure for abnormal conditions - Loss of circulation is a possibility in the horizons below the Top of Grayburg. We expect that normal Loss of Circulation Material will be successful in healing any such loss of circulation events.

Gas detection equipment and pit level flow monitoring equipment will be on location. A flow paddle will be installed in the flow line to monitor relative amount of mud flowing in the non-pressurized return line. Mud probes will be installed in the individual tanks to monitor pit volumes of the drilling fluid with a pit volume totalizer. Gas detecting equipment and H₂S monitor alarm will be installed in the mud return system and will be monitored. A mud gas separator will be installed and operable before drilling out from the Surface Casing. The gases shall be piped into the flare system. Drilling mud containing H₂S shall be degassed in accordance with API RP-49, item 5.14. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

X	H ₂ S is present
X	H ₂ S Plan attached

8. Other facets of operation

Is this a walking operation? If yes, describe.

Will be pre-setting casing? If yes, describe.

A 10' rathole is planned between TD and production casing set depth.

Attachments


 X Directional Plan

 X Other, describe: Two-Stage contingency cementing diagram; "Drill Plan Attachment"

Drill Plan Attachment

Two-Stage Cementing (Alternative for Shallow Gas)

Provide contingency plan for using two-stage cementing for the production casing cement job if gas flow occurs during the drilling operations. See APD Drill Plan Section 3.

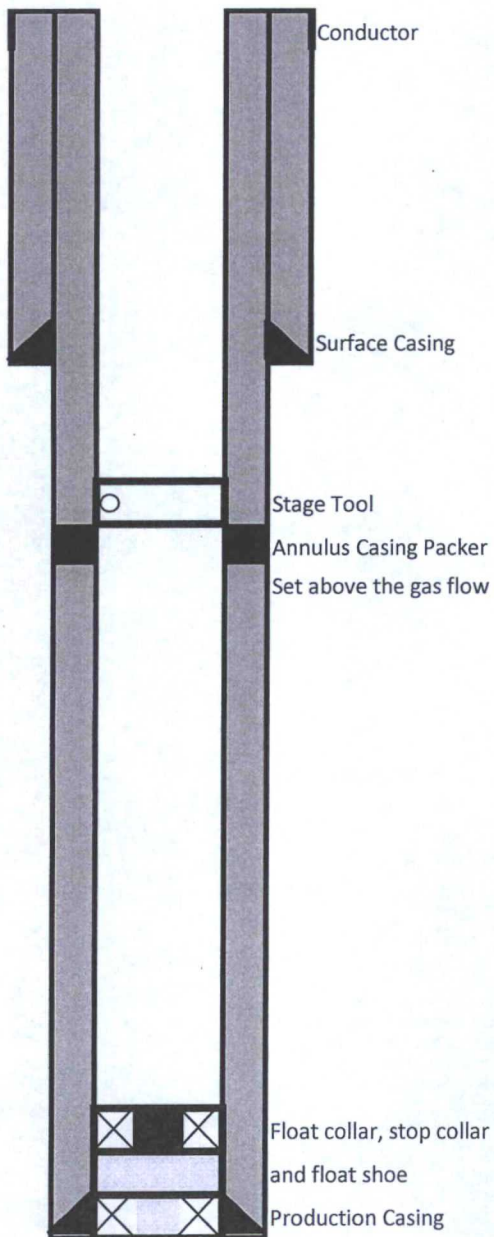

Two-Stage Cementing (Alternative for Oil/Water/Gas & Water Flow)

Provide contingency plan for using two-stage cementing for the production casing cement job if oil or water flow occurs during drilling operations. See APD Drill Plan Section 3.

