

Submit 1 Copy To Appropriate District Office  
District I - (575) 393-6161  
1625 N. French Dr., Hobbs, NM 88240  
District II - (575) 748-1283  
811 S. First St., Artesia, NM 88210  
District III - (505) 334-6178  
1000 Rio Brazos Rd., Aztec, NM 87410  
District IV - (505) 476-3460  
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico  
Energy, Minerals and Natural Resources  
OIL CONSERVATION DIVISION  
1220 South St. Francis Dr.  
Santa Fe, NM 87505

Form C-103  
Revised July 18, 2013

<b>SUNDRY NOTICES AND REPORTS ON WELLS</b> (DO NOT USE THIS FORM FOR PROPOSALS TO DRILL OR TO DEEPEN OR PLUG BACK TO A DIFFERENT RESERVOIR. USE "APPLICATION FOR PERMIT" (FORM C-101) FOR SUCH PROPOSALS.)		WELL API NO. 30-025-40420
1. Type of Well: Oil Well <input type="checkbox"/> Gas Well <input checked="" type="checkbox"/> Other Acid Gas Injection <input checked="" type="checkbox"/>		5. Indicate Type of Lease STATE <input type="checkbox"/> FEE <input type="checkbox"/> BLM <input checked="" type="checkbox"/>
2. Name of Operator Frontier Field Services, LLC		6. State Oil & Gas Lease No. N/A
3. Address of Operator 4200 Skelly DR. ST. 00, TULSA, OK 74135		7. Lease Name or Unit Agreement Name Maljamar AGI
4. Well Location Unit Letter <u>O</u> : <u>130</u> feet from the <u>SOUTH</u> line and <u>1813</u> feet from the <u>EAST</u> line Section <u>21</u> Township <u>17S</u> Range <u>32E</u> NMPM County <u>LEA</u>		8. Well Number 1
11. Elevation (Show whether DR, RKB, RT, GR, etc.) 4016 ft (GI)		9. OGRID Number 221115
		10. Pool name or Wildcat Wildcat (Lower Wolfcamp)

12. Check Appropriate Box to Indicate Nature of Notice, Report or Other Data

NOTICE OF INTENTION TO:	SUBSEQUENT REPORT OF:
PERFORM REMEDIAL WORK <input type="checkbox"/>	REMEDIAL WORK <input type="checkbox"/>
TEMPORARILY ABANDON <input type="checkbox"/>	ALTERING CASING <input type="checkbox"/>
PULL OR ALTER CASING <input type="checkbox"/>	COMMENCE DRILLING OPNS. <input type="checkbox"/>
DOWNHOLE COMMINGLE <input type="checkbox"/>	P AND A <input type="checkbox"/>
CLOSED-LOOP SYSTEM <input type="checkbox"/>	CASING/CEMENT JOB <input type="checkbox"/>
OTHER: <input type="checkbox"/>	OTHER: Subsequent MIT and Bradenhead <input checked="" type="checkbox"/>

13. Describe proposed or completed operations.

The MIT and Braden head test were conducted on Thursday, August 9 at 9:38 am.

- Initially the starting injection pressure and the annular space pressure between casing and tubing was 308 psig.
- Place chart on annular space and began recording annular space pressure.
- Bled off annular fluid (diesel) to bring observed annular space pressure to zero psig.
- Slowly raised annular pressure by introducing diesel to the annulus to bring pressure to 600 psig.
- When annulus pressure reached 600 psig closed valves to pumping truck and recorded annular space pressure for 32 minutes
- The Frontier Maljamar AGI #1 was injecting TAG at 2278 psig and 106.5° F.
- After 32 minutes bled off annular fluid to reduce observed pressure to zero psig.
- Stopped recording TEST COMPLETE.
- Restored annular pressure to normal.

The Braden head test was conducted concurrent with the MIT, which included bleeding off the pressure and monitoring pressure while keeping the valves open during the MIT test.

I hereby certify that the information above is true and complete to the best of my knowledge.

Spud Date:

Rig Release Date:


I hereby certify that the information above is true and complete to the best of my knowledge and belief.

SIGNATURE Rudy Quiroz TITLE Plant Manager DATE 8/9/2018

Type or print name Rudy Quiroz E-mail address: rquiroz@akaenergy.com PHONE: 575-942-4104

For State Use Only

APPROVED BY: [Signature] TITLE Compliance Supervisor DATE 8/9/18  
Conditions of Approval (if any):

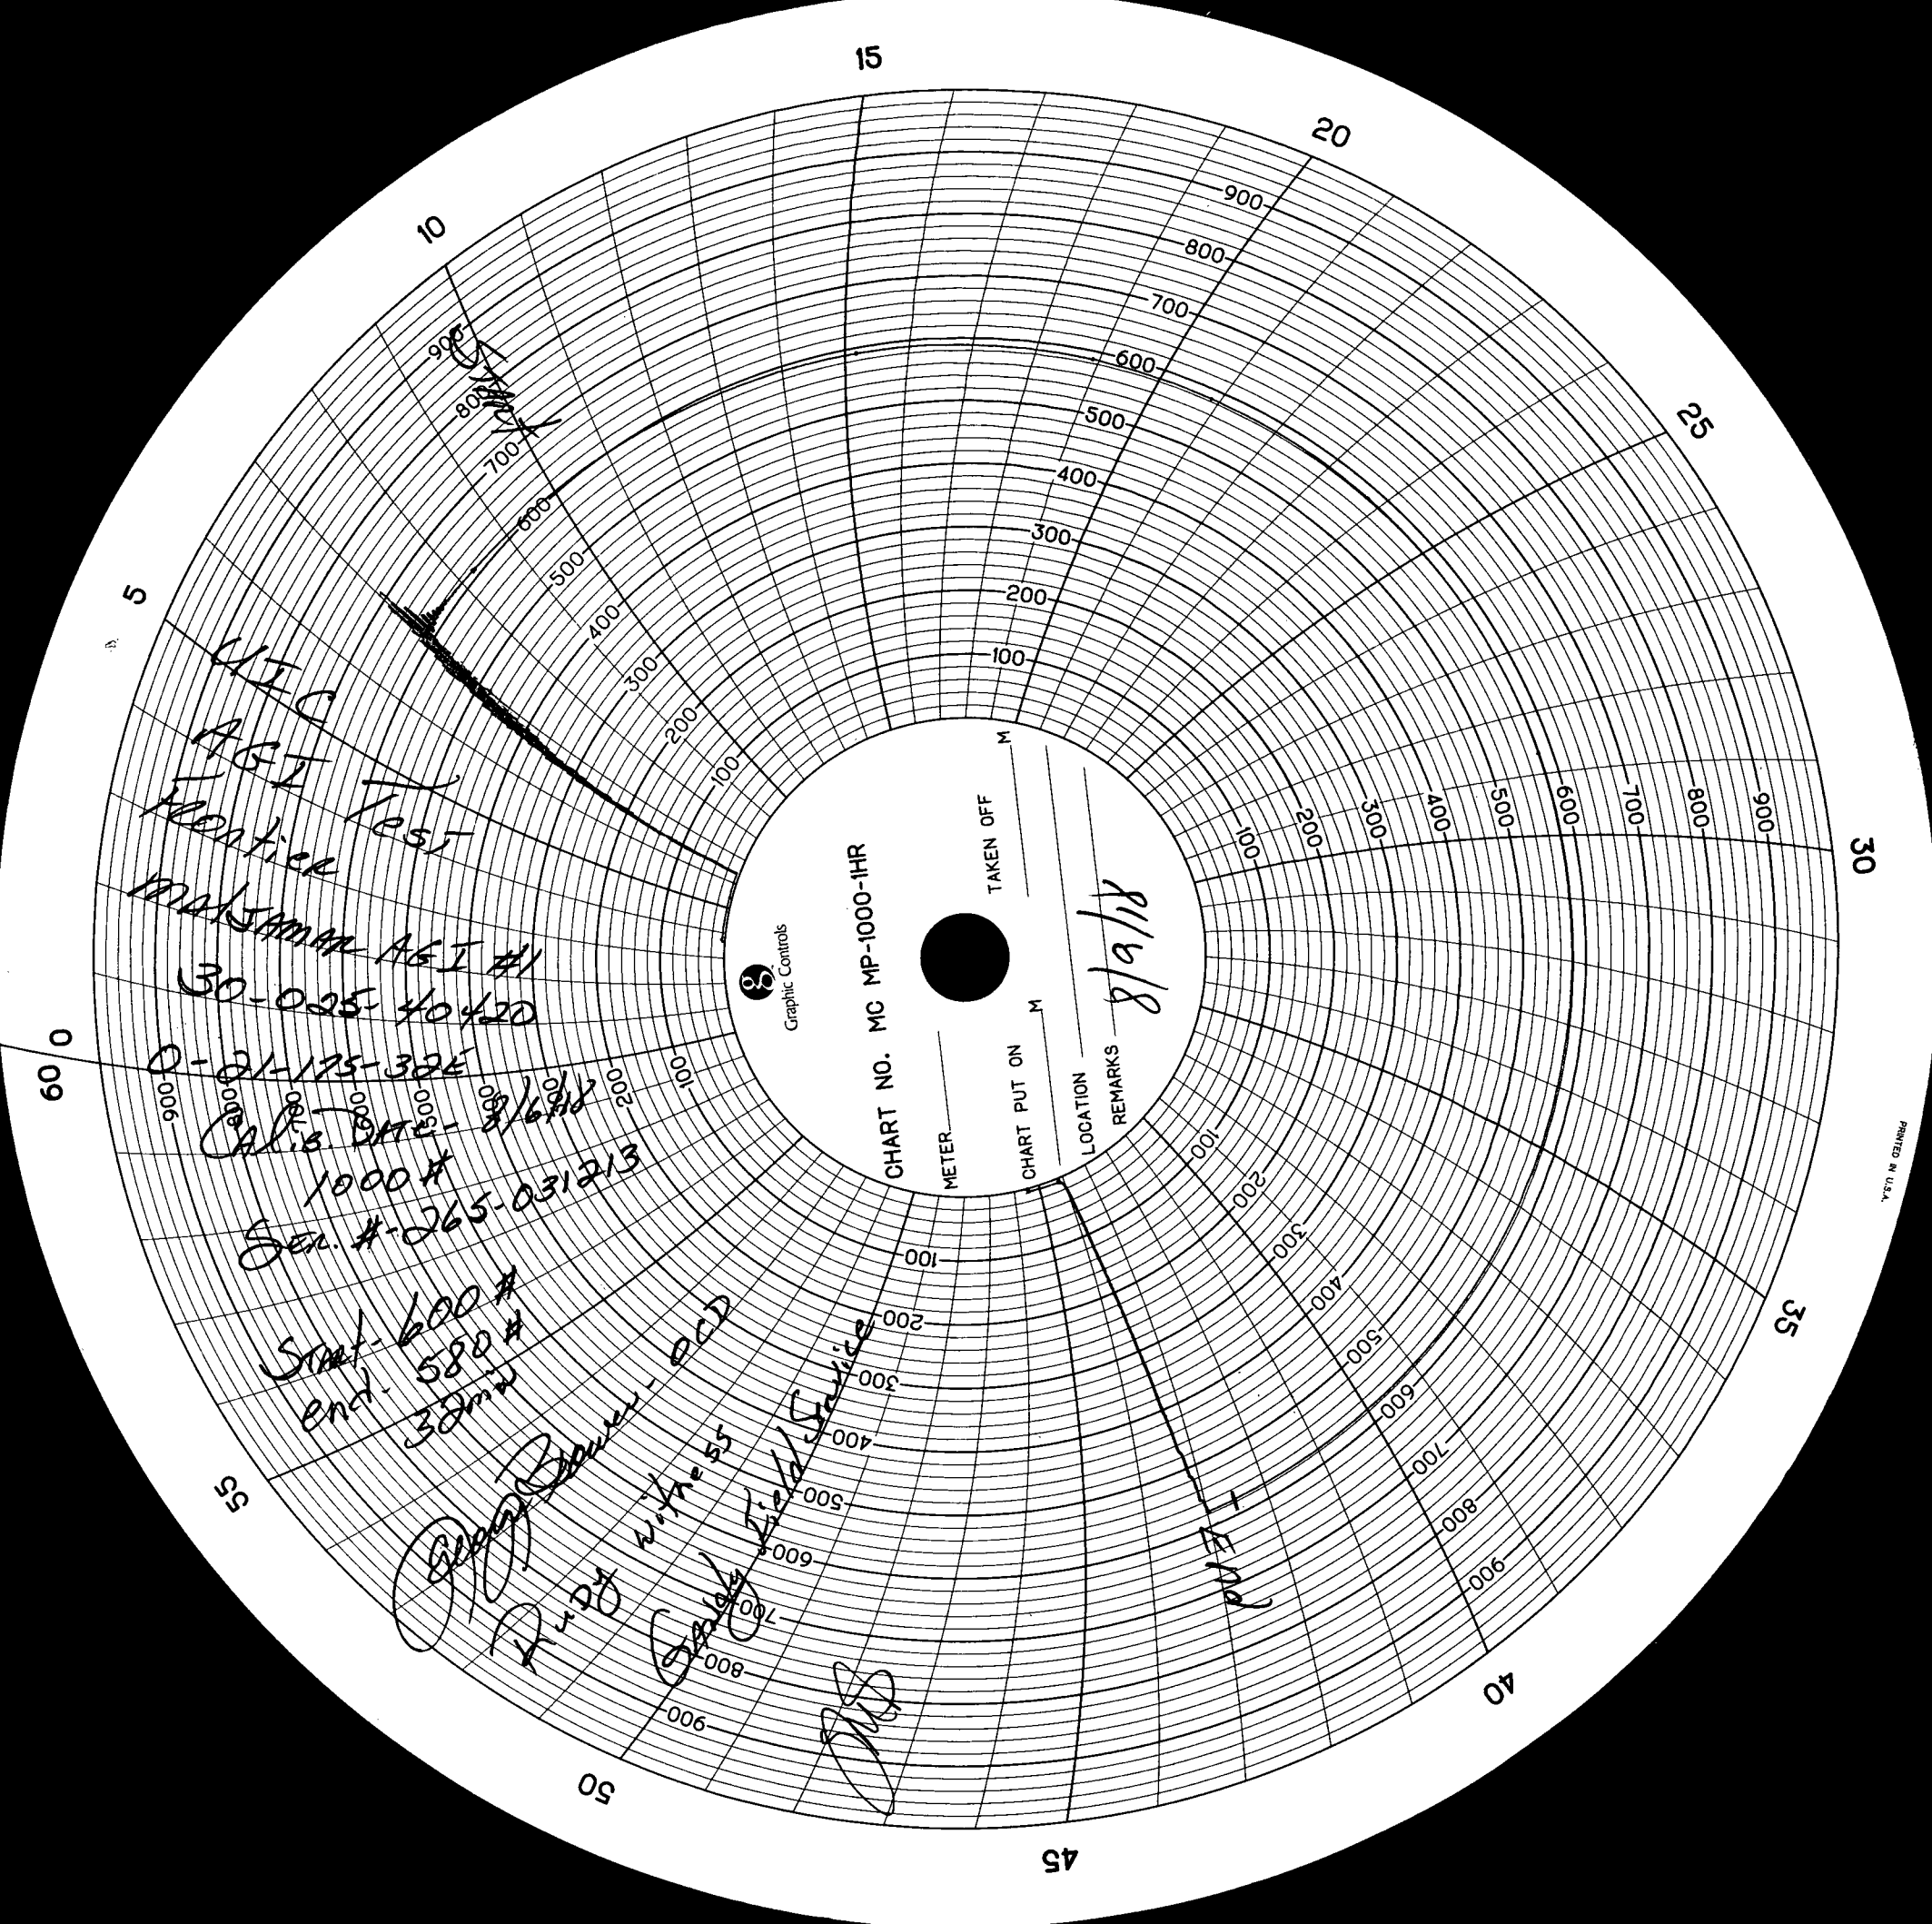

15

20

25

30

35

40

45

50

55

60

5

10

CHART NO. MC MP-1000-IHR

Graphic Controls

TAKEN OFF

METER

CHART PUT ON

LOCATION

REMARKS

8/6/18

END

PRINTED IN U.S.A.
