

OCD Hobbs

FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. NMNM084728
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other		6. If Indian, Allottee or Tribe Name
1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		If Unit or CA Agreement, Name and No.
2. Name of Operator DEVON ENERGY PRODUCTION COMPANY LP (6137)		8. Lease Name and Well No. GRUMPY CAT 15-FED 214H (325132)
3a. Address 333 West Sheridan Avenue Oklahoma City OK 73102		9. API-Well No. 30-025-45732
3b. Phone No. (include area code) (800)583-3866		10. Field and Pool, or Exploratory SAND DUNES SOUTH / BONE SPRING (17644)
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NENE / 175 FNL / 1040 FEL / LAT 32.3114483 / LONG -103.6573333 At proposed prod. zone SESE / 330 FSL / 400 FEL / LAT 32.2983179 / LONG -103.6552588		11. Sec., T, R, M, or Blk. and Survey or Area SEC 15 / T23S / R32E / NMP
14. Distance in miles and direction from nearest town or post office*		12. County or Parish LEA
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 175 feet		13. State NM
16. No of acres in lease 800		17. Spacing Unit dedicated to this well 160
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 414 feet		20. BLM/BIA Bond No. in file FED: CO1104
19. Proposed Depth 10545 feet / 15243 feet		21. Estimated duration 45 days
22. Approximate date work will start* 09/02/2019		23. Estimated duration 45 days
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM. |

25. Signature (Electronic Submission)	Name (Printed/Typed) Jenny Harms / Ph: (405)552-6560	Date 07/24/2018
Title Regulatory Compliance Professional		
Approved by (Signature) (Electronic Submission)	Name (Printed/Typed) Cody Layton / Ph: (575)234-5959	Date 01/30/2019
Title Assistant Field Manager Lands & Minerals		
Office CARLSBAD		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

6CP Rec 03/08/19

KZ 03/12/19

APPROVED WITH CONDITIONS

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM 1: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

1. SHL: NENE / 175 FNL / 1040 FEL / TWSP: 23S / RANGE: 32E / SECTION: 15 / LAT: 32.3114483 / LONG: -103.6573333 (TVD: 0 feet, MD: 0 feet)
PPP: NENE / 330 FNL / 400 FEL / TWSP: 23S / RANGE: 32E / SECTION: 15 / LAT: 32.3290369 / LONG: -103.6539639 (TVD: 10545 feet, MD: 10942 feet)
BHL: SESE / 330 FSL / 400 FEL / TWSP: 23S / RANGE: 32E / SECTION: 15 / LAT: 32.2983179 / LONG: -103.6552588 (TVD: 10545 feet, MD: 15243 feet)

BLM Point of Contact

Name: Katrina Ponder
Title: Geologist
Phone: 5752345969
Email: kponder@blm.gov

CONFIDENTIAL

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	DEVON ENERGY
LEASE NO.:	NMNM 084728
WELL NAME & NO.:	Grumpy Cat 15 FED-214H
SURFACE HOLE FOOTAGE:	175'/N & 1040'/E
BOTTOM HOLE FOOTAGE:	330'/S & 400'/E
LOCATION:	SECTION 15, T23S, R32E, NMP
COUNTY:	LEA

Potash	<input checked="" type="radio"/> None	<input type="radio"/> Secretary	<input type="radio"/> R-111-P
Cave/Karst Potential	<input checked="" type="radio"/> Low	<input type="radio"/> Medium	<input type="radio"/> High
Variance	<input type="radio"/> None	<input checked="" type="radio"/> Flex Hose	<input type="radio"/> Other
Wellhead	<input type="radio"/> Conventional	<input checked="" type="radio"/> Multibowl	
Other	<input type="checkbox"/> 4 String Area	<input type="checkbox"/> Capitan Reef	<input type="checkbox"/> WIPP

A. Hydrogen Sulfide

1. A Hydrogen Sulfide (H₂S) Drilling Plan shall be activated 500 feet prior to drilling into the **Delaware** formation. As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The **13 3/8** inch surface casing shall be set at approximately **1278** feet (a minimum of 25 feet into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater (this is to include the lead cement).
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength,

whichever is greater.

- d. If cement falls back, remedial cementing will be done prior to drilling out that string.

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

2. The minimum required fill of cement behind the 9 5/8 inch first intermediate casing, which shall be set at 4917 feet, is:

Option 1:

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

Option 2:

Operator has proposed DV tool. DV tool shall be set a minimum of 50' below previous shoe and a minimum of 200' above current shoe. Operator shall submit sundry if DV tool depth cannot be set in this range. If operator circulates cement on the first stage, operator is approved to inflate the ACP and run the DV tool cancellation plug and cancel the second stage of the proposed cement plan. If cement does not circulate, operator will inflate ACP and proceed with the second stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
 - b. Second stage above DV tool:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office.
3. The minimum required fill of cement behind the 5 1/2 inch production casing is:
 - Cement should tie-back at least 200 feet into previous casing string. Operator shall provide method of verification. **Excess calculates to 6% - additional cement might be required.**

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).

2.

Option 1:

- i. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi.**

Option 2:

- i. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.

JJP 11262018

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Chaves and Roosevelt Counties
Call the Roswell Field Office, 2909 West Second St., Roswell NM 88201.
During office hours call (575) 627-0272.
After office hours call (575)

☒ Eddy County
Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County
Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the

plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time.
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

PECOS DISTRICT SURFACE USE CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Devon Energy Production Company LP
LEASE NO.:	NMNM084728
WELL NAME & NO.:	Grumpy Cat 15 Fed 214H
SURFACE HOLE FOOTAGE:	175'/N & 1040'/E
BOTTOM HOLE FOOTAGE:	330'/S & 400'/E
LOCATION:	Section 15, T.23 S., R.32 E., NMPM
COUNTY:	Lea County, New Mexico

TABLE OF CONTENTS

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
 - Lesser Prairie-Chicken Timing Stipulations
 - Ground-level Abandoned Well Marker
 - Escape Ramps
 - Power Line Avian Protection
 - Raptor Nest Mitigation
 - Hydrology
 - Range
- ☐ **Construction**
 - Notification
 - Topsoil
 - Closed Loop System
 - Federal Mineral Material Pits
 - Well Pads
 - Roads
- ☐ **Road Section Diagram**
- ☒ **Production (Post Drilling)**
 - Well Structures & Facilities
 - Pipelines
 - Electric Lines
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**

I. GENERAL PROVISIONS

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

II. PERMIT EXPIRATION

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

Any cultural and/or paleontological resource discovered by the operator or by any person working on the operator's behalf shall immediately report such findings to the Authorized Officer. The operator is fully accountable for the actions of their contractors and subcontractors. The operator shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery shall be made by the Authorized Officer to determine the appropriate actions that shall be required to prevent the loss of significant cultural or scientific values of the discovery. The operator shall be held responsible for the cost of the proper mitigation measures that the Authorized Officer assesses after consultation with the operator on the evaluation and decisions of the discovery. Any unauthorized collection or disturbance of cultural or paleontological resources may result in a shutdown order by the Authorized Officer.

IV. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

V. SPECIAL REQUIREMENT(S)

**The Pads are build as you go. No grading the 600*600
Just the sub pad.**

Lesser Prairie-Chicken

Oil and gas activities will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well. For more installation details, contact the Carlsbad Field Office at 575-234-5972.

Power line Avian Protection

Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006. The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all power line structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. The holder without liability or expense shall make such modifications and/or additions to the United States.

Escape Ramps

The operator will construct and maintain pipeline/utility trenches that are not otherwise fenced, screened, or netted to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.

- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

Raptor Nest Mitigation

- A BLM Wildlife Biologist must be contacted by the operator prior to construction activities to determine if the raptor nest is active.
- Raptor nests on special, natural habitat features, such as trees, large brush, cliff faces and escarpments, will be protected by not allowing surface disturbance within up to 200 meters of nests or by delaying activity for up to 90 days, or a combination of both. Exceptions to this requirement for raptor nests will be considered if the nests expected to be disturbed are inactive, the proposed activity is of short duration (e.g. habitat enhancement projects, fences, pipelines), and will not result in continuing activity in proximity to the nest.

Hydrology:

Tank battery locations will be lined and bermed. A 20 mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Tank battery berms must be large enough to contain 1 ½ times the content of the largest tank or 24 hour production, whichever is greater. Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

Electric Lines: Any water erosion that may occur due to the construction of overhead electric line and during the life of the power line will be quickly corrected and proper measures will be taken to prevent future erosion.

Temporary Fence Crossing Requirement

Where entry is granted across a fence line, the fence must be braced and tied off on both sides of the passageway with H-braces prior to cutting. Once the work is completed, the fence will be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

Cattle Guard Requirement

Where entry is granted across a fence line for an access road, the fence must be braced and tied off on both sides of the passageway with H-braces prior to cutting. Once the work is completed, the fence will be restored to its prior condition with an appropriately sized cattle guard sufficient to carry out the project. Any new or existing cattle guards on the access route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations. Once the road is abandoned, the fence would be restored to its prior condition, or better. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

Livestock Watering Requirement

The operator must contact the allotment holder prior to construction to identify the location of the pipeline. The operator must take measures to protect the pipeline from compression or other damages. If the pipeline is damaged or compromised in any way near the proposed project as a result of oil and gas activity, the operator is responsible for repairing the pipeline immediately. The operator must notify the BLM office (575-234-5972) and the private surface landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

During construction, the proponent shall minimize disturbance to existing fences, water lines, troughs, windmills, and other improvements on public lands. The proponent is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the grazing permittee/allottee prior to disturbing any range improvement projects. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

VI. CONSTRUCTION

A. NOTIFICATION

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

B. TOPSOIL

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

C. CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

D. FEDERAL MINERAL MATERIALS PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

E. WELL PAD SURFACING

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

F. EXCLOSURE FENCING (CELLARS & PITS)

Exclosure Fencing

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

G. ON LEASE ACCESS ROADS**Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

Surfacing

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

Crowning

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

Ditching

Ditching shall be required on both sides of the road.

Turnouts


Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

Drainage

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill out sloping and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

Cross Section of a Typical Lead-off Ditch



All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

Formula for Spacing Interval of Lead-off Ditches

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

Cattle guards

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

Fence Requirement

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

Livestock Watering Requirement

Any damage to structures that provide water to livestock throughout the life of the well, caused by operations from the well site, must be immediately corrected by the operator. The operator must notify the BLM office (575-234-5972) and the private surface

landowner or the grazing allotment holder if any damage occurs to structures that provide water to livestock.

Public Access

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes

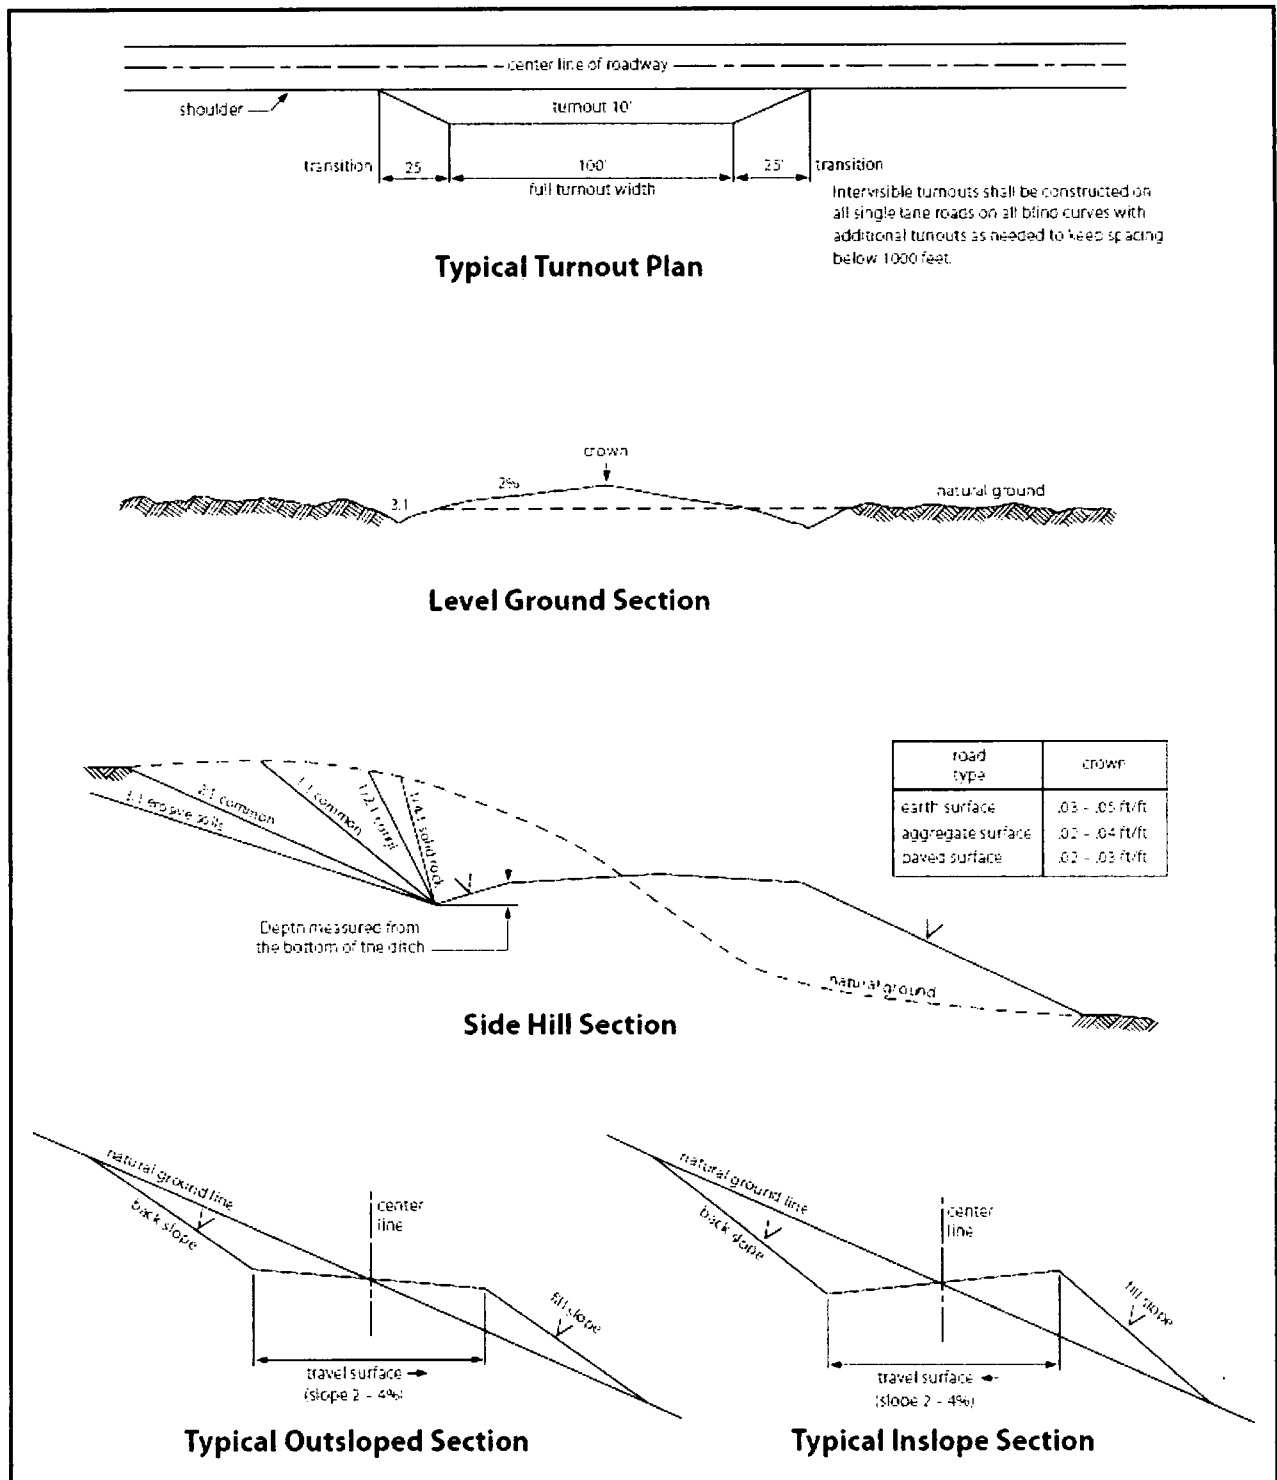


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

VII. PRODUCTION (POST DRILLING)

A. WELL STRUCTURES & FACILITIES

Placement of Production Facilities

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

Exclosure Netting (Open-top Tanks)

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

Chemical and Fuel Secondary Containment and Exclosure Screening

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

Open-Vent Exhaust Stack Exclosures

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

Containment Structures

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

Painting Requirement

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

B. PIPELINES

BURIED PIPELINE STIPULATIONS

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.

5. All construction and maintenance activity will be confined to the authorized right-of-way.
6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.
7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:
- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 20 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
 - Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
 - The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)
8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.
9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.
10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.
11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.

12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- | | |
|--|--|
| <input type="checkbox"/> seed mixture 1 | <input type="checkbox"/> seed mixture 3 |
| <input type="checkbox"/> seed mixture 2 | <input type="checkbox"/> seed mixture 4 |
| <input checked="" type="checkbox"/> seed mixture 2/LPC | <input type="checkbox"/> Aplomado Falcon Mixture |

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural and/or paleontological resources (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

17. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

18. Escape Ramps - The operator will construct and maintain pipeline/utility trenches that are not otherwise fenced, screened, or netted to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or

other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- c. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.
- d. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

19. Special Stipulations:

Lesser Prairie-Chicken

Oil and gas activities will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

C. ELECTRIC LINES

STANDARD STIPULATIONS FOR OVERHEAD ELECTRIC DISTRIBUTION LINES

A copy of the grant and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the

Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.

3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. There will be no clearing or blading of the right-of-way unless otherwise agreed to in writing by the Authorized Officer.

5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The holder shall assume the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the holder without liability or expense to the United States.

Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.

6. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

7. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.

8. Upon cancellation, relinquishment, or expiration of this grant, the holder shall comply with those abandonment procedures as prescribed by the Authorized Officer.

9. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this grant, whichever comes first. This will not apply where the power line extends service to an active, adjoining facility or facilities.

10. Any cultural and/or paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the Authorized Officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

11. Special Stipulations:

- For reclamation remove poles, lines, transformer, etc. and dispose of properly.
- Fill in any holes from the poles removed.

Timing Limitation Stipulation/Condition of Approval for Lesser Prairie-Chicken:

Oil and gas activities including 3-D geophysical exploration, and drilling will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Additionally, no new drilling will be allowed within up to 200 meters of leks known at the time of permitting. Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

VIII. INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce

the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

IX. FINAL ABANDONMENT & RECLAMATION

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Below Ground-level Abandoned Well Marker to avoid raptor perching: Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well.

(Insert Seed Mixture Here)

Seed Mixture for LPC Sand/Shinnery Sites

Holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed shall be done in accordance with State law(s) and within nine (9) months prior to purchase. Commercial seed shall be either certified or registered seed. The seed container shall be tagged in accordance with State law(s) and available for inspection by the Authorized Officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). Holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. Seeding shall be repeated until a satisfactory stand is established as determined by the Authorized Officer. Evaluation of growth may not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed* per acre:

<u>Species</u>	<u>lb/acre</u>
Plains Bristlegrass	5lbs/A
Sand Bluestem	5lbs/A
Little Bluestem	3lbs/A
Big Bluestem	6lbs/A
Plains Coreopsis	2lbs/A
Sand Dropseed	1lbs/A

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Operator Certification Data Report

02/13/2019

I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.

NAME: Jenny Harms

Signed on: 07/18/2018

Title: Regulatory Compliance Professional

Street Address: 333 W Sheridan Ave

City: Oklahoma City

State: OK

Zip: 73102

Phone: (405)552-6560

Email address: jenny.harms@dvni.com

Representative Name: Ray Vaz

Street Address: 6488 Seven Rivers Hwy

City: Artesia

State: NM

Zip: 88210

Phone: (575)748-1871

Email address: ray.vaz@dvni.com



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Application Data Report

02/13/2019

APD ID: 10400032225

Submission Date: 07/24/2018

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Well Type: OIL WELL

Well Work Type: Drill

Highlighted data
reflects the most
recent changes

[Show Final Text](#)

APD ID: 10400032225

Tie to previous NOS?

Submission Date: 07/24/2018

BLM Office: CARLSBAD

User: Jenny Harms

Title: Regulatory Compliance
Professional

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMNM084728

Lease Acres: 800

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? NO

Federal or Indian agreement:

Agreement number:

Agreement name:

Keep application confidential? YES

Permitting Agent? NO

APD Operator: DEVON ENERGY PRODUCTION COMPANY LP

Operator letter of designation:

Operator Organization Name: DEVON ENERGY PRODUCTION COMPANY LP

Operator Address: 333 West Sheridan Avenue

Zip: 73102

Operator PO Box:

Operator City: Oklahoma City

State: OK

Operator Phone: (800)583-3866

Operator Internet Address:

Well in Master Development Plan? NEW

Master Development Plan name: Todd-Apache MDP 3

Well in Master SUPO? NO

Master SUPO name:

Well in Master Drilling Plan? NO

Master Drilling Plan name:

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Well API Number:

Field/Pool or Exploratory? Field and Pool

Field Name: SAND DUNES,
SOUTH

Pool Name: BONE SPRING

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Is the proposed well in an area containing other mineral resources? NATURAL GAS,OIL

Describe other minerals:

Is the proposed well in a Helium production area? N **Use Existing Well Pad?** NO **New surface disturbance?**

Type of Well Pad: MULTIPLE WELL

Multiple Well Pad Name: TODD **Number:** 4

Well Class: HORIZONTAL

MDP3 15 WELL PAD

Number of Legs: 1

Well Work Type: Drill

Well Type: OIL WELL

Describe Well Type:

Well sub-Type: DELINEATION

Describe sub-type:

Distance to town:

Distance to nearest well: 414 FT

Distance to lease line: 175 FT

Reservoir well spacing assigned acres Measurement: 160 Acres

Well plat: Grumpy_Cat_15_Fed_214H_C_102__signed_20180718144237.pdf

Well work start Date: 09/02/2019

Duration: 45 DAYS

Survey Type: RECTANGULAR

Describe Survey Type:

Datum: NAD83

Vertical Datum: NAVD88

Survey number: 5805A

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
SHL Leg #1	175	FNL	104 0	FEL	23S	32E	15	Aliquot NENE	32.31144 83	- 103.6573 333	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	370 3	0	0
KOP Leg #1	175	FNL	400	FEL	23S	32E	15	Aliquot NENE	32.31193 55	- 103.6539 639	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	- 626 9	100 13	997 2
PPP Leg #1	330	FNL	400	FEL	23S	32E	15	Aliquot NENE	32.32903 69	- 103.6539 639	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	- 684 2	109 42	105 45


Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

	NS-Foot	NS Indicator	EW-Foot	EW Indicator	Twsp	Range	Section	Aliquot/Lot/Tract	Latitude	Longitude	County	State	Meridian	Lease Type	Lease Number	Elevation	MD	TVD
EXIT Leg #1	330	FSL	400	FEL	23S	32E	22	Aliquot SESE	32.29831 79	- 103.6552 588	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	- 684 2	152 43	105 45
BHL Leg #1	330	FSL	400	FEL	23S	32E	15	Aliquot SESE	32.29831 79	- 103.6552 588	LEA	NEW MEXI CO	NEW MEXI CO	F	NMNM 084728	- 684 2	152 43	105 45

SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
INTERIM SITE BUILD PLAN

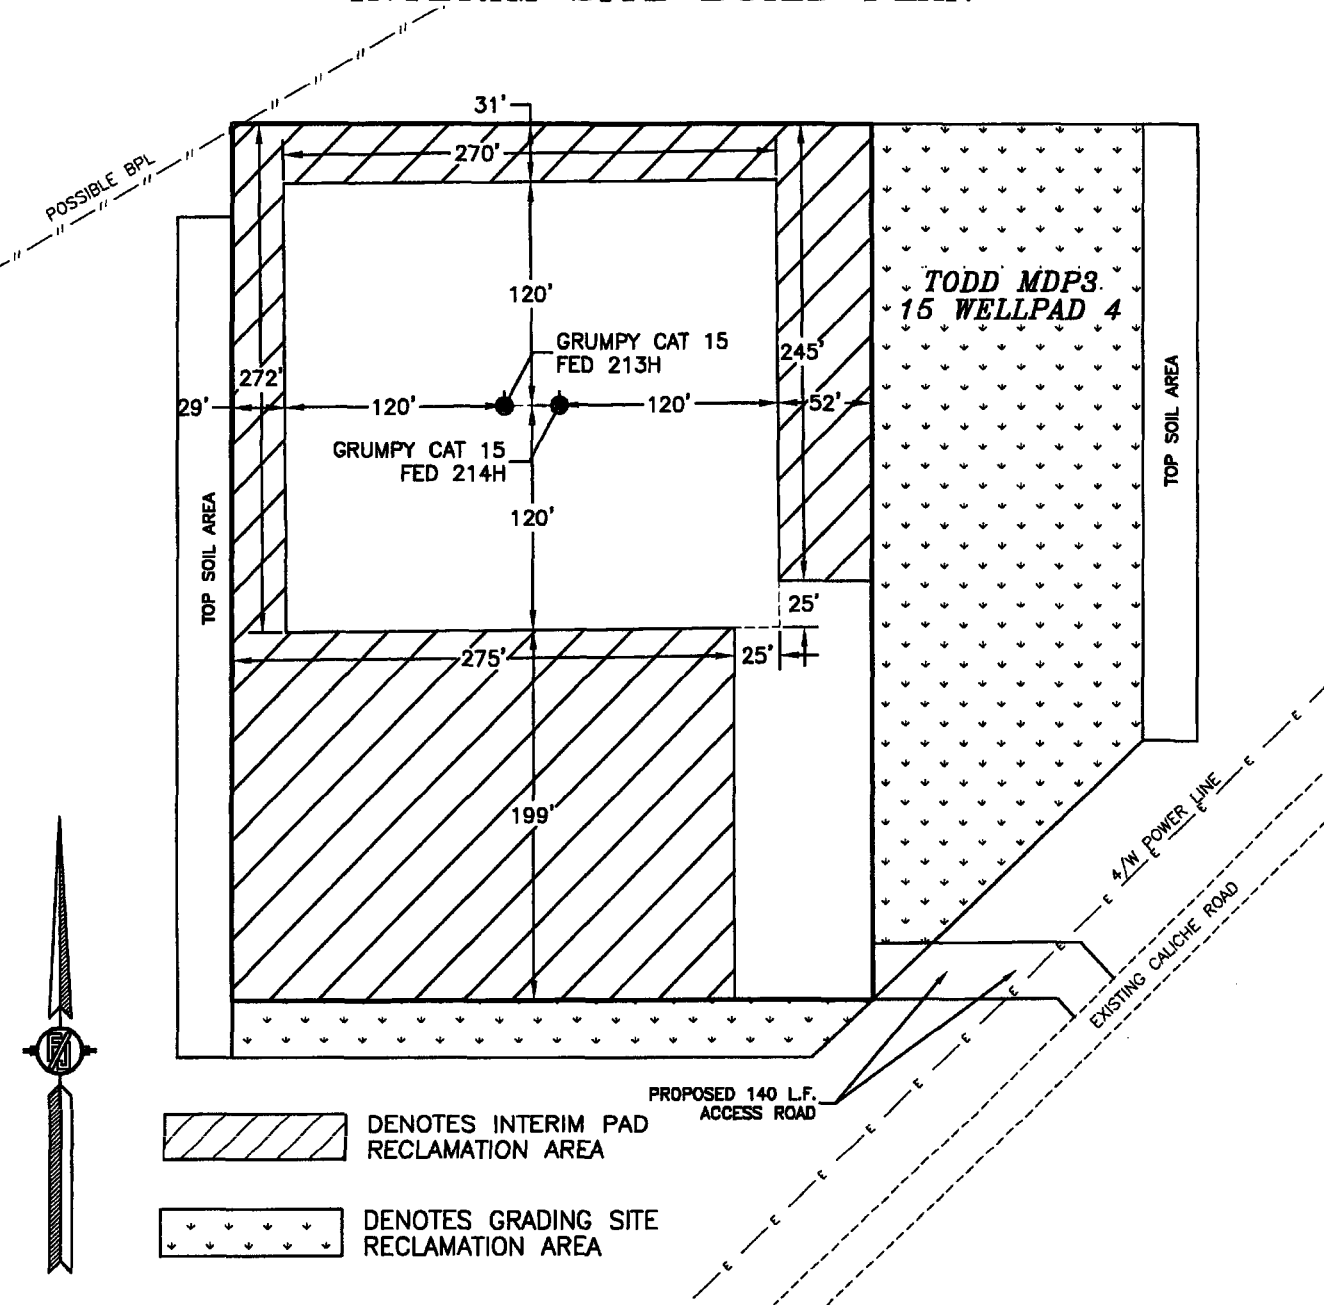

DENOTES INTERIM PAD RECLAMATION AREA

DENOTES GRADING SITE RECLAMATION AREA

0 10 50 100 200
SCALE 1" = 100'

1.915± ACRES INTERIM PAD RECLAMATION AREA
1.597± ACRES GRADING SITE RECLAMATION AREA
1.876± ACRES NON-RECLAIMED AREA
5.388± ACRES TODD MDP3 15 WELLPAD 4


DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H
LOCATED 175 FT. FROM THE NORTH LINE
AND 1040 FT. FROM THE EAST LINE OF
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

APRIL 30, 2018

SURVEY NO. 6805A

MADRON SURVEYING, INC. 301 SOUTH CANAL (575) 234-3341 CARLSBAD, NEW MEXICO

SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
LOCATION VERIFICATION MAP

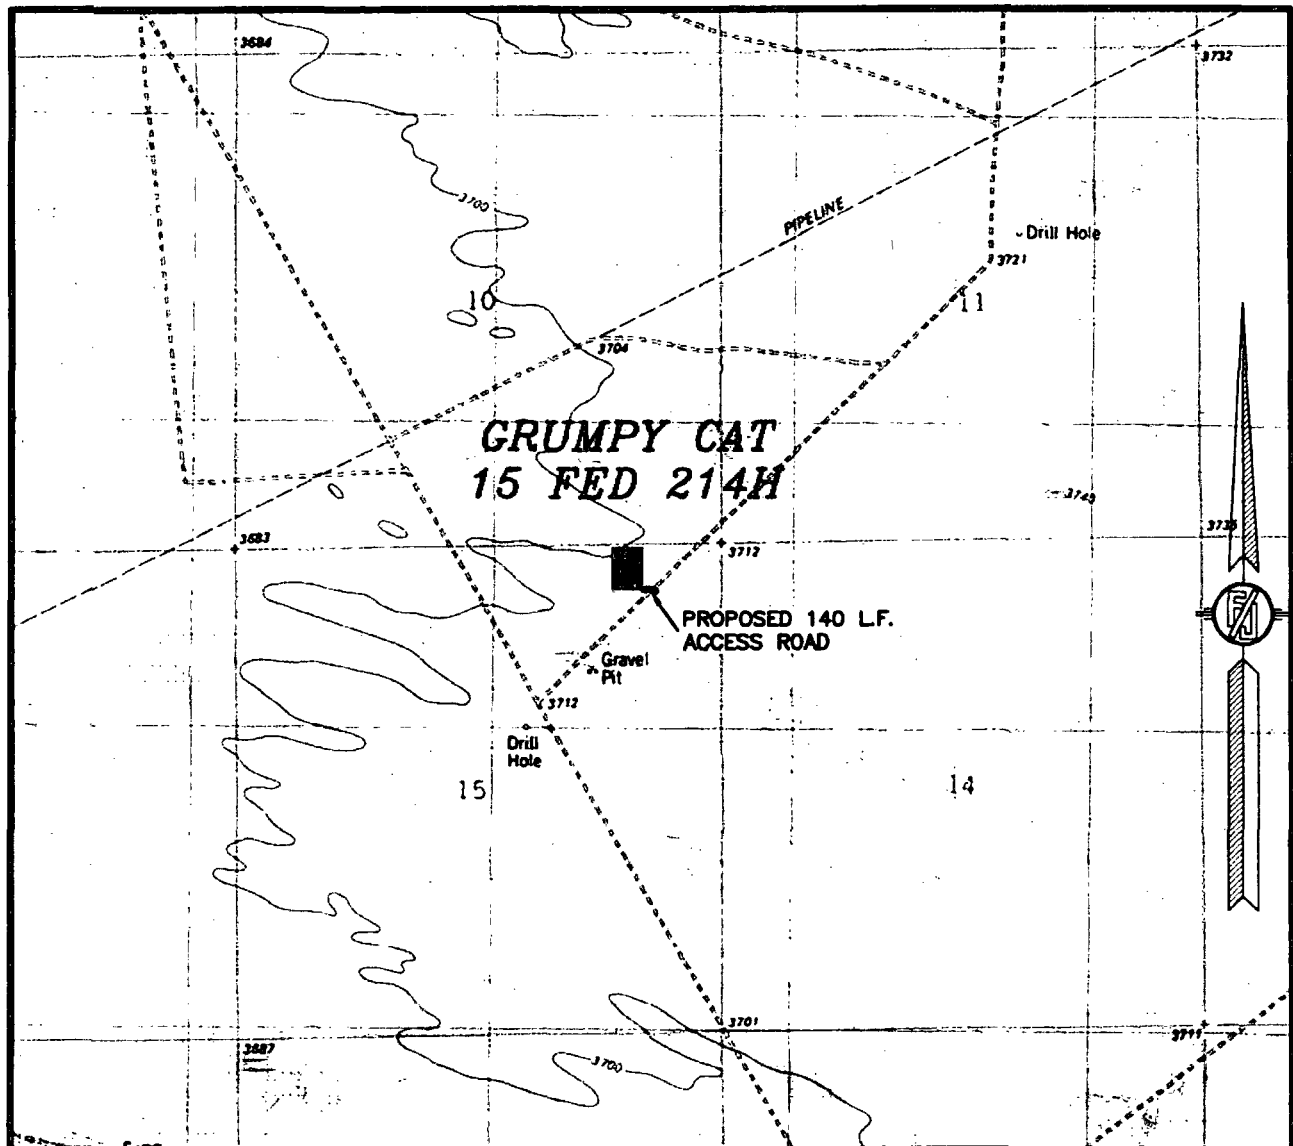

USGS QUAD MAP:
BOOTLEG RIDGE

NOT TO SCALE

DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H


LOCATED 175 FT. FROM THE NORTH LINE
AND 1040 FT. FROM THE EAST LINE OF
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

APRIL 30, 2018

MADRON SURVEYING, INC. 301 SOUTH CANAL
(575) 234-3341

SURVEY NO. 5805A
CARLSBAD, NEW MEXICO

SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
VICINITY MAP

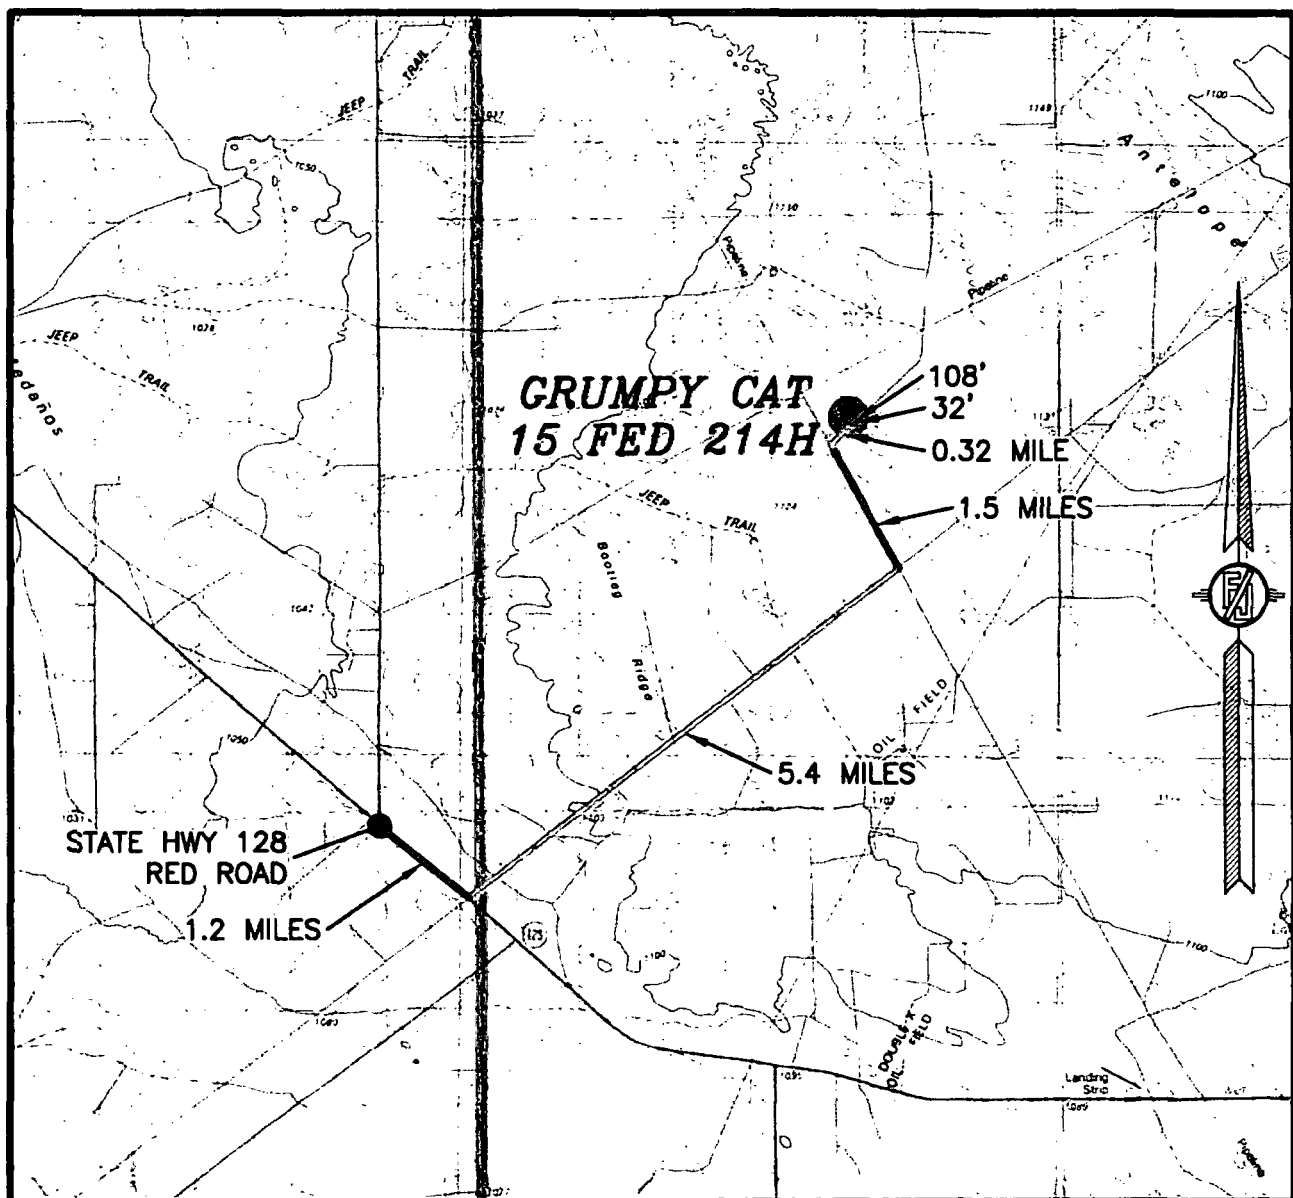

DISTANCES IN MILES

NOT TO SCALE

DIRECTIONS TO LOCATION

FROM THE INTERSECTION OF RED ROAD & STATE HWY 128, GO EAST ON HWY 128 APPROX. 1.2 MILES TO A PIPELINE ROAD ON LEFT (NORTH), TURN AT PIPELINE ROAD GO NORTHEAST APPROX. 5.4 MILES TO A LEASE ROAD ON LEFT (NORTH), TURN NORTH AT LEASE ROAD GO APPROX. 1.5 MILES TO A LEASE ROAD GOING NORTHEAST, TURN NORTHEAST GO APPROX. 0.32 MILE TO ROAD LATH ON LEFT (NORTH), GO NORTHWEST 32' FEET, THEN WEST 108' TO LOCATION.

DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H
LOCATED 175 FT. FROM THE NORTH LINE
AND 1040 FT. FROM THE EAST LINE OF
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO


APRIL 30, 2018

SURVEY NO. 5805A

MADRON SURVEYING, INC. 301 SOUTH CANAL (575) 234-3341

CARLSBAD, NEW MEXICO

SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
AERIAL PHOTO

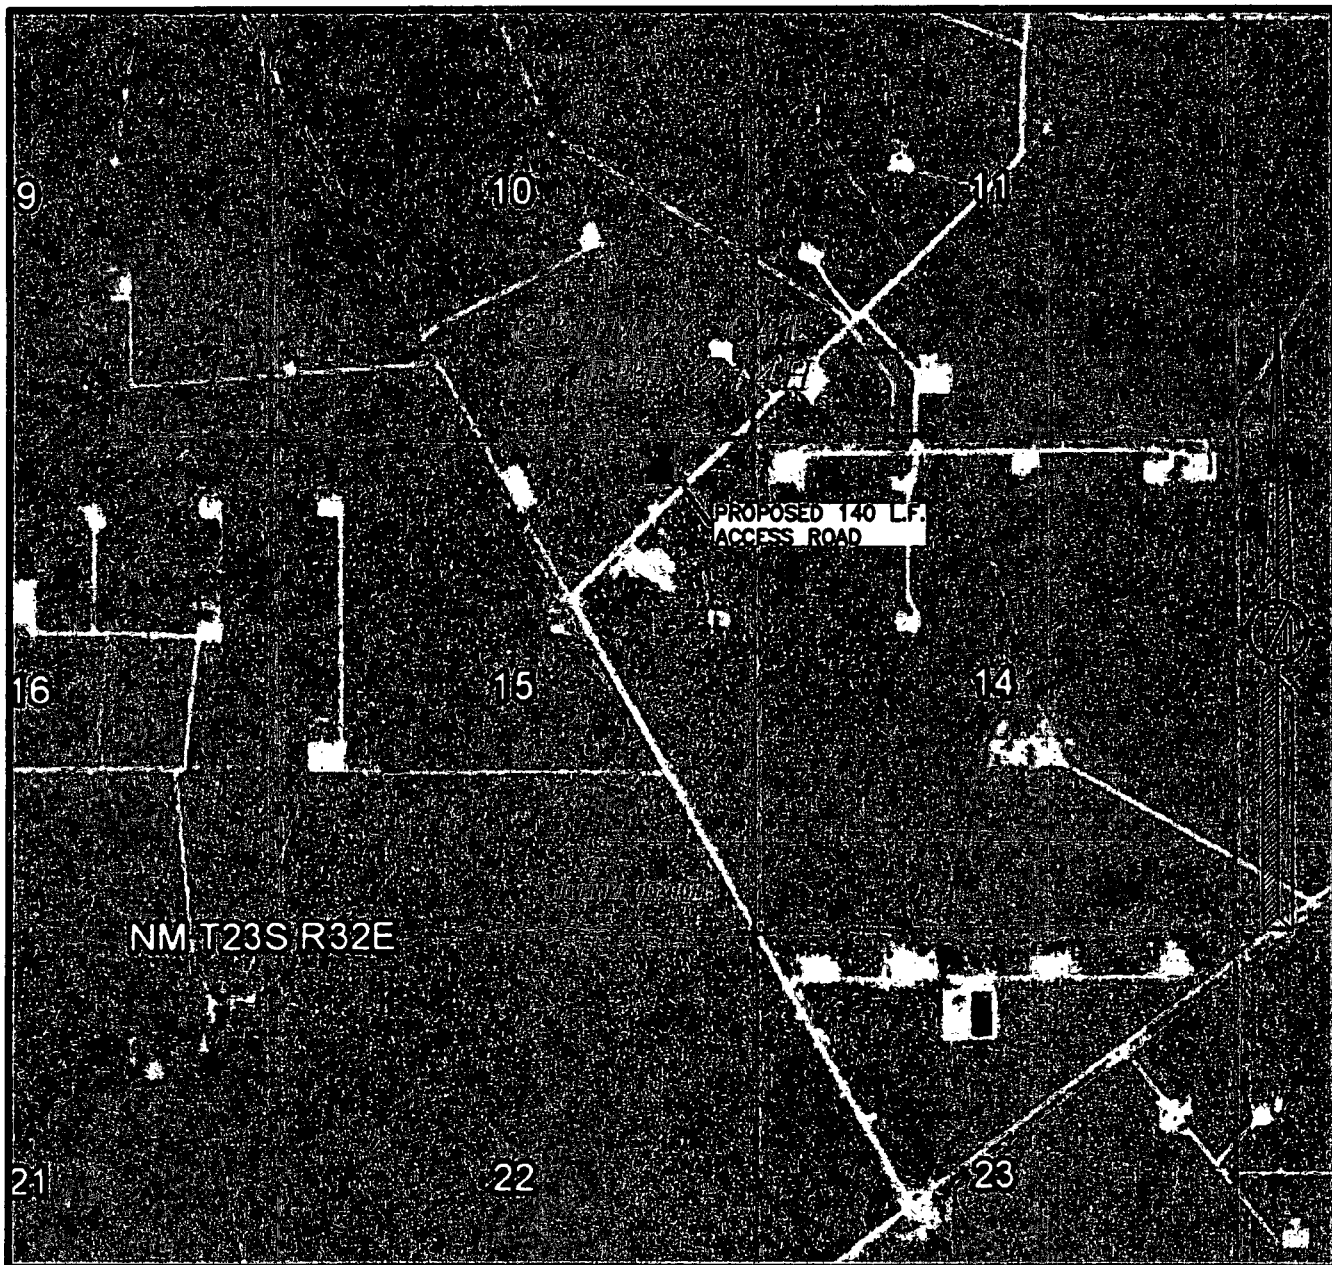

NOT TO SCALE
AERIAL PHOTO:
GOOGLE EARTH
NOV. 2017


DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H
LOCATED 175 FT. FROM THE NORTH LINE
AND 1040 FT. FROM THE EAST LINE OF
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

APRIL 30, 2018

MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO
(575) 234-3341

SURVEY NO. 5805A

SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
AERIAL ACCESS ROUTE MAP

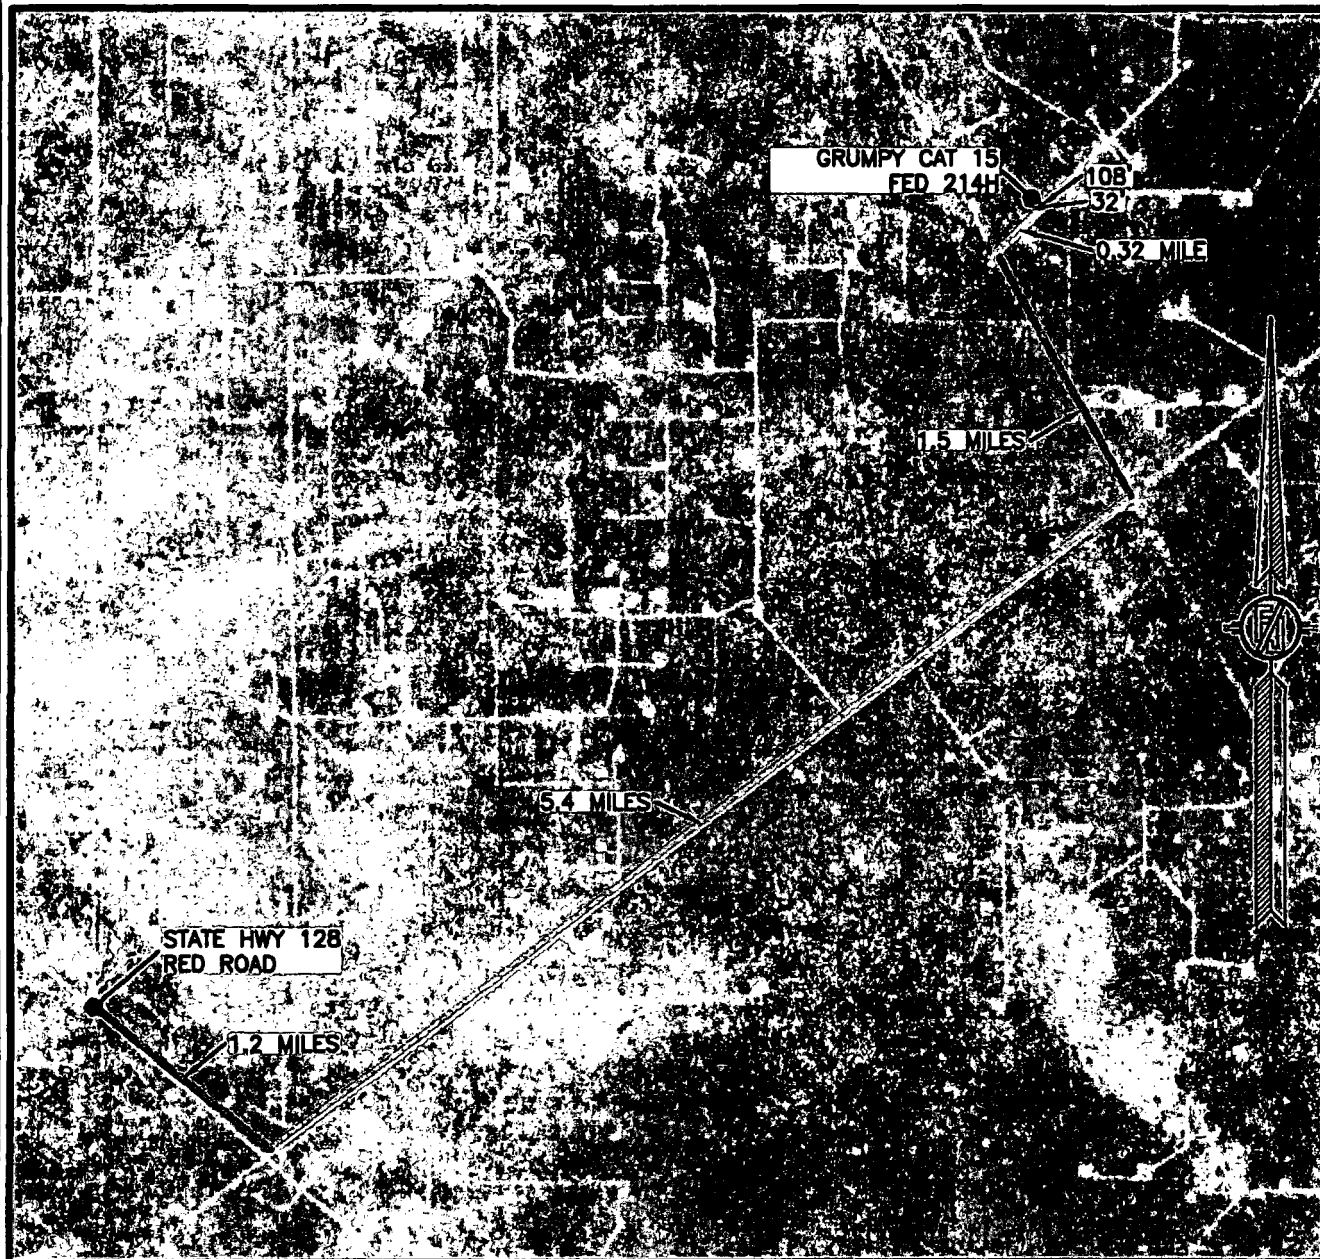

NOT TO SCALE
AERIAL PHOTO:
GOOGLE EARTH
NOV. 2017

DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H


LOCATED 175 FT. FROM THE NORTH LINE
AND 1040 FT. FROM THE EAST LINE OF
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

APRIL 30, 2018

SURVEY NO. 5805A

MADRON SURVEYING, INC. 531 SOUTH CANA: CARLSBAD, NEW MEXICO
(575) 234-3341

1-MILE WELL MAP

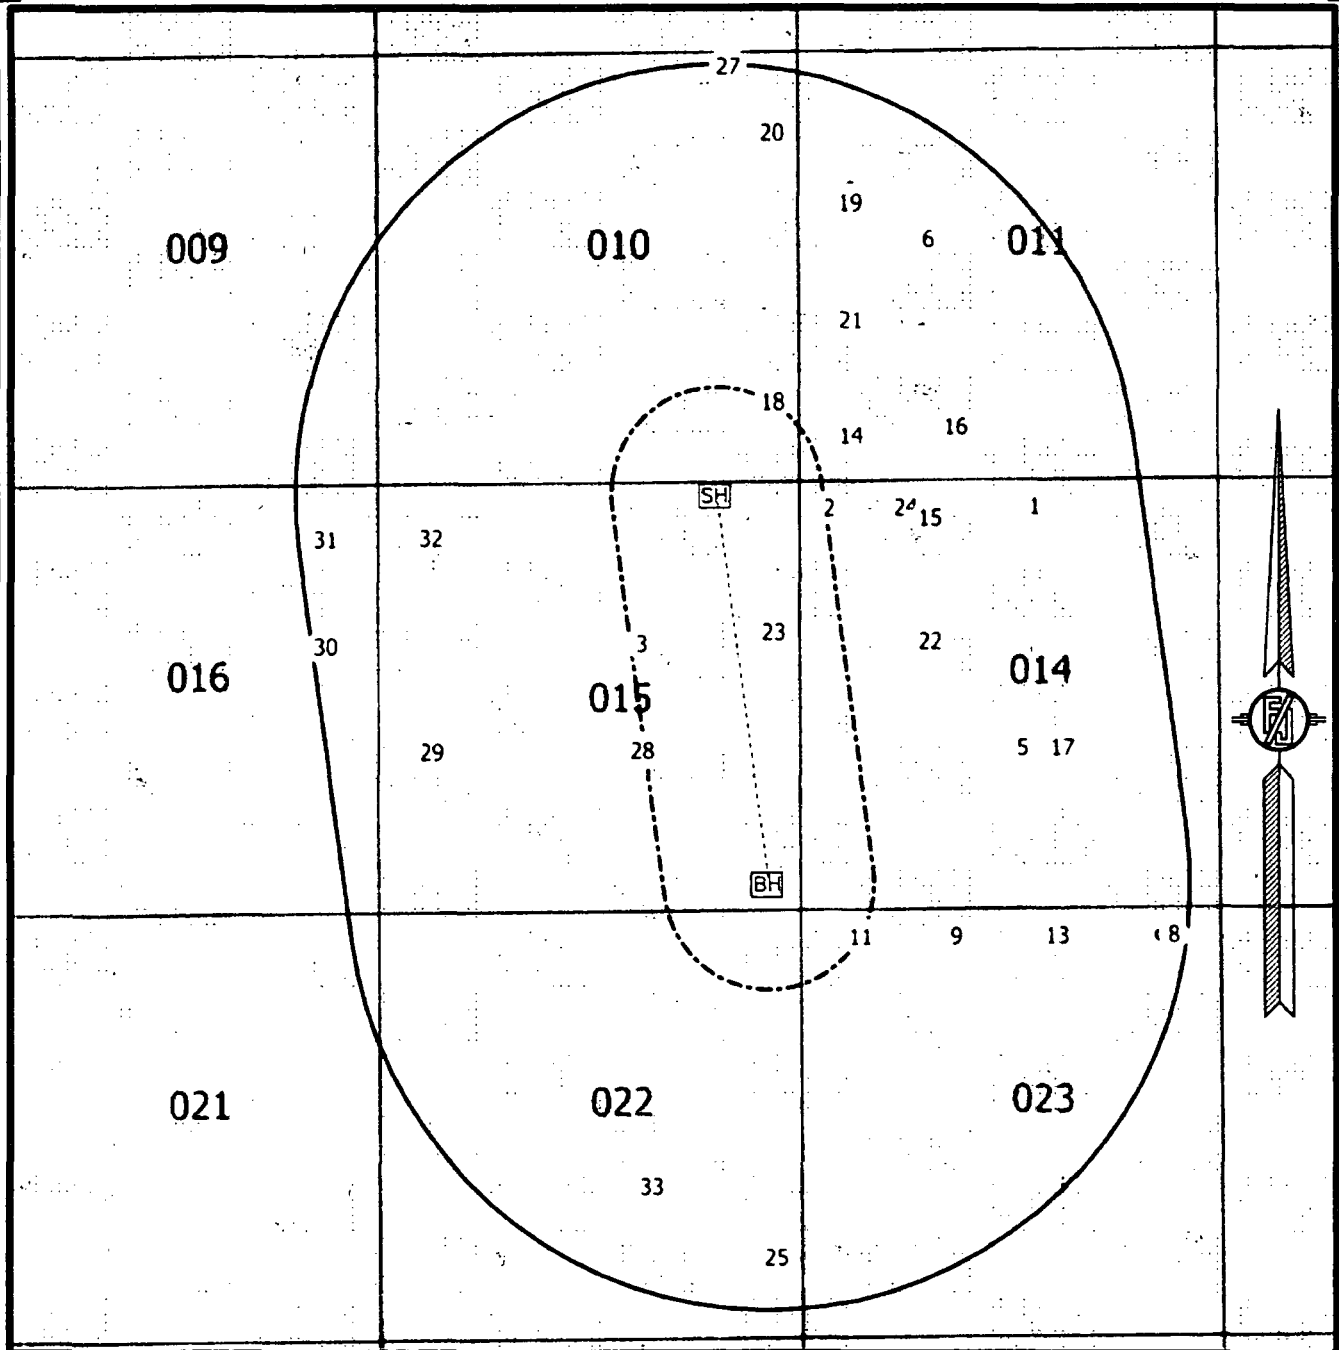

WELL DATA FROM NMOC GIS - 4/25/18

[SH] SURFACE LOCATION

[BH] BOTTOM OF HOLE

(XX) WELLS WITHIN 1 MILE

----- WELL PATH

----- 1/4 MILE BOUNDARY

----- 1-MILE BOUNDARY

DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H

LOCATED 175 FT. FROM THE NORTH LINE
 AND 1040 FT. FROM THE EAST LINE OF
 SECTION 15, TOWNSHIP 23 SOUTH,
 RANGE 32 EAST, N.M.P.M.
 LEA COUNTY, STATE OF NEW MEXICO

APRIL 30, 2018


SURVEY NO. 5805A

MADRON SURVEYING, INC.

501 SOUTH CANAL
 (675) 234-3341

CARLSBAD, NEW MEXICO

PLAN VIEW

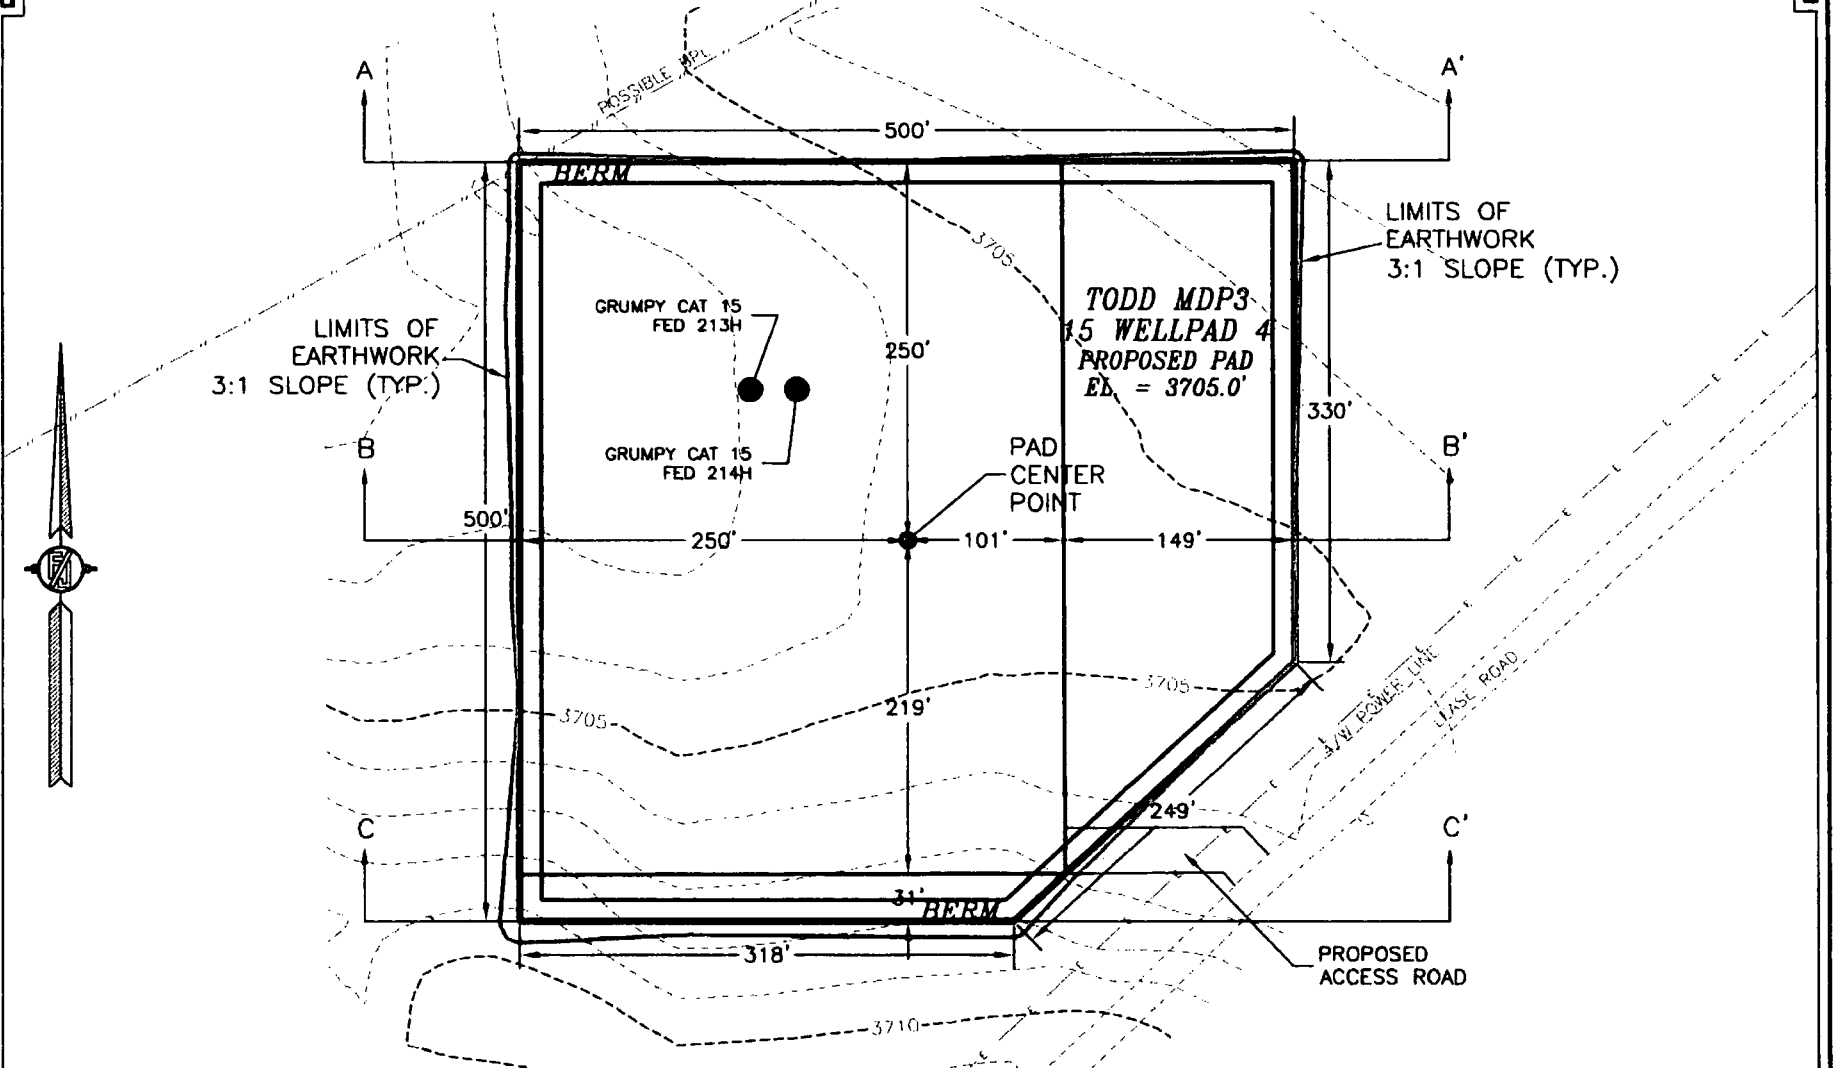

012 60 120 240
SCALE 1" = 120'

DEVON ENERGY PRODUCTION COMPANY, L.P.
PAD GRADING AND CROSS SECTIONS
GRUMPY CAT 15 FED 214H
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

CUT	FILL	NET
3880 CU. YD	5746 CU. YD	1866 CU. YD (FILL)

EARTHWORK QUANTITIES ARE ESTIMATED


APRIL 30, 2018

MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO


SHEET 1-2
SURVEY NO. 5805A

CROSS-SECTIONS


SECTION A-A'



SECTION B-B'



SECTION C-C'



012 60 120 240
SCALE 1" = 120' - 1" = 20' VER

DEVON ENERGY PRODUCTION COMPANY, L.P.
PAD GRADING AND CROSS SECTIONS
GRUMPY CAT 16 FED 214H
SECTION 16, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

CUT	FILL	NET
3880 CU. YD	5746 CU. YD	1866 CU. YD (FILL)

EARTHWORK QUANTITIES ARE ESTIMATED

APRIL 30, 2018

MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO


(575) 234-3341

SHEET 2-2
SURVEY NO. 5805A


ACCESS ROAD PLAT

ACCESS ROAD FOR ACCESS ROAD FOR GRUMPY CAT 15 FED 213H & 214H

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF AN ACCESS ROAD CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
APRIL 30, 2018

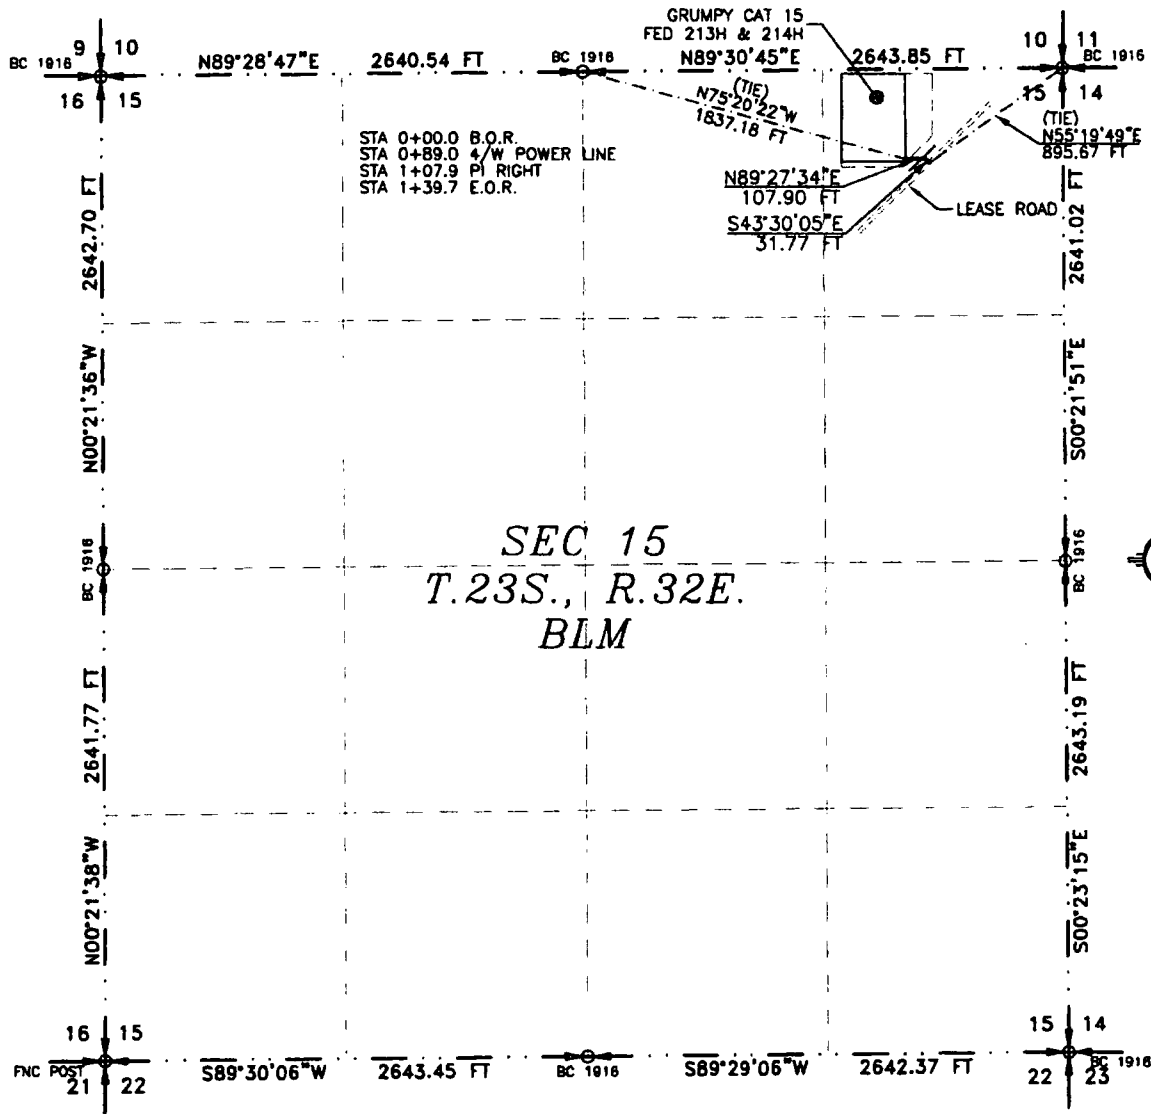

SEE NEXT SHEET (2-2) FOR DESCRIPTION



GENERAL NOTES

- 1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.
- 2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.

SHEET: 1-2

MADRON SURVEYING, INC. CARLSBAD, NEW MEXICO

SURVEYOR CERTIFICATE

I, FILIMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF THIS CERTIFICATE IS EXECUTED AT CARLSBAD,

NEW MEXICO, THIS 14 DAY OF MAY 2018

[Signature of Filimon F. Jaramillo]
FILIMON F. JARAMILLO, S.S. 12797

MADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341

SURVEY NO. 5805A

ACCESS ROAD PLAT

ACCESS ROAD FOR ACCESS ROAD FOR GRUMPY CAT 15 FED 213H & 214H

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF AN ACCESS ROAD CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
APRIL 30, 2018

DESCRIPTION

A STRIP OF LAND 30 FEET WIDE CROSSING BUREAU OF LAND MANAGEMENT LAND IN SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., LEA COUNTY, STATE OF NEW MEXICO AND BEING 15 FEET EACH SIDE OF THE FOLLOWING DESCRIBED CENTERLINE SURVEY:

BEGINNING AT A POINT WITHIN THE NE/4 NE/4 OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., WHENCE THE NORTH QUARTER CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N75°20'22"W, A DISTANCE OF 1837.18 FEET;
THENCE N89°27'34"E A DISTANCE OF 107.90 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;
THENCE S43°30'05"E A DISTANCE OF 31.77 FEET THE TERMINUS OF THIS CENTERLINE SURVEY, WHENCE THE NORTHEAST CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N55°19'49"E, A DISTANCE OF 895.67 FEET;

SAID STRIP OF LAND BEING 139.67 FEET OR 8.46 RODS IN LENGTH, CONTAINING 0.096 ACRES MORE OR LESS AND BEING ALLOCATED BY FORTIES AS FOLLOWS:

NE/4 NE/4 139.67 L.F. 8.46 RODS 0.096 ACRES

GENERAL NOTES

1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.

2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.

SHEET: 2-2

MADRON SURVEYING, INC. 301 SOUTH CANAL
(575) 234-3341 **CARLSBAD, NEW MEXICO**

SURVEYOR CERTIFICATE

I, FILMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF, THIS CERTIFICATE IS EXECUTED AT CARLSBAD, NEW MEXICO, THIS 12TH DAY OF MAY 2018.

FILMON F. JARAMILLO PLSL 12797

MADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341

SURVEY NO. 5805A



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Drilling Plan Data Report

02/13/2019

APD ID: 10400032225

Submission Date: 07/24/2018

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Well Type: OIL WELL

Well Work Type: Drill

Highlighted data
reflects the most
recent changes

[Show Final Text](#)

Formation ID	Formation Name	Elevation	True Vertical Depth	Measured Depth	Lithologies	Mineral Resources	Producing Formation
1	UNKNOWN	3703	0	0	ALLUVIUM	NONE	No
2	RUSTLER	2518	1185	1185	ANHYDRITE	NONE	No
3	SALADO	2098	1605	1605	SALT	NONE	No
4	DELAWARE	-1202	4905	4905	SANDSTONE	NATURAL GAS,OIL	No
5	BONE SPRING	-5042	8745	8745	LIMESTONE	NATURAL GAS,OIL	No
6	BONE SPRING 1ST	-6217	9920	9920	SANDSTONE	NATURAL GAS,OIL	No
7	BONE SPRING 2ND	-6827	10530	10530	SANDSTONE	NATURAL GAS,OIL	Yes

Pressure Rating (PSI): 5M

Rating Depth: 10545

Equipment: BOP/BOPE will be installed per Onshore Oil & Gas Order #2 requirements prior to drilling below 13-3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 5M will be installed on the wellhead system. BOP/BOPE will be tested by an independent service company per Onshore Oil & Gas Order #2 requirements and MASP (Maximum Anticipated Surface Pressure) calculations. If the system is upgraded, all the components installed will be functional and tested.

Requesting Variance? YES

Variance request: A variance is requested for the use of a flexible choke line from the BOP stack to the choke manifold. See attached for specs for hydrostatic test chart.

Testing Procedure: A multibowl wellhead may be used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

Choke Diagram Attachment:

Grumpy_Cat_15_Fed_214H_5M_BOPE__CK_20180718142033.pdf

BOP Diagram Attachment:

Grumpy_Cat_15_Fed_214H_5M_BOPE__CK_20180718142110.pdf

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Pressure Rating (PSI): 5M

Rating Depth: 6000

Equipment: BOP/BOPE will be installed per Onshore Oil & Gas Order #2 requirements prior to drilling below 13-3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 5M will be installed on the wellhead system. BOP/BOPE will be tested by an independent service company per Onshore Oil & Gas Order #2 requirements and MASP (Maximum Anticipated Surface Pressure) calculations. If the system is upgraded, all the components installed will be functional and tested.

Requesting Variance? YES

Variance request: A variance is requested for the use of a flexible choke line from the BOP stack to the choke manifold. See attached for specs for hydrostatic test chart.

Testing Procedure: A multibowl wellhead may be used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

Choke Diagram Attachment:

Grumpy_Cat_15_Fed_214H_5M_BOPE__CK_20180718142129.pdf

BOP Diagram Attachment:

Grumpy_Cat_15_Fed_214H_5M_BOPE__CK_20180718142144.pdf

Casing ID	String Type	Hole Size	Csg Size	Condition	Standard	Tapered String	Top Set MD	Bottom Set MD	Top Set TVD	Bottom Set TVD	Top Set MSL	Bottom Set MSL	Calculated casing length MD	Grade	Weight	Joint Type	Collapse SF	Burst SF	Joint SF Type	Joint SF	Body SF Type	Body SF
1	SURFACE	17.5	13.375	NEW	API	N	0	1230	0	1230			1230	H-40	48	OTHER - BTC	1.125	1.25	BUOY	1.6	BUOY	1.6
2	INTERMEDIATE	12.25	9.625	NEW	API	N	0	6000	0	6000			6000	J-55	40	OTHER - BTC	1.125	1.25	BUOY	1.6	BUOY	1.6
3	PRODUCTION	8.75	5.5	NEW	API	N	0	15243	0	10545			15243	P-110	17	OTHER - BTC	1.125	1.25	BUOY	1.6	BUOY	1.6

Casing Attachments

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Casing Attachments

Casing ID: 1 **String Type:** SURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Grumpy_Cat_15_Fed_214H_Surf_Csg_Ass_20180718142311.pdf

Casing ID: 2 **String Type:** INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Grumpy_Cat_15_Fed_214H_Int_Csg_Ass_20180718142322.pdf

Casing ID: 3 **String Type:** PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

Grumpy_Cat_15_Fed_214H_Prod_Csg_Ass_20180718142334.pdf

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

String Type	Lead/Tail	Stage Tool Depth	Top MD	Bottom MD	Quantity(sx)	Yield	Density	Cu Ft	Excess%	Cement type	Additives
SURFACE	Lead		0	730	440	1.73	10.2	761	50	C	0.125 lbs/sack Poly-F-Flake
SURFACE	Tail		730	1230	389	1.34	14.8	521	50	C	0.125 lbs/sack Poly-F-Flake
INTERMEDIATE	Lead		0	5500	1211	1.85	9.5	2239	30	C	(65:35) Class C Cement: Poz (Fly Ash): 6% BWOC Bentonite + 5% BWOW Sodium Chloride + 0.125 lbs/sks Poly-E-Flake
INTERMEDIATE	Tail		5500	6000	153	1.33	14.8	204	30	C	0.125 lbs/sack Poly-F-Flake
PRODUCTION	Lead		5800	1004 2	360	3.27	9	1179	10	TUNED	TUNEDLITE
PRODUCTION	Tail		1004 2	1524 3	1369	1.2	14.5	1642	25	H	(50:50) Clas H Cement: Poz (Fly Ash) + 0.5% bwoc HALAD-344 + 0.4% bwoc CFR-3 + 0.2% BWOC HR-601 + 2% bwoc Bentonite

Mud System Type: Closed

Will an air or gas system be Used? NO

Description of the equipment for the circulating system in accordance with Onshore Order #2:

Diagram of the equipment for the circulating system in accordance with Onshore Order #2:

Describe what will be on location to control well or mitigate other conditions: Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

Describe the mud monitoring system utilized: PVT/Pason/Visual Monitoring

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Top Depth	Bottom Depth	Mud Type	Min Weight (lbs/gal)	Max Weight (lbs/gal)	Density (lbs/cu ft)	Gel Strength (lbs/100 sqft)	PH	Viscosity (CP)	Salinity (ppm)	Filtration (cc)	Additional Characteristics
0	1230	OTHER : FW GEL	8.6	8.8							
1177	6000	SALT SATURATED	10	11							
6000	1054 5	OTHER : CUT BRINE	8.5	9							

List of production tests including testing procedures, equipment and safety measures:

Will run GRMWD from TD to from KOP. Cement bond logs will be run in vertical to determine top of cement. Stated logs run will be in the Completion Report and submitted to the BLM.

List of open and cased hole logs run in the well:

CALIPER,CBL,DS,GR,MUDLOG

Coring operation description for the well:

N/A

Anticipated Bottom Hole Pressure: 4935

Anticipated Surface Pressure: 2615.1

Anticipated Bottom Hole Temperature(F): 168

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards attachment:

Hydrogen Sulfide drilling operations plan required? YES

Hydrogen sulfide drilling operations plan:

Grumpy_Cat_15_Fed_214H_H2S_Plan_20180718142642.pdf

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Proposed horizontal/directional/multi-lateral plan submission:

Devon_Grumpy_Cat_15_Fed_214H_Permit_Plan_2_20180718142701.pdf

Devon_Grumpy_Cat_15_Fed_Com_214H_Permit_Plan_2_AC_Report_20180718142702.pdf

Devon_Grumpy_Cat_15_Fed_Com_214H_Permit_Plan_2_Plot_20180718142702.pdf

Other proposed operations facets description:



Other proposed operations facets attachment:

Grumpy_Cat_15_Fed_214H_Clsd_Loop_20180718142752.pdf

Grumpy_Cat_15_Fed_214H_MB_Verb_20180718142753.pdf

Grumpy_Cat_15_Fed_214H_MB_Wellhd_20180718142754.pdf


Grumpy_Cat_15_Fed_214H_GasCapturePlan_20180719133258.pdf

Grumpy_Cat_15_Fed_214H_Drilling_Plan_20181024091540.pdf


Other Variance attachment:

Grumpy_Cat_15_Fed_214H_Co_flex_20180718142801.pdf


13-5/8" 5M BOPE & Closed Loop Equipment Schematic

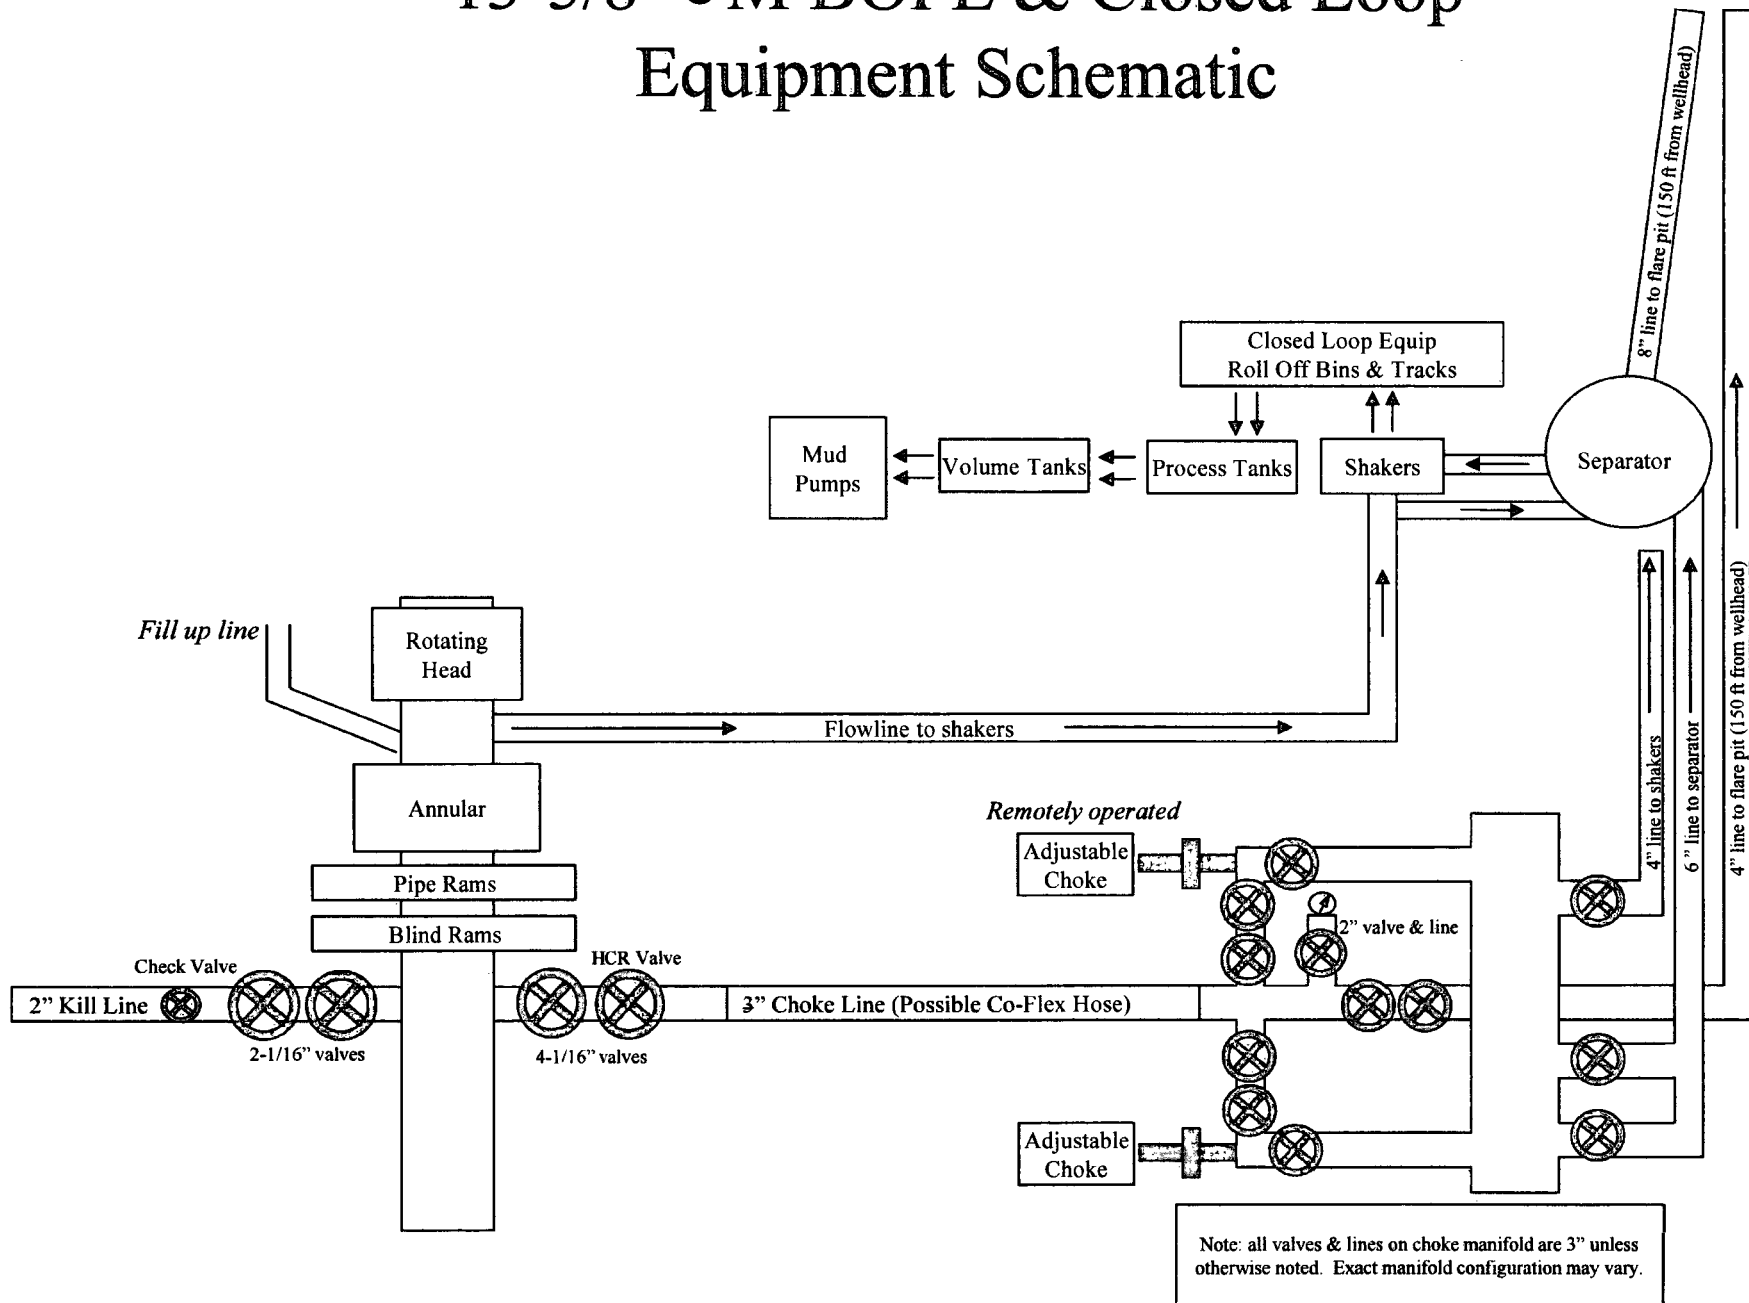


13-5/8" 5M BOPE & Closed Loop Equipment Schematic

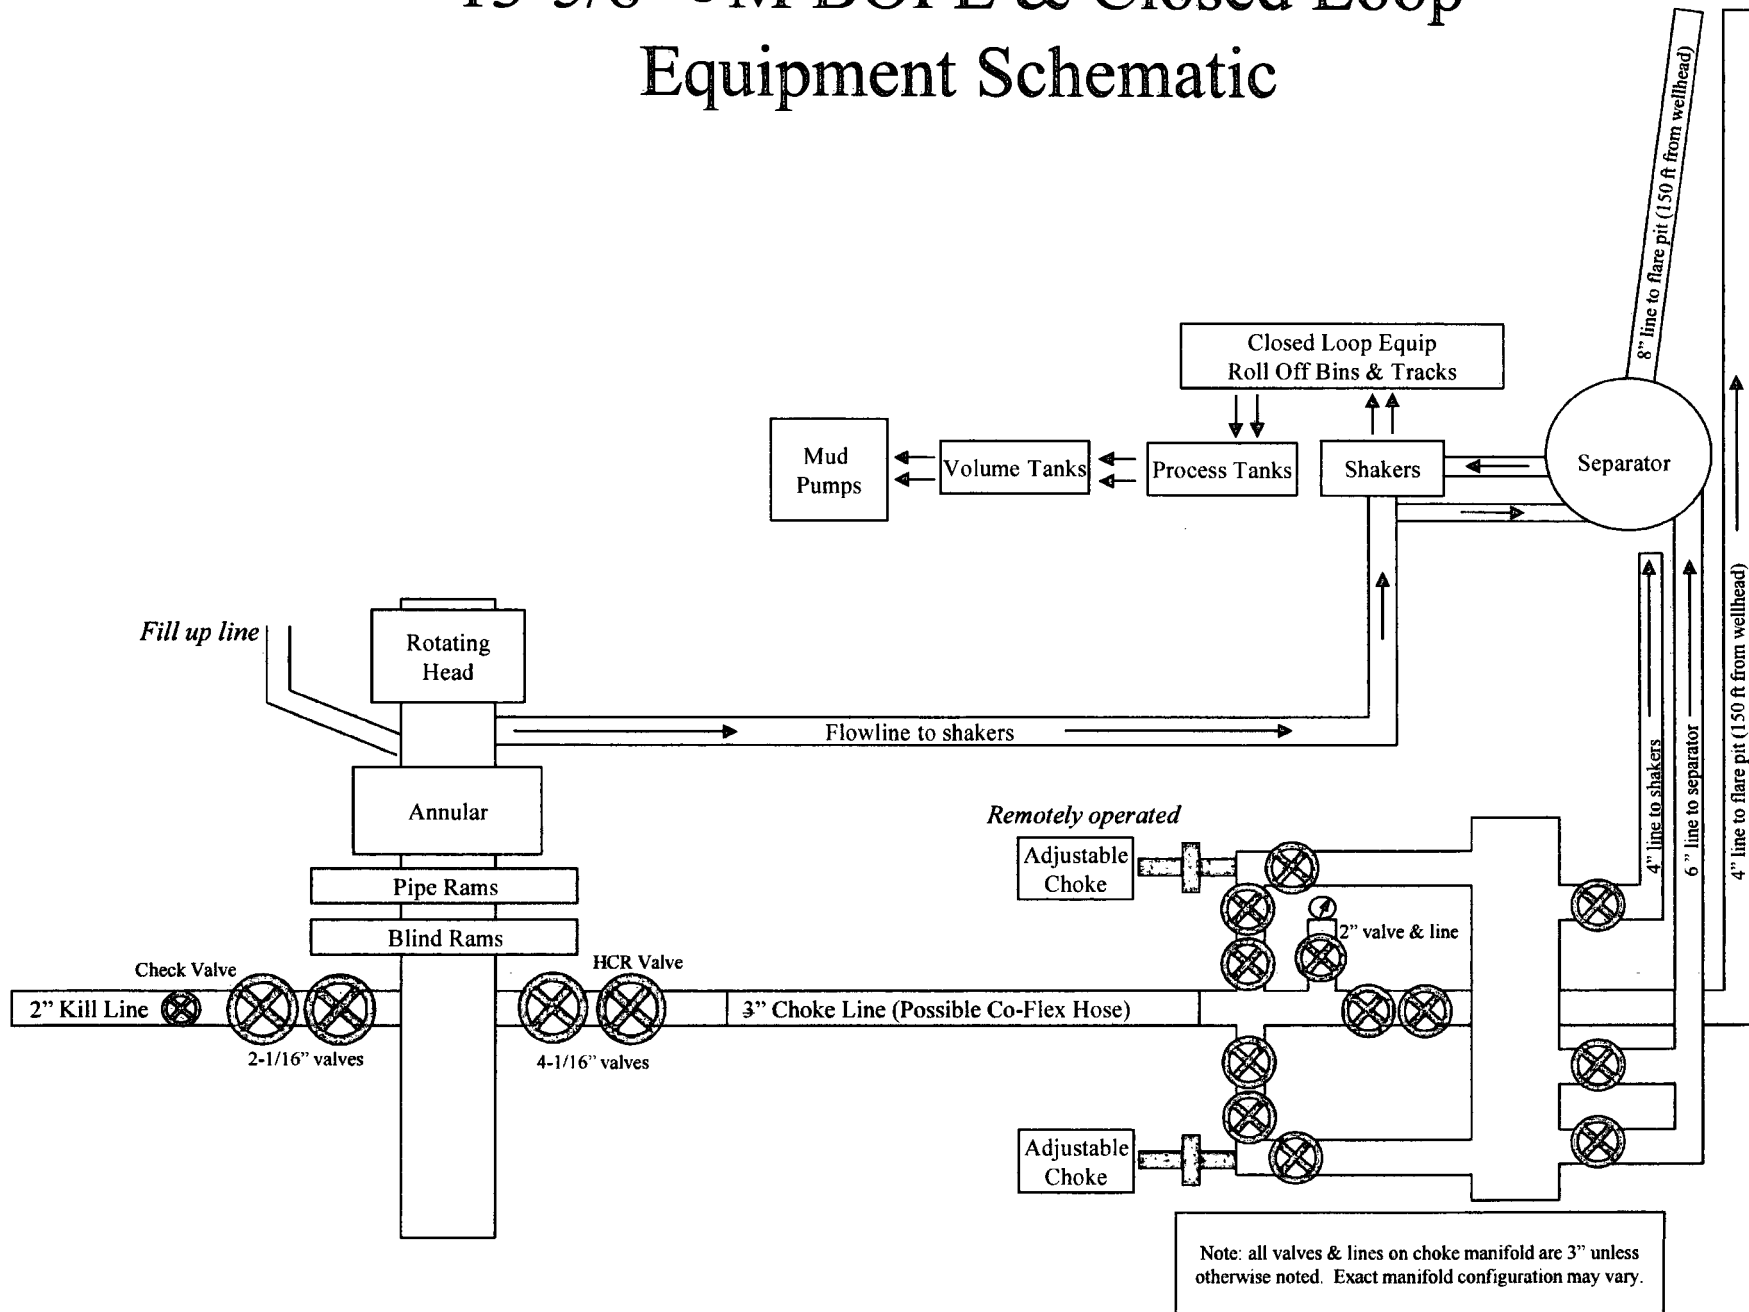

13-5/8" 5M BOPE & Closed Loop Equipment Schematic

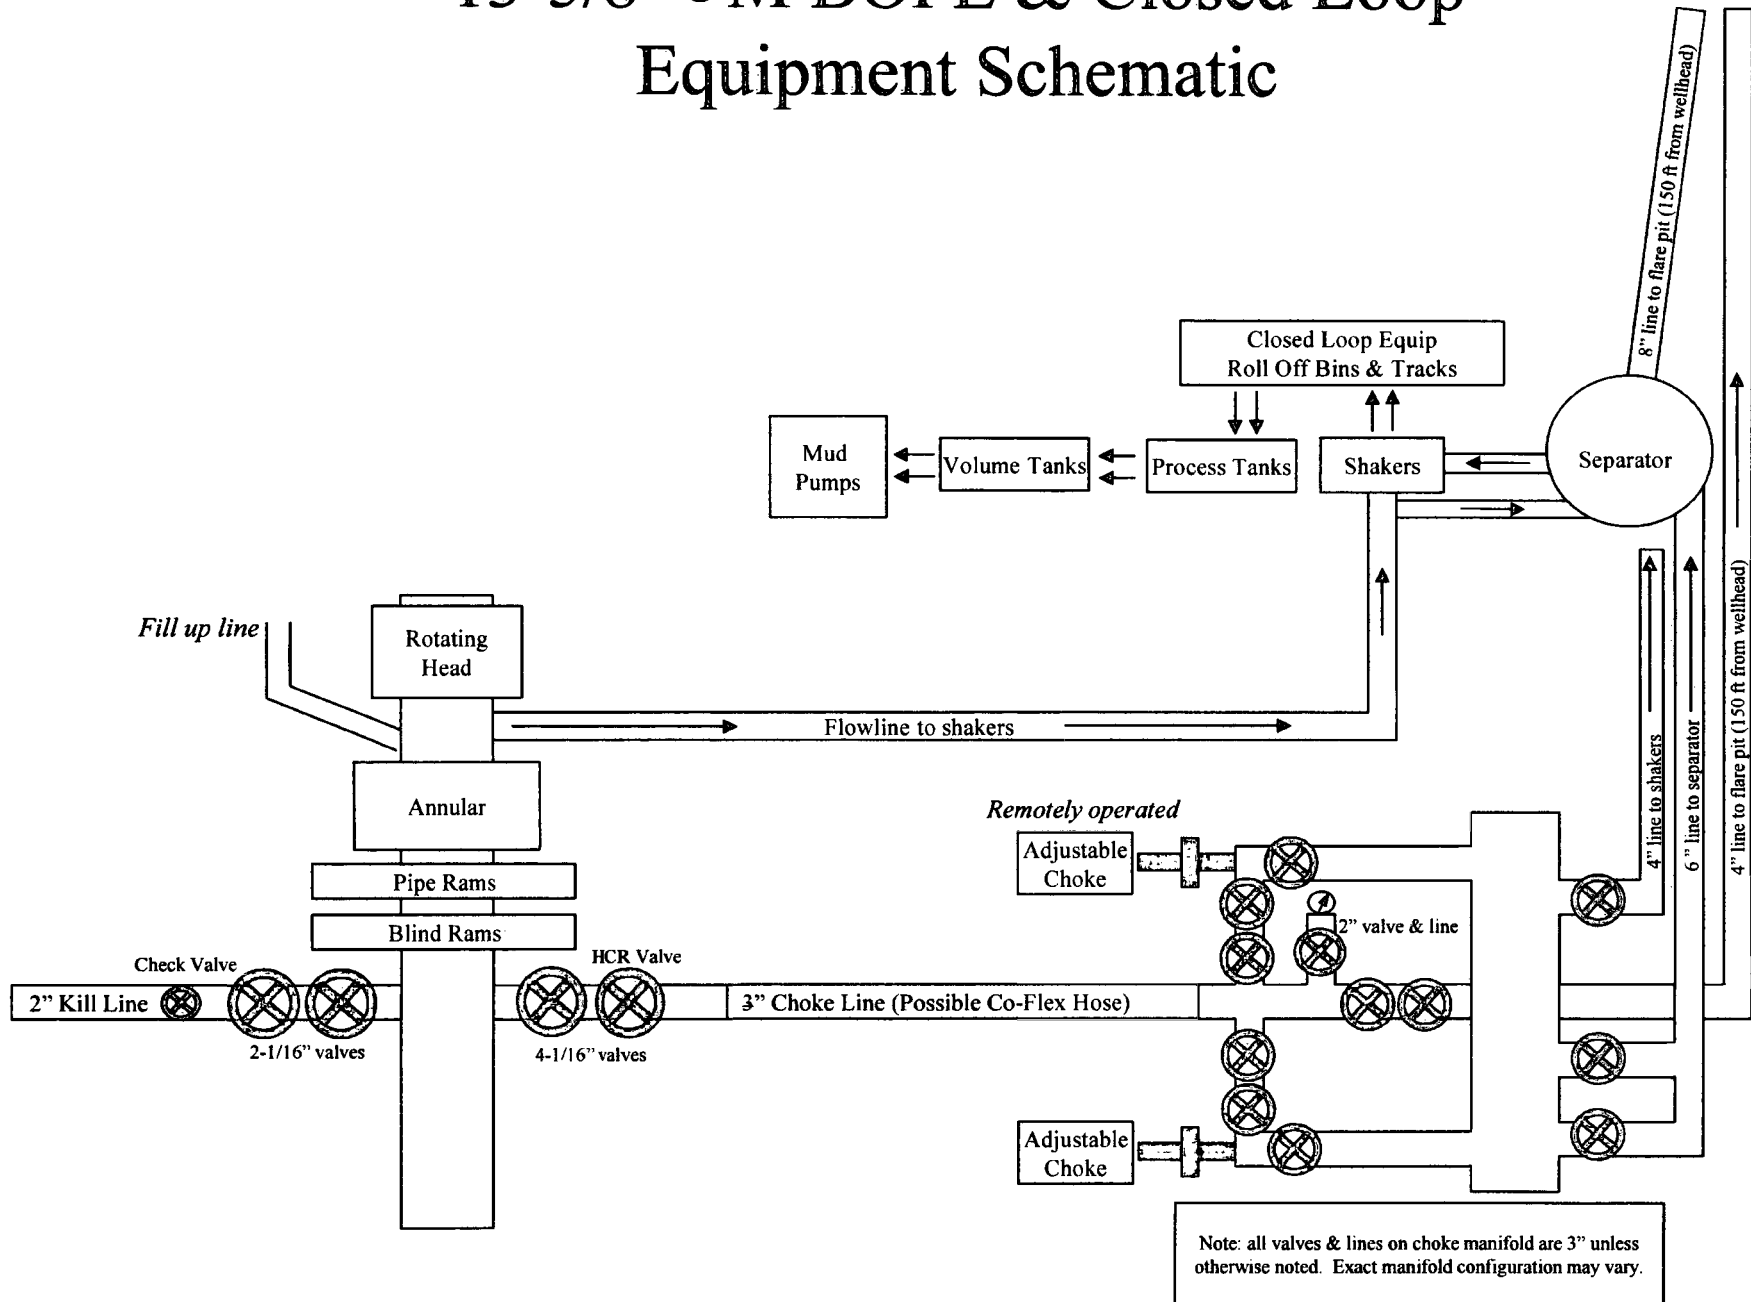

13-5/8" 5M BOPE & Closed Loop Equipment Schematic

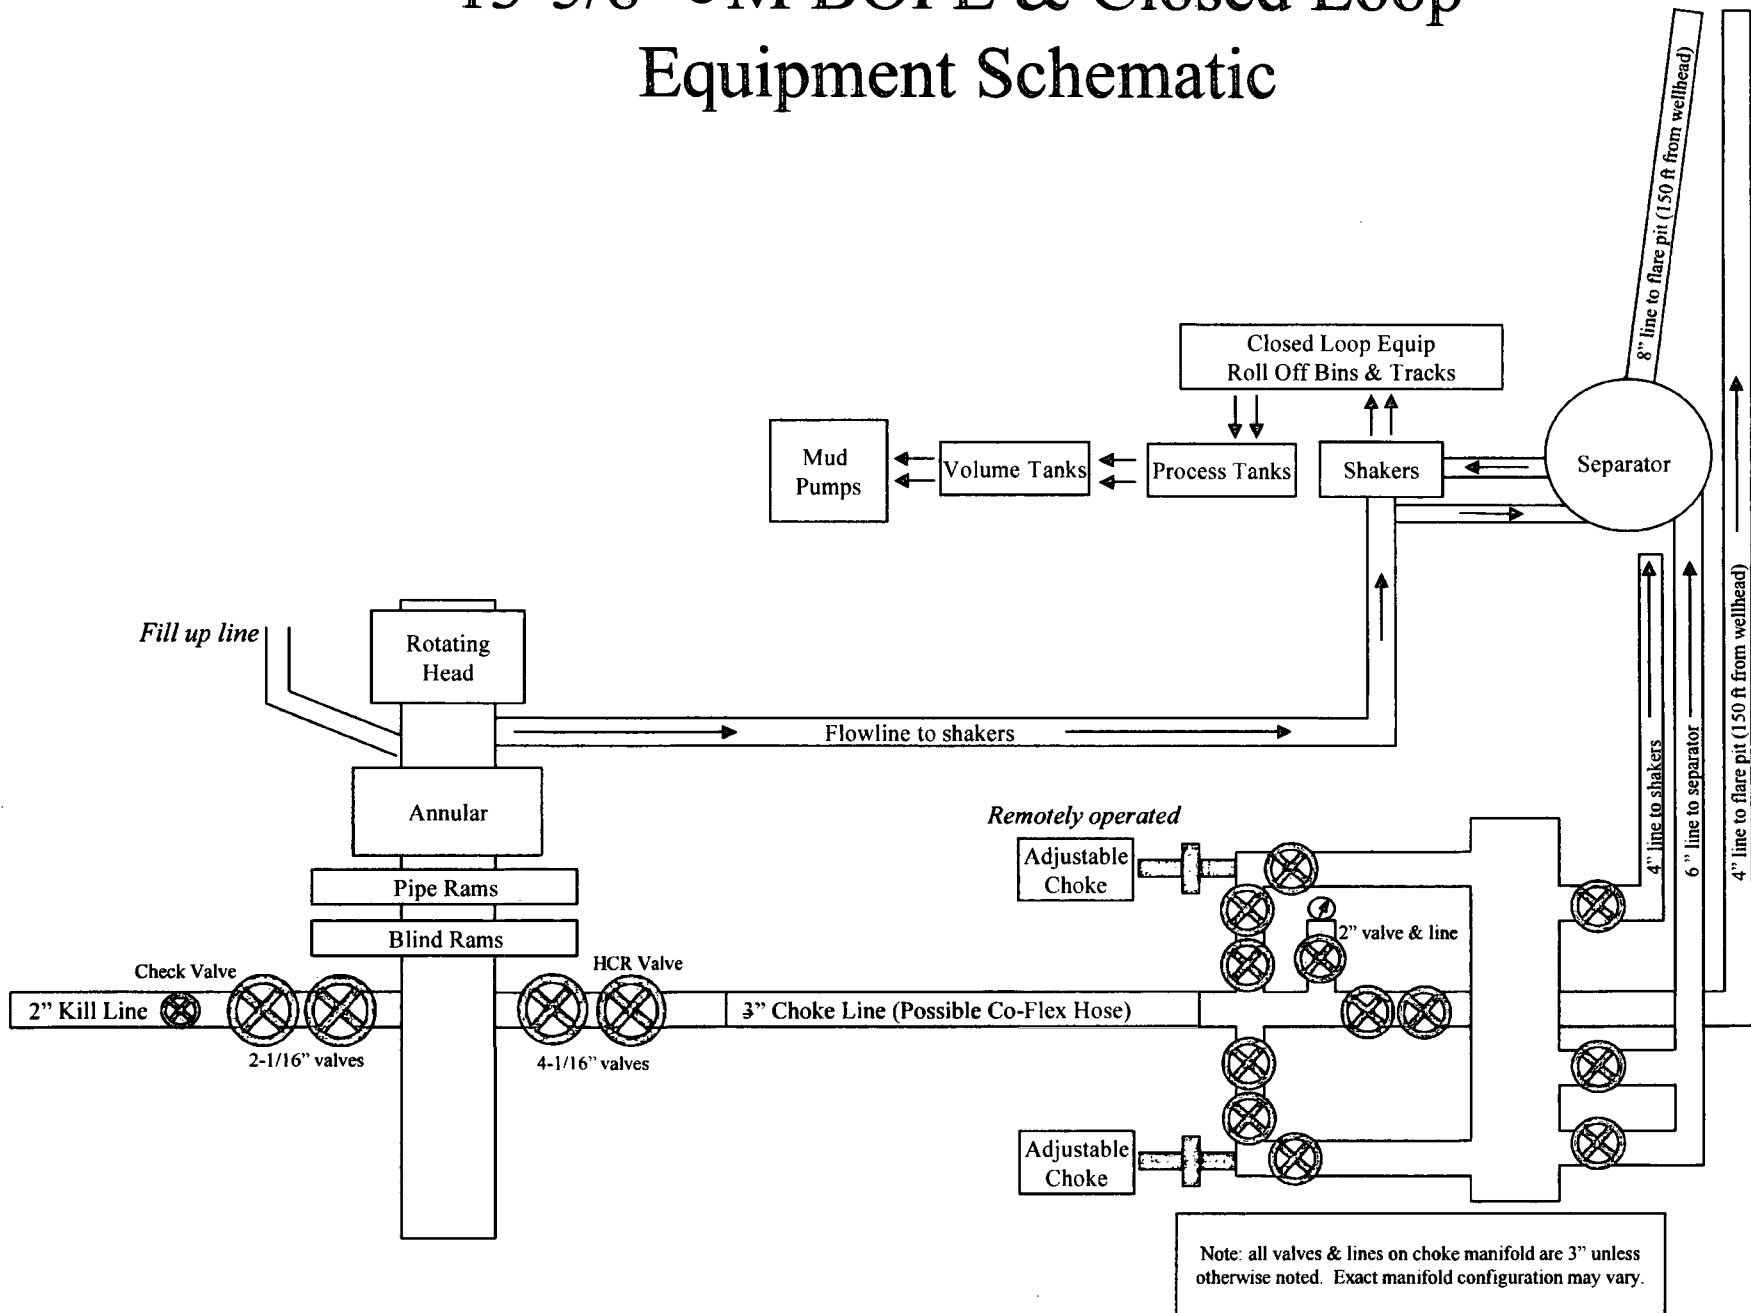

Casing Assumptions and Load Cases

Surface

All casing design assumptions were ran in Stress Check to determine safety factor which meet or exceed both Devon Energy and BLM minimum requirements. All casing strings will be filled while running in hole in order to not exceed collapse rating of the pipe.

Surface Casing Burst Design		
Load Case	External Pressure	Internal Pressure
Pressure Test	Formation Pore Pressure	Max mud weight of next hole-section plus Test psi
Drill Ahead	Formation Pore Pressure	Max mud weight of next hole section
Displace to Gas	Formation Pore Pressure	Dry gas from next casing point

Surface Casing Collapse Design		
Load Case	External Pressure	Internal Pressure
Full Evacuation	Water gradient in cement, mud above TOC	None
Cementing	Wet cement weight	Water (8.33ppg)

Surface Casing Tension Design	
Load Case	Assumptions
Overpull	100kips
Runing in hole	3 ft/s
Service Loads	N/A

Casing Assumptions and Load Cases

Intermediate

All casing design assumptions were ran in Stress Check to determine safety factor which meet or exceed both Devon Energy and BLM minimum requirements. All casing strings will be filled while running in hole in order to not exceed collapse rating of the pipe.

Intermediate Casing Burst Design		
Load Case	External Pressure	Internal Pressure
Pressure Test	Formation Pore Pressure	Max mud weight of next hole-section plus Test psi
Drill Ahead	Formation Pore Pressure	Max mud weight of next hole section
Fracture @ Shoe	Formation Pore Pressure	Dry gas

Intermediate Casing Collapse Design		
Load Case	External Pressure	Internal Pressure
Full Evacuation	Water gradient in cement, mud above TOC	None
Cementing	Wet cement weight	Water (8.33ppg)

Intermediate Casing Tension Design	
Load Case	Assumptions
Overpull	100kips
Runing in hole	2 ft/s
Service Loads	N/A

Casing Assumptions and Load Cases

Production

All casing design assumptions were ran in Stress Check to determine safety factor which meet or exceed both Devon Energy and BLM minimum requirements. All casing strings will be filled while running in hole in order to not exceed collapse rating of the pipe.

Production Casing Burst Design		
Load Case	External Pressure	Internal Pressure
Pressure Test	Formation Pore Pressure	Fluid in hole (water or produced water) + test psi
Tubing Leak	Formation Pore Pressure	Packer @ KOP, leak below surface 8.6 ppg packer fluid
Stimulation	Formation Pore Pressure	Max frac pressure with heaviest frac fluid

Production Casing Collapse Design		
Load Case	External Pressure	Internal Pressure
Full Evacuation	Water gradient in cement, mud above TOC.	None
Cementing	Wet cement weight	Water (8.33ppg)

Production Casing Tension Design	
Load Case	Assumptions
Overpull	100kips
Runing in hole	2 ft/s
Service Loads	N/A



Devon Energy Center
333 West Sheridan Avenue
Oklahoma City, Oklahoma 73102-5015

Hydrogen Sulfide (H_2S) Contingency Plan

For



Grumpy Cat 15 Fed 214H

**Sec-15 T-23S R-32E
175' FNL & 1040' FEL
LAT. = 32.3114483' N (NAD83)
LONG = 103.6573333' W**

Lea County NM

Grumpy Cat 15 Fed 214H

This is an open drilling site. H₂S monitoring equipment and emergency response equipment will be used within 500' of zones known to contain H₂S, including warning signs, wind indicators and H₂S monitor.

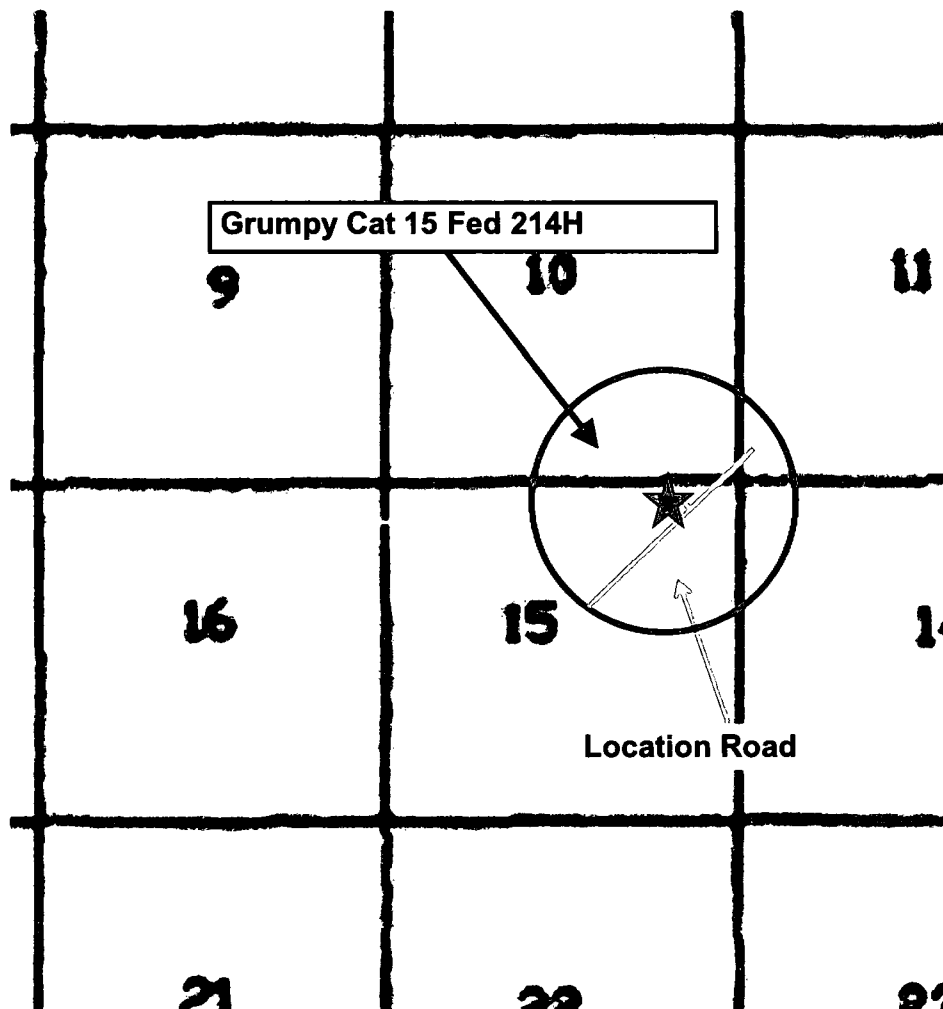

Assumed 100 ppm ROE = 3000' (Radius of Exposure)
100 ppm H₂S concentration shall trigger activation of this plan.

Escape

Crews shall escape upwind of escaping gas in the event of an emergency release of gas. Escape can be facilitated from the location entrance road. Crews should then block the entrance to the location from the lease road so as not to allow anyone traversing into a hazardous area. The blockade should be at a safe distance outside of the ROE. There are no homes or buildings in or near the ROE.

Assumed 100 ppm ROE = 3000'

100 ppm H₂S concentration shall trigger activation of this plan.

Emergency Procedures

In the event of a release of gas containing H₂S, the first responder(s) must

- **Isolate the area and prevent entry by other persons into the 100 ppm ROE.**
- **Evacuate any public places encompassed by the 100 ppm ROE.**
- **Be equipped with H₂S monitors and air packs in order to control the release.**
- **Use the “buddy system” to ensure no injuries occur during the response**
- **Take precautions to avoid personal injury during this operation.**
- **Contact operator and/or local officials to aid in operation. See list of phone numbers attached.**
- **Have received training in the**
 - **Detection of H₂S, and**
 - **Measures for protection against the gas,**
 - **Equipment used for protection and emergency response.**

Ignition of Gas Source

Should control of the well be considered lost and ignition considered, take care to protect against exposure to Sulfur Dioxide (SO₂). Intentional ignition must be coordinated with the NMOC and local officials. Additionally the NM State Police may become involved. NM State Police shall be the Incident Command on scene of any major release. Take care to protect downwind whenever there is an ignition of the gas

Characteristics of H₂S and SO₂

Common Name	Chemical Formula	Specific Gravity	Threshold Limit	Hazardous Limit	lethal Concentration
Hydrogen Sulfide	H₂S	1.189 Air = 1	10 ppm	100 ppm/hr	600 ppm
Sulfur Dioxide	SO₂	2.21 Air = 1	2 ppm	N/A	1000 ppm

Contacting Authorities

Devon Energy Corp. personnel must liaison with local and state agencies to ensure a proper response to a major release. Additionally, the OCD must be notified of the release as soon as possible but no later than 4 hours. Agencies will ask for information such as type and volume of release, wind direction, location of release, etc. Be prepared with all information available. The following call list of essential and potential responders has been prepared for use during a release. Devon Energy Corp. Company response must be in coordination with the State of New Mexico's 'Hazardous Materials Emergency Response Plan' (HMER)

Hydrogen Sulfide Drilling Operation Plan

I. HYDROGEN SULFIDE (H₂S) TRAINING

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

1. The hazards and characteristics of hydrogen sulfide (H₂S)
2. The proper use and maintenance of personal protective equipment and life support systems.
3. The proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
4. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

1. The effects of H₂S metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
2. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
3. The contents and requirements of the H₂S Drilling Operations Plan and Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H₂S zone (within 3 days or 500 feet) and weekly H₂S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H₂S Drilling Operations Plan and the Public Protection Plan.

II. HYDROGEN SULFIDE TRAINING

Note: All H₂S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H₂S.

1. Well Control Equipment

- A. Flare line
- B. Choke manifold – Remotely Operated
- C. Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit
- D. Auxiliary equipment may include if applicable: annular preventer and rotating head.
- E. Mud/Gas Separator

2. Protective equipment for essential personnel:

30-minute SCBA units located at briefing areas, as indicated on well site diagram, with escape units available in the top doghouse. As it may be difficult to communicate audibly while wearing these units, hand signals shall be utilized.

3. H₂S detection and monitoring equipment:

Portable H₂S monitors positioned on location for best coverage and response. These units have warning lights which activate when H₂S levels reach 10 ppm and audible sirens which activate at 15 ppm. Sensor locations:

- Bell nipple
- Possum Belly/Shale shaker
- Rig floor
- Choke manifold
- Cellar

Visual warning systems:

- A. Wind direction indicators as shown on well site diagram
- B. Caution/ Danger signs shall be posted on roads providing direct access to locations. Signs will be painted a high visibility yellow with black lettering of sufficient size to be reasonable distance from the immediate location. Bilingual signs will be used when appropriate.

4. Mud program:

The mud program has been designed to minimize the volume of H₂S circulated to surface. Proper mud weight, safe drilling practices and the use of H₂S scavengers will minimize hazards when penetrating H₂S bearing zones.

5. Metallurgy:

- A. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold lines, and valves shall be H₂S trim.
- B. All elastomers used for packing and seals shall be H₂S trim.

6. Communication:

- A. Company personnel have/use cellular telephones in the field.
- B. Land line (telephone) communications at Office

7. Well testing:

- A. Drill stem testing will be performed with a minimum number of personnel in the immediate vicinity, which are necessary to safety and adequately conduct the test. The drill stem testing will be conducted during daylight hours and formation fluids will not be flowed to the surface. All drill-stem-testing operations conducted in an H₂S environment will use the closed chamber method of testing.
- B. There will be no drill stem testing.

<u>Devon Energy Corp. Company Call List</u>		
Drilling Supervisor – Basin – Mark Kramer		405-823-4796
EHS Professional – Laura Wright		405-439-8129
<u>Agency Call List</u>		
<u>Lea County (575)</u>	Hobbs	
	Lea County Communication Authority	393-3981
	State Police	392-5588
	City Police	397-9265
	Sheriff's Office	393-2515
	Ambulance	911
	Fire Department	397-9308
	LEPC (Local Emergency Planning Committee)	393-2870
	NMOCD	393-6161
	US Bureau of Land Management	393-3612
<u>Eddy County (575)</u>	Carlsbad	
	State Police	885-3137
	City Police	885-2111
	Sheriff's Office	887-7551
	Ambulance	911
	Fire Department	885-3125
	LEPC (Local Emergency Planning Committee)	887-3798
	US Bureau of Land Management	887-6544
	NM Emergency Response Commission (Santa Fe)	(505) 476-9600
	24 HR	(505) 827-9126
	National Emergency Response Center	(800) 424-8802
	National Pollution Control Center: Direct	(703) 872-6000
	For Oil Spills	(800) 280-7118
	Emergency Services	
	Wild Well Control	(281) 784-4700
	Cudd Pressure Control	(915) 699-0139 (915) 563-3356
	Halliburton	(575) 746-2757
	B. J. Services	(575) 746-3569
<u>Give GPS position:</u>	Native Air – Emergency Helicopter – Hobbs	(575) 392-6429
	Flight For Life - Lubbock, TX	(806) 743-9911
	Aerocare - Lubbock, TX	(806) 747-8923
	Med Flight Air Amb - Albuquerque, NM	(575) 842-4433
	Lifeguard Air Med Svc. Albuquerque, NM	(800) 222-1222
	Poison Control (24/7)	(575) 272-3115
	Oil & Gas Pipeline 24 Hour Service	(800) 364-4366
	NOAA – Website - www.nhc.noaa.gov	

Prepared in conjunction with
Dave Small



WCDSC Permian NM

Lea County (NAD83 New Mexico East)

Sec 15-T23S-R32E

Grumpy Cat 15 Fed Com 214H

Wellbore #1

Plan: Permit Plan 1

Standard Planning Report - Geographic

09 May, 2018

Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference	Well Grumpy Cat 15-22 Fed Com 214H
Company:	WCDSC Permian NM	TVD Reference:	RKB @ 3728.80ft
Project:	Lea County (NAD83 New Mexico East)	MD Reference:	RKB @ 3728.80ft
Site:	Sec 15-T23S-R32E	North Reference:	Grid
Well:	Grumpy Cat 15-22 Fed Com 214H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Project	Lea County (NAD83 New Mexico East)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Sec 15-T23S-R32E			
Site Position:		Northing:	477,833.18 usft	Latitude: 32.311899
From:	Map	Easting:	745,935.72 usft	Longitude: -103.671069
Position Uncertainty:	0.00 ft	Slot Radius:	13-3/16 "	Grid Convergence: 0.35 °

Well	Grumpy Cat 15-22 Fed Com 214H			
Well Position	+N/-S	0.00 ft	Northing:	477,695.83 usft
	+E/-W	0.00 ft	Easting:	750,180.09 usft
Position Uncertainty		0.50 ft	Wellhead Elevation:	Ground Level: 3,703.80 ft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination	Dip Angle	Field Strength
			(°)	(°)	(nT)
	IGRF2015	4/19/2018	6.91	60.12	47,892.70414982

Design	Permit Plan 1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W	Direction
	(ft)	(ft)	(ft)	(°)
	0.00	0.00	0.00	172.00

Plan Survey Tool Program	Date	5/9/2018		
Depth From	Depth To	Survey (Wellbore)	Tool Name	Remarks
(ft)	(ft)			
1	0.00	15,243.83 Permit Plan 1 (Wellbore #1)	MWD+HDGM	
			OWSG MWD + HDGM	

Plan Sections										
Measured	Inclination	Azimuth	Vertical	+N/-S	+E/-W	Dogleg	Build	Turn	TFO	Target
Depth	(°)	(°)	Depth	(ft)	(ft)	Rate	Rate	Rate	(°)	
(ft)			(ft)			(°/100usft)	(°/100usft)	(°/100usft)		
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00	
3,263.90	7.64	78.48	3,261.64	10.16	49.82	1.00	1.00	0.00	78.48	
7,532.38	7.64	78.48	7,492.24	123.52	605.80	0.00	0.00	0.00	0.00	
8,041.65	0.00	0.00	8,000.00	130.29	639.01	1.50	-1.50	0.00	180.00	Vertical Point - Grump
10,013.69	0.00	0.00	9,972.04	130.29	639.01	0.00	0.00	0.00	0.00	
10,913.69	90.00	179.62	10,545.00	-442.65	642.77	10.00	10.00	0.00	179.62	PBHL - Grumpy Cat 2
15,243.83	90.00	179.62	10,545.00	-4,772.69	671.17	0.00	0.00	0.00	0.00	PBHL - Grumpy Cat 2

Planning Report - Geographic

Database: EDM r5000.141_Prod US
Company: WCDSC Permian NM
Project: Lea County (NAD83 New Mexico East)
Site: Sec 15-T23S-R32E
Well: Grumpy Cat 15-22 Fed Com 214H
Wellbore: Wellbore #1
Design: Permit Plan 1

Local Co-ordinate Reference Well Grumpy Cat 15-22 Fed Com 214H
TVD Reference: RKB @ 3728.80ft
MD Reference: RKB @ 3728.80ft
North Reference: Grid
Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
0.00	0.00	0.00	0.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
100.00	0.00	0.00	100.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
200.00	0.00	0.00	200.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
300.00	0.00	0.00	300.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
400.00	0.00	0.00	400.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
500.00	0.00	0.00	500.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
600.00	0.00	0.00	600.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
700.00	0.00	0.00	700.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
800.00	0.00	0.00	800.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
900.00	0.00	0.00	900.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,000.00	0.00	0.00	1,000.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,100.00	0.00	0.00	1,100.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,200.00	0.00	0.00	1,200.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,300.00	0.00	0.00	1,300.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,400.00	0.00	0.00	1,400.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,500.00	0.00	0.00	1,500.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,600.00	0.00	0.00	1,600.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,700.00	0.00	0.00	1,700.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,800.00	0.00	0.00	1,800.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
1,900.00	0.00	0.00	1,900.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
2,000.00	0.00	0.00	2,000.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
2,100.00	0.00	0.00	2,100.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
2,200.00	0.00	0.00	2,200.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
2,300.00	0.00	0.00	2,300.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
2,400.00	0.00	0.00	2,400.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
2,500.00	0.00	0.00	2,500.00	0.00	0.00	477,695.83	750,180.09	32.311448	-103.657334
Begin Nudge									
2,600.00	1.00	78.48	2,599.99	0.17	0.86	477,696.01	750,180.94	32.311449	-103.657331
2,700.00	2.00	78.48	2,699.96	0.70	3.42	477,696.53	750,183.51	32.311450	-103.657323
2,800.00	3.00	78.48	2,799.86	1.57	7.69	477,697.40	750,187.78	32.311453	-103.657309
2,900.00	4.00	78.48	2,899.68	2.79	13.68	477,698.62	750,193.76	32.311456	-103.657289
3,000.00	5.00	78.48	2,999.37	4.36	21.36	477,700.19	750,201.45	32.311460	-103.657264
3,100.00	6.00	78.48	3,098.90	6.27	30.75	477,702.10	750,210.84	32.311465	-103.657234
3,200.00	7.00	78.48	3,198.26	8.53	41.85	477,704.36	750,221.93	32.311471	-103.657198
3,263.90	7.64	78.48	3,261.64	10.16	49.82	477,705.99	750,229.91	32.311475	-103.657172
EOB									
3,300.00	7.64	78.48	3,297.42	11.12	54.53	477,706.95	750,234.61	32.311478	-103.657157
3,400.00	7.64	78.48	3,396.53	13.77	67.55	477,709.60	750,247.64	32.311485	-103.657115
3,500.00	7.64	78.48	3,495.64	16.43	80.58	477,712.26	750,260.66	32.311492	-103.657072
3,600.00	7.64	78.48	3,594.76	19.08	93.60	477,714.92	750,273.69	32.311499	-103.657030
3,700.00	7.64	78.48	3,693.87	21.74	106.63	477,717.57	750,286.71	32.311506	-103.656988
3,800.00	7.64	78.48	3,792.98	24.40	119.65	477,720.23	750,299.74	32.311513	-103.656946
3,900.00	7.64	78.48	3,892.09	27.05	132.68	477,722.88	750,312.76	32.311520	-103.656904
4,000.00	7.64	78.48	3,991.21	29.71	145.70	477,725.54	750,325.79	32.311528	-103.656861
4,100.00	7.64	78.48	4,090.32	32.36	158.73	477,728.19	750,338.81	32.311535	-103.656819
4,200.00	7.64	78.48	4,189.43	35.02	171.75	477,730.85	750,351.84	32.311542	-103.656777
4,300.00	7.64	78.48	4,288.54	37.68	184.78	477,733.51	750,364.86	32.311549	-103.656735
4,400.00	7.64	78.48	4,387.66	40.33	197.80	477,736.16	750,377.89	32.311556	-103.656693
4,500.00	7.64	78.48	4,486.77	42.99	210.83	477,738.82	750,390.91	32.311563	-103.656650
4,600.00	7.64	78.48	4,585.88	45.64	223.85	477,741.47	750,403.94	32.311570	-103.656608
4,700.00	7.64	78.48	4,684.99	48.30	236.88	477,744.13	750,416.96	32.311577	-103.656566
4,800.00	7.64	78.48	4,784.11	50.95	249.90	477,746.79	750,429.99	32.311584	-103.656524
4,900.00	7.64	78.48	4,883.22	53.61	262.93	477,749.44	750,443.01	32.311591	-103.656481

Planning Report - Geographic

Database: EDM r5000.141_Prod US
Company: WCDSC Permian NM
Project: Lea County (NAD83 New Mexico East)
Site: Sec 15-T23S-R32E
Well: Grumpy Cat 15-22 Fed Com 214H
Wellbore: Wellbore #1
Design: Permit Plan 1

Local Co-ordinate Reference Well Grumpy Cat 15-22 Fed Com 214H
TVD Reference: RKB @ 3728.80ft
MD Reference: RKB @ 3728.80ft
North Reference: Grid
Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
5,000.00	7.64	78.48	4,982.33	56.27	275.95	477,752.10	750,456.04	32.311598	-103.656439
5,100.00	7.64	78.48	5,081.44	58.92	288.98	477,754.75	750,469.06	32.311605	-103.656397
5,200.00	7.64	78.48	5,180.56	61.58	302.00	477,757.41	750,482.09	32.311612	-103.656355
5,300.00	7.64	78.48	5,279.67	64.23	315.03	477,760.06	750,495.11	32.311620	-103.656313
5,400.00	7.64	78.48	5,378.78	66.89	328.05	477,762.72	750,508.14	32.311627	-103.656270
5,500.00	7.64	78.48	5,477.89	69.55	341.08	477,765.38	750,521.16	32.311634	-103.656228
5,600.00	7.64	78.48	5,577.01	72.20	354.10	477,768.03	750,534.19	32.311641	-103.656186
5,700.00	7.64	78.48	5,676.12	74.86	367.13	477,770.69	750,547.21	32.311648	-103.656144
5,800.00	7.64	78.48	5,775.23	77.51	380.15	477,773.34	750,560.24	32.311655	-103.656102
5,900.00	7.64	78.48	5,874.34	80.17	393.18	477,776.00	750,573.26	32.311662	-103.656059
6,000.00	7.64	78.48	5,973.46	82.82	406.20	477,778.65	750,586.29	32.311669	-103.656017
6,100.00	7.64	78.48	6,072.57	85.48	419.23	477,781.31	750,599.31	32.311676	-103.655975
6,200.00	7.64	78.48	6,171.68	88.14	432.25	477,783.97	750,612.34	32.311683	-103.655933
6,300.00	7.64	78.48	6,270.79	90.79	445.28	477,786.62	750,625.36	32.311690	-103.655890
6,400.00	7.64	78.48	6,369.91	93.45	458.30	477,789.28	750,638.39	32.311697	-103.655848
6,500.00	7.64	78.48	6,469.02	96.10	471.33	477,791.93	750,651.41	32.311704	-103.655806
6,600.00	7.64	78.48	6,568.13	98.76	484.35	477,794.59	750,664.44	32.311711	-103.655764
6,700.00	7.64	78.48	6,667.24	101.41	497.38	477,797.25	750,677.47	32.311719	-103.655722
6,800.00	7.64	78.48	6,766.36	104.07	510.40	477,799.90	750,690.49	32.311726	-103.655679
6,900.00	7.64	78.48	6,865.47	106.73	523.43	477,802.56	750,703.52	32.311733	-103.655637
7,000.00	7.64	78.48	6,964.58	109.38	536.45	477,805.21	750,716.54	32.311740	-103.655595
7,100.00	7.64	78.48	7,063.69	112.04	549.48	477,807.87	750,729.57	32.311747	-103.655553
7,200.00	7.64	78.48	7,162.81	114.69	562.50	477,810.52	750,742.59	32.311754	-103.655511
7,300.00	7.64	78.48	7,261.92	117.35	575.53	477,813.18	750,755.62	32.311761	-103.655468
7,400.00	7.64	78.48	7,361.03	120.01	588.56	477,815.84	750,768.64	32.311768	-103.655426
7,500.00	7.64	78.48	7,460.14	122.66	601.58	477,818.49	750,781.67	32.311775	-103.655384
7,532.38	7.64	78.48	7,492.24	123.52	605.80	477,819.35	750,785.88	32.311777	-103.655370
EOH									
7,600.00	6.62	78.48	7,559.33	125.20	614.02	477,821.03	750,794.11	32.311782	-103.655344
7,700.00	5.12	78.48	7,658.81	127.24	624.05	477,823.07	750,804.14	32.311787	-103.655311
7,800.00	3.62	78.48	7,758.51	128.77	631.53	477,824.60	750,811.61	32.311791	-103.655287
7,900.00	2.12	78.48	7,858.38	129.77	636.44	477,825.60	750,816.53	32.311794	-103.655271
8,000.00	0.62	78.48	7,958.35	130.25	638.79	477,826.08	750,818.88	32.311795	-103.655263
8,041.65	0.00	0.00	8,000.00	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
Drop to Vertical									
8,100.00	0.00	0.00	8,058.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,200.00	0.00	0.00	8,158.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,300.00	0.00	0.00	8,258.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,400.00	0.00	0.00	8,358.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,500.00	0.00	0.00	8,458.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,600.00	0.00	0.00	8,558.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,700.00	0.00	0.00	8,658.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,800.00	0.00	0.00	8,758.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
8,900.00	0.00	0.00	8,858.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,000.00	0.00	0.00	8,958.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,100.00	0.00	0.00	9,058.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,200.00	0.00	0.00	9,158.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,300.00	0.00	0.00	9,258.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,400.00	0.00	0.00	9,358.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,500.00	0.00	0.00	9,458.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,600.00	0.00	0.00	9,558.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,700.00	0.00	0.00	9,658.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
9,800.00	0.00	0.00	9,758.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263

Planning Report - Geographic

Database: EDM r5000.141_Prod US
Company: WCDSC Permian NM
Project: Lea County (NAD83 New Mexico East)
Site: Sec 15-T23S-R32E
Well: Grumpy Cat 15-22 Fed Com 214H
Wellbore: Wellbore #1
Design: Permit Plan 1

Local Co-ordinate Reference Well Grumpy Cat 15-22 Fed Com 214H
TVD Reference: RKB @ 3728.80ft
MD Reference: RKB @ 3728.80ft
North Reference: Grid
Survey Calculation Method: Minimum Curvature

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude Longitude		
9,900.00	0.00	0.00	9,858.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263	
10,000.00	0.00	0.00	9,958.35	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263	
10,013.69	0.00	0.00	9,972.04	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263	
KOP @ 10014' MD, 50' FNL, 400' FEL										
10,100.00	8.63	179.62	10,058.02	123.81	639.06	477,819.64	750,819.14	32.311778	-103.655263	
10,200.00	18.63	179.62	10,155.08	100.27	639.21	477,796.10	750,819.30	32.311713	-103.655263	
10,300.00	28.63	179.62	10,246.58	60.24	639.47	477,756.07	750,819.56	32.311603	-103.655263	
10,400.00	38.63	179.62	10,329.74	4.92	639.84	477,700.75	750,819.92	32.311451	-103.655263	
10,500.00	48.63	179.62	10,402.03	-63.99	640.29	477,631.84	750,820.37	32.311261	-103.655262	
10,600.00	58.63	179.62	10,461.25	-144.41	640.82	477,551.43	750,820.90	32.311040	-103.655262	
10,612.33	59.86	179.62	10,467.56	-155.00	640.88	477,540.83	750,820.97	32.311011	-103.655262	
1st Take Point @ 10612' MD, 330' FNL, 400' FEL										
10,700.00	68.63	179.62	10,505.61	-233.89	641.40	477,461.95	750,821.49	32.310794	-103.655262	
10,800.00	78.63	179.62	10,533.76	-329.71	642.03	477,366.12	750,822.12	32.310531	-103.655262	
10,900.00	88.63	179.62	10,544.84	-428.96	642.68	477,266.87	750,822.77	32.310258	-103.655262	
10,913.69	90.00	179.62	10,545.00	-442.65	642.77	477,253.18	750,822.86	32.310221	-103.655262	
Land Point										
11,000.00	90.00	179.62	10,545.00	-528.96	643.34	477,166.87	750,823.42	32.309983	-103.655262	
11,100.00	90.00	179.62	10,545.00	-628.96	643.99	477,066.88	750,824.08	32.309708	-103.655262	
11,200.00	90.00	179.62	10,545.00	-728.95	644.65	476,966.88	750,824.73	32.309434	-103.655262	
11,300.00	90.00	179.62	10,545.00	-828.95	645.31	476,866.88	750,825.39	32.309159	-103.655262	
11,400.00	90.00	179.62	10,545.00	-928.95	645.96	476,766.88	750,826.05	32.308884	-103.655262	
11,500.00	90.00	179.62	10,545.00	-1,028.95	646.62	476,666.88	750,826.70	32.308609	-103.655262	
11,600.00	90.00	179.62	10,545.00	-1,128.95	647.27	476,566.89	750,827.36	32.308334	-103.655262	
11,700.00	90.00	179.62	10,545.00	-1,228.94	647.93	476,466.89	750,828.01	32.308059	-103.655262	
11,800.00	90.00	179.62	10,545.00	-1,328.94	648.58	476,366.89	750,828.67	32.307784	-103.655262	
11,900.00	90.00	179.62	10,545.00	-1,428.94	649.24	476,266.89	750,829.33	32.307509	-103.655261	
12,000.00	90.00	179.62	10,545.00	-1,528.94	649.90	476,166.90	750,829.98	32.307235	-103.655261	
12,100.00	90.00	179.62	10,545.00	-1,628.94	650.55	476,066.90	750,830.64	32.306960	-103.655261	
12,200.00	90.00	179.62	10,545.00	-1,728.93	651.21	475,966.90	750,831.29	32.306685	-103.655261	
12,300.00	90.00	179.62	10,545.00	-1,828.93	651.86	475,866.90	750,831.95	32.306410	-103.655261	
12,400.00	90.00	179.62	10,545.00	-1,928.93	652.52	475,766.91	750,832.61	32.306135	-103.655261	
12,500.00	90.00	179.62	10,545.00	-2,028.93	653.18	475,666.91	750,833.26	32.305860	-103.655261	
12,600.00	90.00	179.62	10,545.00	-2,128.92	653.83	475,566.91	750,833.92	32.305585	-103.655261	
12,700.00	90.00	179.62	10,545.00	-2,228.92	654.49	475,466.91	750,834.57	32.305310	-103.655261	
12,800.00	90.00	179.62	10,545.00	-2,328.92	655.14	475,366.91	750,835.23	32.305036	-103.655261	
12,900.00	90.00	179.62	10,545.00	-2,428.92	655.80	475,266.92	750,835.88	32.304761	-103.655261	
13,000.00	90.00	179.62	10,545.00	-2,528.92	656.46	475,166.92	750,836.54	32.304486	-103.655261	
13,100.00	90.00	179.62	10,545.00	-2,628.91	657.11	475,066.92	750,837.20	32.304211	-103.655261	
13,200.00	90.00	179.62	10,545.00	-2,728.91	657.77	474,966.92	750,837.85	32.303936	-103.655260	
13,300.00	90.00	179.62	10,545.00	-2,828.91	658.42	474,866.93	750,838.51	32.303661	-103.655260	
13,400.00	90.00	179.62	10,545.00	-2,928.91	659.08	474,766.93	750,839.16	32.303386	-103.655260	
13,500.00	90.00	179.62	10,545.00	-3,028.91	659.73	474,666.93	750,839.82	32.303111	-103.655260	
13,600.00	90.00	179.62	10,545.00	-3,128.90	660.39	474,566.93	750,840.48	32.302837	-103.655260	
13,700.00	90.00	179.62	10,545.00	-3,228.90	661.05	474,466.94	750,841.13	32.302562	-103.655260	
13,800.00	90.00	179.62	10,545.00	-3,328.90	661.70	474,366.94	750,841.79	32.302287	-103.655260	
13,900.00	90.00	179.62	10,545.00	-3,428.90	662.36	474,266.94	750,842.44	32.302012	-103.655260	
14,000.00	90.00	179.62	10,545.00	-3,528.89	663.01	474,166.94	750,843.10	32.301737	-103.655260	
14,100.00	90.00	179.62	10,545.00	-3,628.89	663.67	474,066.95	750,843.76	32.301462	-103.655260	
14,200.00	90.00	179.62	10,545.00	-3,728.89	664.33	473,966.95	750,844.41	32.301187	-103.655260	
14,300.00	90.00	179.62	10,545.00	-3,828.89	664.98	473,866.95	750,845.07	32.300913	-103.655260	
14,400.00	90.00	179.62	10,545.00	-3,928.89	665.64	473,766.95	750,845.72	32.300638	-103.655260	
14,500.00	90.00	179.62	10,545.00	-4,028.88	666.29	473,666.95	750,846.38	32.300363	-103.655259	

Planning Report - Geographic

Database:	EDM r5000.141_Prod US	Local Co-ordinate Reference	Well Grumpy Cat 15-22 Fed Com 214H
Company:	WCDSC Permian NM	TVD Reference:	RKB @ 3728.80ft
Project:	Lea County (NAD83 New Mexico East)	MD Reference:	RKB @ 3728.80ft
Site:	Sec 15-T23S-R32E	North Reference:	Grid
Well:	Grumpy Cat 15-22 Fed Com 214H	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Permit Plan 1		

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Map Northing (usft)	Map Easting (usft)	Latitude	Longitude
14,600.00	90.00	179.62	10,545.00	-4,128.88	666.95	473,566.96	750,847.03	32.300088	-103.655259
14,700.00	90.00	179.62	10,545.00	-4,228.88	667.60	473,466.96	750,847.69	32.299813	-103.655259
14,800.00	90.00	179.62	10,545.00	-4,328.88	668.26	473,366.96	750,848.35	32.299538	-103.655259
14,900.00	90.00	179.62	10,545.00	-4,428.88	668.92	473,266.96	750,849.00	32.299263	-103.655259
15,000.00	90.00	179.62	10,545.00	-4,528.87	669.57	473,166.97	750,849.66	32.298988	-103.655259
15,100.00	90.00	179.62	10,545.00	-4,628.87	670.23	473,066.97	750,850.31	32.298714	-103.655259
15,200.00	90.00	179.62	10,545.00	-4,728.87	670.88	472,966.97	750,850.97	32.298439	-103.655259
15,243.83	90.00	179.62	10,545.00	-4,772.69	671.17	472,923.15	750,851.26	32.298318	-103.655259
PBHL; 330' FSL, 400' FEL									

Design Targets

Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (usft)	Easting (usft)	Latitude	Longitude
- hit/miss target									
- Shape									
PBHL - Grumpy Cat 214	0.00	0.00	0.00	-4,772.69	671.17	472,923.15	750,851.26	32.298318	-103.655259
- plan misses target center by 4819.65ft at 0.00ft MD (0.00 TVD, 0.00 N, 0.00 E)									
- Point									
Vertical Point - Grumpy Cat	0.00	0.00	8,000.00	130.29	639.01	477,826.12	750,819.10	32.311795	-103.655263
- plan hits target center									
- Point									

Plan Annotations

Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment
		+N/-S (ft)	+E/-W (ft)	
2,500.00	2,500.00	0.00	0.00	Begin Nudge
3,263.90	3,261.64	10.16	49.82	EOB
7,532.38	7,492.24	123.52	605.80	EOH
8,041.65	8,000.00	130.29	639.01	Drop to Vertical
10,013.69	9,972.04	130.29	639.01	KOP @ 10014' MD, 50' FNL, 400' FEL
10,612.33	10,467.56	-155.00	640.88	1st Take Point @ 10612' MD, 330' FNL, 400' FEL
10,913.69	10,545.00	-442.65	642.77	Land Point
15,243.83	10,545.00	-4,772.69	671.17	PBHL; 330' FSL, 400' FEL

WCDSC Permian NM

Lea County (NAD83 New Mexico East)

Sec 15-T23S-R32E

Grumpy Cat 15 Fed Com 214H

Wellbore #1

Permit Plan 1

Anticollision Report

09 May, 2018

Anticollision Report

Company:	WCDSC Permian NM	Local Co-ordinate Reference	Well Grumpy Cat 15-22 Fed Com 214H
Project:	Lea County (NAD83 New Mexico East)	TVD Reference:	RKB @ 3728.80ft
Reference Site:	Sec 15-T23S-R32E	MD Reference:	RKB @ 3728.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Grumpy Cat 15-22 Fed Com 214H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

Reference	Permit Plan 1
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria
Interpolation Method	MD Interval 100.00ft
Depth Range:	Unlimited
Results Limited by:	Maximum center-center distance of 1,500.00 ft
Warning Levels Evaluated at:	2.00 Sigma
Error Model:	ISCWSA
Scan Method:	Closest Approach 3D
Error Surface:	Pedal Curve
Casing Method:	Not applied

Survey Tool Program	Date	5/9/2018		
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description
0.00	15,243.83	Permit Plan 1 (Wellbore #1)	MWD+HDGM	OWSG MWD + HDGM

Site Name	Reference Measure	Offset Measure	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Separation	Warning
Offset Well - Wellbore - Design						
Sec 15-T23S-R32E						
Codomiz Fed #003 (P&A) - Wellbore #1 - Wellbore #1						Out of range
Grumpy Cat 15-22 Fed Com 211H - Wellbore #1 - Permit						Out of range
Grumpy Cat 15-22 Fed Com 212H - Wellbore #1 - Permit						Out of range
Grumpy Cat 15-22 Fed Com 213H - Wellbore #1 - Permit	2,500.00	2,500.00	30.04	12.54	1.716	Minor Risk, CC, ES, SF
Pre-Ongard Well #001 (P&A) - Wellbore #1 - Wellbore #1						Out of range
Tomcat 15 Fed #002 (P&A) - Wellbore #1 - Wellbore #1						Out of range
Tomcat 15 Fed Com #001 (Active) - Wellbore #1 - Wellbo						Out of range
Tomcat 15 Federal #003 SWD (Active) - Wellbore #1 - W						Out of range
Sec 22-T23S-R32E						
Avion Federal #002 (Active) - Wellbore #1 - Wellbore #1						Out of range
Avion Federal #003 (Active) - Wellbore #1 - Wellbore #1						Out of range

Offset Design	Sec 15-T23S-R32E - Grumpy Cat 15-22 Fed Com 213H - Wellbore #1 - Permit Plan 1	Offset Site Error:	0.00 ft								
Survey Program:	O-MWD+HDGM	Offset Well Error:	0.50 ft								
Reference	Offset	Semi Major Axis	Distance								
Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
0.00	0.00	0.00	0.00	0.50	0.50	-90.53	-0.28	-30.04	30.04		
100.00	100.00	100.00	100.00	0.52	0.52	-90.53	-0.28	-30.04	30.04	1.04	29.011
200.00	200.00	200.00	200.00	0.70	0.70	-90.53	-0.28	-30.04	30.04	28.64	1.40 21.394
300.00	300.00	300.00	300.00	0.99	0.99	-90.53	-0.28	-30.04	30.04	28.07	1.97 15.213
400.00	400.00	400.00	400.00	1.31	1.31	-90.53	-0.28	-30.04	30.04	27.42	2.62 11.474
500.00	500.00	500.00	500.00	1.65	1.65	-90.53	-0.28	-30.04	30.04	26.75	3.29 9.125
600.00	600.00	600.00	600.00	1.99	1.99	-90.53	-0.28	-30.04	30.04	26.06	3.98 7.546
700.00	700.00	700.00	700.00	2.34	2.34	-90.53	-0.28	-30.04	30.04	25.36	4.68 6.421
800.00	800.00	800.00	800.00	2.69	2.69	-90.53	-0.28	-30.04	30.04	24.66	5.38 5.583
900.00	900.00	900.00	900.00	3.04	3.04	-90.53	-0.28	-30.04	30.04	23.95	6.09 4.935 Alert
1,000.00	1,000.00	1,000.00	1,000.00	3.40	3.40	-90.53	-0.28	-30.04	30.04	23.25	6.80 4.421 Alert
1,100.00	1,100.00	1,100.00	1,100.00	3.75	3.75	-90.53	-0.28	-30.04	30.04	22.54	7.51 4.003 Alert
1,200.00	1,200.00	1,200.00	1,200.00	4.11	4.11	-90.53	-0.28	-30.04	30.04	21.83	8.22 3.656 Alert
1,300.00	1,300.00	1,300.00	1,300.00	4.46	4.46	-90.53	-0.28	-30.04	30.04	21.11	8.93 3.365 Alert
1,400.00	1,400.00	1,400.00	1,400.00	4.82	4.82	-90.53	-0.28	-30.04	30.04	20.40	9.64 3.116 Alert

CC = Min centres to center distance or convergent point SF = min separation factor ES = min ellipse separation

Anticollision Report

Company: WCDSC Permian NM
Project: Lea County (NAD83 New Mexico East)
Reference Site: Sec 15-T23S-R32E
Site Error: 0.00 ft
Reference Well: Grumpy Cat 15-22 Fed Com 214H
Well Error: 0.50 ft
Reference Wellbore: Wellbore #1
Reference Design: Permit Plan 1

Local Co-ordinate Reference
TVD Reference: RKB @ 3728.80ft
MD Reference: RKB @ 3728.80ft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Output errors are at 2.00 sigma
Database: EDM r5000.141_Prod US
Offset TVD Reference: Offset Datum

Offset Design Sec 15-T23S-R32E - Grumpy Cat 15-22 Fed Com 213H - Wellbore #1 - Permit Plan 1													Offset Site Error:
Survey Program: 0-MWD+HDGM													Offset Well Error:
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
1,500.00	1,500.00	1,500.00	1,500.00	5.18	5.18	-90.53	-0.28	-30.04	30.04	18.69	10.35	2.901	Alert
1,600.00	1,600.00	1,600.00	1,600.00	5.53	5.53	-90.53	-0.28	-30.04	30.04	18.97	11.07	2.714	Alert
1,700.00	1,700.00	1,700.00	1,700.00	5.89	5.89	-90.53	-0.28	-30.04	30.04	18.26	11.78	2.550	Alert
1,800.00	1,800.00	1,800.00	1,800.00	6.25	6.25	-90.53	-0.28	-30.04	30.04	17.54	12.50	2.404	Minor Risk
1,900.00	1,900.00	1,900.00	1,900.00	6.61	6.61	-90.53	-0.28	-30.04	30.04	16.83	13.21	2.274	Minor Risk
2,000.00	2,000.00	2,000.00	2,000.00	6.96	6.96	-90.53	-0.28	-30.04	30.04	16.11	13.93	2.157	Minor Risk
2,100.00	2,100.00	2,100.00	2,100.00	7.32	7.32	-90.53	-0.28	-30.04	30.04	15.40	14.64	2.052	Minor Risk
2,200.00	2,200.00	2,200.00	2,200.00	7.68	7.68	-90.53	-0.28	-30.04	30.04	14.68	15.36	1.956	Minor Risk
2,300.00	2,300.00	2,300.00	2,300.00	8.04	8.04	-90.53	-0.28	-30.04	30.04	13.97	16.07	1.869	Minor Risk
2,400.00	2,400.00	2,400.00	2,400.00	8.39	8.39	-90.53	-0.28	-30.04	30.04	13.25	16.79	1.789	Minor Risk
2,500.00	2,500.00	2,500.00	2,500.00	8.75	8.75	-90.53	-0.28	-30.04	30.04	12.54	17.50	1.716	Minor Risk, CC, ES, SF
2,600.00	2,599.99	2,599.46	2,599.45	9.10	9.10	-169.07	-0.16	-30.89	31.76	13.56	18.20	1.745	Minor Risk
2,700.00	2,699.96	2,698.73	2,698.69	9.45	9.44	-169.23	0.20	-33.45	36.90	18.02	18.88	1.954	Minor Risk
2,800.00	2,799.86	2,797.67	2,797.53	9.79	9.78	-169.40	0.80	-37.69	45.45	25.90	19.55	2.325	Minor Risk
2,900.00	2,899.68	2,896.08	2,895.76	10.14	10.13	-169.56	1.63	-43.59	57.41	37.19	20.22	2.838	Alert
3,000.00	2,999.37	2,993.80	2,993.19	10.49	10.47	-169.67	2.69	-51.10	72.74	51.86	20.88	3.484	Alert
3,100.00	3,098.90	3,090.67	3,089.62	10.85	10.81	-169.76	3.98	-60.16	91.42	69.89	21.53	4.246	Alert
3,200.00	3,198.26	3,186.53	3,184.89	11.20	11.15	-169.81	5.47	-70.72	113.40	91.22	22.17	5.114	
3,300.00	3,297.42	3,281.27	3,278.85	11.56	11.49	-169.86	7.16	-82.70	138.53	115.73	22.80	6.075	
3,400.00	3,396.53	3,375.09	3,371.69	11.92	11.83	-169.84	9.05	-96.08	165.57	142.15	23.43	7.068	
3,500.00	3,495.64	3,468.04	3,463.44	12.29	12.17	-169.74	11.13	-110.82	194.16	170.12	24.04	8.077	
3,600.00	3,594.76	3,561.47	3,555.43	12.65	12.52	-169.61	13.42	-127.00	224.15	199.48	24.67	9.085	
3,700.00	3,693.87	3,656.78	3,649.22	13.02	12.88	-169.50	15.79	-143.78	254.43	229.08	25.35	10.038	
3,800.00	3,792.98	3,752.08	3,743.01	13.39	13.24	-169.41	18.16	-160.56	284.70	258.68	26.02	10.940	
3,900.00	3,892.09	3,847.39	3,836.79	13.77	13.61	-169.34	20.53	-177.34	314.98	288.27	26.71	11.795	
4,000.00	3,991.21	3,942.70	3,930.58	14.14	13.98	-169.28	22.90	-194.12	345.25	317.87	27.39	12.606	
4,100.00	4,090.32	4,038.00	4,024.37	14.52	14.35	-169.23	25.27	-210.90	375.53	347.46	28.07	13.378	
4,200.00	4,189.43	4,133.31	4,118.16	14.89	14.72	-169.19	27.64	-227.68	405.81	377.05	28.76	14.111	
4,300.00	4,288.54	4,228.61	4,211.94	15.27	15.10	-169.15	30.01	-244.46	436.08	406.64	29.44	14.810	
4,400.00	4,387.66	4,323.92	4,305.73	15.65	15.48	-169.12	32.38	-261.24	466.36	436.23	30.13	15.476	
4,500.00	4,486.77	4,419.23	4,399.52	16.03	15.86	-169.09	34.75	-278.02	496.64	465.81	30.82	16.112	
4,600.00	4,585.88	4,514.53	4,493.31	16.41	16.24	-169.06	37.12	-294.80	526.91	495.40	31.52	16.718	
4,700.00	4,684.99	4,609.84	4,587.09	16.80	16.63	-169.04	39.49	-311.58	557.19	524.98	32.21	17.299	
4,800.00	4,784.11	4,705.14	4,680.88	17.18	17.01	-169.02	41.86	-328.36	587.47	554.56	32.90	17.854	
4,900.00	4,883.22	4,800.45	4,774.67	17.57	17.40	-169.00	44.23	-345.14	617.75	584.15	33.60	18.385	
5,000.00	4,982.33	4,895.76	4,868.46	17.95	17.79	-168.99	46.60	-361.91	648.02	613.73	34.30	18.894	
5,100.00	5,081.44	4,991.06	4,962.24	18.34	18.18	-168.97	48.98	-378.69	678.30	643.31	35.00	19.383	
5,200.00	5,180.56	5,086.37	5,056.03	18.72	18.57	-168.96	51.35	-395.47	708.58	672.88	35.69	19.851	
5,300.00	5,279.67	5,181.67	5,149.82	19.11	18.97	-168.95	53.72	-412.25	738.86	702.46	36.39	20.302	
5,400.00	5,378.78	5,276.98	5,243.60	19.50	19.36	-168.94	56.09	-429.03	769.13	732.04	37.09	20.734	
5,500.00	5,477.89	5,372.29	5,337.39	19.89	19.76	-168.93	58.46	-445.81	799.41	761.62	37.80	21.151	
5,600.00	5,577.01	5,467.59	5,431.18	20.28	20.15	-168.92	60.83	-462.59	829.69	791.19	38.50	21.551	
5,700.00	5,676.12	5,562.90	5,524.97	20.67	20.55	-168.91	63.20	-479.37	859.97	820.77	39.20	21.937	
5,800.00	5,775.23	5,658.20	5,618.75	21.06	20.95	-168.90	65.57	-496.15	890.24	850.34	39.91	22.309	
5,900.00	5,874.34	5,753.51	5,712.54	21.45	21.35	-168.89	67.94	-512.93	920.52	879.91	40.61	22.667	
6,000.00	5,973.46	5,848.82	5,806.33	21.84	21.75	-168.88	70.31	-529.71	950.80	909.48	41.32	23.013	
6,100.00	6,072.57	5,944.12	5,900.12	22.23	22.15	-168.88	72.68	-546.49	981.08	939.06	42.02	23.347	
6,200.00	6,171.68	6,039.43	5,993.90	22.62	22.55	-168.87	75.05	-563.27	1,011.36	968.63	42.73	23.670	
6,300.00	6,270.79	6,134.74	6,087.69	23.02	22.95	-168.86	77.42	-580.05	1,041.63	998.20	43.43	23.982	
6,400.00	6,369.91	6,230.04	6,181.48	23.41	23.35	-168.86	79.79	-596.83	1,071.91	1,027.77	44.14	24.283	
6,500.00	6,469.02	6,325.35	6,275.27	23.80	23.75	-168.85	82.16	-613.61	1,102.19	1,057.34	44.85	24.575	

CC - Min centre to center distance or coverdient point SF - min separation factor ES - min ellipse separation

Anticollision Report

Company:	WCDSC Permian NM	Local Co-ordinate Reference	Well Grumpy Cat 15-22 Fed Com 214H
Project:	Lea County (NAD83 New Mexico East)	TVD Reference:	RKB @ 3728.80ft
Reference Site:	Sec 15-T23S-R32E	MD Reference:	RKB @ 3728.80ft
Site Error:	0.00 ft	North Reference:	Grid
Reference Well:	Grumpy Cat 15-22 Fed Com 214H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.50 ft	Output errors are at	2.00 sigma
Reference Wellbore	Wellbore #1	Database:	EDM r5000.141_Prod US
Reference Design:	Permit Plan 1	Offset TVD Reference:	Offset Datum

Offset Design Sec 15-T23S-R32E - Grumpy Cat 15-22 Fed Com 213H - Wellbore #1 - Permit Plan 1													Offset Site Error:	0.00 ft
Survey Program: 0-MWD+HDGM													Offset Well Error:	0.50 ft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth	Vertical Depth	Measured Depth	Vertical Depth	Reference	Offset	Highside Toolface	Offset Wellbore Centre		Between Centres	Between Ellipses	Minimum Separation	Separation Factor		
(ft)	(ft)	(ft)	(ft)	(ft)	(ft)	(°)	+N/-S (ft)	+E/-W (ft)	(ft)	(ft)	(ft)			
6,600.00	6,568.13	6,420.65	6,369.05	24.19	24.16	-168.85	84.53	-630.39	1,132.47	1,086.91	45.56	24.857		
6,700.00	6,667.24	6,515.96	6,462.84	24.59	24.56	-168.84	86.90	-647.17	1,162.74	1,116.48	46.27	25.130		
6,800.00	6,766.36	6,611.27	6,556.63	24.98	24.97	-168.84	89.27	-663.95	1,193.02	1,146.04	46.98	25.395		
6,900.00	6,865.47	6,706.57	6,650.42	25.38	25.37	-168.83	91.64	-680.72	1,223.30	1,175.61	47.69	25.652		
7,000.00	6,964.58	6,801.88	6,744.20	25.77	25.78	-168.83	94.01	-697.50	1,253.58	1,205.18	48.40	25.901		
7,100.00	7,063.69	6,902.82	6,837.99	26.16	26.21	-168.82	96.38	-714.28	1,283.86	1,234.72	49.13	26.131		
7,200.00	7,162.81	7,007.51	6,931.78	26.56	26.65	-168.82	98.76	-731.06	1,314.13	1,264.25	49.88	26.347		
7,300.00	7,261.92	7,087.80	7,025.57	26.95	27.00	-168.82	101.13	-747.84	1,344.41	1,293.88	50.53	26.604		
7,400.00	7,361.03	7,183.10	7,119.35	27.35	27.40	-168.81	103.50	-764.62	1,374.69	1,323.44	51.25	26.825		
7,500.00	7,460.14	7,278.41	7,213.14	27.75	27.81	-168.81	105.87	-781.40	1,404.97	1,353.01	51.96	27.039		
7,600.00	7,559.33	7,373.89	7,307.10	28.14	28.22	-168.86	108.24	-798.21	1,434.68	1,382.01	52.67	27.237		
7,700.00	7,658.81	7,520.08	7,451.34	28.52	28.83	-168.91	111.56	-821.72	1,460.66	1,406.87	53.79	27.156		
7,800.00	7,758.51	7,678.43	7,608.48	28.89	29.46	-168.95	114.29	-841.01	1,480.24	1,425.32	54.92	26.955		
7,900.00	7,858.38	7,839.64	7,769.14	29.25	30.05	-168.97	116.13	-854.02	1,493.19	1,437.22	55.97	26.677		
8,000.00	7,958.35	8,002.56	7,931.92	29.60	30.62	-168.98	117.02	-860.33	1,499.42	1,442.47	56.95	26.329		

Anticollision Report


Company: WCDSC Permian NM
Project: Lea County (NAD83 New Mexico East)
Reference Site: Sec 15-T23S-R32E
Site Error: 0.00 ft
Reference Well: Grumpy Cat 15-22 Fed Com 214H
Well Error: 0.50 ft
Reference Wellbore: Wellbore #1
Reference Design: Permit Plan 1

Local Co-ordinate Reference
TVD Reference: RKB @ 3728.80ft
MD Reference: RKB @ 3728.80ft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Output errors are at 2.00 sigma
Database: EDM r5000.141_Prod US
Offset TVD Reference: Offset Datum

Reference Depths are relative to RKB @ 3728.80ft
Offset Depths are relative to Offset Datum
Central Meridian is -104.333334

Coordinates are relative to: Grumpy Cat 15-22 Fed Com 214H
Coordinate System is US State Plane 1983, New Mexico Eastern Zone
Grid Convergence at Surface is: 0.36°

Ladder Plot

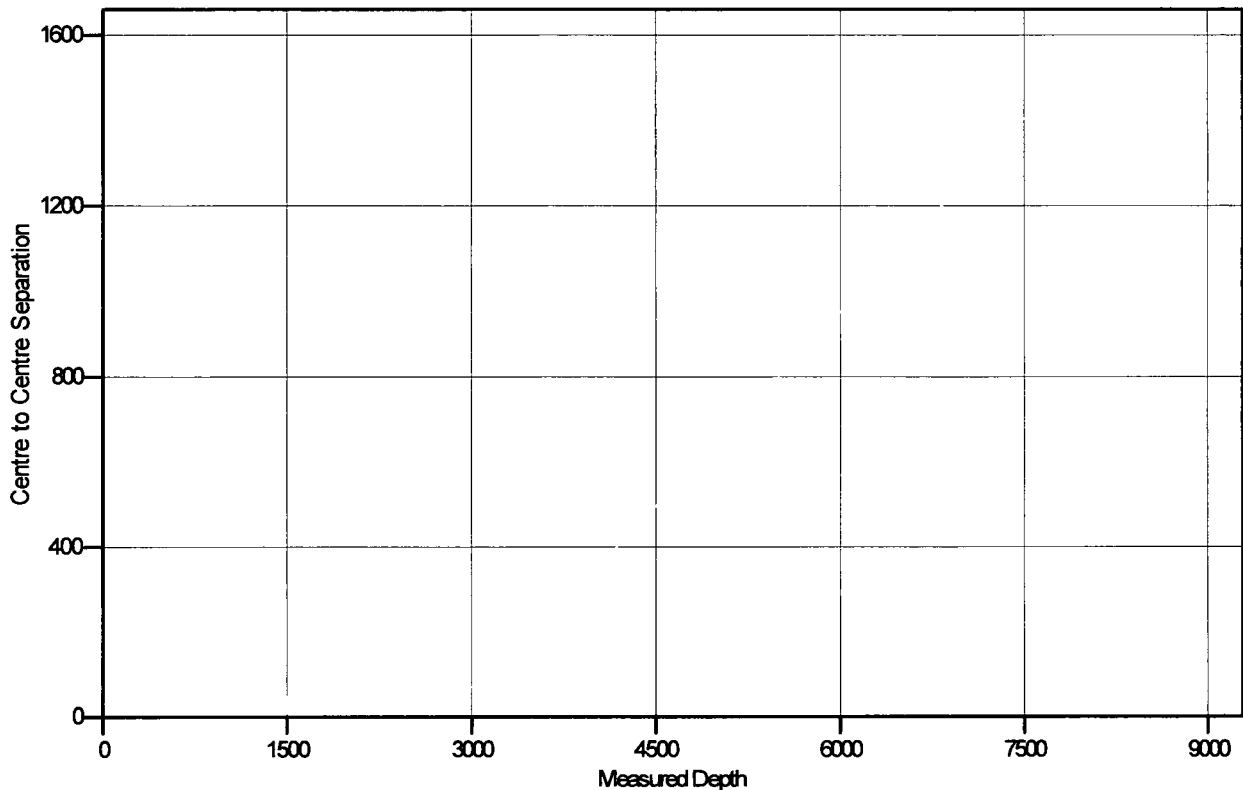

LEGEND

Grumpy Cat 15-22 Fed Com 214H, Wellbore #1, Permit Plan 1 V0

Anticollision Report


Company: WCDSC Permian NM
Project: Lea County (NAD83 New Mexico East)
Reference Site: Sec 15-T23S-R32E
Site Error: 0.00 ft
Reference Well: Grumpy Cat 15-22 Fed Com 214H
Well Error: 0.50 ft
Reference Wellbore: Wellbore #1
Reference Design: Permit Plan 1

Local Co-ordinate Reference
TVD Reference: Well Grumpy Cat 15-22 Fed Com 214H
RKB @ 3728.80ft
MD Reference: RKB @ 3728.80ft
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Output errors are at 2.00 sigma
Database: EDM r5000.141_Prod US
Offset TVD Reference: Offset Datum

Reference Depths are relative to RKB @ 3728.80ft
Offset Depths are relative to Offset Datum
Central Meridian is -104.333334

Coordinates are relative to: Grumpy Cat 15-22 Fed Com 214H
Coordinate System is US State Plane 1983, New Mexico Eastern Zone
Grid Convergence at Surface is: 0.36°

Separation Factor Plot

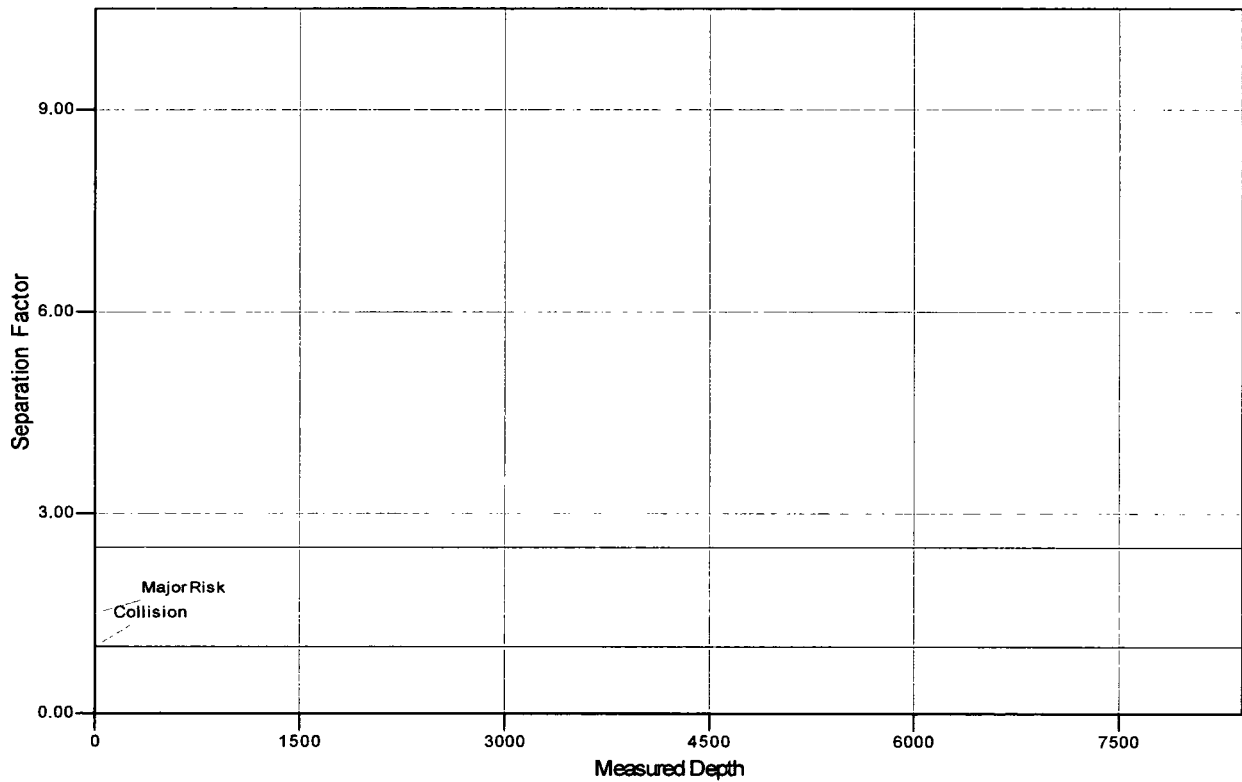

LEGEND

Grumpy Cat 15-22 Fed Com 214H, Wellbore #1, Permit Plan 1 V0

Devon Energy

WELL DETAILS: Grumpy Cat 15 Fed Com 214H




RKB @ 3728.80ft

Northing 477695.83 Easting 750180.09 Latitude 32.311448 Longitude -103.657333

devon

SECTION DETAILS Permit Plan 1

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	V/Sect	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2500.00	0.00	0.00	2500.00	0.00	0.00	0.00	0.00	Begin Nudge
3263.90	7.64	78.48	3261.64	10.16	49.82	1.00	-3.12	EOB
7532.38	7.64	78.48	7492.24	123.52	605.80	0.00	-37.96	EOH
5 8041.65	0.00	0.00	8000.00	130.29	639.01	1.50	-40.04	Drop to Vertical
6 10013.69	0.00	0.00	9972.04	130.29	639.01	0.00	-40.04	KOP @ 10014' MD, 50' FNL, 400' FEL
7 10913.69	90.00	179.62	10545.00	-442.65	642.77	10.00	527.85	Land Point
8 15243.83	90.00	179.62	10545.00	-4772.69	671.17	0.00	4819.65	PBHL: 330' FSL, 400' FEL

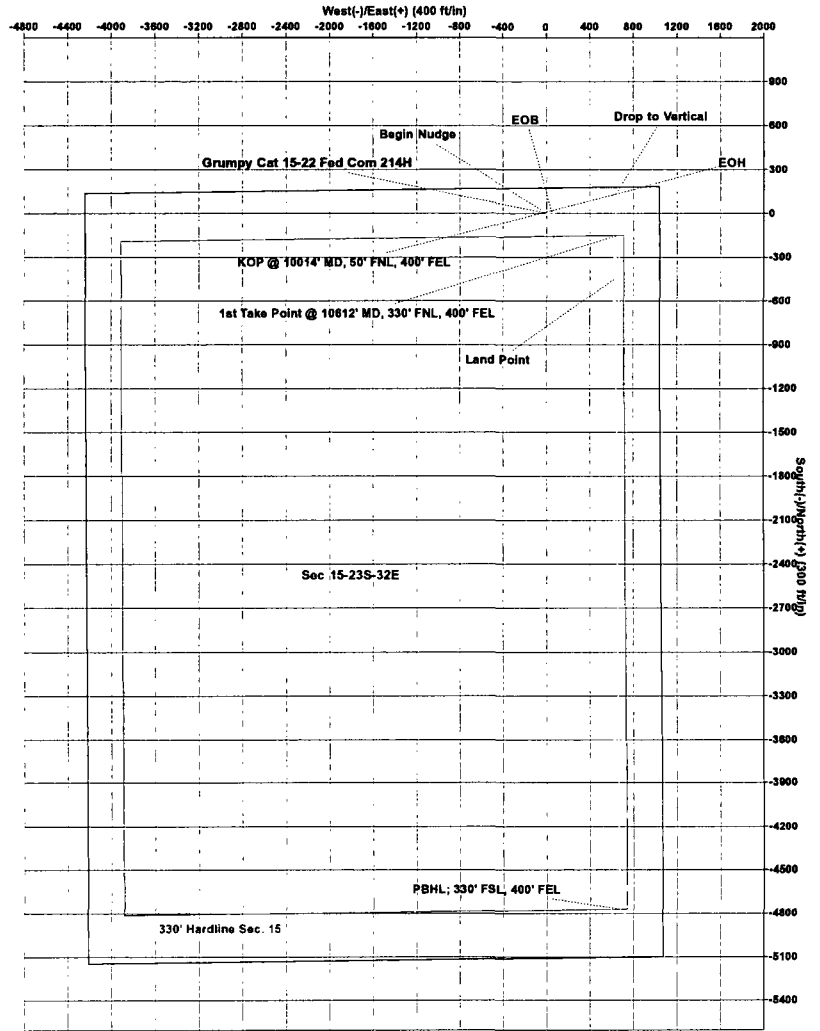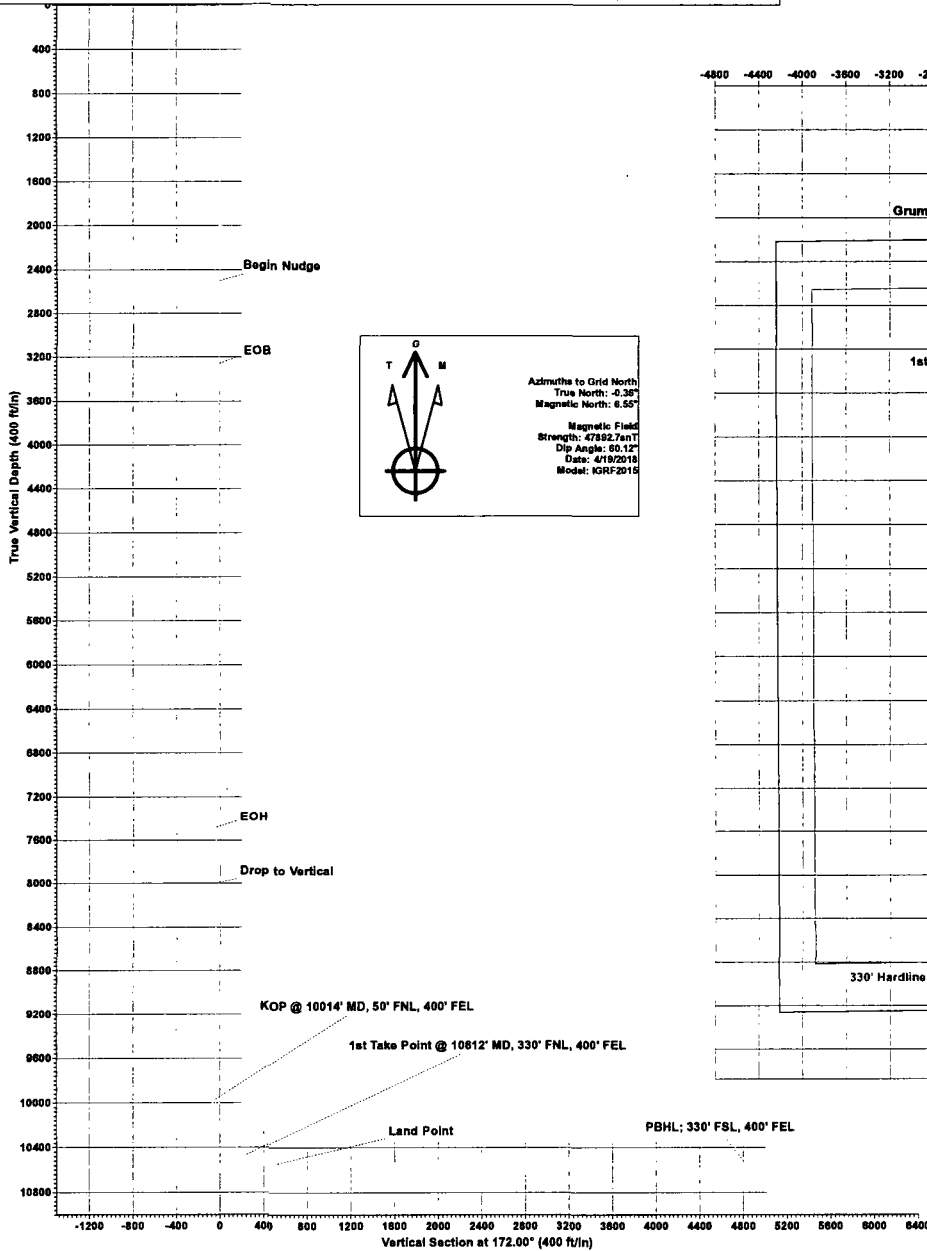



Commitment Runs Deep



Design Plan
Operation and Maintenance Plan
Closure Plan

SENM - Closed Loop Systems
June 2010

I. Design Plan

Devon uses MI SWACO closed loop system (CLS). The MI SWACO CLS is designed to maintain drill solids at or below 5%. The equipment is arranged to progressively remove solids from the largest to the smallest size. Drilling fluids can thus be reused and savings is realized on mud and disposal costs. Dewatering may be required with the centrifuges to insure removal of ultra fine solids.

The drilling location is constructed to allow storm water to flow to a central sump normally the cellar. This insures no contamination leaves the drilling pad in the event of a spill. Storm water is reused in the mud system or stored in a reserve fluid tank farm until it can be reused. All lubricants, oils, or chemicals are removed immediately from the ground to prevent the contamination of storm water. An oil trap is normally installed on the sump if an oil spill occurs during a storm.

A tank farm is utilized to store drilling fluids including fresh water and brine fluids. The tank farm is constructed on a 20 ml plastic lined, bermed pad to prevent the contamination of the drilling site during a spill. Fluids from other sites may be stored in these tanks for processing by the solids control equipment and reused in the mud system. At the end of the well the fluids are transported from the tank farm to an adjoining well or to the next well for the rig.

Prior to installing a closed-loop system on site, the topsoil, if present, will be stripped and stockpiled for use as the final cover or fill at the time of closure.

Signs will be posted on the fence surrounding the closed-loop system unless the closed-loop system is located on a site where there is an existing well, that is operated by Devon.


II. Operations and Maintenance Plan

Primary Shakers: The primary shakers make the first removal of drill solids from the drilling mud as it leaves the well bore. The shakers are sized to handle maximum drilling rate at optimal screen size. The shakers normally remove solids down to 74 microns.

Mud Cleaner: The Mud Cleaner cleans the fluid after it leaves the shakers. A set of hydrocyclones are sized to handle 1.25 to 1.5 times the maximum circulating rate. This ensures all the fluid is being processed to an average cut point of 25 microns. The wet discharged is dewatered on a shaker equipped with ultra fine mesh screens and generally cut at 40 microns.



Closed Loop Schematic

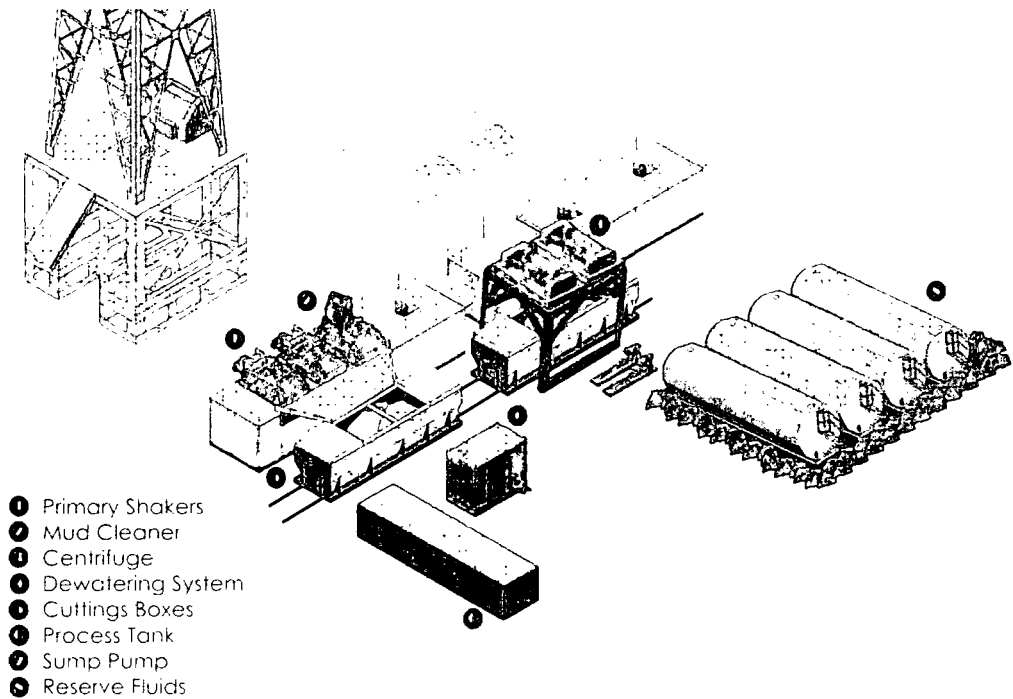

Centrifuges: The centrifuges can be one or two in number depending on the well geometry or depth of well. The centrifuges are sized to maintain low gravity solids at 5% or below. They may or may not need a dewatering system to enhance the removal rates. The centrifuges can make a cut point of 8-10 microns depending on bowl speed, feed rate, solids loading and other factors.

The centrifuge system is designed to work on the active system and be flexible to process incoming fluids from other locations. This set-up is also dependant on well factors.

Dewatering System: The dewatering system is a chemical mixing and dosing system designed to enhance the solids removal of the centrifuge. Not commonly used in shallow wells. It may contain pH adjustment, coagulant mixing and dosing, and polymer mixing and dosing. Chemical flocculation binds ultra fine solids into a mass that is within the centrifuge operating design. The

dewatering system improves the centrifuge cut point to infinity or allows for the return of clear water or brine fluid. This ability allows for the ultimate control of low gravity solids.

Cuttings Boxes: Cuttings boxes are utilized to capture drill solids that are discarded from the solids control equipment. These boxes are set upon a rail system that allows for the removal and replacement of a full box of cuttings with an empty one. They are equipped with a cover that insures no product is spilled into the environment during the transportation phase.

Process Tank: (Optional) The process tank allows for the holding and process of fluids that are being transferred into the mud system. Additionally, during times of lost circulation the process tank may hold active fluids that are removed for additional treatment. It can further be used as a mixing tank during well control conditions.

Sump and Sump Pump: The sump is used to collect storm water and the pump is used to transfer this fluid to the active system or to the tank for to hold in reserve. It can also be used to collect fluids that may escape during spills. The location contains drainage ditches that allow the location fluids to drain to the sump.

Reserve Fluids (Tank Farm): A series of frac tanks are used to replace the reserve pit. These are steel tanks that are equipped with a manifold system and a transfer pump. These tanks can contain any number of fluids used during the drilling process. These can include fresh water, cut brine, and saturated salt fluid. The fluid can be from the active well or reclaimed fluid from other locations. A 20 ml liner and berm system is employed to ensure the fluids do not migrate to the environment during a spill.

If a leak develops, the appropriate division district office will be notified within 48 hours of the discovery and the leak will be addressed. Spill prevention is accomplished by maintaining pump packing, hoses, and pipe fittings to insure no leaks are occurring. During an upset condition the source of the spill is isolated and repaired as soon as it is discovered. Free liquid is removed by a diaphragm pump and returned to the mud system. Loose topsoil may be used to stabilize the spill and the contaminated soil is excavated and placed in the cuttings boxes. After the well is finished and the rig has moved, the entire location is scrapped and testing will be performed to determine if a release has occurred.

All trash is kept in a wire mesh enclosure and removed to an approved landfill when full. All spent motor oils are kept in separate containers and they are removed and sent to an approved recycling center. Any spilled lubricants, pipe

dope, or regulated chemicals are removed from soil and sent to landfills approved for these products.

These operations are monitored by Mi Swaco service technicians. Daily logs are maintained to ensure optimal equipment operation and maintenance. Screen and chemical use is logged to maintain inventory control. Fluid properties are monitored and recorded and drilling mud volumes are accounted for in the mud storage farm. This data is kept for end of well review to insure performance goals are met. Lessons learned are logged and used to help with continuous improvement.

A MI SWACO field supervisor manages from 3-5 wells. They are responsible for training personnel, supervising installations, and inspecting sites for compliance of MI SWACO safety and operational policy.

III. Closure Plan

A maximum 340' X 340' caliche pad is built per well. All of the trucks and steel tanks fit on this pad. All fluid cuttings go to the steel tanks to be hauled by various trucking companies to an agency approved disposal.

A multibowl wellhead may be used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

Devon proposes using a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 5000 (5M) psi.


- Wellhead will be installed by wellhead representatives.
- If the welding is performed by a third party, the wellhead representative will monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
- Wellhead representative will install the test plug for the initial BOP test.
- Wellhead company will install a solid steel body pack-off to completely isolate the lower head after cementing intermediate casing. After installation of the pack-off, the pack-off and the lower flange will be tested to 5M, as shown on the attached schematic. Everything above the pack-off will not have been altered whatsoever from the initial nipple up. Therefore the BOP components will not be retested at that time.
- If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head will be cut and top out operations will be conducted.
- Devon will pressure test all seals above and below the mandrel (but still above the casing) to full working pressure rating.
- Devon will test the casing to 0.22 psi/ft or 1500 psi, whichever is greater, as per Onshore Order #2.

After running the 13-3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 5M will be installed on the wellhead system and will undergo a 250 psi low pressure test followed by a 5,000 psi high pressure test. The 5,000 psi high and 250 psi low test will cover testing requirements a maximum of 30 days, as per Onshore Order #2. If the well is not complete within 30 days of this BOP test, another full BOP test will be conducted, as per Onshore Order #2.

After running the 9-5/8' intermediate casing with a mandrel hanger, the 13-5/8" BOP/BOPE system with a minimum rating of 5M will already be installed on the wellhead.

The pipe rams will be operated and checked each 24 hour period and each time the drill pipe is out of the hole. These tests will be logged in the daily driller's log. A 2" kill line and 3" choke line will be incorporated into the drilling spool below the ram BOP. In addition to the rams and annular preventer, additional BOP accessories include a kelly cock, floor safety valve, choke lines, and choke manifold rated at 5,000 psi WP.

Devon's proposed wellhead manufactures will be FMC Technologies, Cactus Wellhead, or Cameron.

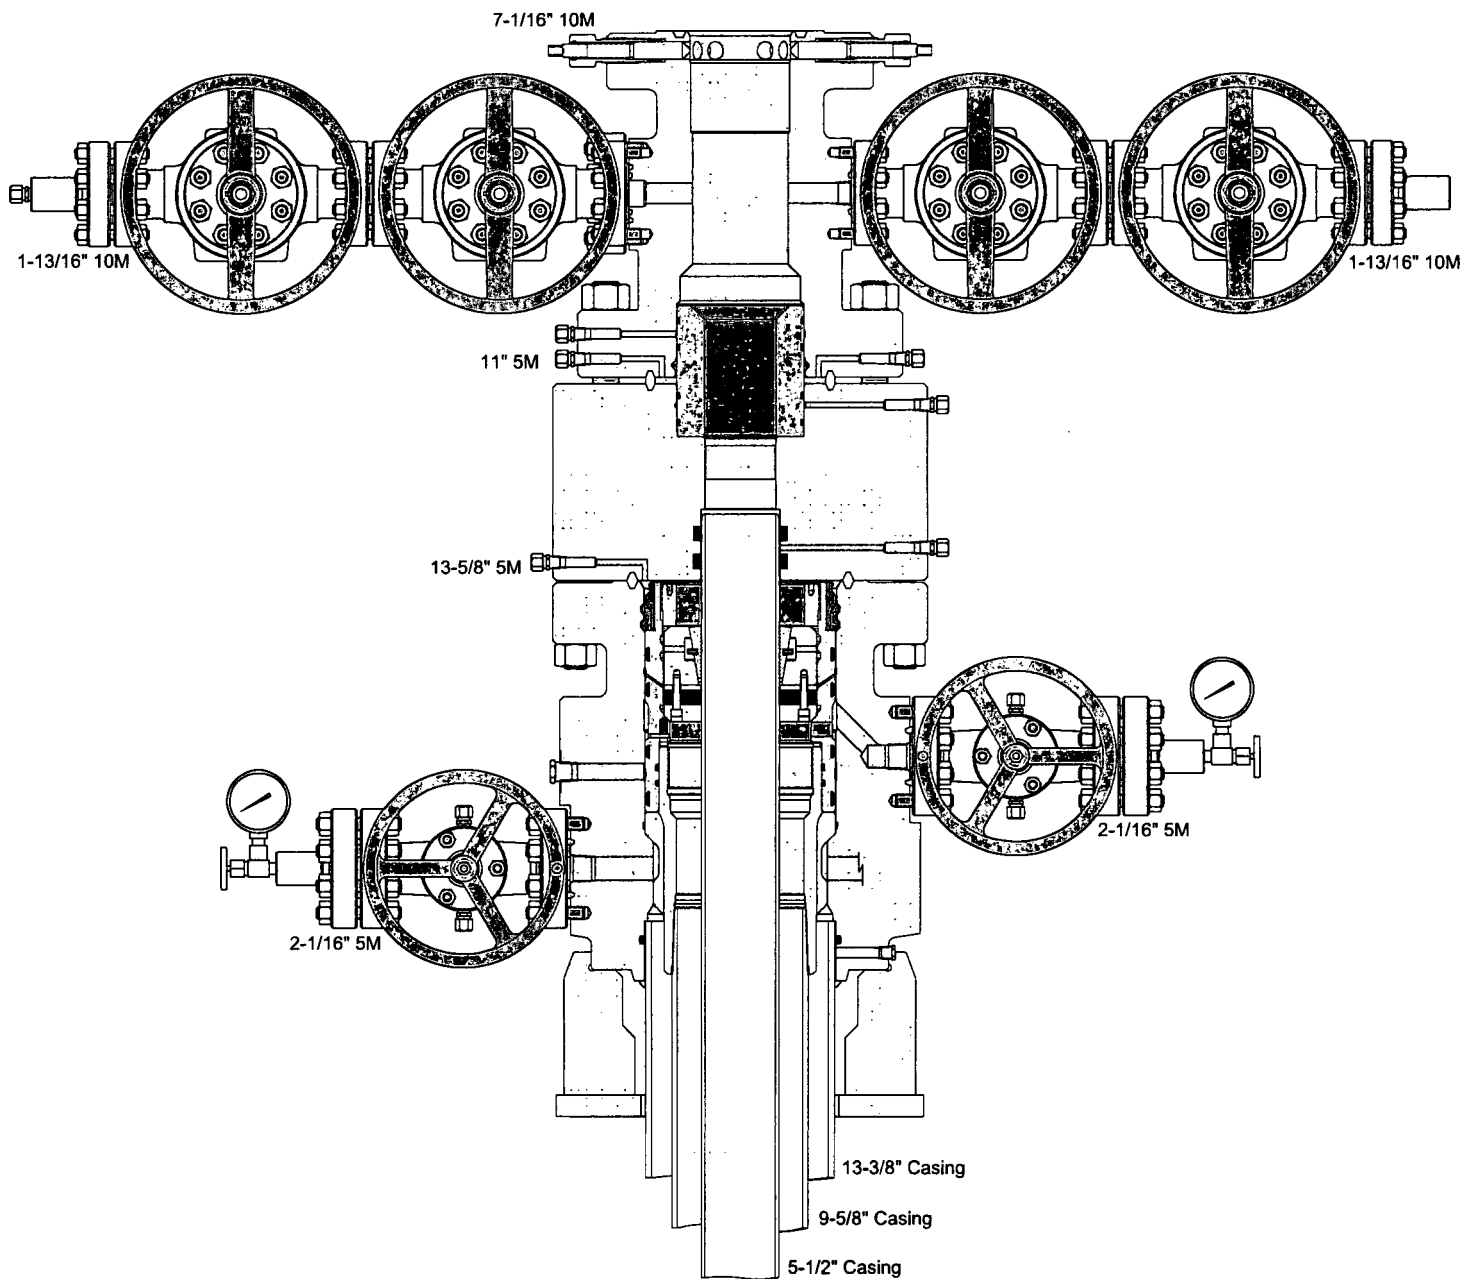

Devon Energy, Grumpy Cat 15 Fed 214H

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Tension
	From	To							
17.5"	0	1230	13.375"	48	H40	BTC	1.125	1.25	1.6
12.25"	0	6000	9.625"	40	J55	BTC	1.125	1.6	1.6
8.75"	0	TD	5.5"	17	P110	BTC	1.125	1.6	1.6
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet

A variance is requested for collapse SF for the intermediate

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

Must have table for contingency casing

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary.	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

Devon Energy, Grumpy Cat 15 Fed 214H

3. Cementing Program

Casing	# Sks	Wt. lb/gal	Yld ft ³ /sack	H ₂ O gal/sk	500# Comp. Strength (hours)	Slurry Description
Surf.	798	14.8	1.33	6.32	6	Lead: Class C Cement + additives
Inter.	1211	9.5	1.85	9.81	14	Lead: (65:35) Class C Cement + additives
	153	14.8	1.33	6.32	6	Tail: Class C Cement + additives
Prod.	360	9	3.27	13.5	21	Lead: Tuned Light Cement
	1369	14.5	1.2	5.31	25	Tail: (50:50) Class H Cement: Poz (Fly Ash)

DV tool depth(s) will be adjusted based on hole conditions and cement volumes will be adjusted proportionally. DV tool will be set a minimum of 50 feet below previous casing and a minimum of 200 feet above current shoe. Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

Casing String	TOC	% Excess
13-3/8" Surface	0'	50%
9-5/8" Intermediate	0'	30%
5-1/2" Production	5,800'	10%

4. Pressure Control Equipment

N	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
---	--

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	✓	Tested to:
12-1/4"	13-5/8"	5M	Annular	x	50% of working pressure
			Blind Ram		5M
			Pipe Ram		
			Double Ram	x	
			Other*		
8-3/4"	13-5/8"	5M	Annular	x	50% testing pressure
			Blind Ram		5M
			Pipe Ram		
			Double Ram	x	

Devon Energy, Grumpy Cat 15 Fed 214H

			Other *			
			Annular			
			Blind Ram			
			Pipe Ram			
			Double Ram			
			Other *			

*Specify if additional ram is utilized.

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

Y	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
Y	Are anchors required by manufacturer?
Y	<p>A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.</p> <p>Devon proposes using a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be 5000 (5M) psi.</p> <ul style="list-style-type: none"> Wellhead will be installed by wellhead representatives. If the welding is performed by a third party, the wellhead representative will monitor the temperature to verify that it does not exceed the maximum temperature of the seal. Wellhead representative will install the test plug for the initial BOP test. Wellhead company will install a solid steel body pack-off to completely isolate the lower head after cementing intermediate casing. After installation of the packoff, the pack-off and the lower flange will be tested to 5M, as shown on the attached schematic. Everything above the pack-off will not have been altered

Devon Energy, Grumpy Cat 15 Fed 214H

	<p>whatsoever from the initial nipple up. Therefore the BOP components will not be retested at that time.</p> <ul style="list-style-type: none">○ If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head will be cut and top out operations will be conducted.○ Devon will pressure test all seals above and below the mandrel (but still above the casing) to full working pressure rating.○ Devon will test the casing to 0.22 psi/ft or 1500 psi, whichever is greater, as per Onshore Order #2. <p>After running the 13-3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum rating of 5M will be installed on the wellhead system and will undergo a 250 psi low pressure test followed by a 3,000 psi high pressure test. The 3,000 psi high and 250 psi. Low test will cover testing requirements a maximum of 30 days, as per Onshore Order #2. If the well is not complete within 30 days of this BOP test, another full BOP test will be conducted, as per Onshore Order #2.</p> <p>After running the 9-5/8' intermediate casing with a mandrel hanger, the 13-5/8" BOP/BOPE system with a minimum rating of 5M will already be installed on the wellhead.</p> <p>The pipe rams will be operated and checked each 24 hour period and each time the drill pipe is out of the hole. These tests will be logged in the daily driller's log. A 2" kill line and 3" choke line will be incorporated into the drilling spool below the ram BOP. In addition to the rams and annular preventer, additional BOP accessories include a Kelly cock, floor safety valve, choke lines, and choke manifold rated at 5,000 psi WP.</p> <p>Devon's proposed wellhead manufactures will be EMC Technologies, Cactus Wellhead, or Cameron.</p> <p>The pipe rams will be operated and checked each 24 hour period and each time the drill pipe is out of the hole. These tests will be logged in the daily driller's log. A 2" kill line and 3" choke line will be incorporated into the drilling spool below the ram BOP. In addition to the rams and annular preventer, additional BOP accessories include a kelly cock, floor safety valve, choke lines, and choke manifold rated at 5,000 psi WP.</p> <p>See attached schematic.</p>
--	--

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	1230	FW Gel	8.6-8.8	28-34	N/C
1177	6000	Saturated Brine	10.0-11.0	28-34	N/C
6000	TD	Cut Brine	8.5-9.0	28-34	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

Devon Energy, Grumpy Cat 15 Fed 214H

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
X	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
	No Logs are planned based on well control or offset log information.
	Drill stem test? If yes, explain
	Coring? If yes, explain

Additional logs planned	Interval
Resistivity	Int. shoe to KOP
Density	Int. shoe to KOP
X CBL	Production casing
X Mud log	KOP to TD
PEX	

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	4935 psi
Abnormal Temperature	No

Mitigation measure for abnormal conditions. Describe. Lost circulation material/sweeps/mud scavengers.

Hydrogen Sulfide (H ₂ S) monitors will be installed prior to drilling out the surface shoe. If H ₂ S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.	
N	H ₂ S is present
Y	H ₂ S Plan attached

8. Other facets of operation

Is this a walking operation? Potentially

1. If operator elects, drilling rig will batch drill the surface holes and run/cement surface casing; walking the rig to next wells on the pad.
2. The drilling rig will then batch drill the intermediate sections and run/cement intermediate casing; the wellbore will be isolated with a blind flange and pressure gauge installed for monitoring the well before walking to the next well.
3. The drilling rig will then batch drill the production hole sections on the wells with OBM, run/cement production casing, and install TA caps or tubing heads for completions.

NOTE: During batch operations the drilling rig will be moved from well to well however, it will not be removed from the pad until all wells have production casing run/cemented.

Will be pre-setting casing? Potentially

1. Spudder rig will move in and drill surface hole.
 - a. Rig will utilize fresh water based mud to drill surface hole to TD. Solids control will be handled entirely on a closed loop basis.
2. After drilling the surface hole section, the spudder rig will run casing and cement following all of the applicable rules and regulations (OnShore Order 2, all COAs and NMOCD regulations).
3. The wellhead will be installed and tested once the 10 3/4" surface casing is cut off and the WOC time has been reached.
4. A blind flange with the same pressure rating as the wellhead will be installed to seal the wellbore. Pressure will be monitored with a pressure gauge installed on the wellhead.
5. Spudder rig operations is expected to take 4-5 days per well on a multi well pad.
6. The NMOCD will be contacted and notified 24 hours prior to commencing spudder rig operations.
7. Drilling operations will be performed with the drilling rig. At that time an approved BOP stack will be nipped up and tested on the wellhead before drilling operations commences on each well.
 - a. The NMOCD will be contacted / notified 24 hours before the drilling rig moves back on to the pad with the pre-set surface casing.

Attachments

- ☒ Directional Plan
☐ Other, describe



Fluid Technology

ContiTech Beattie Corp.
Website: www.contitechbeattie.com

Monday, June 14, 2010

RE: Drilling & Production Hoses
Lifting & Safety Equipment

To Helmerich & Payne,

A Continental ContiTech hose assembly can perform as intended and suitable for the application regardless of whether the hose is secured or unsecured in its configuration. As a manufacturer of High Pressure Hose Assemblies for use in Drilling & Production, we do offer the corresponding lifting and safety equipment, this has the added benefit of easing the lifting and handling of each hose assembly whilst affording hose longevity by ensuring correct handling methods and procedures as well as securing the hose in the unlikely event of a failure; but in no way does the lifting and safety equipment affect the performance of the hoses providing the hoses have been handled and installed correctly. It is good practice to use lifting & safety equipment but not mandatory.

Should you have any questions or require any additional information/clarifications then please do not hesitate to contact us.

ContiTech Beattie is part of the Continental AG Corporation and can offer the full support resources associated with a global organization.

Best regards,

Robin Hodgson
Sales Manager
ContiTech Beattie Corp

ContiTech Beattie Corp,
11535 Brittnmoore Park Drive,
Houston, TX 77041
Phone: +1 (832) 327-0141
Fax: +1 (832) 327-0148
www.contitechbeattie.com



RIG 212



QUALITY DOCUMENT


**PHOENIX RUBBER
INDUSTRIAL LTD.**

 6728 Szeged, Budapest út 10. Hungary • H-6701 Szeged, P. O. Box 152
 Phone: (3662) 566-737 • Fax: (3662) 566-738

 SALES & MARKETING: H-1092 Budapest, Ráday u. 42-44. Hungary • H-1440 Budapest, P. O. Box 26
 Phone: (361) 456-4200 • Fax: (361) 217-2872, 456-4273 • www.taurusemergo.hu

QUALITY CONTROL INSPECTION AND TEST CERTIFICATE				CERT. N°: 552	
PURCHASER: Phoenix Beattie Co.				P.O. N°: 1519FA-871	
PHOENIX RUBBER order N°: 170466		HOSE TYPE: 3" ID Choke and Kill Hose			
HOSE SERIAL N°: 34128		NOMINAL / ACTUAL LENGTH: 11,43 m			
W.P. 68,96 MPa	10000	psi	T.P. 103,4 MPa	15000	psi
			Duration:	60	min.
Pressure test with water at ambient temperature <div style="text-align: center;">See attachment. (1 page)</div>					
↑ 10 mm = 10 Min. → 10 mm = 25 MPa					
COUPLINGS					
Type	Serial N°		Quality	Heat N°	
3" coupling with 4 1/16" Flange end	720	719	AISI 4130	C7626	
			AISI 4130	47357	
API Spec 16 C Temperature rate: "B"					
All metal parts are flawless					
WE CERTIFY THAT THE ABOVE HOSE HAS BEEN MANUFACTURED IN ACCORDANCE WITH THE TERMS OF THE ORDER AND PRESSURE TESTED AS ABOVE WITH SATISFACTORY RESULT.					
Date:		Inspector		Quality Control	
29. April. 2002.				PHOENIX RUBBER Industrial Ltd. Hose Inspection and Pressure Test Control PHOENIX RUBBER S.C.	

40920-0-00015 N800C 14094-65

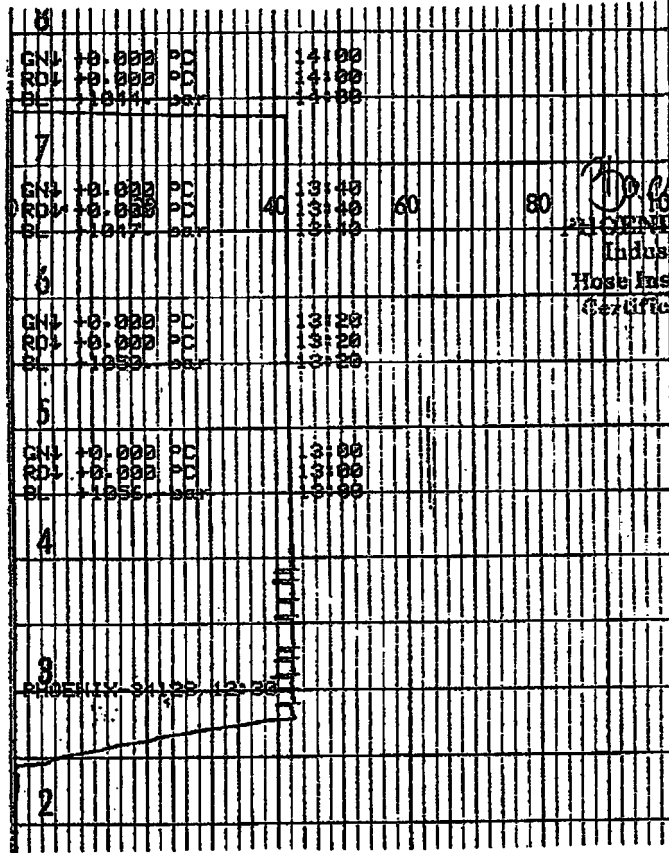

[Signature]
PHOENIX RUBBER
 Industrial Ltd.
 Hose Inspection and
 Certification Dept.

VERIFIED TRUE CO.
 PHOENIX RUBBER CO.

APD ID: 10400032225

Submission Date: 07/24/2018

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Well Type: OIL WELL

Well Work Type: Drill



[Show Final Text](#)

Will existing roads be used? YES

Existing Road Map:

Grumpy_Cat_15_Fed_214H_Ex_Access_Rd_20180718142944.pdf

Existing Road Purpose: ACCESS,FLUID TRANSPORT

Row(s) Exist? NO

ID:

Do the existing roads need to be improved? YES

Existing Road Improvement Description: Improve road to accommodate Drilling and Completion operations.

Existing Road Improvement Attachment:

Will new roads be needed? YES

New Road Map:

Grumpy_Cat_15_Fed_214H_Access_Rd_20180718143009.pdf

New road type: COLLECTOR,RESOURCE

Length: 140

Feet

Width (ft.): 30

Max slope (%): 6

Max grade (%): 4

Army Corp of Engineers (ACOE) permit required? NO

ACOE Permit Number(s):

New road travel width: 14

New road access erosion control: WATER DRAINAGE DITCH

New road access plan or profile prepared? NO

New road access plan attachment:

Access road engineering design? NO

Access road engineering design attachment:

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Access surfacing type: GRAVEL

Access topsoil source: ONSITE

Access surfacing type description:

Access onsite topsoil source depth: 6

Offsite topsoil source description:

Onsite topsoil removal process: See attached Interim reclamation diagram.

Access other construction information:

Access miscellaneous information:

Number of access turnouts:

Access turnout map:

New road drainage crossing: OTHER

Drainage Control comments: WATER DRAINAGE DRIP

Road Drainage Control Structures (DCS) description: N/A

Road Drainage Control Structures (DCS) attachment:

Additional Attachment(s):

Existing Wells Map? YES

Attach Well map:

Grumpy_Cat_15_Fed_214H_1Mile_Map_20180718143256.pdf

Existing Wells description:

Submit or defer a Proposed Production Facilities plan? DEFER

Estimated Production Facilities description: All flowlines will be buried going to the Grumpy Cat 15 CTB 2.

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Water source use type: STIMULATION

Water source type: RECYCLED

Describe type:

Source latitude:

Source longitude:

Source datum:

Water source permit type: OTHER

Source land ownership: STATE

Water source transport method: PIPELINE

Source transportation land ownership: STATE

Water source volume (barrels): 103500

Source volume (acre-feet): 13.340435

Source volume (gal): 4347000

Water source and transportation map:

Grumpy_Cat_15_Fed_214H_Wtr_Xfr_Map_20180718143234.PDF

Water source comments: The attached Water Transfer Map is a proposal only and the final route and documentation will be provided by a Devon contractor prior to installation. When available Devon will always follow existing disturbance.

New water well? NO

Well latitude:

Well Longitude:

Well datum:

Well target aquifer:

Est. depth to top of aquifer(ft):

Est thickness of aquifer:

Aquifer comments:

Aquifer documentation:

Well depth (ft):

Well casing type:

Well casing outside diameter (in.):

Well casing inside diameter (in.):

New water well casing?

Used casing source:

Drilling method:

Drill material:

Grout material:

Grout depth:

Casing length (ft.):

Casing top depth (ft.):

Well Production type:

Completion Method:

Water well additional information:

State appropriation permit:

Additional information attachment:

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Construction Materials description: Dirt fill and caliche will be used to construct well pad. See attached map.

Construction Materials source location attachment:

Grumpy_Cat_15_Fed_214H_Caliche_Map_20180718143329.pdf

Waste type: COMPLETIONS/STIMULATION

Waste content description: FLOW BACK WATER DURING COMPLETION OPERATIONS

Amount of waste: 3000 barrels

Waste disposal frequency : One Time Only

Safe containment description: N/A

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

Disposal type description:

Disposal location description: VARIOUS DISPOSAL LOCATIONS IN LEA AND EDDY COUNTIES.

Waste type: DRILLING

Waste content description: WATER BASED CUTTINGS

Amount of waste: 1574 barrels

Waste disposal frequency : Daily

Safe containment description: N/A

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

Disposal type description:

Disposal location description: ALL CUTTINGS WILL BE DISPOSED OF AT R360, SUNDANCE OR EQUIVALENT.

Waste type: PRODUCED WATER

Waste content description: PRODUCED WATER DURING FLOW BACK OPERATIONS. THIS AMOUNT IS A DAILY AVERAGE DURING FLOW BACK (BWPD).

Amount of waste: 1000 barrels

Waste disposal frequency : Daily

Safe containment description: N/A

Safe containmant attachment:

Waste disposal type: OFF-LEASE INJECTION **Disposal location ownership:** COMMERCIAL

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Disposal type description:

Disposal location description: VARIOUS DISPOSAL LOCATIONS IN LEA AND EDDY COUNTIES.

Waste type: FLOWBACK

Waste content description: PRODUCED WATER DURING FLOW BACK OPERATIONS. THIS AMOUNT IS A DAILY AVERAGE DURING FLOW BACK (BWPD).

Amount of waste: 1500 barrels

Waste disposal frequency : Daily

Safe containment description: N/A

Safe containmant attachment:

Waste disposal type: OFF-LEASE INJECTION **Disposal location ownership:** COMMERCIAL

Disposal type description:

Disposal location description: VARIOUS DISPOSAL LOCATIONS IN LEA AND EDDY COUNTIES.

Reserve Pit being used? NO

Temporary disposal of produced water into reserve pit?

Reserve pit length (ft.) **Reserve pit width (ft.)**

Reserve pit depth (ft.) **Reserve pit volume (cu. yd.)**

Is at least 50% of the reserve pit in cut?

Reserve pit liner

Reserve pit liner specifications and installation description

Cuttings Area being used? NO

Are you storing cuttings on location? NO

Description of cuttings location

Cuttings area length (ft.) **Cuttings area width (ft.)**

Cuttings area depth (ft.) **Cuttings area volume (cu. yd.)**

Is at least 50% of the cuttings area in cut?

WCuttings area liner

Cuttings area liner specifications and installation description

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Are you requesting any Ancillary Facilities?: NO

Ancillary Facilities attachment:

Comments:

Well Site Layout Diagram:

Grumpy_Cat_15_Fed_214H_Rig_Layout_20180718143438.pdf

Comments:

Type of disturbance: New Surface Disturbance

Multiple Well Pad Name: TODD MDP3 15 WELL PAD

Multiple Well Pad Number: 4

Recontouring attachment:

Grumpy_Cat_15_Fed_214H_Reclamation_20180718143527.pdf

Drainage/Erosion control construction: All areas disturbed shall be reclaimed as early and as nearly as practicable to their original condition or their final land use and shall be maintained to control dust and minimize erosion to the extent practicable.

Drainage/Erosion control reclamation: Topsoils and subsoils shall be replaced to their original relative positions and contoured so as to achieve erosion control, long-term stability and preservation of surface water flow patterns. The disturbed area then shall be reseeded in the first favorable growing season.

Well pad proposed disturbance (acres): 3.78	Well pad interim reclamation (acres): 1.915	Well pad long term disturbance (acres): 1.876
Road proposed disturbance (acres): 0.096	Road interim reclamation (acres): 0	Road long term disturbance (acres): 0.096
Powerline proposed disturbance (acres): 0.26	Powerline interim reclamation (acres): 0	Powerline long term disturbance (acres): 0.26
Pipeline proposed disturbance (acres): 1.656	Pipeline interim reclamation (acres): 0	Pipeline long term disturbance (acres): 1.656
Other proposed disturbance (acres): 0	Other interim reclamation (acres): 0	Other long term disturbance (acres): 0
Total proposed disturbance: 5.792	Total interim reclamation: 1.915	Total long term disturbance: 3.888

Disturbance Comments:

Reconstruction method: Operator will use Best Management Practices "BMP" to mechanically recontour to obtain the desired outcome.

Topsoil redistribution: Topsoils shall be replaced to their original relative positions and contoured so as to achieve erosion control, long-term stability and preservation of surface water flow patterns.

Soil treatment: Topsoils shall be replaced to their original relative positions and contoured so as to achieve erosion control, long-term stability and preservation of surface water flow patterns.

Existing Vegetation at the well pad:

Existing Vegetation at the well pad attachment:

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Existing Vegetation Community at the road:

Existing Vegetation Community at the road attachment:

Existing Vegetation Community at the pipeline:

Existing Vegetation Community at the pipeline attachment:

Existing Vegetation Community at other disturbances:

Existing Vegetation Community at other disturbances attachment:

Non native seed used? NO

Non native seed description:

Seedling transplant description:

Will seedlings be transplanted for this project? NO

Seedling transplant description attachment:

Will seed be harvested for use in site reclamation? NO

Seed harvest description:

Seed harvest description attachment:

Seed type:

Seed source:

Seed name:

Source name:

Source address:

Source phone:

Seed cultivar:

Seed use location:

PLS pounds per acre:

Proposed seeding season:

Total pounds/Acre:

Seed Type

Pounds/Acre

Seed reclamation attachment:

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

First Name: JACOB

Last Name: OCHOA

Phone: (575)748-9934

Email: jacob.choa@dv.com

Seedbed prep:

Seed BMP:

Seed method:

Existing invasive species? NO

Existing invasive species treatment description:

Existing invasive species treatment attachment:

Weed treatment plan description: Maintain weeds on an as need basis.

Weed treatment plan attachment:

Monitoring plan description: MONITOR AS NEEDED

Monitoring plan attachment:

Success standards: N/A

Pit closure description: N/A

Pit closure attachment:

Disturbance type: PIPELINE

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Disturbance type: NEW ACCESS ROAD

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Disturbance type: EXISTING ACCESS ROAD

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Operator Name: DEVON ENERGY PRODUCTION COMPANY LP

Well Name: GRUMPY CAT 15 FED

Well Number: 214H

Disturbance type: WELL PAD

Describe:

Surface Owner: BUREAU OF LAND MANAGEMENT

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Right of Way needed? NO

Use APD as ROW?

ROW Type(s):

SUPO Additional Information: CTB ELECTRIC PLAT FLOWLINE PLAT CTB WP ELECTRIC PLAT

Use a previously conducted onsite? YES

Previous Onsite information: 9/1/2017; well name on previous onsite-Todd MDP 15 well pad 14

GRUMPY_CAT_15_FED_214H__FLOWLINE_RV1_20180718143954.pdf


GRUMPY_CAT_15_FED_214H__CTB_20180718144011.pdf

GRUMPY_CAT_15_FED_214H__ELECTRIC_20180718144014.PDF

GRUMPY_CAT_15_FED_214H__ELECTRIC2_20180718144016.PDF

Pay.gov__Receipt_GRUMPY_CAT_15_FED_214H_20180724124032.pdf

SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
AERIAL ACCESS ROUTE MAP

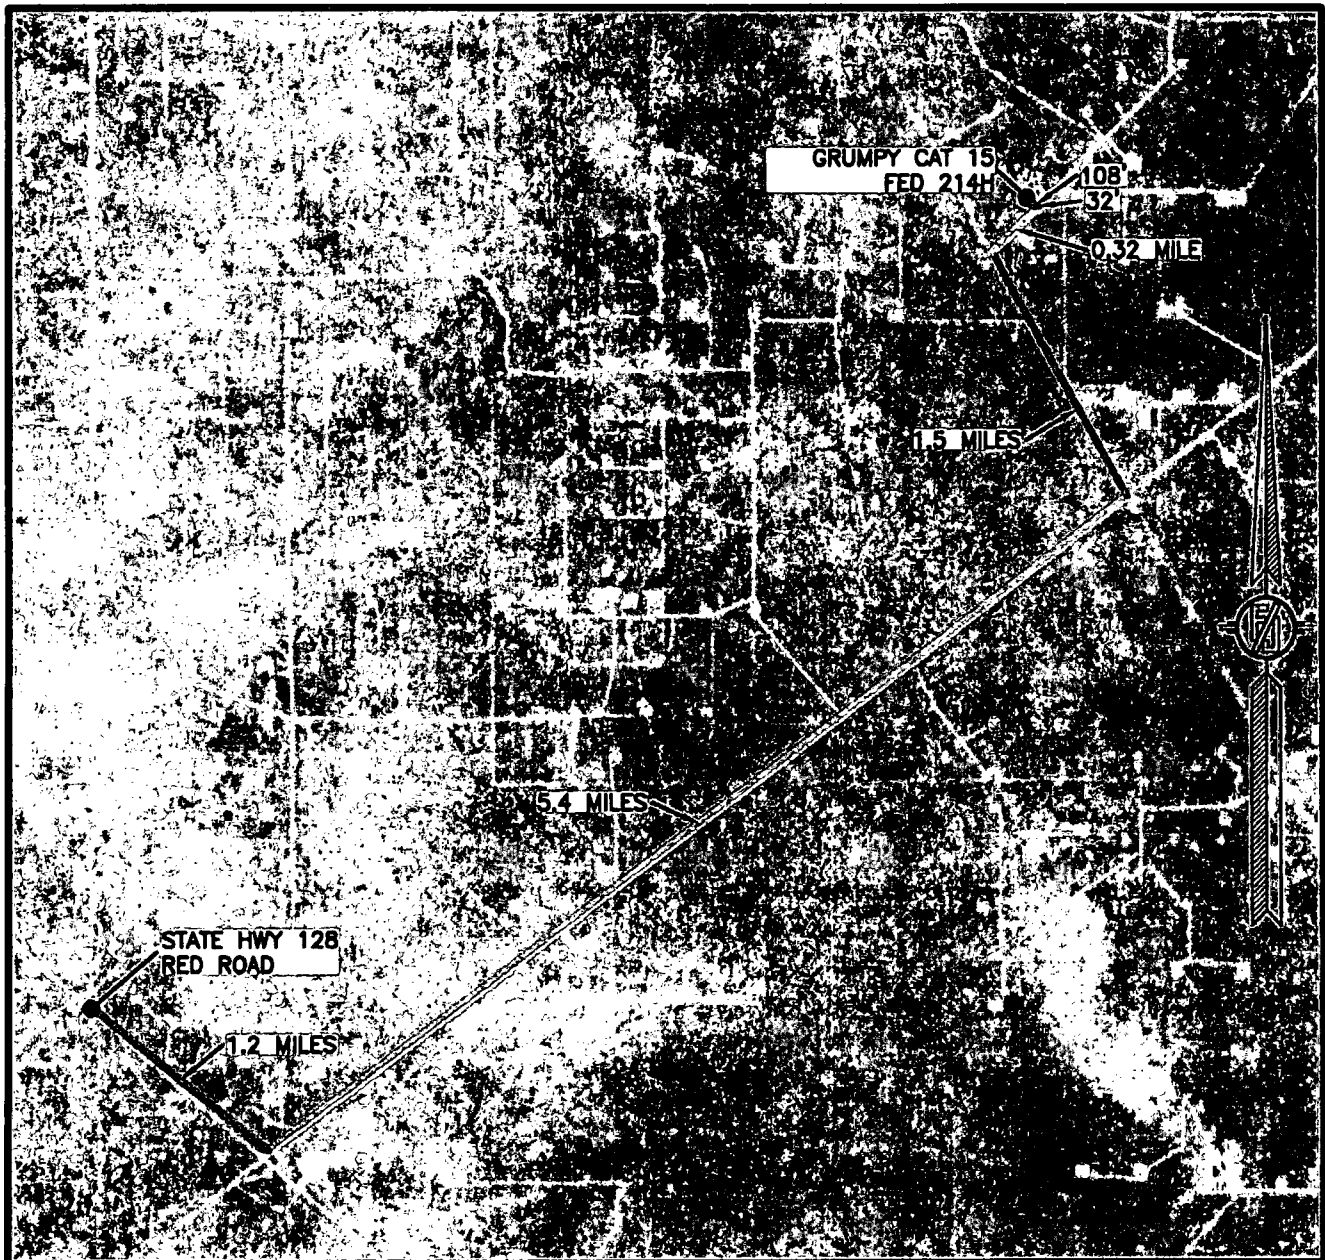

NOT TO SCALE
AERIAL PHOTO:
GOOGLE EARTH
NOV. 2017

DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H

LOCATED 175 FT. FROM THE NORTH LINE
AND 1040 FT. FROM THE EAST LINE OF
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

APRIL 30, 2018


SURVEY NO. 5805A

MADRON SURVEYING, INC. 301 SOUTH CANAL (575) 734-3341 CARLSBAD, NEW MEXICO


ACCESS ROAD PLAT

ACCESS ROAD FOR ACCESS ROAD FOR GRUMPY CAT 15 FED 213H & 214H

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF AN ACCESS ROAD CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
APRIL 30, 2018

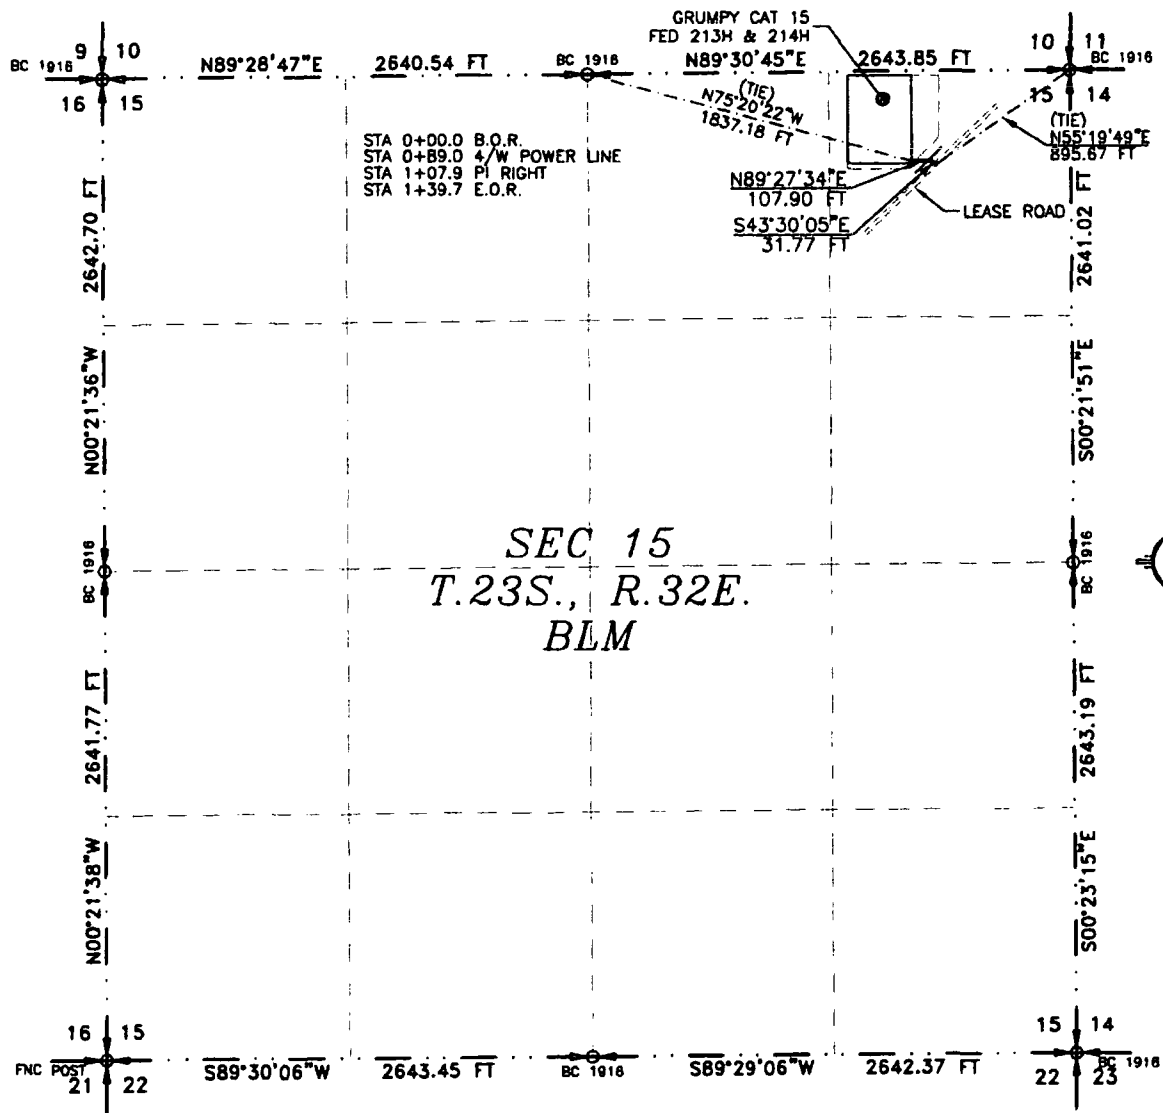

SEE NEXT SHEET (2-2) FOR DESCRIPTION



GENERAL NOTES

- 1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.
- 2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.

SHEET: 1-2

MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO

SURVEYOR CERTIFICATE

I, FILMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF, THIS CERTIFICATE IS EXECUTED AT CARLSBAD,

NEW MEXICO, THIS 30 DAY OF MAY, 2018

FILMON F. JARAMILLO, P.S. 12797

MADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88223
Phone (575) 234-3341

SURVEY NO. 5805A

ACCESS ROAD PLAT

ACCESS ROAD FOR ACCESS ROAD FOR GRUMPY CAT 15 FED 213H & 214H

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF AN ACCESS ROAD CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
APRIL 30, 2018

DESCRIPTION

A STRIP OF LAND 30 FEET WIDE CROSSING BUREAU OF LAND MANAGEMENT LAND IN SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., LEA COUNTY, STATE OF NEW MEXICO AND BEING 15 FEET EACH SIDE OF THE FOLLOWING DESCRIBED CENTERLINE SURVEY:

BEGINNING AT A POINT WITHIN THE NE/4 NE/4 OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., WHENCE THE NORTH QUARTER CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N75°20'22"W, A DISTANCE OF 1837.18 FEET;
THENCE N89°27'34"E A DISTANCE OF 107.90 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;
THENCE S43°30'05"E A DISTANCE OF 31.77 FEET THE TERMINUS OF THIS CENTERLINE SURVEY, WHENCE THE NORTHEAST CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N55°19'49"E, A DISTANCE OF 895.67 FEET;

SAID STRIP OF LAND BEING 139.67 FEET OR 8.46 RODS IN LENGTH, CONTAINING 0.096 ACRES MORE OR LESS AND BEING ALLOCATED BY FORTIES AS FOLLOWS:

NE/4 NE/4 139.67 L.F. 8.46 RODS 0.096 ACRES

GENERAL NOTES

- 1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.
- 2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.

SHEET: 2-2

MADRON SURVEYING, INC.

SURVEYOR CERTIFICATE

I, FILIMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF, THIS CERTIFICATE IS EXECUTED AT CARLSBAD, NEW MEXICO, THIS 12th DAY OF MAY 2018

FILIMON F. JARAMILLO PLS-12797

MADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341

SURVEY NO. 5805A

CARLSBAD, NEW MEXICO

One Mile Radius Map

devon

This map is for illustrative purposes only and is neither a legally recorded map nor a survey and is not intended to be used as one. Devon makes no warranty, representation, or guarantee of any kind regarding this map.

USA Contiguous Equidistant Conic
Datum: North American 1983
Created by: FME Server
Map is current as of 4/5/2018



 Miles 1 inch = 0.44 miles

GRUMPY CAT 15 FED 214H
WA017193383

CUERVO FEDERAL 23H

Nearest wellbore to SHL:


1388 ft.

DIAMONDTAIL 23 FEDERAL 1H

Nearest wellbore to BHL:

1042 ft.

- Unknown SHL
- Active SHL
- Inactive SHL
- × BHL

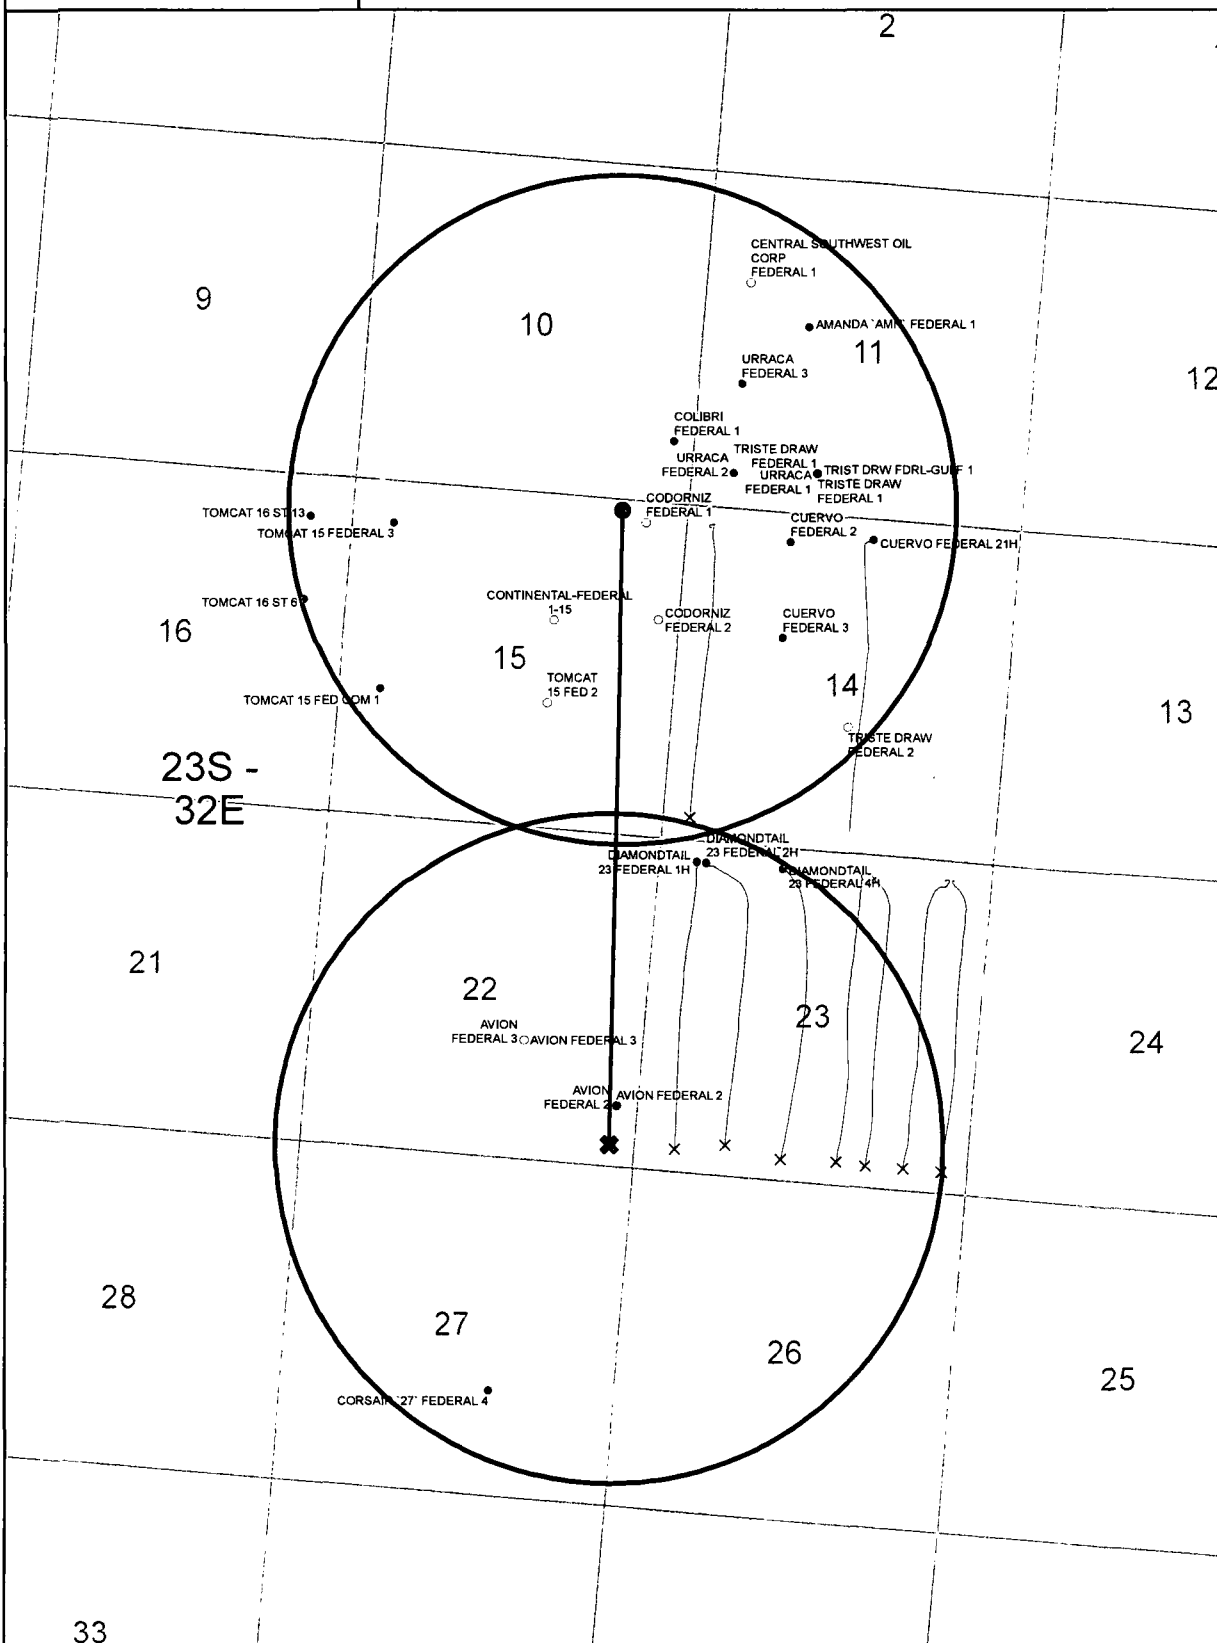

GRUMPY CAT 15 FED 213H

GRUMPY CAT 15 FED 214H

devon

This map is for illustrative purposes only and is neither a legally recorded map nor survey and is not intended to be used as one. Devon makes no warranty, representation, or guarantee of any kind regarding this map.

WG5_1984_Web_Mercator_Auxiliary_Sphere

Prepared by: _User

Map is current as of: 17-Jul-2018



Miles

0 0.25 0.50 1.00 1.56,913

TODD2 TW & FW POND

FW LINE 43 023

GRUMPY CAT 15 FED 213H
GRUMPY CAT 15 FED 214H

1. DEVON 30 DAYS, INSTALL PRIOR TO COMPLETION

2. DEVON WILL CONTACT BLM, IF ADDITIONAL TIME IS NEEDED

3. DISTURBANCE EXISTING

4. CONTENT: TREATED WATER & FRESH WATER

5. TYPE OF PIPE: LAYFLAT

6. SIZE OF PIPE: 10" OR 12"

7. LENGTH OF PIPE: 43 023' FOR TW & 43 023' FOR FW

Grumpy Cat Water

NENE

NWNW

NENW

NWNE

NENE

SENE

SWNW

SENW

SWNE

Caliche Map
SENE

Total Depth 50 ft

15


NESE

NWSW


NESW

NWSE

NESE

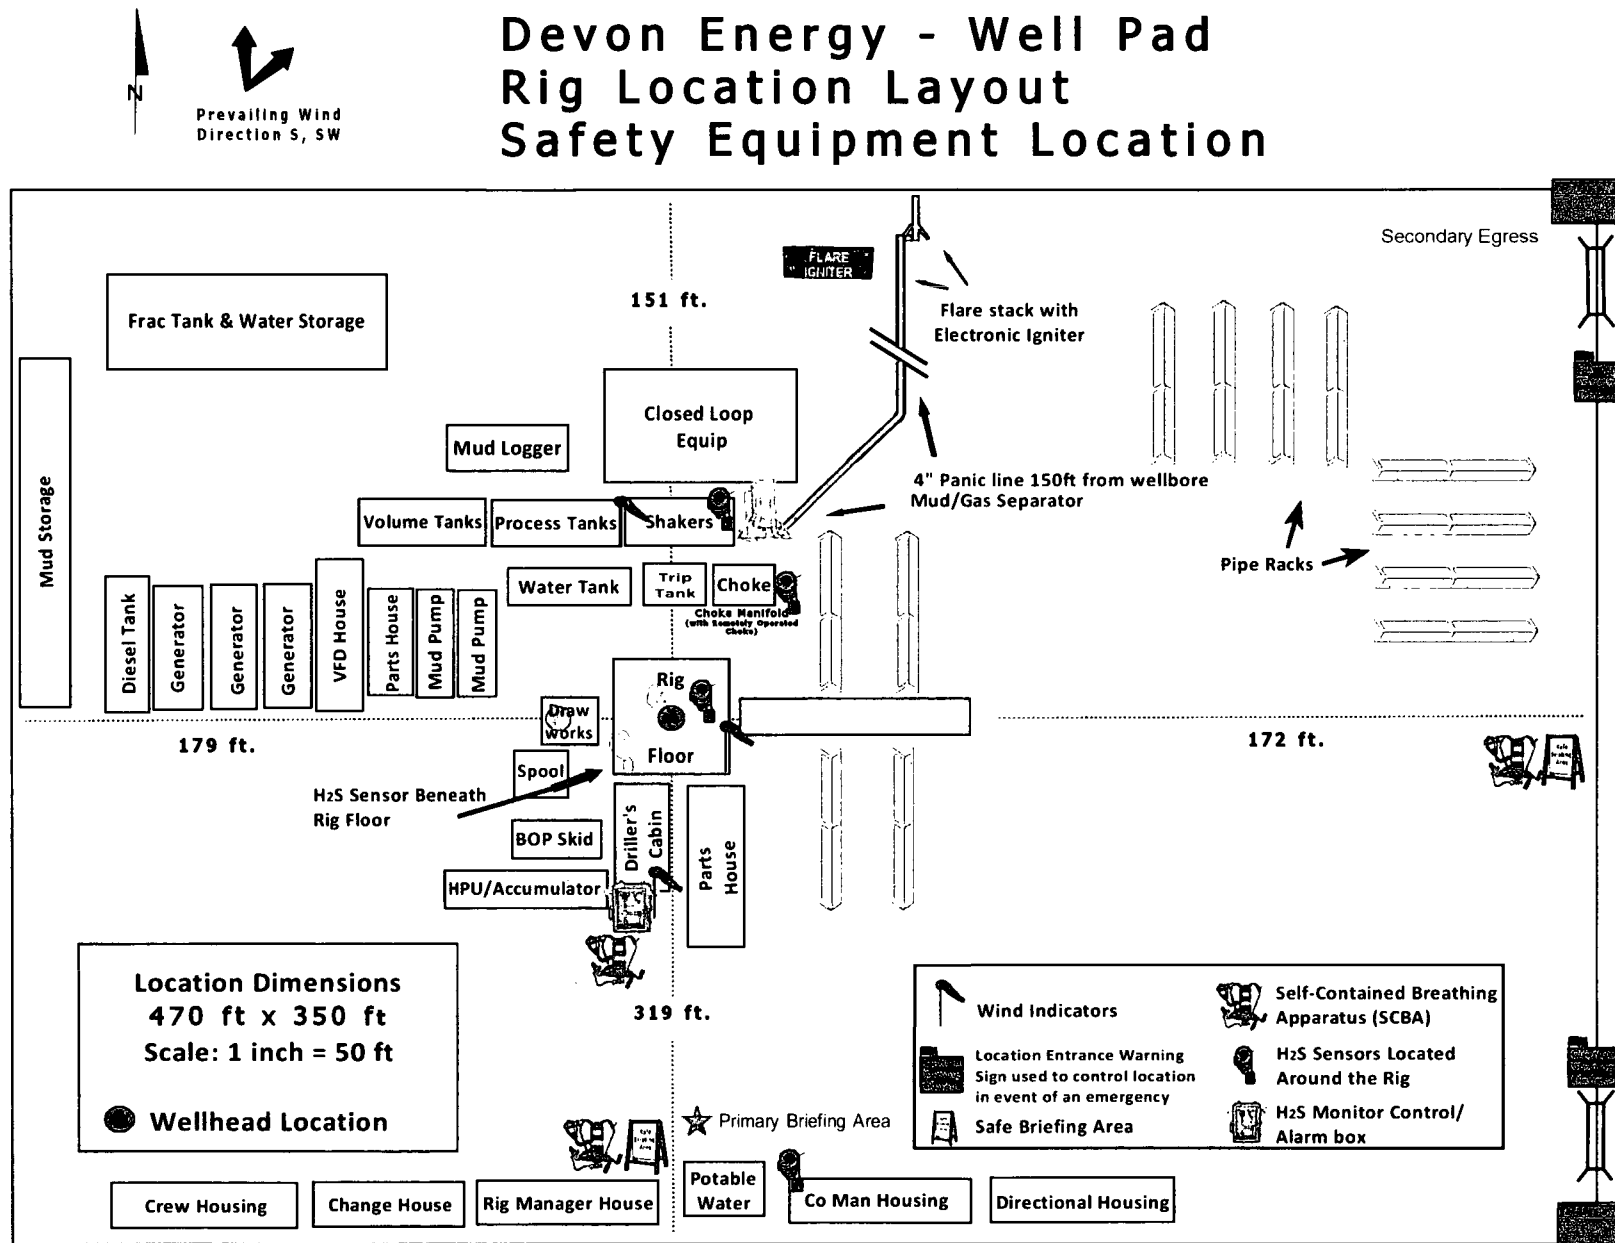

SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
INTERIM SITE BUILD PLAN

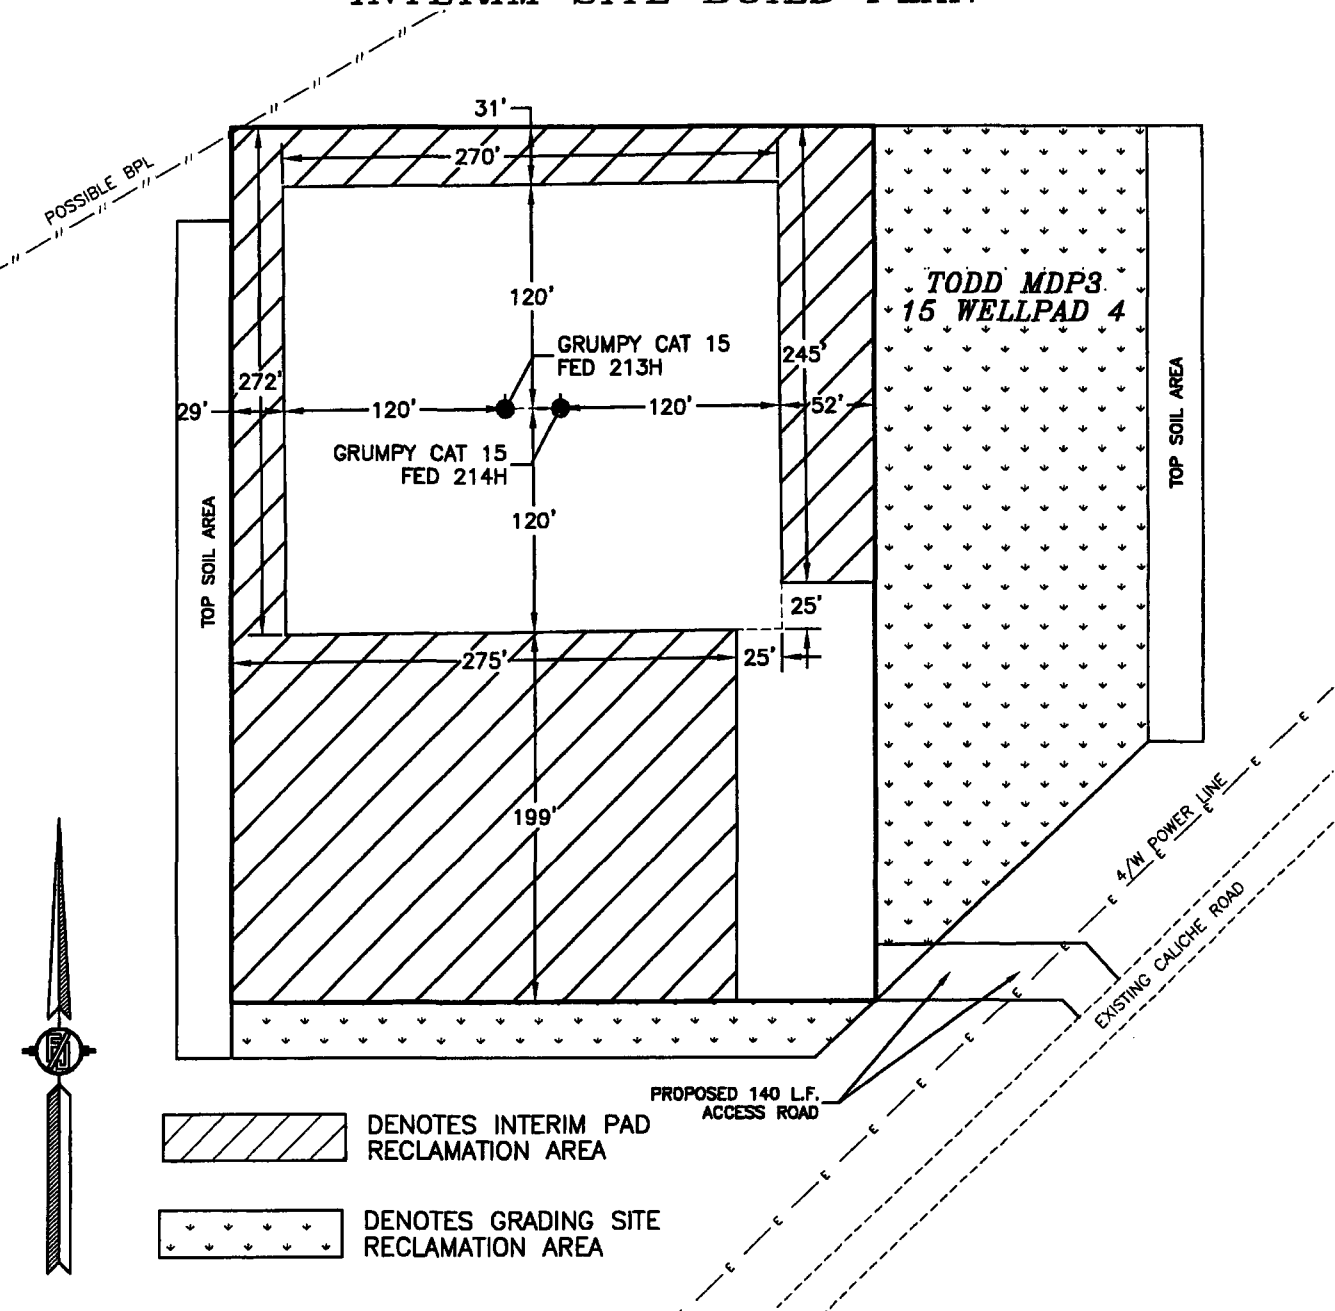

010 50 100 200
SCALE 1" = 100'

1.915± ACRES INTERIM PAD RECLAMATION AREA
1.597± ACRES GRADING SITE RECLAMATION AREA
1.876± ACRES NON-RECLAIMED AREA
5.388± ACRES TODD MDP3 15 WELLPAD 4

DEVON ENERGY PRODUCTION COMPANY, L.P.
GRUMPY CAT 15 FED 214H
LOCATED 175 FT. FROM THE NORTH LINE
AND 1040 FT. FROM THE EAST LINE OF
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

APRIL 30, 2018


SURVEY NO. 6806A

MADRON SURVEYING, INC. 301 SOUTH CANAL (575) 234-3341 CARLSBAD, NEW MEXICO

FLOWLINE PLAT

TWO-8" FLOWLINES & ONE-8" GAS LIFT LINE (BURIED IN THE SAME DITCH)
FROM GRUMPY CAT 15-22 FED 213H & 214H TO TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF A PIPELINE CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
FEBRUARY 20, 2018

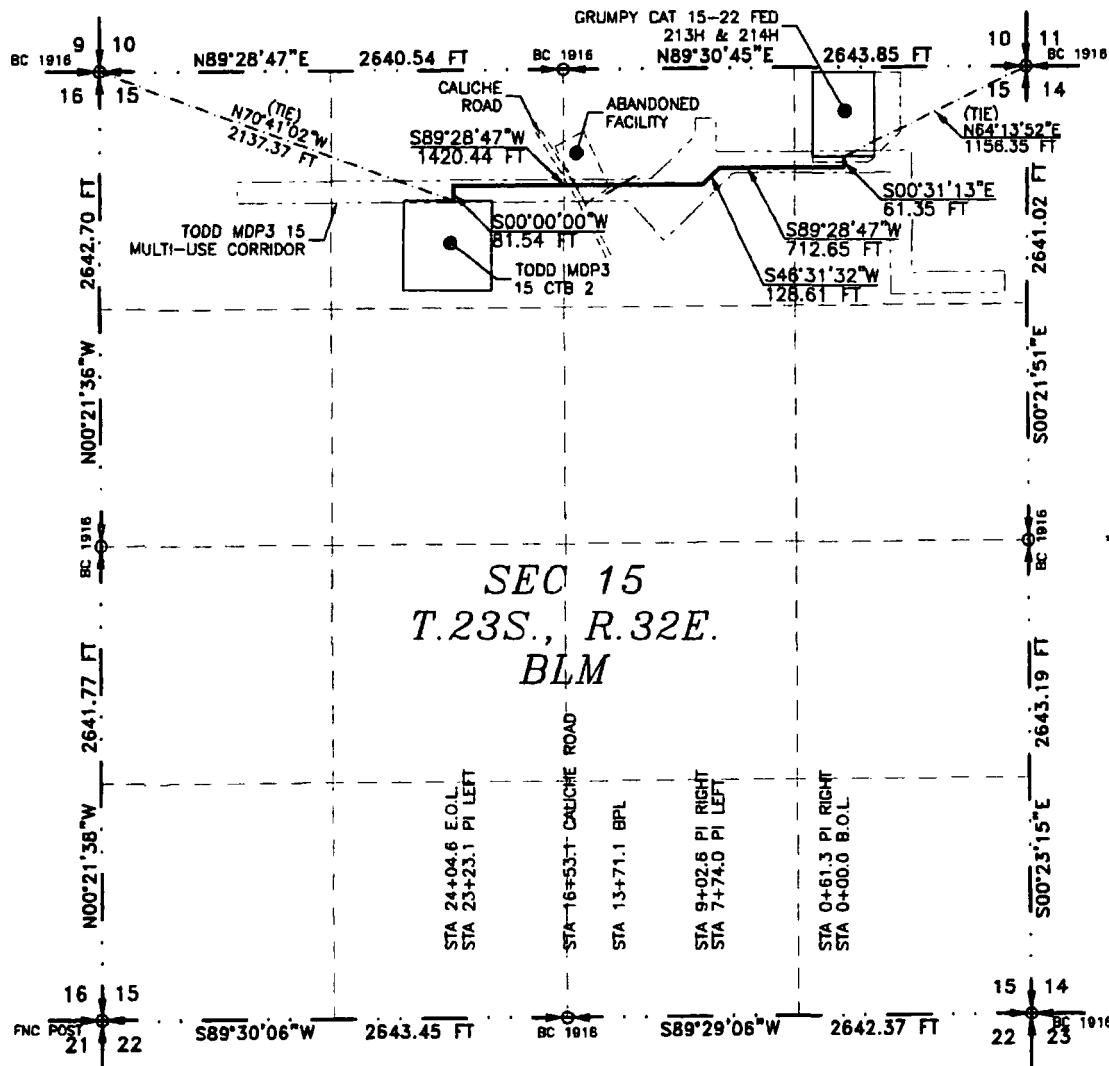

SEE NEXT SHEET (2-4) FOR DESCRIPTION

SURVEYOR CERTIFICATE

I, FILMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF, THIS CERTIFICATE IS EXECUTED AT CARLSBAD, NEW MEXICO, THIS 20 DAY OF FEBRUARY, 2018

FILMON F. JARAMILLO PLS. 12797
301 SOUTH CANAL
(575) 234-3341

MADRON SURVEYING, INC
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 86220
Phone (575) 234-3341

SURVEY NO. 6050

GENERAL NOTES

- 1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.
- 2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.

SHEET: 1-4

MADRON SURVEYING, INC. CARLSBAD, NEW MEXICO

FLOWLINE PLAT

TWO-8" FLOWLINES & ONE-8" GAS LIFT LINE (BURIED IN THE SAME DITCH)
FROM GRUMPY CAT 15-22 FED ---- 213H & 214H TO TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF A PIPELINE CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
FEBRUARY 20, 2018

DESCRIPTION

A STRIP OF LAND 30 FEET WIDE CROSSING BUREAU OF LAND MANAGEMENT LAND IN SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., LEA COUNTY, STATE OF NEW MEXICO AND BEING 15 FEET EACH SIDE OF THE FOLLOWING DESCRIBED CENTERLINE SURVEY:

BEGINNING AT A POINT WITHIN THE NE/4 NE/4 OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., WHENCE THE NORTHEAST CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N64°13'52"E, A DISTANCE OF 1156.35 FEET;
THENCE S00°31'13"E A DISTANCE OF 61.35 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;
THENCE S89°28'47"W A DISTANCE OF 712.65 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;
THENCE S46°31'32"W A DISTANCE OF 128.61 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;
THENCE S89°28'47"W A DISTANCE OF 1420.44 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;
THENCE S00°00'00"W A DISTANCE OF 81.54 FEET THE TERMINUS OF THIS CENTERLINE SURVEY, WHENCE THE NORTHWEST CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N70°41'02"W, A DISTANCE OF 2137.37 FEET;

SAID STRIP OF LAND BEING 2404.60 FEET OR 145.73 RODS IN LENGTH, CONTAINING 1.656 ACRES MORE OR LESS AND BEING ALLOCATED BY FORTIES AS FOLLOWS:

NE/4 NE/4	338.72 L.F.	20.53 RODS	0.233 ACRES
NW/4 NE/4	1356.53 L.F.	82.21 RODS	0.934 ACRES
NE/4 NW/4	709.35 L.F.	42.99 RODS	0.489 ACRES

SURVEYOR CERTIFICATE

I, FILMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF THIS CERTIFICATE IS EXECUTED AT CARLSBAD,

NEW MEXICO, THIS 27 DAY OF FEBRUARY 2018

VADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341

GENERAL NOTES

1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.

2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.

SHEET: 2-4


MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO
(575) 234-3341

SURVEY NO. 6050

FLOWLINE PLAT

TWO-8" FLOWLINES & ONE-8" GAS LIFT LINE (BURIED IN THE SAME DITCH)
FROM GRUMPY CAT 15-22 FED 213H & 214H TO TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF A PIPELINE CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
FEBRUARY 20, 2018

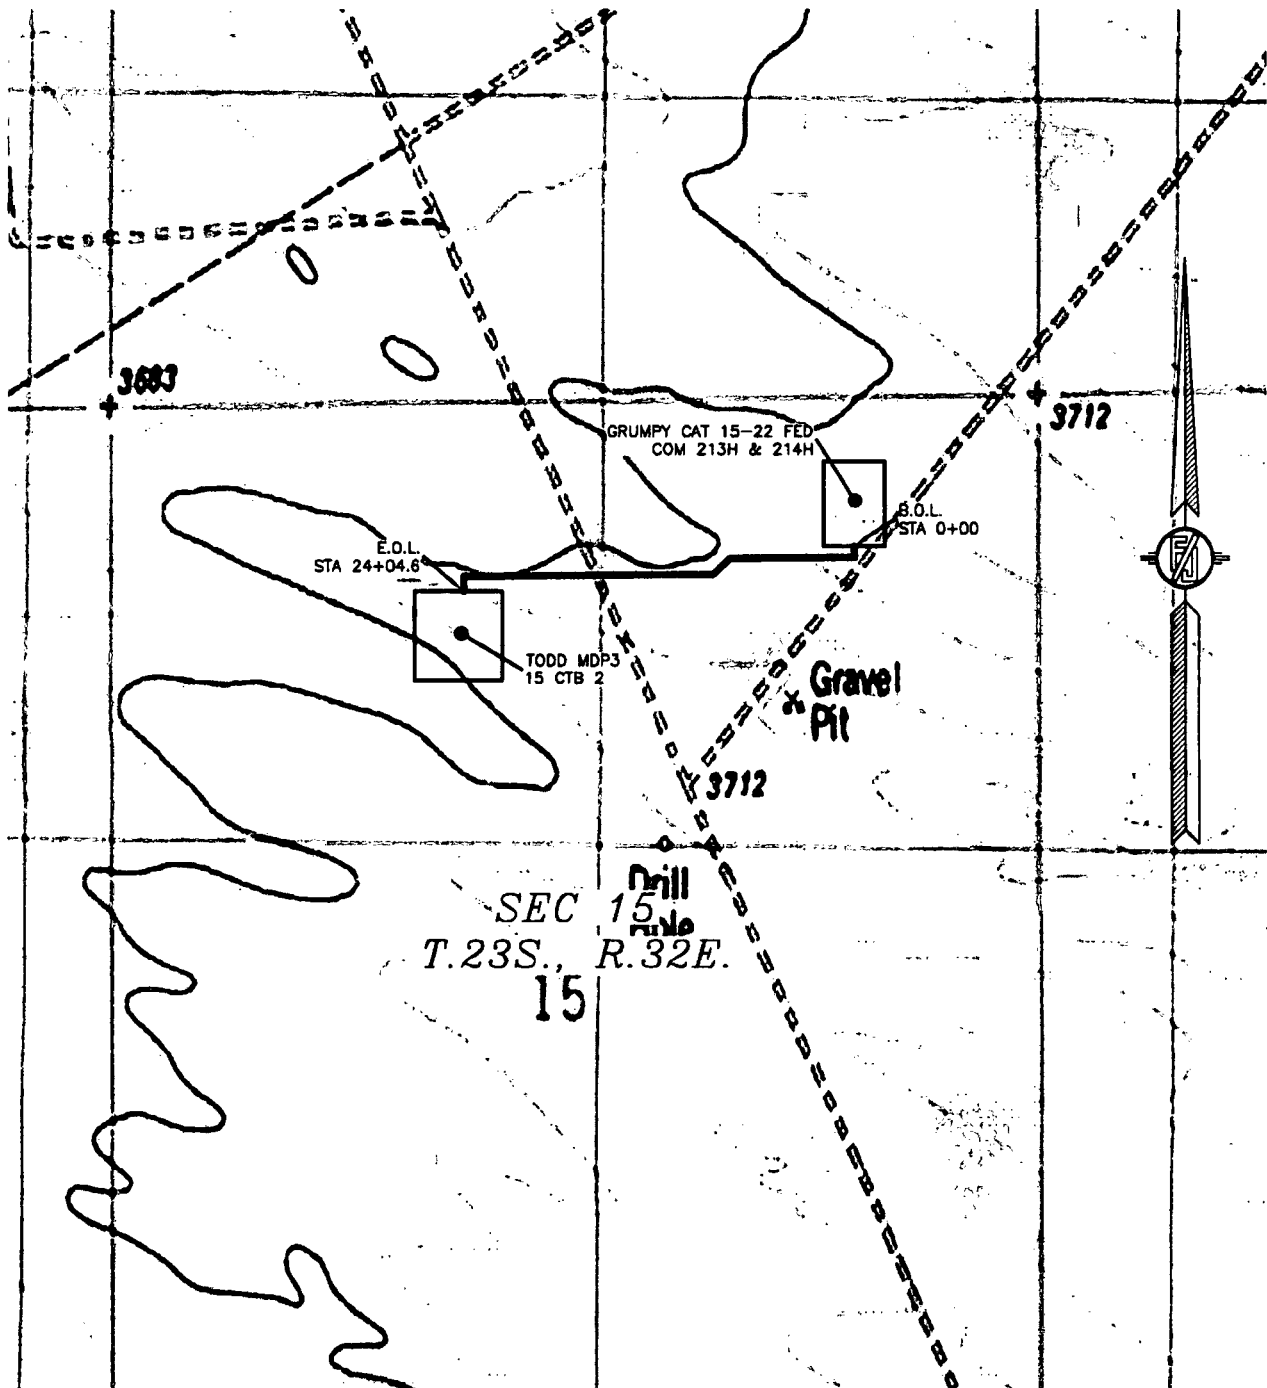

SHEET: 3-4

MADRON SURVEYING, INC.

301 SOUTH CANAL
(575) 234-3341


CARLSBAD, NEW MEXICO

SURVEY NO. 6050

FLOWLINE PLAT

**TWO-8" FLOWLINES & ONE-8" GAS LIFT LINE (BURIED IN THE SAME DITCH)
FROM GRUMPY CAT 15-22 FED 213H & 214H TO TODD MDP3 15 CTB 2**


**DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF A PIPELINE CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
FEBRUARY 20, 2018**

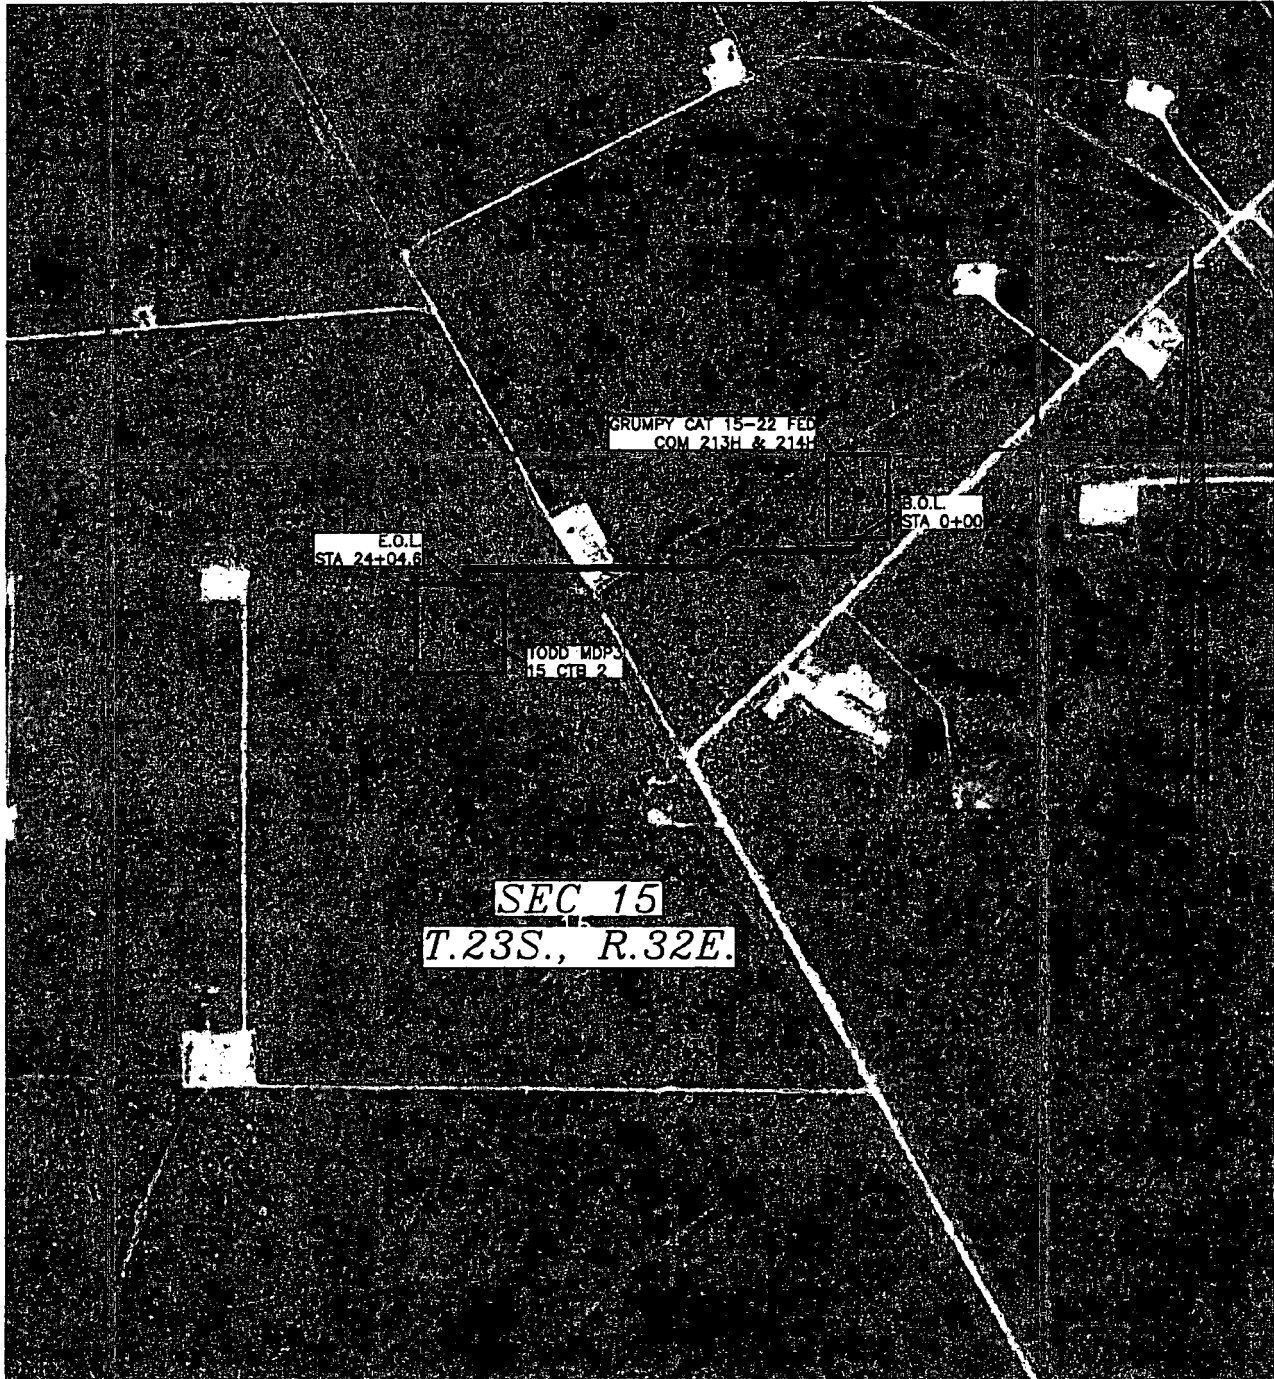

TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
IN THE NE/4 NW/4 OF
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

OCTOBER 2, 2017

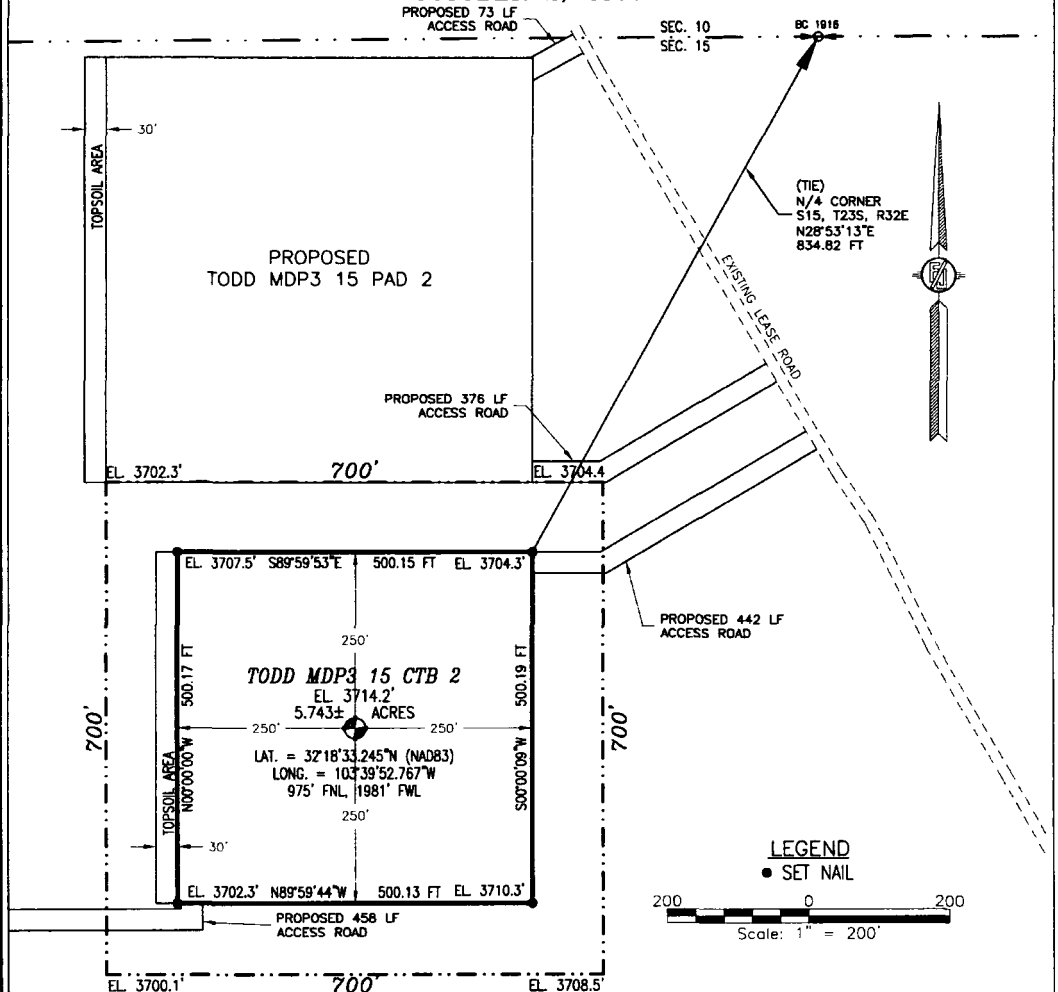

DESCRIPTION

A CERTAIN PIECE OR PARCEL OF LAND AND REAL ESTATE LYING IN THE NE/4 NW/4 OF SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST N.M.P.M., LEA COUNTY, NEW MEXICO.

BEGINNING AT THE NORTHEAST CORNER OF THE PARCEL, WHENCE THE NORTH QUARTER CORNER OF SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N28°53'13"E, A DISTANCE OF 834.82 FEET; THENCE S00°00'09"W A DISTANCE OF 500.19 FEET TO THE SOUTHEAST CORNER OF THE PARCEL; THENCE N89°59'44"W A DISTANCE OF 500.13 FEET TO THE SOUTHWEST CORNER OF THE PARCEL; THENCE N00°00'00"W A DISTANCE OF 500.17 FEET TO THE NORTHWEST CORNER OF THE PARCEL; THENCE S89°59'53"E A DISTANCE OF 500.15 FEET TO THE NORTHEAST CORNER OF THE PARCEL, TO THE POINT OF BEGINNING; CONTAINING 5.743 ACRES MORE OR LESS.

GENERAL NOTES

1.) THE INTENT OF THIS SURVEY IS TO ACQUIRE A BUSINESS LEASE FOR THE PURPOSE OF BUILDING A CENTRAL TANK BATTERY

2.) BASIS OF BEARING IS NEW MEXICO STATE PLANE EAST ZONE MODIFIED TO THE SURFACE (NAD83)

DRIVING DIRECTIONS: FROM INTERSECTION OF RED ROAD AND STATE HIGHWAY 128 GO EAST ON STATE HIGHWAY 128 APPROX. 1.2 MILES TO A PIPELINE ROAD ON LEFT (NORTH) TURN NORTHEAST ON PIPELINE ROAD AND GO NORTHEAST APPROX. 5.4 MILES TO A LEASE ROAD ON LEFT (NORTH) TURN NORTH GO APPROX. 1.0 MILE TO A LEASE ROAD ON LEFT (WEST) TURN WEST GO APPROX. 0.7 OF A MILE, ROAD TURNS RIGHT (NORTH) GO NORTH APPROX. 0.4 OF A MILE TO ROAD LATH WITH RED & WHITE FLAGGING ON RIGHT (EAST) GO EAST 988' THEN NORTH 23' TO SOUTHWEST PAD CORNER FOR THIS LOCATION.

SHEET: 1-3

MADRON SURVEYING, INC. CARLSBAD, NEW MEXICO

SURVEYOR CERTIFICATE

I, FILMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF, THIS CERTIFICATE IS EXECUTED AT CARLSBAD,

NEW MEXICO, THIS 3 DAY OF OCTOBER 2017

Filmon F. Jaramillo
FILMON F. JARAMILLO, P.S. 12797
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341

MADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341


SURVEY NO. 4968A

TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
IN THE NE/4 NW/4 OF
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

OCTOBER 2, 2017

QUAD MAP

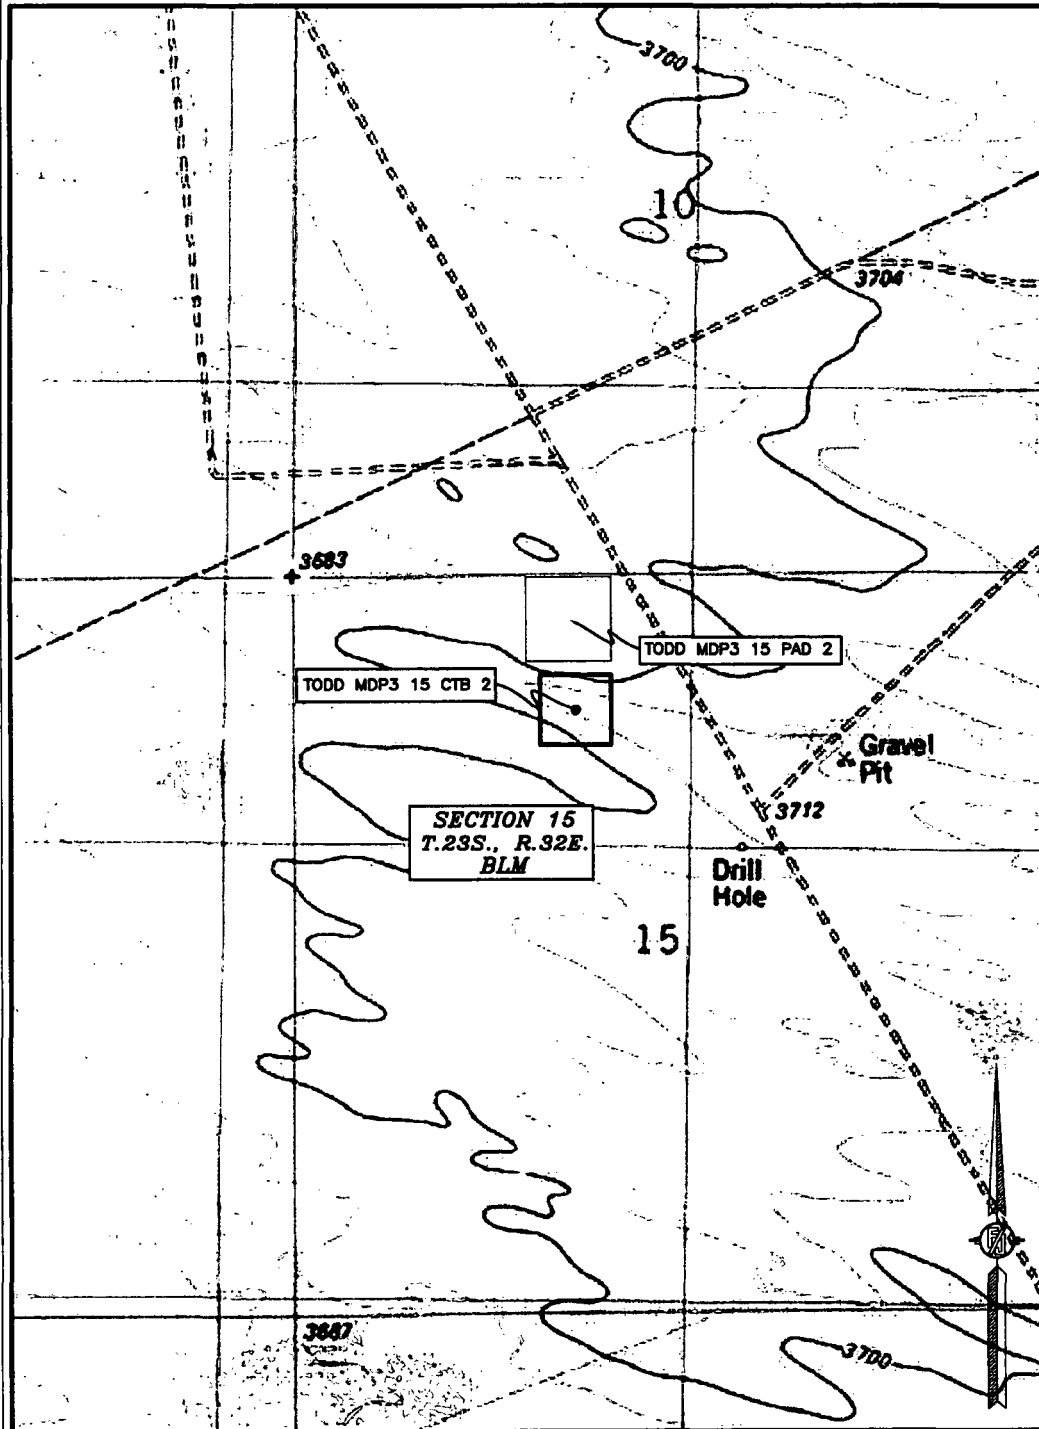

SHEET: 2-3

MADRON SURVEYING, INC. 301 SOUTH CANAL (575) 234-3341 CARLSBAD, NEW MEXICO


SURVEY NO. 4968A

TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
IN THE NE/4 NW/4 OF
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

OCTOBER 2, 2017

AERIAL PHOTO

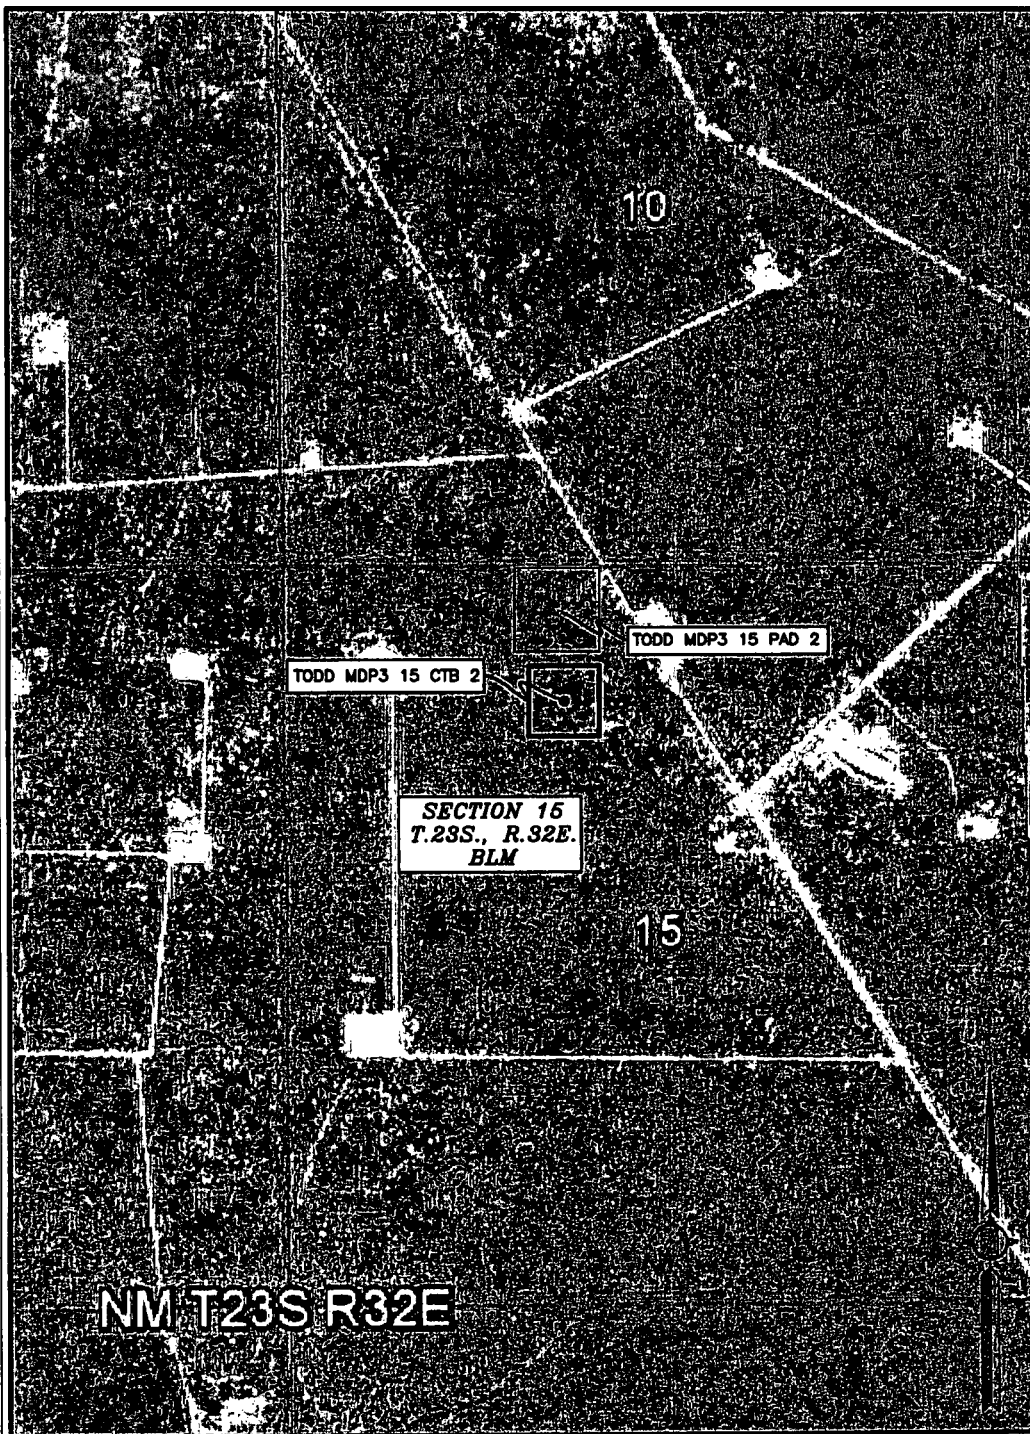

SHEET: 3-3


SURVEY NO. 4968A

MADRON SURVEYING, INC.

301 SOUTH CANAL
(575) 234-3341

CARLSBAD, NEW MEXICO

PLAN VIEW

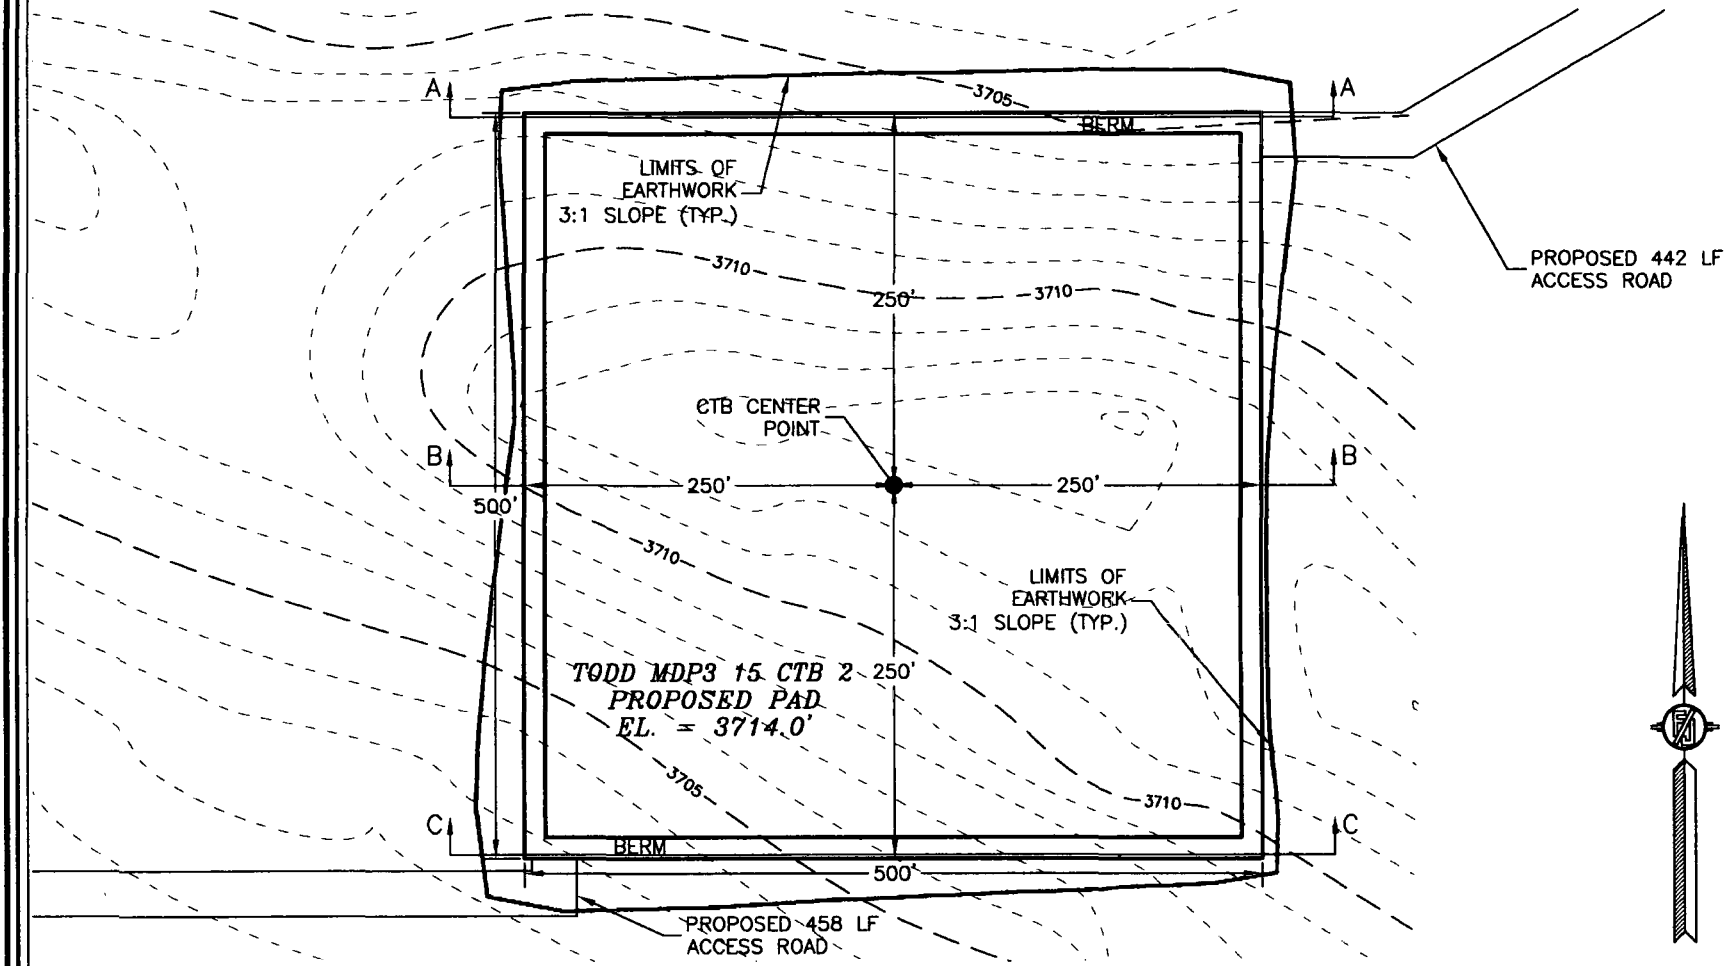

DEVON ENERGY PRODUCTION COMPANY, L.P.
GRADING PLAN AND CROSS SECTIONS
TODD MDP3 15 CTB 2
SECTION 15, TOWNSHIP 23 SOUTH,
RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO

012 60 120 240
SCALE 1" = 120'




CUT	FILL	NET
1 CU. YD	47087 CU. YD	47085 CU. YD (FILL)

EARTHWORK QUANTITIES ARE ESTIMATED

OCTOBER 2, 2017
MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO
(575) 234-3341

SHEET 1-2
SURVEY NO. 4968A

CROSS SECTIONS

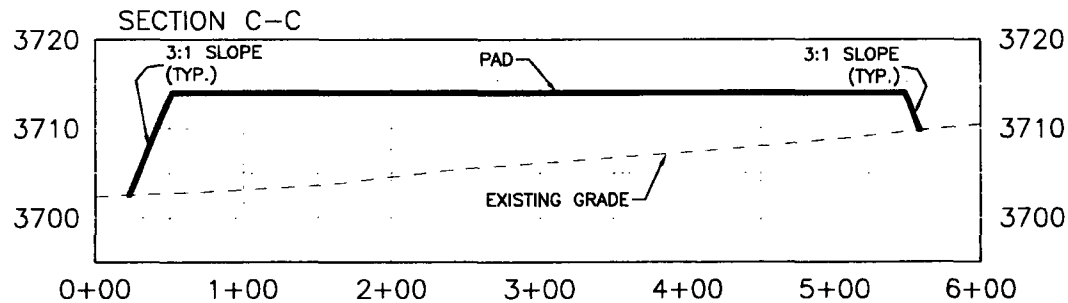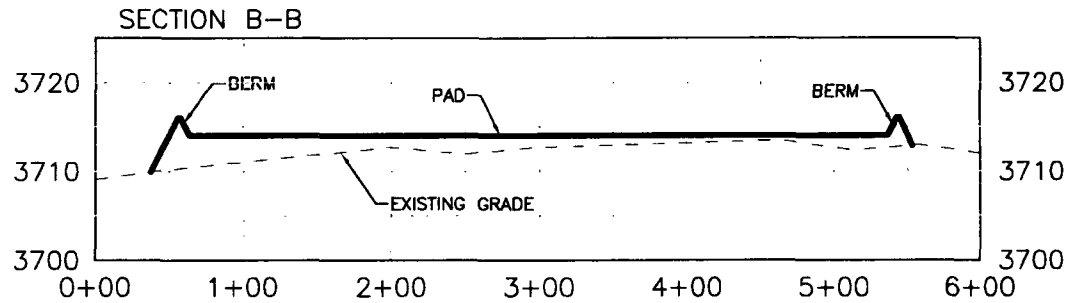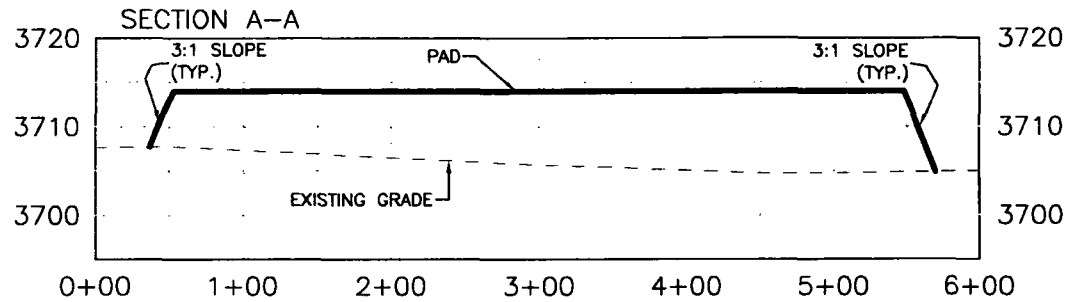

DEVON ENERGY PRODUCTION COMPANY, L.P.
 GRADING PLAN AND CROSS SECTIONS
TODD MDP3 15 CTB 2
 SECTION 15, TOWNSHIP 23 SOUTH,
 RANGE 32 EAST, N.M.P.M.
 LEA COUNTY, STATE OF NEW MEXICO

012 60 120 240
 SCALE 1" = 120' - 1" = 20' VER


OCTOBER 2, 2017

MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO

SHEET 2-2
 SURVEY NO. 4968A


ACCESS ROAD PLAT
ACCESS ROAD TO THE TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF AN ACCESS ROAD CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
OCTOBER 2, 2017

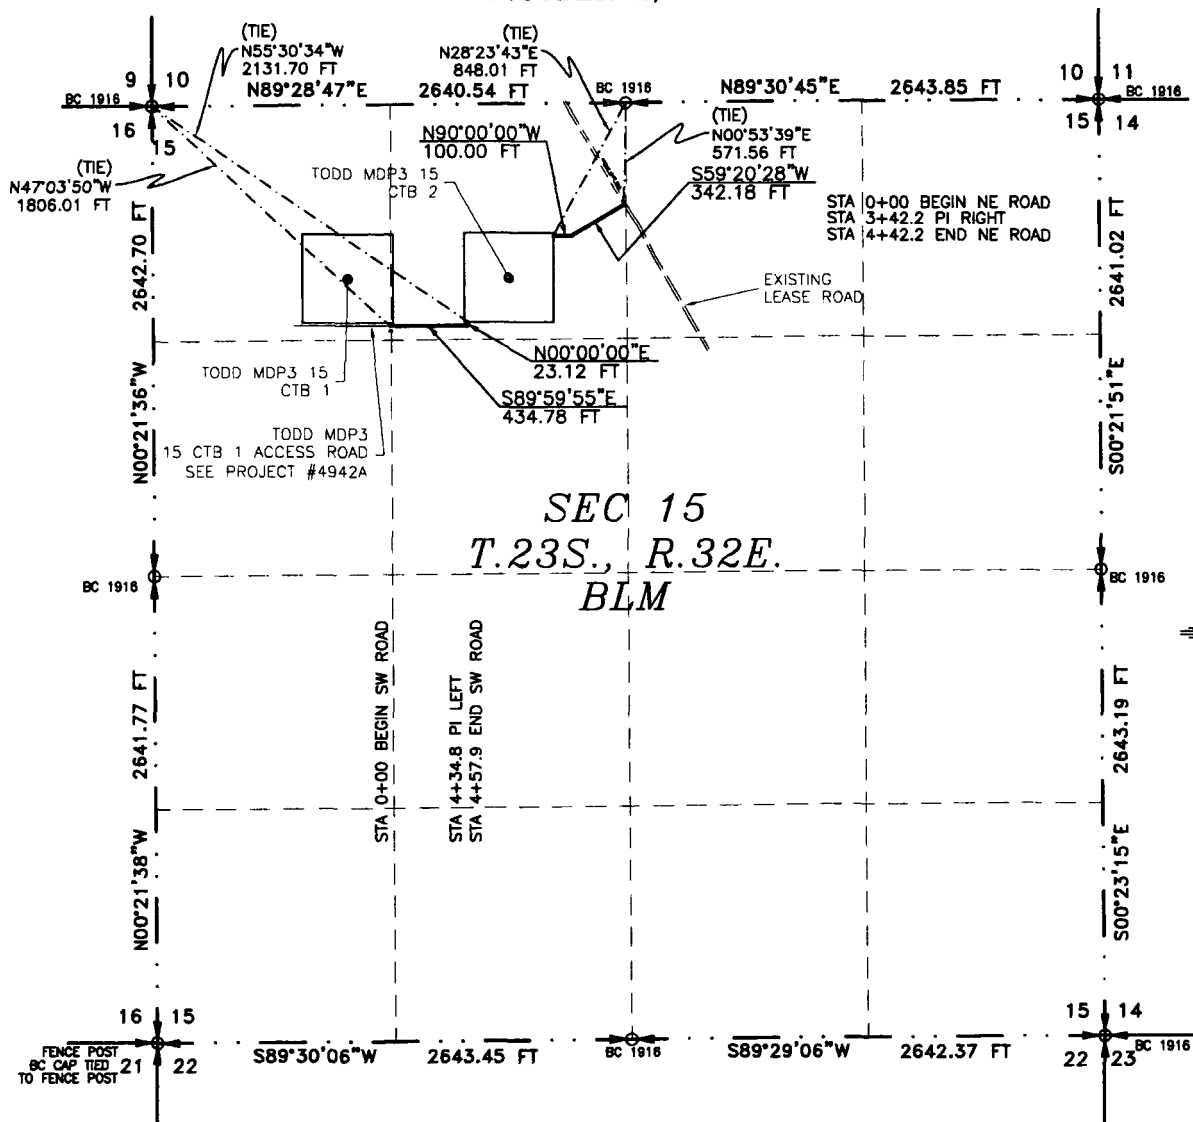

SEC 15
T.23S., R.32E.
BLM

SEE NEXT SHEET (2-2) FOR DESCRIPTION



GENERAL NOTES

1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.

2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.

SHEET: 1-2

MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO (575) 234-3341

SURVEYOR CERTIFICATE

I, FILMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF, THIS CERTIFICATE IS EXECUTED AT CARLSBAD,

NEW MEXICO, THIS 3 DAY OF OCTOBER 2017

Filmon F. Jaramillo
FILMON F. JARAMILLO PLS. 12797

MADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341

SURVEY NO. 4968A

ACCESS ROAD PLAT
ACCESS ROAD TO THE TODD MDP3 15 CTB 2

DEVON ENERGY PRODUCTION COMPANY, L.P.
CENTERLINE SURVEY OF AN ACCESS ROAD CROSSING
SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M.
LEA COUNTY, STATE OF NEW MEXICO
OCTOBER 2, 2017

DESCRIPTION

A STRIP OF LAND 30 FEET WIDE CROSSING BUREAU OF LAND MANAGEMENT LAND IN SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., LEA COUNTY, STATE OF NEW MEXICO AND BEING 15 FEET EACH SIDE OF THE FOLLOWING DESCRIBED CENTERLINE SURVEY:

SOUTHWEST ACCESS ROAD

BEGINNING AT A POINT WITHIN THE NW/4 NW/4 OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., WHENCE THE NORTHWEST CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N47°03'50"W, A DISTANCE OF 1806.01 FEET;

THENCE S89°59'55"E A DISTANCE OF 434.78 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;

THENCE N00°00'00"E A DISTANCE OF 23.12 FEET THE TERMINUS OF THIS CENTERLINE SURVEY, WHENCE THE NORTHWEST CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N55°30'34"W, A DISTANCE OF 2131.70 FEET;

SAID STRIP OF LAND BEING 457.90 FEET OR 27.75 RODS IN LENGTH, CONTAINING 0.315 ACRES MORE OR LESS AND BEING ALLOCATED BY FORTIES AS FOLLOWS:

NW/4 NW/4	6.16 L.F.	0.37 RODS	0.004 ACRES
NE/4 NW/4	451.74 L.F.	27.38 RODS	0.311 ACRES

NORTHEAST ACCESS ROAD

BEGINNING AT A POINT WITHIN THE NW/4 NE/4 OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M., WHENCE THE NORTH QUARTER CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N00°53'39"E, A DISTANCE OF 571.56 FEET;

THENCE S59°20'28"W A DISTANCE OF 342.18 FEET TO AN ANGLE POINT OF THE LINE HEREIN DESCRIBED;

THENCE N90°00'00"W A DISTANCE OF 100.00 FEET THE TERMINUS OF THIS CENTERLINE SURVEY, WHENCE THE NORTH QUARTER CORNER OF SAID SECTION 15, TOWNSHIP 23 SOUTH, RANGE 32 EAST, N.M.P.M. BEARS N28°23'43"E, A DISTANCE OF 848.01 FEET;

SAID STRIP OF LAND BEING 442.18 FEET OR 26.80 RODS IN LENGTH, CONTAINING 0.305 ACRES MORE OR LESS AND BEING ALLOCATED BY FORTIES AS FOLLOWS:

NE/4 NW/4	442.18 L.F.	26.80 RODS	0.305 ACRES
-----------	-------------	------------	-------------

SURVEYOR CERTIFICATE

I, FILIMON F. JARAMILLO, A NEW MEXICO PROFESSIONAL SURVEYOR NO. 12797, HEREBY CERTIFY THAT I HAVE CONDUCTED AND AM RESPONSIBLE FOR THIS SURVEY, THAT THIS SURVEY IS TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF, AND THAT THIS SURVEY AND PLAT MEET THE MINIMUM STANDARDS FOR LAND SURVEYING IN THE STATE OF NEW MEXICO.

IN WITNESS WHEREOF, THIS CERTIFICATE IS EXECUTED AT CARLSBAD,

NEW MEXICO, THIS 3 DAY OF OCTOBER 2017

GENERAL NOTES

1.) THE INTENT OF THIS ROUTE SURVEY IS TO ACQUIRE AN EASEMENT.

2.) BASIS OF BEARING AND DISTANCE IS NMSP EAST (NAD83) MODIFIED TO SURFACE COORDINATES. NAD 83 (FEET) AND NAVD 88 (FEET) COORDINATE SYSTEMS USED IN THE SURVEY.


SHEET: 2-2

MADRON SURVEYING, INC. 301 SOUTH CANAL CARLSBAD, NEW MEXICO
(575) 234-3341

MADRON SURVEYING, INC.
301 SOUTH CANAL
CARLSBAD, NEW MEXICO 88220
Phone (575) 234-3341

SURVEY NO. 4968A

EXHIBIT "A"
PAGE 1 of 4
ELECTRIC LINE PLAT
SECTION 15, T23S-R32E, N.M.P.M.
LEA COUNTY, NEW MEXICO

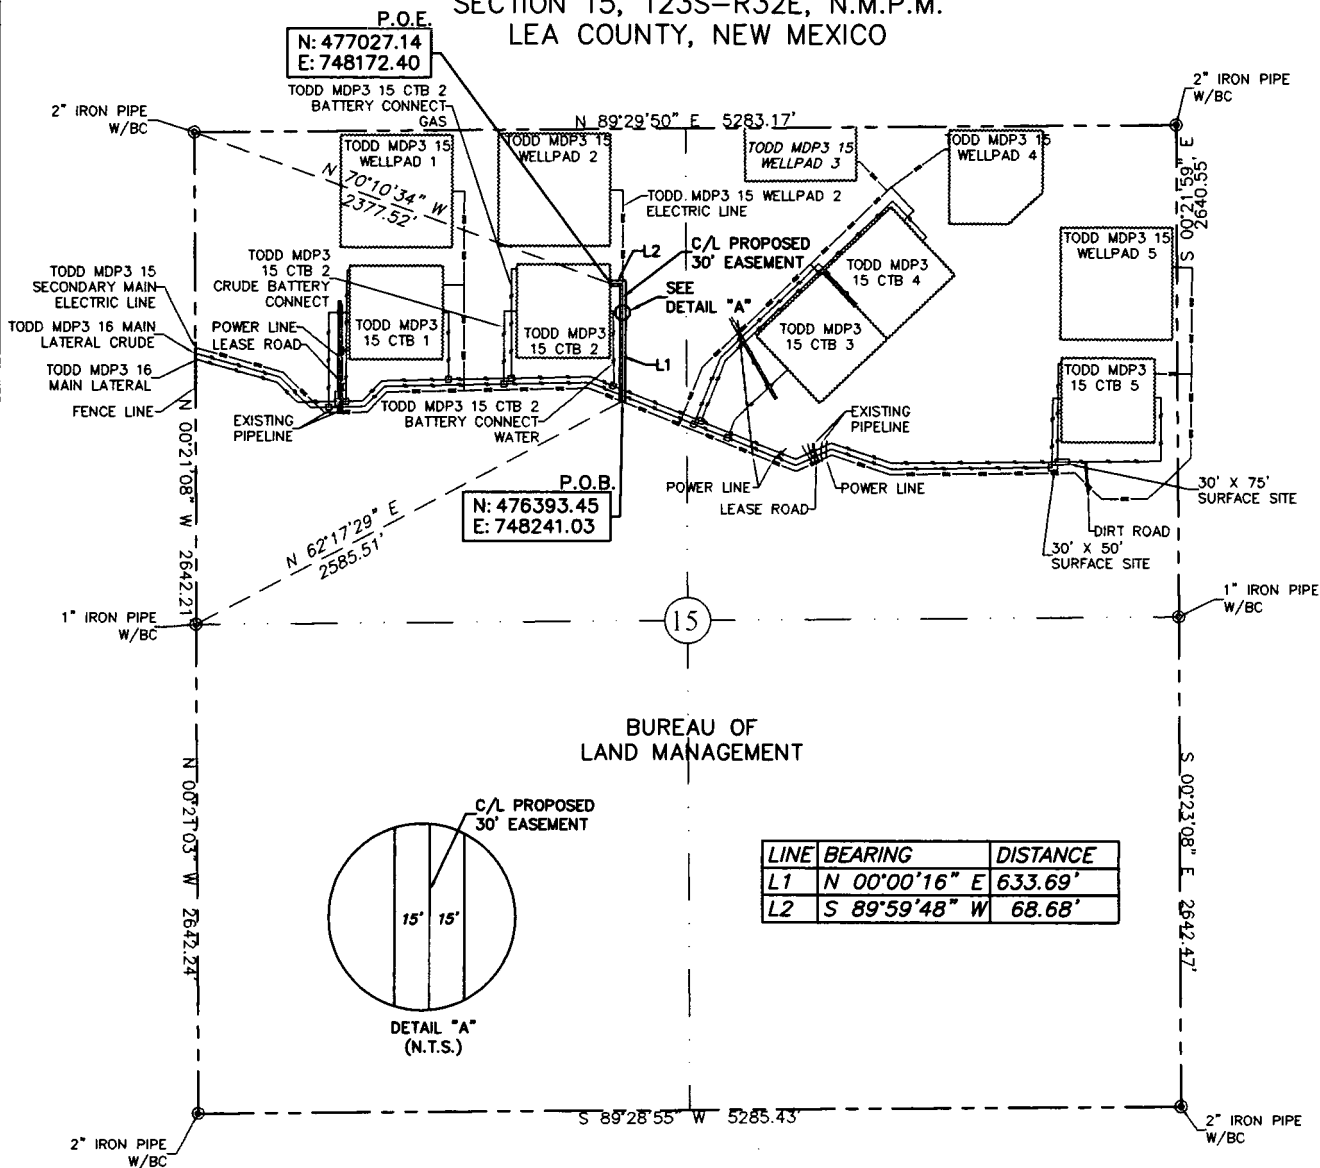


30' EASEMENT AREA = 0.484 ACRE(S)
702.37 FEET OR 42.57 RODS

SEE THE ATTACHED LEGAL DESCRIPTION

Note: All bearings recited herein are based on the New Mexico State Plane Coordinate System, NAD 83, New Mexico East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.

B.L. Laman PLS #22404
Date Signed: 10-10-2017
924 Richardson Dr., Jasper, TX.
(903) 388-3045 75951
Employee of Horizonrow, LLC



HORIZON ROW LLC

Drawn for:

devon

Drawn by:
JEANNIE PERRY

Date: 09/25/2017

DEVON ENERGY PRODUCTION COMPANY, L.P.

TODD MDP3 15 CTB 2
ELECTRIC LINE

PROPOSED 30' EASEMENT
ON THE PROPERTY OF
BUREAU OF LAND MANAGEMENT
SECTION 15, T23S-R32E, N.M.P.M.

LINE NUMBER:
EL7881

WBS NUMBER:
XX-125607.AL

SCALE:
1" = 1000'

REVISIONS:

SHEET:
1 OF 4

0+00 P.O.B./TODD MDP3 15 SECONDARY MAIN EL
0+32.3 TODD MDP3 16 MAIN LATERAL GAS/WATER
0+64.6 TODD MDP3 16 MAIN LATERAL CRUDE
2+11.5 STAKED POWER POLE
4+22.6 STAKED POWER POLE
6+33.7 STAKED POWER POLE/TODD MDP3 15 WELLPAD 2 EL
7+02.4 P.O.E./TODD MDP3 15 CTB 2

0 1000 2000

**SECTION 15, T23S-R32E, N.M.P.M.,
LEA COUNTY, NEW MEXICO**

ELECTRIC LINE PLAT

LEGAL DESCRIPTION

FOR

DEVON ENERGY PRODUCTION COMPANY, L.P.

BUREAU OF LAND MANAGEMENT

30' EASEMENT DESCRIPTION:

BEING an easement thirty (30) feet in width lying fifteen (15) feet on the right side and fifteen (15) feet on the left side of the survey centerline described below, being out of the northwest quarter (NW ¼) of Section 15, Township 23 South, Range 32 East, N.M.P.M., Lea County, New Mexico, and being out of a parcel of land owned by the Bureau of Land Management. Said centerline of easement being more particularly described as follows:

Commencing from a 1" iron pipe w/ BC found for the west quarter corner of Section 15, T23S-R32E, N.M.P.M., Lea County, New Mexico;

Thence N 62°17'29" E a distance of 2585.51' to the **Point of Beginning** of this easement having coordinates of Northing=476393.45 feet, Easting=748241.03 feet, and continuing the following courses;

Thence N 00°00'16" E, a distance of 633.69' to an angle point;

Thence S 89°59'48" W, a distance of 68.68' to the **Point of Ending** having coordinates of Northing=477027.14 feet, Easting=748172.40 feet, in Section 15, T23S-R32E, from said point a 2" iron pipe w/ BC found for the northwest corner of Section 15, T23S-R32E, N.M.P.M., Lea County, New Mexico bears N 70°10'34" W, a distance of 2377.52', covering **702.37' or 42.57 rods** and having an area of **0.484 acres**.

NOTES:

Bearings, distances and coordinates shown herein are based on New Mexico State Plane Coordinate System, NAD 83, East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.


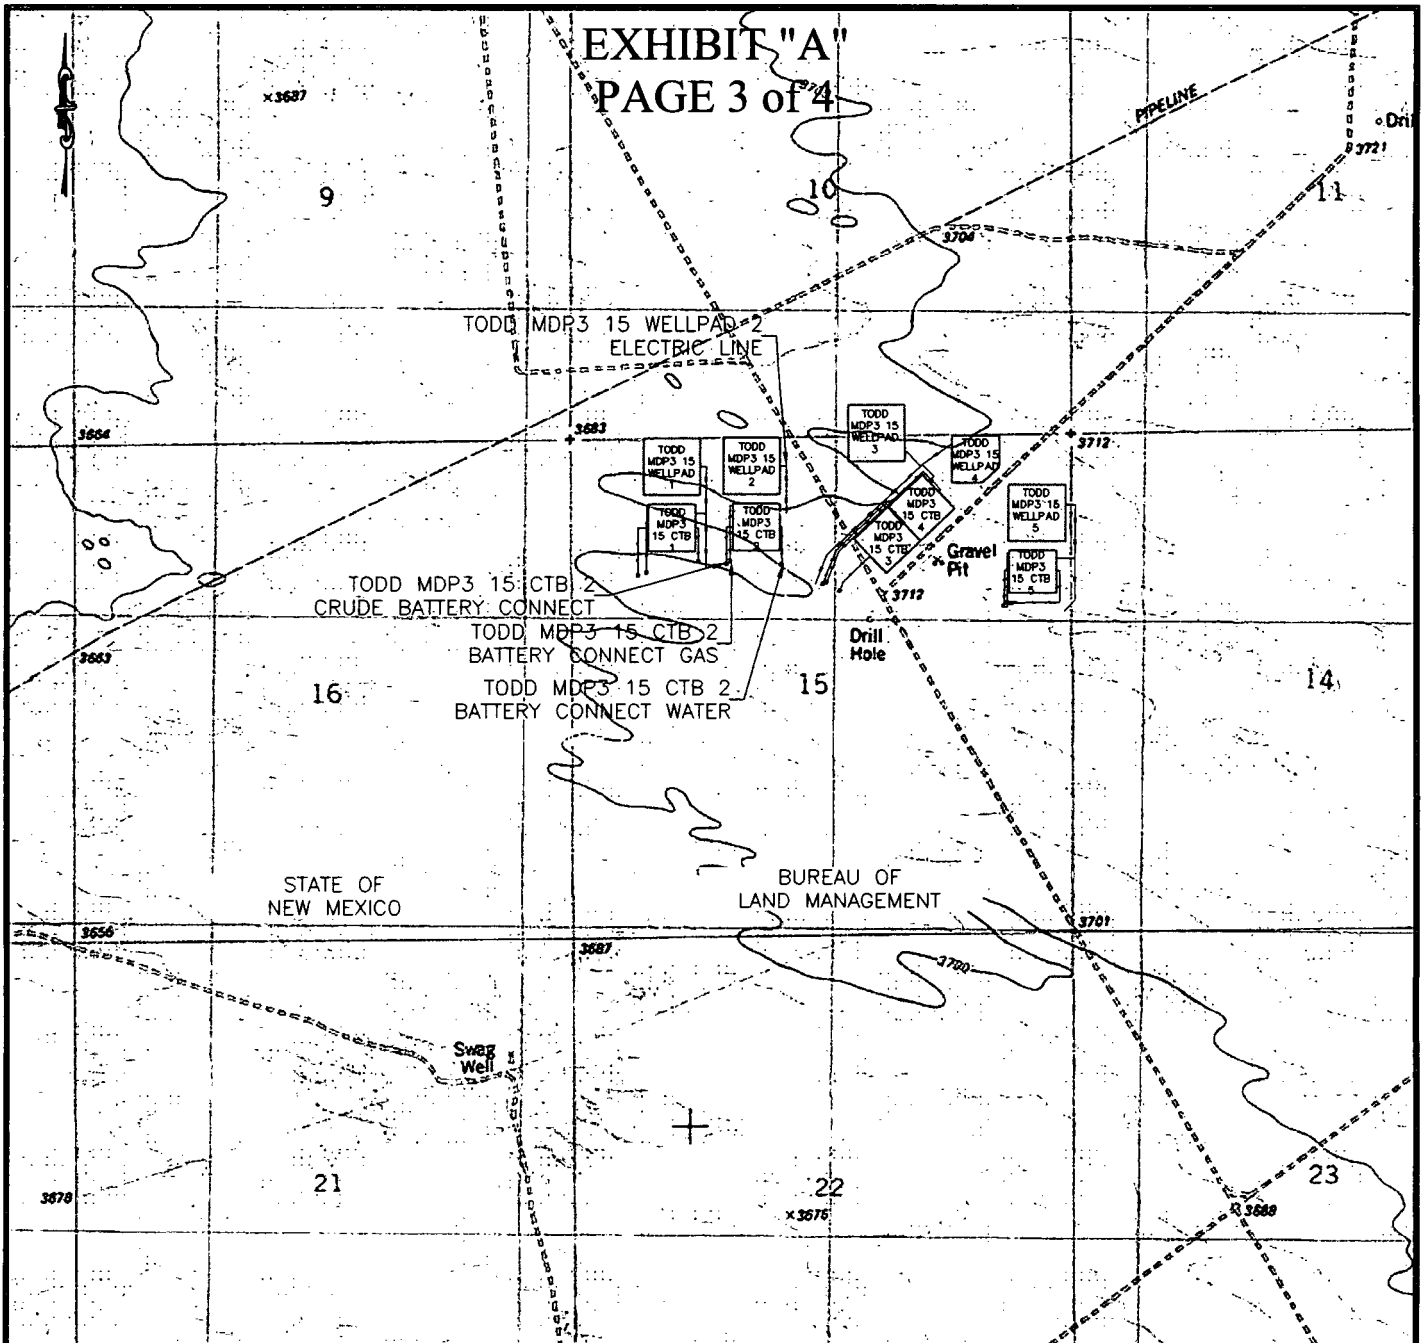

B.L. Laman PLS 22404
Date Signed: 10/10/2017
Horizon Row, LLC
924 Richardson Dr., Jasper, TX
(903) 388-3045 75951
Employee of Horizon Row, LLC



EXHIBIT "A"

PAGE 3 of 4



QUAD MAP

SECTION 15, T23S-R32E, N.M.P.M.;
LEA COUNTY, NEW MEXICO

HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

PROPOSED 30' EASEMENT

Drawn by:
JEANNIE PERRY

Date: 09/25/2017

Drawn for:

devon

LINE NUMBER:
EL7881

WBS NUMBER:
XX-125607.AL


SCALE:
1" = 2000'

REVISIONS:

SHEET:
3 OF 4

EXHIBIT "A"

PAGE 4 of 4

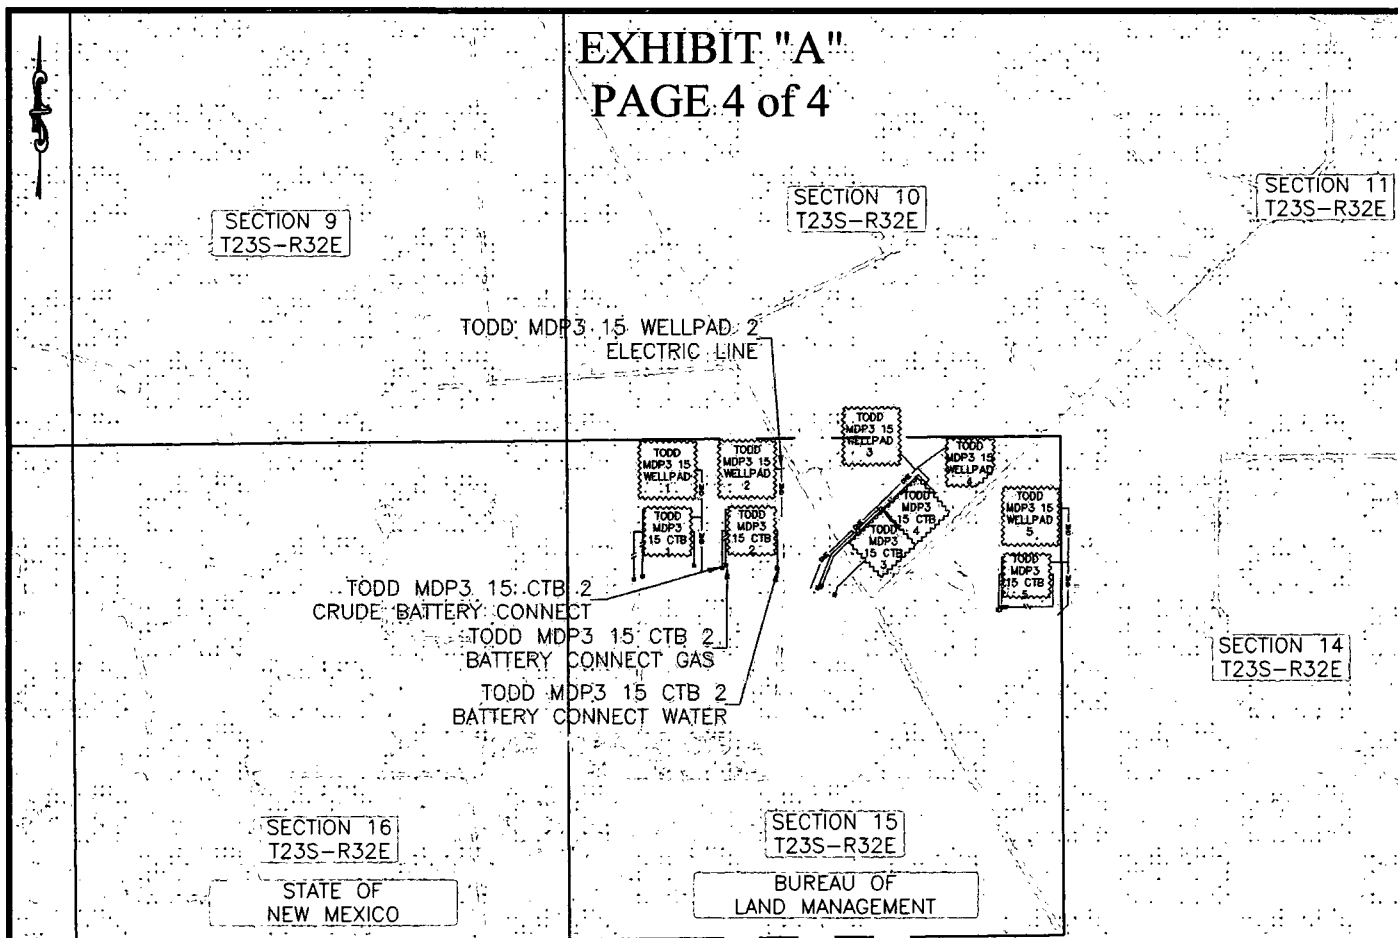

AERIAL MAP

SECTION 15, T23S-R32E, N.M.P.M.;
LEA COUNTY, NEW MEXICO


HORIZON ROW LLC	
DEVON ENERGY PRODUCTION CO., L.P.	
PROPOSED 30' EASEMENT	
Drawn by: JEANNIE PERRY	Date: 09/25/2017

Drawn for:



LINE NUMBER: EL7881
WBS NUMBER: XX-125607.AL
SCALE: 1" = 2000'
REVISIONS:
SHEET: 4 OF 4

EXHIBIT "A"
PAGE 1 of 4
ELECTRIC LINE PLAT
SECTION 15, T23S-R32E, N.M.P.M.
LEA COUNTY, NEW MEXICO

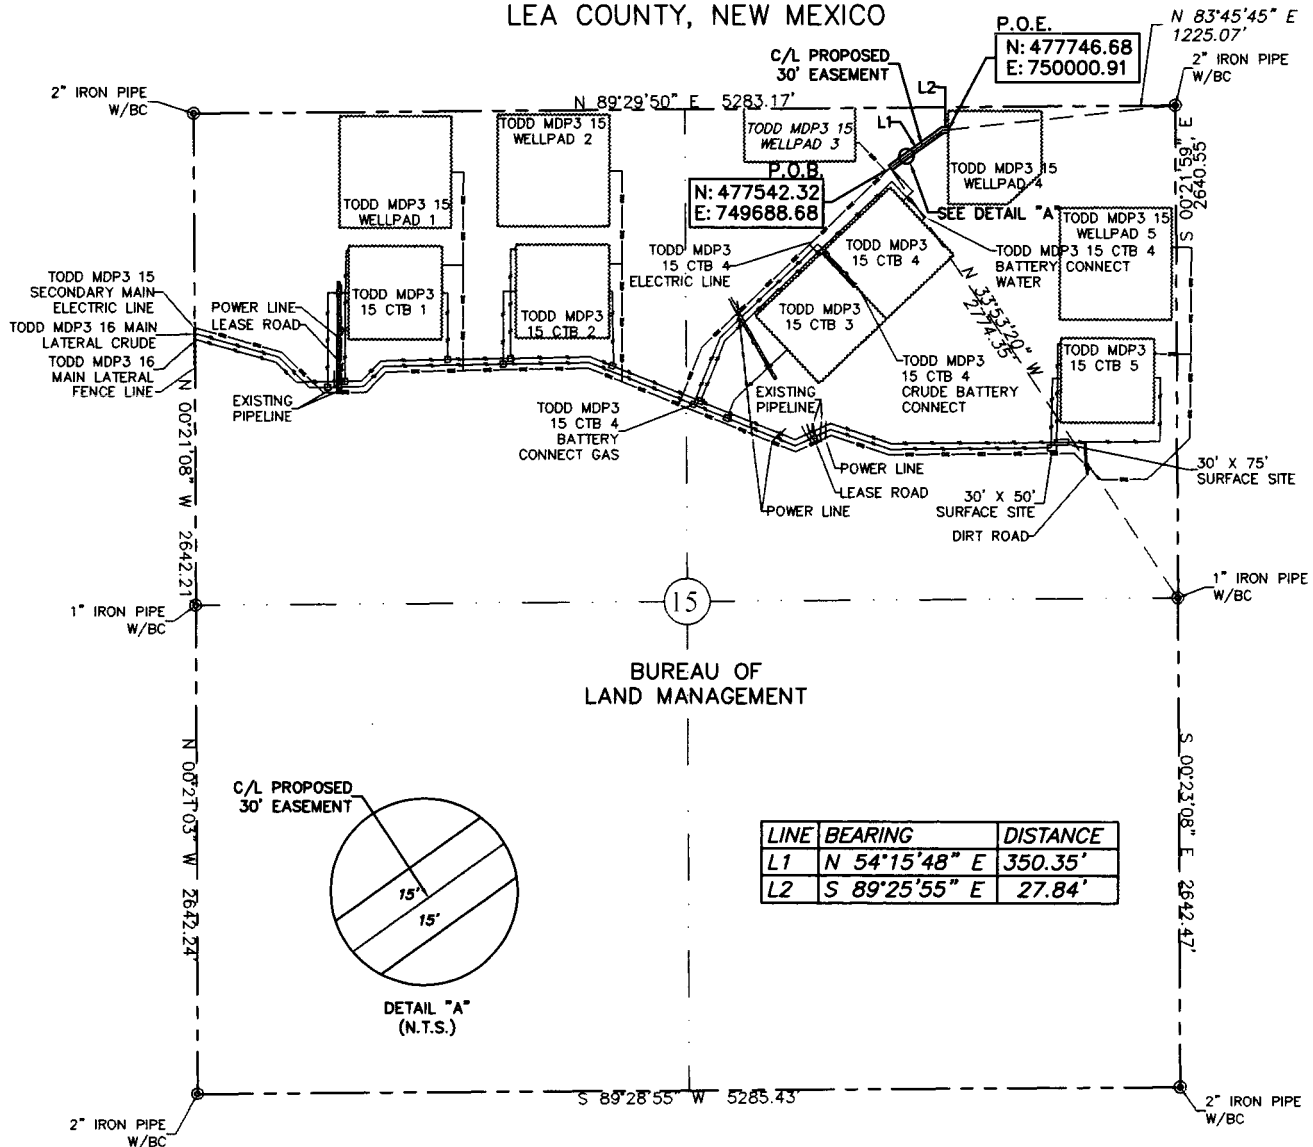

30' EASEMENT AREA = 0.260 ACRE(S)
378.19 FEET OR 22.92 RODS


0+00 P.O.B./TODD MDP3 15 CTB 4 EL
2+10.2 STAKED POWER POLE
3+50.4 STAKED POWER POLE
3+78.2 P.O.E./TODD MDP3 15 WELLPAD 4

SEE THE ATTACHED LEGAL DESCRIPTION

Note: All bearings recited herein are based on the New Mexico State Plane Coordinate System, NAD 83, New Mexico East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.

B.L. Laman PLS #22404
Date Signed: 10-10-2017
924 Richardson Dr., Jasper, TX.
(903) 388-3045 75951
Employee of Horizonrow, LLC



HORIZON ROW LLC

Drawn for:

Drawn by: JEANNIE PERRY Date: 09/27/2017

DEVON ENERGY PRODUCTION COMPANY, L.P.

TODD MDP3 15 WELLPAD 4
ELECTRIC LINE

PROPOSED 30' EASEMENT
ON THE PROPERTY OF
BUREAU OF LAND MANAGEMENT
SECTION 15, T23S-R32E, N.M.P.M.


LINE NUMBER:
EL7888

WBS NUMBER:
XX-128507.AL

SCALE:
1" = 1000'

REVISIONS:

SHEET:
1 OF 4



**SECTION 15, T23S-R32E, N.M.P.M.,
LEA COUNTY, NEW MEXICO**

ELECTRIC LINE PLAT

LEGAL DESCRIPTION

FOR

DEVON ENERGY PRODUCTION COMPANY, L.P.

BUREAU OF LAND MANAGEMENT

30' EASEMENT DESCRIPTION:

BEING an easement thirty (30) feet in width lying fifteen (15) feet on the right side and fifteen (15) feet on the left side of the survey centerline described below, being out of the northeast quarter (NE ¼) of Section 15, Township 23 South, Range 32 East, N.M.P.M., Lea County, New Mexico, and being out of a parcel of land owned by the Bureau of Land Management. Said centerline of easement being more particularly described as follows:

Commencing from a 1" iron pipe w/ BC found for the east quarter corner of Section 15, T23S-R32E, N.M.P.M., Lea County, New Mexico;

Thence N 33°53'20" W a distance of 2774.35' to the **Point of Beginning** of this easement having coordinates of Northing=477542.32 feet, Easting=749688.68 feet, and continuing the following courses;


Thence N 54°15'48" E, a distance of 350.35' to an angle point;

Thence S 89°25'55" E, a distance of 27.84' to the **Point of Ending** having coordinates of Northing=477746.68 feet, Easting=750000.91 feet, in Section 15, T23S-R32E, from said point a 2" iron pipe w/ BC found for the northeast corner of Section 15, T23S-R32E, N.M.P.M., Lea County, New Mexico bears N 83°45'45" E, a distance of 1225.07', covering **378.19' or 22.92 rods** and having an area of **0.260 acres**.

NOTES:

Bearings, distances and coordinates shown herein are based on New Mexico State Plane Coordinate System, NAD 83, East Zone 3001, US Survey Feet, all distances are grid.

I, B.L. Laman, New Mexico PLS No. 22404, hereby certify this survey to reflect an actual survey made on the ground under my supervision. This survey meets the minimum standards for surveying in New Mexico.



B.L. Laman PLS 22404

Date Signed: 10/10/2017
Horizon Row, LLC
924 Richardson Dr., Jasper, TX
(903) 388-3045 75951
Employee of Horizon Row, LLC



EXHIBIT "A"

PAGE 3 of 4

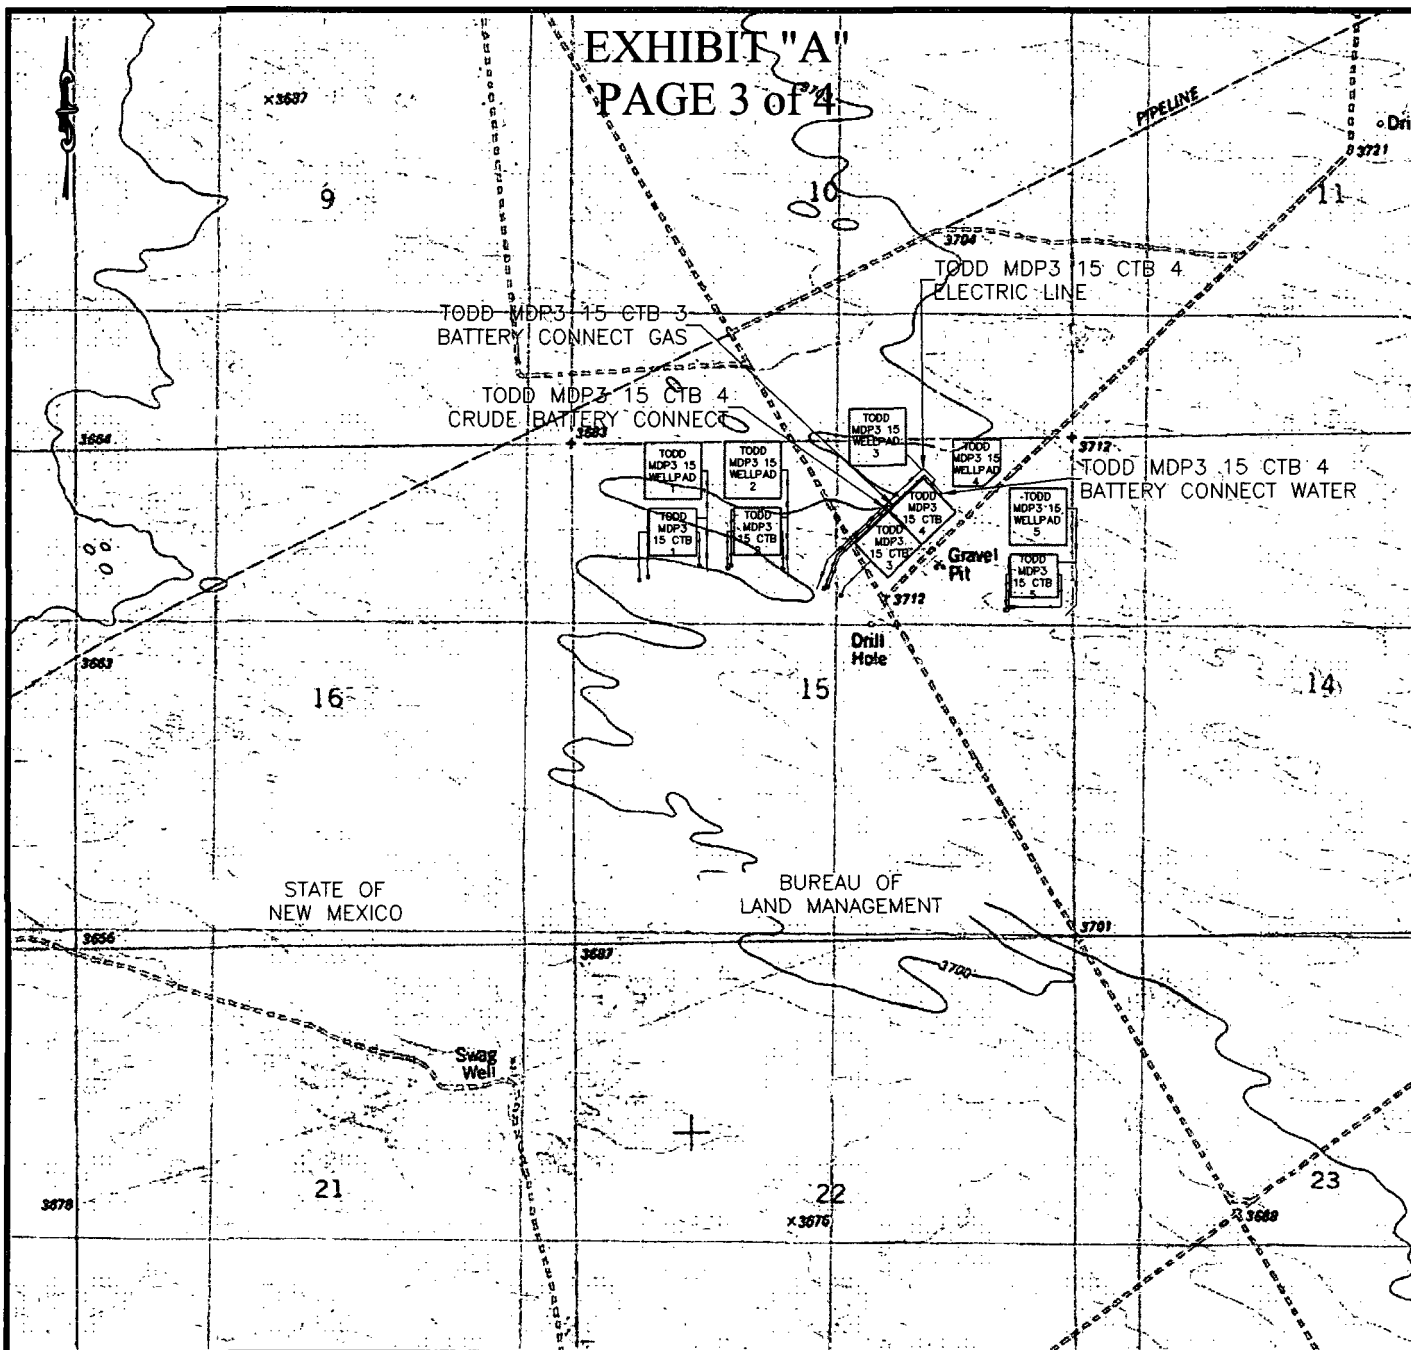

QUAD MAP

SECTION 15, T23S-R32E, N.M.P.M.;
LEA COUNTY, NEW MEXICO

HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

PROPOSED 30' EASEMENT

Drawn by:
JEANNIE PERRY

Date: 09/27/2017

Drawn for:



LINE NUMBER:
EL7888

WBS NUMBER:
XX-125607.AL


SCALE:
1" = 2000'

REVISIONS:

SHEET:
3 OF 4

EXHIBIT "A"

PAGE 4 of 4

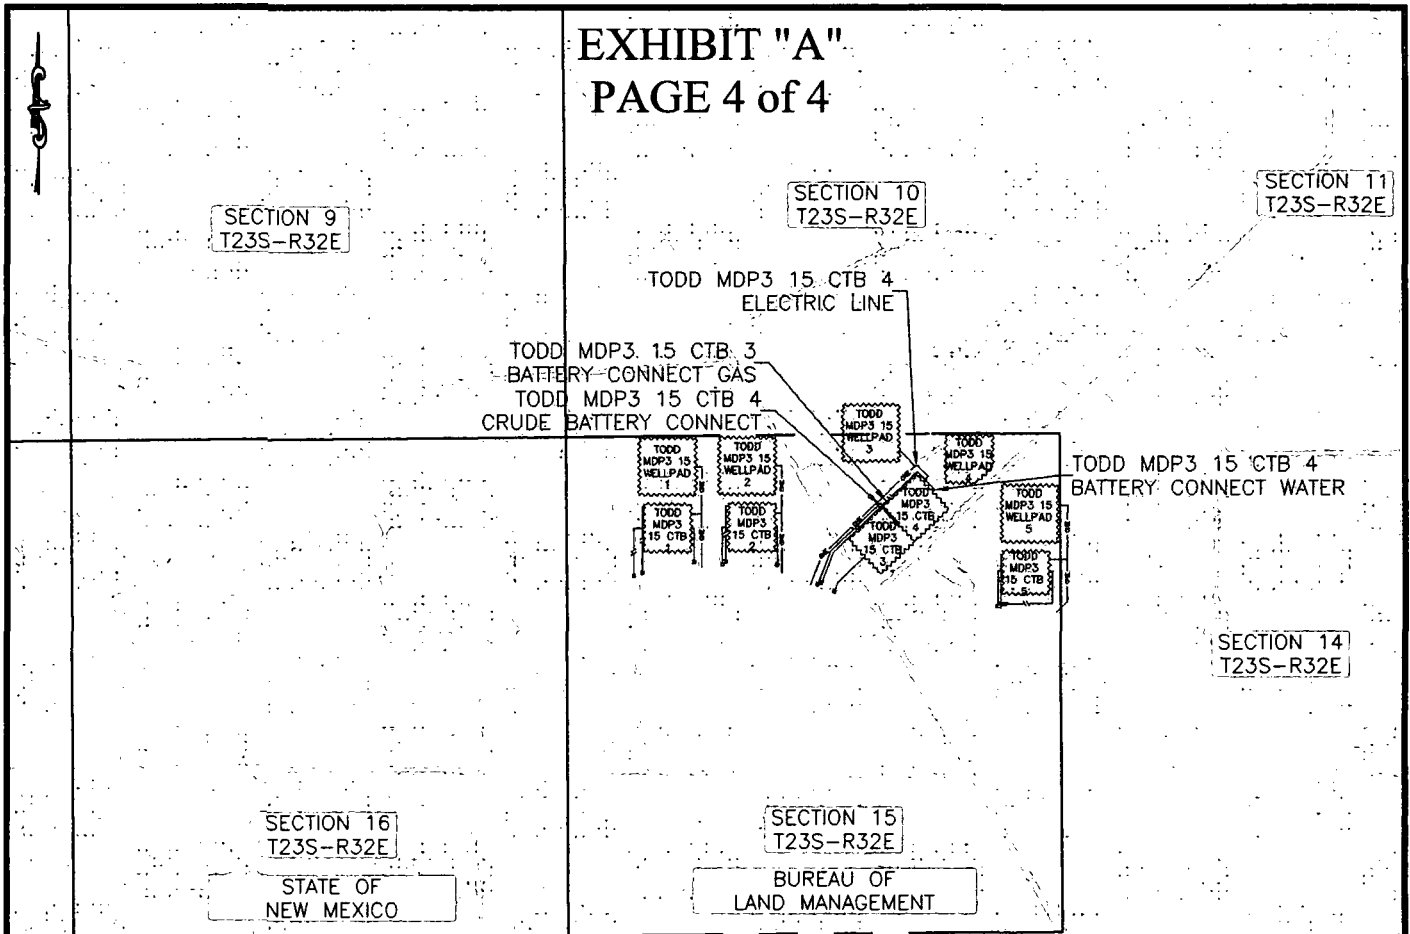

AERIAL MAP

SECTION 15, T23S-R32E, N.M.P.M.;
LEA COUNTY, NEW MEXICO

HORIZON ROW LLC

DEVON ENERGY PRODUCTION CO., L.P.

PROPOSED 30' EASEMENT

Drawn by:
JEANNIE PERRY

Date: 09/27/2017

Drawn for:



LINE NUMBER:
EL7888

WBS NUMBER:
XX-125807.AL

SCALE:
1" = 2000'

REVISIONS:

SHEET:
4 OF 4



Receipt

Your payment is submitted

Pay.gov Tracking ID: 26B5G93H

Agency Tracking ID: 75536864002

Form Name: Bureau of Land Management (BLM) Application for Permit to Drill (APD) Fee

Application Name: BLM Oil and Gas Online Payment

Payment Information

Payment Type: Bank account (ACH)

Payment Amount: \$9,790.00

Transaction Date: 07/24/2018 02:39:33 PM EDT

Payment Date: 07/25/2018

Company: DEVON ENERGY PRODUCTION CO., L.P.

APD IDs: 10400032225

Lease Numbers: NMNM084728

Well Numbers: 214H

Note: You will need your Pay.gov Tracking ID to complete your APD transaction in AFMSS II. Please ensure you write this number down upon completion of payment.

Account Information

Account Holder Name: Devon Energy Production Company, L.P.

Routing Number: 061000052

Account Number: *****9892

Email Confirmation Receipt

Confirmation Receipts have been emailed to:

JENNY.HARMS@DVN.COM

jeff.walla@dvn.com

lisa.othon@dvn.com



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

PWD Data Report

02/13/2019

Would you like to address long-term produced water disposal? NO

Would you like to utilize Lined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Lined pit PWD on or off channel:

Lined pit PWD discharge volume (bbl/day):

Lined pit specifications:

Pit liner description:

Pit liner manufacturers information:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Lined pit precipitated solids disposal schedule:

Lined pit precipitated solids disposal schedule attachment:

Lined pit reclamation description:

Lined pit reclamation attachment:

Leak detection system description:

Leak detection system attachment:

Lined pit Monitor description:

Lined pit Monitor attachment:

Lined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Lined pit bond number:

Lined pit bond amount:

Additional bond information attachment:

Would you like to utilize Unlined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Unlined pit PWD on or off channel:

Unlined pit PWD discharge volume (bbl/day):

Unlined pit specifications:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Unlined pit precipitated solids disposal schedule:

Unlined pit precipitated solids disposal schedule attachment:

Unlined pit reclamation description:

Unlined pit reclamation attachment:

Unlined pit Monitor description:

Unlined pit Monitor attachment:

Do you propose to put the produced water to beneficial use?

Beneficial use user confirmation:

Estimated depth of the shallowest aquifer (feet):

Does the produced water have an annual average Total Dissolved Solids (TDS) concentration equal to or less than that of the existing water to be protected?

TDS lab results:

Geologic and hydrologic evidence:

State authorization:

Unlined Produced Water Pit Estimated percolation:

Unlined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Unlined pit bond number:

Unlined pit bond amount:

Additional bond information attachment:

Would you like to utilize Injection PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Injection PWD discharge volume (bbl/day):

Injection well mineral owner:

Injection well type:

Injection well number:

Injection well name:

Assigned injection well API number?

Injection well API number:

Injection well new surface disturbance (acres):

Minerals protection information:

Mineral protection attachment:

Underground Injection Control (UIC) Permit?

UIC Permit attachment:

Would you like to utilize Surface Discharge PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Surface discharge PWD discharge volume (bbl/day):

Surface Discharge NPDES Permit?

Surface Discharge NPDES Permit attachment:

Surface Discharge site facilities information:

Surface discharge site facilities map:

Would you like to utilize Other PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Other PWD discharge volume (bbl/day):

Other PWD type description:

Other PWD type attachment:

Have other regulatory requirements been met?

Other regulatory requirements attachment:

Devon Energy, Grumpy Cat 15 Fed 214H

1. Geologic Formations

TVD of target	10,545	Pilot hole depth	N/A
MD at TD:	15,243	Deepest expected fresh water:	

Basin

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Rustler	1180		
Salado	1635		
Base of Salt	4905		
Delaware	4915		
1st BSPG Lime	8795		
2nd BSPG Sand	10545		

*H2S, water flows, loss of circulation, abnormal pressures, etc.



U.S. Department of the Interior
BUREAU OF LAND MANAGEMENT

Bond Info Data Report

02/13/2019

Federal/Indian APD: FED

BLM Bond number: CO1104

BIA Bond number:

Do you have a reclamation bond? NO

Is the reclamation bond a rider under the BLM bond?

Is the reclamation bond BLM or Forest Service?

BLM reclamation bond number:

Forest Service reclamation bond number:

Forest Service reclamation bond attachment:

Reclamation bond number:

Reclamation bond amount:

Reclamation bond rider amount:

Additional reclamation bond information attachment:
