

HOBBS OCD
JUN 07 2019
RECEIVED

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

| | | |
|--|---|---|
| 1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER | | 5. Lease Serial No. NMNM015091 |
| 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other | | 6. If Indian, Allottee or Tribe Name |
| 1c. Type of Completion: <input type="checkbox"/> Hydraulic Fracturing <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone | | 7. If Unit or CA Agreement, Name and No. |
| 2. Name of Operator BTA OIL PRODUCERS LLC (260287) | | 8. Lease Name and Well No. ROJO 7811 22 FEDERAL COM 26H (322775) |
| 3a. Address 104 S. Pecos Midland TX 79701 | 3b. Phone No. (include area code) (432)682-3753 | 9. API-Well No. 30-025-46080 (98094) |
| 4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface SESE / 420 FSL / 1250 FEL / LAT 32.109935 / LONG -103.555695 At proposed prod. zone NENE / 100 FNL / 380 FEL / LAT 32.12302 / LONG -103.552891 | | 10. Field and Pool, or Exploratory BOBCAT DRAW / UPPER WOLFCAMP |
| 11. Sec., T. R. M. or Blk. and Survey or Area SEC 22 / T25S / R33E / NMP | | 12. County or Parish LEA |
| 13. State NM | | 14. Distance in miles and direction from nearest town or post office* 21 miles |
| 15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 50 feet | 16. No of acres in lease 840 | 17. Spacing Unit dedicated to this well 160 |
| 18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 640 feet | 19. Proposed Depth 12940 feet / 17900 feet | 20. BLM/BIA Bond No. in file FED: NMB000849 |
| 21. Elevations (Show whether DF, KDB, RT, GL, etc.) 3346 feet | 22. Approximate date work will start* 03/15/2019 | 23. Estimated duration 30 days |
| 24. Attachments | | |

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be requested by the BLM. |

| | | |
|--|---|--------------------|
| 25. Signature (Electronic Submission) | Name (Printed/Typed) Sammy Hajar / Ph: (432)682-3753 | Date 11/08/2018 |
| Title Regulatory Analyst | | |
| Approved by (Signature) (Electronic Submission) | Name (Printed/Typed) Cody Layton / Ph: (575)234-5959 | Date 05/24/2019 |
| Title Assistant Field Manager Lands & Minerals | | |
| Office CARLSBAD | | |

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

6CA Rec 06/07/19

Kb
06/07/19

APPROVED WITH CONDITIONS
Approval Date: 05/24/2019

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM 1: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM collects this information to allow evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

1. SHL: SESE / 420 FSL / 1250 FEL / TWSP: 25S / RANGE: 33E / SECTION: 22 / LAT: 32.109935 / LONG: -103.555695 (TVD: 0 feet, MD: 0 feet)
PPP: SESE / 330 FSL / 380 FEL / TWSP: 25S / RANGE: 33E / SECTION: 22 / LAT: 32.109686 / LONG: -103.552885 (TVD: 12270 feet, MD: 12320 feet)
PPP: SENE / 2557 FNL / 236 FEL / TWSP: 25S / RANGE: 33E / SECTION: 22 / LAT: 32.116238 / LONG: -103.552425 (TVD: 12940 feet, MD: 15400 feet)
BHL: NENE / 100 FNL / 380 FEL / TWSP: 25S / RANGE: 33E / SECTION: 22 / LAT: 32.12302 / LONG: -103.552891 (TVD: 12940 feet, MD: 17900 feet)

BLM Point of Contact

Name: Ciji Methola

Title: GIS Support - Adjudicator

Phone: 5752345924

Email: cmethola@blm.gov

CONFIDENTIAL

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

| | |
|------------------------------|---|
| OPERATOR'S NAME: | BTA Oil Producers LLC |
| LEASE NO.: | NMNM015091 |
| WELL NAME & NO.: | ROJO 7811 22 FEDERAL COM 26H |
| SURFACE HOLE FOOTAGE: | 420'/S & 1250'/E |
| BOTTOM HOLE FOOTAGE: | 100'/N & 380'/E |
| LOCATION: | Section 22, T.25 S., R.33 E., NMPM |
| COUNTY: | Lea County, New Mexico |

COA

| | | | |
|----------------------|--|--|---------------------------------------|
| H2S | <input checked="" type="radio"/> Yes | <input type="radio"/> No | |
| Potash | <input checked="" type="radio"/> None | <input type="radio"/> Secretary | <input type="radio"/> R-111-P |
| Cave/Karst Potential | <input checked="" type="radio"/> Low | <input type="radio"/> Medium | <input type="radio"/> High |
| Variance | <input type="radio"/> None | <input checked="" type="radio"/> Flex Hose | <input type="radio"/> Other |
| Wellhead | <input type="radio"/> Conventional | <input type="radio"/> Multibowl | <input checked="" type="radio"/> Both |
| Other | <input type="checkbox"/> 4 String Area | <input type="checkbox"/> Capitan Reef | <input type="checkbox"/> WIPP |
| Other | <input checked="" type="checkbox"/> Fluid Filled | <input type="checkbox"/> Cement Squeeze | <input type="checkbox"/> Pilot Hole |
| Special Requirements | <input type="checkbox"/> Water Disposal | <input checked="" type="checkbox"/> COM | <input type="checkbox"/> Unit |

A. HYDROGEN SULFIDE

A Hydrogen Sulfide (H2S) Drilling Plan shall be activated 500 feet prior to drilling into the **Wildcat Pool** formation. As a result, the Hydrogen Sulfide area must meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, please provide measured values and formations to the BLM.

B. CASING

1. The 13-3/8 inch surface casing shall be set at approximately **1160 feet** (a minimum of 25 feet (Lea County) into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to

- include the lead cement)
- c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

2. The minimum required fill of cement behind the 9-5/8 inch intermediate casing shall be set at approximately **5000 feet** is:

Option 1 (Single Stage):

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

Option 2:

Operator has proposed a DV tool, the depth may be adjusted as long as the cement is changed proportionally. The DV tool may be cancelled if cement circulates to surface on the first stage.

- a. First stage to DV tool: Cement to circulate. If cement does not circulate off the DV tool, contact the appropriate BLM office before proceeding with second stage cement job.
 - b. Second stage above DV tool:
 - Cement to surface. If cement does not circulate, contact the appropriate BLM office.
3. The minimum required fill of cement behind the 7 inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.
 4. The minimum required fill of cement behind the 4-1/2 inch production liner is:
 - Cement should tie-back **100 feet** into the previous casing. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
- 2.

Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi.**
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the intermediate casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**

Option 2:

1. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Carlsbad Field Office, 620 E Greene St. Carlsbad, New Mexico 88220, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by

the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.

- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Chaves and Roosevelt Counties

Call the Roswell Field Office, 2909 West Second St., Roswell NM 88201.
During office hours call (575) 627-0272.
After office hours call (575)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.

3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the

plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time.
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

**PECOS DISTRICT
SURFACE USE
CONDITIONS OF APPROVAL**

| | |
|-----------------------|------------------------------------|
| OPERATOR'S NAME: | BTA Oil Producers LLC |
| WELL NAME & NO.: | ROJO 7811 22 FEDERAL COM 26H |
| SURFACE HOLE FOOTAGE: | 420'/S & 1250'/E |
| BOTTOM HOLE FOOTAGE | 100'/N & 380'/E |
| LOCATION: | Section 22, T.25 S., R.33 E., NMPM |
| COUNTY: | Lea County, New Mexico |

TABLE OF CONTENTS

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☐ **Special Requirements**

- ☐ **Construction**
 - Notification
 - Topsoil
 - Closed Loop System
 - Federal Mineral Material Pits
 - Well Pads
 - Roads
- ☐ **Road Section Diagram**
- ☐ **Production (Post Drilling)**
 - Well Structures & Facilities
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**

I. GENERAL PROVISIONS

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

II. PERMIT EXPIRATION

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

Any cultural and/or paleontological resource discovered by the operator or by any person working on the operator's behalf shall immediately report such findings to the Authorized Officer. The operator is fully accountable for the actions of their contractors and subcontractors. The operator shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery shall be made by the Authorized Officer to determine the appropriate actions that shall be required to prevent the loss of significant cultural or scientific values of the discovery. The operator shall be held responsible for the cost of the proper mitigation measures that the Authorized Officer assesses after consultation with the operator on the evaluation and decisions of the discovery. Any unauthorized collection or disturbance of cultural or paleontological resources may result in a shutdown order by the Authorized Officer.

IV. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

V. SPECIAL REQUIREMENT(S)

VI. CONSTRUCTION

A. NOTIFICATION

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

B. TOPSOIL

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

C. CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

D. FEDERAL MINERAL MATERIALS PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

E. WELL PAD SURFACING

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

F. EXCLOSURE FENCING (CELLARS & PITS)

Exclosure Fencing

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

G. ON LEASE ACCESS ROADS**Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

Surfacing

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

Crowning

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

Ditching

Ditching shall be required on both sides of the road.

Turnouts


Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

Drainage

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outslowing and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

Cross Section of a Typical Lead-off Ditch



All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

Formula for Spacing Interval of Lead-off Ditches

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

Cattle guards

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

Fence Requirement

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.


Public Access

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.


Construction Steps

1. Salvage topsoil
2. Construct road


3. Redistribute topsoil
4. Revegetate slopes



Typical Turnout Plan



Level Ground Section

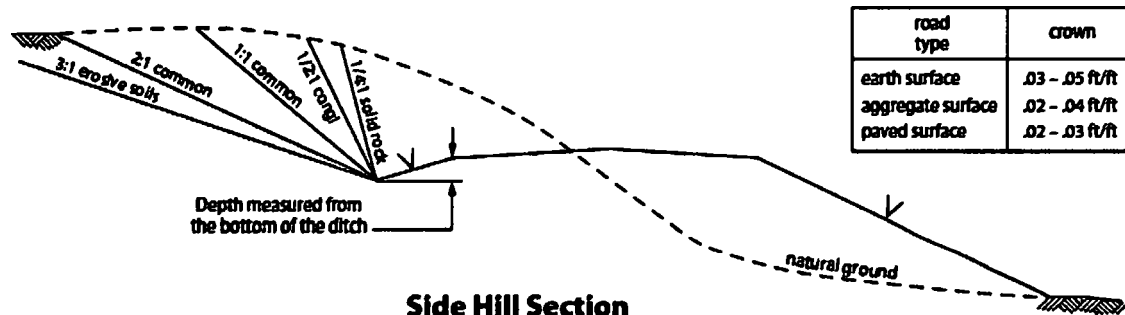

Side Hill Section

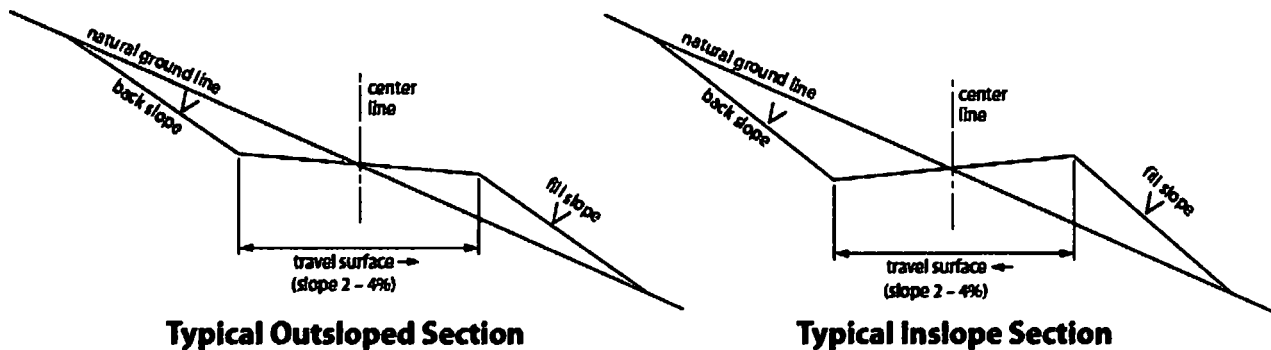


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

VII. PRODUCTION (POST DRILLING)

A. WELL STRUCTURES & FACILITIES

Placement of Production Facilities

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

Exclosure Netting (Open-top Tanks)

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

Chemical and Fuel Secondary Containment and Exclosure Screening

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

Open-Vent Exhaust Stack Exclosures

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

Containment Structures

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

Painting Requirement

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, Shale Green from the BLM Standard Environmental Color Chart (CC-001: June 2008).

VIII. INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

IX. FINAL ABANDONMENT & RECLAMATION

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Operator Certification

I hereby certify that I, or someone under my direct supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.

NAME: Sammy Hajar

Signed on: 11/08/2018

Title: Regulatory Analyst

Street Address: 104 S Pecos Street

City: Midland

State: TX

Zip: 79701

Phone: (432)682-3753

Email address: SHajar@btaoil.com

Field Representative

Representative Name: Nick Eaton

Street Address: 104 South Pecos

City: Midland

State: TX

Zip: 79701

Phone: (432)682-3753

Email address: neaton@btaoil.com

APD ID: 10400035877

Submission Date: 11/08/2018

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Well Type: OIL WELL

Well Work Type: Drill

[Show Final Text](#)

Section 1 - General

APD ID: 10400035877

Tie to previous NOS? 10400030731

Submission Date: 11/08/2018

BLM Office: CARLSBAD

User: Sammy Hajar

Title: Regulatory Analyst

Federal/Indian APD: FED

Is the first lease penetrated for production Federal or Indian? FED

Lease number: NMNM015091

Lease Acres: 840

Surface access agreement in place?

Allotted?

Reservation:

Agreement in place? NO

Federal or Indian agreement:

Agreement number:

Agreement name:

Keep application confidential? YES

Permitting Agent? NO

APD Operator: BTA OIL PRODUCERS LLC

Operator letter of designation:

Operator Info

Operator Organization Name: BTA OIL PRODUCERS LLC

Operator Address: 104 S. Pecos

Zip: 79701

Operator PO Box:

Operator City: Midland

State: TX

Operator Phone: (432)682-3753

Operator Internet Address:

Section 2 - Well Information

Well in Master Development Plan? NO

Master Development Plan name:

Well in Master SUPO? NO

Master SUPO name:

Well in Master Drilling Plan? NO

Master Drilling Plan name:

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Well API Number:

Field/Pool or Exploratory? Field and Pool

Field Name: BOBCAT DRAW

Pool Name: UPPER
WOLFCAMP

Is the proposed well in an area containing other mineral resources? NONE

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Describe other minerals:

Is the proposed well in a Helium production area? N Use Existing Well Pad? NO New surface disturbance?

Type of Well Pad: MULTIPLE WELL

Multiple Well Pad Name: ROJO Number: 26-29

Well Class: HORIZONTAL

7811 22 FEDERAL COM

Number of Legs:

Well Work Type: Drill

Well Type: OIL WELL

Describe Well Type:

Well sub-Type: INFILL

Describe sub-type:

Distance to town: 21 Miles

Distance to nearest well: 640 FT

Distance to lease line: 50 FT

Reservoir well spacing assigned acres Measurement: 160 Acres

Well plat: Rojo_7811_FED_COM_26H_c102_20181106064905.pdf

Well work start Date: 03/15/2019

Duration: 30 DAYS

Section 3 - Well Location Table

Survey Type: RECTANGULAR

Describe Survey Type:

Datum: NAD83

Vertical Datum: NGVD29

Survey number:

| | NS-Foot | NS Indicator | EW-Foot | EW Indicator | Twsp | Range | Section | Aliquot/Lot/Tract | Latitude | Longitude | County | State | Meridian | Lease Type | Lease Number | Elevation | MD | TVD |
|------------------|---------|--------------|---------|--------------|------|-------|---------|-------------------|---------------|---------------------|--------|-------------------|-------------------|------------|--------------|---------------|-----------|-----------|
| SHL Leg #1 | | | | FEL | 25S | 33E | 22 | Aliquot SESE | 32.10993 5 | - 103.5556 95 | LEA | NEW MEXI CO | NEW MEXI CO | F | FEE | 334 6 | 0 | 0 |
| KOP Leg #1 | | | | FEL | 25S | 33E | 22 | Aliquot SESE | 32.10968 6 | - 103.5528 85 | LEA | NEW MEXI CO | NEW MEXI CO | F | FEE | - 902 1 | 124 16 | 123 67 |
| PPP Leg #1 | | | | FEL | 25S | 33E | 22 | Aliquot SESE | 32.10968 6 | - 103.5528 85 | LEA | NEW MEXI CO | NEW MEXI CO | F | FEE | - 892 4 | 123 20 | 122 70 |

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

| | NS-Foot | NS Indicator | EW-Foot | EW Indicator | Twsp | Range | Section | Aliquot/Lot/Tract | Latitude | Longitude | County | State | Meridian | Lease Type | Lease Number | Elevation | MD | TVD |
|-------------------|---------|--------------|---------|--------------|------|-------|---------|-------------------|---------------|---------------------|--------|-------------------|-------------------|------------|----------------|---------------|-----------|-----------|
| PPP Leg #1 | 255 | FEL | 233 | FEL | 25S | 33E | 22 | Aliquot SENE | 32.11623 8 | - 103.5524 25 | LEA | NEW MEXI CO | NEW MEXI CO | F | NMNM 015091 | - 959 4 | 154 00 | 129 40 |
| EXIT Leg #1 | 330 | FEL | 330 | FEL | 25S | 33E | 22 | Aliquot NENE | 32.12238 8 | - 103.5528 91 | LEA | NEW MEXI CO | NEW MEXI CO | F | NMNM 015091 | - 959 4 | 176 20 | 129 40 |
| BHL Leg #1 | 100 | FEL | 330 | FEL | 25S | 33E | 22 | Aliquot NENE | 32.12302 | - 103.5528 91 | LEA | NEW MEXI CO | NEW MEXI CO | F | NMNM 015091 | - 959 4 | 179 00 | 129 40 |

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

10M_choke_mannifold_20190326075726.pdf

Choke_Hose___Test_Chart_and_Specs_20190326075727.pdf

5M_annular_well_control_plan_for_BLM_20190326075753.docx

10M_annular_variance_20190326075753.pdf

BLM_10M_BOP_with_5M_annular_20190326075754.pdf

Section 3 - Casing

| Casing ID | String Type | Hole Size | Csg Size | Condition | Standard | Tapered String | Top Set MD | Bottom Set MD | Top Set TVD | Bottom Set TVD | Top Set MSL | Bottom Set MSL | Calculated casing length MD | Grade | Weight | Joint Type | Collapse SF | Burst SF | Joint SF Type | Joint SF | Body SF Type |
|-----------|--------------|-----------|----------|-----------|----------|----------------|------------|---------------|-------------|----------------|-------------|----------------|-----------------------------|-------|--------|------------|-------------|----------|---------------|----------|--------------|
| 1 | SURFACE | 17.5 | 13.375 | NEW | API | N | 0 | 1040 | 0 | | | | 1040 | J-55 | 54.5 | STC | 2.5 | 6.1 | DRY | 9.1 | DRY |
| 2 | INTERMEDIATE | 12.25 | 9.625 | NEW | API | N | 0 | 5050 | 0 | | | | 5050 | J-55 | 40 | LTC | 1.8 | 1.5 | DRY | 2.6 | DRY |
| 3 | PRODUCTION | 8.75 | 7.0 | NEW | API | N | 0 | 13020 | 0 | | | | 13020 | P-110 | 29 | LTC | 1.4 | 1.8 | DRY | 2.1 | DRY |
| 4 | LINER | 6.125 | 4.5 | NEW | API | N | 12390 | 17900 | 12341 | | | | 5510 | P-110 | 13.5 | LTC | 1.4 | 2.5 | DRY | 1.9 | DRY |

Casing Attachments

Casing ID: 1 String Type: SURFACE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

ROJO_26H_casing_assumption_20181107130352.JPG

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Casing Attachments

Casing ID: 2 String Type: INTERMEDIATE

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

ROJO_26H_casing_assumption_20181107130408.JPG

Casing ID: 3 String Type: PRODUCTION

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

ROJO_26H_casing_assumption_20181107130416.JPG

Casing ID: 4 String Type: LINER

Inspection Document:

Spec Document:

Tapered String Spec:

Casing Design Assumptions and Worksheet(s):

ROJO_26H_casing_assumption_20181107130423.JPG

Section 4 - Cement

Operator Name: BTA OIL PRODUCERS LLC**Well Name:** ROJO 7811 22 FEDERAL COM**Well Number:** 26H

| String Type | Lead/Tail | Stage Tool Depth | Top MD | Bottom MD | Quantity(sx) | Yield | Density | Cu Ft | Excess% | Cement type | Additives |
|--------------|-----------|------------------|--------|-----------|--------------|-------|---------|--------|---------|---------------------|------------------|
| SURFACE | Lead | | 0 | 850 | 690 | 1.8 | 13.5 | 1242 | 100 | Class C | 2% CaCl2 |
| SURFACE | Tail | | 850 | 1040 | 200 | 1.34 | 14.8 | 268 | 100 | Class C | 2% CaCl2 |
| INTERMEDIATE | Lead | | 0 | 4400 | 1195 | 2.18 | 12.7 | 2605.1 | 100 | Class C | 0.5%CaCl2 |
| INTERMEDIATE | Tail | | 4400 | 5050 | 250 | 1.33 | 14.8 | 332.5 | 25 | Class C | 1% CaCl2 |
| PRODUCTION | Lead | | 4078 | 11517 | 470 | 2.99 | 10.5 | 1405.3 | 15 | 25% Poz 75% Class C | 0.4% Fluid Loss |
| PRODUCTION | Tail | | 11517 | 13020 | 200 | 1.19 | 15.6 | 238 | 15 | Class H | 0.2% LT Retarder |
| LINER | Lead | | 12390 | 17900 | 315 | 1.86 | 13.2 | 585.9 | 10 | 25% Poz 75%Class C | 0.1% Fluid loss |

Section 5 - Circulating Medium

Mud System Type: Closed**Will an air or gas system be Used?** NO**Description of the equipment for the circulating system in accordance with Onshore Order #2:****Diagram of the equipment for the circulating system in accordance with Onshore Order #2:**

Describe what will be on location to control well or mitigate other conditions: Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

Describe the mud monitoring system utilized: PVT/Pason/Visual Monitoring

Circulating Medium Table

| Top Depth | Bottom Depth | Mud Type | Min Weight (lbs/gal) | Max Weight (lbs/gal) | Density (lbs/cu ft) | Gel Strength (lbs/100 sqft) | PH | Viscosity (CP) | Salinity (ppm) | Filtration (cc) | Additional Characteristics |
|-----------|--------------|-----------------|----------------------|----------------------|---------------------|-----------------------------|----|----------------|----------------|-----------------|----------------------------|
| 0 | 1050 | OTHER : FW SPUD | 8.3 | 8.4 | | | | | | | |

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

| Top Depth | Bottom Depth | Mud Type | Min Weight (lbs/gal) | Max Weight (lbs/gal) | Density (lbs/cu ft) | Gel Strength (lbs/100 sqft) | PH | Viscosity (CP) | Salinity (ppm) | Filtration (cc) | Additional Characteristics |
|-----------|--------------|-------------------------|----------------------|----------------------|---------------------|-----------------------------|----|----------------|----------------|-----------------|----------------------------|
| 1040 | 5050 | OTHER : SATURATED BRINE | 10 | 10.2 | | | | | | | |
| 5050 | 12864 | OTHER : CUT BRINE | 8.6 | 9.2 | | | | | | | |
| 12864 | 12940 | OIL-BASED MUD | 11 | 11.5 | | | | | | | |

Section 6 - Test, Logging, Coring

List of production tests including testing procedures, equipment and safety measures:

All Stem Tests will be based on geological sample shows.

List of open and cased hole logs run in the well:

DL,GR,MUDLOG

Logging operation description for the well:

None planned

Section 7 - Pressure

Anticipated Bottom Hole Pressure: 7738

Anticipated Surface Pressure: 4891.2

Anticipated Bottom Hole Temperature(F): 185

Anticipated abnormal pressures, temperatures, or potential geologic hazards? NO

Describe:

Contingency Plans geohazards description:

Contingency Plans geohazards attachment:

Hydrogen Sulfide drilling operations plan required? YES

Hydrogen sulfide drilling operations plan:

Rojo_7811_27_Fed_Com__H2S_Equipment_Schematic_03_24_2017_20181105160549.pdf

Rojo_7811_27_Fed_Com__H2S_Plan_03_24_2017_20181105160549.pdf

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Section 8 - Other Information

Proposed horizontal/directional/multi-lateral plan submission:

Rojo__26H_directional_plan_20181101155238.pdf

Rojo__26H_Wall_plot_20181102084710.pdf

Other proposed operations facets description:

A variance is requested for a Multi Bowl Wellhead. See the attached schematic and running procedure. *All strings will be kept 1/3 full while running.

Other proposed operations facets attachment:


BTA_Oil_Producers_LLC___EMERGENCY_CALL_LIST_9_11_17_20171005093924.pdf

Other Variance attachment:

Multi_Bowl_Diagram_20180420093359_20180810091253.pdf

Rojo_7811_27_Fed_Com___Casing_Head_Running_Procedure_03-24-2017.pdf

26H_Gas_Capture_Plan_20181108140745.pdf

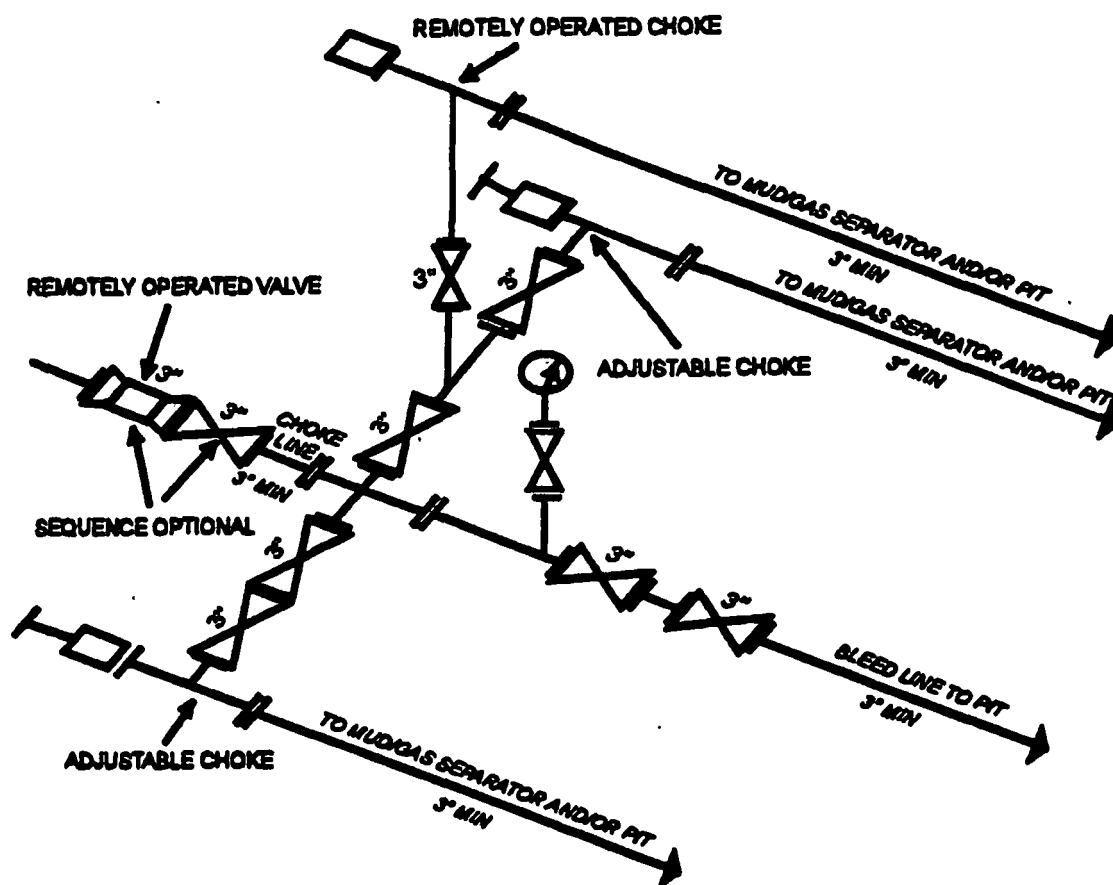

10M AND 15M CHOKE MANIFOLD EQUIPMENT - CONFIGURATION OF CHOKES MAY VARY
 [53 FR 49661, Dec. 9, 1988 and 54 FR 39528, Sept. 27, 1989]

Continental

ContiTech

CONTITECH RUBBER
Industrial Kft.

No: QC-DB- 599/ 2014

Page: 16 / 176

Rig 94

Asset 24455


| QUALITY CONTROL INSPECTION AND TEST CERTIFICATE | | | | CERT. N°: 1592 | |
|--|--|--|--|--|--|
| PURCHASER: ContiTech Oil & Marine Corp. | | P.O. N°: 4500461753 | | | |
| CONTITECH ORDER N°: 539225 | | HOSE TYPE: 3" ID Choke & Kill Hose | | | |
| HOSE SERIAL N°: [REDACTED] | | NOMINAL / ACTUAL LENGTH: 7,62 m / 7,68 m | | | |
| W.P. 68,9 MPa 10000 psi | | T.P. 103,4 MPa 15000 psi | | Duration: 60 min. | |
| Pressure test with water at ambient temperature | | | | | |
| See attachment. (1 page) | | | | | |
| → 10 Min. ↑ 50 MPa | | | | | |
| COUPLINGS Type | | Serial N° | | Quality | |
| 3" coupling with 4 1/16" 10K API Swivel Flange end Hub | | 2574 5533 | | AISI 4130 AISI 4130 AISI 4130 | |
| | | | | Heat N° A1582N H8672 58855 A1199N A1423N | |
| Not Designed For Well Testing | | | | API Spec 16 C | |
| Fire Rated | | | | Temperature rate: "B" | |
| All metal parts are flawless | | | | | |
| WE CERTIFY THAT THE ABOVE HOSE HAS BEEN MANUFACTURED IN ACCORDANCE WITH THE TERMS OF THE ORDER INSPECTED AND PRESSURE TESTED AS ABOVE WITH SATISFACTORY RESULT. | | | | | |
| STATEMENT OF CONFORMITY: We hereby certify that the above items/equipment supplied by us are in conformity with the terms, conditions and specifications of the above Purchaser Order and that these items/equipment were fabricated inspected and tested in accordance with the referenced standards, codes and specifications and meet the relevant acceptance criteria and design requirements. | | | | | |
| Date: 04. September 2014. | | Inspector | | Quality Control | |
| | | | | Continental Rubber Industrial Kft. Quality Control Dept. [Signature] | |

1/

File Name : 000220_68543_68545+547.GEV.....000236_68543_68545+547.GEV
 File Message : 68543_68545_68547
 Device Type : GX10
 Serial No. : SGP606399
 Data Count : 9946
 Print Group :
 Print Range :
 Comment :
 Press-Temp :
 2014/09/04 01:53:54.000 - 2014/09/04 01:39:39.000

Sampling Int. : 1.000 sec
 Start Time : 2014/09/04 01:53:54.000
 Stop Time : 2014/09/04 01:39:39.000

| Dist No | Cursor A | Cursor B | Distance |
|-------------------------|-------------------------|-------------------------|--------------|
| 7022 | 24.22 | 7022 | 3600 |
| Absolute Time | 2014/09/04 02:51:05.000 | 2014/09/04 03:51:05.000 | 21 00:00.000 |
| Tag Comment | Value A | Value B | Value B-A |
| Pressure(bar) | 1062.95 | -1048.57 | -14.38 |
| Ambient Temperature(°C) | 23.23 | 23.14 | -0.10 |

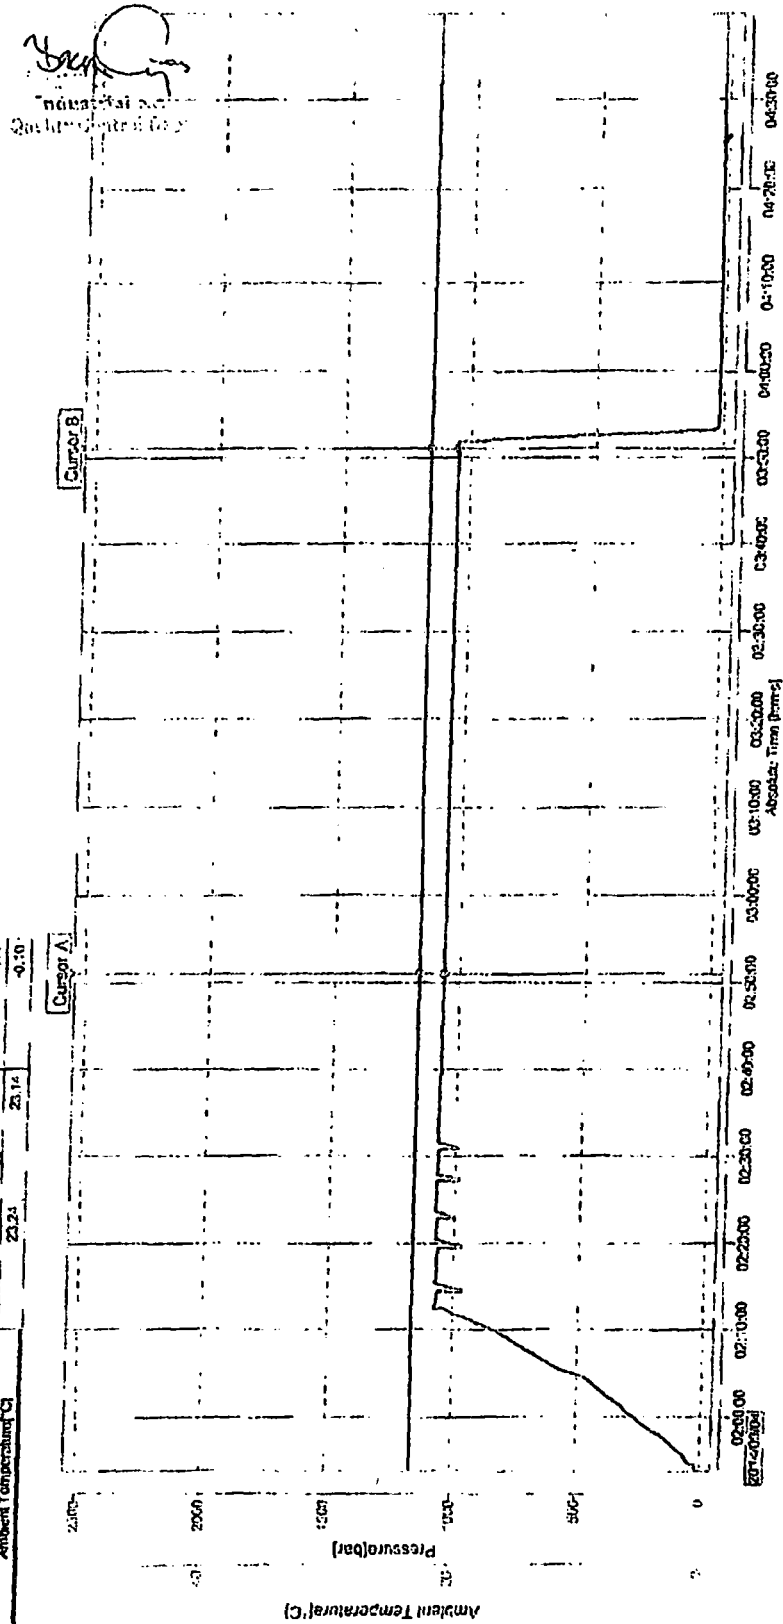

Industrial
 Quality Control

1588/1590/1592

Well control plan for 10M BOPE with 5M annular

Drilling

1. Sound alarm (alert crew).
2. Space out drill string.
3. Shut down pumps (stop pumps and rotary).
4. Shut-in Well with annular with HCR and choke in closed position.
5. Confirm shut-in.
6. Notify tool pusher/company representative.
7. Read and record the following:
 - a. SIDPP & SICP
 - b. Time of shut in
 - c. Pit gain
8. Regroup and identify forward plan. If pressure has increased to 2500 psi, confirm spacing and close the upper variable bore rams.
9. Prepare for well kill operation.

Tripping

1. Sound alarm (alert rig crew)
2. Stab full opening safety valve and close valve
3. Space out drill string
4. Shut in the well with the annular with HCR and choke in closed position
5. Confirm shut in
6. Notify tool pusher/company representative
7. Read and record the following
 - a. Time of shut in
 - b. SIDPP and SICP
 - c. Pit gain
8. If pressure has increased to 2500 psi, confirm spacing and close the upper most variable bore ram.
9. Prepare for well kill operation.

While Running Casing

1. Sound alarm (alert rig crew)
2. Stab crossover and full opening safety valve and close valve
3. Space out casing string
4. Shut in well with annular with HCR and choke in closed position
5. Confirm shut in
6. Notify tool pusher/company representative
7. Read and record the following:
 - a. SIDPP & SICP
 - b. Pit gain
 - c. Time
8. If pressure has increased to 2500 psi, confirm spacing and close the upper most variable bore ram.
9. Prepare for well kill operation.

No Pipe In Hole (Open Hole)

1. Sound alarm (alert rig crew)

Well control plan for 10M BOPE with 5M annular

2. Shut in blind rams with HCR and choke in closed position
3. Confirm shut in
4. Notify tool pusher/company representative
5. Read and record the following:
 - a. SICP
 - b. Pit gain
 - c. Time
6. Prepare for well kill operation

Pulling BHA thru Stack

1. Prior to pulling last joint of drill pipe thru the stack
 - a. Perform flow check, if flowing:
 - a.i. Sound Alarm (alert crew)
 - a.ii. Stab full opening safety valve and close valve
 - a.iii. Space out drill string
 - a.iv. Shut in using upper most VBR, choke and HCR in closed position
 - a.v. Confirm shut in
 - a.vi. Notify tool pusher/company representative.
 - a.vii. Read and record the following:
 - a.vii.1. SIDPP and SICP
 - a.vii.2. Pit gain
 - a.vii.3. Time
 - a.viii. Prepare for well kill operation
 2. With BHA in the stack:
 - a. If possible pull BHA clear of stack
 - a.i. Follow 'open hole' procedure above
 - b. If unable to pull BHA clear of stack
 - b.i. Stab crossover with full opening safety valve, close valve.
 - b.ii. Space out
 - b.iii. Shut in using upper most VBR. HCR and choke in closed position.
 - b.iv. Confirm shut in
 - b.v. Notify tool pusher/company rep
 - b.vi. Read and record the following:
 - b.vi.1. SIDPP and SICP
 - b.vi.2. Pit gain
 - b.vi.3. Time
 - b.vii. Prepare for well kill operation


Drilling component and preventer compatibility table **for 10M approval**

The following table outlines the drilling and production liner components for Wolfcamp targets requiring 10M BOPE approval. Variance is requested to utilize a 5M annular preventer in 6-1/8" hole as all components can be covered using 10M rated VBR's (variable bore rams). 5M annular on the 10M system will be tested to 100% of rated working pressure.

| 6-1/8" hole section – 10M BOPE requirement (13-5/8" BOP) | | | |
|---|-----------|------------------|------------|
| Component | OD | Preventer | RWP |
| Drill pipe | 4" | 3.5"-5.5" VBR | 10M |
| HWDP | 4" | 3.5"-5.5" VBR | 10M |
| Jars | 5" | 3.5"-5.5" VBR | 10M |
| DC's and NMDC's | 4-3/4" | 3.5"-5.5" VBR | 10M |
| Mud motor | 5" | 3.5"-5.5" VBR | 10M |
| Casing | 4-1/2" | 3.5"-5.5" VBR | 10M |
| Open hole | NA | Blind rams | 10M |

| 12-1/4" & 8-3/4" hole sections – 5M BOPE requirement (13-5/8" BOP) | | | |
|---|-------------|-------------------------------|------------|
| Component | OD | Preventer | RWP |
| Drill pipe | 5" | 3.5"-5.5" VBR or 5" pipe rams | 10M |
| HWDP | 5" | 3.5"-5.5" VBR or 5" pipe rams | 10M |
| Jars | 6-1/4" | Annular | 5M |
| DC's and NMDC's | 7"-8" | Annular | 5M |
| Mud motor | 7"-8" | Annular | 5M |
| Casing | 9-5/8" & 7" | Annular | 5M |
| Open hole | NA | Blind rams | 10M |

13-5/8" 10M PSI BOP Stack

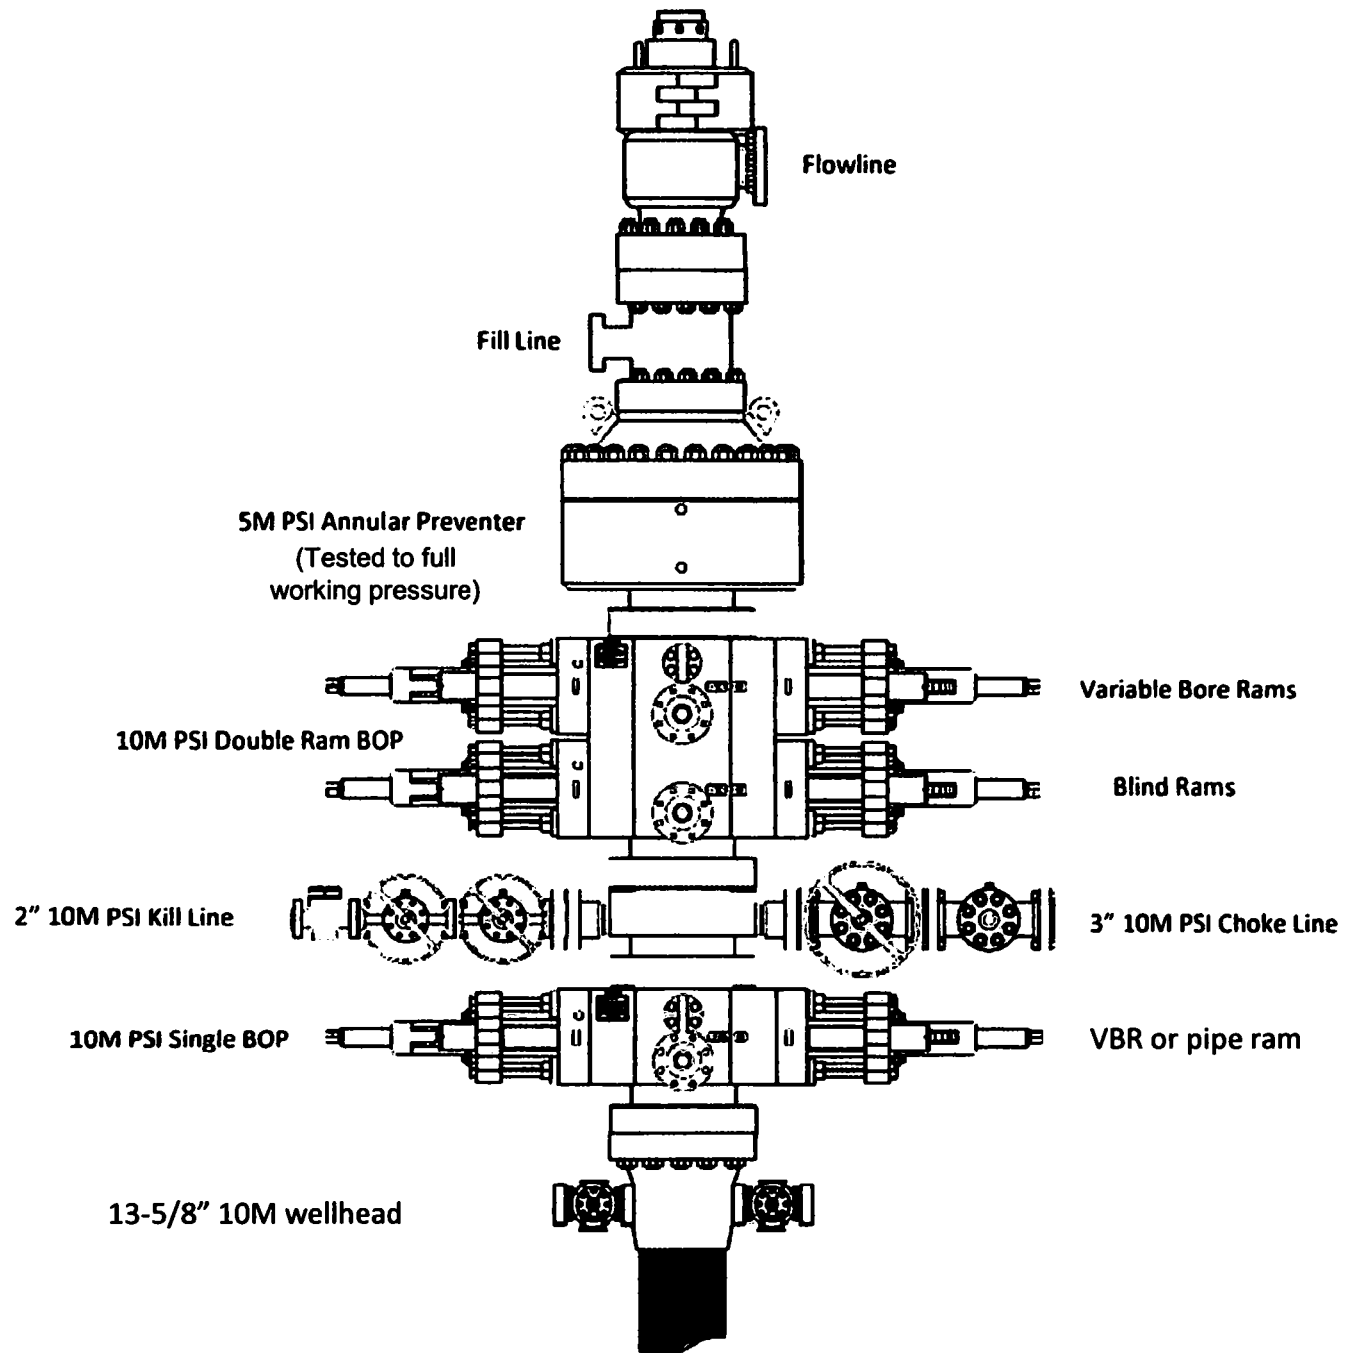



BTA Oil Producers, LLC
104 S Pecos
Midland, TX 79701

WELL: Rojo 7811 22 Fed Com #26H
TVD: 12940
MD: 17900

DRILLING PLAN

Casing Program

| Hole Size | Csg. Size | From (MD) | To (MD) | From (TVD) | To (TVD) | Tapered String | Weight (lbs) | Grade | Conn. | Collapse | Burst | Body Tension | Joint Tension | Dry/Buoyant | Mud Weight (ppg) |
|-----------|-----------|-----------|---------|------------|----------|----------------|--------------|-------|-------|----------|-------|--------------|---------------|-------------|------------------|
| 17 1/2 | 13 3/8 | 0 | 1040 | 0 | 1040 | No | 54.5 | J-55 | STC | 2.5 | 8.1 | 15.0 | 8.1 | Dry | 8.3 |
| 12 1/4 | 9 5/8 | 0 | 5050 | 0 | 5050 | No | 40 | J-55 | LTC | 1.8 | 1.5 | 3.1 | 2.8 | Dry | 10 |
| 8 3/4 | 7 | 0 | 13020 | 0 | 12864 | No | 29 | P110 | LTC | 1.4 | 1.8 | 2.5 | 2.1 | Dry | 8.2 |
| 6 1/8 | 4 1/2 | 12390 | 17900 | 12341 | 12940 | No | 13.5 | P110 | LTC | 1.4 | 2.5 | 2.4 | 1.9 | Dry | 11.5 |
| | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | |

Cementing Program



BTA Oil Producers, LLC
104 S Pecos
Midland, TX 79701

WELL: Rojo 7811 22 Fed Com #26H
TVD: 12940
MD: 17900

DRILLING PLAN

Casing Program

| Hole Size | Csg. Size | From (MD) | To (MD) | From (TVD) | To (TVD) | Tapered String | Weight (lbs) | Grade | Conn. | Collapse | Burst | Body Tension | Joint Tension | Dry/Buoyant | Mod Weight (ppg) |
|-----------|-----------|-----------|---------|------------|----------|----------------|--------------|-------|-------|----------|-------|--------------|---------------|-------------|------------------|
| 17 1/2 | 13 3/8 | 0 | 1040 | 0 | 1040 | No | 54.5 | J-55 | STC | 2.5 | 8.1 | 15.0 | 8.1 | Dry | 8.3 |
| 12 1/4 | 9 5/8 | 0 | 5050 | 0 | 5050 | No | 40 | J-55 | LTC | 1.8 | 1.5 | 3.1 | 2.6 | Dry | 10 |
| 8 3/4 | 7 | 0 | 13020 | 0 | 12884 | No | 29 | P110 | LTC | 1.4 | 1.8 | 2.5 | 2.1 | Dry | 8.2 |
| 6 1/8 | 4 1/2 | 12390 | 17900 | 12341 | 12940 | No | 13.5 | P110 | LTC | 1.4 | 2.5 | 2.4 | 1.9 | Dry | 11.5 |
| | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | |

Cementing Program



BTA Oil Producers, LLC
104 S Pecos
Midland, TX 79701

WELL: Rojo 7811 22 Fed Com #26H
TVD: 12940
MD: 17900

DRILLING PLAN

Casing Program

| Hole Size | Csg. Size | From (MD) | To (MD) | From (TVD) | To (TVD) | Tapered String | Weight (lbs) | Grade | Conn. | Collapse | Burst | Body Tension | Joint Tension | Dry/Buoyant | Mud Weight (ppg) |
|-----------|-----------|-----------|---------|------------|----------|----------------|--------------|-------|-------|----------|-------|--------------|---------------|-------------|------------------|
| 17 1/2 | 13 3/8 | 0 | 1040 | 0 | 1040 | No | 54.5 | J-55 | STC | 2.5 | 8.1 | 15.0 | 8.1 | Dry | 8.3 |
| 12 1/4 | 9 5/8 | 0 | 5050 | 0 | 5050 | No | 40 | J-55 | LTC | 1.8 | 1.5 | 3.1 | 2.6 | Dry | 10 |
| 8 3/4 | 7 | 0 | 13020 | 0 | 12864 | No | 29 | P110 | LTC | 1.4 | 1.8 | 2.5 | 2.1 | Dry | 9.2 |
| 6 1/8 | 4 1/2 | 12390 | 17900 | 12341 | 12940 | No | 13.5 | P110 | LTC | 1.4 | 2.5 | 2.4 | 1.9 | Dry | 11.5 |
| | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | |

Cementing Program



BTA Oil Producers, LLC
104 S Pecos
Midland, TX 79701


WELL: Rojo 7811 22 Fed Corn #26H
TVD: 12940
MD: 17900

DRILLING PLAN

Casing Program

| Hole Size | Csg. Size | From (MD) | To (MD) | From (TVD) | To (TVD) | Tapered String | Weight (lbs) | Grade | Conn. | Collapse | Burst | Body Tension | Joint Tension | Dry/Buoyant | Mod Weight (ppg) |
|-----------|-----------|-----------|---------|------------|----------|----------------|--------------|-------|-------|----------|-------|--------------|---------------|-------------|------------------|
| 17 1/2 | 13 3/8 | 0 | 1040 | 0 | 1040 | No | 54.5 | J-55 | STC | 2.5 | 8.1 | 15.0 | 8.1 | Dry | 8.3 |
| 12 1/4 | 9 5/8 | 0 | 5050 | 0 | 5050 | No | 40 | J-55 | LTC | 1.8 | 1.5 | 3.1 | 2.6 | Dry | 10 |
| 8 3/4 | 7 | 0 | 13020 | 0 | 12864 | No | 29 | P110 | LTC | 1.4 | 1.8 | 2.5 | 2.1 | Dry | 8.2 |
| 6 1/8 | 4 1/2 | 12390 | 17900 | 12341 | 12940 | No | 13.5 | P110 | LTC | 1.4 | 2.5 | 2.4 | 1.9 | Dry | 11.5 |
| | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | |

Cementing Program

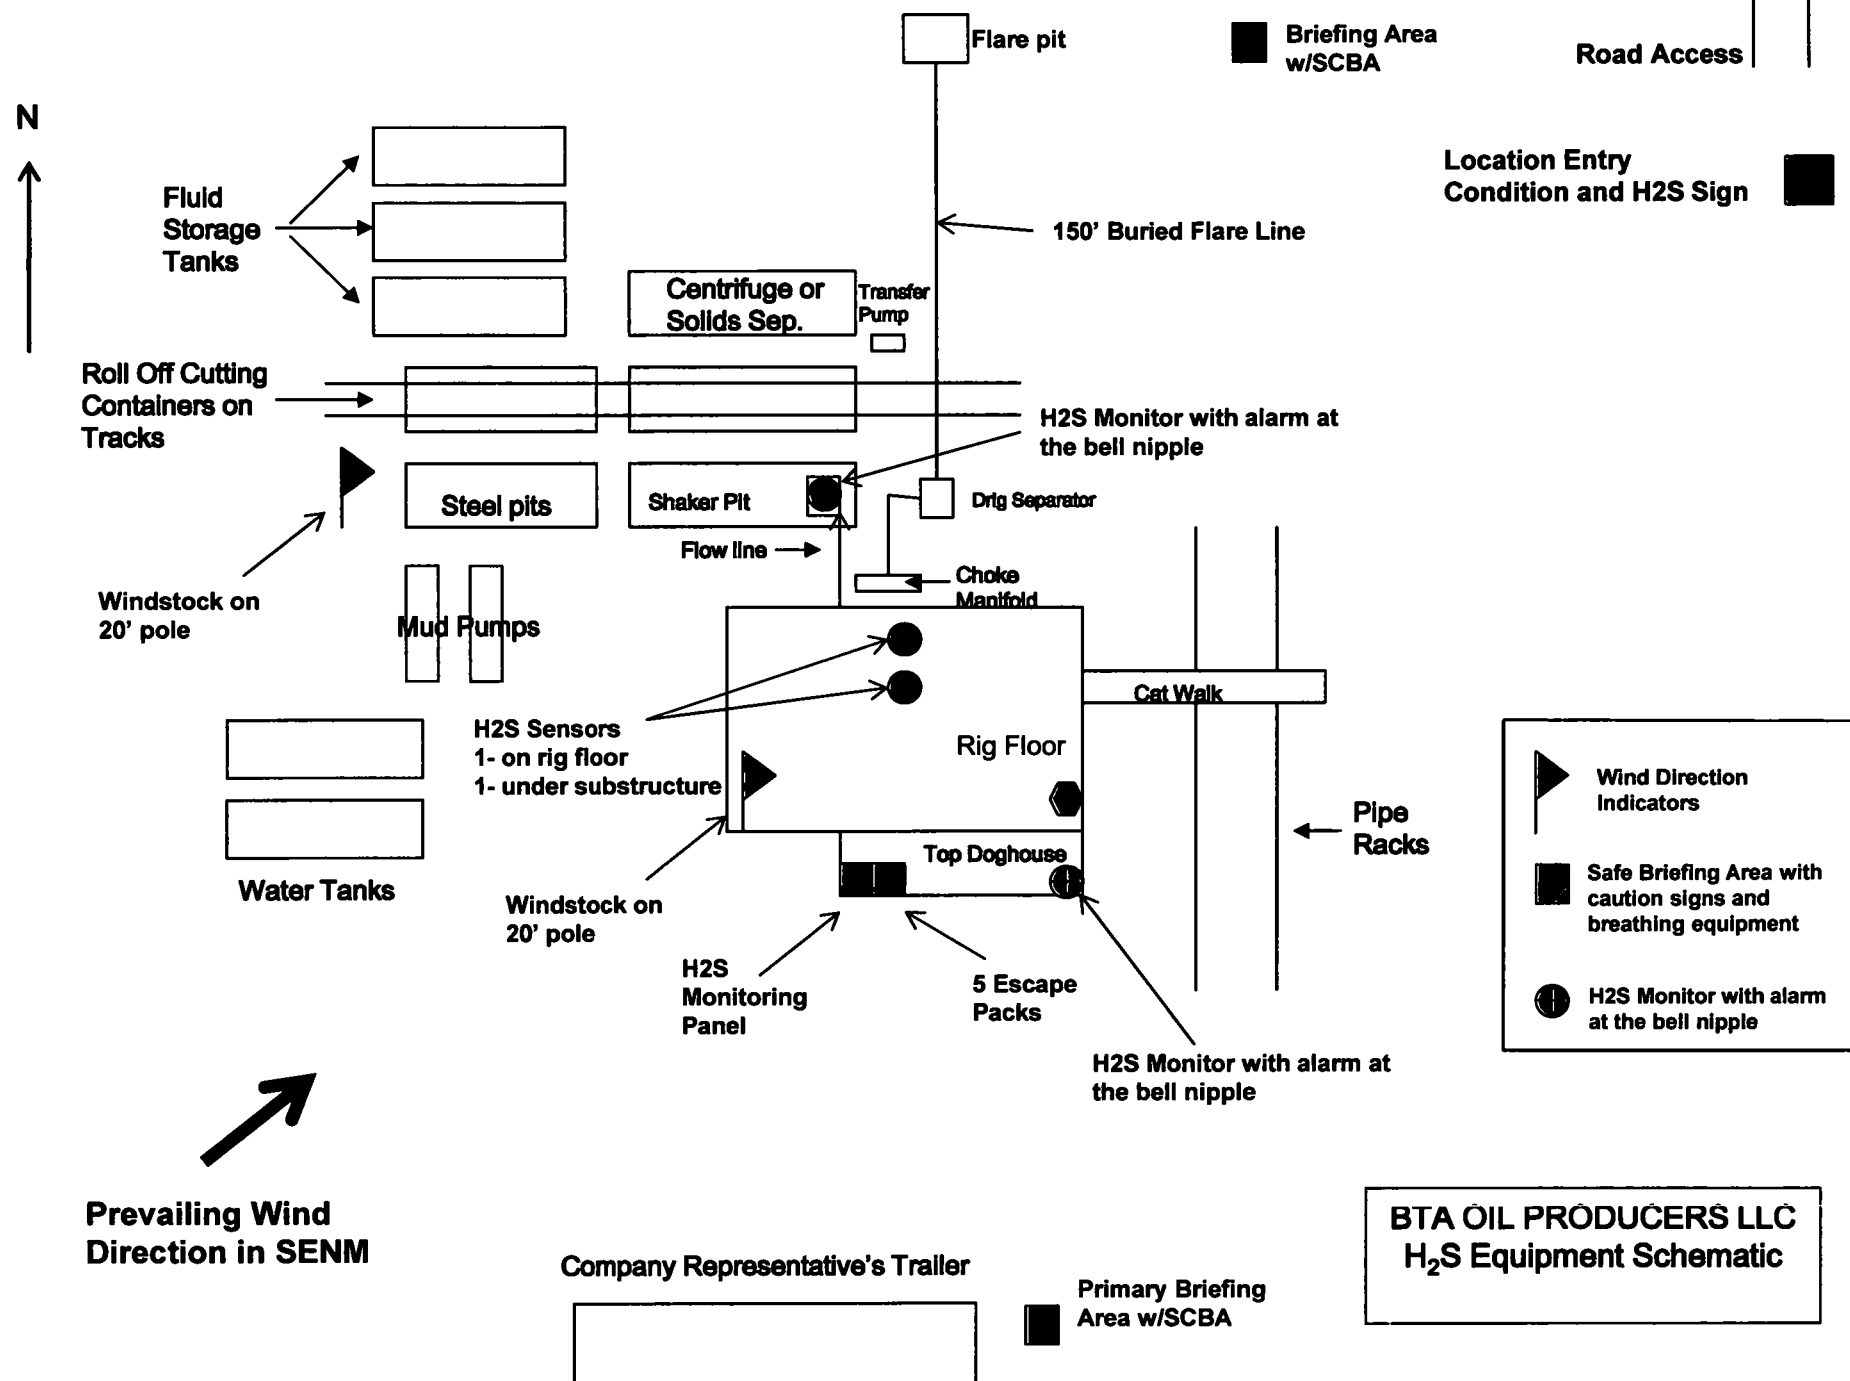

BTA OIL PRODUCERS LLC



HYDROGEN SULFIDE DRILLING OPERATIONS PLAN

1. HYDROGEN SULFIDE TRAINING

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

- a. The hazards and characteristics of hydrogen sulfide (H₂S).
- b. The proper use and maintenance of personal protective equipment and life support systems.
- c. The proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
- d. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

- a. The effects of H₂S on metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
- b. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
- c. The contents and requirements of the H₂S Drilling Operations Plan and the Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H₂S zone (within 3 days or 500 feet) and weekly H₂S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H₂S Drilling Operations Plan and the Public Protection Plan. This plan shall be available at the well site. All personnel will be required to carry documentation that they have received the proper training.

2. H₂S SAFETY EQUIPMENT AND SYSTEMS

Note: All H₂S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H₂S. If H₂S greater than 100 ppm is encountered in the gas stream we will shut in and install H₂S equipment.

- a. Well Control Equipment:
 - Flare line.
 - Choke manifold with remotely operated choke.
 - Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit.
 - Auxiliary equipment to include: annular preventer, mud-gas separator, rotating head.
- b. Protective equipment for essential personnel:
 - Mark II Surviveair 30-minute units located in the dog house and at briefing areas.
- c. H₂S detection and monitoring equipment:

2 - portable H₂S monitor positioned on location for best coverage and response. These units have warning lights and audible sirens when H₂S levels of 20 ppm are reached.

d. Visual warning systems:

Caution/Danger signs shall be posted on roads providing direct access to location. Signs will be painted a high visibility yellow with black lettering of sufficient size to be readable at a reasonable distance from the immediate location. Bilingual signs will be used, when appropriate. See example attached.

e. Mud Program:

The mud program has been designed to minimize the volume of H₂S circulated to the surface.

f. Metallurgy:

All drill strings, casings, tubing, wellhead, blowout preventers, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H₂S service.

g. Communication:

Company vehicles equipped with cellular telephone.

W A R N I N G

**YOU ARE ENTERING AN H₂S AREA
AUTHORIZED PERSONNEL ONLY**

- 1. BEARDS OR CONTACT LENSES NOT ALLOWED**
- 2. HARD HATS REQUIRED**
- 3. SMOKING IN DESIGNATED AREAS ONLY**
- 4. BE WIND CONSCIOUS AT ALL TIMES**
- 5. CK WITH BTA OIL PRODUCERS LLC FOREMAN AT MAIN OFFICE**

BTA OIL PRODUCERS LLC

1-432-682-3753

BTA Oil Producers, LLC

Lea County, NM (NAD 83)

Rojo

Rojo #26H

Wellbore #1

Plan: Design #1

Standard Planning Report - Geographic

01 November, 2018

BTA

Planning Report - Geographic

| | | |
|-------------------------------------|--|--|
| Database: EDM 5000.1 Single User Db | Local Co-ordinate Reference: Well Rojo #26H | |
| Company: BTA Oil Producers, LLC | TVD Reference: GL @ 3346.0usft | |
| Project: Lea County, NM (NAD 83) | MD Reference: GL @ 3346.0usft | |
| Site: Rojo | North Reference: Grid | |
| Well: Rojo #26H | Survey Calculation Method: Minimum Curvature | |
| Wellbore: Wellbore #1 | | |
| Design: Design #1 | | |

| | | | |
|--------------------|---|----------------------|-----------------------------|
| Project | Lea County, NM (NAD 83), Lea County, NM | | |
| Map System: | US State Plane 1983 | System Datum: | Ground Level |
| Geo Datum: | North American Datum 1983 | | |
| Map Zone: | New Mexico Eastern Zone | | Using geodetic scale factor |

| | | | |
|------------------------------|------------------|-------------------------------|------------------------------------|
| Site | Rojo | | |
| Site Position: | Northing: | 399,077.50 usft | Latitude: 32° 5' 41.057 N |
| From: Map | Easting: | 783,078.55 usft | Longitude: 103° 33' 9.721 W |
| Position Uncertainty: | 0.0 usft | Slot Radius: 13-3/16 " | Grid Convergence: 0.41 ° |

| | | | |
|-----------------------------|-------------|----------------------------|----------------------------------|
| Well | Rojo #26H | | |
| Well Position | +N-S | 0.0 usft | Northing: 404,599.00 usft |
| | +E-W | 0.0 usft | Easting: 782,111.00 usft |
| Position Uncertainty | 0.0 usft | Wellhead Elevation: | 0.0 usft |
| | | Ground Level: | 3,346.0 usft |

| | | | | | |
|------------------|-------------------|--------------------|------------------------|----------------------|----------------------------|
| Wellbore | Wellbore #1 | | | | |
| Magnetics | Model Name | Sample Date | Declination (°) | Dip Angle (°) | Field Strength (nT) |
| | IGRF200510 | 12/31/2009 | 7.73 | 60.14 | 48,726 |

| | | | | |
|--------------------------|--------------------------------|--------------------|----------------------|----------------------|
| Design | Design #1 | | | |
| Audit Notes: | | | | |
| Version: | Phase: | PROTOTYPE | Tie On Depth: | 0.0 |
| Vertical Section: | Depth From (TVD) (usft) | +N-S (usft) | +E-W (usft) | Direction (°) |
| | 0.0 | 0.0 | 0.0 | 9.93 |

| Plan Sections | | | | | | | | | | |
|-----------------------|-----------------|-------------|-----------------------|-------------|-------------|-------------------------|------------------------|-----------------------|---------|---------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N-S (usft) | +E-W (usft) | Dogleg Rate (°/100usft) | Build Rate (°/100usft) | Turn Rate (°/100usft) | TFO (°) | Target |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 2,945.6 | 0.00 | 0.00 | 2,945.6 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 3,245.6 | 6.00 | 114.15 | 3,245.0 | -6.4 | 14.3 | 2.00 | 2.00 | 0.00 | 114.15 | |
| 12,066.4 | 6.00 | 114.15 | 12,017.5 | -383.6 | 855.7 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 12,366.4 | 0.00 | 0.00 | 12,317.0 | -390.0 | 870.0 | 2.00 | -2.00 | 0.00 | 180.00 | |
| 12,416.5 | 0.00 | 0.00 | 12,367.0 | -390.0 | 870.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 13,316.5 | 90.00 | 359.60 | 12,940.0 | 182.9 | 866.0 | 10.00 | 10.00 | 0.00 | 359.60 | |
| 17,899.7 | 90.00 | 359.60 | 12,940.0 | 4,766.1 | 834.0 | 0.00 | 0.00 | 0.00 | 0.00 | Rojo #26H BHL |

BTA

Planning Report - Geographic

| | |
|-------------------------------------|--|
| Database: EDM 5000.1 Single User Db | Local Co-ordinate Reference: Well Rojo #26H |
| Company: BTA Oil Producers, LLC | TVD Reference: GL @ 3346.0usft |
| Project: Lea County, NM (NAD 83) | MD Reference: GL @ 3346.0usft |
| Site: Rojo | North Reference: Grid |
| Well: Rojo #26H | Survey Calculation Method: Minimum Curvature |
| Wellbore: Wellbore #1 | |
| Design: Design #1 | |

Planned Survey

| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Map Northing (usft) | Map Easting (usft) | Latitude | Longitude |
|-----------------------------|--------------------|----------------|-----------------------------|-----------------|-----------------|---------------------------|--------------------------|-----------------|-------------------|
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 100.0 | 0.00 | 0.00 | 100.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 200.0 | 0.00 | 0.00 | 200.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 300.0 | 0.00 | 0.00 | 300.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 400.0 | 0.00 | 0.00 | 400.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 500.0 | 0.00 | 0.00 | 500.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 700.0 | 0.00 | 0.00 | 700.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 800.0 | 0.00 | 0.00 | 800.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 900.0 | 0.00 | 0.00 | 900.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,000.0 | 0.00 | 0.00 | 1,000.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,100.0 | 0.00 | 0.00 | 1,100.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,200.0 | 0.00 | 0.00 | 1,200.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,300.0 | 0.00 | 0.00 | 1,300.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,400.0 | 0.00 | 0.00 | 1,400.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,500.0 | 0.00 | 0.00 | 1,500.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,600.0 | 0.00 | 0.00 | 1,600.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,700.0 | 0.00 | 0.00 | 1,700.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,800.0 | 0.00 | 0.00 | 1,800.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 1,900.0 | 0.00 | 0.00 | 1,900.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,000.0 | 0.00 | 0.00 | 2,000.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,100.0 | 0.00 | 0.00 | 2,100.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,200.0 | 0.00 | 0.00 | 2,200.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,300.0 | 0.00 | 0.00 | 2,300.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,400.0 | 0.00 | 0.00 | 2,400.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,500.0 | 0.00 | 0.00 | 2,500.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,600.0 | 0.00 | 0.00 | 2,600.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,700.0 | 0.00 | 0.00 | 2,700.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,800.0 | 0.00 | 0.00 | 2,800.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,900.0 | 0.00 | 0.00 | 2,900.0 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 2,945.6 | 0.00 | 0.00 | 2,945.6 | 0.0 | 0.0 | 404,599.00 | 782,111.00 | 32° 6' 35.763 N | 103° 33' 20.505 W |
| 3,000.0 | 1.09 | 114.15 | 3,000.0 | -0.2 | 0.5 | 404,598.79 | 782,111.47 | 32° 6' 35.761 N | 103° 33' 20.500 W |
| 3,100.0 | 3.09 | 114.15 | 3,099.9 | -1.7 | 3.8 | 404,597.30 | 782,114.79 | 32° 6' 35.746 N | 103° 33' 20.461 W |
| 3,200.0 | 5.09 | 114.15 | 3,199.7 | -4.6 | 10.3 | 404,594.38 | 782,121.30 | 32° 6' 35.717 N | 103° 33' 20.386 W |
| 3,245.6 | 6.00 | 114.15 | 3,245.0 | -6.4 | 14.3 | 404,592.58 | 782,125.32 | 32° 6' 35.699 N | 103° 33' 20.339 W |
| 3,300.0 | 6.00 | 114.15 | 3,299.2 | -8.7 | 19.5 | 404,590.25 | 782,130.51 | 32° 6' 35.675 N | 103° 33' 20.279 W |
| 3,400.0 | 6.00 | 114.15 | 3,398.6 | -13.0 | 29.0 | 404,585.98 | 782,140.05 | 32° 6' 35.632 N | 103° 33' 20.169 W |
| 3,500.0 | 6.00 | 114.15 | 3,498.1 | -17.3 | 38.6 | 404,581.70 | 782,149.58 | 32° 6' 35.589 N | 103° 33' 20.058 W |
| 3,600.0 | 6.00 | 114.15 | 3,597.5 | -21.6 | 48.1 | 404,577.43 | 782,159.12 | 32° 6' 35.547 N | 103° 33' 19.948 W |
| 3,700.0 | 6.00 | 114.15 | 3,697.0 | -25.8 | 57.7 | 404,573.15 | 782,168.66 | 32° 6' 35.504 N | 103° 33' 19.837 W |
| 3,800.0 | 6.00 | 114.15 | 3,796.4 | -30.1 | 67.2 | 404,568.87 | 782,178.20 | 32° 6' 35.461 N | 103° 33' 19.726 W |
| 3,900.0 | 6.00 | 114.15 | 3,895.9 | -34.4 | 76.7 | 404,564.60 | 782,187.74 | 32° 6' 35.418 N | 103° 33' 19.616 W |
| 4,000.0 | 6.00 | 114.15 | 3,995.3 | -38.7 | 86.3 | 404,560.32 | 782,197.27 | 32° 6' 35.375 N | 103° 33' 19.505 W |
| 4,100.0 | 6.00 | 114.15 | 4,094.8 | -43.0 | 95.8 | 404,556.05 | 782,206.81 | 32° 6' 35.332 N | 103° 33' 19.395 W |
| 4,200.0 | 6.00 | 114.15 | 4,194.2 | -47.2 | 105.4 | 404,551.77 | 782,216.35 | 32° 6' 35.289 N | 103° 33' 19.284 W |
| 4,300.0 | 6.00 | 114.15 | 4,293.7 | -51.5 | 114.9 | 404,547.50 | 782,225.89 | 32° 6' 35.246 N | 103° 33' 19.174 W |
| 4,400.0 | 6.00 | 114.15 | 4,393.1 | -55.8 | 124.4 | 404,543.22 | 782,235.43 | 32° 6' 35.203 N | 103° 33' 19.063 W |
| 4,500.0 | 6.00 | 114.15 | 4,492.6 | -60.1 | 134.0 | 404,538.94 | 782,244.96 | 32° 6' 35.160 N | 103° 33' 18.953 W |
| 4,600.0 | 6.00 | 114.15 | 4,592.0 | -64.3 | 143.5 | 404,534.67 | 782,254.50 | 32° 6' 35.117 N | 103° 33' 18.842 W |
| 4,700.0 | 6.00 | 114.15 | 4,691.5 | -68.6 | 153.0 | 404,530.39 | 782,264.04 | 32° 6' 35.074 N | 103° 33' 18.732 W |
| 4,800.0 | 6.00 | 114.15 | 4,790.9 | -72.9 | 162.6 | 404,526.12 | 782,273.58 | 32° 6' 35.031 N | 103° 33' 18.621 W |
| 4,900.0 | 6.00 | 114.15 | 4,890.4 | -77.2 | 172.1 | 404,521.84 | 782,283.12 | 32° 6' 34.988 N | 103° 33' 18.511 W |
| 5,000.0 | 6.00 | 114.15 | 4,989.8 | -81.4 | 181.7 | 404,517.57 | 782,292.65 | 32° 6' 34.945 N | 103° 33' 18.400 W |
| 5,100.0 | 6.00 | 114.15 | 5,089.3 | -85.7 | 191.2 | 404,513.29 | 782,302.19 | 32° 6' 34.902 N | 103° 33' 18.290 W |
| 5,200.0 | 6.00 | 114.15 | 5,188.7 | -90.0 | 200.7 | 404,509.01 | 782,311.73 | 32° 6' 34.859 N | 103° 33' 18.179 W |

BTA

Planning Report - Geographic

Database: EDM 5000.1 Single User Db
 Company: BTA Oil Producers, LLC
 Project: Lea County, NM (NAD 83)
 Site: Rojo
 Well: Rojo #26H
 Wellbore: Wellbore #1
 Design: Design #1

Local Co-ordinate Reference: Well Rojo #26H
 TVD Reference: GL @ 3346.0usft
 MD Reference: GL @ 3346.0usft
 North Reference: Grid
 Survey Calculation Method: Minimum Curvature

Planned Survey

| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Map Northing (usft) | Map Easting (usft) | Latitude | Longitude |
|-----------------------------|--------------------|----------------|-----------------------------|-----------------|-----------------|---------------------------|--------------------------|-----------------|-------------------|
| 5,300.0 | 6.00 | 114.15 | 5,288.2 | -94.3 | 210.3 | 404,504.74 | 782,321.27 | 32° 6' 34.816 N | 103° 33' 18.068 W |
| 5,400.0 | 6.00 | 114.15 | 5,387.6 | -98.5 | 219.8 | 404,500.46 | 782,330.81 | 32° 6' 34.773 N | 103° 33' 17.958 W |
| 5,500.0 | 6.00 | 114.15 | 5,487.1 | -102.8 | 229.4 | 404,496.19 | 782,340.35 | 32° 6' 34.730 N | 103° 33' 17.847 W |
| 5,600.0 | 6.00 | 114.15 | 5,586.6 | -107.1 | 238.9 | 404,491.91 | 782,349.88 | 32° 6' 34.687 N | 103° 33' 17.737 W |
| 5,700.0 | 6.00 | 114.15 | 5,686.0 | -111.4 | 248.4 | 404,487.64 | 782,359.42 | 32° 6' 34.644 N | 103° 33' 17.626 W |
| 5,800.0 | 6.00 | 114.15 | 5,785.5 | -115.6 | 258.0 | 404,483.36 | 782,368.96 | 32° 6' 34.601 N | 103° 33' 17.516 W |
| 5,900.0 | 6.00 | 114.15 | 5,884.9 | -119.9 | 267.5 | 404,479.09 | 782,378.50 | 32° 6' 34.558 N | 103° 33' 17.405 W |
| 6,000.0 | 6.00 | 114.15 | 5,984.4 | -124.2 | 277.0 | 404,474.81 | 782,388.04 | 32° 6' 34.515 N | 103° 33' 17.295 W |
| 6,100.0 | 6.00 | 114.15 | 6,083.8 | -128.5 | 286.6 | 404,470.53 | 782,397.57 | 32° 6' 34.472 N | 103° 33' 17.184 W |
| 6,200.0 | 6.00 | 114.15 | 6,183.3 | -132.7 | 296.1 | 404,466.26 | 782,407.11 | 32° 6' 34.429 N | 103° 33' 17.074 W |
| 6,300.0 | 6.00 | 114.15 | 6,282.7 | -137.0 | 305.7 | 404,461.98 | 782,416.65 | 32° 6' 34.386 N | 103° 33' 16.963 W |
| 6,400.0 | 6.00 | 114.15 | 6,382.2 | -141.3 | 315.2 | 404,457.71 | 782,426.19 | 32° 6' 34.343 N | 103° 33' 16.853 W |
| 6,500.0 | 6.00 | 114.15 | 6,481.6 | -145.6 | 324.7 | 404,453.43 | 782,435.73 | 32° 6' 34.300 N | 103° 33' 16.742 W |
| 6,600.0 | 6.00 | 114.15 | 6,581.1 | -149.8 | 334.3 | 404,449.16 | 782,445.26 | 32° 6' 34.257 N | 103° 33' 16.632 W |
| 6,700.0 | 6.00 | 114.15 | 6,680.5 | -154.1 | 343.8 | 404,444.88 | 782,454.80 | 32° 6' 34.214 N | 103° 33' 16.521 W |
| 6,800.0 | 6.00 | 114.15 | 6,780.0 | -158.4 | 353.4 | 404,440.60 | 782,464.34 | 32° 6' 34.171 N | 103° 33' 16.411 W |
| 6,900.0 | 6.00 | 114.15 | 6,879.4 | -162.7 | 362.9 | 404,436.33 | 782,473.88 | 32° 6' 34.128 N | 103° 33' 16.300 W |
| 7,000.0 | 6.00 | 114.15 | 6,978.9 | -167.0 | 372.4 | 404,432.05 | 782,483.42 | 32° 6' 34.085 N | 103° 33' 16.189 W |
| 7,100.0 | 6.00 | 114.15 | 7,078.3 | -171.2 | 382.0 | 404,427.78 | 782,492.95 | 32° 6' 34.042 N | 103° 33' 16.079 W |
| 7,200.0 | 6.00 | 114.15 | 7,177.8 | -175.5 | 391.5 | 404,423.50 | 782,502.49 | 32° 6' 33.999 N | 103° 33' 15.968 W |
| 7,300.0 | 6.00 | 114.15 | 7,277.2 | -179.8 | 401.0 | 404,419.23 | 782,512.03 | 32° 6' 33.956 N | 103° 33' 15.858 W |
| 7,400.0 | 6.00 | 114.15 | 7,376.7 | -184.1 | 410.6 | 404,414.95 | 782,521.57 | 32° 6' 33.913 N | 103° 33' 15.747 W |
| 7,500.0 | 6.00 | 114.15 | 7,476.1 | -188.3 | 420.1 | 404,410.67 | 782,531.11 | 32° 6' 33.870 N | 103° 33' 15.637 W |
| 7,600.0 | 6.00 | 114.15 | 7,575.6 | -192.6 | 429.7 | 404,406.40 | 782,540.65 | 32° 6' 33.827 N | 103° 33' 15.526 W |
| 7,700.0 | 6.00 | 114.15 | 7,675.1 | -196.9 | 439.2 | 404,402.12 | 782,550.18 | 32° 6' 33.784 N | 103° 33' 15.416 W |
| 7,800.0 | 6.00 | 114.15 | 7,774.5 | -201.2 | 448.7 | 404,397.85 | 782,559.72 | 32° 6' 33.741 N | 103° 33' 15.305 W |
| 7,900.0 | 6.00 | 114.15 | 7,874.0 | -205.4 | 458.3 | 404,393.57 | 782,569.26 | 32° 6' 33.698 N | 103° 33' 15.195 W |
| 8,000.0 | 6.00 | 114.15 | 7,973.4 | -209.7 | 467.8 | 404,389.30 | 782,578.80 | 32° 6' 33.655 N | 103° 33' 15.084 W |
| 8,100.0 | 6.00 | 114.15 | 8,072.9 | -214.0 | 477.3 | 404,385.02 | 782,588.34 | 32° 6' 33.612 N | 103° 33' 14.974 W |
| 8,200.0 | 6.00 | 114.15 | 8,172.3 | -218.3 | 486.9 | 404,380.74 | 782,597.87 | 32° 6' 33.569 N | 103° 33' 14.863 W |
| 8,300.0 | 6.00 | 114.15 | 8,271.8 | -222.5 | 496.4 | 404,376.47 | 782,607.41 | 32° 6' 33.526 N | 103° 33' 14.753 W |
| 8,400.0 | 6.00 | 114.15 | 8,371.2 | -226.8 | 506.0 | 404,372.19 | 782,616.95 | 32° 6' 33.483 N | 103° 33' 14.642 W |
| 8,500.0 | 6.00 | 114.15 | 8,470.7 | -231.1 | 515.5 | 404,367.92 | 782,626.49 | 32° 6' 33.440 N | 103° 33' 14.531 W |
| 8,600.0 | 6.00 | 114.15 | 8,570.1 | -235.4 | 525.0 | 404,363.64 | 782,636.03 | 32° 6' 33.397 N | 103° 33' 14.421 W |
| 8,700.0 | 6.00 | 114.15 | 8,669.6 | -239.6 | 534.6 | 404,359.37 | 782,645.56 | 32° 6' 33.354 N | 103° 33' 14.310 W |
| 8,800.0 | 6.00 | 114.15 | 8,769.0 | -243.9 | 544.1 | 404,355.09 | 782,655.10 | 32° 6' 33.311 N | 103° 33' 14.200 W |
| 8,900.0 | 6.00 | 114.15 | 8,868.5 | -248.2 | 553.7 | 404,350.81 | 782,664.64 | 32° 6' 33.268 N | 103° 33' 14.089 W |
| 9,000.0 | 6.00 | 114.15 | 8,967.9 | -252.5 | 563.2 | 404,346.54 | 782,674.18 | 32° 6' 33.225 N | 103° 33' 13.979 W |
| 9,100.0 | 6.00 | 114.15 | 9,067.4 | -256.7 | 572.7 | 404,342.26 | 782,683.72 | 32° 6' 33.182 N | 103° 33' 13.868 W |
| 9,200.0 | 6.00 | 114.15 | 9,166.8 | -261.0 | 582.3 | 404,337.99 | 782,693.25 | 32° 6' 33.139 N | 103° 33' 13.758 W |
| 9,300.0 | 6.00 | 114.15 | 9,266.3 | -265.3 | 591.8 | 404,333.71 | 782,702.79 | 32° 6' 33.096 N | 103° 33' 13.647 W |
| 9,400.0 | 6.00 | 114.15 | 9,365.7 | -269.6 | 601.3 | 404,329.44 | 782,712.33 | 32° 6' 33.053 N | 103° 33' 13.537 W |
| 9,500.0 | 6.00 | 114.15 | 9,465.2 | -273.8 | 610.9 | 404,325.16 | 782,721.87 | 32° 6' 33.010 N | 103° 33' 13.426 W |
| 9,600.0 | 6.00 | 114.15 | 9,564.6 | -278.1 | 620.4 | 404,320.88 | 782,731.41 | 32° 6' 32.967 N | 103° 33' 13.316 W |
| 9,700.0 | 6.00 | 114.15 | 9,664.1 | -282.4 | 630.0 | 404,316.61 | 782,740.95 | 32° 6' 32.924 N | 103° 33' 13.205 W |
| 9,800.0 | 6.00 | 114.15 | 9,763.5 | -286.7 | 639.5 | 404,312.33 | 782,750.48 | 32° 6' 32.881 N | 103° 33' 13.095 W |
| 9,900.0 | 6.00 | 114.15 | 9,863.0 | -290.9 | 649.0 | 404,308.06 | 782,760.02 | 32° 6' 32.838 N | 103° 33' 12.984 W |
| 10,000.0 | 6.00 | 114.15 | 9,962.5 | -295.2 | 658.6 | 404,303.78 | 782,769.56 | 32° 6' 32.795 N | 103° 33' 12.874 W |
| 10,100.0 | 6.00 | 114.15 | 10,061.9 | -299.5 | 668.1 | 404,299.51 | 782,779.10 | 32° 6' 32.752 N | 103° 33' 12.763 W |
| 10,200.0 | 6.00 | 114.15 | 10,161.4 | -303.8 | 677.7 | 404,295.23 | 782,788.64 | 32° 6' 32.709 N | 103° 33' 12.652 W |
| 10,300.0 | 6.00 | 114.15 | 10,260.8 | -308.1 | 687.2 | 404,290.95 | 782,798.17 | 32° 6' 32.666 N | 103° 33' 12.542 W |
| 10,400.0 | 6.00 | 114.15 | 10,360.3 | -312.3 | 696.7 | 404,286.68 | 782,807.71 | 32° 6' 32.623 N | 103° 33' 12.431 W |
| 10,500.0 | 6.00 | 114.15 | 10,459.7 | -316.6 | 706.3 | 404,282.40 | 782,817.25 | 32° 6' 32.580 N | 103° 33' 12.321 W |
| 10,600.0 | 6.00 | 114.15 | 10,559.2 | -320.9 | 715.8 | 404,278.13 | 782,826.79 | 32° 6' 32.537 N | 103° 33' 12.210 W |
| 10,700.0 | 6.00 | 114.15 | 10,658.6 | -325.2 | 725.3 | 404,273.85 | 782,836.33 | 32° 6' 32.494 N | 103° 33' 12.100 W |

BTA

Planning Report - Geographic

Database: EDM 5000.1 Single User Db
 Company: BTA Oil Producers, LLC
 Project: Lea County, NM (NAD 83)
 Site: Rojo
 Well: Rojo #26H
 Wellbore: Wellbore #1
 Design: Design #1

Local Co-ordinate Reference: Well Rojo #26H
 TVD Reference: GL @ 3346.0usft
 MD Reference: GL @ 3346.0usft
 North Reference: Grid
 Survey Calculation Method: Minimum Curvature

| Planned Survey | | | | | | | | | |
|-----------------------------|--------------------|----------------|-----------------------------|-----------------|-----------------|---------------------------|--------------------------|-----------------|-------------------|
| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Map Northing (usft) | Map Easting (usft) | Latitude | Longitude |
| 10,800.0 | 6.00 | 114.15 | 10,758.1 | -329.4 | 734.9 | 404,269.58 | 782,845.86 | 32° 6' 32.451 N | 103° 33' 11.989 W |
| 10,900.0 | 6.00 | 114.15 | 10,857.5 | -333.7 | 744.4 | 404,265.30 | 782,855.40 | 32° 6' 32.408 N | 103° 33' 11.879 W |
| 11,000.0 | 6.00 | 114.15 | 10,957.0 | -338.0 | 754.0 | 404,261.02 | 782,864.94 | 32° 6' 32.365 N | 103° 33' 11.768 W |
| 11,100.0 | 6.00 | 114.15 | 11,056.4 | -342.3 | 763.5 | 404,256.75 | 782,874.48 | 32° 6' 32.322 N | 103° 33' 11.658 W |
| 11,200.0 | 6.00 | 114.15 | 11,155.9 | -346.5 | 773.0 | 404,252.47 | 782,884.02 | 32° 6' 32.279 N | 103° 33' 11.547 W |
| 11,300.0 | 6.00 | 114.15 | 11,255.3 | -350.8 | 782.6 | 404,248.20 | 782,893.55 | 32° 6' 32.236 N | 103° 33' 11.437 W |
| 11,400.0 | 6.00 | 114.15 | 11,354.8 | -355.1 | 792.1 | 404,243.92 | 782,903.09 | 32° 6' 32.193 N | 103° 33' 11.326 W |
| 11,500.0 | 6.00 | 114.15 | 11,454.2 | -359.4 | 801.7 | 404,239.65 | 782,912.63 | 32° 6' 32.150 N | 103° 33' 11.216 W |
| 11,600.0 | 6.00 | 114.15 | 11,553.7 | -363.6 | 811.2 | 404,235.37 | 782,922.17 | 32° 6' 32.107 N | 103° 33' 11.105 W |
| 11,700.0 | 6.00 | 114.15 | 11,653.1 | -367.9 | 820.7 | 404,231.09 | 782,931.71 | 32° 6' 32.064 N | 103° 33' 10.994 W |
| 11,800.0 | 6.00 | 114.15 | 11,752.6 | -372.2 | 830.3 | 404,226.82 | 782,941.24 | 32° 6' 32.021 N | 103° 33' 10.884 W |
| 11,900.0 | 6.00 | 114.15 | 11,852.0 | -376.5 | 839.8 | 404,222.54 | 782,950.78 | 32° 6' 31.978 N | 103° 33' 10.773 W |
| 12,000.0 | 6.00 | 114.15 | 11,951.5 | -380.7 | 849.3 | 404,218.27 | 782,960.32 | 32° 6' 31.935 N | 103° 33' 10.663 W |
| 12,066.4 | 6.00 | 114.15 | 12,017.5 | -383.6 | 855.7 | 404,215.43 | 782,966.66 | 32° 6' 31.907 N | 103° 33' 10.589 W |
| 12,100.0 | 5.33 | 114.15 | 12,051.0 | -384.9 | 858.7 | 404,214.07 | 782,969.68 | 32° 6' 31.893 N | 103° 33' 10.554 W |
| 12,200.0 | 3.33 | 114.15 | 12,150.7 | -388.0 | 865.6 | 404,210.99 | 782,976.57 | 32° 6' 31.862 N | 103° 33' 10.475 W |
| 12,300.0 | 1.33 | 114.15 | 12,250.6 | -389.7 | 869.3 | 404,209.32 | 782,980.27 | 32° 6' 31.845 N | 103° 33' 10.432 W |
| 12,366.4 | 0.00 | 0.00 | 12,317.0 | -390.0 | 870.0 | 404,209.01 | 782,980.98 | 32° 6' 31.842 N | 103° 33' 10.424 W |
| 12,400.0 | 0.00 | 0.00 | 12,350.6 | -390.0 | 870.0 | 404,209.01 | 782,980.98 | 32° 6' 31.842 N | 103° 33' 10.424 W |
| 12,416.5 | 0.00 | 0.00 | 12,367.0 | -390.0 | 870.0 | 404,209.01 | 782,980.98 | 32° 6' 31.842 N | 103° 33' 10.424 W |
| 12,500.0 | 8.35 | 359.60 | 12,450.3 | -383.9 | 870.0 | 404,215.09 | 782,980.93 | 32° 6' 31.902 N | 103° 33' 10.424 W |
| 12,600.0 | 18.35 | 359.60 | 12,547.5 | -360.9 | 869.8 | 404,238.15 | 782,980.77 | 32° 6' 32.131 N | 103° 33' 10.423 W |
| 12,700.0 | 28.35 | 359.60 | 12,639.2 | -321.3 | 869.5 | 404,277.74 | 782,980.50 | 32° 6' 32.522 N | 103° 33' 10.423 W |
| 12,800.0 | 38.35 | 359.60 | 12,722.6 | -266.4 | 869.1 | 404,332.65 | 782,980.11 | 32° 6' 33.066 N | 103° 33' 10.423 W |
| 12,900.0 | 48.35 | 359.60 | 12,795.2 | -197.8 | 868.7 | 404,401.21 | 782,979.63 | 32° 6' 33.744 N | 103° 33' 10.423 W |
| 13,000.0 | 58.35 | 359.60 | 12,854.8 | -117.7 | 868.1 | 404,481.34 | 782,979.08 | 32° 6' 34.537 N | 103° 33' 10.423 W |
| 13,100.0 | 68.35 | 359.60 | 12,899.6 | -28.4 | 867.5 | 404,570.60 | 782,978.45 | 32° 6' 35.420 N | 103° 33' 10.422 W |
| 13,200.0 | 78.35 | 359.60 | 12,928.2 | 67.3 | 866.8 | 404,666.28 | 782,977.79 | 32° 6' 36.367 N | 103° 33' 10.422 W |
| 13,300.0 | 88.35 | 359.60 | 12,939.8 | 166.5 | 866.1 | 404,765.48 | 782,977.09 | 32° 6' 37.349 N | 103° 33' 10.422 W |
| 13,316.5 | 90.00 | 359.60 | 12,940.0 | 182.9 | 866.0 | 404,781.94 | 782,976.98 | 32° 6' 37.512 N | 103° 33' 10.422 W |
| 13,400.0 | 90.00 | 359.60 | 12,940.0 | 266.5 | 865.4 | 404,865.47 | 782,976.40 | 32° 6' 38.338 N | 103° 33' 10.422 W |
| 13,500.0 | 90.00 | 359.60 | 12,940.0 | 366.5 | 864.7 | 404,965.47 | 782,975.70 | 32° 6' 39.328 N | 103° 33' 10.421 W |
| 13,600.0 | 90.00 | 359.60 | 12,940.0 | 466.5 | 864.0 | 405,085.46 | 782,975.00 | 32° 6' 40.317 N | 103° 33' 10.421 W |
| 13,700.0 | 90.00 | 359.60 | 12,940.0 | 566.5 | 863.3 | 405,165.46 | 782,974.30 | 32° 6' 41.307 N | 103° 33' 10.421 W |
| 13,800.0 | 90.00 | 359.60 | 12,940.0 | 666.5 | 862.6 | 405,265.46 | 782,973.60 | 32° 6' 42.297 N | 103° 33' 10.420 W |
| 13,900.0 | 90.00 | 359.60 | 12,940.0 | 766.5 | 861.9 | 405,365.45 | 782,972.91 | 32° 6' 43.286 N | 103° 33' 10.420 W |
| 14,000.0 | 90.00 | 359.60 | 12,940.0 | 866.5 | 861.2 | 405,465.45 | 782,972.21 | 32° 6' 44.276 N | 103° 33' 10.420 W |
| 14,100.0 | 90.00 | 359.60 | 12,940.0 | 966.5 | 860.5 | 405,565.44 | 782,971.51 | 32° 6' 45.265 N | 103° 33' 10.419 W |
| 14,200.0 | 90.00 | 359.60 | 12,940.0 | 1,066.5 | 859.8 | 405,665.44 | 782,970.81 | 32° 6' 46.255 N | 103° 33' 10.419 W |
| 14,300.0 | 90.00 | 359.60 | 12,940.0 | 1,166.5 | 859.1 | 405,765.43 | 782,970.12 | 32° 6' 47.244 N | 103° 33' 10.419 W |
| 14,400.0 | 90.00 | 359.60 | 12,940.0 | 1,266.5 | 858.4 | 405,865.43 | 782,969.42 | 32° 6' 48.234 N | 103° 33' 10.418 W |
| 14,500.0 | 90.00 | 359.60 | 12,940.0 | 1,366.5 | 857.7 | 405,965.42 | 782,968.72 | 32° 6' 49.223 N | 103° 33' 10.418 W |
| 14,600.0 | 90.00 | 359.60 | 12,940.0 | 1,466.5 | 857.0 | 406,065.42 | 782,968.02 | 32° 6' 50.213 N | 103° 33' 10.418 W |
| 14,700.0 | 90.00 | 359.60 | 12,940.0 | 1,566.5 | 856.3 | 406,165.41 | 782,967.32 | 32° 6' 51.202 N | 103° 33' 10.418 W |
| 14,800.0 | 90.00 | 359.60 | 12,940.0 | 1,666.4 | 855.7 | 406,265.41 | 782,966.63 | 32° 6' 52.192 N | 103° 33' 10.417 W |
| 14,900.0 | 90.00 | 359.60 | 12,940.0 | 1,766.4 | 855.0 | 406,365.40 | 782,965.93 | 32° 6' 53.181 N | 103° 33' 10.417 W |
| 15,000.0 | 90.00 | 359.60 | 12,940.0 | 1,866.4 | 854.3 | 406,465.40 | 782,965.23 | 32° 6' 54.171 N | 103° 33' 10.417 W |
| 15,100.0 | 90.00 | 359.60 | 12,940.0 | 1,966.4 | 853.6 | 406,565.39 | 782,964.53 | 32° 6' 55.160 N | 103° 33' 10.416 W |
| 15,200.0 | 90.00 | 359.60 | 12,940.0 | 2,066.4 | 852.9 | 406,665.39 | 782,963.84 | 32° 6' 56.150 N | 103° 33' 10.416 W |
| 15,300.0 | 90.00 | 359.60 | 12,940.0 | 2,166.4 | 852.2 | 406,765.38 | 782,963.14 | 32° 6' 57.140 N | 103° 33' 10.416 W |
| 15,400.0 | 90.00 | 359.60 | 12,940.0 | 2,266.4 | 851.5 | 406,865.38 | 782,962.44 | 32° 6' 58.129 N | 103° 33' 10.415 W |
| 15,500.0 | 90.00 | 359.60 | 12,940.0 | 2,366.4 | 850.8 | 406,965.37 | 782,961.74 | 32° 6' 59.119 N | 103° 33' 10.415 W |
| 15,600.0 | 90.00 | 359.60 | 12,940.0 | 2,466.4 | 850.1 | 407,065.37 | 782,961.04 | 32° 7' 0.108 N | 103° 33' 10.415 W |
| 15,700.0 | 90.00 | 359.60 | 12,940.0 | 2,566.4 | 849.4 | 407,165.36 | 782,960.35 | 32° 7' 1.098 N | 103° 33' 10.414 W |
| 15,800.0 | 90.00 | 359.60 | 12,940.0 | 2,666.4 | 848.7 | 407,265.36 | 782,959.65 | 32° 7' 2.087 N | 103° 33' 10.414 W |

BTA
Planning Report - Geographic

| | | | |
|------------------|---------------------------|-------------------------------------|-------------------|
| Database: | EDM 5000.1 Single User Db | Local Co-ordinate Reference: | Well Rojo #26H |
| Company: | BTA Oil Producers, LLC | TVD Reference: | GL @ 3346.0usft |
| Project: | Lea County, NM (NAD 83) | MD Reference: | GL @ 3346.0usft |
| Site: | Rojo | North Reference: | Grid |
| Well: | Rojo #26H | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | Design #1 | | |


Planned Survey

| Measured Depth (usft) | Inclination (°) | Azimuth (°) | Vertical Depth (usft) | +N/-S (usft) | +E/-W (usft) | Map Northing (usft) | Map Easting (usft) | Latitude | Longitude |
|-----------------------------|--------------------|----------------|-----------------------------|-----------------|-----------------|---------------------------|--------------------------|-----------------|-------------------|
| 15,900.0 | 90.00 | 359.60 | 12,940.0 | 2,766.4 | 848.0 | 407,365.35 | 782,958.95 | 32° 7' 3.077 N | 103° 33' 10.414 W |
| 16,000.0 | 90.00 | 359.60 | 12,940.0 | 2,866.4 | 847.3 | 407,465.35 | 782,958.25 | 32° 7' 4.066 N | 103° 33' 10.414 W |
| 16,100.0 | 90.00 | 359.60 | 12,940.0 | 2,966.4 | 846.6 | 407,565.34 | 782,957.56 | 32° 7' 5.056 N | 103° 33' 10.413 W |
| 16,200.0 | 90.00 | 359.60 | 12,940.0 | 3,066.4 | 845.9 | 407,665.34 | 782,956.86 | 32° 7' 6.045 N | 103° 33' 10.413 W |
| 16,300.0 | 90.00 | 359.60 | 12,940.0 | 3,166.4 | 845.2 | 407,765.33 | 782,956.16 | 32° 7' 7.035 N | 103° 33' 10.413 W |
| 16,400.0 | 90.00 | 359.60 | 12,940.0 | 3,266.4 | 844.5 | 407,865.33 | 782,955.46 | 32° 7' 8.024 N | 103° 33' 10.412 W |
| 16,500.0 | 90.00 | 359.60 | 12,940.0 | 3,366.4 | 843.8 | 407,965.32 | 782,954.76 | 32° 7' 9.014 N | 103° 33' 10.412 W |
| 16,600.0 | 90.00 | 359.60 | 12,940.0 | 3,466.4 | 843.1 | 408,065.32 | 782,954.07 | 32° 7' 10.003 N | 103° 33' 10.412 W |
| 16,700.0 | 90.00 | 359.60 | 12,940.0 | 3,566.4 | 842.4 | 408,165.31 | 782,953.37 | 32° 7' 10.993 N | 103° 33' 10.411 W |
| 16,800.0 | 90.00 | 359.60 | 12,940.0 | 3,666.4 | 841.7 | 408,265.31 | 782,952.67 | 32° 7' 11.983 N | 103° 33' 10.411 W |
| 16,900.0 | 90.00 | 359.60 | 12,940.0 | 3,766.4 | 841.0 | 408,365.30 | 782,951.97 | 32° 7' 12.972 N | 103° 33' 10.411 W |
| 17,000.0 | 90.00 | 359.60 | 12,940.0 | 3,866.4 | 840.3 | 408,465.30 | 782,951.28 | 32° 7' 13.962 N | 103° 33' 10.410 W |
| 17,100.0 | 90.00 | 359.60 | 12,940.0 | 3,966.4 | 839.6 | 408,565.29 | 782,950.58 | 32° 7' 14.951 N | 103° 33' 10.410 W |
| 17,200.0 | 90.00 | 359.60 | 12,940.0 | 4,066.4 | 838.9 | 408,665.29 | 782,949.88 | 32° 7' 15.941 N | 103° 33' 10.410 W |
| 17,300.0 | 90.00 | 359.60 | 12,940.0 | 4,166.4 | 838.2 | 408,765.28 | 782,949.18 | 32° 7' 16.930 N | 103° 33' 10.410 W |
| 17,400.0 | 90.00 | 359.60 | 12,940.0 | 4,266.4 | 837.5 | 408,865.28 | 782,948.48 | 32° 7' 17.920 N | 103° 33' 10.409 W |
| 17,500.0 | 90.00 | 359.60 | 12,940.0 | 4,366.4 | 836.8 | 408,965.27 | 782,947.79 | 32° 7' 18.909 N | 103° 33' 10.409 W |
| 17,600.0 | 90.00 | 359.60 | 12,940.0 | 4,466.4 | 836.1 | 409,065.27 | 782,947.09 | 32° 7' 19.899 N | 103° 33' 10.409 W |
| 17,700.0 | 90.00 | 359.60 | 12,940.0 | 4,566.4 | 835.4 | 409,165.26 | 782,946.39 | 32° 7' 20.888 N | 103° 33' 10.408 W |
| 17,800.0 | 90.00 | 359.60 | 12,940.0 | 4,666.4 | 834.7 | 409,265.26 | 782,945.69 | 32° 7' 21.878 N | 103° 33' 10.408 W |
| 17,899.7 | 90.00 | 359.60 | 12,940.0 | 4,766.1 | 834.0 | 409,365.00 | 782,945.00 | 32° 7' 22.865 N | 103° 33' 10.408 W |

Design Targets

| Target Name - hit/miss target - Shape | Dip Angle (°) | Dip Dir. (°) | TVD (usft) | +N/-S (usft) | +E/-W (usft) | Northing (usft) | Easting (usft) | Latitude | Longitude |
|---|------------------|-----------------|---------------|-----------------|-----------------|--------------------|-------------------|-----------------|-------------------|
| Rojo #26H BHL - plan hits target center - Point | 0.00 | 0.00 | 12,940.0 | 4,766.1 | 834.0 | 409,365.00 | 782,945.00 | 32° 7' 22.865 N | 103° 33' 10.408 W |

BTA Oil Producers, LLC



Azimuths to Grid North
 True North: -0.41°
 Magnetic North: 7.32°
 Magnetic Field
 Strength: 48726.4snT
 Dip Angle: 60.14°
 Date: 12/31/2009
 Model: IGRF200510

SITE DETAILS: Rojo

Site Centre Northing: 399077.50
 Easting: 783078.55

Positional Uncertainty: 0.0
 Convergence: 0.41
 Local North: Grid

SECTION DETAILS

| Sec | MD | Inc | Azi | TVD | +N/-S | +E/-W | Dleg |
|-----|---------|-------|--------|---------|--------|-------|-------|
| 1 | 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 |
| 2 | 2945.6 | 0.00 | 0.00 | 2945.6 | 0.0 | 0.0 | 0.00 |
| 3 | 3245.6 | 6.00 | 114.15 | 3245.0 | -6.4 | 14.3 | 2.00 |
| 4 | 12066.4 | 6.00 | 114.15 | 12017.5 | -383.6 | 855.7 | 0.00 |
| 5 | 12366.4 | 0.00 | 0.00 | 12317.0 | -390.0 | 870.0 | 2.00 |
| 6 | 12416.5 | 0.00 | 0.00 | 12367.0 | -390.0 | 870.0 | 0.00 |
| 7 | 13316.5 | 90.00 | 359.60 | 12940.0 | 182.9 | 866.0 | 10.00 |
| 8 | 17899.7 | 90.00 | 359.60 | 12940.0 | 4766.1 | 834.0 | 0.00 |



PROJECT DETAILS: Lea County, NM (NAD 83)

Geodetic System: US State Plane 1983
 Datum: North American Datum 1983
 Ellipsoid: GRS 1980
 Zone: New Mexico Eastern Zone

System Datum: Ground Level

WELL DETAILS: Rojo #26H

| +N/-S | +E/-W | Northing | Easting | Ground Level: | Latitude | Longitude |
|-------|-------|-----------|-----------|---------------|-----------------|-------------------|
| 0.0 | 0.0 | 404599.00 | 782111.00 | 3346.0 | 32° 6' 35.763 N | 103° 33' 20.505 W |

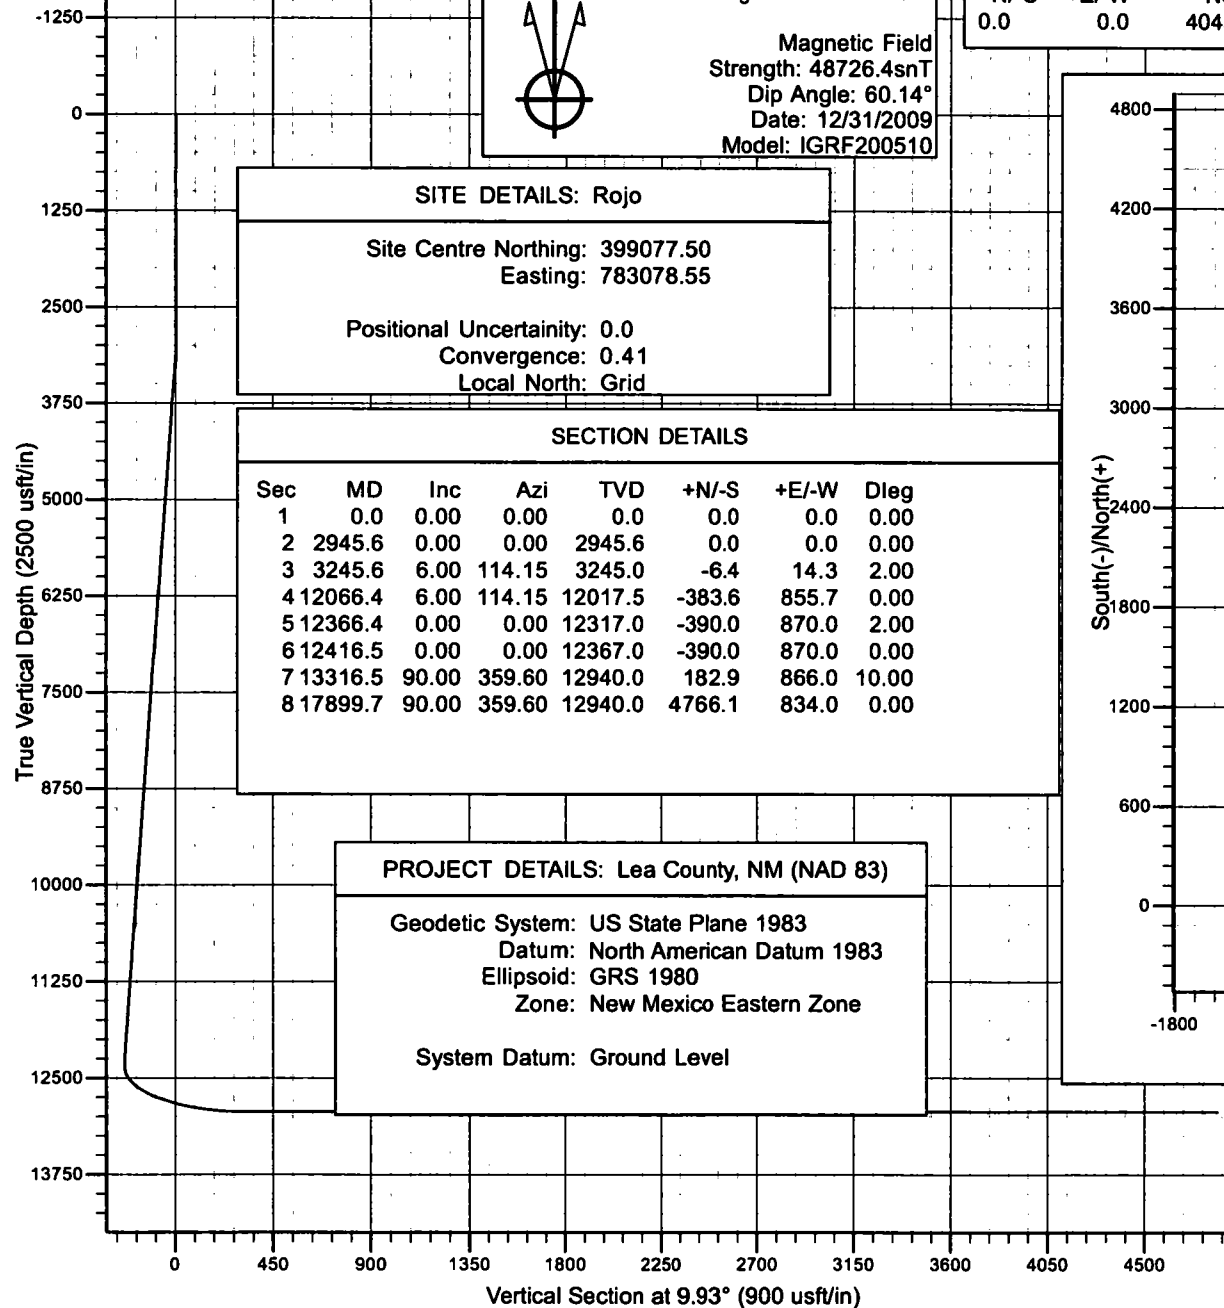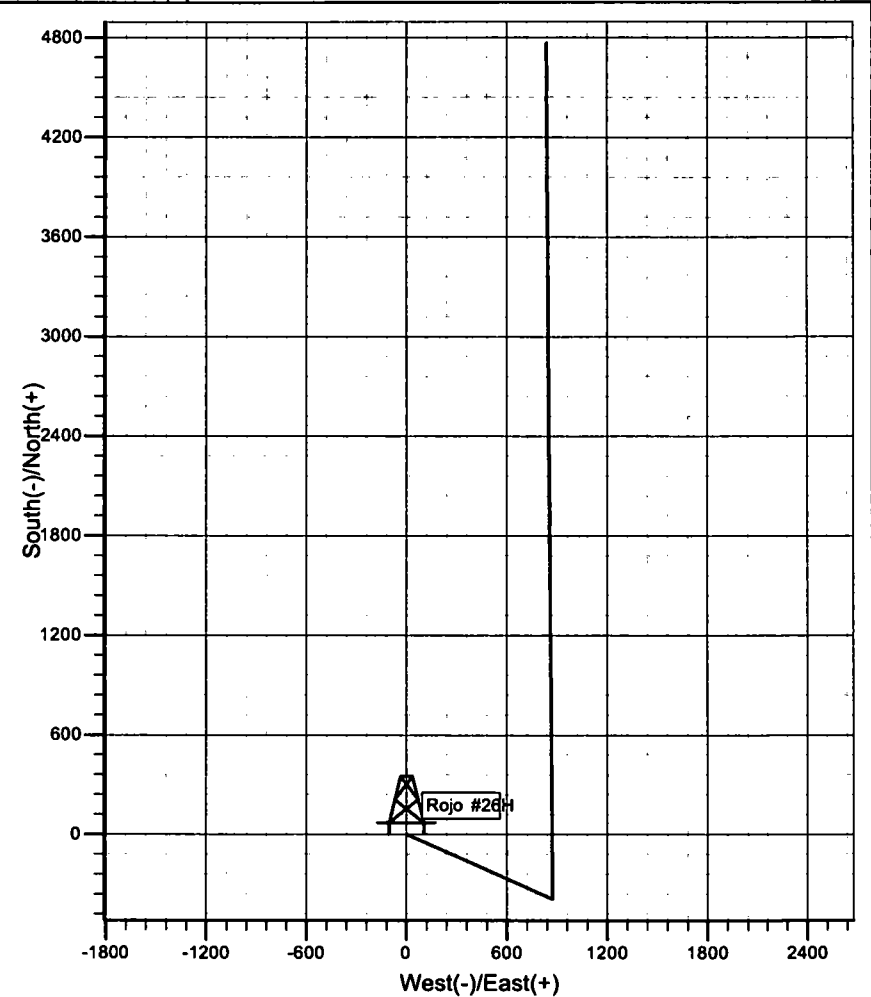

EMERGENCY CALL LIST

| | <u>OFFICE</u> | <u>MOBILE</u> |
|------------------------------|----------------------|----------------------|
| BTA Oil Producers LLC OFFICE | 432-682-3753 | |
| BEN GRIMES, Operations | 432-682-3753 | 432-559-4309 |
| NICK EATON, Drilling | 432-682-3753 | 432-260-7841 |
| TRACE WOHLFAHRT, Completions | 432-682-3753 | |

EMERGENCY RESPONSE NUMBERS

| | <u>OFFICE</u> |
|--|----------------------|
| STATE POLICE | 575-748-9718 |
| EDDY COUNTY SHERIFF | 575-746-2701 |
| EMERGENCY MEDICAL SERVICES (AMBULANCE) | 911 or 575-746-2701 |
| EDDY COUNTY EMERGENCY MANAGEMENT (HARRY BURGESS) | 575-887-9511 |
| STATE EMERGENCY RESPONSE CENTER (SERC) | 575-476-9620 |
| CARLSBAD POLICE DEPARTMENT | 575-885-2111 |
| CARLSBAD FIRE DEPARTMENT | 575-885-3125 |
| NEW MEXICO OIL CONSERVATION DIVISION | 575-748-1283 |
| INDIAN FIRE & SAFETY | 800-530-8693 |
| HALLIBURTON SERVICES | 800-844-8451 |



Multi-Bowl System

13-5/8" x 9-5/8" x 7"

With 4-1/2" liner
downhole

ng head

13-5/8" 10M x 7-1/16" 10M

7-1/16-10M

g spool

8" 5M x 13-5/8" 10M

13-5/8" 10M

13-5/8" x 7" C-22
Csg hanger

1-1/2" VR Plug

13-5/8"-5M

13-5/8" x 9-5/8" MBS
Packoff Assembly

g Head- MBS

13-5/8"-5M x 13-3/8" SOW

13-5/8" x 9-5/8" Mandr
Casing Hanger

13-3/8" SOW






Weatherford[®]

WFT Casing Head (Slip on Weld with O-Ring) Running Procedure

Publication RP-001

October 21, 2010

© 2010 Weatherford International Inc. All rights reserved

| | | | | |
|--|---|--|---|---------------|
|  Weatherford 5-2-GL-GL-WES-00052 | WFT Casing Head (Slip on Weld with O-Ring) Running Procedure | Approved By: | Reviewed By: | RP-001 |
| | |  |  | Rev 0 |
| | | Date: Oct 21, 2010 | Date: Oct 21, 2010 | |

Install the Casing Head



1. Examine the **WFT Casing Head**. Verify the following:
 - bore is clean and free of debris
 - seal areas, threads and ring grooves are clean and undamaged
 - o-ring is properly installed, clean and undamaged
 - all peripheral equipment is intact and undamaged
2. Measure the pocket depth of the Casing Head and record this dimension.
3. Run the surface casing and cement as required.
4. Determine the required elevation of the Casing Head as required by the Drilling Supervisor.
5. Use the following calculation to determine the correct final cut location of the surface casing.

X = Pocket Depth

Y = Overall Casing Head Height

Y - X = Distance from correct elevation point to surface casing cutoff height.

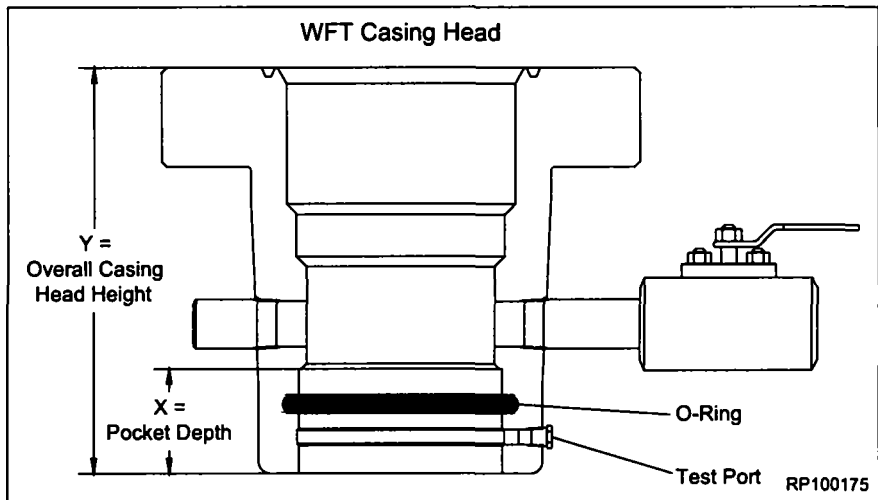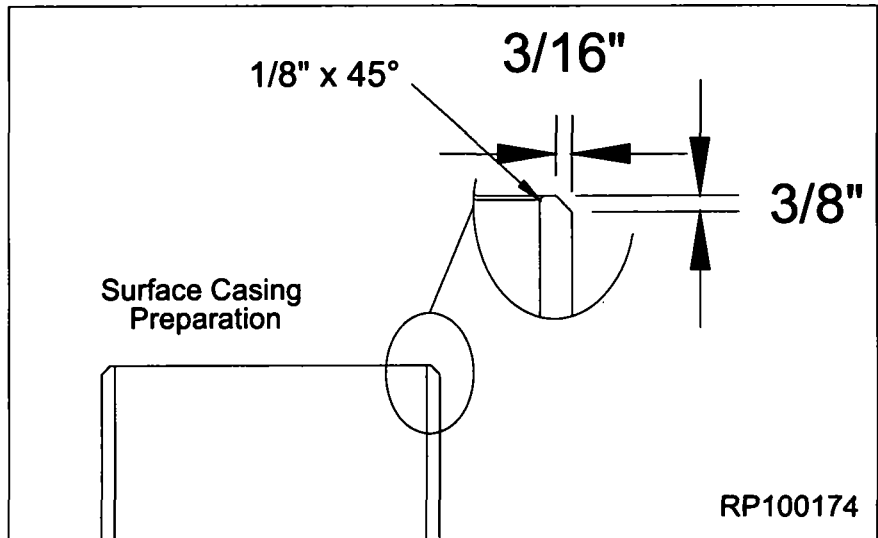


6. Lift the riser assembly high enough to rough cut the surface casing a minimum of 12" above the anticipated final cut location, if applicable.
7. Remove the spent portion of surface casing and the riser assembly and set aside.
8. Determine the correct elevation for the wellhead assembly.
9. Rough cut the surface casing a minimum of 12" above the final cut location.
10. Cut the conductor pipe a comfortable level below the final cut location of the surface casing.



11. Final cut the surface casing at the correct elevation.

NOTE: Ensure the cut on the surface casing is level as this will determine the orientation of the remainder of the wellhead equipment.

12. Bevel the surface casing with a 3/16" x 3/8" bevel and remove any sharp edges from the OD of the casing.
13. Break a 1/8" x 45° bevel on the ID of the surface casing.


| | | | | |
|--|---|--|---|---------------|
|  Weatherford 5-2-GL-GL-WES-00052 | WFT Casing Head (Slip on Weld with O-Ring) Running Procedure | Approved By: | Reviewed By: | RP-001 |
| | |  |  | Rev 0 |
| | | Date: Oct 21, 2010 | Date: Oct 21, 2010 | Page 1 |


Install the Casing Head

14. Wipe the ID of the o-ring of the Casing Head with a light coat of oil or grease.

NOTE: Excessive oil or grease will prevent a positive seal from forming.

15. Lower the Casing Head over the surface casing stub to a positive stop.
16. Remove the fitting from the test port and set aside.
17. Orient the Casing Head as per the Drilling Superintendents instructions ensuring the face of the Casing Head is level and two holed to the drilling rig substructure.
18. Weld and test the surface casing to the Casing Head as per the **RECOMMENDED FIELD WELDING PROCEDURE** located in the back of this manual.
19. Once all welding and testing is completed, replace the fitting into the open port and close the valve on the Casing Head.

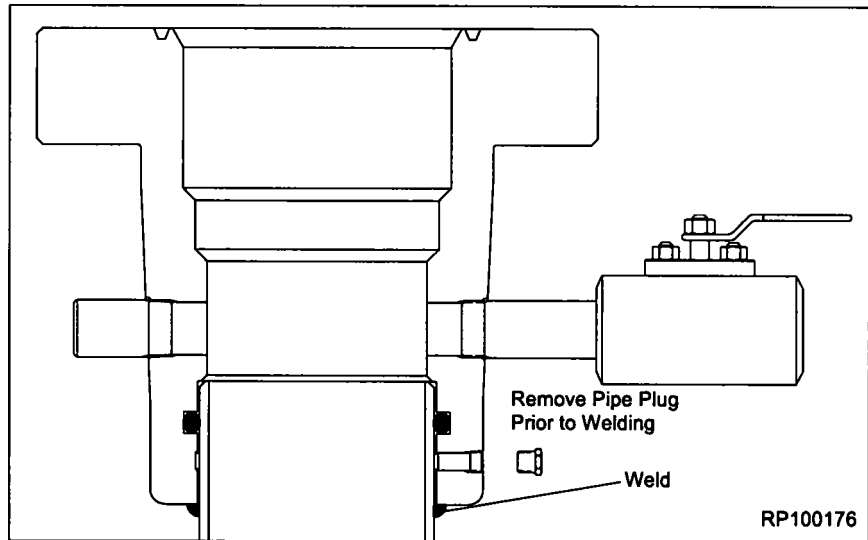

| | | | | |
|--------|-----------------------|-----------------------|--|---|
| RP-001 | Reviewed By: | Approved By: | WFT Casing Head (Slip on Weld with O-Ring) Running Procedure |  Weatherford |
| Rev 0 | <i>Bruce J. Ross</i> | <i>BO</i> | | |
| Page 2 | Date: Oct 21, 2010 | Date: Oct 21, 2010 | | |
| | | | 5-2-GL-GL-WES-00052 | |

Recommended Procedure for Field Welding Pipe to Well-head Parts for Pressure Seal

1. **Introduction and Scope.** The following recommended procedure has been prepared with particular regard to attaining pressure-tight weld when attaching casing heads, flanges, etc., to casing. Although most of the high strength casing used (such as N-80) is not normally considered field weldable, some success may be obtained by using the following or similar procedures.

Caution: In some wellheads, the seal weld is also a structural weld and can be subjected to high tensile stresses. Consideration must therefore be given by competent authority to the mechanical properties of the weld and its heat affected zone.

a. The steels used in wellhead parts and in casing are high strength steels that are susceptible to cracking when welded. It is imperative that the finished weld and adjacent metal be free from cracks. The heat from welding also affects the mechanical properties. This is especially serious if the weld is subjected to service tension stresses.

b. This procedure is offered only as a recommendation. The responsibility for welding lies with the user and results are largely governed by the welder's skill. Weldability of the several makes and grades of casing varies widely, thus placing added responsibility on the welder. Transporting a qualified welder to the job, rather than using a less-skilled man who may be at hand, will, in most cases, prove economical. The responsible operating representative should ascertain the welder's qualifications and, if necessary, assure himself by instruction or demonstration, that the welder is able to perform the work satisfactorily.

2. **Welding Conditions.** Unfavorable welding conditions must be avoided or minimized in every way possible, as even the most skilled welder cannot successfully weld steels that are susceptible to cracking under adverse working conditions, or when the work is rushed. Work above the welder on the drilling floor should be avoided. The weld should be protected from dripping mud, water, and oil and from wind, rain, or other adverse weather conditions. The drilling mud, water, or other fluids must be lowered in the casing and kept at a low level until the weld has properly cooled. It is the responsibility of the user to provide supervision that will assure favorable working conditions, adequate time, and the necessary cooperation of the rig personnel.

3. **Welding.** The welding should be done by the shielded metal-arc or other approved process.




4. **Filler Metal.** Filler Metals. For root pass, it's recommended to use E6010, E6011 (AC), E6019 or equivalent electrodes. The E7018 or E7018-A1 electrodes may also be used for root pass operations but has the tendency to trap slag in tight grooves. The E6010, E6011 and E6019 offer good penetration and weld deposit ductility with relatively high intrinsic hydrogen content. Since the E7018 and E7018-A1 are less susceptible to hydrogen induced cracking, it is recommended for use as the filler metal for completion of the weld groove after the root pass is completed. The E6010, E6011 (AC), E6019, E7018 and E7018-A1 are classified under one of the following codes AWS A5.1 (latest edition): Mild Steel covered electrodes or the AWS A5.5 (latest edition): Low Alloy Steel Covered Arc-Welding Electrodes. The low hydrogen electrodes, E7018 and E7018-A1, should not be exposed to the atmosphere until ready for use. It's recommended that hydrogen electrodes remain in their sealed containers. When a job arises, the container shall be opened and all unused remaining electrodes to be stored in heat electrode storage ovens. Low hydrogen electrodes exposed to the atmosphere, except water, for more than two hours should be dried 1 to 2 hours at 600°F to 700 °F (316°C to 371 °C) just before use. It's recommended for any low hydrogen electrode containing water on the surface should be scrapped.

5. **Preparation of Base Metal.** The area to be welded should be dry and free of any paint, grease/oil and dirt. All rust and heat-treat surface scale shall be ground to bright metal before welding.

6. **Preheating.** Prior to any heating, the wellhead member shall be inspected for the presence of any o-rings or other polymeric seals. If any o-rings or seals are identified then preheating requires close monitoring as noted in paragraph 6a. Before applying preheat, the fluid should be bailed out of the casing to a point several inches (>6" or 150 mm) below the weld joint/location. Preheat both the casing and wellhead member for a minimum distance of three (3) inches on each side of the weld joint using a suitable preheating torch in accordance with the temperatures shown below in a and b. The preheat temperature should be checked by the use of heat sensitive crayons. Special attention must be given to preheating the thick sections of wellhead parts to be welded, to insure uniform heating and expansion with respect to the relatively thin casing.

a. Wellhead members containing o-rings and other polymeric seals have tight limits on the preheat and interpass temperatures. Those temperatures must be controlled at 200°F to 325°F or 93 °C to 160°C and closely monitored to prevent damage to the o-ring or seals.

b. Wellhead members not containing o-rings and other polymeric seals should be maintained at a preheat and interpass temperature of 400°F to 600°F or 200°C to 300°C.

| | | | | |
|--|---|--|---|---------------|
|  Weatherford 5-2-GL-GL-WES-00052 | WFT Casing Head (Slip on Weld with O-Ring) Running Procedure | Approved By: | Reviewed By: | RP-001 |
| | |  |  | Rev 0 |
| | | Date: Oct 21, 2010 | Date: Oct 21, 2010 | Page 3 |

Recommended Procedure for Field Welding Pipe to Well-head Parts for Pressure Seal (continued)

7. **Welding Technique.** Use a 1/8 or 5/32-inch (3.2 or 4.0 mm) E6010 or E7018 electrode and step weld the first bead (root pass); that, weld approximately 2 to 4 inches (50 to 100 mm) and then move diametrically opposite this point and weld 2 to 4 inches (50 to 100 mm) halfway between the first two welds, move diametrically opposite this weld, and so on until the first pass is completed. This second pass should be made with a 5/32-inch (4.0 mm) low hydrogen electrode of the proper strength and may be continuous. The balance of the welding groove may then be filled with continuous passes without back stepping or lacing, using a 3/16-inch (4.8 mm) low hydrogen electrode. All beads should be stringer beads with good penetration. There should be no undercutting and weld shall be workmanlike in appearance.

a. Test ports should be open when welding is performed to prevent pressure buildup within the test cavity.

b. During welding the temperature of the base metal on either side of the weld should be maintained at 200 to 300°F (93 to 149°C).

c. Care should be taken to insure that the welding cable is properly grounded to the casing, but ground wire should not be welded to the casing or the wellhead. Ground wire should be firmly clamped to the casing, the wellhead, or fixed in position between pipe slips. Bad contact may cause sparking, with resultant hard spots beneath which incipient cracks may develop. The welding cable should not be grounded to the steel derrick, nor to the rotary-table base.

8. **Cleaning.** All slag or flux remaining on any welding bead should be removed before laying the next bead. This also applies to the completed weld.

9. **Defects.** Any cracks or blow holes that appear on any bead should be removed to sound metal by chipping or grinding before depositing the next bead.

10. **Postheating.** Post-heating should be performed at the temperatures shown below and held at that temperature for no less than one hour followed by a slow cooling. The post-heating temperature should be in accordance with the following paragraphs.


a. Wellhead members containing o-rings and other polymeric seals have tight limits on the post-heating temperatures. Those temperatures must be controlled at 250°F to 300°F or 120 °C to 150°C and closely monitored to prevent damage to the o-ring or seals.

b. Wellhead members not containing o-rings and other polymeric seals should be post-heated at a temperature of 400°F to 600°F or 200°C to 300°C.

11. **Cooling.** Rapid cooling must be avoided. To assure slow cooling, welds should be protected from extreme weather conditions (cold, rain, high winds, etc.) by the use of suitable insulating material. (Specially designed insulating blankets are available at many welding supply stores.) Particular attention should be given to maintaining uniform cooling of the thick sections of the wellhead parts and the relatively thin casing, as the relatively thin casing will pull away from the head or hanger if allowed to cool more rapidly. The welds should cool in air to less than 200°F (93°C) (measured with a heat sensitive crayon) prior to permitting the mud to rise in the casing.

12. **Test the Weld.** After cooling, test the weld. The weld must be cool otherwise the test media will crack the weld. The test pressure should be no more than 80% of the casing collapse pressure.

| Test Media | |
|---|--|
| Acceptable Medias | Unacceptable Medias |
| Water Water Soluable Oil Inert Gas •Nitrogen •Argon Gas | Oxygen Acetylene Hydraulic Oil Motor Oil Brake Fluid |

| | | | | |
|---------------|-----------------------|-----------------------|---|--|
| RP-001 | Reviewed By: | Approved By: | WFT Casing Head (Slip on Weld with O-Ring) Running Procedure |  Weatherford 5-2-GL-GL-WES-00052 |
| Rev 0 | <i>Bruce J. Ross</i> | <i>BO</i> | | |
| Page 4 | Date: Oct 21, 2010 | Date: Oct 21, 2010 | | |



Weatherford®




Wellhead Field Service Manual

WFT-SB Wellhead System Running Procedure

Publication: SM-11-1

Release Date: December 2014

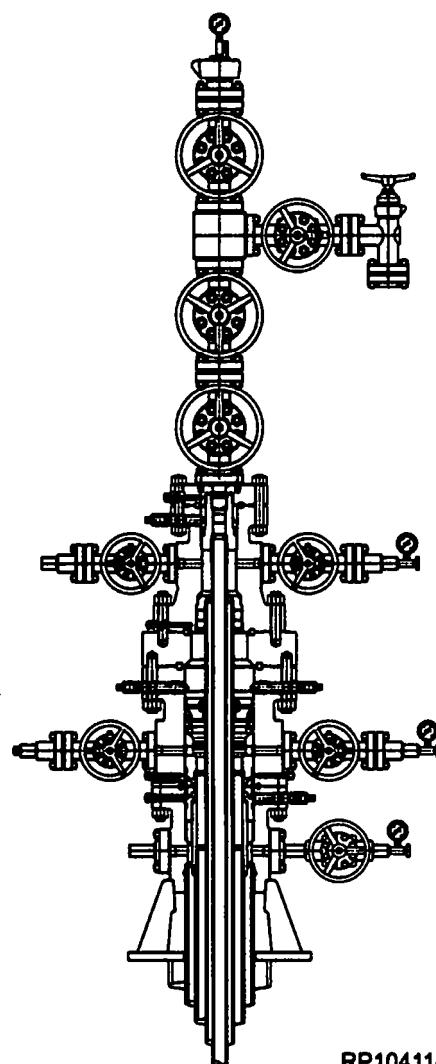

RP104114

©2014 Weatherford International Ltd. All Rights Reserved




| | | | | | |
|--|---------------------------------|-------------------------|-------------------|------------------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-11-1 |
| | | <i>Marion Robertson</i> | <i>Bruce Ross</i> | <i>Manuel Zaragoza</i> | Rev WIP |
| | | Marion Robertson | Bruce Ross | Manuel Zaragoza | Page 1 of 24 |
| | | Dec 2014 | Dec 2014 | Dec 2014 | |

Table of Content


WFT-Split Bowl (SB) Wellhead System

| | |
|--|----|
| Wellhead System Assembly Drawing | 3 |
| Running Procedure | |
| Casing Head/Spool Assembly Rig-Up and Installation | 4 |
| Testing the BOP | 5 |
| Running and Retrieving the Long Bowl Protector..... | 3 |
| Running the Bowl Protector Prior to Drilling | 6 |
| Retrieving the Bowl Protector After Drilling | 7 |
| Hanging Off the Intermediate Casing..... | 7 |
| Hanging Off the Intermediate Casing- Contingency Completion..... | 9 |
| Installation of the Pack-Off Bushing and Energizing the Seals | 10 |
| Installation | 10 |
| Energizing the Seal | 12 |
| Retesting the BOP Stack..... | 14 |
| Running and Retrieving the Short Bowl Protector | 15 |
| Running Short Bowl Protector | 15 |
| Retrieving the Short Bowl Protector | 16 |
| Running the Production Casing | 16 |
| Installation of the Slip-Type Casing Hanger Under the BOP Stack | 16 |
| Installation of the Slip-Type Casing Hanger Through the BOP Stack..... | 17 |
| Hanging Off the Production Casing | 18 |
| Installation and Testing the Tubing Spool Assembly | 20 |
| Installation | 20 |
| Testing the Secondary Seal and Flange Connection | 20 |
| Testing the BOP | 21 |
| Hanging Off the Production Tubing String..... | 22 |
| Installing and Testing of the Production Tree..... | 23 |
| Installation | 23 |
| Testing | 24 |

| | | | | | |
|--|----------------------------------|---|--------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Services Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 2 of 24 |
| | | Dec 2014 | Dec 2014 | Dec 2014 | |

WFT Split Bowl (SB) Wellhead System

WFT-SB Split Multi-Bowl/ Conventional Wellhead System

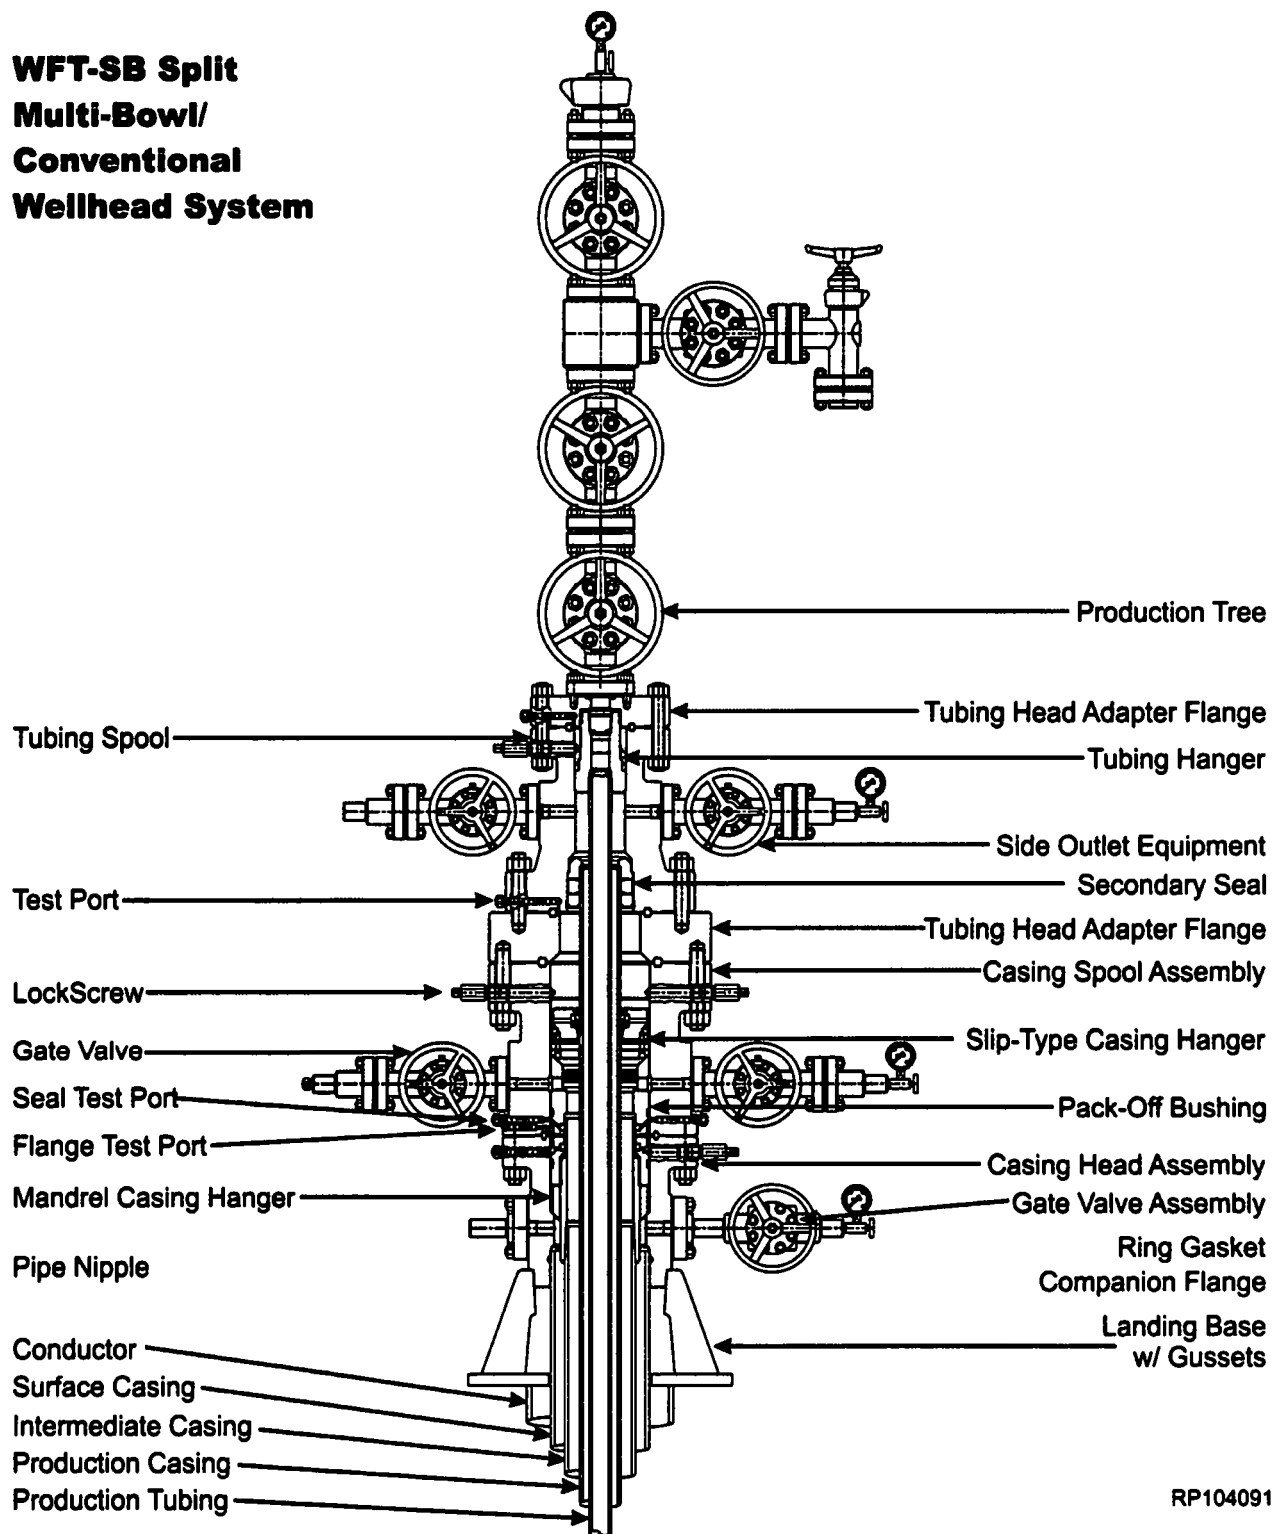

RP104091



Weatherford

5-3-GL-GL-WES-00XXX

Field Service Manual

Prepared By:

Marion Robertson

Marion Robertson

December 2014

Reviewed By:

Brad Franks

Brad Franks

December 2014

Approved By:

Manual Zaragoza

Manual Zaragoza

December 2014

SM-13-1

Rev WIP

Page 3 of 24

WFT Split Bowl (SB) Multi-Bowl/Conventional Wellhead System (Continued)

WFT-SB Casing Head/Spool Assembly Rig Up and Installation


1. Determine the correct elevation for the wellhead system, and cut the conductor pipe at a comfortable elevation, below the surface casing final cut.

NOTE

Ensure that the cut on the conductor is level, as this will determine the orientation of all remaining wellhead equipment.

2. Remove any excess conductor pipe and set aside.
3. Grind the conductor pipe and remove any sharp edges, ensuring that the conductor pipe cut is level.
4. Run the surface casing to the required depth and cement casing in place. Allow the cement to set.
5. Lift the blow-out preventer (BOP) or diverter and prepare to cut off the surface casing at a sufficient height above the cellar deck to facilitate the installation of the WFT-SB Casing Head/Spool Assembly with Base Plate.
6. Once the surface casing is released from the rig floor, cut it approximately 12 inches (or more) above the final cut location.
7. Remove the excess surface casing, and the BOP or diverter, and set aside.
8. Bevel the surface casing outer diameter (3/16" x 3/8") and inner diameter (1/8" x 45 degrees). Remove any sharp edges.

9. Examine the Casing Head with Slip-On Weld (SOW) bottom prep. Verify the following:
 - O-ring seal, bore, ports and exposed ring grooves are clean and in good condition.
 - Test fittings, studs and nuts, valves, flanges and bull plugs are intact and in good condition.

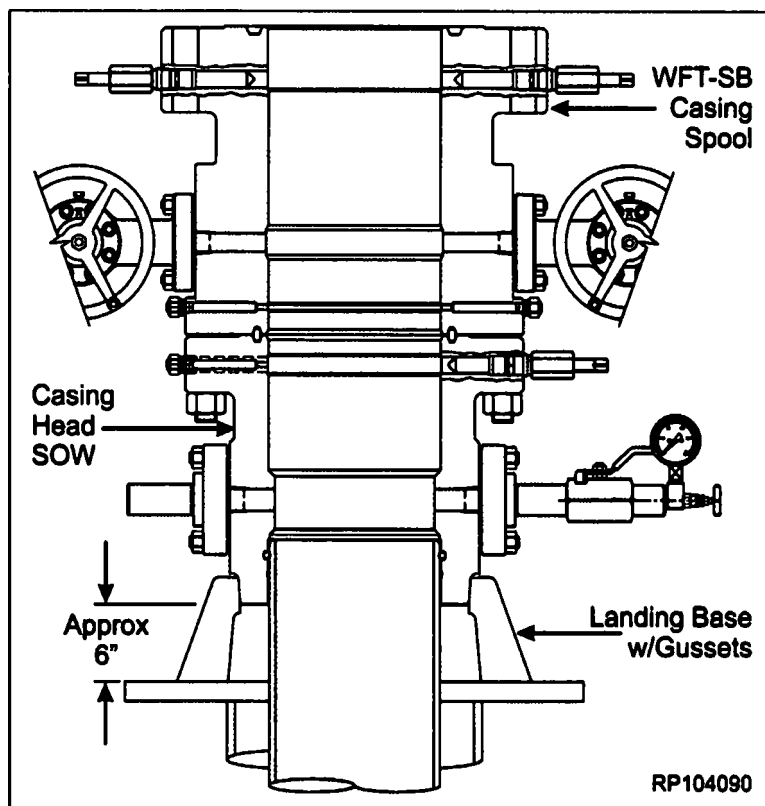



10. Determine the correct elevation for the wellhead assembly. Measure depth of the surface casing socket in SOW with O-ring bottom prep.
11. Lightly lubricate the casing stub with an oil or light grease.

▲WARNING▲

Excessive oil or grease will prevent a positive seal from forming.

12. Align and level the WFT-SB Casing Head/Spool Assembly over the casing stub, orienting the outlets to drilling equipment, per the drilling supervisor's direction.

| | | | | | |
|--|---------------------------------|---|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 4 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

14. Slowly and carefully lower the assembly over the casing stub until the stub bottoms in the casing socket.
15. Remove the test fitting from the casing head test port, and set aside.
16. Ensure that the WFT-SB Casing Head/Spool Assembly is plumb and level.
17. Weld and test the surface casing using the recommended welding procedure located in the Appendices Section of this manual.

Testing the BOP Stack

1. Examine the Test Plug/Running & Retrieval Tool. Verify the following:
 - Elastomer seals, threads and plugs are intact and in good condition.
 - Drill pipe threads are correct size, clean and in good condition.
2. Install a new, appropriately sized ring gasket in the ring groove of the WFT-SB Spool and make up the BOP stack.

NOTE

Immediately after make-up of the BOP stack and periodically during drilling of hole for the casing string, the BOP stack (flanged connections and rams) must be tested.

3. Orient the test plug with elastomer down/ACME threads up, and make up a joint of drill pipe to the test plug.


NOTE


If pressure is to be supplied through the drill pipe, remove the pipe plug from the weep port.

CAUTION

Ensure that the test plug elastomer is down and Acme threads are up when testing.

4. Fully retract all lockscrews in the entire WFT-SB casing head/spool assembly.
5. Lubricate the test plug elastomer seal with a light oil or grease.
6. Lower the test plug through the BOP stack into the WFT-SB assembly, until it lands on the casing head load shoulder.

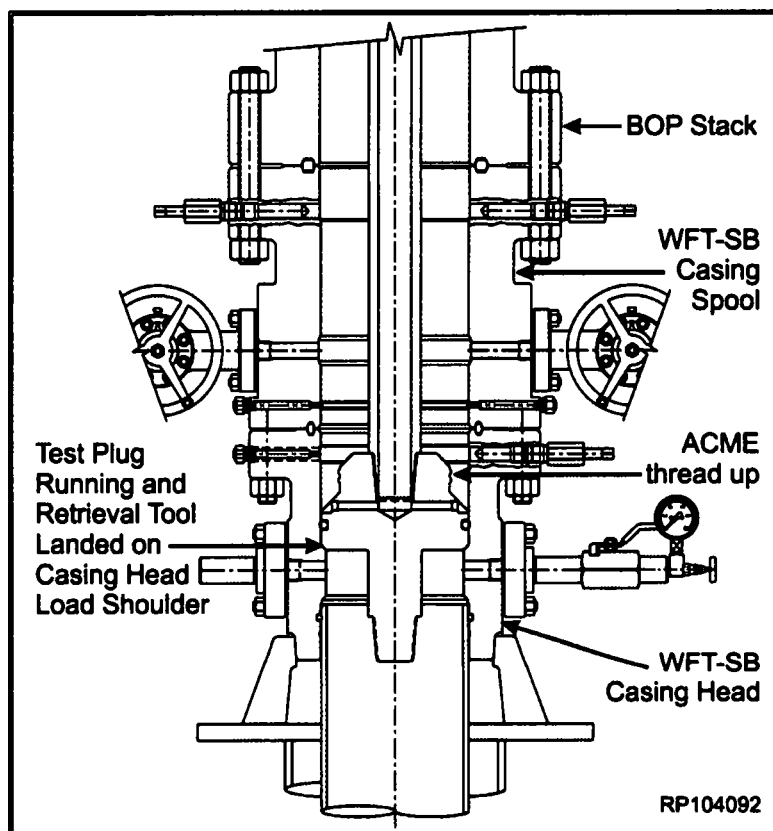

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 5 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

- Open lower casing head side outlet valve. Monitor any leakage past the test plug seal.
- Close the BOP rams on the drill pipe, and test to **5,000 psi or as required by the drilling supervisor**.
- After a satisfactory test is achieved, release pressure and open the rams.
- Remove as much fluid from the BOP stack as possible.
- Retrieve the test plug assembly slowly to avoid damage to the seal.
- Close all outlet valves on WFT-SB Casing Head/Spool Assembly.
- Repeat Steps 1 thru 12, as required during drilling of the hole.
- Examine the Bowl Protector Running/Retrieval Tool. Verify the following:
 - Threads are clean, undamaged and free of debris
 - Ports are clean and unobstructed.
 - Drill Pipe threads are correct size, clean and in good condition.
- Orient the Bowl Protector Running Tool with Acme threads down.

▲ CAUTION ▲

Ensure that the left hand (LH) Acme threads are down prior to engaging Bowl Protector Running Tool into Long Bowl Protector.


Running and Retrieval of the Long Bowl Protector


NOTE

Always use a bowl protector while drilling to protect wellhead load shoulders from damage by drill bit or rotating drill pipe. The bowl protector must be retrieved prior to running the casing string.

Running in the Bowl Protector prior to Drilling

- Examine the Long Bowl Protector. Verify the following:
 - Bore drift is correct size, clean, in good condition, and free of debris
 - Threads are clean and undamaged
 - O-ring seals are properly installed, clean, and undamaged.

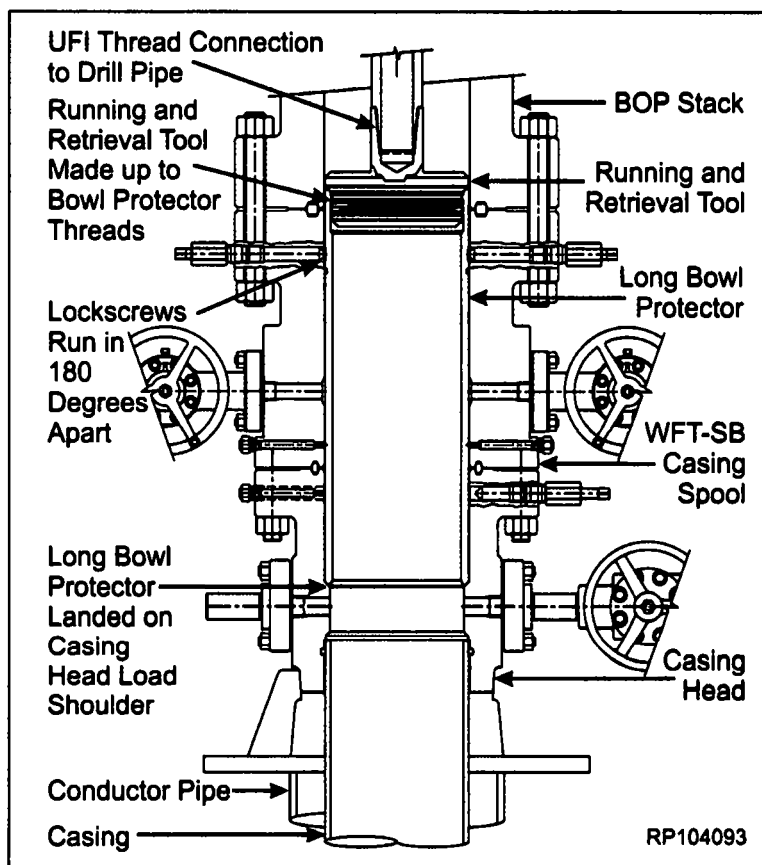

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 6 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

4. Make-up a drill pipe joint to the Running Tool.
5. Thread Running Tool into the Long Bowl Protector, rotating two turns counterclockwise.
6. Verify that all lockscrews in the WFT-SB Casing Head/Spool Assembly are fully retracted.
7. Slowly lower the Running Tool/Bowl Protector Assembly through the BOP stack and into the WFT-SB Casing Head/Spool Assembly, until it lands securely on the casing head load shoulder.
8. On WFT-SB Casing Spool, run in two Lockscrews ("snug" tight **ONLY**), 180 degrees apart, to hold Bowl Protector in place.

▲WARNING▲

Do NOT over tighten the lockscrews, as this will cause damage to the Bowl Protector and the lockscrews.

9. Remove the running tool from the bowl protector, by rotating the drill pipe clockwise two turns while lifting straight up.
10. Drill out and prepare to run the casing string per the drilling supervisor's instruction.

Retrieving the Bowl Protector after Drilling

1. Make-up the retrieval tool to the drill pipe, with Acme threads down.
2. Slowly lower the retrieval tool through the BOP Stack into the Bowl Protector.
3. Rotate the retrieval Tool counterclockwise, two turns, to engage with bowl protector Acme threads.

4. Fully retract both lockscrews on the WFT-SB casing spool, and retrieve the bowl protector.

NOTE

Ensure that all lockscrews in both the upper flange (casing spool) and lower flange (casing head) of the wellhead Assembly are fully retracted from well bore.

5. Remove the bowl protector and the running and retrieval tool from the drill floor.

Hanging off the Intermediate Casing

1. Run the intermediate casing as required and space out appropriately for the mandrel casing hanger.



NOTE

If the intermediate casing becomes stuck and the mandrel casing hanger cannot be landed, refer to STAGE 4B.

2. Examine the WFT-SBD-SN Mandrel Casing Hanger. Verify the following:
 - Bore drift is correct size, clean and free of debris
 - All threads are clean and undamaged.
 - Flow-By flutes are clear and unobstructed.
 - Slick Neck seal area is clean and undamaged.
3. Examine the Mandrel Casing Hanger Running Tool. Verify the following:
 - Threads are clean and in good condition.
 - O-ring seals are clean and undamaged.
4. Thread the mandrel hanger onto the last joint of casing to be run. Torque the connection thread to manufacturer's optimum "make-up" torque value.
5. Make up a landing joint to the top of the running tool. Torque the connection to thread manufacturer's maximum "make-up" torque valve.

▲CAUTION▲

If Steps 4 and 5 were performed prior to being shipped to location, the hanger running tool should be backed off and made back up to ensure it will back off freely.

| | | | | | |
|--|-----------------------------|---|------------------------------|----------------------------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson December 2014 | Brad Franks December 2014 | Manual Zaragoza December 2014 | Page 7 of 24 |

WFT Split Bowl (SB) Wellhead System (Continued)

6. Liberally lubricate the outer diameter of the hanger neck and inner diameter of the running tool O-ring seals with a light oil or grease.

▲WARNING▲

Do NOT use pipe dope or other metal based compounds. This will cause galling.


7. Maintaining a neutral weight, rotate the hanger running tool with chain tongs, first clockwise until a thread "jump" can be felt, then counterclockwise, approximately eight turns, to a positive stop, and then back off (clockwise) one quarter (1/4) turn.


▲CAUTION▲

Do NOT torque the running tool to the casing hanger connection. Do NOT back off more than one quarter (1/4) turn.

8. Remove the flush fitting hex head pipe plug from the outer diameter of the running tool and attach a test pump.
9. Apply hydraulic test pressure to **5,000 psi** and hold for **15 minutes** or as required by the drilling supervisor.
10. Upon completion of a successful test, bleed off test pressure through the test pump and remove the pump. Replace the pipe plug.
11. Locate indicator groove machined in outer diameter of Running Tool, coat with white paint.

12. Verify that all lockscrews in the WFT-SB casing head/casing spool assembly are fully retracted.
13. Slowly and carefully lower the mandrel hanger through the BOP stack, and land the hanger onto the casing head load shoulder.
14. Slack off weight on the casing.
15. Check that the well is stable and no pressure buildup or mud flow is occurring.

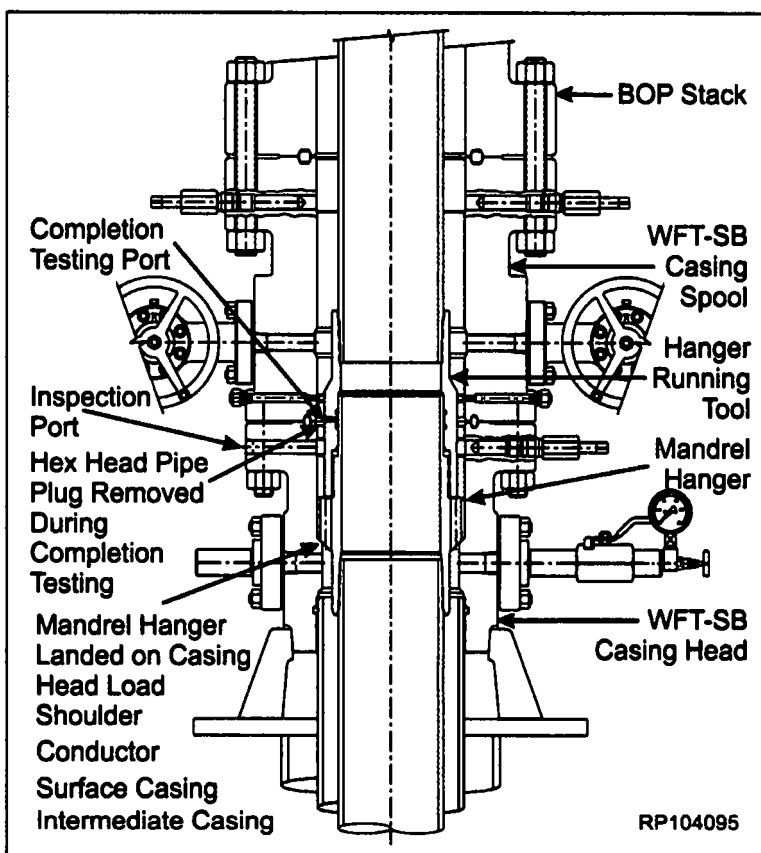

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 8 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

16. Drain the BOP stack through the casing head side outlet valves.
17. Remove the pipe plug from the casing head flange port marked "Inspection Port."
18. Visually verify that the running tool groove is in the center of the inspection port, and that the mandrel hanger has landed properly.
19. Reinstall the pipe plug and tighten securely.
20. Place a paint mark on the landing joint level with the rig floor, and cement casing as required.

NOTE

If the casing is to be reciprocated during cementing, it is advisable to pick up the mandrel hanger a minimum of eight feet above the landing point. Place a mark on the landing joint, level with the rig floor, and then reciprocate above that point. If at any time resistance is felt, land the mandrel casing hanger immediately.



21. Retrieve the hanger running tool and landing joint by rotating landing joint clockwise (to the right), fourteen full turns.

Hanging off Intermediate Casing – Contingency Completion

NOTE

The following procedure should **ONLY** be followed if the intermediate casing should become stuck in the hole. If the casing did **NOT** get stuck and is successfully hung off with the mandrel casing hanger, skip this stage.

1. Cement the intermediate casing in accordance with the program, taking returns through the flow-by flutes of the mandrel casing hanger as required.
2. Drain the casing head bowl through the side outlet.
3. Separate the WFT-SB casing spool from the casing head.
4. Pull up on WFT-SB casing spool and suspend it above casing head, high enough to install a WFT-21 Slip Type Casing Hanger.
5. Wash out as required.
6. Examine the WFT-21 slip type casing hanger. Verify the following:
 - Hanger is correct size, clean and undamaged.
 - Slip segments are sharp and in proper position.
 - All screws are in place.
7. Remove the latch screw to open the slip type hanger.
8. Place two boards on the casing head flange, against the casing, to support the hanger.
9. Wrap the hanger around the casing and replace the latch screw.
10. Prepare to lower the hanger into the casing head bowl.
11. Grease the WFT-21 slip type casing hanger body and remove the slip retaining cap screws.
12. Remove the boards and allow the hanger to slide down into the casing head.

| | | | | | |
|--|-----------------------------|---|------------------------------|----------------------------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson December 2014 | Brad Franks December 2014 | Manual Zaragoza December 2014 | Page 9 of 24 |

WFT Split Bowl (SB) Wellhead System (Continued)

13. Once the hanger has landed securely on the casing head bowl load shoulder, pull tension on the casing to the desired hanging weight, and then slack off.

NOTE

A sharp decrease on weight indicator will signify that the hanger has taken weight. If this does not occur, pull tension again and slack once more.

14. Rough cut the casing approximately eight inches, or more, above the top of the casing head flange. Remove the excess casing.
15. Final cut the casing at $2\frac{1}{2}'' \pm 1/8''$ above casing head flange.
16. Bevel the casing outer diameter ($1/4'' \times 30$ degrees) and inner diameter ($1/8'' \times 30$ degrees).
17. Remove and discard the used gasket ring from the casing head.
18. Clean the mating ring grooves on the WFT-SB casing spool and casing head. Lightly wipe with oil or grease.


▲WARNING▲

Excessive oil or grease will prevent a positive seal from forming.

19. Install a new appropriately sized ring gasket into the casing head groove.
20. Loosely reconnect or make up the WFT-SB casing spool to the casing head.

NOTE

The casing spool to casing head connection will be fully tightened after the pack-off bushing is run and proper setting is verified.

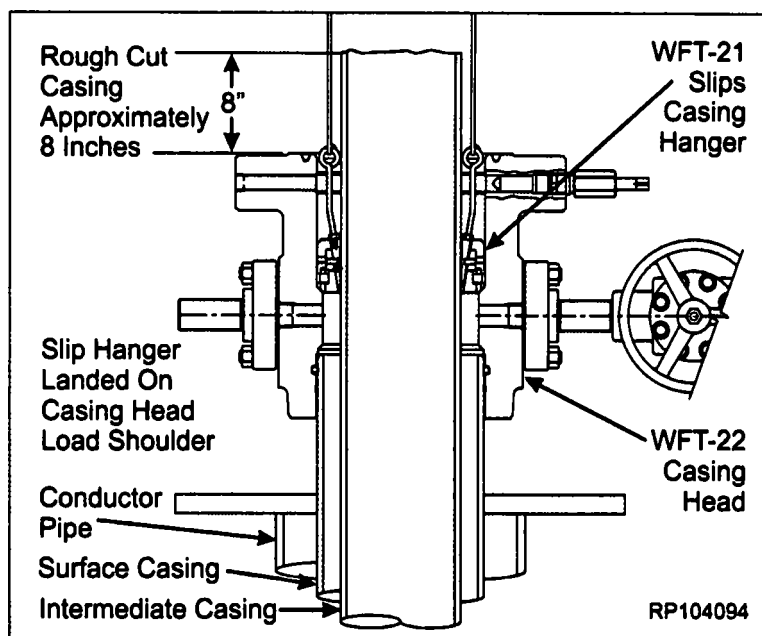



Installation of the Pack-Off Bushing and Energizing the P-Seals

WFT-SB Pack-Off Bushing Installation

NOTE

Installation procedure is identical for both Standard and Emergency WFT-SB Pack-Off Bushings.

- Determine which pack-off bushing to use:
 - If casing has been run normally and is hung off with a mandrel casing hanger, use a standard packoff bushing.
- Examine the appropriate pack-off bushing. Verify the following:
 - All elastomer seals are in place and undamaged.
 - Bore, ports and alignment lugs are clean and in good condition.
 - Coat the lockscrew relief groove with white paint.
- Liberalily lubricate the inner diameter of the double P-seal grooves and outer diameter of dovetail seals with a light oil or grease.

| | | | | | |
|--|-----------------------------|---|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 10 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

4. Examine the pack-off bushing running tool. Verify the following:
 - All elastomer seals are properly installed, clean and undamaged
 - Threads are clean, undamaged and free of debris
 - Bore and ports are clean and unobstructed.
5. Make-up a landing joint to the running tool and rack back assembly.
6. Run two or three stands of heavy weight drill pipe or collars in the hole and set floor slips.

NOTE


Use heavy weight drill pipe or drill collars. Weight required to push Pack-Off Bushing into Casing Head, over Mandrel Hanger slick neck, is approximately 14,000 lbs.

▲WARNING▲


When lowering the drill pipe into the well, extreme caution must be taken to not damage the top of the mandrel hanger with the end of the drill pipe. It is recommended that the drill pipe be centralized to the hanger inner diameter, as closely as possible, when entering the hanger.

7. Carefully lower the bushing over the drill pipe and set it on top of floor slips.
8. Make up the landing joint/running tool assembly to the drill pipe suspended in floor slips.
9. Carefully pick up the pack-off bushing, thread the bushing into the running tool, then rotate the bushing approximately two turns counterclockwise (to the left), coming to a positive stop.

10. Lower the assembly through the BOP Stack and the WFT-SB spool assembly until the pack-off bushing lands on the casing hanger.

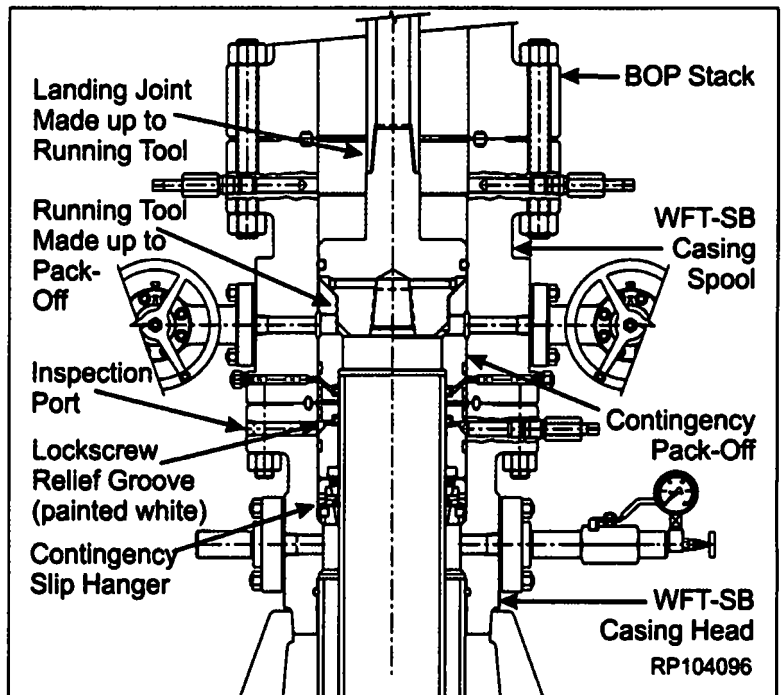

11. Verify, through inspection port that the pack-off bushing has landed properly after:
 - ensuring well is stable and no pressure buildup or mud flow is occurring.
 - drain BOP Stack through Casing Head side outlet valves.
 - remove Pipe Plug (1"-NPT) from Casing Head flange port marked "Inspection Port".
 - Check, to ensure, bottom of Lockscrew relief groove (painted white) on Support Bushing is at bottom of inspection port.
 - Reinstall Pipe Plug and tighten securely.
12. Fully run in all Casing Head Lockscrews (lower flange), in an alternating cross pattern.
13. Using two chain tongs, 180° apart, rotate Landing Joint/Running Tool approximately 2 turns clockwise (to the

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 11 of 24 |
| | | December 2014 | December 2014 | December 2014 | |


right), coming to a stop and carefully lift tool to Drill Floor, set aside.

NOTE

If the Contingency Pack-Off Bushing is being installed, it is now necessary to make up the Speed Head Casing Head/Casing Spool connection. Tighten all studs in an alternating cross pattern until the flange bolting is fully made up.

Energizing the P-Seals


1. Locate the two lower injection fittings ("INJ"), located 180 degrees apart on the casing head. Remove the dust cap from one fitting and remove the second fitting entirely.
2. Attach a bleeder tool to the injection fitting without the dust cap, in the casing head. Open the bleeder tool.
3. Attach a plastic injection tool to the open port and inject plastic packing into the port until a continuous stream flows from the bleeder tool. Close the bleeder tool.
4. Remove the injection tool. Reinstall the injection fitting into the open port and remove the dust cap. Reattach the injection tool.
5. Continue injecting plastic packing to **5,000 psi. or to 80% of casing collapse pressure, whichever is less.**

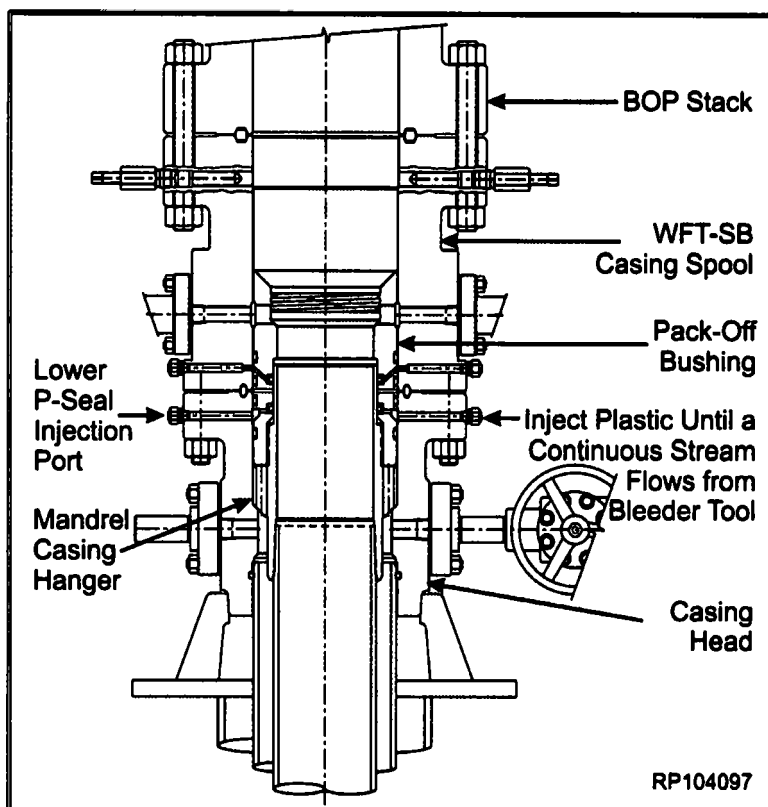

NOTE

The strength of a mandrel casing hanger slick neck is equivalent to P110 Grade casing with the same weight as run in the casing string.

6. Hold and monitor pressure for 15 minutes or as required by the drilling supervisor.
7. If pressure drops, the plastic packing has not filled the seal area completely. Open the bleeder tool, bleed off the pressure and repeat Steps 5 and 6, until pressure is stabilized.
8. Remove the plastic injection tool and bleeder tool. Reinstall the dust caps on both injection fittings.
9. Repeat Steps 1 thru 8 to pack off and energize the upper P-Seal.

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 12 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

10. Locate the "SEAL TEST" fitting, slightly below and 90 degrees from the injection fittings. Remove the dust cap from this fitting.
11. Attach a test pump to the fitting.
12. Pump clean test fluid between the P-Seals until a test pressure of 5,000 psi or 80% of casing collapse pressure is attained, whichever is lower.

▲WARNING▲

Do NOT exceed 80% of casing collapse pressure when a slip type casing hanger and contingency pack-off bushing are utilized.

13. Hold test pressure for 15 minutes or as required by the drilling supervisor.
14. If pressure drops, a leak has developed. Take the appropriate action per the following table:


| Leak Location | Cause | Action |
|----------------------------------|----------------------|--|
| Into the bore of the casing head | Upper P-seal leaking | Bleed off pressure and re-inject plastic packing into leaking upper P-seal port. |
| Around the casing | Lower P-Seal leaking | Bleed off pressure and re-inject plastic packing into lower P-seal port. |

15. Repeat Steps 12 thru 14 until a satisfactory test is achieved.
16. Once a satisfactory test is achieved, carefully bleed off pressure and remove Test Pump.
17. Attach the bleeder tool to the test port fitting and open the tool to vent any remaining trapped pressure.


▲CAUTION▲

Always direct the bleeder tool port away from people and property.

18. Remove the bleeder tool and reinstall dust cap in Test Port Fitting.

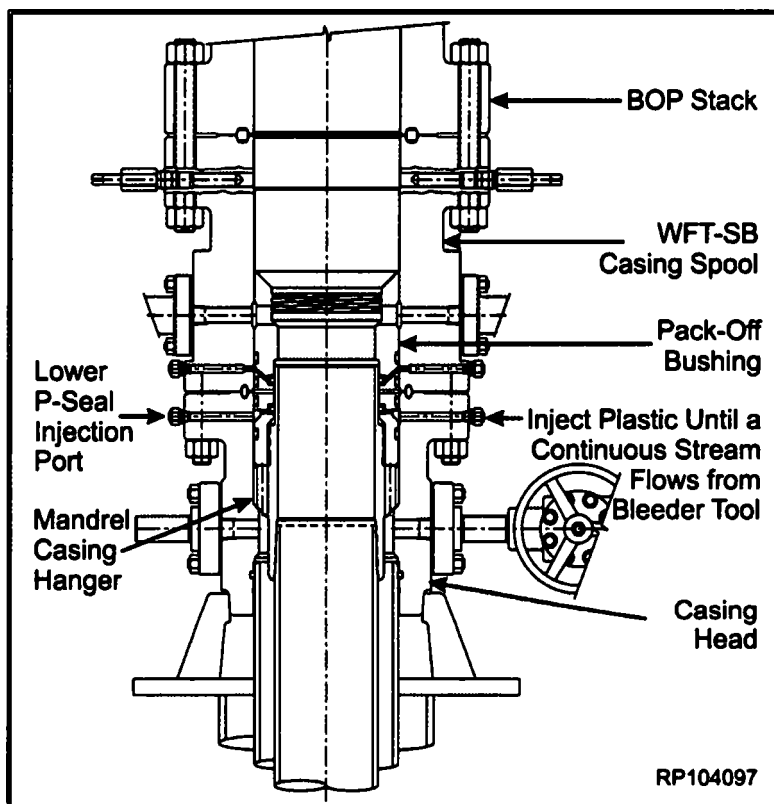

RP104097

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 13 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

Retesting the BOP Stack

1. Examine the Test Plug/Running Tool.
Verify the following:

- Elastomer seals are intact and in good condition.
- Drill pipe threads are clean and in good condition.

NOTE

Immediately after testing the support bushing seals and periodically during conditioning of the hole prior to running tubing, the BOP stack (flanged connections and rams) must be tested.

2. Orient the test plug with elastomer down/ACME threads up. Make up a joint of drill pipe to the test plug.

NOTE

Remove the pipe plug from the weep port if pressure is to be supplied through the drill pipe.

CAUTION


Make sure the elastomer is down and ACME threads are up when testing.

3. Fully retract all lockscrews in the upper WFT-SB Spool Assembly.

WARNING



Do NOT retract the lockscrews located in the casing head (lower flange). Doing so could allow the pack-off support bushing to rise out of position.

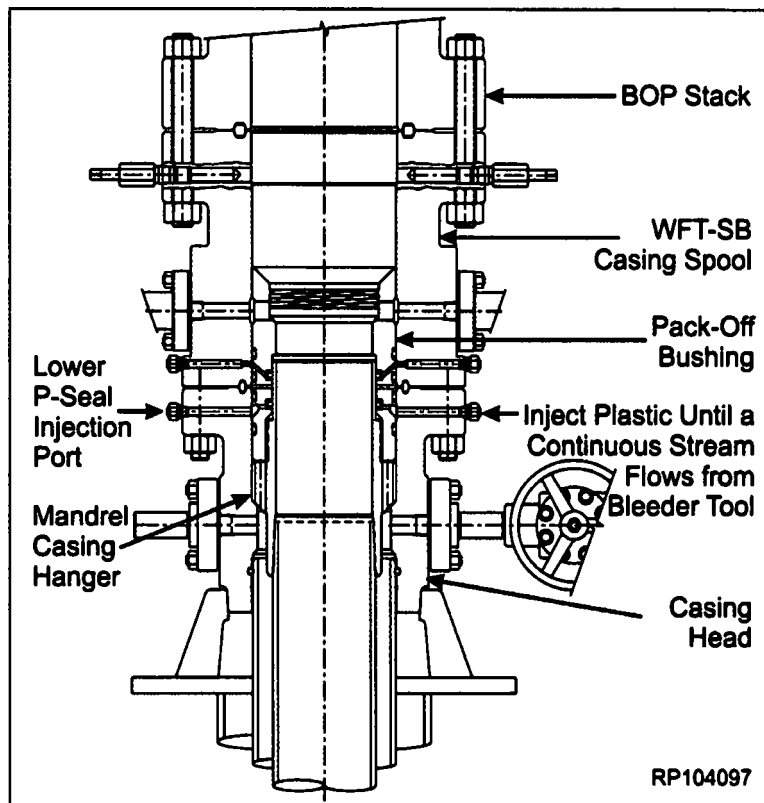4. Lubricate the test plug elastomer seal with light oil or grease.



RP104097

5. Lower the test plug through the BOP stack into the WFT-SB spool assembly until it lands on top of the pack-off bushing.
6. Open the upper WFT-SB casing spool side outlet valves. Monitor for any leakage past the test plug seal.
7. Close the BOP rams on the drill pipe and test to **10,000 psi or as required by the drilling supervisor**.
8. After a satisfactory test is achieved, release all pressure and open the rams.
9. Remove as much fluid from the BOP stack as possible.
10. Retrieve the test plug assembly slowly to avoid damage to the seal.
11. Close all outlet valves on the WFT-SB casing head/spool assembly.

| | | | | | |
|--|-----------------------------|---|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 14 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

Running and Retrieving the Short Bowl Protector

NOTE

Always use a bowl protector while drilling to protect the wellhead load shoulders from damage by the drill bit or rotating drill pipe. The bowl protector must be retrieved prior to running the casing string!

Running the Bowl Protector Prior to Drilling

1. Examine the short bowl protector.
Verify the following:
 - Bore drift is correct size, is clean, in good condition, and free of debris.
 - Threads are correct size and type.
 - Threads are clean and in good condition.
2. Orient the bowl protector running tool with ACME threads down.

NOTE

The running tool is the same tool used for handling the long bowl protector.

CAUTION

Make sure that the left hand (LH) ACME threads are down prior to engaging the bowl protector running tool into the short bowl protector.

3. Make-up a drill pipe joint to the running tool.
4. Thread the running tool into the short bowl protector, rotating two turns counterclockwise (to the left).
5. Verify that all upper lockscrews in the WFT-SB spool assembly are fully retracted. Slowly lower the running

tool/bowl protector assembly through the BOP stack into the WFT-SB spool assembly until it lands on top of the pack-off bushing.

WARNING


Do NOT retract the lower lockscrews located in the WFT-SB casing head, as this could allow the pack-off bushing to rise out of position.


6. On the upper WFT-SB spool assembly, run in two lockscrews ("snug" tight ONLY), 180 degrees apart, to hold the bowl protector in place.

WARNING

Do NOT over tighten the lockscrews, as this will cause damage to both the bowl protector and lockscrews.

7. Remove the running tool from the bowl protector, by rotating the drill pipe clockwise two turns while lifting straight up.
8. Drill out and prepare to the production casing string per the drilling supervisor's instructions.

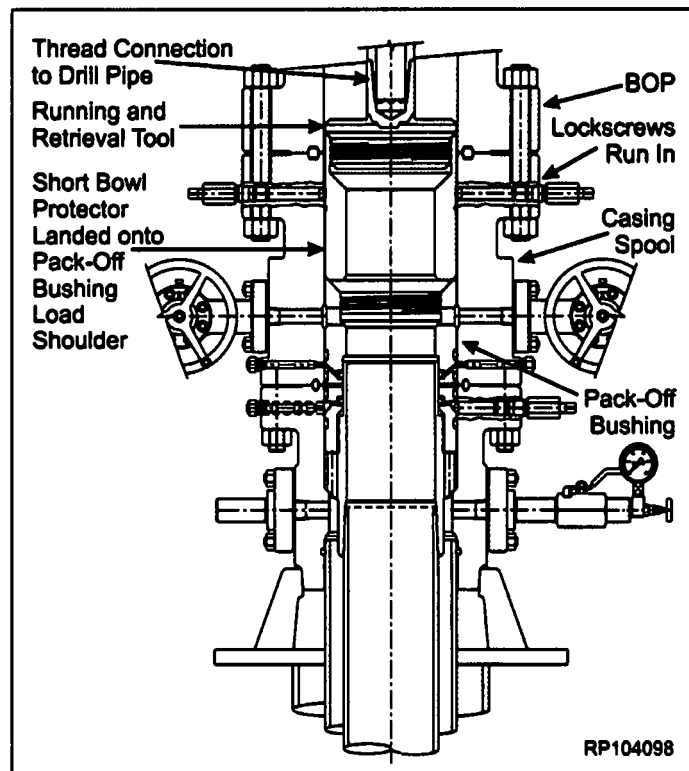

| | | | | | |
|--|-----------------------------|-----------------------------------|------------------------------|----------------------------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson December 2014 | Brad Franks December 2014 | Manual Zaragoza December 2014 | Page 15 of 24 |

WFT Split Bowl (SB) Wellhead System (Continued)

Retrieval of the Short Bowl Protector After Drilling

1. Make up the retrieval tool to the drill pipe with ACME threads down.
2. Slowly lower the retrieval tool into the bowl protector.
3. Rotate the retrieval tool counterclockwise, two turns, to engage with the bowl protector ACME threads.
4. Fully retract both lockscrews on the casing spool (upper flange), and retrieve the bowl protector.
5. Remove the bowl protector and retrieval tool from the drill string.

Running the Production Casing

1. Run the production casing to necessary depth and cement as required.

NOTE

There are two methods for installing WFT-22 Slip Type Casing Hangers:

- Under the BOP stack.
- Through the BOP stack.

Installation of the Slip-Type Casing Hanger Under the BOP Stack

1. Drain the casing head through the uppermost side outlet valve.
2. Lift and suspend the BOP stack above the WFT-SB spool assembly to a minimum of 18 inches.
3. Wash out the WFT-SB casing head/spool assembly as required.
4. Confirm that ONLY the lockscrews in the casing spool (upper flange) are fully retracted.

5. Examine the WFT-22 slip-type casing hanger. Verify the following:

- Slip segments are clean and undamaged.
- All screws are in place.
- Packing element is clean and undamaged.


CAUTION

The packing element should not protrude past the casing hanger outer diameter. If the packing element does extend past the outer diameter, loosen the cap screws in the bottom of the hanger.



6. Place two boards across the casing spool face, against the casing, to support the hanger.
7. Disengage the spring loaded latch, open the hanger and wrap the hanger around the casing, allowing the support boards to carry weight.
8. Re-engage the casing hanger spring loaded latch.
9. Remove the slip retaining cap screws from the outer diameter of the hanger body, allowing the slip segments to settle around the casing.
10. Supporting the weight of the casing hanger, remove the support boards and lower the hanger into the WFT-SB casing head/spool assembly until it lands on the pack-off bushing load shoulder.

CAUTION

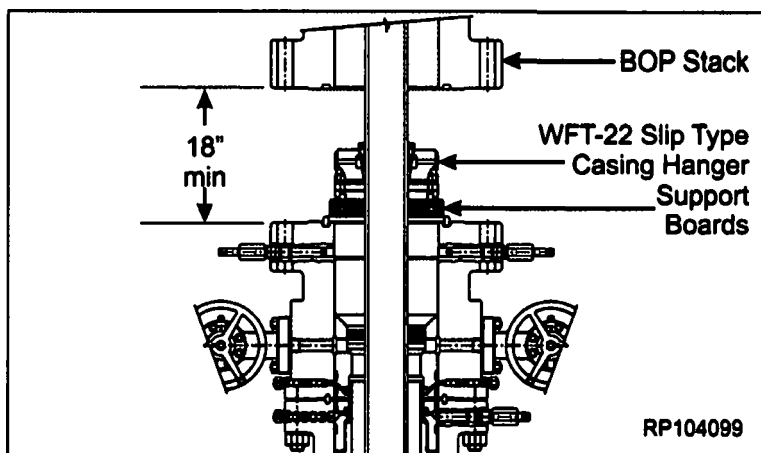Do NOT drop the hanger; lower it carefully.



RP104099

| | | | | | |
|--|-----------------------------|---|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 16 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

Installation of the Slip-Type Casing Hanger through the BOP Stack

1. Drain the WFT-SB casing head/spool assembly and BOP stack through the side outlet valves on the spool assembly.
2. Wash out the wellhead assembly until clean returns are seen.
3. Examine the slip type casing hanger. Verify the following:
 - slip segments are clean and undamaged
 - all screws are in place
 - Packing Element is clean and undamaged.
4. Place two boards across the rotary table, against the casing, to support the hanger.
5. Disengage the spring loaded latch, open the hanger and wrap it around the casing, allowing the support boards to carry the weight.
6. Re-engage the casing hanger's spring loaded latch.
7. Measure the distance from the top flange of the WFT-SB casing spool to the drilling rig floor (RKB).
8. Measure out two lengths of soft-line cord (rope) to the same length as the

CAUTION


The packing element should not protrude past the casing hanger outer diameter. If the packing element does extend past the outer diameter, loosen the cap screws in the bottom of the hanger.


RKB measurement, and adding an additional 10 feet to each line.

9. Mark the soft line cord at the required length.
10. Install two eyebolts into the tapped holes in the top of the casing hanger slip segments, 180 degrees apart.
11. Securely tie the soft-line cord to the eyebolts.

NOTE

Measuring the soft-line cord and installing the eyebolts into the hanger segments should be done offline.

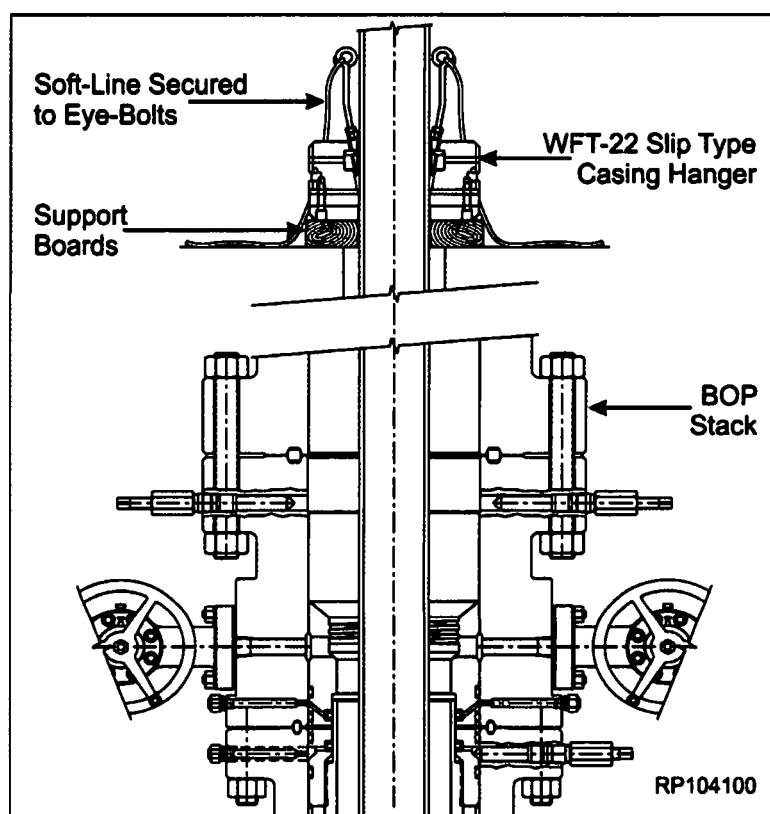

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 17 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

12. Remove the slip retaining cap screws from the outer diameter of the hanger body, allowing the slip segments to settle around the casing.
13. Supporting the weight of the casing hanger, remove the support boards and carefully lower the hanger through the BOP stack into the WFT-SB casing head/spool assembly, until it securely lands on the pack-off bushing load shoulder.

CAUTION

Do NOT drop hanger; lower it carefully.



Hanging off the Production Casing


1. With the casing hanger now landed onto the pack-off bushing load shoulder, pull tension on the casing to the desired hanging weight, and then slack off.

NOTE

A sharp decrease on the weight indicator will signify that the hanger has taken weight. If this does not occur, pull tension again and slack off once more.

2. Rough cut casing approximately 16" above top of WFT-SB Spool top flange. Remove excess casing.
3. Carefully remove BOP stack, set aside.
4. Final cut the casing at about $12\frac{7}{8}" \pm \frac{1}{8}"$ above the face of the WFT-SB spool, which will allow room for the double studded adapter flange.
5. Grind the casing stub level and bevel the casing outer diameter ($\frac{1}{4}" \times \frac{1}{8}"$) and inner diameter ($\frac{1}{8}" \times 45$ degrees).

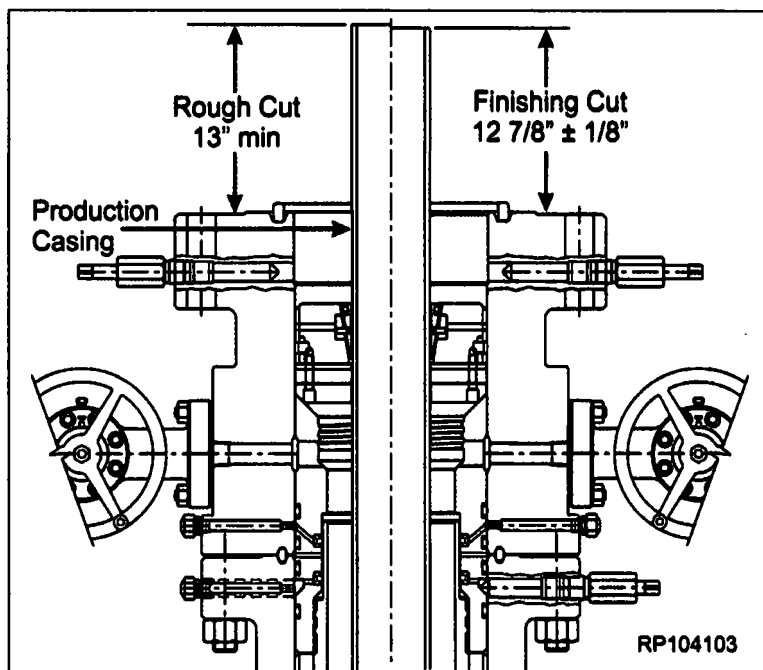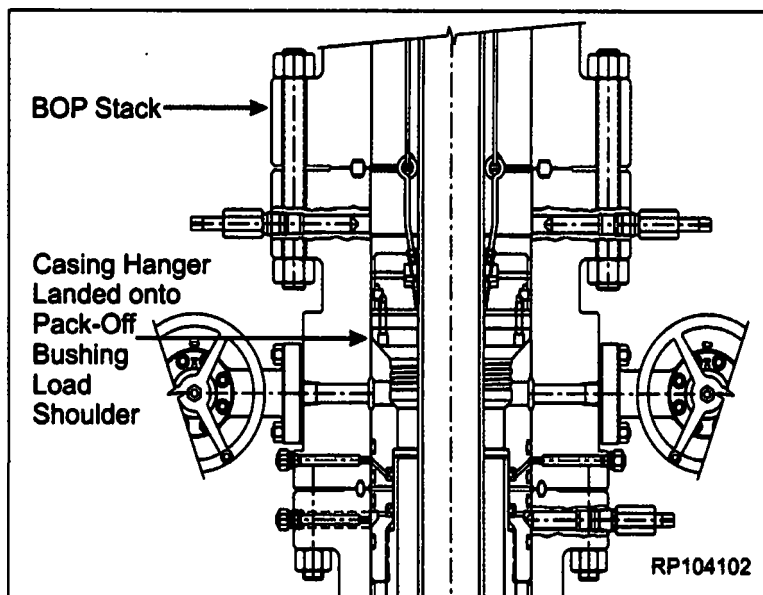

| | | | | | |
|--|-----------------------------|-----------------------------------|------------------------------|----------------------------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson December 2014 | Brad Franks December 2014 | Manual Zaragoza December 2014 | Page 18 of 24 |

WFT Split Bowl (SB) Wellhead System (Continued)

Installation of the Double-Studded Adapter (DSA) Flange

1. Examine the double studded adapter (DSA) Flange. Verify the following:
 - Ring grooves are clean and undamaged.
 - Stud threads are clean and undamaged.
2. Orient the DSA flange with the 10M side down.
3. Thoroughly clean the mating grooves of the DSA flange and the WFT-SB spool assembly. Wipe lightly with oil or grease.





Excessive oil or grease will prevent a positive seal from forming.

4. Install a new appropriately sized ring gasket into the WFT-SB spool assembly groove.
5. Lift, while holding level, and carefully lower the DSA over the production casing stub until it lands on the ring gasket.
6. Make-up the flange connection with appropriate nuts, tightening in alternate cross pattern, as required by API 6A.
7. Fill the void area in the DSA around the production casing with a light weight oil.
8. Continue filling with a light weight oil to the top of the DSA.



Do NOT allow oil to run into the ring groove. This may prevent a positive seal from forming.

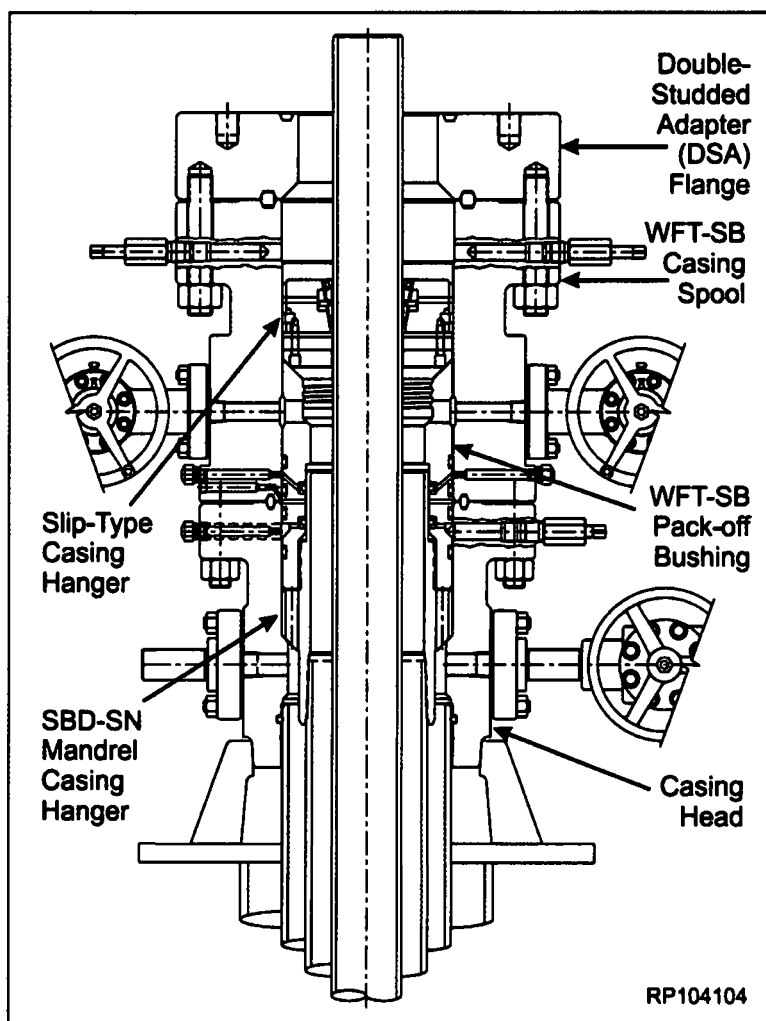

| | | | | | |
|--|-----------------------------|-----------------------------------|------------------------------|----------------------------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson December 2014 | Brad Franks December 2014 | Manual Zaragoza December 2014 | Page 19 of 24 |

WFT Split Bowl (SB) Wellhead System (Continued)

Installation and Testing of the Tubing Spool Assembly

Installation of the TCM Tubing Spool Assembly

1. Examine the tubing spool assembly. Verify the following:
 - bore is clean and free of debris
 - ring grooves and seals are clean and undamaged
 - PE-seal assembly is properly installed, clean and undamaged.
2. Thoroughly clean the mating ring grooves of the WFT-TCM Tubing Spool and WFT-SB Casing Spool.
3. Lightly lubricate the inner diameter of the PE-seal and outer diameter of the casing stub with oil or grease.

▲WARNING▲

Excessive oil or grease will prevent a positive seal from forming.

4. Install a new appropriately sized ring gasket into the WFT-SB casing spool assembly groove.
5. Orient the tubing spool assembly as required and carefully lower it over the casing stub, until it lands on the ring gasket.
6. Make up the flange connection with the appropriate studs and nuts, tightening in an alternating cross pattern, as required by API 6A.

Testing the Secondary Seal and Flange Connection Test


1. Locate the test port fitting on the OD of the tubing spool lower flange. Remove the dust cap from the fitting.
2. Attach a test pump to the test port fitting.


3. Pump clean test fluid into the void area between the flanges until a test pressure of **10,000 psi or 80% of casing collapse pressure is attained**, whichever is lower.
4. Hold and monitor pressure for 15 minutes or as required by the drilling supervisor.
5. Once a satisfactory test is achieved, carefully bleed off pressure and remove the test pump
6. Attach a bleeder tool to the test port fitting and open the tool to vent any remaining trapped pressure.

▲CAUTION▲

Always direct the bleeder tool port away from people and property.

7. Remove the bleeder tool and reinstall the dust cap on the test port fitting.
8. Install a new appropriately sized ring gasket into the tubing spool groove.

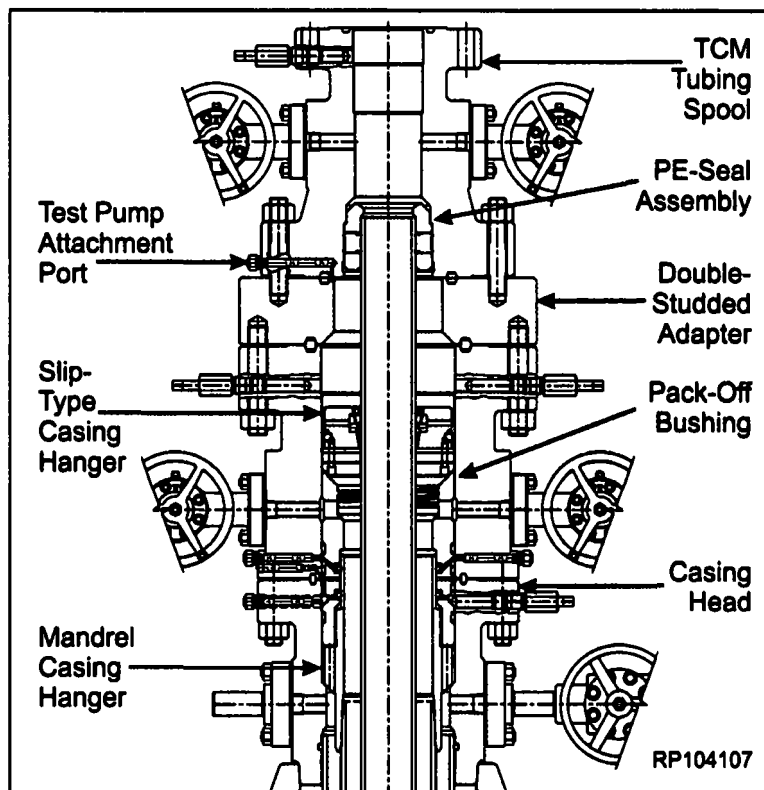

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 20 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

Testing the BOP

NOTE

Immediately after the make-up of the BOP Stack and periodically during drilling of hole for the next string, the BOP stack (flanged connections and rams) must be tested.


1. Examine the test plug. Verify that:
 - O-ring seals and plugs are properly installed, clean and undamaged.
 - All threads are clean and undamaged.
2. Orient the test plug with O-ring seals up and drill pipe pin connection down.
3. Make up a joint of drill pipe to the top of the test plug.


NOTE

If pressure is to be supplied through the drill pipe, the pipe plug should be removed from the weep port.

4. Fully retract all lockscrews on the WFT-TCM tubing spool assembly.
5. Open the side outlet valves on the tubing spool.
6. Wipe the test plug O-ring seals with a light oil or grease.
7. Lower the test plug through the BOP until it lands on the tubing spool load shoulder.
8. Close the BOP rams on the drill pipe and test to **10,000 psi maximum**.
9. Monitor the open outlets for signs of leakage past the test plug.

10. Once a satisfactory test is achieved, release pressure and open the rams.
11. Close the side outlet valves.
12. Remove as much fluid from the BOP stack as possible.
13. Slowly retrieve the test plug, avoiding damage to the seals.
14. Repeat this procedure, as required, during drilling or conditioning of the hole.

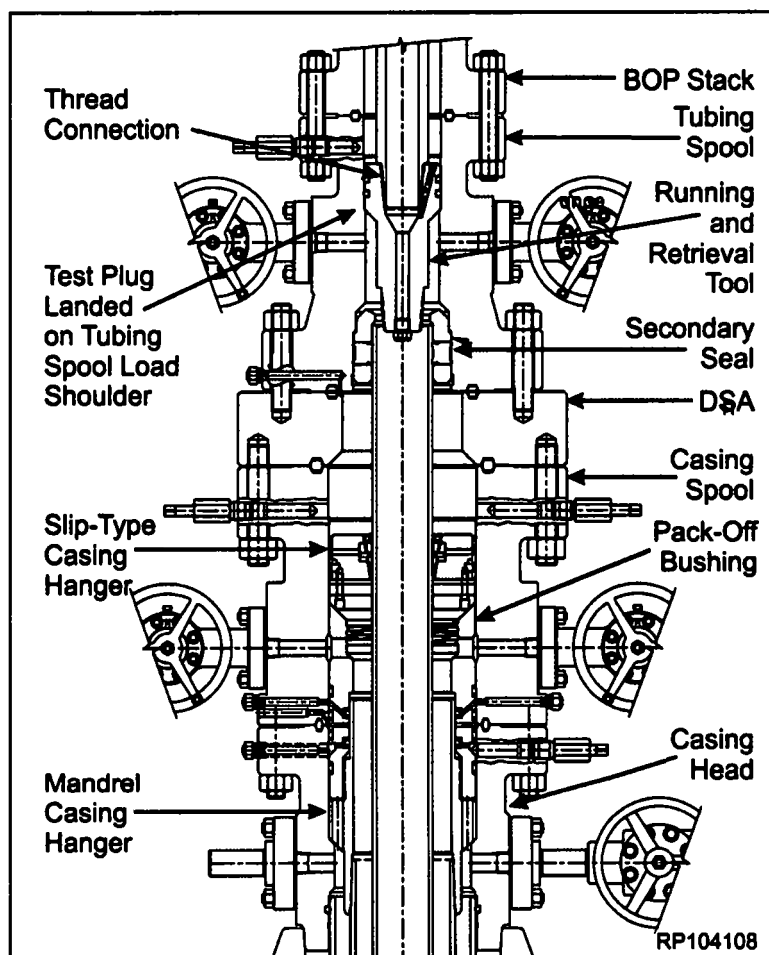

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 21 of 24 |
| | | December 2014 | December 2014 | December 2014 | |


WFT Split Bowl (SB) Wellhead System (Continued)



Hanging off the Production Tubing String

1. Run the production tubing and space out appropriately for the tubing hanger.
2. Examine the TC1AEN Tubing Hanger. Verify the following:
 - Packing element is clean and undamaged.
 - S-seals are properly installed.
 - S-seals are clean and undamaged.
 - All threads are clean and undamaged.
3. Make-up a short handling joint to the top of the tubing hanger.
4. Pick up the tubing hanger and make it up to the tubing string, tightening the connection to the thread manufacturer's recommended optimum torque value.
5. Remove the short handling joint from the top of the hanger. Make up the landing joint to the top of the tubing hanger, tightening the connection to the thread manufacturer's recommended minimum torque values.
6. Ensure that all tubing spool lockscrews are fully retracted from the bore and open side outlet valves. Drain the BOP stack.
7. Calculate the distance from the tubing spool load shoulder to the rig floor. Measure from the face of the tubing spool.
8. Carefully lower the tubing hanger into the well, tallying the tubing every five feet, until the tubing hanger lands securely on the tubing spool load shoulder.
9. Run in all tubing spool lockscrews, in an alternating cross pattern, to 300 ft-lbs, in 75 ft-lb increments.
10. Remove the landing joint from the tubing hanger, and set it aside.

NOTE

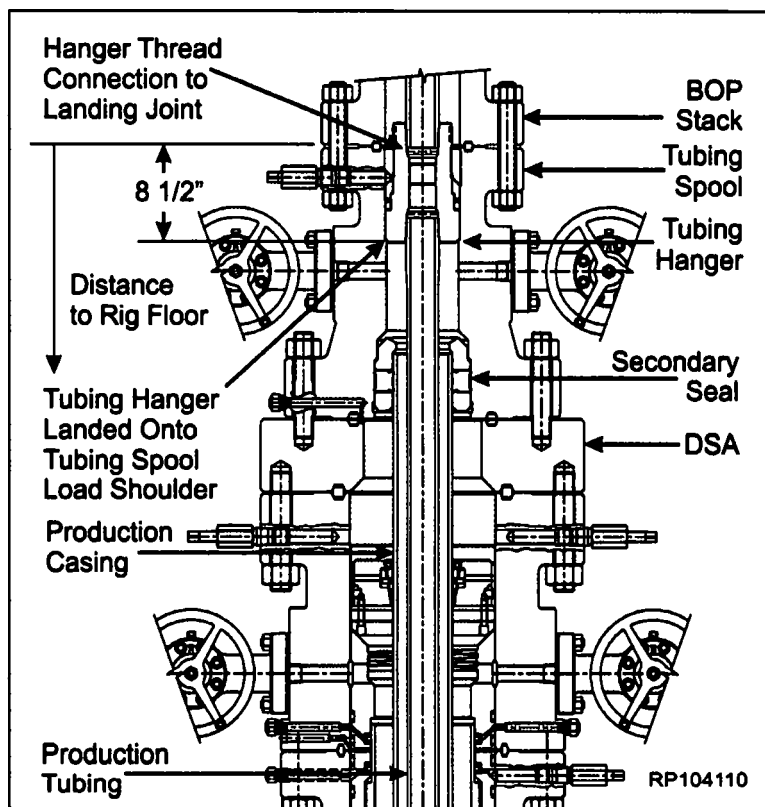The side outlet valves should remain open while landing the tubing hanger.



| | | | | | |
|--|-----------------------------|---|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | |  | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 22 of 24 |
| | | December 2014 | December 2014 | December 2014 | |

WFT Split Bowl (SB) Wellhead System (Continued)

11. Install the Type H Back Pressure Valve, carefully lowering the BPV through the BOP stack into the tubing hanger. Rotate the BPV counterclockwise (to the left) until it bottoms out in the tubing hanger BPV prep. Continue rotating counterclockwise, approximately 7 turns, to retrieve the running tool.
12. With the well safe and under control, the BOP stack may be removed.

Installation and Testing of the Production Tree

Installation

1. Examine the production tree assembly. Verify the following:
 - Bore is clean and free of debris.
 - All valves are in the fully open position.
 - All threads and seal areas are clean and undamaged.
 - All fittings, nuts and handwheels are intact and undamaged.
2. Thoroughly clean all exposed portions of the tubing hanger, tubing head adapter flange and bottom prep of the tubing head adapter.
3. Thoroughly clean mating ring grooves of the tubing head adapter flange and WFT-TCM tubing spool.
4. Lightly lubricate the tubing hanger neck outer diameter and tubing head adapter flange bottom prep with oil or grease.

▲WARNING▲



Excessive oil or grease will prevent a positive seal from forming.

5. Install a new appropriately sized ring gasket into the WFT-TCM tubing spool groove.

6. Fill the void area around the hanger with hydraulic fluid, to the top of the tubing spool assembly.

▲WARNING▲

Do NOT overfill the void area, allowing oil to run into the ring groove. This may prevent a positive seal from forming.

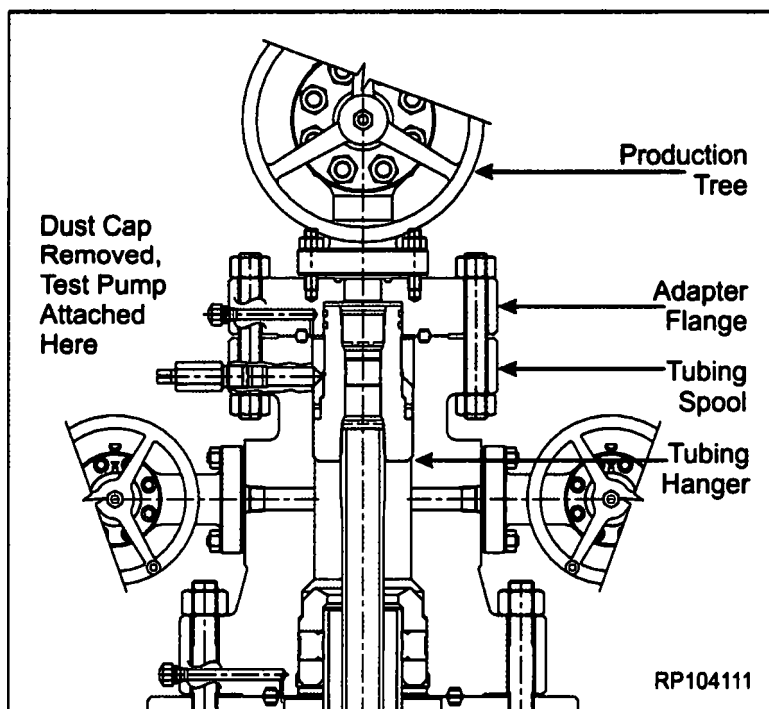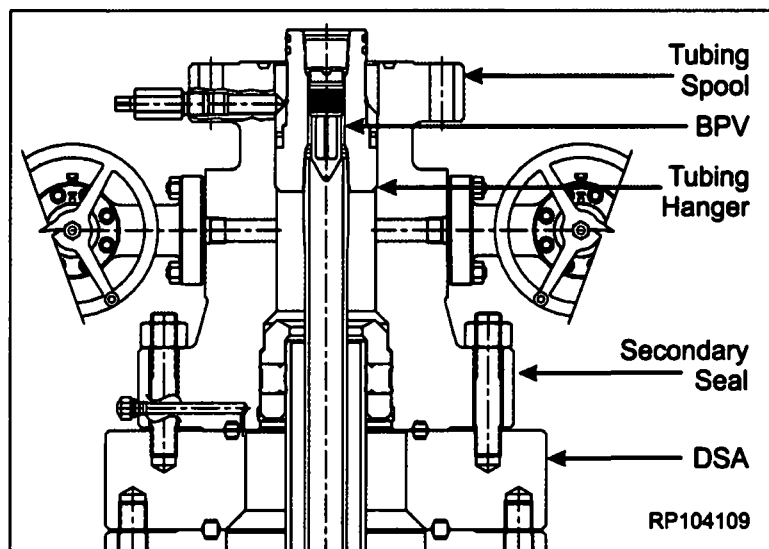

Weatherford

5-3-GL-GL-WES-00XXX

Field Service Manual

| Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
|-------------------------|---------------|-----------------|---------------|
| <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| Marion Robertson | Brad Franks | Manual Zaragoza | Page 23 of 24 |
| December 2014 | December 2014 | December 2014 | |

APD ID: 10400035877

Submission Date: 11/08/2018


Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Well Type: OIL WELL

Well Work Type: Drill



[Show Final Text](#)

Section 1 - Existing Roads

Will existing roads be used? YES

Existing Road Map:

ROJO_7811_22_FED_COM_26H_Vic_Map_20181101134826.pdf

Existing Road Purpose: ACCESS,FLUID TRANSPORT

Row(s) Exist? NO

ROW ID(s)

ID:

Do the existing roads need to be improved? NO

Existing Road Improvement Description:

Existing Road Improvement Attachment:

Section 2 - New or Reconstructed Access Roads

Will new roads be needed? YES

New Road Map:

ROJO_7811_22_FED_COM_26H_Topo_Access_rd_Map_20181101135131.pdf

New road type: RESOURCE

Length: 472

Feet

Width (ft.): 25

Max slope (%): 2

Max grade (%): 2

Army Corp of Engineers (ACOE) permit required? NO

ACOE Permit Number(s):

New road travel width: 15

New road access erosion control: Road construction requirements and regular maintenance would alleviate potential impacts to the access road from water erosion damage.

New road access plan or profile prepared? NO

New road access plan attachment:

Access road engineering design? NO

Access road engineering design attachment:

Operator Name: BIA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Access surfacing type: OTHER

Access topsoil source: BOTH

Access surfacing type description: Native Caliche

Access onsite topsoil source depth: 6

Offsite topsoil source description: Material will be obtained from the closest existing caliche pit as designated by the BLM.

Onsite topsoil removal process: The top 6 inches of topsoil is pushed off and stockpiled along the side of the location. An approximate 160' X 160' area is used within the proposed well site to remove caliche. Subsoil is removed and stockpiled within the pad site to build the location and road. Then subsoil is pushed back in the hole and caliche is spread accordingly across proposed access road.

Access other construction information:

Access miscellaneous information:

Number of access turnouts:

Access turnout map:

Drainage Control

New road drainage crossing: OTHER

Drainage Control comments: Proposed access road will be crowned and ditched and constructed of 6 inch rolled and compacted caliche. Water will be diverted where necessary to avoid ponding, maintain good drainage, and to be consistent with local drainage patterns.

Road Drainage Control Structures (DCS) description: Any ditches will be at 3:1 slope and 3 feet wide.

Road Drainage Control Structures (DCS) attachment:

Access Additional Attachments

Additional Attachment(s):

Section 3 - Location of Existing Wells

Existing Wells Map? YES

Attach Well map:

ROJO_7811_22_FED_COM_26H_1_mile_radius_map_20181101151204.pdf

Existing Wells description:

Section 4 - Location of Existing and/or Proposed Production Facilities

Submit or defer a Proposed Production Facilities plan? SUBMIT

Production Facilities description: If well is productive, we will use the existing well pad for the tank battery and all necessary production facilities.

Production Facilities map:

Production_Facility_Layout_20180131163053.pdf

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Section 5 - Location and Types of Water Supply

Water Source Table

Water source use type: DUST CONTROL,
INTERMEDIATE/PRODUCTION CASING, STIMULATION, SURFACE
CASING

Water source type: OTHER

Describe type:

Source longitude: -103.33122

Source latitude: 32.063675

Source datum: NAD27

Water source permit type: PRIVATE CONTRACT

Source land ownership: PRIVATE

Water source transport method: TRUCKING

Source transportation land ownership: PRIVATE

Water source volume (barrels): 100000

Source volume (acre-feet): 12.88931

Source volume (gal): 4200000

Water source and transportation map:

Rojo_7811_FED_COM_26H_29H_Water_Transportation_map_20181107084520.pdf

Water source comments:

New water well? NO

New Water Well Info

Well latitude:

Well Longitude:

Well datum:

Well target aquifer:

Est. depth to top of aquifer(ft):

Est thickness of aquifer:

Aquifer comments:

Aquifer documentation:

Well depth (ft):

Well casing type:

Well casing outside diameter (in.):

Well casing inside diameter (in.):

New water well casing?

Used casing source:

Drilling method:

Drill material:

Grout material:

Grout depth:

Casing length (ft.):

Casing top depth (ft.):

Well Production type:

Completion Method:

Water well additional information:

State appropriation permit:

Operator Name: BIA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Additional information attachment:

Section 6 - Construction Materials

Construction Materials description: Caliche used for construction of the drilling pad and access road will be obtained from the closest existing caliche pit as approved by the BLM or from prevailing deposits found under the location. If there is not sufficient material available, caliche will be purchased from the nearest caliche pit located in Section 23 T25S R33E Lea County, NM. Alternative location if original location closes will be located in Sec 3 T26S R33E Lea County, NM.

Construction Materials source location attachment:

Section 7 - Methods for Handling Waste

Waste type: GARBAGE

Waste content description: Trash

Amount of waste: 500 pounds

Waste disposal frequency : One Time Only

Safe containment description: Trash produced during drilling and completion operations will be collected in a trash container and disposed of properly.

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

Disposal type description:

Disposal location description: Trucked to an approved disposal facility.

Waste type: DRILLING

Waste content description: Drilling fluids and cuttings.

Amount of waste: 4164 barrels

Waste disposal frequency : One Time Only

Safe containment description: All drilling fluids will be stored safely and disposed of properly.

Safe containmant attachment:

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

Disposal type description:

Disposal location description: Trucked to an approved disposal facility.

Waste type: SEWAGE

Waste content description: Human waste and grey water.

Amount of waste: 1000 gallons

Waste disposal frequency : One Time Only

Safe containment description: Waste material will be stored safely and disposed of properly.

Safe containmant attachment:

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Waste disposal type: HAUL TO COMMERCIAL FACILITY **Disposal location ownership:** COMMERCIAL

Disposal type description:

Disposal location description: Trucked to an approved disposal facility.

Reserve Pit

Reserve Pit being used? NO

Temporary disposal of produced water into reserve pit?

Reserve pit length (ft.)

Reserve pit width (ft.)

Reserve pit depth (ft.)

Reserve pit volume (cu. yd.)

Is at least 50% of the reserve pit in cut?

Reserve pit liner

Reserve pit liner specifications and installation description

Cuttings Area

Cuttings Area being used? NO

Are you storing cuttings on location? NO

Description of cuttings location

Cuttings area length (ft.)

Cuttings area width (ft.)

Cuttings area depth (ft.)

Cuttings area volume (cu. yd.)

Is at least 50% of the cuttings area in cut?

WCuttings area liner

Cuttings area liner specifications and installation description

Section 8 - Ancillary Facilities

Are you requesting any Ancillary Facilities?: NO

Ancillary Facilities attachment:

Comments: It is possible that a mobile home will be used at the well site during drilling operations.

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Section 9 - Well Site Layout

Well Site Layout Diagram:

ROJO_7811_22_FED_COM_26H_Well_Site_Plan_20181101152018.pdf

ROJO_7811_22_FED_COM_26H_Well_Site_Plan_with_Topsoil_and_IR_20190326083248.pdf

Comments:

Section 10 - Plans for Surface Reclamation

Type of disturbance: New Surface Disturbance

Multiple Well Pad Name: ROJO 7811 22 FEDERAL COM

Multiple Well Pad Number: 26-29

Recontouring attachment:

Drainage/Erosion control construction: During construction proper erosion control methods will be used to control erosion, runoff, and siltation of the surrounding area.

Drainage/Erosion control reclamation: Proper erosion control methods will be used on the area to control erosion, runoff, and siltation of the surrounding area.

| | | |
|---|--|--|
| Well pad proposed disturbance (acres): 0 | Well pad interim reclamation (acres): 4.49 | Well pad long term disturbance (acres): 4.49 |
| Road proposed disturbance (acres): 0 | Road interim reclamation (acres): 0.26 | Road long term disturbance (acres): 0.16 |
| Powerline proposed disturbance (acres): 0 | Powerline interim reclamation (acres): 0 | Powerline long term disturbance (acres): 0 |
| Pipeline proposed disturbance (acres): 0 | Pipeline interim reclamation (acres): 0 | Pipeline long term disturbance (acres): 0 |
| Other proposed disturbance (acres): 0 | Other interim reclamation (acres): 0 | Other long term disturbance (acres): 0 |
| Total proposed disturbance: 0 | Total interim reclamation: 4.75 | Total long term disturbance: 4.65 |

Disturbance Comments: Interim Reclamation will be at North side of well pad, 50' (see attachment under SUPO Section 9).

Reconstruction method: The areas planned for interim reclamation will then be recontoured to the original contour if feasible, or if not feasible, to an interim contour that blends with the surrounding topography as much as possible. Where applicable, the fill material of the well pad will be backfilled into the cut to bring the area back to the original contour. The interim cut and fill slopes prior to re-seeding will not be steeper than a 3:1 ratio, unless the adjacent native topography is steeper. Note: Constructed slopes may be much steeper during drilling, but will be recontoured to the above ratios during interim reclamation.

Topsoil redistribution: Topsoil will be evenly respread and aggressively revegetated over the entire disturbed area not needed for all-weather operations. Topsoil will be at North side of well pad, 30' (see attachment under SUPO Section 9).

Soil treatment: To seed the area, the proper BLM seed mixture, free of noxious weeds, will be used. Final seedbed preparation will consist of contour cultivating to a depth of 4 to 6 inches within 24 hours prior to seeding, dozer tracking, or other imprinting in order to break the soil crust and create seed germination micro-sites.

Existing Vegetation at the well pad: The historic climax plant community is a grassland dominated by black grama, dropseeds, and blue stems with sand sage and shinnery oak distributed evenly throughout. Current landscape displays mesquite, shinnery oak, yucca, desert sage, fourwing saltbush, snakeweed, and bunch grasses.

Existing Vegetation at the well pad attachment:

Existing Vegetation Community at the road: Refer to "Existing Vegetation at the well pad"

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Existing Vegetation Community at the road attachment:

Existing Vegetation Community at the pipeline: Refer to "Existing Vegetation at the well pad"

Existing Vegetation Community at the pipeline attachment:

Existing Vegetation Community at other disturbances: Refer to "Existing Vegetation at the well pad"

Existing Vegetation Community at other disturbances attachment:

Non native seed used? NO

Non native seed description:

Seedling transplant description:

Will seedlings be transplanted for this project? NO

Seedling transplant description attachment:

Will seed be harvested for use in site reclamation? NO

Seed harvest description:

Seed harvest description attachment:

Seed Management

Seed Table

Seed type:

Seed source:

Seed name:

Source name:

Source address:

Source phone:

Seed cultivar:

Seed use location:

PLS pounds per acre:

Proposed seeding season:

Seed Summary

Total pounds/Acre:

| Seed Type | Pounds/Acre |
|-----------|-------------|
|-----------|-------------|

Seed reclamation attachment:

Operator Contact/Responsible Official Contact Info

First Name:

Last Name:

Operator Name: BIA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Phone:

Email:

Seedbed prep:

Seed BMP:

Seed method:

Existing invasive species? NO

Existing invasive species treatment description:

Existing invasive species treatment attachment:

Weed treatment plan description: No invasive species present. Standard regular maintenance to maintain a clear location and road.

Weed treatment plan attachment:

Monitoring plan description: Identify areas supporting weeds prior to construction; prevent the introduction and spread of weeds from construction equipment during construction; and contain weed seeds and propagules by preventing segregated topsoil from being spread to adjacent areas. No invasive species present. Standard regular maintenance to maintain a clear location and road.

Monitoring plan attachment:

Success standards: To maintain all disturbed areas as per Gold Book standards.

Pit closure description: N/A

Pit closure attachment:

Section 11 - Surface Ownership

Disturbance type: WELL PAD

Describe:

Surface Owner: PRIVATE OWNERSHIP

Other surface owner description:

BIA Local Office:

BOR Local Office:

COE Local Office:

DOD Local Office:

NPS Local Office:

State Local Office:

Military Local Office:

USFWS Local Office:

Other Local Office:

USFS Region:

USFS Forest/Grassland:

USFS Ranger District:

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Section 12 - Other Information

Right of Way needed? NO

Use APD as ROW?

ROW Type(s):

ROW Applications


SUPO Additional Information:

Use a previously conducted onsite? YES

Previous Onsite information: Onsite was conducted Wednesday, June 13, 2018 by William DeGrush.

Other SUPO Attachment

VICINITY MAP

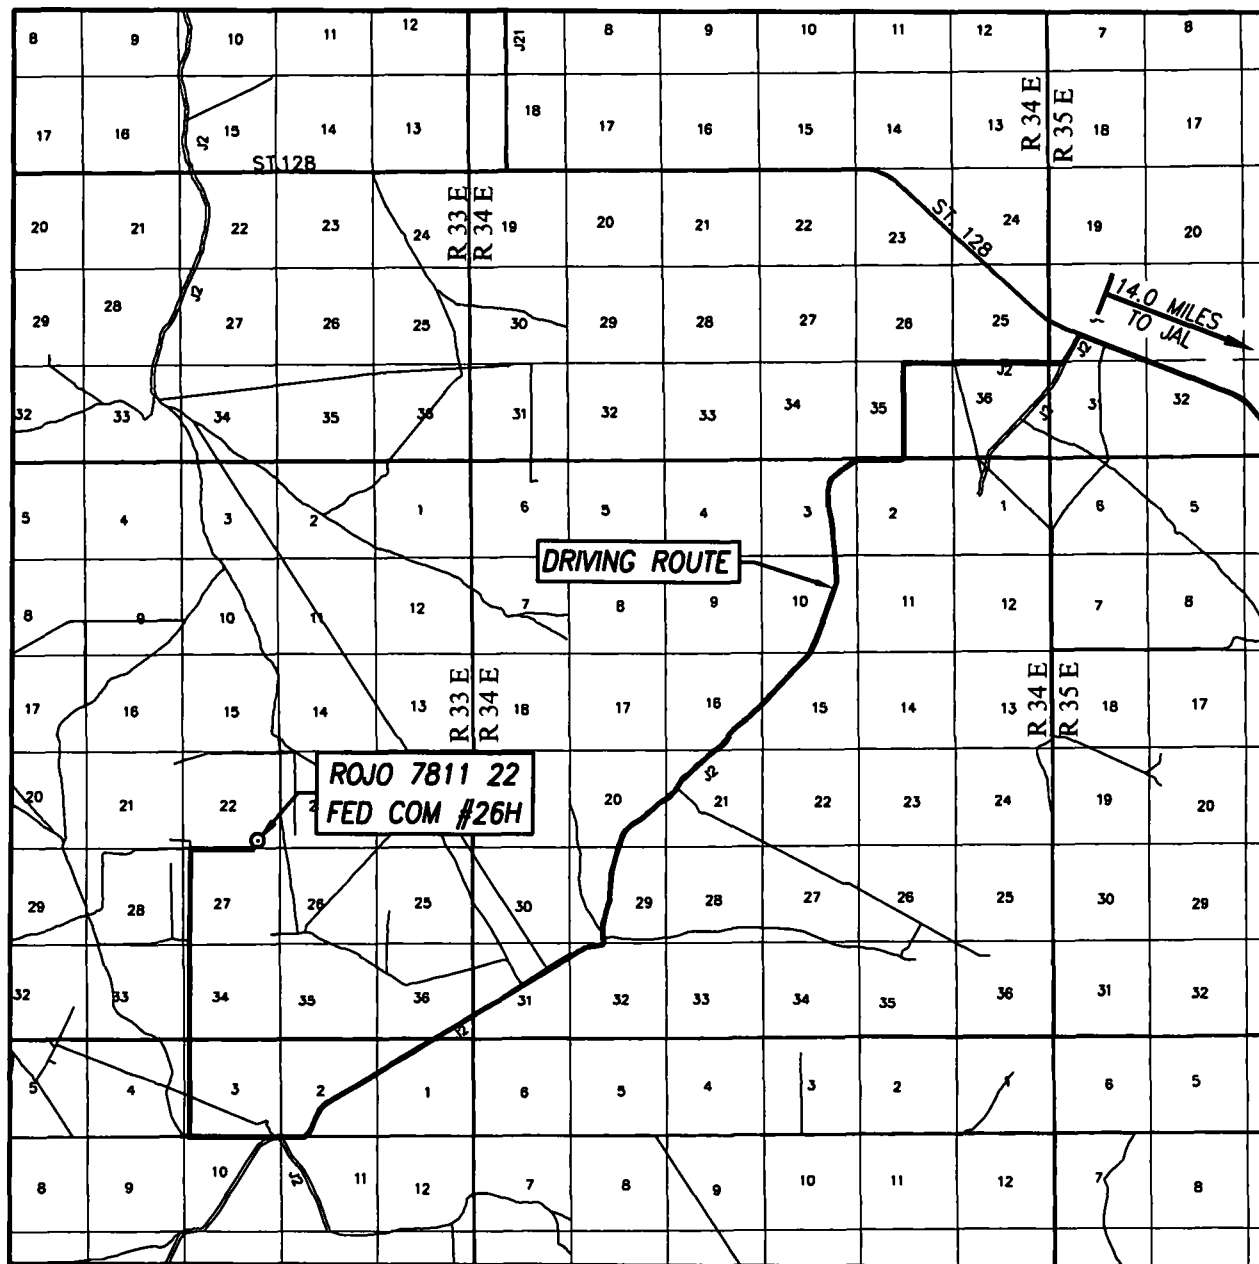

SCALE: 1" = 2 MILES

DRIVING ROUTE: SEE TOPOGRAPHICAL AND ACCESS ROAD MAP

SEC. 22 TWP. 25-S RGE. 33-E

SURVEY N.M.P.M.

COUNTY LEA STATE NEW MEXICO

DESCRIPTION 420' FSL & 1250' FEL

ELEVATION 3346'

OPERATOR BTA OIL PRODUCERS, LLC


LEASE ROJO 7811 22 FED COM

PROVIDING SURVEYING SERVICES
SINCE 1946

JOHN WEST SURVEYING COMPANY

412 N. DAL PASO HOBBS, N.M. 88240
(575) 393-3117 www.jwsc.biz
TBPLS# 10021000

TOPOGRAPHIC AND ACCESS ROAD MAP

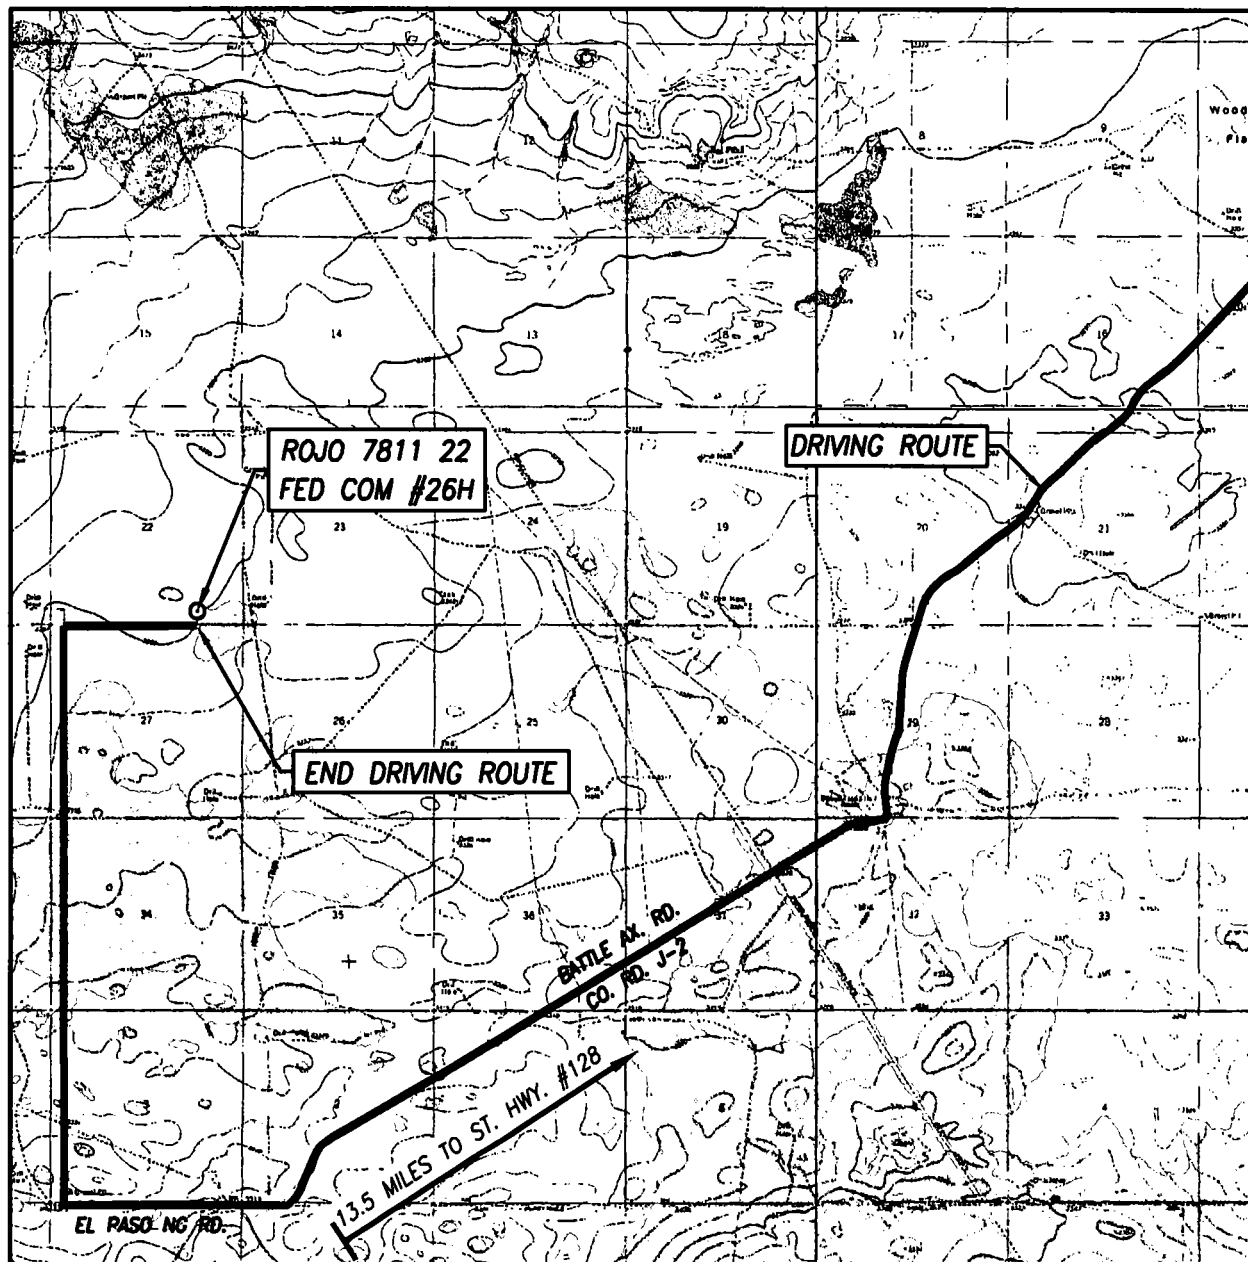

SCALE: 1" = 2000'

CONTOUR INTERVAL:
PADUCCA BREAKS EAST, N.M. - 10'

SEC. 22 TWP. 25-S RGE. 33-E

SURVEY N.M.P.M.

COUNTY LEA STATE NEW MEXICO

DESCRIPTION 420' FSL & 1250' FEL

ELEVATION 3346'

OPERATOR BTA OIL PRODUCERS, LLC

LEASE ROJO 7811 22 FED COM

U.S.G.S. TOPOGRAPHIC MAP

PADUCCA BREAKS EAST, N.M.

DIRECTIONS TO LOCATION:

FROM THE INTERSECTION OF ST. HWY. 128 AND ST. HWY. 18 IN JAL. GO WESTERLY ON ST. HWY. 128 APPROX. 14 MILES, TURN LEFT ON CO. RD. J-2(BATTLE AXE). FOLLOW MENDERING CO. RD. J-2 SOUTHWEST APPROX. 13.5 MILES TO EL PASO N.G. ROAD; TURN RIGHT AND GO WEST ON EL PASO N.G. ROAD APPROX. 1.2 MILES, TURN RIGHT AND GO NORTH 3.0 MILES, TURN RIGHT AND GO EAST 0.6 MILES TO EXISTING PAD. WELL IS NORTHEAST 534 FEET.



PROVIDING SURVEYING SERVICES
SINCE 1946
JOHN WEST SURVEYING COMPANY
412 N. DAL PASO HOBBS, N.M. 88240
(575) 393-3117 www.jwsc.biz
TBPLS# 10021000

DISTRICT I
 1625 N. French Dr., Hobbs, NM 88240
 Phone: (575) 393-6161 Fax: (575) 393-0720

DISTRICT II
 811 S. First St., Artesia, NM 88210
 Phone: (575) 748-1283 Fax: (575) 748-9720

DISTRICT III
 1000 Rio Brazos Road, Aztec, NM 87410
 Phone: (505) 334-6178 Fax: (505) 334-6170

DISTRICT IV
 1220 S. St. Francis Dr., Santa Fe, NM 87505
 Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, New Mexico 87505

Form C-102
 Revised August 1, 2011
 Submit one copy to appropriate
 District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

| | | | |
|---------------|--|-----------|---------------------------|
| API Number | | Pool Code | Pool Name |
| Property Code | Property Name ROJO 7811 22 FED COM | | Well Number 26H |
| OGRID No. | Operator Name BTA OIL PRODUCERS, LLC | | Elevation 3346' |

Surface Location


| UL or lot No. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|-----------|-------------|-------------|---------|---------------|------------------|---------------|----------------|------------|
| P | 22 | 25-S | 33-E | | 420 | SOUTH | 1250 | EAST | LEA |

Bottom Hole Location If Different From Surface


| UL or lot No. | Section | Township | Range | Lot Idn | Feet from the | North/South line | Feet from the | East/West line | County |
|---------------|-----------|-------------|-------------|---------|---------------|------------------|---------------|----------------|------------|
| A | 22 | 25-S | 33-E | | 100 | NORTH | 380 | EAST | LEA |


| | | | |
|-----------------|-----------------|--------------------|-----------|
| Dedicated Acres | Joint or Infill | Consolidation Code | Order No. |
|-----------------|-----------------|--------------------|-----------|

NO ALLOWABLE WILL BE ASSIGNED TO THIS COMPLETION UNTIL ALL INTERESTS HAVE BEEN CONSOLIDATED OR A NON-STANDARD UNIT HAS BEEN APPROVED BY THE DIVISION

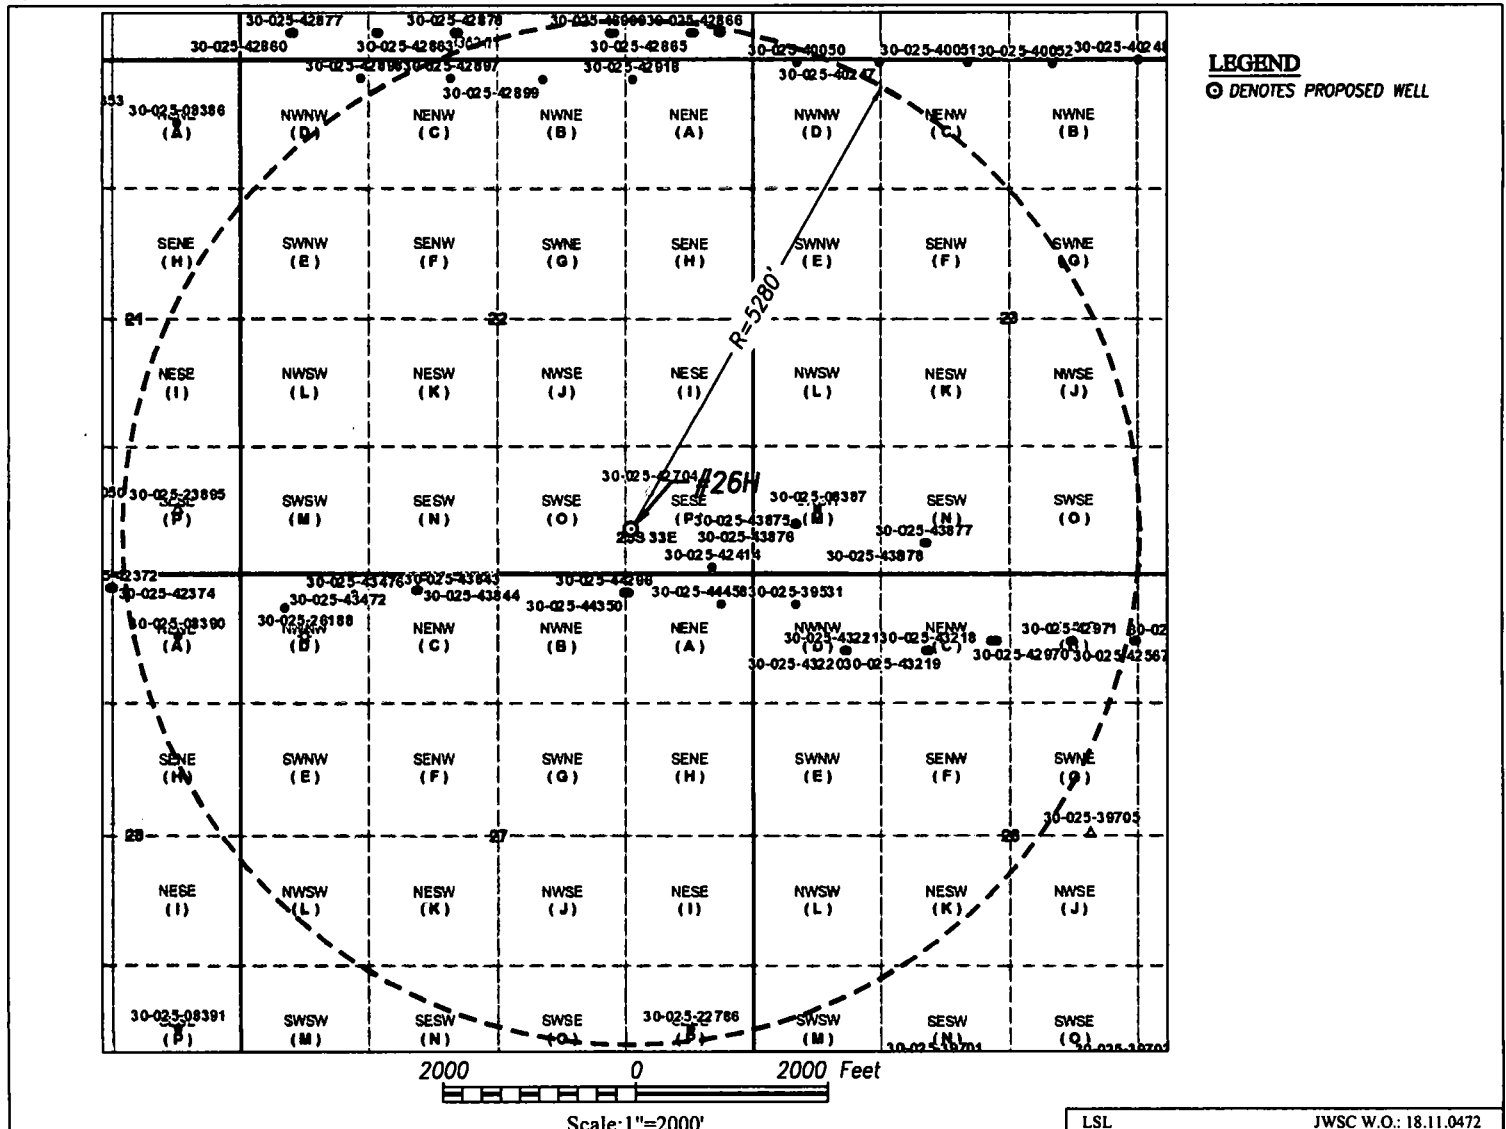

PRODUCTION FACILITY LAYOUT

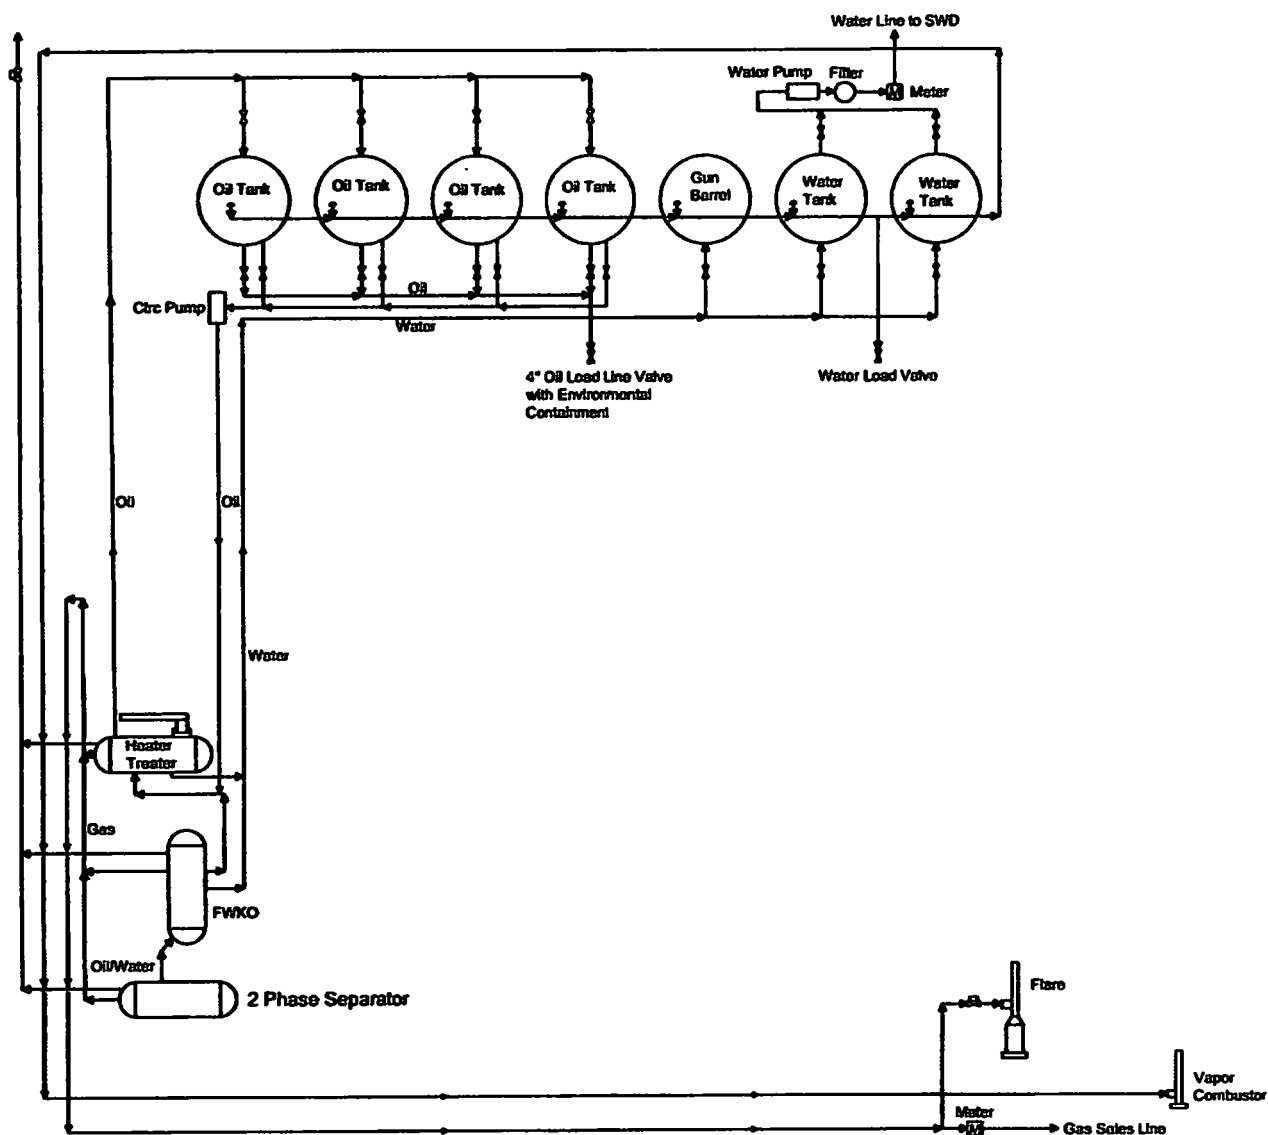


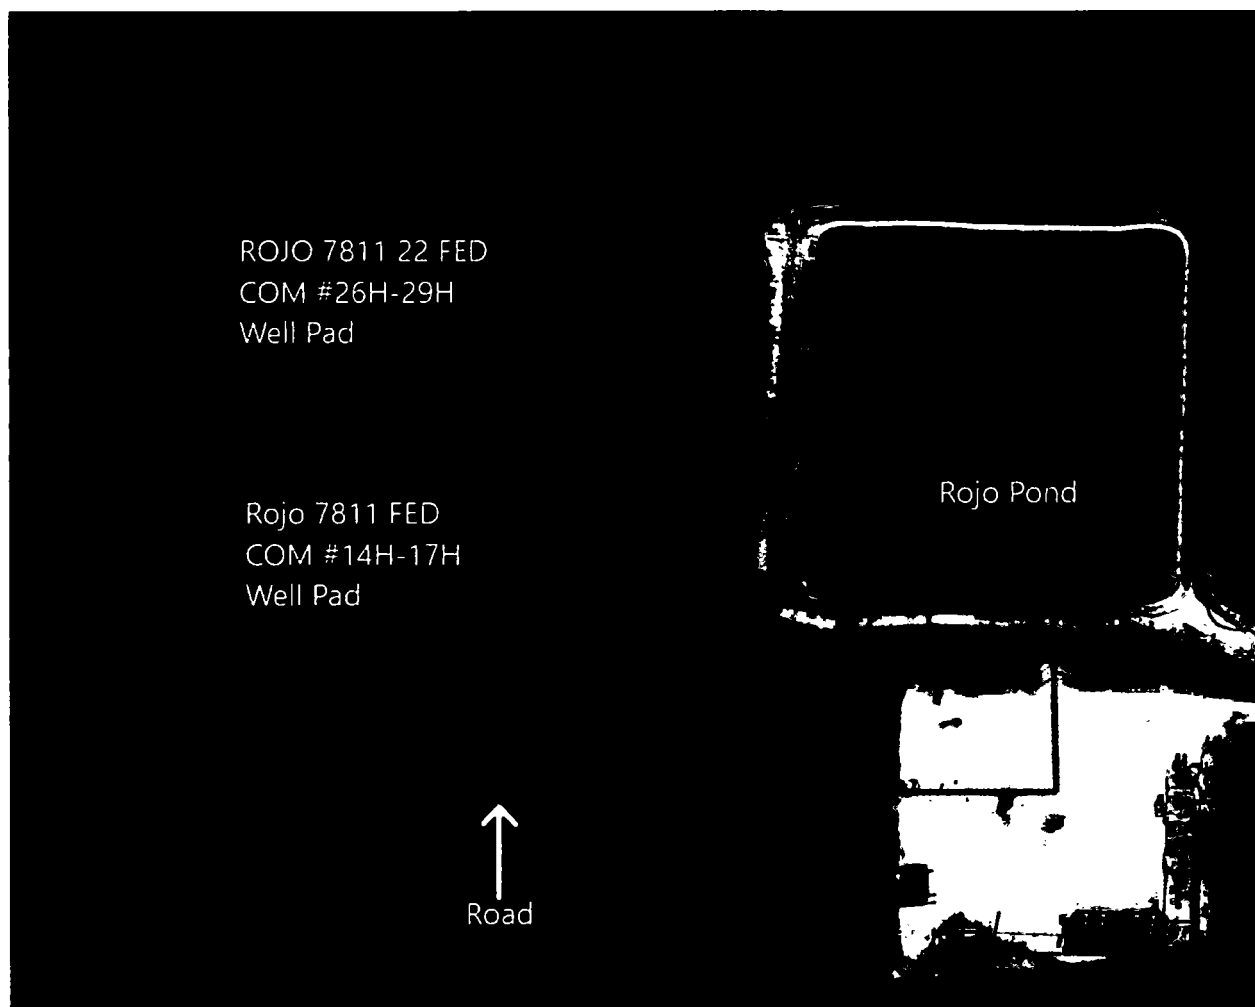

BTA OIL PRODUCERS, LLC
WATER TRANSPORTATION MAP
ROJO 7811 JV-P FED COM #26H - #29H WELLPAD TO ROJO Pond
SEC 22 T25S - R33E
LEA COUNTY, NM




WELL SITE PLAN

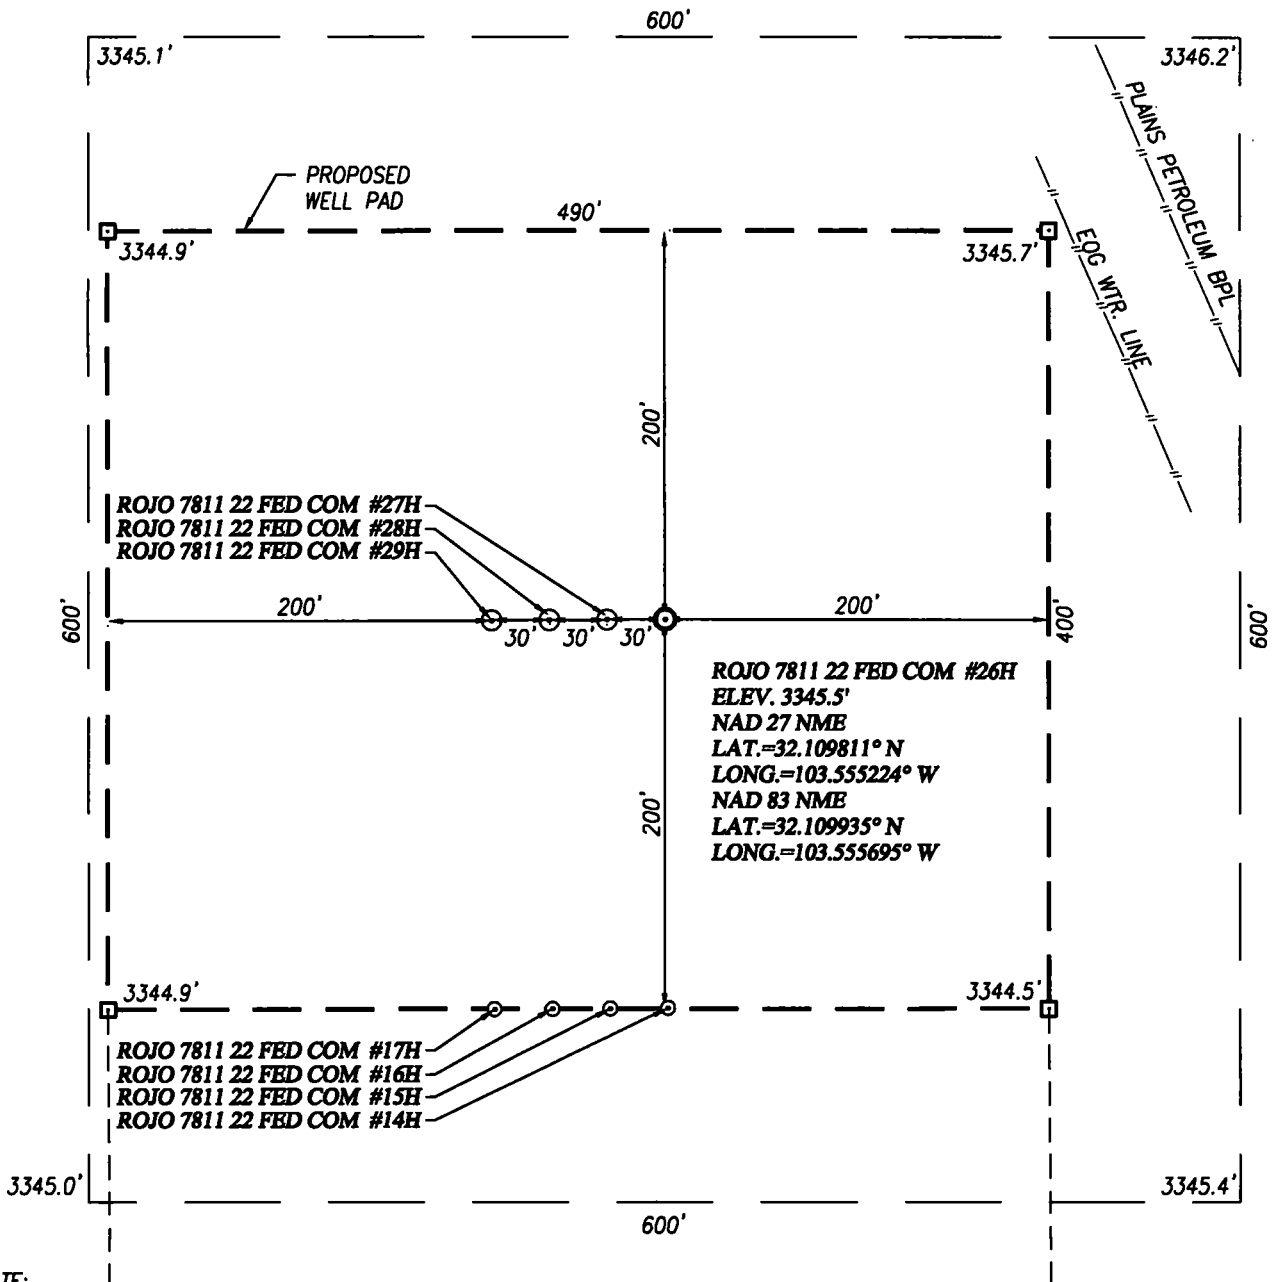

1) SEE "TOPOGRAPHICAL AND ACCESS ROAD MAP" FOR PROPOSED ROAD LOCATION.

DIRECTIONS TO LOCATION:

FROM THE INTERSECTION OF ST. HWY. 128 AND ST. HWY. 18 IN JAL. GO WESTERLY ON ST. HWY. 128 APPROX. 14 MILES, TURN LEFT ON CO. RD. J-2(BATTLE AXE). FOLLOW MENDERING CO. RD. J-2 SOUTHWEST APPROX. 13.5 MILES TO EL PASO N.G. ROAD; TURN RIGHT AND GO WEST ON EL PASO N.G. ROAD APPROX. 1.2 MILES, TURN RIGHT AND GO NORTH 3.0 MILES, TURN RIGHT AND GO EAST 0.6 MILES TO EXISTING PAD. WELL IS NORTHEAST 534 FEET.



BTA OIL PRODUCERS, LLC

**ROJO 7811 22 FED COM #26H WELL LOCATED 420 FEET FROM
THE SOUTH LINE AND 1250 FEET FROM THE EAST LINE OF
SECTION 22, TOWNSHIP 25 SOUTH, RANGE 33 EAST, N.M.P.M.,
LEA COUNTY, NEW MEXICO**

Survey Date: 04/24/18

CAD Date: 05/24/18

Drawn By: LSL

W.O. No.: 18110472

Rev: .

Rel. W.O.:

Sheet 1 of 1




**PROVIDING SURVEYING SERVICES
SINCE 1946**

JOHN WEST SURVEYING COMPANY

412 N. DAL PASO HOBBS, N.M. 88240

(575) 393-3117 www.jwsc.biz
TBPLS# 10021000


WELL SITE PLAN

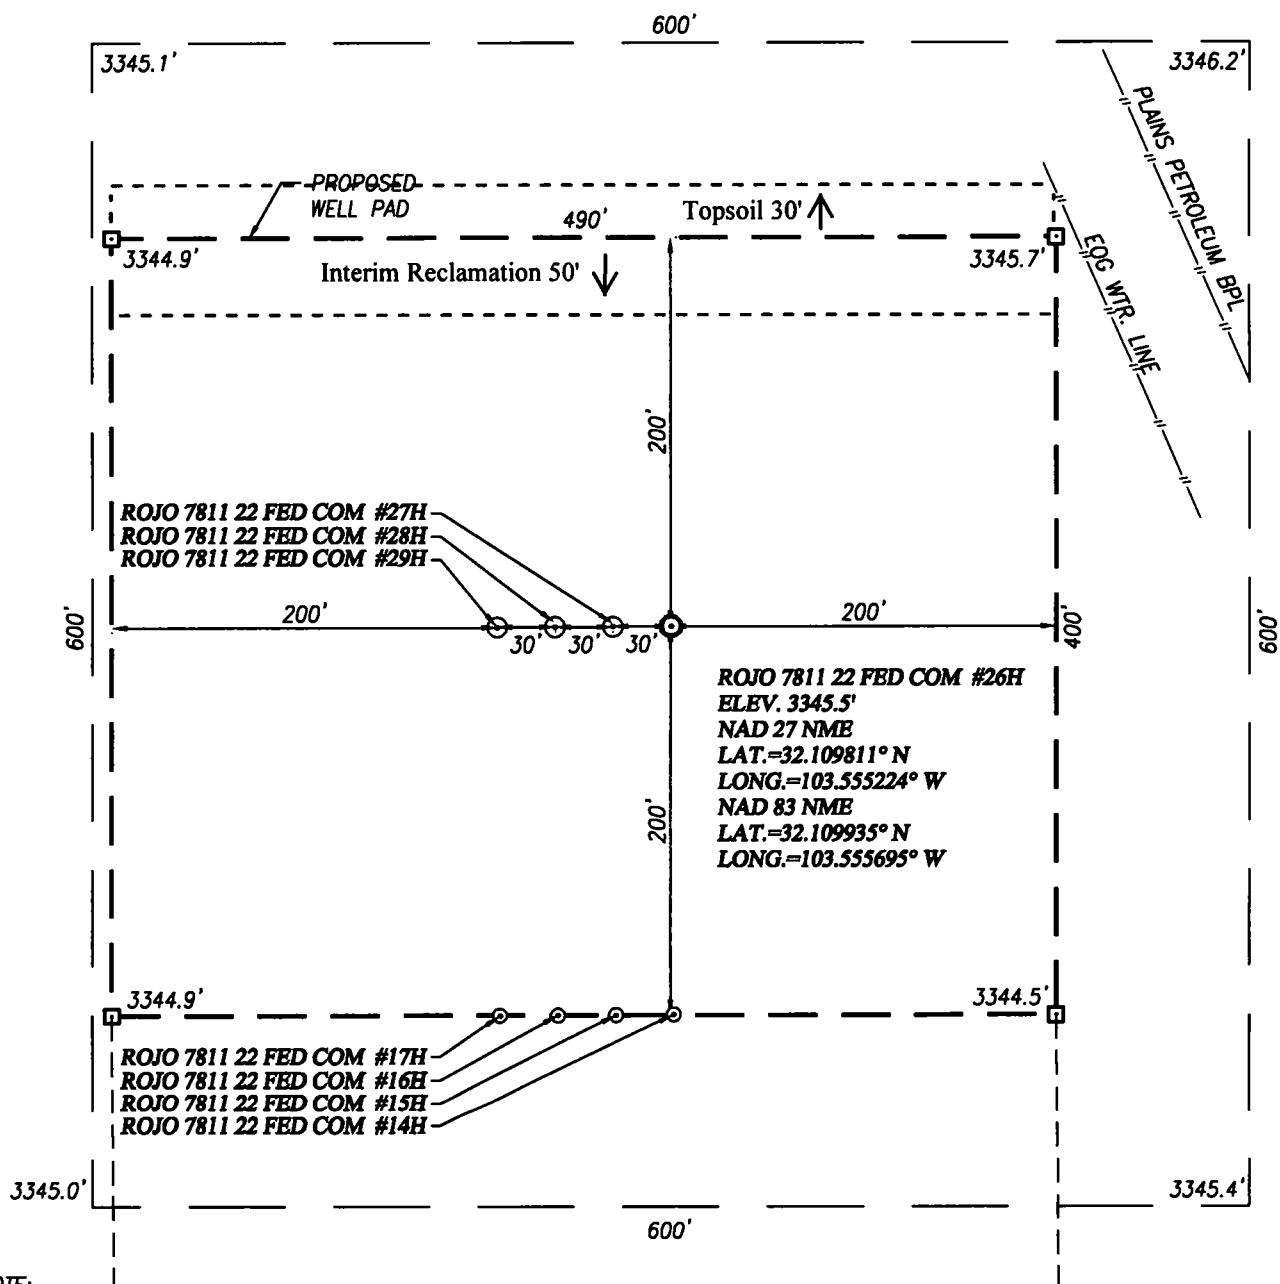

1) SEE "TOPOGRAPHICAL AND ACCESS ROAD MAP" FOR PROPOSED ROAD LOCATION.

DIRECTIONS TO LOCATION:

FROM THE INTERSECTION OF ST. HWY. 128 AND ST. HWY. 18 IN JAL. GO WESTERLY ON ST. HWY. 128 APPROX. 14 MILES, TURN LEFT ON CO. RD. J-2(BATTLE AXE). FOLLOW MENDERING CO. RD. J-2 SOUTHWEST APPROX. 13.5 MILES TO EL PASO N.G. ROAD; TURN RIGHT AND GO WEST ON EL PASO N.G. ROAD APPROX. 1.2 MILES, TURN RIGHT AND GO NORTH 3.0 MILES, TURN RIGHT AND GO EAST 0.6 MILES TO EXISTING PAD. WELL IS NORTHEAST 534 FEET.



BTA OIL PRODUCERS, LLC

**ROJO 7811 22 FED COM #26H WELL LOCATED 420 FEET FROM
THE SOUTH LINE AND 1250 FEET FROM THE EAST LINE OF
SECTION 22, TOWNSHIP 25 SOUTH, RANGE 33 EAST, N.M.P.M.,
LEA COUNTY, NEW MEXICO**



**PROVIDING SURVEYING SERVICES
SINCE 1946
JOHN WEST SURVEYING COMPANY
412 N. DAL PASO HOBBS, N.M. 88240
(575) 393-3117 www.jwsc.biz
TBPLS# 10021000**

Survey Date: 04/24/18

CAD Date: 05/24/18

Drawn By: LSL

W.O. No.: 18110472

Rev: .

Rel. W.O.:

Sheet 1 of 1

Section 1 - General

Would you like to address long-term produced water disposal? NO

Section 2 - Lined Pits

Would you like to utilize Lined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Lined pit PWD on or off channel:

Lined pit PWD discharge volume (bbl/day):

Lined pit specifications:

Pit liner description:

Pit liner manufacturers information:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Lined pit precipitated solids disposal schedule:

Lined pit precipitated solids disposal schedule attachment:

Lined pit reclamation description:

Lined pit reclamation attachment:

Leak detection system description:

Leak detection system attachment:

Lined pit Monitor description:

Lined pit Monitor attachment:

Lined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Lined pit bond number:

Lined pit bond amount:

Section 3 - Unlined Pits

Would you like to utilize Unlined Pit PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Unlined pit PWD on or off channel:

Unlined pit PWD discharge volume (bbl/day):

Unlined pit specifications:

Precipitated solids disposal:

Describe precipitated solids disposal:

Precipitated solids disposal permit:

Unlined pit precipitated solids disposal schedule:

Unlined pit precipitated solids disposal schedule attachment:

Unlined pit reclamation description:

Unlined pit reclamation attachment:

Unlined pit Monitor description:

Unlined pit Monitor attachment:

Do you propose to put the produced water to beneficial use?

Beneficial use user confirmation:

Estimated depth of the shallowest aquifer (feet):

Does the produced water have an annual average Total Dissolved Solids (TDS) concentration equal to or less than that of the existing water to be protected?

TDS lab results:

Geologic and hydrologic evidence:

State authorization:

Unlined Produced Water Pit Estimated percolation:

Unlined pit: do you have a reclamation bond for the pit?

Is the reclamation bond a rider under the BLM bond?

Unlined pit bond number:

Unlined pit bond amount:

Additional bond information attachment:

Section 4 - Injection

Would you like to utilize Injection PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Injection PWD discharge volume (bbl/day):

Injection well mineral owner:

Injection well number:

Injection well name:

Assigned injection well API number?

Injection well API number:

Injection well new surface disturbance (acres):

Minerals protection information:

Mineral protection attachment:

Underground Injection Control (UIC) Permit?

UIC Permit attachment:

Section 5 - Surface Discharge

Would you like to utilize Surface Discharge PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Surface discharge PWD discharge volume (bbl/day):

Surface Discharge NPDES Permit?

Surface Discharge NPDES Permit attachment:

Surface Discharge site facilities information:

Surface discharge site facilities map:

Section 6 - Other

Would you like to utilize Other PWD options? NO

Produced Water Disposal (PWD) Location:

PWD surface owner:

PWD disturbance (acres):

Other PWD discharge volume (bbl/day):

Other PWD type description:

Other PWD type attachment:

Have other regulatory requirements been met?

Other regulatory requirements attachment:

Bond Information

Federal/Indian APD: FED

BLM Bond number: NMB000849

BIA Bond number:

Do you have a reclamation bond? NO

Is the reclamation bond a rider under the BLM bond?

Is the reclamation bond BLM or Forest Service?

BLM reclamation bond number:

Forest Service reclamation bond number:

Forest Service reclamation bond attachment:

Reclamation bond number:

Reclamation bond amount:

Reclamation bond rider amount:

Additional reclamation bond information attachment:

APD ID: 10400035877

Submission Date: 11/08/2018

Operator Name: BTA OIL PRODUCERS LLC

Well Name: ROJO 7811 22 FEDERAL COM

Well Number: 26H

Show Final Text

Well Type: OIL WELL

Well Work Type: Drill

Section 1 - Geologic Formations

| Formation ID | Formation Name | Elevation | True Vertical Depth | Measured Depth | Lithologies | Mineral Resources | Producing Formation |
|--------------|----------------|-----------|---------------------|----------------|-------------|-------------------|---------------------|
| 1 | QUATERNARY | 3346 | 0 | 0 | ALLUVIUM | NONE | No |
| 2 | RUSTLER | 2328 | 1021 | 1021 | | NONE | No |
| 3 | TOP SALT | 1753 | 1593 | 1593 | | NONE | No |
| 4 | BASE OF SALT | -1504 | 4850 | 4850 | | NONE | No |
| 5 | DELAWARE | -1742 | 5088 | 5088 | | NATURAL GAS,OIL | No |
| 6 | BONE SPRING | -5846 | 9192 | 9192 | | NATURAL GAS,OIL | No |
| 7 | WOLFCAMP | -8924 | 12270 | 12270 | | NATURAL GAS,OIL | Yes |

Section 2 - Blowout Prevention

Pressure Rating (PSI): 10M

Rating Depth: 14000

Equipment: The blowout preventer equipment (BOP) shown in Exhibit A will consist of a (10M system) double ram type (10,000 psi WP) preventer and a bag-type (Hydril) preventer (5000 psi WP). Both units will be hydraulically operated and the ram type preventer will be equipped with blind rams on top and 5" drill pipe rams on bottom. The BOP's will be installed on the 13-3/8" surface casing and utilized continuously until total depth is reached. A 2" kill line and 3" choke line will be incorporated in the drilling spool below the ram-type BOP. A remote kill line will be used for the 10M system as per onshore order #2. Other accessory BOP equipment will include a Kelly cock, floor safety valve, choke lines, and choke manifold having a 10,000 psi WP rating. The 5M annular on the 10M system will be tested to 100% of rated working pressure.

Requesting Variance? YES

Variance request: A Choke Hose Variance is requested. See attached test chart and spec. 5M annular variance requested.

Testing Procedure: Pipe rams will be operated and checked each 24-hour period and each time the drill pipe is out of the hole. These functional tests will be documented on the daily driller's log. All BOP's and associated equipment will be tested as per BLM drilling Operations Order No. 2.

Choke Diagram Attachment:

10M_choke_mannifold_20190326075726.pdf

Choke_Hose___Test_Chart_and_Specs_20190326075727.pdf

BOP Diagram Attachment:

WFT Split Bowl (SB) Wellhead System (Continued)

- Align and level the production tree above the tubing hanger and carefully lower it over the tubing hanger neck, landing it on the ring gasket.

▲WARNING▲

Do NOT damage the hanger neck seals, as this will impair their sealing ability.

- Make up the connection using the appropriate studs and nuts, and tightening in an alternating cross pattern, as required by API 6A.

Testing the Production Tree Connection


- Locate the test port fitting on the outer diameter of the tubing head adapter flange. Remove the dust cap from the fitting.
- Attach a test pump to test port fitting, and open the pump.
- Pump clean test fluid into void area between flanges, test to 10,000 psi maximum.
- Hold and monitor pressure for **15 minutes or as required by the production supervisor**.
- Once a satisfactory test is achieved, carefully bleed off test pressure and remove the test pump.
- Attach a bleeder tool to the test port fitting, and open the tool to vent any remaining trapped pressure.


▲CAUTION▲

Always direct the bleeder tool away from people and property.

- Remove the bleeder tool and reinstall the dust cap on the test port fitting.

- Remove the type 'H' back pressure valve (BPV) through the production tree.
- Ensure that the well is safe and secure by closing all gate valves.

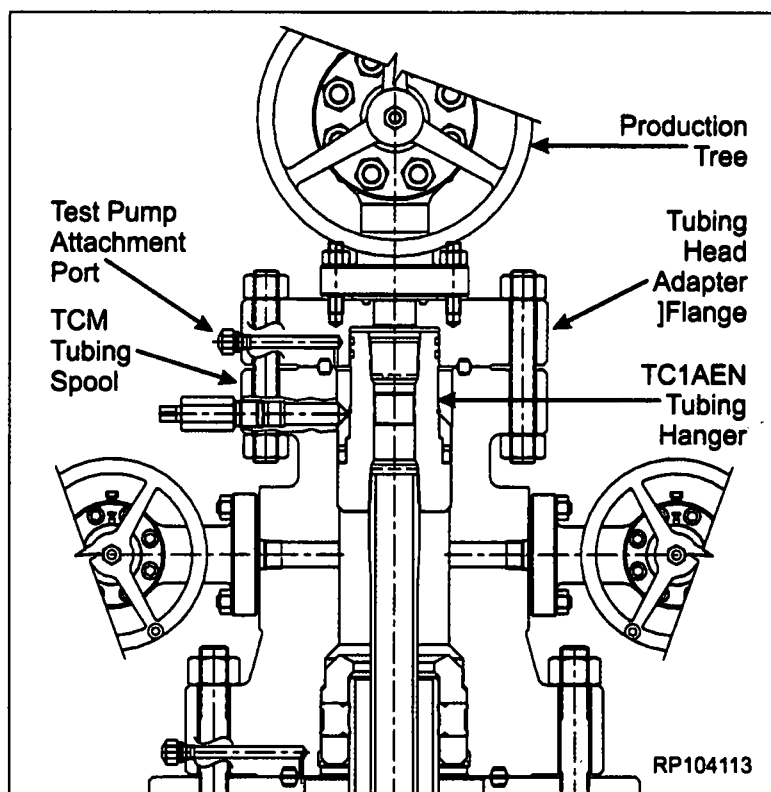

| | | | | | |
|--|-----------------------------|-------------------------|---------------|-----------------|----------------|
|  Weatherford 5-3-GL-GL-WES-00XXX | Field Service Manual | Prepared By: | Reviewed By: | Approved By: | SM-13-1 |
| | | <i>Marion Robertson</i> | Brad Franks | Manual Zaragoza | Rev WIP |
| | | Marion Robertson | Brad Franks | Manual Zaragoza | Page 24 of 24 |
| | | December 2014 | December 2014 | December 2014 | |
