

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER 1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other 1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No. [329952]	
2. Name of Operator [229137]		9. API Well No. 30-025-48322	
3a. Address		3b. Phone No. (include area code)	
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		10. Field and Pool, or Exploratory [96603] 11. Sec., T. R. M. or Blk. and Survey or Area	
14. Distance in miles and direction from nearest town or post office*		12. County or Parish	
13. State		15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	
16. No of acres in lease		17. Spacing Unit dedicated to this well	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.		19. Proposed Depth	
20. BLM/BIA Bond No. in file		21. Elevations (Show whether DF, KDB, RT, GL, etc.)	
22. Approximate date work will start*		23. Estimated duration	
24. Attachments The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable) 1. Well plat certified by a registered surveyor. 2. A Drilling Plan. 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). 5. Operator certification. 6. Such other site specific information and/or plans as may be requested by the BLM.			
25. Signature		Name (Printed/Typed)	
Title		Date	
Approved by (Signature)		Name (Printed/Typed)	
Title		Office	
Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. Conditions of approval, if any, are attached.			
Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.			

GCP Rec 12/29/2020

SL

(Continued on page 2)

**Approval Date: 12/18/2020**

01/06/2021

*(Instructions on page 2)

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM I: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

0. SHL: SESW / 225 FSL / 1485 FWL / TWSP: 23S / RANGE: 32E / SECTION: 35 / LAT: 32.2544955 / LONG: -103.6491604 (TVD: 0 feet, MD: 0 feet)
PPP: SWSW / 1 FSL / 1130 FWL / TWSP: 23S / RANGE: 32E / SECTION: 26 / LAT: 32.26839 / LONG: -103.6503012 (TVD: 10874 feet, MD: 15981 feet)
PPP: SWSW / 100 FSL / 1130 FWL / TWSP: 23S / RANGE: 32E / SECTION: 35 / LAT: 32.2541489 / LONG: -103.6503091 (TVD: 10738 feet, MD: 10800 feet)
BHL: NWNW / 50 FNL / 1130 FWL / TWSP: 23S / RANGE: 32E / SECTION: 26 / LAT: 32.2827749 / LONG: -103.6503003 (TVD: 10848 feet, MD: 21080 feet)

BLM Point of Contact

Name: Gavin Mickwee
Title: Land Law Examiner
Phone: (575) 234-5972
Email: gmickwee@blm.gov

CONFIDENTIAL

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL

**PECOS DISTRICT
SURFACE USE
CONDITIONS OF APPROVAL**

OPERATOR'S NAME:	COG Operating LLC
LEASE NO.:	Lease Number NMNM136217
COUNTY:	Lea

Wells:

Bedlington Fed Com 201H
Surface Hole Location: 425' FSL & 1795' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 726' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 202H
Surface Hole Location: 425' FSL & 1825' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 1518' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 301H
Surface Hole Location: 425' FSL & 1535' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 330' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 302h
Surface Hole Location: 425' FSL & 1565' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 1122' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 303H
Surface Hole Location: 425' FSL & 1595' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 1914' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 501H
Surface Hole Location: 225' FSL & 1455' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 330' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 502H
Surface Hole Location: 225' FSL & 1485' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 1130' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 503H
Surface Hole Location: 225' FSL & 1515' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 1930' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 701H
Surface Hole Location: 225' FSL & 1715' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 330' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 702H
Surface Hole Location: 225' FSL & 1745' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 995' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 703H
Surface Hole Location: 225' FSL & 1775' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 1650' FWL, Section 26, T. 23 S, R 32 E.

Bedlington Fed Com 704H
Surface Hole Location: 225' FSL & 1805' FWL, Section 35, T. 23 S., R. 32 E.
Bottom Hole Location: 50' FNL & 2310' FWL, Section 26, T. 23 S, R 32 E.

CTB Location: 900' FSL & 1900' FEL, Sec. 35-T23S-R32E

TABLE OF CONTENTS

Standard Conditions of Approval (COA) apply to this APD. If any deviations to these standards exist or special COAs are required, the section with the deviation or requirement will be checked below.

- ☐ **General Provisions**
- ☐ **Permit Expiration**
- ☐ **Archaeology, Paleontology, and Historical Sites**
- ☐ **Noxious Weeds**
- ☒ **Special Requirements**
 - Watershed
 - Lesser Prairie Chicken
 - VRM IV
- ☐ **Construction**
 - Notification
 - Topsoil
 - Closed Loop System
 - Federal Mineral Material Pits
 - Well Pads
 - Roads
- ☐ **Road Section Diagram**
- ☒ **Production (Post Drilling)**
 - Well Structures & Facilities
 - Pipelines
 - Electric Lines
- ☐ **Interim Reclamation**
- ☐ **Final Abandonment & Reclamation**

I. GENERAL PROVISIONS

The approval of the Application For Permit To Drill (APD) is in compliance with all applicable laws and regulations: 43 Code of Federal Regulations 3160, the lease terms, Onshore Oil and Gas Orders, Notices To Lessees, New Mexico Oil Conservation Division (NMOCD) Rules, National Historical Preservation Act As Amended, and instructions and orders of the Authorized Officer. Any request for a variance shall be submitted to the Authorized Officer on Form 3160-5, Sundry Notices and Report on Wells.

II. PERMIT EXPIRATION

If the permit terminates prior to drilling and drilling cannot be commenced within 60 days after expiration, an operator is required to submit Form 3160-5, Sundry Notices and Reports on Wells, requesting surface reclamation requirements for any surface disturbance. However, if the operator will be able to initiate drilling within 60 days after the expiration of the permit, the operator must have set the conductor pipe in order to allow for an extension of 60 days beyond the expiration date of the APD. (Filing of a Sundry Notice is required for this 60 day extension.)

III. ARCHAEOLOGICAL, PALEONTOLOGY & HISTORICAL SITES

Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See information below discussing NAGPRA.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

IV. NOXIOUS WEEDS

The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes the roads, pads, associated pipeline corridor, and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

SPECIAL REQUIREMENT(S)

Watershed:

The entire well pad(s) will be bermed to prevent oil, salt, and other chemical contaminants from leaving the well pad. The compacted berm shall be constructed at a minimum of 12 inches with impermeable mineral material (e.g. caliche). Topsoil shall not be used to construct the berm. No water flow from the uphill side(s) of the pad shall be allowed to enter the well pad. The integrity of the berm shall be maintained around the surfaced pad throughout the life of the well and around the downsized pad after interim reclamation has been completed. Any water erosion that may occur due to the construction of the well pad during the life of the well will be quickly corrected and proper measures will be taken to prevent future erosion. Stockpiling of topsoil is required. The topsoil shall be stockpiled in an appropriate location to prevent loss of soil due to water or wind erosion and not used for berming or erosion control. If fluid collects within the bermed area, the fluid must be vacuumed into a safe container and disposed of properly at a state approved facility.

TANK BATTERY:

Tank battery locations will be lined and bermed. A 20 mil permanent liner will be installed with a 4 oz. felt backing to prevent tears or punctures. Tank battery berms must be large enough to contain 1 ½ times the content of the largest tank or 24 hour production, whichever is greater. Automatic shut off, check valves, or similar systems will be installed for tanks to minimize the effects of catastrophic line failures used in production or drilling.

BURIED/SURFACE LINE(S):

When crossing ephemeral drainages the pipeline(s) will be buried to a minimum depth of 48 inches from the top of pipe to ground level. Erosion control methods such as gabions and/or rock aprons should be placed on both up and downstream sides of the pipeline crossing. In addition, curled (weed free) wood/straw fiber wattles/logs and/or silt fences should be placed on the downstream side for sediment control during construction and maintained until soils and vegetation have stabilized. Water bars should be placed within the ROW to divert and dissipate surface runoff. A pipeline access road is not permitted to cross these ephemeral drainages. Traffic should be diverted to a preexisting route. Additional seeding may be required in floodplains and drainages to restore energy dissipating vegetation.

Prior to pipeline installation/construction a leak detection plan will be developed. The method(s) could incorporate gauges to detect pressure drops, situating valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present.

The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.

ELECTRIC LINE(S):

Any water erosion that may occur due to the construction of overhead electric line and during the life of the power line will be quickly corrected and proper measures will be taken to prevent future erosion. A power pole should not be placed in drainages, playas, wetlands, riparian areas, or floodplains and must span across the features at a distance away that would not promote further erosion.

Lesser Prairie Chicken:**Timing Limitation Stipulation/Condition of Approval for Lesser Prairie-Chicken:**

Oil and gas activities including 3-D geophysical exploration, and drilling will not be allowed in lesser prairie-chicken habitat during the period from March 1st through June 15th annually. During that period, other activities that produce noise or involve human activity, such as the maintenance of oil and gas facilities, geophysical exploration other than 3-D operations, and pipeline, road, and well pad construction, will be allowed except between 3:00 am and 9:00 am. The 3:00 am to 9:00 am restriction will not apply to normal, around-the-clock operations, such as venting, flaring, or pumping, which do not require a human presence during this period. Additionally, no new drilling will be allowed within up to 200 meters of leks known at the time of permitting. Normal vehicle use on existing roads will not be restricted. Exhaust noise from pump jack engines must be muffled or otherwise controlled so as not to exceed 75 db measured at 30 ft. from the source of the noise.

Timing Limitation Exceptions:

The Carlsbad Field Office will publish an annual map of where the LPC timing and noise stipulations and conditions of approval (Limitations) will apply for the identified year (between March 1 and June 15) based on the latest survey information. The LPC Timing Area map will identify areas which are Habitat Areas (HA), Isolated Population Area (IPA), and Primary Population Area (PPA). The LPC Timing Area map will also have an area in red crosshatch. The red crosshatch area is the only area where an operator is required to submit a request for exception to the LPC Limitations. If an operator is operating outside the red crosshatch area, the LPC Limitations do not apply for that year and an exception to LPC Limitations is not required.

Ground-level Abandoned Well Marker to avoid raptor perching:

Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well. For more installation details, contact the Carlsbad Field Office at 575-234-5972.

VRM IV:

Above-ground structures including meter housing that are not subject to safety requirements are painted a flat non-reflective paint color, Shale Green from the BLM Standard Environmental Color Chart (CC-001: June 2008).

Short-term mitigation measures include painting all above-ground structures that are not subject to safety requirements (including meter housing) Shale Green, which is a flat non-reflective paint color listed in the BLM Standard Environmental Color Chart (CC-001: June 2013). Long-term mitigation measures include the removal of wells and associated infrastructure following abandonment (end of cost-effective production). Previously impacted areas will be reclaimed by removing structures and caliche pads, returning disturbed areas to natural grade, and revegetating with an approved BLM seed mixture; thereby eliminating visual impacts.

V. CONSTRUCTION**A. NOTIFICATION**

The BLM shall administer compliance and monitor construction of the access road and well pad. Notify the Carlsbad Field Office at (575) 234-5909 at least 3 working days prior to commencing construction of the access road and/or well pad.

When construction operations are being conducted on this well, the operator shall have the approved APD and Conditions of Approval (COA) on the well site and they shall be made available upon request by the Authorized Officer.

B. TOPSOIL

The operator shall strip the top portion of the soil (root zone) from the entire well pad area and stockpile the topsoil along the edge of the well pad as depicted in the APD. The root zone is typically six (6) inches in depth. All the stockpiled topsoil will be redistributed over the interim reclamation areas. Topsoil shall not be used for berming the pad or facilities. For final reclamation, the topsoil shall be spread over the entire pad area for seeding preparation.

Other subsoil (below six inches) stockpiles must be completely segregated from the topsoil stockpile. Large rocks or subsoil clods (not evident in the surrounding terrain) must be buried within the approved area for interim and final reclamation.

C. CLOSED LOOP SYSTEM

Tanks are required for drilling operations: No Pits.

The operator shall properly dispose of drilling contents at an authorized disposal site.

D. FEDERAL MINERAL MATERIALS PIT

Payment shall be made to the BLM prior to removal of any federal mineral materials. Call the Carlsbad Field Office at (575) 234-5972.

E. WELL PAD SURFACING

Surfacing of the well pad is not required.

If the operator elects to surface the well pad, the surfacing material may be required to be removed at the time of reclamation. The well pad shall be constructed in a manner which creates the smallest possible surface disturbance, consistent with safety and operational needs.

F. EXCLOSURE FENCING (CELLARS & PITS)**Exclosure Fencing**

The operator will install and maintain exclosure fencing for all open well cellars to prevent access to public, livestock, and large forms of wildlife before and after drilling operations until the pit is free of fluids and the operator initiates backfilling. (For examples of exclosure fencing design, refer to BLM's Oil and Gas Gold Book, Exclosure Fence Illustrations, Figure 1, Page 18.)

G. ON LEASE ACCESS ROADS**Road Width**

The access road shall have a driving surface that creates the smallest possible surface disturbance and does not exceed fourteen (14) feet in width. The maximum width of surface disturbance, when constructing the access road, shall not exceed twenty-five (25) feet.

Surfacing

Surfacing material is not required on the new access road driving surface. If the operator elects to surface the new access road or pad, the surfacing material may be required to be removed at the time of reclamation.

Where possible, no improvements should be made on the unsurfaced access road other than to remove vegetation as necessary, road irregularities, safety issues, or to fill low areas that may sustain standing water.

The Authorized Officer reserves the right to require surfacing of any portion of the access road at any time deemed necessary. Surfacing may be required in the event the road deteriorates, erodes, road traffic increases, or it is determined to be beneficial for future field development. The surfacing depth and type of material will be determined at the time of notification.

Crowning

Crowning shall be done on the access road driving surface. The road crown shall have a grade of approximately 2% (i.e., a 1" crown on a 14' wide road). The road shall conform to Figure 1; cross section and plans for typical road construction.

Ditching

Ditching shall be required on both sides of the road.

Turnouts


Vehicle turnouts shall be constructed on the road. Turnouts shall be intervisible with interval spacing distance less than 1000 feet. Turnouts shall conform to Figure 1; cross section and plans for typical road construction.

Drainage

Drainage control systems shall be constructed on the entire length of road (e.g. ditches, sidehill outslowing and insloping, lead-off ditches, culvert installation, and low water crossings).

A typical lead-off ditch has a minimum depth of 1 foot below and a berm of 6 inches above natural ground level. The berm shall be on the down-slope side of the lead-off ditch.

Cross Section of a Typical Lead-off Ditch



All lead-off ditches shall be graded to drain water with a 1 percent minimum to 3 percent maximum ditch slope. The spacing interval are variable for lead-off ditches and shall be determined according to the formula for spacing intervals of lead-off ditches, but may be amended depending upon existing soil types and centerline road slope (in %);

Formula for Spacing Interval of Lead-off Ditches

Example - On a 4% road slope that is 400 feet long, the water flow shall drain water into a lead-off ditch. Spacing interval shall be determined by the following formula:

$$400 \text{ foot road with } 4\% \text{ road slope: } \frac{400'}{4\%} + 100' = 200' \text{ lead-off ditch interval}$$

Cattle guards

An appropriately sized cattle guard sufficient to carry out the project shall be installed and maintained at fence/road crossings. Any existing cattle guards on the access road route shall be repaired or replaced if they are damaged or have deteriorated beyond practical use. The operator shall be responsible for the condition of the existing cattle guards that are in place and are utilized during lease operations.

Fence Requirement

Where entry is granted across a fence line, the fence shall be braced and tied off on both sides of the passageway prior to cutting. The operator shall notify the private surface landowner or the grazing allotment holder prior to crossing any fences.

Public Access

Public access on this road shall not be restricted by the operator without specific written approval granted by the Authorized Officer.

Construction Steps

1. Salvage topsoil
2. Construct road

3. Redistribute topsoil
4. Revegetate slopes

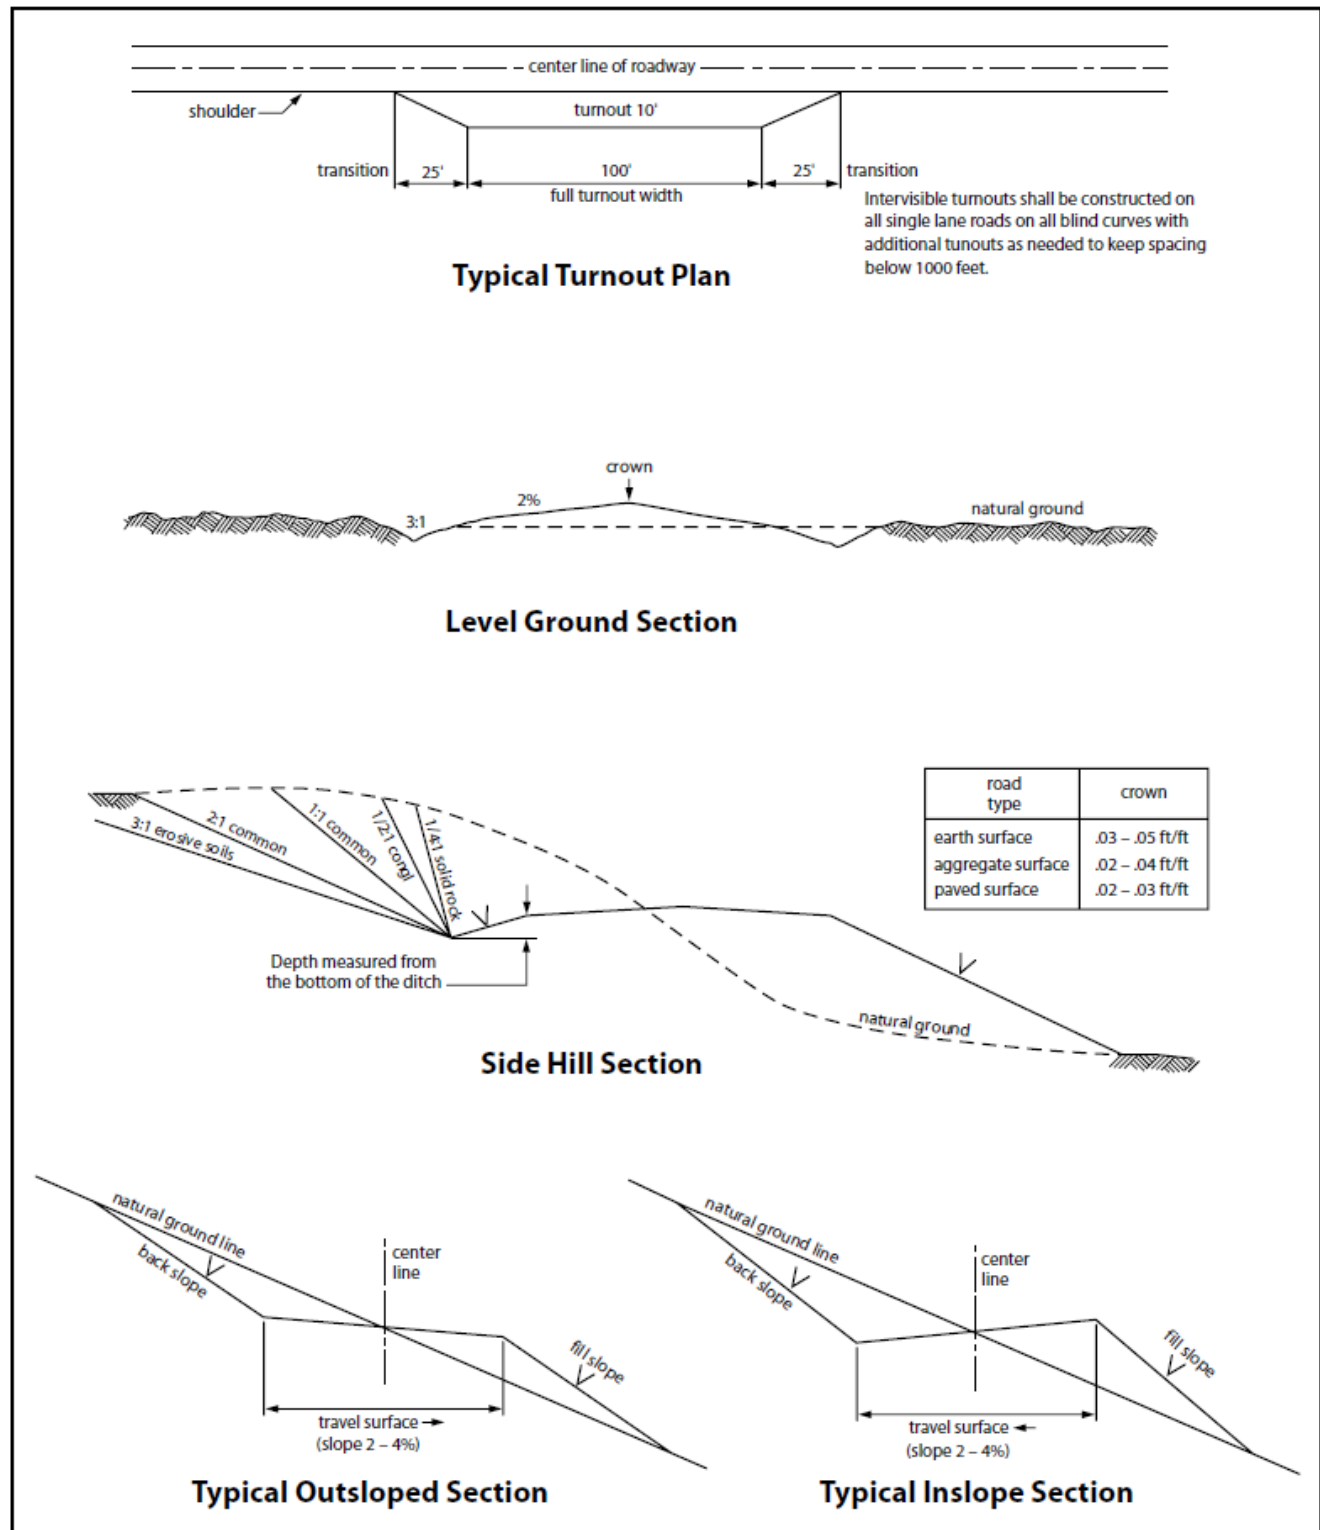


Figure 1. Cross-sections and plans for typical road sections representative of BLM resource or FS local and higher-class roads.

VI. PRODUCTION (POST DRILLING)

A. WELL STRUCTURES & FACILITIES

Placement of Production Facilities

Production facilities should be placed on the well pad to allow for maximum interim recontouring and revegetation of the well location.

Exclosure Netting (Open-top Tanks)

Immediately following active drilling or completion operations, the operator will take actions necessary to prevent wildlife and livestock access, including avian wildlife, to all open-topped tanks that contain or have the potential to contain salinity sufficient to cause harm to wildlife or livestock, hydrocarbons, or Resource Conservation and Recovery Act of 1976-exempt hazardous substances. At a minimum, the operator will net, screen, or cover open-topped tanks to exclude wildlife and livestock and prevent mortality. If the operator uses netting, the operator will cover and secure the open portion of the tank to prevent wildlife entry. The operator will net, screen, or cover the tanks until the operator removes the tanks from the location or the tanks no longer contain substances that could be harmful to wildlife or livestock. Use a maximum netting mesh size of 1 ½ inches. The netting must not be in contact with fluids and must not have holes or gaps.

Chemical and Fuel Secondary Containment and Exclosure Screening

The operator will prevent all hazardous, poisonous, flammable, and toxic substances from coming into contact with soil and water. At a minimum, the operator will install and maintain an impervious secondary containment system for any tank or barrel containing hazardous, poisonous, flammable, or toxic substances sufficient to contain the contents of the tank or barrel and any drips, leaks, and anticipated precipitation. The operator will dispose of fluids within the containment system that do not meet applicable state or U. S. Environmental Protection Agency livestock water standards in accordance with state law; the operator must not drain the fluids to the soil or ground. The operator will design, construct, and maintain all secondary containment systems to prevent wildlife and livestock exposure to harmful substances. At a minimum, the operator will install effective wildlife and livestock exclosure systems such as fencing, netting, expanded metal mesh, lids, and grate covers. Use a maximum netting mesh size of 1 ½ inches.

Open-Vent Exhaust Stack Exclosures

The operator will construct, modify, equip, and maintain all open-vent exhaust stacks on production equipment to prevent birds and bats from entering, and to discourage perching, roosting, and nesting. (*Recommended exclosure structures on open-vent exhaust stacks are in the shape of a cone.*) Production equipment includes, but may not be limited to, tanks, heater-treaters, separators, dehydrators, flare stacks, in-line units, and compressor mufflers.

Containment Structures

Proposed production facilities such as storage tanks and other vessels will have a secondary containment structure that is constructed to hold the capacity of 1.5 times the largest tank, plus freeboard to account for precipitation, unless more stringent protective requirements are deemed necessary.

Painting Requirement

All above-ground structures including meter housing that are not subject to safety requirements shall be painted a flat non-reflective paint color, **Shale Green** from the BLM Standard Environmental Color Chart (CC-001: June 2008).

B. PIPELINES

- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, passages, or voids are intersected by trenching, and no pipe will be laid in the trench at that point until clearance has been issued by the Authorized Officer.
- If a void is encountered alignments may be rerouted to avoid the karst feature and lessen; the potential of subsidence or collapse of karst features, buildup of toxic or combustible gas, or other possible impacts to cave and karst resources from the buried pipeline.
- Special restoration stipulations or realignment may be required at such intersections, if any.
- A leak detection plan will be submitted to the BLM Carlsbad Field Office for approval prior to pipeline installation. The method could incorporate gauges to detect pressure drops, siting valves and lines so they can be visually inspected periodically or installing electronic sensors to alarm when a leak is present. The leak detection plan will incorporate an automatic shut off system that will be installed for proposed pipelines to minimize the effects of an undesirable event.
- Regular monitoring is required to quickly identify leaks for their immediate and proper treatment.
- All spills or leaks will be reported to the BLM immediately for their immediate and proper treatment.

BURIED PIPELINE STIPULATIONS

A copy of the application (Grant, APD, or Sundry Notice) and attachments, including conditions of approval, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The Holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The Holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the

Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.

4. If, during any phase of the construction, operation, maintenance, or termination of the pipeline, any oil or other pollutant should be discharged from the pipeline system, impacting Federal lands, the control and total removal, disposal, and cleaning up of such oil or other pollutant, wherever found, shall be the responsibility of holder, regardless of fault. Upon failure of holder to control, dispose of, or clean up such discharge on or affecting Federal lands, or to repair all damages resulting therefrom, on the Federal lands, the Authorized Officer may take such measures as he deems necessary to control and clean up the discharge and restore the area, including where appropriate, the aquatic environment and fish and wildlife habitats, at the full expense of the holder. Such action by the Authorized Officer shall not relieve holder of any responsibility as provided herein.

5. All construction and maintenance activity will be confined to the authorized right-of-way.

6. The pipeline will be buried with a minimum cover of 36 inches between the top of the pipe and ground level.

7. The maximum allowable disturbance for construction in this right-of-way will be 30 feet:

- Blading of vegetation within the right-of-way will be allowed: maximum width of blading operations will not exceed 20 feet. The trench is included in this area. (*Blading is defined as the complete removal of brush and ground vegetation.*)
- Clearing of brush species within the right-of-way will be allowed: maximum width of clearing operations will not exceed 30 feet. The trench and bladed area are included in this area. (*Clearing is defined as the removal of brush while leaving ground vegetation (grasses, weeds, etc.) intact. Clearing is best accomplished by holding the blade 4 to 6 inches above the ground surface.*)
- The remaining area of the right-of-way (if any) shall only be disturbed by compressing the vegetation. (*Compressing can be caused by vehicle tires, placement of equipment, etc.*)

8. The holder shall stockpile an adequate amount of topsoil where blading is allowed. The topsoil to be stripped is approximately 6 inches in depth. The topsoil will be segregated from other spoil piles from trench construction. The topsoil will be evenly distributed over the bladed area for the preparation of seeding.

9. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting of the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

10. Vegetation, soil, and rocks left as a result of construction or maintenance activity will be randomly scattered on this right-of-way and will not be left in rows, piles, or berms, unless otherwise approved by the Authorized Officer. The entire right-of-way shall be recontoured to match the surrounding landscape. The backfilled soil shall be compacted and a 6 inch berm will be left over the ditch line to allow for settling back to grade.

11. In those areas where erosion control structures are required to stabilize soil conditions, the holder will install such structures as are suitable for the specific soil conditions being encountered and which are in accordance with sound resource management practices.

12. The holder will reseed all disturbed areas. Seeding will be done according to the attached seeding requirements, using the following seed mix.

- | | |
|--|--|
| ☐ seed mixture 1 | ☐ seed mixture 3 |
| ☒ seed mixture 2 | ☐ seed mixture 4 |
| ☐ seed mixture 2/LPC | ☐ Aplomado Falcon Mixture |

13. All above-ground structures not subject to safety requirements shall be painted by the holder to blend with the natural color of the landscape. The paint used shall be color which simulates "Standard Environmental Colors" – **Shale Green**, Munsell Soil Color No. 5Y 4/2.

14. The pipeline will be identified by signs at the point of origin and completion of the right-of-way and at all road crossings. At a minimum, signs will state the holder's name, BLM serial number, and the product being transported. All signs and information thereon will be posted in a permanent, conspicuous manner, and will be maintained in a legible condition for the life of the pipeline.

15. The holder shall not use the pipeline route as a road for purposes other than routine maintenance as determined necessary by the Authorized Officer in consultation with the holder before maintenance begins. The holder will take whatever steps are necessary to ensure that the pipeline route is not used as a roadway. As determined necessary during the life of the pipeline, the Authorized Officer may ask the holder to construct temporary deterrence structures.

16. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 17 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

17. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

18. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

19. The operator shall be held responsible if noxious weeds become established within the areas of operations. Weed control shall be required on the disturbed land where noxious weeds exist, which includes associated roads, pipeline corridor and adjacent land affected by the establishment of weeds due to this action. The operator shall consult with the Authorized Officer for acceptable weed control methods, which include following EPA and BLM requirements and policies.

20. Escape Ramps - The operator will construct and maintain pipeline/utility trenches [that are not otherwise fenced, screened, or netted] to prevent livestock, wildlife, and humans from becoming entrapped. At a minimum, the operator will construct and maintain escape ramps, ladders, or other methods of avian and terrestrial wildlife escape in the trenches according to the following criteria:

- a. Any trench left open for eight (8) hours or less is not required to have escape ramps; however, before the trench is backfilled, the contractor/operator shall inspect the trench for wildlife, remove all trapped wildlife, and release them at least 100 yards from the trench.

- b. For trenches left open for eight (8) hours or more, earthen escape ramps (built at no more than a 30 degree slope and spaced no more than 500 feet apart) shall be placed in the trench.

C. ELECTRIC LINES

- Smaller powerlines will be routed around sinkholes and other karst features to avoid or lessen the possibility of encountering near surface voids and to minimize changes to runoff or possible leaks and spills from entering karst systems. Larger powerlines will adjust their pole spacing to avoid cave and karst features.
- The BLM, Carlsbad Field Office, will be informed immediately if any subsurface drainage channels, cave passages, or voids are penetrated during construction.
- No further construction will be done until clearance has been issued by the Authorized Officer.
- Special restoration stipulations or realignment may be required.

STANDARD STIPULATIONS FOR OVERHEAD ELECTRIC DISTRIBUTION LINES

A copy of the grant and attachments, including stipulations, survey plat and/or map, will be on location during construction. BLM personnel may request to you a copy of your permit during construction to ensure compliance with all stipulations.

Holder agrees to comply with the following stipulations to the satisfaction of the Authorized Officer:

1. The holder shall indemnify the United States against any liability for damage to life or property arising from the occupancy or use of public lands under this grant.
2. The holder shall comply with all applicable Federal laws and regulations existing or hereafter enacted or promulgated. In any event, the holder shall comply with the Toxic Substances Control Act of 1976 as amended, 15 USC 2601 et seq. (1982) with regards to any toxic substances that are used, generated by or stored on the right-of-way or on facilities authorized under this right-of-way grant. (See 40 CFR, Part 702-799 and especially, provisions on polychlorinated biphenyls, 40 CFR 761.1-761.193.) Additionally, any release of toxic substances (leaks, spills, etc.) in excess of the reportable quantity established by 40 CFR, Part 117 shall be reported as required by the Comprehensive Environmental Response, Compensation, and Liability Act, section 102b. A copy of any report required or requested by any Federal agency or State government as a result of a reportable release or spill of any toxic substances shall be furnished to the authorized officer concurrent with the filing of the reports to the involved Federal agency or State government.
3. The holder agrees to indemnify the United States against any liability arising from the release of any hazardous substance or hazardous waste (as these terms are defined in the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. 9601, et seq. or the Resource Conservation and Recovery Act, 42 U.S.C. 6901, et seq.) on the Right-of-Way (unless the release or threatened release is wholly unrelated to the Right-of-Way holder's activity on the Right-of-Way), or resulting from the activity of the Right-of-Way holder on the Right-of-Way. This agreement applies without regard to whether a release is caused by the holder, its agent, or unrelated third parties.
4. There will be no clearing or blading of the right-of-way unless otherwise agreed to in writing by the Authorized Officer.
5. Power lines shall be constructed and designed in accordance to standards outlined in "Suggested Practices for Avian Protection on Power lines: The State of the Art in 2006" Edison Electric Institute, APLIC, and the California Energy Commission 2006 . The holder shall assume

the burden and expense of proving that pole designs not shown in the above publication deter raptor perching, roosting, and nesting. Such proof shall be provided by a raptor expert approved by the Authorized Officer. The BLM reserves the right to require modification or additions to all powerline structures placed on this right-of-way, should they be necessary to ensure the safety of large perching birds. Such modifications and/or additions shall be made by the holder without liability or expense to the United States.

Raptor deterrence will consist of but not limited to the following: triangle perch discouragers shall be placed on each side of the cross arms and a nonconductive perching deterrence shall be placed on all vertical poles that extend past the cross arms.

6. The holder shall minimize disturbance to existing fences and other improvements on public lands. The holder is required to promptly repair improvements to at least their former state. Functional use of these improvements will be maintained at all times. The holder will contact the owner of any improvements prior to disturbing them. When necessary to pass through a fence line, the fence shall be braced on both sides of the passageway prior to cutting the fence. No permanent gates will be allowed unless approved by the Authorized Officer.

7. The BLM serial number assigned to this authorization shall be posted in a permanent, conspicuous manner where the power line crosses roads and at all serviced facilities. Numbers will be at least two inches high and will be affixed to the pole nearest the road crossing and at the facilities served.

8. Upon cancellation, relinquishment, or expiration of this grant, the holder shall comply with those abandonment procedures as prescribed by the Authorized Officer.

9. All surface structures (poles, lines, transformers, etc.) shall be removed within 180 days of abandonment, relinquishment, or termination of use of the serviced facility or facilities or within 180 days of abandonment, relinquishment, cancellation, or expiration of this grant, whichever comes first. This will not apply where the power line extends service to an active, adjoining facility or facilities.

10. Any cultural resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

OR

If the entire project is covered under the Permian Basin Programmatic Agreement (cultural resources only):

The proponent has contributed funds commensurate to the undertaking into an account for offsite mitigation. Participation in the PA serves as mitigation for the effects of this project on cultural resources. If any human skeletal remains, funerary objects, sacred objects, or objects of cultural patrimony are discovered at any time during construction, all construction activities shall halt and the BLM will be notified as soon as possible within 24 hours. Work shall not resume until a Notice to Proceed is issued by the BLM. See Stipulation 11 for more information.

If the proposed project is split between a Class III inventory and a Permian Basin Programmatic Agreement contribution, the portion of the project covered under Class III inventory should default to the first paragraph stipulations.

11. The holder is hereby obligated to comply with procedures established in the Native American Graves Protection and Repatriation Act (NAGPRA) to protect such cultural items as human remains, associated funerary objects, sacred objects, and objects of cultural patrimony discovered inadvertently during the course of project implementation. In the event that any of the cultural items listed above are discovered during the course of project work, the proponent shall immediately halt the disturbance and contact the BLM within 24 hours for instructions. The proponent or initiator of any project shall be held responsible for protecting, evaluating, reporting, excavating, treating, and disposing of these cultural items according to the procedures established by the BLM in consultation with Indian Tribes."

12. Any paleontological resource (historic or prehistoric site or object) discovered by the holder, or any person working on the holder's behalf, on public or Federal land shall be immediately reported to the Authorized Officer. The holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the Authorized Officer. An evaluation of the discovery will be made by the Authorized Officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder will be responsible for the cost of evaluation and any decision as to the proper mitigation measures will be made by the Authorized Officer after consulting with the holder.

13. Special Stipulations:

For reclamation remove poles, lines, transformer, etc. and dispose of properly.
Fill in any holes from the poles removed.

VII. INTERIM RECLAMATION

During the life of the development, all disturbed areas not needed for active support of production operations should undergo interim reclamation in order to minimize the environmental impacts of development on other resources and uses.

Within six (6) months of well completion, operators should work with BLM surface management specialists (Jim Amos: 575-234-5909) to devise the best strategies to reduce the size of the location. Interim reclamation should allow for remedial well operations, as well as safe and efficient removal of oil and gas.

During reclamation, the removal of caliche is important to increasing the success of revegetating the site. Removed caliche that is free of contaminants may be used for road repairs, fire walls or for building other roads and locations. In order to operate the well or complete workover operations, it may be necessary to drive, park and operate on restored interim vegetation within the previously disturbed area. Disturbing revegetated areas for production or workover operations will be allowed. If there is significant disturbance and loss of vegetation, the area will need to be revegetated. Communicate with the appropriate BLM office for any exceptions/exemptions if needed.

All disturbed areas after they have been satisfactorily prepared need to be reseeded with the seed mixture provided below.

Upon completion of interim reclamation, the operator shall submit a Sundry Notices and Reports on Wells, Subsequent Report of Reclamation (Form 3160-5).

VIII. FINAL ABANDONMENT & RECLAMATION

At final abandonment, well locations, production facilities, and access roads must undergo "final" reclamation so that the character and productivity of the land are restored.

Earthwork for final reclamation must be completed within six (6) months of well plugging. All pads, pits, facility locations and roads must be reclaimed to a satisfactory revegetated, safe, and stable condition, unless an agreement is made with the landowner or BLM to keep the road and/or pad intact.

After all disturbed areas have been satisfactorily prepared, these areas need to be revegetated with the seed mixture provided below. Seeding should be accomplished by drilling on the contour whenever practical or by other approved methods. Seeding may need to be repeated until revegetation is successful, as determined by the BLM.

Operators shall contact a BLM surface protection specialist prior to surface abandonment operations for site specific objectives (Jim Amos: 575-234-5909).

Ground-level Abandoned Well Marker to avoid raptor perching: Upon the plugging and subsequent abandonment of the well, the well marker will be installed at ground level on a plate containing the pertinent information for the plugged well.

Seed Mixture 2, for Sandy Sites

The holder shall seed all disturbed areas with the seed mixture listed below. The seed mixture shall be planted in the amounts specified in pounds of pure live seed (PLS)* per acre. There shall be no primary or secondary noxious weeds in the seed mixture. Seed will be tested and the viability testing of seed will be done in accordance with State law (s) and within nine (9) months prior to purchase. Commercial seed will be either certified or registered seed. The seed container will be tagged in accordance with State law(s) and available for inspection by the authorized officer.

Seed will be planted using a drill equipped with a depth regulator to ensure proper depth of planting where drilling is possible. The seed mixture will be evenly and uniformly planted over the disturbed area (smaller/heavier seeds have a tendency to drop the bottom of the drill and are planted first). The holder shall take appropriate measures to ensure this does not occur. Where drilling is not possible, seed will be broadcast and the area shall be raked or chained to cover the seed. When broadcasting the seed, the pounds per acre are to be doubled. The seeding will be repeated until a satisfactory stand is established as determined by the authorized officer. Evaluation of growth will not be made before completion of at least one full growing season after seeding.

Species to be planted in pounds of pure live seed* per acre:

Species

	<u>lb/acre</u>
Sand dropseed (<i>Sporobolus cryptandrus</i>)	1.0
Sand love grass (<i>Eragrostis trichodes</i>)	1.0
Plains bristlegrass (<i>Setaria macrostachya</i>)	2.0

*Pounds of pure live seed:

Pounds of seed x percent purity x percent germination = pounds pure live seed

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	COG Operating LLC
LEASE NO.:	NMNM-136217
WELL NAME & NO.:	Bedlington Federal Com 502H
SURFACE HOLE FOOTAGE:	0225' FSL & 1485' FWL
BOTTOM HOLE FOOTAGE:	0050' FNL & 1130' FWL Sec. 26, T.23 S., R.32 E.
LOCATION:	Section 35, T.23 S., R.32 E., NMPM
COUNTY:	Lea County, New Mexico

COA

H2S	☐ Yes	☒ No	
Potash	☒ None	☐ Secretary	☐ R-111-P
Cave/Karst Potential	☒ Low	☐ Medium	☐ High
Cave/Karst Potential	☐ Critical		
Variance	☐ None	☒ Flex Hose	☐ Other
Wellhead	☒ Conventional	☐ Multibowl	☐ Both
Other	☐ 4 String Area	☐ Capitan Reef	☐ WIPP
Other	☐ Fluid Filled	☐ Cement Squeeze	☐ Pilot Hole
Special Requirements	☐ Water Disposal	☒ COM	☐ Unit

Possible water flows in the Salado and Castile.

Possible lost circulation in the Rustler, Red Beds, and Delaware.

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **1220** feet (a minimum of 25 feet (Lea County) into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing is:
 - Cement to surface. If cement does not circulate see B.1.a, c-d above.
3. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1. Variance approved to use flex line from BOP to choke manifold. Manufacturer's specification to be readily available. No external damage to flex line. Flex line to be installed as straight as possible (no hard bends).
2. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M)** psi.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record), or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.
- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
4. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
5. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
6. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).
 - b. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).

- c. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- d. The results of the test shall be reported to the appropriate BLM office.
- e. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- f. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- g. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.

JAM 10222020

District I1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720District II811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720District III1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170District IV1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

☐ AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

1 API Number 30-025-48322	2 Pool Code 96603	3 Pool Name Triste Draw; Bone Spring
4 Property Code [329952]	5 Property Name BEDLINGTON FEDERAL COM	
7 OGRID No. 229137	8 Operator Name COG OPERATING LLC	6 Well Number 502H
		9 Elevation 3622'

10 Surface Location

U/L or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
N	35	23-S	32-E		225'	SOUTH	1485'	WEST	LEA

11 Bottom Hole Location If Different From Surface

U/L or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
D	26	23-S	32-E		50'	NORTH	1130'	WEST	LEA

12 Dedicated Acres 640	13 Joint or Infill	14 Consolidation Code	15 Order No.
----------------------------------	---------------------------	------------------------------	---------------------

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

CORNER DATA
NEW MEXICO EAST - NAD 83

A - FOUND IRON PIPE W/ BRASS CAP
N:467315.98' E:751289.08'
B - FOUND IRON PIPE W/ BRASS CAP
N:467344.78' E:753927.62'
C - FOUND IRON PIPE W/ BRASS CAP
N:467373.32' E:756564.67'
D - FOUND IRON PIPE W/ BRASS CAP
N:464728.99' E:756583.47'
E - FOUND IRON PIPE W/ BRASS CAP
N:462087.47' E:756602.15'
F - FOUND IRON PIPE W/ BRASS CAP
N:462059.80' E:753961.90'
G - FOUND IRON PIPE W/ BRASS CAP
N:462034.23' E:751322.42'
H - FOUND IRON PIPE W/ BRASS CAP
N:464675.41' E:751305.83'
I - FOUND BENT IRON PIPE W/ BRASS CAP
N:459447.89' E:756620.56'
J - FOUND IRON PIPE W/ BRASS CAP
N:456806.31' E:756639.34'
K - FOUND IRON PIPE W/ BRASS CAP
N:456778.50' E:753996.44'
L - FOUND IRON PIPE W/ BRASS CAP
N:456753.78' E:751353.50'
M - FOUND IRON PIPE W/ BRASS CAP
N:459393.97' E:751338.83'

SURFACE HOLE LOCATION (SHL)
NEW MEXICO EAST - NAD 83
X=752837.19
Y=456992.67
LAT.= 32.25449552° N
LONG.= 103.64916049° W
225' FSL, 1485' FWL
SECTION 35

LAST TAKE POINT (LTP)
NEW MEXICO EAST - NAD 83
X=752419.66
Y=467228.32
LAT.= 32.28263746° N
LONG.= 103.65030035° W
100' FNL, 1130' FWL
SECTION 26

FIRST TAKE POINT (FTP)
NEW MEXICO EAST - NAD 83
X=752482.90
Y=456864.34
LAT.= 32.25414899° N
LONG.= 103.65030914° W
100' FSL, 1130' FWL
SECTION 35

BOTTOM HOLE LOCATION (BHL)
NEW MEXICO EAST - NAD 83
X=752419.34
Y=467278.32
LAT.= 32.28277490° N
LONG.= 103.65030035° W
50' FNL, 1130' FWL
SECTION 26

17 OPERATOR CERTIFICATION
I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

6/24/2020

Signature: Stan Wagner Date: _____
Printed Name: Stan Wagner
E-mail Address: _____

18 SURVEYOR CERTIFICATION
I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

Date of Survey: _____
Signature and Seal of Professional Surveyor: _____
Certificate Number: _____

Intent ☒ As Drilled ☐

API # 30-025-		
Operator Name: COG Operating LLC	Property Name: Bedlington Federal Com	Well Number 502H

Kick Off Point (KOP)

UL N	Section 35	Township 23S	Range 32E	Lot	Feet	From N/S	Feet	From E/W	County Lea
Latitude					Longitude				NAD 83

First Take Point (FTP)

UL M	Section 35	Township 23S	Range 32E	Lot	Feet 100	From N/S South	Feet 1130	From E/W West	County Lea
Latitude 32.25414899					Longitude -103.65030914				NAD 83

Last Take Point (LTP)

UL D	Section 26	Township 23S	Range 32E	Lot	Feet 100	From N/S North	Feet 1930	From E/W West	County Lea
Latitude 32.28263746					Longitude -103.65030035				NAD 83

Is this well the defining well for the Horizontal Spacing Unit? ☐ YESIs this well an infill well? ☐ NO

If infill is yes please provide API if available, Operator Name and well number for Defining well for Horizontal Spacing Unit.

API #		
Operator Name:	Property Name:	Well Number

KZ 06/29/2018

District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Road, Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit Original
to Appropriate
District Office

GAS CAPTURE PLAN

Date: 6/23/20

☒ Original Operator & OGRID No.: COG Operating LLC, (229137)
☐ Amended - Reason for Amendment: _____

This Gas Capture Plan outlines actions to be taken by the Operator to reduce well/production facility flaring/venting for new completion (new drill, recomple to new zone, re-frac) activity.

Note: Form C-129 must be submitted and approved prior to exceeding 60 days allowed by Rule (Subsection A of 19.15.18.12 NMAC).

Well(s)/Production Facility – Name of facility

The well(s) that will be located at the production facility are shown in the table below.

Well Name	API	Well Location (ULSTR)	Footages	Expected MCF/D	Flared or Vented	Comments
Bedlington Federal Com 501H	30-025-	N-35-23S-32E	225' FSL & 1455' FWL	±4000	None Planned	APD Submission Plan Subject to change
Bedlington Federal Com 502H	30-025-	N-35-23S-32E	225' FSL & 1485' FWL	±4000	None Planned	APD Submission Plan Subject to change
Bedlington Federal Com 503H	30-025-	N-35-23S-32E	225' FSL & 1515' FWL	±4000	None Planned	APD Submission Plan Subject to change

Gathering System and Pipeline Notification

Well(s) will be connected to a production facility after flowback operations are complete, if gas transporter system is in place. The gas produced from production facility is dedicated to **DCP Midstream** and will be connected to **Eunice** low pressure gathering system located in **Lea** County, New Mexico. **COG Operating LLC** provides (periodically) to **DCP Midstream** a drilling, completion and estimated first production date for wells that are scheduled to be drilled in the foreseeable future. In addition, **COG Operating LLC** and **DCP Midstream** have periodic conference calls to discuss changes to the drilling and completion schedules. Gas from these wells will be processed at **DCP Midstream-Eunice** Processing Plant located in Sec. **5**, Twn. **21S**, Rng **36E**, **Lea** County, New Mexico. The actual flow of the gas will be based on compression operating parameters and gathering system pressures.

Flowback Strategy

After the fracture treatment/completion operations, well(s) will be produced to temporary production tanks and gas will be flared or vented. During flowback, the fluids and sand content will be monitored. When the produced fluids contain minimal sand, the wells will be turned to production facilities. Gas sales should start as soon as the wells start flowing through the production facilities, unless there are operational issues on Gas Transporter system at that time. Based on current information, it is Operator's belief the system can take this gas upon completion of the well(s).

Safety requirements during cleanout operations from the use of underbalanced air cleanout systems may necessitate that sand and non-pipeline quality gas be vented and/or flared rather than sold on a temporary basis.

Alternatives to Reduce Flaring

Below are alternatives considered from a conceptual standpoint to reduce the amount of gas flared.

- Power Generation – On lease
 - Only a portion of gas is consumed operating the generator, remainder of gas will be flared
- Compressed Natural Gas – On lease
 - Gas flared would be minimal, but might be uneconomical to operate when gas volume declines

- NGL Removal – On lease
 - Plants are expensive, residue gas is still flared, and uneconomical to operate when gas volume declines

COG Production, LLC - Bedlington Federal Com #502H

1. Geologic Formations

TVD of target	10,898' EOL	Pilot hole depth	NA
MD at TD:	21,080'	Deepest expected fresh water:	585'

Formation	Depth (TVD) from KB	Water/Mineral Bearing/ Target Zone?	Hazards*
Quaternary Fill	Surface	Water	
Rustler	1192	Water	
Top of Salt	1532	Salt	
Base of Salt	4693	Salt	
Lamar	4917	Salt Water	
Bell Canyon	4982	Salt Water	
Cherry Canyon	5811	Oil/Gas	
Brushy Canyon	7175	Oil/Gas	
U. Avalon Shale	8727	Oil/Gas	
M. Avalon Shale	9119	Oil/Gas	
L. Avalon Shale	9512	Not Penetrated	
Basal Avalon	X	Not Penetrated	
1st Bone Spring Sand	9905	Not Penetrated	
2nd Bone Spring Sand	10478	Not Penetrated	
3rd Bone Spring Sand	11024	Not Penetrated	

2. Casing Program

Hole Size	Casing Interval		Csg. Size	Weight (lbs)	Grade	Conn.	SF Collapse	SF Burst	SF Tension
	From	To							
17.5"	0	1220	13.375"	54.5	J55	STC	2.02	1.25	7.73
12.25"	0	4000	9.625"	40	J55	LTC	1.22	0.94	3.25
12.25"	4000	4950	9.625"	40	L80	LTC	1.19	1.38	5.73
8.75"	0	21,080	5.5"	17	P110	LTC	1.42	2.55	2.40
BLM Minimum Safety Factor							1.125	1	1.6 Dry 1.8 Wet

Intermediate casing will be kept at least 1/3 full while running casing to mitigate collapse. Intermediate burst based on 0.7 frac gradient at the shoe with Gas Gradient 0.1 psi/ft to surface.

All casing strings will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.h

COG Production, LLC - Bedlington Federal Com #502H

	Y or N
Is casing new? If used, attach certification as required in Onshore Order #1	Y
Does casing meet API specifications? If no, attach casing specification sheet.	Y
Is premium or uncommon casing planned? If yes attach casing specification sheet.	N
Does the above casing design meet or exceed BLM's minimum standards? If not provide justification (loading assumptions, casing design criteria).	Y
Will the intermediate pipe be kept at a minimum 1/3 fluid filled to avoid approaching the collapse pressure rating of the casing?	Y
Is well located within Capitan Reef?	N
If yes, does production casing cement tie back a minimum of 50' above the Reef?	
Is well within the designated 4 string boundary?	
Is well located in SOPA but not in R-111-P?	N
If yes, are the first 2 strings cemented to surface and 3 rd string cement tied back 500' into previous casing?	
Is well located in R-111-P and SOPA?	N
If yes, are the first three strings cemented to surface?	
Is 2 nd string set 100' to 600' below the base of salt?	
Is well located in high Cave/Karst?	N
If yes, are there two strings cemented to surface?	
(For 2 string wells) If yes, is there a contingency casing if lost circulation occurs?	
Is well located in critical Cave/Karst?	N
If yes, are there three strings cemented to surface?	

COG Production, LLC - Bedlington Federal Com #502H

3. Cementing Program

Casing	# Sks	Wt. lb/ gal	Yld ft3/ sack	H ₂ O gal/sk	500# Comp. Strength (hours)	Slurry Description
Surf.	540	13.5	1.75	9	12	Lead: Class C + 4% Gel + 1% CaCl ₂
	250	14.8	1.34	6.34	8	Tail: Class C + 2% CaCl ₂
Inter.	930	12.7	2.0	9.6	16	Lead: 35:65:6 C Blend
	250	14.8	1.34	6.34	8	Tail: Class C + 2% CaCl
5.5 Prod	830	11.9	2.5	19	72	Lead: 50:50:10 H Blend
	2720	14.4	1.24	5.7	19	Tail: 50:50:2 Class H Blend

Volumes Subject to Observed Hole Conditions and/or Fluid Caliper Results

Lab reports with the 500 psi compressive strength time for the cement will be onsite for review.

Casing String	TOC	% Excess
Surface	0'	50%
1 st Intermediate	0'	50%
Production	4,450'	25% OH in Lateral (KOP to EOL) – 40% OH in Vertical

COG Production, LLC - Bedlington Federal Com #502H

4. Pressure Control Equipment

N	A variance is requested for the use of a diverter on the surface casing. See attached for schematic.
---	---

BOP installed and tested before drilling which hole?	Size?	Min. Required WP	Type	x	Tested to:
12-1/4"	13-5/8"	2M	Annular	x	2000 psi
			Blind Ram		2M
			Pipe Ram		
			Double Ram		
			Other*		
8-3/4"	13-5/8"	3M	Annular	x	50% testing pressure
			Blind Ram	x	3M
			Pipe Ram	x	
			Double Ram		
			Other*		

BOP/BOPE will be tested by an independent service company to 250 psi low and the high pressure indicated above per Onshore Order 2 requirements. The System may be upgraded to a higher pressure but still tested to the working pressure listed in the table above. If the system is upgraded all the components installed will be functional and tested.

Pipe rams will be operationally checked each 24 hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets. Other accessories to the BOP equipment will include a Kelly cock and floor safety valve (inside BOP) and choke lines and choke manifold. See attached schematics.

X	Formation integrity test will be performed per Onshore Order #2. On Exploratory wells or on that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Will be tested in accordance with Onshore Oil and Gas Order #2 III.B.1.i.
Y	A variance is requested for the use of a flexible choke line from the BOP to Choke Manifold. See attached for specs and hydrostatic test chart.
N	Are anchors required by manufacturer?
N	A multibowl wellhead is being used. The BOP will be tested per Onshore Order #2 after installation on the surface casing which will cover testing requirements for a maximum of 30 days. If any seal subject to test pressure is broken the system must be tested.

COG Production, LLC - Bedlington Federal Com #502H

5. Mud Program

Depth		Type	Weight (ppg)	Viscosity	Water Loss
From	To				
0	Surf. Shoe	FW Gel	8.6 - 8.8	28-34	N/C
Surf csg	9-5/8" Int shoe	Saturated Brine	10 - 10.1	28-34	N/C
9-5/8" Int shoe	Lateral TD	Cut Brine	8.6 - 9.3	28-34	N/C

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept on location at all times.

What will be used to monitor the loss or gain of fluid?	PVT/Pason/Visual Monitoring
---	-----------------------------

6. Logging and Testing Procedures

Logging, Coring and Testing.	
Y	Will run GR/CNL from TD to surface (horizontal well – vertical portion of hole). Stated logs run will be in the Completion Report and submitted to the BLM.
Y	No Logs are planned based on well control or offset log information.
N	Drill stem test? If yes, explain.
N	Coring? If yes, explain.

Additional logs planned		Interval
N	Resistivity	Pilot Hole TD to ICP
N	Density	Pilot Hole TD to ICP
Y	CBL	Production casing (If cement not circulated to surface)
Y	Mud log	Intermediate shoe to TD
N	PEX	

COG Production, LLC - Bedlington Federal Com #502H

7. Drilling Conditions

Condition	Specify what type and where?
BH Pressure at deepest TVD	5275 psi at 10898' TVD
Abnormal Temperature	NO 165 Deg. F.

No abnormal pressure or temperature conditions are anticipated. Sufficient mud materials to maintain mud properties and weight increase requirements will be kept on location at all times.

Sufficient supplies of Paper/LCM for periodic sweeps to control seepage and losses will be maintained on location.

Hydrogen Sulfide (H₂S) monitors will be installed prior to drilling out the surface shoe. If H₂S is detected in concentrations greater than 100 ppm, the operator will comply with the provisions of Onshore Oil and Gas Order #6. If Hydrogen Sulfide is encountered, measured values and formations will be provided to the BLM.

N H₂S is present

Y H₂S Plan attached

8. Other Facets of Operation

Y	Is it a walking operation?
Y	Is casing pre-set?

x	H ₂ S Plan.
x	BOP & Choke Schematics.
x	Directional Plan

DELAWARE BASIN EAST
BULLDOG PROSPECT (NM-E)
BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)
BEDLINGTON FED COM 502H

OWB
PWP1

Anticollision Report

08 June, 2020

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Reference	PWP1
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria
Interpolation Method:	Stations
Depth Range:	Unlimited
Results Limited by:	Maximum ellipse separation of 1,000.0 usft
Warning Levels Evaluated at:	2.00 Sigma
Error Model:	ISCWSA
Scan Method:	Closest Approach 3D
Error Surface:	Pedal Curve
Casing Method:	Not applied

Survey Tool Program		Date	6/8/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.0	21,080.0	PWP1 (OWB)	MWD+IFR1+FDIR	OWSG MWD + IFR1 + FDIR Correction	

Summary						
Site Name	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)						
AVION FED #301H - OWB - ACTUAL WELLPATH						Out of range
AVION FEDERAL #2 - OWB - ACTUAL WELLPATH						Out of range
BEDLINGTON FED COM 201H - OWB - PWP1	2,506.0	2,509.7	369.5	356.5	28.382	CC, ES
BEDLINGTON FED COM 201H - OWB - PWP1	9,000.0	9,008.3	561.1	519.5	13.510	SF
BEDLINGTON FED COM 202H - OWB - PWP1	2,675.5	2,702.3	394.3	380.8	29.150	CC
BEDLINGTON FED COM 202H - OWB - PWP1	9,106.7	9,110.8	413.3	372.4	10.100	ES
BEDLINGTON FED COM 202H - OWB - PWP1	9,200.0	9,187.8	415.5	374.2	10.063	SF
BEDLINGTON FED COM 301H - OWB - PWP1	2,501.9	2,503.0	206.3	187.8	11.159	CC
BEDLINGTON FED COM 301H - OWB - PWP1	3,400.0	3,408.1	211.2	186.8	8.642	ES
BEDLINGTON FED COM 301H - OWB - PWP1	8,000.0	8,004.2	303.7	246.7	5.331	SF
BEDLINGTON FED COM 302H - OWB - PWP1	9,175.4	9,177.7	184.2	144.1	4.595	CC, ES, SF
BEDLINGTON FED COM 303H - OWB - PWP1	2,500.0	2,501.0	228.6	210.1	12.373	CC, ES
BEDLINGTON FED COM 303H - OWB - PWP1	5,500.0	5,494.0	403.1	364.0	10.306	SF
BEDLINGTON FED COM 501H - OWB - PWP1	2,500.0	2,500.0	30.0	17.3	2.366	CC
BEDLINGTON FED COM 501H - OWB - PWP1	2,700.0	2,697.9	30.4	17.0	2.271	ES, SF
BEDLINGTON FED COM 503H - OWB - PWP1	2,500.0	2,500.0	30.0	17.3	2.363	CC, ES, SF
BEDLINGTON FED COM 701H - OWB - PWP1	10,713.5	10,695.4	119.6	70.0	2.409	CC, ES, SF
BEDLINGTON FED COM 702H - OWB - PWP1	10,532.0	10,551.0	214.8	167.8	4.569	CC, ES
BEDLINGTON FED COM 702H - OWB - PWP1	10,550.0	10,567.6	215.0	167.8	4.558	SF
BEDLINGTON FED COM 703H - OWB - PWP1	2,500.0	2,501.0	290.0	277.3	22.859	CC, ES
BEDLINGTON FED COM 703H - OWB - PWP1	10,800.0	10,739.6	646.8	600.9	14.097	SF
BEDLINGTON FED COM 704H - OWB - PWP1	2,416.3	2,417.3	320.0	302.1	17.866	CC
BEDLINGTON FED COM 704H - OWB - PWP1	2,500.0	2,500.0	320.0	301.5	17.322	ES
BEDLINGTON FED COM 704H - OWB - PWP1	8,900.0	8,846.2	999.3	936.7	15.962	SF
COX 35 FED 2H - OWB - AWP						Out of range

Offset Design	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 201H - OWB - PWP										Offset Site Error:	3.0 usft
Survey Program:	0-Standard Keeper 104, 9001-MWD+IFR1+FDIR										Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Minimum Separation		Warning				
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (")	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Separation Factor	
0.0	0.0	3.0	3.0	3.0	3.0	56.71	202.8	308.9	369.5			
100.0	100.0	103.0	103.0	3.0	3.0	56.71	202.8	308.9	369.5	363.5	6.00	61.558

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 201H - OWB - PWP													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 9001-MVD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
200.0	200.0	203.0	203.0	3.0	3.0	56.71	202.8	308.9	369.5	363.5	6.04	61.155		
300.0	300.0	303.0	303.0	3.1	3.0	56.71	202.8	308.9	369.5	363.4	6.13	60.321		
400.0	400.0	403.0	403.0	3.2	3.0	56.71	202.8	308.9	369.5	363.3	6.25	59.120		
500.0	500.0	503.0	503.0	3.4	3.1	56.71	202.8	308.9	369.5	363.1	6.41	57.632		
600.0	600.0	603.0	603.0	3.6	3.1	56.71	202.8	308.9	369.5	362.9	6.61	55.939		
700.0	700.0	703.0	703.0	3.8	3.1	56.71	202.8	308.9	369.5	362.7	6.83	54.117		
800.0	800.0	803.0	803.0	4.0	3.2	56.71	202.8	308.9	369.5	362.5	7.08	52.230		
900.0	900.0	903.0	903.0	4.2	3.2	56.71	202.8	308.9	369.5	362.2	7.34	50.326		
1,000.0	1,000.0	1,003.0	1,003.0	4.5	3.2	56.71	202.8	308.9	369.5	361.9	7.63	48.444		
1,100.0	1,100.0	1,103.0	1,103.0	4.8	3.3	56.71	202.8	308.9	369.5	361.6	7.93	46.607		
1,200.0	1,200.0	1,203.0	1,203.0	5.1	3.4	56.71	202.8	308.9	369.5	361.3	8.24	44.833		
1,300.0	1,300.0	1,303.0	1,303.0	5.4	3.4	56.71	202.8	308.9	369.5	361.0	8.57	43.132		
1,400.0	1,400.0	1,403.0	1,403.0	5.7	3.5	56.71	202.8	308.9	369.5	360.6	8.90	41.509		
1,500.0	1,500.0	1,503.0	1,503.0	6.0	3.6	56.71	202.8	308.9	369.5	360.3	9.25	39.967		
1,600.0	1,600.0	1,603.0	1,603.0	6.3	3.6	56.71	202.8	308.9	369.5	359.9	9.60	38.503		
1,700.0	1,700.0	1,703.0	1,703.0	6.6	3.7	56.71	202.8	308.9	369.5	359.6	9.96	37.118		
1,800.0	1,800.0	1,803.0	1,803.0	6.9	3.8	56.71	202.8	308.9	369.5	359.2	10.32	35.808		
1,900.0	1,900.0	1,903.0	1,903.0	7.2	3.9	56.71	202.8	308.9	369.5	358.9	10.69	34.570		
2,000.0	2,000.0	2,003.0	2,003.0	7.6	3.9	56.71	202.8	308.9	369.5	358.5	11.06	33.399		
2,100.0	2,100.0	2,103.0	2,103.0	7.9	4.0	56.71	202.8	308.9	369.5	358.1	11.44	32.293		
2,200.0	2,200.0	2,203.0	2,203.0	8.2	4.1	56.71	202.8	308.9	369.5	357.7	11.83	31.246		
2,300.0	2,300.0	2,303.0	2,303.0	8.6	4.2	56.71	202.8	308.9	369.5	357.3	12.21	30.256		
2,400.0	2,400.0	2,403.0	2,403.0	8.9	4.3	56.71	202.8	308.9	369.5	356.9	12.60	29.319		
2,500.0	2,500.0	2,503.3	2,503.3	9.2	4.4	56.71	202.9	308.9	369.5	356.5	13.00	28.431		
2,506.0	2,506.0	2,509.7	2,509.7	9.3	4.4	166.76	202.9	308.9	369.5	356.5	13.02	28.382	CC, ES	
2,600.0	2,600.0	2,611.6	2,611.6	9.6	4.5	166.56	203.6	306.8	370.0	356.7	13.36	27.702		
2,700.0	2,699.8	2,719.8	2,719.6	9.9	4.5	165.98	205.7	301.0	371.7	358.0	13.69	27.154		
2,800.0	2,799.6	2,825.7	2,825.0	10.2	4.6	165.02	209.1	291.6	373.0	359.0	14.03	26.583		
2,900.0	2,899.4	2,925.5	2,924.2	10.5	4.7	163.98	212.7	281.8	373.8	359.4	14.39	25.980		
3,000.0	2,999.1	3,025.2	3,023.4	10.9	4.7	162.95	216.3	272.0	374.7	360.0	14.75	25.407		
3,100.0	3,098.9	3,125.0	3,122.7	11.2	4.8	161.93	219.8	262.2	375.7	360.6	15.11	24.861		
3,200.0	3,198.6	3,224.8	3,221.9	11.5	4.8	160.91	223.4	252.4	376.9	361.4	15.48	24.341		
3,300.0	3,298.4	3,324.5	3,321.1	11.9	4.9	159.89	227.0	242.6	378.2	362.3	15.86	23.847		
3,400.0	3,398.1	3,424.3	3,420.3	12.2	5.0	158.89	230.5	232.8	379.6	363.3	16.24	23.378		
3,500.0	3,497.9	3,524.1	3,519.6	12.5	5.1	157.89	234.1	223.0	381.1	364.5	16.62	22.931		
3,600.0	3,597.6	3,623.8	3,618.8	12.9	5.1	156.90	237.7	213.2	382.7	365.7	17.00	22.507		
3,700.0	3,697.4	3,723.6	3,718.0	13.2	5.2	155.92	241.2	203.4	384.4	367.1	17.39	22.103		
3,800.0	3,797.2	3,823.4	3,817.2	13.5	5.3	154.95	244.8	193.6	386.3	368.5	17.79	21.719		
3,900.0	3,896.9	3,923.1	3,916.4	13.9	5.4	153.98	248.4	183.8	388.3	370.1	18.18	21.353		
4,000.0	3,996.7	4,022.9	4,015.7	14.2	5.5	153.03	251.9	174.0	390.3	371.7	18.58	21.006		
4,100.0	4,096.4	4,122.7	4,114.9	14.6	5.6	152.09	255.5	164.2	392.5	373.5	18.98	20.675		
4,200.0	4,196.2	4,222.4	4,214.1	14.9	5.7	151.16	259.1	154.4	394.8	375.4	19.39	20.360		
4,300.0	4,295.9	4,322.2	4,313.3	15.3	5.7	150.24	262.6	144.6	397.2	377.4	19.80	20.060		
4,400.0	4,395.7	4,422.0	4,412.5	15.6	5.8	149.33	266.2	134.8	399.7	379.5	20.21	19.774		
4,500.0	4,495.5	4,521.7	4,511.8	16.0	5.9	148.43	269.8	125.0	402.3	381.6	20.63	19.502		
4,600.0	4,595.2	4,621.5	4,611.0	16.3	6.0	147.54	273.3	115.2	404.9	383.9	21.04	19.243		
4,700.0	4,695.0	4,721.3	4,710.2	16.7	6.1	146.67	276.9	105.4	407.7	386.3	21.46	18.996		
4,800.0	4,794.7	4,821.0	4,809.4	17.0	6.2	145.81	280.5	95.6	410.6	388.7	21.89	18.760		
4,900.0	4,894.5	4,920.8	4,908.7	17.4	6.3	144.95	284.0	85.8	413.6	391.3	22.31	18.535		
5,000.0	4,994.2	5,020.6	5,007.9	17.7	6.4	144.12	287.6	76.0	416.6	393.9	22.74	18.321		
5,100.0	5,094.0	5,120.4	5,107.1	18.1	6.5	143.29	291.2	66.2	419.8	396.6	23.17	18.116		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 9001-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Semi Major Axis Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,200.0	5,193.7	5,220.1	5,206.3	18.4	6.6	142.48	294.7	56.4	423.0	399.4	23.60	17.921	
5,300.0	5,293.5	5,319.9	5,305.5	18.8	6.7	141.68	298.3	46.6	426.3	402.3	24.04	17.734	
5,400.0	5,393.3	5,419.7	5,404.8	19.1	6.8	140.89	301.9	36.8	429.7	405.2	24.48	17.556	
5,500.0	5,493.0	5,519.4	5,504.0	19.5	6.9	140.11	305.4	27.0	433.2	408.3	24.92	17.385	
5,600.0	5,592.8	5,619.2	5,603.2	19.8	7.1	139.35	309.0	17.2	436.8	411.4	25.36	17.222	
5,700.0	5,692.5	5,719.0	5,702.4	20.2	7.2	138.60	312.6	7.4	440.4	414.6	25.80	17.066	
5,800.0	5,792.3	5,818.7	5,801.6	20.5	7.3	137.86	316.1	-2.4	444.1	417.9	26.25	16.917	
5,900.0	5,892.0	5,918.5	5,900.9	20.9	7.4	137.13	319.7	-12.2	447.9	421.2	26.70	16.775	
6,000.0	5,991.8	6,018.3	6,000.1	21.2	7.5	136.42	323.3	-22.0	451.7	424.6	27.15	16.638	
6,100.0	6,091.6	6,118.0	6,099.3	21.6	7.6	135.71	326.8	-31.8	455.7	428.1	27.60	16.507	
6,200.0	6,191.3	6,217.8	6,198.5	21.9	7.7	135.02	330.4	-41.6	459.7	431.6	28.06	16.382	
6,300.0	6,291.1	6,317.6	6,297.8	22.3	7.8	134.35	334.0	-51.4	463.7	435.2	28.51	16.262	
6,400.0	6,390.8	6,417.3	6,397.0	22.7	7.9	133.68	337.5	-61.2	467.8	438.9	28.97	16.147	
6,500.0	6,490.6	6,517.1	6,496.2	23.0	8.0	133.03	341.1	-71.0	472.0	442.6	29.43	16.037	
6,600.0	6,590.3	6,616.9	6,595.4	23.4	8.2	132.38	344.7	-80.8	476.3	446.4	29.89	15.931	
6,700.0	6,690.1	6,716.6	6,694.6	23.7	8.3	131.75	348.2	-90.6	480.6	450.2	30.36	15.829	
6,800.0	6,789.9	6,816.4	6,793.9	24.1	8.4	131.13	351.8	-100.4	484.9	454.1	30.82	15.732	
6,900.0	6,889.6	6,916.2	6,893.1	24.4	8.5	130.52	355.4	-110.2	489.3	458.0	31.29	15.639	
7,000.0	6,989.4	7,015.9	6,992.3	24.8	8.6	129.92	358.9	-120.0	493.8	462.0	31.76	15.549	
7,100.0	7,089.1	7,115.7	7,091.5	25.1	8.7	129.33	362.5	-129.8	498.3	466.1	32.23	15.462	
7,200.0	7,188.9	7,215.5	7,190.7	25.5	8.9	128.76	366.1	-139.6	502.9	470.2	32.70	15.380	
7,300.0	7,288.6	7,315.2	7,290.0	25.9	9.0	128.19	369.6	-149.4	507.5	474.3	33.17	15.300	
7,400.0	7,388.4	7,415.0	7,389.2	26.2	9.1	127.63	373.2	-159.2	512.2	478.5	33.64	15.223	
7,500.0	7,488.1	7,514.8	7,488.4	26.6	9.2	127.09	376.8	-169.0	516.9	482.8	34.12	15.150	
7,600.0	7,587.9	7,614.6	7,587.6	26.9	9.3	126.55	380.3	-178.8	521.7	487.1	34.60	15.079	
7,700.0	7,687.7	7,714.3	7,686.9	27.3	9.4	126.03	383.9	-188.6	526.5	491.4	35.07	15.011	
7,805.4	7,792.8	7,819.5	7,791.5	27.7	9.6	125.48	387.7	-198.9	531.6	496.0	35.58	14.942	
7,900.0	7,887.2	7,913.8	7,885.3	28.0	9.7	124.97	391.0	-208.2	535.8	499.7	36.03	14.869	
8,000.0	7,987.1	8,013.6	7,984.4	28.4	9.8	124.28	394.6	-218.0	539.3	502.8	36.52	14.766	
8,100.0	8,087.1	8,113.2	8,083.5	28.7	9.9	123.44	398.2	-227.7	541.9	504.9	37.02	14.640	
8,205.4	8,192.5	8,218.1	8,187.9	29.1	10.1	123.33	401.9	-238.0	543.8	506.3	37.54	14.486	
8,300.0	8,287.1	8,312.2	8,281.4	29.4	10.2	11.31	405.3	-247.3	545.3	507.3	38.01	14.344	
8,400.0	8,387.1	8,411.6	8,380.3	29.8	10.3	10.23	408.8	-257.1	546.9	508.4	38.51	14.202	
8,500.0	8,487.1	8,511.1	8,479.2	30.1	10.4	9.16	412.4	-266.8	548.8	509.8	39.01	14.068	
8,600.0	8,587.1	8,610.5	8,578.1	30.4	10.5	8.10	415.9	-276.6	550.9	511.4	39.52	13.941	
8,700.0	8,687.1	8,710.0	8,677.0	30.8	10.7	7.05	419.5	-286.4	553.2	513.1	40.02	13.822	
8,800.0	8,787.1	8,809.4	8,776.0	31.1	10.8	6.00	423.1	-296.1	555.6	515.1	40.52	13.711	
8,900.0	8,887.1	8,908.9	8,874.9	31.5	10.9	4.97	426.6	-305.9	558.2	517.2	41.03	13.606	
9,000.0	8,987.1	9,008.3	8,973.8	31.8	11.0	3.94	430.2	-315.7	561.1	519.5	41.53	13.510 SF	
9,100.0	9,087.1	9,065.8	9,030.7	32.2	11.1	3.27	434.0	-322.0	567.3	525.5	41.82	13.565	
9,200.0	9,187.1	9,116.7	9,080.5	32.5	11.1	2.50	441.7	-329.3	582.0	540.0	42.05	13.839	
9,300.0	9,287.1	9,165.6	9,127.3	32.9	11.1	1.62	453.0	-337.7	604.9	562.7	42.23	14.324	
9,400.0	9,387.1	9,200.0	9,159.5	33.2	11.1	0.94	463.2	-344.5	635.9	593.6	42.27	15.046	
9,500.0	9,487.1	9,250.0	9,204.8	33.5	11.2	-0.12	481.2	-355.5	673.9	631.5	42.37	15.907	
9,600.0	9,587.1	9,300.0	9,248.1	33.9	11.2	-1.23	502.9	-367.8	718.9	676.4	42.45	16.934	
9,700.0	9,687.1	9,331.9	9,274.6	34.2	11.2	-1.95	518.5	-376.3	770.0	727.6	42.38	18.169	
9,800.0	9,787.1	9,365.7	9,301.5	34.6	11.3	-2.71	536.6	-385.7	826.6	784.2	42.32	19.533	
9,900.0	9,887.1	9,400.0	9,327.5	34.9	11.3	-3.48	556.5	-395.9	888.0	845.7	42.27	21.006	
10,000.0	9,987.1	9,424.8	9,345.5	35.3	11.4	-4.02	571.8	-403.5	953.6	911.5	42.16	22.618	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

6/8/2020 12:10:30PM

Page 4

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design		BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 202H - OWB - PWP										Offset Site Error:		3.0 usft
Survey Program: 0-Standard Keeper 104, 8915-MWD+IFR1+FDIR												Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis		Distance								Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	3.0	3.0	3.0	3.0	59.06	203.2	338.9	395.1					
100.0	100.0	103.0	103.0	3.0	3.0	59.06	203.2	338.9	395.1	389.1	6.00	65.815		
200.0	200.0	203.0	203.0	3.0	3.0	59.06	203.2	338.9	395.1	389.1	6.04	65.385		
300.0	300.0	303.0	303.0	3.1	3.0	59.06	203.2	338.9	395.1	389.0	6.13	64.497		
400.0	400.0	403.0	403.0	3.2	3.0	59.06	203.2	338.9	395.1	388.8	6.25	63.217		
500.0	500.0	503.0	503.0	3.4	3.1	59.06	203.2	338.9	395.1	388.7	6.41	61.631		
600.0	600.0	603.0	603.0	3.6	3.1	59.06	203.2	338.9	395.1	388.5	6.60	59.827		
700.0	700.0	703.0	703.0	3.8	3.1	59.06	203.2	338.9	395.1	388.3	6.83	57.885		
800.0	800.0	803.0	803.0	4.0	3.2	59.06	203.2	338.9	395.1	388.0	7.07	55.874		
900.0	900.0	903.0	903.0	4.2	3.2	59.06	203.2	338.9	395.1	387.8	7.34	53.845		
1,000.0	1,000.0	1,003.0	1,003.0	4.5	3.2	59.06	203.2	338.9	395.1	387.5	7.62	51.838		
1,100.0	1,100.0	1,103.0	1,103.0	4.8	3.3	59.06	203.2	338.9	395.1	387.2	7.92	49.880		
1,200.0	1,200.0	1,203.0	1,203.0	5.1	3.4	59.06	203.2	338.9	395.1	386.9	8.23	47.988		
1,300.0	1,300.0	1,303.0	1,303.0	5.4	3.4	59.06	203.2	338.9	395.1	386.5	8.56	46.174		
1,400.0	1,400.0	1,403.0	1,403.0	5.7	3.5	59.06	203.2	338.9	395.1	386.2	8.89	44.443		
1,500.0	1,500.0	1,503.0	1,503.0	6.0	3.6	59.06	203.2	338.9	395.1	385.9	9.23	42.798		
1,600.0	1,600.0	1,603.0	1,603.0	6.3	3.6	59.06	203.2	338.9	395.1	385.5	9.58	41.237		
1,700.0	1,700.0	1,703.0	1,703.0	6.6	3.7	59.06	203.2	338.9	395.1	385.2	9.94	39.759		
1,800.0	1,800.0	1,803.0	1,803.0	6.9	3.8	59.06	203.2	338.9	395.1	384.8	10.30	38.361		
1,900.0	1,900.0	1,903.0	1,903.0	7.2	3.9	59.06	203.2	338.9	395.1	384.4	10.67	37.039		
2,000.0	2,000.0	2,003.0	2,003.0	7.6	3.9	59.06	203.2	338.9	395.1	384.1	11.04	35.789		
2,100.0	2,100.0	2,103.0	2,103.0	7.9	4.0	59.06	203.2	338.9	395.1	383.7	11.42	34.608		
2,200.0	2,200.0	2,203.0	2,203.0	8.2	4.1	59.06	203.2	338.9	395.1	383.3	11.80	33.490		
2,300.0	2,300.0	2,303.0	2,303.0	8.6	4.2	59.06	203.2	338.9	395.1	382.9	12.18	32.433		
2,400.0	2,400.0	2,403.0	2,403.0	8.9	4.3	59.06	203.2	338.9	395.1	382.5	12.57	31.432		
2,500.0	2,500.0	2,503.5	2,503.5	9.2	4.4	59.06	203.2	338.9	395.1	382.1	12.96	30.484		
2,600.0	2,600.0	2,618.9	2,618.8	9.6	4.4	169.26	201.4	337.1	394.7	381.4	13.30	29.677		
2,675.5	2,675.4	2,702.3	2,702.2	9.8	4.4	169.54	198.2	333.9	394.3	380.8	13.53	29.150 CC		
2,700.0	2,699.8	2,726.8	2,726.6	9.9	4.4	169.63	197.1	332.8	394.4	380.8	13.60	28.992		
2,800.0	2,799.6	2,826.7	2,826.3	10.2	4.4	170.05	192.6	328.5	395.2	381.3	13.92	28.389		
2,900.0	2,899.4	2,926.7	2,926.1	10.5	4.4	170.46	188.2	324.1	396.1	381.9	14.25	27.798		
3,000.0	2,999.1	3,026.7	3,025.9	10.9	4.4	170.87	183.8	319.7	397.0	382.4	14.58	27.221		
3,100.0	3,098.9	3,126.6	3,125.6	11.2	4.4	171.28	179.4	315.3	397.9	383.0	14.93	26.658		
3,200.0	3,198.6	3,226.6	3,225.4	11.5	4.4	171.68	175.0	310.9	398.9	383.6	15.28	26.110		
3,300.0	3,298.4	3,326.5	3,325.1	11.9	4.4	172.09	170.5	306.6	399.8	384.2	15.63	25.575		
3,400.0	3,398.1	3,426.5	3,424.9	12.2	4.4	172.49	166.1	302.2	400.8	384.8	16.00	25.056		
3,500.0	3,497.9	3,526.4	3,524.7	12.5	4.4	172.89	161.7	297.8	401.8	385.4	16.36	24.551		
3,600.0	3,597.6	3,626.4	3,624.4	12.9	4.4	173.29	157.3	293.4	402.8	386.1	16.74	24.061		
3,700.0	3,697.4	3,726.3	3,724.2	13.2	4.5	173.68	152.8	289.1	403.8	386.7	17.12	23.586		
3,800.0	3,797.2	3,826.3	3,824.0	13.5	4.5	174.08	148.4	284.7	404.9	387.4	17.51	23.126		
3,900.0	3,896.9	3,926.3	3,923.7	13.9	4.5	174.47	144.0	280.3	406.0	388.1	17.90	22.679		
4,000.0	3,996.7	4,026.2	4,023.5	14.2	4.6	174.86	139.6	275.9	407.0	388.8	18.30	22.247		
4,100.0	4,096.4	4,126.2	4,123.2	14.6	4.6	175.25	135.1	271.5	408.2	389.5	18.70	21.829		
4,200.0	4,196.2	4,226.1	4,223.0	14.9	4.6	175.63	130.7	267.2	409.3	390.2	19.10	21.425		
4,300.0	4,295.9	4,326.1	4,322.8	15.3	4.7	176.02	126.3	262.8	410.4	390.9	19.51	21.034		
4,400.0	4,395.7	4,426.0	4,422.5	15.6	4.7	176.40	121.9	258.4	411.6	391.7	19.93	20.655		
4,500.0	4,495.5	4,526.0	4,522.3	16.0	4.8	176.78	117.4	254.0	412.8	392.4	20.34	20.290		
4,600.0	4,595.2	4,625.9	4,622.0	16.3	4.8	177.16	113.0	249.7	414.0	393.2	20.77	19.936		
4,700.0	4,695.0	4,725.9	4,721.8	16.7	4.9	177.53	108.6	245.3	415.2	394.0	21.19	19.595		
4,800.0	4,794.7	4,825.9	4,821.6	17.0	5.0	177.90	104.2	240.9	416.4	394.8	21.62	19.265		
4,900.0	4,894.5	4,925.8	4,921.3	17.4	5.0	178.28	99.7	236.5	417.7	395.7	22.05	18.946		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

6/8/2020 12:10:30PM

Page 5

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 202H - OWB - PWP													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 8915-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,000.0	4,994.2	5,025.8	5,021.1	17.7	5.1	178.64	95.3	232.1	419.0	396.5	22.48	18.638		
5,100.0	5,094.0	5,125.7	5,120.9	18.1	5.2	179.01	90.9	227.8	420.3	397.3	22.91	18.341		
5,200.0	5,193.7	5,225.7	5,220.6	18.4	5.2	179.37	86.5	223.4	421.6	398.2	23.35	18.053		
5,300.0	5,293.5	5,325.6	5,320.4	18.8	5.3	179.74	82.0	219.0	422.9	399.1	23.79	17.775		
5,400.0	5,393.3	5,425.6	5,420.1	19.1	5.4	-179.91	77.6	214.6	424.2	400.0	24.23	17.507		
5,500.0	5,493.0	5,525.5	5,519.9	19.5	5.5	-179.55	73.2	210.3	425.6	400.9	24.68	17.247		
5,600.0	5,592.8	5,625.5	5,619.7	19.8	5.5	-179.19	68.8	205.9	427.0	401.8	25.12	16.996		
5,700.0	5,692.5	5,725.5	5,719.4	20.2	5.6	-178.84	64.4	201.5	428.3	402.8	25.57	16.754		
5,800.0	5,792.3	5,825.4	5,819.2	20.5	5.7	-178.49	59.9	197.1	429.8	403.7	26.02	16.519		
5,900.0	5,892.0	5,925.4	5,919.0	20.9	5.8	-178.14	55.5	192.7	431.2	404.7	26.46	16.292		
6,000.0	5,991.8	6,025.3	6,018.7	21.2	5.9	-177.80	51.1	188.4	432.6	405.7	26.92	16.073		
6,100.0	6,091.6	6,125.3	6,118.5	21.6	6.0	-177.45	46.7	184.0	434.1	406.7	27.37	15.860		
6,200.0	6,191.3	6,225.2	6,218.2	21.9	6.0	-177.11	42.2	179.6	435.5	407.7	27.82	15.655		
6,300.0	6,291.1	6,325.2	6,318.0	22.3	6.1	-176.77	37.8	175.2	437.0	408.7	28.28	15.456		
6,400.0	6,390.8	6,425.1	6,417.8	22.7	6.2	-176.44	33.4	170.9	438.5	409.8	28.73	15.263		
6,500.0	6,490.6	6,525.1	6,517.5	23.0	6.3	-176.10	29.0	166.5	440.0	410.8	29.19	15.076		
6,600.0	6,590.3	6,625.1	6,617.3	23.4	6.4	-175.77	24.5	162.1	441.6	411.9	29.65	14.894		
6,700.0	6,690.1	6,725.0	6,717.0	23.7	6.5	-175.44	20.1	157.7	443.1	413.0	30.10	14.720		
6,800.0	6,789.9	6,825.0	6,816.8	24.1	6.6	-175.12	15.7	153.3	444.7	414.1	30.56	14.550		
6,900.0	6,889.6	6,924.9	6,916.6	24.4	6.7	-174.79	11.3	149.0	446.2	415.2	31.02	14.386		
7,000.0	6,989.4	7,024.9	7,016.3	24.8	6.8	-174.47	6.8	144.6	447.8	416.3	31.48	14.226		
7,100.0	7,089.1	7,124.8	7,116.1	25.1	6.9	-174.15	2.4	140.2	449.4	417.5	31.94	14.071		
7,200.0	7,188.9	7,224.8	7,215.9	25.5	7.0	-173.83	-2.0	135.8	451.0	418.6	32.40	13.920		
7,300.0	7,288.6	7,324.7	7,315.6	25.9	7.1	-173.51	-6.4	131.4	452.7	419.8	32.86	13.775		
7,400.0	7,388.4	7,424.7	7,415.4	26.2	7.2	-173.20	-10.9	127.1	454.3	421.0	33.32	13.633		
7,500.0	7,488.1	7,524.7	7,515.1	26.6	7.3	-172.89	-15.3	122.7	456.0	422.2	33.79	13.495		
7,600.0	7,587.9	7,624.6	7,614.9	26.9	7.4	-172.58	-19.7	118.3	457.6	423.4	34.25	13.362		
7,700.0	7,687.7	7,724.6	7,714.7	27.3	7.5	-172.27	-24.1	113.9	459.3	424.6	34.71	13.232		
7,805.4	7,792.8	7,829.9	7,819.8	27.7	7.6	-171.95	-28.8	109.3	461.1	425.9	35.20	13.099		
7,900.0	7,887.2	7,924.5	7,914.2	28.0	7.7	-171.65	-33.0	105.2	461.9	426.3	35.64	12.962		
8,000.0	7,987.1	8,024.4	8,014.0	28.4	7.8	-171.31	-37.4	100.8	461.2	425.1	36.10	12.774		
8,100.0	8,087.1	8,124.4	8,113.7	28.7	7.9	-170.92	-41.8	96.4	458.7	422.1	36.56	12.545		
8,205.4	8,192.5	8,229.6	8,218.7	29.1	8.0	79.48	-46.5	91.8	454.2	417.2	37.04	12.262		
8,300.0	8,287.1	8,324.0	8,313.0	29.4	8.1	79.91	-50.7	87.7	449.4	411.9	37.47	11.995		
8,400.0	8,387.1	8,423.8	8,412.6	29.8	8.3	80.37	-55.1	83.3	444.3	406.4	37.92	11.719		
8,500.0	8,487.1	8,523.6	8,512.2	30.1	8.4	80.84	-59.5	78.9	439.3	400.9	38.37	11.450		
8,600.0	8,587.1	8,623.4	8,611.8	30.4	8.5	81.33	-63.9	74.6	434.3	395.5	38.82	11.188		
8,700.0	8,687.1	8,723.3	8,711.4	30.8	8.6	81.82	-68.3	70.2	429.3	390.0	39.27	10.933		
8,800.0	8,787.1	8,823.1	8,811.0	31.1	8.7	82.33	-72.7	65.8	424.3	384.6	39.72	10.684		
8,900.0	8,887.1	8,922.9	8,910.6	31.5	8.8	82.85	-77.2	61.5	419.4	379.3	40.15	10.445		
9,000.0	8,987.1	9,015.9	9,003.4	31.8	8.8	82.59	-75.8	57.3	415.2	374.7	40.52	10.248		
9,100.0	9,087.1	9,105.1	9,091.2	32.2	8.8	80.42	-60.6	53.4	413.3	372.4	40.90	10.107		
9,106.7	9,093.7	9,110.8	9,096.7	32.2	8.8	80.22	-59.1	53.1	413.3	372.4	40.92	10.100 ES		
9,200.0	9,187.1	9,187.8	9,169.5	32.5	8.9	76.78	-34.4	49.8	415.5	374.2	41.29	10.063 SF		
9,300.0	9,287.1	9,261.7	9,235.6	32.9	8.9	72.34	-1.8	46.6	424.1	382.5	41.67	10.180		
9,400.0	9,387.1	9,326.0	9,289.4	33.2	9.0	67.77	33.4	44.0	441.8	399.8	41.99	10.522		
9,500.0	9,487.1	9,381.3	9,332.1	33.5	9.0	63.48	68.3	41.9	470.0	427.8	42.21	11.136		
9,600.0	9,587.1	9,428.4	9,365.8	33.9	9.1	59.70	101.2	40.2	508.9	466.7	42.26	12.042		
9,700.0	9,687.1	9,468.5	9,392.3	34.2	9.1	56.45	131.3	38.9	557.8	515.6	42.18	13.224		
9,800.0	9,787.1	9,500.0	9,411.6	34.6	9.2	53.93	156.2	37.9	615.2	573.3	41.96	14.664		
9,900.0	9,887.1	9,532.2	9,429.8	34.9	9.2	51.42	182.7	36.9	679.8	638.1	41.74	16.288		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 202H - OWB - PWP												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 8915-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance									Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
10,000.0	9,987.1	9,550.0	9,439.3	35.3	9.3	50.05	197.8	36.4	750.3	708.9	41.43	18.112	
10,100.0	10,087.1	9,579.6	9,453.9	35.6	9.3	47.85	223.5	35.6	825.3	784.0	41.28	19.991	
10,200.0	10,187.1	9,600.0	9,463.2	36.0	9.4	46.38	241.6	35.0	904.1	863.0	41.13	21.984	
10,300.0	10,287.1	9,615.9	9,470.0	36.3	9.4	45.26	256.0	34.6	986.0	945.0	41.00	24.046	

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)					
0.0	0.0	1.0	1.0	3.0	3.0	13.71	200.4	48.9	206.3				
100.0	100.0	101.0	101.0	3.0	3.0	13.71	200.4	48.9	206.3	200.3	6.01	34.352	
200.0	200.0	201.0	201.0	3.0	3.0	13.71	200.4	48.9	206.3	200.2	6.08	33.931	
300.0	300.0	301.0	301.0	3.1	3.1	13.71	200.4	48.9	206.3	200.1	6.24	33.080	
400.0	400.0	401.0	401.0	3.2	3.2	13.71	200.4	48.9	206.3	199.8	6.47	31.890	
500.0	500.0	501.0	501.0	3.4	3.4	13.71	200.4	48.9	206.3	199.5	6.77	30.473	
600.0	600.0	601.0	601.0	3.6	3.6	13.71	200.4	48.9	206.3	199.2	7.13	28.933	
700.0	700.0	701.0	701.0	3.8	3.8	13.71	200.4	48.9	206.3	198.8	7.54	27.354	
800.0	800.0	801.0	801.0	4.0	4.0	13.71	200.4	48.9	206.3	198.3	8.00	25.798	
900.0	900.0	901.0	901.0	4.2	4.2	13.71	200.4	48.9	206.3	197.8	8.49	24.306	
1,000.0	1,000.0	1,001.0	1,001.0	4.5	4.5	13.71	200.4	48.9	206.3	197.3	9.01	22.899	
1,100.0	1,100.0	1,101.0	1,101.0	4.8	4.8	13.71	200.4	48.9	206.3	196.8	9.56	21.589	
1,200.0	1,200.0	1,201.0	1,201.0	5.1	5.1	13.71	200.4	48.9	206.3	196.2	10.12	20.378	
1,300.0	1,300.0	1,301.0	1,301.0	5.4	5.4	13.71	200.4	48.9	206.3	195.6	10.71	19.263	
1,400.0	1,400.0	1,401.0	1,401.0	5.7	5.7	13.71	200.4	48.9	206.3	195.0	11.31	18.239	
1,500.0	1,500.0	1,501.0	1,501.0	6.0	6.0	13.71	200.4	48.9	206.3	194.4	11.93	17.301	
1,600.0	1,600.0	1,601.0	1,601.0	6.3	6.3	13.71	200.4	48.9	206.3	193.8	12.55	16.439	
1,700.0	1,700.0	1,701.0	1,701.0	6.6	6.6	13.71	200.4	48.9	206.3	193.1	13.18	15.649	
1,800.0	1,800.0	1,801.0	1,801.0	6.9	6.9	13.71	200.4	48.9	206.3	192.5	13.83	14.922	
1,900.0	1,900.0	1,901.0	1,901.0	7.2	7.2	13.71	200.4	48.9	206.3	191.8	14.48	14.252	
2,000.0	2,000.0	2,001.0	2,001.0	7.6	7.6	13.71	200.4	48.9	206.3	191.2	15.13	13.635	
2,100.0	2,100.0	2,101.0	2,101.0	7.9	7.9	13.71	200.4	48.9	206.3	190.5	15.79	13.065	
2,200.0	2,200.0	2,201.0	2,201.0	8.2	8.2	13.71	200.4	48.9	206.3	189.9	16.46	12.536	
2,300.0	2,300.0	2,301.0	2,301.0	8.6	8.6	13.71	200.4	48.9	206.3	189.2	17.13	12.046	
2,400.0	2,400.0	2,401.0	2,401.0	8.9	8.9	13.71	200.4	48.9	206.3	188.5	17.80	11.591	
2,500.0	2,500.0	2,501.0	2,501.0	9.2	9.2	13.71	200.4	48.9	206.3	187.8	18.48	11.166	
2,501.9	2,501.9	2,503.0	2,503.0	9.2	9.2	123.77	200.4	48.9	206.3	187.8	18.49	11.159 CC	
2,600.0	2,600.0	2,603.6	2,603.6	9.6	9.6	123.69	200.2	47.0	206.6	187.5	19.14	10.795	
2,700.0	2,699.8	2,706.2	2,706.1	9.9	9.9	123.47	199.5	41.5	207.6	187.8	19.79	10.492	
2,800.0	2,799.6	2,808.5	2,807.9	10.2	10.2	122.74	198.4	32.4	208.4	187.9	20.44	10.193	
2,900.0	2,899.4	2,908.5	2,907.3	10.5	10.6	121.65	197.1	22.1	208.7	187.6	21.10	9.890	
3,000.0	2,999.1	3,008.4	3,006.7	10.9	10.9	120.56	195.9	11.7	209.0	187.3	21.76	9.606	
3,100.0	3,098.9	3,108.3	3,106.1	11.2	11.2	119.47	194.6	1.3	209.4	187.0	22.42	9.341	
3,200.0	3,198.6	3,208.2	3,205.4	11.5	11.6	118.39	193.3	-9.0	210.0	186.9	23.09	9.092	
3,300.0	3,298.4	3,308.1	3,304.8	11.9	11.9	117.32	192.1	-19.4	210.5	186.8	23.76	8.860	
3,400.0	3,398.1	3,408.1	3,404.2	12.2	12.3	116.25	190.8	-29.8	211.2	186.8	24.44	8.642 ES	
3,500.0	3,497.9	3,508.0	3,503.6	12.5	12.6	115.18	189.5	-40.1	211.9	186.8	25.12	8.438	
3,600.0	3,597.6	3,607.9	3,602.9	12.9	12.9	114.13	188.2	-50.5	212.7	186.9	25.80	8.246	
3,700.0	3,697.4	3,707.8	3,702.3	13.2	13.3	113.08	187.0	-60.9	213.6	187.1	26.48	8.066	
3,800.0	3,797.2	3,807.7	3,801.7	13.5	13.6	112.05	185.7	-71.2	214.6	187.4	27.17	7.897	
3,900.0	3,896.9	3,907.7	3,901.0	13.9	14.0	111.02	184.4	-81.6	215.6	187.7	27.86	7.739	
4,000.0	3,996.7	4,007.6	4,000.4	14.2	14.3	110.00	183.1	-92.0	216.7	188.1	28.55	7.590	
4,100.0	4,096.4	4,107.5	4,099.8	14.6	14.7	108.99	181.9	-102.3	217.8	188.6	29.24	7.449	
4,200.0	4,196.2	4,207.4	4,199.2	14.9	15.0	107.99	180.6	-112.7	219.0	189.1	29.93	7.318	
4,300.0	4,295.9	4,307.3	4,298.5	15.3	15.4	107.01	179.3	-123.1	220.3	189.7	30.63	7.193	
4,400.0	4,395.7	4,407.3	4,397.9	15.6	15.7	106.03	178.1	-133.4	221.7	190.3	31.32	7.076	
4,500.0	4,495.5	4,507.2	4,497.3	16.0	16.1	105.07	176.8	-143.8	223.1	191.1	32.02	6.966	
4,600.0	4,595.2	4,607.1	4,596.7	16.3	16.4	104.12	175.5	-154.2	224.6	191.8	32.72	6.862	
4,700.0	4,695.0	4,707.0	4,696.0	16.7	16.8	103.19	174.2	-164.5	226.1	192.7	33.42	6.764	
4,800.0	4,794.7	4,806.9	4,795.4	17.0	17.1	102.26	173.0	-174.9	227.7	193.6	34.13	6.672	
4,900.0	4,894.5	4,906.9	4,894.8	17.4	17.5	101.35	171.7	-185.3	229.3	194.5	34.83	6.585	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design		BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 301H - OWB - PWP											Offset Site Error:		3.0 usft
Survey Program: 0-MWD+IFR1+FDIR													Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis		Distance								Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor			
5,000.0	4,994.2	5,006.8	4,994.1	17.7	17.8	100.45	170.4	-195.6	231.0	195.5	35.53	6.502			
5,100.0	5,094.0	5,106.7	5,093.5	18.1	18.2	99.57	169.1	-206.0	232.8	196.6	36.24	6.424			
5,200.0	5,193.7	5,206.6	5,192.9	18.4	18.5	98.70	167.9	-216.4	234.6	197.7	36.95	6.351			
5,300.0	5,293.5	5,306.5	5,292.3	18.8	18.9	97.84	166.6	-226.7	236.5	198.9	37.65	6.281			
5,400.0	5,393.3	5,406.5	5,391.6	19.1	19.3	97.00	165.3	-237.1	238.4	200.1	38.36	6.216			
5,500.0	5,493.0	5,506.4	5,491.0	19.5	19.6	96.17	164.1	-247.5	240.4	201.3	39.07	6.154			
5,600.0	5,592.8	5,606.3	5,590.4	19.8	20.0	95.35	162.8	-257.8	242.4	202.7	39.78	6.095			
5,700.0	5,692.5	5,706.2	5,689.8	20.2	20.3	94.55	161.5	-268.2	244.5	204.0	40.49	6.039			
5,800.0	5,792.3	5,806.1	5,789.1	20.5	20.7	93.76	160.2	-278.6	246.6	205.4	41.20	5.986			
5,900.0	5,892.0	5,906.1	5,888.5	20.9	21.0	92.99	159.0	-288.9	248.8	206.9	41.91	5.936			
6,000.0	5,991.8	6,006.0	5,987.9	21.2	21.4	92.22	157.7	-299.3	251.0	208.4	42.63	5.889			
6,100.0	6,091.6	6,105.9	6,087.3	21.6	21.8	91.48	156.4	-309.7	253.3	209.9	43.34	5.844			
6,200.0	6,191.3	6,205.8	6,186.6	21.9	22.1	90.74	155.1	-320.0	255.6	211.5	44.05	5.802			
6,300.0	6,291.1	6,305.7	6,286.0	22.3	22.5	90.02	153.9	-330.4	257.9	213.2	44.77	5.762			
6,400.0	6,390.8	6,405.7	6,385.4	22.7	22.8	89.31	152.6	-340.8	260.3	214.8	45.48	5.724			
6,500.0	6,490.6	6,505.6	6,484.7	23.0	23.2	88.61	151.3	-351.1	262.7	216.5	46.20	5.687			
6,600.0	6,590.3	6,605.5	6,584.1	23.4	23.6	87.93	150.0	-361.5	265.2	218.3	46.91	5.653			
6,700.0	6,690.1	6,705.4	6,683.5	23.7	23.9	87.26	148.8	-371.9	267.7	220.1	47.63	5.620			
6,800.0	6,789.9	6,805.4	6,782.9	24.1	24.3	86.60	147.5	-382.2	270.2	221.9	48.34	5.590			
6,900.0	6,889.6	6,905.3	6,882.2	24.4	24.6	85.96	146.2	-392.6	272.8	223.7	49.06	5.560			
7,000.0	6,989.4	7,005.2	6,981.6	24.8	25.0	85.32	145.0	-403.0	275.4	225.6	49.78	5.532			
7,100.0	7,089.1	7,105.1	7,081.0	25.1	25.4	84.70	143.7	-413.3	278.0	227.5	50.50	5.506			
7,200.0	7,188.9	7,205.0	7,180.4	25.5	25.7	84.09	142.4	-423.7	280.7	229.5	51.21	5.481			
7,300.0	7,288.6	7,305.0	7,279.7	25.9	26.1	83.50	141.1	-434.1	283.4	231.5	51.93	5.457			
7,400.0	7,388.4	7,404.9	7,379.1	26.2	26.4	82.91	139.9	-444.4	286.1	233.5	52.65	5.434			
7,500.0	7,488.1	7,504.8	7,478.5	26.6	26.8	82.33	138.6	-454.8	288.9	235.5	53.37	5.413			
7,600.0	7,587.9	7,604.7	7,577.8	26.9	27.2	81.77	137.3	-465.2	291.7	237.6	54.09	5.392			
7,700.0	7,687.7	7,704.6	7,677.2	27.3	27.5	81.21	136.0	-475.5	294.5	239.7	54.81	5.373			
7,805.4	7,792.8	7,810.0	7,782.0	27.7	27.9	80.64	134.7	-486.5	297.5	241.9	55.57	5.353			
7,900.0	7,887.2	7,904.4	7,875.9	28.0	28.3	80.02	133.5	-496.3	300.3	244.1	56.25	5.339			
8,000.0	7,987.1	8,004.2	7,975.2	28.4	28.6	79.06	132.2	-506.6	303.7	246.7	56.97	5.331 SF			
8,100.0	8,087.1	8,103.9	8,074.3	28.7	29.0	77.82	131.0	-517.0	307.5	249.8	57.68	5.331			
8,205.4	8,192.5	8,208.9	8,178.7	29.1	29.4	-33.85	129.6	-527.9	312.1	253.7	58.43	5.342			
8,300.0	8,287.1	8,302.9	8,272.2	29.4	29.7	-35.43	128.4	-537.6	316.7	257.7	59.09	5.360			
8,400.0	8,387.1	8,402.4	8,371.2	29.8	30.1	-37.06	127.2	-547.9	321.9	262.1	59.79	5.383			
8,500.0	8,487.1	8,501.8	8,470.1	30.1	30.4	-38.64	125.9	-558.2	327.3	266.8	60.49	5.410			
8,600.0	8,587.1	8,601.3	8,569.0	30.4	30.8	-40.17	124.6	-568.6	332.9	271.7	61.20	5.440			
8,700.0	8,687.1	8,700.7	8,667.9	30.8	31.1	-41.64	123.4	-578.9	338.7	276.8	61.90	5.473			
8,800.0	8,787.1	8,800.2	8,766.8	31.1	31.5	-43.07	122.1	-589.2	344.8	282.2	62.60	5.508			
8,900.0	8,887.1	8,899.7	8,865.7	31.5	31.9	-44.44	120.8	-599.5	351.1	287.8	63.30	5.546			
9,000.0	8,987.1	8,999.1	8,964.6	31.8	32.2	-45.77	119.6	-609.8	357.6	293.6	64.00	5.586			
9,100.0	9,087.1	9,098.6	9,063.5	32.2	32.6	-47.05	118.3	-620.2	364.2	299.5	64.71	5.629			
9,200.0	9,187.1	9,177.9	9,142.4	32.5	32.9	-47.97	118.2	-628.8	372.5	307.3	65.18	5.715			
9,300.0	9,287.1	9,239.3	9,202.8	32.9	33.1	-48.27	123.7	-637.9	389.6	324.5	65.09	5.986			
9,400.0	9,387.1	9,300.0	9,261.3	33.2	33.3	-48.17	135.0	-649.5	416.1	351.4	64.67	6.435			
9,500.0	9,487.1	9,350.0	9,308.1	33.5	33.5	-47.81	148.6	-660.8	451.2	387.6	63.62	7.093			
9,600.0	9,587.1	9,400.0	9,353.2	33.9	33.7	-47.25	165.9	-673.6	494.3	431.8	62.47	7.913			
9,700.0	9,687.1	9,450.0	9,396.3	34.2	33.8	-46.54	186.8	-687.8	544.3	483.0	61.36	8.872			
9,800.0	9,787.1	9,500.0	9,437.1	34.6	33.9	-45.71	211.1	-703.3	600.8	540.4	60.37	9.951			
9,900.0	9,887.1	9,532.0	9,461.8	34.9	34.0	-45.15	228.4	-713.8	662.6	603.8	58.74	11.279			
10,000.0	9,987.1	9,566.3	9,487.0	35.3	34.1	-44.52	248.4	-725.6	729.2	671.7	57.44	12.694			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 301H - OWB - PWP		Offset Site Error:	3.0 usft
Survey Program: 0-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft		
Reference		Offset		Semi Major Axis			Distance							Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor				
							+N/-S (usft)	+E/-W (usft)								
10,100.0	10,087.1	9,600.0	9,510.5	35.6	34.2	-43.88	269.4	-737.7	799.8	743.5	56.34	14.197				
10,200.0	10,187.1	9,624.5	9,526.6	36.0	34.2	-43.42	285.5	-746.7	873.9	818.8	55.08	15.866				
10,300.0	10,287.1	9,650.0	9,542.5	36.3	34.3	-42.93	303.0	-756.4	951.0	896.9	54.09	17.582				
10,337.9	10,325.0	9,650.0	9,542.5	36.5	34.3	-42.93	303.0	-756.4	981.0	927.6	53.43	18.361				
10,350.0	10,337.1	9,650.0	9,542.5	36.5	34.3	-41.52	303.0	-756.4	990.6	937.4	53.22	18.613				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design		BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 302H - OWB - PWP										Offset Site Error:		3.0 usft
Survey Program:		0-Standard Keeper 104, 9190-MWD+IFR1+FDIR										Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis		Distance								Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	1.0	1.0	3.0	3.0	21.45	200.8	78.9	215.7					
100.0	100.0	101.0	101.0	3.0	3.0	21.45	200.8	78.9	215.7	209.7	6.00	35.931		
200.0	200.0	201.0	201.0	3.0	3.0	21.45	200.8	78.9	215.7	209.7	6.04	35.684		
300.0	300.0	301.0	301.0	3.1	3.0	21.45	200.8	78.9	215.7	209.6	6.13	35.172		
400.0	400.0	401.0	401.0	3.2	3.0	21.45	200.8	78.9	215.7	209.4	6.26	34.436		
500.0	500.0	501.0	501.0	3.4	3.1	21.45	200.8	78.9	215.7	209.3	6.43	33.525		
600.0	600.0	601.0	601.0	3.6	3.1	21.45	200.8	78.9	215.7	209.1	6.64	32.489		
700.0	700.0	701.0	701.0	3.8	3.1	21.45	200.8	78.9	215.7	208.8	6.87	31.376		
800.0	800.0	801.0	801.0	4.0	3.2	21.45	200.8	78.9	215.7	208.6	7.14	30.224		
900.0	900.0	901.0	901.0	4.2	3.2	21.45	200.8	78.9	215.7	208.3	7.42	29.065		
1,000.0	1,000.0	1,001.0	1,001.0	4.5	3.2	21.45	200.8	78.9	215.7	208.0	7.73	27.920		
1,100.0	1,100.0	1,101.0	1,101.0	4.8	3.3	21.45	200.8	78.9	215.7	207.7	8.05	26.806		
1,200.0	1,200.0	1,201.0	1,201.0	5.1	3.4	21.45	200.8	78.9	215.7	207.3	8.38	25.732		
1,300.0	1,300.0	1,301.0	1,301.0	5.4	3.4	21.45	200.8	78.9	215.7	207.0	8.73	24.705		
1,400.0	1,400.0	1,401.0	1,401.0	5.7	3.5	21.45	200.8	78.9	215.7	206.6	9.09	23.727		
1,500.0	1,500.0	1,501.0	1,501.0	6.0	3.5	21.45	200.8	78.9	215.7	206.2	9.46	22.800		
1,600.0	1,600.0	1,601.0	1,601.0	6.3	3.6	21.45	200.8	78.9	215.7	205.9	9.84	21.922		
1,700.0	1,700.0	1,701.0	1,701.0	6.6	3.7	21.45	200.8	78.9	215.7	205.5	10.23	21.094		
1,800.0	1,800.0	1,801.0	1,801.0	6.9	3.8	21.45	200.8	78.9	215.7	205.1	10.62	20.313		
1,900.0	1,900.0	1,901.0	1,901.0	7.2	3.9	21.45	200.8	78.9	215.7	204.7	11.02	19.576		
2,000.0	2,000.0	2,001.0	2,001.0	7.6	3.9	21.45	200.8	78.9	215.7	204.3	11.42	18.882		
2,100.0	2,100.0	2,101.0	2,101.0	7.9	4.0	21.45	200.8	78.9	215.7	203.9	11.83	18.227		
2,200.0	2,200.0	2,201.0	2,201.0	8.2	4.1	21.45	200.8	78.9	215.7	203.5	12.25	17.609		
2,300.0	2,300.0	2,301.0	2,301.0	8.6	4.2	21.45	200.8	78.9	215.7	203.0	12.67	17.026		
2,400.0	2,400.0	2,401.0	2,401.0	8.9	4.3	21.45	200.8	78.9	215.7	202.6	13.09	16.476		
2,500.0	2,500.0	2,501.1	2,501.1	9.2	4.4	21.45	200.8	78.9	215.7	202.2	13.52	15.956		
2,600.0	2,600.0	2,606.3	2,606.3	9.6	4.4	131.49	200.1	77.0	215.6	201.7	13.88	15.534		
2,688.3	2,688.1	2,698.7	2,698.5	9.8	4.5	131.44	198.4	72.4	215.5	201.3	14.15	15.232		
2,700.0	2,699.8	2,710.4	2,710.2	9.9	4.5	131.44	198.1	71.7	215.5	201.3	14.18	15.194		
2,800.0	2,799.6	2,810.4	2,810.0	10.2	4.5	131.52	195.9	65.5	215.7	201.3	14.49	14.885		
2,900.0	2,899.4	2,910.4	2,909.8	10.5	4.5	131.60	193.6	59.4	216.0	201.2	14.81	14.585		
3,000.0	2,999.1	3,010.4	3,009.6	10.9	4.5	131.67	191.4	53.2	216.3	201.2	15.13	14.293		
3,100.0	3,098.9	3,110.4	3,109.3	11.2	4.5	131.75	189.2	47.0	216.6	201.1	15.46	14.009		
3,200.0	3,198.6	3,210.4	3,209.1	11.5	4.6	131.83	186.9	40.8	216.8	201.0	15.79	13.733		
3,300.0	3,298.4	3,310.4	3,308.9	11.9	4.6	131.91	184.7	34.6	217.1	201.0	16.12	13.465		
3,400.0	3,398.1	3,410.4	3,408.7	12.2	4.6	131.99	182.4	28.5	217.4	200.9	16.46	13.205		
3,500.0	3,497.9	3,510.4	3,508.5	12.5	4.7	132.06	180.2	22.3	217.7	200.8	16.81	12.952		
3,600.0	3,597.6	3,610.4	3,608.2	12.9	4.7	132.14	177.9	16.1	217.9	200.8	17.15	12.706		
3,700.0	3,697.4	3,710.4	3,708.0	13.2	4.7	132.22	175.7	9.9	218.2	200.7	17.50	12.467		
3,800.0	3,797.2	3,810.4	3,807.8	13.5	4.8	132.29	173.4	3.7	218.5	200.6	17.86	12.235		
3,900.0	3,896.9	3,910.4	3,907.6	13.9	4.8	132.37	171.2	-2.4	218.8	200.5	18.21	12.010		
4,000.0	3,996.7	4,010.4	4,007.4	14.2	4.9	132.45	168.9	-8.6	219.0	200.5	18.58	11.791		
4,100.0	4,096.4	4,110.4	4,107.2	14.6	5.0	132.52	166.7	-14.8	219.3	200.4	18.94	11.579		
4,200.0	4,196.2	4,210.4	4,206.9	14.9	5.0	132.60	164.4	-21.0	219.6	200.3	19.31	11.372		
4,300.0	4,295.9	4,310.4	4,306.7	15.3	5.1	132.68	162.2	-27.1	219.9	200.2	19.68	11.172		
4,400.0	4,395.7	4,410.4	4,406.5	15.6	5.1	132.75	159.9	-33.3	220.1	200.1	20.05	10.977		
4,500.0	4,495.5	4,510.4	4,506.3	16.0	5.2	132.83	157.7	-39.5	220.4	200.0	20.43	10.787		
4,600.0	4,595.2	4,610.4	4,606.1	16.3	5.3	132.90	155.4	-45.7	220.7	199.9	20.81	10.603		
4,700.0	4,695.0	4,710.4	4,705.9	16.7	5.4	132.98	153.2	-51.9	221.0	199.8	21.20	10.425		
4,800.0	4,794.7	4,810.4	4,805.6	17.0	5.4	133.05	150.9	-58.0	221.2	199.7	21.58	10.251		
4,900.0	4,894.5	4,910.4	4,905.4	17.4	5.5	133.13	148.7	-64.2	221.5	199.6	21.97	10.082		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 9190-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Semi Major Axis Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,000.0	4,994.2	5,010.4	5,005.2	17.7	5.6	133.20	146.4	-70.4	221.8	199.4	22.37	9.917	
5,100.0	5,094.0	5,110.4	5,105.0	18.1	5.7	133.28	144.2	-76.6	222.1	199.3	22.76	9.758	
5,200.0	5,193.7	5,210.4	5,204.8	18.4	5.8	133.35	141.9	-82.8	222.4	199.2	23.16	9.602	
5,300.0	5,293.5	5,310.4	5,304.6	18.8	5.8	133.42	139.7	-88.9	222.6	199.1	23.56	9.451	
5,400.0	5,393.3	5,410.4	5,404.3	19.1	5.9	133.50	137.4	-95.1	222.9	199.0	23.96	9.304	
5,500.0	5,493.0	5,510.4	5,504.1	19.5	6.0	133.57	135.2	-101.3	223.2	198.8	24.37	9.161	
5,600.0	5,592.8	5,610.4	5,603.9	19.8	6.1	133.64	132.9	-107.5	223.5	198.7	24.77	9.022	
5,700.0	5,692.5	5,710.4	5,703.7	20.2	6.2	133.72	130.7	-113.6	223.8	198.6	25.18	8.886	
5,800.0	5,792.3	5,810.4	5,803.5	20.5	6.3	133.79	128.4	-119.8	224.1	198.5	25.59	8.754	
5,900.0	5,892.0	5,910.4	5,903.3	20.9	6.4	133.86	126.2	-126.0	224.3	198.3	26.01	8.626	
6,000.0	5,991.8	6,010.4	6,003.0	21.2	6.5	133.94	123.9	-132.2	224.6	198.2	26.42	8.501	
6,100.0	6,091.6	6,110.4	6,102.8	21.6	6.6	134.01	121.7	-138.4	224.9	198.1	26.84	8.379	
6,200.0	6,191.3	6,210.4	6,202.6	21.9	6.7	134.08	119.4	-144.5	225.2	197.9	27.26	8.260	
6,300.0	6,291.1	6,310.4	6,302.4	22.3	6.8	134.15	117.2	-150.7	225.5	197.8	27.68	8.145	
6,400.0	6,390.8	6,410.4	6,402.2	22.7	6.9	134.22	114.9	-156.9	225.8	197.7	28.11	8.032	
6,500.0	6,490.6	6,510.4	6,501.9	23.0	7.0	134.30	112.7	-163.1	226.0	197.5	28.53	7.922	
6,600.0	6,590.3	6,610.4	6,601.7	23.4	7.1	134.37	110.4	-169.3	226.3	197.4	28.96	7.815	
6,700.0	6,690.1	6,710.4	6,701.5	23.7	7.2	134.44	108.2	-175.4	226.6	197.2	29.39	7.711	
6,800.0	6,789.9	6,810.4	6,801.3	24.1	7.3	134.51	105.9	-181.6	226.9	197.1	29.82	7.609	
6,900.0	6,889.6	6,910.4	6,901.1	24.4	7.4	134.58	103.7	-187.8	227.2	196.9	30.25	7.510	
7,000.0	6,989.4	7,010.4	7,000.9	24.8	7.5	134.65	101.4	-194.0	227.5	196.8	30.68	7.414	
7,100.0	7,089.1	7,110.4	7,100.6	25.1	7.6	134.72	99.2	-200.1	227.8	196.6	31.12	7.319	
7,200.0	7,188.9	7,210.4	7,200.4	25.5	7.7	134.79	97.0	-206.3	228.0	196.5	31.55	7.227	
7,300.0	7,288.6	7,310.3	7,300.2	25.9	7.8	134.86	94.7	-212.5	228.3	196.3	31.99	7.137	
7,400.0	7,388.4	7,410.3	7,400.0	26.2	7.9	134.93	92.5	-218.7	228.6	196.2	32.43	7.049	
7,500.0	7,488.1	7,510.3	7,499.8	26.6	8.0	135.00	90.2	-224.9	228.9	196.0	32.87	6.964	
7,600.0	7,587.9	7,610.3	7,599.6	26.9	8.1	135.07	88.0	-231.0	229.2	195.9	33.31	6.880	
7,700.0	7,687.7	7,710.3	7,699.3	27.3	8.2	135.14	85.7	-237.2	229.5	195.7	33.76	6.798	
7,805.4	7,792.8	7,815.8	7,804.5	27.7	8.3	135.22	83.3	-243.7	229.8	195.6	34.22	6.714	
7,900.0	7,892.2	7,910.3	7,898.9	28.0	8.4	135.14	81.2	-249.6	229.5	194.9	34.64	6.625	
8,000.0	7,987.1	8,010.3	7,998.7	28.4	8.6	134.75	79.0	-255.8	228.0	192.9	35.08	6.500	
8,100.0	8,087.1	8,110.2	8,098.4	28.7	8.7	134.04	76.7	-261.9	225.3	189.8	35.52	6.344	
8,205.4	8,192.5	8,215.5	8,203.4	29.1	8.8	22.84	74.3	-268.4	221.2	185.3	35.96	6.151	
8,300.0	8,287.1	8,309.9	8,297.6	29.4	8.9	21.63	72.2	-274.3	217.0	180.7	36.36	5.969	
8,400.0	8,387.1	8,409.7	8,397.1	29.8	9.0	20.31	70.0	-280.4	212.7	175.9	36.78	5.784	
8,500.0	8,487.1	8,509.4	8,496.7	30.1	9.1	18.94	67.7	-286.6	208.5	171.3	37.20	5.606	
8,600.0	8,587.1	8,609.2	8,596.3	30.4	9.2	17.51	65.5	-292.8	204.4	166.8	37.62	5.435	
8,700.0	8,687.1	8,709.0	8,695.8	30.8	9.3	16.02	63.2	-298.9	200.5	162.5	38.04	5.271	
8,800.0	8,787.1	8,808.8	8,795.4	31.1	9.5	14.47	61.0	-305.1	196.7	158.2	38.47	5.114	
8,900.0	8,887.1	8,908.6	8,895.0	31.5	9.6	12.86	58.8	-311.2	193.1	154.2	38.89	4.963	
9,000.0	8,987.1	9,008.4	8,994.5	31.8	9.7	11.20	56.5	-317.4	189.6	150.2	39.32	4.820	
9,100.0	9,087.1	9,108.1	9,094.1	32.2	9.8	9.47	54.3	-323.6	186.2	146.5	39.76	4.684	
9,175.4	9,162.5	9,177.7	9,163.5	32.4	9.9	8.22	53.0	-327.9	184.2	144.1	40.09	4.595 CC, ES, SF	
9,200.0	9,187.1	9,200.0	9,185.8	32.5	9.9	7.76	53.6	-329.3	184.7	144.5	40.18	4.596	
9,300.0	9,287.1	9,271.0	9,256.2	32.9	9.9	6.14	61.4	-333.7	194.5	154.0	40.47	4.805	
9,400.0	9,387.1	9,342.6	9,325.6	33.2	9.9	4.44	78.0	-338.1	217.2	176.4	40.80	5.323	
9,500.0	9,487.1	9,409.0	9,387.7	33.5	10.0	3.00	101.1	-342.1	251.6	210.5	41.06	6.128	
9,600.0	9,587.1	9,469.4	9,441.5	33.9	10.0	1.90	128.2	-345.6	296.4	255.2	41.21	7.193	
9,700.0	9,687.1	9,523.3	9,486.9	34.2	10.0	1.11	157.0	-348.7	350.0	308.7	41.25	8.483	
9,800.0	9,787.1	9,570.9	9,524.6	34.6	10.1	0.55	186.0	-351.2	410.9	369.6	41.23	9.965	
9,900.0	9,887.1	9,612.7	9,555.7	34.9	10.1	0.15	213.9	-353.3	477.8	436.6	41.17	11.606	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 302H - OWB - PWP													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 9190-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance									Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,000.0	9,987.1	9,650.0	9,581.6	35.3	10.1	-0.14	240.7	-355.1	549.7	508.6	41.11	13.371		
10,100.0	10,087.1	9,681.5	9,602.1	35.6	10.2	-0.34	264.6	-356.5	625.6	584.6	41.04	15.243		
10,200.0	10,187.1	9,700.0	9,613.5	36.0	10.2	-0.44	279.1	-357.3	705.0	664.1	40.88	17.244		
10,300.0	10,287.1	9,734.7	9,633.5	36.3	10.3	-0.60	307.3	-358.8	786.8	745.8	41.00	19.192		
10,337.9	10,325.0	9,750.0	9,641.9	36.5	10.3	-0.66	320.2	-359.4	818.6	777.5	41.08	19.928		
10,350.0	10,337.1	9,750.0	9,641.9	36.5	10.3	-0.30	320.2	-359.4	828.6	787.6	41.05	20.187		
10,400.0	10,387.0	9,750.0	9,641.9	36.7	10.3	-0.26	320.2	-359.4	869.3	828.4	40.92	21.244		
10,450.0	10,436.4	9,770.3	9,652.4	36.8	10.3	-0.29	337.5	-360.1	907.8	866.8	40.99	22.146		
10,500.0	10,484.9	9,783.4	9,658.8	37.0	10.3	-0.30	348.9	-360.6	944.2	903.3	40.97	23.047		
10,550.0	10,532.3	9,800.0	9,666.6	37.2	10.4	-0.31	363.6	-361.2	978.4	937.5	40.97	23.882		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Distance							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	1.0	1.0	3.0	3.0	28.45	201.0	108.9	228.6				
100.0	100.0	101.0	101.0	3.0	3.0	28.45	201.0	108.9	228.6	222.6	6.01	38.063	
200.0	200.0	201.0	201.0	3.0	3.0	28.45	201.0	108.9	228.6	222.5	6.08	37.597	
300.0	300.0	301.0	301.0	3.1	3.1	28.45	201.0	108.9	228.6	222.4	6.24	36.654	
400.0	400.0	401.0	401.0	3.2	3.2	28.45	201.0	108.9	228.6	222.1	6.47	35.336	
500.0	500.0	501.0	501.0	3.4	3.4	28.45	201.0	108.9	228.6	221.8	6.77	33.766	
600.0	600.0	601.0	601.0	3.6	3.6	28.45	201.0	108.9	228.6	221.5	7.13	32.059	
700.0	700.0	701.0	701.0	3.8	3.8	28.45	201.0	108.9	228.6	221.1	7.54	30.309	
800.0	800.0	801.0	801.0	4.0	4.0	28.45	201.0	108.9	228.6	220.6	8.00	28.586	
900.0	900.0	901.0	901.0	4.2	4.2	28.45	201.0	108.9	228.6	220.1	8.49	26.932	
1,000.0	1,000.0	1,001.0	1,001.0	4.5	4.5	28.45	201.0	108.9	228.6	219.6	9.01	25.373	
1,100.0	1,100.0	1,101.0	1,101.0	4.8	4.8	28.45	201.0	108.9	228.6	219.1	9.56	23.922	
1,200.0	1,200.0	1,201.0	1,201.0	5.1	5.1	28.45	201.0	108.9	228.6	218.5	10.12	22.580	
1,300.0	1,300.0	1,301.0	1,301.0	5.4	5.4	28.45	201.0	108.9	228.6	217.9	10.71	21.344	
1,400.0	1,400.0	1,401.0	1,401.0	5.7	5.7	28.45	201.0	108.9	228.6	217.3	11.31	20.210	
1,500.0	1,500.0	1,501.0	1,501.0	6.0	6.0	28.45	201.0	108.9	228.6	216.7	11.93	19.170	
1,600.0	1,600.0	1,601.0	1,601.0	6.3	6.3	28.45	201.0	108.9	228.6	216.1	12.55	18.216	
1,700.0	1,700.0	1,701.0	1,701.0	6.6	6.6	28.45	201.0	108.9	228.6	215.4	13.18	17.339	
1,800.0	1,800.0	1,801.0	1,801.0	6.9	6.9	28.45	201.0	108.9	228.6	214.8	13.83	16.534	
1,900.0	1,900.0	1,901.0	1,901.0	7.2	7.2	28.45	201.0	108.9	228.6	214.1	14.48	15.792	
2,000.0	2,000.0	2,001.0	2,001.0	7.6	7.6	28.45	201.0	108.9	228.6	213.5	15.13	15.108	
2,100.0	2,100.0	2,101.0	2,101.0	7.9	7.9	28.45	201.0	108.9	228.6	212.8	15.79	14.476	
2,200.0	2,200.0	2,201.0	2,201.0	8.2	8.2	28.45	201.0	108.9	228.6	212.2	16.46	13.891	
2,300.0	2,300.0	2,301.0	2,301.0	8.6	8.6	28.45	201.0	108.9	228.6	211.5	17.13	13.348	
2,400.0	2,400.0	2,401.0	2,401.0	8.9	8.9	28.45	201.0	108.9	228.6	210.8	17.80	12.843	
2,500.0	2,500.0	2,501.0	2,501.0	9.2	9.2	28.45	201.0	108.9	228.6	210.1	18.48	12.373 CC, ES	
2,600.0	2,600.0	2,601.0	2,601.0	9.6	9.6	138.77	201.0	108.9	229.9	210.8	19.14	12.009	
2,700.0	2,699.8	2,700.8	2,700.8	9.9	9.9	139.57	201.0	108.9	233.9	214.1	19.81	11.809	
2,800.0	2,799.6	2,800.6	2,800.6	10.2	10.3	140.65	201.0	108.9	239.2	218.8	20.47	11.688	
2,900.0	2,899.4	2,900.4	2,900.4	10.5	10.6	141.68	201.0	108.9	244.7	223.5	21.14	11.576	
3,000.0	2,999.1	3,000.1	3,000.1	10.9	10.9	142.67	201.0	108.9	250.2	228.4	21.81	11.474	
3,100.0	3,098.9	3,099.9	3,099.9	11.2	11.3	143.62	201.0	108.9	255.8	233.3	22.48	11.379	
3,200.0	3,198.6	3,199.6	3,199.6	11.5	11.6	144.53	201.0	108.9	261.4	238.3	23.15	11.291	
3,300.0	3,298.4	3,299.4	3,299.4	11.9	12.0	145.39	201.0	108.9	267.2	243.3	23.83	11.209	
3,400.0	3,398.1	3,399.1	3,399.1	12.2	12.3	146.23	201.0	108.9	272.9	248.4	24.51	11.134	
3,500.0	3,497.9	3,498.9	3,498.9	12.5	12.7	147.02	201.0	108.9	278.8	253.6	25.20	11.064	
3,600.0	3,597.6	3,598.6	3,598.6	12.9	13.0	147.79	201.0	108.9	284.6	258.8	25.88	10.999	
3,700.0	3,697.4	3,698.4	3,698.4	13.2	13.4	148.52	201.0	108.9	290.6	264.0	26.57	10.938	
3,800.0	3,797.2	3,798.2	3,798.2	13.5	13.7	149.22	201.0	108.9	296.5	269.3	27.25	10.881	
3,900.0	3,896.9	3,897.9	3,897.9	13.9	14.1	149.90	201.0	108.9	302.6	274.6	27.94	10.828	
4,000.0	3,996.7	3,997.7	3,997.7	14.2	14.4	150.55	201.0	108.9	308.6	280.0	28.63	10.779	
4,100.0	4,096.4	4,097.4	4,097.4	14.6	14.8	151.17	201.0	108.9	314.7	285.4	29.32	10.732	
4,200.0	4,196.2	4,197.2	4,197.2	14.9	15.1	151.77	201.0	108.9	320.8	290.8	30.02	10.689	
4,300.0	4,295.9	4,296.9	4,296.9	15.3	15.5	152.35	201.0	108.9	327.0	296.3	30.71	10.648	
4,400.0	4,395.7	4,396.7	4,396.7	15.6	15.8	152.91	201.0	108.9	333.2	301.8	31.41	10.610	
4,500.0	4,495.5	4,496.5	4,496.5	16.0	16.2	153.44	201.0	108.9	339.4	307.3	32.10	10.573	
4,600.0	4,595.2	4,596.2	4,596.2	16.3	16.5	153.96	201.0	108.9	345.7	312.9	32.80	10.539	
4,700.0	4,695.0	4,696.0	4,696.0	16.7	16.9	154.46	201.0	108.9	352.0	318.5	33.50	10.507	
4,800.0	4,794.7	4,795.7	4,795.7	17.0	17.2	154.94	201.0	108.9	358.3	324.1	34.20	10.477	
4,900.0	4,894.5	4,895.5	4,895.5	17.4	17.6	155.40	201.0	108.9	364.6	329.7	34.90	10.449	
5,000.0	4,994.2	4,995.2	4,995.2	17.7	17.9	155.85	201.0	108.9	371.0	335.4	35.60	10.422	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

6/8/2020 12:10:30PM

Page 14

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference	Offset	Semi Major Axis	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,100.0	5,094.0	5,095.0	5,095.0	18.1	18.3	156.28		201.0	108.9	377.4	341.1	36.30	10.396	
5,200.0	5,193.7	5,194.7	5,194.7	18.4	18.6	156.70		201.0	108.9	383.8	346.8	37.00	10.372	
5,300.0	5,293.5	5,294.5	5,294.5	18.8	19.0	157.11		201.0	108.9	390.2	352.5	37.70	10.349	
5,400.0	5,393.3	5,394.3	5,394.3	19.1	19.3	157.50		201.0	108.9	396.6	358.2	38.41	10.327	
5,500.0	5,493.0	5,494.0	5,494.0	19.5	19.7	157.88		201.0	108.9	403.1	364.0	39.11	10.306 SF	
5,600.0	5,592.8	5,587.8	5,587.8	19.8	20.0	158.39		200.5	110.2	410.2	370.5	39.77	10.315	
5,700.0	5,692.5	5,680.7	5,680.6	20.2	20.3	159.24		199.1	114.2	419.0	378.6	40.41	10.369	
5,800.0	5,792.3	5,774.7	5,774.3	20.5	20.6	160.42		196.5	121.2	429.4	388.4	41.04	10.462	
5,900.0	5,892.0	5,873.6	5,872.8	20.9	21.0	161.69		193.6	129.3	440.5	398.8	41.72	10.559	
6,000.0	5,991.8	5,972.5	5,971.3	21.2	21.3	162.90		190.6	137.4	451.8	409.4	42.40	10.657	
6,100.0	6,091.6	6,071.4	6,069.9	21.6	21.6	164.05		187.7	145.5	463.3	420.2	43.07	10.756	
6,200.0	6,191.3	6,170.3	6,168.4	21.9	22.0	165.15		184.8	153.6	475.0	431.2	43.75	10.856	
6,300.0	6,291.1	6,269.2	6,266.9	22.3	22.3	166.20		181.8	161.7	486.8	442.4	44.43	10.956	
6,400.0	6,390.8	6,368.1	6,365.5	22.7	22.6	167.19		178.9	169.8	498.8	453.7	45.12	11.057	
6,500.0	6,490.6	6,467.1	6,464.0	23.0	23.0	168.14		175.9	177.9	511.0	465.2	45.80	11.157	
6,600.0	6,590.3	6,566.0	6,562.5	23.4	23.3	169.04		173.0	186.0	523.2	476.7	46.48	11.256	
6,700.0	6,690.1	6,664.9	6,661.1	23.7	23.6	169.91		170.0	194.1	535.6	488.5	47.17	11.356	
6,800.0	6,789.9	6,763.8	6,759.6	24.1	24.0	170.73		167.1	202.2	548.1	500.3	47.85	11.454	
6,900.0	6,889.6	6,862.7	6,858.1	24.4	24.3	171.52		164.1	210.3	560.7	512.2	48.54	11.552	
7,000.0	6,989.4	6,961.6	6,956.7	24.8	24.7	172.27		161.2	218.4	573.5	524.2	49.23	11.648	
7,100.0	7,089.1	7,060.5	7,055.2	25.1	25.0	172.99		158.2	226.5	586.3	536.3	49.92	11.744	
7,200.0	7,188.9	7,159.4	7,153.8	25.5	25.3	173.68		155.3	234.6	599.2	548.5	50.61	11.839	
7,300.0	7,288.6	7,258.3	7,252.3	25.9	25.7	174.34		152.3	242.7	612.1	560.8	51.30	11.932	
7,400.0	7,388.4	7,357.3	7,350.8	26.2	26.0	174.97		149.4	250.8	625.2	573.2	51.99	12.024	
7,500.0	7,488.1	7,456.2	7,449.4	26.6	26.4	175.58		146.4	258.9	638.3	585.6	52.69	12.115	
7,600.0	7,587.9	7,555.1	7,547.9	26.9	26.7	176.16		143.5	267.0	651.5	598.1	53.38	12.205	
7,700.0	7,687.7	7,654.0	7,646.4	27.3	27.0	176.72		140.5	275.1	664.8	610.7	54.07	12.294	
7,805.4	7,792.8	7,758.3	7,750.3	27.7	27.4	177.29		137.4	283.6	678.8	624.0	54.81	12.385	
7,900.0	7,887.2	7,851.9	7,843.6	28.0	27.7	177.78		134.6	291.3	690.7	635.2	55.46	12.453	
8,000.0	7,987.1	7,951.1	7,942.4	28.4	28.1	178.28		131.7	299.4	701.6	645.4	56.16	12.493	
8,100.0	8,087.1	8,050.5	8,041.5	28.7	28.4	178.75		128.7	307.5	710.8	654.0	56.86	12.502	
8,205.4	8,192.5	8,155.5	8,146.0	29.1	28.8	69.18		125.6	316.1	718.7	661.2	57.59	12.481	
8,300.0	8,287.1	8,249.7	8,239.9	29.4	29.1	69.61		122.8	323.9	725.0	666.8	58.24	12.449	
8,400.0	8,387.1	8,349.3	8,339.1	29.8	29.5	70.05		119.8	332.0	731.7	672.8	58.93	12.417	
8,500.0	8,487.1	8,448.9	8,438.4	30.1	29.8	70.48		116.8	340.2	738.4	678.8	59.62	12.386	
8,600.0	8,587.1	8,548.6	8,537.6	30.4	30.2	70.91		113.9	348.3	745.1	684.8	60.31	12.356	
8,700.0	8,687.1	8,648.2	8,636.8	30.8	30.5	71.32		110.9	356.5	751.9	690.9	61.00	12.327	
8,800.0	8,787.1	8,747.8	8,736.1	31.1	30.9	71.74		107.9	364.7	758.8	697.1	61.69	12.300	
8,900.0	8,887.1	8,847.4	8,835.3	31.5	31.2	72.14		105.0	372.8	765.6	703.3	62.38	12.273	
9,000.0	8,987.1	8,947.0	8,934.6	31.8	31.6	72.53		102.0	381.0	772.6	709.5	63.08	12.248	
9,100.0	9,087.1	9,046.7	9,033.8	32.2	31.9	72.92		99.0	389.1	779.5	715.7	63.77	12.224	
9,200.0	9,187.1	9,133.2	9,120.0	32.5	32.2	73.17		97.6	396.2	786.9	722.5	64.35	12.228	
9,300.0	9,287.1	9,200.0	9,186.3	32.9	32.5	72.86		103.7	401.4	797.3	732.6	64.70	12.322	
9,400.0	9,387.1	9,275.5	9,259.8	33.2	32.7	71.87		119.9	406.9	811.1	746.0	65.09	12.463	
9,500.0	9,487.1	9,340.7	9,321.1	33.5	32.9	70.51		141.6	411.3	829.1	763.8	65.25	12.706	
9,600.0	9,587.1	9,400.0	9,374.4	33.9	33.1	68.91		167.3	415.0	851.6	786.4	65.21	13.059	
9,700.0	9,687.1	9,450.0	9,417.1	34.2	33.2	67.33		193.1	417.7	879.4	814.5	64.89	13.552	
9,800.0	9,787.1	9,500.0	9,457.4	34.6	33.4	65.56		222.6	420.2	912.6	848.2	64.43	14.164	
9,900.0	9,887.1	9,550.0	9,495.0	34.9	33.5	63.64		255.4	422.3	951.6	887.7	63.87	14.899	
10,000.0	9,987.1	9,580.5	9,516.5	35.3	33.6	62.41		277.0	423.5	996.2	933.3	62.85	15.850	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

6/8/2020 12:10:30PM

Page 15

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 501H - OWB - PWP													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10117-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
0.0	0.0	0.0	0.0	3.0	3.0	-90.53	-0.3	-30.0	30.0					
100.0	100.0	100.0	100.0	3.0	3.0	-90.53	-0.3	-30.0	30.0	24.0	6.00	4.999		
200.0	200.0	200.0	200.0	3.0	3.0	-90.53	-0.3	-30.0	30.0	24.0	6.04	4.968		
300.0	300.0	300.0	300.0	3.1	3.0	-90.53	-0.3	-30.0	30.0	23.9	6.12	4.902		
400.0	400.0	400.0	400.0	3.2	3.0	-90.53	-0.3	-30.0	30.0	23.8	6.24	4.807		
423.6	423.6	423.6	423.6	3.3	3.0	-90.53	-0.3	-30.0	30.0	23.7	6.28	4.781		
500.0	500.0	500.0	500.0	3.4	3.1	-90.53	-0.3	-30.0	30.0	23.6	6.40	4.689		
524.1	524.1	524.1	524.1	3.4	3.1	-90.53	-0.3	-30.0	30.0	23.6	6.44	4.658		
600.0	600.0	600.0	600.0	3.6	3.1	-90.53	-0.3	-30.0	30.0	23.4	6.59	4.556		
633.3	633.3	633.3	633.3	3.6	3.1	-90.53	-0.3	-30.0	30.0	23.4	6.66	4.508		
700.0	700.0	700.0	700.0	3.8	3.1	-90.53	-0.3	-30.0	30.0	23.2	6.80	4.412		
800.0	800.0	800.0	800.0	4.0	3.2	-90.53	-0.3	-30.0	30.0	23.0	7.04	4.262		
900.0	900.0	900.0	900.0	4.2	3.2	-90.53	-0.3	-30.0	30.0	22.7	7.30	4.112		
1,000.0	1,000.0	1,000.0	1,000.0	4.5	3.2	-90.53	-0.3	-30.0	30.0	22.4	7.57	3.962		
1,100.0	1,100.0	1,100.0	1,100.0	4.8	3.3	-90.53	-0.3	-30.0	30.0	22.1	7.86	3.817		
1,200.0	1,200.0	1,200.0	1,200.0	5.1	3.4	-90.53	-0.3	-30.0	30.0	21.8	8.16	3.676		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	3.4	-90.53	-0.3	-30.0	30.0	21.5	8.48	3.541		
1,400.0	1,400.0	1,400.0	1,400.0	5.7	3.5	-90.53	-0.3	-30.0	30.0	21.2	8.80	3.412		
1,500.0	1,500.0	1,500.0	1,500.0	6.0	3.5	-90.53	-0.3	-30.0	30.0	20.9	9.12	3.289		
1,600.0	1,600.0	1,600.0	1,600.0	6.3	3.6	-90.53	-0.3	-30.0	30.0	20.6	9.46	3.173		
1,700.0	1,700.0	1,700.0	1,700.0	6.6	3.7	-90.53	-0.3	-30.0	30.0	20.2	9.80	3.062		
1,800.0	1,800.0	1,800.0	1,800.0	6.9	3.8	-90.53	-0.3	-30.0	30.0	19.9	10.15	2.957		
1,900.0	1,900.0	1,900.0	1,900.0	7.2	3.9	-90.53	-0.3	-30.0	30.0	19.5	10.50	2.859		
2,000.0	2,000.0	2,000.0	2,000.0	7.6	3.9	-90.53	-0.3	-30.0	30.0	19.2	10.85	2.765		
2,100.0	2,100.0	2,100.0	2,100.0	7.9	4.0	-90.53	-0.3	-30.0	30.0	18.8	11.21	2.676		
2,200.0	2,200.0	2,200.0	2,200.0	8.2	4.1	-90.53	-0.3	-30.0	30.0	18.4	11.58	2.592		
2,300.0	2,300.0	2,300.0	2,300.0	8.6	4.2	-90.53	-0.3	-30.0	30.0	18.1	11.94	2.513		
2,400.0	2,400.0	2,400.0	2,400.0	8.9	4.3	-90.53	-0.3	-30.0	30.0	17.7	12.31	2.437		
2,466.7	2,466.7	2,466.7	2,466.7	9.1	4.4	-90.53	-0.3	-30.0	30.0	17.5	12.56	2.389		
2,500.0	2,500.0	2,500.0	2,500.0	9.2	4.4	-90.53	-0.3	-30.0	30.0	17.3	12.69	2.366 CC		
2,600.0	2,600.0	2,599.0	2,598.9	9.6	4.5	20.65	-0.3	-31.7	30.1	17.1	13.04	2.308		
2,700.0	2,699.8	2,697.9	2,697.7	9.9	4.5	23.99	-0.3	-36.8	30.4	17.0	13.40	2.271 ES, SF		
2,800.0	2,799.6	2,797.3	2,796.8	10.2	4.5	27.99	-0.3	-45.0	32.4	18.6	13.79	2.348		
2,900.0	2,899.4	2,897.2	2,896.4	10.5	4.6	31.38	-0.3	-53.7	34.9	20.7	14.20	2.457		
3,000.0	2,999.1	2,997.2	2,995.9	10.9	4.6	34.31	-0.3	-62.5	37.5	22.9	14.63	2.566		
3,100.0	3,098.9	3,097.1	3,095.5	11.2	4.6	36.85	-0.3	-71.2	40.3	25.2	15.07	2.673		
3,200.0	3,198.6	3,197.1	3,195.1	11.5	4.7	39.06	-0.3	-79.9	43.1	27.6	15.51	2.777		
3,300.0	3,298.4	3,297.0	3,294.6	11.9	4.7	41.00	-0.3	-88.6	45.9	30.0	15.96	2.879		
3,400.0	3,398.1	3,397.0	3,394.2	12.2	4.8	42.71	-0.3	-97.3	48.8	32.4	16.40	2.977		
3,500.0	3,497.9	3,496.9	3,493.8	12.5	4.9	44.22	-0.3	-106.0	51.8	34.9	16.85	3.072		
3,600.0	3,597.6	3,596.9	3,593.3	12.9	4.9	45.57	-0.3	-114.7	54.8	37.5	17.30	3.165		
3,700.0	3,697.4	3,696.8	3,692.9	13.2	5.0	46.79	-0.3	-123.4	57.8	40.0	17.75	3.254		
3,800.0	3,797.2	3,796.8	3,792.5	13.5	5.0	47.88	-0.3	-132.1	60.8	42.6	18.20	3.339		
3,900.0	3,896.9	3,896.7	3,892.0	13.9	5.1	48.87	-0.3	-140.9	63.8	45.2	18.65	3.422		
4,000.0	3,996.7	3,996.7	3,991.6	14.2	5.2	49.77	-0.3	-149.6	66.9	47.8	19.10	3.502		
4,100.0	4,096.4	4,096.6	4,091.2	14.6	5.3	50.59	-0.3	-158.3	70.0	50.4	19.55	3.578		
4,200.0	4,196.2	4,196.6	4,190.7	14.9	5.3	51.34	-0.3	-167.0	73.0	53.0	20.00	3.652		
4,300.0	4,295.9	4,296.5	4,290.3	15.3	5.4	52.03	-0.3	-175.7	76.1	55.7	20.45	3.723		
4,400.0	4,395.7	4,396.5	4,389.9	15.6	5.5	52.66	-0.3	-184.4	79.3	58.4	20.90	3.792		
4,500.0	4,495.5	4,496.4	4,489.4	16.0	5.6	53.25	-0.3	-193.1	82.4	61.0	21.35	3.858		
4,600.0	4,595.2	4,596.4	4,589.0	16.3	5.7	53.80	-0.3	-201.8	85.5	63.7	21.81	3.921		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10117-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
4,700.0	4,695.0	4,696.3	4,688.6	16.7	5.7	54.30	-0.3	-210.5	88.6	66.4	22.26	3.982	
4,800.0	4,794.7	4,796.3	4,788.2	17.0	5.8	54.77	-0.3	-219.3	91.8	69.1	22.71	4.041	
4,900.0	4,894.5	4,896.2	4,887.7	17.4	5.9	55.21	-0.3	-228.0	94.9	71.8	23.17	4.098	
5,000.0	4,994.2	4,996.2	4,987.3	17.7	6.0	55.63	-0.3	-236.7	98.1	74.5	23.62	4.152	
5,100.0	5,094.0	5,096.1	5,086.9	18.1	6.1	56.01	-0.3	-245.4	101.2	77.2	24.08	4.205	
5,200.0	5,193.7	5,196.0	5,186.4	18.4	6.2	56.37	-0.3	-254.1	104.4	79.9	24.53	4.256	
5,300.0	5,293.5	5,296.0	5,286.0	18.8	6.3	56.72	-0.3	-262.8	107.6	82.6	24.99	4.305	
5,400.0	5,393.3	5,395.9	5,385.6	19.1	6.4	57.04	-0.3	-271.5	110.7	85.3	25.44	4.352	
5,500.0	5,493.0	5,495.9	5,485.1	19.5	6.5	57.34	-0.3	-280.2	113.9	88.0	25.90	4.398	
5,600.0	5,592.8	5,595.8	5,584.7	19.8	6.6	57.63	-0.3	-288.9	117.1	90.7	26.36	4.442	
5,700.0	5,692.5	5,695.8	5,684.3	20.2	6.7	57.90	-0.3	-297.7	120.3	93.4	26.81	4.485	
5,800.0	5,792.3	5,795.7	5,783.8	20.5	6.8	58.16	-0.3	-306.4	123.4	96.2	27.27	4.526	
5,900.0	5,892.0	5,895.7	5,883.4	20.9	6.9	58.41	-0.3	-315.1	126.6	98.9	27.73	4.566	
6,000.0	5,991.8	5,995.6	5,983.0	21.2	7.0	58.64	-0.3	-323.8	129.8	101.6	28.19	4.605	
6,100.0	6,091.6	6,095.6	6,082.5	21.6	7.1	58.86	-0.3	-332.5	133.0	104.3	28.65	4.642	
6,200.0	6,191.3	6,195.5	6,182.1	21.9	7.2	59.07	-0.3	-341.2	136.2	107.1	29.11	4.678	
6,300.0	6,291.1	6,295.5	6,281.7	22.3	7.3	59.28	-0.3	-349.9	139.4	109.8	29.57	4.713	
6,400.0	6,390.8	6,395.4	6,381.2	22.7	7.4	59.47	-0.3	-358.6	142.6	112.5	30.03	4.747	
6,500.0	6,490.6	6,495.4	6,480.8	23.0	7.5	59.65	-0.3	-367.3	145.8	115.3	30.49	4.780	
6,600.0	6,590.3	6,595.3	6,580.4	23.4	7.6	59.83	-0.3	-376.1	149.0	118.0	30.96	4.812	
6,700.0	6,690.1	6,695.3	6,679.9	23.7	7.7	60.00	-0.3	-384.8	152.2	120.7	31.42	4.843	
6,800.0	6,789.9	6,795.2	6,779.5	24.1	7.8	60.16	-0.3	-393.5	155.4	123.5	31.88	4.873	
6,900.0	6,889.6	6,895.2	6,879.1	24.4	8.0	60.32	-0.3	-402.2	158.6	126.2	32.35	4.902	
7,000.0	6,989.4	6,995.1	6,978.6	24.8	8.1	60.47	-0.3	-410.9	161.8	128.9	32.81	4.930	
7,100.0	7,089.1	7,095.1	7,078.2	25.1	8.2	60.61	-0.3	-419.6	165.0	131.7	33.28	4.957	
7,200.0	7,188.9	7,195.0	7,177.8	25.5	8.3	60.75	-0.3	-428.3	168.2	134.4	33.74	4.984	
7,300.0	7,288.6	7,295.0	7,277.3	25.9	8.4	60.88	-0.3	-437.0	171.4	137.2	34.21	5.010	
7,400.0	7,388.4	7,394.9	7,376.9	26.2	8.5	61.01	-0.3	-445.7	174.6	139.9	34.67	5.035	
7,500.0	7,488.1	7,494.8	7,476.5	26.6	8.6	61.13	-0.3	-454.5	177.8	142.6	35.14	5.059	
7,600.0	7,587.9	7,594.8	7,576.0	26.9	8.7	61.25	-0.3	-463.2	181.0	145.4	35.61	5.083	
7,700.0	7,687.7	7,694.7	7,675.6	27.3	8.9	61.37	-0.3	-471.9	184.2	148.1	36.08	5.106	
7,805.4	7,792.8	7,800.1	7,780.6	27.7	9.0	61.48	-0.3	-481.1	187.6	151.0	36.57	5.129	
7,900.0	7,887.2	7,894.6	7,874.7	28.0	9.1	61.41	-0.3	-489.3	191.0	154.0	37.01	5.160	
8,000.0	7,987.1	7,994.5	7,974.2	28.4	9.2	60.91	-0.3	-498.0	195.4	157.9	37.49	5.213	
8,100.0	8,087.1	8,094.3	8,073.7	28.7	9.3	60.00	-0.3	-506.7	200.7	162.7	37.96	5.287	
8,205.4	8,192.5	8,199.4	8,178.4	29.1	9.4	-51.40	-0.3	-515.9	207.3	168.9	38.46	5.391	
8,300.0	8,287.1	8,293.6	8,272.2	29.4	9.6	-52.78	-0.3	-524.1	213.8	175.0	38.90	5.498	
8,400.0	8,387.1	8,393.2	8,371.5	29.8	9.7	-54.14	-0.3	-532.8	220.9	181.5	39.36	5.612	
8,500.0	8,487.1	8,492.9	8,470.7	30.1	9.8	-55.42	-0.3	-541.4	228.0	188.2	39.82	5.725	
8,600.0	8,587.1	8,592.5	8,569.9	30.4	9.9	-56.63	-0.3	-550.1	235.2	194.9	40.28	5.840	
8,700.0	8,687.1	8,692.1	8,669.2	30.8	10.0	-57.76	-0.3	-558.8	242.6	201.8	40.74	5.954	
8,800.0	8,787.1	8,791.7	8,768.4	31.1	10.1	-58.82	-0.3	-567.5	250.0	208.8	41.20	6.067	
8,900.0	8,887.1	8,891.3	8,867.7	31.5	10.3	-59.83	-0.3	-576.2	257.5	215.8	41.66	6.180	
9,000.0	8,987.1	8,991.0	8,966.9	31.8	10.4	-60.77	-0.3	-584.8	265.1	222.9	42.12	6.293	
9,100.0	9,087.1	9,090.6	9,066.1	32.2	10.5	-61.67	-0.3	-593.5	272.7	230.1	42.58	6.404	
9,200.0	9,187.1	9,190.2	9,165.4	32.5	10.6	-62.51	-0.3	-602.2	280.4	237.4	43.04	6.515	
9,300.0	9,287.1	9,289.8	9,264.6	32.9	10.7	-63.31	-0.3	-610.9	288.2	244.7	43.50	6.625	
9,400.0	9,387.1	9,389.4	9,363.9	33.2	10.9	-64.07	-0.3	-619.6	296.0	252.0	43.96	6.733	
9,500.0	9,487.1	9,489.1	9,463.1	33.5	11.0	-64.79	-0.3	-628.3	303.9	259.4	44.42	6.840	
9,600.0	9,587.1	9,588.7	9,562.3	33.9	11.1	-65.47	-0.3	-636.9	311.8	266.9	44.88	6.946	
9,700.0	9,687.1	9,688.3	9,661.6	34.2	11.2	-66.12	-0.3	-645.6	319.7	274.4	45.35	7.051	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10117-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
9,800.0	9,787.1	9,787.9	9,760.8	34.6	11.3	-66.73	-0.3	-654.3	327.7	281.9	45.81	7.155		
9,900.0	9,887.1	9,887.5	9,860.1	34.9	11.5	-67.32	-0.3	-663.0	335.8	289.5	46.27	7.257		
10,000.0	9,987.1	9,987.2	9,959.3	35.3	11.6	-67.88	-0.3	-671.7	343.8	297.1	46.73	7.357		
10,100.0	10,087.1	10,086.8	10,058.5	35.6	11.7	-68.41	-0.3	-680.4	351.9	304.7	47.19	7.457		
10,200.0	10,187.1	10,165.4	10,136.8	36.0	11.8	-68.58	1.6	-688.0	362.0	314.6	47.47	7.626		
10,300.0	10,287.1	10,233.0	10,203.1	36.3	11.8	-67.84	10.5	-697.5	380.0	332.4	47.67	7.972		
10,337.9	10,325.0	10,250.0	10,219.5	36.5	11.8	-67.53	13.8	-700.3	389.1	341.4	47.69	8.159		
10,350.0	10,337.1	10,265.6	10,234.4	36.5	11.8	-66.57	17.3	-703.1	392.1	344.3	47.76	8.208		
10,400.0	10,387.0	10,300.0	10,266.9	36.7	11.8	-64.83	26.4	-709.7	404.9	357.1	47.86	8.461		
10,450.0	10,436.4	10,329.2	10,294.0	36.8	11.8	-63.37	35.5	-715.8	417.9	370.0	47.91	8.724		
10,500.0	10,484.9	10,360.5	10,322.3	37.0	11.9	-62.10	46.7	-722.9	431.0	383.1	47.97	8.986		
10,550.0	10,532.3	10,400.0	10,357.0	37.2	11.9	-61.07	62.8	-732.7	444.2	396.1	48.08	9.238		
10,600.0	10,578.0	10,422.1	10,375.8	37.3	11.9	-60.14	72.8	-738.5	457.0	408.9	48.06	9.509		
10,650.0	10,621.9	10,450.0	10,398.9	37.5	11.9	-59.38	86.5	-746.2	469.7	421.6	48.08	9.770		
10,700.0	10,663.5	10,482.6	10,424.9	37.6	12.0	-58.87	103.7	-755.6	482.1	434.0	48.13	10.017		
10,750.0	10,702.5	10,512.4	10,447.7	37.7	12.0	-58.46	120.6	-764.7	494.3	446.1	48.17	10.262		
10,800.0	10,738.6	10,550.0	10,475.0	37.9	12.0	-58.40	143.6	-776.6	506.3	458.0	48.28	10.486		
10,850.0	10,771.6	10,571.5	10,489.8	38.0	12.1	-58.04	157.5	-783.7	517.7	469.4	48.26	10.727		
10,900.0	10,801.2	10,600.0	10,508.5	38.1	12.1	-57.98	176.7	-793.3	528.9	480.6	48.32	10.947		
10,950.0	10,827.1	10,630.0	10,527.1	38.2	12.1	-58.08	197.8	-803.7	539.8	491.4	48.40	11.153		
11,000.0	10,849.3	10,650.0	10,538.7	38.2	12.2	-57.89	212.5	-810.8	550.5	502.0	48.42	11.369		
11,050.0	10,867.4	10,688.1	10,559.4	38.3	12.2	-58.50	241.3	-824.6	560.6	512.0	48.59	11.537		
11,100.0	10,881.4	10,717.1	10,573.6	38.4	12.3	-58.85	264.2	-835.4	570.6	521.9	48.71	11.714		
11,150.0	10,891.2	10,750.0	10,588.2	38.4	12.3	-59.44	290.9	-847.8	580.3	531.4	48.86	11.876		
11,200.0	10,896.7	10,775.3	10,598.3	38.5	12.4	-59.77	312.1	-857.4	589.7	540.7	48.97	12.042		
11,240.8	10,898.0	10,800.0	10,607.2	38.5	12.4	-60.26	333.0	-866.9	597.3	548.2	49.09	12.168		
11,300.0	10,897.6	10,834.8	10,617.9	38.6	12.5	-61.81	363.3	-880.4	609.4	560.2	49.25	12.373		
11,400.0	10,897.1	10,900.0	10,632.6	38.7	12.6	-64.17	421.4	-905.9	635.1	585.5	49.56	12.815		
11,500.0	10,896.6	10,965.1	10,640.0	38.8	12.7	-65.79	480.8	-931.2	666.0	616.1	49.88	13.351		
11,600.0	10,896.1	11,057.5	10,640.7	38.9	12.9	-67.11	566.4	-966.3	700.1	649.7	50.40	13.891		
11,700.0	10,895.6	11,180.2	10,640.1	39.1	13.2	-68.44	681.6	-1,008.6	731.8	680.7	51.18	14.300		
11,800.0	10,895.1	11,306.6	10,639.4	39.3	13.7	-69.52	801.9	-1,047.0	759.9	707.8	52.05	14.598		
11,900.0	10,894.6	11,436.2	10,638.8	39.5	14.3	-70.38	927.0	-1,080.9	784.0	730.9	53.03	14.783		
12,000.0	10,894.1	11,568.8	10,638.1	39.7	15.0	-71.06	1,056.4	-1,109.6	803.9	749.9	54.03	14.879		
12,100.0	10,893.6	11,703.7	10,637.4	39.9	15.8	-71.57	1,189.3	-1,132.7	819.6	764.5	55.10	14.875		
12,200.0	10,893.1	11,840.4	10,636.7	40.2	16.6	-71.92	1,325.0	-1,149.7	830.8	774.6	56.20	14.784		
12,300.0	10,892.6	11,978.4	10,636.0	40.4	17.5	-72.13	1,462.6	-1,160.2	837.5	780.2	57.30	14.616		
12,400.0	10,892.1	12,115.4	10,635.3	40.7	18.4	-72.19	1,599.4	-1,164.1	839.6	781.2	58.39	14.380		
12,500.0	10,891.6	12,215.4	10,634.7	41.0	19.0	-72.19	1,699.4	-1,164.7	839.6	780.3	59.35	14.147		
12,600.0	10,891.1	12,315.4	10,634.2	41.3	19.7	-72.19	1,799.4	-1,165.4	839.6	779.3	60.35	13.914		
12,700.0	10,890.5	12,415.4	10,633.7	41.7	20.4	-72.19	1,899.4	-1,166.0	839.6	778.3	61.37	13.682		
12,800.0	10,890.0	12,515.4	10,633.2	42.0	21.1	-72.19	1,999.4	-1,166.6	839.7	777.2	62.42	13.452		
12,900.0	10,889.5	12,615.4	10,632.7	42.4	21.8	-72.19	2,099.4	-1,167.2	839.7	776.2	63.50	13.223		
13,000.0	10,889.0	12,715.4	10,632.2	42.7	22.5	-72.19	2,199.4	-1,167.8	839.7	775.1	64.60	12.998		
13,100.0	10,888.5	12,815.4	10,631.7	43.1	23.2	-72.19	2,299.4	-1,168.4	839.7	774.0	65.73	12.775		
13,200.0	10,888.0	12,915.4	10,631.2	43.5	24.0	-72.19	2,399.4	-1,169.0	839.7	772.8	66.87	12.556		
13,300.0	10,887.5	13,015.4	10,630.7	43.9	24.7	-72.19	2,499.4	-1,169.7	839.7	771.6	68.04	12.341		
13,400.0	10,887.0	13,115.4	10,630.2	44.4	25.5	-72.19	2,599.4	-1,170.3	839.7	770.5	69.23	12.129		
13,500.0	10,886.5	13,215.4	10,629.6	44.8	26.2	-72.19	2,699.4	-1,170.9	839.7	769.3	70.44	11.921		
13,600.0	10,886.0	13,315.4	10,629.1	45.3	27.0	-72.19	2,799.4	-1,171.5	839.7	768.1	71.66	11.717		
13,700.0	10,885.5	13,415.4	10,628.6	45.7	27.7	-72.19	2,899.4	-1,172.1	839.7	766.8	72.91	11.518		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10117-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
13,800.0	10,885.0	13,515.4	10,628.1	46.2	28.5	-72.19	2,999.4	-1,172.7	839.7	765.6	74.17	11.322		
13,900.0	10,884.5	13,615.4	10,627.6	46.7	29.3	-72.19	3,099.4	-1,173.4	839.7	764.3	75.44	11.131		
14,000.0	10,883.9	13,715.4	10,627.1	47.2	30.1	-72.19	3,199.4	-1,174.0	839.7	763.0	76.73	10.944		
14,100.0	10,883.4	13,815.4	10,626.6	47.7	30.9	-72.19	3,299.4	-1,174.6	839.8	761.7	78.03	10.762		
14,200.0	10,882.9	13,915.4	10,626.1	48.2	31.7	-72.19	3,399.4	-1,175.2	839.8	760.4	79.35	10.583		
14,300.0	10,882.4	14,015.4	10,625.6	48.7	32.5	-72.19	3,499.4	-1,175.8	839.8	759.1	80.68	10.409		
14,400.0	10,881.9	14,115.4	10,625.1	49.3	33.3	-72.19	3,599.4	-1,176.4	839.8	757.8	82.02	10.239		
14,500.0	10,881.4	14,215.4	10,624.5	49.8	34.1	-72.19	3,699.4	-1,177.1	839.8	756.4	83.37	10.073		
14,600.0	10,880.9	14,315.4	10,624.0	50.4	34.9	-72.19	3,799.4	-1,177.7	839.8	755.1	84.74	9.911		
14,700.0	10,880.4	14,415.4	10,623.5	51.0	35.7	-72.19	3,899.4	-1,178.3	839.8	753.7	86.11	9.752		
14,800.0	10,879.9	14,515.4	10,623.0	51.5	36.5	-72.19	3,999.4	-1,178.9	839.8	752.3	87.50	9.598		
14,900.0	10,879.4	14,615.4	10,622.5	52.1	37.3	-72.19	4,099.3	-1,179.5	839.8	750.9	88.89	9.447		
15,000.0	10,878.9	14,715.4	10,622.0	52.7	38.1	-72.19	4,199.3	-1,180.1	839.8	749.5	90.30	9.300		
15,100.0	10,878.4	14,815.4	10,621.5	53.3	38.9	-72.19	4,299.3	-1,180.7	839.8	748.1	91.71	9.157		
15,200.0	10,877.9	14,915.4	10,621.0	53.9	39.8	-72.19	4,399.3	-1,181.4	839.8	746.7	93.14	9.017		
15,300.0	10,877.3	15,015.4	10,620.5	54.5	40.6	-72.19	4,499.3	-1,182.0	839.8	745.3	94.57	8.881		
15,400.0	10,876.8	15,115.4	10,620.0	55.1	41.4	-72.19	4,599.3	-1,182.6	839.8	743.8	96.01	8.748		
15,500.0	10,876.3	15,215.4	10,619.4	55.7	42.2	-72.19	4,699.3	-1,183.2	839.9	742.4	97.46	8.618		
15,600.0	10,875.8	15,315.4	10,618.9	56.4	43.1	-72.19	4,799.3	-1,183.8	839.9	741.0	98.91	8.491		
15,700.0	10,875.3	15,415.4	10,618.4	57.0	43.9	-72.19	4,899.3	-1,184.4	839.9	739.5	100.37	8.368		
15,800.0	10,874.8	15,515.4	10,617.9	57.7	44.7	-72.19	4,999.3	-1,185.1	839.9	738.0	101.84	8.247		
15,900.0	10,874.3	15,615.4	10,617.4	58.3	45.5	-72.19	5,099.3	-1,185.7	839.9	736.6	103.32	8.129		
16,000.0	10,873.8	15,715.4	10,616.9	59.0	46.4	-72.19	5,199.3	-1,186.3	839.9	735.1	104.80	8.014		
16,100.0	10,873.3	15,815.4	10,616.4	59.6	47.2	-72.19	5,299.3	-1,186.9	839.9	733.6	106.29	7.902		
16,200.0	10,872.8	15,915.4	10,615.9	60.3	48.0	-72.19	5,399.3	-1,187.5	839.9	732.1	107.78	7.793		
16,300.0	10,872.3	16,015.4	10,615.4	60.9	48.9	-72.19	5,499.3	-1,188.1	839.9	730.6	109.28	7.686		
16,400.0	10,871.8	16,115.4	10,614.9	61.6	49.7	-72.19	5,599.3	-1,188.8	839.9	729.1	110.79	7.581		
16,500.0	10,871.3	16,215.4	10,614.3	62.3	50.5	-72.19	5,699.3	-1,189.4	839.9	727.6	112.30	7.479		
16,600.0	10,870.7	16,315.4	10,613.8	63.0	51.4	-72.19	5,799.3	-1,190.0	839.9	726.1	113.82	7.380		
16,700.0	10,870.2	16,415.4	10,613.3	63.7	52.2	-72.19	5,899.3	-1,190.6	839.9	724.6	115.34	7.283		
16,800.0	10,869.7	16,515.4	10,612.8	64.4	53.1	-72.19	5,999.3	-1,191.2	840.0	723.1	116.86	7.188		
16,900.0	10,869.2	16,615.4	10,612.3	65.1	53.9	-72.19	6,099.3	-1,191.8	840.0	721.6	118.39	7.095		
17,000.0	10,868.7	16,715.4	10,611.8	65.8	54.7	-72.19	6,199.3	-1,192.4	840.0	720.0	119.93	7.004		
17,100.0	10,868.2	16,815.4	10,611.3	66.5	55.6	-72.19	6,299.3	-1,193.1	840.0	718.5	121.47	6.915		
17,200.0	10,867.7	16,915.4	10,610.8	67.2	56.4	-72.19	6,399.3	-1,193.7	840.0	717.0	123.01	6.829		
17,300.0	10,867.2	17,015.4	10,610.3	67.9	57.3	-72.19	6,499.3	-1,194.3	840.0	715.4	124.56	6.744		
17,400.0	10,866.7	17,115.4	10,609.8	68.6	58.1	-72.19	6,599.3	-1,194.9	840.0	713.9	126.11	6.661		
17,500.0	10,866.2	17,215.4	10,609.2	69.3	58.9	-72.19	6,699.3	-1,195.5	840.0	712.3	127.67	6.580		
17,600.0	10,865.7	17,315.4	10,608.7	70.0	59.8	-72.19	6,799.3	-1,196.1	840.0	710.8	129.22	6.500		
17,700.0	10,865.2	17,415.4	10,608.2	70.8	60.6	-72.19	6,899.3	-1,196.8	840.0	709.2	130.79	6.423		
17,800.0	10,864.7	17,515.4	10,607.7	71.5	61.5	-72.19	6,999.3	-1,197.4	840.0	707.7	132.35	6.347		
17,900.0	10,864.1	17,615.4	10,607.2	72.2	62.3	-72.19	7,099.3	-1,198.0	840.0	706.1	133.92	6.273		
18,000.0	10,863.6	17,715.4	10,606.7	73.0	63.2	-72.19	7,199.2	-1,198.6	840.0	704.5	135.49	6.200		
18,100.0	10,863.1	17,815.4	10,606.2	73.7	64.0	-72.19	7,299.2	-1,199.2	840.0	703.0	137.07	6.129		
18,200.0	10,862.6	17,915.4	10,605.7	74.4	64.9	-72.19	7,399.2	-1,199.8	840.1	701.4	138.65	6.059		
18,300.0	10,862.1	18,015.4	10,605.2	75.2	65.7	-72.19	7,499.2	-1,200.4	840.1	699.8	140.23	5.991		
18,400.0	10,861.6	18,115.4	10,604.7	75.9	66.6	-72.19	7,599.2	-1,201.1	840.1	698.3	141.81	5.924		
18,500.0	10,861.1	18,215.4	10,604.1	76.7	67.4	-72.19	7,699.2	-1,201.7	840.1	696.7	143.40	5.858		
18,600.0	10,860.6	18,315.4	10,603.6	77.4	68.3	-72.19	7,799.2	-1,202.3	840.1	695.1	144.99	5.794		
18,700.0	10,860.1	18,415.4	10,603.1	78.2	69.1	-72.19	7,899.2	-1,202.9	840.1	693.5	146.58	5.731		
18,800.0	10,859.6	18,515.4	10,602.6	78.9	70.0	-72.19	7,999.2	-1,203.5	840.1	691.9	148.18	5.670		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10117-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
18,900.0	10,859.1	18,615.4	10,602.1	79.7	70.8	-72.19	8,099.2	-1,204.1	840.1	690.3	149.78	5.609		
19,000.0	10,858.6	18,715.4	10,601.6	80.4	71.7	-72.19	8,199.2	-1,204.8	840.1	688.7	151.37	5.550		
19,100.0	10,858.1	18,815.4	10,601.1	81.2	72.5	-72.19	8,299.2	-1,205.4	840.1	687.1	152.98	5.492		
19,200.0	10,857.5	18,915.4	10,600.6	82.0	73.4	-72.19	8,399.2	-1,206.0	840.1	685.6	154.58	5.435		
19,300.0	10,857.0	19,015.4	10,600.1	82.7	74.2	-72.19	8,499.2	-1,206.6	840.1	684.0	156.19	5.379		
19,400.0	10,856.5	19,115.4	10,599.6	83.5	75.1	-72.19	8,599.2	-1,207.2	840.1	682.4	157.80	5.324		
19,500.0	10,856.0	19,215.4	10,599.0	84.2	75.9	-72.19	8,699.2	-1,207.8	840.2	680.7	159.41	5.271		
19,600.0	10,855.5	19,315.4	10,598.5	85.0	76.8	-72.19	8,799.2	-1,208.5	840.2	679.1	161.02	5.218		
19,700.0	10,855.0	19,415.4	10,598.0	85.8	77.6	-72.19	8,899.2	-1,209.1	840.2	677.5	162.63	5.166		
19,800.0	10,854.5	19,515.4	10,597.5	86.6	78.5	-72.19	8,999.2	-1,209.7	840.2	675.9	164.25	5.115		
19,900.0	10,854.0	19,615.4	10,597.0	87.3	79.3	-72.19	9,099.2	-1,210.3	840.2	674.3	165.87	5.065		
20,000.0	10,853.5	19,715.4	10,596.5	88.1	80.2	-72.19	9,199.2	-1,210.9	840.2	672.7	167.49	5.016		
20,100.0	10,853.0	19,815.4	10,596.0	88.9	81.0	-72.19	9,299.2	-1,211.5	840.2	671.1	169.11	4.968		
20,200.0	10,852.5	19,915.4	10,595.5	89.7	81.9	-72.19	9,399.2	-1,212.1	840.2	669.5	170.73	4.921		
20,300.0	10,852.0	20,015.4	10,595.0	90.5	82.7	-72.19	9,499.2	-1,212.8	840.2	667.9	172.36	4.875		
20,400.0	10,851.5	20,115.4	10,594.5	91.2	83.6	-72.19	9,599.2	-1,213.4	840.2	666.2	173.98	4.829		
20,500.0	10,850.9	20,215.4	10,593.9	92.0	84.4	-72.19	9,699.2	-1,214.0	840.2	664.6	175.61	4.785		
20,600.0	10,850.4	20,315.4	10,593.4	92.8	85.3	-72.19	9,799.2	-1,214.6	840.2	663.0	177.24	4.741		
20,700.0	10,849.9	20,415.4	10,592.9	93.6	86.2	-72.19	9,899.2	-1,215.2	840.2	661.4	178.87	4.697		
20,800.0	10,849.4	20,515.4	10,592.4	94.4	87.0	-72.19	9,999.2	-1,215.8	840.2	659.7	180.50	4.655		
20,900.0	10,848.9	20,615.4	10,591.9	95.2	87.9	-72.19	10,099.2	-1,216.5	840.3	658.1	182.14	4.613		
21,000.0	10,848.4	20,715.4	10,591.4	96.0	88.7	-72.19	10,199.2	-1,217.1	840.3	656.5	183.77	4.572		
21,007.0	10,848.4	20,722.4	10,591.4	96.0	88.8	-72.19	10,206.2	-1,217.1	840.3	656.4	183.89	4.569		
21,080.0	10,848.0	20,792.8	10,591.0	96.6	89.4	-72.19	10,276.6	-1,217.5	840.3	655.2	185.08	4.540		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

6/8/2020 12:10:30PM

Page 20

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design		BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 503H - OWB - PWP										Offset Site Error:		3.0 usft
Survey Program:		0-Standard Keeper 104, 10152-MWD+IFR1+FDIR										Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis		Distance								Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.0	0.0	0.0	0.0	3.0	3.0	89.45	0.3	30.0	30.0					
100.0	100.0	100.0	100.0	3.0	3.0	89.45	0.3	30.0	30.0	24.0	6.00	4.994		
200.0	200.0	200.0	200.0	3.0	3.0	89.45	0.3	30.0	30.0	23.9	6.04	4.963		
300.0	300.0	300.0	300.0	3.1	3.0	89.45	0.3	30.0	30.0	23.9	6.12	4.897		
400.0	400.0	400.0	400.0	3.2	3.0	89.45	0.3	30.0	30.0	23.7	6.24	4.802		
423.6	423.6	423.6	423.6	3.3	3.0	89.45	0.3	30.0	30.0	23.7	6.28	4.776		
500.0	500.0	500.0	500.0	3.4	3.1	89.45	0.3	30.0	30.0	23.6	6.40	4.685		
524.1	524.1	524.1	524.1	3.4	3.1	89.45	0.3	30.0	30.0	23.5	6.44	4.654		
600.0	600.0	600.0	600.0	3.6	3.1	89.45	0.3	30.0	30.0	23.4	6.59	4.551		
633.3	633.3	633.3	633.3	3.6	3.1	89.45	0.3	30.0	30.0	23.3	6.66	4.504		
700.0	700.0	700.0	700.0	3.8	3.1	89.45	0.3	30.0	30.0	23.2	6.80	4.407		
800.0	800.0	800.0	800.0	4.0	3.2	89.45	0.3	30.0	30.0	22.9	7.04	4.258		
900.0	900.0	900.0	900.0	4.2	3.2	89.45	0.3	30.0	30.0	22.7	7.30	4.107		
1,000.0	1,000.0	1,000.0	1,000.0	4.5	3.2	89.45	0.3	30.0	30.0	22.4	7.57	3.958		
1,100.0	1,100.0	1,100.0	1,100.0	4.8	3.3	89.45	0.3	30.0	30.0	22.1	7.86	3.813		
1,200.0	1,200.0	1,200.0	1,200.0	5.1	3.4	89.45	0.3	30.0	30.0	21.8	8.16	3.672		
1,300.0	1,300.0	1,300.0	1,300.0	5.4	3.4	89.45	0.3	30.0	30.0	21.5	8.48	3.537		
1,400.0	1,400.0	1,400.0	1,400.0	5.7	3.5	89.45	0.3	30.0	30.0	21.2	8.80	3.408		
1,500.0	1,500.0	1,500.0	1,500.0	6.0	3.5	89.45	0.3	30.0	30.0	20.9	9.12	3.286		
1,600.0	1,600.0	1,600.0	1,600.0	6.3	3.6	89.45	0.3	30.0	30.0	20.5	9.46	3.169		
1,700.0	1,700.0	1,700.0	1,700.0	6.6	3.7	89.45	0.3	30.0	30.0	20.2	9.80	3.059		
1,800.0	1,800.0	1,800.0	1,800.0	6.9	3.8	89.45	0.3	30.0	30.0	19.8	10.15	2.955		
1,900.0	1,900.0	1,900.0	1,900.0	7.2	3.9	89.45	0.3	30.0	30.0	19.5	10.50	2.856		
2,000.0	2,000.0	2,000.0	2,000.0	7.6	3.9	89.45	0.3	30.0	30.0	19.1	10.85	2.762		
2,100.0	2,100.0	2,100.0	2,100.0	7.9	4.0	89.45	0.3	30.0	30.0	18.8	11.21	2.673		
2,200.0	2,200.0	2,200.0	2,200.0	8.2	4.1	89.45	0.3	30.0	30.0	18.4	11.58	2.590		
2,300.0	2,300.0	2,300.0	2,300.0	8.6	4.2	89.45	0.3	30.0	30.0	18.0	11.94	2.510		
2,400.0	2,400.0	2,400.0	2,400.0	8.9	4.3	89.45	0.3	30.0	30.0	17.7	12.31	2.435		
2,500.0	2,500.0	2,500.0	2,500.0	9.2	4.4	89.45	0.3	30.0	30.0	17.3	12.69	2.363	CC, ES, SF	
2,600.0	2,600.0	2,598.9	2,598.9	9.6	4.4	-160.39	-0.3	31.6	33.2	20.2	13.04	2.548		
2,700.0	2,699.8	2,697.8	2,697.6	9.9	4.5	-160.28	-2.1	36.1	42.7	29.3	13.40	3.188		
2,800.0	2,799.6	2,797.1	2,796.8	10.2	4.5	-160.64	-4.0	41.2	54.4	40.6	13.76	3.953		
2,900.0	2,899.4	2,896.4	2,896.0	10.5	4.5	-160.87	-6.0	46.3	66.1	51.9	14.13	4.676		
3,000.0	2,999.1	2,995.7	2,995.1	10.9	4.5	-161.03	-7.9	51.4	77.8	63.3	14.51	5.361		
3,100.0	3,098.9	3,095.0	3,094.3	11.2	4.5	-161.15	-9.9	56.5	89.4	74.6	14.89	6.008		
3,200.0	3,198.6	3,194.4	3,193.5	11.5	4.5	-161.25	-11.9	61.6	101.1	85.9	15.27	6.621		
3,300.0	3,298.4	3,293.7	3,292.6	11.9	4.6	-161.32	-13.8	66.8	112.8	97.2	15.66	7.202		
3,400.0	3,398.1	3,393.0	3,391.8	12.2	4.6	-161.38	-15.8	71.9	124.5	108.4	16.06	7.752		
3,500.0	3,497.9	3,492.3	3,491.0	12.5	4.6	-161.43	-17.8	77.0	136.2	119.7	16.46	8.273		
3,600.0	3,597.6	3,591.6	3,590.1	12.9	4.7	-161.47	-19.7	82.1	147.9	131.0	16.87	8.768		
3,700.0	3,697.4	3,690.9	3,689.3	13.2	4.7	-161.50	-21.7	87.2	159.6	142.3	17.27	9.237		
3,800.0	3,797.2	3,790.2	3,788.4	13.5	4.8	-161.53	-23.6	92.3	171.2	153.6	17.69	9.683		
3,900.0	3,896.9	3,889.6	3,887.6	13.9	4.8	-161.56	-25.6	97.4	182.9	164.8	18.10	10.106		
4,000.0	3,996.7	3,988.9	3,986.8	14.2	4.9	-161.58	-27.6	102.5	194.6	176.1	18.52	10.509		
4,100.0	4,096.4	4,088.2	4,085.9	14.6	4.9	-161.61	-29.5	107.6	206.3	187.4	18.94	10.892		
4,200.0	4,196.2	4,187.5	4,185.1	14.9	5.0	-161.62	-31.5	112.8	218.0	198.6	19.37	11.257		
4,300.0	4,295.9	4,286.8	4,284.3	15.3	5.0	-161.64	-33.4	117.9	229.7	209.9	19.79	11.605		
4,400.0	4,395.7	4,386.1	4,383.4	15.6	5.1	-161.66	-35.4	123.0	241.4	221.1	20.22	11.936		
4,500.0	4,495.5	4,485.5	4,482.6	16.0	5.2	-161.67	-37.4	128.1	253.1	232.4	20.65	12.253		
4,600.0	4,595.2	4,584.8	4,581.8	16.3	5.2	-161.68	-39.3	133.2	264.7	243.6	21.09	12.555		
4,700.0	4,695.0	4,684.1	4,680.9	16.7	5.3	-161.69	-41.3	138.3	276.4	254.9	21.52	12.843		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10152-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Warning							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
4,800.0	4,794.7	4,783.4	4,780.1	17.0	5.4	-161.70	-43.3	143.4	288.1	266.1	21.96	13.119	
4,900.0	4,894.5	4,882.7	4,879.2	17.4	5.5	-161.71	-45.2	148.5	299.8	277.4	22.40	13.383	
5,000.0	4,994.2	4,982.0	4,978.4	17.7	5.5	-161.72	-47.2	153.6	311.5	288.6	22.84	13.636	
5,100.0	5,094.0	5,081.3	5,077.6	18.1	5.6	-161.73	-49.1	158.8	323.2	299.9	23.29	13.878	
5,200.0	5,193.7	5,180.7	5,176.7	18.4	5.7	-161.74	-51.1	163.9	334.9	311.1	23.73	14.111	
5,300.0	5,293.5	5,280.0	5,275.9	18.8	5.8	-161.75	-53.1	169.0	346.5	322.4	24.18	14.333	
5,400.0	5,393.3	5,379.3	5,375.1	19.1	5.9	-161.75	-55.0	174.1	358.2	333.6	24.63	14.547	
5,500.0	5,493.0	5,478.6	5,474.2	19.5	5.9	-161.76	-57.0	179.2	369.9	344.8	25.07	14.753	
5,600.0	5,592.8	5,577.9	5,573.4	19.8	6.0	-161.76	-59.0	184.3	381.6	356.1	25.52	14.950	
5,700.0	5,692.5	5,677.2	5,672.6	20.2	6.1	-161.77	-60.9	189.4	393.3	367.3	25.98	15.140	
5,800.0	5,792.3	5,776.5	5,771.7	20.5	6.2	-161.78	-62.9	194.5	405.0	378.5	26.43	15.323	
5,900.0	5,892.0	5,875.9	5,870.9	20.9	6.3	-161.78	-64.8	199.6	416.7	389.8	26.88	15.499	
6,000.0	5,991.8	5,975.2	5,970.1	21.2	6.4	-161.78	-66.8	204.8	428.3	401.0	27.34	15.668	
6,100.0	6,091.6	6,074.5	6,069.2	21.6	6.5	-161.79	-68.8	209.9	440.0	412.2	27.79	15.831	
6,200.0	6,191.3	6,173.8	6,168.4	21.9	6.6	-161.79	-70.7	215.0	451.7	423.5	28.25	15.989	
6,300.0	6,291.1	6,273.1	6,267.5	22.3	6.7	-161.80	-72.7	220.1	463.4	434.7	28.71	16.141	
6,400.0	6,390.8	6,372.4	6,366.7	22.7	6.8	-161.80	-74.6	225.2	475.1	445.9	29.17	16.288	
6,500.0	6,490.6	6,471.7	6,465.9	23.0	6.9	-161.80	-76.6	230.3	486.8	457.2	29.63	16.429	
6,600.0	6,590.3	6,571.1	6,565.0	23.4	7.0	-161.81	-78.6	235.4	498.5	468.4	30.09	16.566	
6,700.0	6,690.1	6,670.4	6,664.2	23.7	7.1	-161.81	-80.5	240.5	510.2	479.6	30.55	16.699	
6,800.0	6,789.9	6,769.7	6,763.4	24.1	7.2	-161.81	-82.5	245.6	521.8	490.8	31.01	16.827	
6,900.0	6,889.6	6,869.0	6,862.5	24.4	7.3	-161.82	-84.5	250.8	533.5	502.1	31.48	16.950	
7,000.0	6,989.4	6,968.3	6,961.7	24.8	7.4	-161.82	-86.4	255.9	545.2	513.3	31.94	17.070	
7,100.0	7,089.1	7,067.6	7,060.9	25.1	7.5	-161.82	-88.4	261.0	556.9	524.5	32.40	17.187	
7,200.0	7,188.9	7,167.0	7,160.0	25.5	7.6	-161.83	-90.3	266.1	568.6	535.7	32.87	17.299	
7,300.0	7,288.6	7,266.3	7,259.2	25.9	7.7	-161.83	-92.3	271.2	580.3	546.9	33.33	17.408	
7,400.0	7,388.4	7,365.6	7,358.3	26.2	7.8	-161.83	-94.3	276.3	592.0	558.2	33.80	17.514	
7,500.0	7,488.1	7,464.9	7,457.5	26.6	7.9	-161.83	-96.2	281.4	603.6	569.4	34.27	17.617	
7,600.0	7,587.9	7,564.2	7,556.7	26.9	8.0	-161.84	-98.2	286.5	615.3	580.6	34.73	17.716	
7,700.0	7,687.7	7,663.5	7,655.8	27.3	8.1	-161.84	-100.2	291.6	627.0	591.8	35.20	17.813	
7,805.4	7,792.8	7,768.2	7,760.4	27.7	8.2	-161.84	-102.2	297.0	639.3	603.6	35.69	17.912	
7,900.0	7,887.2	7,862.2	7,854.2	28.0	8.3	-161.85	-104.1	301.9	649.7	613.5	36.14	17.978	
8,000.0	7,987.1	7,961.8	7,953.7	28.4	8.4	-161.82	-106.0	307.0	659.0	622.4	36.60	18.002	
8,100.0	8,087.1	8,061.5	8,053.2	28.7	8.6	-161.73	-108.0	312.1	666.6	629.5	37.07	17.982	
8,205.4	8,192.5	8,166.7	8,158.3	29.1	8.7	88.36	-110.1	317.5	672.9	635.3	37.56	17.917	
8,300.0	8,287.1	8,261.1	8,252.5	29.4	8.8	88.53	-112.0	322.4	677.7	639.7	37.99	17.841	
8,400.0	8,387.1	8,361.0	8,352.2	29.8	8.9	88.71	-113.9	327.5	682.8	644.4	38.44	17.761	
8,500.0	8,487.1	8,460.8	8,451.9	30.1	9.0	88.88	-115.9	332.7	687.9	649.0	38.90	17.684	
8,600.0	8,587.1	8,560.7	8,551.6	30.4	9.1	89.05	-117.9	337.8	693.0	653.7	39.36	17.608	
8,700.0	8,687.1	8,660.5	8,651.3	30.8	9.2	89.22	-119.9	343.0	698.1	658.3	39.82	17.534	
8,800.0	8,787.1	8,760.4	8,751.0	31.1	9.3	89.39	-121.8	348.1	703.3	663.0	40.28	17.461	
8,900.0	8,887.1	8,860.2	8,850.7	31.5	9.5	89.55	-123.8	353.2	708.4	667.7	40.74	17.390	
9,000.0	8,987.1	8,960.1	8,950.4	31.8	9.6	89.71	-125.8	358.4	713.5	672.3	41.20	17.320	
9,100.0	9,087.1	9,059.9	9,050.1	32.2	9.7	89.87	-127.7	363.5	718.7	677.0	41.66	17.252	
9,200.0	9,187.1	9,159.8	9,149.8	32.5	9.8	90.03	-129.7	368.6	723.8	681.7	42.12	17.185	
9,300.0	9,287.1	9,259.6	9,249.5	32.9	9.9	90.19	-131.7	373.8	729.0	686.4	42.58	17.120	
9,400.0	9,387.1	9,359.5	9,349.2	33.2	10.0	90.34	-133.7	378.9	734.1	691.1	43.04	17.055	
9,500.0	9,487.1	9,459.3	9,448.9	33.5	10.2	90.49	-135.6	384.1	739.3	695.8	43.51	16.992	
9,600.0	9,587.1	9,559.2	9,548.6	33.9	10.3	90.64	-137.6	389.2	744.4	700.5	43.97	16.931	
9,700.0	9,687.1	9,659.0	9,648.3	34.2	10.4	90.78	-139.6	394.3	749.6	705.2	44.43	16.870	
9,800.0	9,787.1	9,758.9	9,748.0	34.6	10.5	90.93	-141.5	399.5	754.8	709.9	44.90	16.811	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10152-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference	Offset	Semi Major Axis		Distance		Warning								
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
9,900.0	9,887.1	9,858.7	9,847.7	34.9	10.6	91.07	-143.5	404.6	760.0	714.6	45.36	16.752		
10,000.0	9,987.1	9,958.6	9,947.4	35.3	10.7	91.21	-145.5	409.8	765.2	719.3	45.83	16.695		
10,100.0	10,087.1	10,058.4	10,047.1	35.6	10.9	91.35	-147.5	414.9	770.3	724.1	46.30	16.639		
10,200.0	10,187.1	10,161.1	10,149.5	36.0	11.0	91.13	-144.7	420.1	775.4	728.7	46.76	16.584		
10,300.0	10,287.1	10,260.9	10,247.1	36.3	11.0	89.69	-125.1	425.1	780.3	733.2	47.12	16.558		
10,337.9	10,325.0	10,296.6	10,281.0	36.5	11.0	88.88	-114.1	426.7	782.3	735.1	47.25	16.556		
10,350.0	10,337.1	10,307.7	10,291.4	36.5	11.0	88.89	-110.2	427.2	783.0	735.7	47.29	16.557		
10,400.0	10,387.0	10,352.9	10,332.8	36.7	11.1	87.48	-92.4	429.3	786.1	738.6	47.45	16.566		
10,450.0	10,436.4	10,397.0	10,371.9	36.8	11.1	86.11	-71.9	431.2	789.4	741.8	47.60	16.584		
10,500.0	10,484.9	10,440.2	10,408.4	37.0	11.1	84.77	-49.0	432.9	793.0	745.3	47.75	16.609		
10,550.0	10,532.3	10,482.5	10,442.4	37.2	11.1	83.49	-23.9	434.5	796.8	748.9	47.89	16.640		
10,600.0	10,578.0	10,524.0	10,474.0	37.3	11.2	82.25	3.1	436.0	800.7	752.7	48.02	16.675		
10,650.0	10,621.9	10,564.9	10,503.0	37.5	11.2	81.08	31.8	437.3	804.7	756.5	48.15	16.712		
10,700.0	10,663.5	10,605.2	10,529.6	37.6	11.2	79.97	62.1	438.5	808.6	760.3	48.28	16.749		
10,750.0	10,702.5	10,644.9	10,553.6	37.7	11.3	78.94	93.7	439.5	812.5	764.1	48.40	16.785		
10,800.0	10,738.6	10,684.2	10,575.2	37.9	11.3	77.98	126.5	440.4	816.2	767.7	48.53	16.817		
10,850.0	10,771.6	10,723.0	10,594.3	38.0	11.4	77.10	160.3	441.2	819.7	771.1	48.66	16.845		
10,900.0	10,801.2	10,761.5	10,610.9	38.1	11.5	76.31	195.0	441.9	823.0	774.2	48.79	16.867		
10,950.0	10,827.1	10,800.0	10,625.1	38.2	11.5	75.60	230.7	442.4	826.0	777.0	48.93	16.881		
11,000.0	10,849.3	10,837.6	10,636.6	38.2	11.6	74.99	266.5	442.8	828.6	779.6	49.07	16.887		
11,050.0	10,867.4	10,875.3	10,645.9	38.3	11.7	74.47	303.0	443.0	830.9	781.7	49.21	16.884		
11,100.0	10,881.4	10,912.7	10,652.6	38.4	11.8	74.04	339.9	443.2	832.7	783.4	49.36	16.871		
11,150.0	10,891.2	10,950.0	10,657.0	38.4	11.9	73.71	376.9	443.2	834.2	784.7	49.51	16.848		
11,200.0	10,896.7	10,987.3	10,658.9	38.5	12.0	73.47	414.1	443.1	835.1	785.5	49.67	16.815		
11,240.8	10,898.0	11,023.4	10,658.9	38.5	12.1	73.37	450.2	442.8	835.5	785.7	49.81	16.773		
11,300.0	10,897.6	11,082.6	10,658.6	38.6	12.3	73.37	509.4	442.5	835.5	785.4	50.05	16.694		
11,400.0	10,897.1	11,182.6	10,658.1	38.7	12.7	73.37	609.4	441.9	835.5	785.0	50.50	16.544		
11,500.0	10,896.6	11,282.6	10,657.5	38.8	13.1	73.37	709.4	441.2	835.5	784.5	51.02	16.376		
11,600.0	10,896.1	11,382.6	10,657.0	38.9	13.6	73.37	809.4	440.6	835.5	783.9	51.60	16.193		
11,700.0	10,895.6	11,482.6	10,656.5	39.1	14.1	73.37	909.4	440.0	835.5	783.2	52.23	15.996		
11,800.0	10,895.1	11,582.6	10,656.0	39.3	14.6	73.37	1,009.4	439.4	835.5	782.5	52.91	15.789		
11,900.0	10,894.6	11,682.6	10,655.5	39.5	15.2	73.37	1,109.4	438.8	835.5	781.8	53.65	15.573		
12,000.0	10,894.1	11,782.6	10,655.0	39.7	15.8	73.37	1,209.4	438.2	835.5	781.0	54.43	15.350		
12,100.0	10,893.6	11,882.6	10,654.5	39.9	16.4	73.37	1,309.4	437.6	835.4	780.2	55.25	15.121		
12,200.0	10,893.1	11,982.6	10,654.0	40.2	17.1	73.37	1,409.4	436.9	835.4	779.3	56.11	14.889		
12,300.0	10,892.6	12,082.6	10,653.5	40.4	17.7	73.37	1,509.4	436.3	835.4	778.4	57.01	14.654		
12,400.0	10,892.1	12,182.6	10,653.0	40.7	18.4	73.37	1,609.4	435.7	835.4	777.5	57.94	14.418		
12,500.0	10,891.6	12,282.6	10,652.5	41.0	19.1	73.37	1,709.4	435.1	835.4	776.5	58.91	14.182		
12,600.0	10,891.1	12,382.6	10,652.0	41.3	19.8	73.37	1,809.4	434.5	835.4	775.5	59.90	13.946		
12,700.0	10,890.5	12,482.6	10,651.5	41.7	20.5	73.37	1,909.4	433.9	835.4	774.5	60.93	13.711		
12,800.0	10,890.0	12,582.6	10,651.0	42.0	21.3	73.37	2,009.4	433.3	835.4	773.4	61.98	13.479		
12,900.0	10,889.5	12,682.6	10,650.5	42.4	22.0	73.37	2,109.4	432.6	835.4	772.3	63.06	13.248		
13,000.0	10,889.0	12,782.6	10,649.9	42.7	22.8	73.37	2,209.3	432.0	835.4	771.2	64.16	13.021		
13,100.0	10,888.5	12,882.6	10,649.4	43.1	23.5	73.37	2,309.3	431.4	835.4	770.1	65.28	12.796		
13,200.0	10,888.0	12,982.6	10,648.9	43.5	24.3	73.37	2,409.3	430.8	835.4	769.0	66.43	12.576		
13,300.0	10,887.5	13,082.6	10,648.4	43.9	25.0	73.37	2,509.3	430.2	835.4	767.8	67.60	12.358		
13,400.0	10,887.0	13,182.6	10,647.9	44.4	25.8	73.37	2,609.3	429.6	835.4	766.6	68.78	12.145		
13,500.0	10,886.5	13,282.6	10,647.4	44.8	26.6	73.37	2,709.3	429.0	835.4	765.4	69.99	11.936		
13,600.0	10,886.0	13,382.6	10,646.9	45.3	27.4	73.37	2,809.3	428.3	835.4	764.1	71.21	11.731		
13,700.0	10,885.5	13,482.6	10,646.4	45.7	28.2	73.37	2,909.3	427.7	835.4	762.9	72.45	11.530		
13,800.0	10,885.0	13,582.6	10,645.9	46.2	29.0	73.37	3,009.3	427.1	835.3	761.6	73.71	11.333		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10152-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	
13,900.0	10,884.5	13,682.6	10,645.4	46.7	29.8	73.37	3,109.3	426.5	835.3	760.4	74.98	11.141	
14,000.0	10,883.9	13,782.6	10,644.9	47.2	30.6	73.37	3,209.3	425.9	835.3	759.1	76.27	10.953	
14,100.0	10,883.4	13,882.6	10,644.4	47.7	31.4	73.37	3,309.3	425.3	835.3	757.8	77.57	10.769	
14,200.0	10,882.9	13,982.6	10,643.9	48.2	32.2	73.37	3,409.3	424.7	835.3	756.4	78.88	10.590	
14,300.0	10,882.4	14,082.6	10,643.4	48.7	33.0	73.37	3,509.3	424.0	835.3	755.1	80.21	10.414	
14,400.0	10,881.9	14,182.6	10,642.9	49.3	33.8	73.37	3,609.3	423.4	835.3	753.8	81.55	10.243	
14,500.0	10,881.4	14,282.6	10,642.4	49.8	34.6	73.37	3,709.3	422.8	835.3	752.4	82.90	10.076	
14,600.0	10,880.9	14,382.6	10,641.8	50.4	35.5	73.37	3,809.3	422.2	835.3	751.0	84.27	9.913	
14,700.0	10,880.4	14,482.6	10,641.3	51.0	36.3	73.37	3,909.3	421.6	835.3	749.7	85.64	9.754	
14,800.0	10,879.9	14,582.6	10,640.8	51.5	37.1	73.37	4,009.3	421.0	835.3	748.3	87.03	9.598	
14,900.0	10,879.4	14,682.6	10,640.3	52.1	37.9	73.37	4,109.3	420.4	835.3	746.9	88.42	9.447	
15,000.0	10,878.9	14,782.6	10,639.8	52.7	38.8	73.37	4,209.3	419.7	835.3	745.5	89.83	9.299	
15,100.0	10,878.4	14,882.6	10,639.3	53.3	39.6	73.37	4,309.3	419.1	835.3	744.0	91.24	9.155	
15,200.0	10,877.9	14,982.6	10,638.8	53.9	40.4	73.37	4,409.3	418.5	835.3	742.6	92.66	9.014	
15,300.0	10,877.3	15,082.6	10,638.3	54.5	41.3	73.37	4,509.3	417.9	835.3	741.2	94.09	8.877	
15,400.0	10,876.8	15,182.6	10,637.8	55.1	42.1	73.37	4,609.3	417.3	835.3	739.7	95.53	8.743	
15,500.0	10,876.3	15,282.6	10,637.3	55.7	42.9	73.37	4,709.3	416.7	835.2	738.3	96.98	8.612	
15,600.0	10,875.8	15,382.6	10,636.8	56.4	43.8	73.37	4,809.3	416.1	835.2	736.8	98.44	8.485	
15,700.0	10,875.3	15,482.6	10,636.3	57.0	44.6	73.37	4,909.3	415.4	835.2	735.3	99.90	8.361	
15,800.0	10,874.8	15,582.6	10,635.8	57.7	45.4	73.37	5,009.3	414.8	835.2	733.9	101.37	8.239	
15,900.0	10,874.3	15,682.6	10,635.3	58.3	46.3	73.37	5,109.3	414.2	835.2	732.4	102.85	8.121	
16,000.0	10,873.8	15,782.6	10,634.8	59.0	47.1	73.37	5,209.3	413.6	835.2	730.9	104.33	8.005	
16,100.0	10,873.3	15,882.6	10,634.2	59.6	48.0	73.37	5,309.2	413.0	835.2	729.4	105.82	7.893	
16,200.0	10,872.8	15,982.6	10,633.7	60.3	48.8	73.37	5,409.2	412.4	835.2	727.9	107.32	7.783	
16,300.0	10,872.3	16,082.6	10,633.2	60.9	49.6	73.37	5,509.2	411.8	835.2	726.4	108.82	7.675	
16,400.0	10,871.8	16,182.6	10,632.7	61.6	50.5	73.37	5,609.2	411.1	835.2	724.9	110.33	7.570	
16,500.0	10,871.3	16,282.6	10,632.2	62.3	51.3	73.37	5,709.2	410.5	835.2	723.4	111.84	7.468	
16,600.0	10,870.7	16,382.6	10,631.7	63.0	52.2	73.37	5,809.2	409.9	835.2	721.8	113.36	7.368	
16,700.0	10,870.2	16,482.6	10,631.2	63.7	53.0	73.37	5,909.2	409.3	835.2	720.3	114.88	7.270	
16,800.0	10,869.7	16,582.6	10,630.7	64.4	53.9	73.37	6,009.2	408.7	835.2	718.8	116.41	7.174	
16,900.0	10,869.2	16,682.6	10,630.2	65.1	54.7	73.37	6,109.2	408.1	835.2	717.2	117.94	7.081	
17,000.0	10,868.7	16,782.6	10,629.7	65.8	55.6	73.37	6,209.2	407.5	835.2	715.7	119.48	6.990	
17,100.0	10,868.2	16,882.6	10,629.2	66.5	56.4	73.37	6,309.2	406.8	835.2	714.1	121.02	6.901	
17,200.0	10,867.7	16,982.6	10,628.7	67.2	57.2	73.37	6,409.2	406.2	835.2	712.6	122.57	6.814	
17,300.0	10,867.2	17,082.6	10,628.2	67.9	58.1	73.37	6,509.2	405.6	835.1	711.0	124.12	6.728	
17,400.0	10,866.7	17,182.6	10,627.7	68.6	58.9	73.37	6,609.2	405.0	835.1	709.5	125.68	6.645	
17,500.0	10,866.2	17,282.6	10,627.2	69.3	59.8	73.37	6,709.2	404.4	835.1	707.9	127.23	6.564	
17,600.0	10,865.7	17,382.6	10,626.7	70.0	60.6	73.37	6,809.2	403.8	835.1	706.3	128.80	6.484	
17,700.0	10,865.2	17,482.6	10,626.1	70.8	61.5	73.37	6,909.2	403.2	835.1	704.8	130.36	6.406	
17,800.0	10,864.7	17,582.6	10,625.6	71.5	62.3	73.37	7,009.2	402.5	835.1	703.2	131.93	6.330	
17,900.0	10,864.1	17,682.6	10,625.1	72.2	63.2	73.37	7,109.2	401.9	835.1	701.6	133.50	6.255	
18,000.0	10,863.6	17,782.6	10,624.6	73.0	64.0	73.37	7,209.2	401.3	835.1	700.0	135.08	6.182	
18,100.0	10,863.1	17,882.6	10,624.1	73.7	64.9	73.37	7,309.2	400.7	835.1	698.4	136.66	6.111	
18,200.0	10,862.6	17,982.6	10,623.6	74.4	65.8	73.37	7,409.2	400.1	835.1	696.9	138.24	6.041	
18,300.0	10,862.1	18,082.6	10,623.1	75.2	66.6	73.37	7,509.2	399.5	835.1	695.3	139.83	5.972	
18,400.0	10,861.6	18,182.6	10,622.6	75.9	67.5	73.37	7,609.2	398.9	835.1	693.7	141.41	5.905	
18,500.0	10,861.1	18,282.6	10,622.1	76.7	68.3	73.37	7,709.2	398.2	835.1	692.1	143.00	5.840	
18,600.0	10,860.6	18,382.6	10,621.6	77.4	69.2	73.37	7,809.2	397.6	835.1	690.5	144.60	5.775	
18,700.0	10,860.1	18,482.6	10,621.1	78.2	70.0	73.37	7,909.2	397.0	835.1	688.9	146.19	5.712	
18,800.0	10,859.6	18,582.6	10,620.6	78.9	70.9	73.37	8,009.2	396.4	835.1	687.3	147.79	5.650	
18,900.0	10,859.1	18,682.6	10,620.1	79.7	71.7	73.37	8,109.2	395.8	835.1	685.7	149.39	5.590	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 10152-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,000.0	10,858.6	18,782.6	10,619.6	80.4	72.6	73.37	8,209.2	395.2	835.0	684.1	151.00	5.530		
19,100.0	10,858.1	18,882.6	10,619.1	81.2	73.4	73.37	8,309.2	394.6	835.0	682.4	152.60	5.472		
19,200.0	10,857.5	18,982.6	10,618.5	82.0	74.3	73.37	8,409.2	393.9	835.0	680.8	154.21	5.415		
19,300.0	10,857.0	19,082.6	10,618.0	82.7	75.1	73.37	8,509.1	393.3	835.0	679.2	155.82	5.359		
19,400.0	10,856.5	19,182.6	10,617.5	83.5	76.0	73.37	8,609.1	392.7	835.0	677.6	157.43	5.304		
19,500.0	10,856.0	19,282.6	10,617.0	84.2	76.9	73.37	8,709.1	392.1	835.0	676.0	159.05	5.250		
19,600.0	10,855.5	19,382.6	10,616.5	85.0	77.7	73.37	8,809.1	391.5	835.0	674.3	160.67	5.197		
19,700.0	10,855.0	19,482.6	10,616.0	85.8	78.6	73.37	8,909.1	390.9	835.0	672.7	162.28	5.145		
19,800.0	10,854.5	19,582.6	10,615.5	86.6	79.4	73.37	9,009.1	390.3	835.0	671.1	163.90	5.094		
19,900.0	10,854.0	19,682.6	10,615.0	87.3	80.3	73.37	9,109.1	389.6	835.0	669.5	165.53	5.044		
20,000.0	10,853.5	19,782.6	10,614.5	88.1	81.1	73.37	9,209.1	389.0	835.0	667.8	167.15	4.995		
20,100.0	10,853.0	19,882.6	10,614.0	88.9	82.0	73.37	9,309.1	388.4	835.0	666.2	168.78	4.947		
20,200.0	10,852.5	19,982.6	10,613.5	89.7	82.8	73.37	9,409.1	387.8	835.0	664.6	170.40	4.900		
20,300.0	10,852.0	20,082.6	10,613.0	90.5	83.7	73.37	9,509.1	387.2	835.0	662.9	172.03	4.854		
20,400.0	10,851.5	20,182.6	10,612.5	91.2	84.6	73.37	9,609.1	386.6	835.0	661.3	173.66	4.808		
20,500.0	10,850.9	20,282.6	10,612.0	92.0	85.4	73.37	9,709.1	386.0	835.0	659.7	175.30	4.763		
20,600.0	10,850.4	20,382.6	10,611.5	92.8	86.3	73.37	9,809.1	385.3	835.0	658.0	176.93	4.719		
20,700.0	10,849.9	20,482.6	10,610.9	93.6	87.1	73.37	9,909.1	384.7	835.0	656.4	178.57	4.676		
20,800.0	10,849.4	20,582.6	10,610.4	94.4	88.0	73.37	10,009.1	384.1	834.9	654.7	180.20	4.633		
20,900.0	10,848.9	20,682.6	10,609.9	95.2	88.8	73.37	10,109.1	383.5	834.9	653.1	181.84	4.592		
21,000.0	10,848.4	20,782.6	10,609.4	96.0	89.7	73.37	10,209.1	382.9	834.9	651.5	183.48	4.551		
21,080.0	10,848.0	20,862.5	10,609.0	96.6	90.4	73.37	10,289.1	382.4	834.9	650.1	184.80	4.518		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

6/8/2020 12:10:30PM

Page 25

COMPASS 5000.15 Build 91E

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 701H - OWB - PWP													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 11896-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis			Distance							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
0.0	0.0	1.0	1.0	3.0	3.0	89.46	2.2	230.0	230.0					
100.0	100.0	101.0	101.0	3.0	3.0	89.46	2.2	230.0	230.0	224.0	6.00	38.314		
200.0	200.0	201.0	201.0	3.0	3.0	89.46	2.2	230.0	230.0	224.0	6.04	38.070		
300.0	300.0	301.0	301.0	3.1	3.0	89.46	2.2	230.0	230.0	223.9	6.12	37.566		
400.0	400.0	401.0	401.0	3.2	3.0	89.46	2.2	230.0	230.0	223.8	6.24	36.839		
500.0	500.0	501.0	501.0	3.4	3.1	89.46	2.2	230.0	230.0	223.6	6.40	35.938		
600.0	600.0	601.0	601.0	3.6	3.1	89.46	2.2	230.0	230.0	223.4	6.59	34.912		
700.0	700.0	701.0	701.0	3.8	3.1	89.46	2.2	230.0	230.0	223.2	6.80	33.808		
800.0	800.0	801.0	801.0	4.0	3.2	89.46	2.2	230.0	230.0	223.0	7.04	32.664		
900.0	900.0	901.0	901.0	4.2	3.2	89.46	2.2	230.0	230.0	222.7	7.30	31.509		
1,000.0	1,000.0	1,001.0	1,001.0	4.5	3.2	89.46	2.2	230.0	230.0	222.4	7.57	30.366		
1,100.0	1,100.0	1,101.0	1,101.0	4.8	3.3	89.46	2.2	230.0	230.0	222.1	7.86	29.250		
1,200.0	1,200.0	1,201.0	1,201.0	5.1	3.4	89.46	2.2	230.0	230.0	221.8	8.16	28.171		
1,300.0	1,300.0	1,301.0	1,301.0	5.4	3.4	89.46	2.2	230.0	230.0	221.5	8.48	27.136		
1,400.0	1,400.0	1,401.0	1,401.0	5.7	3.5	89.46	2.2	230.0	230.0	221.2	8.80	26.147		
1,500.0	1,500.0	1,501.0	1,501.0	6.0	3.5	89.46	2.2	230.0	230.0	220.9	9.12	25.206		
1,600.0	1,600.0	1,601.0	1,601.0	6.3	3.6	89.46	2.2	230.0	230.0	220.5	9.46	24.313		
1,700.0	1,700.0	1,701.0	1,701.0	6.6	3.7	89.46	2.2	230.0	230.0	220.2	9.80	23.467		
1,800.0	1,800.0	1,801.0	1,801.0	6.9	3.8	89.46	2.2	230.0	230.0	219.9	10.15	22.665		
1,900.0	1,900.0	1,901.0	1,901.0	7.2	3.9	89.46	2.2	230.0	230.0	219.5	10.50	21.906		
2,000.0	2,000.0	2,001.0	2,001.0	7.6	3.9	89.46	2.2	230.0	230.0	219.1	10.86	21.188		
2,100.0	2,100.0	2,101.0	2,101.0	7.9	4.0	89.46	2.2	230.0	230.0	218.8	11.21	20.509		
2,200.0	2,200.0	2,201.0	2,201.0	8.2	4.1	89.46	2.2	230.0	230.0	218.4	11.58	19.865		
2,300.0	2,300.0	2,301.0	2,301.0	8.6	4.2	89.46	2.2	230.0	230.0	218.1	11.94	19.256		
2,400.0	2,400.0	2,401.0	2,401.0	8.9	4.3	89.46	2.2	230.0	230.0	217.7	12.31	18.678		
2,500.0	2,500.0	2,501.1	2,501.1	9.2	4.4	89.46	2.2	230.0	230.0	217.3	12.69	18.130		
2,600.0	2,600.0	2,609.8	2,609.8	9.6	4.5	-160.64	2.2	227.9	229.7	216.7	13.05	17.608		
2,700.0	2,699.8	2,718.5	2,718.3	9.9	4.5	-161.14	2.2	221.7	228.9	215.5	13.39	17.102		
2,800.0	2,799.6	2,821.0	2,820.4	10.2	4.5	-161.77	2.2	212.9	227.0	213.2	13.74	16.519		
2,900.0	2,899.4	2,920.9	2,919.9	10.5	4.6	-162.40	2.2	204.2	224.9	210.8	14.11	15.942		
3,000.0	2,999.1	3,020.9	3,019.5	10.9	4.6	-163.03	2.2	195.5	222.9	208.4	14.48	15.391		
3,100.0	3,098.9	3,120.8	3,119.1	11.2	4.7	-163.68	2.2	186.8	220.8	206.0	14.86	14.865		
3,200.0	3,198.6	3,220.7	3,218.6	11.5	4.7	-164.34	2.2	178.1	218.8	203.6	15.24	14.363		
3,300.0	3,298.4	3,320.7	3,318.2	11.9	4.8	-165.02	2.2	169.3	216.9	201.2	15.62	13.883		
3,400.0	3,398.1	3,420.6	3,417.8	12.2	4.8	-165.70	2.2	160.6	214.9	198.9	16.01	13.426		
3,500.0	3,497.9	3,520.6	3,517.3	12.5	4.9	-166.40	2.2	151.9	213.0	196.6	16.40	12.990		
3,600.0	3,597.6	3,620.5	3,616.9	12.9	4.9	-167.11	2.2	143.2	211.2	194.4	16.79	12.573		
3,700.0	3,697.4	3,720.5	3,716.5	13.2	5.0	-167.83	2.2	134.5	209.3	192.1	17.19	12.176		
3,800.0	3,797.2	3,820.4	3,816.0	13.5	5.1	-168.57	2.2	125.8	207.5	189.9	17.59	11.796		
3,900.0	3,896.9	3,920.4	3,915.6	13.9	5.1	-169.32	2.2	117.1	205.7	187.8	17.99	11.434		
4,000.0	3,996.7	4,020.3	4,015.2	14.2	5.2	-170.08	2.2	108.4	204.0	185.6	18.40	11.089		
4,100.0	4,096.4	4,120.3	4,114.7	14.6	5.3	-170.85	2.2	99.7	202.3	183.5	18.81	10.759		
4,200.0	4,196.2	4,220.2	4,214.3	14.9	5.4	-171.64	2.2	91.0	200.7	181.4	19.21	10.444		
4,300.0	4,295.9	4,320.2	4,313.9	15.3	5.4	-172.44	2.2	82.2	199.0	179.4	19.62	10.143		
4,400.0	4,395.7	4,420.1	4,413.4	15.6	5.5	-173.25	2.2	73.5	197.5	177.4	20.04	9.855		
4,500.0	4,495.5	4,520.1	4,513.0	16.0	5.6	-174.08	2.2	64.8	195.9	175.5	20.45	9.581		
4,600.0	4,595.2	4,620.0	4,612.6	16.3	5.7	-174.92	2.2	56.1	194.4	173.6	20.86	9.319		
4,700.0	4,695.0	4,720.0	4,712.2	16.7	5.8	-175.77	2.2	47.4	193.0	171.7	21.28	9.068		
4,800.0	4,794.7	4,819.9	4,811.7	17.0	5.9	-176.64	2.2	38.7	191.5	169.9	21.69	8.829		
4,900.0	4,894.5	4,919.9	4,911.3	17.4	5.9	-177.51	2.2	30.0	190.2	168.1	22.11	8.601		
5,000.0	4,994.2	5,019.8	5,010.9	17.7	6.0	-178.40	2.2	21.3	188.9	166.3	22.53	8.382		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 11896-MWD+IFR1+FDIR												Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Semi Major Axis Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,100.0	5,094.0	5,119.8	5,110.4	18.1	6.1	-179.30	2.2	12.6	187.6	164.6	22.95	8.174	
5,200.0	5,193.7	5,219.7	5,210.0	18.4	6.2	179.78	2.2	3.8	186.3	163.0	23.37	7.974	
5,300.0	5,293.5	5,319.7	5,309.6	18.8	6.3	178.86	2.2	-4.9	185.2	161.4	23.79	7.784	
5,400.0	5,393.3	5,419.6	5,409.1	19.1	6.4	177.92	2.2	-13.6	184.0	159.8	24.21	7.601	
5,500.0	5,493.0	5,519.5	5,508.7	19.5	6.5	176.97	2.2	-22.3	182.9	158.3	24.63	7.427	
5,600.0	5,592.8	5,619.5	5,608.3	19.8	6.6	176.01	2.2	-31.0	181.9	156.9	25.05	7.261	
5,700.0	5,692.5	5,719.4	5,707.8	20.2	6.7	175.04	2.2	-39.7	180.9	155.5	25.47	7.102	
5,800.0	5,792.3	5,819.4	5,807.4	20.5	6.8	174.06	2.2	-48.4	180.0	154.1	25.90	6.951	
5,900.0	5,892.0	5,919.3	5,907.0	20.9	6.9	173.07	2.2	-57.1	179.1	152.8	26.32	6.806	
6,000.0	5,991.8	6,019.3	6,006.5	21.2	7.0	172.07	2.2	-65.8	178.3	151.6	26.74	6.667	
6,100.0	6,091.6	6,119.2	6,106.1	21.6	7.1	171.06	2.2	-74.6	177.5	150.4	27.17	6.535	
6,200.0	6,191.3	6,219.2	6,205.7	21.9	7.2	170.04	2.2	-83.3	176.8	149.2	27.59	6.409	
6,300.0	6,291.1	6,319.1	6,305.2	22.3	7.3	169.01	2.2	-92.0	176.2	148.2	28.02	6.288	
6,400.0	6,390.8	6,419.1	6,404.8	22.7	7.4	167.98	2.2	-100.7	175.6	147.1	28.44	6.173	
6,500.0	6,490.6	6,519.0	6,504.4	23.0	7.5	166.94	2.2	-109.4	175.0	146.2	28.87	6.064	
6,600.0	6,590.3	6,619.0	6,603.9	23.4	7.7	165.89	2.2	-118.1	174.6	145.3	29.29	5.959	
6,700.0	6,690.1	6,718.9	6,703.5	23.7	7.8	164.84	2.2	-126.8	174.1	144.4	29.72	5.859	
6,800.0	6,789.9	6,818.9	6,803.1	24.1	7.9	163.79	2.2	-135.5	173.8	143.6	30.15	5.764	
6,900.0	6,889.6	6,918.8	6,902.6	24.4	8.0	162.73	2.2	-144.2	173.5	142.9	30.58	5.673	
7,000.0	6,989.4	7,018.8	7,002.2	24.8	8.1	161.66	2.2	-153.0	173.2	142.2	31.00	5.587	
7,100.0	7,089.1	7,118.7	7,101.8	25.1	8.2	160.60	2.2	-161.7	173.0	141.6	31.43	5.504	
7,200.0	7,188.9	7,218.7	7,201.3	25.5	8.3	159.53	2.2	-170.4	172.9	141.0	31.86	5.426	
7,300.0	7,288.6	7,318.6	7,300.9	25.9	8.4	158.46	2.2	-179.1	172.8	140.5	32.30	5.351	
7,358.7	7,347.2	7,377.3	7,359.4	26.1	8.5	157.83	2.2	-184.2	172.8	140.3	32.55	5.309	
7,400.0	7,388.4	7,418.6	7,400.5	26.2	8.5	157.39	2.2	-187.8	172.8	140.1	32.73	5.281	
7,500.0	7,488.1	7,518.5	7,500.0	26.6	8.7	156.32	2.2	-196.5	172.9	139.7	33.16	5.213	
7,600.0	7,587.9	7,618.5	7,599.6	26.9	8.8	155.25	2.2	-205.2	173.0	139.4	33.60	5.149	
7,700.0	7,687.7	7,718.4	7,699.2	27.3	8.9	154.19	2.2	-213.9	173.2	139.1	34.04	5.088	
7,805.4	7,792.8	7,823.8	7,804.1	27.7	9.0	153.07	2.2	-223.1	173.4	138.9	34.50	5.027	
7,900.0	7,887.2	7,918.3	7,898.3	28.0	9.1	151.94	2.2	-231.4	173.0	138.1	34.91	4.956	
8,000.0	7,987.1	8,018.2	7,997.8	28.4	9.2	150.46	2.2	-240.1	171.2	135.8	35.35	4.843	
8,100.0	8,087.1	8,118.0	8,097.2	28.7	9.3	148.64	2.2	-248.8	168.0	132.2	35.78	4.694	
8,205.4	8,192.5	8,223.1	8,201.9	29.1	9.5	146.21	2.2	-257.9	163.2	127.0	36.23	4.504	
8,300.0	8,287.1	8,317.3	8,295.8	29.4	9.6	143.81	2.2	-266.1	158.4	121.8	36.64	4.324	
8,400.0	8,387.1	8,416.9	8,395.0	29.8	9.7	141.12	2.2	-274.8	153.8	116.7	37.08	4.146	
8,500.0	8,487.1	8,516.5	8,494.3	30.1	9.8	138.27	2.2	-283.5	149.4	111.9	37.53	3.981	
8,600.0	8,587.1	8,616.1	8,593.5	30.4	9.9	135.25	2.2	-292.2	145.5	107.5	38.00	3.828	
8,700.0	8,687.1	8,715.8	8,692.7	30.8	10.1	132.08	2.2	-300.9	142.0	103.5	38.48	3.689	
8,800.0	8,787.1	8,815.4	8,792.0	31.1	10.2	128.76	2.2	-309.5	138.9	99.9	38.99	3.563	
8,900.0	8,887.1	8,915.0	8,891.2	31.5	10.3	125.30	2.2	-318.2	136.4	96.8	39.51	3.451	
9,000.0	8,987.1	9,014.6	8,990.5	31.8	10.4	121.73	2.2	-326.9	134.3	94.3	40.05	3.354	
9,100.0	9,087.1	9,114.2	9,089.7	32.2	10.5	118.06	2.2	-335.6	132.8	92.2	40.61	3.270	
9,200.0	9,187.1	9,213.9	9,188.9	32.5	10.6	114.32	2.2	-344.3	131.9	90.7	41.19	3.202	
9,300.0	9,287.1	9,313.5	9,288.2	32.9	10.8	110.54	2.2	-353.0	131.5	89.7	41.78	3.147	
9,314.3	9,301.4	9,327.7	9,302.4	32.9	10.8	106.00	2.2	-354.2	131.5	89.6	41.87	3.141	
9,400.0	9,387.1	9,413.1	9,387.4	33.2	10.9	101.32	2.2	-361.6	131.7	89.3	42.38	3.107	
9,500.0	9,487.1	9,512.7	9,486.7	33.5	11.0	96.69	2.2	-370.3	132.5	89.5	42.99	3.081	
9,600.0	9,587.1	9,612.3	9,585.9	33.9	11.1	92.08	2.2	-379.0	133.8	90.2	43.61	3.069	
9,700.0	9,687.1	9,712.0	9,685.1	34.2	11.3	87.42	2.2	-387.7	135.7	91.5	44.22	3.069	
9,800.0	9,787.1	9,811.6	9,784.4	34.6	11.4	82.78	2.2	-396.4	138.1	93.3	44.83	3.081	
9,900.0	9,887.1	9,911.2	9,883.6	34.9	11.5	78.14	2.2	-405.1	141.0	95.6	45.43	3.105	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 11896-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Semi Major Axis	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
10,000.0	9,987.1	10,010.8	9,982.9	35.3	11.6	-24.36		2.2	-413.7	144.4	98.4	46.02	3.139	
10,100.0	10,087.1	10,110.4	10,082.1	35.6	11.7	-27.42		2.2	-422.4	148.2	101.7	46.60	3.181	
10,200.0	10,187.1	10,210.1	10,181.3	36.0	11.9	-30.32		2.2	-431.1	152.5	105.3	47.17	3.232	
10,300.0	10,287.1	10,309.7	10,280.6	36.3	12.0	-33.06		2.2	-439.8	157.1	109.3	47.73	3.291	
10,337.9	10,325.0	10,347.5	10,318.2	36.5	12.0	-34.06		2.2	-443.1	158.9	111.0	47.94	3.315	
10,350.0	10,337.1	10,359.5	10,330.2	36.5	12.1	-34.02		2.2	-444.1	159.4	111.4	48.00	3.320	
10,400.0	10,387.0	10,409.2	10,379.7	36.7	12.1	-35.96		2.2	-448.5	159.3	111.0	48.30	3.297	
10,450.0	10,436.4	10,458.4	10,428.7	36.8	12.2	-39.04		2.2	-452.7	155.9	107.3	48.61	3.207	
10,500.0	10,484.9	10,506.8	10,476.9	37.0	12.2	-43.48		2.2	-457.0	149.8	100.8	48.94	3.060	
10,550.0	10,532.3	10,554.0	10,523.9	37.2	12.3	-49.56		2.2	-461.1	141.6	92.3	49.27	2.874	
10,600.0	10,578.0	10,599.6	10,569.4	37.3	12.3	-57.54		2.2	-465.0	132.6	83.0	49.56	2.674	
10,650.0	10,621.9	10,643.2	10,612.9	37.5	12.4	-67.43		2.2	-468.9	124.5	74.7	49.75	2.502	
10,700.0	10,663.5	10,684.7	10,654.2	37.6	12.5	-78.70		2.2	-472.5	119.9	70.2	49.71	2.411	
10,713.5	10,674.2	10,695.4	10,664.9	37.6	12.5	-81.83		2.2	-473.4	119.6	70.0	49.65	2.409 CC, ES, SF	
10,750.0	10,702.5	10,723.5	10,692.9	37.7	12.5	-90.15		2.2	-475.9	121.7	72.3	49.38	2.465	
10,800.0	10,738.6	10,759.6	10,728.8	37.9	12.5	-100.41		2.2	-479.0	132.1	83.2	48.87	2.703	
10,850.0	10,771.6	10,792.4	10,761.5	38.0	12.6	-108.56		2.2	-481.9	151.3	102.9	48.42	3.125	
10,900.0	10,801.2	10,821.9	10,790.9	38.1	12.6	-114.32		2.2	-484.4	178.2	130.1	48.15	3.701	
10,950.0	10,827.1	10,847.8	10,816.7	38.2	12.7	-117.76		2.2	-486.7	211.2	163.1	48.05	4.395	
11,000.0	10,849.3	10,869.9	10,838.7	38.2	12.7	-118.96		2.2	-488.6	248.8	200.7	48.05	5.177	
11,050.0	10,867.4	10,888.0	10,856.7	38.3	12.7	-117.85		2.2	-490.2	289.8	241.7	48.09	6.026	
11,100.0	10,881.4	10,902.0	10,870.7	38.4	12.7	-114.11		2.2	-491.4	333.4	285.3	48.15	6.925	
11,150.0	10,891.2	10,911.8	10,880.4	38.4	12.7	-107.12		2.2	-492.3	379.0	330.8	48.21	7.862	
11,200.0	10,896.7	10,917.3	10,885.9	38.5	12.7	-96.14		2.2	-492.7	425.8	377.5	48.26	8.823	
11,240.8	10,898.0	10,918.5	10,887.1	38.5	12.7	-84.17		2.2	-492.8	464.6	416.3	48.30	9.620	
11,300.0	10,897.6	10,918.3	10,886.9	38.6	12.7	-84.06		2.2	-492.8	521.4	473.0	48.34	10.785	
11,400.0	10,897.1	10,917.8	10,886.4	38.7	12.7	-83.87		2.2	-492.8	618.4	569.9	48.41	12.772	
11,500.0	10,896.6	10,917.4	10,886.0	38.8	12.7	-83.68		2.2	-492.7	716.2	667.7	48.48	14.774	
11,600.0	10,896.1	10,916.9	10,885.5	38.9	12.7	-83.50		2.2	-492.7	814.5	766.0	48.53	16.784	
11,700.0	10,895.6	10,916.4	10,885.1	39.1	12.7	-83.31		2.2	-492.7	913.2	864.6	48.58	18.800	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design		BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 702H - OWB - PWP											Offset Site Error:		3.0 usft
Survey Program:		0-Standard Keeper 104, 11855-MWD+IFR1+FDIR											Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis		Distance								Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor			
0.0	0.0	1.0	1.0	3.0	3.0	89.47	2.4	260.0	260.0						
100.0	100.0	101.0	101.0	3.0	3.0	89.47	2.4	260.0	260.0	254.0	6.00	43.307			
200.0	200.0	201.0	201.0	3.0	3.0	89.47	2.4	260.0	260.0	253.9	6.04	43.031			
300.0	300.0	301.0	301.0	3.1	3.0	89.47	2.4	260.0	260.0	253.8	6.12	42.461			
400.0	400.0	401.0	401.0	3.2	3.0	89.47	2.4	260.0	260.0	253.7	6.24	41.640			
500.0	500.0	501.0	501.0	3.4	3.1	89.47	2.4	260.0	260.0	253.6	6.40	40.621			
600.0	600.0	601.0	601.0	3.6	3.1	89.47	2.4	260.0	260.0	253.4	6.59	39.462			
700.0	700.0	701.0	701.0	3.8	3.1	89.47	2.4	260.0	260.0	253.2	6.80	38.214			
800.0	800.0	801.0	801.0	4.0	3.2	89.47	2.4	260.0	260.0	252.9	7.04	36.920			
900.0	900.0	901.0	901.0	4.2	3.2	89.47	2.4	260.0	260.0	252.7	7.30	35.615			
1,000.0	1,000.0	1,001.0	1,001.0	4.5	3.2	89.47	2.4	260.0	260.0	252.4	7.57	34.323			
1,100.0	1,100.0	1,101.0	1,101.0	4.8	3.3	89.47	2.4	260.0	260.0	252.1	7.86	33.062			
1,200.0	1,200.0	1,201.0	1,201.0	5.1	3.4	89.47	2.4	260.0	260.0	251.8	8.16	31.842			
1,300.0	1,300.0	1,301.0	1,301.0	5.4	3.4	89.47	2.4	260.0	260.0	251.5	8.48	30.672			
1,400.0	1,400.0	1,401.0	1,401.0	5.7	3.5	89.47	2.4	260.0	260.0	251.2	8.80	29.554			
1,500.0	1,500.0	1,501.0	1,501.0	6.0	3.5	89.47	2.4	260.0	260.0	250.8	9.12	28.491			
1,600.0	1,600.0	1,601.0	1,601.0	6.3	3.6	89.47	2.4	260.0	260.0	250.5	9.46	27.481			
1,700.0	1,700.0	1,701.0	1,701.0	6.6	3.7	89.47	2.4	260.0	260.0	250.2	9.80	26.525			
1,800.0	1,800.0	1,801.0	1,801.0	6.9	3.8	89.47	2.4	260.0	260.0	249.8	10.15	25.618			
1,900.0	1,900.0	1,901.0	1,901.0	7.2	3.9	89.47	2.4	260.0	260.0	249.5	10.50	24.761			
2,000.0	2,000.0	2,001.0	2,001.0	7.6	3.9	89.47	2.4	260.0	260.0	249.1	10.86	23.949			
2,100.0	2,100.0	2,101.0	2,101.0	7.9	4.0	89.47	2.4	260.0	260.0	248.8	11.21	23.181			
2,200.0	2,200.0	2,201.0	2,201.0	8.2	4.1	89.47	2.4	260.0	260.0	248.4	11.58	22.454			
2,300.0	2,300.0	2,301.0	2,301.0	8.6	4.2	89.47	2.4	260.0	260.0	248.0	11.94	21.765			
2,400.0	2,400.0	2,401.0	2,401.0	8.9	4.3	89.47	2.4	260.0	260.0	247.7	12.31	21.112			
2,500.0	2,500.0	2,501.0	2,501.0	9.2	4.4	89.47	2.4	260.0	260.0	247.3	12.69	20.493			
2,600.0	2,600.0	2,601.0	2,601.0	9.6	4.5	-160.59	2.4	260.0	261.6	248.6	13.05	20.049			
2,700.0	2,699.8	2,700.8	2,700.8	9.9	4.6	-160.93	2.4	260.0	266.6	253.2	13.40	19.886			
2,800.0	2,799.6	2,800.6	2,800.6	10.2	4.7	-161.41	2.4	260.0	273.2	259.4	13.76	19.848			
2,900.0	2,899.4	2,900.4	2,900.4	10.5	4.8	-161.87	2.4	260.0	279.8	265.7	14.12	19.809			
3,000.0	2,999.1	3,000.1	3,000.1	10.9	4.9	-162.30	2.4	260.0	286.4	271.9	14.49	19.768			
3,100.0	3,098.9	3,099.9	3,099.9	11.2	5.0	-162.72	2.4	260.0	293.1	278.2	14.86	19.725			
3,200.0	3,198.6	3,199.6	3,199.6	11.5	5.1	-163.11	2.4	260.0	299.7	284.5	15.23	19.682			
3,300.0	3,298.4	3,299.4	3,299.4	11.9	5.2	-163.49	2.4	260.0	306.4	290.8	15.60	19.637			
3,400.0	3,398.1	3,399.1	3,399.1	12.2	5.3	-163.85	2.4	260.0	313.1	297.1	15.98	19.592			
3,500.0	3,497.9	3,498.9	3,498.9	12.5	5.4	-164.20	2.4	260.0	319.8	303.5	16.36	19.547			
3,600.0	3,597.6	3,598.6	3,598.6	12.9	5.5	-164.53	2.4	260.0	326.6	309.8	16.74	19.502			
3,700.0	3,697.4	3,698.4	3,698.4	13.2	5.7	-164.85	2.4	260.0	333.3	316.2	17.13	19.457			
3,800.0	3,797.2	3,798.2	3,798.2	13.5	5.8	-165.16	2.4	260.0	340.0	322.5	17.52	19.412			
3,900.0	3,896.9	3,897.9	3,897.9	13.9	5.9	-165.46	2.4	260.0	346.8	328.9	17.91	19.367			
4,000.0	3,996.7	3,997.7	3,997.7	14.2	6.0	-165.74	2.4	260.0	353.5	335.2	18.30	19.322			
4,100.0	4,096.4	4,097.4	4,097.4	14.6	6.1	-166.01	2.4	260.0	360.3	341.6	18.69	19.278			
4,200.0	4,196.2	4,197.2	4,197.2	14.9	6.2	-166.28	2.4	260.0	367.1	348.0	19.08	19.234			
4,300.0	4,295.9	4,296.9	4,296.9	15.3	6.3	-166.53	2.4	260.0	373.8	354.4	19.48	19.191			
4,400.0	4,395.7	4,396.7	4,396.7	15.6	6.5	-166.77	2.4	260.0	380.6	360.8	19.88	19.149			
4,500.0	4,495.5	4,496.5	4,496.5	16.0	6.6	-167.01	2.4	260.0	387.4	367.2	20.28	19.107			
4,600.0	4,595.2	4,596.2	4,596.2	16.3	6.7	-167.24	2.4	260.0	394.2	373.6	20.68	19.065			
4,700.0	4,695.0	4,696.0	4,696.0	16.7	6.8	-167.46	2.4	260.0	401.0	380.0	21.08	19.025			
4,800.0	4,794.7	4,795.7	4,795.7	17.0	6.9	-167.67	2.4	260.0	407.9	386.4	21.48	18.985			
4,900.0	4,894.5	4,895.5	4,895.5	17.4	7.0	-167.88	2.4	260.0	414.7	392.8	21.89	18.945			
5,000.0	4,994.2	4,995.2	4,995.2	17.7	7.2	-168.08	2.4	260.0	421.5	399.2	22.29	18.906			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 11855-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Semi Major Axis Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
5,100.0	5,094.0	5,095.0	5,095.0	18.1	7.3	-168.27	2.4	260.0	428.3	405.6	22.70	18.868		
5,200.0	5,193.7	5,194.7	5,194.7	18.4	7.4	-168.45	2.4	260.0	435.2	412.0	23.11	18.831		
5,300.0	5,293.5	5,294.5	5,294.5	18.8	7.5	-168.64	2.4	260.0	442.0	418.5	23.52	18.794		
5,400.0	5,393.3	5,394.3	5,394.3	19.1	7.6	-168.81	2.4	260.0	448.8	424.9	23.93	18.758		
5,500.0	5,493.0	5,494.0	5,494.0	19.5	7.8	-168.98	2.4	260.0	455.7	431.3	24.34	18.723		
5,600.0	5,592.8	5,611.4	5,611.4	19.8	7.8	-169.13	1.7	257.9	460.7	436.0	24.76	18.607		
5,700.0	5,692.5	5,730.3	5,730.0	20.2	7.8	-169.16	-0.7	251.2	461.7	436.6	25.16	18.353		
5,800.0	5,792.3	5,833.4	5,832.7	20.5	7.9	-169.13	-3.6	242.8	460.0	434.5	25.55	18.005		
5,900.0	5,892.0	5,933.4	5,932.3	20.9	7.9	-169.10	-6.6	234.6	458.3	432.4	25.95	17.664		
6,000.0	5,991.8	6,033.3	6,031.9	21.2	7.9	-169.07	-9.5	226.4	456.6	430.2	26.34	17.332		
6,100.0	6,091.6	6,133.3	6,131.5	21.6	7.9	-169.04	-12.4	218.2	454.9	428.1	26.75	17.007		
6,200.0	6,191.3	6,233.3	6,231.2	21.9	7.9	-169.01	-15.3	210.0	453.1	426.0	27.15	16.690		
6,300.0	6,291.1	6,333.3	6,330.8	22.3	7.9	-168.98	-18.2	201.8	451.4	423.8	27.56	16.380		
6,400.0	6,390.8	6,433.3	6,430.4	22.7	8.0	-168.95	-21.1	193.5	449.7	421.7	27.97	16.078		
6,500.0	6,490.6	6,533.3	6,530.0	23.0	8.0	-168.91	-24.0	185.3	447.9	419.6	28.38	15.783		
6,600.0	6,590.3	6,633.2	6,629.6	23.4	8.0	-168.88	-26.9	177.1	446.2	417.4	28.80	15.495		
6,700.0	6,690.1	6,733.2	6,729.2	23.7	8.1	-168.85	-29.8	168.9	444.5	415.3	29.22	15.214		
6,800.0	6,789.9	6,833.2	6,828.8	24.1	8.1	-168.82	-32.7	160.7	442.8	413.1	29.64	14.939		
6,900.0	6,889.6	6,933.2	6,928.4	24.4	8.1	-168.78	-35.6	152.5	441.0	411.0	30.06	14.671		
7,000.0	6,989.4	7,033.2	7,028.0	24.8	8.2	-168.75	-38.6	144.3	439.3	408.8	30.49	14.410		
7,100.0	7,089.1	7,133.2	7,127.6	25.1	8.2	-168.72	-41.5	136.0	437.6	406.7	30.91	14.154		
7,200.0	7,188.9	7,233.2	7,227.2	25.5	8.3	-168.68	-44.4	127.8	435.8	404.5	31.34	13.905		
7,300.0	7,288.6	7,333.1	7,326.8	25.9	8.3	-168.65	-47.3	119.6	434.1	402.3	31.78	13.661		
7,400.0	7,388.4	7,433.1	7,426.4	26.2	8.3	-168.61	-50.2	111.4	432.4	400.2	32.21	13.424		
7,500.0	7,488.1	7,533.1	7,526.0	26.6	8.4	-168.58	-53.1	103.2	430.7	398.0	32.65	13.191		
7,600.0	7,587.9	7,633.1	7,625.6	26.9	8.4	-168.54	-56.0	95.0	428.9	395.9	33.09	12.965		
7,700.0	7,687.7	7,733.1	7,725.2	27.3	8.5	-168.51	-58.9	86.8	427.2	393.7	33.53	12.743		
7,805.4	7,792.8	7,838.5	7,830.2	27.7	8.6	-168.47	-62.0	78.1	425.4	391.4	33.99	12.515		
7,900.0	7,887.2	7,933.0	7,924.4	28.0	8.6	-168.41	-64.7	70.3	423.0	388.6	34.41	12.293		
8,000.0	7,987.1	8,032.9	8,023.9	28.4	8.7	-168.30	-67.6	62.1	418.8	383.9	34.86	12.015		
8,100.0	8,087.1	8,132.8	8,123.4	28.7	8.7	-168.13	-70.5	53.9	412.9	377.6	35.30	11.696		
8,205.4	8,192.5	8,237.9	8,228.1	29.1	8.8	82.06	-73.6	45.3	404.8	369.1	35.77	11.318		
8,300.0	8,287.1	8,332.1	8,321.9	29.4	8.9	82.30	-76.3	37.5	396.8	360.6	36.19	10.965		
8,400.0	8,387.1	8,431.7	8,421.2	29.8	8.9	82.56	-79.2	29.4	388.2	351.6	36.63	10.599		
8,500.0	8,487.1	8,531.3	8,520.4	30.1	9.0	82.83	-82.1	21.2	379.7	342.6	37.07	10.242		
8,600.0	8,587.1	8,630.9	8,619.7	30.4	9.1	83.12	-85.0	13.0	371.2	333.7	37.52	9.893		
8,700.0	8,687.1	8,730.6	8,718.9	30.8	9.1	83.42	-87.9	4.8	362.7	324.7	37.97	9.552		
8,800.0	8,787.1	8,830.2	8,818.1	31.1	9.2	83.74	-90.8	-3.4	354.2	315.8	38.42	9.219		
8,900.0	8,887.1	8,929.8	8,917.4	31.5	9.3	84.07	-93.7	-11.6	345.7	306.9	38.88	8.893		
9,000.0	8,987.1	9,029.4	9,016.6	31.8	9.4	84.42	-96.6	-19.7	337.3	297.9	39.33	8.574		
9,100.0	9,087.1	9,129.0	9,115.9	32.2	9.4	84.78	-99.5	-27.9	328.8	289.0	39.79	8.263		
9,200.0	9,187.1	9,228.6	9,215.1	32.5	9.5	85.17	-102.4	-36.1	320.4	280.1	40.25	7.959		
9,300.0	9,287.1	9,328.3	9,314.3	32.9	9.6	85.57	-105.3	-44.3	311.9	271.2	40.72	7.661		
9,400.0	9,387.1	9,427.9	9,413.6	33.2	9.7	86.00	-108.2	-52.5	303.5	262.3	41.18	7.370		
9,500.0	9,487.1	9,527.5	9,512.8	33.5	9.8	86.45	-111.1	-60.7	295.1	253.5	41.65	7.086		
9,600.0	9,587.1	9,627.1	9,612.1	33.9	9.8	86.93	-114.0	-68.8	286.8	244.6	42.13	6.808		
9,700.0	9,687.1	9,726.7	9,711.3	34.2	9.9	87.44	-116.9	-77.0	278.4	235.8	42.60	6.536		
9,800.0	9,787.1	9,826.4	9,810.5	34.6	10.0	87.97	-119.8	-85.2	270.1	227.0	43.08	6.270		
9,900.0	9,887.1	9,926.0	9,909.8	34.9	10.1	88.55	-122.7	-93.4	261.8	218.2	43.56	6.010		
10,000.0	9,987.1	10,025.6	10,009.0	35.3	10.2	89.16	-125.6	-101.6	253.5	209.5	44.04	5.757		
10,100.0	10,087.1	10,125.2	10,108.3	35.6	10.3	89.81	-128.5	-109.8	245.3	200.7	44.52	5.509		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 11855-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Semi Major Axis	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Distance Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
10,200.0	10,187.1	10,224.8	10,207.5	36.0	10.4	90.50		-131.4	-118.0	237.1	192.0	45.01	5.266	
10,300.0	10,287.1	10,324.5	10,306.7	36.3	10.5	91.25		-134.3	-126.1	228.9	183.4	45.50	5.030	
10,337.9	10,325.0	10,362.2	10,344.4	36.5	10.5	91.55		-135.4	-129.2	225.8	180.1	45.69	4.942	
10,350.0	10,337.1	10,374.3	10,356.4	36.5	10.5	92.12		-135.8	-130.2	224.8	179.1	45.75	4.914	
10,400.0	10,387.0	10,423.9	10,405.8	36.7	10.6	93.75		-137.2	-134.3	220.9	174.9	46.04	4.799	
10,450.0	10,436.4	10,472.9	10,454.6	36.8	10.6	96.47		-138.6	-138.3	217.6	171.2	46.37	4.692	
10,500.0	10,484.9	10,520.9	10,502.4	37.0	10.7	100.16		-140.0	-142.3	215.3	168.6	46.75	4.605	
10,532.0	10,515.4	10,551.0	10,532.4	37.1	10.7	102.95		-140.9	-144.7	214.8	167.8	47.02	4.569 CC, ES	
10,550.0	10,532.3	10,567.6	10,549.0	37.2	10.7	104.62		-141.4	-146.1	215.0	167.8	47.17	4.558 SF	
10,600.0	10,578.0	10,612.6	10,593.8	37.3	10.8	109.53		-142.7	-149.8	217.6	170.0	47.59	4.573	
10,650.0	10,621.9	10,655.6	10,636.6	37.5	10.8	114.52		-143.9	-153.3	224.2	176.2	47.99	4.671	
10,700.0	10,663.5	10,696.2	10,677.1	37.6	10.8	119.23		-145.1	-156.7	235.4	187.1	48.33	4.871	
10,750.0	10,702.5	10,734.2	10,714.9	37.7	10.9	123.36		-146.2	-159.8	251.9	203.4	48.59	5.185	
10,800.0	10,738.6	10,769.2	10,749.8	37.9	10.9	126.70		-147.2	-162.7	273.8	225.1	48.76	5.616	
10,850.0	10,771.6	10,801.0	10,781.5	38.0	10.9	129.12		-148.2	-165.3	300.8	251.9	48.86	6.156	
10,900.0	10,801.2	10,829.3	10,809.7	38.1	11.0	130.50		-149.0	-167.6	332.4	283.5	48.90	6.798	
10,950.0	10,827.1	10,854.0	10,834.2	38.2	11.0	130.72		-149.7	-169.6	368.1	319.2	48.90	7.527	
11,000.0	10,849.3	10,874.7	10,854.9	38.2	11.0	129.58		-150.3	-171.3	407.2	358.4	48.88	8.331	
11,050.0	10,867.4	10,891.5	10,871.6	38.3	11.0	126.75		-150.8	-172.7	449.2	400.4	48.85	9.196	
11,100.0	10,881.4	10,904.1	10,884.2	38.4	11.0	121.66		-151.2	-173.8	493.4	444.6	48.80	10.111	
11,150.0	10,891.2	10,912.4	10,892.5	38.4	11.1	113.47		-151.4	-174.4	539.3	490.6	48.75	11.064	
11,200.0	10,896.7	10,916.5	10,896.5	38.5	11.1	101.27		-151.5	-174.8	586.4	537.7	48.69	12.043	
11,240.8	10,898.0	10,916.5	10,896.6	38.5	11.1	88.27		-151.5	-174.8	625.4	576.8	48.65	12.855	
11,300.0	10,897.6	10,914.6	10,894.6	38.6	11.1	87.64		-151.5	-174.6	682.3	633.7	48.59	14.041	
11,400.0	10,897.1	10,911.2	10,891.2	38.7	11.0	86.57		-151.4	-174.3	779.2	730.7	48.51	16.062	
11,500.0	10,896.6	10,907.8	10,887.9	38.8	11.0	85.52		-151.3	-174.1	876.8	828.4	48.45	18.096	
11,600.0	10,896.1	10,904.5	10,884.5	38.9	11.0	84.47		-151.2	-173.8	974.9	926.5	48.41	20.139	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design		BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 703H - OWB - PWP											Offset Site Error:		3.0 usft
Survey Program:		0-Standard Keeper 104, 11837-MWD+IFR1+FDIR											Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis		Distance								Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor			
0.0	0.0	1.0	1.0	3.0	3.0	89.46		2.7	290.0	290.0					
100.0	100.0	101.0	101.0	3.0	3.0	89.46		2.7	290.0	290.0	284.0	6.00	48.308		
200.0	200.0	201.0	201.0	3.0	3.0	89.46		2.7	290.0	290.0	284.0	6.04	48.000		
300.0	300.0	301.0	301.0	3.1	3.0	89.46		2.7	290.0	290.0	283.9	6.12	47.364		
400.0	400.0	401.0	401.0	3.2	3.0	89.46		2.7	290.0	290.0	283.7	6.24	46.448		
500.0	500.0	501.0	501.0	3.4	3.1	89.46		2.7	290.0	290.0	283.6	6.40	45.312		
600.0	600.0	601.0	601.0	3.6	3.1	89.46		2.7	290.0	290.0	283.4	6.59	44.019		
700.0	700.0	701.0	701.0	3.8	3.1	89.46		2.7	290.0	290.0	283.2	6.80	42.627		
800.0	800.0	801.0	801.0	4.0	3.2	89.46		2.7	290.0	290.0	283.0	7.04	41.184		
900.0	900.0	901.0	901.0	4.2	3.2	89.46		2.7	290.0	290.0	282.7	7.30	39.728		
1,000.0	1,000.0	1,001.0	1,001.0	4.5	3.2	89.46		2.7	290.0	290.0	282.4	7.57	38.287		
1,100.0	1,100.0	1,101.0	1,101.0	4.8	3.3	89.46		2.7	290.0	290.0	282.1	7.86	36.880		
1,200.0	1,200.0	1,201.0	1,201.0	5.1	3.4	89.46		2.7	290.0	290.0	281.8	8.16	35.520		
1,300.0	1,300.0	1,301.0	1,301.0	5.4	3.4	89.46		2.7	290.0	290.0	281.5	8.48	34.214		
1,400.0	1,400.0	1,401.0	1,401.0	5.7	3.5	89.46		2.7	290.0	290.0	281.2	8.80	32.967		
1,500.0	1,500.0	1,501.0	1,501.0	6.0	3.5	89.46		2.7	290.0	290.0	280.9	9.12	31.781		
1,600.0	1,600.0	1,601.0	1,601.0	6.3	3.6	89.46		2.7	290.0	290.0	280.5	9.46	30.655		
1,700.0	1,700.0	1,701.0	1,701.0	6.6	3.7	89.46		2.7	290.0	290.0	280.2	9.80	29.588		
1,800.0	1,800.0	1,801.0	1,801.0	6.9	3.8	89.46		2.7	290.0	290.0	279.8	10.15	28.577		
1,900.0	1,900.0	1,901.0	1,901.0	7.2	3.9	89.46		2.7	290.0	290.0	279.5	10.50	27.620		
2,000.0	2,000.0	2,001.0	2,001.0	7.6	3.9	89.46		2.7	290.0	290.0	279.1	10.86	26.715		
2,100.0	2,100.0	2,101.0	2,101.0	7.9	4.0	89.46		2.7	290.0	290.0	278.8	11.21	25.858		
2,200.0	2,200.0	2,201.0	2,201.0	8.2	4.1	89.46		2.7	290.0	290.0	278.4	11.58	25.047		
2,300.0	2,300.0	2,301.0	2,301.0	8.6	4.2	89.46		2.7	290.0	290.0	278.0	11.94	24.279		
2,400.0	2,400.0	2,401.0	2,401.0	8.9	4.3	89.46		2.7	290.0	290.0	277.7	12.31	23.550		
2,500.0	2,500.0	2,501.0	2,501.0	9.2	4.4	89.46		2.7	290.0	290.0	277.3	12.69	22.859	CC, ES	
2,600.0	2,600.0	2,601.0	2,601.0	9.6	4.5	-160.58		2.7	290.0	291.6	278.6	13.05	22.349		
2,700.0	2,699.8	2,700.8	2,700.8	9.9	4.6	-160.89		2.7	290.0	296.6	283.2	13.40	22.126		
2,800.0	2,799.6	2,800.6	2,800.6	10.2	4.7	-161.32		2.7	290.0	303.2	289.4	13.76	22.030		
2,900.0	2,899.4	2,900.4	2,900.4	10.5	4.8	-161.73		2.7	290.0	309.8	295.7	14.12	21.934		
3,000.0	2,999.1	3,000.1	3,000.1	10.9	4.9	-162.13		2.7	290.0	316.4	301.9	14.49	21.839		
3,100.0	3,098.9	3,099.9	3,099.9	11.2	5.0	-162.51		2.7	290.0	323.1	308.2	14.86	21.745		
3,200.0	3,198.6	3,199.6	3,199.6	11.5	5.1	-162.87		2.7	290.0	329.7	314.5	15.23	21.652		
3,300.0	3,298.4	3,299.4	3,299.4	11.9	5.2	-163.22		2.7	290.0	336.4	320.8	15.60	21.560		
3,400.0	3,398.1	3,399.1	3,399.1	12.2	5.3	-163.56		2.7	290.0	343.1	327.1	15.98	21.470		
3,500.0	3,497.9	3,498.9	3,498.9	12.5	5.4	-163.88		2.7	290.0	349.8	333.4	16.36	21.380		
3,600.0	3,597.6	3,598.6	3,598.6	12.9	5.5	-164.19		2.7	290.0	356.5	339.8	16.74	21.293		
3,700.0	3,697.4	3,698.4	3,698.4	13.2	5.7	-164.49		2.7	290.0	363.2	346.1	17.13	21.207		
3,800.0	3,797.2	3,798.2	3,798.2	13.5	5.8	-164.78		2.7	290.0	370.0	352.4	17.51	21.123		
3,900.0	3,896.9	3,897.9	3,897.9	13.9	5.9	-165.06		2.7	290.0	376.7	358.8	17.90	21.041		
4,000.0	3,996.7	3,997.7	3,997.7	14.2	6.0	-165.33		2.7	290.0	383.4	365.1	18.29	20.960		
4,100.0	4,096.4	4,097.4	4,097.4	14.6	6.1	-165.59		2.7	290.0	390.2	371.5	18.69	20.882		
4,200.0	4,196.2	4,197.2	4,197.2	14.9	6.2	-165.84		2.7	290.0	396.9	377.9	19.08	20.805		
4,300.0	4,295.9	4,296.9	4,296.9	15.3	6.3	-166.08		2.7	290.0	403.7	384.2	19.48	20.729		
4,400.0	4,395.7	4,396.7	4,396.7	15.6	6.5	-166.31		2.7	290.0	410.5	390.6	19.87	20.656		
4,500.0	4,495.5	4,496.5	4,496.5	16.0	6.6	-166.54		2.7	290.0	417.3	397.0	20.27	20.584		
4,600.0	4,595.2	4,596.2	4,596.2	16.3	6.7	-166.76		2.7	290.0	424.1	403.4	20.67	20.514		
4,700.0	4,695.0	4,696.0	4,696.0	16.7	6.8	-166.97		2.7	290.0	430.9	409.8	21.07	20.445		
4,800.0	4,794.7	4,795.7	4,795.7	17.0	6.9	-167.18		2.7	290.0	437.7	416.2	21.48	20.378		
4,900.0	4,894.5	4,895.5	4,895.5	17.4	7.0	-167.38		2.7	290.0	444.5	422.6	21.88	20.313		
5,000.0	4,994.2	4,995.2	4,995.2	17.7	7.2	-167.57		2.7	290.0	451.3	429.0	22.29	20.249		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-Standard Keeper 104, 11837-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Semi Major Axis (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
5,100.0	5,094.0	5,095.0	5,095.0	18.1	7.3	-167.76		2.7	290.0	458.1	435.4	22.69	20.187	
5,200.0	5,193.7	5,194.7	5,194.7	18.4	7.4	-167.94		2.7	290.0	464.9	441.8	23.10	20.126	
5,300.0	5,293.5	5,294.5	5,294.5	18.8	7.5	-168.12		2.7	290.0	471.7	448.2	23.51	20.066	
5,400.0	5,393.3	5,394.3	5,394.3	19.1	7.6	-168.29		2.7	290.0	478.6	454.6	23.92	20.008	
5,500.0	5,493.0	5,494.0	5,494.0	19.5	7.8	-168.46		2.7	290.0	485.4	461.1	24.33	19.952	
5,600.0	5,592.8	5,593.8	5,593.8	19.8	7.9	-168.62		2.7	290.0	492.2	467.5	24.74	19.896	
5,700.0	5,692.5	5,693.5	5,693.5	20.2	8.0	-168.78		2.7	290.0	499.1	473.9	25.15	19.842	
5,800.0	5,792.3	5,793.3	5,793.3	20.5	8.1	-168.93		2.7	290.0	505.9	480.3	25.56	19.789	
5,900.0	5,892.0	5,893.0	5,893.0	20.9	8.3	-169.08		2.7	290.0	512.8	486.8	25.98	19.738	
6,000.0	5,991.8	5,992.8	5,992.8	21.2	8.4	-169.23		2.7	290.0	519.6	493.2	26.39	19.687	
6,100.0	6,091.6	6,092.6	6,092.6	21.6	8.5	-169.37		2.7	290.0	526.5	499.7	26.81	19.638	
6,200.0	6,191.3	6,192.3	6,192.3	21.9	8.6	-169.51		2.7	290.0	533.3	506.1	27.22	19.590	
6,300.0	6,291.1	6,292.1	6,292.1	22.3	8.7	-169.64		2.7	290.0	540.2	512.5	27.64	19.543	
6,400.0	6,390.8	6,391.8	6,391.8	22.7	8.9	-169.77		2.7	290.0	547.1	519.0	28.06	19.497	
6,500.0	6,490.6	6,491.6	6,491.6	23.0	9.0	-169.90		2.7	290.0	553.9	525.4	28.48	19.452	
6,600.0	6,590.3	6,591.3	6,591.3	23.4	9.1	-170.03		2.7	290.0	560.8	531.9	28.90	19.407	
6,700.0	6,690.1	6,691.1	6,691.1	23.7	9.2	-170.15		2.7	290.0	567.7	538.3	29.31	19.364	
6,800.0	6,789.9	6,790.9	6,790.9	24.1	9.4	-170.27		2.7	290.0	574.5	544.8	29.73	19.322	
6,900.0	6,889.6	6,890.6	6,890.6	24.4	9.5	-170.38		2.7	290.0	581.4	551.3	30.15	19.281	
7,000.0	6,989.4	6,990.4	6,990.4	24.8	9.6	-170.50		2.7	290.0	588.3	557.7	30.58	19.241	
7,100.0	7,089.1	7,090.1	7,090.1	25.1	9.7	-170.61		2.7	290.0	595.2	564.2	31.00	19.201	
7,200.0	7,188.9	7,189.9	7,189.9	25.5	9.9	-170.72		2.7	290.0	602.1	570.6	31.42	19.162	
7,300.0	7,288.6	7,289.6	7,289.6	25.9	10.0	-170.82		2.7	290.0	608.9	577.1	31.84	19.125	
7,400.0	7,388.4	7,389.4	7,389.4	26.2	10.1	-170.93		2.7	290.0	615.8	583.6	32.26	19.087	
7,500.0	7,488.1	7,489.1	7,489.1	26.6	10.2	-171.03		2.7	290.0	622.7	590.0	32.69	19.051	
7,600.0	7,587.9	7,588.9	7,588.9	26.9	10.4	-171.13		2.7	290.0	629.6	596.5	33.11	19.015	
7,700.0	7,687.7	7,688.7	7,688.7	27.3	10.5	-171.22		2.7	290.0	636.5	603.0	33.53	18.981	
7,805.4	7,792.8	7,793.8	7,793.8	27.7	10.6	-171.32		2.7	290.0	643.8	609.8	33.98	18.945	
7,900.0	7,887.2	7,888.2	7,888.2	28.0	10.7	-171.41		2.7	290.0	649.5	615.1	34.38	18.891	
8,000.0	7,987.1	7,988.1	7,988.1	28.4	10.9	-171.47		2.7	290.0	653.9	619.1	34.81	18.788	
8,100.0	8,087.1	8,088.1	8,088.1	28.7	11.0	-171.51		2.7	290.0	656.6	621.4	35.23	18.640	
8,205.4	8,192.5	8,193.5	8,193.5	29.1	11.1	78.42		2.7	290.0	657.6	621.9	35.66	18.439	
8,300.0	8,287.1	8,288.1	8,288.1	29.4	11.3	78.42		2.7	290.0	657.6	621.5	36.05	18.241	
8,400.0	8,387.1	8,388.1	8,388.1	29.8	11.4	78.42		2.7	290.0	657.6	621.1	36.46	18.037	
8,500.0	8,487.1	8,488.1	8,488.1	30.1	11.5	78.42		2.7	290.0	657.6	620.7	36.87	17.837	
8,600.0	8,587.1	8,588.1	8,588.1	30.4	11.6	78.42		2.7	290.0	657.6	620.3	37.28	17.641	
8,700.0	8,687.1	8,688.1	8,688.1	30.8	11.8	78.42		2.7	290.0	657.6	619.9	37.69	17.448	
8,800.0	8,787.1	8,788.1	8,788.1	31.1	11.9	78.42		2.7	290.0	657.6	619.5	38.10	17.260	
8,900.0	8,887.1	8,888.1	8,888.1	31.5	12.0	78.42		2.7	290.0	657.6	619.1	38.51	17.076	
9,000.0	8,987.1	8,988.1	8,988.1	31.8	12.1	78.42		2.7	290.0	657.6	618.7	38.92	16.895	
9,100.0	9,087.1	9,088.1	9,088.1	32.2	12.3	78.42		2.7	290.0	657.6	618.2	39.33	16.718	
9,200.0	9,187.1	9,188.1	9,188.1	32.5	12.4	78.42		2.7	290.0	657.6	617.8	39.74	16.545	
9,300.0	9,287.1	9,288.1	9,288.1	32.9	12.5	78.42		2.7	290.0	657.6	617.4	40.16	16.375	
9,400.0	9,387.1	9,388.1	9,388.1	33.2	12.7	78.42		2.7	290.0	657.6	617.0	40.57	16.208	
9,500.0	9,487.1	9,488.1	9,488.1	33.5	12.8	78.42		2.7	290.0	657.6	616.6	40.98	16.044	
9,600.0	9,587.1	9,588.1	9,588.1	33.9	12.9	78.42		2.7	290.0	657.6	616.2	41.40	15.884	
9,700.0	9,687.1	9,688.1	9,688.1	34.2	13.0	78.42		2.7	290.0	657.6	615.8	41.81	15.727	
9,800.0	9,787.1	9,788.1	9,788.1	34.6	13.2	78.42		2.7	290.0	657.6	615.3	42.23	15.572	
9,900.0	9,887.1	9,888.1	9,888.1	34.9	13.3	78.42		2.7	290.0	657.6	614.9	42.64	15.421	
10,000.0	9,987.1	9,988.1	9,988.1	35.3	13.4	78.42		2.7	290.0	657.6	614.5	43.06	15.272	
10,100.0	10,087.1	10,088.1	10,088.1	35.6	13.6	78.42		2.7	290.0	657.6	614.1	43.47	15.126	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design		BEDLINGTON FEDERAL PROJECT (BULLDOG 2332) - BEDLINGTON FED COM 703H - OWB - PWP										Offset Site Error:		3.0 usft
Survey Program: 0-Standard Keeper 104, 11837-MWD+IFR1+FDIR												Offset Well Error:		3.0 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth	Vertical Depth	Measured Depth	Vertical Depth	Reference	Offset	Highside Toolface	Offset Wellbore Centre		Between Centres	Between Ellipses	Minimum Separation	Separation Factor		
(usft)	(usft)	(usft)	(usft)	(usft)	(usft)	(°)	+N/-S (usft)	+E/-W (usft)	(usft)	(usft)	(usft)			
10,200.0	10,187.1	10,188.1	10,188.1	36.0	13.7	78.42	2.7	290.0	657.6	613.7	43.89	14.983		
10,300.0	10,287.1	10,288.1	10,288.1	36.3	13.8	78.42	2.7	290.0	657.6	613.3	44.31	14.842		
10,337.9	10,325.0	10,326.0	10,326.0	36.5	13.9	78.42	2.7	290.0	657.6	613.1	44.46	14.789		
10,350.0	10,337.1	10,338.1	10,338.1	36.5	13.9	78.78	2.7	290.0	657.5	613.0	44.51	14.772		
10,400.0	10,387.0	10,388.0	10,388.0	36.7	13.9	79.11	2.7	290.0	656.9	612.2	44.70	14.695		
10,450.0	10,436.4	10,437.4	10,437.4	36.8	14.0	79.89	2.7	290.0	655.5	610.7	44.87	14.608		
10,500.0	10,484.9	10,485.9	10,485.9	37.0	14.1	81.09	2.7	290.0	653.5	608.5	45.02	14.516		
10,550.0	10,532.3	10,533.3	10,533.3	37.2	14.1	82.64	2.7	290.0	651.1	606.0	45.15	14.420		
10,600.0	10,578.0	10,579.0	10,579.0	37.3	14.2	84.50	2.7	290.0	648.7	603.4	45.27	14.328		
10,650.0	10,621.9	10,622.9	10,622.9	37.5	14.2	86.57	2.7	290.0	646.6	601.2	45.40	14.243		
10,700.0	10,663.5	10,664.5	10,664.5	37.6	14.3	88.75	2.7	290.0	645.2	599.7	45.53	14.172		
10,728.6	10,686.1	10,687.1	10,687.1	37.7	14.3	90.00	2.7	290.0	645.0	599.4	45.61	14.140		
10,750.0	10,702.5	10,703.5	10,703.5	37.7	14.3	90.92	2.7	290.0	645.1	599.4	45.69	14.121		
10,800.0	10,738.6	10,739.6	10,739.6	37.9	14.4	92.97	2.7	290.0	646.8	600.9	45.88	14.097 SF		
10,850.0	10,771.6	10,772.6	10,772.6	38.0	14.4	94.77	2.7	290.0	650.7	604.5	46.13	14.106		
10,900.0	10,801.2	10,802.2	10,802.2	38.1	14.5	96.21	2.7	290.0	657.2	610.8	46.42	14.156		
10,950.0	10,827.1	10,828.1	10,828.1	38.2	14.5	97.19	2.7	290.0	666.7	619.9	46.77	14.255		
11,000.0	10,849.3	10,850.3	10,850.3	38.2	14.5	97.61	2.7	290.0	679.4	632.3	47.16	14.407		
11,050.0	10,867.4	10,868.4	10,868.4	38.3	14.6	97.41	2.7	290.0	695.5	647.9	47.57	14.619		
11,100.0	10,881.4	10,882.4	10,882.4	38.4	14.6	96.50	2.7	290.0	714.8	666.8	48.00	14.894		
11,150.0	10,891.2	10,892.2	10,892.2	38.4	14.6	94.84	2.7	290.0	737.3	688.9	48.41	15.231		
11,200.0	10,896.7	10,897.7	10,897.7	38.5	14.6	92.39	2.7	290.0	762.6	713.8	48.80	15.628		
11,240.8	10,898.0	10,899.0	10,899.0	38.5	14.6	89.80	2.7	290.0	785.2	736.1	49.09	15.994		
11,300.0	10,897.6	10,898.6	10,898.6	38.6	14.6	89.77	2.7	290.0	820.3	770.8	49.49	16.577		
11,400.0	10,897.1	10,898.1	10,898.1	38.7	14.6	89.73	2.7	290.0	885.6	835.6	50.07	17.687		
11,500.0	10,896.6	10,897.6	10,897.6	38.8	14.6	89.68	2.7	290.0	956.9	906.4	50.56	18.927		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference	Offset	Semi Major Axis	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
0.0	0.0	1.0	1.0	3.0	3.0	89.46		3.0	320.0	320.0				
100.0	100.0	101.0	101.0	3.0	3.0	89.46		3.0	320.0	320.0	314.0	6.01	53.279	
200.0	200.0	201.0	201.0	3.0	3.0	89.46		3.0	320.0	320.0	313.9	6.08	52.627	
300.0	300.0	301.0	301.0	3.1	3.1	89.46		3.0	320.0	320.0	313.8	6.24	51.306	
400.0	400.0	401.0	401.0	3.2	3.2	89.46		3.0	320.0	320.0	313.5	6.47	49.462	
500.0	500.0	501.0	501.0	3.4	3.4	89.46		3.0	320.0	320.0	313.2	6.77	47.264	
600.0	600.0	601.0	601.0	3.6	3.6	89.46		3.0	320.0	320.0	312.9	7.13	44.874	
700.0	700.0	701.0	701.0	3.8	3.8	89.46		3.0	320.0	320.0	312.5	7.54	42.425	
800.0	800.0	801.0	801.0	4.0	4.0	89.46		3.0	320.0	320.0	312.0	8.00	40.013	
900.0	900.0	901.0	901.0	4.2	4.2	89.46		3.0	320.0	320.0	311.5	8.49	37.698	
1,000.0	1,000.0	1,001.0	1,001.0	4.5	4.5	89.46		3.0	320.0	320.0	311.0	9.01	35.516	
1,100.0	1,100.0	1,101.0	1,101.0	4.8	4.8	89.46		3.0	320.0	320.0	310.4	9.56	33.484	
1,200.0	1,200.0	1,201.0	1,201.0	5.1	5.1	89.46		3.0	320.0	320.0	309.9	10.12	31.606	
1,300.0	1,300.0	1,301.0	1,301.0	5.4	5.4	89.46		3.0	320.0	320.0	309.3	10.71	29.877	
1,400.0	1,400.0	1,401.0	1,401.0	5.7	5.7	89.46		3.0	320.0	320.0	308.7	11.31	28.289	
1,500.0	1,500.0	1,501.0	1,501.0	6.0	6.0	89.46		3.0	320.0	320.0	308.1	11.93	26.833	
1,600.0	1,600.0	1,601.0	1,601.0	6.3	6.3	89.46		3.0	320.0	320.0	307.4	12.55	25.497	
1,700.0	1,700.0	1,701.0	1,701.0	6.6	6.6	89.46		3.0	320.0	320.0	306.8	13.18	24.271	
1,800.0	1,800.0	1,801.0	1,801.0	6.9	6.9	89.46		3.0	320.0	320.0	306.2	13.83	23.143	
1,900.0	1,900.0	1,901.0	1,901.0	7.2	7.2	89.46		3.0	320.0	320.0	305.5	14.48	22.105	
2,000.0	2,000.0	2,001.0	2,001.0	7.6	7.6	89.46		3.0	320.0	320.0	304.9	15.13	21.148	
2,100.0	2,100.0	2,101.0	2,101.0	7.9	7.9	89.46		3.0	320.0	320.0	304.2	15.79	20.263	
2,200.0	2,200.0	2,201.0	2,201.0	8.2	8.2	89.46		3.0	320.0	320.0	303.5	16.46	19.444	
2,300.0	2,300.0	2,301.0	2,301.0	8.6	8.6	89.46		3.0	320.0	320.0	302.9	17.13	18.684	
2,400.0	2,400.0	2,401.0	2,401.0	8.9	8.9	89.46		3.0	320.0	320.0	302.2	17.80	17.977	
2,416.3	2,416.3	2,417.3	2,417.3	9.0	9.0	89.46		3.0	320.0	320.0	302.1	17.91	17.866	CC
2,500.0	2,500.0	2,500.0	2,500.0	9.2	9.2	89.46		3.0	320.0	320.0	301.5	18.47	17.322	ES
2,600.0	2,600.0	2,591.2	2,591.2	9.6	9.5	-160.47		2.6	321.4	323.2	304.1	19.09	16.925	
2,700.0	2,699.8	2,683.9	2,683.7	9.9	9.8	-160.46		1.3	325.5	332.5	312.8	19.69	16.882	
2,800.0	2,799.6	2,783.2	2,782.9	10.2	10.2	-160.57		-0.4	330.6	344.2	323.8	20.33	16.926	
2,900.0	2,899.4	2,882.5	2,882.1	10.5	10.5	-160.67		-2.0	335.7	355.9	334.9	20.98	16.964	
3,000.0	2,999.1	2,981.8	2,981.2	10.9	10.8	-160.76		-3.6	340.8	367.6	346.0	21.63	16.997	
3,100.0	3,098.9	3,081.1	3,080.4	11.2	11.1	-160.85		-5.2	346.0	379.3	357.0	22.28	17.024	
3,200.0	3,198.6	3,180.4	3,179.6	11.5	11.5	-160.94		-6.8	351.1	391.0	368.0	22.94	17.047	
3,300.0	3,298.4	3,279.7	3,278.7	11.9	11.8	-161.02		-8.4	356.2	402.7	379.1	23.60	17.066	
3,400.0	3,398.1	3,379.0	3,377.9	12.2	12.1	-161.09		-10.0	361.3	414.4	390.1	24.26	17.081	
3,500.0	3,497.9	3,478.4	3,477.1	12.5	12.5	-161.16		-11.7	366.4	426.1	401.2	24.93	17.094	
3,600.0	3,597.6	3,577.7	3,576.2	12.9	12.8	-161.23		-13.3	371.6	437.8	412.2	25.60	17.104	
3,700.0	3,697.4	3,677.0	3,675.4	13.2	13.1	-161.29		-14.9	376.7	449.5	423.2	26.27	17.112	
3,800.0	3,797.2	3,776.3	3,774.6	13.5	13.5	-161.35		-16.5	381.8	461.2	434.3	26.94	17.118	
3,900.0	3,896.9	3,875.6	3,873.7	13.9	13.8	-161.41		-18.1	386.9	472.9	445.3	27.62	17.122	
4,000.0	3,996.7	3,974.9	3,972.9	14.2	14.1	-161.46		-19.7	392.1	484.6	456.3	28.30	17.125	
4,100.0	4,096.4	4,074.2	4,072.1	14.6	14.5	-161.52		-21.3	397.2	496.3	467.3	28.98	17.127	
4,200.0	4,196.2	4,173.5	4,171.2	14.9	14.8	-161.56		-23.0	402.3	508.0	478.4	29.66	17.127	
4,300.0	4,295.9	4,272.8	4,270.4	15.3	15.2	-161.61		-24.6	407.4	519.7	489.4	30.35	17.127	
4,400.0	4,395.7	4,372.2	4,369.6	15.6	15.5	-161.66		-26.2	412.5	531.5	500.4	31.03	17.125	
4,500.0	4,495.5	4,471.5	4,468.7	16.0	15.9	-161.70		-27.8	417.7	543.2	511.4	31.72	17.123	
4,600.0	4,595.2	4,570.8	4,567.9	16.3	16.2	-161.74		-29.4	422.8	554.9	522.5	32.41	17.121	
4,700.0	4,695.0	4,670.1	4,667.1	16.7	16.5	-161.78		-31.0	427.9	566.6	533.5	33.10	17.117	
4,800.0	4,794.7	4,769.4	4,766.2	17.0	16.9	-161.82		-32.7	433.0	578.3	544.5	33.79	17.114	
4,900.0	4,894.5	4,868.7	4,865.4	17.4	17.2	-161.86		-34.3	438.2	590.0	555.5	34.48	17.110	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	3.0 usft
Survey Program: 0-MWD+IFR1+FDIR													Offset Well Error:	3.0 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)						
5,000.0	4,994.2	4,968.0	4,964.6	17.7	17.6	-161.89	-35.9	443.3	601.7	566.5	35.18	17.105		
5,100.0	5,094.0	5,067.3	5,063.7	18.1	17.9	-161.92	-37.5	448.4	613.4	577.5	35.87	17.100		
5,200.0	5,193.7	5,166.6	5,162.9	18.4	18.3	-161.96	-39.1	453.5	625.1	588.6	36.57	17.095		
5,300.0	5,293.5	5,266.0	5,262.1	18.8	18.6	-161.99	-40.7	458.6	636.8	599.6	37.26	17.090		
5,400.0	5,393.3	5,365.3	5,361.2	19.1	19.0	-162.02	-42.3	463.8	648.5	610.6	37.96	17.084		
5,500.0	5,493.0	5,464.6	5,460.4	19.5	19.3	-162.05	-44.0	468.9	660.3	621.6	38.66	17.079		
5,600.0	5,592.8	5,563.9	5,559.6	19.8	19.7	-162.08	-45.6	474.0	672.0	632.6	39.36	17.073		
5,700.0	5,692.5	5,663.2	5,658.7	20.2	20.0	-162.10	-47.2	479.1	683.7	643.6	40.06	17.067		
5,800.0	5,792.3	5,762.5	5,757.9	20.5	20.4	-162.13	-48.8	484.3	695.4	654.6	40.76	17.061		
5,900.0	5,892.0	5,861.8	5,857.1	20.9	20.7	-162.15	-50.4	489.4	707.1	665.6	41.46	17.055		
6,000.0	5,991.8	5,961.1	5,956.2	21.2	21.1	-162.18	-52.0	494.5	718.8	676.7	42.16	17.049		
6,100.0	6,091.6	6,060.5	6,055.4	21.6	21.4	-162.20	-53.6	499.6	730.5	687.7	42.86	17.043		
6,200.0	6,191.3	6,159.8	6,154.6	21.9	21.8	-162.23	-55.3	504.7	742.2	698.7	43.57	17.037		
6,300.0	6,291.1	6,259.1	6,253.7	22.3	22.1	-162.25	-56.9	509.9	753.9	709.7	44.27	17.031		
6,400.0	6,390.8	6,358.4	6,352.9	22.7	22.5	-162.27	-58.5	515.0	765.7	720.7	44.97	17.025		
6,500.0	6,490.6	6,457.7	6,452.1	23.0	22.8	-162.29	-60.1	520.1	777.4	731.7	45.68	17.018		
6,600.0	6,590.3	6,557.0	6,551.2	23.4	23.2	-162.31	-61.7	525.2	789.1	742.7	46.38	17.012		
6,700.0	6,690.1	6,656.3	6,650.4	23.7	23.5	-162.33	-63.3	530.3	800.8	753.7	47.09	17.006		
6,800.0	6,789.9	6,755.6	6,749.6	24.1	23.9	-162.35	-65.0	535.5	812.5	764.7	47.79	17.000		
6,900.0	6,889.6	6,854.9	6,848.7	24.4	24.2	-162.37	-66.6	540.6	824.2	775.7	48.50	16.994		
7,000.0	6,989.4	6,954.3	6,947.9	24.8	24.6	-162.39	-68.2	545.7	835.9	786.7	49.21	16.988		
7,100.0	7,089.1	7,053.6	7,047.1	25.1	24.9	-162.40	-69.8	550.8	847.6	797.7	49.91	16.982		
7,200.0	7,188.9	7,152.9	7,146.2	25.5	25.3	-162.42	-71.4	556.0	859.4	808.7	50.62	16.976		
7,300.0	7,288.6	7,252.2	7,245.4	25.9	25.6	-162.44	-73.0	561.1	871.1	819.7	51.33	16.970		
7,400.0	7,388.4	7,351.5	7,344.6	26.2	26.0	-162.45	-74.6	566.2	882.8	830.7	52.04	16.964		
7,500.0	7,488.1	7,450.8	7,443.7	26.6	26.4	-162.47	-76.3	571.3	894.5	841.8	52.75	16.959		
7,600.0	7,587.9	7,550.1	7,542.9	26.9	26.7	-162.48	-77.9	576.4	906.2	852.8	53.45	16.953		
7,700.0	7,687.7	7,649.4	7,642.1	27.3	27.1	-162.50	-79.5	581.6	917.9	863.8	54.16	16.947		
7,805.4	7,792.8	7,754.1	7,746.6	27.7	27.4	-162.51	-81.2	587.0	930.3	875.4	54.91	16.941		
7,900.0	7,887.2	7,848.1	7,840.5	28.0	27.8	-162.55	-82.7	591.8	940.6	885.0	55.58	16.923		
8,000.0	7,987.1	7,947.7	7,939.9	28.4	28.1	-162.54	-84.3	597.0	949.9	893.6	56.29	16.875		
8,100.0	8,087.1	8,047.4	8,039.4	28.7	28.5	-162.50	-86.0	602.1	957.6	900.6	57.00	16.800		
8,205.4	8,192.5	8,152.6	8,144.5	29.1	28.9	87.52	-87.7	607.5	963.9	906.1	57.74	16.693		
8,300.0	8,287.1	8,247.1	8,238.8	29.4	29.2	87.62	-89.2	612.4	968.7	910.3	58.40	16.586		
8,400.0	8,387.1	8,346.9	8,338.5	29.8	29.5	87.73	-90.8	617.5	973.8	914.7	59.10	16.476		
8,500.0	8,487.1	8,446.8	8,438.2	30.1	29.9	87.84	-92.5	622.7	978.9	919.1	59.80	16.368		
8,600.0	8,587.1	8,546.6	8,537.9	30.4	30.3	87.94	-94.1	627.8	984.0	923.5	60.50	16.263		
8,700.0	8,687.1	8,646.5	8,637.6	30.8	30.6	88.05	-95.7	633.0	989.1	927.9	61.20	16.161		
8,800.0	8,787.1	8,746.3	8,737.3	31.1	31.0	88.15	-97.3	638.1	994.2	932.3	61.90	16.060		
8,900.0	8,887.1	8,846.2	8,837.0	31.5	31.3	88.26	-98.9	643.3	999.3	936.7	62.60	15.962 SF		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to KB=26' @ 3648.0usft (McVay 8)


Offset Depths are relative to Offset Datum

Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: BEDLINGTON FED COM 502H

Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30

Grid Convergence at Surface is: 0.37°

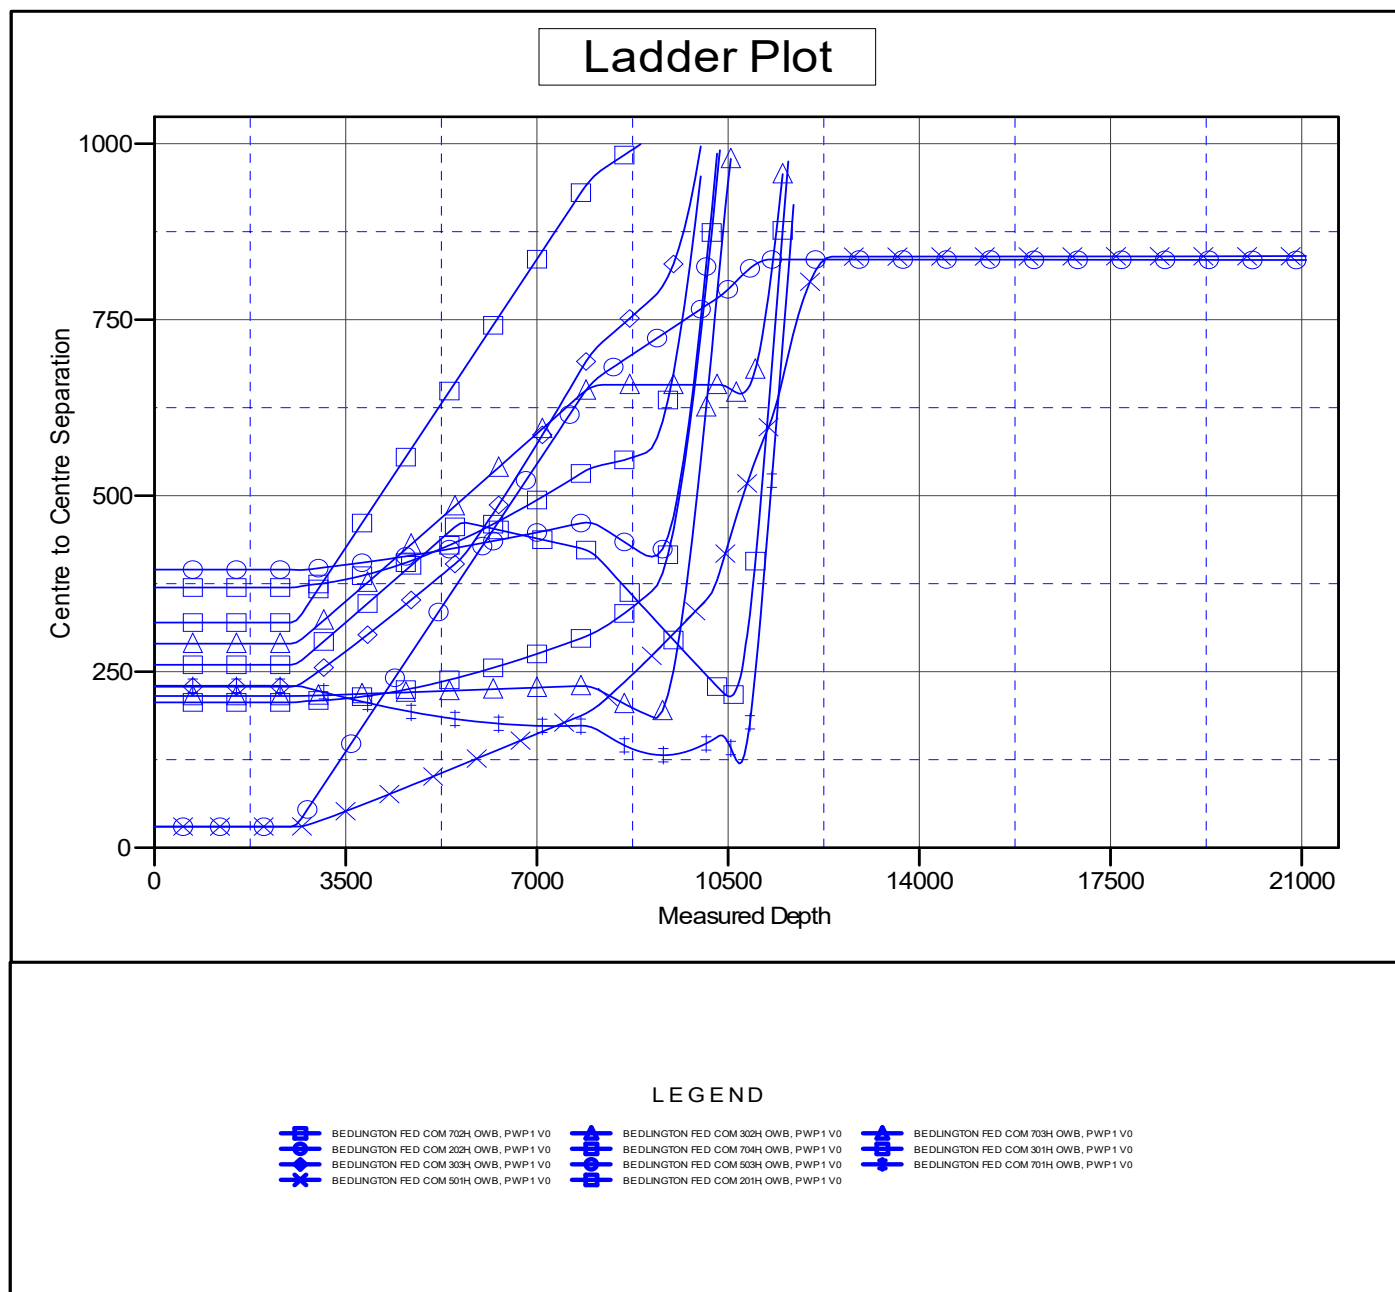

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Concho Resources LLC

Anticollision Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Reference Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site Error:	3.0 usft	North Reference:	Grid
Reference Well:	BEDLINGTON FED COM 502H	Survey Calculation Method:	Minimum Curvature
Well Error:	3.0 usft	Output errors are at	2.00 sigma
Reference Wellbore	OWB	Database:	edm
Reference Design:	PWP1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to KB=26' @ 3648.0usft (McVay 8)

Offset Depths are relative to Offset Datum


Central Meridian is 104° 20' 0.000 W

Coordinates are relative to: BEDLINGTON FED COM 502H

Coordinate System is US State Plane 1927 (Exact solution), New Mexico East 30

Grid Convergence at Surface is: 0.37°

Separation Factor Plot

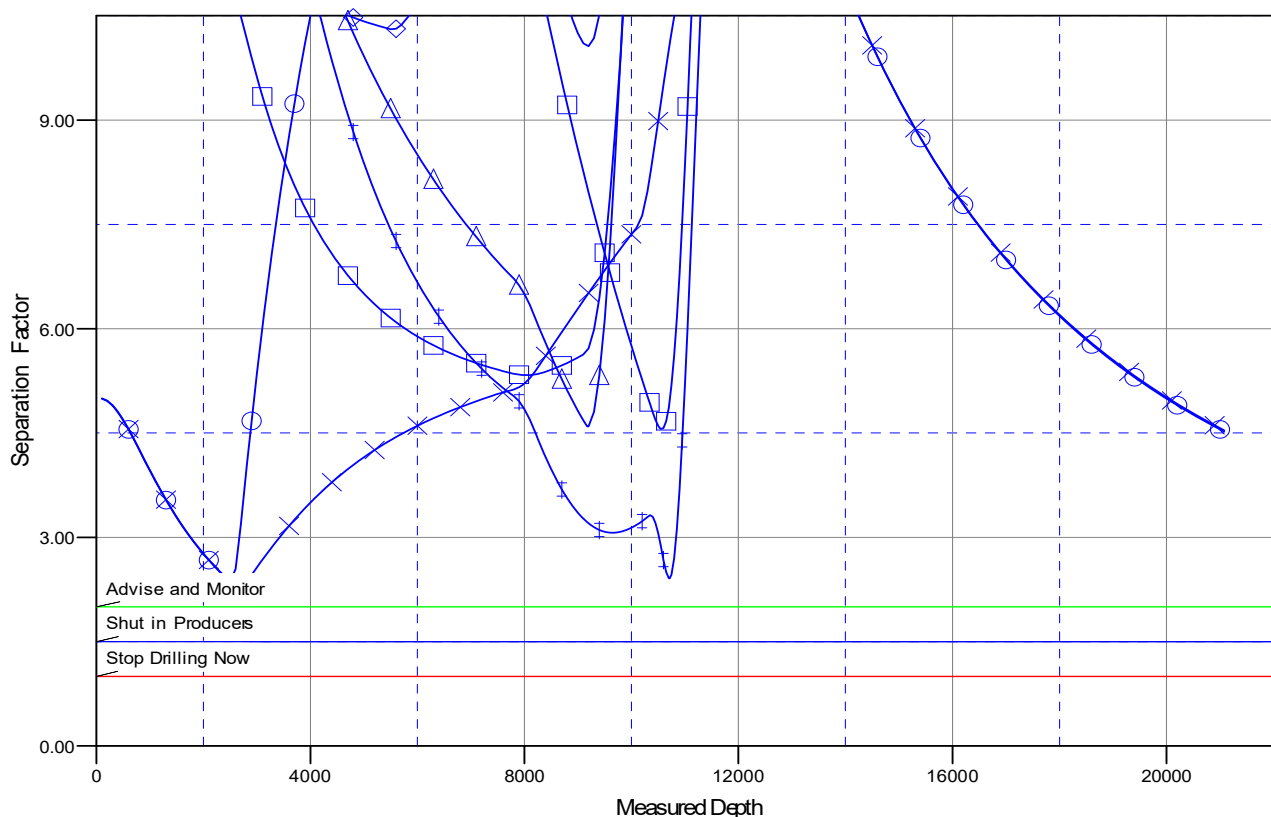

LEGEND

	BEDLINGTON FED COM 702H OWB, PWP1 V0		BEDLINGTON FED COM 302H OWB, PWP1 V0		BEDLINGTON FED COM 703H OWB, PWP1 V0
	BEDLINGTON FED COM 202H OWB, PWP1 V0		BEDLINGTON FED COM 704H OWB, PWP1 V0		BEDLINGTON FED COM 301H OWB, PWP1 V0
	BEDLINGTON FED COM 303H OWB, PWP1 V0		BEDLINGTON FED COM 503H OWB, PWP1 V0		BEDLINGTON FED COM 701H OWB, PWP1 V0
	BEDLINGTON FED COM 501H OWB, PWP1 V0		BEDLINGTON FED COM 201H OWB, PWP1 V0		

DELAWARE BASIN EAST

BULLDOG PROSPECT (NM-E)

BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)

BEDLINGTON FED COM 502H

OWB

Plan: PWP1

Standard Survey Report

08 June, 2020

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Well:	BEDLINGTON FED COM 502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Project	BULLDOG PROSPECT (NM-E)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	New Mexico East 3001		

Well	BEDLINGTON FED COM 502H			
Well Position	+N/-S	0.0 usft	Northing:	456,933.55 usft
	+E/-W	0.0 usft	Easting:	711,653.45 usft
Position Uncertainty		3.0 usft	Wellhead Elevation:	usft
			Latitude:	32° 15' 15.739 N
			Longitude:	103° 38' 55.244 W
			Ground Level:	3,622.0 usft

Wellbore	OWB
-----------------	-----

Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	6/8/2020	6.70	59.95	47,608.67205915

Design	PWP1
---------------	------

Audit Notes:	
Version:	Phase: PLAN Tie On Depth: 0.0

Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.0	0.0	0.0	357.68

Survey Tool Program		Date	6/8/2020		
From (usft)	To (usft)	Survey (Wellbore)	Tool Name	Description	
0.0	21,080.0	PWP1 (OWB)	MWD+IFR1+FDIR	OWSG MWD + IFR1 + FDIR Correction	

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	0.00	0.00	700.0	0.0	0.0	0.0	0.00	0.00	0.00
800.0	0.00	0.00	800.0	0.0	0.0	0.0	0.00	0.00	0.00
900.0	0.00	0.00	900.0	0.0	0.0	0.0	0.00	0.00	0.00
1,000.0	0.00	0.00	1,000.0	0.0	0.0	0.0	0.00	0.00	0.00
1,100.0	0.00	0.00	1,100.0	0.0	0.0	0.0	0.00	0.00	0.00
1,200.0	0.00	0.00	1,200.0	0.0	0.0	0.0	0.00	0.00	0.00
1,300.0	0.00	0.00	1,300.0	0.0	0.0	0.0	0.00	0.00	0.00
1,400.0	0.00	0.00	1,400.0	0.0	0.0	0.0	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Well:	BEDLINGTON FED COM 502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
1,500.0	0.00	0.00	1,500.0	0.0	0.0	0.0	0.00	0.00	0.00
1,600.0	0.00	0.00	1,600.0	0.0	0.0	0.0	0.00	0.00	0.00
1,700.0	0.00	0.00	1,700.0	0.0	0.0	0.0	0.00	0.00	0.00
1,800.0	0.00	0.00	1,800.0	0.0	0.0	0.0	0.00	0.00	0.00
1,900.0	0.00	0.00	1,900.0	0.0	0.0	0.0	0.00	0.00	0.00
2,000.0	0.00	0.00	2,000.0	0.0	0.0	0.0	0.00	0.00	0.00
2,100.0	0.00	0.00	2,100.0	0.0	0.0	0.0	0.00	0.00	0.00
2,200.0	0.00	0.00	2,200.0	0.0	0.0	0.0	0.00	0.00	0.00
2,300.0	0.00	0.00	2,300.0	0.0	0.0	0.0	0.00	0.00	0.00
2,400.0	0.00	0.00	2,400.0	0.0	0.0	0.0	0.00	0.00	0.00
2,500.0	0.00	0.00	2,500.0	0.0	0.0	0.0	0.00	0.00	0.00
Start Build 2.00									
2,600.0	2.00	249.94	2,600.0	-0.6	-1.6	-0.5	2.00	2.00	0.00
2,700.0	4.00	249.94	2,699.8	-2.4	-6.6	-2.1	2.00	2.00	0.00
Start 5105.4 hold at 2700.0 MD									
2,800.0	4.00	249.94	2,799.6	-4.8	-13.1	-4.3	0.00	0.00	0.00
2,900.0	4.00	249.94	2,899.4	-7.2	-19.7	-6.4	0.00	0.00	0.00
3,000.0	4.00	249.94	2,999.1	-9.6	-26.2	-8.5	0.00	0.00	0.00
3,100.0	4.00	249.94	3,098.9	-12.0	-32.8	-10.6	0.00	0.00	0.00
3,200.0	4.00	249.94	3,198.6	-14.4	-39.3	-12.7	0.00	0.00	0.00
3,300.0	4.00	249.94	3,298.4	-16.7	-45.9	-14.9	0.00	0.00	0.00
3,400.0	4.00	249.94	3,398.1	-19.1	-52.4	-17.0	0.00	0.00	0.00
3,500.0	4.00	249.94	3,497.9	-21.5	-59.0	-19.1	0.00	0.00	0.00
3,600.0	4.00	249.94	3,597.6	-23.9	-65.5	-21.2	0.00	0.00	0.00
3,700.0	4.00	249.94	3,697.4	-26.3	-72.1	-23.4	0.00	0.00	0.00
3,800.0	4.00	249.94	3,797.2	-28.7	-78.6	-25.5	0.00	0.00	0.00
3,900.0	4.00	249.94	3,896.9	-31.1	-85.2	-27.6	0.00	0.00	0.00
4,000.0	4.00	249.94	3,996.7	-33.5	-91.7	-29.7	0.00	0.00	0.00
4,100.0	4.00	249.94	4,096.4	-35.9	-98.3	-31.9	0.00	0.00	0.00
4,200.0	4.00	249.94	4,196.2	-38.3	-104.8	-34.0	0.00	0.00	0.00
4,300.0	4.00	249.94	4,295.9	-40.7	-111.4	-36.1	0.00	0.00	0.00
4,400.0	4.00	249.94	4,395.7	-43.1	-117.9	-38.2	0.00	0.00	0.00
4,500.0	4.00	249.94	4,495.5	-45.5	-124.5	-40.4	0.00	0.00	0.00
4,600.0	4.00	249.94	4,595.2	-47.9	-131.1	-42.5	0.00	0.00	0.00
4,700.0	4.00	249.94	4,695.0	-50.2	-137.6	-44.6	0.00	0.00	0.00
4,800.0	4.00	249.94	4,794.7	-52.6	-144.2	-46.7	0.00	0.00	0.00
4,900.0	4.00	249.94	4,894.5	-55.0	-150.7	-48.9	0.00	0.00	0.00
5,000.0	4.00	249.94	4,994.2	-57.4	-157.3	-51.0	0.00	0.00	0.00
5,100.0	4.00	249.94	5,094.0	-59.8	-163.8	-53.1	0.00	0.00	0.00
5,200.0	4.00	249.94	5,193.7	-62.2	-170.4	-55.2	0.00	0.00	0.00
5,300.0	4.00	249.94	5,293.5	-64.6	-176.9	-57.4	0.00	0.00	0.00
5,400.0	4.00	249.94	5,393.3	-67.0	-183.5	-59.5	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Well:	BEDLINGTON FED COM 502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
5,500.0	4.00	249.94	5,493.0	-69.4	-190.0	-61.6	0.00	0.00	0.00
5,600.0	4.00	249.94	5,592.8	-71.8	-196.6	-63.7	0.00	0.00	0.00
5,700.0	4.00	249.94	5,692.5	-74.2	-203.1	-65.9	0.00	0.00	0.00
5,800.0	4.00	249.94	5,792.3	-76.6	-209.7	-68.0	0.00	0.00	0.00
5,900.0	4.00	249.94	5,892.0	-79.0	-216.2	-70.1	0.00	0.00	0.00
6,000.0	4.00	249.94	5,991.8	-81.3	-222.8	-72.2	0.00	0.00	0.00
6,100.0	4.00	249.94	6,091.6	-83.7	-229.3	-74.4	0.00	0.00	0.00
6,200.0	4.00	249.94	6,191.3	-86.1	-235.9	-76.5	0.00	0.00	0.00
6,300.0	4.00	249.94	6,291.1	-88.5	-242.4	-78.6	0.00	0.00	0.00
6,400.0	4.00	249.94	6,390.8	-90.9	-249.0	-80.7	0.00	0.00	0.00
6,500.0	4.00	249.94	6,490.6	-93.3	-255.6	-82.9	0.00	0.00	0.00
6,600.0	4.00	249.94	6,590.3	-95.7	-262.1	-85.0	0.00	0.00	0.00
6,700.0	4.00	249.94	6,690.1	-98.1	-268.7	-87.1	0.00	0.00	0.00
6,800.0	4.00	249.94	6,789.9	-100.5	-275.2	-89.2	0.00	0.00	0.00
6,900.0	4.00	249.94	6,889.6	-102.9	-281.8	-91.4	0.00	0.00	0.00
7,000.0	4.00	249.94	6,989.4	-105.3	-288.3	-93.5	0.00	0.00	0.00
7,100.0	4.00	249.94	7,089.1	-107.7	-294.9	-95.6	0.00	0.00	0.00
7,200.0	4.00	249.94	7,188.9	-110.1	-301.4	-97.7	0.00	0.00	0.00
7,300.0	4.00	249.94	7,288.6	-112.4	-308.0	-99.9	0.00	0.00	0.00
7,400.0	4.00	249.94	7,388.4	-114.8	-314.5	-102.0	0.00	0.00	0.00
7,500.0	4.00	249.94	7,488.1	-117.2	-321.1	-104.1	0.00	0.00	0.00
7,600.0	4.00	249.94	7,587.9	-119.6	-327.6	-106.2	0.00	0.00	0.00
7,700.0	4.00	249.94	7,687.7	-122.0	-334.2	-108.4	0.00	0.00	0.00
7,800.0	4.00	249.94	7,787.4	-124.4	-340.7	-110.5	0.00	0.00	0.00
7,805.4	4.00	249.94	7,792.8	-124.5	-341.1	-110.6	0.00	0.00	0.00
Start Drop -1.00									
7,900.0	3.05	249.94	7,887.2	-126.5	-346.6	-112.4	1.00	-1.00	0.00
8,000.0	2.05	249.94	7,987.1	-128.1	-350.7	-113.7	1.00	-1.00	0.00
8,100.0	1.05	249.94	8,087.1	-129.0	-353.3	-114.6	1.00	-1.00	0.00
8,200.0	0.05	249.94	8,187.1	-129.3	-354.2	-114.9	1.00	-1.00	0.00
8,205.4	0.00	0.00	8,192.5	-129.3	-354.2	-114.9	1.00	-1.00	0.00
Start 2132.5 hold at 8205.4 MD									
8,300.0	0.00	0.00	8,287.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
8,400.0	0.00	0.00	8,387.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
8,500.0	0.00	0.00	8,487.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
8,600.0	0.00	0.00	8,587.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
8,700.0	0.00	0.00	8,687.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
8,800.0	0.00	0.00	8,787.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
8,900.0	0.00	0.00	8,887.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,000.0	0.00	0.00	8,987.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,100.0	0.00	0.00	9,087.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,200.0	0.00	0.00	9,187.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,300.0	0.00	0.00	9,287.1	-129.3	-354.2	-114.9	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Well:	BEDLINGTON FED COM 502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
9,400.0	0.00	0.00	9,387.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,500.0	0.00	0.00	9,487.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,600.0	0.00	0.00	9,587.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,700.0	0.00	0.00	9,687.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,800.0	0.00	0.00	9,787.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
9,900.0	0.00	0.00	9,887.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
10,000.0	0.00	0.00	9,987.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
10,100.0	0.00	0.00	10,087.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
10,200.0	0.00	0.00	10,187.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
10,300.0	0.00	0.00	10,287.1	-129.3	-354.2	-114.9	0.00	0.00	0.00
10,337.9	0.00	0.00	10,325.0	-129.3	-354.2	-114.9	0.00	0.00	0.00
Start DLS 10.00 TFO 359.65									
10,400.0	6.21	359.65	10,387.0	-126.0	-354.2	-111.5	10.00	10.00	0.00
10,500.0	16.21	359.65	10,484.9	-106.6	-354.3	-92.1	10.00	10.00	0.00
10,600.0	26.21	359.65	10,578.0	-70.4	-354.6	-56.0	10.00	10.00	0.00
10,700.0	36.21	359.65	10,663.5	-18.7	-354.9	-4.3	10.00	10.00	0.00
10,800.0	46.21	359.65	10,738.6	47.1	-355.3	61.5	10.00	10.00	0.00
10,900.0	56.21	359.65	10,801.2	125.0	-355.7	139.3	10.00	10.00	0.00
11,000.0	66.21	359.65	10,849.3	212.5	-356.3	226.8	10.00	10.00	0.00
11,100.0	76.21	359.65	10,881.4	307.0	-356.9	321.3	10.00	10.00	0.00
11,200.0	86.21	359.65	10,896.7	405.7	-357.5	419.9	10.00	10.00	0.00
11,240.8	90.29	359.65	10,898.0	446.5	-357.7	460.7	10.00	10.00	0.00
Start 9839.1 hold at 11240.8 MD									
11,300.0	90.29	359.65	10,897.6	505.7	-358.1	519.8	0.00	0.00	0.00
11,400.0	90.29	359.65	10,897.1	605.7	-358.7	619.7	0.00	0.00	0.00
11,500.0	90.29	359.65	10,896.6	705.7	-359.3	719.7	0.00	0.00	0.00
11,600.0	90.29	359.65	10,896.1	805.7	-359.9	819.6	0.00	0.00	0.00
11,700.0	90.29	359.65	10,895.6	905.7	-360.5	919.6	0.00	0.00	0.00
11,800.0	90.29	359.65	10,895.1	1,005.7	-361.1	1,019.5	0.00	0.00	0.00
11,900.0	90.29	359.65	10,894.6	1,105.7	-361.7	1,119.4	0.00	0.00	0.00
12,000.0	90.29	359.65	10,894.1	1,205.7	-362.3	1,219.4	0.00	0.00	0.00
12,100.0	90.29	359.65	10,893.6	1,305.7	-362.9	1,319.3	0.00	0.00	0.00
12,200.0	90.29	359.65	10,893.1	1,405.7	-363.5	1,419.3	0.00	0.00	0.00
12,300.0	90.29	359.65	10,892.6	1,505.7	-364.2	1,519.2	0.00	0.00	0.00
12,400.0	90.29	359.65	10,892.1	1,605.7	-364.8	1,619.1	0.00	0.00	0.00
12,500.0	90.29	359.65	10,891.6	1,705.7	-365.4	1,719.1	0.00	0.00	0.00
12,600.0	90.29	359.65	10,891.1	1,805.7	-366.0	1,819.0	0.00	0.00	0.00
12,700.0	90.29	359.65	10,890.5	1,905.7	-366.6	1,919.0	0.00	0.00	0.00
12,800.0	90.29	359.65	10,890.0	2,005.6	-367.2	2,018.9	0.00	0.00	0.00
12,900.0	90.29	359.65	10,889.5	2,105.6	-367.8	2,118.8	0.00	0.00	0.00
13,000.0	90.29	359.65	10,889.0	2,205.6	-368.4	2,218.8	0.00	0.00	0.00
13,100.0	90.29	359.65	10,888.5	2,305.6	-369.0	2,318.7	0.00	0.00	0.00
13,200.0	90.29	359.65	10,888.0	2,405.6	-369.6	2,418.6	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Well:	BEDLINGTON FED COM 502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
13,300.0	90.29	359.65	10,887.5	2,505.6	-370.2	2,518.6	0.00	0.00	0.00
13,400.0	90.29	359.65	10,887.0	2,605.6	-370.8	2,618.5	0.00	0.00	0.00
13,500.0	90.29	359.65	10,886.5	2,705.6	-371.5	2,718.5	0.00	0.00	0.00
13,600.0	90.29	359.65	10,886.0	2,805.6	-372.1	2,818.4	0.00	0.00	0.00
13,700.0	90.29	359.65	10,885.5	2,905.6	-372.7	2,918.3	0.00	0.00	0.00
13,800.0	90.29	359.65	10,885.0	3,005.6	-373.3	3,018.3	0.00	0.00	0.00
13,900.0	90.29	359.65	10,884.5	3,105.6	-373.9	3,118.2	0.00	0.00	0.00
14,000.0	90.29	359.65	10,883.9	3,205.6	-374.5	3,218.2	0.00	0.00	0.00
14,100.0	90.29	359.65	10,883.4	3,305.6	-375.1	3,318.1	0.00	0.00	0.00
14,200.0	90.29	359.65	10,882.9	3,405.6	-375.7	3,418.0	0.00	0.00	0.00
14,300.0	90.29	359.65	10,882.4	3,505.6	-376.3	3,518.0	0.00	0.00	0.00
14,400.0	90.29	359.65	10,881.9	3,605.6	-376.9	3,617.9	0.00	0.00	0.00
14,500.0	90.29	359.65	10,881.4	3,705.6	-377.5	3,717.9	0.00	0.00	0.00
14,600.0	90.29	359.65	10,880.9	3,805.6	-378.2	3,817.8	0.00	0.00	0.00
14,700.0	90.29	359.65	10,880.4	3,905.6	-378.8	3,917.7	0.00	0.00	0.00
14,800.0	90.29	359.65	10,879.9	4,005.6	-379.4	4,017.7	0.00	0.00	0.00
14,900.0	90.29	359.65	10,879.4	4,105.6	-380.0	4,117.6	0.00	0.00	0.00
15,000.0	90.29	359.65	10,878.9	4,205.6	-380.6	4,217.6	0.00	0.00	0.00
15,100.0	90.29	359.65	10,878.4	4,305.6	-381.2	4,317.5	0.00	0.00	0.00
15,200.0	90.29	359.65	10,877.9	4,405.6	-381.8	4,417.4	0.00	0.00	0.00
15,300.0	90.29	359.65	10,877.3	4,505.6	-382.4	4,517.4	0.00	0.00	0.00
15,400.0	90.29	359.65	10,876.8	4,605.6	-383.0	4,617.3	0.00	0.00	0.00
15,500.0	90.29	359.65	10,876.3	4,705.6	-383.6	4,717.3	0.00	0.00	0.00
15,600.0	90.29	359.65	10,875.8	4,805.6	-384.2	4,817.2	0.00	0.00	0.00
15,700.0	90.29	359.65	10,875.3	4,905.6	-384.8	4,917.1	0.00	0.00	0.00
15,800.0	90.29	359.65	10,874.8	5,005.6	-385.5	5,017.1	0.00	0.00	0.00
15,900.0	90.29	359.65	10,874.3	5,105.5	-386.1	5,117.0	0.00	0.00	0.00
16,000.0	90.29	359.65	10,873.8	5,205.5	-386.7	5,216.9	0.00	0.00	0.00
16,100.0	90.29	359.65	10,873.3	5,305.5	-387.3	5,316.9	0.00	0.00	0.00
16,200.0	90.29	359.65	10,872.8	5,405.5	-387.9	5,416.8	0.00	0.00	0.00
16,300.0	90.29	359.65	10,872.3	5,505.5	-388.5	5,516.8	0.00	0.00	0.00
16,400.0	90.29	359.65	10,871.8	5,605.5	-389.1	5,616.7	0.00	0.00	0.00
16,500.0	90.29	359.65	10,871.3	5,705.5	-389.7	5,716.6	0.00	0.00	0.00
16,600.0	90.29	359.65	10,870.7	5,805.5	-390.3	5,816.6	0.00	0.00	0.00
16,700.0	90.29	359.65	10,870.2	5,905.5	-390.9	5,916.5	0.00	0.00	0.00
16,800.0	90.29	359.65	10,869.7	6,005.5	-391.5	6,016.5	0.00	0.00	0.00
16,900.0	90.29	359.65	10,869.2	6,105.5	-392.1	6,116.4	0.00	0.00	0.00
17,000.0	90.29	359.65	10,868.7	6,205.5	-392.8	6,216.3	0.00	0.00	0.00
17,100.0	90.29	359.65	10,868.2	6,305.5	-393.4	6,316.3	0.00	0.00	0.00
17,200.0	90.29	359.65	10,867.7	6,405.5	-394.0	6,416.2	0.00	0.00	0.00
17,300.0	90.29	359.65	10,867.2	6,505.5	-394.6	6,516.2	0.00	0.00	0.00
17,400.0	90.29	359.65	10,866.7	6,605.5	-395.2	6,616.1	0.00	0.00	0.00
17,500.0	90.29	359.65	10,866.2	6,705.5	-395.8	6,716.0	0.00	0.00	0.00

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Well:	BEDLINGTON FED COM 502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
17,600.0	90.29	359.65	10,865.7	6,805.5	-396.4	6,816.0	0.00	0.00	0.00
17,700.0	90.29	359.65	10,865.2	6,905.5	-397.0	6,915.9	0.00	0.00	0.00
17,800.0	90.29	359.65	10,864.7	7,005.5	-397.6	7,015.9	0.00	0.00	0.00
17,900.0	90.29	359.65	10,864.1	7,105.5	-398.2	7,115.8	0.00	0.00	0.00
18,000.0	90.29	359.65	10,863.6	7,205.5	-398.8	7,215.7	0.00	0.00	0.00
18,100.0	90.29	359.65	10,863.1	7,305.5	-399.5	7,315.7	0.00	0.00	0.00
18,200.0	90.29	359.65	10,862.6	7,405.5	-400.1	7,415.6	0.00	0.00	0.00
18,300.0	90.29	359.65	10,862.1	7,505.5	-400.7	7,515.6	0.00	0.00	0.00
18,400.0	90.29	359.65	10,861.6	7,605.5	-401.3	7,615.5	0.00	0.00	0.00
18,500.0	90.29	359.65	10,861.1	7,705.5	-401.9	7,715.4	0.00	0.00	0.00
18,600.0	90.29	359.65	10,860.6	7,805.5	-402.5	7,815.4	0.00	0.00	0.00
18,700.0	90.29	359.65	10,860.1	7,905.5	-403.1	7,915.3	0.00	0.00	0.00
18,800.0	90.29	359.65	10,859.6	8,005.5	-403.7	8,015.2	0.00	0.00	0.00
18,900.0	90.29	359.65	10,859.1	8,105.5	-404.3	8,115.2	0.00	0.00	0.00
19,000.0	90.29	359.65	10,858.6	8,205.5	-404.9	8,215.1	0.00	0.00	0.00
19,100.0	90.29	359.65	10,858.1	8,305.4	-405.5	8,315.1	0.00	0.00	0.00
19,200.0	90.29	359.65	10,857.5	8,405.4	-406.1	8,415.0	0.00	0.00	0.00
19,300.0	90.29	359.65	10,857.0	8,505.4	-406.8	8,514.9	0.00	0.00	0.00
19,400.0	90.29	359.65	10,856.5	8,605.4	-407.4	8,614.9	0.00	0.00	0.00
19,500.0	90.29	359.65	10,856.0	8,705.4	-408.0	8,714.8	0.00	0.00	0.00
19,600.0	90.29	359.65	10,855.5	8,805.4	-408.6	8,814.8	0.00	0.00	0.00
19,700.0	90.29	359.65	10,855.0	8,905.4	-409.2	8,914.7	0.00	0.00	0.00
19,800.0	90.29	359.65	10,854.5	9,005.4	-409.8	9,014.6	0.00	0.00	0.00
19,900.0	90.29	359.65	10,854.0	9,105.4	-410.4	9,114.6	0.00	0.00	0.00
20,000.0	90.29	359.65	10,853.5	9,205.4	-411.0	9,214.5	0.00	0.00	0.00
20,100.0	90.29	359.65	10,853.0	9,305.4	-411.6	9,314.5	0.00	0.00	0.00
20,200.0	90.29	359.65	10,852.5	9,405.4	-412.2	9,414.4	0.00	0.00	0.00
20,300.0	90.29	359.65	10,852.0	9,505.4	-412.8	9,514.3	0.00	0.00	0.00
20,400.0	90.29	359.65	10,851.5	9,605.4	-413.5	9,614.3	0.00	0.00	0.00
20,500.0	90.29	359.65	10,850.9	9,705.4	-414.1	9,714.2	0.00	0.00	0.00
20,600.0	90.29	359.65	10,850.4	9,805.4	-414.7	9,814.2	0.00	0.00	0.00
20,700.0	90.29	359.65	10,849.9	9,905.4	-415.3	9,914.1	0.00	0.00	0.00
20,800.0	90.29	359.65	10,849.4	10,005.4	-415.9	10,014.0	0.00	0.00	0.00
20,900.0	90.29	359.65	10,848.9	10,105.4	-416.5	10,114.0	0.00	0.00	0.00
21,000.0	90.29	359.65	10,848.4	10,205.4	-417.1	10,213.9	0.00	0.00	0.00
21,080.0	90.29	359.65	10,848.0	10,285.3	-417.6	10,293.8	0.00	0.00	0.00
TD at 21080.0									

Concho Resources LLC

Survey Report

Company:	DELAWARE BASIN EAST	Local Co-ordinate Reference:	Well BEDLINGTON FED COM 502H
Project:	BULLDOG PROSPECT (NM-E)	TVD Reference:	KB=26' @ 3648.0usft (McVay 8)
Site:	BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)	MD Reference:	KB=26' @ 3648.0usft (McVay 8)
Well:	BEDLINGTON FED COM 502H	North Reference:	Grid
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	PWP1	Database:	edm

Design Targets

Target Name

- hit/miss target - Shape	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
LTP (BEDLINGTON F - plan misses target center by 30.0usft at 21000.0usft MD (10848.4 TVD, 10205.4 N, -417.1 E) - Point	0.00	0.00	10,848.0	10,235.4	-417.3	467,168.91	711,236.18	32° 16' 57.051 N	103° 38' 59.343 W
PBHL (BEDLINGTON - plan hits target center - Rectangle (sides W100.0 H10,415.0 D20.0)	0.29	179.65	10,848.0	10,285.3	-417.6	467,218.90	711,235.86	32° 16' 57.545 N	103° 38' 59.343 W
FTP (BEDLINGTON F - plan misses target center by 237.0usft at 10800.0usft MD (10738.6 TVD, 47.1 N, -355.3 E) - Circle (radius 50.0)	0.00	0.00	10,898.0	-128.3	-354.3	456,805.23	711,299.15	32° 15' 14.492 N	103° 38' 59.379 W

Plan Annotations

Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment
		+N/-S (usft)	+E/-W (usft)	
2500	2500	0	0	Start Build 2.00
2700	2700	-2	-7	Start 5105.4 hold at 2700.0 MD
7805	7793	-125	-341	Start Drop -1.00
8205	8192	-129	-354	Start 2132.5 hold at 8205.4 MD
10,338	10,325	-129	-354	Start DLS 10.00 TFO 359.65
11,241	10,898	447	-358	Start 9839.1 hold at 11240.8 MD
21,080	10,848	10,285	-418	TD at 21080.0



Checked By: _____ Approved By: _____ Date: _____








Project: BULLDOG PROSPECT (NM-E)
Site: BEDLINGTON FEDERAL PROJECT (BULLDOG 2332)
Well: BEDLINGTON FED COM 502H
Wellbore: OWB
Design: PWP1
GL: 3622.0
KB=26' @ 3648.0usft (McVay 8)

WELL DETAILS: BEDLINGTON FED COM 502H					
+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.0	0.0	456933.55	711653.45	32° 15' 15.739 N	103° 38' 55.244 W

DESIGN TARGET DETAILS						
Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude
LTP (BEDLINGTON FED COM 502H)	10848.0	10235.4	-417.3	467168.91	711236.18	32° 16' 57.051 N
PBHL (BEDLINGTON FED COM 502H)	10848.0	10285.3	-417.6	467218.90	711235.86	32° 16' 57.545 N
FTP (BEDLINGTON FED COM 502H)	10898.0	-128.3	-354.3	456805.23	711299.15	32° 15' 14.492 N

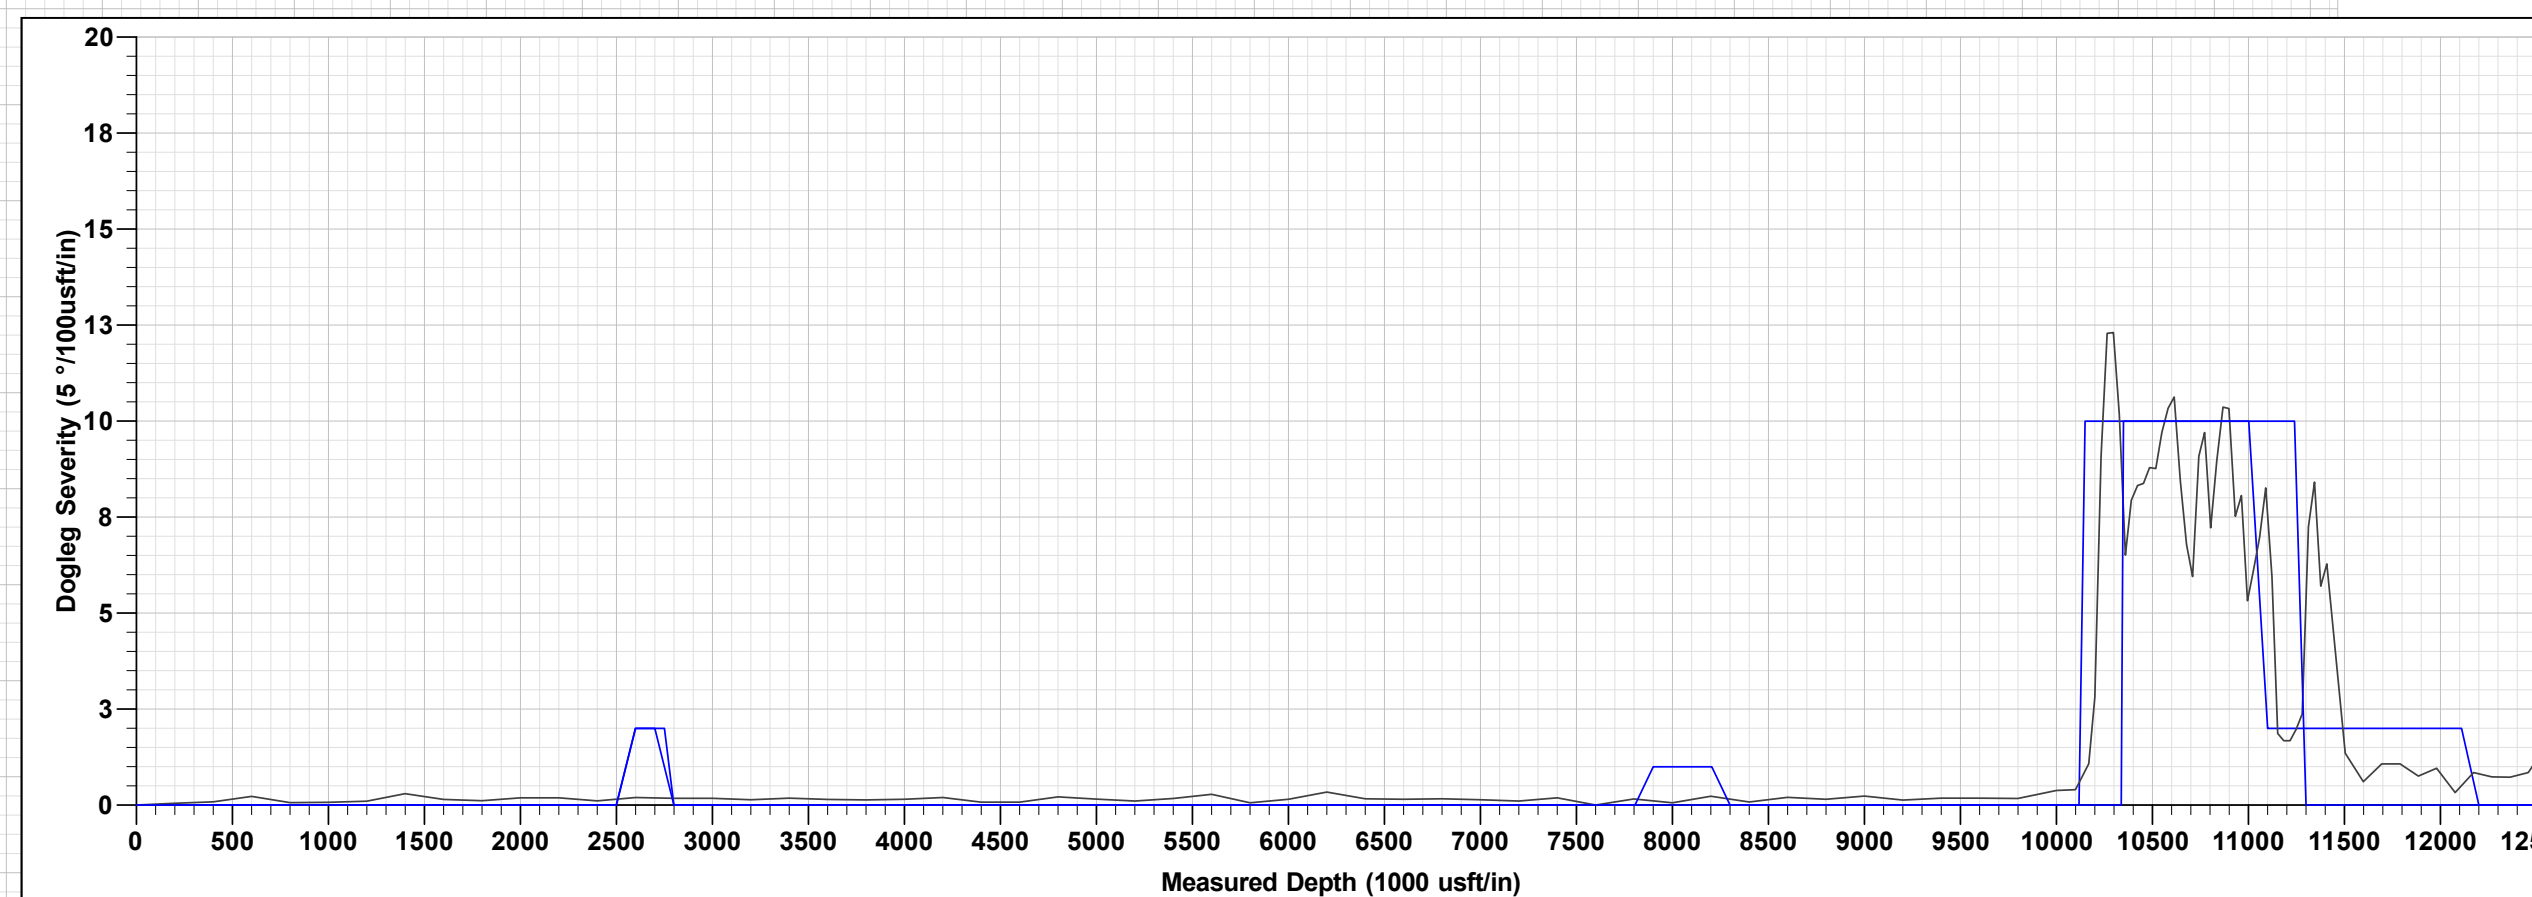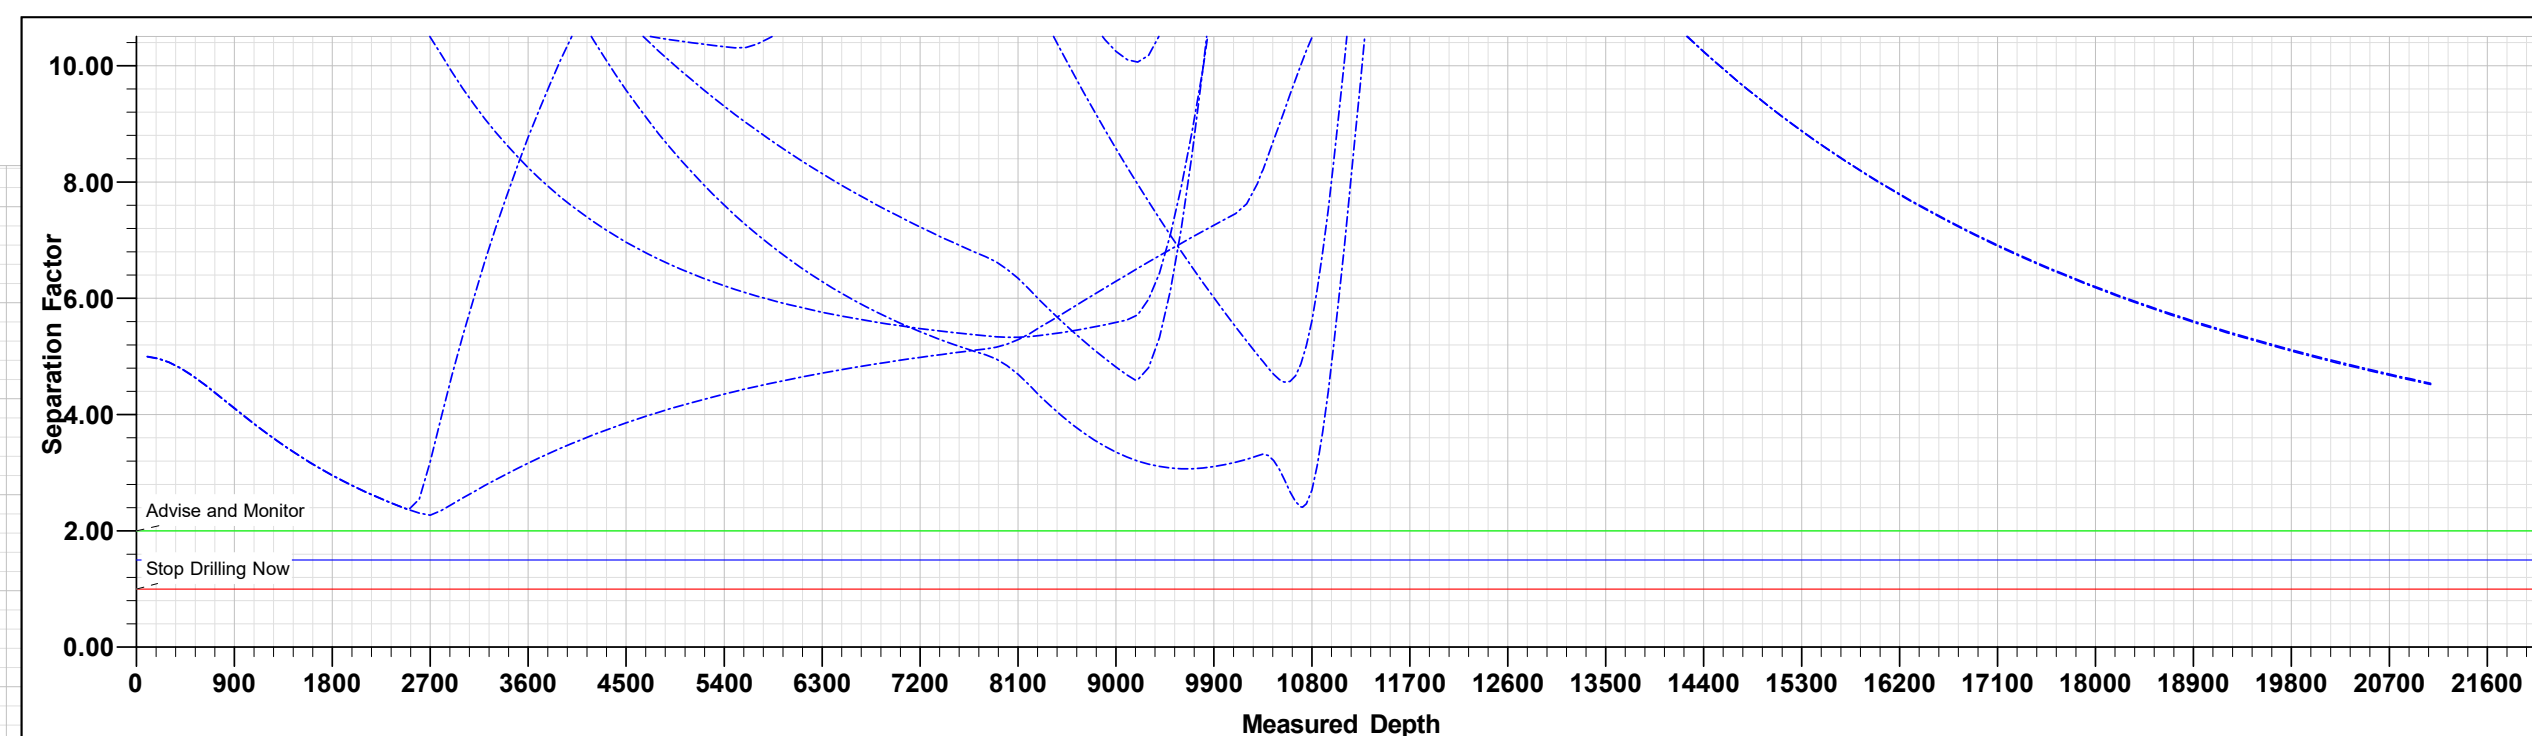

BEDLINGTON FED COM 502H									
MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Annotation
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2500.0	0.00	0.00	2500.0	0.0	0.0	0.00	0.00	0.0	Start Build 2.00
2700.0	4.00	249.94	2699.8	-2.4	-6.6	2.00	249.94	-2.1	Start 5105.4 hold at 2700.0 MD
7805.4	4.00	249.94	7792.8	-124.5	-341.1	0.00	0.00	-110.6	Start Drop -1.00
8205.4	0.00	0.00	8192.5	-129.3	-354.2	1.00	180.00	-114.9	Start DLS 10.00 TFO 359.65
10337.9	0.00	0.00	10325.0	-129.3	-354.2	0.00	0.00	-114.9	Start 9839.1 hold at 11240.8 MD
11240.8	90.29	359.65	10898.0	446.5	-357.7	10.00	359.65	460.7	
21080.0	90.29	359.65	10848.0	10285.3	-417.6	0.00	0.00	10293.8	TD at 21080.0

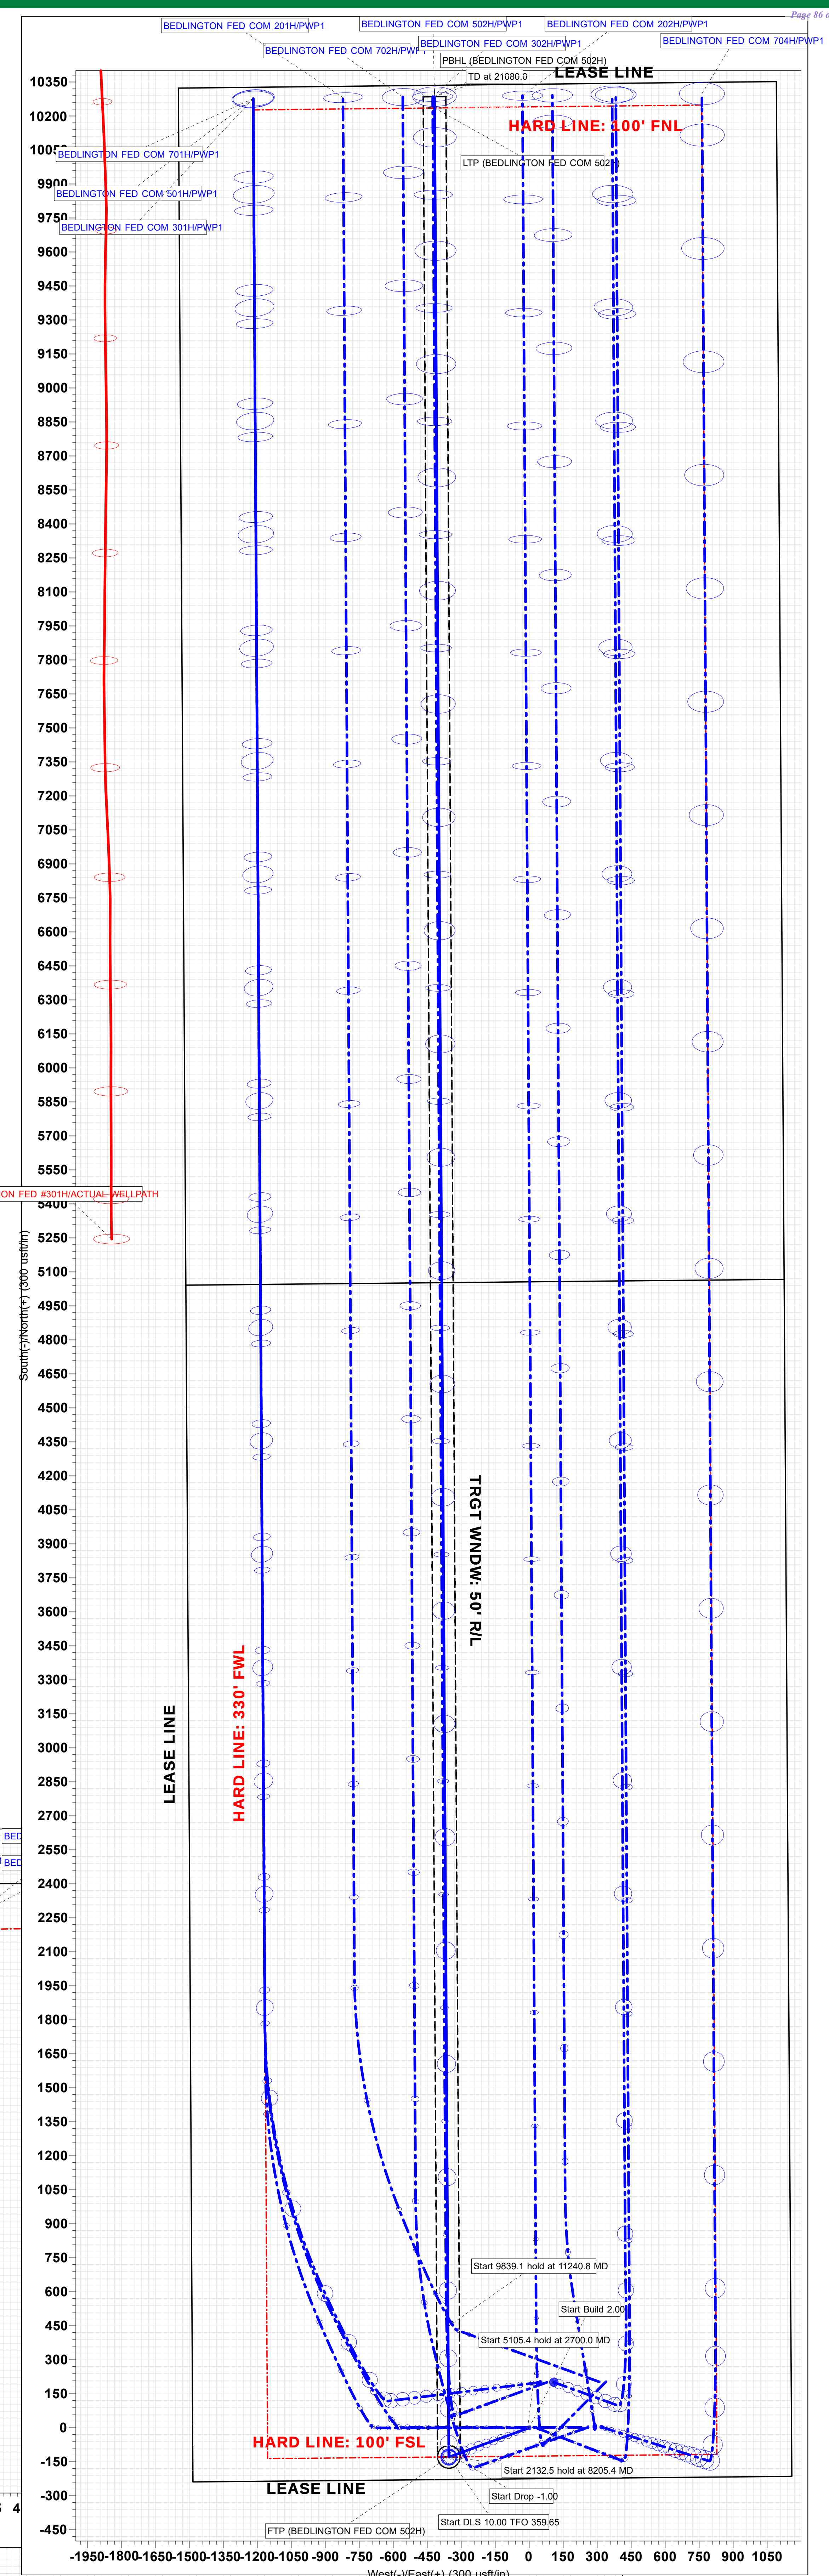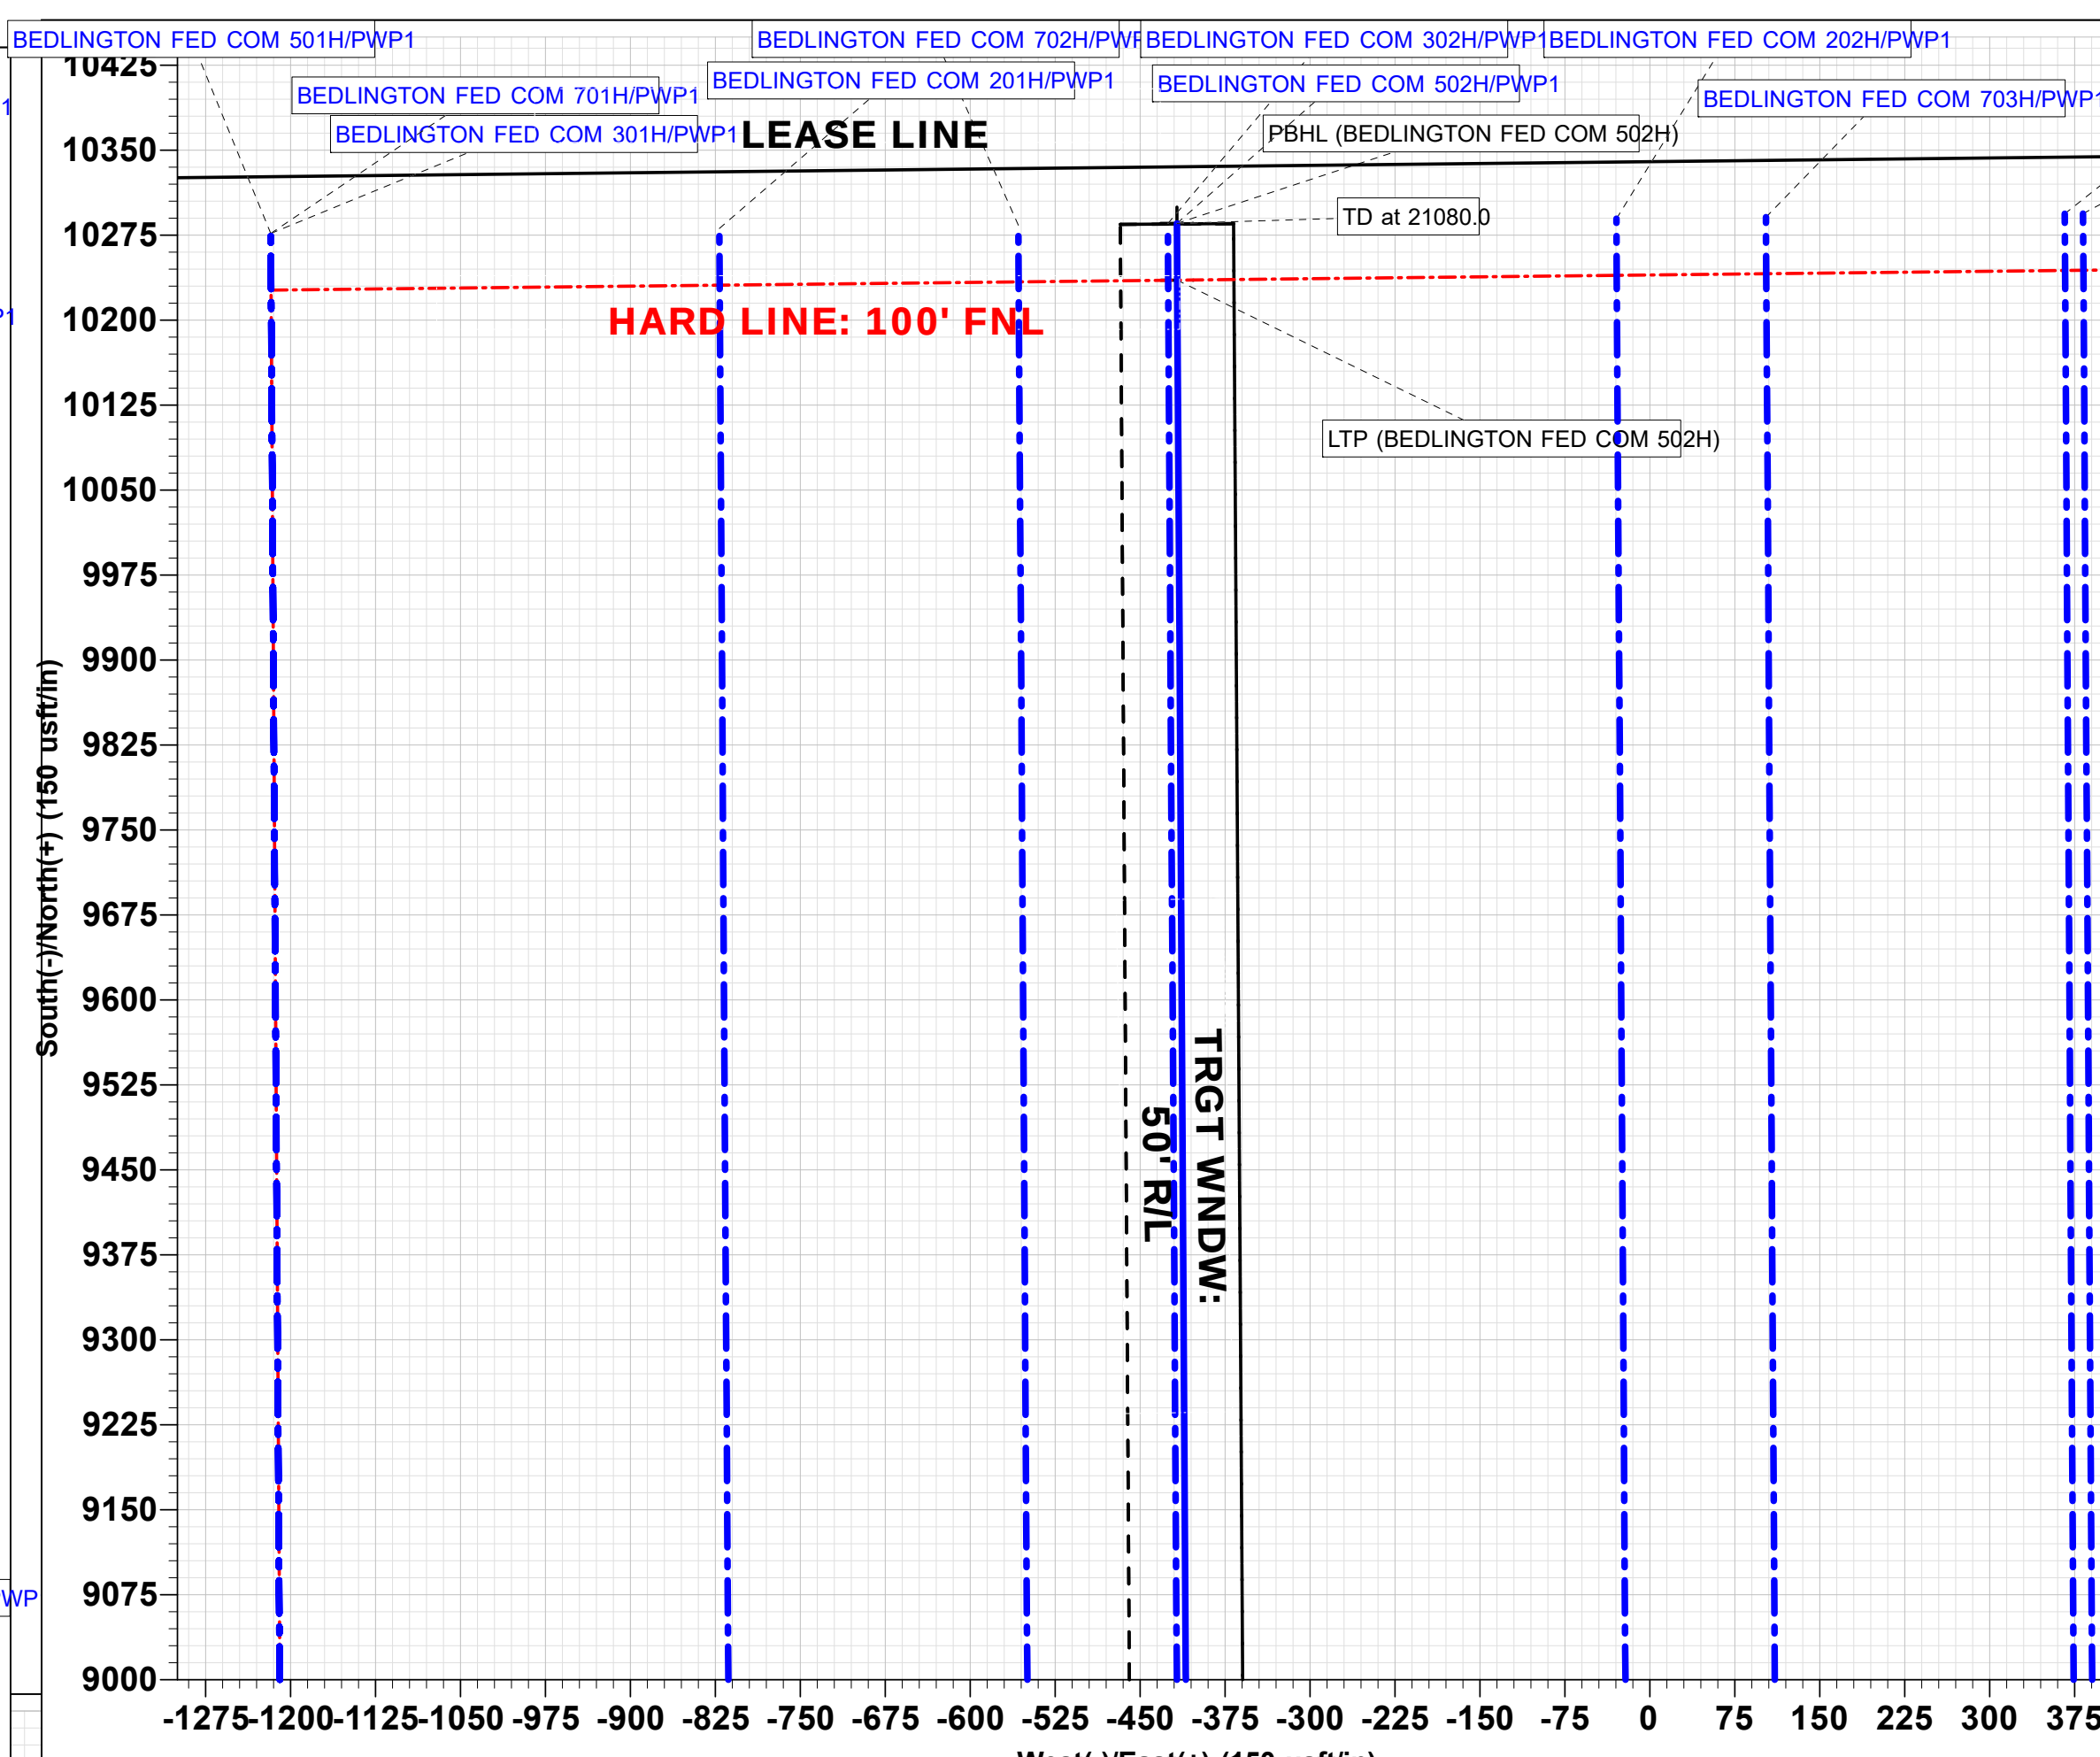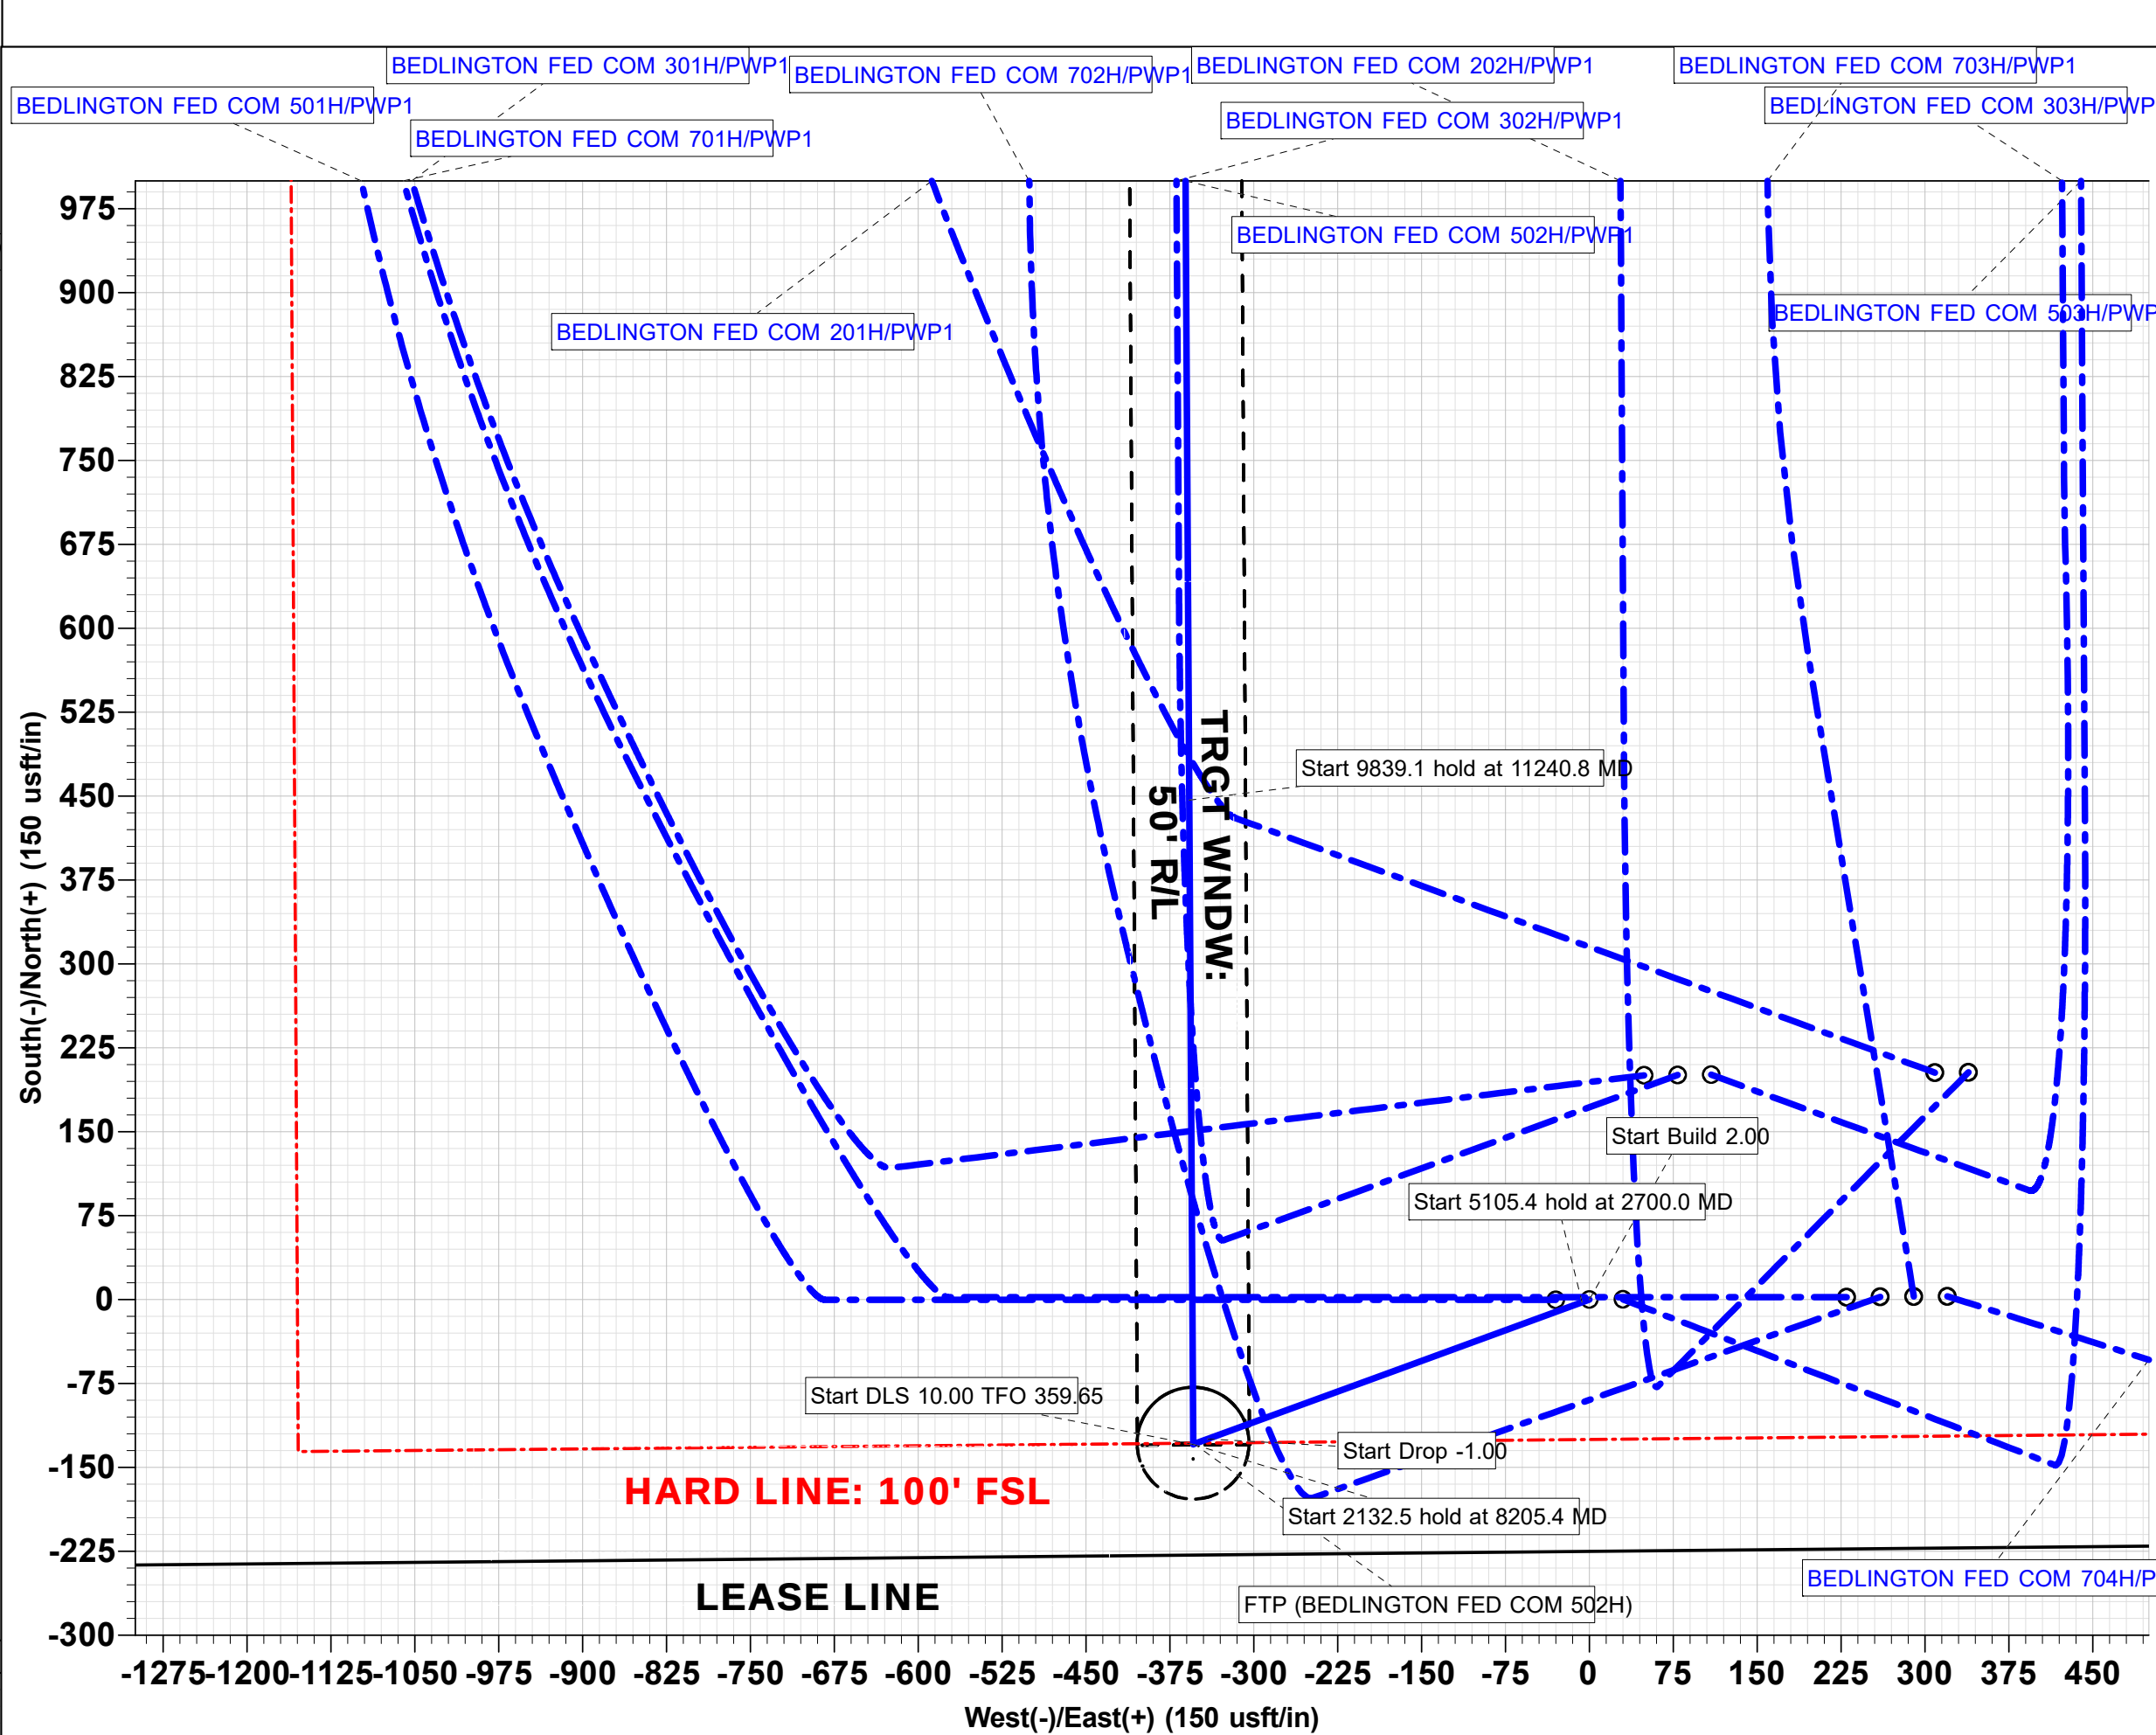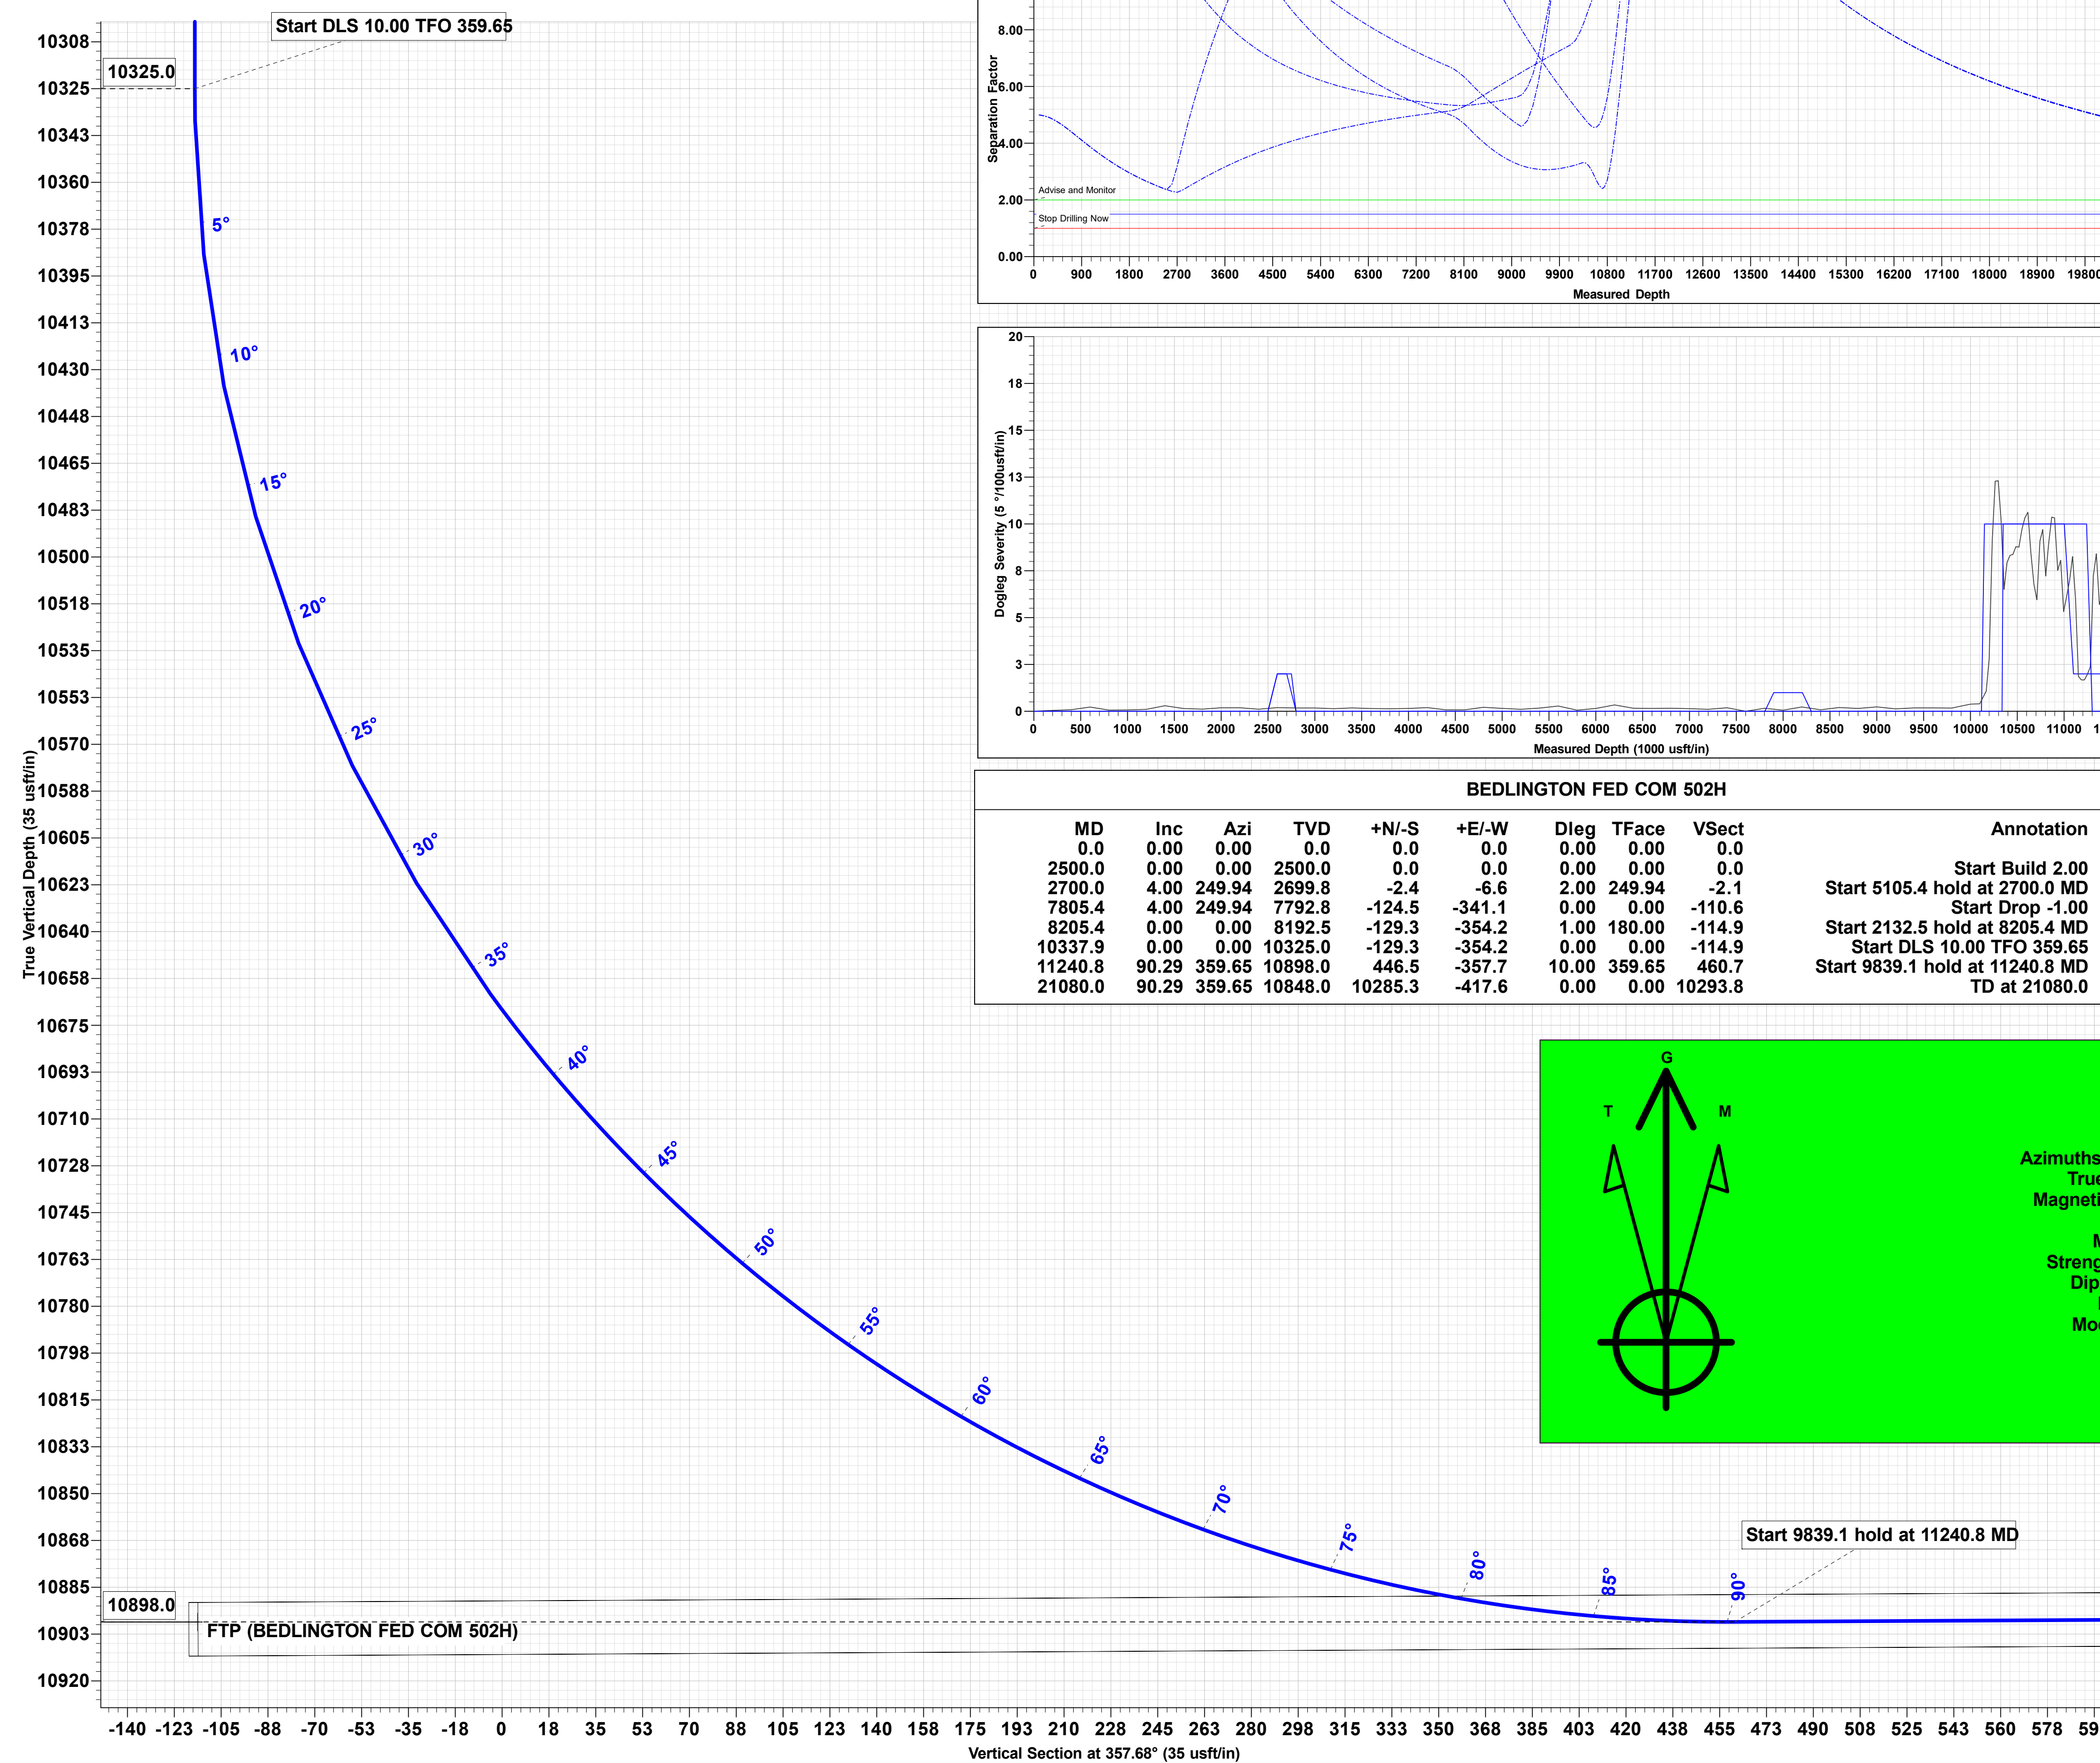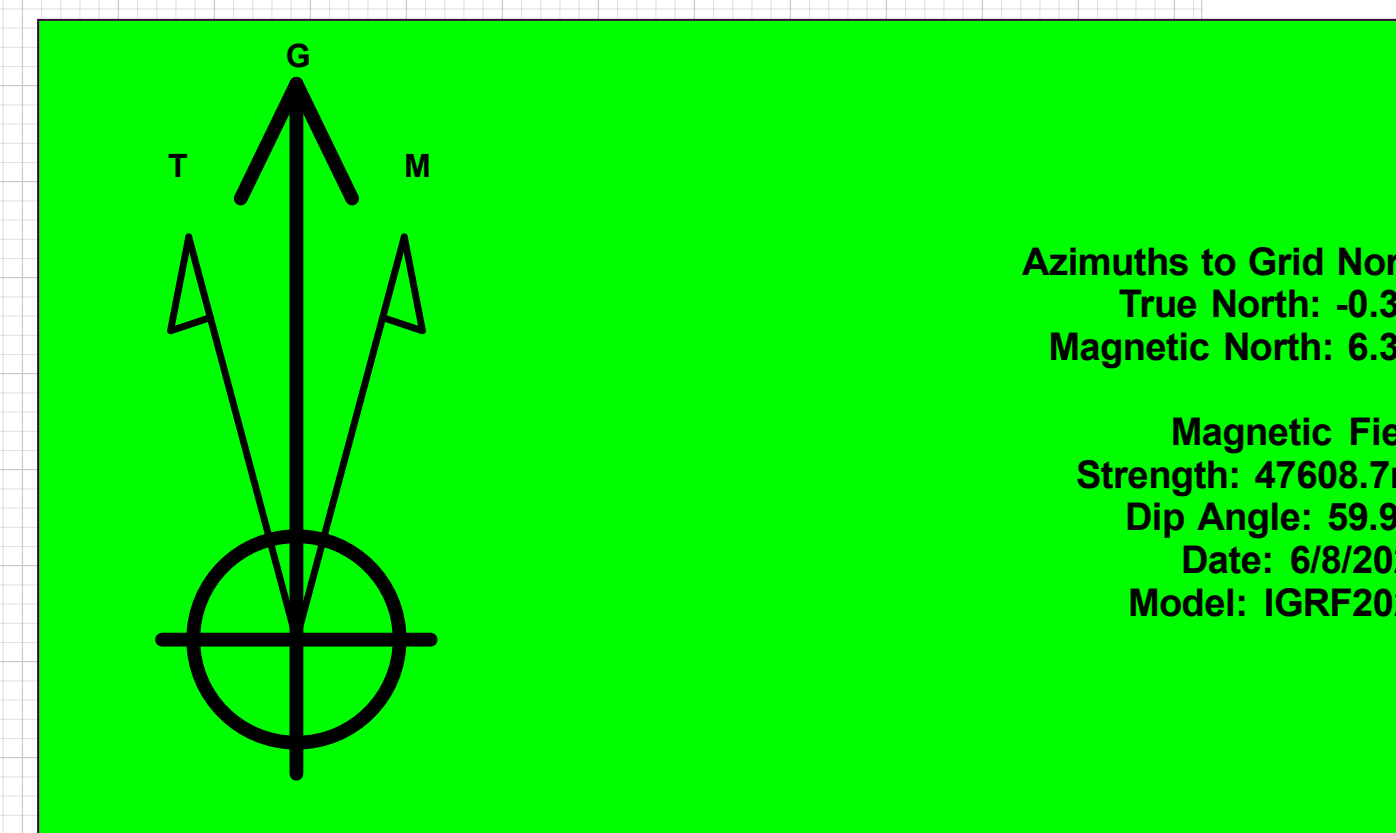

TRGT WNDW:
10 A/B

COG OPERATING LLC
HYDROGEN SULFIDE DRILLING OPERATIONS PLAN

1. HYDROGEN SULFIDE TRAINING

All personnel, whether regularly assigned, contracted, or employed on an unscheduled basis, will receive training from a qualified instructor in the following areas prior to commencing drilling operations on this well:

- a. The hazards and characteristics of hydrogen sulfide (H₂S).
- b. The proper use and maintenance of personal protective equipment and life support systems.
- c. The proper use of H₂S detectors, alarms, warning systems, briefing areas, evacuation procedures, and prevailing winds.
- d. The proper techniques for first aid and rescue procedures.

In addition, supervisory personnel will be trained in the following areas:

- a. The effects of H₂S on metal components. If high tensile tubulars are to be used, personnel will be trained in their special maintenance requirements.
- b. Corrective action and shut-in procedures when drilling or reworking a well and blowout prevention and well control procedures.
- c. The contents and requirements of the H₂S Drilling Operations Plan and the Public Protection Plan.

There will be an initial training session just prior to encountering a known or probable H₂S zone (within 3 days or 500 feet) and weekly H₂S and well control drills for all personnel in each crew. The initial training session shall include a review of the site specific H₂S Drilling Operations Plan and the Public Protection Plan. This plan shall be available at the well site. All personnel will be required to carry documentation that they have received the proper training.

2. H₂S SAFETY EQUIPMENT AND SYSTEMS

Note: All H₂S safety equipment and systems will be installed, tested, and operational when drilling reaches a depth of 500 feet above, or three days prior to penetrating the first zone containing or reasonably expected to contain H₂S. If H₂S greater than 100 ppm is encountered in the gas stream we will shut in and install H₂S equipment.

- a. Well Control Equipment:
 - Flare line.
 - Choke manifold with remotely operated choke.
 - Blind rams and pipe rams to accommodate all pipe sizes with properly sized closing unit.
 - Auxiliary equipment to include: annular preventer, mud-gas separator, rotating head.

- b. Protective equipment for essential personnel:
Mark II Surviveair 30-minute units located in the dog house and at briefing areas.
- c. H2S detection and monitoring equipment:
2 - portable H2S monitor positioned on location for best coverage and response. These units have warning lights and audible sirens when H2S levels of 20 ppm are reached.
- d. Visual warning systems:
Caution/Danger signs shall be posted on roads providing direct access to location. Signs will be painted a high visibility yellow with black lettering of sufficient size to be readable at a reasonable distance from the immediate location. Bilingual signs will be used, when appropriate. See example attached.
- e. Mud Program:
The mud program has been designed to minimize the volume of H2S circulated to the surface.
- f. Metallurgy:
All drill strings, casings, tubing, wellhead, blowout preventers, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service.
- g. Communication:
Company vehicles equipped with cellular telephone.

COG OPERATING LLC has conducted a review to determine if an H2S contingency plan is required for the above referenced well. We were able to conclude that any potential hazardous volume would be minimal. H2S concentrations of wells in this area from surface to TD are low enough; therefore, we do not believe that an H2S contingency plan is necessary.

W A R N I N G

**YOU ARE ENTERING AN H₂S AREA
AUTHORIZED PERSONNEL ONLY**

- 1. BEARDS OR CONTACT LENSES NOT ALLOWED***
- 2. HARD HATS REQUIRED***
- 3. SMOKING IN DESIGNATED AREAS ONLY***
- 4. BE WIND CONSCIOUS AT ALL TIMES***
- 5. CK WITH COG OPERATING LLC FOREMAN AT MAIN OFFICE***

COG OPERATING LLC

1-575-748-6940

EMERGENCY CALL LIST

	<u>OFFICE</u>	<u>MOBILE</u>
COG OPERATING LLC OFFICE	575-748-6940	
SETH WILD	432-683-7443	432-528-3633
WALTER ROYE	575-748-6940	432-934-1886

EMERGENCY RESPONSE NUMBERS

	<u>OFFICE</u>
STATE POLICE	575-748-9718
EDDY COUNTY SHERIFF	575-746-2701
EMERGENCY MEDICAL SERVICES (AMBULANCE)	911 or 575-746-2701
EDDY COUNTY EMERGENCY MANAGEMENT (HARRY BURGESS)	575-887-9511
STATE EMERGENCY RESPONSE CENTER (SERC)	575-476-9620
CARLSBAD POLICE DEPARTMENT	575-885-2111
CARLSBAD FIRE DEPARTMENT	575-885-3125
NEW MEXICO OIL CONSERVATION DIVISION	575-748-1283
INDIAN FIRE & SAFETY	800-530-8693
HALLIBURTON SERVICES	800-844-8451

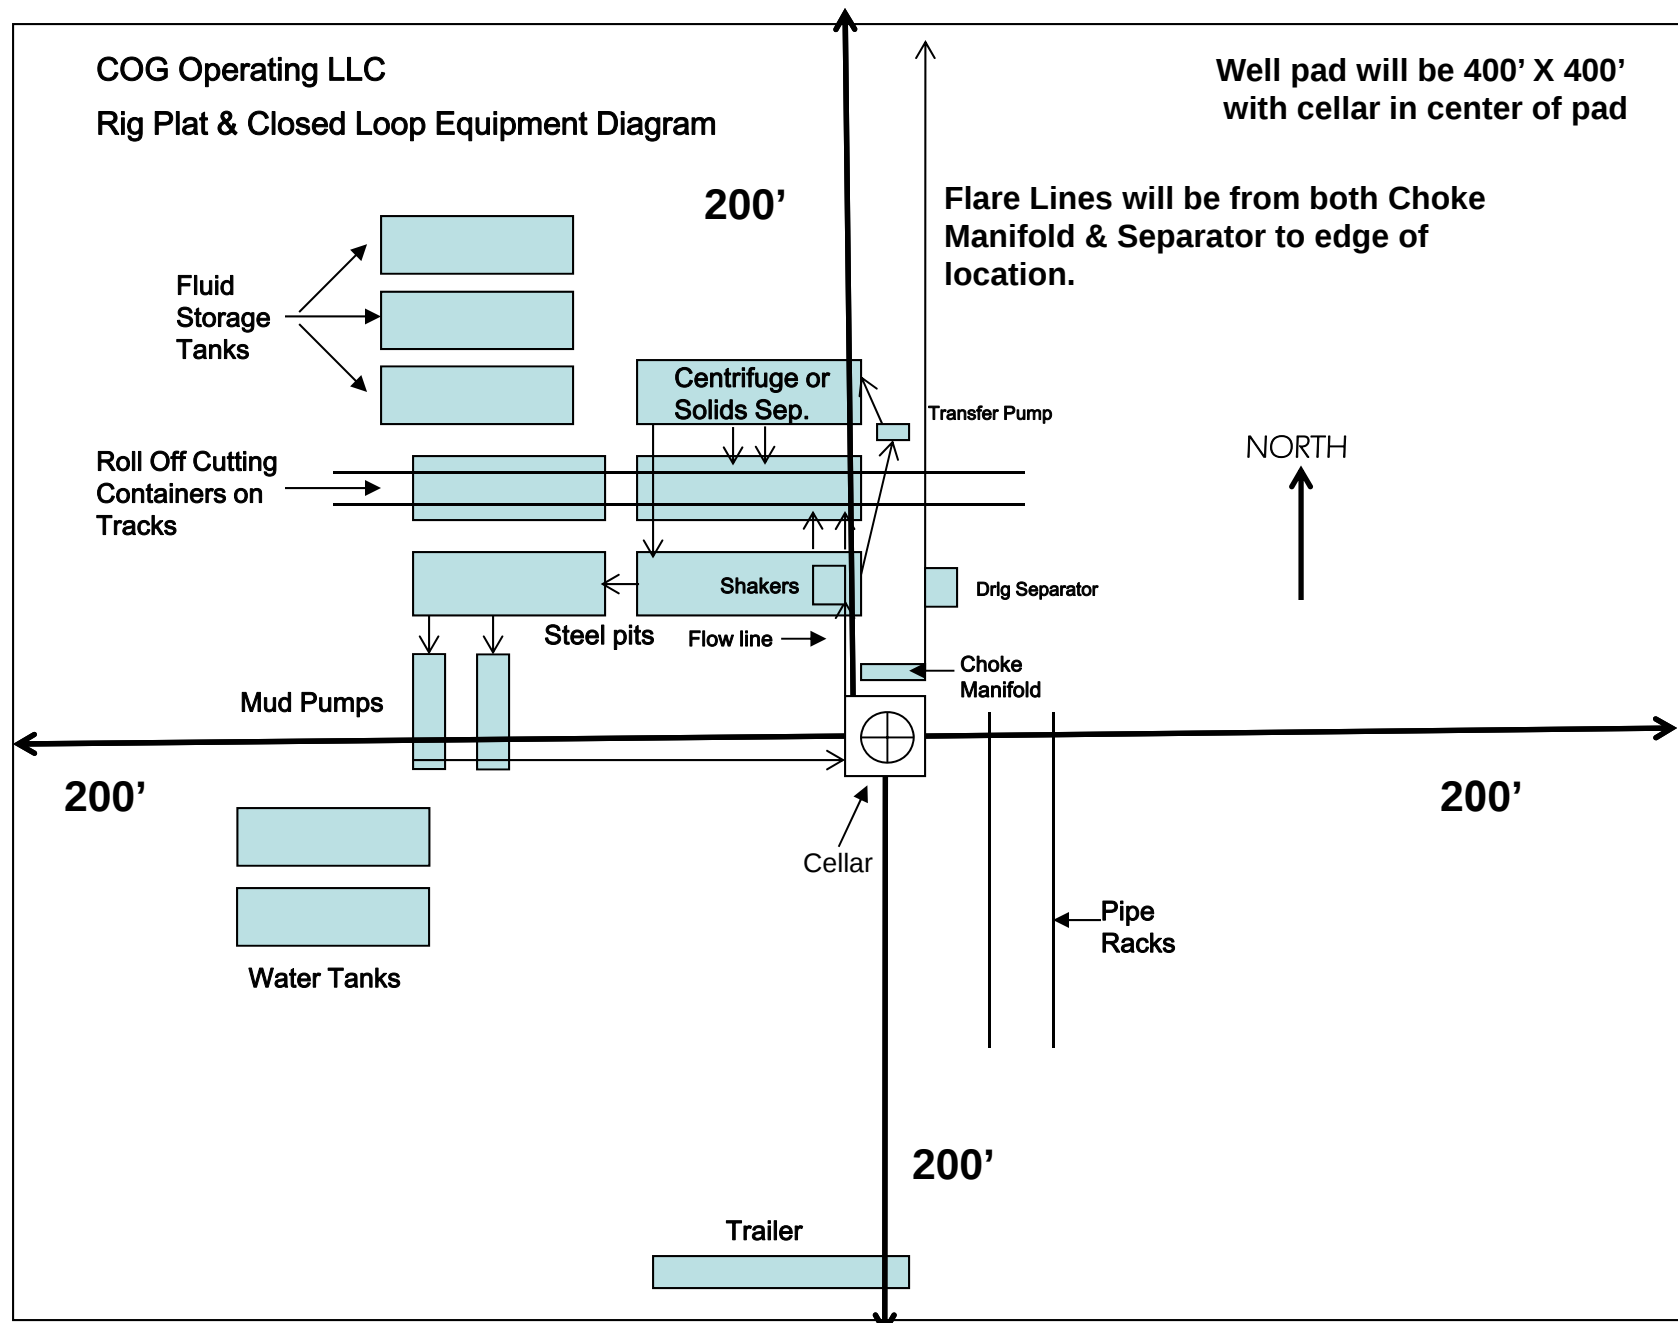


Exhibit 1

"I further certify that COG will comply with Rule 19.15.17 NMAC by using a Closed Loop System."

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 13276

CONDITIONS OF APPROVAL

Operator:	COG OPERATING LLC	600 W Illinois Ave	Midland, TX79701	OGRID:	229137	Action Number:	13276	Action Type:	FORM 3160-3
-----------	-------------------	--------------------	------------------	--------	--------	----------------	-------	--------------	-------------

OCD Reviewer	Condition
pkautz	Notify OCD 24 hours prior to casing &cement
pkautz	Will require a File As Drilled C-102 and a Directional Survey with the C-104
pkautz	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string
