

Form 3160-3
(June 2015)FORM APPROVED
OMB No. 1004-0137
Expires: January 31, 2018

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: ☐ DRILL ☐ REENTER 1b. Type of Well: ☐ Oil Well ☐ Gas Well ☐ Other 1c. Type of Completion: ☐ Hydraulic Fracturing ☐ Single Zone ☐ Multiple Zone		5. Lease Serial No. 6. If Indian, Allottee or Tribe Name 7. If Unit or CA Agreement, Name and No. 8. Lease Name and Well No. [330443]
2. Name of Operator [373910]		9. API Well No.
3a. Address	3b. Phone No. (include area code)	10. Field and Pool, or Exploratory
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area
14. Distance in miles and direction from nearest town or post office*		12. County or Parish 13. State
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)	16. No of acres in lease	17. Spacing Unit dedicated to this well
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.	19. Proposed Depth	20. BLM/BIA Bond No. in file
21. Elevations (Show whether DF, KDB, RT, GL, etc.)	22. Approximate date work will start*	23. Estimated duration
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, and the Hydraulic Fracturing rule per 43 CFR 3162.3-3 (as applicable)

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be requested by the BLM. |
|---|---|

25. Signature	Name (Printed/Typed)	Date
Title		
Approved by (Signature)	Name (Printed/Typed)	Date
Title		
Office		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

GCP Rec 04/07/2021

SL

(Continued on page 2)



Approval Date: 01/15/2021

KZ
04/09/2021

*(Instructions on page 2)

INSTRUCTIONS

GENERAL: This form is designed for submitting proposals to perform certain well operations, as indicated on Federal and Indian lands and leases for action by appropriate Federal agencies, pursuant to applicable Federal laws and regulations. Any necessary special instructions concerning the use of this form and the number of copies to be submitted, particularly with regard to local, area, or regional procedures and practices, either are shown below or will be issued by, or may be obtained from local Federal offices.

ITEM I: If the proposal is to redrill to the same reservoir at a different subsurface location or to a new reservoir, use this form with appropriate notations. Consult applicable Federal regulations concerning subsequent work proposals or reports on the well.

ITEM 4: Locations on Federal or Indian land should be described in accordance with Federal requirements. Consult local Federal offices for specific instructions.

ITEM 14: Needed only when location of well cannot readily be found by road from the land or lease description. A plat, or plats, separate or on the reverse side, showing the roads to, and the surveyed location of, the well, and any other required information, should be furnished when required by Federal agency offices.

ITEMS 15 AND 18: If well is to be, or has been directionally drilled, give distances for subsurface location of hole in any present or objective productive zone.

ITEM 22: Consult applicable Federal regulations, or appropriate officials, concerning approval of the proposal before operations are started.

ITEM 24: If the proposal will involve hydraulic fracturing operations, you must comply with 43 CFR 3162.3-3, including providing information about the protection of usable water. Operators should provide the best available information about all formations containing water and their depths. This information could include data and interpretation of resistivity logs run on nearby wells. Information may also be obtained from state or tribal regulatory agencies and from local BLM offices.

NOTICES

The Privacy Act of 1974 and regulation in 43 CFR 2.48(d) provide that you be furnished the following information in connection with information required by this application.

AUTHORITY: 30 U.S.C. 181 et seq., 25 U.S.C. 396; 43 CFR 3160

PRINCIPAL PURPOSES: The information will be used to: (1) process and evaluate your application for a permit to drill a new oil, gas, or service well or to reenter a plugged and abandoned well; and (2) document, for administrative use, information for the management, disposal and use of National Resource Lands and resources including (a) analyzing your proposal to discover and extract the Federal or Indian resources encountered; (b) reviewing procedures and equipment and the projected impact on the land involved; and (c) evaluating the effects of the proposed operation on the surface and subsurface water and other environmental impacts.

ROUTINE USE: Information from the record and/or the record will be transferred to appropriate Federal, State, and local or foreign agencies, when relevant to civil, criminal or regulatory investigations or prosecution, in connection with congressional inquiries and for regulatory responsibilities.

EFFECT OF NOT PROVIDING INFORMATION: Filing of this application and disclosure of the information is mandatory only if you elect to initiate a drilling or reentry operation on an oil and gas lease.

The Paperwork Reduction Act of 1995 requires us to inform you that:

The BLM connects this information to an evaluation of the technical, safety, and environmental factors involved with drilling for oil and/or gas on Federal and Indian oil and gas leases. This information will be used to analyze and approve applications. Response to this request is mandatory only if the operator elects to initiate drilling or reentry operations on an oil and gas lease. The BLM would like you to know that you do not have to respond to this or any other Federal agency-sponsored information collection unless it displays a currently valid OMB control number.

BURDEN HOURS STATEMENT: Public reporting burden for this form is estimated to average 8 hours per response, including the time for reviewing instructions, gathering and maintaining data, and completing and reviewing the form. Direct comments regarding the burden estimate or any other aspect of this form to U.S. Department of the Interior, Bureau of Land Management (1004-0137), Bureau Information Connection Clearance Officer (WO-630), 1849 C Street, N.W., Mail Stop 401 LS, Washington, D.C. 20240.

Additional Operator Remarks

Location of Well

0. SHL: LOT 2 / 250 FNL / 1442 FEL / TWSP: 25S / RANGE: 35E / SECTION: 1 / LAT: 32.16603 / LONG: -103.31738 (TVD: 0 feet, MD: 0 feet)

PPP: NWNE / 0 FNL / 1860 FEL / TWSP: 25S / RANGE: 35E / SECTION: 12 / LAT: 32.152174 / LONG: -103.318728 (TVD: 11732 feet, MD: 16700 feet)

PPP: LOT 2 / 611 FNL / 1859 FEL / TWSP: 25S / RANGE: 35E / SECTION: 1 / LAT: 32.16504 / LONG: -103.318728 (TVD: 11660 feet, MD: 12002 feet)

BHL: SWSE / 150 FSL / 1860 FEL / TWSP: 25S / RANGE: 35E / SECTION: 12 / LAT: 32.138077 / LONG: -103.318728 (TVD: 11811 feet, MD: 21813 feet)

BLM Point of Contact

Name: TYLER HILL

Title: LIE

Phone: (575) 234-5972

Email: tjhill@blm.gov

CONFIDENTIAL

Review and Appeal Rights

A person contesting a decision shall request a State Director review. This request must be filed within 20 working days of receipt of the Notice with the appropriate State Director (see 43 CFR 3165.3). The State Director review decision may be appealed to the Interior Board of Land Appeals, 801 North Quincy Street, Suite 300, Arlington, VA 22203 (see 43 CFR 3165.4). Contact the above listed Bureau of Land Management office for further information.

CONFIDENTIAL

District I
1625 N. French Dr., Hobbs, NM 88240
Phone: (575) 393-6161 Fax: (575) 393-0720

District II
811 S. First St., Artesia, NM 88210
Phone: (575) 748-1283 Fax: (575) 748-9720

District III
1000 Rio Brazos Road, Aztec, NM 87410
Phone: (505) 334-6178 Fax: (505) 334-6170

District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505
Phone: (505) 476-3460 Fax: (505) 476-3462

State of New Mexico
Energy, Minerals & Natural Resources Department
OIL CONSERVATION DIVISION
1220 South St. Francis Dr.
Santa Fe, NM 87505

Form C-102
Revised August 1, 2011
Submit one copy to appropriate
District Office

AMENDED REPORT

WELL LOCATION AND ACREAGE DEDICATION PLAT

¹ API Number 30-025-48621		² Pool Code 98185	³ Pool Name WC-025 G-09 S253502B;LWR BONE SPRING	
⁴ Property Code 330443	⁵ Property Name MISSION FED COM			⁶ Well Number 603H
⁷ OGRID No. 373910	⁸ Operator Name FRANKLIN MOUNTAIN ENERGY LLC			⁹ Elevation 3328.7'


¹⁰Surface Location

UL or lot no.	Section	Township	Range	Lot Idn	Feet from the	North/South line	Feet from the	East/West line	County
2	1	25S	35E		250	NORTH	1442	EAST	LEA

¹¹ Bottom Hole Location If Different From Surface

UL or lot no. O	Section 12	Township 25S	Range 35E	Lot Idn	Feet from the 150	North/South line SOUTH	Feet from the 1860	East/West line EAST	County LEA
¹² Dedicated Acres 640		¹³ Joint or Infill		¹⁴ Consolidation Code		¹⁵ Order No.			

No allowable will be assigned to this completion until all interests have been consolidated or a non-standard unit has been approved by the division.

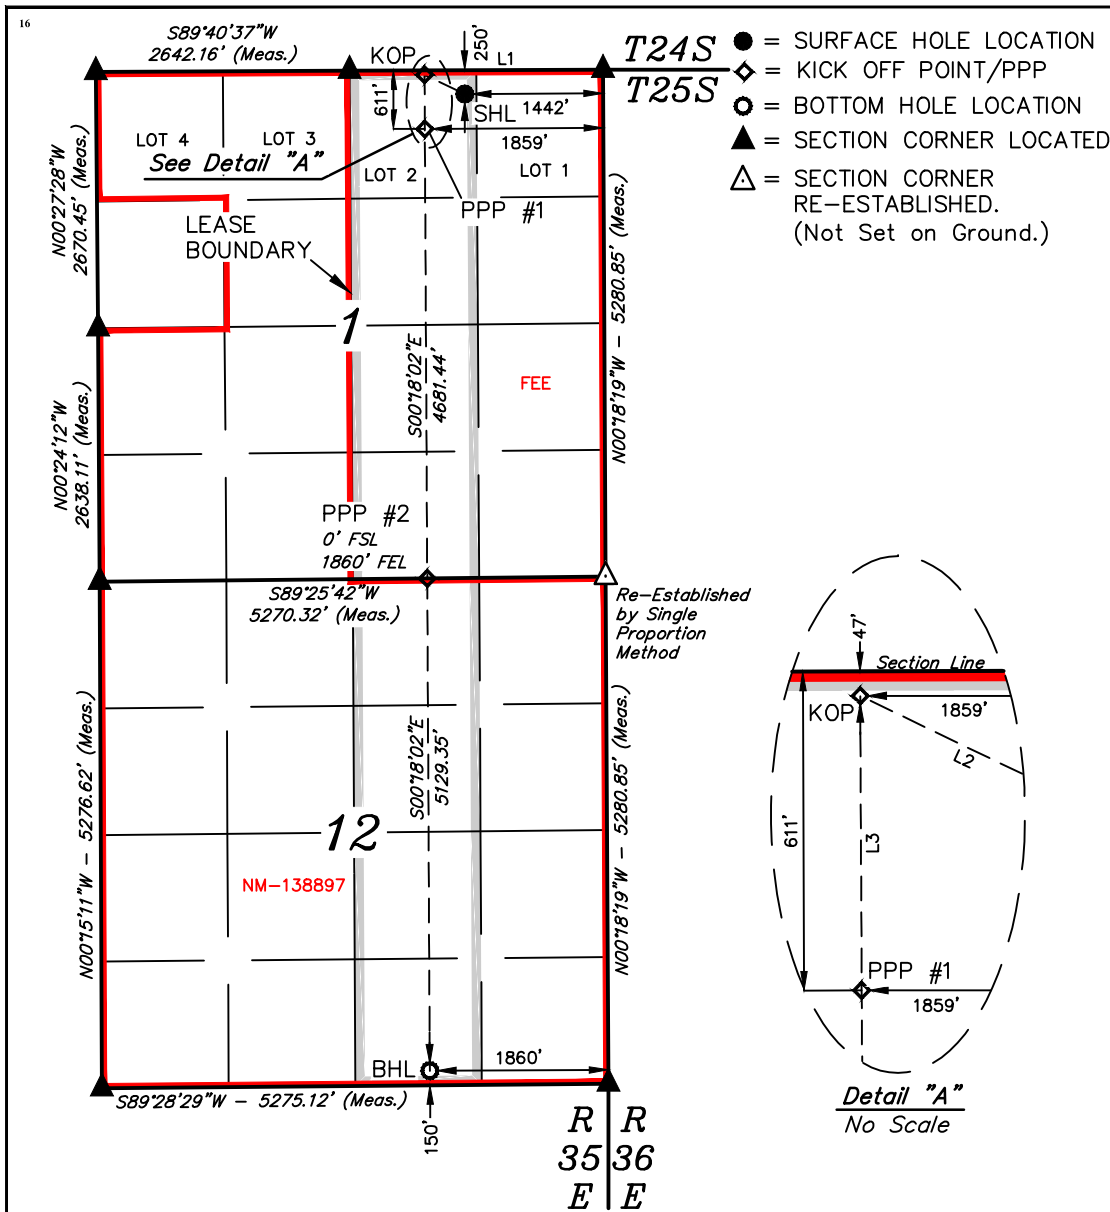

17 OPERATOR CERTIFICATION

I hereby certify that the information contained herein is true and complete to the best of my knowledge and belief, and that this organization either owns a working interest or unleased mineral interest in the land including the proposed bottom hole location or has a right to drill this well at this location pursuant to a contract with an owner of such a mineral or working interest, or to a voluntary pooling agreement or a compulsory pooling order heretofore entered by the division.

Signature 6-9-2020 Date

Shelly Albrecht
Printed Name


salbrecht@fmelc.com
E-mail Address

18 SURVEYOR CERTIFICATION

I hereby certify that the well location shown on this plat was plotted from field notes of actual surveys made by me or under my supervision, and that the same is true and correct to the best of my belief.

February 13, 2020

Date of Survey _____
Signature and Seal of Professional Surveyor: _____



Certificate Number:

LINE TABLE		
LINE	DIRECTION	LENGTH
L1	S89°46'55"W	2639.71'
L2	N64°14'40"W	464.35'
L3	S00°18'02"E	564.25'

NOTE:

- Distances referenced on plat to section lines are perpendicular.
- Basis of Bearing is a Transverse Mercator Projection with a Central Meridian of W103°53'00" (NAD 83)

NAD 83 (SURFACE HOLE LOCATION)	NAD 83 (KICK OFF POINT)
LATITUDE = 32°09'57.71" (32.166030°)	LATITUDE = 32°09'59.73" (32.166590°)
LONGITUDE = 103°19'02.57" (103.317380°)	LONGITUDE = 103°19'07.42" (103.318728°)
NAD 27 (SURFACE HOLE LOCATION)	NAD 27 (KICK OFF POINT)
LATITUDE = 32°09'57.25" (32.165903°)	LATITUDE = 32°09'59.27" (32.166464°)
LONGITUDE = 103°19'00.89" (103.316915°)	LONGITUDE = 103°19'05.75" (103.318263°)
STATE PLANE NAD 83 (N.M. EAST)	STATE PLANE NAD 83 (N.M. EAST)
N: 425620.61' E: 855709.27'	N: 425820.61' E: 855290.27'
STATE PLANE NAD 27 (N.M. EAST)	STATE PLANE NAD 27 (N.M. EAST)
N: 425561.80' E: 814522.79'	N: 425761.79' E: 814103.81'

NAD 83 (PPP #1)	NAD 83 (PPP #2)
LATITUDE = 32°09'54.14" (32.165040°)	LATITUDE = 32°09'07.83" (32.152174°)
LONGITUDE = 103°19'07.42" (103.318728°)	LONGITUDE = 103°19'07.42" (103.318728°)
NAD 27 (PPP #1)	NAD 27 (PPP #2)
LATITUDE = 32°09'53.69" (32.164913°)	LATITUDE = 32°09'07.37" (32.152047°)
LONGITUDE = 103°19'05.75" (103.318263°)	LONGITUDE = 103°19'05.75" (103.318264°)
STATE PLANE NAD 83 (N.M. EAST)	STATE PLANE NAD 83 (N.M. EAST)
N: 425256.46' E: 855295.59'	N: 420575.91' E: 855339.72'
STATE PLANE NAD 27 (N.M. EAST)	STATE PLANE NAD 27 (N.M. EAST)
N: 425197.66' E: 814109.10'	N: 420517.24' E: 814153.05'

NAD 83 (BOTTOM HOLE LOCATION)
LATITUDE = 32°08'17.08" (32.138077°)
LONGITUDE = 103°19'07.42" (103.318728°)
NAD 27 (BOTTOM HOLE LOCATION)
LATITUDE = 32°08'16.62" (32.137951°)
LONGITUDE = 103°19'05.75" (103.318264°)
STATE PLANE NAD 83 (N.M. EAST)
N: 415447.53' E: 855388.07'
STATE PLANE NAD 27 (N.M. EAST)
N: 415389.00' E: 814201.20'



District I
1625 N. French Dr., Hobbs, NM 88240
District II
811 S. First St., Artesia, NM 88210
District III
1000 Rio Brazos Road, Aztec, NM 87410
District IV
1220 S. St. Francis Dr., Santa Fe, NM 87505

State of New Mexico
Energy, Minerals and Natural Resources Department
Oil Conservation Division
1220 South St. Francis Dr.
Santa Fe, NM 87505

Submit Original
to Appropriate
District Office

GAS CAPTURE PLAN

Date: 12/2/2020

☒ Original

Operator & OGRID No.: Franklin Mountain Energy, LLC 373910

☐ Amended - Reason for Amendment: _____

This Gas Capture Plan outlines actions to be taken by the Operator to reduce well/production facility flaring/venting for new completion (new drill, recomple to new zone, re-frac) activity.

Note: Form C-129 must be submitted and approved prior to exceeding 60 days allowed by Rule (Subsection A of 19.15.18.12 NMAC).

Well(s)/Production Facility – Name of facility

The well(s) that will be located at the production facility are shown in the table below.

Well Name	API	Well Location (ULSTR)	Footages	Expected MCF/D	Flared or Vented	Comments
Mission Fed Com 603H	TBD 30-025-48621	Lot 2-1-25S-35E	250 FNL 1442 FEL	1100 +/-	Flared	New well; expect to tie-in at IP
Mission Fed Com 705H	TBD	Lot 2-1-25S-35E	250 FNL 1407 FEL	1100 +/-	Flared	New well; expect to tie-in at IP
Vested Fed Com 706H	TBD	Lot 2-1-25S-35E	250 FNL 1372 FEL	1100 +/-	Flared	New well; expect to tie-in at IP
Vested Fed Com 604H	TBD	Lot 2-1-25S-35E	250 FNL 1337 FEL	1100 +/-	Flared	New well; expect to tie-in at IP

Gathering System and Pipeline Notification

Well(s) will be connected to a production facility after flowback operations are complete, if gas transporter system is in place. The gas produced from production facility is dedicated to Lucid Energy and will be connected to Lucid Energy's gathering system located in Lea County, New Mexico. It will require 5,000' of pipeline to connect the facility to low/high pressure gathering system. Franklin Mountain Energy, LLC provides (periodically) to Lucid Energy a drilling, completion and estimated first production date for wells that are scheduled to be drilled in the foreseeable future. In addition, Franklin Mountain Energy, LLC and Lucid Energy have periodic conference calls to discuss changes to drilling and completion schedules. Gas from these wells will be processed at Lucid Energy's Red Hills Processing Plant located in Sec.13, Twn. 24S, Rng. 33E, Lea County, New Mexico. The actual flow of the gas will be based on compression operating parameters and gathering system pressures.

Flowback Strategy

After the fracture treatment/completion operations, well(s) will be produced to permanent central tank battery and gas will be sold or flared. Gas sales should start as soon as the wells start producing gas unless there are operational issues on Lucid Energy's system at that time. Based on current information, it is Franklin Mountain Energy's belief the system can take this gas upon completion of the well(s).

Safety requirements during cleanout operations from the use of underbalanced air cleanout systems may necessitate that sand and non-pipeline quality gas be vented and/or flared rather than sold on a temporary basis.

Alternatives to Reduce Flaring

Below are alternatives considered from a conceptual standpoint to reduce the amount of gas flared.

- Power Generation – On lease
 - Only a portion of gas is consumed operating the generator, remainder of gas will be flared
- Compressed Natural Gas – On lease
 - Gas flared would be minimal, but might be uneconomical to operate when gas volume declines
- NGL Removal – On lease
 - Plants are expensive, residue gas is still flared, and uneconomical to operate when gas volume declines



Mission Fed Com 603H

1. Geologic name of surface location: Permian

2. Estimated tops of important geological markers:

Formations	PROG SS	PROG TVD	Picked TVD	delta	Potential/Issues
Cenozoic Alluvium (surface)	3,329'	30'	30'	0	Sand/Gravels/unconsolidated
Rustler	2,227'	1,132'			Carbonates
Salado	2,109'	1,250'			Salt, Carbonate & Clastics
Base Salt	-42'	3,401'			Shaley Carbonate & Shale
Lamar	-1,607'	4,966'			Carbonate & Clastics
Bell Canyon	-1,665'	5,024'			Sandstone - oil/gas/water
Cherry Canyon	-2,553'	5,912'			Sandstone - oil/gas/water
Brushy Canyon	-3,974'	7,333'			Sand/carb/shales - oil/gas/water
Bone Spring Lime	-5,249'	8,608'			Shale/Carbonates - oil/gas
Avalon	-5,346'	8,705'			Shale/Carbonates - oil/gas
First Bone Spring Sand	-6,538'	9,897'			Sandstone - oil/gas/water
Second Bone Spring Carbonates	-6,668'	10,027'			Shale/Carbonates - oil/gas
Second Bone Spring Sand	-7,044'	10,403'			Sandstone - oil/gas/water
Third Bone Spring Carbonates	-7,592'	10,951'			Shale/Carbonates - oil/gas
Third Bone Spring Sand	-8,124'	11,483'			Sandstone - oil/gas/water
HZ Target at SHL	-8,296'	11,655'			Overpressure shale/sand- Oil/Gas
Wolfcamp	-8,441'	11,800'			Overpressure shale/sand- Oil/Gas
Wolfcamp A	-8,476'	11,835'			Overpressure Shale - Oil/Gas
Wolfcamp B	-8,668'	12,027'			Overpressure Shale - Oil/Gas

3. Estimated depth of anticipated fresh water, oil or gas:

Upper Permian Sands	0- 400'	Fresh Water
Delaware Sands	5,024'	Oil
Bone Spring	9,897'	Oil
Wolfcamp	11,800'	Oil

No other formations are expected to give up oil, gas or fresh water in measurable quantities. Surface freshwater sands will be protected by setting 13 3/8" casing at 1,300' and circulating cement back to surface.

4. Casing Program:

All casings strings will be run new. Safety factors calculated assuming the well is vertical.

Casing string	Weight	Grade	Burst	Collapse	Tension	Conn	Length	API design factor			
								Burst	Collapse	Tension	Coupling
Surface 13 3/8"	54.5	J-55	2730	1130	853	BTC 909	1300	1.18	1.67	4.99	5.32
Intermediate 9 5/8"	40	HCL-80	7430	4230	916	BTC 1042	5400	1.72	1.67	2.90	3.30
Intermediate 7 5/8"	29.7	HCP-110	8280	7150	827	Stinger 564	12002	1.11	1.27	1.81	1.24
Long string 5 1/2"	23	P-110	14520	14520	729	Anaconda 656	21813	1.32	1.42	1.21	1.09



Cementing Program:

Cementing Stage tool can be placed in the 1st Intermediate string as a contingency to ensure required TOC to surface.

String Type	Hole Size	Casing Size	Setting Depth	Sacks	Type of cmt	Lead Yield ft3/sk	Water gal/sk	TOC ft	Sacks	Type of cmt	Tail Yield ft3/sk	Water gal/sk	TOC	Excess
Surf	17.5	13.375	1300	795	Extenda Cem, 13.5 ppg Class C, 3lb/sk Kol-Seal	1.747	9.06	0	334	HalCem TM, 14.8 ppg, Class C, 1% CaCl ₂ , 0.125pps Celo-Flake	1.349	6.51	1000	100%
Int1	12.25	9.625	5400	1167	Neocem TM, 11.5 ppg, Class C 5% Salt, 0.125 pps Poly-E-Flake, 3lb/sk Kol-Seal	2.444	14.32	0	153	HalCem TM, 14.8 ppg, Class C, 0.1% HR 800 .125 pps Poly-E-Flake	1.334	6.42	5100	100%
Int2	8.75	7.625	12002	340	NeoCem, 11 ppg, Class C 3lb/sk Bridgemaker Gel, 5% Salt, 5pps LCM, 0.25pps Cello-Flake	2.798	17.15	4400	112	NeoCem 13.2 ppg, Class C 0.25 pps Cello-Flake, 2% CaCl ₂	1.44	7.29	11002	50%
Prod	6.75	5.5	21813	796	NeoCem, 13.5 ppg, Gas Migration Control	1.357	6.65	11002						20%

5. Minimum Specifications for Pressure Control:

The minimum blowout preventer equipment (BOPE) shown in Exhibit #1 will consist of a single ram, mud cross and double ram-type (10,000 psi WP) preventer and an annular preventer (5,000-psi WP). Both units will be hydraulically operated, and the ram-type will be equipped with blind rams on bottom and 4 ½" x 7" variable pipe rams on top. All BOPE will be tested in accordance with Onshore Oil & Gas order No. 2.

Before drilling out of the surface casing, the ram-type BOP and accessory equipment will be tested to 5,000/250 psig and the annular preventer to 5,000/250 psig. The surface casing will be tested to 1500 psi for 30 minutes.

Before drilling out of the second intermediate casing, the ram-type BOP and accessory equipment will be tested to 10,000/250 psig and the annular preventer to 5,000/250 psig. The second intermediate casing will be tested to 2000 psi for 30 minutes prior to drillout.

Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets.

A hydraulically operated choke will be installed prior to drilling out of the intermediate casing shoe.



6. Types and characteristics of the proposed mud system:

During this procedure we plan to use a Closed-Loop System and haul contents to the required disposal. The applicable depths and properties of the drilling fluid systems are as follows.

Depth	Type	Weight (ppg)	Viscosity	Water Loss
0 – 1,300'	Fresh - Gel	8.6-8.8	28-34	N/c
1,300' – 12,002'	Brine	8.8-10.2	28-34	N/c
12,002' – 21,813' Lateral	Oil Base	10.0-11.0	58-68	3 - 6

The highest mud weight needed to balance formation is expected to be 10-11 ppg. In order to maintain hole stability, mud weights up to 12 ppg may be utilized.

An electronic pit volume totalizer (PVT) will be utilized on the circulating system, to monitor pit volume, flow rate, pump pressure and stroke rate.

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept at the wellsite at all times.

7. Auxiliary well control and monitoring equipment:

(A) A kelly cock will be kept in the drill string at all times.

(B) A full opening drill pipe-stabbing valve (inside BOP) with proper drill pipe connections will be on the rig floor at all times.

(C) H₂S monitoring and detection equipment will be utilized from surface casing point to TD.

(D) A wear bushing will be installed in the wellhead prior to drilling out of the surface casing.

8. Logging, testing and coring program:

GR–CCL–CNL Will be run in cased hole during completions phase of operations.

Open-hole logs are not planned for this well.

9. Abnormal conditions, pressures, temperatures and potential hazards:

The estimated bottom-hole temperature at 11,811' TVD (deepest point of the well) is 195F with an estimated maximum bottom-hole pressure (BHP) at the same point of 7,370 psig (based on 12 ppg MW). Hydrogen sulfate may be present in the area. All necessary precautions will be taken before drilling operations commence. See Hydrogen Sulfide Plan below:

10. Hydrogen Sulfide Plan:

A. All personnel shall receive proper awareness H₂S training.

B. Briefing Area: two perpendicular areas will be designated by signs and readily accessible.

C. Required Emergency Equipment

a. Well Control Equipment

i. Flare line 150' from wellhead to be ignited by auto ignition sparking system.

ii. Choke manifold with a remotely operated hydraulic choke.

iii. Mud/gas separator

b. Protective equipment for essential personnel

i. Breathing Apparatus

1. Rescue packs (SCBA) – 1 unit shall be placed at each briefing area, 2 shall be stored in a safety trailer on site.

2. Work/Escapes packs – 4 packs shall be stored on the rig floor with sufficient air hose not to restrict work activity



3. Emergency Escape Packs – 4 packs shall be stored in the doghouse for emergency evacuation
- ii. Auxiliary Rescue Equipment
 1. Stretcher
 2. Two OSHA full body harnesses
 3. 100 feet of 5/8 inches OSHA approved rope
 4. 1-20# class ABC fire extinguisher
- c. H2S Detection and Monitoring Equipment
 - i. A stationary detector with three sensors will be placed in the doghouse if equipped, set to visually alarm at 10 ppm and audible at 14 ppm. The detector will be calibrated a minimum of every 30 days or as needed. The sensors will be placed in the following places:
 1. Rig Floor
 2. Below Rig Floor / Near BOPs
 3. End of flow line or where well bore fluid is being discharged (near shakers)
 - ii. If H2S is encountered, measured values and formations will be provided to the BLM.
- d. Visual Warning Systems
 - i. One color code condition sign will be placed at the entrance to the site reflecting the possible conditions at the site.
 - ii. A colored condition flag will be on display, reflecting the current condition at the site at the time.
 - iii. Two windsocks will be placed in strategic locations, visible from all angles.
- e. Mud Program
 - i. The Mud program will be designed to minimize the volume of H2S circulated to surface. The operator will have the necessary mud products to minimize hazards while drilling in H2S bearing zones.
- f. Metallurgy
 - i. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service at the anticipated operating pressures to prevent sour sulfide stress cracking.
- g. Communication
 - i. Communication will be via cell phones and walkie talkies on location.

Franklin Mountain Energy has conducted a review of offset operated wells to determine if an H2S contingency plan is required for the proposed well. Based on concentrations of offset wells, proximity to main roads, and distance to populated areas, the radius of exposure created by a potential release was determined to be minimal and low enough to not necessitate an H2S contingency plan. This will be reevaluated during wellbore construction if H2S is observed and after the well is on production.

11. Anticipated starting date and duration of operations:

The drilling operations on the well should be finished in approximately one month. However, in order to minimize disturbance in the area and to improve efficiency Franklin Mountain is planning to drill all the wells on the pad prior to commence completion operations. To even further reduce the time heavy machinery is used the “batch drilling” method may be used. A batch drilling sequence sundry will be submitted for BLM approval prior to spud. A drilling rig with walking/skidding capabilities will be used.

**12. Disposal/environmental concerns:**

- (A) Drilled cuttings will be hauled to and disposed of in a state-certified disposal site.
- (B) Non-hazardous waste mud/cement from the drilling process will be also be hauled to and disposed of in a state-certified disposal site.
- (C) Garbage will be hauled to the Pecos City Landfill.
- (D) Sewage (grey water) will be hauled to the Carlsbad City Landfill

13. Wellhead:

A multi-bowl wellhead system will be utilized.

After running the 13 3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum working pressure of 10,000 psi will be installed on the wellhead system and will be pressure tested to 250 psi low followed by a 5,000 psi pressure test. This pressure test will be repeated at least every 21 days, as per Onshore Order No. 2

The minimum working pressure of the BOP and related BOPE required for drilling below the surface casing shoe shall be 5,000 psi.

After running the 2nd intermediate casing, and before drilling out, the wellhead, BOP, and related equipment will be tested to 10,000/250 psig.

The multi-bowl wellhead will be installed by vendor's representative(s). A copy of the installation instructions for the Cameron Multi-Bowl WH system has been sent to the BLM office in Carlsbad.

The wellhead will be installed by a third party welder while being monitored by WH vendor's representative.

All BOP equipment will be tested utilizing a conventional test plug. Not a cup or J-packer type.

A solid steel body pack-off will be utilized after running and cementing the intermediate casing strings. After installation of the first intermediate string the pack-off and lower flanges will be pressure tested to 5000 psi. After installation of the second intermediate string, the pack-off and upper flange will be pressure tested to 10,000 psi.

Both the surface and intermediate casing strings will be tested as per Onshore Order No. 2 to at least 0.22 psi/ft or 1500 psi, whichever is greater.

14. Additional variance requests**A. Casing.**

In order to minimize potential environmental and technical hazards, this well is planned with two intermediate strings of casing.

1. Variance is requested to wave the centralizer requirements for the 7 5/8" casing due to the tight clearance with 9 5/8" string.
2. Variance is requested to wave/reduce the centralizer requirements for the 5 1/2" casing due to the tight clearance with 6 3/4" hole and 5 1/2" casing due to tight clearances.

Project: Lea County, NM (NAD83)
 Site: Mission/Vested Fed Com
 Well: Mission Fed Com 603H
 Wellbore: OH
 Design: Plan #1

3328.7' GE + 30' KB @ 3358.70usft



Azimuths to Grid North
 True North: -0.54°
 Magnetic North: 6.01°

Magnetic Field
 Strength: 47600.3nT
 Dip Angle: 59.92°
 Date: 5/11/2020
 Model: IGRF2020

PROJECT DETAILS: Lea County, NM (NAD83)

Geodetic System: US State Plane 1983
 Datum: North American Datum 1983
 Ellipsoid: GRS 1980
 Zone: New Mexico Eastern Zone






SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	Vsect	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
4200.00	0.00	0.00	4200.00	0.00	0.00	0.00	0.00	0.00	Start Build 1.50
4600.27	6.00	295.52	4599.54	9.03	-18.91	1.50	295.52	-8.42	Start 4038.07 hold at 4600.27 MD
8638.34	6.00	295.52	8615.46	190.97	-400.09	0.00	0.00	-178.25	Start Drop -1.50
9038.62	0.00	0.00	9015.00	200.00	-419.00	1.50	180.00	-186.68	Start 2073.00 hold at 9038.62 MD
11111.62	0.00	0.00	11088.00	200.00	-419.00	0.00	0.00	-186.68	Start DLS 10.00 TFO 179.46
12002.83	89.12	179.46	11660.89	-364.15	-413.68	10.00	179.46	377.02	Start 9810.52 hold at 12002.83 MD
21813.35	89.12	179.46	11811.34	-10173.08	-321.20	0.00	0.00	10178.15	TD at 21813.35

DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Latitude	Longitude
LP (Mission Fed Com 603H)	11660.89	-364.15	-413.68	32.165040	-103.318728
PBHL (Mission Fed Com 603H)	11811.34	-10173.08	-321.20	32.138077	-103.318728
SHL (Mission Fed Com 603H)	0.00	0.00	0.00	32.166030	-103.317380

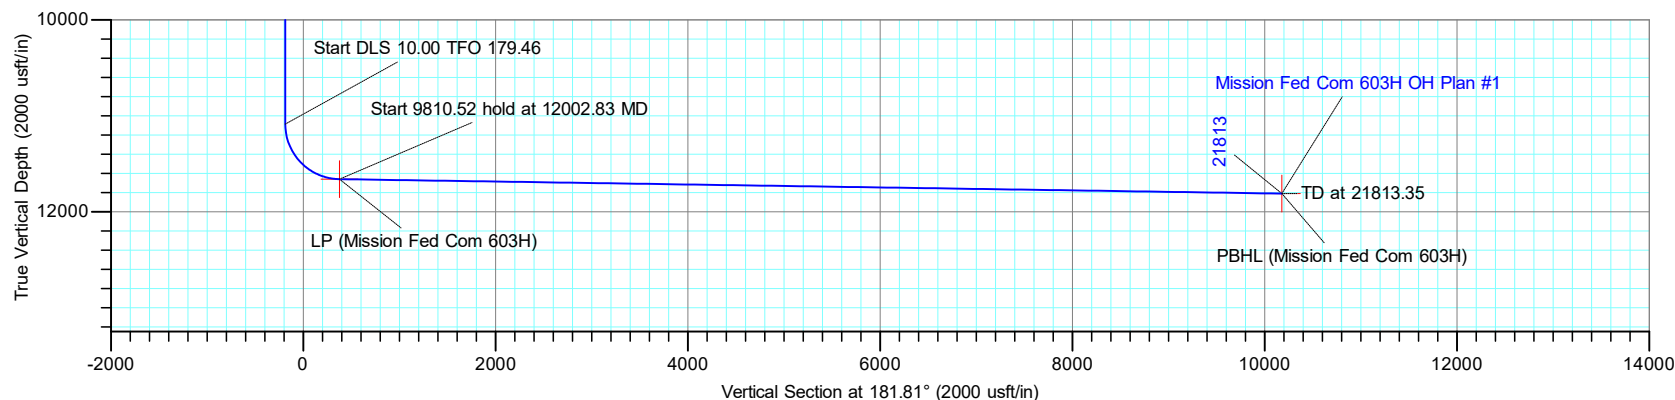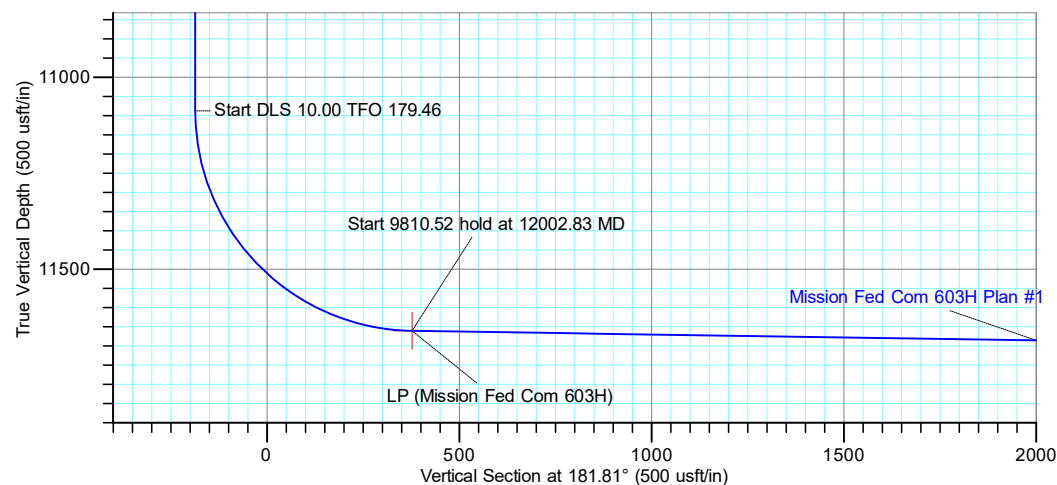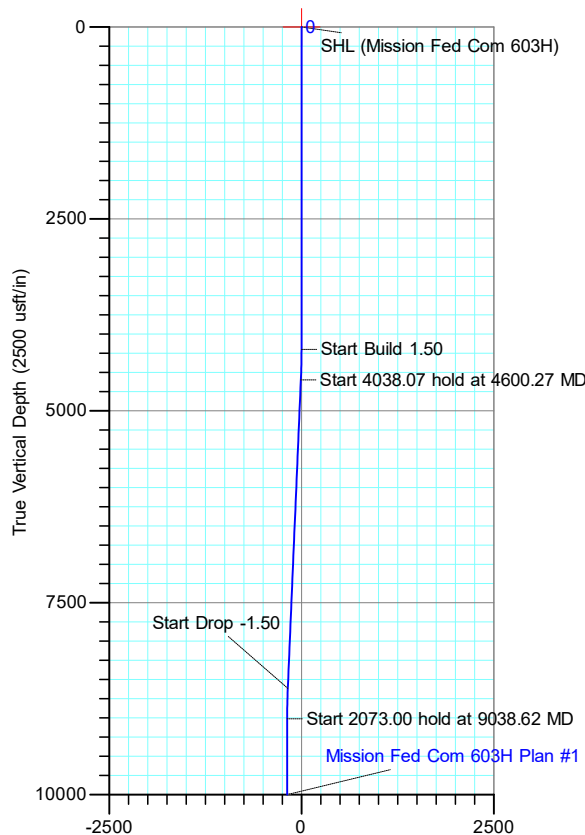

Project: Lea County, NM (NAD83)
 Site: Mission/Vested Fed Com
 Well: Mission Fed Com 603H
 Wellbore: OH
 Design: Plan #1



Azimuths to Grid North
 True North: -0.54°
 Magnetic North: 6.01°

Magnetic Field
 Strength: 47600.3nT
 Dip Angle: 59.92°
 Date: 5/11/2020
 Model: IGRF2020

PROJECT DETAILS: Lea County, NM (NAD83)
 Geodetic System: US State Plane 1983
 Datum: North American Datum 1983
 Ellipsoid: GRS 1980
 Zone: New Mexico Eastern Zone





DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
LP (Mission Fed Com 603H)	11660.89	-364.15	-413.68	425256.46	855295.59	32.165040	-103.318728
PBHL (Mission Fed Com 603H)	11811.34	-10173.08	-321.20	415447.53	855388.07	32.138077	-103.318728
SHL (Mission Fed Com 603H)	0.00	0.00	0.00	425620.61	855709.27	32.166030	-103.317380

SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSec	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
4200.00	0.00	0.00	4200.00	0.00	0.00	0.00	0.00	0.00	Start Build 1.50
4600.27	6.00	295.52	4599.54	9.03	-18.91	1.50	295.52	-8.42	Start 4038.07 hold at 4600.27 MD
8638.34	6.00	295.52	8615.46	190.97	-400.09	0.00	0.00	-178.25	Start Drop -1.50
9038.62	0.00	0.00	9015.00	200.00	-419.00	1.50	180.00	-186.68	Start 2073.00 hold at 9038.62 MD
11111.62	0.00	0.00	11088.00	200.00	-419.00	0.00	0.00	-186.68	Start DLS 10.00 TFO 179.46
12002.83	89.12	179.46	11660.89	-364.15	-413.68	10.00	179.46	377.02	Start 9810.52 hold at 12002.83 MD
21813.35	89.12	179.46	11811.34	-10173.08	-321.20	0.00	0.00	10178.15	TD at 21813.35

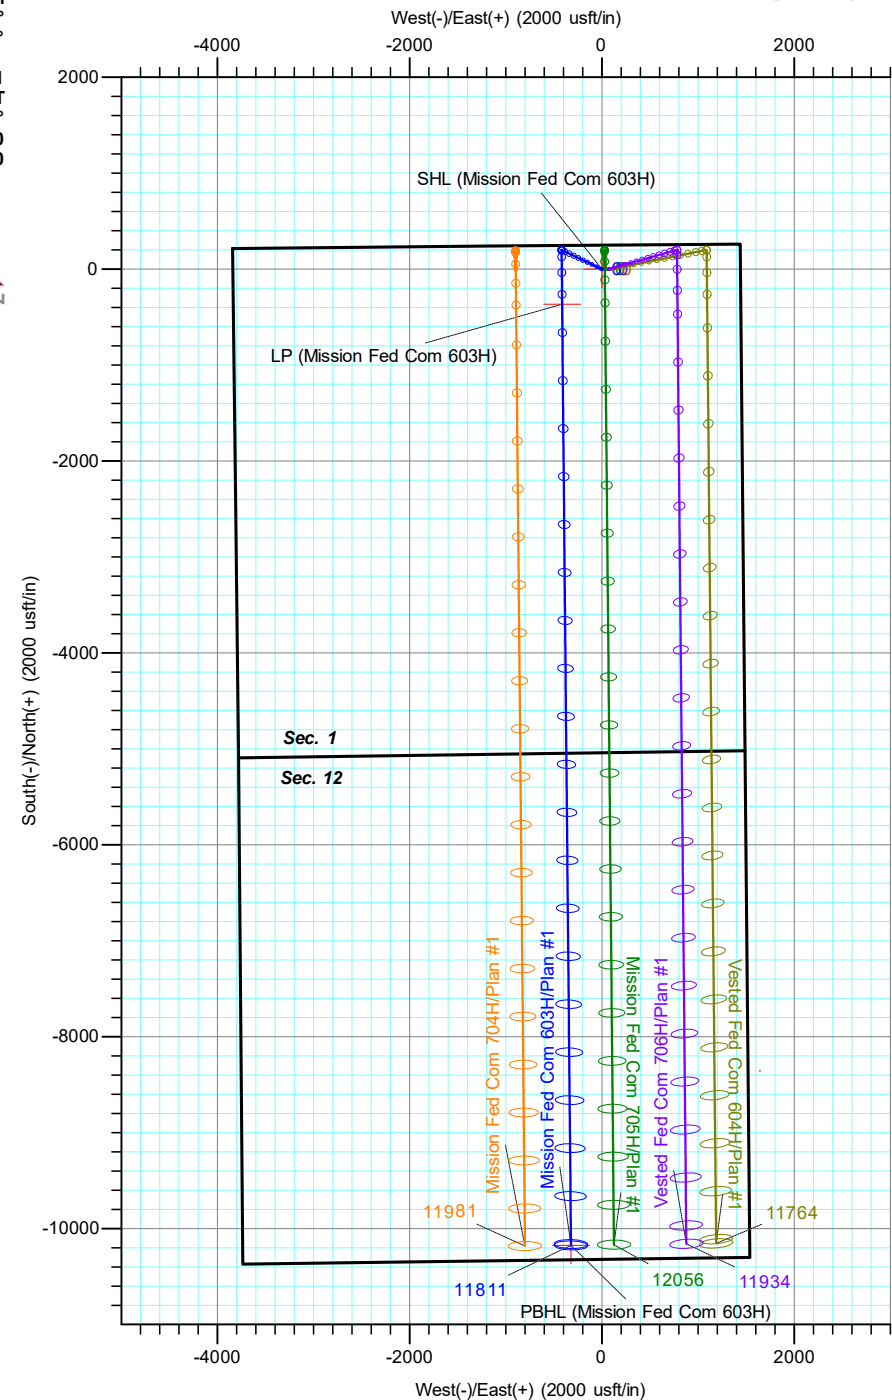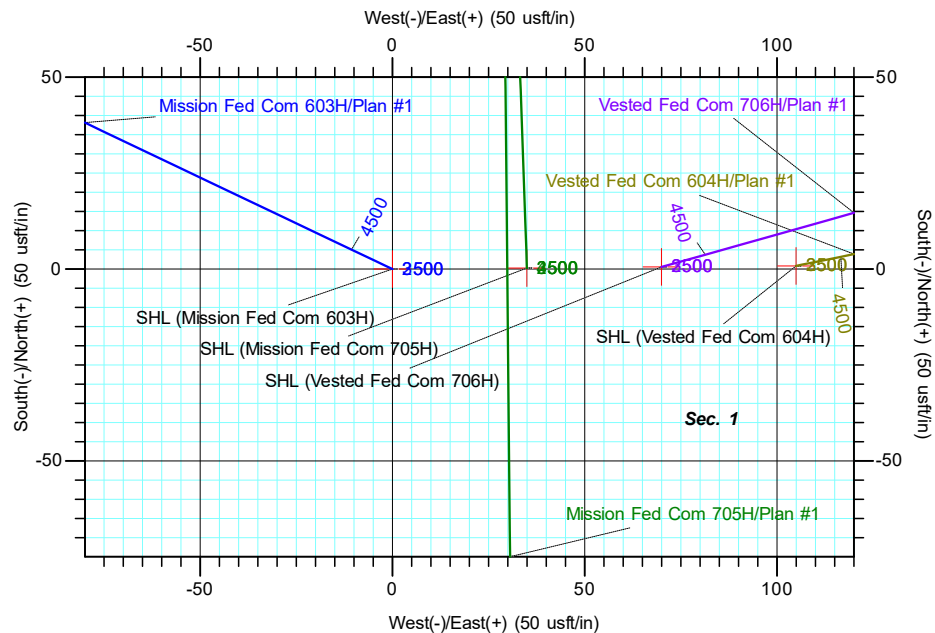



Franklin Mountain Energy

Lea County, NM (NAD83)

Mission/Vested Fed Com

Mission Fed Com 603H

OH

Plan: Plan #1

Standard Planning Report

11 May, 2020





Total Directional Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Company:	Franklin Mountain Energy	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Project:	Lea County, NM (NAD83)	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site:	Mission/Vested Fed Com	North Reference:	Grid
Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Project	Lea County, NM (NAD83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	New Mexico Eastern Zone		

Site	Mission/Vested Fed Com			
Site Position:		Northing:	425,620.61 usft	Latitude: 32.166030
From: Map		Easting:	855,709.27 usft	Longitude: -103.317380
Position Uncertainty:	0.00 usft	Slot Radius:	13-3/16 "	Grid Convergence: 0.54 °

Well	Mission Fed Com 603H			
Well Position	+N/-S	0.00 usft	Northing:	425,620.61 usft
	+E/-W	0.00 usft	Easting:	855,709.27 usft
Position Uncertainty	0.00 usft		Wellhead Elevation:	Ground Level: 3,328.70 usft

Wellbore	OH				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2020	5/11/2020	6.55	59.92	47,600.31731909

Design	Plan #1			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (usft)	+N/-S (usft)	+E/-W (usft)	Direction (°)
	0.00	0.00	0.00	181.81

Plan Survey Tool Program	Date	5/11/2020		
Depth From (usft)	Depth To (usft)	Survey (Wellbore)	Tool Name	Remarks
1	0.00	21,813.35 Plan #1 (OH)	OWSG (Rev2) MWD	
			OWSG MWD - Standard	

Plan Sections										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
4,200.00	0.00	0.00	4,200.00	0.00	0.00	0.00	0.00	0.00	0.00	
4,600.27	6.00	295.52	4,599.54	9.03	-18.91	1.50	1.50	0.00	295.52	
8,638.34	6.00	295.52	8,615.46	190.97	-400.09	0.00	0.00	0.00	0.00	
9,038.62	0.00	0.00	9,015.00	200.00	-419.00	1.50	-1.50	0.00	180.00	
11,111.62	0.00	0.00	11,088.00	200.00	-419.00	0.00	0.00	0.00	0.00	
12,002.83	89.12	179.46	11,660.89	-364.15	-413.68	10.00	10.00	20.14	179.46	
21,813.35	89.12	179.46	11,811.34	-10,173.08	-321.20	0.00	0.00	0.00	0.00	PBHL (Mission Fed C



Total Directional Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Company:	Franklin Mountain Energy	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Project:	Lea County, NM (NAD83)	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site:	Mission/Vested Fed Com	North Reference:	Grid
Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N-S (usft)	+E-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
SHL (Mission Fed Com 603H)									
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.00	0.00	1,100.00	0.00	0.00	0.00	0.00	0.00	0.00
1,200.00	0.00	0.00	1,200.00	0.00	0.00	0.00	0.00	0.00	0.00
1,300.00	0.00	0.00	1,300.00	0.00	0.00	0.00	0.00	0.00	0.00
1,400.00	0.00	0.00	1,400.00	0.00	0.00	0.00	0.00	0.00	0.00
1,500.00	0.00	0.00	1,500.00	0.00	0.00	0.00	0.00	0.00	0.00
1,600.00	0.00	0.00	1,600.00	0.00	0.00	0.00	0.00	0.00	0.00
1,700.00	0.00	0.00	1,700.00	0.00	0.00	0.00	0.00	0.00	0.00
1,800.00	0.00	0.00	1,800.00	0.00	0.00	0.00	0.00	0.00	0.00
1,900.00	0.00	0.00	1,900.00	0.00	0.00	0.00	0.00	0.00	0.00
2,000.00	0.00	0.00	2,000.00	0.00	0.00	0.00	0.00	0.00	0.00
2,100.00	0.00	0.00	2,100.00	0.00	0.00	0.00	0.00	0.00	0.00
2,200.00	0.00	0.00	2,200.00	0.00	0.00	0.00	0.00	0.00	0.00
2,300.00	0.00	0.00	2,300.00	0.00	0.00	0.00	0.00	0.00	0.00
2,400.00	0.00	0.00	2,400.00	0.00	0.00	0.00	0.00	0.00	0.00
2,500.00	0.00	0.00	2,500.00	0.00	0.00	0.00	0.00	0.00	0.00
2,600.00	0.00	0.00	2,600.00	0.00	0.00	0.00	0.00	0.00	0.00
2,700.00	0.00	0.00	2,700.00	0.00	0.00	0.00	0.00	0.00	0.00
2,800.00	0.00	0.00	2,800.00	0.00	0.00	0.00	0.00	0.00	0.00
2,900.00	0.00	0.00	2,900.00	0.00	0.00	0.00	0.00	0.00	0.00
3,000.00	0.00	0.00	3,000.00	0.00	0.00	0.00	0.00	0.00	0.00
3,100.00	0.00	0.00	3,100.00	0.00	0.00	0.00	0.00	0.00	0.00
3,200.00	0.00	0.00	3,200.00	0.00	0.00	0.00	0.00	0.00	0.00
3,300.00	0.00	0.00	3,300.00	0.00	0.00	0.00	0.00	0.00	0.00
3,400.00	0.00	0.00	3,400.00	0.00	0.00	0.00	0.00	0.00	0.00
3,500.00	0.00	0.00	3,500.00	0.00	0.00	0.00	0.00	0.00	0.00
3,600.00	0.00	0.00	3,600.00	0.00	0.00	0.00	0.00	0.00	0.00
3,700.00	0.00	0.00	3,700.00	0.00	0.00	0.00	0.00	0.00	0.00
3,800.00	0.00	0.00	3,800.00	0.00	0.00	0.00	0.00	0.00	0.00
3,900.00	0.00	0.00	3,900.00	0.00	0.00	0.00	0.00	0.00	0.00
4,000.00	0.00	0.00	4,000.00	0.00	0.00	0.00	0.00	0.00	0.00
4,100.00	0.00	0.00	4,100.00	0.00	0.00	0.00	0.00	0.00	0.00
4,200.00	0.00	0.00	4,200.00	0.00	0.00	0.00	0.00	0.00	0.00
Start Build 1.50									
4,300.00	1.50	295.52	4,299.99	0.56	-1.18	-0.53	1.50	1.50	0.00
4,400.00	3.00	295.52	4,399.91	2.25	-4.72	-2.10	1.50	1.50	0.00
4,500.00	4.50	295.52	4,499.69	5.07	-10.63	-4.73	1.50	1.50	0.00
4,600.27	6.00	295.52	4,599.54	9.03	-18.91	-8.42	1.50	1.50	0.00
Start 4038.07 hold at 4600.27 MD									
4,700.00	6.00	295.52	4,698.72	13.52	-28.32	-12.62	0.00	0.00	0.00
4,800.00	6.00	295.52	4,798.17	18.03	-37.76	-16.82	0.00	0.00	0.00
4,900.00	6.00	295.52	4,897.62	22.53	-47.20	-21.03	0.00	0.00	0.00



Total Directional Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Company:	Franklin Mountain Energy	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Project:	Lea County, NM (NAD83)	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site:	Mission/Vested Fed Com	North Reference:	Grid
Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
5,000.00	6.00	295.52	4,997.08	27.04	-56.64	-25.24	0.00	0.00	0.00	
5,100.00	6.00	295.52	5,096.53	31.54	-66.08	-29.44	0.00	0.00	0.00	
5,200.00	6.00	295.52	5,195.98	36.05	-75.52	-33.65	0.00	0.00	0.00	
5,300.00	6.00	295.52	5,295.43	40.55	-84.96	-37.85	0.00	0.00	0.00	
5,400.00	6.00	295.52	5,394.88	45.06	-94.40	-42.06	0.00	0.00	0.00	
5,500.00	6.00	295.52	5,494.33	49.57	-103.84	-46.26	0.00	0.00	0.00	
5,600.00	6.00	295.52	5,593.78	54.07	-113.28	-50.47	0.00	0.00	0.00	
5,700.00	6.00	295.52	5,693.24	58.58	-122.72	-54.68	0.00	0.00	0.00	
5,800.00	6.00	295.52	5,792.69	63.08	-132.16	-58.88	0.00	0.00	0.00	
5,900.00	6.00	295.52	5,892.14	67.59	-141.60	-63.09	0.00	0.00	0.00	
6,000.00	6.00	295.52	5,991.59	72.10	-151.04	-67.29	0.00	0.00	0.00	
6,100.00	6.00	295.52	6,091.04	76.60	-160.48	-71.50	0.00	0.00	0.00	
6,200.00	6.00	295.52	6,190.49	81.11	-169.92	-75.70	0.00	0.00	0.00	
6,300.00	6.00	295.52	6,289.94	85.61	-179.36	-79.91	0.00	0.00	0.00	
6,400.00	6.00	295.52	6,389.40	90.12	-188.80	-84.12	0.00	0.00	0.00	
6,500.00	6.00	295.52	6,488.85	94.62	-198.24	-88.32	0.00	0.00	0.00	
6,600.00	6.00	295.52	6,588.30	99.13	-207.68	-92.53	0.00	0.00	0.00	
6,700.00	6.00	295.52	6,687.75	103.64	-217.12	-96.73	0.00	0.00	0.00	
6,800.00	6.00	295.52	6,787.20	108.14	-226.56	-100.94	0.00	0.00	0.00	
6,900.00	6.00	295.52	6,886.65	112.65	-236.00	-105.14	0.00	0.00	0.00	
7,000.00	6.00	295.52	6,986.10	117.15	-245.44	-109.35	0.00	0.00	0.00	
7,100.00	6.00	295.52	7,085.56	121.66	-254.88	-113.56	0.00	0.00	0.00	
7,200.00	6.00	295.52	7,185.01	126.16	-264.32	-117.76	0.00	0.00	0.00	
7,300.00	6.00	295.52	7,284.46	130.67	-273.76	-121.97	0.00	0.00	0.00	
7,400.00	6.00	295.52	7,383.91	135.18	-283.19	-126.17	0.00	0.00	0.00	
7,500.00	6.00	295.52	7,483.36	139.68	-292.63	-130.38	0.00	0.00	0.00	
7,600.00	6.00	295.52	7,582.81	144.19	-302.07	-134.58	0.00	0.00	0.00	
7,700.00	6.00	295.52	7,682.26	148.69	-311.51	-138.79	0.00	0.00	0.00	
7,800.00	6.00	295.52	7,781.72	153.20	-320.95	-142.99	0.00	0.00	0.00	
7,900.00	6.00	295.52	7,881.17	157.71	-330.39	-147.20	0.00	0.00	0.00	
8,000.00	6.00	295.52	7,980.62	162.21	-339.83	-151.41	0.00	0.00	0.00	
8,100.00	6.00	295.52	8,080.07	166.72	-349.27	-155.61	0.00	0.00	0.00	
8,200.00	6.00	295.52	8,179.52	171.22	-358.71	-159.82	0.00	0.00	0.00	
8,300.00	6.00	295.52	8,278.97	175.73	-368.15	-164.02	0.00	0.00	0.00	
8,400.00	6.00	295.52	8,378.42	180.23	-377.59	-168.23	0.00	0.00	0.00	
8,500.00	6.00	295.52	8,477.88	184.74	-387.03	-172.43	0.00	0.00	0.00	
8,600.00	6.00	295.52	8,577.33	189.25	-396.47	-176.64	0.00	0.00	0.00	
8,638.34	6.00	295.52	8,615.46	190.97	-400.09	-178.25	0.00	0.00	0.00	
Start Drop -1.50										
8,700.00	5.08	295.52	8,676.83	193.54	-405.46	-180.65	1.50	-1.50	0.00	
8,800.00	3.58	295.52	8,776.54	196.79	-412.28	-183.68	1.50	-1.50	0.00	
8,900.00	2.08	295.52	8,876.42	198.92	-416.73	-185.67	1.50	-1.50	0.00	
9,000.00	0.58	295.52	8,976.39	199.92	-418.82	-186.60	1.50	-1.50	0.00	
9,038.62	0.00	0.00	9,015.00	200.00	-419.00	-186.68	1.50	-1.50	166.99	
Start 2073.00 hold at 9038.62 MD										
9,100.00	0.00	0.00	9,076.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,200.00	0.00	0.00	9,176.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,300.00	0.00	0.00	9,276.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,400.00	0.00	0.00	9,376.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,500.00	0.00	0.00	9,476.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,600.00	0.00	0.00	9,576.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,700.00	0.00	0.00	9,676.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,800.00	0.00	0.00	9,776.38	200.00	-419.00	-186.68	0.00	0.00	0.00	
9,900.00	0.00	0.00	9,876.38	200.00	-419.00	-186.68	0.00	0.00	0.00	



Total Directional Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Company:	Franklin Mountain Energy	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Project:	Lea County, NM (NAD83)	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site:	Mission/Vested Fed Com	North Reference:	Grid
Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
10,000.00	0.00	0.00	9,976.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,100.00	0.00	0.00	10,076.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,200.00	0.00	0.00	10,176.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,300.00	0.00	0.00	10,276.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,400.00	0.00	0.00	10,376.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,500.00	0.00	0.00	10,476.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,600.00	0.00	0.00	10,576.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,700.00	0.00	0.00	10,676.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,800.00	0.00	0.00	10,776.38	200.00	-419.00	-186.68	0.00	0.00	0.00
10,900.00	0.00	0.00	10,876.38	200.00	-419.00	-186.68	0.00	0.00	0.00
11,000.00	0.00	0.00	10,976.38	200.00	-419.00	-186.68	0.00	0.00	0.00
11,100.00	0.00	0.00	11,076.38	200.00	-419.00	-186.68	0.00	0.00	0.00
11,111.62	0.00	0.00	11,088.00	200.00	-419.00	-186.68	0.00	0.00	0.00
Start DLS 10.00 TFO 179.46									
11,150.00	3.84	179.46	11,126.36	198.71	-418.99	-185.39	10.00	10.00	0.00
11,200.00	8.84	179.46	11,176.03	193.20	-418.94	-179.88	10.00	10.00	0.00
11,250.00	13.84	179.46	11,225.04	183.37	-418.84	-170.06	10.00	10.00	0.00
11,300.00	18.84	179.46	11,273.01	169.31	-418.71	-156.01	10.00	10.00	0.00
11,350.00	23.84	179.46	11,319.57	151.12	-418.54	-137.84	10.00	10.00	0.00
11,400.00	28.84	179.46	11,364.36	128.95	-418.33	-115.68	10.00	10.00	0.00
11,450.00	33.84	179.46	11,407.05	102.95	-418.09	-89.71	10.00	10.00	0.00
11,500.00	38.84	179.46	11,447.32	73.33	-417.81	-60.11	10.00	10.00	0.00
11,550.00	43.84	179.46	11,484.85	40.32	-417.49	-27.13	10.00	10.00	0.00
11,600.00	48.84	179.46	11,519.36	4.16	-417.15	9.00	10.00	10.00	0.00
11,650.00	53.84	179.46	11,550.58	-34.87	-416.79	48.00	10.00	10.00	0.00
11,700.00	58.84	179.46	11,578.29	-76.47	-416.39	89.57	10.00	10.00	0.00
11,750.00	63.84	179.46	11,602.26	-120.32	-415.98	133.39	10.00	10.00	0.00
11,800.00	68.84	179.46	11,622.32	-166.10	-415.55	179.14	10.00	10.00	0.00
11,850.00	73.84	179.46	11,638.32	-213.46	-415.10	226.45	10.00	10.00	0.00
11,900.00	78.84	179.46	11,650.12	-262.03	-414.64	274.98	10.00	10.00	0.00
11,950.00	83.84	179.46	11,657.65	-311.44	-414.18	324.35	10.00	10.00	0.00
12,002.83	89.12	179.46	11,660.89	-364.15	-413.68	377.02	10.00	10.00	0.00
Start 9810.52 hold at 12002.83 MD - LP (Mission Fed Com 603H)									
12,100.00	89.12	179.46	11,662.38	-461.30	-412.77	474.10	0.00	0.00	0.00
12,200.00	89.12	179.46	11,663.91	-561.29	-411.82	574.00	0.00	0.00	0.00
12,300.00	89.12	179.46	11,665.45	-661.27	-410.88	673.91	0.00	0.00	0.00
12,400.00	89.12	179.46	11,666.98	-761.25	-409.94	773.81	0.00	0.00	0.00
12,500.00	89.12	179.46	11,668.52	-861.24	-408.99	873.72	0.00	0.00	0.00
12,600.00	89.12	179.46	11,670.05	-961.22	-408.05	973.62	0.00	0.00	0.00
12,700.00	89.12	179.46	11,671.58	-1,061.20	-407.11	1,073.52	0.00	0.00	0.00
12,800.00	89.12	179.46	11,673.12	-1,161.19	-406.17	1,173.43	0.00	0.00	0.00
12,900.00	89.12	179.46	11,674.65	-1,261.17	-405.22	1,273.33	0.00	0.00	0.00
13,000.00	89.12	179.46	11,676.18	-1,361.16	-404.28	1,373.24	0.00	0.00	0.00
13,100.00	89.12	179.46	11,677.72	-1,461.14	-403.34	1,473.14	0.00	0.00	0.00
13,200.00	89.12	179.46	11,679.25	-1,561.12	-402.40	1,573.04	0.00	0.00	0.00
13,300.00	89.12	179.46	11,680.78	-1,661.11	-401.45	1,672.95	0.00	0.00	0.00
13,400.00	89.12	179.46	11,682.32	-1,761.09	-400.51	1,772.85	0.00	0.00	0.00
13,500.00	89.12	179.46	11,683.85	-1,861.08	-399.57	1,872.76	0.00	0.00	0.00
13,600.00	89.12	179.46	11,685.38	-1,961.06	-398.63	1,972.66	0.00	0.00	0.00
13,700.00	89.12	179.46	11,686.92	-2,061.04	-397.68	2,072.57	0.00	0.00	0.00
13,800.00	89.12	179.46	11,688.45	-2,161.03	-396.74	2,172.47	0.00	0.00	0.00
13,900.00	89.12	179.46	11,689.98	-2,261.01	-395.80	2,272.37	0.00	0.00	0.00
14,000.00	89.12	179.46	11,691.52	-2,360.99	-394.85	2,372.28	0.00	0.00	0.00
14,100.00	89.12	179.46	11,693.05	-2,460.98	-393.91	2,472.18	0.00	0.00	0.00



Total Directional Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Company:	Franklin Mountain Energy	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Project:	Lea County, NM (NAD83)	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site:	Mission/Vested Fed Com	North Reference:	Grid
Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey									
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
14,200.00	89.12	179.46	11,694.59	-2,560.96	-392.97	2,572.09	0.00	0.00	0.00
14,300.00	89.12	179.46	11,696.12	-2,660.95	-392.03	2,671.99	0.00	0.00	0.00
14,400.00	89.12	179.46	11,697.65	-2,760.93	-391.08	2,771.90	0.00	0.00	0.00
14,500.00	89.12	179.46	11,699.19	-2,860.91	-390.14	2,871.80	0.00	0.00	0.00
14,600.00	89.12	179.46	11,700.72	-2,960.90	-389.20	2,971.70	0.00	0.00	0.00
14,700.00	89.12	179.46	11,702.25	-3,060.88	-388.26	3,071.61	0.00	0.00	0.00
14,800.00	89.12	179.46	11,703.79	-3,160.86	-387.31	3,171.51	0.00	0.00	0.00
14,900.00	89.12	179.46	11,705.32	-3,260.85	-386.37	3,271.42	0.00	0.00	0.00
15,000.00	89.12	179.46	11,706.85	-3,360.83	-385.43	3,371.32	0.00	0.00	0.00
15,100.00	89.12	179.46	11,708.39	-3,460.82	-384.48	3,471.23	0.00	0.00	0.00
15,200.00	89.12	179.46	11,709.92	-3,560.80	-383.54	3,571.13	0.00	0.00	0.00
15,300.00	89.12	179.46	11,711.45	-3,660.78	-382.60	3,671.03	0.00	0.00	0.00
15,400.00	89.12	179.46	11,712.99	-3,760.77	-381.66	3,770.94	0.00	0.00	0.00
15,500.00	89.12	179.46	11,714.52	-3,860.75	-380.71	3,870.84	0.00	0.00	0.00
15,600.00	89.12	179.46	11,716.06	-3,960.73	-379.77	3,970.75	0.00	0.00	0.00
15,700.00	89.12	179.46	11,717.59	-4,060.72	-378.83	4,070.65	0.00	0.00	0.00
15,800.00	89.12	179.46	11,719.12	-4,160.70	-377.89	4,170.56	0.00	0.00	0.00
15,900.00	89.12	179.46	11,720.66	-4,260.69	-376.94	4,270.46	0.00	0.00	0.00
16,000.00	89.12	179.46	11,722.19	-4,360.67	-376.00	4,370.36	0.00	0.00	0.00
16,100.00	89.12	179.46	11,723.72	-4,460.65	-375.06	4,470.27	0.00	0.00	0.00
16,200.00	89.12	179.46	11,725.26	-4,560.64	-374.12	4,570.17	0.00	0.00	0.00
16,300.00	89.12	179.46	11,726.79	-4,660.62	-373.17	4,670.08	0.00	0.00	0.00
16,400.00	89.12	179.46	11,728.32	-4,760.61	-372.23	4,769.98	0.00	0.00	0.00
16,500.00	89.12	179.46	11,729.86	-4,860.59	-371.29	4,869.89	0.00	0.00	0.00
16,600.00	89.12	179.46	11,731.39	-4,960.57	-370.34	4,969.79	0.00	0.00	0.00
16,700.00	89.12	179.46	11,732.92	-5,060.56	-369.40	5,069.69	0.00	0.00	0.00
16,800.00	89.12	179.46	11,734.46	-5,160.54	-368.46	5,169.60	0.00	0.00	0.00
16,900.00	89.12	179.46	11,735.99	-5,260.52	-367.52	5,269.50	0.00	0.00	0.00
17,000.00	89.12	179.46	11,737.52	-5,360.51	-366.57	5,369.41	0.00	0.00	0.00
17,100.00	89.12	179.46	11,739.06	-5,460.49	-365.63	5,469.31	0.00	0.00	0.00
17,200.00	89.12	179.46	11,740.59	-5,560.48	-364.69	5,569.21	0.00	0.00	0.00
17,300.00	89.12	179.46	11,742.13	-5,660.46	-363.75	5,669.12	0.00	0.00	0.00
17,400.00	89.12	179.46	11,743.66	-5,760.44	-362.80	5,769.02	0.00	0.00	0.00
17,500.00	89.12	179.46	11,745.19	-5,860.43	-361.86	5,868.93	0.00	0.00	0.00
17,600.00	89.12	179.46	11,746.73	-5,960.41	-360.92	5,968.83	0.00	0.00	0.00
17,700.00	89.12	179.46	11,748.26	-6,060.39	-359.98	6,068.74	0.00	0.00	0.00
17,800.00	89.12	179.46	11,749.79	-6,160.38	-359.03	6,168.64	0.00	0.00	0.00
17,900.00	89.12	179.46	11,751.33	-6,260.36	-358.09	6,268.54	0.00	0.00	0.00
18,000.00	89.12	179.46	11,752.86	-6,360.35	-357.15	6,368.45	0.00	0.00	0.00
18,100.00	89.12	179.46	11,754.39	-6,460.33	-356.20	6,468.35	0.00	0.00	0.00
18,200.00	89.12	179.46	11,755.93	-6,560.31	-355.26	6,568.26	0.00	0.00	0.00
18,300.00	89.12	179.46	11,757.46	-6,660.30	-354.32	6,668.16	0.00	0.00	0.00
18,400.00	89.12	179.46	11,758.99	-6,760.28	-353.38	6,768.07	0.00	0.00	0.00
18,500.00	89.12	179.46	11,760.53	-6,860.27	-352.43	6,867.97	0.00	0.00	0.00
18,600.00	89.12	179.46	11,762.06	-6,960.25	-351.49	6,967.87	0.00	0.00	0.00
18,700.00	89.12	179.46	11,763.60	-7,060.23	-350.55	7,067.78	0.00	0.00	0.00
18,800.00	89.12	179.46	11,765.13	-7,160.22	-349.61	7,167.68	0.00	0.00	0.00
18,900.00	89.12	179.46	11,766.66	-7,260.20	-348.66	7,267.59	0.00	0.00	0.00
19,000.00	89.12	179.46	11,768.20	-7,360.18	-347.72	7,367.49	0.00	0.00	0.00
19,100.00	89.12	179.46	11,769.73	-7,460.17	-346.78	7,467.40	0.00	0.00	0.00
19,200.00	89.12	179.46	11,771.26	-7,560.15	-345.84	7,567.30	0.00	0.00	0.00
19,300.00	89.12	179.46	11,772.80	-7,660.14	-344.89	7,667.20	0.00	0.00	0.00
19,400.00	89.12	179.46	11,774.33	-7,760.12	-343.95	7,767.11	0.00	0.00	0.00
19,500.00	89.12	179.46	11,775.86	-7,860.10	-343.01	7,867.01	0.00	0.00	0.00



Total Directional Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Company:	Franklin Mountain Energy	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Project:	Lea County, NM (NAD83)	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site:	Mission/Vested Fed Com	North Reference:	Grid
Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Planned Survey										
Measured Depth (usft)	Inclination (°)	Azimuth (°)	Vertical Depth (usft)	+N/-S (usft)	+E/-W (usft)	Vertical Section (usft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
19,600.00	89.12	179.46	11,777.40	-7,960.09	-342.06	7,966.92	0.00	0.00	0.00	
19,700.00	89.12	179.46	11,778.93	-8,060.07	-341.12	8,066.82	0.00	0.00	0.00	
19,800.00	89.12	179.46	11,780.46	-8,160.05	-340.18	8,166.73	0.00	0.00	0.00	
19,900.00	89.12	179.46	11,782.00	-8,260.04	-339.24	8,266.63	0.00	0.00	0.00	
20,000.00	89.12	179.46	11,783.53	-8,360.02	-338.29	8,366.53	0.00	0.00	0.00	
20,100.00	89.12	179.46	11,785.07	-8,460.01	-337.35	8,466.44	0.00	0.00	0.00	
20,200.00	89.12	179.46	11,786.60	-8,559.99	-336.41	8,566.34	0.00	0.00	0.00	
20,300.00	89.12	179.46	11,788.13	-8,659.97	-335.47	8,666.25	0.00	0.00	0.00	
20,400.00	89.12	179.46	11,789.67	-8,759.96	-334.52	8,766.15	0.00	0.00	0.00	
20,500.00	89.12	179.46	11,791.20	-8,859.94	-333.58	8,866.06	0.00	0.00	0.00	
20,600.00	89.12	179.46	11,792.73	-8,959.92	-332.64	8,965.96	0.00	0.00	0.00	
20,700.00	89.12	179.46	11,794.27	-9,059.91	-331.70	9,065.86	0.00	0.00	0.00	
20,800.00	89.12	179.46	11,795.80	-9,159.89	-330.75	9,165.77	0.00	0.00	0.00	
20,900.00	89.12	179.46	11,797.33	-9,259.88	-329.81	9,265.67	0.00	0.00	0.00	
21,000.00	89.12	179.46	11,798.87	-9,359.86	-328.87	9,365.58	0.00	0.00	0.00	
21,100.00	89.12	179.46	11,800.40	-9,459.84	-327.92	9,465.48	0.00	0.00	0.00	
21,200.00	89.12	179.46	11,801.93	-9,559.83	-326.98	9,565.39	0.00	0.00	0.00	
21,300.00	89.12	179.46	11,803.47	-9,659.81	-326.04	9,665.29	0.00	0.00	0.00	
21,400.00	89.12	179.46	11,805.00	-9,759.80	-325.10	9,765.19	0.00	0.00	0.00	
21,500.00	89.12	179.46	11,806.53	-9,859.78	-324.15	9,865.10	0.00	0.00	0.00	
21,600.00	89.12	179.46	11,808.07	-9,959.76	-323.21	9,965.00	0.00	0.00	0.00	
21,700.00	89.12	179.46	11,809.60	-10,059.75	-322.27	10,064.91	0.00	0.00	0.00	
21,800.00	89.12	179.46	11,811.14	-10,159.73	-321.33	10,164.81	0.00	0.00	0.00	
21,813.35	89.12	179.46	11,811.34	-10,173.08	-321.20	10,178.15	0.00	0.00	0.00	
TD at 21813.35 - PBHL (Mission Fed Com 603H)										

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (usft)	+N/-S (usft)	+E/-W (usft)	Northing (usft)	Easting (usft)	Latitude	Longitude
SHL (Mission Fed Com 603H) - hit/miss target - Shape - Point	0.00	0.00	0.00	0.00	0.00	425,620.61	855,709.27	32.166030	-103.317380
LP (Mission Fed Com 603H) - plan hits target center - Point	0.00	0.00	11,660.89	-364.15	-413.68	425,256.46	855,295.59	32.165040	-103.318728
PBHL (Mission Fed Com 603H) - plan hits target center - Point	0.00	0.00	11,811.34	-10,173.08	-321.20	415,447.53	855,388.07	32.138078	-103.318728



Total Directional Services

Planning Report



Database:	EDM 5000.15 Single User Db	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Company:	Franklin Mountain Energy	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Project:	Lea County, NM (NAD83)	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site:	Mission/Vested Fed Com	North Reference:	Grid
Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Wellbore:	OH		
Design:	Plan #1		

Plan Annotations					
Measured Depth (usft)	Vertical Depth (usft)	Local Coordinates		Comment	
		+N/-S (usft)	+E/-W (usft)		
4,200.00	4,200.00	0.00	0.00	Start Build 1.50	
4,600.27	4,599.54	9.03	-18.91	Start 4038.07 hold at 4600.27 MD	
8,638.34	8,615.46	190.97	-400.09	Start Drop -1.50	
9,038.62	9,015.00	200.00	-419.00	Start 2073.00 hold at 9038.62 MD	
11,111.62	11,088.00	200.00	-419.00	Start DLS 10.00 TFO 179.46	
12,002.83	11,660.89	-364.15	-413.68	Start 9810.52 hold at 12002.83 MD	
21,813.35	11,811.34	-10,173.08	-321.20	TD at 21813.35	



Franklin Mountain Energy

Lea County, NM (NAD83)

Mission/Vested Fed Com

Mission Fed Com 603H

OH

Plan #1

Anticollision Report

11 May, 2020





Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Reference	Plan #1		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	Stations	Error Model:	ISCWSA
Depth Range:	Unlimited	Scan Method:	Closest Approach 3D
Results Limited by:	Maximum ellipse separation of 1,000.00 usft	Error Surface:	Combined Separation
Warning Levels Evaluated at:	2.00 Sigma	Casing Method:	Not applied

Survey Tool Program	Date 5/11/2020	
From (usft)	To (usft)	Survey (Wellbore)
0.00	21,813.35	Plan #1 (OH)
		Tool Name
		OWSG (Rev2) MWD
		Description
		OWSG MWD - Standard

Summary						
Site Name	Reference Measured Depth (usft)	Offset Measured Depth (usft)	Distance Between Centres (usft)	Distance Between Ellipses (usft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
Merit/Mission Fed Com						
Mission Fed Com 704H - OH - Plan #1	11,166.67	11,145.98	478.89	422.77	8.535	CC
Mission Fed Com 704H - OH - Plan #1	21,813.35	21,986.90	507.95	279.10	2.220	ES, SF
Mission/Vested Fed Com						
Mission Fed Com 705H - OH - Plan #1	4,200.00	4,200.40	34.99	14.03	1.669	CC, ES, SF
Vested Fed Com 604H - OH - Plan #1	4,116.33	4,117.33	104.98	84.44	5.111	CC
Vested Fed Com 604H - OH - Plan #1	4,200.00	4,200.00	104.99	84.03	5.009	ES, SF
Vested Fed Com 706H - OH - Plan #1	4,116.47	4,117.07	69.99	49.45	3.408	CC
Vested Fed Com 706H - OH - Plan #1	4,200.00	4,200.00	69.99	49.03	3.339	ES, SF

Offset Design												
Merit/Mission Fed Com - Mission Fed Com 704H - OH - Plan #1												
Survey Program: 0-OWSG (Rev2) MWD												
Reference Offset Semi Major Axis Distance												
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	Offset Wellbore Centre +E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor
0.00	0.00	0.00	0.00	0.00	0.00	-90.46	-7.16	-896.84	896.88			
100.00	100.00	94.70	94.70	0.13	0.12	-90.46	-7.16	-896.84	896.87	896.70	0.17	5,190.314
200.00	200.00	194.70	194.70	0.48	0.46	-90.46	-7.16	-896.84	896.87	896.20	0.67	1,336.435
300.00	300.00	294.70	294.70	0.84	0.82	-90.46	-7.16	-896.84	896.87	895.69	1.18	761.357
400.00	400.00	394.70	394.70	1.20	1.18	-90.46	-7.16	-896.84	896.87	895.18	1.68	532.292
500.00	500.00	494.70	494.70	1.56	1.54	-90.46	-7.16	-896.84	896.87	894.68	2.19	409.181
600.00	600.00	594.70	594.70	1.92	1.90	-90.46	-7.16	-896.84	896.87	894.17	2.70	332.320
700.00	700.00	694.70	694.70	2.28	2.26	-90.46	-7.16	-896.84	896.87	893.66	3.21	279.768
800.00	800.00	794.70	794.70	2.63	2.62	-90.46	-7.16	-896.84	896.87	893.16	3.71	241.567
900.00	900.00	894.70	894.70	2.99	2.97	-90.46	-7.16	-896.84	896.87	892.65	4.22	212.545
1,000.00	1,000.00	994.70	994.70	3.35	3.33	-90.46	-7.16	-896.84	896.87	892.14	4.73	189.749
1,100.00	1,100.00	1,094.70	1,094.70	3.71	3.69	-90.46	-7.16	-896.84	896.87	891.64	5.23	171.368
1,200.00	1,200.00	1,194.70	1,194.70	4.07	4.05	-90.46	-7.16	-896.84	896.87	891.13	5.74	156.235
1,300.00	1,300.00	1,294.70	1,294.70	4.43	4.41	-90.46	-7.16	-896.84	896.87	890.62	6.25	143.557
1,400.00	1,400.00	1,394.70	1,394.70	4.79	4.77	-90.46	-7.16	-896.84	896.87	890.11	6.75	132.782
1,500.00	1,500.00	1,494.70	1,494.70	5.14	5.13	-90.46	-7.16	-896.84	896.87	889.61	7.26	123.512
1,600.00	1,600.00	1,594.70	1,594.70	5.50	5.48	-90.46	-7.16	-896.84	896.87	889.10	7.77	115.452
1,700.00	1,700.00	1,694.70	1,694.70	5.86	5.84	-90.46	-7.16	-896.84	896.87	888.59	8.28	108.379
1,800.00	1,800.00	1,794.70	1,794.70	6.22	6.20	-90.46	-7.16	-896.84	896.87	888.09	8.78	102.123

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
1,900.00	1,900.00	1,894.70	1,894.70	6.58	6.56	-90.46	-7.16	-896.84	896.87	887.58	9.29	96.550		
2,000.00	2,000.00	1,994.70	1,994.70	6.94	6.92	-90.46	-7.16	-896.84	896.87	887.07	9.80	91.553		
2,100.00	2,100.00	2,094.70	2,094.70	7.29	7.28	-90.46	-7.16	-896.84	896.87	886.57	10.30	87.048		
2,200.00	2,200.00	2,194.70	2,194.70	7.65	7.63	-90.46	-7.16	-896.84	896.87	886.06	10.81	82.966		
2,300.00	2,300.00	2,294.70	2,294.70	8.01	7.99	-90.46	-7.16	-896.84	896.87	885.55	11.32	79.250		
2,400.00	2,400.00	2,394.70	2,394.70	8.37	8.35	-90.46	-7.16	-896.84	896.87	885.04	11.82	75.852		
2,500.00	2,500.00	2,494.70	2,494.70	8.73	8.71	-90.46	-7.16	-896.84	896.87	884.54	12.33	72.733		
2,600.00	2,600.00	2,594.70	2,594.70	9.09	9.07	-90.46	-7.16	-896.84	896.87	884.03	12.84	69.861		
2,700.00	2,700.00	2,694.70	2,694.70	9.45	9.43	-90.46	-7.16	-896.84	896.87	883.52	13.34	67.207		
2,800.00	2,800.00	2,794.70	2,794.70	9.80	9.79	-90.46	-7.16	-896.84	896.87	883.02	13.85	64.747		
2,900.00	2,900.00	2,894.70	2,894.70	10.16	10.14	-90.46	-7.16	-896.84	896.87	882.51	14.36	62.461		
3,000.00	3,000.00	2,994.70	2,994.70	10.52	10.50	-90.46	-7.16	-896.84	896.87	882.00	14.87	60.331		
3,100.00	3,100.00	3,094.70	3,094.70	10.88	10.86	-90.46	-7.16	-896.84	896.87	881.50	15.37	58.342		
3,200.00	3,200.00	3,194.70	3,194.70	11.24	11.22	-90.46	-7.16	-896.84	896.87	880.99	15.88	56.479		
3,300.00	3,300.00	3,294.70	3,294.70	11.60	11.58	-90.46	-7.16	-896.84	896.87	880.48	16.39	54.732		
3,400.00	3,400.00	3,394.70	3,394.70	11.96	11.94	-90.46	-7.16	-896.84	896.87	879.98	16.89	53.089		
3,500.00	3,500.00	3,494.70	3,494.70	12.31	12.29	-90.46	-7.16	-896.84	896.87	879.47	17.40	51.543		
3,600.00	3,600.00	3,594.70	3,594.70	12.67	12.65	-90.46	-7.16	-896.84	896.87	878.96	17.91	50.084		
3,700.00	3,700.00	3,694.70	3,694.70	13.03	13.01	-90.46	-7.16	-896.84	896.87	878.45	18.41	48.705		
3,800.00	3,800.00	3,794.70	3,794.70	13.39	13.37	-90.46	-7.16	-896.84	896.87	877.95	18.92	47.400		
3,900.00	3,900.00	3,894.70	3,894.70	13.75	13.73	-90.46	-7.16	-896.84	896.87	877.44	19.43	46.163		
4,000.00	4,000.00	3,994.70	3,994.70	14.11	14.09	-90.46	-7.16	-896.84	896.87	876.93	19.94	44.989		
4,100.00	4,100.00	4,094.70	4,094.70	14.46	14.45	-90.46	-7.16	-896.84	896.87	876.43	20.44	43.873		
4,200.00	4,200.00	4,194.70	4,194.70	14.82	14.80	-90.46	-7.16	-896.84	896.87	875.92	20.95	42.812		
4,300.00	4,299.99	4,294.75	4,294.74	15.18	15.16	-25.94	-5.98	-896.85	895.69	874.24	21.45	41.753		
4,400.00	4,399.91	4,394.69	4,394.61	15.53	15.52	-25.83	-2.20	-896.86	892.15	870.20	21.95	40.643		
4,500.00	4,499.69	4,494.41	4,494.12	15.88	15.88	-25.64	4.18	-896.90	886.27	863.82	22.45	39.481		
4,600.27	4,599.54	4,594.19	4,593.54	16.23	16.23	-25.40	12.68	-896.94	878.04	855.09	22.95	38.265		
4,700.00	4,698.72	4,693.39	4,692.36	16.58	16.59	-25.12	21.32	-896.98	868.69	845.25	23.44	37.057		
4,800.00	4,798.17	4,792.86	4,791.45	16.94	16.94	-24.83	29.99	-897.03	859.35	835.41	23.94	35.895		
4,900.00	4,897.62	4,892.33	4,890.54	17.30	17.30	-24.54	38.66	-897.07	850.02	825.58	24.44	34.779		
5,000.00	4,997.08	4,991.80	4,989.63	17.66	17.66	-24.25	47.32	-897.11	840.72	815.78	24.94	33.708		
5,100.00	5,096.53	5,091.27	5,088.72	18.02	18.02	-23.94	55.99	-897.16	831.44	805.99	25.44	32.678		
5,200.00	5,195.98	5,190.74	5,187.82	18.38	18.38	-23.63	64.66	-897.20	822.18	796.23	25.95	31.688		
5,300.00	5,295.43	5,290.21	5,286.91	18.74	18.74	-23.31	73.33	-897.24	812.95	786.50	26.45	30.735		
5,400.00	5,394.88	5,389.68	5,386.00	19.11	19.10	-22.99	81.99	-897.29	803.74	776.79	26.96	29.818		
5,500.00	5,494.33	5,489.15	5,485.09	19.47	19.46	-22.65	90.66	-897.33	794.56	767.10	27.46	28.935		
5,600.00	5,593.78	5,588.62	5,584.18	19.84	19.83	-22.31	99.33	-897.37	785.41	757.44	27.97	28.083		
5,700.00	5,693.24	5,688.09	5,683.27	20.21	20.19	-21.96	108.00	-897.42	776.28	747.81	28.47	27.263		
5,800.00	5,792.69	5,787.56	5,782.37	20.57	20.55	-21.60	116.66	-897.46	767.19	738.21	28.98	26.471		
5,900.00	5,892.14	5,887.03	5,881.46	20.94	20.92	-21.24	125.33	-897.50	758.12	728.63	29.49	25.707		
6,000.00	5,991.59	5,986.50	5,980.55	21.32	21.28	-20.86	134.00	-897.55	749.09	719.09	30.00	24.970		
6,100.00	6,091.04	6,085.97	6,079.64	21.69	21.65	-20.48	142.67	-897.59	740.09	709.58	30.51	24.258		
6,200.00	6,190.49	6,185.44	6,178.73	22.06	22.02	-20.09	151.33	-897.63	731.12	700.10	31.02	23.570		
6,300.00	6,289.94	6,284.91	6,277.82	22.43	22.38	-19.68	160.00	-897.68	722.19	690.66	31.53	22.905		
6,400.00	6,389.40	6,384.38	6,376.91	22.81	22.75	-19.27	168.67	-897.72	713.30	681.25	32.04	22.262		
6,500.00	6,488.85	6,483.85	6,476.01	23.18	23.12	-18.85	177.34	-897.76	704.44	671.89	32.55	21.640		
6,600.00	6,588.30	6,583.45	6,577.30	23.56	23.49	-18.49	185.12	-897.80	695.48	662.42	33.07	21.032		
6,700.00	6,687.75	6,682.40	6,679.13	23.93	23.86	-18.35	190.24	-897.83	686.21	652.62	33.58	20.433		
6,800.00	6,787.20	6,782.31	6,781.00	24.31	24.23	-18.43	192.64	-897.84	676.58	642.49	34.09	19.845		
6,900.00	6,886.65	6,881.66	6,881.35	24.68	24.59	-18.70	192.84	-897.84	666.68	632.09	34.60	19.269		
7,000.00	6,986.10	6,981.11	6,980.80	25.06	24.94	-19.00	192.84	-897.84	656.78	621.68	35.10	18.710		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
7,100.00	7,085.56	7,088.56	7,080.26	25.44	25.29	-19.30	192.84	-897.84	646.89	611.29	35.61	18.168		
7,200.00	7,185.01	7,188.01	7,179.71	25.82	25.65	-19.61	192.84	-897.84	637.02	600.91	36.11	17.640		
7,300.00	7,284.46	7,287.47	7,279.16	26.20	26.00	-19.93	192.84	-897.84	627.17	590.56	36.62	17.128		
7,400.00	7,383.91	7,386.92	7,378.61	26.58	26.35	-20.26	192.84	-897.84	617.34	580.22	37.12	16.630		
7,500.00	7,483.36	7,486.37	7,478.06	26.96	26.71	-20.60	192.84	-897.84	607.54	569.91	37.63	16.146		
7,600.00	7,582.81	7,585.82	7,577.51	27.34	27.06	-20.95	192.84	-897.84	597.75	559.62	38.13	15.675		
7,700.00	7,682.26	7,685.27	7,676.96	27.72	27.42	-21.32	192.84	-897.84	587.99	549.35	38.64	15.217		
7,800.00	7,781.72	7,784.72	7,776.42	28.10	27.77	-21.69	192.84	-897.84	578.25	539.10	39.15	14.771		
7,900.00	7,881.17	7,884.17	7,875.87	28.48	28.12	-22.08	192.84	-897.84	568.53	528.88	39.65	14.337		
8,000.00	7,980.62	7,983.63	7,975.32	28.86	28.48	-22.49	192.84	-897.84	558.85	518.69	40.16	13.915		
8,100.00	8,080.07	8,083.08	8,074.77	29.24	28.83	-22.90	192.84	-897.84	549.19	508.52	40.67	13.504		
8,200.00	8,179.52	8,182.53	8,174.22	29.62	29.19	-23.33	192.84	-897.84	539.56	498.38	41.18	13.103		
8,300.00	8,278.97	8,281.98	8,273.67	30.01	29.54	-23.78	192.84	-897.84	529.96	488.28	41.69	12.713		
8,400.00	8,378.42	8,381.43	8,373.12	30.39	29.90	-24.25	192.84	-897.84	520.40	478.21	42.20	12.333		
8,500.00	8,477.88	8,480.88	8,472.58	30.77	30.25	-24.73	192.84	-897.84	510.87	468.17	42.71	11.963		
8,600.00	8,577.33	8,580.33	8,572.03	31.16	30.60	-25.23	192.84	-897.84	501.38	458.17	43.22	11.602		
8,638.34	8,615.46	8,618.47	8,610.16	31.30	30.74	-25.42	192.84	-897.84	497.75	454.34	43.41	11.466		
8,700.00	8,676.83	8,679.84	8,671.53	31.54	30.96	-25.69	192.84	-897.84	492.38	448.65	43.73	11.260		
8,800.00	8,776.54	8,779.55	8,771.24	31.91	31.31	-26.03	192.84	-897.84	485.58	441.34	44.24	10.977		
8,900.00	8,876.42	8,879.42	8,871.12	32.28	31.67	-26.26	192.84	-897.84	481.15	436.41	44.74	10.754		
9,000.00	8,976.39	8,979.39	8,971.09	32.63	32.03	-26.36	192.84	-897.84	479.07	433.82	45.25	10.588		
9,038.62	9,015.00	9,018.01	9,009.70	32.76	32.16	-90.86	192.84	-897.84	478.89	433.45	45.44	10.539		
9,100.00	9,076.38	9,079.39	9,071.08	32.98	32.38	-90.86	192.84	-897.84	478.89	433.15	45.75	10.468		
9,200.00	9,176.38	9,179.39	9,171.08	33.32	32.74	-90.86	192.84	-897.84	478.89	432.65	46.25	10.355		
9,300.00	9,276.38	9,279.39	9,271.08	33.67	33.10	-90.86	192.84	-897.84	478.89	432.14	46.75	10.244		
9,400.00	9,376.38	9,379.39	9,371.08	34.02	33.45	-90.86	192.84	-897.84	478.89	431.64	47.25	10.135		
9,500.00	9,476.38	9,479.39	9,471.08	34.37	33.81	-90.86	192.84	-897.84	478.89	431.14	47.75	10.029		
9,600.00	9,576.38	9,579.39	9,571.08	34.71	34.17	-90.86	192.84	-897.84	478.89	430.64	48.25	9.925		
9,700.00	9,676.38	9,679.39	9,671.08	35.06	34.52	-90.86	192.84	-897.84	478.89	430.14	48.76	9.822		
9,800.00	9,776.38	9,779.39	9,771.08	35.41	34.88	-90.86	192.84	-897.84	478.89	429.64	49.26	9.722		
9,900.00	9,876.38	9,879.39	9,871.08	35.76	35.24	-90.86	192.84	-897.84	478.89	429.13	49.76	9.624		
10,000.00	9,976.38	9,979.39	9,971.08	36.11	35.60	-90.86	192.84	-897.84	478.89	428.63	50.26	9.528		
10,100.00	10,076.38	10,079.39	10,071.08	36.46	35.95	-90.86	192.84	-897.84	478.89	428.13	50.76	9.434		
10,200.00	10,176.38	10,179.39	10,171.08	36.81	36.31	-90.86	192.84	-897.84	478.89	427.63	51.27	9.342		
10,300.00	10,276.38	10,279.39	10,271.08	37.16	36.67	-90.86	192.84	-897.84	478.89	427.13	51.77	9.251		
10,400.00	10,376.38	10,379.39	10,371.08	37.51	37.02	-90.86	192.84	-897.84	478.89	426.62	52.27	9.162		
10,500.00	10,476.38	10,479.39	10,471.08	37.86	37.38	-90.86	192.84	-897.84	478.89	426.12	52.77	9.075		
10,600.00	10,576.38	10,579.39	10,571.08	38.20	37.74	-90.86	192.84	-897.84	478.89	425.62	53.27	8.989		
10,700.00	10,676.38	10,679.39	10,671.08	38.55	38.09	-90.86	192.84	-897.84	478.89	425.12	53.78	8.905		
10,800.00	10,776.38	10,779.39	10,771.08	38.90	38.45	-90.86	192.84	-897.84	478.89	424.61	54.28	8.823		
10,900.00	10,876.38	10,879.39	10,871.08	39.26	38.81	-90.86	192.84	-897.84	478.89	424.11	54.78	8.742		
11,000.00	10,976.38	10,979.39	10,971.08	39.61	39.17	-90.86	192.84	-897.84	478.89	423.61	55.29	8.662		
11,100.00	11,076.38	11,079.39	11,071.08	39.96	39.52	-90.86	192.84	-897.84	478.89	423.10	55.79	8.584		
11,111.62	11,088.00	11,091.01	11,082.70	40.00	39.57	-90.86	192.84	-897.84	478.89	423.05	55.85	8.575		
11,150.00	11,126.36	11,129.36	11,121.06	40.12	39.70	89.84	192.84	-897.84	478.89	422.85	56.03	8.546		
11,166.67	11,142.97	11,145.98	11,137.67	40.18	39.76	90.00	192.84	-897.84	478.89	422.77	56.11	8.535 CC		
11,200.00	11,176.03	11,179.04	11,170.73	40.28	39.88	90.49	192.84	-897.84	478.90	422.64	56.27	8.511		
11,250.00	11,225.04	11,228.05	11,219.74	40.43	40.05	91.62	192.84	-897.84	479.09	422.60	56.49	8.481		
11,300.00	11,273.01	11,276.02	11,267.71	40.57	40.23	93.17	192.84	-897.84	479.71	423.00	56.70	8.460		
11,350.00	11,319.57	11,325.36	11,317.03	40.70	40.39	95.06	191.77	-897.83	481.02	424.12	56.90	8.454		
11,400.00	11,364.36	11,377.15	11,368.51	40.81	40.55	96.99	186.27	-897.78	482.96	425.87	57.08	8.461		
11,450.00	11,407.05	11,430.80	11,421.09	40.92	40.71	98.89	175.70	-897.68	485.47	428.23	57.24	8.482		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Merit/Mission Fed Com - Mission Fed Com 704H - OH - Plan #1		Offset Site Error:		0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:		0.00 usft		
Reference		Offset		Semi Major Axis			Distance										
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning				
11,500.00	11,447.32	11,486.49	11,474.37	41.02	40.86	100.76	159.58	-897.53	488.48	431.13	57.35	8.517					
11,550.00	11,484.85	11,544.37	11,527.82	41.10	41.01	102.57	137.43	-897.32	491.93	434.51	57.41	8.568					
11,600.00	11,519.36	11,604.58	11,580.75	41.17	41.16	104.30	108.79	-897.05	495.68	438.28	57.40	8.636					
11,650.00	11,550.58	11,667.24	11,632.33	41.24	41.31	105.94	73.27	-896.71	499.60	442.30	57.30	8.719					
11,700.00	11,578.29	11,732.41	11,681.52	41.29	41.46	107.46	30.58	-896.31	503.55	446.42	57.12	8.815					
11,750.00	11,602.26	11,800.07	11,727.12	41.34	41.61	108.83	-19.35	-895.84	507.35	450.48	56.87	8.920					
11,800.00	11,622.32	11,870.14	11,767.80	41.40	41.76	110.04	-76.34	-895.30	510.84	454.25	56.59	9.027					
11,850.00	11,638.32	11,942.39	11,802.15	41.48	41.92	111.04	-139.85	-894.71	513.85	457.55	56.31	9.126					
11,900.00	11,650.12	12,016.51	11,828.80	41.58	42.09	111.81	-208.96	-894.05	516.24	460.15	56.08	9.205					
11,950.00	11,657.65	12,092.05	11,846.55	41.71	42.27	112.33	-282.32	-893.36	517.86	461.89	55.98	9.252					
12,002.83	11,660.89	12,172.78	11,854.69	41.85	42.47	112.58	-362.57	-892.61	518.66	462.63	56.03	9.256					
12,100.00	11,662.38	12,273.60	11,856.02	42.14	42.75	112.56	-463.37	-891.66	518.57	462.18	56.39	9.196					
12,200.00	11,663.91	12,373.60	11,857.25	42.50	43.09	112.53	-563.36	-890.71	518.46	461.62	56.84	9.121					
12,300.00	11,665.45	12,473.60	11,858.48	42.92	43.49	112.50	-663.35	-889.77	518.34	460.98	57.37	9.036					
12,400.00	11,666.98	12,573.60	11,859.71	43.40	43.94	112.47	-763.34	-888.83	518.22	460.26	57.97	8.940					
12,500.00	11,668.52	12,673.60	11,860.93	43.93	44.46	112.44	-863.32	-887.89	518.11	459.46	58.65	8.834					
12,600.00	11,670.05	12,773.60	11,862.16	44.52	45.03	112.40	-963.31	-886.95	517.99	458.59	59.40	8.721					
12,700.00	11,671.58	12,873.60	11,863.39	45.16	45.65	112.37	-1,063.30	-886.00	517.88	457.65	60.22	8.600					
12,800.00	11,673.12	12,973.59	11,864.62	45.84	46.32	112.34	-1,163.29	-885.06	517.76	456.65	61.11	8.473					
12,900.00	11,674.65	13,073.59	11,865.84	46.58	47.04	112.31	-1,263.27	-884.12	517.64	455.58	62.06	8.340					
13,000.00	11,676.18	13,173.59	11,867.07	47.36	47.81	112.28	-1,363.26	-883.18	517.53	454.45	63.08	8.204					
13,100.00	11,677.72	13,273.59	11,868.30	48.19	48.62	112.25	-1,463.25	-882.23	517.41	453.26	64.15	8.065					
13,200.00	11,679.25	13,373.59	11,869.52	49.05	49.47	112.22	-1,563.24	-881.29	517.30	452.01	65.28	7.924					
13,300.00	11,680.78	13,473.59	11,870.75	49.96	50.36	112.18	-1,663.22	-880.35	517.18	450.72	66.47	7.781					
13,400.00	11,682.32	13,573.59	11,871.98	50.90	51.29	112.15	-1,763.21	-879.41	517.07	449.37	67.70	7.638					
13,500.00	11,683.85	13,673.59	11,873.21	51.88	52.26	112.12	-1,863.20	-878.47	516.95	447.97	68.98	7.494					
13,600.00	11,685.38	13,773.59	11,874.43	52.89	53.26	112.09	-1,963.19	-877.52	516.84	446.53	70.30	7.351					
13,700.00	11,686.92	13,873.59	11,875.66	53.93	54.29	112.06	-2,063.17	-876.58	516.72	445.05	71.67	7.210					
13,800.00	11,688.45	13,973.59	11,876.89	55.01	55.35	112.03	-2,163.16	-875.64	516.61	443.53	73.08	7.069					
13,900.00	11,689.98	14,073.59	11,878.12	56.11	56.44	112.00	-2,263.15	-874.70	516.49	441.97	74.52	6.931					
14,000.00	11,691.52	14,173.59	11,879.34	57.23	57.56	111.96	-2,363.14	-873.75	516.38	440.37	76.00	6.794					
14,100.00	11,693.05	14,273.59	11,880.57	58.39	58.70	111.93	-2,463.12	-872.81	516.27	438.75	77.52	6.660					
14,200.00	11,694.59	14,373.59	11,881.80	59.56	59.87	111.90	-2,563.11	-871.87	516.15	437.09	79.06	6.528					
14,300.00	11,696.12	14,473.59	11,883.03	60.76	61.06	111.87	-2,663.10	-870.93	516.04	435.40	80.64	6.399					
14,400.00	11,697.65	14,573.59	11,884.25	61.98	62.26	111.84	-2,763.09	-869.99	515.92	433.68	82.24	6.273					
14,500.00	11,699.19	14,673.59	11,885.48	63.22	63.49	111.81	-2,863.07	-869.04	515.81	431.94	83.87	6.150					
14,600.00	11,700.72	14,773.59	11,886.71	64.47	64.74	111.77	-2,963.06	-868.10	515.70	430.17	85.53	6.030					
14,700.00	11,702.25	14,873.59	11,887.93	65.75	66.01	111.74	-3,063.05	-867.16	515.58	428.38	87.21	5.912					
14,800.00	11,703.79	14,973.59	11,889.16	67.04	67.29	111.71	-3,163.04	-866.22	515.47	426.57	88.91	5.798					
14,900.00	11,705.32	15,073.59	11,890.39	68.35	68.59	111.68	-3,263.02	-865.27	515.36	424.73	90.63	5.687					
15,000.00	11,706.85	15,173.58	11,891.62	69.67	69.90	111.65	-3,363.01	-864.33	515.25	422.88	92.37	5.578					
15,100.00	11,708.39	15,273.58	11,892.84	71.00	71.23	111.62	-3,463.00	-863.39	515.13	421.01	94.13	5.473					
15,200.00	11,709.92	15,373.58	11,894.07	72.35	72.57	111.58	-3,562.99	-862.45	515.02	419.12	95.90	5.370					
15,300.00	11,711.45	15,473.58	11,895.30	73.71	73.93	111.55	-3,662.97	-861.51	514.91	417.21	97.70	5.271					
15,400.00	11,712.99	15,573.58	11,896.53	75.08	75.29	111.52	-3,762.96	-860.56	514.80	415.29	99.50	5.174					
15,500.00	11,714.52	15,673.58	11,897.75	76.47	76.67	111.49	-3,862.95	-859.62	514.69	413.36	101.33	5.079					
15,600.00	11,716.06	15,773.58	11,898.98	77.86	78.06	111.46	-3,962.94	-858.68	514.57	411.41	103.16	4.988					
15,700.00	11,717.59	15,873.58	11,900.21	79.26	79.46	111.43	-4,062.92	-857.74	514.46	409.45	105.01	4.899					
15,800.00	11,719.12	15,973.58	11,901.44	80.68	80.86	111.39	-4,162.91	-856.80	514.35	407.47	106.88	4.813					
15,900.00	11,720.66	16,073.58	11,902.66	82.10	82.28	111.36	-4,262.90	-855.85	514.24	405.49	108.75	4.729					
16,000.00	11,722.19	16,173.58	11,903.89	83.53	83.71	111.33	-4,362.89	-854.91	514.13	403.49	110.64	4.647					
16,100.00	11,723.72	16,273.58	11,905.12	84.97	85.14	111.30	-4,462.88	-853.97	514.02	401.49	112.53	4.568					

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Merit/Mission Fed Com - Mission Fed Com 704H - OH - Plan #1		Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft		
Reference		Offset		Semi Major Axis			Distance							Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor				
16,200.00	11,725.26	16,373.58	11,906.35	86.41	86.58	111.27	-4,562.86	-853.03	513.91	399.47	114.44	4.491				
16,300.00	11,726.79	16,473.58	11,907.57	87.87	88.03	111.24	-4,662.85	-852.08	513.80	397.44	116.36	4.416				
16,400.00	11,728.32	16,573.58	11,908.80	89.33	89.48	111.20	-4,762.84	-851.14	513.69	395.41	118.28	4.343				
16,500.00	11,729.86	16,673.58	11,910.03	90.79	90.95	111.17	-4,862.83	-850.20	513.58	393.36	120.21	4.272				
16,600.00	11,731.39	16,773.58	11,911.25	92.27	92.42	111.14	-4,962.81	-849.26	513.47	391.31	122.16	4.203				
16,700.00	11,732.92	16,873.58	11,912.48	93.75	93.89	111.11	-5,062.80	-848.32	513.36	389.25	124.11	4.136				
16,800.00	11,734.46	16,973.58	11,913.71	95.23	95.37	111.08	-5,162.79	-847.37	513.25	387.19	126.06	4.071				
16,900.00	11,735.99	17,073.58	11,914.94	96.72	96.86	111.04	-5,262.78	-846.43	513.14	385.11	128.03	4.008				
17,000.00	11,737.52	17,173.58	11,916.16	98.22	98.35	111.01	-5,362.76	-845.49	513.03	383.03	130.00	3.946				
17,100.00	11,739.06	17,273.57	11,917.39	99.72	99.85	110.98	-5,462.75	-844.55	512.92	380.95	131.97	3.887				
17,200.00	11,740.59	17,373.57	11,918.62	101.22	101.35	110.95	-5,562.74	-843.60	512.81	378.85	133.96	3.828				
17,300.00	11,742.13	17,473.57	11,919.85	102.73	102.85	110.92	-5,662.73	-842.66	512.70	376.76	135.94	3.771				
17,400.00	11,743.66	17,573.57	11,921.07	104.25	104.37	110.88	-5,762.71	-841.72	512.59	374.65	137.94	3.716				
17,500.00	11,745.19	17,673.57	11,922.30	105.77	105.88	110.85	-5,862.70	-840.78	512.48	372.55	139.94	3.662				
17,600.00	11,746.73	17,773.57	11,923.53	107.29	107.40	110.82	-5,962.69	-839.84	512.38	370.43	141.94	3.610				
17,700.00	11,748.26	17,873.57	11,924.76	108.81	108.92	110.79	-6,062.68	-838.89	512.27	368.32	143.95	3.559				
17,800.00	11,749.79	17,973.57	11,925.98	110.34	110.45	110.76	-6,162.66	-837.95	512.16	366.20	145.96	3.509				
17,900.00	11,751.33	18,073.57	11,927.21	111.88	111.98	110.72	-6,262.65	-837.01	512.05	364.07	147.98	3.460				
18,000.00	11,752.86	18,173.57	11,928.44	113.41	113.51	110.69	-6,362.64	-836.07	511.94	361.94	150.00	3.413				
18,100.00	11,754.39	18,273.57	11,929.67	114.95	115.05	110.66	-6,462.63	-835.12	511.84	359.81	152.03	3.367				
18,200.00	11,755.93	18,373.57	11,930.89	116.49	116.59	110.63	-6,562.61	-834.18	511.73	357.67	154.06	3.322				
18,300.00	11,757.46	18,473.57	11,932.12	118.04	118.13	110.60	-6,662.60	-833.24	511.62	355.53	156.09	3.278				
18,400.00	11,758.99	18,573.57	11,933.35	119.59	119.68	110.56	-6,762.59	-832.30	511.51	353.39	158.13	3.235				
18,500.00	11,760.53	18,673.57	11,934.57	121.14	121.23	110.53	-6,862.58	-831.36	511.41	351.24	160.17	3.193				
18,600.00	11,762.06	18,773.57	11,935.80	122.69	122.78	110.50	-6,962.56	-830.41	511.30	349.09	162.21	3.152				
18,700.00	11,763.60	18,873.57	11,937.03	124.25	124.33	110.47	-7,062.55	-829.47	511.19	346.94	164.25	3.112				
18,800.00	11,765.13	18,973.57	11,938.26	125.81	125.89	110.43	-7,162.54	-828.53	511.09	344.78	166.30	3.073				
18,900.00	11,766.66	19,073.57	11,939.48	127.37	127.45	110.40	-7,262.53	-827.59	510.98	342.63	168.35	3.035				
19,000.00	11,768.20	19,173.57	11,940.71	128.93	129.01	110.37	-7,362.51	-826.64	510.87	340.47	170.41	2.998				
19,100.00	11,769.73	19,273.57	11,941.94	130.50	130.57	110.34	-7,462.50	-825.70	510.77	338.30	172.46	2.962				
19,200.00	11,771.26	19,373.57	11,943.17	132.07	132.14	110.31	-7,562.49	-824.76	510.66	336.14	174.52	2.926				
19,300.00	11,772.80	19,473.56	11,944.39	133.64	133.71	110.27	-7,662.48	-823.82	510.56	333.97	176.58	2.891				
19,400.00	11,774.33	19,573.56	11,945.62	135.21	135.28	110.24	-7,762.46	-822.88	510.45	331.80	178.65	2.857				
19,500.00	11,775.86	19,673.56	11,946.85	136.78	136.85	110.21	-7,862.45	-821.93	510.35	329.63	180.71	2.824				
19,600.00	11,777.40	19,773.56	11,948.08	138.36	138.42	110.18	-7,962.44	-820.99	510.24	327.46	182.78	2.792				
19,700.00	11,778.93	19,873.56	11,949.30	139.94	140.00	110.14	-8,062.43	-820.05	510.13	325.29	184.85	2.760				
19,800.00	11,780.46	19,973.56	11,950.53	141.52	141.57	110.11	-8,162.41	-819.11	510.03	323.11	186.92	2.729				
19,900.00	11,782.00	20,073.56	11,951.76	143.10	143.15	110.08	-8,262.40	-818.16	509.93	320.94	188.99	2.698				
20,000.00	11,783.53	20,173.56	11,952.99	144.68	144.73	110.05	-8,362.39	-817.22	509.82	318.76	191.06	2.668				
20,100.00	11,785.07	20,273.56	11,954.21	146.26	146.32	110.02	-8,462.38	-816.28	509.72	316.58	193.14	2.639				
20,200.00	11,786.60	20,373.56	11,955.44	147.85	147.90	109.98	-8,562.37	-815.34	509.61	314.40	195.21	2.611				
20,300.00	11,788.13	20,473.56	11,956.67	149.44	149.48	109.95	-8,662.35	-814.40	509.51	312.22	197.29	2.583				
20,400.00	11,789.67	20,573.56	11,957.89	151.02	151.07	109.92	-8,762.34	-813.45	509.40	310.03	199.37	2.555				
20,500.00	11,791.20	20,673.56	11,959.12	152.61	152.66	109.89	-8,862.33	-812.51	509.30	307.85	201.45	2.528				
20,600.00	11,792.73	20,773.56	11,960.35	154.20	154.25	109.85	-8,962.32	-811.57	509.20	305.67	203.53	2.502				
20,700.00	11,794.27	20,873.56	11,961.58	155.80	155.84	109.82	-9,062.30	-810.63	509.09	303.48	205.61	2.476				
20,800.00	11,795.80	20,973.56	11,962.80	157.39	157.43	109.79	-9,162.29	-809.69	508.99	301.29	207.70	2.451				
20,900.00	11,797.33	21,073.56	11,964.03	158.98	159.02	109.76	-9,262.28	-808.74	508.89	299.11	209.78	2.426				
21,000.00	11,798.87	21,173.56	11,965.26	160.58	160.62	109.72	-9,362.27	-807.80	508.78	296.92	211.87	2.401				
21,100.00	11,800.40	21,273.56	11,966.49	162.18	162.21	109.69	-9,462.25	-806.86	508.68	294.73	213.95	2.378				
21,200.00	11,801.93	21,373.56	11,967.71	163.78	163.81	109.66	-9,562.24	-805.92	508.58	292.54	216.04	2.354				
21,300.00	11,803.47	21,473.56	11,968.94	165.37	165.41	109.63	-9,662.23	-804.97	508.48	290.35	218.13	2.331				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	0.00 usft
Merit/Mission Fed Com - Mission Fed Com 704H - OH - Plan #1												Offset Well Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													
Reference		Offset		Semi Major Axis		Distance							
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning
21,400.00	11,805.00	21,573.55	11,970.17	166.98	167.01	109.59	-9,762.22	-804.03	508.37	288.16	220.21	2.309	
21,500.00	11,806.53	21,673.55	11,971.40	168.58	168.61	109.56	-9,862.20	-803.09	508.27	285.97	222.30	2.286	
21,600.00	11,808.07	21,773.55	11,972.62	170.18	170.21	109.53	-9,962.19	-802.15	508.17	283.78	224.39	2.265	
21,700.00	11,809.60	21,873.55	11,973.85	171.78	171.81	109.50	-10,062.18	-801.21	508.07	281.59	226.48	2.243	
21,800.00	11,811.14	21,973.55	11,975.08	173.39	173.41	109.46	-10,162.17	-800.26	507.97	279.39	228.57	2.222	
21,813.35	11,811.34	21,986.90	11,975.24	173.60	173.63	109.46	-10,175.52	-800.14	507.95	279.10	228.85	2.220 ES, SF	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance							Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
0.00	0.00	0.40	0.40	0.00	0.00	89.54	0.28	34.99	34.99					
100.00	100.00	100.40	100.40	0.13	0.13	89.54	0.28	34.99	34.99	34.81	0.18	196.082		
200.00	200.00	200.40	200.40	0.48	0.49	89.54	0.28	34.99	34.99	34.31	0.69	51.052		
300.00	300.00	300.40	300.40	0.84	0.84	89.54	0.28	34.99	34.99	33.80	1.19	29.346		
400.00	400.00	400.40	400.40	1.20	1.20	89.54	0.28	34.99	34.99	33.29	1.70	20.591		
500.00	500.00	500.40	500.40	1.56	1.56	89.54	0.28	34.99	34.99	32.78	2.21	15.860		
600.00	600.00	600.40	600.40	1.92	1.92	89.54	0.28	34.99	34.99	32.28	2.71	12.897		
700.00	700.00	700.40	700.40	2.28	2.28	89.54	0.28	34.99	34.99	31.77	3.22	10.866		
800.00	800.00	800.40	800.40	2.63	2.64	89.54	0.28	34.99	34.99	31.26	3.73	9.388		
900.00	900.00	900.40	900.40	2.99	2.99	89.54	0.28	34.99	34.99	30.76	4.23	8.264		
1,000.00	1,000.00	1,000.40	1,000.40	3.35	3.35	89.54	0.28	34.99	34.99	30.25	4.74	7.380		
1,100.00	1,100.00	1,100.40	1,100.40	3.71	3.71	89.54	0.28	34.99	34.99	29.74	5.25	6.668		
1,200.00	1,200.00	1,200.40	1,200.40	4.07	4.07	89.54	0.28	34.99	34.99	29.24	5.75	6.080		
1,300.00	1,300.00	1,300.40	1,300.40	4.43	4.43	89.54	0.28	34.99	34.99	28.73	6.26	5.588		
1,400.00	1,400.00	1,400.40	1,400.40	4.79	4.79	89.54	0.28	34.99	34.99	28.22	6.77	5.169		
1,500.00	1,500.00	1,500.40	1,500.40	5.14	5.15	89.54	0.28	34.99	34.99	27.72	7.28	4.809		
1,600.00	1,600.00	1,600.40	1,600.40	5.50	5.50	89.54	0.28	34.99	34.99	27.21	7.78	4.496		
1,700.00	1,700.00	1,700.40	1,700.40	5.86	5.86	89.54	0.28	34.99	34.99	26.70	8.29	4.221		
1,800.00	1,800.00	1,800.40	1,800.40	6.22	6.22	89.54	0.28	34.99	34.99	26.19	8.80	3.978		
1,900.00	1,900.00	1,900.40	1,900.40	6.58	6.58	89.54	0.28	34.99	34.99	25.69	9.30	3.761		
2,000.00	2,000.00	2,000.40	2,000.40	6.94	6.94	89.54	0.28	34.99	34.99	25.18	9.81	3.567		
2,100.00	2,100.00	2,100.40	2,100.40	7.29	7.30	89.54	0.28	34.99	34.99	24.67	10.32	3.391		
2,200.00	2,200.00	2,200.40	2,200.40	7.65	7.65	89.54	0.28	34.99	34.99	24.17	10.82	3.233		
2,300.00	2,300.00	2,300.40	2,300.40	8.01	8.01	89.54	0.28	34.99	34.99	23.66	11.33	3.088		
2,400.00	2,400.00	2,400.40	2,400.40	8.37	8.37	89.54	0.28	34.99	34.99	23.15	11.84	2.956		
2,500.00	2,500.00	2,500.40	2,500.40	8.73	8.73	89.54	0.28	34.99	34.99	22.65	12.35	2.834		
2,600.00	2,600.00	2,600.40	2,600.40	9.09	9.09	89.54	0.28	34.99	34.99	22.14	12.85	2.723		
2,700.00	2,700.00	2,700.40	2,700.40	9.45	9.45	89.54	0.28	34.99	34.99	21.63	13.36	2.619		
2,800.00	2,800.00	2,800.40	2,800.40	9.80	9.81	89.54	0.28	34.99	34.99	21.12	13.87	2.523		
2,900.00	2,900.00	2,900.40	2,900.40	10.16	10.16	89.54	0.28	34.99	34.99	20.62	14.37	2.434		
3,000.00	3,000.00	3,000.40	3,000.40	10.52	10.52	89.54	0.28	34.99	34.99	20.11	14.88	2.352		
3,100.00	3,100.00	3,100.40	3,100.40	10.88	10.88	89.54	0.28	34.99	34.99	19.60	15.39	2.274		
3,200.00	3,200.00	3,200.40	3,200.40	11.24	11.24	89.54	0.28	34.99	34.99	19.10	15.89	2.202		
3,300.00	3,300.00	3,300.40	3,300.40	11.60	11.60	89.54	0.28	34.99	34.99	18.59	16.40	2.133		
3,400.00	3,400.00	3,400.40	3,400.40	11.96	11.96	89.54	0.28	34.99	34.99	18.08	16.91	2.070		
3,500.00	3,500.00	3,500.40	3,500.40	12.31	12.31	89.54	0.28	34.99	34.99	17.58	17.41	2.009		
3,600.00	3,600.00	3,600.40	3,600.40	12.67	12.67	89.54	0.28	34.99	34.99	17.07	17.92	1.952		
3,700.00	3,700.00	3,700.40	3,700.40	13.03	13.03	89.54	0.28	34.99	34.99	16.56	18.43	1.899		
3,800.00	3,800.00	3,800.40	3,800.40	13.39	13.39	89.54	0.28	34.99	34.99	16.06	18.94	1.848		
3,900.00	3,900.00	3,900.40	3,900.40	13.75	13.75	89.54	0.28	34.99	34.99	15.55	19.44	1.800		
4,000.00	4,000.00	4,000.40	4,000.40	14.11	14.11	89.54	0.28	34.99	34.99	15.04	19.95	1.754		
4,100.00	4,100.00	4,100.40	4,100.40	14.46	14.47	89.54	0.28	34.99	34.99	14.53	20.46	1.711		
4,200.00	4,200.00	4,200.40	4,200.40	14.82	14.82	89.54	0.28	34.99	34.99	14.03	20.96	1.669 CC, ES, SF		
4,300.00	4,299.99	4,300.39	4,300.39	15.18	15.18	154.93	0.28	34.99	36.17	14.71	21.47	1.685		
4,400.00	4,399.91	4,400.31	4,400.31	15.53	15.54	157.30	0.28	34.99	39.76	17.80	21.97	1.810		
4,500.00	4,499.69	4,500.09	4,500.09	15.88	15.90	160.43	0.28	34.99	45.87	23.40	22.47	2.042		
4,600.27	4,599.54	4,599.94	4,599.94	16.23	16.26	163.62	0.28	34.99	54.60	31.64	22.96	2.378		
4,700.00	4,698.72	4,699.50	4,699.49	16.58	16.61	165.11	1.58	34.94	64.39	40.93	23.46	2.744		
4,800.00	4,798.17	4,799.45	4,799.36	16.94	16.97	164.22	5.48	34.81	73.65	49.69	23.96	3.074		
4,900.00	4,897.62	4,899.38	4,899.08	17.30	17.33	161.75	12.00	34.58	82.46	58.01	24.46	3.372		
5,000.00	4,997.08	4,999.00	4,998.32	17.66	17.68	158.49	20.53	34.28	91.16	66.20	24.96	3.653		
5,100.00	5,096.53	5,098.49	5,097.44	18.02	18.04	155.72	29.20	33.98	100.09	74.63	25.46	3.932		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Mission/Vested Fed Com - Mission Fed Com 705H - OH - Plan #1		Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD															Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance							Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor				
				(usft)	(usft)	(°)										
5,200.00	5,195.98	5,197.98	5,196.55	18.38	18.39	153.41	37.87	33.67	109.21	83.25	25.96	4.207				
5,300.00	5,295.43	5,297.48	5,295.67	18.74	18.75	151.45	46.54	33.37	118.48	92.02	26.46	4.478				
5,400.00	5,394.88	5,396.97	5,394.78	19.11	19.11	149.78	55.21	33.07	127.87	100.91	26.96	4.742				
5,500.00	5,494.33	5,496.47	5,493.90	19.47	19.47	148.34	63.88	32.76	137.36	109.89	27.47	5.000				
5,600.00	5,593.78	5,595.96	5,593.01	19.84	19.83	147.09	72.55	32.46	146.91	118.94	27.98	5.251				
5,700.00	5,693.24	5,695.45	5,692.13	20.21	20.19	145.99	81.22	32.16	156.53	128.05	28.48	5.496				
5,800.00	5,792.69	5,794.95	5,791.24	20.57	20.55	145.01	89.89	31.85	166.20	137.21	28.99	5.733				
5,900.00	5,892.14	5,894.44	5,890.36	20.94	20.91	144.15	98.56	31.55	175.91	146.41	29.50	5.963				
6,000.00	5,991.59	5,993.94	5,989.47	21.32	21.28	143.37	107.23	31.25	185.66	155.65	30.01	6.186				
6,100.00	6,091.04	6,093.43	6,088.59	21.69	21.64	142.68	115.90	30.94	195.44	164.91	30.52	6.403				
6,200.00	6,190.49	6,192.93	6,187.70	22.06	22.00	142.05	124.57	30.64	205.24	174.20	31.03	6.613				
6,300.00	6,289.94	6,292.42	6,286.82	22.43	22.37	141.47	133.24	30.34	215.07	183.52	31.55	6.817				
6,400.00	6,389.40	6,391.91	6,385.93	22.81	22.73	140.95	141.91	30.03	224.91	192.85	32.06	7.015				
6,500.00	6,488.85	6,491.41	6,485.05	23.18	23.10	140.47	150.58	29.73	234.77	202.20	32.58	7.207				
6,600.00	6,588.30	6,590.90	6,584.16	23.56	23.46	140.03	159.25	29.43	244.65	211.56	33.09	7.393				
6,700.00	6,687.75	6,690.40	6,683.28	23.93	23.83	139.62	167.92	29.12	254.54	220.93	33.61	7.574				
6,800.00	6,787.20	6,789.89	6,782.40	24.31	24.19	139.25	176.60	28.82	264.44	230.32	34.12	7.750				
6,900.00	6,886.65	6,889.38	6,881.51	24.68	24.56	138.90	185.27	28.52	274.36	239.72	34.64	7.920				
7,000.00	6,986.10	6,990.55	6,982.38	25.06	24.93	138.80	192.89	28.25	284.00	248.83	35.17	8.076				
7,100.00	7,085.56	7,091.88	7,083.59	25.44	25.30	139.23	197.84	28.08	293.04	257.35	35.69	8.212				
7,200.00	7,185.01	7,193.14	7,184.82	25.82	25.67	140.12	200.12	28.00	301.52	265.32	36.20	8.329				
7,300.00	7,284.46	7,293.18	7,284.86	26.20	26.02	141.34	200.28	27.99	309.67	272.96	36.71	8.437				
7,400.00	7,383.91	7,392.63	7,384.31	26.58	26.37	142.52	200.28	27.99	317.92	280.71	37.21	8.544				
7,500.00	7,483.36	7,492.08	7,483.76	26.96	26.73	143.63	200.28	27.99	326.30	288.59	37.71	8.653				
7,600.00	7,582.81	7,591.53	7,583.21	27.34	27.08	144.69	200.28	27.99	334.80	296.58	38.21	8.761				
7,700.00	7,682.26	7,690.98	7,682.66	27.72	27.44	145.70	200.28	27.99	343.40	304.69	38.72	8.870				
7,800.00	7,781.72	7,790.43	7,782.12	28.10	27.79	146.65	200.28	27.99	352.11	312.89	39.22	8.978				
7,900.00	7,881.17	7,889.89	7,881.57	28.48	28.14	147.57	200.28	27.99	360.90	321.18	39.72	9.086				
8,000.00	7,980.62	7,989.34	7,981.02	28.86	28.50	148.43	200.28	27.99	369.79	329.56	40.22	9.193				
8,100.00	8,080.07	8,088.79	8,080.47	29.24	28.85	149.26	200.28	27.99	378.75	338.03	40.73	9.300				
8,200.00	8,179.52	8,188.24	8,179.92	29.62	29.21	150.05	200.28	27.99	387.79	346.56	41.23	9.406				
8,300.00	8,278.97	8,287.69	8,279.37	30.01	29.56	150.80	200.28	27.99	396.90	355.17	41.73	9.511				
8,400.00	8,378.42	8,387.14	8,378.82	30.39	29.92	151.52	200.28	27.99	406.08	363.84	42.24	9.615				
8,500.00	8,477.88	8,486.59	8,478.28	30.77	30.27	152.21	200.28	27.99	415.31	372.57	42.74	9.717				
8,600.00	8,577.33	8,586.05	8,577.73	31.16	30.63	152.87	200.28	27.99	424.60	381.36	43.24	9.819				
8,638.34	8,615.46	8,624.18	8,615.86	31.30	30.76	153.11	200.28	27.99	428.18	384.75	43.44	9.858				
8,700.00	8,676.83	8,685.55	8,677.23	31.54	30.98	153.50	200.28	27.99	433.51	389.76	43.75	9.910				
8,800.00	8,776.54	8,785.26	8,776.94	31.91	31.34	153.99	200.28	27.99	440.28	396.03	44.25	9.950				
8,900.00	8,876.42	8,885.13	8,876.82	32.28	31.69	154.29	200.28	27.99	444.72	399.97	44.75	9.937				
9,000.00	8,976.39	8,985.10	8,976.79	32.63	32.05	154.44	200.28	27.99	446.81	401.56	45.25	9.873				
9,038.62	9,015.00	9,023.72	9,015.40	32.76	32.19	89.96	200.28	27.99	446.99	401.54	45.45	9.835				
9,100.00	9,076.38	9,085.10	9,076.78	32.98	32.40	89.96	200.28	27.99	446.99	401.23	45.76	9.769				
9,200.00	9,176.38	9,185.10	9,176.78	33.32	32.76	89.96	200.28	27.99	446.99	400.73	46.26	9.663				
9,300.00	9,276.38	9,285.10	9,276.78	33.67	33.12	89.96	200.28	27.99	446.99	400.23	46.76	9.560				
9,400.00	9,376.38	9,385.10	9,376.78	34.02	33.47	89.96	200.28	27.99	446.99	399.73	47.26	9.458				
9,500.00	9,476.38	9,485.10	9,476.78	34.37	33.83	89.96	200.28	27.99	446.99	399.23	47.76	9.359				
9,600.00	9,576.38	9,585.10	9,576.78	34.71	34.19	89.96	200.28	27.99	446.99	398.73	48.26	9.262				
9,700.00	9,676.38	9,685.10	9,676.78	35.06	34.55	89.96	200.28	27.99	446.99	398.23	48.76	9.166				
9,800.00	9,776.38	9,785.10	9,776.78	35.41	34.90	89.96	200.28	27.99	446.99	397.72	49.27	9.073				
9,900.00	9,876.38	9,885.10	9,876.78	35.76	35.26	89.96	200.28	27.99	446.99	397.22	49.77	8.981				
10,000.00	9,976.38	9,985.10	9,976.78	36.11	35.62	89.96	200.28	27.99	446.99	396.72	50.27	8.892				
10,100.00	10,076.38	10,085.10	10,076.78	36.46	35.97	89.96	200.28	27.99	446.99	396.22	50.77	8.804				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Mission/Vested Fed Com - Mission Fed Com 705H - OH - Plan #1		Offset Site Error:		0.00 usft	
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:		0.00 usft			
Reference		Offset		Semi Major Axis			Distance											
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning					
10,200.00	10,176.38	10,185.10	10,176.78	36.81	36.33	89.96	200.28	27.99	446.99	395.72	51.27	8.718						
10,300.00	10,276.38	10,285.10	10,276.78	37.16	36.69	89.96	200.28	27.99	446.99	395.21	51.78	8.633						
10,400.00	10,376.38	10,385.10	10,376.78	37.51	37.04	89.96	200.28	27.99	446.99	394.71	52.28	8.550						
10,500.00	10,476.38	10,485.10	10,476.78	37.86	37.40	89.96	200.28	27.99	446.99	394.21	52.78	8.469						
10,600.00	10,576.38	10,585.10	10,576.78	38.20	37.76	89.96	200.28	27.99	446.99	393.71	53.28	8.389						
10,700.00	10,676.38	10,685.10	10,676.78	38.55	38.12	89.96	200.28	27.99	446.99	393.20	53.79	8.310						
10,800.00	10,776.38	10,785.10	10,776.78	38.90	38.47	89.96	200.28	27.99	446.99	392.70	54.29	8.233						
10,900.00	10,876.38	10,885.10	10,876.78	39.26	38.83	89.96	200.28	27.99	446.99	392.20	54.79	8.158						
11,000.00	10,976.38	10,985.10	10,976.78	39.61	39.19	89.96	200.28	27.99	446.99	391.69	55.30	8.084						
11,100.00	11,076.38	11,085.10	11,076.78	39.96	39.54	89.96	200.28	27.99	446.99	391.19	55.80	8.011						
11,111.62	11,088.00	11,096.72	11,088.40	40.00	39.59	89.96	200.28	27.99	446.99	391.13	55.86	8.002						
11,150.00	11,126.36	11,135.07	11,126.76	40.12	39.72	-89.66	200.28	27.99	446.98	390.93	56.05	7.975						
11,178.56	11,154.79	11,163.51	11,155.19	40.21	39.82	-90.00	200.28	27.99	446.97	390.79	56.18	7.956						
11,200.00	11,176.03	11,184.75	11,176.43	40.28	39.90	-90.36	200.28	27.99	446.98	390.70	56.28	7.941						
11,250.00	11,225.04	11,233.76	11,225.44	40.43	40.08	-91.58	200.28	27.99	447.15	390.63	56.52	7.911						
11,300.00	11,273.01	11,281.73	11,273.41	40.57	40.25	-93.24	200.28	27.99	447.77	391.02	56.75	7.890						
11,350.00	11,319.57	11,328.88	11,320.56	40.70	40.41	-95.28	200.23	27.99	449.22	392.25	56.98	7.884						
11,400.00	11,364.36	11,379.75	11,371.33	40.81	40.58	-97.56	197.30	28.02	451.60	394.40	57.20	7.896						
11,450.00	11,407.05	11,432.68	11,423.66	40.92	40.74	-99.83	189.49	28.09	454.78	397.39	57.39	7.924						
11,500.00	11,447.32	11,487.90	11,477.25	41.02	40.89	-102.05	176.23	28.22	458.69	401.14	57.55	7.970						
11,550.00	11,484.85	11,545.66	11,531.65	41.10	41.05	-104.21	156.92	28.40	463.22	405.58	57.64	8.037						
11,600.00	11,519.36	11,606.16	11,586.25	41.17	41.20	-106.30	130.93	28.64	468.22	410.58	57.63	8.124						
11,650.00	11,550.58	11,669.63	11,640.25	41.24	41.36	-108.29	97.63	28.96	473.51	415.99	57.52	8.232						
11,700.00	11,578.29	11,736.22	11,692.58	41.29	41.51	-110.16	56.52	29.34	478.89	421.61	57.29	8.360						
11,750.00	11,602.26	11,806.01	11,741.91	41.34	41.66	-111.87	7.22	29.81	484.13	427.19	56.94	8.502						
11,800.00	11,622.32	11,878.96	11,786.68	41.40	41.82	-113.37	-50.32	30.35	488.99	432.46	56.53	8.650						
11,850.00	11,638.32	11,954.89	11,825.12	41.48	41.99	-114.65	-115.73	30.97	493.23	437.12	56.11	8.790						
11,900.00	11,650.12	12,033.41	11,855.42	41.58	42.17	-115.64	-188.10	31.65	496.62	440.85	55.77	8.905						
11,950.00	11,657.65	12,113.95	11,875.93	41.71	42.36	-116.32	-265.91	32.38	498.96	443.38	55.58	8.977						
12,002.83	11,660.89	12,200.40	11,885.58	41.85	42.57	-116.66	-351.74	33.19	500.15	444.52	55.63	8.990						
12,100.00	11,662.38	12,301.86	11,887.45	42.14	42.85	-116.69	-453.18	34.15	500.27	444.27	56.00	8.934						
12,200.00	11,663.91	12,401.86	11,889.19	42.50	43.19	-116.71	-553.16	35.09	500.36	443.92	56.44	8.865						
12,300.00	11,665.45	12,501.86	11,890.93	42.92	43.58	-116.73	-653.14	36.03	500.46	443.50	56.96	8.786						
12,400.00	11,666.98	12,601.86	11,892.67	43.40	44.04	-116.75	-753.12	36.97	500.55	442.99	57.55	8.697						
12,500.00	11,668.52	12,701.86	11,894.41	43.93	44.55	-116.77	-853.10	37.92	500.64	442.42	58.22	8.599						
12,600.00	11,670.05	12,801.86	11,896.14	44.52	45.12	-116.79	-953.08	38.86	500.73	441.78	58.95	8.494						
12,700.00	11,671.58	12,901.86	11,897.88	45.16	45.74	-116.82	-1,053.06	39.80	500.83	441.08	59.75	8.382						
12,800.00	11,673.12	13,001.86	11,899.62	45.84	46.41	-116.84	-1,153.04	40.74	500.92	440.31	60.61	8.265						
12,900.00	11,674.65	13,101.86	11,901.36	46.58	47.13	-116.86	-1,253.02	41.69	501.01	439.48	61.53	8.143						
13,000.00	11,676.18	13,201.86	11,903.10	47.36	47.89	-116.88	-1,353.00	42.63	501.10	438.60	62.51	8.017						
13,100.00	11,677.72	13,301.86	11,904.84	48.19	48.70	-116.90	-1,452.98	43.57	501.20	437.66	63.54	7.888						
13,200.00	11,679.25	13,401.86	11,906.58	49.05	49.55	-116.92	-1,552.96	44.51	501.29	436.67	64.62	7.757						
13,300.00	11,680.78	13,501.86	11,908.32	49.96	50.45	-116.94	-1,652.94	45.45	501.38	435.63	65.75	7.625						
13,400.00	11,682.32	13,601.86	11,910.06	50.90	51.37	-116.96	-1,752.92	46.40	501.48	434.54	66.93	7.492						
13,500.00	11,683.85	13,701.86	11,911.80	51.88	52.34	-116.98	-1,852.90	47.34	501.57	433.41	68.16	7.359						
13,600.00	11,685.38	13,801.86	11,913.54	52.89	53.34	-117.01	-1,952.88	48.28	501.66	432.24	69.42	7.227						
13,700.00	11,686.92	13,901.86	11,915.28	53.93	54.37	-117.03	-2,052.86	49.22	501.76	431.03	70.72	7.095						
13,800.00	11,688.45	14,001.86	11,917.02	55.01	55.43	-117.05	-2,152.84	50.17	501.85	429.79	72.06	6.964						
13,900.00	11,689.98	14,101.86	11,918.76	56.11	56.52	-117.07	-2,252.82	51.11	501.94	428.51	73.43	6.835						
14,000.00	11,691.52	14,201.86	11,920.50	57.23	57.63	-117.09	-2,352.80	52.05	502.04	427.20	74.84	6.708						
14,100.00	11,693.05	14,301.86	11,922.24	58.39	58.77	-117.11	-2,452.79	52.99	502.13	425.86	76.27	6.583						
14,200.00	11,694.59	14,401.86	11,923.98	59.56	59.94	-117.13	-2,552.77	53.93	502.22	424.49	77.74	6.460						

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,300.00	11,696.12	14,501.86	11,925.72	60.76	61.12	-117.15	-2,652.75	54.88	502.32	423.09	79.23	6.340		
14,400.00	11,697.65	14,601.86	11,927.46	61.98	62.33	-117.17	-2,752.73	55.82	502.41	421.67	80.75	6.222		
14,500.00	11,699.19	14,701.86	11,929.20	63.22	63.56	-117.19	-2,852.71	56.76	502.51	420.22	82.28	6.107		
14,600.00	11,700.72	14,801.86	11,930.94	64.47	64.81	-117.22	-2,952.69	57.70	502.60	418.75	83.84	5.994		
14,700.00	11,702.25	14,901.86	11,932.68	65.75	66.07	-117.24	-3,052.67	58.65	502.69	417.27	85.43	5.885		
14,800.00	11,703.79	15,001.86	11,934.42	67.04	67.35	-117.26	-3,152.65	59.59	502.79	415.76	87.03	5.777		
14,900.00	11,705.32	15,101.86	11,936.16	68.35	68.65	-117.28	-3,252.63	60.53	502.88	414.23	88.65	5.673		
15,000.00	11,706.85	15,201.86	11,937.90	69.67	69.96	-117.30	-3,352.61	61.47	502.98	412.69	90.28	5.571		
15,100.00	11,708.39	15,301.86	11,939.64	71.00	71.29	-117.32	-3,452.59	62.41	503.07	411.14	91.93	5.472		
15,200.00	11,709.92	15,401.86	11,941.38	72.35	72.63	-117.34	-3,552.57	63.36	503.16	409.56	93.60	5.376		
15,300.00	11,711.45	15,501.86	11,943.12	73.71	73.98	-117.36	-3,652.55	64.30	503.26	407.98	95.28	5.282		
15,400.00	11,712.99	15,601.86	11,944.86	75.08	75.35	-117.38	-3,752.53	65.24	503.35	406.38	96.97	5.191		
15,500.00	11,714.52	15,701.86	11,946.60	76.47	76.72	-117.40	-3,852.51	66.18	503.45	404.77	98.68	5.102		
15,600.00	11,716.06	15,801.86	11,948.34	77.86	78.11	-117.42	-3,952.49	67.12	503.54	403.15	100.40	5.016		
15,700.00	11,717.59	15,901.86	11,950.08	79.26	79.51	-117.44	-4,052.47	68.07	503.64	401.51	102.12	4.932		
15,800.00	11,719.12	16,001.86	11,951.82	80.68	80.92	-117.47	-4,152.45	69.01	503.73	399.87	103.86	4.850		
15,900.00	11,720.66	16,101.86	11,953.56	82.10	82.33	-117.49	-4,252.43	69.95	503.83	398.22	105.61	4.771		
16,000.00	11,722.19	16,201.86	11,955.30	83.53	83.76	-117.51	-4,352.41	70.89	503.92	396.56	107.36	4.694		
16,100.00	11,723.72	16,301.85	11,957.04	84.97	85.19	-117.53	-4,452.39	71.84	504.02	394.89	109.13	4.619		
16,200.00	11,725.26	16,401.85	11,958.78	86.41	86.63	-117.55	-4,552.37	72.78	504.11	393.21	110.90	4.546		
16,300.00	11,726.79	16,501.85	11,960.52	87.87	88.08	-117.57	-4,652.35	73.72	504.21	391.53	112.67	4.475		
16,400.00	11,728.32	16,601.85	11,962.26	89.33	89.53	-117.59	-4,752.33	74.66	504.30	389.84	114.46	4.406		
16,500.00	11,729.86	16,701.85	11,964.00	90.79	90.99	-117.61	-4,852.31	75.60	504.40	388.15	116.25	4.339		
16,600.00	11,731.39	16,801.85	11,965.74	92.27	92.46	-117.63	-4,952.29	76.55	504.49	386.45	118.04	4.274		
16,700.00	11,732.92	16,901.85	11,967.48	93.75	93.94	-117.65	-5,052.27	77.49	504.59	384.74	119.85	4.210		
16,800.00	11,734.46	17,001.85	11,969.22	95.23	95.42	-117.67	-5,152.25	78.43	504.68	383.03	121.65	4.149		
16,900.00	11,735.99	17,101.85	11,970.96	96.72	96.90	-117.69	-5,252.23	79.37	504.78	381.32	123.46	4.089		
17,000.00	11,737.52	17,201.85	11,972.70	98.22	98.39	-117.72	-5,352.21	80.32	504.87	379.60	125.28	4.030		
17,100.00	11,739.06	17,301.85	11,974.43	99.72	99.89	-117.74	-5,452.19	81.26	504.97	377.87	127.09	3.973		
17,200.00	11,740.59	17,401.85	11,976.17	101.22	101.39	-117.76	-5,552.17	82.20	505.06	376.15	128.92	3.918		
17,300.00	11,742.13	17,501.85	11,977.91	102.73	102.89	-117.78	-5,652.15	83.14	505.16	374.42	130.74	3.864		
17,400.00	11,743.66	17,601.85	11,979.65	104.25	104.40	-117.80	-5,752.13	84.08	505.26	372.69	132.57	3.811		
17,500.00	11,745.19	17,701.85	11,981.39	105.77	105.92	-117.82	-5,852.11	85.03	505.35	370.95	134.40	3.760		
17,600.00	11,746.73	17,801.85	11,983.13	107.29	107.44	-117.84	-5,952.09	85.97	505.45	369.22	136.23	3.710		
17,700.00	11,748.26	17,901.85	11,984.87	108.81	108.96	-117.86	-6,052.07	86.91	505.54	367.48	138.07	3.662		
17,800.00	11,749.79	18,001.85	11,986.61	110.34	110.49	-117.88	-6,152.05	87.85	505.64	365.74	139.90	3.614		
17,900.00	11,751.33	18,101.85	11,988.35	111.88	112.02	-117.90	-6,252.03	88.80	505.73	363.99	141.74	3.568		
18,000.00	11,752.86	18,201.85	11,990.09	113.41	113.55	-117.92	-6,352.01	89.74	505.83	362.25	143.58	3.523		
18,100.00	11,754.39	18,301.85	11,991.83	114.95	115.08	-117.94	-6,451.99	90.68	505.93	360.51	145.42	3.479		
18,200.00	11,755.93	18,401.85	11,993.57	116.49	116.62	-117.96	-6,551.97	91.62	506.02	358.76	147.26	3.436		
18,300.00	11,757.46	18,501.85	11,995.31	118.04	118.17	-117.98	-6,651.95	92.56	506.12	357.02	149.10	3.394		
18,400.00	11,758.99	18,601.85	11,997.05	119.59	119.71	-118.00	-6,751.93	93.51	506.22	355.27	150.95	3.354		
18,500.00	11,760.53	18,701.85	11,998.79	121.14	121.26	-118.03	-6,851.91	94.45	506.31	353.52	152.79	3.314		
18,600.00	11,762.06	18,801.85	12,000.53	122.69	122.81	-118.05	-6,951.89	95.39	506.41	351.77	154.64	3.275		
18,700.00	11,763.60	18,901.85	12,002.27	124.25	124.37	-118.07	-7,051.88	96.33	506.51	350.02	156.48	3.237		
18,800.00	11,765.13	19,001.85	12,004.01	125.81	125.92	-118.09	-7,151.86	97.27	506.60	348.28	158.33	3.200		
18,900.00	11,766.66	19,101.85	12,005.75	127.37	127.48	-118.11	-7,251.84	98.22	506.70	346.53	160.17	3.164		
19,000.00	11,768.20	19,201.85	12,007.49	128.93	129.04	-118.13	-7,351.82	99.16	506.80	344.78	162.01	3.128		
19,100.00	11,769.73	19,301.85	12,009.23	130.50	130.60	-118.15	-7,451.80	100.10	506.89	343.04	163.86	3.093		
19,200.00	11,771.26	19,401.85	12,010.97	132.07	132.17	-118.17	-7,551.78	101.04	506.99	341.29	165.70	3.060		
19,300.00	11,772.80	19,501.85	12,012.71	133.64	133.74	-118.19	-7,651.76	101.99	507.09	339.54	167.54	3.027		
19,400.00	11,774.33	19,601.85	12,014.45	135.21	135.31	-118.21	-7,751.74	102.93	507.18	337.80	169.39	2.994		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Mission/Vested Fed Com - Mission Fed Com 705H - OH - Plan #1		Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD															Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance							Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor				
19,500.00	11,775.86	19,701.85	12,016.19	136.78	136.88	-118.23	-7,851.72	103.87	507.28	336.05	171.23	2.963				
19,600.00	11,777.40	19,801.85	12,017.93	138.36	138.45	-118.25	-7,951.70	104.81	507.38	334.31	173.07	2.932				
19,700.00	11,778.93	19,901.85	12,019.67	139.94	140.03	-118.27	-8,051.68	105.75	507.48	332.57	174.91	2.901				
19,800.00	11,780.46	20,001.85	12,021.41	141.52	141.60	-118.29	-8,151.66	106.70	507.57	330.83	176.75	2.872				
19,900.00	11,782.00	20,101.85	12,023.15	143.10	143.18	-118.31	-8,251.64	107.64	507.67	329.09	178.58	2.843				
20,000.00	11,783.53	20,201.85	12,024.89	144.68	144.76	-118.33	-8,351.62	108.58	507.77	327.35	180.42	2.814				
20,100.00	11,785.07	20,301.85	12,026.63	146.26	146.34	-118.35	-8,451.60	109.52	507.87	325.61	182.25	2.787				
20,200.00	11,786.60	20,401.85	12,028.37	147.85	147.93	-118.38	-8,551.58	110.47	507.96	323.88	184.09	2.759				
20,300.00	11,788.13	20,501.85	12,030.11	149.44	149.51	-118.40	-8,651.56	111.41	508.06	322.14	185.92	2.733				
20,400.00	11,789.67	20,601.85	12,031.85	151.02	151.10	-118.42	-8,751.54	112.35	508.16	320.41	187.75	2.707				
20,500.00	11,791.20	20,701.85	12,033.59	152.61	152.69	-118.44	-8,851.52	113.29	508.26	318.68	189.57	2.681				
20,600.00	11,792.73	20,801.85	12,035.33	154.20	154.28	-118.46	-8,951.50	114.23	508.35	316.96	191.40	2.656				
20,700.00	11,794.27	20,901.85	12,037.07	155.80	155.87	-118.48	-9,051.48	115.18	508.45	315.23	193.22	2.631				
20,800.00	11,795.80	21,001.85	12,038.81	157.39	157.46	-118.50	-9,151.46	116.12	508.55	313.50	195.05	2.607				
20,900.00	11,797.33	21,101.84	12,040.55	158.98	159.05	-118.52	-9,251.44	117.06	508.65	311.78	196.86	2.584				
21,000.00	11,798.87	21,201.84	12,042.29	160.58	160.65	-118.54	-9,351.42	118.00	508.75	310.06	198.68	2.561				
21,100.00	11,800.40	21,301.84	12,044.03	162.18	162.24	-118.56	-9,451.40	118.95	508.84	308.35	200.50	2.538				
21,200.00	11,801.93	21,401.84	12,045.77	163.78	163.84	-118.58	-9,551.38	119.89	508.94	306.63	202.31	2.516				
21,300.00	11,803.47	21,501.84	12,047.51	165.37	165.43	-118.60	-9,651.36	120.83	509.04	304.92	204.12	2.494				
21,400.00	11,805.00	21,601.84	12,049.25	166.98	167.03	-118.62	-9,751.34	121.77	509.14	303.21	205.93	2.472				
21,500.00	11,806.53	21,701.84	12,050.99	168.58	168.63	-118.64	-9,851.32	122.71	509.24	301.50	207.74	2.451				
21,600.00	11,808.07	21,801.84	12,052.72	170.18	170.23	-118.66	-9,951.30	123.66	509.34	299.80	209.54	2.431				
21,700.00	11,809.60	21,901.84	12,054.46	171.78	171.84	-118.68	-10,051.28	124.60	509.43	298.09	211.34	2.410				
21,800.00	11,811.14	22,001.84	12,056.20	173.39	173.44	-118.70	-10,151.26	125.54	509.53	296.39	213.14	2.391				
21,813.35	11,811.34	22,015.19	12,056.44	173.60	173.65	-118.70	-10,164.61	125.67	509.55	296.17	213.38	2.388				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Mission/Vested Fed Com - Vested Fed Com 604H - OH - Plan #1		Offset Site Error: 0.00 usft	
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error: 0.00 usft			
Reference		Offset		Semi Major Axis			Distance						Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor				
0.00	0.00	1.00	1.00	0.00	0.00	89.54	0.84	104.98	104.98							
100.00	100.00	101.00	101.00	0.13	0.13	89.54	0.84	104.98	104.98	104.80	0.18	583.282				
200.00	200.00	201.00	201.00	0.48	0.49	89.54	0.84	104.98	104.98	104.30	0.69	152.830				
300.00	300.00	301.00	301.00	0.84	0.85	89.54	0.84	104.98	104.98	103.79	1.19	87.934				
400.00	400.00	401.00	401.00	1.20	1.20	89.54	0.84	104.98	104.98	103.28	1.70	61.725				
500.00	500.00	501.00	501.00	1.56	1.56	89.54	0.84	104.98	104.98	102.78	2.21	47.551				
600.00	600.00	601.00	601.00	1.92	1.92	89.54	0.84	104.98	104.98	102.27	2.71	38.672				
700.00	700.00	701.00	701.00	2.28	2.28	89.54	0.84	104.98	104.98	101.76	3.22	32.586				
800.00	800.00	801.00	801.00	2.63	2.64	89.54	0.84	104.98	104.98	101.25	3.73	28.156				
900.00	900.00	901.00	901.00	2.99	3.00	89.54	0.84	104.98	104.98	100.75	4.24	24.786				
1,000.00	1,000.00	1,001.00	1,001.00	3.35	3.36	89.54	0.84	104.98	104.98	100.24	4.74	22.136				
1,100.00	1,100.00	1,101.00	1,101.00	3.71	3.71	89.54	0.84	104.98	104.98	99.73	5.25	19.999				
1,200.00	1,200.00	1,201.00	1,201.00	4.07	4.07	89.54	0.84	104.98	104.98	99.23	5.76	18.237				
1,300.00	1,300.00	1,301.00	1,301.00	4.43	4.43	89.54	0.84	104.98	104.98	98.72	6.26	16.761				
1,400.00	1,400.00	1,401.00	1,401.00	4.79	4.79	89.54	0.84	104.98	104.98	98.21	6.77	15.506				
1,500.00	1,500.00	1,501.00	1,501.00	5.14	5.15	89.54	0.84	104.98	104.98	97.71	7.28	14.426				
1,600.00	1,600.00	1,601.00	1,601.00	5.50	5.51	89.54	0.84	104.98	104.98	97.20	7.78	13.487				
1,700.00	1,700.00	1,701.00	1,701.00	5.86	5.86	89.54	0.84	104.98	104.98	96.69	8.29	12.662				
1,800.00	1,800.00	1,801.00	1,801.00	6.22	6.22	89.54	0.84	104.98	104.98	96.19	8.80	11.932				
1,900.00	1,900.00	1,901.00	1,901.00	6.58	6.58	89.54	0.84	104.98	104.98	95.68	9.31	11.282				
2,000.00	2,000.00	2,001.00	2,001.00	6.94	6.94	89.54	0.84	104.98	104.98	95.17	9.81	10.699				
2,100.00	2,100.00	2,101.00	2,101.00	7.29	7.30	89.54	0.84	104.98	104.98	94.66	10.32	10.174				
2,200.00	2,200.00	2,201.00	2,201.00	7.65	7.66	89.54	0.84	104.98	104.98	94.16	10.83	9.697				
2,300.00	2,300.00	2,301.00	2,301.00	8.01	8.02	89.54	0.84	104.98	104.98	93.65	11.33	9.264				
2,400.00	2,400.00	2,401.00	2,401.00	8.37	8.37	89.54	0.84	104.98	104.98	93.14	11.84	8.867				
2,500.00	2,500.00	2,501.00	2,501.00	8.73	8.73	89.54	0.84	104.98	104.98	92.64	12.35	8.503				
2,600.00	2,600.00	2,601.00	2,601.00	9.09	9.09	89.54	0.84	104.98	104.98	92.13	12.85	8.167				
2,700.00	2,700.00	2,701.00	2,701.00	9.45	9.45	89.54	0.84	104.98	104.98	91.62	13.36	7.858				
2,800.00	2,800.00	2,801.00	2,801.00	9.80	9.81	89.54	0.84	104.98	104.98	91.12	13.87	7.570				
2,900.00	2,900.00	2,901.00	2,901.00	10.16	10.17	89.54	0.84	104.98	104.98	90.61	14.37	7.303				
3,000.00	3,000.00	3,001.00	3,001.00	10.52	10.52	89.54	0.84	104.98	104.98	90.10	14.88	7.055				
3,100.00	3,100.00	3,101.00	3,101.00	10.88	10.88	89.54	0.84	104.98	104.98	89.59	15.39	6.822				
3,200.00	3,200.00	3,201.00	3,201.00	11.24	11.24	89.54	0.84	104.98	104.98	89.09	15.90	6.605				
3,300.00	3,300.00	3,301.00	3,301.00	11.60	11.60	89.54	0.84	104.98	104.98	88.58	16.40	6.400				
3,400.00	3,400.00	3,401.00	3,401.00	11.96	11.96	89.54	0.84	104.98	104.98	88.07	16.91	6.209				
3,500.00	3,500.00	3,501.00	3,501.00	12.31	12.32	89.54	0.84	104.98	104.98	87.57	17.42	6.028				
3,600.00	3,600.00	3,601.00	3,601.00	12.67	12.68	89.54	0.84	104.98	104.98	87.06	17.92	5.857				
3,700.00	3,700.00	3,701.00	3,701.00	13.03	13.03	89.54	0.84	104.98	104.98	86.55	18.43	5.696				
3,800.00	3,800.00	3,801.00	3,801.00	13.39	13.39	89.54	0.84	104.98	104.98	86.05	18.94	5.544				
3,900.00	3,900.00	3,901.00	3,901.00	13.75	13.75	89.54	0.84	104.98	104.98	85.54	19.44	5.399				
4,000.00	4,000.00	4,001.00	4,001.00	14.11	14.11	89.54	0.84	104.98	104.98	85.03	19.95	5.262				
4,100.00	4,100.00	4,101.00	4,101.00	14.46	14.47	89.54	0.84	104.98	104.98	84.53	20.46	5.132				
4,116.33	4,116.33	4,117.33	4,117.33	14.52	14.53	89.54	0.84	104.98	104.98	84.44	20.54	5.111 CC				
4,200.00	4,200.00	4,200.00	4,200.00	14.82	14.82	89.54	0.84	104.98	104.99	84.03	20.96	5.009 ES, SF				
4,300.00	4,299.99	4,298.29	4,298.28	15.18	15.17	154.18	1.09	106.22	107.44	85.99	21.45	5.009				
4,400.00	4,399.91	4,395.25	4,395.17	15.53	15.50	154.60	1.83	109.87	114.74	92.83	21.91	5.237				
4,500.00	4,499.69	4,491.53	4,491.24	15.88	15.84	155.19	3.05	115.88	126.87	104.51	22.36	5.675				
4,600.27	4,599.54	4,587.03	4,586.37	16.23	16.17	155.84	4.74	124.18	143.85	121.06	22.79	6.312				
4,700.00	4,698.72	4,680.95	4,679.68	16.58	16.50	156.41	6.86	134.61	164.30	141.10	23.20	7.081				
4,800.00	4,798.17	4,774.14	4,771.98	16.94	16.83	156.69	9.41	147.19	187.14	163.53	23.61	7.928				
4,900.00	4,897.62	4,868.03	4,864.66	17.30	17.17	156.76	12.40	161.93	212.12	188.09	24.03	8.828				
5,000.00	4,997.08	4,964.74	4,960.04	17.66	17.52	156.79	15.58	177.58	237.56	213.06	24.51	9.693				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
5,100.00	5,096.53	5,061.45	5,055.42	18.02	17.87	156.81	18.76	193.22	263.01	238.02	24.99	10.525		
5,200.00	5,195.98	5,158.16	5,150.80	18.38	18.23	156.83	21.93	208.87	288.46	262.99	25.47	11.324		
5,300.00	5,295.43	5,254.86	5,246.18	18.74	18.59	156.84	25.11	224.51	313.91	287.95	25.96	12.094		
5,400.00	5,394.88	5,351.57	5,341.56	19.11	18.95	156.86	28.29	240.16	339.35	312.91	26.44	12.834		
5,500.00	5,494.33	5,448.28	5,436.94	19.47	19.32	156.87	31.46	255.80	364.80	337.87	26.93	13.547		
5,600.00	5,593.78	5,544.99	5,532.33	19.84	19.69	156.88	34.64	271.45	390.25	362.83	27.41	14.235		
5,700.00	5,693.24	5,641.69	5,627.71	20.21	20.06	156.89	37.82	287.09	415.70	387.79	27.90	14.898		
5,800.00	5,792.69	5,738.40	5,723.09	20.57	20.43	156.90	40.99	302.74	441.14	412.75	28.39	15.538		
5,900.00	5,892.14	5,835.11	5,818.47	20.94	20.81	156.90	44.17	318.38	466.59	437.71	28.88	16.155		
6,000.00	5,991.59	5,931.82	5,913.85	21.32	21.19	156.91	47.35	334.03	492.04	462.67	29.37	16.752		
6,100.00	6,091.04	6,028.53	6,009.23	21.69	21.56	156.92	50.52	349.67	517.49	487.62	29.86	17.329		
6,200.00	6,190.49	6,125.23	6,104.61	22.06	21.95	156.92	53.70	365.32	542.93	512.58	30.36	17.886		
6,300.00	6,289.94	6,221.94	6,199.99	22.43	22.33	156.92	56.88	380.96	568.38	537.53	30.85	18.425		
6,400.00	6,389.40	6,318.65	6,295.37	22.81	22.71	156.93	60.05	396.61	593.83	562.49	31.34	18.946		
6,500.00	6,488.85	6,415.36	6,390.76	23.18	23.10	156.93	63.23	412.25	619.28	587.44	31.84	19.451		
6,600.00	6,588.30	6,512.07	6,486.14	23.56	23.49	156.94	66.41	427.90	644.72	612.39	32.33	19.940		
6,700.00	6,687.75	6,608.77	6,581.52	23.93	23.88	156.94	69.58	443.54	670.17	637.34	32.83	20.415		
6,800.00	6,787.20	6,705.48	6,676.90	24.31	24.27	156.94	72.76	459.19	695.62	662.29	33.32	20.874		
6,900.00	6,886.65	6,802.19	6,772.28	24.68	24.66	156.95	75.94	474.83	721.07	687.25	33.82	21.320		
7,000.00	6,986.10	6,898.90	6,867.66	25.06	25.06	156.95	79.11	490.48	746.51	712.20	34.32	21.752		
7,100.00	7,085.56	6,995.61	6,963.04	25.44	25.45	156.95	82.29	506.12	771.96	737.15	34.82	22.172		
7,200.00	7,185.01	7,092.31	7,058.42	25.82	25.85	156.95	85.47	521.77	797.41	762.09	35.32	22.579		
7,300.00	7,284.46	7,189.02	7,153.80	26.20	26.24	156.96	88.64	537.41	822.86	787.04	35.81	22.975		
7,400.00	7,383.91	7,285.73	7,249.19	26.58	26.64	156.96	91.82	553.06	848.30	811.99	36.31	23.360		
7,500.00	7,483.36	7,382.44	7,344.57	26.96	27.04	156.96	95.00	568.70	873.75	836.94	36.82	23.734		
7,600.00	7,582.81	7,479.14	7,439.95	27.34	27.44	156.96	98.17	584.35	899.20	861.88	37.32	24.097		
7,700.00	7,682.26	7,575.85	7,535.33	27.72	27.84	156.96	101.35	599.99	924.65	886.83	37.82	24.450		
7,800.00	7,781.72	7,672.56	7,630.71	28.10	28.24	156.96	104.53	615.64	950.10	911.78	38.32	24.794		
7,900.00	7,881.17	7,769.27	7,726.09	28.48	28.65	156.97	107.70	631.28	975.54	936.72	38.82	25.129		
8,000.00	7,980.62	7,865.98	7,821.47	28.86	29.05	156.97	110.88	646.93	1,000.99	961.67	39.32	25.455		
8,100.00	8,080.07	7,962.68	7,916.85	29.24	29.45	156.97	114.06	662.57	1,026.44	986.61	39.83	25.773		
8,200.00	8,179.52	8,059.39	8,012.23	29.62	29.86	156.97	117.23	678.22	1,051.89	1,011.56	40.33	26.082		
8,300.00	8,278.97	8,156.10	8,107.62	30.01	30.26	156.97	120.41	693.87	1,077.33	1,036.50	40.83	26.383		
8,400.00	8,378.42	8,252.81	8,203.00	30.39	30.67	156.97	123.59	709.51	1,102.78	1,061.44	41.34	26.677		
8,500.00	8,477.88	8,349.52	8,298.38	30.77	31.08	156.97	126.76	725.16	1,128.23	1,086.39	41.84	26.963		
8,600.00	8,577.33	8,446.22	8,393.76	31.16	31.49	156.98	129.94	740.80	1,153.68	1,111.33	42.35	27.243		
8,638.34	8,615.46	8,483.31	8,430.33	31.30	31.64	156.98	131.16	746.80	1,163.43	1,120.89	42.54	27.348		
8,700.00	8,676.83	8,543.05	8,489.25	31.54	31.89	157.06	133.12	756.46	1,178.68	1,135.83	42.85	27.505		
8,800.00	8,776.54	8,640.39	8,585.27	31.91	32.31	157.14	136.32	772.21	1,201.52	1,158.16	43.36	27.711		
8,900.00	8,876.42	8,738.25	8,681.78	32.28	32.72	157.16	139.53	788.04	1,222.00	1,178.13	43.86	27.858		
9,000.00	8,976.39	8,836.54	8,778.72	32.63	33.14	157.12	142.76	803.94	1,240.12	1,195.75	44.37	27.949		
9,038.62	9,015.00	8,874.60	8,816.26	32.76	33.30	92.61	144.01	810.10	1,246.48	1,201.92	44.57	27.970		
9,100.00	9,076.38	8,935.14	8,875.97	32.98	33.55	92.50	146.00	819.90	1,256.32	1,211.45	44.88	27.996		
9,200.00	9,176.38	9,033.77	8,973.25	33.32	33.97	92.32	149.24	835.85	1,272.36	1,226.98	45.38	28.037		
9,300.00	9,276.38	9,132.40	9,070.52	33.67	34.39	92.14	152.48	851.81	1,288.41	1,242.52	45.89	28.078		
9,400.00	9,376.38	9,231.03	9,167.80	34.02	34.81	91.97	155.72	867.76	1,304.47	1,258.08	46.39	28.118		
9,500.00	9,476.38	9,329.66	9,265.07	34.37	35.23	91.80	158.96	883.72	1,320.55	1,273.65	46.90	28.157		
9,600.00	9,576.38	9,428.28	9,362.34	34.71	35.65	91.64	162.20	899.68	1,336.63	1,289.22	47.41	28.195		
9,700.00	9,676.38	9,526.91	9,459.62	35.06	36.08	91.48	165.44	915.63	1,352.72	1,304.81	47.91	28.233		
9,800.00	9,776.38	9,625.54	9,556.89	35.41	36.50	91.33	168.68	931.59	1,368.82	1,320.40	48.42	28.270		
9,900.00	9,876.38	9,724.17	9,654.17	35.76	36.92	91.18	171.92	947.54	1,384.94	1,336.01	48.93	28.306		
10,000.00	9,976.38	9,822.80	9,751.44	36.11	37.34	91.03	175.16	963.50	1,401.06	1,351.62	49.43	28.342		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,100.00	10,076.38	9,921.42	9,848.72	36.46	37.77	90.88	178.40	979.45	1,417.19	1,367.25	49.94	28.377		
10,200.00	10,176.38	10,020.05	9,945.99	36.81	38.19	90.74	181.64	995.41	1,433.33	1,382.88	50.45	28.411		
10,300.00	10,276.38	10,118.68	10,043.27	37.16	38.61	90.61	184.88	1,011.37	1,449.48	1,398.52	50.96	28.445		
10,400.00	10,376.38	10,217.31	10,140.54	37.51	39.04	90.47	188.12	1,027.32	1,465.63	1,414.17	51.47	28.478		
10,500.00	10,476.38	10,333.56	10,255.25	37.86	39.53	90.32	191.88	1,045.86	1,481.63	1,429.55	52.08	28.449		
10,600.00	10,576.38	10,493.86	10,414.13	38.20	40.19	90.15	196.10	1,066.64	1,494.59	1,441.68	52.91	28.247		
10,700.00	10,676.38	10,655.69	10,575.28	38.55	40.81	90.04	199.01	1,080.98	1,503.45	1,449.78	53.67	28.011		
10,800.00	10,776.38	10,818.47	10,737.86	38.90	41.39	89.98	200.57	1,088.64	1,508.16	1,453.79	54.37	27.740		
10,900.00	10,876.38	10,958.01	10,877.38	39.26	41.85	89.97	200.84	1,089.98	1,508.98	1,454.03	54.95	27.461		
11,000.00	10,976.38	11,058.01	10,977.38	39.61	42.18	89.97	200.84	1,089.98	1,508.98	1,453.54	55.44	27.216		
11,100.00	11,076.38	11,154.90	11,073.86	39.96	42.47	90.26	193.10	1,090.05	1,509.07	1,453.16	55.92	26.988		
11,111.62	11,088.00	11,165.91	11,084.70	40.00	42.50	90.33	191.19	1,090.07	1,509.10	1,453.13	55.97	26.963		
11,150.00	11,126.36	11,201.96	11,119.91	40.12	42.60	-88.87	183.50	1,090.14	1,509.23	1,453.09	56.14	26.884		
11,200.00	11,176.03	11,248.36	11,164.39	40.28	42.73	-88.54	170.36	1,090.27	1,509.43	1,453.09	56.35	26.789		
11,250.00	11,225.04	11,294.16	11,207.12	40.43	42.84	-88.22	153.90	1,090.43	1,509.68	1,453.13	56.54	26.700		
11,300.00	11,273.01	11,339.41	11,247.92	40.57	42.94	-87.91	134.34	1,090.61	1,509.95	1,453.23	56.73	26.618		
11,350.00	11,319.57	11,384.17	11,286.62	40.70	43.04	-87.62	111.89	1,090.83	1,510.26	1,453.36	56.90	26.542		
11,400.00	11,364.36	11,428.47	11,323.09	40.81	43.12	-87.35	86.76	1,091.06	1,510.58	1,453.51	57.07	26.470		
11,450.00	11,407.05	11,472.36	11,357.20	40.92	43.20	-87.10	59.16	1,091.33	1,510.90	1,453.68	57.22	26.403		
11,500.00	11,447.32	11,515.88	11,388.84	41.02	43.27	-86.86	29.30	1,091.61	1,511.23	1,453.86	57.38	26.339		
11,550.00	11,484.85	11,559.08	11,417.92	41.10	43.33	-86.65	-2.64	1,091.92	1,511.55	1,454.03	57.52	26.278		
11,600.00	11,519.36	11,600.00	11,443.17	41.17	43.39	-86.47	-34.83	1,092.22	1,511.85	1,454.19	57.66	26.220		
11,650.00	11,550.58	11,644.66	11,468.02	41.24	43.44	-86.29	-71.91	1,092.57	1,512.12	1,454.32	57.81	26.159		
11,700.00	11,578.29	11,687.11	11,488.91	41.29	43.49	-86.15	-108.86	1,092.93	1,512.37	1,454.42	57.95	26.098		
11,750.00	11,602.26	11,729.40	11,506.93	41.34	43.54	-86.04	-147.10	1,093.29	1,512.58	1,454.48	58.09	26.037		
11,800.00	11,622.32	11,771.55	11,522.04	41.40	43.58	-85.95	-186.44	1,093.66	1,512.74	1,454.50	58.24	25.973		
11,850.00	11,638.32	11,813.60	11,534.20	41.48	43.64	-85.88	-226.69	1,094.05	1,512.86	1,454.46	58.40	25.906		
11,900.00	11,650.12	11,855.59	11,543.36	41.58	43.70	-85.85	-267.65	1,094.44	1,512.93	1,454.38	58.56	25.837		
11,950.00	11,657.65	11,900.00	11,549.75	41.71	43.77	-85.84	-311.59	1,094.85	1,512.96	1,454.23	58.73	25.763		
12,002.83	11,660.89	11,941.89	11,552.65	41.85	43.84	-85.86	-353.37	1,095.25	1,512.92	1,454.02	58.90	25.685		
12,100.00	11,662.38	12,037.86	11,554.77	42.14	44.05	-85.88	-449.30	1,096.16	1,512.88	1,453.57	59.31	25.510		
12,200.00	11,663.91	12,137.86	11,556.93	42.50	44.34	-85.91	-549.27	1,097.11	1,512.84	1,453.04	59.80	25.297		
12,300.00	11,665.45	12,237.85	11,559.10	42.92	44.70	-85.93	-649.24	1,098.06	1,512.81	1,452.42	60.39	25.051		
12,400.00	11,666.98	12,337.85	11,561.26	43.40	45.12	-85.95	-749.21	1,099.02	1,512.77	1,451.71	61.06	24.777		
12,500.00	11,668.52	12,437.85	11,563.43	43.93	45.60	-85.98	-849.18	1,099.97	1,512.73	1,450.93	61.81	24.476		
12,600.00	11,670.05	12,537.85	11,565.60	44.52	46.15	-86.00	-949.15	1,100.92	1,512.70	1,450.06	62.63	24.152		
12,700.00	11,671.58	12,637.85	11,567.76	45.16	46.75	-86.03	-1,049.12	1,101.87	1,512.66	1,449.13	63.53	23.809		
12,800.00	11,673.12	12,737.84	11,569.93	45.84	47.40	-86.05	-1,149.09	1,102.82	1,512.63	1,448.12	64.51	23.449		
12,900.00	11,674.65	12,837.84	11,572.10	46.58	48.11	-86.07	-1,249.06	1,103.77	1,512.59	1,447.04	65.55	23.075		
13,000.00	11,676.18	12,937.84	11,574.26	47.36	48.86	-86.10	-1,349.03	1,104.72	1,512.56	1,445.90	66.66	22.691		
13,100.00	11,677.72	13,037.84	11,576.43	48.19	49.66	-86.12	-1,449.00	1,105.67	1,512.52	1,444.69	67.83	22.299		
13,200.00	11,679.25	13,137.84	11,578.59	49.05	50.50	-86.15	-1,548.97	1,106.62	1,512.49	1,443.43	69.06	21.902		
13,300.00	11,680.78	13,237.83	11,580.76	49.96	51.38	-86.17	-1,648.94	1,107.57	1,512.45	1,442.11	70.34	21.502		
13,400.00	11,682.32	13,337.83	11,582.93	50.90	52.30	-86.19	-1,748.91	1,108.52	1,512.42	1,440.74	71.68	21.100		
13,500.00	11,683.85	13,437.83	11,585.09	51.88	53.25	-86.22	-1,848.88	1,109.47	1,512.38	1,439.32	73.07	20.699		
13,600.00	11,685.38	13,537.83	11,587.26	52.89	54.24	-86.24	-1,948.85	1,110.42	1,512.35	1,437.85	74.50	20.300		
13,700.00	11,686.92	13,637.83	11,589.43	53.93	55.26	-86.27	-2,048.82	1,111.38	1,512.32	1,436.34	75.98	19.904		
13,800.00	11,688.45	13,737.82	11,591.59	55.01	56.31	-86.29	-2,148.80	1,112.33	1,512.29	1,434.78	77.50	19.513		
13,900.00	11,689.98	13,837.82	11,593.76	56.11	57.39	-86.31	-2,248.77	1,113.28	1,512.25	1,433.19	79.06	19.127		
14,000.00	11,691.52	13,937.82	11,595.92	57.23	58.49	-86.34	-2,348.74	1,114.23	1,512.22	1,431.56	80.66	18.748		
14,100.00	11,693.05	14,037.82	11,598.09	58.39	59.62	-86.36	-2,448.71	1,115.18	1,512.19	1,429.89	82.30	18.375		
14,200.00	11,694.59	14,137.82	11,600.26	59.56	60.78	-86.38	-2,548.68	1,116.13	1,512.16	1,428.19	83.96	18.010		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Mission/Vested Fed Com - Vested Fed Com 604H - OH - Plan #1													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,300.00	11,696.12	14,237.81	11,602.42	60.76	61.96	-86.41	-2,648.65	1,117.08	1,512.12	1,426.46	85.66	17.652		
14,400.00	11,697.65	14,337.81	11,604.59	61.98	63.15	-86.43	-2,748.62	1,118.03	1,512.09	1,424.70	87.39	17.303		
14,500.00	11,699.19	14,437.81	11,606.75	63.22	64.37	-86.46	-2,848.59	1,118.98	1,512.06	1,422.92	89.14	16.962		
14,600.00	11,700.72	14,537.81	11,608.92	64.47	65.61	-86.48	-2,948.56	1,119.93	1,512.03	1,421.11	90.93	16.629		
14,700.00	11,702.25	14,637.81	11,611.09	65.75	66.87	-86.50	-3,048.53	1,120.88	1,512.00	1,419.27	92.73	16.305		
14,800.00	11,703.79	14,737.80	11,613.25	67.04	68.14	-86.53	-3,148.50	1,121.83	1,511.97	1,417.41	94.56	15.989		
14,900.00	11,705.32	14,837.80	11,615.42	68.35	69.43	-86.55	-3,248.47	1,122.78	1,511.94	1,415.53	96.41	15.682		
15,000.00	11,706.85	14,937.80	11,617.59	69.67	70.73	-86.58	-3,348.44	1,123.74	1,511.91	1,413.63	98.28	15.383		
15,100.00	11,708.39	15,037.80	11,619.75	71.00	72.05	-86.60	-3,448.41	1,124.69	1,511.88	1,411.71	100.17	15.092		
15,200.00	11,709.92	15,137.80	11,621.92	72.35	73.38	-86.62	-3,548.38	1,125.64	1,511.85	1,409.77	102.08	14.810		
15,300.00	11,711.45	15,237.79	11,624.08	73.71	74.73	-86.65	-3,648.35	1,126.59	1,511.82	1,407.81	104.01	14.535		
15,400.00	11,712.99	15,337.79	11,626.25	75.08	76.08	-86.67	-3,748.32	1,127.54	1,511.79	1,405.84	105.96	14.268		
15,500.00	11,714.52	15,437.79	11,628.42	76.47	77.45	-86.70	-3,848.29	1,128.49	1,511.77	1,403.85	107.91	14.009		
15,600.00	11,716.06	15,537.79	11,630.58	77.86	78.83	-86.72	-3,948.26	1,129.44	1,511.74	1,401.85	109.89	13.757		
15,700.00	11,717.59	15,637.79	11,632.75	79.26	80.22	-86.74	-4,048.23	1,130.39	1,511.71	1,399.83	111.88	13.512		
15,800.00	11,719.12	15,737.78	11,634.92	80.68	81.62	-86.77	-4,148.20	1,131.34	1,511.68	1,397.81	113.88	13.275		
15,900.00	11,720.66	15,837.78	11,637.08	82.10	83.03	-86.79	-4,248.17	1,132.29	1,511.66	1,395.76	115.89	13.044		
16,000.00	11,722.19	15,937.78	11,639.25	83.53	84.44	-86.82	-4,348.14	1,133.24	1,511.63	1,393.71	117.92	12.819		
16,100.00	11,723.72	16,037.78	11,641.41	84.97	85.87	-86.84	-4,448.11	1,134.19	1,511.60	1,391.65	119.95	12.602		
16,200.00	11,725.26	16,137.78	11,643.58	86.41	87.30	-86.86	-4,548.08	1,135.14	1,511.58	1,389.57	122.00	12.390		
16,300.00	11,726.79	16,237.77	11,645.75	87.87	88.74	-86.89	-4,648.05	1,136.10	1,511.55	1,387.49	124.06	12.184		
16,400.00	11,728.32	16,337.77	11,647.91	89.33	90.19	-86.91	-4,748.02	1,137.05	1,511.52	1,385.40	126.13	11.984		
16,500.00	11,729.86	16,437.77	11,650.08	90.79	91.65	-86.94	-4,847.99	1,138.00	1,511.50	1,383.29	128.20	11.790		
16,600.00	11,731.39	16,537.77	11,652.25	92.27	93.11	-86.96	-4,947.96	1,138.95	1,511.47	1,381.18	130.29	11.601		
16,700.00	11,732.92	16,637.77	11,654.41	93.75	94.58	-86.98	-5,047.93	1,139.90	1,511.45	1,379.06	132.38	11.417		
16,800.00	11,734.46	16,737.76	11,656.58	95.23	96.05	-87.01	-5,147.90	1,140.85	1,511.42	1,376.94	134.49	11.239		
16,900.00	11,735.99	16,837.76	11,658.74	96.72	97.53	-87.03	-5,247.87	1,141.80	1,511.40	1,374.80	136.60	11.065		
17,000.00	11,737.52	16,937.76	11,660.91	98.22	99.02	-87.06	-5,347.84	1,142.75	1,511.37	1,372.66	138.71	10.896		
17,100.00	11,739.06	17,037.76	11,663.08	99.72	100.51	-87.08	-5,447.81	1,143.70	1,511.35	1,370.51	140.84	10.731		
17,200.00	11,740.59	17,137.76	11,665.24	101.22	102.00	-87.10	-5,547.78	1,144.65	1,511.32	1,368.36	142.97	10.571		
17,300.00	11,742.13	17,237.75	11,667.41	102.73	103.50	-87.13	-5,647.75	1,145.60	1,511.30	1,366.20	145.10	10.415		
17,400.00	11,743.66	17,337.75	11,669.58	104.25	105.01	-87.15	-5,747.72	1,146.55	1,511.28	1,364.03	147.25	10.264		
17,500.00	11,745.19	17,437.75	11,671.74	105.77	106.52	-87.18	-5,847.69	1,147.50	1,511.25	1,361.86	149.40	10.116		
17,600.00	11,746.73	17,537.75	11,673.91	107.29	108.03	-87.20	-5,947.66	1,148.46	1,511.23	1,359.68	151.55	9.972		
17,700.00	11,748.26	17,637.75	11,676.07	108.81	109.55	-87.22	-6,047.63	1,149.41	1,511.21	1,357.50	153.71	9.831		
17,800.00	11,749.79	17,737.74	11,678.24	110.34	111.07	-87.25	-6,147.60	1,150.36	1,511.19	1,355.31	155.88	9.695		
17,900.00	11,751.33	17,837.74	11,680.41	111.88	112.60	-87.27	-6,247.57	1,151.31	1,511.16	1,353.12	158.05	9.561		
18,000.00	11,752.86	17,937.74	11,682.57	113.41	114.12	-87.30	-6,347.54	1,152.26	1,511.14	1,350.92	160.22	9.432		
18,100.00	11,754.39	18,037.74	11,684.74	114.95	115.66	-87.32	-6,447.51	1,153.21	1,511.12	1,348.72	162.40	9.305		
18,200.00	11,755.93	18,137.74	11,686.90	116.49	117.19	-87.34	-6,547.48	1,154.16	1,511.10	1,346.52	164.58	9.181		
18,300.00	11,757.46	18,237.73	11,689.07	118.04	118.73	-87.37	-6,647.45	1,155.11	1,511.08	1,344.31	166.77	9.061		
18,400.00	11,758.99	18,337.73	11,691.24	119.59	120.27	-87.39	-6,747.42	1,156.06	1,511.06	1,342.09	168.96	8.943		
18,500.00	11,760.53	18,437.73	11,693.40	121.14	121.82	-87.42	-6,847.39	1,157.01	1,511.04	1,339.88	171.16	8.828		
18,600.00	11,762.06	18,537.73	11,695.57	122.69	123.36	-87.44	-6,947.36	1,157.96	1,511.02	1,337.66	173.36	8.716		
18,700.00	11,763.60	18,637.73	11,697.74	124.25	124.91	-87.46	-7,047.33	1,158.91	1,511.00	1,335.43	175.56	8.607		
18,800.00	11,765.13	18,737.72	11,699.90	125.81	126.46	-87.49	-7,147.30	1,159.86	1,510.98	1,333.21	177.77	8.500		
18,900.00	11,766.66	18,837.72	11,702.07	127.37	128.02	-87.51	-7,247.27	1,160.82	1,510.96	1,330.98	179.98	8.395		
19,000.00	11,768.20	18,937.72	11,704.23	128.93	129.58	-87.54	-7,347.24	1,161.77	1,510.94	1,328.75	182.19	8.293		
19,100.00	11,769.73	19,037.72	11,706.40	130.50	131.14	-87.56	-7,447.21	1,162.72	1,510.92	1,326.51	184.41	8.193		
19,200.00	11,771.26	19,137.72	11,708.57	132.07	132.70	-87.58	-7,547.18	1,163.67	1,510.90	1,324.27	186.63	8.096		
19,300.00	11,772.80	19,237.71	11,710.73	133.64	134.26	-87.61	-7,647.15	1,164.62	1,510.88	1,322.03	188.85	8.000		
19,400.00	11,774.33	19,337.71	11,712.90	135.21	135.83	-87.63	-7,747.12	1,165.57	1,510.87	1,319.79	191.08	7.907		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Distance		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor	Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)		Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)						
19,500.00	11,775.86	19,437.71	11,715.07	136.78	137.40	-87.66	-7,847.09	1,166.52	1,510.85	1,317.54	193.30	7.816		
19,600.00	11,777.40	19,537.71	11,717.23	138.36	138.97	-87.68	-7,947.06	1,167.47	1,510.83	1,315.30	195.53	7.727		
19,700.00	11,778.93	19,637.71	11,719.40	139.94	140.54	-87.70	-8,047.03	1,168.42	1,510.81	1,313.05	197.77	7.639		
19,800.00	11,780.46	19,737.70	11,721.56	141.52	142.11	-87.73	-8,147.00	1,169.37	1,510.80	1,310.79	200.00	7.554		
19,900.00	11,782.00	19,837.70	11,723.73	143.10	143.69	-87.75	-8,246.97	1,170.32	1,510.78	1,308.54	202.24	7.470		
20,000.00	11,783.53	19,937.70	11,725.90	144.68	145.27	-87.78	-8,346.94	1,171.27	1,510.76	1,306.28	204.48	7.388		
20,100.00	11,785.07	20,037.70	11,728.06	146.26	146.84	-87.80	-8,446.91	1,172.22	1,510.75	1,304.03	206.72	7.308		
20,200.00	11,786.60	20,137.70	11,730.23	147.85	148.42	-87.82	-8,546.88	1,173.18	1,510.73	1,301.77	208.96	7.230		
20,300.00	11,788.13	20,237.69	11,732.40	149.44	150.01	-87.85	-8,646.85	1,174.13	1,510.72	1,299.50	211.21	7.153		
20,400.00	11,789.67	20,337.69	11,734.56	151.02	151.59	-87.87	-8,746.82	1,175.08	1,510.70	1,297.24	213.46	7.077		
20,500.00	11,791.20	20,437.69	11,736.73	152.61	153.18	-87.90	-8,846.79	1,176.03	1,510.68	1,294.98	215.71	7.003		
20,600.00	11,792.73	20,537.69	11,738.89	154.20	154.76	-87.92	-8,946.76	1,176.98	1,510.67	1,292.71	217.96	6.931		
20,700.00	11,794.27	20,637.69	11,741.06	155.80	156.35	-87.94	-9,046.73	1,177.93	1,510.66	1,290.44	220.21	6.860		
20,800.00	11,795.80	20,737.68	11,743.23	157.39	157.94	-87.97	-9,146.70	1,178.88	1,510.64	1,288.17	222.47	6.790		
20,900.00	11,797.33	20,837.68	11,745.39	158.98	159.53	-87.99	-9,246.67	1,179.83	1,510.63	1,285.90	224.73	6.722		
21,000.00	11,798.87	20,937.68	11,747.56	160.58	161.12	-88.02	-9,346.64	1,180.78	1,510.61	1,283.63	226.99	6.655		
21,100.00	11,800.40	21,037.68	11,749.73	162.18	162.71	-88.04	-9,446.61	1,181.73	1,510.60	1,281.35	229.25	6.589		
21,200.00	11,801.93	21,137.68	11,751.89	163.78	164.31	-88.06	-9,546.58	1,182.68	1,510.59	1,279.08	231.51	6.525		
21,300.00	11,803.47	21,237.67	11,754.06	165.37	165.90	-88.09	-9,646.55	1,183.63	1,510.57	1,276.80	233.77	6.462		
21,400.00	11,805.00	21,337.67	11,756.22	166.98	167.50	-88.11	-9,746.52	1,184.58	1,510.56	1,274.52	236.04	6.400		
21,500.00	11,806.53	21,437.67	11,758.39	168.58	169.10	-88.14	-9,846.49	1,185.54	1,510.55	1,272.24	238.30	6.339		
21,600.00	11,808.07	21,537.67	11,760.56	170.18	170.70	-88.16	-9,946.46	1,186.49	1,510.54	1,269.96	240.57	6.279		
21,700.00	11,809.60	21,637.67	11,762.72	171.78	172.30	-88.18	-10,046.43	1,187.44	1,510.52	1,267.68	242.84	6.220		
21,800.00	11,811.14	21,737.66	11,764.89	173.39	173.90	-88.21	-10,146.40	1,188.39	1,510.51	1,265.40	245.11	6.163		
21,806.77	11,811.24	21,744.20	11,765.03	173.49	174.00	-88.21	-10,152.93	1,188.45	1,510.51	1,265.25	245.26	6.159		
21,813.35	11,811.34	21,744.20	11,765.03	173.60	174.00	-88.21	-10,152.93	1,188.45	1,510.53	1,265.16	245.36	6.156		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Mission/Vested Fed Com - Vested Fed Com 706H - OH - Plan #1													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance				Warning			
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)		Minimum Separation (usft)	Separation Factor	
0.00	0.00	0.60	0.60	0.00	0.00	89.54	0.56	69.99	69.99					
100.00	100.00	100.60	100.60	0.13	0.13	89.54	0.56	69.99	69.99	69.81	0.18	391.101		
200.00	200.00	200.60	200.60	0.48	0.49	89.54	0.56	69.99	69.99	69.31	0.69	102.043		
300.00	300.00	300.60	300.60	0.84	0.84	89.54	0.56	69.99	69.99	68.80	1.19	58.676		
400.00	400.00	400.60	400.60	1.20	1.20	89.54	0.56	69.99	69.99	68.29	1.70	41.176		
500.00	500.00	500.60	500.60	1.56	1.56	89.54	0.56	69.99	69.99	67.79	2.21	31.717		
600.00	600.00	600.60	600.60	1.92	1.92	89.54	0.56	69.99	69.99	67.28	2.71	25.792		
700.00	700.00	700.60	700.60	2.28	2.28	89.54	0.56	69.99	69.99	66.77	3.22	21.732		
800.00	800.00	800.60	800.60	2.63	2.64	89.54	0.56	69.99	69.99	66.26	3.73	18.777		
900.00	900.00	900.60	900.60	2.99	3.00	89.54	0.56	69.99	69.99	65.76	4.23	16.529		
1,000.00	1,000.00	1,000.60	1,000.60	3.35	3.35	89.54	0.56	69.99	69.99	65.25	4.74	14.761		
1,100.00	1,100.00	1,100.60	1,100.60	3.71	3.71	89.54	0.56	69.99	69.99	64.74	5.25	13.336		
1,200.00	1,200.00	1,200.60	1,200.60	4.07	4.07	89.54	0.56	69.99	69.99	64.24	5.76	12.161		
1,300.00	1,300.00	1,300.60	1,300.60	4.43	4.43	89.54	0.56	69.99	69.99	63.73	6.26	11.177		
1,400.00	1,400.00	1,400.60	1,400.60	4.79	4.79	89.54	0.56	69.99	69.99	63.22	6.77	10.340		
1,500.00	1,500.00	1,500.60	1,500.60	5.14	5.15	89.54	0.56	69.99	69.99	62.72	7.28	9.619		
1,600.00	1,600.00	1,600.60	1,600.60	5.50	5.50	89.54	0.56	69.99	69.99	62.21	7.78	8.993		
1,700.00	1,700.00	1,700.60	1,700.60	5.86	5.86	89.54	0.56	69.99	69.99	61.70	8.29	8.443		
1,800.00	1,800.00	1,800.60	1,800.60	6.22	6.22	89.54	0.56	69.99	69.99	61.20	8.80	7.956		
1,900.00	1,900.00	1,900.60	1,900.60	6.58	6.58	89.54	0.56	69.99	69.99	60.69	9.30	7.523		
2,000.00	2,000.00	2,000.60	2,000.60	6.94	6.94	89.54	0.56	69.99	69.99	60.18	9.81	7.134		
2,100.00	2,100.00	2,100.60	2,100.60	7.29	7.30	89.54	0.56	69.99	69.99	59.67	10.32	6.783		
2,200.00	2,200.00	2,200.60	2,200.60	7.65	7.66	89.54	0.56	69.99	69.99	59.17	10.83	6.466		
2,300.00	2,300.00	2,300.60	2,300.60	8.01	8.01	89.54	0.56	69.99	69.99	58.66	11.33	6.177		
2,400.00	2,400.00	2,400.60	2,400.60	8.37	8.37	89.54	0.56	69.99	69.99	58.15	11.84	5.912		
2,500.00	2,500.00	2,500.60	2,500.60	8.73	8.73	89.54	0.56	69.99	69.99	57.65	12.35	5.669		
2,600.00	2,600.00	2,600.60	2,600.60	9.09	9.09	89.54	0.56	69.99	69.99	57.14	12.85	5.446		
2,700.00	2,700.00	2,700.60	2,700.60	9.45	9.45	89.54	0.56	69.99	69.99	56.63	13.36	5.239		
2,800.00	2,800.00	2,800.60	2,800.60	9.80	9.81	89.54	0.56	69.99	69.99	56.13	13.87	5.047		
2,900.00	2,900.00	2,900.60	2,900.60	10.16	10.16	89.54	0.56	69.99	69.99	55.62	14.37	4.869		
3,000.00	3,000.00	3,000.60	3,000.60	10.52	10.52	89.54	0.56	69.99	69.99	55.11	14.88	4.704		
3,100.00	3,100.00	3,100.60	3,100.60	10.88	10.88	89.54	0.56	69.99	69.99	54.60	15.39	4.549		
3,200.00	3,200.00	3,200.60	3,200.60	11.24	11.24	89.54	0.56	69.99	69.99	54.10	15.89	4.404		
3,300.00	3,300.00	3,300.60	3,300.60	11.60	11.60	89.54	0.56	69.99	69.99	53.59	16.40	4.267		
3,400.00	3,400.00	3,400.60	3,400.60	11.96	11.96	89.54	0.56	69.99	69.99	53.08	16.91	4.139		
3,500.00	3,500.00	3,500.60	3,500.60	12.31	12.32	89.54	0.56	69.99	69.99	52.58	17.42	4.019		
3,600.00	3,600.00	3,600.60	3,600.60	12.67	12.67	89.54	0.56	69.99	69.99	52.07	17.92	3.905		
3,700.00	3,700.00	3,700.60	3,700.60	13.03	13.03	89.54	0.56	69.99	69.99	51.56	18.43	3.798		
3,800.00	3,800.00	3,800.60	3,800.60	13.39	13.39	89.54	0.56	69.99	69.99	51.06	18.94	3.696		
3,900.00	3,900.00	3,900.60	3,900.60	13.75	13.75	89.54	0.56	69.99	69.99	50.55	19.44	3.600		
4,000.00	4,000.00	4,000.60	4,000.60	14.11	14.11	89.54	0.56	69.99	69.99	50.04	19.95	3.508		
4,100.00	4,100.00	4,100.60	4,100.60	14.46	14.47	89.54	0.56	69.99	69.99	49.54	20.46	3.421		
4,116.47	4,116.47	4,117.07	4,117.07	14.52	14.53	89.54	0.56	69.99	69.99	49.45	20.54	3.408 CC		
4,200.00	4,200.00	4,200.60	4,200.00	14.82	14.82	89.54	0.56	69.99	69.99	49.03	20.96	3.339 ES, SF		
4,300.00	4,299.99	4,298.79	4,298.78	15.18	15.17	154.19	0.91	71.22	72.42	50.97	21.45	3.376		
4,400.00	4,399.91	4,396.65	4,396.57	15.53	15.51	154.62	1.93	74.86	79.68	57.77	21.91	3.636		
4,500.00	4,499.69	4,493.82	4,493.53	15.88	15.85	155.19	3.62	80.86	91.75	69.39	22.36	4.103		
4,600.27	4,599.54	4,590.24	4,589.56	16.23	16.19	155.75	5.95	89.16	108.63	85.84	22.80	4.765		
4,700.00	4,698.72	4,685.65	4,684.34	16.58	16.52	156.15	8.90	99.63	128.91	105.68	23.23	5.549		
4,800.00	4,798.17	4,783.40	4,781.37	16.94	16.87	156.36	12.12	111.10	149.99	126.28	23.71	6.325		
4,900.00	4,897.62	4,881.15	4,878.39	17.30	17.22	156.51	15.35	122.57	171.08	146.88	24.20	7.069		
5,000.00	4,997.08	4,978.90	4,975.41	17.66	17.57	156.63	18.58	134.04	192.17	167.48	24.69	7.785		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design													Mission/Vested Fed Com - Vested Fed Com 706H - OH - Plan #1		Offset Site Error: 0.00 usft	
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error: 0.00 usft			
Reference		Offset		Semi Major Axis			Distance							Warning		
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre		Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor				
							+N/-S (usft)	+E/-W (usft)								
5,100.00	5,096.53	5,076.65	5,072.43	18.02	17.92	156.73	21.81	145.52	213.26	188.09	25.17	8.472				
5,200.00	5,195.98	5,174.40	5,169.45	18.38	18.27	156.81	25.03	156.99	234.35	208.69	25.66	9.133				
5,300.00	5,295.43	5,272.15	5,266.47	18.74	18.63	156.87	28.26	168.46	255.44	229.29	26.15	9.768				
5,400.00	5,394.88	5,369.90	5,363.49	19.11	18.99	156.93	31.49	179.94	276.53	249.89	26.64	10.380				
5,500.00	5,494.33	5,467.65	5,460.51	19.47	19.35	156.98	34.71	191.41	297.62	270.49	27.13	10.970				
5,600.00	5,593.78	5,565.40	5,557.53	19.84	19.71	157.02	37.94	202.88	318.71	291.09	27.62	11.539				
5,700.00	5,693.24	5,663.15	5,654.55	20.21	20.07	157.05	41.17	214.36	339.80	311.69	28.11	12.087				
5,800.00	5,792.69	5,760.90	5,751.58	20.57	20.43	157.09	44.40	225.83	360.89	332.29	28.61	12.616				
5,900.00	5,892.14	5,858.65	5,848.60	20.94	20.80	157.12	47.62	237.30	381.99	352.89	29.10	13.127				
6,000.00	5,991.59	5,956.40	5,945.62	21.32	21.17	157.14	50.85	248.77	403.08	373.48	29.59	13.621				
6,100.00	6,091.04	6,054.15	6,042.64	21.69	21.53	157.16	54.08	260.25	424.17	394.08	30.09	14.098				
6,200.00	6,190.49	6,151.90	6,139.66	22.06	21.90	157.19	57.31	271.72	445.26	414.68	30.58	14.559				
6,300.00	6,289.94	6,249.65	6,236.68	22.43	22.27	157.20	60.53	283.19	466.35	435.27	31.08	15.005				
6,400.00	6,389.40	6,347.40	6,333.70	22.81	22.64	157.22	63.76	294.67	487.44	455.87	31.58	15.437				
6,500.00	6,488.85	6,445.15	6,430.72	23.18	23.01	157.24	66.99	306.14	508.54	476.46	32.07	15.855				
6,600.00	6,588.30	6,542.90	6,527.74	23.56	23.38	157.25	70.21	317.61	529.63	497.06	32.57	16.261				
6,700.00	6,687.75	6,640.65	6,624.76	23.93	23.76	157.27	73.44	329.09	550.72	517.65	33.07	16.654				
6,800.00	6,787.20	6,738.40	6,721.79	24.31	24.13	157.28	76.67	340.56	571.81	538.24	33.57	17.034				
6,900.00	6,886.65	6,836.15	6,818.81	24.68	24.50	157.29	79.90	352.03	592.90	558.84	34.07	17.404				
7,000.00	6,986.10	6,933.90	6,915.83	25.06	24.88	157.30	83.12	363.50	614.00	579.43	34.57	17.763				
7,100.00	7,085.56	7,031.65	7,012.85	25.44	25.26	157.31	86.35	374.98	635.09	600.02	35.07	18.111				
7,200.00	7,185.01	7,129.40	7,109.87	25.82	25.63	157.32	89.58	386.45	656.18	620.61	35.57	18.449				
7,300.00	7,284.46	7,227.15	7,206.89	26.20	26.01	157.33	92.81	397.92	677.27	641.20	36.07	18.777				
7,400.00	7,383.91	7,324.90	7,303.91	26.58	26.39	157.34	96.03	409.40	698.36	661.79	36.57	19.097				
7,500.00	7,483.36	7,422.65	7,400.93	26.96	26.76	157.35	99.26	420.87	719.46	682.38	37.07	19.407				
7,600.00	7,582.81	7,520.40	7,497.95	27.34	27.14	157.35	102.49	432.34	740.55	702.97	37.57	19.709				
7,700.00	7,682.26	7,618.15	7,594.97	27.72	27.52	157.36	105.72	443.82	761.64	723.56	38.08	20.003				
7,800.00	7,781.72	7,715.90	7,691.99	28.10	27.90	157.37	108.94	455.29	782.73	744.15	38.58	20.289				
7,900.00	7,881.17	7,813.66	7,789.02	28.48	28.28	157.37	112.17	466.76	803.82	764.74	39.08	20.567				
8,000.00	7,980.62	7,911.41	7,886.04	28.86	28.66	157.38	115.40	478.24	824.92	785.33	39.59	20.838				
8,100.00	8,080.07	8,009.16	7,983.06	29.24	29.04	157.38	118.62	489.71	846.01	805.92	40.09	21.103				
8,200.00	8,179.52	8,106.91	8,080.08	29.62	29.43	157.39	121.85	501.18	867.10	826.51	40.59	21.360				
8,300.00	8,278.97	8,204.66	8,177.10	30.01	29.81	157.40	125.08	512.65	888.19	847.09	41.10	21.611				
8,400.00	8,378.42	8,302.41	8,274.12	30.39	30.19	157.40	128.31	524.13	909.28	867.68	41.60	21.856				
8,500.00	8,477.88	8,400.16	8,371.14	30.77	30.57	157.40	131.53	535.60	930.38	888.27	42.11	22.094				
8,600.00	8,577.33	8,497.91	8,468.16	31.16	30.96	157.41	134.76	547.07	951.47	908.85	42.61	22.327				
8,638.34	8,615.46	8,535.39	8,505.36	31.30	31.10	157.41	136.00	551.47	959.56	916.75	42.81	22.415				
8,700.00	8,676.83	8,595.75	8,565.28	31.54	31.34	157.48	137.99	558.56	972.11	928.99	43.12	22.544				
8,800.00	8,776.54	8,694.03	8,662.82	31.91	31.73	157.52	141.24	570.09	990.56	946.93	43.63	22.706				
8,900.00	8,876.42	8,792.70	8,760.76	32.28	32.11	157.50	144.49	581.67	1,006.62	962.49	44.13	22.810				
9,000.00	8,976.39	8,891.72	8,859.03	32.63	32.50	157.41	147.76	593.30	1,020.30	975.67	44.64	22.858				
9,038.62	9,015.00	8,930.03	8,897.06	32.76	32.65	92.87	149.03	597.79	1,024.95	980.12	44.83	22.863				
9,100.00	9,076.38	8,990.95	8,957.53	32.98	32.89	92.74	151.04	604.94	1,032.05	986.91	45.14	22.863				
9,200.00	9,176.38	9,090.21	9,056.04	33.32	33.29	92.53	154.32	616.59	1,043.63	997.99	45.64	22.864				
9,300.00	9,276.38	9,189.46	9,154.56	33.67	33.68	92.32	157.59	628.24	1,055.23	1,009.08	46.15	22.866				
9,400.00	9,376.38	9,288.71	9,253.07	34.02	34.07	92.12	160.87	639.89	1,066.83	1,020.18	46.65	22.867				
9,500.00	9,476.38	9,387.97	9,351.58	34.37	34.46	91.92	164.15	651.54	1,078.46	1,031.30	47.16	22.869				
9,600.00	9,576.38	9,487.22	9,450.10	34.71	34.85	91.72	167.42	663.19	1,090.09	1,042.43	47.66	22.870				
9,700.00	9,676.38	9,586.48	9,548.61	35.06	35.25	91.53	170.70	674.84	1,101.74	1,053.57	48.17	22.872				
9,800.00	9,776.38	9,685.73	9,647.12	35.41	35.64	91.35	173.98	686.49	1,113.39	1,064.72	48.67	22.874				
9,900.00	9,876.38	9,784.98	9,745.64	35.76	36.03	91.17	177.25	698.14	1,125.06	1,075.88	49.18	22.877				
10,000.00	9,976.38	9,884.24	9,844.15	36.11	36.42	90.99	180.53	709.79	1,136.74	1,087.06	49.69	22.879				

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Mission/Vested Fed Com - Vested Fed Com 706H - OH - Plan #1													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis		Distance								Warning
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
10,100.00	10,076.38	9,983.49	9,942.66	36.46	36.82	90.81	183.81	721.44	1,148.43	1,098.24	50.19	22.881		
10,200.00	10,176.38	10,082.75	10,041.18	36.81	37.21	90.64	187.09	733.09	1,160.14	1,109.44	50.70	22.884		
10,300.00	10,276.38	10,182.00	10,139.69	37.16	37.61	90.47	190.36	744.74	1,171.85	1,120.64	51.20	22.887		
10,400.00	10,376.38	10,291.48	10,248.38	37.51	38.04	90.30	193.94	757.44	1,183.46	1,131.70	51.77	22.861		
10,500.00	10,476.38	10,433.55	10,389.80	37.86	38.58	90.12	197.57	770.36	1,192.56	1,140.07	52.49	22.720		
10,600.00	10,576.38	10,576.42	10,532.43	38.20	39.11	90.01	199.79	778.24	1,198.07	1,144.91	53.16	22.538		
10,700.00	10,676.38	10,719.71	10,675.68	38.55	39.61	89.97	200.56	780.99	1,199.99	1,146.21	53.78	22.314		
10,800.00	10,776.38	10,821.02	10,776.98	38.90	39.95	89.97	200.56	780.99	1,199.99	1,145.71	54.28	22.109		
10,900.00	10,876.38	10,921.02	10,876.98	39.26	40.29	89.97	200.56	780.99	1,199.99	1,145.22	54.77	21.909		
11,000.00	10,976.38	11,021.02	10,976.98	39.61	40.63	89.97	200.56	780.99	1,199.99	1,144.72	55.27	21.712		
11,100.00	11,076.38	11,121.02	11,076.98	39.96	40.97	89.97	200.56	780.99	1,199.99	1,144.22	55.77	21.518		
11,111.62	11,088.00	11,132.63	11,088.60	40.00	41.01	89.97	200.56	780.99	1,199.99	1,144.17	55.82	21.496		
11,150.00	11,126.36	11,170.99	11,126.96	40.12	41.14	-89.55	200.56	780.99	1,199.98	1,143.97	56.01	21.425		
11,200.00	11,176.03	11,220.55	11,176.51	40.28	41.30	-89.80	200.32	780.99	1,199.95	1,143.71	56.24	21.337		
11,233.48	11,208.95	11,253.64	11,209.55	40.38	41.41	-90.00	198.41	781.01	1,199.94	1,143.56	56.39	21.281		
11,250.00	11,225.04	11,270.06	11,225.89	40.43	41.46	-90.10	196.76	781.03	1,199.94	1,143.49	56.46	21.254		
11,300.00	11,273.01	11,320.12	11,275.30	40.57	41.61	-90.40	188.84	781.10	1,199.97	1,143.31	56.66	21.177		
11,350.00	11,319.57	11,370.75	11,324.38	40.70	41.75	-90.69	176.48	781.22	1,200.03	1,143.17	56.86	21.104		
11,400.00	11,364.36	11,421.95	11,372.71	40.81	41.89	-90.99	159.62	781.38	1,200.12	1,143.07	57.05	21.036		
11,450.00	11,407.05	11,473.75	11,419.86	40.92	42.01	-91.28	138.24	781.58	1,200.24	1,143.01	57.23	20.971		
11,500.00	11,447.32	11,526.13	11,465.40	41.02	42.13	-91.55	112.39	781.82	1,200.39	1,142.98	57.41	20.911		
11,550.00	11,484.85	11,579.11	11,508.86	41.10	42.23	-91.82	82.12	782.11	1,200.56	1,142.98	57.57	20.853		
11,600.00	11,519.36	11,632.67	11,549.76	41.17	42.33	-92.08	47.57	782.43	1,200.74	1,143.00	57.74	20.797		
11,650.00	11,550.58	11,686.79	11,587.63	41.24	42.41	-92.32	8.94	782.79	1,200.93	1,143.04	57.90	20.743		
11,700.00	11,578.29	11,741.46	11,622.02	41.29	42.49	-92.54	-33.54	783.19	1,201.13	1,143.08	58.05	20.690		
11,750.00	11,602.26	11,796.64	11,652.46	41.34	42.56	-92.74	-79.53	783.63	1,201.33	1,143.11	58.21	20.637		
11,800.00	11,622.32	11,852.29	11,678.54	41.40	42.63	-92.92	-128.67	784.09	1,201.51	1,143.13	58.38	20.582		
11,850.00	11,638.32	11,908.37	11,699.87	41.48	42.70	-93.08	-180.50	784.58	1,201.68	1,143.14	58.54	20.527		
11,900.00	11,650.12	11,964.80	11,716.12	41.58	42.78	-93.21	-234.52	785.09	1,201.83	1,143.11	58.71	20.469		
11,950.00	11,657.65	12,021.54	11,727.03	41.71	42.88	-93.31	-290.17	785.61	1,201.95	1,143.06	58.89	20.409		
12,002.83	11,660.89	12,081.73	11,732.52	41.85	43.00	-93.39	-350.08	786.18	1,202.04	1,142.95	59.09	20.344		
12,100.00	11,662.38	12,180.21	11,734.65	42.14	43.26	-93.42	-448.53	787.10	1,202.07	1,142.59	59.48	20.209		
12,200.00	11,663.91	12,280.20	11,736.71	42.50	43.59	-93.44	-548.50	788.04	1,202.10	1,142.14	59.97	20.046		
12,300.00	11,665.45	12,380.20	11,738.77	42.92	43.98	-93.47	-648.47	788.98	1,202.13	1,141.59	60.54	19.856		
12,400.00	11,666.98	12,480.20	11,740.84	43.40	44.44	-93.49	-748.44	789.93	1,202.17	1,140.97	61.20	19.643		
12,500.00	11,668.52	12,580.20	11,742.90	43.93	44.95	-93.52	-848.42	790.87	1,202.20	1,140.26	61.94	19.410		
12,600.00	11,670.05	12,680.20	11,744.96	44.52	45.53	-93.54	-948.39	791.81	1,202.23	1,139.47	62.75	19.158		
12,700.00	11,671.58	12,780.20	11,747.02	45.16	46.15	-93.57	-1,048.36	792.75	1,202.26	1,138.61	63.65	18.890		
12,800.00	11,673.12	12,880.20	11,749.08	45.84	46.82	-93.59	-1,148.34	793.69	1,202.29	1,137.68	64.61	18.609		
12,900.00	11,674.65	12,980.19	11,751.15	46.58	47.54	-93.62	-1,248.31	794.63	1,202.32	1,136.68	65.64	18.317		
13,000.00	11,676.18	13,080.19	11,753.21	47.36	48.31	-93.65	-1,348.28	795.57	1,202.36	1,135.62	66.74	18.016		
13,100.00	11,677.72	13,180.19	11,755.27	48.19	49.12	-93.67	-1,448.25	796.52	1,202.39	1,134.49	67.90	17.709		
13,200.00	11,679.25	13,280.19	11,757.33	49.05	49.97	-93.70	-1,548.23	797.46	1,202.42	1,133.30	69.12	17.397		
13,300.00	11,680.78	13,380.19	11,759.39	49.96	50.86	-93.72	-1,648.20	798.40	1,202.45	1,132.06	70.39	17.082		
13,400.00	11,682.32	13,480.19	11,761.46	50.90	51.79	-93.75	-1,748.17	799.34	1,202.49	1,130.77	71.72	16.766		
13,500.00	11,683.85	13,580.19	11,763.52	51.88	52.75	-93.77	-1,848.15	800.28	1,202.52	1,129.42	73.10	16.451		
13,600.00	11,685.38	13,680.18	11,765.58	52.89	53.75	-93.80	-1,948.12	801.22	1,202.55	1,128.03	74.52	16.136		
13,700.00	11,686.92	13,780.18	11,767.64	53.93	54.78	-93.82	-2,048.09	802.16	1,202.59	1,126.59	75.99	15.825		
13,800.00	11,688.45	13,880.18	11,769.70	55.01	55.84	-93.85	-2,148.07	803.11	1,202.62	1,125.12	77.51	15.516		
13,900.00	11,689.98	13,980.18	11,771.77	56.11	56.92	-93.87	-2,248.04	804.05	1,202.66	1,123.60	79.06	15.212		
14,000.00	11,691.52	14,080.18	11,773.83	57.23	58.04	-93.90	-2,348.01	804.99	1,202.69	1,122.04	80.65	14.913		
14,100.00	11,693.05	14,180.18	11,775.89	58.39	59.18	-93.92	-2,447.98	805.93	1,202.73	1,120.45	82.27	14.619		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Mission/Vested Fed Com - Vested Fed Com 706H - OH - Plan #1													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
14,200.00	11,694.59	14,280.18	11,777.95	59.56	60.34	-93.95	-2,547.96	806.87	1,202.76	1,118.83	83.93	14.330		
14,300.00	11,696.12	14,380.18	11,780.01	60.76	61.52	-93.97	-2,647.93	807.81	1,202.80	1,117.18	85.62	14.048		
14,400.00	11,697.65	14,480.17	11,782.08	61.98	62.73	-94.00	-2,747.90	808.75	1,202.83	1,115.49	87.34	13.772		
14,500.00	11,699.19	14,580.17	11,784.14	63.22	63.95	-94.02	-2,847.88	809.69	1,202.87	1,113.78	89.09	13.502		
14,600.00	11,700.72	14,680.17	11,786.20	64.47	65.20	-94.05	-2,947.85	810.64	1,202.90	1,112.05	90.86	13.239		
14,700.00	11,702.25	14,780.17	11,788.26	65.75	66.46	-94.07	-3,047.82	811.58	1,202.94	1,110.28	92.66	12.983		
14,800.00	11,703.79	14,880.17	11,790.32	67.04	67.74	-94.10	-3,147.79	812.52	1,202.98	1,108.50	94.48	12.733		
14,900.00	11,705.32	14,980.17	11,792.39	68.35	69.03	-94.12	-3,247.77	813.46	1,203.01	1,106.70	96.32	12.490		
15,000.00	11,706.85	15,080.17	11,794.45	69.67	70.34	-94.15	-3,347.74	814.40	1,203.05	1,104.87	98.18	12.253		
15,100.00	11,708.39	15,180.16	11,796.51	71.00	71.67	-94.17	-3,447.71	815.34	1,203.09	1,103.03	100.06	12.023		
15,200.00	11,709.92	15,280.16	11,798.57	72.35	73.00	-94.20	-3,547.69	816.28	1,203.12	1,101.16	101.96	11.800		
15,300.00	11,711.45	15,380.16	11,800.63	73.71	74.35	-94.22	-3,647.66	817.23	1,203.16	1,099.28	103.88	11.582		
15,400.00	11,712.99	15,480.16	11,802.70	75.08	75.71	-94.25	-3,747.63	818.17	1,203.20	1,097.39	105.81	11.371		
15,500.00	11,714.52	15,580.16	11,804.76	76.47	77.09	-94.27	-3,847.60	819.11	1,203.24	1,095.48	107.76	11.166		
15,600.00	11,716.06	15,680.16	11,806.82	77.86	78.47	-94.30	-3,947.58	820.05	1,203.28	1,093.55	109.73	10.966		
15,700.00	11,717.59	15,780.16	11,808.88	79.26	79.87	-94.32	-4,047.55	820.99	1,203.31	1,091.61	111.70	10.772		
15,800.00	11,719.12	15,880.15	11,810.94	80.68	81.27	-94.35	-4,147.52	821.93	1,203.35	1,089.66	113.70	10.584		
15,900.00	11,720.66	15,980.15	11,813.00	82.10	82.68	-94.37	-4,247.50	822.87	1,203.39	1,087.69	115.70	10.401		
16,000.00	11,722.19	16,080.15	11,815.07	83.53	84.10	-94.40	-4,347.47	823.82	1,203.43	1,085.72	117.71	10.223		
16,100.00	11,723.72	16,180.15	11,817.13	84.97	85.53	-94.42	-4,447.44	824.76	1,203.47	1,083.73	119.74	10.051		
16,200.00	11,725.26	16,280.15	11,819.19	86.41	86.97	-94.45	-4,547.41	825.70	1,203.51	1,081.73	121.78	9.883		
16,300.00	11,726.79	16,380.15	11,821.25	87.87	88.42	-94.47	-4,647.39	826.64	1,203.55	1,079.73	123.82	9.720		
16,400.00	11,728.32	16,480.15	11,823.31	89.33	89.87	-94.50	-4,747.36	827.58	1,203.59	1,077.71	125.88	9.561		
16,500.00	11,729.86	16,580.14	11,825.38	90.79	91.33	-94.52	-4,847.33	828.52	1,203.63	1,075.68	127.95	9.407		
16,600.00	11,731.39	16,680.14	11,827.44	92.27	92.79	-94.55	-4,947.31	829.46	1,203.67	1,073.65	130.02	9.257		
16,700.00	11,732.92	16,780.14	11,829.50	93.75	94.26	-94.57	-5,047.28	830.41	1,203.71	1,071.61	132.10	9.112		
16,800.00	11,734.46	16,880.14	11,831.56	95.23	95.74	-94.60	-5,147.25	831.35	1,203.75	1,069.56	134.19	8.970		
16,900.00	11,735.99	16,980.14	11,833.62	96.72	97.23	-94.62	-5,247.23	832.29	1,203.80	1,067.50	136.29	8.833		
17,000.00	11,737.52	17,080.14	11,835.69	98.22	98.71	-94.65	-5,347.20	833.23	1,203.84	1,065.44	138.40	8.698		
17,100.00	11,739.06	17,180.14	11,837.75	99.72	100.21	-94.67	-5,447.17	834.17	1,203.88	1,063.37	140.51	8.568		
17,200.00	11,740.59	17,280.13	11,839.81	101.22	101.71	-94.70	-5,547.14	835.11	1,203.92	1,061.29	142.63	8.441		
17,300.00	11,742.13	17,380.13	11,841.87	102.73	103.21	-94.72	-5,647.12	836.05	1,203.96	1,059.21	144.75	8.318		
17,400.00	11,743.66	17,480.13	11,843.93	104.25	104.72	-94.75	-5,747.09	836.99	1,204.01	1,057.12	146.88	8.197		
17,500.00	11,745.19	17,580.13	11,846.00	105.77	106.23	-94.77	-5,847.06	837.94	1,204.05	1,055.03	149.02	8.080		
17,600.00	11,746.73	17,680.13	11,848.06	107.29	107.75	-94.80	-5,947.04	838.88	1,204.09	1,052.93	151.16	7.966		
17,700.00	11,748.26	17,780.13	11,850.12	108.81	109.27	-94.82	-6,047.01	839.82	1,204.13	1,050.83	153.31	7.854		
17,800.00	11,749.79	17,880.13	11,852.18	110.34	110.79	-94.85	-6,146.98	840.76	1,204.18	1,048.72	155.46	7.746		
17,900.00	11,751.33	17,980.12	11,854.24	111.88	112.32	-94.87	-6,246.95	841.70	1,204.22	1,046.61	157.61	7.640		
18,000.00	11,752.86	18,080.12	11,856.31	113.41	113.85	-94.90	-6,346.93	842.64	1,204.26	1,044.49	159.77	7.537		
18,100.00	11,754.39	18,180.12	11,858.37	114.95	115.38	-94.93	-6,446.90	843.58	1,204.31	1,042.37	161.94	7.437		
18,200.00	11,755.93	18,280.12	11,860.43	116.49	116.92	-94.95	-6,546.87	844.53	1,204.35	1,040.25	164.11	7.339		
18,300.00	11,757.46	18,380.12	11,862.49	118.04	118.46	-94.98	-6,646.85	845.47	1,204.40	1,038.12	166.28	7.243		
18,400.00	11,758.99	18,480.12	11,864.55	119.59	120.01	-95.00	-6,746.82	846.41	1,204.44	1,035.99	168.46	7.150		
18,500.00	11,760.53	18,580.12	11,866.62	121.14	121.55	-95.03	-6,846.79	847.35	1,204.49	1,033.85	170.64	7.059		
18,600.00	11,762.06	18,680.12	11,868.68	122.69	123.10	-95.05	-6,946.76	848.29	1,204.53	1,031.71	172.82	6.970		
18,700.00	11,763.60	18,780.11	11,870.74	124.25	124.65	-95.08	-7,046.74	849.23	1,204.58	1,029.57	175.01	6.883		
18,800.00	11,765.13	18,880.11	11,872.80	125.81	126.21	-95.10	-7,146.71	850.17	1,204.62	1,027.43	177.20	6.798		
18,900.00	11,766.66	18,980.11	11,874.86	127.37	127.77	-95.13	-7,246.68	851.12	1,204.67	1,025.28	179.39	6.715		
19,000.00	11,768.20	19,080.11	11,876.93	128.93	129.33	-95.15	-7,346.66	852.06	1,204.72	1,023.13	181.59	6.634		
19,100.00	11,769.73	19,180.11	11,878.99	130.50	130.89	-95.18	-7,446.63	853.00	1,204.76	1,020.98	183.79	6.555		
19,200.00	11,771.26	19,280.11	11,881.05	132.07	132.45	-95.20	-7,546.60	853.94	1,204.81	1,018.82	185.99	6.478		
19,300.00	11,772.80	19,380.11	11,883.11	133.64	134.02	-95.23	-7,646.58	854.88	1,204.86	1,016.66	188.19	6.402		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Offset Design Mission/Vested Fed Com - Vested Fed Com 706H - OH - Plan #1													Offset Site Error:	0.00 usft
Survey Program: 0-OWSG (Rev2) MWD													Offset Well Error:	0.00 usft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (usft)	Vertical Depth (usft)	Measured Depth (usft)	Vertical Depth (usft)	Reference (usft)	Offset (usft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (usft)	+E/-W (usft)	Between Centres (usft)	Between Ellipses (usft)	Minimum Separation (usft)	Separation Factor		
19,400.00	11,774.33	19,480.10	11,885.17	135.21	135.59	-95.25	-7,746.55	855.82	1,204.90	1,014.50	190.40	6.328		
19,500.00	11,775.86	19,580.10	11,887.24	136.78	137.16	-95.28	-7,846.52	856.76	1,204.95	1,012.34	192.61	6.256		
19,600.00	11,777.40	19,680.10	11,889.30	138.36	138.73	-95.30	-7,946.49	857.70	1,205.00	1,010.18	194.82	6.185		
19,700.00	11,778.93	19,780.10	11,891.36	139.94	140.30	-95.33	-8,046.47	858.65	1,205.05	1,008.01	197.04	6.116		
19,800.00	11,780.46	19,880.10	11,893.42	141.52	141.88	-95.35	-8,146.44	859.59	1,205.09	1,005.84	199.25	6.048		
19,900.00	11,782.00	19,980.10	11,895.48	143.10	143.45	-95.38	-8,246.41	860.53	1,205.14	1,003.67	201.47	5.982		
20,000.00	11,783.53	20,080.10	11,897.54	144.68	145.03	-95.40	-8,346.39	861.47	1,205.19	1,001.50	203.69	5.917		
20,100.00	11,785.07	20,180.09	11,899.61	146.26	146.61	-95.43	-8,446.36	862.41	1,205.24	999.33	205.91	5.853		
20,200.00	11,786.60	20,280.09	11,901.67	147.85	148.20	-95.45	-8,546.33	863.35	1,205.29	997.15	208.14	5.791		
20,300.00	11,788.13	20,380.09	11,903.73	149.44	149.78	-95.48	-8,646.30	864.29	1,205.34	994.97	210.36	5.730		
20,400.00	11,789.67	20,480.09	11,905.79	151.02	151.36	-95.50	-8,746.28	865.24	1,205.39	992.80	212.59	5.670		
20,500.00	11,791.20	20,580.09	11,907.85	152.61	152.95	-95.53	-8,846.25	866.18	1,205.44	990.62	214.82	5.611		
20,600.00	11,792.73	20,680.09	11,909.92	154.20	154.54	-95.55	-8,946.22	867.12	1,205.49	988.43	217.05	5.554		
20,700.00	11,794.27	20,780.09	11,911.98	155.80	156.13	-95.58	-9,046.20	868.06	1,205.54	986.25	219.28	5.498		
20,800.00	11,795.80	20,880.08	11,914.04	157.39	157.72	-95.60	-9,146.17	869.00	1,205.59	984.07	221.52	5.442		
20,900.00	11,797.33	20,980.08	11,916.10	158.98	159.31	-95.63	-9,246.14	869.94	1,205.64	981.88	223.75	5.388		
21,000.00	11,798.87	21,080.08	11,918.16	160.58	160.90	-95.65	-9,346.11	870.88	1,205.69	979.70	225.99	5.335		
21,100.00	11,800.40	21,180.08	11,920.23	162.18	162.50	-95.68	-9,446.09	871.83	1,205.74	977.51	228.23	5.283		
21,200.00	11,801.93	21,280.08	11,922.29	163.78	164.09	-95.70	-9,546.06	872.77	1,205.79	975.32	230.47	5.232		
21,300.00	11,803.47	21,380.08	11,924.35	165.37	165.69	-95.73	-9,646.03	873.71	1,205.84	973.13	232.71	5.182		
21,400.00	11,805.00	21,480.08	11,926.41	166.98	167.29	-95.75	-9,746.01	874.65	1,205.89	970.94	234.95	5.133		
21,500.00	11,806.53	21,580.07	11,928.47	168.58	168.89	-95.78	-9,845.98	875.59	1,205.94	968.75	237.19	5.084		
21,600.00	11,808.07	21,680.07	11,930.54	170.18	170.49	-95.80	-9,945.95	876.53	1,206.00	966.56	239.43	5.037		
21,700.00	11,809.60	21,780.07	11,932.60	171.78	172.09	-95.83	-10,045.93	877.47	1,206.05	964.37	241.68	4.990		
21,800.00	11,811.14	21,880.07	11,934.66	173.39	173.69	-95.85	-10,145.90	878.41	1,206.10	962.18	243.92	4.945		
21,813.35	11,811.34	21,891.24	11,934.89	173.60	173.87	-95.85	-10,157.06	878.52	1,206.11	961.91	244.20	4.939		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to 3328.7' GE + 30' KB @ 3358.70usft


Offset Depths are relative to Offset Datum

Central Meridian is -104.333334

Coordinates are relative to: Mission Fed Com 603H

Coordinate System is US State Plane 1983, New Mexico Eastern Zone

Grid Convergence at Surface is: 0.54°

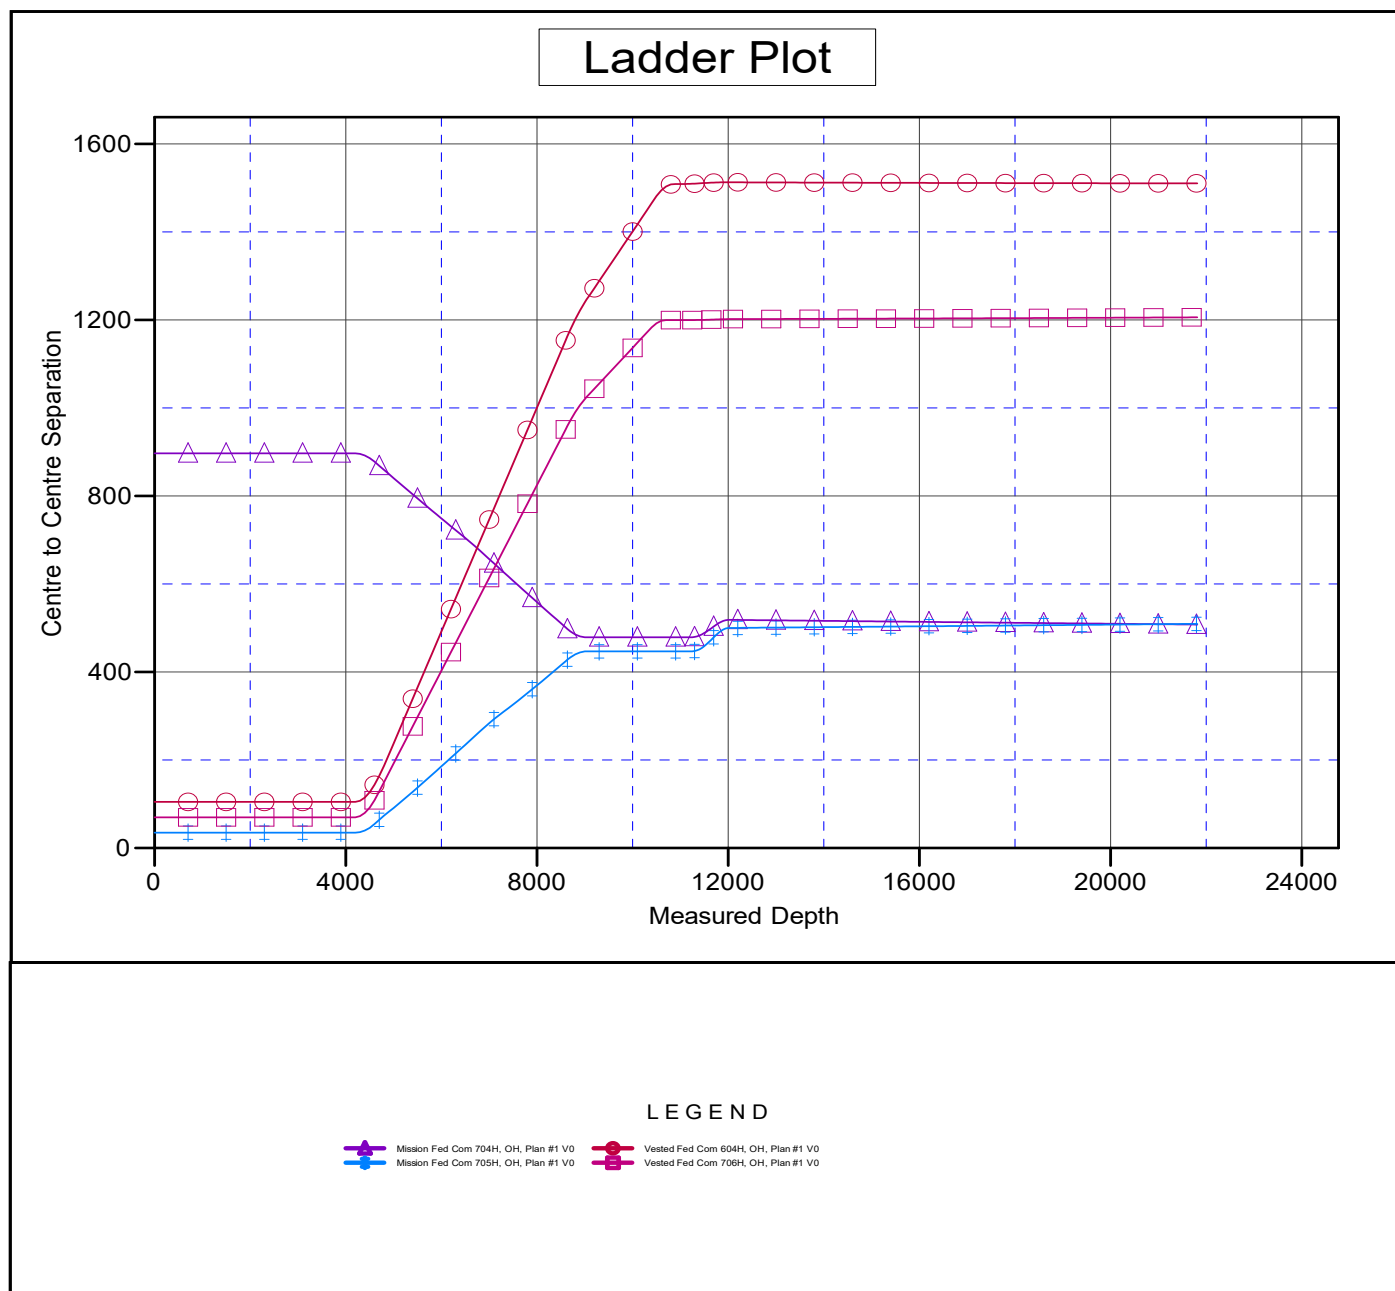

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Total Directional Services

Anticollision Report



Company:	Franklin Mountain Energy	Local Co-ordinate Reference:	Well Mission Fed Com 603H
Project:	Lea County, NM (NAD83)	TVD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Reference Site:	Mission/Vested Fed Com	MD Reference:	3328.7' GE + 30' KB @ 3358.70usft
Site Error:	0.00 usft	North Reference:	Grid
Reference Well:	Mission Fed Com 603H	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00 usft	Output errors are at	2.00 sigma
Reference Wellbore	OH	Database:	EDM 5000.15 Single User Db
Reference Design:	Plan #1	Offset TVD Reference:	Offset Datum

Reference Depths are relative to 3328.7' GE + 30' KB @ 3358.70usft

Coordinates are relative to: Mission Fed Com 603H


Offset Depths are relative to Offset Datum

Coordinate System is US State Plane 1983, New Mexico Eastern Zone

Central Meridian is -104.333334

Grid Convergence at Surface is: 0.54°

Separation Factor Plot

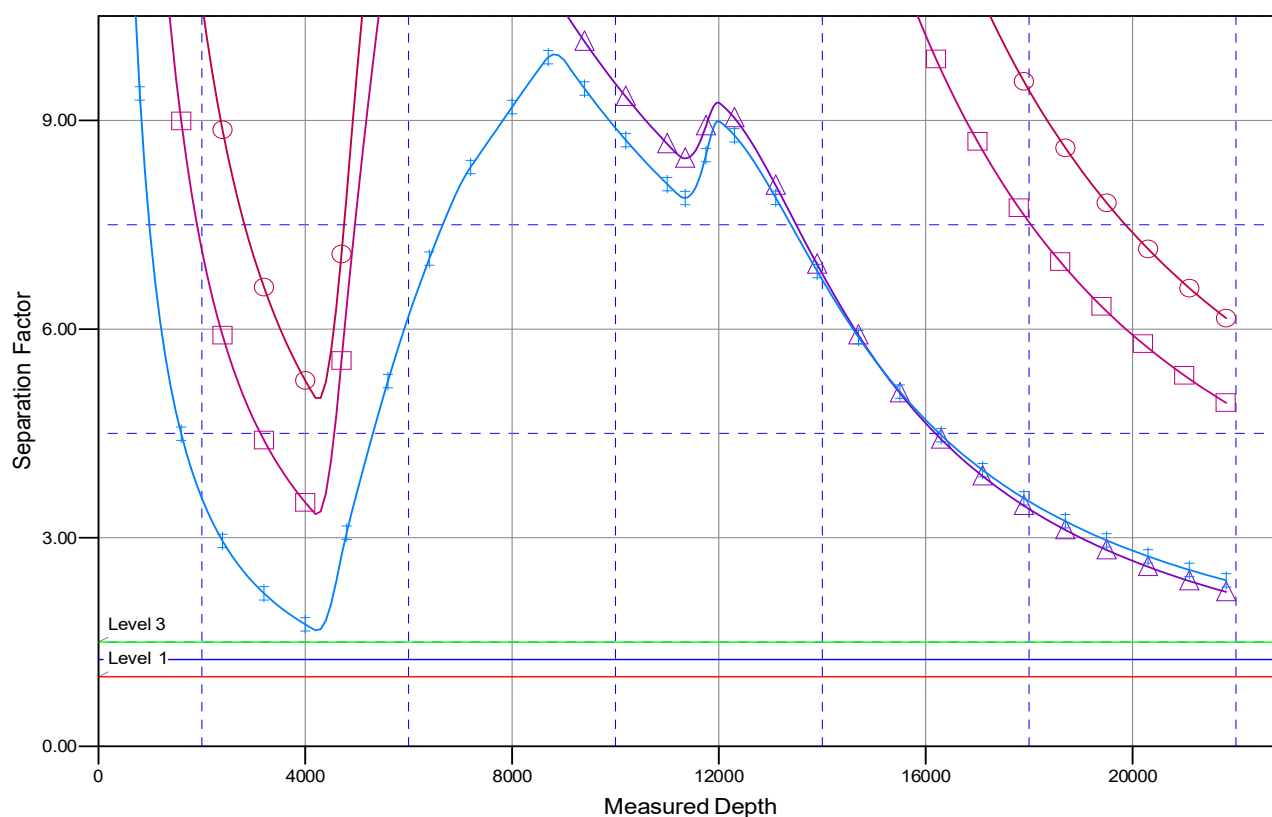

LEGEND

Mission Fed Com 704H, OH, Plan #1 V0
 Mission Fed Com 705H, OH, Plan #1 V0
 Vested Fed Com 604H, OH, Plan #1 V0
 Vested Fed Com 706H, OH, Plan #1 V0

PECOS DISTRICT DRILLING CONDITIONS OF APPROVAL

OPERATOR'S NAME:	Franklin Mountain Energy LLC
LEASE NO.:	NMNM138897
LOCATION:	Section 1, T.25 S., R.35 E., NMPM
COUNTY:	Lea County, New Mexico

WELL NAME & NO.:	Mission Fed Com 603H
SURFACE HOLE FOOTAGE:	250'/N & 1442'/E
BOTTOM HOLE FOOTAGE:	150'/S & 1860'/E

WELL NAME & NO.:	Mission Fed Com 704H
SURFACE HOLE FOOTAGE:	250'/N & 2339'/E
BOTTOM HOLE FOOTAGE:	150'/S & 2339'/E

WELL NAME & NO.:	Mission Fed Com 705H
SURFACE HOLE FOOTAGE:	250'/N & 1407'/E
BOTTOM HOLE FOOTAGE:	150'/S & 1413'/E

COA

H2S	☐ Yes	☒ No	
Potash	☒ None	☐ Secretary	☐ R-111-P
Cave/Karst Potential	☒ Low	☐ Medium	☐ High
Cave/Karst Potential	☐ Critical		
Variance	☒ None	☐ Flex Hose	☐ Other
Wellhead	☐ Conventional	☐ Multibowl	☒ Both
Other	☒ 4 String Area	☐ Capitan Reef	☐ WIPP
Other	☒ Fluid Filled	☐ Cement Squeeze	☐ Pilot Hole
Special Requirements	☐ Water Disposal	☒ COM	☐ Unit

A. HYDROGEN SULFIDE

Hydrogen Sulfide (H2S) monitors shall be installed prior to drilling out the surface shoe. If H2S is detected in concentrations greater than 100 ppm, the Hydrogen Sulfide area shall meet Onshore Order 6 requirements, which includes equipment and personnel/public protection items. If Hydrogen Sulfide is encountered, provide measured values and formations to the BLM.

B. CASING

1. The **13-3/8** inch surface casing shall be set at approximately **1335 feet** (a minimum of **25 feet (Lea County)** into the Rustler Anhydrite and above the salt) and cemented to the surface.
 - a. If cement does not circulate to the surface, the appropriate BLM office shall be notified and a temperature survey utilizing an electronic type temperature survey with surface log readout will be used or a cement bond log shall be run to verify the top of the cement. Temperature survey will be run a minimum of six hours after pumping cement and ideally between 8-10 hours after completing the cement job.
 - b. Wait on cement (WOC) time for a primary cement job will be a minimum of **8 hours** or 500 pounds compressive strength, whichever is greater. (This is to include the lead cement)
 - c. Wait on cement (WOC) time for a remedial job will be a minimum of 4 hours after bringing cement to surface or 500 pounds compressive strength, whichever is greater.
 - d. If cement falls back, remedial cementing will be done prior to drilling out that string.
2. The minimum required fill of cement behind the **9-5/8** inch intermediate casing shall be set at approximately **5400 feet** is:

- Cement to surface. If cement does not circulate see B.1.a, c-d above.

Intermediate casing must be kept fluid filled to meet BLM minimum collapse requirement.

3. The minimum required fill of cement behind the **7-5/8** inch intermediate casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.
4. The minimum required fill of cement behind the **5-1/2** inch production casing is:
 - Cement should tie-back at least **200 feet** into previous casing string. Operator shall provide method of verification.

C. PRESSURE CONTROL

1.

Option 1:

- a. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **5000 (5M) psi.**
- b. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the **7-5/8** inch intermediate casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**

Option 2:

1. Operator has proposed a multi-bowl wellhead assembly. This assembly will only be tested when installed on the surface casing. Minimum working pressure of the blowout preventer (BOP) and related equipment (BOPE) required for drilling below the surface casing shoe shall be **10,000 (10M) psi. Variance is approved to use a 5000 (5M) Annular which shall be tested to 5000 (5M) psi.**
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
 - e. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.

D. SPECIAL REQUIREMENT (S)

Communitization Agreement

- The operator will submit a Communitization Agreement to the Santa Fe Office, 301 Dinosaur Trail Santa Fe, New Mexico 87508, at least 90 days before the anticipated date of first production from a well subject to a spacing order issued by the New Mexico Oil Conservation Division. The Communitization Agreement will include the signatures of all working interest owners in all Federal and Indian leases subject to the Communitization Agreement (i.e., operating rights owners and lessees of record),

or certification that the operator has obtained the written signatures of all such owners and will make those signatures available to the BLM immediately upon request.

- If the operator does not comply with this condition of approval, the BLM may take enforcement actions that include, but are not limited to, those specified in 43 CFR 3163.1.
- In addition, the well sign shall include the surface and bottom hole lease numbers. When the Communitization Agreement number is known, it shall also be on the sign.

GENERAL REQUIREMENTS

The BLM is to be notified in advance for a representative to witness:

- a. Spudding well (minimum of 24 hours)
- b. Setting and/or Cementing of all casing strings (minimum of 4 hours)
- c. BOPE tests (minimum of 4 hours)

☒ Eddy County

Call the Carlsbad Field Office, 620 East Greene St., Carlsbad, NM 88220,
(575) 361-2822

☒ Lea County

Call the Hobbs Field Station, 414 West Taylor, Hobbs NM 88240, (575)
393-3612

1. Unless the production casing has been run and cemented or the well has been properly plugged, the drilling rig shall not be removed from over the hole without prior approval.
 - a. In the event the operator has proposed to drill multiple wells utilizing a skid/walking rig. Operator shall secure the wellbore on the current well, after installing and testing the wellhead, by installing a blind flange of like pressure rating to the wellhead and a pressure gauge that can be monitored while drilling is performed on the other well(s).
 - b. When the operator proposes to set surface casing with Spudder Rig
 - Notify the BLM when moving in and removing the Spudder Rig.
 - Notify the BLM when moving in the 2nd Rig. Rig to be moved in within 90 days of notification that Spudder Rig has left the location.
 - BOP/BOPE test to be conducted per Onshore Oil and Gas Order No. 2 as soon as 2nd Rig is rigged up on well.
2. Floor controls are required for 3M or Greater systems. These controls will be on the rig floor, unobstructed, readily accessible to the driller and will be operational at all times during drilling and/or completion activities. Rig floor is defined as the area immediately around the rotary table; the area immediately above the substructure on which the draw works are located, this does not include the dog house or stairway area.
3. The record of the drilling rate along with the GR/N well log run from TD to surface (horizontal well – vertical portion of hole) shall be submitted to the BLM office as well as all other logs run on the borehole 30 days from completion. If available, a digital copy of the logs is to be submitted in addition to the paper copies. The Rustler top and top and bottom of Salt are to be recorded on the Completion Report.

A. CASING

1. Changes to the approved APD casing program need prior approval if the items substituted are of lesser grade or different casing size or are Non-API. The Operator can exchange the components of the proposal with that of superior strength (i.e. changing from J-55 to N-80, or from 36# to 40#). Changes to the approved cement program need prior approval if the altered cement plan has less volume or strength or if the changes are substantial (i.e. Multistage tool, ECP, etc.). The initial wellhead installed on the well will remain on the well with spools used as needed.
2. Wait on cement (WOC) for Potash Areas: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi for all cement blends, 2) until cement has been in place at least 24 hours. WOC time will be recorded in the driller's log. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
3. Wait on cement (WOC) for Water Basin: After cementing but before commencing any tests, the casing string shall stand cemented under pressure until both of the following conditions have been met: 1) cement reaches a minimum compressive strength of 500 psi at the shoe, 2) until cement has been in place at least 8 hours. WOC time will be recorded in the driller's log. See individual casing strings for details regarding lead cement slurry requirements. The casing integrity test can be done (prior to the cement setting up) immediately after bumping the plug.
4. Provide compressive strengths including hours to reach required 500 pounds compressive strength prior to cementing each casing string. Have well specific cement details onsite prior to pumping the cement for each casing string.
5. No pea gravel permitted for remedial or fall back remedial without prior authorization from the BLM engineer.
6. On that portion of any well approved for a 5M BOPE system or greater, a pressure integrity test of each casing shoe shall be performed. Formation at the shoe shall be tested to a minimum of the mud weight equivalent anticipated to control the formation pressure to the next casing depth or at total depth of the well. This test shall be performed before drilling more than 20 feet of new hole.
7. If hardband drill pipe is rotated inside casing, returns will be monitored for metal. If metal is found in samples, drill pipe will be pulled and rubber protectors which have a larger diameter than the tool joints of the drill pipe will be installed prior to continuing drilling operations.
8. Whenever a casing string is cemented in the R-111-P potash area, the NMOCD requirements shall be followed.

B. PRESSURE CONTROL

1. All blowout preventer (BOP) and related equipment (BOPE) shall comply with well control requirements as described in Onshore Oil and Gas Order No. 2 and API RP 53 Sec. 17.
2. If a variance is approved for a flexible hose to be installed from the BOP to the choke manifold, the following requirements apply: The flex line must meet the requirements of API 16C. Check condition of flexible line from BOP to choke manifold, replace if exterior is damaged or if line fails test. Line to be as straight as possible with no hard bends and is to be anchored according to Manufacturer's requirements. The flexible hose can be exchanged with a hose of equal size and equal or greater pressure rating. Anchor requirements, specification sheet and hydrostatic pressure test certification matching the hose in service, to be onsite for review. These documents shall be posted in the company man's trailer and on the rig floor.
3. 5M or higher system requires an HCR valve, remote kill line and annular to match. The remote kill line is to be installed prior to testing the system and tested to stack pressure.
4. If the operator has proposed a multi-bowl wellhead assembly in the APD. The following requirements must be met:
 - a. Wellhead shall be installed by manufacturer's representatives, submit documentation with subsequent sundry.
 - b. If the welding is performed by a third party, the manufacturer's representative shall monitor the temperature to verify that it does not exceed the maximum temperature of the seal.
 - c. Manufacturer representative shall install the test plug for the initial BOP test.
 - d. Whenever any seal subject to test pressure is broken, all the tests in OOGO2.III.A.2.i must be followed.
 - e. If the cement does not circulate and one inch operations would have been possible with a standard wellhead, the well head shall be cut off, cementing operations performed and another wellhead installed.
5. The appropriate BLM office shall be notified a minimum of 4 hours in advance for a representative to witness the tests.
 - a. In a water basin, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. The casing cut-off and BOP installation can be initiated four hours after installing the slips, which will be approximately six hours after bumping the plug. For those casing strings not using slips, the minimum wait time before cut-off is eight hours after bumping the plug. BOP/BOPE testing can begin after cut-off or once cement reaches 500 psi compressive strength (including lead when specified), whichever is greater. However, if the float does not

hold, cut-off cannot be initiated until cement reaches 500 psi compressive strength (including lead when specified).

- b. In potash areas, for all casing strings utilizing slips, these are to be set as soon as the crew and rig are ready and any fallback cement remediation has been done. For all casing strings, casing cut-off and BOP installation can be initiated at twelve hours after bumping the plug. However, **no tests** shall commence until the cement has had a minimum of 24 hours setup time, except the casing pressure test can be initiated immediately after bumping the plug (only applies to single stage cement jobs).
- c. The tests shall be done by an independent service company utilizing a test plug not a cup or J-packer. The operator also has the option of utilizing an independent tester to test without a plug (i.e. against the casing) pursuant to Onshore Order 2 with the pressure not to exceed 70% of the burst rating for the casing. Any test against the casing must meet the WOC time for water basin (8 hours) or potash (24 hours) or 500 pounds compressive strength, whichever is greater, prior to initiating the test (see casing segment as lead cement may be critical item).
- d. The test shall be run on a 5000 psi chart for a 2-3M BOP/BOP, on a 10000 psi chart for a 5M BOP/BOPE and on a 15000 psi chart for a 10M BOP/BOPE. If a linear chart is used, it shall be a one hour chart. A circular chart shall have a maximum 2 hour clock. If a twelve hour or twenty-four hour chart is used, tester shall make a notation that it is run with a two hour clock.
- e. The results of the test shall be reported to the appropriate BLM office.
- f. All tests are required to be recorded on a calibrated test chart. A copy of the BOP/BOPE test chart and a copy of independent service company test will be submitted to the appropriate BLM office.
- g. The BOP/BOPE test shall include a low pressure test from 250 to 300 psi. The test will be held for a minimum of 10 minutes if test is done with a test plug and 30 minutes without a test plug. This test shall be performed prior to the test at full stack pressure.
- h. BOP/BOPE must be tested by an independent service company within 500 feet of the top of the Wolfcamp formation if the time between the setting of the intermediate casing and reaching this depth exceeds 20 days. This test does not exclude the test prior to drilling out the casing shoe as per Onshore Order No. 2.

C. DRILLING MUD

Mud system monitoring equipment, with derrick floor indicators and visual and audio alarms, shall be operating before drilling into the Wolfcamp formation, and shall be used until production casing is run and cemented.

D. WASTE MATERIAL AND FLUIDS

All waste (i.e. drilling fluids, trash, salts, chemicals, sewage, gray water, etc.) created as a result of drilling operations and completion operations shall be safely contained and disposed of properly at a waste disposal facility. No waste material or fluid shall be disposed of on the well location or surrounding area.

Porto-johns and trash containers will be on-location during fracturing operations or any other crew-intensive operations.



Hydrogen Sulfide Plan

- A. All personnel shall receive proper awareness H₂S training.
- B. Briefing Area: two perpendicular areas will be designated by signs and readily accessible.
- C. Required Emergency Equipment
 - a. Well Control Equipment
 - i. Flare line 150' from wellhead to be ignited by auto ignition sparking system.
 - ii. Choke manifold with a remotely operated hydraulic choke.
 - iii. Mud/gas separator
 - b. Protective equipment for essential personnel
 - i. Breathing Apparatus
 - 1. Rescue packs (SCBA) – 1 unit shall be placed at each briefing area, 2 shall be stored in a safety trailer on site.
 - 2. Work/Escapes packs – 4 packs shall be stored on the rig floor with sufficient air hose not to restrict work activity
 - 3. Emergency Escape Packs – 4 packs shall be stored in the doghouse for emergency evacuation
 - ii. Auxiliary Rescue Equipment
 - 1. Stretcher
 - 2. Two OSHA full body harnesses
 - 3. 100 feet of 5/8 inches OSHA approved rope
 - 4. 1-20# class ABC fire extinguisher
 - c. H₂S Detection and Monitoring Equipment
 - i. A stationary detector with three sensors will be placed in the doghouse if equipped, set to visually alarm at 10 ppm and audible at 14 ppm. The detector will be calibrated a minimum of every 30 days or as needed. The sensors will be placed in the following places:
 - 1. Rig Floor
 - 2. Below Rig Floor / Near BOPs
 - 3. End of flow line or where well bore fluid is being discharged (near shakers)
 - ii. If H₂S is encountered, measured values and formations will be provided to the BLM.
 - d. Visual Warning Systems
 - i. One color code condition sign will be placed at the entrance to the site reflecting the possible conditions at the site.
 - ii. A colored condition flag will be on display, reflecting the current condition at the site at the time.
 - iii. Two windsocks will be placed in strategic locations, visible from all angles.
 - e. Mud Program
 - i. The Mud program will be designed to minimize the volume of H₂S circulated to surface. The operator will have the necessary mud products to minimize hazards while drilling in H₂S bearing zones.



- f. Metallurgy
 - i. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H₂S service at the anticipated operating pressures to prevent sour sulfide stress cracking.
- g. Communication
 - i. Communication will be via cell phones and walkie talkies on location.

Franklin Mountain Energy has conducted a review of offset operated wells to determine if an H₂S contingency plan is required for the proposed well. Based on concentrations of offset wells, proximity to main roads, and distance to populated areas, the radius of exposure created by a potential release was determined to be minimal and low enough to not necessitate an H₂S contingency plan. This will be reevaluated during wellbore construction if H₂S is observed and after the well is on production.



Emergency Contact List:

Vladimir Roudakov, Drilling Engineer	Cell 720 933 9784
Rachael Overbey, Project and Regulatory Director	Cell 303 570 4057
Franklin Mountain Energy Afterhours Emergency Call Tree:	720-640-7517

EMERGENCY NUMBERS:

<u>Agency</u>	<u>Telephone Number</u>
BLM – Carlsbad Mainline	575-234-5972
BLM – Spill Emergency	575-234-6235
BLM – Engineering Emergency	575-361-2822
NMOCD District 1 – Hobbs Mainline	575-393-6161
NMOCD Emergency Line	575-370-3186
Wild Well Control	281-784-4700
H2S Emergency response:	
Air Ambulance New Mexico – Lea Co Reginal	575-391-2934
Lea County Sheriff's Department	575-396-3611
Fire Department:	
Carlsbad	575-885-3125
Artesia	575-746-5050
Lea County Regional Medical Center	575-492-5000
Jal Community Hospital	505-395-2511
Lea County Emergency Management	575-396-8602
Poison Control Center	800-222-1222



Mission Fed Com 603H

1. Geologic name of surface location: Permian
2. Estimated tops of important geological markers:

Formations	PROG SS	PROG TVD	Picked TVD	delta	Potential/Issues
Cenozoic Alluvium (surface)	3,329'	30'	30'	0	Sand/Gravels/unconsolidated
Rustler	2,227'	1,132'			Carbonates
Salado	2,109'	1,250'			Salt, Carbonate & Clastics
Base Salt	-42'	3,401'			Shaley Carbonate & Shale
Lamar	-1,607'	4,966'			Carbonate & Clastics
Bell Canyon	-1,665'	5,024'			Sandstone - oil/gas/water
Cherry Canyon	-2,553'	5,912'			Sandstone - oil/gas/water
Brushy Canyon	-3,974'	7,333'			Sand/carb/shales - oil/gas/water
Bone Spring Lime	-5,249'	8,608'			Shale/Carbonates - oil/gas
Avalon	-5,346'	8,705'			Shale/Carbonates - oil/gas
First Bone Spring Sand	-6,538'	9,897'			Sandstone - oil/gas/water
Second Bone Spring Carbonates	-6,668'	10,027'			Shale/Carbonates - oil/gas
Second Bone Spring Sand	-7,044'	10,403'			Sandstone - oil/gas/water
Third Bone Spring Carbonates	-7,592'	10,951'			Shale/Carbonates - oil/gas
Third Bone Spring Sand	-8,124'	11,483'			Sandstone - oil/gas/water
HZ Target at SHL	-8,296'	11,655'			Overpressure shale/sand- Oil/Gas
Wolfcamp	-8,441'	11,800'			Overpressure shale/sand- Oil/Gas
Wolfcamp A	-8,476'	11,835'			Overpressure Shale - Oil/Gas
Wolfcamp B	-8,668'	12,027'			Overpressure Shale - Oil/Gas

3. Estimated depth of anticipated fresh water, oil or gas:

Upper Permian Sands	0- 400'	Fresh Water
Delaware Sands	5,024'	Oil
Bone Spring	9,897'	Oil
Wolfcamp	11,800'	Oil

No other formations are expected to give up oil, gas or fresh water in measurable quantities. Surface freshwater sands will be protected by setting 13 3/8" casing at 1,300' and circulating cement back to surface.

4. Casing Program:

All casings strings will be run new. Safety factors calculated assuming the well is vertical.

Casing string	Weight	Grade	Burst	Collapse	Tension	Conn	Length	API design factor			
								Burst	Collapse	Tension	Coupling
Surface 13 3/8"	54.5	J-55	2730	1130	853	BTC 909	1300	1.18	1.67	4.99	5.32
Intermediate 9 5/8"	40	HCL-80	7430	4230	916	BTC 1042	5400	1.72	1.67	2.90	3.30
Intermediate 7 5/8"	29.7	HCP-110	8280	7150	827	Stinger 564	12002	1.11	1.27	1.81	1.24
Long string 5 1/2"	23	P-110	14520	14520	729	Anaconda 656	21813	1.32	1.42	1.21	1.09



Cementing Program:

Cementing Stage tool can be placed in the 1st Intermediate string as a contingency to ensure required TOC to surface.

String Type	Hole Size	Casing Size	Setting Depth	Sacks	Type of cmt	Lead Yield ft3/sk	Water gal/sk	TOC ft	Sacks	Type of cmt	Tail Yield ft3/sk	Water gal/sk	TOC	Excess
Surf	17.5	13.375	1300	795	Extenda Cem, 13.5 ppg Class C, 3lb/sk Kol-Seal	1.747	9.06	0	334	HalCem TM, 14.8 ppg, Class C, 1% CaCl ₂ , 0.125pps Celo-Flake	1.349	6.51	1000	100%
Int1	12.25	9.625	5400	1167	Neocem TM, 11.5 ppg, Class C 5% Salt, 0.125 pps Poly-E-Flake, 3lb/sk Kol-Seal	2.444	14.32	0	153	HalCem TM, 14.8 ppg, Class C, 0.1% HR 800 .125 pps Poly-E-Flake	1.334	6.42	5100	100%
Int2	8.75	7.625	12002	340	NeoCem, 11 ppg, Class C 3lb/sk Bridgemaker Gel, 5% Salt, 5pps LCM, 0.25pps Cello-Flake	2.798	17.15	4400	112	NeoCem 13.2 ppg, Class C 0.25 pps Cello-Flake, 2% CaCl ₂	1.44	7.29	11002	50%
Prod	6.75	5.5	21813	796	NeoCem, 13.5 ppg, Gas Migration Control	1.357	6.65	11002						20%

5. Minimum Specifications for Pressure Control:

The minimum blowout preventer equipment (BOPE) shown in Exhibit #1 will consist of a single ram, mud cross and double ram-type (10,000 psi WP) preventer and an annular preventer (5,000-psi WP). Both units will be hydraulically operated, and the ram-type will be equipped with blind rams on bottom and 4 ½" x 7" variable pipe rams on top. All BOPE will be tested in accordance with Onshore Oil & Gas order No. 2.

Before drilling out of the surface casing, the ram-type BOP and accessory equipment will be tested to 5,000/250 psig and the annular preventer to 5,000/250 psig. The surface casing will be tested to 1500 psi for 30 minutes.

Before drilling out of the second intermediate casing, the ram-type BOP and accessory equipment will be tested to 10,000/250 psig and the annular preventer to 5,000/250 psig. The second intermediate casing will be tested to 2000 psi for 30 minutes prior to drillout.

Pipe rams will be operationally checked each 24-hour period. Blind rams will be operationally checked on each trip out of the hole. These checks will be noted on the daily tour sheets.

A hydraulically operated choke will be installed prior to drilling out of the intermediate casing shoe.



6. Types and characteristics of the proposed mud system:

During this procedure we plan to use a Closed-Loop System and haul contents to the required disposal. The applicable depths and properties of the drilling fluid systems are as follows.

Depth	Type	Weight (ppg)	Viscosity	Water Loss
0 – 1,300'	Fresh - Gel	8.6-8.8	28-34	N/c
1,300' – 12,002'	Brine	8.8-10.2	28-34	N/c
12,002' – 21,813' Lateral	Oil Base	10.0-11.0	58-68	3 - 6

The highest mud weight needed to balance formation is expected to be 10-11 ppg. In order to maintain hole stability, mud weights up to 12 ppg may be utilized.

An electronic pit volume totalizer (PVT) will be utilized on the circulating system, to monitor pit volume, flow rate, pump pressure and stroke rate.

Sufficient mud materials to maintain mud properties and meet minimum lost circulation and weight increase requirements will be kept at the wellsite at all times.

7. Auxiliary well control and monitoring equipment:

(A) A kelly cock will be kept in the drill string at all times.

(B) A full opening drill pipe-stabbing valve (inside BOP) with proper drill pipe connections will be on the rig floor at all times.

(C) H₂S monitoring and detection equipment will be utilized from surface casing point to TD.

(D) A wear bushing will be installed in the wellhead prior to drilling out of the surface casing.

8. Logging, testing and coring program:

GR–CCL–CNL Will be run in cased hole during completions phase of operations.

Open-hole logs are not planned for this well.

9. Abnormal conditions, pressures, temperatures and potential hazards:

The estimated bottom-hole temperature at 11,811' TVD (deepest point of the well) is 195F with an estimated maximum bottom-hole pressure (BHP) at the same point of 7,370 psig (based on 12 ppg MW). Hydrogen sulfate may be present in the area. All necessary precautions will be taken before drilling operations commence. See Hydrogen Sulfide Plan below:

10. Hydrogen Sulfide Plan:

A. All personnel shall receive proper awareness H₂S training.

B. Briefing Area: two perpendicular areas will be designated by signs and readily accessible.

C. Required Emergency Equipment

a. Well Control Equipment

i. Flare line 150' from wellhead to be ignited by auto ignition sparking system.

ii. Choke manifold with a remotely operated hydraulic choke.

iii. Mud/gas separator

b. Protective equipment for essential personnel

i. Breathing Apparatus

1. Rescue packs (SCBA) – 1 unit shall be placed at each briefing area, 2 shall be stored in a safety trailer on site.

2. Work/Escapes packs – 4 packs shall be stored on the rig floor with sufficient air hose not to restrict work activity



3. Emergency Escape Packs – 4 packs shall be stored in the doghouse for emergency evacuation
- ii. Auxiliary Rescue Equipment
 1. Stretcher
 2. Two OSHA full body harnesses
 3. 100 feet of 5/8 inches OSHA approved rope
 4. 1-20# class ABC fire extinguisher
- c. H2S Detection and Monitoring Equipment
 - i. A stationary detector with three sensors will be placed in the doghouse if equipped, set to visually alarm at 10 ppm and audible at 14 ppm. The detector will be calibrated a minimum of every 30 days or as needed. The sensors will be placed in the following places:
 1. Rig Floor
 2. Below Rig Floor / Near BOPs
 3. End of flow line or where well bore fluid is being discharged (near shakers)
 - ii. If H2S is encountered, measured values and formations will be provided to the BLM.
- d. Visual Warning Systems
 - i. One color code condition sign will be placed at the entrance to the site reflecting the possible conditions at the site.
 - ii. A colored condition flag will be on display, reflecting the current condition at the site at the time.
 - iii. Two windsocks will be placed in strategic locations, visible from all angles.
- e. Mud Program
 - i. The Mud program will be designed to minimize the volume of H2S circulated to surface. The operator will have the necessary mud products to minimize hazards while drilling in H2S bearing zones.
- f. Metallurgy
 - i. All drill strings, casings, tubing, wellhead, blowout preventer, drilling spool, kill lines, choke manifold and lines, and valves shall be suitable for H2S service at the anticipated operating pressures to prevent sour sulfide stress cracking.
- g. Communication
 - i. Communication will be via cell phones and walkie talkies on location.

Franklin Mountain Energy has conducted a review of offset operated wells to determine if an H2S contingency plan is required for the proposed well. Based on concentrations of offset wells, proximity to main roads, and distance to populated areas, the radius of exposure created by a potential release was determined to be minimal and low enough to not necessitate an H2S contingency plan. This will be reevaluated during wellbore construction if H2S is observed and after the well is on production.

11. Anticipated starting date and duration of operations:

The drilling operations on the well should be finished in approximately one month. However, in order to minimize disturbance in the area and to improve efficiency Franklin Mountain is planning to drill all the wells on the pad prior to commence completion operations. To even further reduce the time heavy machinery is used the “batch drilling” method may be used. A batch drilling sequence sundry will be submitted for BLM approval prior to spud. A drilling rig with walking/skidding capabilities will be used.

**12. Disposal/environmental concerns:**

- (A) Drilled cuttings will be hauled to and disposed of in a state-certified disposal site.
- (B) Non-hazardous waste mud/cement from the drilling process will be also be hauled to and disposed of in a state-certified disposal site.
- (C) Garbage will be hauled to the Pecos City Landfill.
- (D) Sewage (grey water) will be hauled to the Carlsbad City Landfill

13. Wellhead:

A multi-bowl wellhead system will be utilized.

After running the 13 3/8" surface casing, a 13-5/8" BOP/BOPE system with a minimum working pressure of 10,000 psi will be installed on the wellhead system and will be pressure tested to 250 psi low followed by a 5,000 psi pressure test. This pressure test will be repeated at least every 21 days, as per Onshore Order No. 2

The minimum working pressure of the BOP and related BOPE required for drilling below the surface casing shoe shall be 5,000 psi.

After running the 2nd intermediate casing, and before drilling out, the wellhead, BOP, and related equipment will be tested to 10,000/250 psig.

The multi-bowl wellhead will be installed by vendor's representative(s). A copy of the installation instructions for the Cameron Multi-Bowl WH system has been sent to the BLM office in Carlsbad.

The wellhead will be installed by a third party welder while being monitored by WH vendor's representative.

All BOP equipment will be tested utilizing a conventional test plug. Not a cup or J-packer type.

A solid steel body pack-off will be utilized after running and cementing the intermediate casing strings. After installation of the first intermediate string the pack-off and lower flanges will be pressure tested to 5000 psi. After installation of the second intermediate string, the pack-off and upper flange will be pressure tested to 10,000 psi.

Both the surface and intermediate casing strings will be tested as per Onshore Order No. 2 to at least 0.22 psi/ft or 1500 psi, whichever is greater.

14. Additional variance requests**A. Casing.**

In order to minimize potential environmental and technical hazards, this well is planned with two intermediate strings of casing.

1. Variance is requested to wave the centralizer requirements for the 7 5/8" casing due to the tight clearance with 9 5/8" string.
2. Variance is requested to wave/reduce the centralizer requirements for the 5 1/2" casing due to the tight clearance with 6 3/4" hole and 5 1/2" casing due to tight clearances.

District I

1625 N. French Dr., Hobbs, NM 88240
Phone:(575) 393-6161 Fax:(575) 393-0720

District II

811 S. First St., Artesia, NM 88210
Phone:(575) 748-1283 Fax:(575) 748-9720

District III

1000 Rio Brazos Rd., Aztec, NM 87410
Phone:(505) 334-6178 Fax:(505) 334-6170

District IV

1220 S. St Francis Dr., Santa Fe, NM 87505
Phone:(505) 476-3470 Fax:(505) 476-3462

State of New Mexico
Energy, Minerals and Natural Resources
Oil Conservation Division
1220 S. St Francis Dr.
Santa Fe, NM 87505

CONDITIONS

Action 23281

CONDITIONS OF APPROVAL

Operator:		OGRID:	Action Number:	Action Type:
FRANKLIN MOUNTAIN ENERGY LLC	44 Cook Street	373910	23281	FORM 3160-3
Suite 1000	Denver, CO80206			

OCD Reviewer	Condition
pkautz	Will require a File As Drilled C-102 and a Directional Survey with the C-104
pkautz	Once the well is spud, to prevent ground water contamination through whole or partial conduits from the surface, the operator shall drill without interruption through the fresh water zone or zones and shall immediately set in cement the water protection string
